
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R F		163	19.4%	14.11%	28-Mar-26	24-Dec-26	01-Jun-26 A	02-Nov-26	939,341.79	683,511.82	4,842,719.29	45
KEY MILESTONES		0	0%	0%	28-Mar-26	28-Mar-26	29-Sep-26	29-Sep-26	0.00	0.00	0.00	-154
CONTRACTUAL MILESTONE		0	0%	0%	28-Mar-26	28-Mar-26	29-Sep-26	29-Sep-26	0.00	0.00	0.00	-154
MLTX-02-005-MS-1100	Completion of Engineering	0	100%	0%		28-Mar-26		29-Sep-26	0.00	0.00	0.00	-154
ARAR		151	14.46%	8.2%	15-Apr-26	24-Dec-26	11-Jun-26 A	02-Nov-26	332,143.01	188,427.38	2,296,631.10	45
ENGINEERING		30	0%	0%	15-Apr-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
SHOP DRAWINGS		30	0%	0%	15-Apr-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
SHOP DRAWINGS SUBMISSION		30	0%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
ELECTRICAL WORKS		30	0%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
MLTX-02-005-EN-2580	Shop DWG Submittal for Power Layout	30	100%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
MLTX-02-005-EN-2610	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
SHOP DRAWINGS APPROVALS		30	0%	0%	03-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		30	0%	0%	03-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
ARCHITECTURE WORKS		30	0%	0%	03-May-26	09-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-124
MLTX-02-005-EN-3480	Shop DWG Approval for Dome Internal Layout	30	100%	0%	03-May-26	09-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-124
AIR DOME SYSTEM		30	0%	0%	20-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-EN-3560	Shop DWG Approval for Membrane Panel Layout	30	100%	0%	20-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-EN-3570	Shop DWG Approval for Cable Tension Layout	30	100%	0%	20-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
ELECTRICAL WORKS		15	0%	0%	20-May-26	09-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-EN-3680	Shop DWG Approval for Lighting Layout	15	100%	0%	20-May-26	09-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-109
PROCUREMENT		29	0%	0%	19-May-26	18-Oct-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-12
SHORT LEAD ITEM		29	0%	0%	25-May-26	18-Oct-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-12
TOILET/SERVICE WORKS		29	0%	0%	09-Jun-26	04-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-75
LIGHTING FIXTURES		10	0%	0%	08-Jul-26	19-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8490	Material Delivery for Lighting Fixtures	10	100%	0%	08-Jul-26	19-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-70
SWITCHES/SOCKETS		12	0%	0%	08-Jul-26	21-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8510	PO for Switches/Sockets	5	100%	0%	08-Jul-26	13-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8530	Material Delivery for Switches/Sockets	7	100%	0%	14-Jul-26	21-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-70
DISTRIBUTION PANNELS		20	0%	0%	09-Jun-26	01-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-8590	PO for Distribution Panels	5	100%	0%	09-Jun-26	14-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-8610	Material Delivery for Distribution Panels	15	100%	0%	15-Jun-26	01-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-95
FURNITURES		29	0%	0%	02-Jul-26	04-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-8150	PO for Furnitures	9	100%	0%	02-Jul-26	12-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-8170	Material Delivery for Furnitures	20	100%	0%	13-Jul-26	04-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-75
PLAYGROUND WORKS		21	0%	0%	25-May-26	18-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-55
PVC MEMBRANE		21	0%	0%	24-Jun-26	18-Jul-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-8650	Material Delivery for PVC Membrane	21	100%	0%	24-Jun-26	18-Jul-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-82
RUBBER GRANULES		12	0%	0%	18-Jun-26	01-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-87
MLTX-02-005-PR-8890	Material Delivery for Rubber Granules	12	100%	0%	18-Jun-26	01-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-87
PADEL GLASS		18	0%	0%	25-May-26	17-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-8930	Material Delivery for Padel Glass	18	100%	0%	25-May-26	17-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-105
PADEL WIRE MESH/STEEL SETS		15	0%	0%	03-Jun-26	20-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	03-Jun-26	20-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-100
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	15-Jun-26	22-Jun-26	29-Sep-26	06-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9030	Material Delivery for the Site	7	100%	0%	15-Jun-26	22-Jun-26	29-Sep-26	06-Oct-26	0.00	0.00	0.00	-90
INTERLOCKING PAVING		7	0%	0%	20-Jul-26	27-Jul-26	07-Oct-26	14-Oct-26	0.00	0.00	0.00	-67
MLTX-02-005-PR-9070	Material Delivery for Interlocking Block Pavers	7	100%	0%	20-Jul-26	27-Jul-26	07-Oct-26	14-Oct-26	0.00	0.00	0.00	-67
MARKING PAINT		12	0%	0%	15-Jun-26	28-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9090	PO for Marking Paint	5	100%	0%	15-Jun-26	20-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9110	Material Delivery for Marking Paint	7	100%	0%	21-Jun-26	28-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-90
AIR DIFUSSERS/GRILLS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9170	PO for Air Difussers/Grills	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9190	Material Delivery for Air Difussers/Grills	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
GALVANIZED DUCTS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9210	PO for Galvanized Duct	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9230	Material Delivery for Galvanized Duct	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
EXHAUST FANS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9250	PO for Exhaust Fans	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9270	Material Delivery for Exhaust Fans	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
CCTV MATERIALS		5	0%	0%	20-Jul-26	25-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-9410	PO for CCTV	5	100%	0%	20-Jul-26	25-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-60
POWER OUTLETS/SWITCHES		15	0%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49

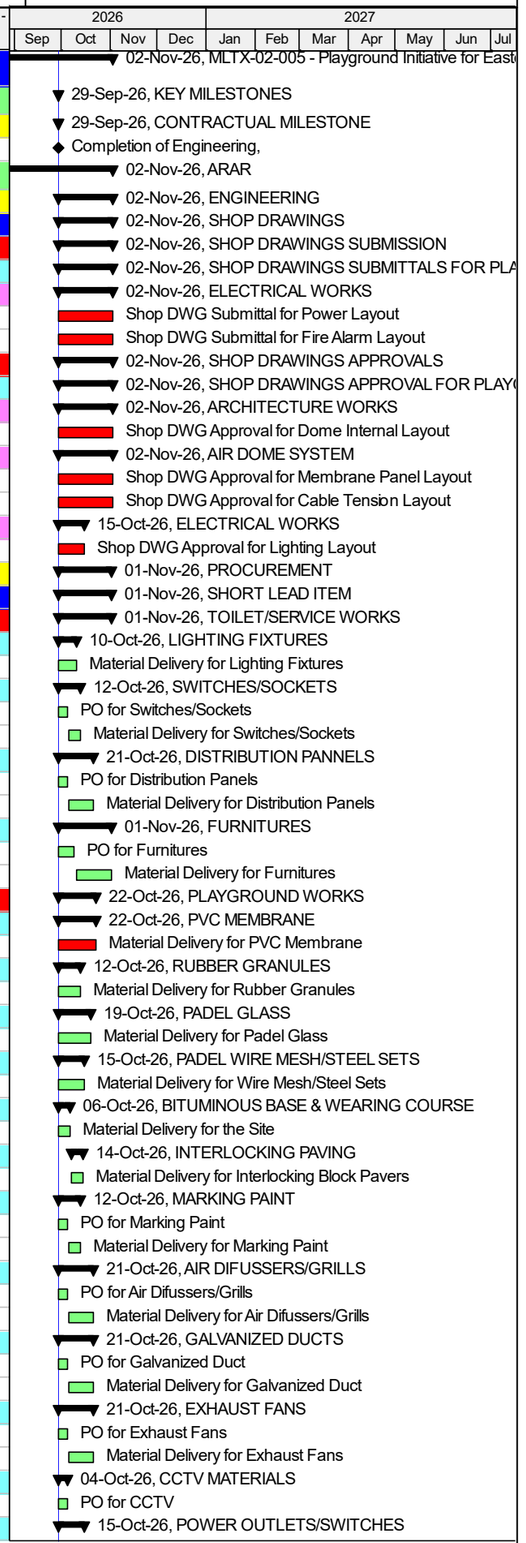

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	15	100%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49
LANDSCAPE WORKS		19	0%	0%	02-Aug-26	18-Oct-26	29-Sep-26	20-Oct-26	0.00	0.00	0.00	-2
PAVEMENT MARKING		15	0%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	02-Aug-26	06-Aug-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9600	Material Delivery for Pavement Markings	10	100%	0%	08-Aug-26	18-Aug-26	05-Oct-26	15-Oct-26	0.00	0.00	0.00	-49
TRAFFIC SIGNS		14	0%	0%	03-Oct-26	18-Oct-26	05-Oct-26	20-Oct-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-9620	PO for Traffic Signs	5	0%	0%	03-Oct-26	07-Oct-26	05-Oct-26	10-Oct-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-9640	Material Delivery for Traffic Signs	9	0%	0%	08-Oct-26	18-Oct-26	11-Oct-26	20-Oct-26	0.00	0.00	0.00	-2
LONG LEAD ITEM		28	0%	0%	19-May-26	23-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-110
PLAYGROUND WORKS		28	0%	0%	19-May-26	23-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-110
STEEL TENSION CABLES		28	0%	0%	19-May-26	23-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8670	PO for Steel Tension Cables	8	100%	0%	19-May-26	31-May-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8680	Material Fabrication for Steel Tension Cables	20	100%	0%	01-Jun-26	23-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-110
CONSTRUCTION PHASE		151	14.46%	8.2%	23-Jul-26	24-Dec-26	11-Jun-26 A	21-Oct-26	332,143.01	188,427.38	2,296,631.10	55
SITE WORKS		151	0%	9.26%	29-Sep-26	24-Dec-26	11-Jun-26 A	21-Oct-26	0.00	181,927.84	1,964,488.09	55
LANDSCAPE WORKS		151	0%	9.46%	29-Sep-26	24-Dec-26	11-Jun-26 A	21-Oct-26	0.00	181,927.84	1,923,542.76	55
PLAYGROUND AREA		10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	147,733.78	60
PADEL FENCE		10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	147,733.78	60
MLTX-02-005-CN-1025	Backfilling and Reinstatement for Concrete Foundation	7	0%	0%	08-Dec-26	15-Dec-26	29-Sep-26	06-Oct-26	0.00	0.00	4,143.45	60
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	33,147.63	60
MLTX-02-005-CN-1027(	Chain Link Fence Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	16,573.82	60
MLTX-02-005-CN-1028(	Install of Fence Gates	2	0%	0%	08-Dec-26	09-Dec-26	29-Sep-26	30-Sep-26	0.00	0.00	93,868.88	60
AIR DOME		10	0%	0%	21-Oct-26	01-Nov-26	29-Sep-26	10-Oct-26	0.00	0.00	936,278.81	19
CIVIL WORKS		10	0%	0%	21-Oct-26	01-Nov-26	29-Sep-26	10-Oct-26	0.00	0.00	936,278.81	19
MLTX-02-005-CN-1036(	Install of Membrane Covering System (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	29-Sep-26	10-Oct-26	0.00	0.00	936,278.81	19
IRRIGATION NETWORK		4	0%	70%	08-Oct-26	12-Oct-26	10-Sep-26 A	03-Oct-26	0.00	16,492.59	23,560.84	8
MLTX-02-005-CN-11450	Installing of Valves and fittings for Irrigation Network	4	0%	70%	08-Oct-26	12-Oct-26	10-Sep-26 A	03-Oct-26	0.00	16,492.59	23,560.84	8
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	165,435.26	367,633.90	57
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	84,399.35	187,554.12	57
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	81,035.90	180,079.78	57
GENERAL/FURNITURE		20	0%	0%	29-Sep-26	24-Dec-26	29-Sep-26	21-Oct-26	0.00	0.00	448,335.43	55
MLTX-02-005-CN-10610	Stamped Concrete Works for LandScape (Including Finishing Works)	5	0%	0%	05-Dec-26	09-Dec-26	29-Sep-26	04-Oct-26	0.00	0.00	93,594.00	57
MLTX-02-005-CN-10630	Fixation and Installation of Steel Frame for Benches	7	0%	0%	05-Dec-26	12-Dec-26	29-Sep-26	06-Oct-26	0.00	0.00	17,274.79	57
MLTX-02-005-CN-10640	Fixation and Installation of Benches	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	40,307.84	57
MLTX-02-005-CN-10650	Fixation and Installation of Precast Concrete Seats (Rectangular)	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	32,757.76	57
MLTX-02-005-CN-10660	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	12,869.04	57
MLTX-02-005-CN-11710	Preleminary Works for Site Light Poles Including Cable and Bases Works	7	0%	0%	29-Sep-26	06-Oct-26	29-Sep-26	06-Oct-26	0.00	0.00	75,459.60	0
MLTX-02-005-CN-11800	Installing of Site Light Poles	13	0%	0%	10-Dec-26	24-Dec-26	07-Oct-26	21-Oct-26	0.00	0.00	176,072.40	55
PARKING		3	0%	0%	14-Dec-26	16-Dec-26	29-Sep-26	01-Oct-26	0.00	0.00	40,945.33	65
MLTX-02-005-CN-10690	Interlock Installation (8 Cm) for Parking Area (Including Finishing Works)	3	0%	0%	14-Dec-26	16-Dec-26	29-Sep-26	01-Oct-26	0.00	0.00	40,945.33	65
TOILET/SERVICE BUILDING		29	100%	1.96%	23-Jul-26	09-Sep-26	28-Sep-26 A	20-Oct-26	332,143.01	6,499.54	332,143.01	-34
THERMAL & MOISTER PROTECTION		19	100%	0%	30-Jul-26	20-Aug-26	29-Sep-26	20-Oct-26	32,592.46	0.00	32,592.46	-51
MLTX-02-005-CN-11060	Preparing Surface and Preliminary Works for Roofing and Wet Areas Insulation	5	100%	0%	06-Aug-26	11-Aug-26	06-Oct-26	11-Oct-26	11,071.52	0.00	11,071.52	-51
MLTX-02-005-CN-11070	Finalize Water Proofing Works for Toilets	6	100%	0%	30-Jul-26	05-Aug-26	29-Sep-26	05-Oct-26	4,913.66	0.00	4,913.66	-51
MLTX-02-005-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	0%	12-Aug-26	20-Aug-26	12-Oct-26	20-Oct-26	16,607.28	0.00	16,607.28	-51
MECHANICAL WORK		29	100%	3.91%	09-Aug-26	09-Sep-26	28-Sep-26 A	15-Oct-26	166,144.58	6,499.54	166,144.58	-30
WATER SUPPLY SYSTEM		29	100%	4.65%	15-Aug-26	09-Sep-26	28-Sep-26 A	15-Oct-26	139,740.28	6,499.54	139,740.28	-30
MLTX-02-005-CN-11530	Installing of HDPE Pipes and Valves for Water Supply Network	3	100%	0%	15-Aug-26	17-Aug-26	29-Sep-26	01-Oct-26	25,998.40	0.00	25,998.40	-38
MLTX-02-005-CN-11550	Installing of Booster Pump Units Including fittings and accessories	7	100%	0%	02-Sep-26	09-Sep-26	08-Oct-26	15-Oct-26	48,746.52	0.00	48,746.52	-30
MLTX-02-005-CN-11560	Installing of GRP Tanks	8	100%	10%	24-Aug-26	01-Sep-26	28-Sep-26 A	07-Oct-26	64,995.36	6,499.54	64,995.36	-30
SEWER/DRAINAGE SYSTEM		9	100%	0%	09-Aug-26	18-Aug-26	29-Sep-26	08-Oct-26	26,404.30	0.00	26,404.30	-43
MLTX-02-005-CN-11580	Installing UPVC Pipes for External Connection for Sewage Network	4	100%	0%	15-Aug-26	18-Aug-26	05-Oct-26	08-Oct-26	14,217.67	0.00	14,217.67	-43
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	0%	09-Aug-26	13-Aug-26	29-Sep-26	04-Oct-26	12,186.63	0.00	12,186.63	-43
DOORS/WINDOWS		3	100%	0%	28-Jul-26	30-Jul-26	29-Sep-26	01-Oct-26	60,445.68	0.00	60,445.68	-53
MLTX-02-005-CN-11100	Preliminary Works For Windows/Curtain Wall	2	100%	0%	28-Jul-26	29-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-53
MLTX-02-005-CN-11110	Preliminary Works For Doors	3	100%	0%	28-Jul-26	30-Jul-26	29-Sep-26	01-Oct-26	7,799.44	0.00	7,799.44	-53
METAL WORKS		4	100%	0%	23-Jul-26	27-Jul-26	29-Sep-26	03-Oct-26	3,899.72	0.00	3,899.72	-57
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	23-Jul-26	27-Jul-26	29-Sep-26	03-Oct-26	3,899.72	0.00	3,899.72	-57
FINISHING WORKS		15	100%	0%	12-Aug-26	03-Sep-26	29-Sep-26	15-Oct-26	69,060.57	0.00	69,060.57	-35
FLOOR FINISHES		10	100%	0%	12-Aug-26	23-Aug-26	04-Oct-26	14-Oct-26	15,989.09	0.00	15,989.09	-44
MLTX-02-005-CN-11200	Creamic Tiles Floor Finish Works	2	100%	0%	12-Aug-26	13-Aug-26	04-Oct-26	05-Oct-26	11,894.39	0.00	11,894.39	-44
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	15-Aug-26	18-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-44
MLTX-02-005-CN-11230	Ceramic Skirting Tiles Finish Works	4	100%	0%	19-Aug-26	23-Aug-26	11-Oct-26	14-Oct-26	1,169.88	0.00	1,169.88	-44
WALL FINISHES		12	100%	0%	18-Aug-26	31-Aug-26	03-Oct-26	15-Oct-26	38,100.58	0.00	38,100.58	-38

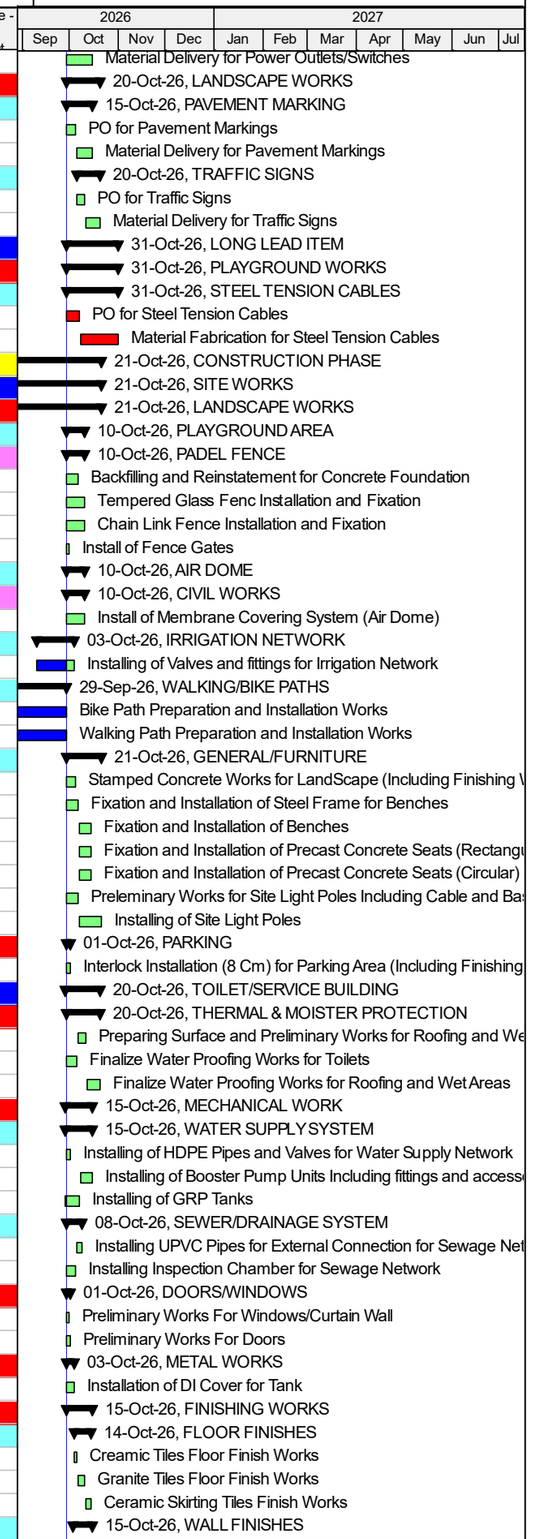

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-11250	Stone Cladding Finish Works for External Walls	5	100%	0%	26-Aug-26	31-Aug-26	11-Oct-26	15-Oct-26	2,275.00	0.00	2,275.00	-38
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	0%	18-Aug-26	25-Aug-26	03-Oct-26	10-Oct-26	35,825.58	0.00	35,825.58	-38
CELLING FINISHES		10	100%	0%	12-Aug-26	03-Sep-26	29-Sep-26	10-Oct-26	14,970.90	0.00	14,970.90	-30
MLTX-02-005-CN-11340	Preliminary Works for Ceiling Painting Works	3	100%	0%	12-Aug-26	15-Aug-26	29-Sep-26	01-Oct-26	5,771.52	0.00	5,771.52	-40
MLTX-02-005-CN-11350	Painting Finish Works for Ceiling	3	100%	0%	01-Sep-26	03-Sep-26	07-Oct-26	10-Oct-26	3,427.86	0.00	3,427.86	-30
MLTX-02-005-CN-11360	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	24-Aug-26	31-Aug-26	29-Sep-26	06-Oct-26	5,771.52	0.00	5,771.52	-30
HASA OASIS		136	14.8%	19.76%	30-Apr-26	23-Dec-26	01-Jun-26 A	02-Nov-26	289,911.97	386,957.04	1,958,309.28	44
ENGINEERING		30	0%	0%	30-Apr-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS		30	0%	0%	30-Apr-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS SUBMISSION		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MECHANCAL WORKS		21	0%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8760	Shop DWG Submittal for HVAC Plan	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8770	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
ELECTRICAL WORKS		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8650	Shop DWG Submittal for Lighting Layout	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8670	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8680	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8690	Shop DWG Submittal for Power Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8700	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8720	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EN-8730	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
SHOP DRAWINGS APPROVALS		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EN-1207(	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
PROCUREMENT		29	0%	0%	20-May-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
SHORT LEAD ITEM		29	0%	0%	25-May-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
TOILET/SERVICE WORKS		29	0%	0%	10-Jun-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
LIGHTING FIXTURES		10	0%	0%	09-Jul-26	20-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-10300	Material Delivery for Lighting Fixtures	10	100%	0%	09-Jul-26	20-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-69
SWITCHES/SOCKETS		12	0%	0%	09-Jul-26	22-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-10310	PO for Switches/Sockets	5	100%	0%	09-Jul-26	14-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-10320	Material Delivery for Switches/Sockets	7	100%	0%	15-Jul-26	22-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-69
DISTRIBUTION PANNELS		20	0%	0%	10-Jun-26	02-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-10130	PO for Distribution Panels	5	100%	0%	10-Jun-26	15-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-10140	Material Delivery for Distribution Panels	15	100%	0%	16-Jun-26	02-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-94
FURNITURES		29	0%	0%	04-Jul-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10330	PO for Furnitures	9	100%	0%	04-Jul-26	13-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10340	Material Delivery for Furnitures	20	100%	0%	14-Jul-26	05-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-74
PLAYGROUND WORKS		20	0%	0%	25-May-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
PVC MEMBRANE		4	0%	0%	25-May-26	01-Jun-26	29-Sep-26	03-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-10540	Material Delivery for PVC Membrane	4	100%	0%	25-May-26	01-Jun-26	29-Sep-26	03-Oct-26	0.00	0.00	0.00	-105
ARTIFICIAL TURF		12	0%	0%	30-May-26	11-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	12	100%	0%	30-May-26	11-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-104
RUBBER GRANULES		12	0%	0%	20-Jun-26	02-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	12	100%	0%	20-Jun-26	02-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-86
PADEL GLASS		18	0%	0%	30-May-26	18-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	18	100%	0%	30-May-26	18-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-104
PADEL WIRE MESH/STEEL SETS		15	0%	0%	04-Jun-26	21-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	04-Jun-26	21-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-99
MARKING PAINT		12	0%	0%	16-Jun-26	29-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-10350	PO for Marking Paint	5	100%	0%	16-Jun-26	21-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-10360	Material Delivery for Marking Paint	7	100%	0%	22-Jun-26	29-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-89
AIR DIFUSSERS/GRILLS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10480	Material Delivery for Air Difussers/Grills	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74
GALVANIZED DUCTS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10490	PO for Galvanized Duct	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10500	Material Delivery for Galvanized Duct	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74
EXHAUST FANS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10510	PO for Exhaust Fans	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-10520	Material Delivery for Exhaust Fans	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74

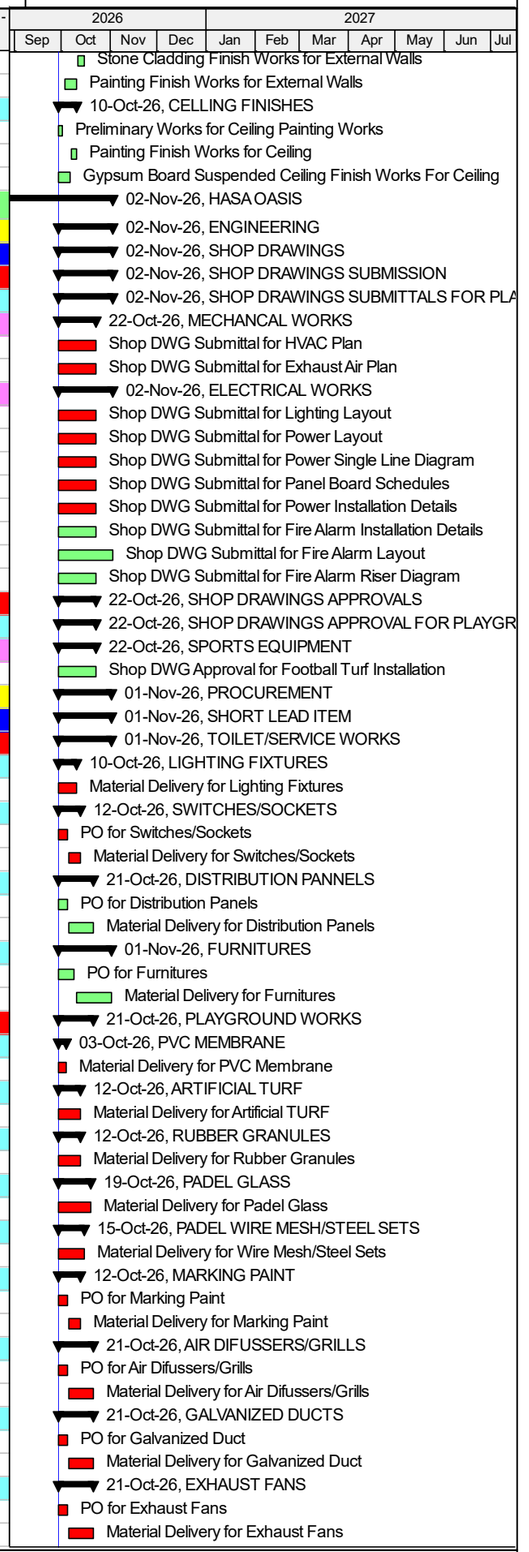

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CCTV MATERIALS		5	0%	0%	21-Jul-26	26-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-10690	PO for CCTV	5	100%	0%	21-Jul-26	26-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-59
LONG LEAD ITEM		28	0%	0%	20-May-26	24-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-109
PLAYGROUND WORKS		28	0%	0%	20-May-26	24-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-109
STEEL TENSION CABLES		28	0%	0%	20-May-26	24-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-10550	PO for Steel Tension Cables	8	100%	0%	20-May-26	01-Jun-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-10930	Material Fabrication for Steel Tension Cables	20	100%	0%	02-Jun-26	24-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-109
CONSTRUCTION PHASE		136	14.8%	19.76%	18-Jul-26	23-Dec-26	01-Jun-26 A	27-Oct-26	289,911.97	386,957.04	1,958,309.28	49
SITE WORKS		129	2.52%	20.35%	22-Sep-26	23-Dec-26	01-Jun-26 A	27-Oct-26	42,981.11	347,741.41	1,708,941.10	49
LANDSCAPE WORKS		129	2.52%	20.35%	22-Sep-26	23-Dec-26	01-Jun-26 A	27-Oct-26	42,981.11	347,741.41	1,708,941.10	49
PLAYGROUND AREA		49	23.28%	58.65%	22-Sep-26	23-Dec-26	21-Sep-26 A	22-Oct-26	42,981.11	108,312.40	184,664.12	53
PADEL FENCE		6	0%	0%	17-Dec-26	23-Dec-26	29-Sep-26	05-Oct-26	0.00	0.00	4,143.45	68
MLTX-02-005-CN-1224	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	17-Dec-26	23-Dec-26	29-Sep-26	05-Oct-26	0.00	0.00	4,143.45	68
CURBSTOEN/INTERLOCK		21	23.81%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	22-Oct-26	42,981.11	108,312.40	180,520.67	-5
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	21	23.81%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	22-Oct-26	42,981.11	108,312.40	180,520.67	-5
AIR DOME		21	0%	0%	30-Sep-26	24-Oct-26	04-Oct-26	27-Oct-26	0.00	0.00	936,278.81	-3
CIVIL WORKS		21	0%	0%	30-Sep-26	24-Oct-26	04-Oct-26	27-Oct-26	0.00	0.00	936,278.81	-3
MLTX-02-005-CN-1231(	Install of Membrane Covering System (Air Dome)	21	0%	0%	30-Sep-26	24-Oct-26	04-Oct-26	27-Oct-26	0.00	0.00	936,278.81	-3
IRRIGATION NETWORK		10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	25
MLTX-02-005-CN-13210	Installing of Valves and fittings for Irrigation Network	10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	25
WALKING/BIKE PATHS		8	0%	60%	31-Oct-26	08-Nov-26	01-Jun-26 A	29-Sep-26	0.00	220,580.34	367,633.90	35
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	0%	60%	31-Oct-26	08-Nov-26	01-Jun-26 A	29-Sep-26	0.00	112,532.47	187,554.12	35
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	0%	60%	31-Oct-26	08-Nov-26	10-Jun-26 A	29-Sep-26	0.00	108,047.87	180,079.78	35
GENERAL/FURNITURE		16	0%	0%	09-Nov-26	26-Nov-26	29-Sep-26	17-Oct-26	0.00	0.00	196,803.43	35
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	8	0%	0%	09-Nov-26	17-Nov-26	29-Sep-26	07-Oct-26	0.00	0.00	93,594.00	35
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	8	0%	0%	09-Nov-26	17-Nov-26	29-Sep-26	07-Oct-26	0.00	0.00	17,274.79	35
MLTX-02-005-CN-12450	Fixation and Installation of Benches	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	40,307.84	35
MLTX-02-005-CN-12460	Fixation and Installation of Precast Concrete Seats (Rectangular)	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	32,757.76	35
MLTX-02-005-CN-12470	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	12,869.04	35
TOILET/SERVICE BUILDING		27	99.02%	15.73%	18-Jul-26	29-Sep-26	19-Sep-26 A	21-Oct-26	246,930.85	39,215.63	249,368.18	-19
THERMAL & MOISTER PROTECTION		8	100%	50%	02-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	16,607.28	8,303.64	16,607.28	-49
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	50%	02-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	16,607.28	8,303.64	16,607.28	-49
MECHANICAL WORK		27	97.59%	12.85%	28-Jul-26	29-Sep-26	19-Sep-26 A	21-Oct-26	98,711.89	12,999.20	101,149.22	-19
WATER SUPPLY SYSTEM		27	96.74%	17.39%	10-Aug-26	29-Sep-26	19-Sep-26 A	21-Oct-26	72,307.59	12,999.20	74,744.92	-19
MLTX-02-005-CN-12760	Installing of HDPE Pipes and Valves for Water Supply Network	7	100%	50%	10-Aug-26	17-Aug-26	19-Sep-26 A	06-Oct-26	25,998.40	12,999.20	25,998.40	-42
MLTX-02-005-CN-12770	Installing of Booster Pump Units Including fittings and accessories	20	95%	0%	06-Sep-26	29-Sep-26	29-Sep-26	21-Oct-26	46,309.19	0.00	48,746.52	-19
SEWER/DRAINAGE SYSTEM		18	100%	0%	28-Jul-26	17-Aug-26	29-Sep-26	19-Oct-26	26,404.30	0.00	26,404.30	-53
MLTX-02-005-CN-13180	Installing UPVC Pipes for External Connection for Sewage Network	8	100%	0%	09-Aug-26	17-Aug-26	11-Oct-26	19-Oct-26	14,217.67	0.00	14,217.67	-53
MLTX-02-005-CN-13250	Installing Inspection Chamber for Sewage Network	10	100%	0%	28-Jul-26	08-Aug-26	29-Sep-26	10-Oct-26	12,186.63	0.00	12,186.63	-53
DOORS/WINDOWS		3	100%	0%	18-Jul-26	20-Jul-26	29-Sep-26	01-Oct-26	60,445.68	0.00	60,445.68	-62
MLTX-02-005-CN-12660	Preliminary Works For Doors	3	100%	0%	18-Jul-26	20-Jul-26	29-Sep-26	01-Oct-26	7,799.44	0.00	7,799.44	-62
MLTX-02-005-CN-13120	Preliminary Works For Windows/Curtain Wall	2	100%	0%	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-62
METAL WORKS		4	100%	0%	13-Aug-26	17-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-49
MLTX-02-005-CN-12610	Installation of Galvanized Steel Ladder	4	100%	0%	13-Aug-26	17-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-49
FINISHING WORKS		10	100%	27.42%	06-Aug-26	26-Aug-26	27-Sep-26 A	10-Oct-26	65,316.42	17,912.79	65,316.42	-37
FLOOR FINISHES		10	100%	0%	06-Aug-26	17-Aug-26	29-Sep-26	10-Oct-26	4,094.70	0.00	4,094.70	-45
MLTX-02-005-CN-13050	Granite Tiles Floor Finish Works	6	100%	0%	06-Aug-26	12-Aug-26	29-Sep-26	05-Oct-26	2,924.82	0.00	2,924.82	-45
MLTX-02-005-CN-13070	Ceramic Skirting Tiles Finish Works	4	100%	0%	13-Aug-26	17-Aug-26	06-Oct-26	10-Oct-26	1,169.88	0.00	1,169.88	-45
WALL FINISHES		7	100%	38.73%	11-Aug-26	26-Aug-26	27-Sep-26 A	10-Oct-26	46,250.82	17,912.79	46,250.82	-37
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	100%	50%	18-Aug-26	20-Aug-26	27-Sep-26 A	01-Oct-26	35,825.58	17,912.79	35,825.58	-35
MLTX-02-005-CN-13130	Stone Cladding Finish Works for External Walls	5	100%	0%	22-Aug-26	26-Aug-26	03-Oct-26	07-Oct-26	2,275.00	0.00	2,275.00	-35
MLTX-02-005-CN-13150	Granite Capping for Parpet	2	100%	0%	11-Aug-26	12-Aug-26	08-Oct-26	10-Oct-26	8,150.24	0.00	8,150.24	-49
CELLING FINISHES		8	100%	0%	11-Aug-26	24-Aug-26	29-Sep-26	07-Oct-26	14,970.90	0.00	14,970.90	-37
MLTX-02-005-CN-13280	Painting Finish Works for Ceiling	3	100%	0%	22-Aug-26	24-Aug-26	05-Oct-26	07-Oct-26	3,427.86	0.00	3,427.86	-37
MLTX-02-005-CN-13290	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5	100%	0%	16-Aug-26	20-Aug-26	29-Sep-26	04-Oct-26	5,771.52	0.00	5,771.52	-37
MLTX-02-005-CN-13300	Preliminary Works for Ceiling Painting Works	3	100%	0%	11-Aug-26	13-Aug-26	29-Sep-26	01-Oct-26	5,771.52	0.00	5,771.52	-41
DAMMAM		99	53.98%	18.4%	06-Apr-26	13-Dec-26	06-Sep-26 A	01-Nov-26	317,286.81	108,127.40	587,778.91	36
ENGINEERING		21	0%	0%	06-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SHOP DRAWINGS		21	0%	0%	06-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SHOP DRAWINGS SUBMISSION		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
AIR DOME SYSTEM		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1316(	Shop DWG Submittal for Cable Tension Layout	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1317(	Shop DWG Submittal for Airlock Door Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147

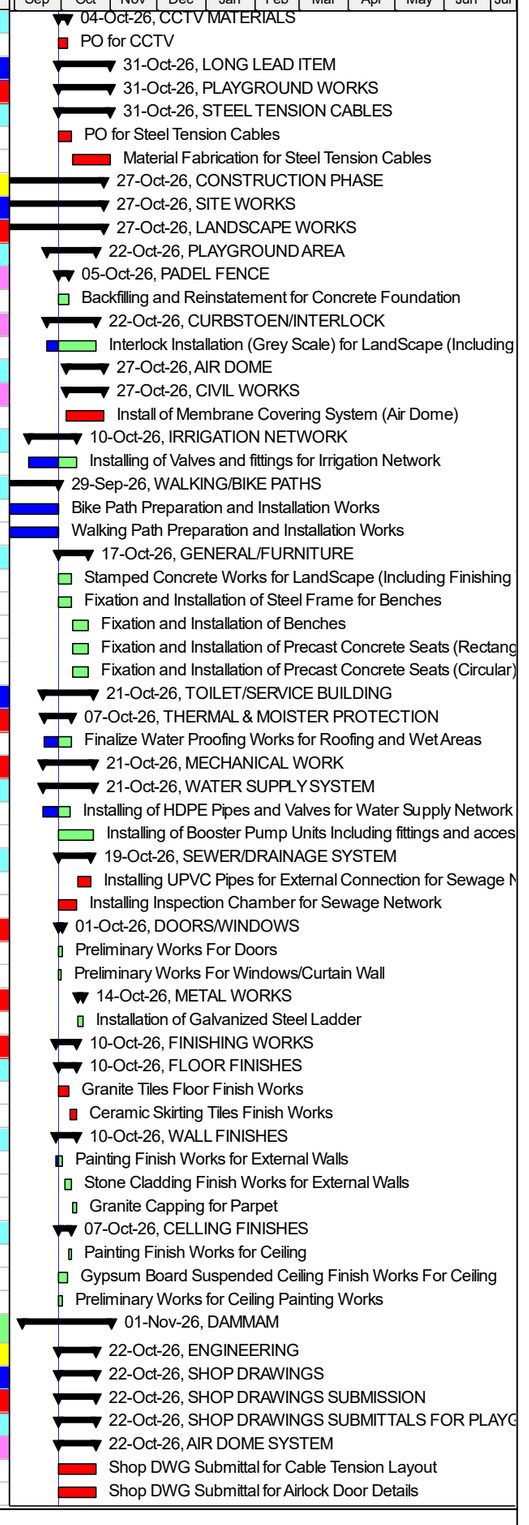

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-1318(	Shop DWG Submittal for Emergency Exit Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1303(	Shop DWG Submittal for HVAC Plan	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1304(	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
ELECTRICAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1293(	Shop DWG Submittal for Power Layout	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1294(	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1295(	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN-1296(	Shop DWG Submittal for Power Installation Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
SHOP DRAWINGS APPROVALS		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
AIR DOME SYSTEM		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EN-1627(	Shop DWG Approval for Air Dome Structural Layout	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EN-1634(	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
PROCUREMENT		29	0%	0%	21-May-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
SHORT LEAD ITEM		29	0%	0%	31-May-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
TOILET/SERVICE WORKS		29	0%	0%	11-Jun-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
LIGHTING FIXTURES		10	0%	0%	11-Jul-26	21-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-11380	Material Delivery for Lighting Fixtures	10	100%	0%	11-Jul-26	21-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-68
SWITCHES/SOCKETS		12	0%	0%	11-Jul-26	23-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-11390	PO for Switches/Sockets	5	100%	0%	11-Jul-26	15-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-11400	Material Delivery for Switches/Sockets	7	100%	0%	16-Jul-26	23-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-68
DISTRIBUTION PANNELS		20	0%	0%	11-Jun-26	04-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11210	PO for Distribution Panels	5	100%	0%	11-Jun-26	16-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11220	Material Delivery for Distribution Panels	15	100%	0%	17-Jun-26	04-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-93
FURNITURES		29	0%	0%	05-Jul-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11410	PO for Furnitures	9	100%	0%	05-Jul-26	14-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11420	Material Delivery for Furnitures	20	100%	0%	15-Jul-26	06-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-73
PLAYGROUND WORKS		21	0%	0%	31-May-26	27-Jul-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-74
PVC MEMBRANE		21	0%	0%	06-Jun-26	29-Jun-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	06-Jun-26	29-Jun-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-98
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-103
PADEL GLASS		18	0%	0%	31-May-26	20-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-11900	Material Delivery for Padel Glass	18	100%	0%	31-May-26	20-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-103
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-98
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	11-Jun-26	24-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11080	PO for Bituminous Base & Wearing Course	5	100%	0%	11-Jun-26	16-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11090	Material Delivery for the Site	7	100%	0%	17-Jun-26	24-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-93
MARKING PAINT		12	0%	0%	17-Jun-26	30-Jun-26	05-Oct-26	18-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11430	PO for Marking Paint	5	100%	0%	17-Jun-26	22-Jun-26	05-Oct-26	10-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-11440	Material Delivery for Marking Paint	7	100%	0%	23-Jun-26	30-Jun-26	11-Oct-26	18-Oct-26	0.00	0.00	0.00	-93
AIR DIFUSSERS/GRILLS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11550	PO for Air Difussers/Grills	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11560	Material Delivery for Air Difussers/Grills	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
GALVANIZED DUCTS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11570	PO for Galvanized Duct	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11580	Material Delivery for Galvanized Duct	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
EXHAUST FANS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11590	PO for Exhaust Fans	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-11600	Material Delivery for Exhaust Fans	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
CCTV MATERIALS		5	0%	0%	22-Jul-26	27-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-58
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	22-Jul-26	27-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-58
LONG LEAD ITEM		28	0%	0%	21-May-26	25-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-108
PLAYGROUND WORKS		28	0%	0%	21-May-26	25-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-108
STEEL TENSION CABLES		28	0%	0%	21-May-26	25-Jun-26	29-Sep-26	31-Oct-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-11630	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-12010	Material Fabrication for Steel Tension Cables	20	100%	0%	03-Jun-26	25-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-108
CONSTRUCTION PHASE		99	53.98%	18.4%	22-Jul-26	13-Dec-26	06-Sep-26 A	20-Oct-26	317,286.81	108,127.40	587,778.91	46
SITE WORKS		87	21.81%	21.4%	07-Sep-26	13-Dec-26	19-Sep-26 A	19-Oct-26	75,459.60	74,042.86	345,951.70	47
LANDSCAPE WORKS		87	21.81%	21.4%	07-Sep-26	13-Dec-26	19-Sep-26 A	19-Oct-26	75,459.60	74,042.86	345,951.70	47
IRRIGATION NETWORK		6	0%	80%	30-Sep-26	06-Oct-26	19-Sep-26 A	01-Oct-26	0.00	58,950.94	73,688.67	4



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 29-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-14630	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	3	0%	80%	30-Sep-26	03-Oct-26	19-Sep-26 A	01-Oct-26	0.00	40,102.26	50,127.83	1
MLTX-02-005-CN-14640	Installing of Valves and fittings for Irrigation Network	3	0%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	01-Oct-26	0.00	18,848.67	23,560.84	4
GENERAL/FURNITURE		22	27.72%	5.54%	07-Sep-26	13-Dec-26	20-Sep-26 A	19-Oct-26	75,459.60	15,091.92	272,263.03	47
MLTX-02-005-CN-13400	Stamped Concrete Works for LandScape (Including Finishing Works)	8	0%	0%	23-Nov-26	01-Dec-26	29-Sep-26	07-Oct-26	0.00	0.00	93,594.00	47
MLTX-02-005-CN-13870	Fixation and Installation of Steel Frame for Benches	8	0%	0%	23-Nov-26	01-Dec-26	29-Sep-26	07-Oct-26	0.00	0.00	17,274.79	47
MLTX-02-005-CN-13880	Fixation and Installation of Benches	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	40,307.84	47
MLTX-02-005-CN-13890	Fixation and Installation of Precast Concrete Seats (Rectangular)	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	32,757.76	47
MLTX-02-005-CN-13900	Fixation and Installation of Precast Concrete Seats (Circular)	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	12,869.04	47
MLTX-02-005-CN-14350	Preleminary Works for Site Light Poles Including Cable and Bases Works	13	100%	20%	07-Sep-26	21-Sep-26	20-Sep-26 A	13-Oct-26	75,459.60	15,091.92	75,459.60	-18
TOILET/SERVICE BUILDING		31	100%	14.09%	22-Jul-26	22-Sep-26	06-Sep-26 A	20-Oct-26	241,827.21	34,084.54	241,827.21	-23
THERMAL & MOISTER PROTECTION		8	100%	80%	06-Aug-26	15-Aug-26	06-Sep-26 A	07-Oct-26	16,607.28	13,285.82	16,607.28	-45
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	80%	06-Aug-26	15-Aug-26	06-Sep-26 A	07-Oct-26	16,607.28	13,285.82	16,607.28	-45
MECHANICAL WORK		18	100%	23.89%	08-Aug-26	20-Sep-26	19-Sep-26 A	11-Oct-26	87,053.47	20,798.72	87,053.47	-17
WATER SUPPLY SYSTEM		18	100%	27.83%	08-Aug-26	01-Sep-26	19-Sep-26 A	11-Oct-26	74,744.92	20,798.72	74,744.92	-33
MLTX-02-005-CN-14190	Installing of HDPE Pipes and Valves for Water Supply Network	6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	05-Oct-26	25,998.40	20,798.72	25,998.40	-44
MLTX-02-005-CN-14200	Installing of Booster Pump Units Including fittings and accessories	5	100%	0%	27-Aug-26	01-Sep-26	06-Oct-26	11-Oct-26	48,746.52	0.00	48,746.52	-33
SEWER/DRAINAGE SYSTEM		4	100%	0%	17-Aug-26	20-Aug-26	29-Sep-26	03-Oct-26	10,358.68	0.00	10,358.68	-36
MLTX-02-005-CN-14230	Installing of Plumping Fixtures and Accessories	4	100%	0%	17-Aug-26	20-Aug-26	29-Sep-26	03-Oct-26	10,358.68	0.00	10,358.68	-36
FIRE PROTECTION		2	100%	0%	19-Sep-26	20-Sep-26	29-Sep-26	30-Sep-26	1,949.87	0.00	1,949.87	-8
MLTX-02-005-CN-14240	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	2	100%	0%	19-Sep-26	20-Sep-26	29-Sep-26	30-Sep-26	1,949.87	0.00	1,949.87	-8
ELECTRICAL WORKS		14	100%	0%	19-Sep-26	22-Sep-26	29-Sep-26	14-Oct-26	20,499.02	0.00	20,499.02	-18
FIXTURE WORKS		14	100%	0%	19-Sep-26	22-Sep-26	29-Sep-26	14-Oct-26	20,499.02	0.00	20,499.02	-18
MLTX-02-005-CN-14320	Installing and Finalize Works of Lighting Works including Light Fixtures	4	100%	0%	19-Sep-26	22-Sep-26	11-Oct-26	14-Oct-26	14,259.43	0.00	14,259.43	-18
MLTX-02-005-CN-14340	Installing Data and Telecommunication System with all Accessories	4	100%	0%	19-Sep-26	22-Sep-26	29-Sep-26	03-Oct-26	6,239.59	0.00	6,239.59	-8
DOORS/WINDOWS		2	100%	0%	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-58
MLTX-02-005-CN-14550	Preliminary Works For Windows/Curtain Wall	2	100%	0%	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-58
METAL WORKS		4	100%	0%	18-Aug-26	22-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-45
MLTX-02-005-CN-14040	Installation of Galvanized Steel Ladder	4	100%	0%	18-Aug-26	22-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-45
FINISHING WORKS		19	100%	0%	10-Aug-26	08-Sep-26	29-Sep-26	20-Oct-26	44,547.66	0.00	44,547.66	-35
FLOOR FINISHES		4	100%	0%	10-Aug-26	13-Aug-26	29-Sep-26	03-Oct-26	2,924.82	0.00	2,924.82	-42
MLTX-02-005-CN-14480	Granite Tiles Floor Finish Works	4	100%	0%	10-Aug-26	13-Aug-26	29-Sep-26	03-Oct-26	2,924.82	0.00	2,924.82	-42
WALL FINISHES		19	100%	0%	16-Aug-26	08-Sep-26	29-Sep-26	20-Oct-26	41,622.84	0.00	41,622.84	-35
MLTX-02-005-CN-14460	Phenolic Partitions for Toilets	11	100%	0%	27-Aug-26	08-Sep-26	08-Oct-26	20-Oct-26	31,197.60	0.00	31,197.60	-35
MLTX-02-005-CN-14560	Stone Cladding Finish Works for External Walls	5	100%	0%	18-Aug-26	23-Aug-26	29-Sep-26	04-Oct-26	2,275.00	0.00	2,275.00	-35
MLTX-02-005-CN-14580	Granite Capping for Parpet	2	100%	0%	16-Aug-26	17-Aug-26	08-Oct-26	10-Oct-26	8,150.24	0.00	8,150.24	-45
SPECIALTIES WORK		4	100%	0%	22-Aug-26	25-Aug-26	04-Oct-26	07-Oct-26	14,623.96	0.00	14,623.96	-36
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	100%	0%	22-Aug-26	25-Aug-26	04-Oct-26	07-Oct-26	14,623.96	0.00	14,623.96	-36

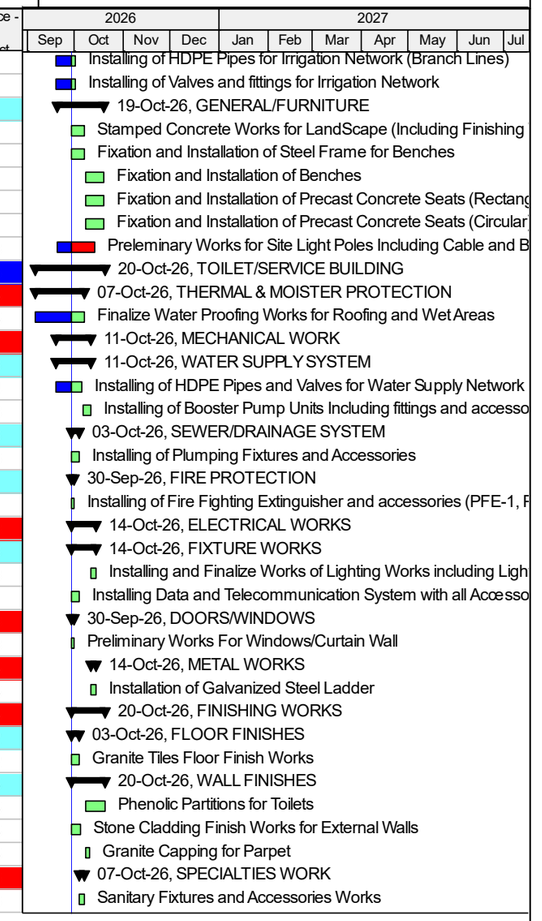

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
