
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oa		251	41.27%	34.21%	03-Mar-26	02-Jan-27	03-Mar-26 A	21-Apr-27	12,378,902.56	10,262,093.38	29,997,851.67	-90
KEY MILESTONES		251	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	21-Apr-27	0.00	0.00	0.00	-90
GENERAL MILESTONES		251	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	21-Apr-27	0.00	0.00	0.00	-90
CONTRACTUAL MILESTONE		216	0%	0%	28-Mar-26	02-Jan-27	02-Apr-26 A	08-Apr-27	0.00	0.00	0.00	-79
ARAR		240	30.37%	30.96%	03-Mar-26	02-Jan-27	04-Mar-26 A	08-Apr-27	3,070,829.55	3,129,803.79	10,110,715.45	-79
MOBILIZATION		23	0%	0%	03-Mar-26	01-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
ENGINEERING		196	0%	0%	07-Mar-26	25-Oct-26	07-Mar-26 A	15-Feb-27	0.00	0.00	0.00	-97
PROCUREMENT		183	0%	0%	19-May-26	22-Nov-26	02-Apr-26 A	13-Feb-27	0.00	0.00	0.00	-71
CONSTRUCTION PHASE		238	30.37%	30.96%	15-Apr-26	02-Jan-27	04-Apr-26 A	23-Mar-27	3,070,829.55	3,129,803.79	10,110,715.45	-65
SITE WORKS		238	21%	29.46%	15-Apr-26	02-Jan-27	04-Apr-26 A	23-Mar-27	1,871,465.86	2,625,596.66	8,911,351.76	-65
EARTH WORKS		81	100%	100%	15-Apr-26	11-Jun-26	04-Apr-26 A	05-Aug-26 A	1,017,621.97	1,017,621.97	1,017,621.97	-46
LANDSCAPE WORKS		205	10.9%	20.3%	13-Jun-26	02-Jan-27	17-May-26 A	23-Mar-27	853,843.90	1,590,426.69	7,835,236.46	-65
PLAYGROUND AREA		194	36.23%	50.77%	13-Jun-26	02-Jan-27	19-May-26 A	15-Mar-27	516,114.43	723,206.72	1,424,564.96	-58
FOOTBALL PLAYGROUND		182	35%	35%	13-Jun-26	01-Dec-26	19-May-26 A	06-Mar-27	110,897.50	110,897.50	316,849.99	-80
PADEL PLAYGROUND		189	45%	70%	06-Jul-26	01-Dec-26	19-May-26 A	06-Mar-27	105,292.80	163,788.80	233,984.00	-80
BASKETBALL PLAYGROUND		173	36.55%	70%	30-Jul-26	07-Dec-26	19-May-26 A	15-Mar-27	118,139.79	226,230.90	323,187.00	-80
PADEL FENCE		168	0%	21.52%	08-Dec-26	19-Dec-26	08-Aug-26 A	10-Oct-26	0.00	40,505.18	188,238.96	60
CURBSTOEN/INTERLOCK		65	50.17%	50.17%	15-Sep-26	02-Jan-27	15-Aug-26 A	08-Nov-26	181,784.34	181,784.34	362,305.01	47
AIR DOME		169	6.92%	11.91%	24-Aug-26	09-Dec-26	17-May-26 A	23-Mar-27	337,729.47	581,544.30	4,881,359.87	-85
CIVIL WORKS		112	17.18%	29.58%	24-Aug-26	01-Nov-26	17-May-26 A	27-Oct-26	337,729.47	581,544.30	1,966,294.68	4
MECHANICAL WORKS		76	0%	0%	02-Nov-26	16-Nov-26	28-Oct-26	24-Jan-27	0.00	0.00	1,233,296.81	-59
ELECTRICAL WORKS		20	0%	0%	17-Nov-26	09-Dec-26	25-Jan-27	16-Feb-27	0.00	0.00	1,513,591.54	-59
FINISHES WORKS		49	0%	0%	14-Nov-26	09-Dec-26	21-Jan-27	23-Mar-27	0.00	0.00	168,176.84	-85
IRRIGATION NETWORK		81	0%	78.89%	29-Sep-26	22-Oct-26	18-Aug-26 A	16-Feb-27	0.00	120,240.42	152,414.87	-100
NATURAL GROUND		81	0%	0%	13-Oct-26	22-Oct-26	15-Nov-26	16-Feb-27	0.00	0.00	191,740.00	-100
PLANTING		24	0%	0%	24-Oct-26	19-Nov-26	17-Feb-27	21-Mar-27	0.00	0.00	347,251.46	-100
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	165,435.26	367,633.90	57
GENERAL/FURNITURE		27	0%	0%	29-Sep-26	02-Jan-27	29-Sep-26	29-Oct-26	0.00	0.00	470,271.40	55
PARKING		159	0%	30%	10-Dec-26	16-Dec-26	16-May-26 A	01-Oct-26	0.00	17,548.00	58,493.33	65
TOILET/SERVICE BUILDING		123	100%	42.04%	06-Jun-26	26-Sep-26	21-May-26 A	30-Nov-26	1,199,363.69	504,207.13	1,199,363.69	-56
STRUCTURE WORKS		98	100%	100%	06-Jun-26	27-Jul-26	21-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-5
MASONARY WORK		5	100%	100%	06-Jul-26	11-Jul-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
THERMAL & MOISTER PROTECTION		21	100%	6.07%	28-Jul-26	20-Aug-26	26-Sep-26 A	20-Oct-26	34,698.32	2,105.86	34,698.32	-51
MECHANICAL WORK		57	100%	16.98%	06-Aug-26	21-Sep-26	18-Jul-26 A	12-Nov-26	264,673.10	44,947.89	264,673.10	-44
ELECTRICAL WORKS		113	100%	53.29%	28-Jul-26	26-Sep-26	19-Jul-26 A	30-Nov-26	386,998.59	206,217.32	386,998.59	-56
DOORS/WINDOWS		42	100%	0%	28-Jul-26	26-Sep-26	29-Sep-26	16-Nov-26	68,245.12	0.00	68,245.12	-44
METAL WORKS		25	100%	28.57%	23-Jul-26	01-Sep-26	16-Sep-26 A	27-Oct-26	13,649.02	3,899.72	13,649.02	-47
FINISHING WORKS		71	100%	24.42%	06-Aug-26	20-Sep-26	10-Aug-26 A	11-Nov-26	166,130.97	40,563.60	166,130.97	-44
SPECIALTIES WORK		24	100%	0%	26-Aug-26	22-Sep-26	18-Oct-26	14-Nov-26	58,495.83	0.00	58,495.83	-44
TESTING & COMMISSIONING		40	0%	0%	24-Oct-26	26-Dec-26	17-Feb-27	08-Apr-27	0.00	0.00	0.00	-85
HASA OASIS		246	45.43%	36.64%	03-Mar-26	02-Jan-27	04-Mar-26 A	15-Apr-27	4,535,089.67	3,657,877.35	9,982,829.07	-85
MOBILIZATION		24	0%	0%	03-Mar-26	02-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
ENGINEERING		121	0%	0%	08-Mar-26	20-Sep-26	08-Mar-26 A	16-Nov-26	0.00	0.00	0.00	-48
PROCUREMENT		183	0%	0%	20-May-26	04-Nov-26	04-Apr-26 A	13-Feb-27	0.00	0.00	0.00	-86
CONSTRUCTION PHASE		226	45.43%	36.64%	29-Mar-26	28-Dec-26	04-Apr-26 A	23-Mar-27	4,535,089.67	3,657,877.35	9,982,829.07	-69
SITE WORKS		226	38.71%	34.47%	29-Mar-26	28-Dec-26	04-Apr-26 A	23-Mar-27	3,399,715.08	3,028,078.94	8,783,465.12	-69
EARTH WORKS		73	100%	100%	29-Mar-26	02-Jun-26	04-Apr-26 A	08-Aug-26 A	979,460.76	979,460.76	979,460.76	-56
LANDSCAPE WORKS		224	31.25%	25.69%	16-May-26	28-Dec-26	16-May-26 A	23-Mar-27	2,420,254.33	1,990,124.85	7,745,511.03	-69
PLAYGROUND AREA		212	51.19%	74.16%	16-May-26	28-Dec-26	18-May-26 A	06-Mar-27	683,283.74	989,944.11	1,334,839.53	-57
FOOTBALL PLAYGROUND		174	50%	85%	16-May-26	24-Oct-26	18-May-26 A	28-Nov-26	158,425.00	269,322.49	316,849.99	-30
PADEL PLAYGROUND		191	45%	70%	11-Jun-26	16-Dec-26	18-May-26 A	27-Dec-26	105,292.80	163,788.80	233,984.00	-9
BASKETBALL PLAYGROUND		161	57.49%	71.39%	05-Jul-26	14-Dec-26	18-May-26 A	06-Mar-27	194,800.49	241,875.35	338,831.45	-69
PADEL FENCE		65	0%	30%	17-Dec-26	28-Dec-26	06-Aug-26 A	31-Oct-26	0.00	24,860.73	82,869.08	50
CURBSTOEN/INTERLOCK		58	62.04%	80.07%	03-Sep-26	17-Oct-26	12-Aug-26 A	22-Oct-26	224,765.45	290,096.74	362,305.01	-5
AIR DOME		138	34.25%	11.91%	27-Jul-26	09-Dec-26	16-May-26 A	14-Mar-27	1,671,935.00	581,544.30	4,881,359.87	-77
CIVIL WORKS		81	28.34%	29.58%	30-Jul-26	24-Oct-26	16-May-26 A	17-Nov-26	557,162.82	581,544.30	1,966,294.68	-21
MECHANICAL WORKS		98	13.64%	0%	27-Jul-26	15-Nov-26	22-Oct-26	13-Feb-27	168,176.84	0.00	1,233,296.81	-77
ELECTRICAL WORKS		58	62.54%	0%	03-Sep-26	15-Oct-26	26-Nov-26	01-Feb-27	946,595.34	0.00	1,513,591.54	-93
FINISHES WORKS		68	0%	0%	17-Oct-26	09-Dec-26	21-Dec-26	14-Mar-27	0.00	0.00	168,176.84	-77
IRRIGATION NETWORK		78	11.73%	80.44%	22-Sep-26	17-Nov-26	18-Jul-26 A	16-Feb-27	17,873.33	122,596.50	152,414.87	-78
NATURAL GROUND		63	0%	0%	09-Nov-26	17-Nov-26	06-Dec-26	16-Feb-27	0.00	0.00	191,740.00	-78
PLANTING		13	0%	0%	12-Oct-26	29-Oct-26	10-Feb-27	25-Feb-27	0.00	0.00	347,251.46	-101
WALKING/BIKE PATHS		8	0%	60%	31-Oct-26	08-Nov-26	01-Jun-26 A	29-Sep-26	0.00	220,580.34	367,633.90	35

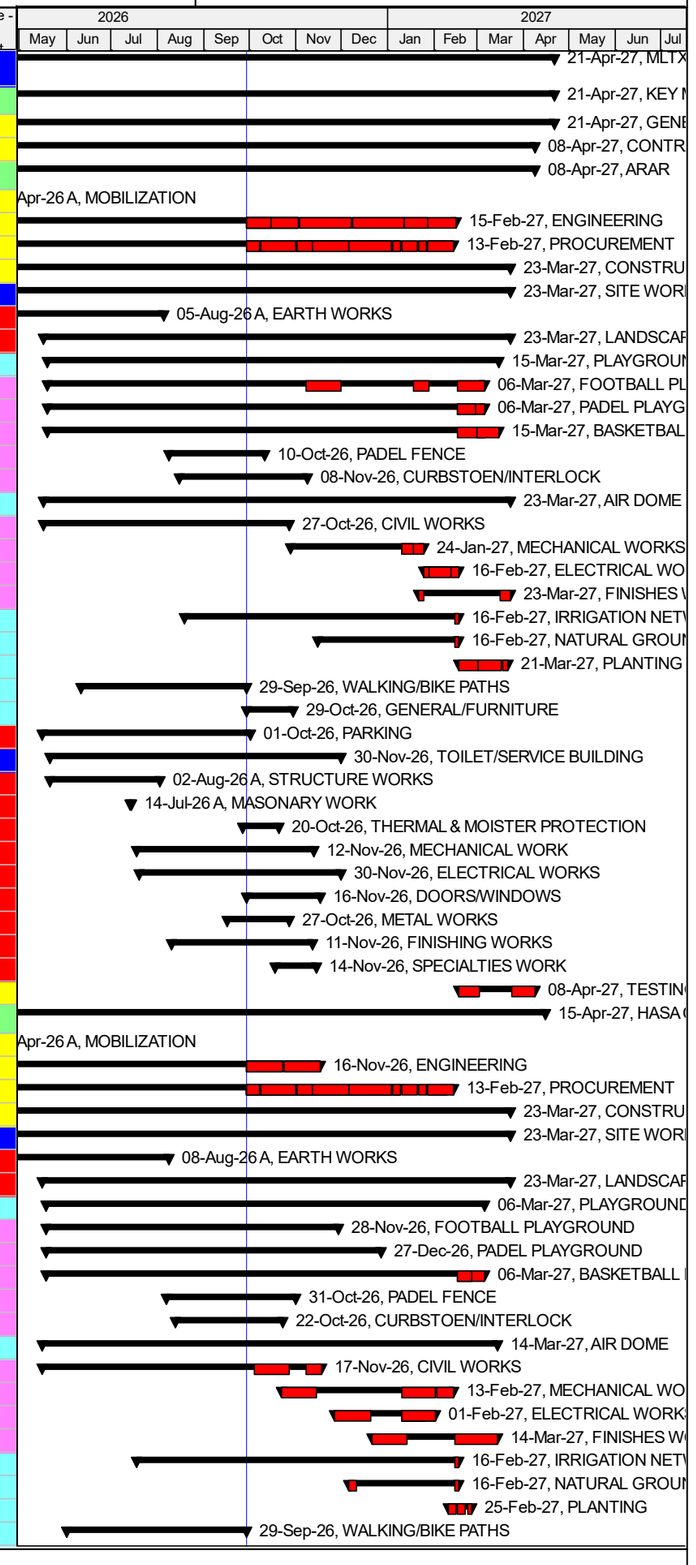

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	167	10.03%	16.05%	22-Sep-26	10-Dec-26	03-Sep-26 A	23-Mar-27	47,162.25	75,459.60	470,271.40	-84
	PARKING	148	0%	100%	18-Nov-26	01-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	63
	TOILET/SERVICE BUILDING	135	94.66%	52.51%	03-Jun-26	21-Oct-26	24-May-26 A	22-Dec-26	1,135,374.59	629,798.41	1,199,363.95	-53
	STRUCTURE WORKS	78	100%	100%	03-Jun-26	16-Jul-26	24-May-26 A	10-Aug-26 A	194,188.64	194,188.64	194,188.64	-21
	MASONARY WORK	5	100%	100%	28-Jun-26	02-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-4
	THERMAL & MOISTER PROTECTION	22	100%	76.07%	18-Jul-26	10-Aug-26	10-Sep-26 A	07-Oct-26	34,698.32	26,394.68	34,698.32	-49
	MECHANICAL WORK	79	98.23%	43.99%	26-Jul-26	07-Oct-26	12-Jul-26 A	08-Dec-26	259,998.07	116,442.91	264,673.10	-53
	ELECTRICAL WORKS	116	84.67%	53.29%	18-Jul-26	21-Oct-26	14-Jul-26 A	22-Dec-26	327,684.52	206,217.58	386,998.85	-53
	DOORS/WINDOWS	39	100%	0%	18-Jul-26	10-Sep-26	29-Sep-26	12-Nov-26	68,245.12	0.00	68,245.12	-53
	METAL WORKS	9	100%	28.57%	18-Jul-26	22-Aug-26	06-Sep-26 A	19-Oct-26	13,649.02	3,899.72	13,649.02	-49
	FINISHING WORKS	69	100%	42.36%	26-Jul-26	13-Sep-26	17-Aug-26 A	15-Nov-26	166,130.97	70,370.78	166,130.97	-53
	SPECIALTIES WORK	24	100%	0%	24-Aug-26	20-Sep-26	26-Oct-26	22-Nov-26	58,495.83	0.00	58,495.83	-53
	TESTING & COMMISSIONING	46	0%	0%	18-Nov-26	02-Jan-27	17-Feb-27	15-Apr-27	0.00	0.00	0.00	-85
	DAMMAM	245	48.19%	35.08%	03-Mar-26	29-Dec-26	04-Mar-26 A	14-Apr-27	4,772,983.34	3,474,412.25	9,904,307.16	-87
	MOBILIZATION	25	0%	0%	03-Mar-26	04-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
	ENGINEERING	179	0%	0%	09-Mar-26	07-Jul-26	08-Mar-26 A	28-Jan-27	0.00	0.00	0.00	-175
	PROCUREMENT	183	0%	0%	21-May-26	08-Nov-26	04-Apr-26 A	13-Feb-27	0.00	0.00	0.00	-83
	CONSTRUCTION PHASE	240	48.19%	35.08%	16-Apr-26	29-Dec-26	04-Apr-26 A	08-Apr-27	4,772,983.34	3,474,412.25	9,904,307.16	-82
	SITE WORKS	240	41.67%	31.7%	16-Apr-26	29-Dec-26	04-Apr-26 A	08-Apr-27	3,627,240.60	2,759,479.99	8,704,943.25	-82
	EARTH WORKS	66	100%	100%	16-Apr-26	31-May-26	04-Apr-26 A	13-Aug-26 A	947,872.24	947,872.24	947,872.24	-63
	LANDSCAPE WORKS	223	34.8%	22.77%	23-May-26	29-Dec-26	19-May-26 A	08-Apr-27	2,679,368.36	1,753,114.43	7,698,577.68	-82
	PLAYGROUND AREA	213	69.28%	53.64%	23-May-26	08-Dec-26	19-May-26 A	28-Mar-27	913,960.35	707,562.27	1,319,195.08	-90
	FOOTBALL PLAYGROUND	205	87.38%	35%	23-May-26	11-Nov-26	19-May-26 A	18-Mar-27	276,866.54	110,897.50	316,849.99	-105
	PADEL PLAYGROUND	184	70%	70%	07-Jun-26	11-Nov-26	19-May-26 A	18-Mar-27	163,788.80	163,788.80	233,984.00	-105
	BASKETBALL PLAYGROUND	171	42.32%	70%	15-Jun-26	21-Nov-26	19-May-26 A	28-Mar-27	136,788.67	226,230.90	323,187.00	-105
	PADEL FENCE	153	0%	30%	22-Nov-26	08-Dec-26	08-Aug-26 A	05-Nov-26	0.00	24,860.73	82,869.08	28
	CURBSTOEN/INTERLOCK	62	92.88%	50.17%	12-Aug-26	01-Oct-26	10-Aug-26 A	30-Nov-26	336,516.34	181,784.34	362,305.01	-51
	AIR DOME	184	33.89%	11.91%	14-Jul-26	24-Nov-26	14-Jul-26 A	08-Apr-27	1,654,201.74	581,544.30	4,881,359.87	-112
	CIVIL WORKS	113	84.13%	29.58%	14-Jul-26	04-Oct-26	14-Jul-26 A	25-Nov-26	1,654,201.74	581,544.30	1,966,294.68	-45
	MECHANICAL WORKS	33	0%	0%	29-Sep-26	05-Nov-26	30-Jan-27	09-Mar-27	0.00	0.00	1,233,296.81	-105
	ELECTRICAL WORKS	39	0%	0%	11-Oct-26	24-Nov-26	10-Feb-27	31-Mar-27	0.00	0.00	1,513,591.54	-105
	FINISHES WORKS	29	0%	0%	31-Oct-26	22-Nov-26	03-Mar-27	08-Apr-27	0.00	0.00	168,176.84	-114
	IRRIGATION NETWORK	46	23.45%	73.86%	27-Sep-26	14-Oct-26	24-Aug-26 A	11-Feb-27	35,746.67	112,570.94	152,414.87	-103
	NATURAL GROUND	30	0%	0%	07-Oct-26	10-Nov-26	14-Oct-26	17-Nov-26	0.00	0.00	191,740.00	-6
	PLANTING	23	0%	0%	15-Oct-26	10-Nov-26	13-Feb-27	15-Mar-27	0.00	0.00	347,251.46	-103
	WALKING/BIKE PATHS	10	0%	100%	11-Nov-26	22-Nov-26	19-Jul-26 A	16-Sep-26 A	0.00	336,345.00	336,345.00	56
	GENERAL/FURNITURE	159	16.05%	3.21%	07-Sep-26	29-Dec-26	20-Sep-26 A	06-Apr-27	75,459.60	15,091.92	470,271.40	-80
	PARKING	145	0%	100%	02-Dec-26	19-Dec-26	18-Jul-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	77
	TOILET/SERVICE BUILDING	110	95.53%	59.61%	01-Jun-26	11-Oct-26	23-May-26 A	21-Nov-26	1,145,742.74	714,932.25	1,199,363.91	-35
	STRUCTURE WORKS	97	100%	100%	01-Jun-26	21-Jul-26	23-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-10
	MASONARY WORK	5	100%	100%	30-Jun-26	05-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
	THERMAL & MOISTER PROTECTION	23	100%	90.43%	22-Jul-26	15-Aug-26	25-Aug-26 A	07-Oct-26	34,698.32	31,376.86	34,698.32	-45
	MECHANICAL WORK	46	100%	57.58%	30-Jul-26	20-Sep-26	12-Jul-26 A	31-Oct-26	264,673.10	152,401.60	264,673.10	-34
	ELECTRICAL WORKS	110	86.14%	53.29%	22-Jul-26	11-Oct-26	14-Jul-26 A	21-Nov-26	333,377.65	206,217.55	386,998.82	-35
	DOORS/WINDOWS	29	100%	11.43%	22-Jul-26	20-Sep-26	17-Sep-26 A	01-Nov-26	68,245.12	7,799.44	68,245.12	-35
	METAL WORKS	16	100%	28.57%	18-Jul-26	26-Aug-26	05-Sep-26 A	19-Oct-26	13,649.02	3,899.72	13,649.02	-45
	FINISHING WORKS	70	100%	64.27%	30-Jul-26	17-Sep-26	17-Aug-26 A	29-Oct-26	166,130.96	106,764.34	166,130.96	-35
	SPECIALTIES WORK	30	100%	0%	22-Aug-26	24-Sep-26	04-Oct-26	07-Nov-26	58,495.83	0.00	58,495.83	-37
	TESTING & COMMISSIONING	49	0%	0%	15-Oct-26	29-Dec-26	13-Feb-27	14-Apr-27	0.00	0.00	0.00	-87
	PROJECT CLOSEOUT & DEMOBILIZATION	18	0%	0%	24-Dec-26	02-Jan-27	01-Apr-27	21-Apr-27	0.00	0.00	0.00	-90
	As-Built DWGs	17	0%	0%	24-Dec-26	31-Dec-26	01-Apr-27	20-Apr-27	0.00	0.00	0.00	-90
	Demobilization	4	0%	0%	30-Dec-26	02-Jan-27	18-Apr-27	21-Apr-27	0.00	0.00	0.00	-90

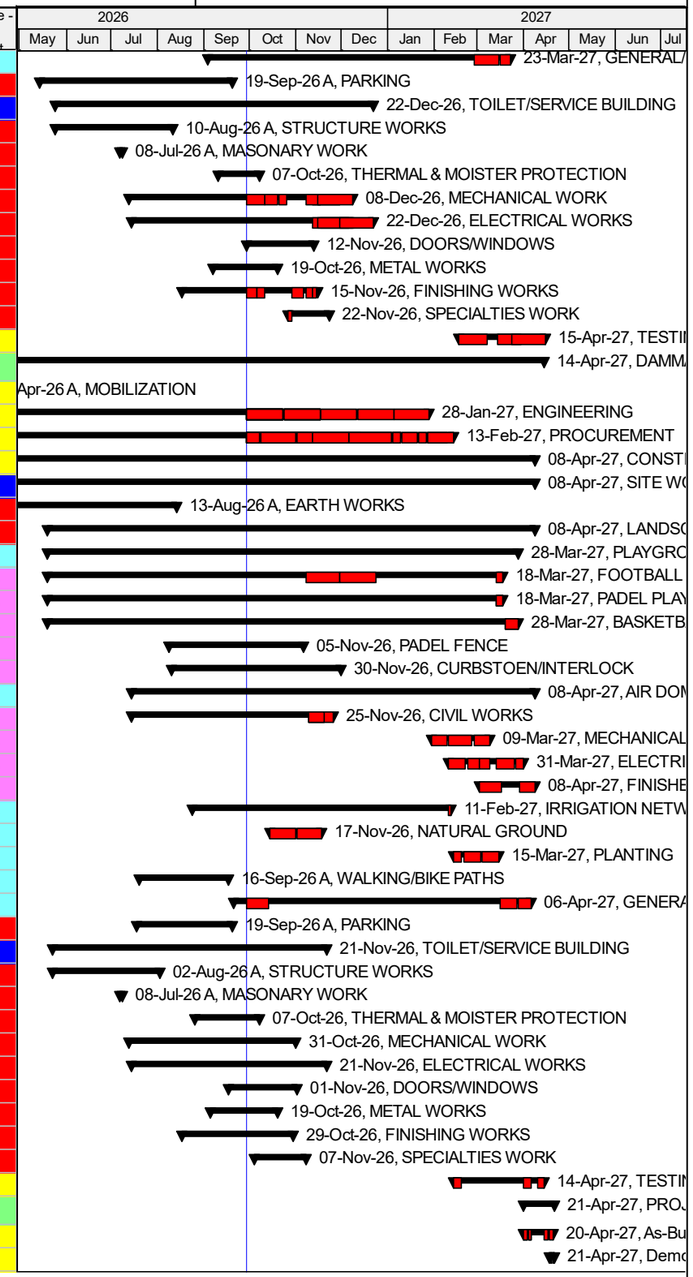

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
