
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oa		184	21.48%	3.35%	28-Mar-26	02-Jan-27	01-Jun-26 A	21-Apr-27	4,385,441.82	683,511.82	20,419,270.11	-90
KEY MILESTONES		172	0%	0%	28-Mar-26	02-Jan-27	29-Sep-26	21-Apr-27	0.00	0.00	0.00	-90
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	21-Apr-27	21-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		21-Apr-27	0.00	0.00	0.00	-90
CONTRACTUAL MILESTONE		161	0%	0%	28-Mar-26	02-Jan-27	29-Sep-26	08-Apr-27	0.00	0.00	0.00	-79
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		26-Dec-26		08-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-MS-1100	Completion of Engineering	0	100%	0%		28-Mar-26		29-Sep-26	0.00	0.00	0.00	-154
MLTX-02-005-MS-1130	Completion of Toilet Building	0	100%	0%		26-Sep-26		22-Nov-26	0.00	0.00	0.00	-49
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		02-Jan-27		18-Mar-27	0.00	0.00	0.00	-61
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		19-Nov-26		21-Mar-27	0.00	0.00	0.00	-100
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		04-Nov-26		02-Mar-27	0.00	0.00	0.00	-100
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		22-Dec-26		25-Oct-26	0.00	0.00	0.00	50
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		29-Dec-26		06-Apr-27	0.00	0.00	0.00	-80
ARAR		161	9.79%	2.63%	15-Apr-26	02-Jan-27	11-Jun-26 A	08-Apr-27	701,656.10	188,427.38	7,169,339.04	-79
ENGINEERING		120	0%	0%	15-Apr-26	21-Sep-26	29-Sep-26	15-Feb-27	0.00	0.00	0.00	-125
SHOP DRAWINGS		120	0%	0%	15-Apr-26	21-Sep-26	29-Sep-26	15-Feb-27	0.00	0.00	0.00	-125
SHOP DRAWINGS SUBMISSION		60	0%	0%	15-Apr-26	19-May-26	29-Sep-26	07-Dec-26	0.00	0.00	0.00	-169
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		60	0%	0%	15-Apr-26	19-May-26	29-Sep-26	07-Dec-26	0.00	0.00	0.00	-169
ELECTRICAL WORKS		60	0%	0%	15-Apr-26	19-May-26	29-Sep-26	07-Dec-26	0.00	0.00	0.00	-169
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	30	100%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	15-Apr-26	19-May-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-139
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	30	100%	0%	15-Apr-26	19-May-26	03-Nov-26	07-Dec-26	0.00	0.00	0.00	-169
SHOP DRAWINGS APPROVALS		120	0%	0%	03-May-26	21-Sep-26	29-Sep-26	15-Feb-27	0.00	0.00	0.00	-125
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		120	0%	0%	03-May-26	21-Sep-26	29-Sep-26	15-Feb-27	0.00	0.00	0.00	-125
ARCHITECTURE WORKS		30	0%	0%	03-May-26	09-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-124
MLTX-02-005-EM	Shop DWG Approval for Dome Internal Layout	30	100%	0%	03-May-26	09-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-124
AIR DOME SYSTEM		90	0%	0%	20-May-26	27-Jun-26	29-Sep-26	11-Jan-27	0.00	0.00	0.00	-169
MLTX-02-005-EM	Shop DWG Approval for Membrane Panel Layout	30	100%	0%	20-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Approval for Cable Tension Layout	30	100%	0%	20-May-26	27-Jun-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Approval for Airlock Door Details	30	100%	0%	20-May-26	27-Jun-26	03-Nov-26	07-Dec-26	0.00	0.00	0.00	-139
MLTX-02-005-EM	Shop DWG Approval for Emergency Exit Details	30	100%	0%	20-May-26	27-Jun-26	08-Dec-26	11-Jan-27	0.00	0.00	0.00	-169
SPORTS EQUIPMENT		30	0%	0%	20-May-26	27-Jun-26	12-Jan-27	15-Feb-27	0.00	0.00	0.00	-199
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	30	100%	0%	20-May-26	27-Jun-26	12-Jan-27	15-Feb-27	0.00	0.00	0.00	-199
ELECTRICAL WORKS		104	0%	0%	20-May-26	21-Sep-26	29-Sep-26	27-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	15	100%	0%	20-May-26	09-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Approval for Power Layout	30	100%	0%	02-Aug-26	05-Sep-26	08-Dec-26	11-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	14	100%	0%	06-Sep-26	21-Sep-26	12-Jan-27	27-Jan-27	0.00	0.00	0.00	-109
PROCUREMENT		118	0%	0%	19-May-26	19-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-100
SHORT LEAD ITEM		118	0%	0%	25-May-26	19-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-100
TOILET/SERVICE WORKS		29	0%	0%	09-Jun-26	04-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-75
LIGHTING FIXTURES		10	0%	0%	08-Jul-26	19-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8	Material Delivery for Lighting Fixtures	10	100%	0%	08-Jul-26	19-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-70
SWITCHES/SOCKETS		12	0%	0%	08-Jul-26	21-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8	PO for Switches/Sockets	5	100%	0%	08-Jul-26	13-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-70
MLTX-02-005-PR-8	Material Delivery for Switches/Sockets	7	100%	0%	14-Jul-26	21-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-70
DISTRIBUTION PANNELS		20	0%	0%	09-Jun-26	01-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-8	PO for Distribution Panels	5	100%	0%	09-Jun-26	14-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-8	Material Delivery for Distribution Panels	15	100%	0%	15-Jun-26	01-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-95
FURNITURES		29	0%	0%	02-Jul-26	04-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-8	PO for Furnitures	9	100%	0%	02-Jul-26	12-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-8	Material Delivery for Furnitures	20	100%	0%	13-Jul-26	04-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-75
PLAYGROUND WORKS		50	0%	0%	25-May-26	12-Sep-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-63
PVC MEMBRANE		21	0%	0%	24-Jun-26	18-Jul-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-82
MLTX-02-005-PR-8	Material Delivery for PVC Membrane	21	100%	0%	24-Jun-26	18-Jul-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-82
ARTIFICIAL TURF		12	0%	0%	20-Jul-26	02-Aug-26	24-Oct-26	05-Nov-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	Material Delivery for Artificial TURF	12	100%	0%	20-Jul-26	02-Aug-26	24-Oct-26	05-Nov-26	0.00	0.00	0.00	-81
RUBBER GRANULES		12	0%	0%	18-Jun-26	01-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-87
MLTX-02-005-PR-8	Material Delivery for Rubber Granules	12	100%	0%	18-Jun-26	01-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-87
PADEL GLASS		18	0%	0%	25-May-26	17-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-8	Material Delivery for Padel Glass	18	100%	0%	25-May-26	17-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-105
PADEL WIRE MESH/STEEL SETS		15	0%	0%	03-Jun-26	20-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-8	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	03-Jun-26	20-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-100
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	15-Jun-26	22-Jun-26	29-Sep-26	06-Oct-26	0.00	0.00	0.00	-90

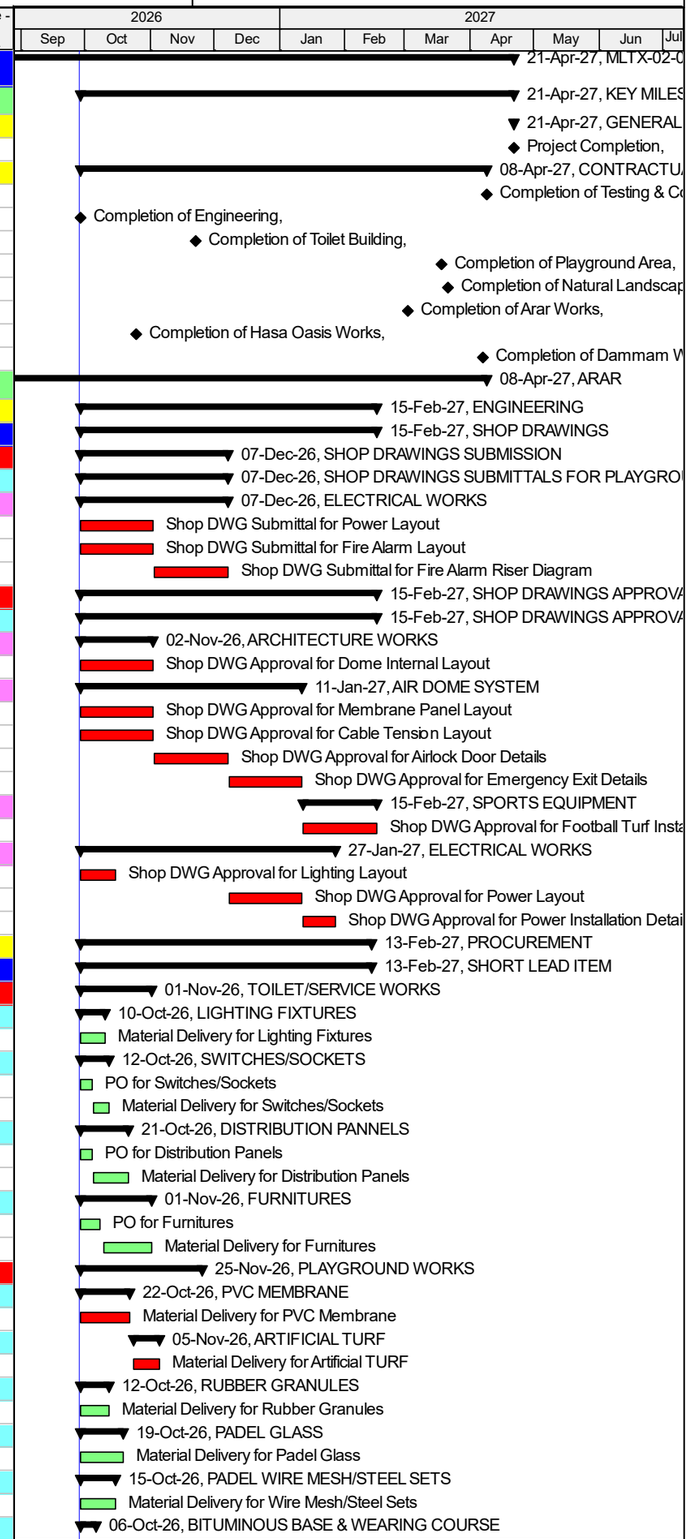

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for the Site	7	100%	0%	15-Jun-26	22-Jun-26	29-Sep-26	06-Oct-26	0.00	0.00	0.00	-90
INTERLOCKING PAVING		7	0%	0%	20-Jul-26	27-Jul-26	07-Oct-26	14-Oct-26	0.00	0.00	0.00	-67
MLTX-02-005-PR-9	Material Delivery for Interlocking Block Pavers	7	100%	0%	20-Jul-26	27-Jul-26	07-Oct-26	14-Oct-26	0.00	0.00	0.00	-67
MARKING PAINT		12	0%	0%	15-Jun-26	28-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	PO for Marking Paint	5	100%	0%	15-Jun-26	20-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	Material Delivery for Marking Paint	7	100%	0%	21-Jun-26	28-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-90
AIR DIFUSSERS/GRILLS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	PO for Air Difussers/Grills	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	Material Delivery for Air Difussers/Grills	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
GALVANIZED DUCTS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	PO for Galvanized Duct	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	Material Delivery for Galvanized Duct	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
EXHAUST FANS		20	0%	0%	02-Jul-26	25-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	PO for Exhaust Fans	5	100%	0%	02-Jul-26	07-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-9	Material Delivery for Exhaust Fans	15	100%	0%	08-Jul-26	25-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-75
DISTRIBUTION BOARDS		20	0%	0%	02-Jul-26	25-Jul-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	PO for Distribution Boards	5	100%	0%	02-Jul-26	07-Jul-26	17-Oct-26	21-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	Material Delivery for Distribution Boards	15	100%	0%	08-Jul-26	25-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-90
POWER CABLES		15	0%	0%	08-Jul-26	25-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	PO for Power Cables	5	100%	0%	08-Jul-26	13-Jul-26	22-Oct-26	27-Oct-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-9	Material Delivery for Power Cables	10	100%	0%	14-Jul-26	25-Jul-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-90
LIGHT FIXTURES		10	0%	0%	20-Jul-26	30-Jul-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-85
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	100%	0%	20-Jul-26	30-Jul-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-85
CCTV MATERIALS		50	0%	0%	20-Jul-26	12-Sep-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-63
MLTX-02-005-PR-9	PO for CCTV	5	100%	0%	20-Jul-26	25-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-60
MLTX-02-005-PR-9	Material Delivery for CCTV	15	100%	0%	26-Aug-26	12-Sep-26	09-Nov-26	25-Nov-26	0.00	0.00	0.00	-63
POWER OUTLETS/SWITCHES		15	0%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	15	100%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49
LANDSCAPE WORKS		118	0%	0%	02-Aug-26	19-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-100
PAVEMENT MARKING		15	0%	0%	02-Aug-26	18-Aug-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	02-Aug-26	06-Aug-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-49
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	10	100%	0%	08-Aug-26	18-Aug-26	05-Oct-26	15-Oct-26	0.00	0.00	0.00	-49
TRAFFIC SIGNS		14	0%	0%	03-Oct-26	18-Oct-26	05-Oct-26	20-Oct-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-9	PO for Traffic Signs	5	0%	0%	03-Oct-26	07-Oct-26	05-Oct-26	10-Oct-26	0.00	0.00	0.00	-2
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	9	0%	0%	08-Oct-26	18-Oct-26	11-Oct-26	20-Oct-26	0.00	0.00	0.00	-2
AGRICULTURE SOIL		17	0%	0%	20-Sep-26	10-Oct-26	21-Jan-27	09-Feb-27	0.00	0.00	0.00	-105
MLTX-02-005-PR-9	PO for Agriculture Soil	5	100%	0%	20-Sep-26	26-Sep-26	21-Jan-27	26-Jan-27	0.00	0.00	0.00	-105
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	12	16.67%	0%	27-Sep-26	10-Oct-26	27-Jan-27	09-Feb-27	0.00	0.00	0.00	-105
TRACK SURFACE		10	0%	0%	08-Sep-26	19-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-105
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	08-Sep-26	19-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-105
GRASS/TREES		15	0%	0%	03-Oct-26	19-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	15	0%	0%	03-Oct-26	19-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-100
LONG LEAD ITEM		88	0%	0%	19-May-26	01-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-110
PLAYGROUND WORKS		88	0%	0%	19-May-26	01-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-110
STEEL TENSION CABLES		65	0%	0%	19-May-26	09-Aug-26	29-Sep-26	13-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-8	PO for Steel Tension Cables	8	100%	0%	19-May-26	31-May-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Fabrication for Steel Tension Cables	20	100%	0%	01-Jun-26	23-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	30	100%	0%	28-Jun-26	01-Aug-26	01-Nov-26	05-Dec-26	0.00	0.00	0.00	-107
MLTX-02-005-PR-9	Staging time	7	100%	0%	02-Aug-26	09-Aug-26	06-Dec-26	13-Dec-26	0.00	0.00	0.00	-107
EMERGENCY DOORS		60	0%	0%	24-Jun-26	01-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	PO for Emergency Doors	10	100%	0%	24-Jun-26	05-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Fabrication for Emergency Doors	20	100%	0%	06-Jul-26	28-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	25	100%	0%	29-Jul-26	26-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-110
PRESSURE UNITS		60	0%	0%	24-Jun-26	01-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	PO for Pressure Units	10	100%	0%	24-Jun-26	05-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Fabrication for Pressure Units	20	100%	0%	06-Jul-26	28-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	100%	0%	29-Jul-26	26-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-110
AIR LOCK DOORS		60	0%	0%	24-Jun-26	01-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	PO for Lock Doors	10	100%	0%	24-Jun-26	05-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	100%	0%	06-Jul-26	28-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	100%	0%	29-Jul-26	26-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-110

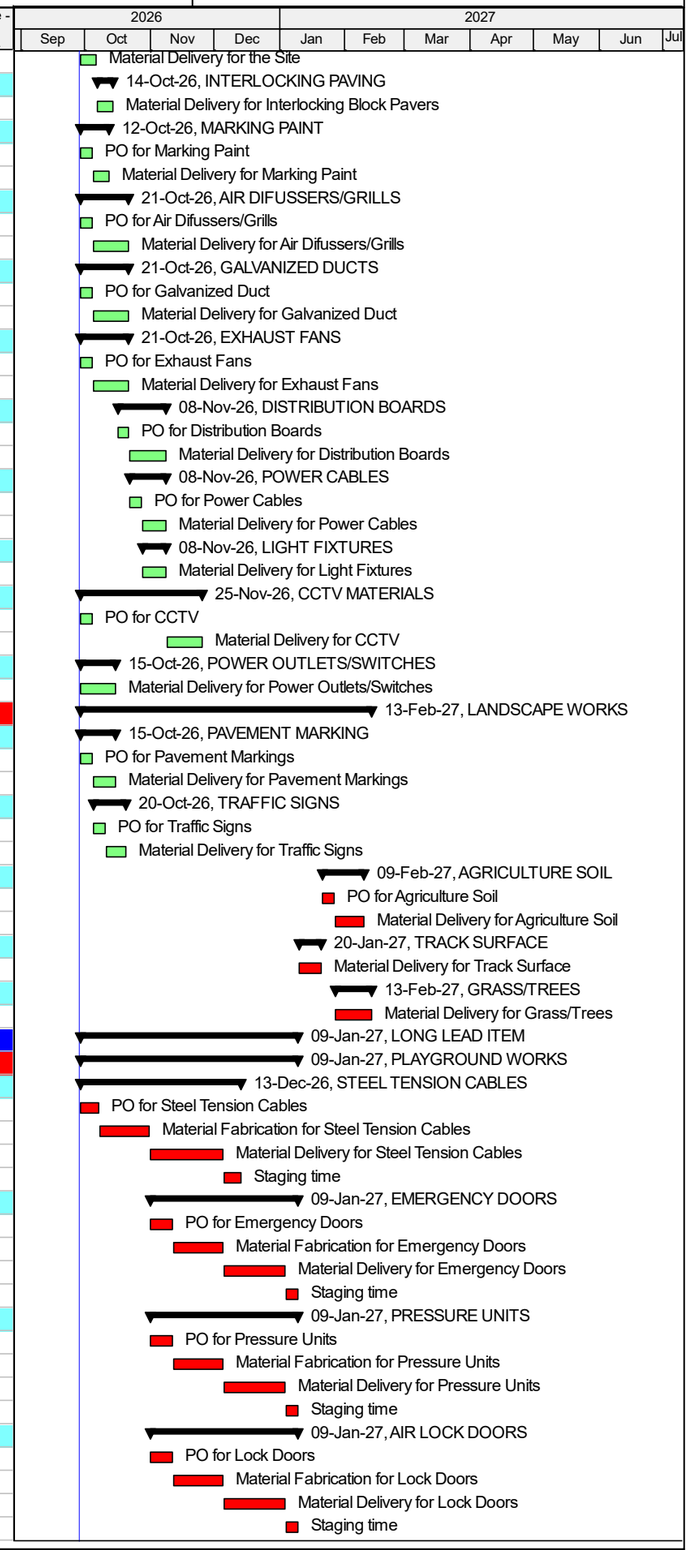

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CONSTRUCTION PHASE		151	9.79%	2.63%	23-Jul-26	02-Jan-27	11-Jun-26 A	23-Mar-27	701,656.10	188,427.38	7,169,339.04	-65
SITE WORKS		151	0%	2.81%	29-Sep-26	02-Jan-27	11-Jun-26 A	23-Mar-27	0.00	181,927.84	6,467,682.94	-65
LANDSCAPE WORKS		151	0%	2.83%	29-Sep-26	02-Jan-27	11-Jun-26 A	23-Mar-27	0.00	181,927.84	6,426,737.61	-65
PLAYGROUND AREA		140	0%	0%	21-Oct-26	02-Jan-27	29-Sep-26	15-Mar-27	0.00	0.00	701,358.24	-58
FOOTBALL PLAYGROUND		102	0%	0%	21-Oct-26	01-Dec-26	07-Nov-26	06-Mar-27	0.00	0.00	205,952.49	-80
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	21	0%	0%	21-Oct-26	14-Nov-26	07-Nov-26	30-Nov-26	0.00	0.00	158,424.99	-14
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	15	0%	0%	15-Nov-26	01-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	31,685.00	-80
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	10	0%	0%	15-Nov-26	25-Nov-26	18-Jan-27	28-Jan-27	0.00	0.00	15,842.50	-55
PADEL PLAYGROUND		15	0%	0%	15-Nov-26	01-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	70,195.20	-80
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	15-Nov-26	01-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	58,496.00	-80
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	10	0%	0%	15-Nov-26	25-Nov-26	16-Feb-27	28-Feb-27	0.00	0.00	11,699.20	-80
BASKETBALL PLAYGROUND		20	0%	0%	15-Nov-26	07-Dec-26	16-Feb-27	15-Mar-27	0.00	0.00	96,956.10	-80
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	80,796.75	-80
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	10	0%	0%	26-Nov-26	07-Dec-26	01-Mar-27	15-Mar-27	0.00	0.00	16,159.35	-80
PADEL FENCE		10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	147,733.78	60
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	7	0%	0%	08-Dec-26	15-Dec-26	29-Sep-26	06-Oct-26	0.00	0.00	4,143.45	60
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	33,147.63	60
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	29-Sep-26	10-Oct-26	0.00	0.00	16,573.82	60
MLTX-02-005-CI	Install of Fence Gates	2	0%	0%	08-Dec-26	09-Dec-26	29-Sep-26	30-Sep-26	0.00	0.00	93,868.88	60
CURBSTOEN/INTERLOCK		20	0%	0%	10-Dec-26	02-Jan-27	17-Oct-26	08-Nov-26	0.00	0.00	180,520.67	47
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	10-Dec-26	02-Jan-27	17-Oct-26	08-Nov-26	0.00	0.00	180,520.67	47
AIR DOME		147	0%	0%	21-Oct-26	09-Dec-26	29-Sep-26	23-Mar-27	0.00	0.00	4,299,815.57	-85
CIVIL WORKS		25	0%	0%	21-Oct-26	01-Nov-26	29-Sep-26	27-Oct-26	0.00	0.00	1,384,750.38	4
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	29-Sep-26	10-Oct-26	0.00	0.00	936,278.81	19
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	17-Oct-26	27-Oct-26	0.00	0.00	448,471.57	4
MECHANICAL WORKS		76	0%	0%	02-Nov-26	16-Nov-26	28-Oct-26	24-Jan-27	0.00	0.00	1,233,296.81	-59
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	02-Nov-26	12-Nov-26	28-Oct-26	08-Nov-26	0.00	0.00	728,766.30	4
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	02-Nov-26	16-Nov-26	10-Jan-27	24-Jan-27	0.00	0.00	336,353.67	-59
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	7	0%	0%	02-Nov-26	09-Nov-26	10-Jan-27	17-Jan-27	0.00	0.00	168,176.84	-59
ELECTRICAL WORKS		20	0%	0%	17-Nov-26	09-Dec-26	25-Jan-27	16-Feb-27	0.00	0.00	1,513,591.54	-59
MLTX-02-005-CI	Light Fixture Works (Air Dome)	6	0%	0%	17-Nov-26	23-Nov-26	25-Jan-27	31-Jan-27	0.00	0.00	224,235.78	-59
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	10	0%	0%	17-Nov-26	28-Nov-26	25-Jan-27	04-Feb-27	0.00	0.00	168,176.84	-59
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	25-Jan-27	16-Feb-27	0.00	0.00	168,176.84	-59
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	25-Jan-27	16-Feb-27	0.00	0.00	504,530.51	-59
MLTX-02-005-CI	Control System Installation (Air Dome)	13	0%	0%	17-Nov-26	01-Dec-26	28-Jan-27	11-Feb-27	0.00	0.00	448,471.57	-62
FINISHES WORKS		49	0%	0%	14-Nov-26	09-Dec-26	21-Jan-27	23-Mar-27	0.00	0.00	168,176.84	-85
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	3	0%	0%	14-Nov-26	16-Nov-26	21-Jan-27	24-Jan-27	0.00	0.00	112,117.89	-59
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	7	0%	0%	02-Dec-26	09-Dec-26	16-Mar-27	23-Mar-27	0.00	0.00	56,058.95	-85
IRRIGATION NETWORK		45	0%	33.89%	08-Oct-26	22-Oct-26	10-Sep-26 A	16-Feb-27	0.00	16,492.59	48,667.04	-100
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	4	0%	70%	08-Oct-26	12-Oct-26	10-Sep-26 A	03-Oct-26	0.00	16,492.59	23,560.84	8
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	20-Oct-26	22-Oct-26	14-Feb-27	16-Feb-27	0.00	0.00	25,106.20	-100
NATURAL GROUND		81	0%	0%	13-Oct-26	22-Oct-26	15-Nov-26	16-Feb-27	0.00	0.00	191,740.00	-100
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	20-Oct-26	22-Oct-26	14-Feb-27	16-Feb-27	0.00	0.00	126,740.00	-100
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	13-Oct-26	19-Oct-26	15-Nov-26	21-Nov-26	0.00	0.00	65,000.00	-28
PLANTING		24	0%	0%	24-Oct-26	19-Nov-26	17-Feb-27	21-Mar-27	0.00	0.00	347,251.46	-100
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	10	0%	0%	24-Oct-26	03-Nov-26	17-Feb-27	01-Mar-27	0.00	0.00	104,175.44	-100
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	17-Nov-26	19-Nov-26	18-Mar-27	21-Mar-27	0.00	0.00	141,732.50	-100
MLTX-02-005-CN-1	Placement and Fixation of Trees	11	0%	0%	04-Nov-26	16-Nov-26	02-Mar-27	17-Mar-27	0.00	0.00	101,343.52	-100
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	165,435.26	367,633.90	57
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	84,399.35	187,554.12	57
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	29-Sep-26	0.00	81,035.90	180,079.78	57
GENERAL/FURNITURE		27	0%	0%	29-Sep-26	02-Jan-27	29-Sep-26	29-Oct-26	0.00	0.00	470,271.40	55
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	05-Dec-26	09-Dec-26	29-Sep-26	04-Oct-26	0.00	0.00	93,594.00	57
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	26-Dec-26	02-Jan-27	22-Oct-26	29-Oct-26	0.00	0.00	9,749.30	55
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	05-Dec-26	12-Dec-26	29-Sep-26	06-Oct-26	0.00	0.00	17,274.79	57
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	40,307.84	57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	32,757.76	57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	13-Dec-26	20-Dec-26	07-Oct-26	14-Oct-26	0.00	0.00	12,869.04	57
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	21-Dec-26	02-Jan-27	15-Oct-26	27-Oct-26	0.00	0.00	12,186.67	57
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	7	0%	0%	29-Sep-26	06-Oct-26	29-Sep-26	06-Oct-26	0.00	0.00	75,459.60	0
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	0%	10-Dec-26	24-Dec-26	07-Oct-26	21-Oct-26	0.00	0.00	176,072.40	55
PARKING		3	0%	0%	14-Dec-26	16-Dec-26	29-Sep-26	01-Oct-26	0.00	0.00	40,945.33	65
MLTX-02-005-CN-10	Interlock Installation (8 Cm) for Parking Area (Including	3	0%	0%	14-Dec-26	16-Dec-26	29-Sep-26	01-Oct-26	0.00	0.00	40,945.33	65
TOILET/SERVICE BUILDING		54	100%	0.93%	23-Jul-26	26-Sep-26	28-Sep-26 A	30-Nov-26	701,656.10	6,499.54	701,656.10	-56

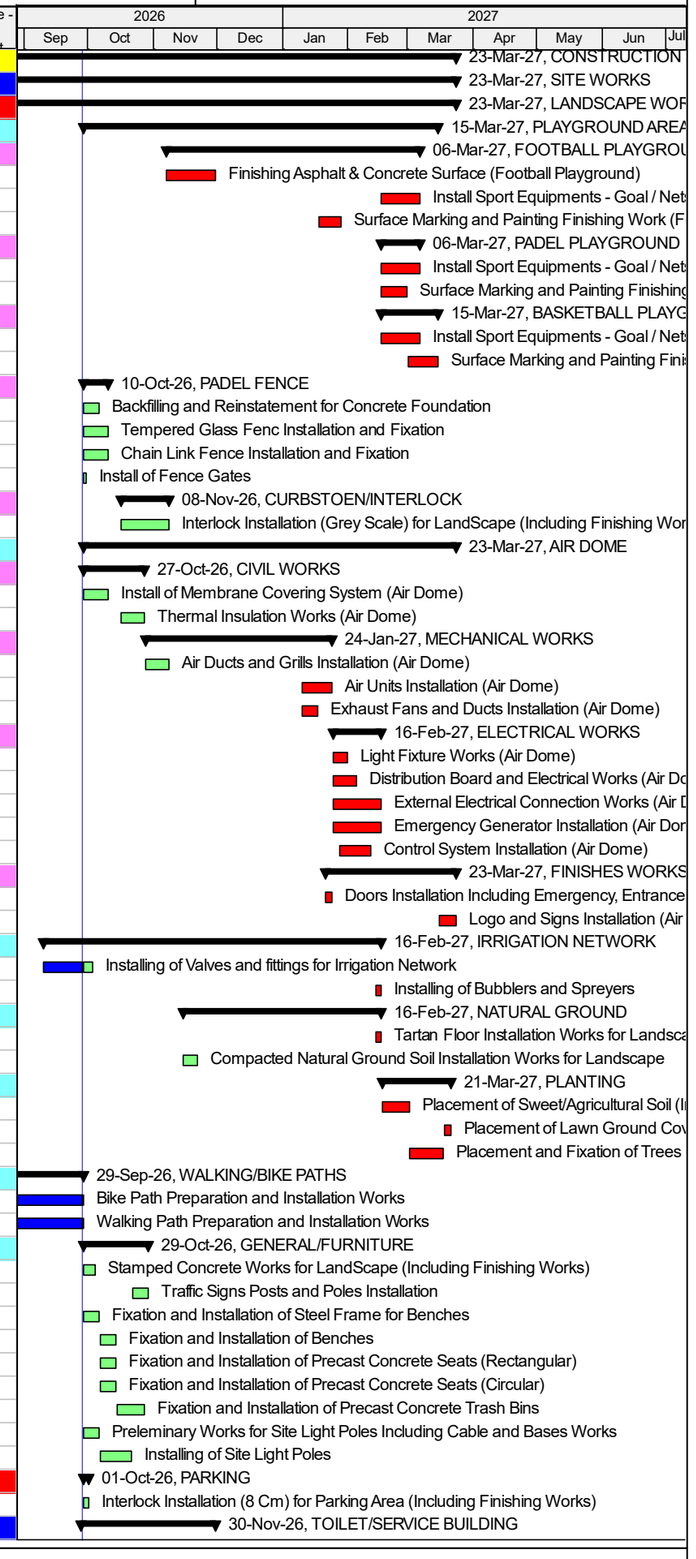

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
THERMAL & MOISTER PROTECTION		19	100%	0%	30-Jul-26	20-Aug-26	29-Sep-26	20-Oct-26	32,592.46	0.00	32,592.46	-51
MLTX-02-005-CN-110	Preparing Surface and Preliminary Works for Roofing and	5	100%	0%	06-Aug-26	11-Aug-26	06-Oct-26	11-Oct-26	11,071.52	0.00	11,071.52	-51
MLTX-02-005-CN-110	Finalize Water Proofing Works for Toilets	6	100%	0%	30-Jul-26	05-Aug-26	29-Sep-26	05-Oct-26	4,913.66	0.00	4,913.66	-51
MLTX-02-005-CN-110	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	0%	12-Aug-26	20-Aug-26	12-Oct-26	20-Oct-26	16,607.28	0.00	16,607.28	-51
MECHANICAL WORK		39	100%	2.87%	09-Aug-26	21-Sep-26	28-Sep-26 A	12-Nov-26	226,224.75	6,499.54	226,224.75	-44
HVAC SYSTEM		3	100%	0%	17-Sep-26	20-Sep-26	09-Nov-26	11-Nov-26	14,623.96	0.00	14,623.96	-44
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	100%	0%	17-Sep-26	20-Sep-26	09-Nov-26	11-Nov-26	14,623.96	0.00	14,623.96	-44
WATER SUPPLY SYSTEM		32	100%	4.59%	15-Aug-26	13-Sep-26	28-Sep-26 A	04-Nov-26	141,495.15	6,499.54	141,495.15	-44
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	0%	15-Aug-26	17-Aug-26	29-Sep-26	01-Oct-26	25,998.40	0.00	25,998.40	-38
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	100%	0%	02-Sep-26	09-Sep-26	08-Oct-26	15-Oct-26	48,746.52	0.00	48,746.52	-30
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	10%	24-Aug-26	01-Sep-26	28-Sep-26 A	07-Oct-26	64,995.36	6,499.54	64,995.36	-30
MLTX-02-005-CN-1	Installing of Water Heater	4	100%	0%	09-Sep-26	13-Sep-26	01-Nov-26	04-Nov-26	1,754.87	0.00	1,754.87	-44
SEWER/DRAINAGE SYSTEM		32	100%	0%	09-Aug-26	13-Sep-26	29-Sep-26	04-Nov-26	68,155.77	0.00	68,155.77	-44
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	15-Aug-26	18-Aug-26	05-Oct-26	08-Oct-26	14,217.67	0.00	14,217.67	-43
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	24-Aug-26	25-Aug-26	15-Oct-26	17-Oct-26	10,358.68	0.00	10,358.68	-44
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	09-Aug-26	13-Aug-26	29-Sep-26	04-Oct-26	12,186.63	0.00	12,186.63	-43
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	01-Nov-26	04-Nov-26	31,392.79	0.00	31,392.79	-44
FIRE PROTECTION		2	100%	0%	20-Sep-26	21-Sep-26	11-Nov-26	12-Nov-26	1,949.87	0.00	1,949.87	-44
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	20-Sep-26	21-Sep-26	11-Nov-26	12-Nov-26	1,949.87	0.00	1,949.87	-44
ELECTRICAL WORKS		19	100%	0%	17-Sep-26	26-Sep-26	09-Nov-26	30-Nov-26	180,781.27	0.00	180,781.27	-56
FIXTURE WORKS		19	100%	0%	17-Sep-26	26-Sep-26	09-Nov-26	30-Nov-26	180,781.27	0.00	180,781.27	-56
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	100%	0%	17-Sep-26	22-Sep-26	09-Nov-26	14-Nov-26	102,367.69	0.00	102,367.69	-44
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	20-Sep-26	24-Sep-26	11-Nov-26	15-Nov-26	6,239.59	0.00	6,239.59	-44
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	100%	0%	20-Sep-26	24-Sep-26	11-Nov-26	15-Nov-26	7,085.10	0.00	7,085.10	-44
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	17-Sep-26	20-Sep-26	09-Nov-26	11-Nov-26	6,824.51	0.00	6,824.51	-44
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	100%	0%	21-Sep-26	26-Sep-26	12-Nov-26	16-Nov-26	34,317.53	0.00	34,317.53	-44
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	20-Sep-26	24-Sep-26	11-Nov-26	15-Nov-26	14,259.43	0.00	14,259.43	-44
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	100%	0%	17-Sep-26	24-Sep-26	09-Nov-26	15-Nov-26	2,437.33	0.00	2,437.33	-44
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	17-Sep-26	21-Sep-26	26-Nov-26	30-Nov-26	7,250.09	0.00	7,250.09	-59
DOORS/WINDOWS		42	100%	0%	28-Jul-26	26-Sep-26	29-Sep-26	16-Nov-26	68,245.12	0.00	68,245.12	-44
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	28-Jul-26	29-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-53
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	0%	28-Jul-26	30-Jul-26	29-Sep-26	01-Oct-26	7,799.44	0.00	7,799.44	-53
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	7	100%	0%	17-Sep-26	26-Sep-26	09-Nov-26	16-Nov-26	1,949.86	0.00	1,949.86	-44
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	100%	0%	17-Sep-26	26-Sep-26	09-Nov-26	16-Nov-26	5,849.58	0.00	5,849.58	-44
METAL WORKS		25	100%	0%	23-Jul-26	27-Aug-26	29-Sep-26	27-Oct-26	9,749.30	0.00	9,749.30	-51
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	4	100%	0%	24-Aug-26	27-Aug-26	24-Oct-26	27-Oct-26	5,849.58	0.00	5,849.58	-51
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	23-Jul-26	27-Jul-26	29-Sep-26	03-Oct-26	3,899.72	0.00	3,899.72	-57
FINISHING WORKS		38	100%	0%	12-Aug-26	20-Sep-26	29-Sep-26	11-Nov-26	125,567.37	0.00	125,567.37	-44
FLOOR FINISHES		34	100%	0%	12-Aug-26	20-Sep-26	04-Oct-26	11-Nov-26	17,159.03	0.00	17,159.03	-44
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	12-Aug-26	13-Aug-26	04-Oct-26	05-Oct-26	11,894.39	0.00	11,894.39	-44
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	15-Aug-26	18-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-44
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	17-Sep-26	20-Sep-26	09-Nov-26	11-Nov-26	1,169.94	0.00	1,169.94	-44
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	19-Aug-26	23-Aug-26	11-Oct-26	14-Oct-26	1,169.88	0.00	1,169.88	-44
WALL FINISHES		34	100%	0%	18-Aug-26	19-Sep-26	03-Oct-26	10-Nov-26	93,437.44	0.00	93,437.44	-44
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	26-Aug-26	31-Aug-26	11-Oct-26	15-Oct-26	2,275.00	0.00	2,275.00	-38
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	100%	0%	09-Sep-26	16-Sep-26	01-Nov-26	08-Nov-26	13,649.02	0.00	13,649.02	-44
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	22-Aug-26	23-Aug-26	21-Oct-26	22-Oct-26	8,150.24	0.00	8,150.24	-51
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	0%	18-Aug-26	25-Aug-26	03-Oct-26	10-Oct-26	35,825.58	0.00	35,825.58	-38
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	01-Sep-26	08-Sep-26	24-Oct-26	31-Oct-26	31,197.60	0.00	31,197.60	-44
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	0%	17-Sep-26	19-Sep-26	09-Nov-26	10-Nov-26	2,340.00	0.00	2,340.00	-44
CELLING FINISHES		10	100%	0%	12-Aug-26	03-Sep-26	29-Sep-26	10-Oct-26	14,970.90	0.00	14,970.90	-30
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	0%	12-Aug-26	15-Aug-26	29-Sep-26	01-Oct-26	5,771.52	0.00	5,771.52	-40
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	0%	01-Sep-26	03-Sep-26	07-Oct-26	10-Oct-26	3,427.86	0.00	3,427.86	-30
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	24-Aug-26	31-Aug-26	29-Sep-26	06-Oct-26	5,771.52	0.00	5,771.52	-30
SPECIALTIES WORK		24	100%	0%	26-Aug-26	22-Sep-26	18-Oct-26	14-Nov-26	58,495.83	0.00	58,495.83	-44
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	100%	0%	09-Sep-26	12-Sep-26	01-Nov-26	03-Nov-26	24,373.26	0.00	24,373.26	-44
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	26-Aug-26	31-Aug-26	18-Oct-26	22-Oct-26	14,623.96	0.00	14,623.96	-44
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	100%	0%	20-Sep-26	22-Sep-26	11-Nov-26	14-Nov-26	19,498.61	0.00	19,498.61	-44
TESTING & COMMISSIONING		40	0%	0%	24-Oct-26	26-Dec-26	17-Feb-27	08-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	24-Mar-27	08-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	10	0%	0%	24-Oct-26	03-Nov-26	17-Feb-27	01-Mar-27	0.00	0.00	0.00	-100
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	11	0%	0%	24-Oct-26	04-Nov-26	17-Feb-27	02-Mar-27	0.00	0.00	0.00	-100
HASA OASIS		174	26.07%	5.77%	30-Apr-26	02-Jan-27	01-Jun-26 A	15-Apr-27	1,750,072.60	386,957.04	6,711,908.76	-85
ENGINEERING		42	0%	0%	30-Apr-26	20-Sep-26	29-Sep-26	16-Nov-26	0.00	0.00	0.00	-48

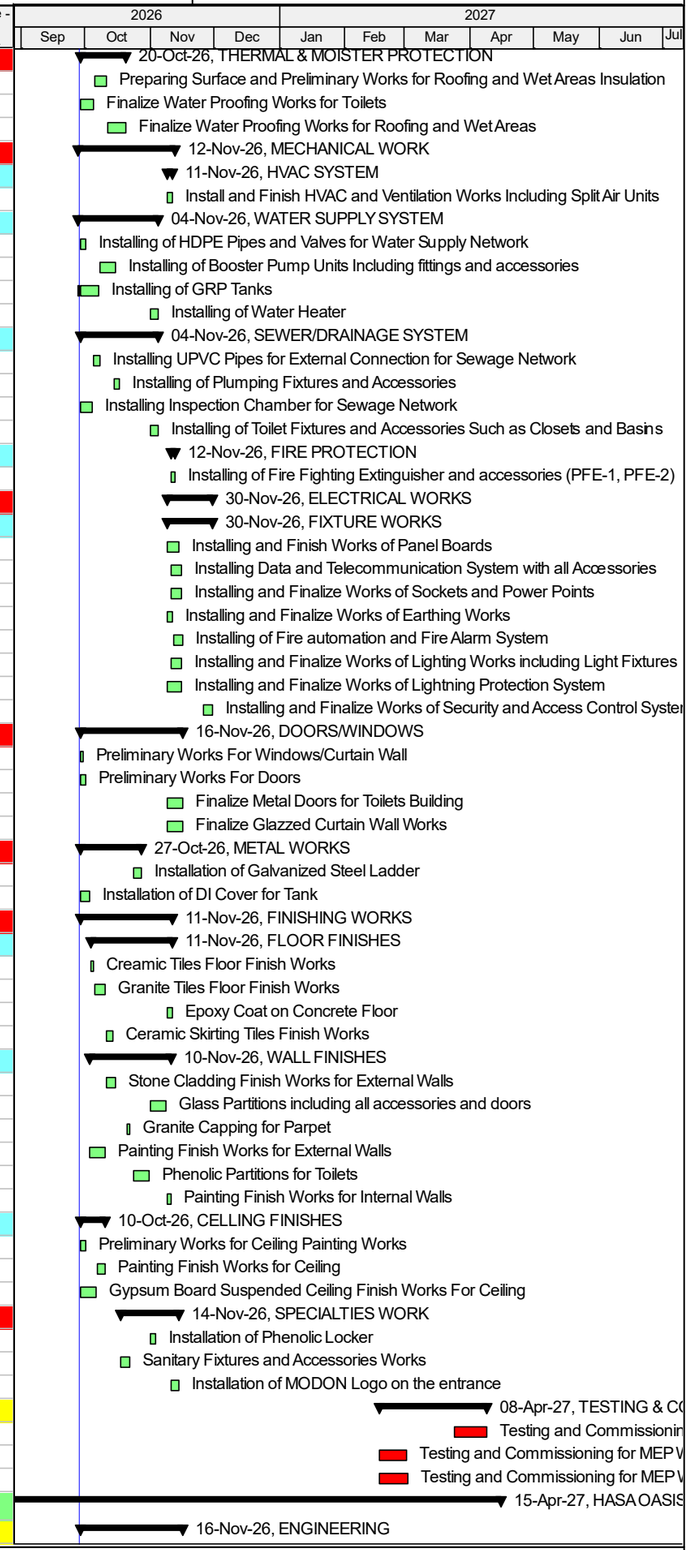

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SHOP DRAWINGS		42	0%	0%	30-Apr-26	20-Sep-26	29-Sep-26	16-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS SUBMISSION		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MECHANCAL WORKS		21	0%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for HVAC Plan	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
ELECTRICAL WORKS		30	0%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Lighting Layout	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Power Layout	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Power Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	03-Aug-26	06-Sep-26	29-Sep-26	02-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	0%	03-Aug-26	26-Aug-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-48
SHOP DRAWINGS APPROVALS		42	0%	0%	30-Apr-26	20-Sep-26	29-Sep-26	16-Nov-26	0.00	0.00	0.00	-48
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		42	0%	0%	30-Apr-26	20-Sep-26	29-Sep-26	16-Nov-26	0.00	0.00	0.00	-48
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MECHANCAL WORKS		21	0%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
ELECTRICAL WORKS		21	0%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Power Layout	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	21	100%	0%	27-Aug-26	20-Sep-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-48
PROCUREMENT		118	0%	0%	20-May-26	20-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-99
SHORT LEAD ITEM		118	0%	0%	25-May-26	20-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-99
TOILET/SERVICE WORKS		29	0%	0%	10-Jun-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
LIGHTING FIXTURES		10	0%	0%	09-Jul-26	20-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	09-Jul-26	20-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-69
SWITCHES/SOCKETS		12	0%	0%	09-Jul-26	22-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	09-Jul-26	14-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	15-Jul-26	22-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-69
DISTRIBUTION PANNELS		20	0%	0%	10-Jun-26	02-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	10-Jun-26	15-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	16-Jun-26	02-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-94
FURNITURES		29	0%	0%	04-Jul-26	05-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	04-Jul-26	13-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	14-Jul-26	05-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-74
PLAYGROUND WORKS		50	0%	0%	25-May-26	19-Aug-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-83
PVC MEMBRANE		4	0%	0%	25-May-26	01-Jun-26	29-Sep-26	03-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	4	100%	0%	25-May-26	01-Jun-26	29-Sep-26	03-Oct-26	0.00	0.00	0.00	-105
ARTIFICIAL TURF		12	0%	0%	30-May-26	11-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	30-May-26	11-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-104
RUBBER GRANULES		12	0%	0%	20-Jun-26	02-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	20-Jun-26	02-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-86
PADEL GLASS		18	0%	0%	30-May-26	18-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	30-May-26	18-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-104
PADEL WIRE MESH/STEEL SETS		15	0%	0%	04-Jun-26	21-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	04-Jun-26	21-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-99
MARKING PAINT		12	0%	0%	16-Jun-26	29-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	16-Jun-26	21-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	22-Jun-26	29-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-89
AIR DIFUSSERS/GRILLS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74
GALVANIZED DUCTS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74
EXHAUST FANS		20	0%	0%	04-Jul-26	26-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	04-Jul-26	08-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-74

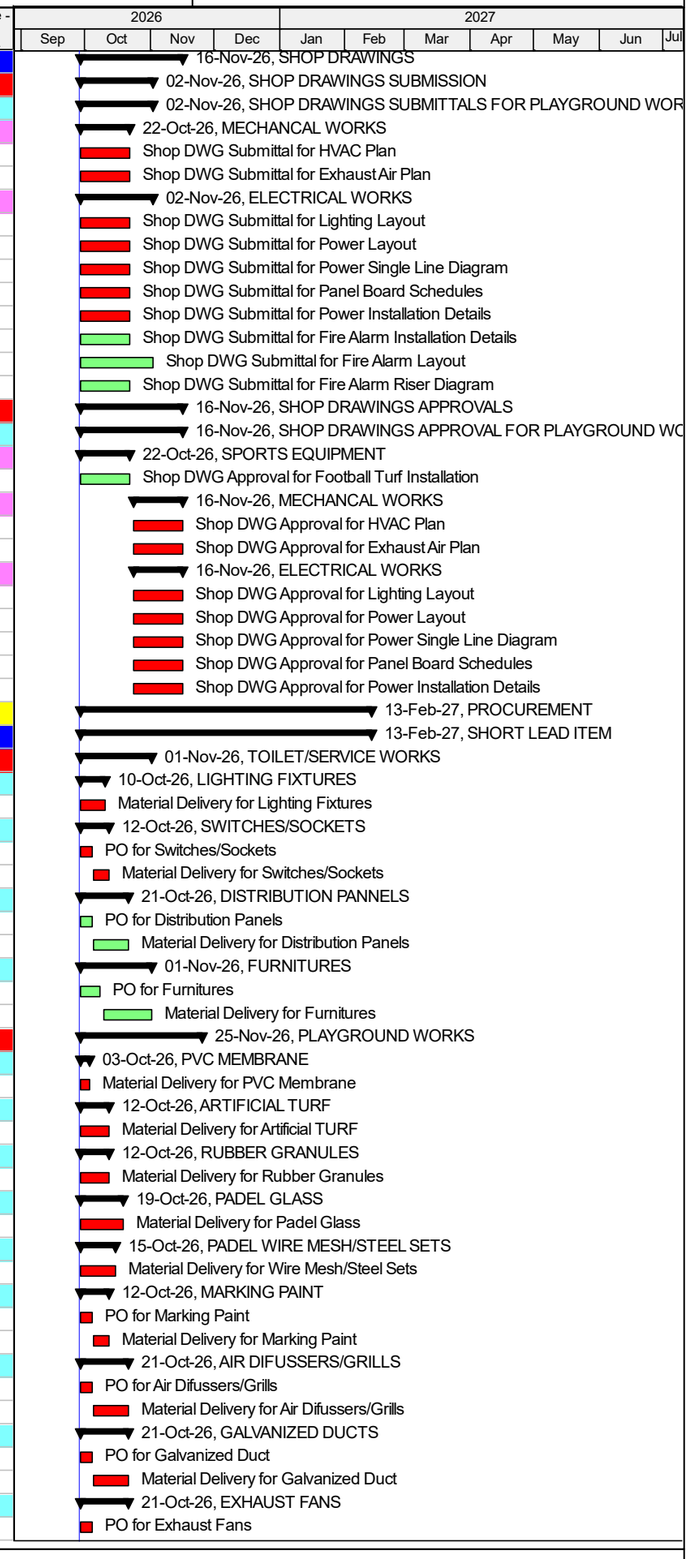

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	09-Jul-26	26-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-74
DISTRIBUTION BOARDS		20	0%	0%	04-Jul-26	26-Jul-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	04-Jul-26	08-Jul-26	17-Oct-26	21-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	09-Jul-26	26-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-89
POWER CABLES		15	0%	0%	09-Jul-26	26-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	09-Jul-26	14-Jul-26	22-Oct-26	27-Oct-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	15-Jul-26	26-Jul-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-89
LIGHT FIXTURES		10	0%	0%	21-Jul-26	01-Aug-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-84
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	21-Jul-26	01-Aug-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-84
CCTV MATERIALS		50	0%	0%	21-Jul-26	12-Aug-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	21-Jul-26	26-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-59
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	27-Jul-26	12-Aug-26	09-Nov-26	25-Nov-26	0.00	0.00	0.00	-89
POWER OUTLETS/SWITCHES		21	0%	0%	27-Jul-26	19-Aug-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	27-Jul-26	02-Aug-26	13-Oct-26	19-Oct-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	03-Aug-26	19-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-66
LANDSCAPE WORKS		100	0%	0%	03-Aug-26	20-Oct-26	20-Oct-26	13-Feb-27	0.00	0.00	0.00	-99
PAVEMENT MARKING		15	0%	0%	03-Aug-26	19-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	03-Aug-26	08-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	09-Aug-26	19-Aug-26	26-Oct-26	05-Nov-26	0.00	0.00	0.00	-66
TRAFFIC SIGNS		14	0%	0%	04-Oct-26	19-Oct-26	26-Oct-26	10-Nov-26	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	PO for Traffic Signs	5	0%	0%	04-Oct-26	08-Oct-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	10-Oct-26	19-Oct-26	01-Nov-26	10-Nov-26	0.00	0.00	0.00	-19
AGRICULTURE SOIL		17	0%	0%	21-Sep-26	11-Oct-26	21-Jan-27	09-Feb-27	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	PO for Agriculture Soil	5	100%	0%	21-Sep-26	27-Sep-26	21-Jan-27	26-Jan-27	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	12	8.33%	0%	28-Sep-26	11-Oct-26	27-Jan-27	09-Feb-27	0.00	0.00	0.00	-104
TRACK SURFACE		10	0%	0%	09-Sep-26	20-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	09-Sep-26	20-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-104
GRASS/TREES		15	0%	0%	04-Oct-26	20-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	0%	04-Oct-26	20-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-99
LONG LEAD ITEM		88	0%	0%	20-May-26	02-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-109
PLAYGROUND WORKS		88	0%	0%	20-May-26	02-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-109
STEEL TENSION CABLES		65	0%	0%	20-May-26	06-Aug-26	29-Sep-26	13-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	20-May-26	01-Jun-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	25-Jun-26	29-Jul-26	01-Nov-26	05-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	02-Jun-26	24-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Staging time	7	100%	0%	30-Jul-26	06-Aug-26	06-Dec-26	13-Dec-26	0.00	0.00	0.00	-109
EMERGENCY DOORS		60	0%	0%	25-Jun-26	02-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	25-Jun-26	06-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	30-Jul-26	27-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	07-Jul-26	29-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-109
PRESSURE UNITS		60	0%	0%	25-Jun-26	02-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	25-Jun-26	06-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	30-Jul-26	27-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	07-Jul-26	29-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-109
AIR LOCK DOORS		60	0%	0%	25-Jun-26	02-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	25-Jun-26	06-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	30-Jul-26	27-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	07-Jul-26	29-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-109
CONSTRUCTION PHASE		154	26.07%	5.77%	30-Jun-26	28-Dec-26	01-Jun-26 A	23-Mar-27	1,750,072.60	386,957.04	6,711,908.76	-69
SITE WORKS		147	19.75%	5.7%	30-Jun-26	28-Dec-26	01-Jun-26 A	23-Mar-27	1,205,280.80	347,741.41	6,103,127.59	-69
LANDSCAPE WORKS		147	19.75%	5.7%	30-Jun-26	28-Dec-26	01-Jun-26 A	23-Mar-27	1,205,280.80	347,741.41	6,103,127.59	-69
PLAYGROUND AREA		135	19.97%	23.9%	30-Jun-26	28-Dec-26	21-Sep-26 A	06-Mar-27	90,508.61	108,312.40	453,207.82	-57
FOOTBALL PLAYGROUND		40	100%	0%	30-Jun-26	15-Aug-26	13-Oct-26	28-Nov-26	47,527.50	0.00	47,527.50	-89
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	100%	0%	23-Jul-26	15-Aug-26	05-Nov-26	28-Nov-26	31,685.00	0.00	31,685.00	-89
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	20	100%	0%	30-Jun-26	22-Jul-26	13-Oct-26	04-Nov-26	15,842.50	0.00	15,842.50	-89
PADEL PLAYGROUND		25	0%	0%	18-Nov-26	16-Dec-26	29-Nov-26	27-Dec-26	0.00	0.00	70,195.20	-9
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	18-Nov-26	05-Dec-26	29-Nov-26	15-Dec-26	0.00	0.00	58,496.00	-9
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	10	0%	0%	06-Dec-26	16-Dec-26	16-Dec-26	27-Dec-26	0.00	0.00	11,699.20	-9
BASKETBALL PLAYGROUND		15	0%	0%	15-Nov-26	14-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	96,956.10	-69
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	16-Feb-27	06-Mar-27	0.00	0.00	80,796.75	-80
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	06-Dec-26	14-Dec-26	16-Feb-27	25-Feb-27	0.00	0.00	16,159.35	-62

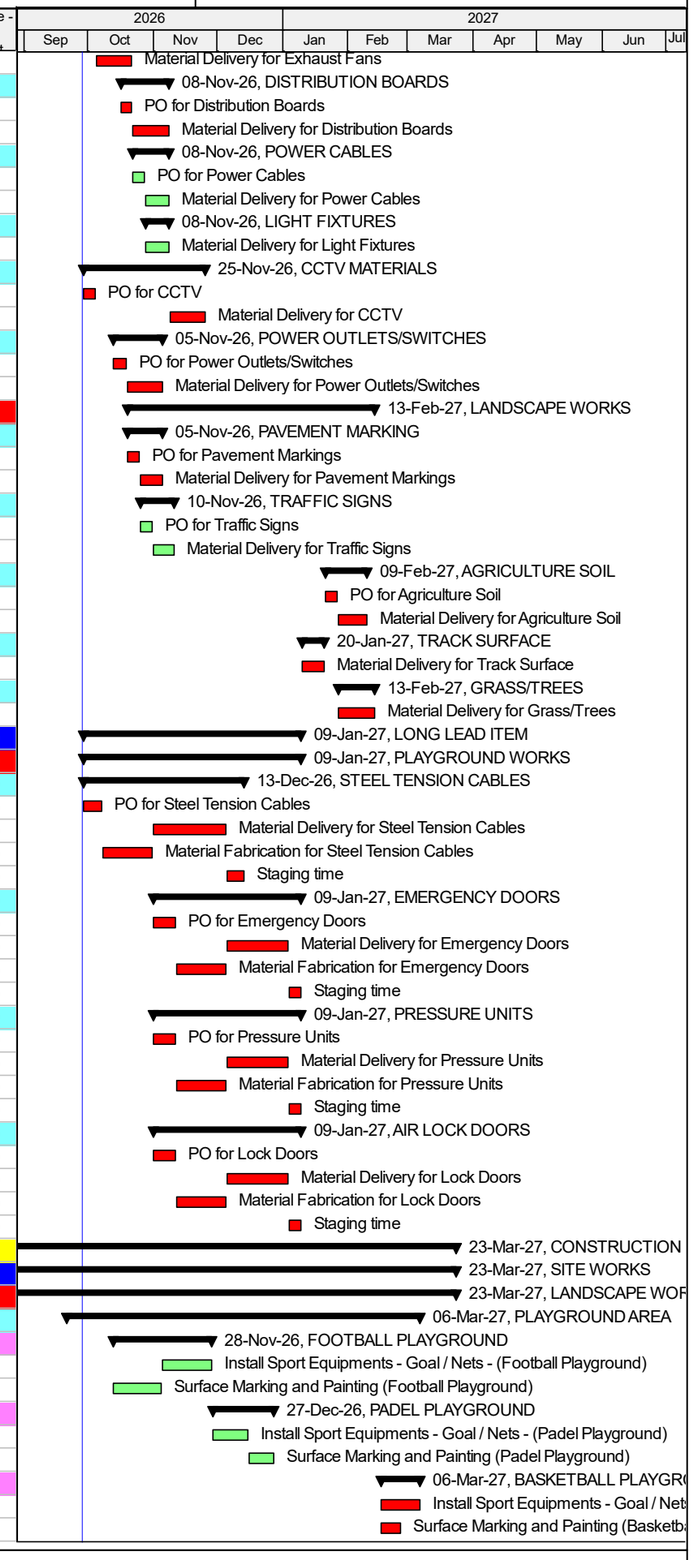

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PADEL FENCE		28	0%	0%	17-Dec-26	28-Dec-26	29-Sep-26	31-Oct-26	0.00	0.00	58,008.35	50
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	17-Dec-26	23-Dec-26	29-Sep-26	05-Oct-26	0.00	0.00	4,143.45	68
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	20-Oct-26	31-Oct-26	0.00	0.00	33,147.63	50
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	20-Oct-26	31-Oct-26	0.00	0.00	16,573.82	50
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	17-Dec-26	22-Dec-26	20-Oct-26	25-Oct-26	0.00	0.00	4,143.45	50
CURBSTOEN/INTERLOCK		21	23.81%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	22-Oct-26	42,981.11	108,312.40	180,520.67	-5
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	23.81%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	22-Oct-26	42,981.11	108,312.40	180,520.67	-5
AIR DOME		135	25.93%	0%	27-Jul-26	09-Dec-26	04-Oct-26	14-Mar-27	1,114,772.18	0.00	4,299,815.57	-77
CIVIL WORKS		39	0%	0%	30-Sep-26	24-Oct-26	04-Oct-26	17-Nov-26	0.00	0.00	1,384,750.38	-21
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	21	0%	0%	30-Sep-26	24-Oct-26	04-Oct-26	27-Oct-26	0.00	0.00	936,278.81	-3
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	0%	0%	30-Sep-26	11-Oct-26	07-Nov-26	17-Nov-26	0.00	0.00	448,471.57	-32
MECHANICAL WORKS		98	13.64%	0%	27-Jul-26	15-Nov-26	22-Oct-26	13-Feb-27	168,176.84	0.00	1,233,296.81	-77
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	20	0%	0%	12-Oct-26	03-Nov-26	10-Jan-27	01-Feb-27	0.00	0.00	728,766.30	-77
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	04-Nov-26	15-Nov-26	02-Feb-27	13-Feb-27	0.00	0.00	336,353.67	-77
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	20	100%	0%	27-Jul-26	18-Aug-26	22-Oct-26	14-Nov-26	168,176.84	0.00	168,176.84	-74
ELECTRICAL WORKS		58	62.54%	0%	03-Sep-26	15-Oct-26	26-Nov-26	01-Feb-27	946,595.34	0.00	1,513,591.54	-93
MLTX-02-005-CI	Light Fixture Works (Air Dome)	12	100%	0%	03-Sep-26	16-Sep-26	10-Jan-27	23-Jan-27	224,235.78	0.00	224,235.78	-109
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	14	42.86%	0%	21-Sep-26	07-Oct-26	10-Jan-27	25-Jan-27	72,075.79	0.00	168,176.84	-94
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	30%	0%	21-Sep-26	14-Oct-26	10-Jan-27	01-Feb-27	50,453.05	0.00	168,176.84	-94
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	30%	0%	21-Sep-26	14-Oct-26	10-Jan-27	01-Feb-27	151,359.15	0.00	504,530.51	-94
MLTX-02-005-CI	Control System Installation (Air Dome)	21	28.57%	0%	21-Sep-26	15-Oct-26	26-Nov-26	20-Dec-26	448,471.57	0.00	448,471.57	-56
FINISHES WORKS		68	0%	0%	17-Oct-26	09-Dec-26	21-Dec-26	14-Mar-27	0.00	0.00	168,176.84	-77
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	21	0%	0%	17-Oct-26	09-Nov-26	21-Dec-26	13-Jan-27	0.00	0.00	112,117.89	-56
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	21	0%	0%	16-Nov-26	09-Dec-26	14-Feb-27	14-Mar-27	0.00	0.00	56,058.95	-77
IRRIGATION NETWORK		15	0%	38.73%	28-Oct-26	17-Nov-26	10-Sep-26 A	16-Feb-27	0.00	18,848.67	48,667.04	-78
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	25
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	15-Nov-26	17-Nov-26	14-Feb-27	16-Feb-27	0.00	0.00	25,106.20	-78
NATURAL GROUND		63	0%	0%	09-Nov-26	17-Nov-26	06-Dec-26	16-Feb-27	0.00	0.00	191,740.00	-78
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	15-Nov-26	17-Nov-26	14-Feb-27	16-Feb-27	0.00	0.00	126,740.00	-78
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	09-Nov-26	14-Nov-26	06-Dec-26	10-Dec-26	0.00	0.00	65,000.00	-23
PLANTING		13	0%	0%	12-Oct-26	29-Oct-26	10-Feb-27	25-Feb-27	0.00	0.00	347,251.46	-101
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	5	0%	0%	12-Oct-26	17-Oct-26	10-Feb-27	15-Feb-27	0.00	0.00	104,175.44	-104
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	27-Oct-26	29-Oct-26	23-Feb-27	25-Feb-27	0.00	0.00	141,732.50	-101
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	0%	0%	21-Oct-26	26-Oct-26	16-Feb-27	21-Feb-27	0.00	0.00	101,343.52	-101
WALKING/BIKE PATHS		8	0%	60%	31-Oct-26	08-Nov-26	01-Jun-26 A	29-Sep-26	0.00	220,580.34	367,633.90	35
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	0%	60%	31-Oct-26	08-Nov-26	01-Jun-26 A	29-Sep-26	0.00	112,532.47	187,554.12	35
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	0%	60%	31-Oct-26	08-Nov-26	10-Jun-26 A	29-Sep-26	0.00	108,047.87	180,079.78	35
GENERAL/FURNITURE		147	0%	0%	09-Nov-26	10-Dec-26	29-Sep-26	23-Mar-27	0.00	0.00	394,811.80	-84
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	09-Nov-26	17-Nov-26	29-Sep-26	07-Oct-26	0.00	0.00	93,594.00	35
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	02-Dec-26	09-Dec-26	16-Mar-27	23-Mar-27	0.00	0.00	9,749.30	-85
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	09-Nov-26	17-Nov-26	29-Sep-26	07-Oct-26	0.00	0.00	17,274.79	35
MLTX-02-005-CN-1	Fixation and Installation of Benches	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	40,307.84	35
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	32,757.76	35
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	18-Nov-26	26-Nov-26	08-Oct-26	17-Oct-26	0.00	0.00	12,869.04	35
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	02-Dec-26	10-Dec-26	18-Oct-26	26-Oct-26	0.00	0.00	12,186.67	39
MLTX-02-005-CN-1	Installing of Site Light Poles	12	0%	0%	18-Nov-26	01-Dec-26	27-Feb-27	15-Mar-27	0.00	0.00	176,072.40	-85
TOILET/SERVICE BUILDING		80	89.49%	6.44%	18-Jul-26	21-Oct-26	19-Sep-26 A	22-Dec-26	544,791.81	39,215.63	608,781.17	-53
THERMAL & MOISTER PROTECTION		8	100%	50%	02-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	16,607.28	8,303.64	16,607.28	-49
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	50%	02-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	16,607.28	8,303.64	16,607.28	-49
MECHANICAL WORK		68	97.1%	8.06%	28-Jul-26	07-Oct-26	19-Sep-26 A	08-Dec-26	156,554.36	12,999.20	161,229.39	-53
HVAC SYSTEM		4	100%	0%	10-Sep-26	14-Sep-26	12-Nov-26	16-Nov-26	14,623.96	0.00	14,623.96	-53
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	4	100%	0%	10-Sep-26	14-Sep-26	12-Nov-26	16-Nov-26	14,623.96	0.00	14,623.96	-53
WATER SUPPLY SYSTEM		60	96.81%	16.99%	10-Aug-26	29-Sep-26	19-Sep-26 A	29-Nov-26	74,062.46	12,999.20	76,499.79	-52
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	7	100%	50%	10-Aug-26	17-Aug-26	19-Sep-26 A	06-Oct-26	25,998.40	12,999.20	25,998.40	-42
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	20	95%	0%	06-Sep-26	29-Sep-26	29-Sep-26	21-Oct-26	46,309.19	0.00	48,746.52	-19
MLTX-02-005-CN-1	Installing of Water Heater	20	100%	0%	05-Sep-26	28-Sep-26	07-Nov-26	29-Nov-26	1,754.87	0.00	1,754.87	-53
SEWER/DRAINAGE SYSTEM		54	97.81%	0%	28-Jul-26	29-Sep-26	29-Sep-26	30-Nov-26	66,660.88	0.00	68,155.77	-53
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	5	100%	0%	18-Aug-26	23-Aug-26	20-Oct-26	25-Oct-26	10,358.68	0.00	10,358.68	-53
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	8	100%	0%	09-Aug-26	17-Aug-26	11-Oct-26	19-Oct-26	14,217.67	0.00	14,217.67	-53
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	10	100%	0%	28-Jul-26	08-Aug-26	29-Sep-26	10-Oct-26	12,186.63	0.00	12,186.63	-53
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	21	95.24%	0%	05-Sep-26	29-Sep-26	07-Nov-26	30-Nov-26	29,897.90	0.00	31,392.79	-53
FIRE PROTECTION		21	61.9%	0%	13-Sep-26	07-Oct-26	15-Nov-26	08-Dec-26	1,207.06	0.00	1,949.87	-53
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	61.9%	0%	13-Sep-26	07-Oct-26	15-Nov-26	08-Dec-26	1,207.06	0.00	1,949.87	-53
ELECTRICAL WORKS		35	67.19%	0%	10-Sep-26	21-Oct-26	12-Nov-26	22-Dec-26	121,466.94	0.00	180,781.27	-53

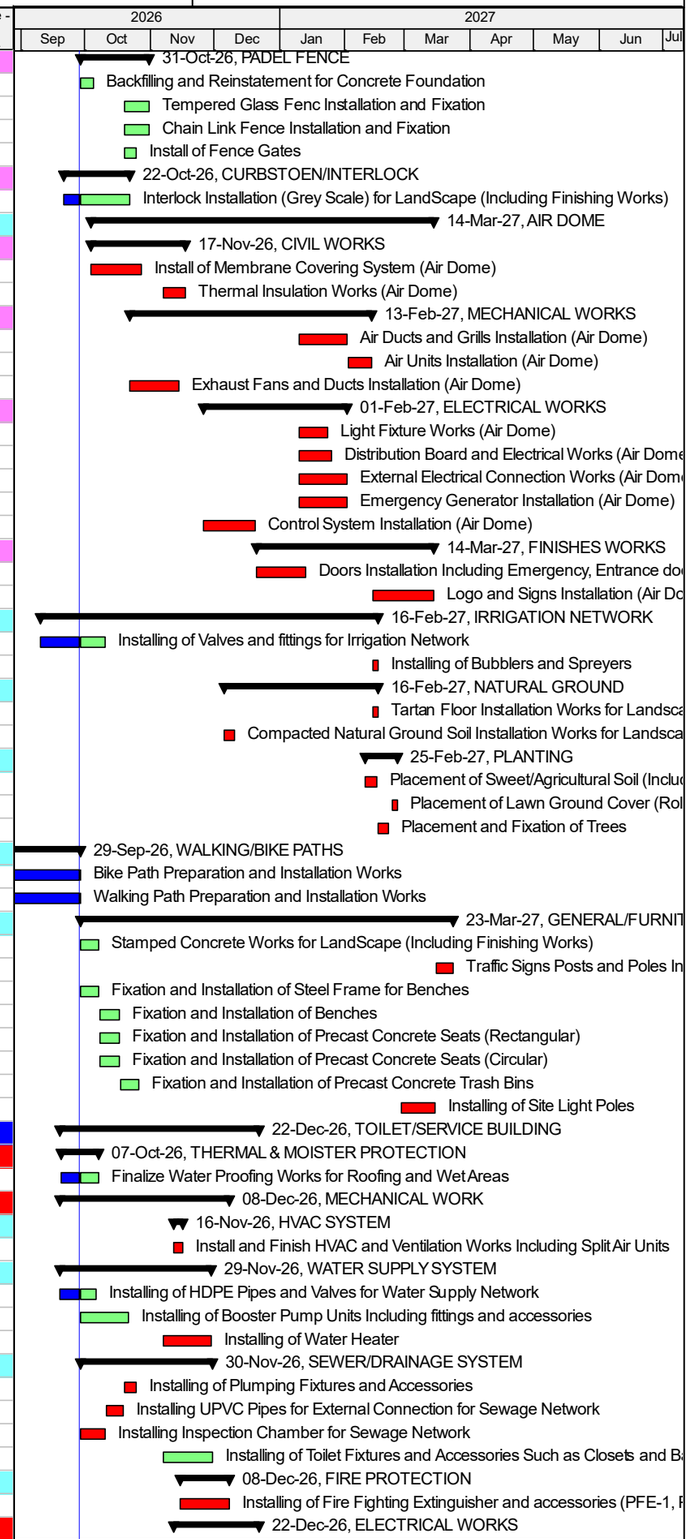

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FIXTURE WORKS		35	67.19%	0%	10-Sep-26	21-Oct-26	12-Nov-26	22-Dec-26	121,466.94	0.00	180,781.27	-53
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	20	55%	0%	15-Sep-26	08-Oct-26	17-Nov-26	09-Dec-26	18,874.64	0.00	34,317.53	-53
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	75%	0%	10-Sep-26	04-Oct-26	12-Nov-26	05-Dec-26	76,775.77	0.00	102,367.69	-53
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	65%	0%	13-Sep-26	06-Oct-26	15-Nov-26	07-Dec-26	4,605.31	0.00	7,085.10	-53
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	61.9%	0%	13-Sep-26	07-Oct-26	15-Nov-26	08-Dec-26	8,827.27	0.00	14,259.43	-53
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	0%	0%	29-Sep-26	21-Oct-26	30-Nov-26	22-Dec-26	0.00	0.00	6,239.59	-53
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	75%	0%	10-Sep-26	04-Oct-26	12-Nov-26	05-Dec-26	5,437.57	0.00	7,250.09	-53
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	75%	0%	10-Sep-26	04-Oct-26	12-Nov-26	05-Dec-26	5,118.38	0.00	6,824.51	-53
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	75%	0%	10-Sep-26	04-Oct-26	12-Nov-26	05-Dec-26	1,828.00	0.00	2,437.33	-53
DOORS/WINDOWS		39	100%	0%	18-Jul-26	10-Sep-26	29-Sep-26	12-Nov-26	68,245.12	0.00	68,245.12	-53
MLTX-02-005-CN-126	Preliminary Works For Doors	3	100%	0%	18-Jul-26	20-Jul-26	29-Sep-26	01-Oct-26	7,799.44	0.00	7,799.44	-62
MLTX-02-005-CN-126	Finalize Metal Doors for Toilets Building	1	100%	0%	10-Sep-26	10-Sep-26	12-Nov-26	12-Nov-26	1,949.86	0.00	1,949.86	-53
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	1	100%	0%	10-Sep-26	10-Sep-26	12-Nov-26	12-Nov-26	5,849.58	0.00	5,849.58	-53
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	2	100%	0%	18-Jul-26	19-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-62
METAL WORKS		8	100%	0%	18-Jul-26	17-Aug-26	11-Oct-26	19-Oct-26	9,749.30	0.00	9,749.30	-53
MLTX-02-005-CN-126	Installation of Galvanized Steel Ladder	4	100%	0%	13-Aug-26	17-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-49
MLTX-02-005-CN-129	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	15-Oct-26	19-Oct-26	3,899.72	0.00	3,899.72	-76
FINISHING WORKS		41	100%	15.76%	06-Aug-26	13-Sep-26	27-Sep-26 A	15-Nov-26	113,672.98	17,912.79	113,672.98	-53
FLOOR FINISHES		41	100%	0%	06-Aug-26	13-Sep-26	29-Sep-26	15-Nov-26	5,264.64	0.00	5,264.64	-53
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	06-Aug-26	12-Aug-26	29-Sep-26	05-Oct-26	2,924.82	0.00	2,924.82	-45
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	10-Sep-26	13-Sep-26	12-Nov-26	15-Nov-26	1,169.94	0.00	1,169.94	-53
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	13-Aug-26	17-Aug-26	06-Oct-26	10-Oct-26	1,169.88	0.00	1,169.88	-45
WALL FINISHES		37	100%	19.17%	11-Aug-26	12-Sep-26	27-Sep-26 A	14-Nov-26	93,437.44	17,912.79	93,437.44	-53
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	50%	18-Aug-26	20-Aug-26	27-Sep-26 A	01-Oct-26	35,825.58	17,912.79	35,825.58	-35
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	27-Aug-26	03-Sep-26	29-Oct-26	05-Nov-26	31,197.60	0.00	31,197.60	-53
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	22-Aug-26	26-Aug-26	03-Oct-26	07-Oct-26	2,275.00	0.00	2,275.00	-35
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	100%	0%	05-Sep-26	09-Sep-26	07-Nov-26	11-Nov-26	13,649.02	0.00	13,649.02	-53
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	11-Aug-26	12-Aug-26	08-Oct-26	10-Oct-26	8,150.24	0.00	8,150.24	-49
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	0%	10-Sep-26	12-Sep-26	12-Nov-26	14-Nov-26	2,340.00	0.00	2,340.00	-53
CELLING FINISHES		8	100%	0%	11-Aug-26	24-Aug-26	29-Sep-26	07-Oct-26	14,970.90	0.00	14,970.90	-37
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	0%	22-Aug-26	24-Aug-26	05-Oct-26	07-Oct-26	3,427.86	0.00	3,427.86	-37
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5	100%	0%	16-Aug-26	20-Aug-26	29-Sep-26	04-Oct-26	5,771.52	0.00	5,771.52	-37
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	0%	11-Aug-26	13-Aug-26	29-Sep-26	01-Oct-26	5,771.52	0.00	5,771.52	-41
SPECIALTIES WORK		24	100%	0%	24-Aug-26	20-Sep-26	26-Oct-26	22-Nov-26	58,495.83	0.00	58,495.83	-53
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	0%	24-Aug-26	26-Aug-26	26-Oct-26	28-Oct-26	14,623.96	0.00	14,623.96	-53
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	7	100%	0%	13-Sep-26	20-Sep-26	15-Nov-26	22-Nov-26	19,498.61	0.00	19,498.61	-53
MLTX-02-005-CN-131	Installation of Phenolic Locker	2	100%	0%	05-Sep-26	06-Sep-26	07-Nov-26	08-Nov-26	24,373.26	0.00	24,373.26	-53
TESTING & COMMISSIONING		46	0%	0%	18-Nov-26	02-Jan-27	17-Feb-27	15-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	15-Mar-27	30-Mar-27	0.00	0.00	0.00	-77
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	15	0%	0%	18-Nov-26	05-Dec-26	17-Feb-27	07-Mar-27	0.00	0.00	0.00	-78
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	20	0%	0%	10-Dec-26	02-Jan-27	24-Mar-27	15-Apr-27	0.00	0.00	0.00	-85
DAMMAM		178	29.58%	1.65%	06-Apr-26	29-Dec-26	06-Sep-26 A	14-Apr-27	1,933,713.11	108,127.40	6,538,022.31	-87
ENGINEERING		105	0%	0%	06-Apr-26	24-May-26	29-Sep-26	28-Jan-27	0.00	0.00	0.00	-210
SHOP DRAWINGS		105	0%	0%	06-Apr-26	24-May-26	29-Sep-26	28-Jan-27	0.00	0.00	0.00	-210
SHOP DRAWINGS SUBMISSION		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
AIR DOME SYSTEM		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Cable Tension Layout	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Airlock Door Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Emergency Exit Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
ELECTRICAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	21	100%	0%	06-Apr-26	29-Apr-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-147
SHOP DRAWINGS APPROVALS		105	0%	0%	30-Apr-26	24-May-26	29-Sep-26	28-Jan-27	0.00	0.00	0.00	-210
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		105	0%	0%	30-Apr-26	24-May-26	29-Sep-26	28-Jan-27	0.00	0.00	0.00	-210
AIR DOME SYSTEM		84	0%	0%	30-Apr-26	24-May-26	29-Sep-26	04-Jan-27	0.00	0.00	0.00	-189
MLTX-02-005-EN	Shop DWG Approval for Air Dome Structural Layout	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EN	Shop DWG Approval for Membrane Panel Layout	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EN	Shop DWG Approval for Cable Tension Layout	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147



Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	21	100%	0%	30-Apr-26	24-May-26	17-Nov-26	10-Dec-26	0.00	0.00	0.00	-168
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	21	100%	0%	30-Apr-26	24-May-26	12-Dec-26	04-Jan-27	0.00	0.00	0.00	-189
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-126
MECHANCAL WORKS		84	0%	0%	30-Apr-26	24-May-26	24-Oct-26	28-Jan-27	0.00	0.00	0.00	-210
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	30-Apr-26	24-May-26	05-Jan-27	28-Jan-27	0.00	0.00	0.00	-210
ELECTRICAL WORKS		21	0%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Power Layout	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	21	100%	0%	30-Apr-26	24-May-26	24-Oct-26	16-Nov-26	0.00	0.00	0.00	-147
PROCUREMENT		118	0%	0%	21-May-26	21-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-98
SHORT LEAD ITEM		118	0%	0%	31-May-26	21-Oct-26	29-Sep-26	13-Feb-27	0.00	0.00	0.00	-98
TOILET/SERVICE WORKS		29	0%	0%	11-Jun-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
LIGHTING FIXTURES		10	0%	0%	11-Jul-26	21-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	11-Jul-26	21-Jul-26	29-Sep-26	10-Oct-26	0.00	0.00	0.00	-68
SWITCHES/SOCKETS		12	0%	0%	11-Jul-26	23-Jul-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	11-Jul-26	15-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-68
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	16-Jul-26	23-Jul-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-68
DISTRIBUTION PANNELS		20	0%	0%	11-Jun-26	04-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	11-Jun-26	16-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	17-Jun-26	04-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-93
FURNITURES		29	0%	0%	05-Jul-26	06-Aug-26	29-Sep-26	01-Nov-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	05-Jul-26	14-Jul-26	29-Sep-26	08-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	15-Jul-26	06-Aug-26	10-Oct-26	01-Nov-26	0.00	0.00	0.00	-73
PLAYGROUND WORKS		50	0%	0%	31-May-26	29-Aug-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-75
PVC MEMBRANE		21	0%	0%	06-Jun-26	29-Jun-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	06-Jun-26	29-Jun-26	29-Sep-26	22-Oct-26	0.00	0.00	0.00	-98
ARTIFICIAL TURF		12	0%	0%	06-Jul-26	19-Jul-26	24-Oct-26	05-Nov-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	06-Jul-26	19-Jul-26	24-Oct-26	05-Nov-26	0.00	0.00	0.00	-93
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-103
PADEL GLASS		18	0%	0%	31-May-26	20-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	31-May-26	20-Jun-26	29-Sep-26	19-Oct-26	0.00	0.00	0.00	-103
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-98
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	29-Sep-26	15-Oct-26	0.00	0.00	0.00	-98
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	11-Jun-26	24-Jun-26	29-Sep-26	12-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	5	100%	0%	11-Jun-26	16-Jun-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for the Site	7	100%	0%	17-Jun-26	24-Jun-26	05-Oct-26	12-Oct-26	0.00	0.00	0.00	-93
INTERLOCKING PAVING		12	0%	0%	16-Jul-26	29-Jul-26	19-Oct-26	01-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	0%	16-Jul-26	21-Jul-26	19-Oct-26	24-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	7	100%	0%	22-Jul-26	29-Jul-26	25-Oct-26	01-Nov-26	0.00	0.00	0.00	-80
MARKING PAINT		12	0%	0%	17-Jun-26	30-Jun-26	05-Oct-26	18-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	17-Jun-26	22-Jun-26	05-Oct-26	10-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	23-Jun-26	30-Jun-26	11-Oct-26	18-Oct-26	0.00	0.00	0.00	-93
AIR DIFUSSERS/GRILLS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
GALVANIZED DUCTS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
EXHAUST FANS		20	0%	0%	05-Jul-26	27-Jul-26	29-Sep-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	05-Jul-26	09-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	11-Jul-26	27-Jul-26	05-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
DISTRIBUTION BOARDS		20	0%	0%	05-Jul-26	27-Jul-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	05-Jul-26	09-Jul-26	17-Oct-26	21-Oct-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	11-Jul-26	27-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-88
POWER CABLES		15	0%	0%	11-Jul-26	27-Jul-26	22-Oct-26	08-Nov-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	11-Jul-26	15-Jul-26	22-Oct-26	27-Oct-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	16-Jul-26	27-Jul-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-88
LIGHT FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-83
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	28-Oct-26	08-Nov-26	0.00	0.00	0.00	-83
CCTV MATERIALS		50	0%	0%	22-Jul-26	29-Aug-26	29-Sep-26	25-Nov-26	0.00	0.00	0.00	-75

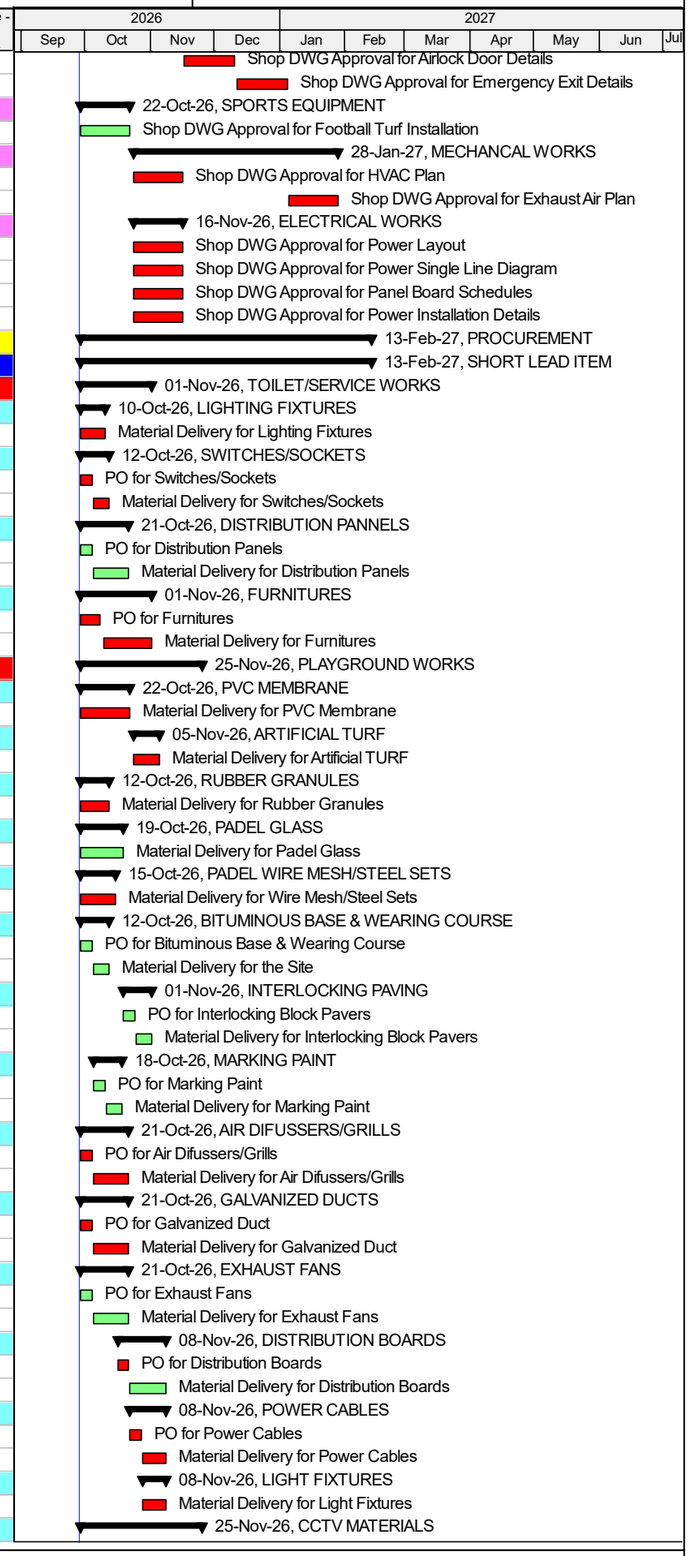

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	22-Jul-26	27-Jul-26	29-Sep-26	04-Oct-26	0.00	0.00	0.00	-58
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	12-Aug-26	29-Aug-26	09-Nov-26	25-Nov-26	0.00	0.00	0.00	-75
POWER OUTLETS/SWITCHES		21	0%	0%	28-Jul-26	20-Aug-26	13-Oct-26	05-Nov-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	28-Jul-26	03-Aug-26	13-Oct-26	19-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	04-Aug-26	20-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-65
LANDSCAPE WORKS		100	0%	0%	04-Aug-26	21-Oct-26	20-Oct-26	13-Feb-27	0.00	0.00	0.00	-98
PAVEMENT MARKING		15	0%	0%	04-Aug-26	20-Aug-26	20-Oct-26	05-Nov-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	04-Aug-26	09-Aug-26	20-Oct-26	25-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	10-Aug-26	20-Aug-26	26-Oct-26	05-Nov-26	0.00	0.00	0.00	-65
TRAFFIC SIGNS		14	0%	0%	05-Oct-26	20-Oct-26	26-Oct-26	10-Nov-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	PO for Traffic Signs	5	0%	0%	05-Oct-26	10-Oct-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	-18
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	11-Oct-26	20-Oct-26	01-Nov-26	10-Nov-26	0.00	0.00	0.00	-18
IRRIGATION PIPES/SPRINKLERS		14	0%	0%	10-Aug-26	24-Aug-26	26-Oct-26	10-Nov-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	0%	10-Aug-26	15-Aug-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	16-Aug-26	24-Aug-26	02-Nov-26	10-Nov-26	0.00	0.00	0.00	-66
AGRICULTURE SOIL		17	0%	0%	22-Sep-26	12-Oct-26	21-Jan-27	09-Feb-27	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	PO for Agriculture Soil	5	100%	0%	22-Sep-26	28-Sep-26	21-Jan-27	26-Jan-27	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	12	0%	0%	29-Sep-26	12-Oct-26	27-Jan-27	09-Feb-27	0.00	0.00	0.00	-103
TRACK SURFACE		10	0%	0%	10-Sep-26	21-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-103
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	10-Sep-26	21-Sep-26	10-Jan-27	20-Jan-27	0.00	0.00	0.00	-103
GRASS/TREES		15	0%	0%	05-Oct-26	21-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-98
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	0%	0%	05-Oct-26	21-Oct-26	27-Jan-27	13-Feb-27	0.00	0.00	0.00	-98
LONG LEAD ITEM		88	0%	0%	21-May-26	03-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-108
PLAYGROUND WORKS		88	0%	0%	21-May-26	03-Sep-26	29-Sep-26	09-Jan-27	0.00	0.00	0.00	-108
STEEL TENSION CABLES		65	0%	0%	21-May-26	08-Aug-26	29-Sep-26	13-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	29-Sep-26	07-Oct-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	27-Jun-26	30-Jul-26	01-Nov-26	05-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	03-Jun-26	25-Jun-26	08-Oct-26	31-Oct-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Staging time	7	100%	0%	01-Aug-26	08-Aug-26	06-Dec-26	13-Dec-26	0.00	0.00	0.00	-108
EMERGENCY DOORS		60	0%	0%	27-Jun-26	03-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	27-Jun-26	07-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	01-Aug-26	29-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	08-Jul-26	30-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-108
PRESSURE UNITS		60	0%	0%	27-Jun-26	03-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	27-Jun-26	07-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	01-Aug-26	29-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	08-Jul-26	30-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-108
AIR LOCK DOORS		60	0%	0%	27-Jun-26	03-Sep-26	01-Nov-26	09-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	27-Jun-26	07-Jul-26	01-Nov-26	11-Nov-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	01-Aug-26	29-Aug-26	06-Dec-26	03-Jan-27	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	08-Jul-26	30-Jul-26	12-Nov-26	05-Dec-26	0.00	0.00	0.00	-108
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	04-Jan-27	09-Jan-27	0.00	0.00	0.00	-108
CONSTRUCTION PHASE		173	29.58%	1.65%	18-Jul-26	29-Dec-26	06-Sep-26 A	08-Apr-27	1,933,713.11	108,127.40	6,538,022.31	-82
SITE WORKS		161	24.4%	1.23%	24-Aug-26	29-Dec-26	19-Sep-26 A	08-Apr-27	1,468,818.08	74,042.86	6,019,506.11	-82
LANDSCAPE WORKS		161	24.4%	1.23%	24-Aug-26	29-Dec-26	19-Sep-26 A	08-Apr-27	1,468,818.08	74,042.86	6,019,506.11	-82
PLAYGROUND AREA		133	52.43%	0%	24-Aug-26	08-Dec-26	20-Oct-26	28-Mar-27	320,701.04	0.00	611,632.81	-90
FOOTBALL PLAYGROUND		110	80.59%	0%	24-Aug-26	11-Nov-26	07-Nov-26	18-Mar-27	165,969.04	0.00	205,952.49	-105
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	24-Aug-26	15-Sep-26	07-Nov-26	29-Nov-26	158,424.99	0.00	158,424.99	-63
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	07-Nov-26	11-Nov-26	14-Mar-27	18-Mar-27	0.00	0.00	31,685.00	-105
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	21	47.62%	0%	16-Sep-26	11-Oct-26	30-Nov-26	23-Dec-26	7,544.05	0.00	15,842.50	-63
PADEL PLAYGROUND		5	0%	0%	07-Nov-26	11-Nov-26	14-Mar-27	18-Mar-27	0.00	0.00	70,195.20	-105
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	14-Mar-27	18-Mar-27	0.00	0.00	58,496.00	-105
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	14-Mar-27	18-Mar-27	0.00	0.00	11,699.20	-105
BASKETBALL PLAYGROUND		8	0%	0%	12-Nov-26	21-Nov-26	20-Mar-27	28-Mar-27	0.00	0.00	96,956.10	-105
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	8	0%	0%	12-Nov-26	21-Nov-26	20-Mar-27	28-Mar-27	0.00	0.00	80,796.75	-105
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	12-Nov-26	21-Nov-26	20-Mar-27	28-Mar-27	0.00	0.00	16,159.35	-105
PADEL FENCE		15	0%	0%	22-Nov-26	08-Dec-26	20-Oct-26	05-Nov-26	0.00	0.00	58,008.35	28
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	22-Nov-26	28-Nov-26	20-Oct-26	26-Oct-26	0.00	0.00	4,143.45	28
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	20-Oct-26	05-Nov-26	0.00	0.00	33,147.63	28
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	20-Oct-26	05-Nov-26	0.00	0.00	16,573.82	28
MLTX-02-005-CI	Install of Fence Gates	15	0%	0%	22-Nov-26	08-Dec-26	20-Oct-26	05-Nov-26	0.00	0.00	4,143.45	28
CURBSTOEN/INTERLOCK		21	85.71%	0%	07-Sep-26	01-Oct-26	07-Nov-26	30-Nov-26	154,732.00	0.00	180,520.67	-51

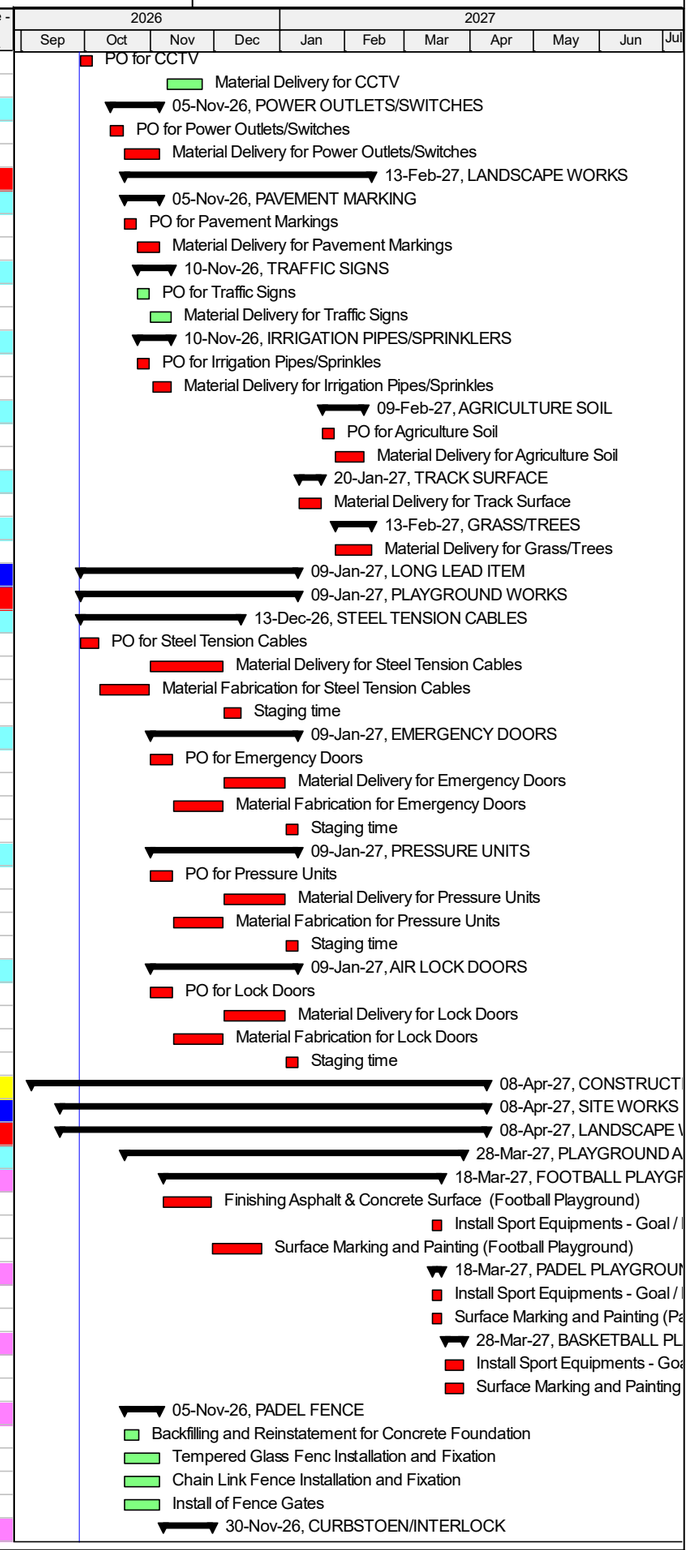

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Remaining work
D.D 28-09-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	85.71%	0%	07-Sep-26	01-Oct-26	07-Nov-26	30-Nov-26	154,732.00	0.00	180,520.67	-51
AIR DOME		126	24.95%	0%	16-Sep-26	24-Nov-26	09-Nov-26	08-Apr-27	1,072,657.44	0.00	4,299,815.57	-112
CIVIL WORKS		15	77.46%	0%	16-Sep-26	04-Oct-26	09-Nov-26	25-Nov-26	1,072,657.44	0.00	1,384,750.38	-45
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	15	66.67%	0%	16-Sep-26	04-Oct-26	09-Nov-26	25-Nov-26	624,185.87	0.00	936,278.81	-45
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	100%	0%	16-Sep-26	28-Sep-26	09-Nov-26	19-Nov-26	448,471.57	0.00	448,471.57	-45
MECHANICAL WORKS		33	0%	0%	29-Sep-26	05-Nov-26	30-Jan-27	09-Mar-27	0.00	0.00	1,233,296.81	-105
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	29-Sep-26	10-Oct-26	30-Jan-27	09-Feb-27	0.00	0.00	728,766.30	-105
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	11-Oct-26	25-Oct-26	10-Feb-27	25-Feb-27	0.00	0.00	336,353.67	-105
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	26-Oct-26	05-Nov-26	27-Feb-27	09-Mar-27	0.00	0.00	168,176.84	-105
ELECTRICAL WORKS		39	0%	0%	11-Oct-26	24-Nov-26	10-Feb-27	31-Mar-27	0.00	0.00	1,513,591.54	-105
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	11-Oct-26	21-Oct-26	10-Feb-27	21-Feb-27	0.00	0.00	224,235.78	-105
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	22-Oct-26	29-Oct-26	23-Feb-27	02-Mar-27	0.00	0.00	168,176.84	-105
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	31-Oct-26	05-Nov-26	03-Mar-27	09-Mar-27	0.00	0.00	168,176.84	-105
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	11	0%	0%	07-Nov-26	18-Nov-26	14-Mar-27	25-Mar-27	0.00	0.00	504,530.51	-105
MLTX-02-005-CI	Control System Installation (Air Dome)	5	0%	0%	19-Nov-26	24-Nov-26	27-Mar-27	31-Mar-27	0.00	0.00	448,471.57	-105
FINISHES WORKS		29	0%	0%	31-Oct-26	22-Nov-26	03-Mar-27	08-Apr-27	0.00	0.00	168,176.84	-114
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	10	0%	0%	31-Oct-26	10-Nov-26	03-Mar-27	17-Mar-27	0.00	0.00	112,117.89	-105
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	10	0%	0%	11-Nov-26	22-Nov-26	29-Mar-27	08-Apr-27	0.00	0.00	56,058.95	-114
IRRIGATION NETWORK		36	0%	59.67%	30-Sep-26	14-Oct-26	19-Sep-26 A	11-Feb-27	0.00	58,950.94	98,794.87	-103
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	3	0%	80%	30-Sep-26	03-Oct-26	19-Sep-26 A	01-Oct-26	0.00	40,102.26	50,127.83	1
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	3	0%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	01-Oct-26	0.00	18,848.67	23,560.84	4
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	13-Oct-26	14-Oct-26	10-Feb-27	11-Feb-27	0.00	0.00	25,106.20	-103
NATURAL GROUND		30	0%	0%	07-Oct-26	10-Nov-26	14-Oct-26	17-Nov-26	0.00	0.00	191,740.00	-6
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	25-Oct-26	10-Nov-26	01-Nov-26	17-Nov-26	0.00	0.00	126,740.00	-6
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	0%	0%	07-Oct-26	24-Oct-26	14-Oct-26	31-Oct-26	0.00	0.00	65,000.00	-6
PLANTING		23	0%	0%	15-Oct-26	10-Nov-26	13-Feb-27	15-Mar-27	0.00	0.00	347,251.46	-103
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	0%	15-Oct-26	21-Oct-26	13-Feb-27	18-Feb-27	0.00	0.00	104,175.44	-103
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	03-Nov-26	10-Nov-26	04-Mar-27	15-Mar-27	0.00	0.00	141,732.50	-103
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	22-Oct-26	02-Nov-26	20-Feb-27	03-Mar-27	0.00	0.00	101,343.52	-103
GENERAL/FURNITURE		159	16.05%	3.21%	07-Sep-26	29-Dec-26	20-Sep-26 A	06-Apr-27	75,459.60	15,091.92	470,271.40	-80
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	23-Nov-26	01-Dec-26	29-Sep-26	07-Oct-26	0.00	0.00	93,594.00	47
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	9	0%	0%	20-Dec-26	29-Dec-26	28-Mar-27	06-Apr-27	0.00	0.00	9,749.30	-80
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	23-Nov-26	01-Dec-26	29-Sep-26	07-Oct-26	0.00	0.00	17,274.79	47
MLTX-02-005-CN-1	Fixation and Installation of Benches	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	40,307.84	47
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	32,757.76	47
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	10	0%	0%	02-Dec-26	13-Dec-26	08-Oct-26	19-Oct-26	0.00	0.00	12,869.04	47
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	20-Dec-26	28-Dec-26	20-Oct-26	28-Oct-26	0.00	0.00	12,186.67	52
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	13	100%	20%	07-Sep-26	21-Sep-26	20-Sep-26 A	13-Oct-26	75,459.60	15,091.92	75,459.60	-18
MLTX-02-005-CN-1	Installing of Site Light Poles	10	0%	0%	02-Dec-26	13-Dec-26	16-Mar-27	27-Mar-27	0.00	0.00	176,072.40	-85
TOILET/SERVICE BUILDING		58	89.66%	6.57%	18-Jul-26	11-Oct-26	06-Sep-26 A	21-Nov-26	464,895.03	34,084.54	518,516.20	-35
THERMAL & MOISTER PROTECTION		8	100%	80%	06-Aug-26	15-Aug-26	06-Sep-26 A	07-Oct-26	16,607.28	13,285.82	16,607.28	-45
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	80%	06-Aug-26	15-Aug-26	06-Sep-26 A	07-Oct-26	16,607.28	13,285.82	16,607.28	-45
MECHANICAL WORK		35	100%	15.63%	08-Aug-26	20-Sep-26	19-Sep-26 A	31-Oct-26	133,070.22	20,798.72	133,070.22	-34
HVAC SYSTEM		3	100%	0%	16-Sep-26	19-Sep-26	28-Oct-26	31-Oct-26	14,623.96	0.00	14,623.96	-35
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	100%	0%	16-Sep-26	19-Sep-26	28-Oct-26	31-Oct-26	14,623.96	0.00	14,623.96	-35
WATER SUPPLY SYSTEM		18	100%	27.83%	08-Aug-26	01-Sep-26	19-Sep-26 A	11-Oct-26	74,744.92	20,798.72	74,744.92	-33
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	05-Oct-26	25,998.40	20,798.72	25,998.40	-44
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	5	100%	0%	27-Aug-26	01-Sep-26	06-Oct-26	11-Oct-26	48,746.52	0.00	48,746.52	-33
SEWER/DRAINAGE SYSTEM		23	100%	0%	17-Aug-26	13-Sep-26	29-Sep-26	25-Oct-26	41,751.47	0.00	41,751.47	-35
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	4	100%	0%	17-Aug-26	20-Aug-26	29-Sep-26	03-Oct-26	10,358.68	0.00	10,358.68	-36
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	21-Oct-26	25-Oct-26	31,392.79	0.00	31,392.79	-35
FIRE PROTECTION		2	100%	0%	19-Sep-26	20-Sep-26	29-Sep-26	30-Sep-26	1,949.87	0.00	1,949.87	-8
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	19-Sep-26	20-Sep-26	29-Sep-26	30-Sep-26	1,949.87	0.00	1,949.87	-8
ELECTRICAL WORKS		46	70.34%	0%	16-Sep-26	11-Oct-26	29-Sep-26	21-Nov-26	127,160.10	0.00	180,781.27	-35
FIXTURE WORKS		46	70.34%	0%	16-Sep-26	11-Oct-26	29-Sep-26	21-Nov-26	127,160.10	0.00	180,781.27	-35
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	5	100%	0%	20-Sep-26	26-Sep-26	01-Nov-26	05-Nov-26	34,317.53	0.00	34,317.53	-35
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	47.62%	0%	16-Sep-26	11-Oct-26	28-Oct-26	21-Nov-26	48,746.52	0.00	102,367.69	-35
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	3	100%	0%	19-Sep-26	21-Sep-26	13-Oct-26	15-Oct-26	7,085.10	0.00	7,085.10	-20
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	19-Sep-26	22-Sep-26	11-Oct-26	14-Oct-26	14,259.43	0.00	14,259.43	-18
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	19-Sep-26	22-Sep-26	29-Sep-26	03-Oct-26	6,239.59	0.00	6,239.59	-8
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	16-Sep-26	20-Sep-26	28-Oct-26	01-Nov-26	7,250.09	0.00	7,250.09	-35
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	16-Sep-26	19-Sep-26	28-Oct-26	31-Oct-26	6,824.51	0.00	6,824.51	-35
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	5	100%	0%	16-Sep-26	21-Sep-26	28-Oct-26	02-Nov-26	2,437.33	0.00	2,437.33	-35
DOORS/WINDOWS		29	100%	0%	22-Jul-26	20-Sep-26	29-Sep-26	01-Nov-26	60,445.68	0.00	60,445.68	-35

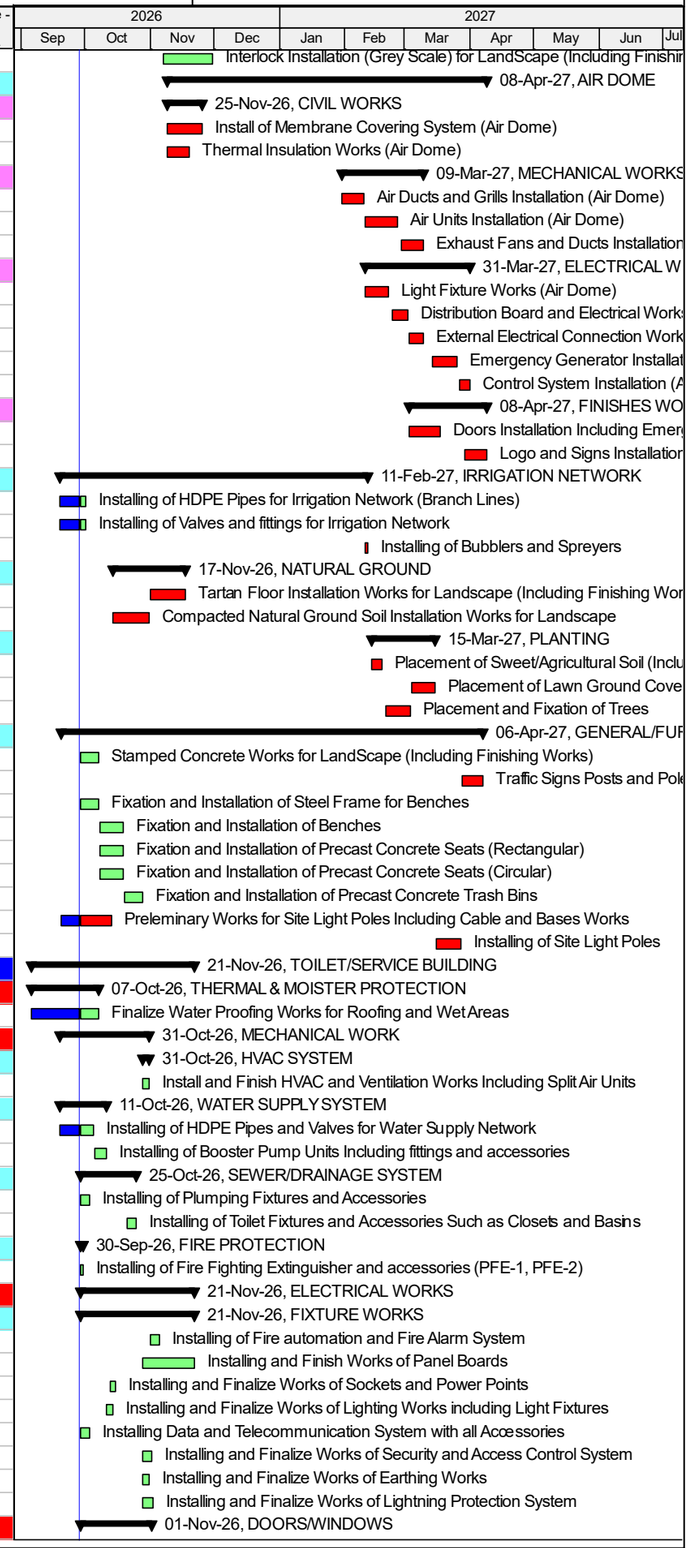

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 28-09-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-141	Finalize Metal Doors for Toilets Building	3	100%	0%	16-Sep-26	19-Sep-26	28-Oct-26	31-Oct-26	1,949.86	0.00	1,949.86	-35
MLTX-02-005-CN-142	Finalize Glazzed Curtain Wall Works	4	100%	0%	16-Sep-26	20-Sep-26	28-Oct-26	01-Nov-26	5,849.58	0.00	5,849.58	-35
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	2	100%	0%	22-Jul-26	23-Jul-26	29-Sep-26	30-Sep-26	52,646.24	0.00	52,646.24	-58
METAL WORKS		8	100%	0%	18-Jul-26	22-Aug-26	11-Oct-26	19-Oct-26	9,749.30	0.00	9,749.30	-49
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	4	100%	0%	18-Aug-26	22-Aug-26	11-Oct-26	14-Oct-26	5,849.58	0.00	5,849.58	-45
MLTX-02-005-CN-142	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	15-Oct-26	19-Oct-26	3,899.72	0.00	3,899.72	-76
FINISHING WORKS		27	100%	0%	10-Aug-26	17-Sep-26	29-Sep-26	29-Oct-26	59,366.62	0.00	59,366.62	-35
FLOOR FINISHES		27	100%	0%	10-Aug-26	17-Sep-26	29-Sep-26	29-Oct-26	4,094.76	0.00	4,094.76	-35
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	10-Aug-26	13-Aug-26	29-Sep-26	03-Oct-26	2,924.82	0.00	2,924.82	-42
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	2	100%	0%	16-Sep-26	17-Sep-26	28-Oct-26	29-Oct-26	1,169.94	0.00	1,169.94	-35
WALL FINISHES		25	100%	0%	16-Aug-26	15-Sep-26	29-Sep-26	27-Oct-26	55,271.86	0.00	55,271.86	-35
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	100%	0%	27-Aug-26	08-Sep-26	08-Oct-26	20-Oct-26	31,197.60	0.00	31,197.60	-35
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	18-Aug-26	23-Aug-26	29-Sep-26	04-Oct-26	2,275.00	0.00	2,275.00	-35
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	100%	0%	09-Sep-26	15-Sep-26	21-Oct-26	27-Oct-26	13,649.02	0.00	13,649.02	-35
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	16-Aug-26	17-Aug-26	08-Oct-26	10-Oct-26	8,150.24	0.00	8,150.24	-45
SPECIALTIES WORK		30	100%	0%	22-Aug-26	24-Sep-26	04-Oct-26	07-Nov-26	58,495.83	0.00	58,495.83	-37
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	0%	22-Aug-26	25-Aug-26	04-Oct-26	07-Oct-26	14,623.96	0.00	14,623.96	-36
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	5	100%	0%	19-Sep-26	24-Sep-26	02-Nov-26	07-Nov-26	19,498.61	0.00	19,498.61	-37
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	100%	0%	09-Sep-26	10-Sep-26	21-Oct-26	22-Oct-26	24,373.26	0.00	24,373.26	-35
TESTING & COMMISSIONING		49	0%	0%	15-Oct-26	29-Dec-26	13-Feb-27	14-Apr-27	0.00	0.00	0.00	-87
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	25-Nov-26	30-Nov-26	10-Apr-27	14-Apr-27	0.00	0.00	0.00	-112
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	6	0%	0%	15-Oct-26	21-Oct-26	13-Feb-27	18-Feb-27	0.00	0.00	0.00	-103
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	24-Dec-26	29-Dec-26	01-Apr-27	06-Apr-27	0.00	0.00	0.00	-80
PROJECT CLOSEOUT & DEMOBILIZATION		18	0%	0%	24-Dec-26	02-Jan-27	01-Apr-27	21-Apr-27	0.00	0.00	0.00	-90
As-Built DWGs		17	0%	0%	24-Dec-26	31-Dec-26	01-Apr-27	20-Apr-27	0.00	0.00	0.00	-90
As-Built DWGs Submittals		14	0%	0%	24-Dec-26	28-Dec-26	01-Apr-27	17-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	27-Dec-26	28-Dec-26	15-Apr-27	17-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	24-Dec-26	26-Dec-26	01-Apr-27	03-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	2	0%	0%	24-Dec-26	26-Dec-26	01-Apr-27	03-Apr-27	0.00	0.00	0.00	-80
As-Built DWGs Approvals		15	0%	0%	27-Dec-26	31-Dec-26	04-Apr-27	20-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	29-Dec-26	31-Dec-26	18-Apr-27	20-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	27-Dec-26	29-Dec-26	04-Apr-27	06-Apr-27	0.00	0.00	0.00	-80
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	27-Dec-26	29-Dec-26	04-Apr-27	06-Apr-27	0.00	0.00	0.00	-80
Demobilization		4	0%	0%	30-Dec-26	02-Jan-27	18-Apr-27	21-Apr-27	0.00	0.00	0.00	-90
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	30-Dec-26	30-Dec-26	18-Apr-27	18-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	30-Dec-26	30-Dec-26	18-Apr-27	18-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	19-Apr-27	19-Apr-27	0.00	0.00	0.00	-89
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	21-Apr-27	21-Apr-27	0.00	0.00	0.00	-90

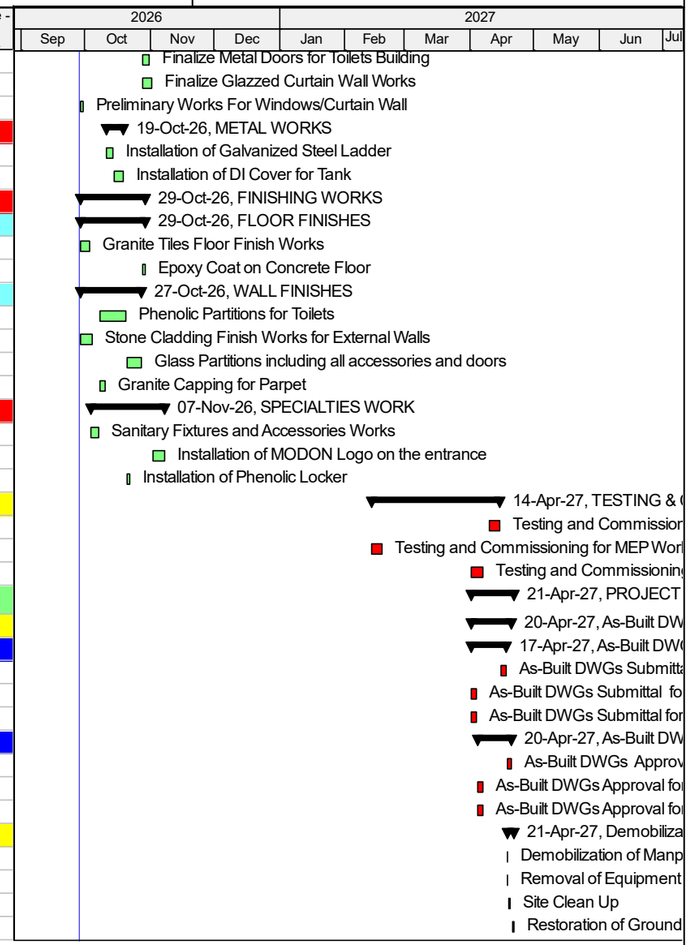

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: Remaining works.

© Oracle Corporation
