Weekly Progress Report – Construction Projects

Projects Department

Disclaimer

This report is not all inclusive, nor it is intended to address the entirety of construction progress. It is concerned primarily with construction progress and is intended to provide near term management information. The report itself serves as the Agenda for the weekly/Biweekly/Monthly or as required progress meetings.

Introduction

Introduction

Purpose

This report is to be prepared by the construction contractor and submitted to the Construction Consultant and MODON Project Manager **before 12:00 PM on every Wednesdays** with Progress data cut off date is Tuesday. The premise behind this report and the key to successfully managing projects is to update schedules weekly.

Calendar

The complete report will serve as the agenda for the weekly site meetings. The Construction Manger will chair the meeting. Attendance shall be limited to essential personnel only.

Construction Contractor, appropriate Contractor staff, Construction Manager, Program Manager, and MODON Project Manager shall be in attendance.

Minutes of Meeting will be taken by the Construction Manager and submitted to the Program Manager (If Applicable) within 48 hours. Minutes shall describe attendance, the conduct of the meeting, discussion items, and problem resolutions, and shall provide action items with responsible parties and due dates.

Construction Manager shall maintain the Action Items Register. At subsequent meetings, open action items shall be discussed first.

Weekly Progress Report Dashboard



Weekly Progress Report Attachment

Weekly Progress Report Attachement

Contractor/Consultant should ensure that the weekly progress report are supported with required attachment.

Those attachment should include the following as a minimum requirement:

- Approved Primavera P6 Schedule in .xer format.
- 3-5 latest progress photographs in JPG format
- Updated Primavera P6 schedule in .xer format & PDF Format Three weeks look ahead in PDF format. (as per plf link)
- Remaining Works in PDF format.
- Any other supporting document required per the development of the project.

Weekly Report
Areas / Sections

Weekly Report Areas / Sections

- Contract General Information
- Key Dates
- Progress Overview
- Construction Milestones
- Submittals Status
- Shop Drawing Status
- Material Approval Status
- Quality
- HSE
- Invoices
- Contract Change Order Log
- Major Quantity Trackers
- Resources at Site
- Primavera P6 Schedule Status
- Testing And Commissioning
- Top Issues

Weekly Report Areas / General Information

- **Contract General Information**

Weekly Progress Report - Construction Projects	
Contract General Information	
Project Name	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam)
Project ID	MLTX-02-005
Contractor	Profast Company Ltd.
Consultant	EGIS SAUDI ARABIA ENGINEERING COSULTANCY/ CCG
Stage	Construction
Status	Active
Modon PM	Engr. Mohamed Alisa

Weekly Report Areas / Dates

- Ke

Key Dates	
Contract Award Date	19-Jan-26
Contract Sign Date	11-Feb-26
Site Handover Date	03-Mar-26
Original Completion	02-Jan-27
Contract Award Date (Hijri)	30/07/1447
Contract Sign Date (Hijri)	12/08/1447
Site Handover Date (Hijri)	14/09/1447
Original Completion (Hijri)	24/07/1448
Revised Completion Date	02-Jan-27
Committed Completion Date	02-Jan-27
Forecast Completion	21-Apr-27
Variance	(109)

Weekly Report Areas / Dates

- **Key Dates**

Key Project Submittals	Submission Date	Days taken to approve orginal plan from site handover date
Quality Plan submission	11-Mar-26	8
Quality Plan approval	08-Apr-26	
Quality Plan Last Update	08-Apr-26	
Safety Plan submission	11-Mar-26	8
Safety Plan approval	28-Jun-26	
Safety Plan Last Update	13-Jun-26	
Risk Management Plan submission	11-Mar-26	8
Risk Management Plan approval		
Risk Management Plan Last Update		
Baseline Schedule submission	18-Mar-26	15
Baseline Schedule approval	27-Apr-26	
No of Schedule Versions	2	
Last Recovery Schedule Approval Date	27-Apr-26	
BOQ submission		
BOQ approval		
No of Approved Version of BOQ		
Project Execution Plan submission	30-Mar-26	27
Execution Plan Approval	02-Apr-26	

Weekly Report Areas / Progress


Earned Value Progress (SAR)						
WBS	BOQ Value (SAR)	% Wt.	Weekly (SAR)		To Date (SAR)	
			Planned	Earned	Planned	Earned
ARRAR	**10,110,715.45**	**33.70%**	**209,546**	**217,418**	**3,070,830**	**3,129,804**
Mobilization	-	0.00%	-	-	-	-
Engineering	-	0.00%				
Procurement	-	0.00%	-	-	-	-
Construction	10,110,715	33.70%	209,546	217,418	3,070,830	3,129,804
Testing and Commissioning	-	0.00%	-	-	-	-
HASA OASIS	**9,982,829.07**	**33.28%**	**545,731**	**258,797**	**4,535,090**	**3,657,877**
Mobilization	-	0.00%	-	-	-	-
Engineering	-	0.00%				
Procurement	-	0.00%	-	-	-	-
Construction	9,982,829	33.28%	545,731	258,797	4,535,090	3,657,877
Testing and Commissioning	-	0.00%	-	-	-	-
DAMMAM	**9,904,307.15**	**33.02%**	**722,284**	**298,880**	**4,772,983**	**3,474,412**
Mobilization	-	0.00%	-	-	-	-
Engineering	-	0.00%				
Procurement	-	0.00%	-	-	-	-
Construction	9,904,307	33.02%	722,284	298,880	4,772,983	3,474,412
Testing and Commissioning	-	0.00%	-	-	-	-
Project Closeout & Demobilization	**-**	**0.00%**	**-**	**-**	**-**	**-**
Project Closeout & Demobilization	-	0.00%				
Total	**29,997,851.67**	**100%**	**1,477,561**	**775,094**	**12,378,903**	**10,262,093**

Weekly Report Areas / Progress

WBS	Physical Progress (Effort)					
	Budgeted (Manhours	% Wt.	Weekly Physical Progress		To Date Physical Progress	
			Planned	Earned	Planned	Earned
ARRAR	**136,388**	**32.6%**	**3,018**	**278**	**64,506**	**53,947**
Mobilization	4,193	1.0%	-	-	4,193	4,193
Engineering	6,986	1.7%	3	-	6,957	6,793
Procuments	16,766	4.0%	200	-	15,716	8,257
Construction	104,250	24.9%	2,815	278	37,640	34,704
Testing and Commissioning	4,193	1.0%	-	-	-	-
HASA OASIS	**136,958**	**32.7%**	**4,034**	**909**	**70,982**	**63,200**
Mobilization	4,193	1.0%	-	-	4,193	4,193
Engineering	6,986	1.7%	-	-	6,986	6,697
Procuments	16,766	4.0%	187	-	15,748	7,939
Construction	104,820	25.0%	3,847	909	44,055	44,371
Testing and Commissioning	4,193	1.0%	-	-	-	-
DAMMAM	**136,958**	**32.7%**	**3,627**	**2,083**	**72,949**	**62,805**
Mobilization	4,193	1.0%	-	-	4,193	4,193
Engineering	6,986	1.7%	-	-	6,986	6,986
Procuments	16,766	4.0%	175	-	15,691	7,414
Construction	104,820	25.0%	3,452	2,083	46,079	44,212
Testing and Commissioning	4,193	1.0%	-	-	-	-
Project Closeout & Demobilization	**8,380**	**2.0%**	**-**	**-**	**-**	**-**
Project Closeout & Demobilization	8,380	2.0%	-	-	-	-
Total	**418,684**	**100%**	**10,679**	**3,270**	**208,437**	**179,952**


Weekly Report Areas / Progress

- **Progress Overview**

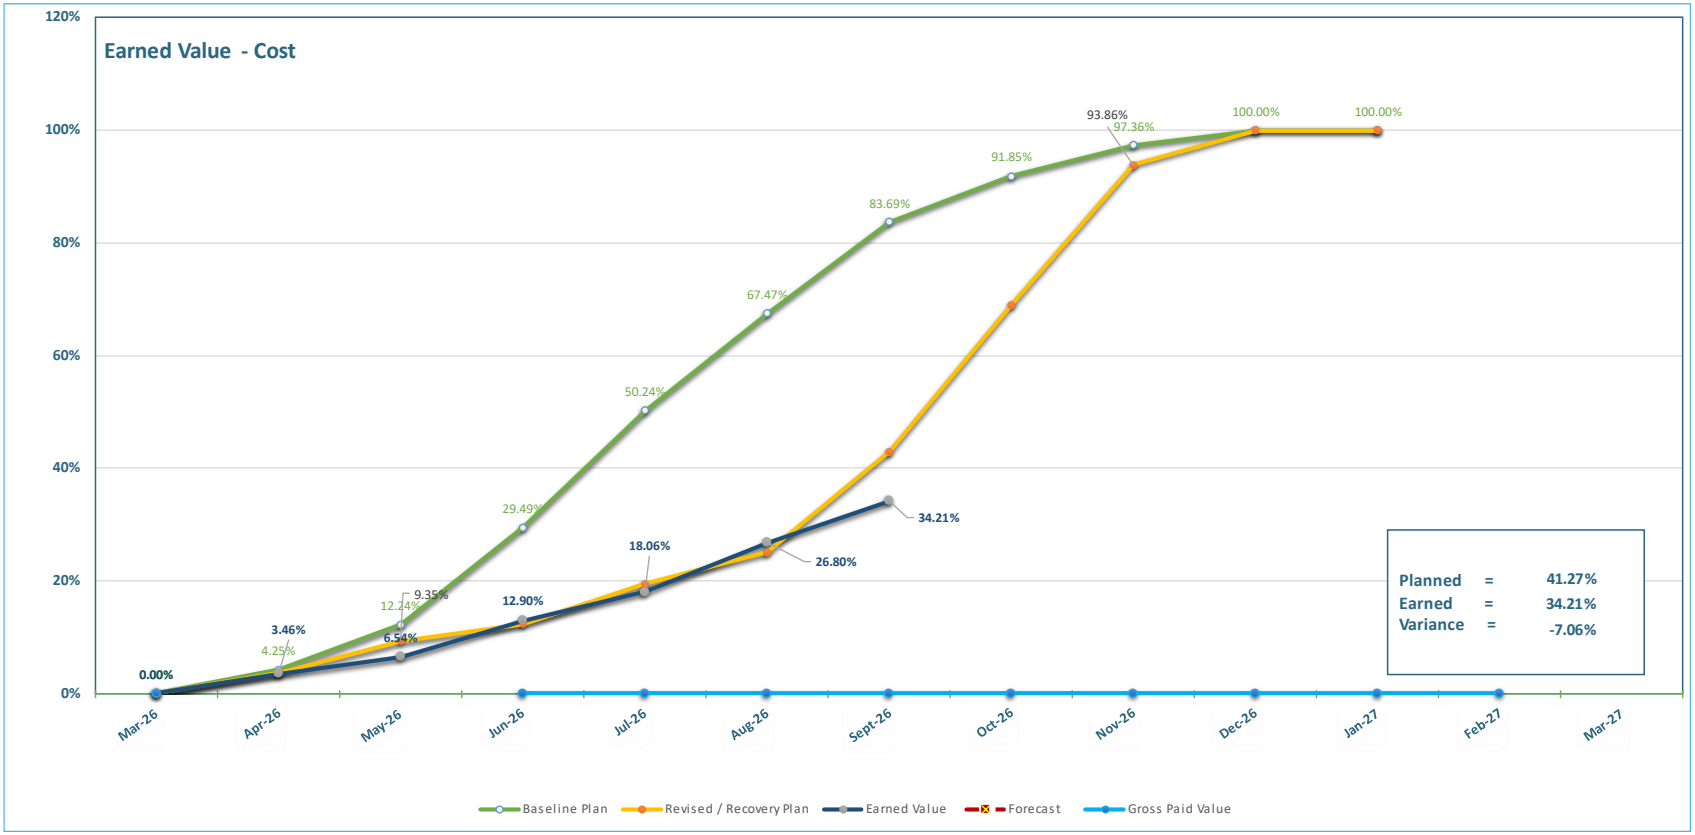

Weekly Report Areas / Progress

- **Progress Overview**

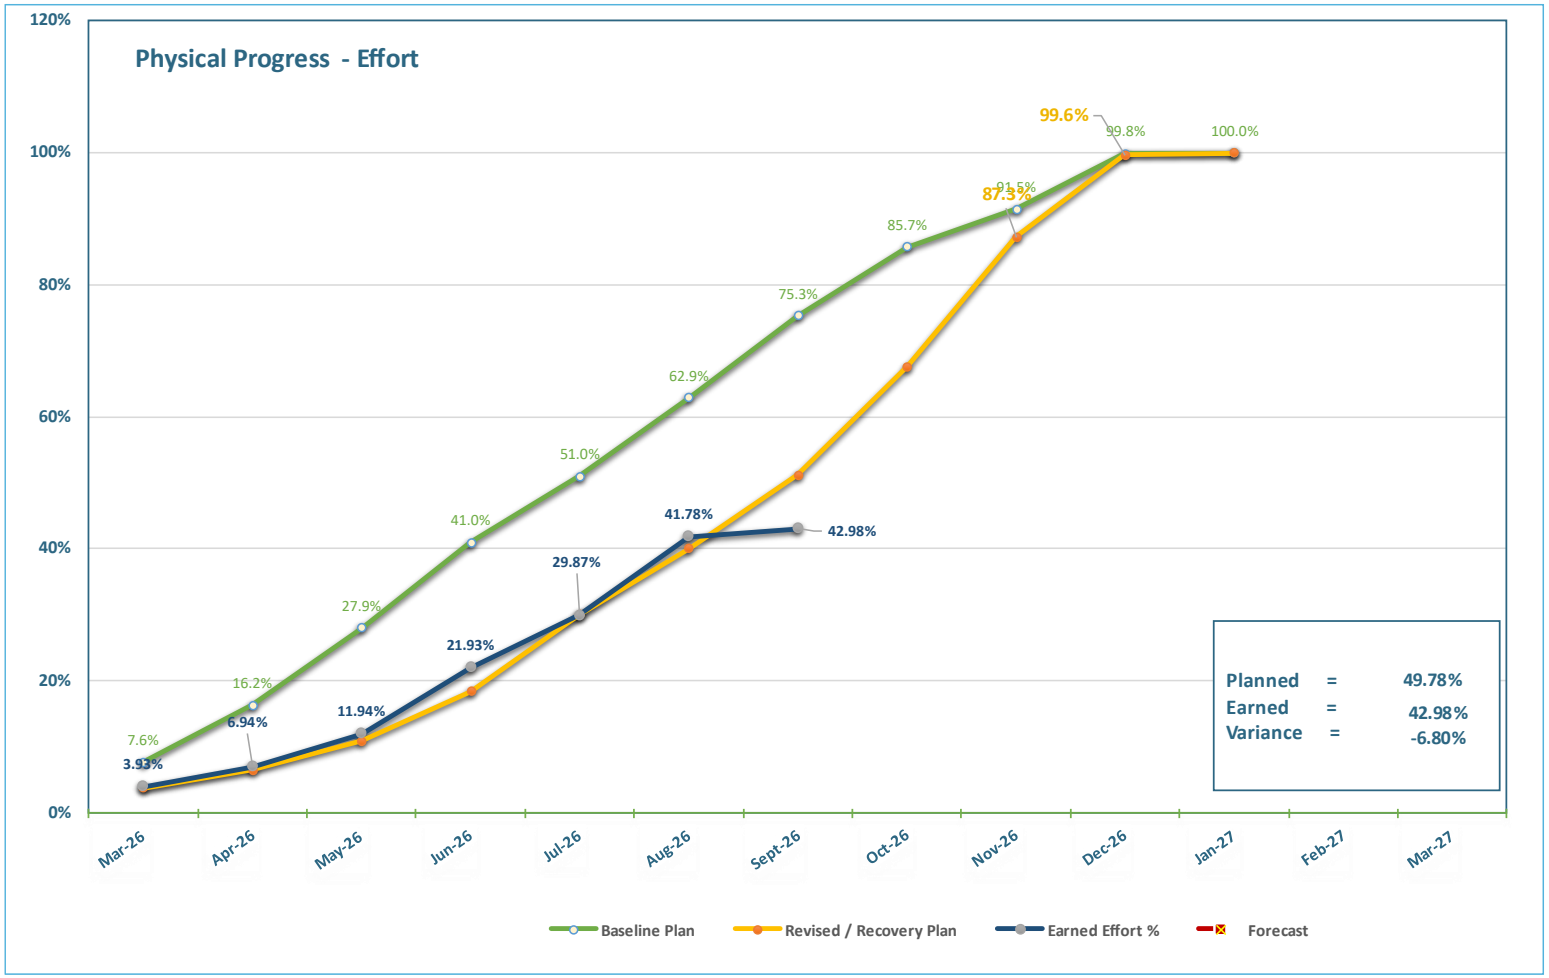

Weekly Report Areas / Milestones

- **Construction Milestones**

Milestones Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam)						
Item No.	Milestones	Original (Baseline)	Latest	Forecast		Days Change
	Contract Duration **Current Contract Weeks : 25 of 44**	**44**	**44**	**59**		**(109)**
1	Project Commencement Date	03-Mar-26	03-Mar-26	03-Mar-26	A	**0**
2	Project Completion	02-Jan-27	02-Jan-27	21-Apr-27	F	**(109)**
3	Completion of Mobilization	01-Apr-26	02-Apr-26	02-Apr-26	A	**0**
4	Baseline Programme Approval	02-Apr-26	04-Apr-26	04-Apr-26	A	**0**
5	Completion of Engineering	02-Apr-26	28-Mar-26	29-Sep-26	F	**(185)**
6	Completion of Levelling Works	02-May-26	04-Jun-26	26-Sep-26	A	**(114)**
7	Completion of Toilet Building	02-Aug-26	26-Sep-26	22-Nov-26	F	**(57)**
8	Completion of Playground Area	24-Aug-26	02-Jan-27	18-Mar-27	F	**(75)**
9	Completion of Natural Landscape Works	02-Nov-26	19-Nov-26	21-Mar-27	F	**(122)**
10	Completion of Testing & Commissioning	21-Dec-26	26-Dec-26	08-Apr-27	F	**(103)**
11	Completion of Arar Works	21-Dec-26	04-Nov-26	02-Mar-27	F	**(118)**
12	Completion of Hasa Oasis Works	21-Dec-26	22-Dec-26	25-Oct-26	F	**58**
13	Completion of Dammam Works	21-Dec-26	29-Dec-26	06-Apr-27	F	**(98)**

Weekly Report Areas / Quality

- **Quality Reports**

Quality Reports									
Item	Issued	Closed	Pending	Avg. Closing (Days)	Pending				
					0-10 Days	11-20 Days	21-30 Days	31-60 Days	> 60 Days
Non Conforomance Report (NCR)	28	25	3	-	3	-	-	-	-
Site Instruction (SIR/SOR)	14	6	8	-	8		-	-	-
Material Inspection Report (MRIR)	150	146	4	-	4	-	-	-	-
Field Inspection Report (FIR)	743	734	9	-	9	-	-	-	-

Shop Drawings									
Item Per WBS	Total Planned	Total Drawings Submitted					Remaining Drawings	Pending Submittals With Consultant	Total Submittals
		A	B	C	D	Processed			
Civil/Structure	52	5	40	5	2	52	-	-	52
Architecture	29	5	17	5	2	29	-	-	29
Mechanical	25	-	22	5	-	27	2	4	31
Electrical	28	-	25	3	-	28	-	-	28
Landscape	15	1	8	4	-	13	2	-	13
TOTAL	**149**	**11**	**112**	**22**	**4**	**149**	**4**	**4**	**153**

Material Approval									
Item Per WBS	Total Planned	Total Materials Submitted					Remaining	Pending Submittals With Consultant	Total Submittals
		A	B	C	D	Approved			
Civil/Structure	29	-	27	-	1	27	2	-	**28**
Architecture	39	1	33	4	-	34	5	1	**39**
Mechanical	30	-	22	4	1	22	8	3	**30**
Electrical	43	-	32	8	3	32	11	-	**43**
	-					-			**-**
TOTAL	**141**	**1**	**114**	**16**	**5**	**115**	**26**	**4**	**140**

Procurement Summary							
Item Per WBS	Total Materials Planned	Total Number of P.O.	Actual P.O. To Date	Remaining P.O	Actual Material on Site	Remaining Materials	Material Delivery Completion (Date)
Civil/Structure	22	27	5	22	5	22	
Architecture	30	18	15	3	9	9	
Mechanical	30	18	10	8	10	8	
Electrical	35	13	7	6	4	9	
		-	-	-	-	-	
TOTAL	**117**	**76**	**37**	**39**	**28**	**48**	**00-Jan-00**

Weekly Report Areas / Quality

Quality Audit

QC OBSERVATIONS CHECKLIST

Project No.	MLTX-02-005	OBS No.	22	Inspection Day:	September 28, 2026
Project	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam)	Contractor: Consultant:	Profast Company Ltd. EGIS SAUDI ARABIA ENGINEERING COSULTANCY		

4	Excellent	Quality Management System is being practiced and applies to MODON System	90 - 100	QC Overall Score	85.88%
3	Good	Evidence of compliance with plans and procedures.	80 - 89		
2	Average	Indication level of compliance with standards but there is room for improvement	70 - 79		
1	Improve	Quality and Control is NOT being managed effectively. Needs Improvement	≤ 69		
0	N/A	Item was not applicable or this item was not reviewed during the inspection.	Zero		

No.	Topic	E (4)	G (3)	A (2)	I (1)	N/A (0)
1	Control of Access to Site/Office					
2	Document Control Administration					
3	Project Documents and Progress					
4	Contractor's Quality Plan/CM (Updated and Reviewed)					
5	MS Log and Paperwork					
6	RFI, FIR, & MIR Procedure					
7	RFI, FIR, & MIR Inventory system					
8	NCRs Control & Procedure					
9	NCR Log					
10	MODON Standard*					
11	Project Risk Plan/Management*					
12	Monthly Quality Reports*					
13	ITP					
14	MODON Weekly Report					
15	Design Change Official Paperwork*					
16	Design Change was Applied*					
17	Material List					
18	Pending Material Status					
19	Lifting Plan*					
20	DWG Log					
21	Invoice Status					
22	Site Handover Letter					
23	Material Testing Results & Certification					
24	As Build Drawings Status*					
25	Calibrated Lab Tools & Equipment					
26	Storage Inventory System					
27	Logistics Plan					
28	Project Progress Planview					
29	Sufficient Number of QC Inspectors					

No.	Topic	E (4)	G (3)	A (2)	I (1)	N/A (0)
30	QC of Excavation					
31	QC of Roads/Round about					
32	QC of Interlock & Curbstone					
33	Layers/Backfilling Sampling					
34	Pump Stations Units					
35	Quality of Form Work					
36	Design Change List					
37	Quality of Concrete Placing					
38	Concrete Surface Finishing					
39	Pedestals/Columns/Beams Alignment					
40	Siporex Lifting & Unloading					
41	Siporex Quality Pre-installation					
42	Siporex Finishing Quality					
43	Roads / Parking Markings					
44	QC of Finishing Outdoors					
45	Quality of Finishing Indoors					
46	Stairs Quality					
47	Tanks Method Statement Work					
48	Electric Rooms					
49	QC of MCC/ATS Plant Units					
50	Qualified Subcontractor					
51	Scaffold/Ladders/Slope/Bridge Compliance					
52	Protection Applied to Completed Work					
53	Storage Management in/out Control					
54	Material Control					
55	Manholes Storing and Quality					
56	Reinforced Steel Quality					
57	Safety Overview					
58	Waste Management Control					

Prepared by:	Eng: Mahfouz Zaki	Issued to PM:	Engr. Abdallah Aljulaifi

*QC Observations refer only to the practices and documentation observed at time of inspection. The responsibility of the CM and Contractor is to ensure that aspects of Quality are suitably managed.
*Scores are a reflection of the general site conditions based upon the findings at the time of the walk through
*If Applicable

Weekly Report Areas / HSE

- **Health, Safety & Environmental (HSE)**

Safety Statistics					
Category	**Item**	**This Week**	**This Month**	**Year to Date**	**Cumulative**
Category	Total Hours Worked	1305	5619	32352	32352
	Safe Hours Worked	1305	5619	32352	32352
Reactive	LTI	0	0		0
	MTC (Healed w/o Disability	0	0	0	0
	MTC (Healed w/ Disability)	0	0	0	0
	Near Miss	0	0	0	0
	First Aid Cases	0	0	0	0
	Fatality	0	0	0	0
	Fire Incident Cases	0	0	0	0
	Vehicle Incident	0	0	0	0
	Property Damages	0	0	0	0
Proactive	Induction Training	1(9)	3(13)	28(96)	28(96)
	No.of Internal Training	0	0	2(20)	2(20)
	No.of Internal Audit	0	3	5	5
	No. of Toolbox Talks	3(24)	13(174)	91(705)	91(705)
	Safety Awards/Incentives	0	0	0	0

Weekly Report Areas / HSE

- **Health, Safety & Environmental (HSE) Audits**

MODON HSE Site Inspection Report

Date:	28-Sept-26	Inspected By:	Engr.		
Project ID.	MLTX-02-005	Report No.	22	MODON PM Name	Engr. Mohamed Alisa
Project Name:	Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam)	Contractor:	Profast Company Ltd.	Safety Performance	86.46%

Inspections are a snapshot in time and refer only to the practices and documentation observed at the time of the Inspection. It remains the responsibility of the Consultant and Contractor to ensure that all aspects of Health & Safety are suitably managed.

	Good Practice		Need Improvement		Fail (Life Threatening Activity) / Comliance with Plan & Procedures	N/A	Atcitty Not Applicable for this Site Inspection Report

No.	Topic	HSE Compliance
1	Access and Egress - (General access to site, segregated from vehicles, / Overhead protection, while entering into the building /Adequate lighting provided when dark or overnight work)	
2	Traffic Management - (Loading/unloading/sheeting/temp. routes/speed/parking/competence)	
3	Site Signage - (Project Notice Board & General Signage)	
4	PPE Compliance - (Use, storage, stock, handling & checks - Head, Foot, Eye, Hearing)	
5	Housekeeping - (Material correctly stored/Rubbish cleaned & removed daily/slips & trips hazards)	
6	Storage of Materials - (Transporting, storage, training and use - Combustible / Flammable / Hazardous substances (COSHH)	
7	Site Waste Management - (Hazardous waste /Combustible waste / Human waste / Construction waste - asphalt, cable, timber, paving roof sheeting tiles, plastic & bricks)	
8	Health Surveillance - (Expose to excessive noise/vibration/dust/silica/CO/cement/radiation/extreme weather condition)	
9	Electrical Safety - (Electrical qualified /RCD/GFCI/Industrial Cocket/LOTO/Cable-overhung or buried/Cords in good condition/current inspection tag)	
10	Tools & Equipment - (Includes, powered, hydraulic & pneumatic/Guards in place/Properly stored/RCD Protection/Earthed/Good condition & tagged)	
11	Manual Handling - (Lifting/loading/pulling/pushing/twisting/awkward posture/repetitive task/frequent and prolong physical effort/Reasonable practicable use of mechanical aid)	
12	Vehicle and mobile equipment / Plant - (dumpers; excavators, cranes, piling rigs, grader, roller, loaders/condition/KSA License/certification)	
13	Lifting Operations & Rigging - (Lifting Plan/Lifting devices & gears/PTW/Condition/3rd party certification/bank-man/rigger/slingers/man-basket/inspection record/tagged)	

No.	Topic	HSE Compliance
14	Work at Height - (PPE/Fall Protection(Same level, above and blow) / Training / Fall restraint / competency /Safe access & egress to and from work at height / Ladders / Openings (floor/shafts/Provision of emergency rescue)	
15	Scaffolding - (Temp. Scaffolding Work-platform (All types) - qualified scaffolder / Inspection / Tagged / Safe Access/egress / PTW/Falsework & Formwork)	
16	Mobile Elevated Work platform (MEWP) - (PTW/competence requirements/conditions/inspections/tagged/training/Full-body harness)	N/A
17	Excavation & Trenches - (PTW/Edge protection/buffer zone/Slope/Benching/Shoring/Geo-tech report/Atmospheric hazards/Acess&egress/Emergency management / MS&RA/H.E)	
18	Confined Space - (PTW/Training/competence/Emergency Management/MS & RA/Safe access/egress)	N/A
19	Fire Protection - (Flammable/Oxy. LPG /Combustible separated/FE's/Flashback arrestor/Sparks & slags/Smoking area/PTW/Generators/MS & RA/Emergency Management)	
20	Health & Welfare - (Adequate drinking water/shaded - eating & rest area/washing & sanitary facilities/Certified FA/FA Box & Stock/adequate toilets/Ambulance)	
21	Environmental Incident Measures - (Spill/ Leakage / Concrete wash / vehicle & eqpts. wash / waste disposal/Sewers and drains/emissions/Emergency Management/Training/site run-off water)	
22	HSE Communications & Meetings - (Schedule HSE Meetings/Safety Committee meetings/Alerts / Lesson learned/Safety Bulletin contains latest HSE KPI)	
23	HSE Plan & Associated Procedures - (Approved updated HSE Plan/ CEMP/HAZComm/Procedures/Standards/Project Safety Risk Register)	
24	Health, Safety & Environment Incident reporting - (Review of HSE Statistics, Reporting of Unsafe Act & Conditions/ Reporting of Near Miss incident/Reporting of FA cases/Record MT cases)	
25	HSE Awareness, Training & Competence - (Policy /Objective & targets/Information, training/Climatic condition awareness/Reponses in emergency situation/ Safety Behavior Observation)	
26	Project Leadership Site Tours - (Provide evidence of proactive safety performance/Deficient discovered discussed/Positive feedback/Workers resolving safety issues)	

Prepared by:	yasir janat	Sent to MODON PM:	Engr. Abdallah Aljulaifi

Safety Results					
	11		13.00		0

Weekly Report Areas / Invoices

- Invoice Log

Weekly Progress Report - Invoice Log

Project Value				Payment Status				Invoices Summary						Average Invoices durations	
Original Contract Value	29,997,851.67	O&M Value	0.00	Advance Payment %	0%	Advance Payment (SAR)	0.00	No of Submitted Invoices	4	Submitted Invoices (SAR)	3,673,916.30	Submitted Invoice Period	21-Sep-26	CM / PgM Average Approval duration	0
Revised Contract Value	29,997,851.67	Revised O&M Value	0.00	Retention %	0%	Retention (SAR)	0.00	No of Approved Invoices (CM)	4	Approved Invoices (CM) (SAR)	2,851,846.24			MODON PM & Accounts Average Approval duration	1
Estimate At Completion Value	29,997,851.67	Submitted Invoices (Gross Value)	3,673,916.30	Penalties and deduction %	0.2%	AP Recovery (SAR)	0.00	No of Approved Invoices (PM)	3	Approved Invoices (PM) (SAR)	1,918,913.81	Invoice Submitted Compared to Contract Value	12.25%	Payments Average Duration	#DIV/0!
Potential Changes	0.00	Total Deduction	-53,000.00	Penalties and deduction (SAR)	-53,000	Retention Cumulative (SAR)	0.00	No of Paid Invoices	0	Paid Invoices (SAR)	2,178,750.88			Invoices Average total Duration	

Invoice Reference				Invoice Value					Period Covered		CM / PgM Approval Timeline				Modon PM & Accounts Approval							Payment Status						
#	Invoice No.	Doc Control reference	Submittal Rev. #	Gross Value	AP Recovery	Retention	Deduction / Penalties	Amount (net) + VAT 15%	Start Date	End Date	Date to CM / PgM	CM / PgM Approval (Yes/No)	CM / PgM Reply Date	Days Elapsed	Date to PM	PM Approval (Yes/No)	PM Reply Date	Date to Accounts	Accounts Approval (Yes/No)	Accounts Approval Date	Days Elapsed	Date Paid	Amount Paid	Paid %	Payment Period (d)	Amount Pending	Total Invoice Duration	Remarks
1	1	MLTX-02-005-PRO-TS9-1-IPC-DSF-0001-02	02	386,851.26	0.00	0.00	(25,000.00)	419,878.95	03-Mar-26	13-Jun-26	18-Jun-26	Y	18-Jun-26	0	21-Jun-26	Y	21-Jun-26	21-Jun-26	Y	22-Jun-26	1		419,878.95	100.0%		0.00		
2	2	MLTX-02-005-PRO-TS9-1-IPC-DSF-0002-00	00	614,971.62	0.00	0.00	0.00	707,217.36	14-Jun-26	06-Jul-26	06-Jul-26	Y	06-Jul-26	0	06-Jul-26	Y	08-Jul-26						707,217.36	100.0%		0.00		
3	3	MLTX-02-005-PRO-TS9-1-IPC-DSF-0003-01	01	917,090.93	0.00	0.00	(3,000.00)	1,051,654.57	07-Jul-26	05-Aug-26	06-Aug-26	Y	06-Aug-26	0		Y							1,051,654.57	100.0%		0.00		
4	4	MLTX-02-005-PRO-TS9-1-IPC-DSF-0004-01	01	932,932.43	0.00	0.00	(7,000.00)	1,065,872.29	06-Aug-26	26-Aug-26	29-Aug-26	Y	29-Aug-26	0													
5	5	MLTX-02-005-PRO-TS9-1-IPC-DSF-0005-01	01	822,070.06	0.00	0.00	(18,000.00)	927,380.57	27-Aug-26	21-Sep-26																	

Weekly Report Areas / CCOs

- **Contract Change Orders (CCOs)**

CONTRACT CHANGE ORDER (CCO)							
CCO No.	Date Added	Description of Change	Status	SR	Sch Impact (Months)	Date Approved	Duration (days)


Weekly Report Areas / Quantities


- **Major Quantity Trackers**

BOQ Number	Description of Item	Total Quantity	Unit of Measurement	Plan To Date	Actual To Date	Remaining Total	Variance	Variance %	Notices
2.1.1	Excavation in any type of soil from existing level	10,295	m^3	10,295	4,509.53	5,785	-5,785	-56.20%	
2.1.2	Backfilling with selected fill material	10,266	m^3	10,266	2,992.24	7,274	-7,274	-70.85%	
2.3.1.2	stamped concrete	1,800	m^2	1,800	163.28	1,637	-1,637	-90.93%	
2.3.1.5	Bike path	2,300	m^2	2,300	133.79	2,166	-2,166	-94.18%	
2.3.1.6	Walking path	2,200	m^2	2,200	130.05	2,070	-2,070	-94.09%	
2.3.2.3	'Kerb type K4	9,080.00	L.m	9,080	636.74	8,444	-8,444	-92.99%	
2.3.5.1	Football playground	3,000	m^2	3,000	148.88	2,851	-2,851	-95.04%	
2.3.5.2	padel playground	600	m^2	600	240.00	360	-360	-60.00%	
2.3.5.3	Basketball playground	1,530	m^2	1,530	484.37	1,046	-1,046	-68.34%	
2.3.9	oxes and MDBs: - all the required electrical connections to the main source excluding KWIL:- logo: - main air package u	3	item	3	0.25	3	-3	-91.60%	
3.1.1	lean concrete under foundation	9	m^3	9	3.26	6	-6	-63.78%	
3.2.1	Tank foundation	9	m^3	9	15.45	-6	6	71.67%	
3.2.2	Tank Walls	18	m^3	18	11.52	6	-6	-36.00%	
3.2.3	Tank Slab	9	m^3	9	7.45	2	-2	17.22%	
3.3	st 35 Mpa concrete floor slab on grade including but notlimited to construction joints, control joints, as per drawings ar	45	m^3	45	46.17	-1	1	2.60%	
3.4	The autoclaved aerated panel for slabs, external and internal walls and parapet with lintels for all openings with necessary joining reinforcement between walls, straps, filler board and steel reinforcement and whatever needed to do a perfect work all as per drawings and specifications	750	m^2	750	693.30	57	-57	-7.56%	
4.1.1	Concrete masonry unit, 100 mm thick wall	135	m^2	135	129.42	6	-6	4.13%	
7.1	Supply and lay 250 micron thk polyethylene sheet under grade slab	270	m^2	270	288.75	-19	19	6.94%	
7.2	Supply and apply anti termite under all concrete in contact with soil.	270	m^2	270	288.75	-19	19	6.94%	
7.5	Provide and lay 2 layers of waterproofing membrane 4mm including 1 layer protection board for RC footings and RC walls in contact with soil according to the drawings and specification	60	m^2	60	101.55	-42	42	69.25%	
7.6	Provide and lay epoxy 2 coating for inner surfaces for RC walls, RC footings and bottom of the roof	75.00	m^2	75	72.84	2	-2	-2.88%	
9.2.2	Supply and install plastering to walls and min. 15mm thick with cement mortar of specified grade including galvanized mesh, corner beads, angle beads, CE bonds to rough and smooth plaster complete the work as per drawing and specification.	471.00	m^2	471	551.07	-80	80	17.00%	
15.2.1.1	Pipe with 65 mm Ø Cold water	18.00	lm	18	7.34	11	-11	-59.22%	
15.2.1.2	Pipe with 50 mm Ø Cold water	12.00	lm	12	24.46	-12	12	103.83%	
15.2.1.3	Pipe with 40 mm Ø Cold water	3.00	lm	3	7.22	-4	4	140.67%	
15.2.1.4	Pipe with 32 mm Ø Cold water	6.00	lm	6	2.08	4	-4	-65.33%	
15.2.1.5	Pipe with 25 mm Ø Cold water	12.00	lm	12	6.06	6	-6	-49.50%	
15.2.1.6	Pipe with 20 mm Ø Cold water	21.00	lm	21	58.06	-37	37	176.48%	
15.2.1.7	Pipe with 20 mm Ø Hot water	66.00	lm	66	66.70	1	1	1.06%	
15.2.2.1	50 mm Ø	200.00	lm	200	28.00	172	-172	-86.00%	
15.3.1.1	Pipe with Ø 4" (110mm)	63.00	lm	63	76.83	-14	14	21.95%	
15.3.1.2	Pipe with Ø 3" (75mm)	39	lm	39	28.68	10	-10	-26.46%	
15.3.1.3	Pipe with Ø 2" (50mm)	60	lm	60	104.74	45	-45	74.57%	
15.3.1.4	Pipe with Ø 1" (25mm)	15	lm	15	11.26	4	4	-24.93%	
15.3.7	Supply and install 150 mm uPVC pipes to external wastewater network as specified on drawings including coordination with Authorities, supplying and installing manholes, pipeworks, earthworks (excavation, backfilling,...etc.), cutting asphalt, civil works, reinstatement of surfraces, concrete encasment (if required), ancilliary works etc.All complete as specified and as approved by Authority and to the discretion of the Engineer	50.00	m	50	126.81	-77	77	153.62%	
15.4.1	Supply, install, test and commission inline exhaust fans duct mounted AMCA,UL listed, direct drive complete with grill, supports, controls, accessories and as per drawings and specification.	3	NOS	3	1	2	-2	-66.67%	
15.4.3	Supply, install, test and commission indoor ductwork as per SMACNA Standards, complete, VD, duct tape, Flexible Duct adhesive, duct sealant, hangers, supports and all other accessories, (Flanged TDC Type) and as per drawings and specification.	300	KG	300	46.33	254	-254	-84.56%	
15.5.1.1	pipe line O.D 90 mm PN 10, in depth 0 to 1.5 m	750	m	750	34.77	715	-715	-95.36%	
15.5.1.2	pipe line O.D 50 mm PN 10, in depth 0 to 1.5 m	350	M	350	10.59	339	-339	-96.97%	

Weekly Report Areas / Resources

- Resources

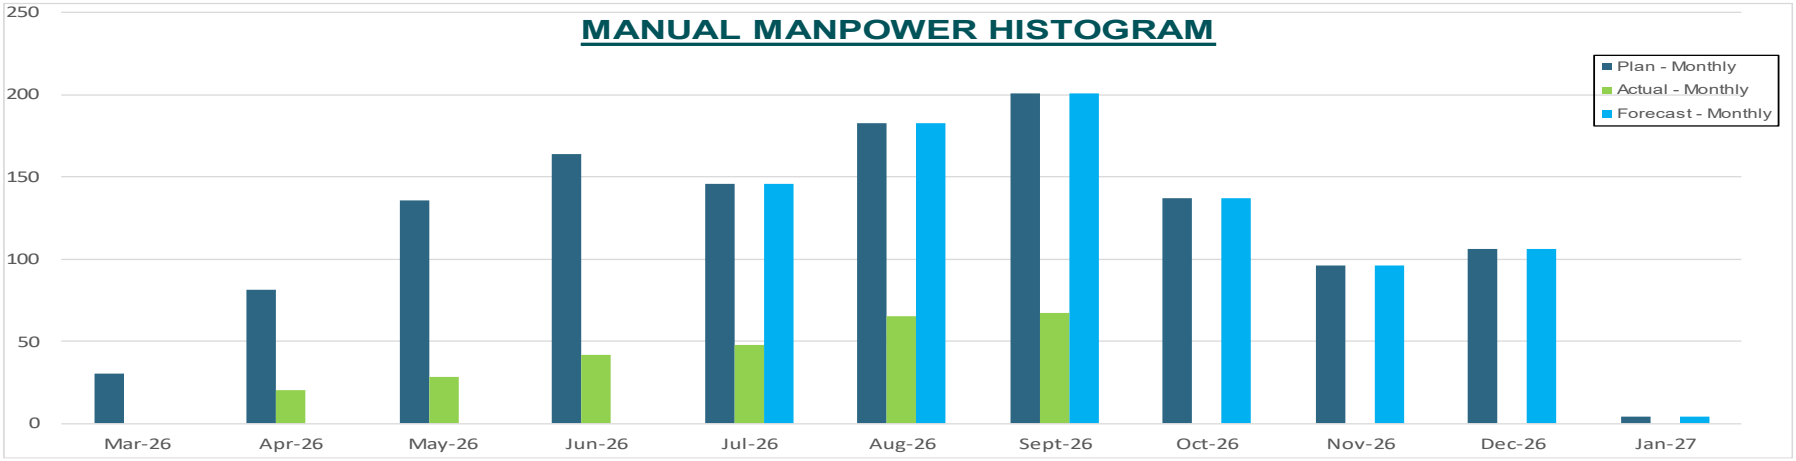

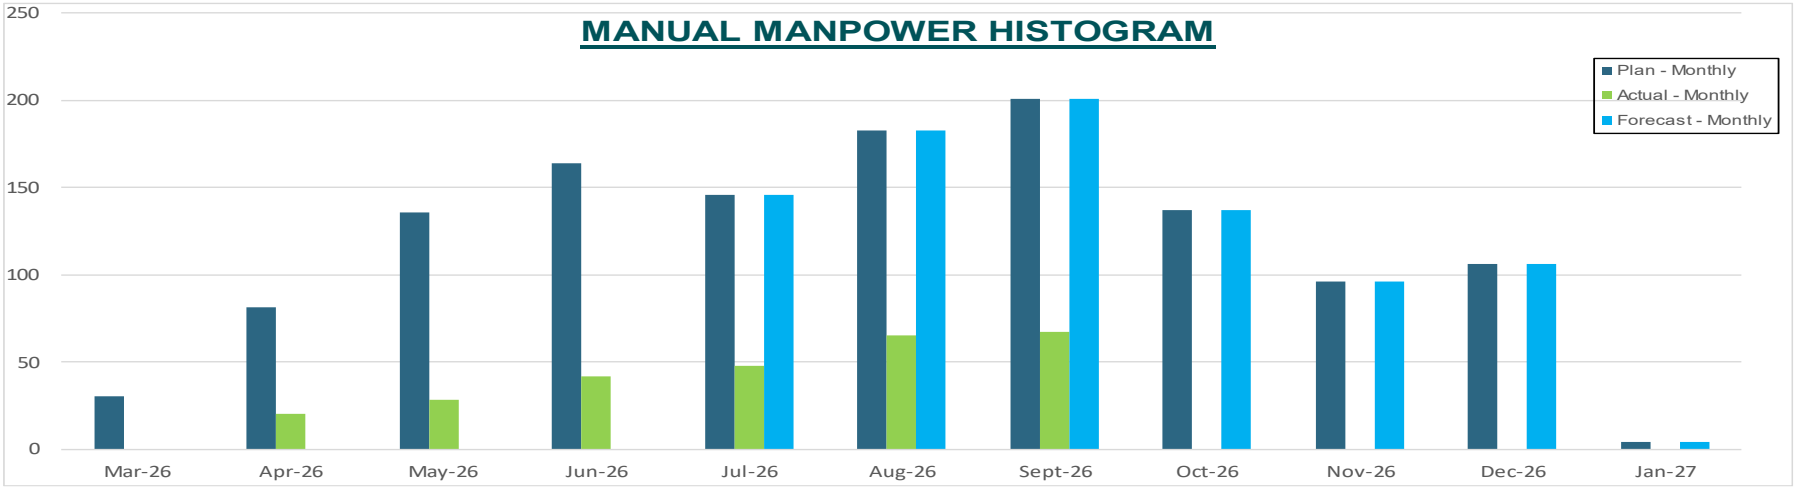

Weekly Report Areas / Schedule Status

- **Primavera P6 Schedule Status**

Primavera P6 Schedule Status									
Project Activities Overview									
Schedule Statistics					Active Schedule Activities				
Total Act.	Not Started	In Progress	Completed	%	Active	Ahead	On	Behind	Flag
2,150	464	16	1,670	77.67%	16	9	0	7	2
Critical Path Activities			Free Float Management (Total)				Failed Start Activities		
			Greater Than 14 Days		Less Than 14 Days				
Last Week	This Week	Diff	Last Week	This Week	Last Week	This Week	Last Week	This Week	Flag
243	268	-25	182	160	299	318	329	326	3

Weekly Report Areas / Testing and Commissioning

- Testing And Commissioning

Testing and Commissioning									
Item	Planned Start Date	Planned Finish Date	Forecast Start Date	Forecast Finish Date	Actual Start Date	Actual Finish Date	% Completed	Open Comments	Closed Comments
Test for Toilet/Service Building	25-Nov-26	30-Nov-26	10-Apr-27	14-Apr-27			0%		
Test for Playground Area	15-Oct-26	21-Oct-26	13-Feb-27	18-Feb-27			0%		
Test for Landscape Works	24-Dec-26	29-Dec-26	01-Apr-27	06-Apr-27			0%		

Weekly Report Areas / Issues

- **Active Issues**

Issue Log							
Issue No	Date Identified	Issue Description	Responsibility	Action Taken	Current Status	Expected/Actual Closure	Duration Elapsed
1	20-Apr-26	Approval of Air Dome Design	Contractor	Submission dates revised in the tracking log; additional resources assigned to expedite the preparation and checking of drawings	Closed	7-Sep-26	**140**
2	3-Apr-26	Completion of Shop Drawing Submittal	Contractor	Submission dates revised in the tracking log; additional resources assigned to expedite the preparation and checking of drawings	Open	5-Oct-26	**185**
3	4-Apr-26	Completion of Material Submittal	Contractor	Submission dates revised in the tracking log; additional resources assigned to expedite the preparation and checking of drawings	Open	5-Oct-26	**184**
4	13-May-26	Calculations of Electrical Load	Contractor	The Calculation of Electrical Load depend on design approval for Air Dome which is under Review from Modon	Open	5-Oct-26	**145**


Thanks
