Infrastructure Network Development, Sudair City for Industry and Business

تطوير شبكات البنية التحتية بالمنطقة الصناعية بسدير المرحلة الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Eng. Zyad Al Shabat	06-Jan-2026	05-Jul-2027

Scope: roads and paving, potable water, TSE, sewer, storm water, irrigation and landscaping, electrical (medium voltage, telecom, street lighting) and CCTV networks in Zones A and G, over 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 09-Nov-2026 the project is 47.9% complete against 45.9% planned, 2.0% ahead (SPI 1.04). This week it gained 1.13% against 2.25% planned, half of the plan, so the lead narrowed from 3.1% to 2.0%, the fourth weekly drop in a row. Potable water, electrical and road works earned most of the week's man-hours. Road works and the storm, sewer and potable water networks are ahead; procurement, engineering, electrical works and CCTV are behind.

PHYSICAL % COMPLETE

47.9% / 45.9% plan

▲ SPI 1.04 +2.0%

PROGRESS THIS WEEK

+1.13% / +2.25% plan

▼ 1.12% below the weekly plan

CONTRACT TIME ELAPSED

56.3% · day 307 of 545

● P6 finish 05-Jul-2027

INVOICED TO DATE (GROSS)

20.6% · 34.7M SAR

5 invoices, last period ends 28-Oct-2026

Ahead overall, but the lead keeps shrinking and procurement is still behind.

This week's progress (1.13%) was half of the weekly plan (2.25%). Storm water earned 815 of 7,965 planned man-hours, sewer 35 of 2,549 and CCTV none of 1,147. Procurement is at 60.4% against 99.9% planned (SPI 0.61): MV cables (0 of 51,500 m), unit substations, street lighting poles and lighting panels are still not delivered, and the final substation location is still pending between the Client and SEC. The P6 update still finishes the project on 05-Jul-2027 with zero float, but it moved road works, MV works and all network works 7 to 8 days later, and finishing works now have only 0.7 days of float.

Site photos this week

The six photos from the "Weekly Progress Photos" sheet of the 09-Nov-2026 weekly report, with the sheet's captions. Two carry a date stamp (05 and 07-Nov-2026); none shows GPS. Five show road works in Zone A (prime coat, base course and the first asphalt layer) and one shows kerbstone concrete in Zone G. Select a photo to view it larger, then use the arrows to move between photos.



Prime coat (MC1) on base course, MCF0 Zone A

Spraying MC1 on the base course layer.



Base course compaction, Art MC10 Zone A

Compaction of the base course layer.



Base course compaction test, roundabout MC20 – Art MC10, Zone A

Compaction test of the base course layer.



First asphalt layer of the base course, MCG0 Zone A

Asphalt paving; stamp 07-Nov-2026 11:32.



Asphalt compaction, MCG0 Zone A

Compaction of the first asphalt layer of the base course.




Kerbstone concrete pouring, MCF0 Zone G

Concrete pouring for kerbstone; stamp 05-Nov-2026 12:11.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly points dated the 6th of each month; the latest actual (09-Nov) is shown on the November point. Source: Physical-Chart Data sheet. There is no revised plan.

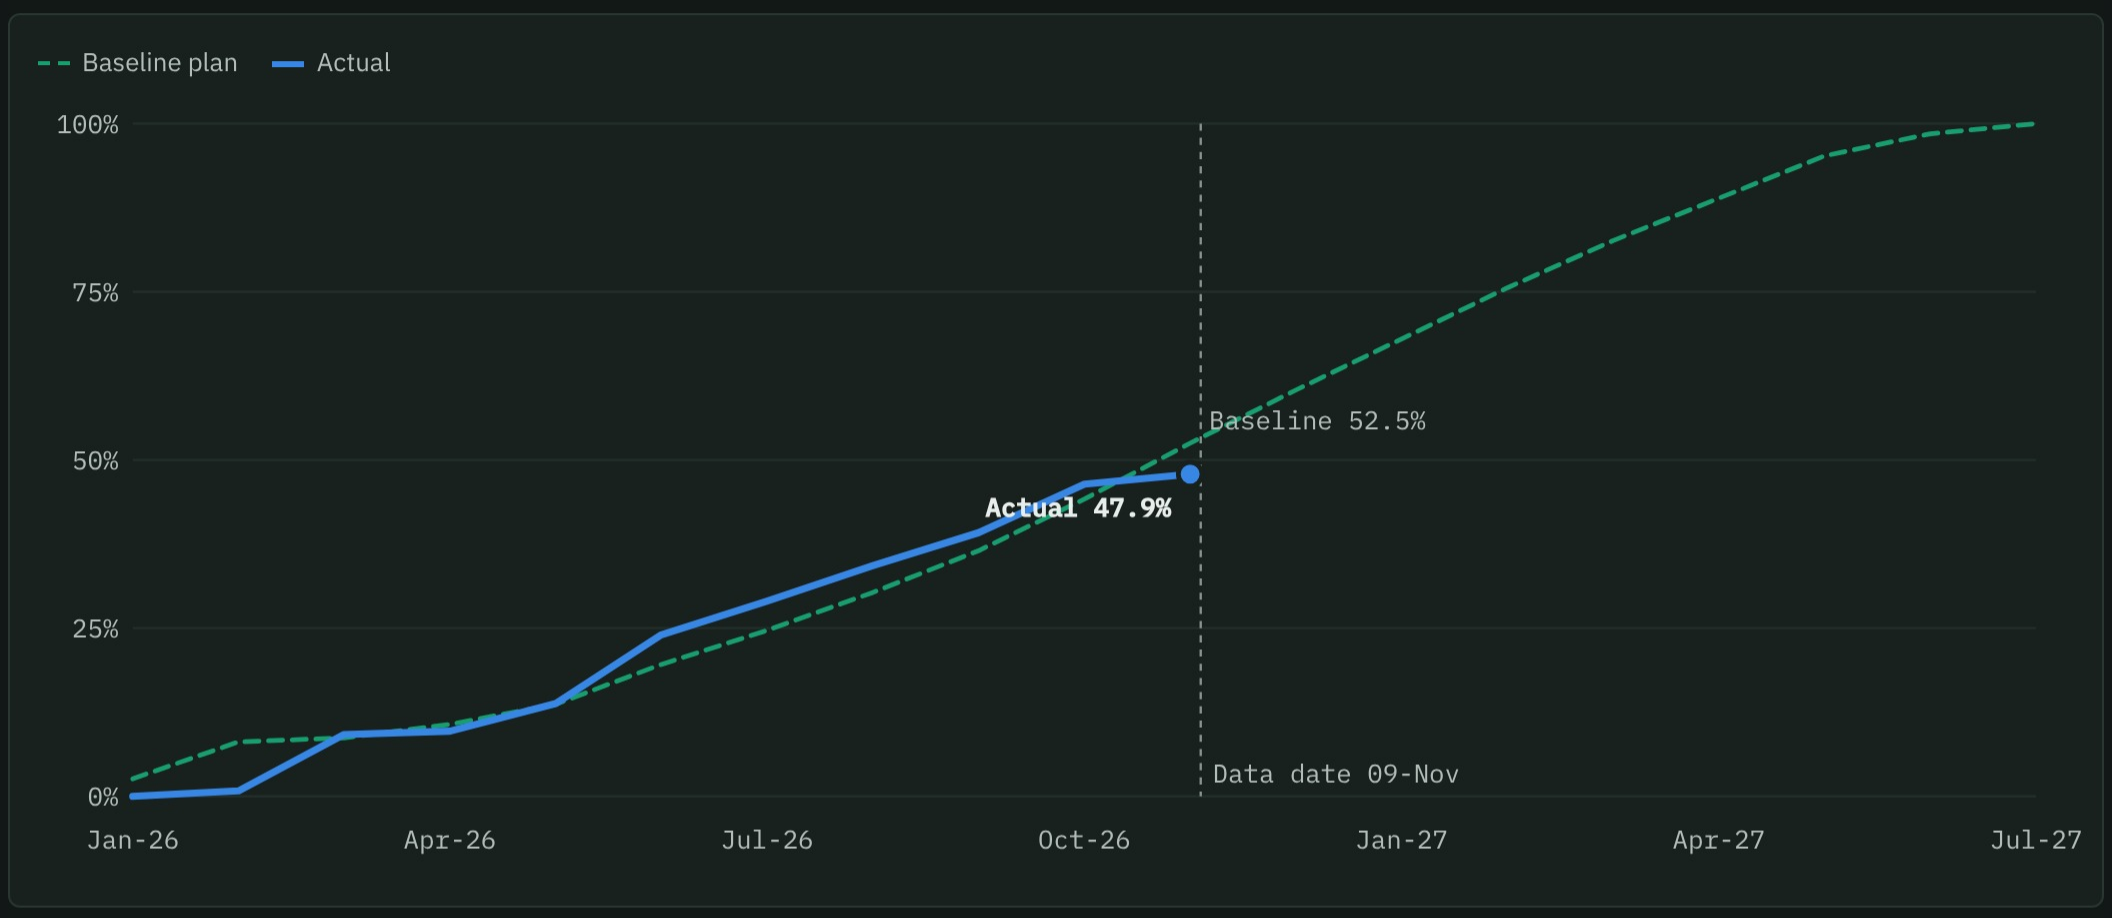

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	39.10	44.79	+5.69	–	1.15
19-Oct-2026	40.66	45.43	+4.77	+0.64	1.12
26-Oct-2026	42.15	46.41	+4.26	+0.99	1.10
02-Nov-2026	43.63	46.74	+3.10	+0.32	1.07
09-Nov-2026	**45.89**	**47.87**	**+1.98**	**+1.13**	**1.04**

Physical % complete from the weekly reports of 19-Oct, 26-Oct, 02-Nov and 09-Nov-2026. The 12-Oct-2026 row is the previous-week value in the 19-Oct report; its weekly gain is not stated. The chart's baseline plans 52.5% at 06-Nov, while the weekly report plans 45.9% to 09-Nov; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Network rows are part of Construction; their weights are shares of the whole project. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5%	100.0%	93.4%	−6.6%	0.93	▼ Behind
Procurement	13%	99.9%	60.4%	−39.5%	0.61	▼ Behind
Construction	75%	33.2%	43.1%	+9.9%	1.30	▲ Ahead
· Road works	16.4%	80.3%	85.0%	+4.7%	1.06	▲ Ahead
· Storm water drainage	16.5%	28.8%	46.8%	+18.0%	1.62	▲ Ahead
· Sewerage	5.5%	16.3%	72.7%	+56.4%	4.45	▲ Ahead
· TSE	7.7%	0.0%	7.7%	+7.7%	–	▲ Started early
· Potable water	12.3%	0.0%	18.0%	+18.0%	–	▲ Started early
· Electrical works	8.7%	63.7%	40.2%	−23.4%	0.63	▼ Behind
· Landscape & irrigation	6.8%	0.0%	4.7%	+4.7%	–	▲ Started early
· CCTV	1.2%	48.1%	12.2%	−35.9%	0.25	▼ Behind
Testing & commissioning	2%	0.0%	0.0%	0.0%	–	● Not yet due
Close-out	2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**45.9%**	**47.9%**	**+2.0%**	**1.04**	▲ Ahead

The P6 update (data date 09-Nov-2026) has 2,115 activities: 823 completed, 351 in progress and 941 not started. Its scheduled finish is 05-Jul-2027, the contract completion date.

Scope of work: quantities

Quantity executed on site for the major items, from the Major Quantities sheet of the 09-Nov-2026 weekly report. "This week" is the change since the 02-Nov-2026 report. The report gives no zone split. The scope table on the report's summary page shows no executed quantity for any network and was not used.

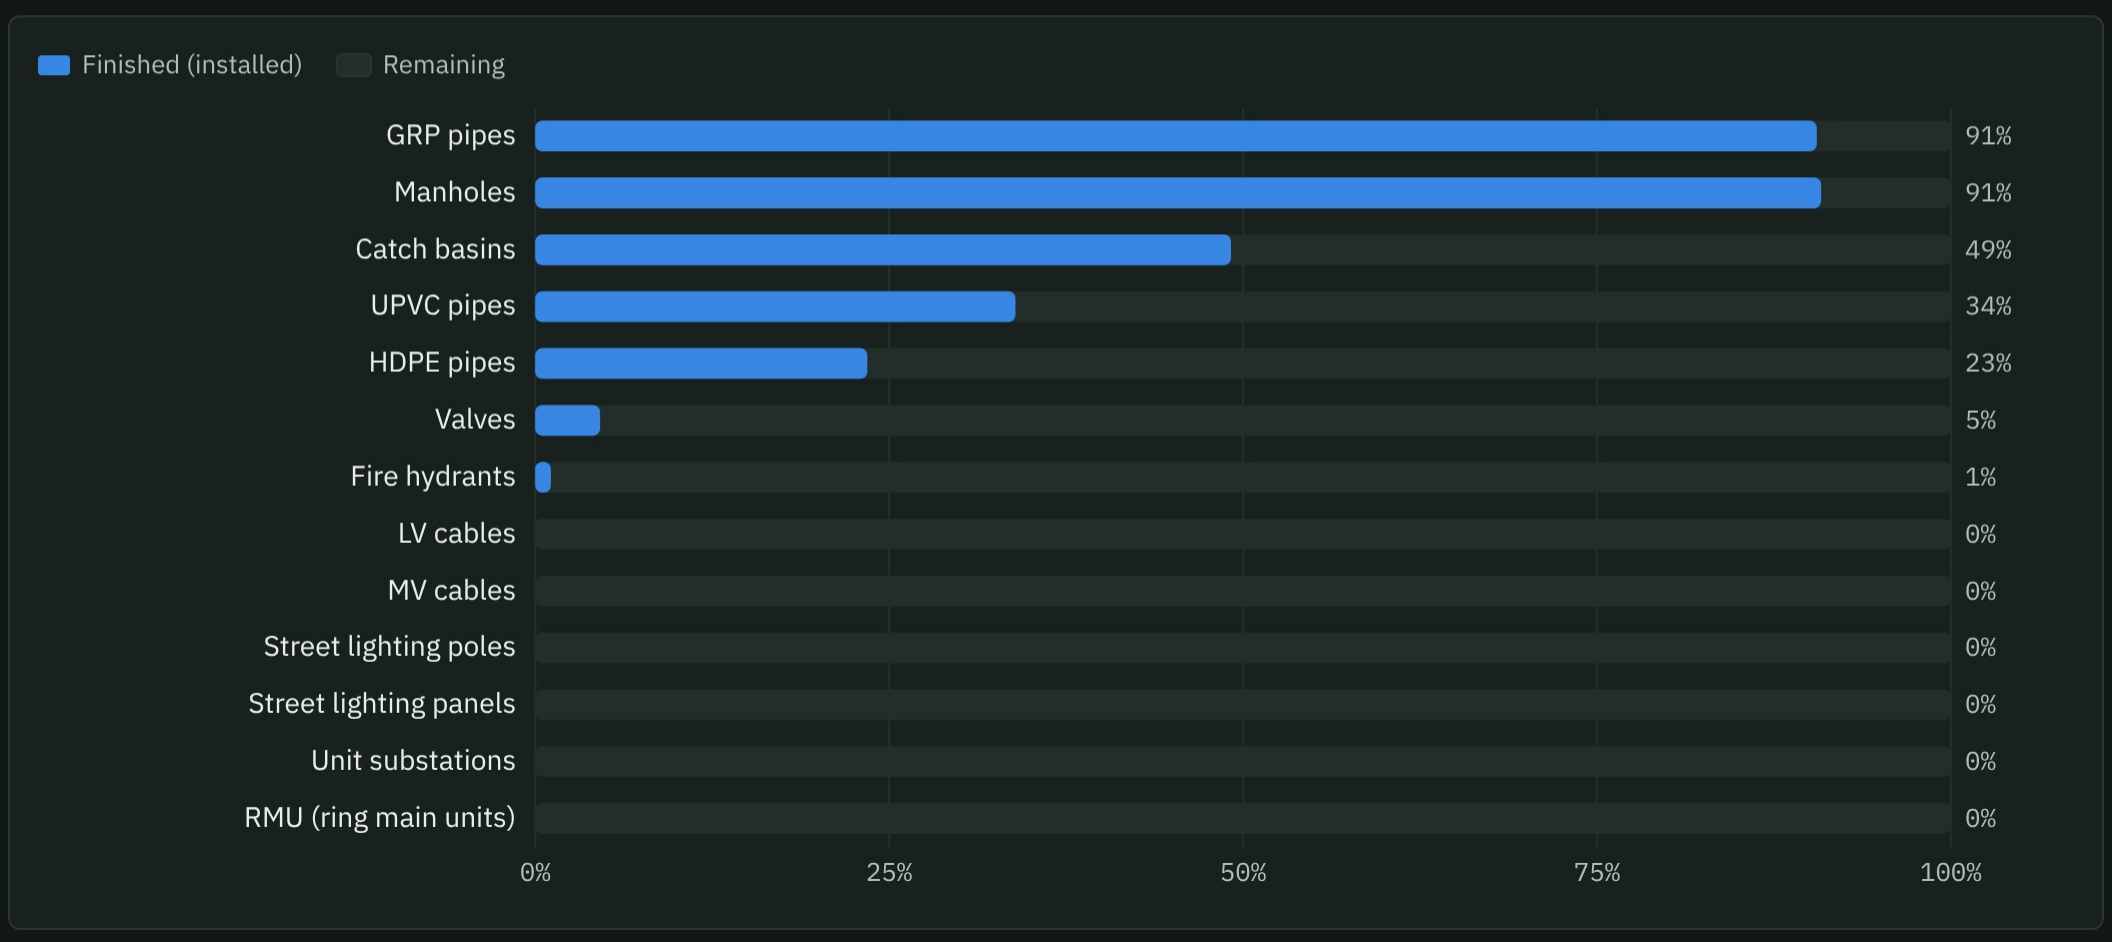

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
GRP pipes	All zones	m	18,337	16,600	+100	1,737	90.5%	–
Manholes	All zones	EA	251	228	0	23	90.8%	–
Catch basins	All zones	EA	295	145	+5	150	49.2%	–
UPVC pipes	All zones	m	4,716	1,600	+100	3,116	33.9%	–
HDPE pipes	All zones	m	28,557	6,700	+200	21,857	23.5%	–
Valves	All zones	EA	218	10	0	208	4.6%	–
Fire hydrants	All zones	EA	90	1	0	89	1.1%	–
LV cables	All zones	m	68,400	0	0	68,400	0.0%	–
MV cables	All zones	m	51,500	0	0	51,500	0.0%	–
Street lighting poles	All zones	EA	592	0	0	592	0.0%	–
Street lighting panels	All zones	EA	52	0	0	52	0.0%	–
Unit substations	All zones	EA	5	0	0	5	0.0%	–
RMU (ring main units)	All zones	EA	11	0	0	11	0.0%	–

Small additions to the wet networks this week

GRP pipes are 91% installed (16,600 of 18,337 m) and manholes 91% (228 of 251). Catch basins are at 49%, UPVC pipes 34% and HDPE pipes 23%. This week added 100 m of GRP pipe, 100 m of UPVC pipe, 200 m of HDPE pipe and 5 catch basins; no other item changed.

Not yet started or barely started

Fire hydrants (1 of 90) and valves (10 of 218) have barely started. No LV or MV cable, street lighting pole, lighting panel, unit substation or RMU is installed yet.

Milestones

The weekly report and the P6 schedule update give different dates for several milestones. Both are shown so the difference can be resolved with the contractor. Baselines for the last four contractual milestones are from the approved baseline schedule uploaded with the 19-Oct report.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	06-Jan-2026	06-Jan-2026	06-Jan-2026 (actual)	–	✓ Done
Mobilisation finish	05-Feb-2026	05-Feb-2026	06-Apr-2026 (actual)	–	✓ Done
Baseline submission	05-Feb-2026	06-Apr-2026 (+60 d)	06-Apr-2026 (actual)	–	✓ Done
Quality lab	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
RBF	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
Technical submittals (plans and materials)	05-Mar-2026	16-Aug-2026 (+164 d)	25-Jul-2026 (actual)	–	✓ Done late
Engineering phase finish	05-Mar-2026	28-Sep-2026 (+207 d)	09-Nov-2026	80	▼ Late
Procurement phase finish	23-Jan-2027	17-Jan-2027	12-Jan-2027	18	● On track
Medium voltage works complete	21-Jan-2027	–	04-Mar-2027	21	▼ At risk
All network works complete	04-May-2027	–	05-May-2027	47	▼ At risk
Road works complete	14-Apr-2027	–	05-May-2027	7	▼ At risk
Finishing works complete	05-Jul-2027	–	05-Jul-2027	0.7	▼ At risk
Project finish (all works)	05-Jul-2027	05-Jul-2027	05-Jul-2027	0	● On time

The weekly report and the P6 update disagree on four milestone dates, and P6 moved the network, road and MV milestones later again.

Mobilisation finished on 05-Feb-2026 in the weekly report but on 06-Apr-2026 in P6. Technical submittals finished on 16-Aug-2026 in the weekly report but on 25-Jul-2026 in P6. The weekly report forecasts the engineering phase to finish on 28-Sep-2026, while P6 keeps it open and moves it to each data date (now 09-Nov-2026). Procurement finishes on 17-Jan-2027 in the weekly report and 12-Jan-2027 in P6. In this week's P6 update road works moved 8 days later, to 21 days after their baseline (float 7 days, from 12); all network works moved 8 days later, now 1 day after their baseline (float 47 days, from 54); MV works moved 7 days later, to 42 days after their baseline (float 21 days, from 25); finishing works moved to 05-Jul-2027 (float 0.7 days, from 2.7). Project finish has no float left.

Procurement of key materials

Share of total quantity delivered to site. Source: Major Quantities sheet; asphalt, interlock and kerbstone from the completion rate in the Procurement sheet, weekly report 09-Nov-2026. No delivery figure changed this week.



MV cables: nothing delivered


0 of 51,500 m. The Procurement sheet lists the material approval as not submitted, with the cables required on site by 31-May-2026. The risk register says the cables have been procured and that the final substation location is still pending between the Client and SEC.

Street lighting, substations and paving materials

Street lighting poles 1 of 592 delivered, lighting panels 0 of 52 and unit substations 0 of 5 (approval not submitted). Kerbstone and interlock tiles are at 15% delivered and asphalt mix at 40%, unchanged from last week.

Manpower

Monthly head count on site (manual plus non-manual), planned vs actual. Source: Manpower sheet.

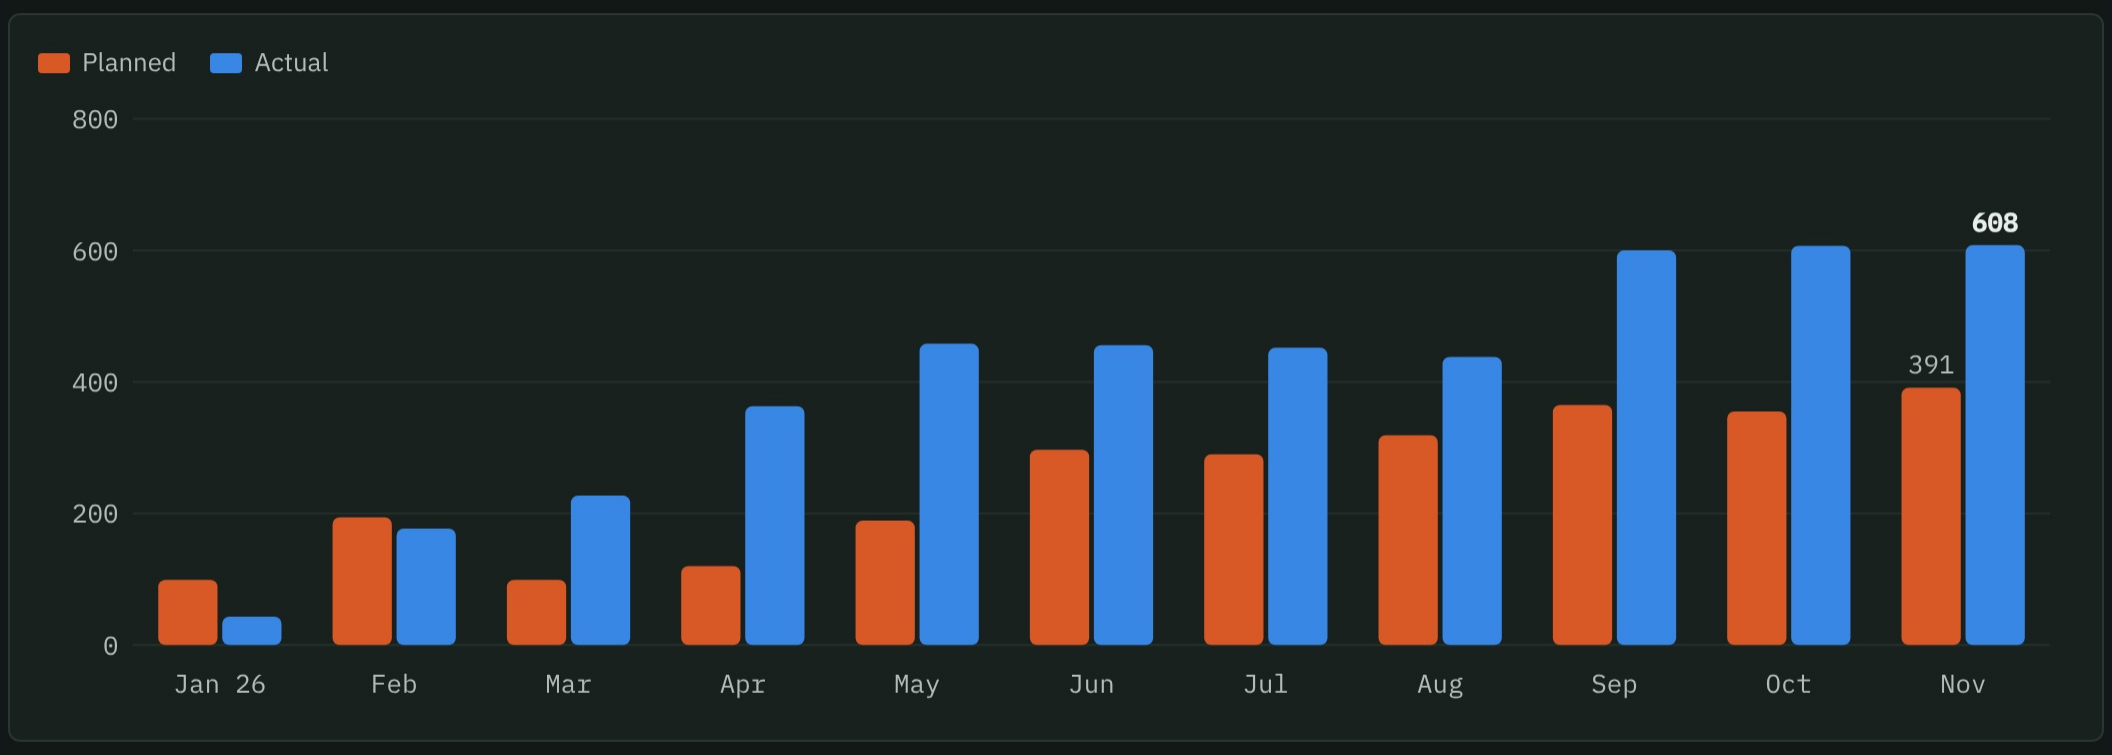

November head count is 608 (540 manual, 68 non-manual) against 391 planned (+55%), one more than in October. Actual head count has been above plan every month since February, yet this week's progress was half of the plan. The site has 332 pieces of equipment against 250 planned.

Cost and invoicing

Contract value

Road works	88,002,863
Storm water drainage network	25,405,198
Electrical works	20,082,302
CCTV works	9,305,708
Potable water network	7,779,405
Sewer network	7,071,027
Landscape & irrigation	6,835,461
TSE network	4,147,557
BOQ total (excl. VAT)	**168,629,520**
Contract value incl. 15% VAT	193,923,948
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. No change orders are registered.

Invoices

Invoices submitted	5
Gross value	34,697,865
Advance payment recovery (10%)	−3,469,787
Retention	0
Deductions and penalties	−35,000
VAT	4,684,212
Net incl. VAT	35,877,290
PM-approved / paid	0 / 0
Advance payment (10%)	16,862,952

Invoicing is 20.6% of the contract value against 47.9% physical progress. No invoice was added this week; the last, invoice 5 (10,122,463 gross), covers 01–28 Oct 2026. The invoice log shows none of the five invoices approved by the PM or paid yet; the first covers work up to 28-Jun-2026.

Health, safety and quality

Safety Score 83.0%

Safe man-hours (cumulative)	1,009,826
Man-hours this week	36,450
Man-hours this month (November)	48,590
Internal trainings (cumulative)	58
Toolbox talks (cumulative)	58
Consultant safety inspection score	80.7%
Safety observations logged / closed	19 / 19

All man-hours are reported as safe. The report does not state incident counts clearly.

Quality Score 91.0%

NCRs issued / closed / open	25 / 21 / 4
Site instructions issued / open	7 / 1
MIRs issued / open	249 / 4
FIRs issued / open	4,455 / 75
Shop drawings submitted / processed	424 / 340
Shop drawings pending with consultant	21
Material submittals processed	63 of 66

Open issues and risks

ISSUE	OWNER	DETAIL
Substation location (MV)	Client / SEC	The final substation location is still pending confirmation between the Client and SEC. The MV cable size was settled by RFI (answered 09-Feb-2026) and the contractor is building MV road-crossing ducts at its own risk. Further delay may affect testing, energization and handover. Rated high (5 × 5).
Landscape proposal approval	Client	The landscape proposal (RFI-0036, 23-Aug-2026) awaits Client approval, which is needed to finalise the landscape shop drawings and procure the materials. Rated medium.
Procurement behind plan	Contractor	Procurement is at 60.4% against 99.9% planned and has earned no man-hours for two weeks. Approval of MV cables, unit substations, KWH meters, the fence for electrical works and road marking is still not submitted.
Weekly output half of plan	Contractor	The project earned 12,926 man-hours this week against 25,655 planned. Storm water earned 815 of 7,965 planned (Zone A storm water is now 24.5% against 31.4% planned), sewer 35 of 2,549 and CCTV 0 of 1,147. Electrical works are at 40.2% against 63.7% planned and CCTV at 12.2% against 48.1%. P6 moved road works completion to 05-May-2027 (float 7 days).
Engineering not closed	Contractor	Engineering is at 93.4% against 100% planned, unchanged for four weeks, and P6 still has the engineering phase open. 4 NCRs remain open and 21 shop drawings are pending with the consultant (13 wet-network, 8 CCTV).

All 19 safety observations in the issue log (08-Sep to 05-Nov-2026) and 22 of the 24 risks in the register are closed.

Data notes

- The uploaded files name the project "Phase Two – Part Two" (SUD1-02-011), while the repository folder and the project tracker call it Phase 3 (المرحلة الثالثة).
- The summary sheet labels cost-based progress as "Plan" and "Actual". This report uses physical progress (man-hour weighted) only: 45.89% planned and 47.87% actual.
- The Physical-Chart Data sheet's baseline plans 52.5% at 06-Nov, well above the 45.89% planned to 09-Nov on the front sheet, and it shows the 09-Nov actual (47.87%) on the 06-Nov point. Measured against that chart baseline the project would be behind plan.
- The front sheet leaves physical progress for electrical, landscape and CCTV works blank; the man-hours in the Progress sheet were used. Its BOQ values for CCTV Zone A and Zone G read 46,056 and 2 SAR instead of 6,513,996 and 2,791,854.
- The P6 update has the same data date as the weekly report (09-Nov-2026), and its activity counts match the Schedule sheet (823 completed, 351 in progress, 941 not started), but the front sheet still shows 144 in progress.
- The weekly report puts the procurement phase baseline at 23-Jan-2027; the approved baseline schedule (uploaded with the 19-Oct report) has 21-Nov-2026.
- The summary page's scope table shows 0 executed for every network, and its totals differ from the hidden Conclusion sheet (for example roads 15,234 m vs 18,252 m). Manholes are labelled "m" in the Major Quantities sheet but are counted in units.

- Procurement figures disagree: street lighting poles are 590 units and 10% complete in the Procurement sheet but 592 units with 1 delivered in Major Quantities; LV cables are 29,700 m vs 68,400 m. MV cables are "not submitted" in procurement, while the risk register says they have been procured.
- November planned head count is 391 in the monthly table (365 manual, 26 non-manual) but 390 in the head-count panel (350 manual, 40 non-manual). Cumulative toolbox talks rose from 43 to 58 although only one was held this week.
- Several cells show #REF ! errors (EAC, risk scores, safety score in the status score). The substation risk carries a value of 6,835,460.61 SAR, which is the landscape BOQ value.
- Several sheets (front sheet header, Major Quantities, Physical-Chart Data) still carry 19-Oct-2026 as their date and the Milestones sheet now carries 09-Oct-2026, although the report's data date is 09-Nov-2026. The Procurement sheet is unchanged from 26-Oct. The report week is the contract week the report states (44 of 78); whole weeks since handover give 43.

Compiled 10-Nov-2026 from the weekly reports of 19-Oct, 26-Oct, 02-Nov and 09-Nov-2026, with the P6 updates and the approved baseline schedule.
