
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		366	95,996,525.00	07-Jan-26	06-Mar-27	07-Jan-26		67,542,189.81	67,562,476.35	1.00
PROJECT MILESTONES		353	0.00	07-Jan-26	06-Mar-27	07-Jan-26		0.00	0.00	0.00
CONTRACTUAL MILESTONES		353	0.00	07-Jan-26	06-Mar-27	07-Jan-26		0.00	0.00	0.00
DAM3-PMS-MMS-0010	Project Start Date	0	0.00	07-Jan-26		07-Jan-26		0.00	0.00	0.00
DAM3-PMS-MMS-0040	Completion of Time Schedule submission	0	0.00		28-Jan-26		11-Feb-26	0.00	0.00	0.00
DAM3-PMS-MMS-0050	Completion of Plans (PEP,PQP,HSE, Procurement Plan)	0	0.00		04-Feb-26		04-May-26	0.00	0.00	0.00
DAM3-PMS-MMS-0020	Completion of Mobilization Works	0	0.00		07-Feb-26		18-Jan-26	0.00	0.00	0.00
DAM3-PMS-MMS-0030	Completion of Site Suvey Works	0	0.00		09-Feb-26		12-Feb-26	0.00	0.00	0.00
DAM3-PMS-MMS-0070	Completion of Site levelling, local roads & parkings	0	0.00		12-Feb-26			0.00	0.00	0.00
DAM3-PMS-MMS-0060	Completion of Engineering and Materials	0	0.00		07-May-26		05-Jul-26	0.00	0.00	0.00
DAM3-PMS-MMS-0080	Network start	0	0.00	07-Sep-26		01-Aug-26		0.00	0.00	0.00
DAM3-PMS-MMS-0110	Competion of Testing and Commissioning	0	0.00		06-Feb-27			0.00	0.00	0.00
DAM3-PMS-MMS-0090	Completion of Construction	0	0.00		21-Feb-27			0.00	0.00	0.00
DAM3-PMS-MMS-0100	Project Completion Date	0	0.00		06-Mar-27			0.00	0.00	0.00
DISCIPLINE MILESTONES		294	0.00	27-Jan-26	21-Feb-27	15-Feb-26		0.00	0.00	0.00
900 SQM FACTORIES		294	0.00	27-Jan-26	21-Feb-27	15-Feb-26		0.00	0.00	0.00
DAM3-PMS-DMS-2360	Construction Start	0	0.00	27-Jan-26		15-Feb-26		0.00	0.00	0.00
DAM3-PMS-DMS-2310	Completion of Civil works	0	0.00		01-Oct-26			0.00	0.00	0.00
DAM3-PMS-DMS-2330	Completion of Mechanical works	0	0.00		14-Dec-26			0.00	0.00	0.00
DAM3-PMS-DMS-2320	Completion of Electrical works	0	0.00		21-Dec-26			0.00	0.00	0.00
DAM3-PMS-DMS-2340	Completion of Architectural works	0	0.00		21-Dec-26			0.00	0.00	0.00
DAM3-PMS-DMS-2370	Construction Finish	0	0.00		21-Feb-27			0.00	0.00	0.00
SITE INFRASTRUCTURE		21	0.00	22-Dec-26	21-Feb-27			0.00	0.00	0.00
DAM3-PMS-DMS-2460	Completion of Environmentall works	0	0.00		22-Dec-26			0.00	0.00	0.00
DAM3-PMS-DMS-2450	Completion of External works	0	0.00		21-Feb-27			0.00	0.00	0.00
MOBILIZATION		35	0.00	07-Jan-26	16-Feb-26	07-Jan-26	04-May-26	0.00	0.00	0.00
SITE FACILITIES AND OFFICES		27	0.00	07-Jan-26	07-Feb-26	07-Jan-26	23-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0010	Site Survey	2	0.00	07-Jan-26	08-Jan-26	12-Feb-26	12-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0011	Site Layout Plan Prep	2	0.00	10-Jan-26	11-Jan-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0012	Site Layout Plan Submittal	2	0.00	12-Jan-26	13-Jan-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0013	Site Layout Plan Owner Approval	2	0.00	14-Jan-26	15-Jan-26	04-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0014	Clear and Grub for Offices and Access Roads	2	0.00	15-Jan-26	17-Jan-26	11-Jan-26	16-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0015	Construct Site Offices	4	0.00	18-Jan-26	21-Jan-26	19-Jan-26	10-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0016	Electrical Works and Connections	4	0.00	22-Jan-26	26-Jan-26	09-Feb-26	23-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0017	Site Utilities	4	0.00	27-Jan-26	31-Jan-26	11-Feb-26	23-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0018	Install Project Signs	4	0.00	01-Feb-26	04-Feb-26	03-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0019	Mobilization of Manpower	2	0.00	05-Feb-26	07-Feb-26	07-Jan-26	23-Feb-26	0.00	0.00	0.00
DAM3-MOB-SO.0020	Mobilization of Equipment	2	0.00	05-Feb-26	07-Feb-26	25-Jan-26	23-Feb-26	0.00	0.00	0.00
PRELIMINARY SUBMITTALS		31	0.00	22-Jan-26	16-Feb-26	14-Jan-26	04-May-26	0.00	0.00	0.00
PREPARATION AND SUBMITTALS		21	0.00	22-Jan-26	04-Feb-26	14-Jan-26	21-Feb-26	0.00	0.00	0.00
DAM3-PRE-SUB-0010	Project Execution Plan	2	0.00	22-Jan-26	24-Jan-26	21-Feb-26	21-Feb-26	0.00	0.00	0.00
DAM3-PRE-SUB-0011	Health & Safety Plan	2	0.00	25-Jan-26	26-Jan-26	26-Jan-26	26-Jan-26	0.00	0.00	0.00
DAM3-PRE-SUB-0012	Baseline Schedule	2	0.00	27-Jan-26	28-Jan-26	14-Jan-26	14-Jan-26	0.00	0.00	0.00
DAM3-PRE-SUB-0013	Risk Management plan	2	0.00	29-Jan-26	31-Jan-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
DAM3-PRE-SUB-0014	Communication Plan	2	0.00	01-Feb-26	02-Feb-26	21-Feb-26	21-Feb-26	0.00	0.00	0.00
DAM3-PRE-SUB-0015	Quality Control Plan	2	0.00	03-Feb-26	04-Feb-26	28-Jan-26	28-Jan-26	0.00	0.00	0.00
REVIEW AND APPROVALS		29	0.00	25-Jan-26	16-Feb-26	14-Jan-26	04-May-26	0.00	0.00	0.00
DAM3-PRE-SUB-1010	Project Execution Plan	10	0.00	25-Jan-26	04-Feb-26	21-Feb-26	03-May-26	0.00	0.00	0.00
DAM3-PRE-SUB-1011	Health & Safety Plan	10	0.00	27-Jan-26	07-Feb-26	26-Jan-26	28-Jan-26	0.00	0.00	0.00
DAM3-PRE-SUB-1012	Risk Management plan	10	0.00	01-Feb-26	11-Feb-26	28-Jan-26	03-Feb-26	0.00	0.00	0.00
DAM3-PRE-SUB-1013	Communication Plan	10	0.00	03-Feb-26	14-Feb-26	21-Feb-26	03-May-26	0.00	0.00	0.00
DAM3-PRE-SUB-1014	Quality Control Plan	10	0.00	05-Feb-26	16-Feb-26	28-Jan-26	04-May-26	0.00	0.00	0.00
DAM3-PRE-SUB-1015	Baseline Schedule	10	0.00	05-Feb-26	16-Feb-26	14-Jan-26	10-Feb-26	0.00	0.00	0.00
ENGINEERING (3%)		159	2,879,895.75	22-Jan-26	17-May-26	15-Jan-26	05-Jul-26	2,879,895.75	2,879,895.75	1.00
SHOP DRAWINGS		138	0.00	27-Jan-26	17-May-26	20-Jan-26	05-Jul-26	0.00	0.00	0.00
PREPARATION AND SUBMITTAL		136	0.00	27-Jan-26	07-May-26	20-Jan-26	01-Jul-26	0.00	0.00	0.00
STRUCTURAL		87	0.00	10-Feb-26	22-Mar-26	03-Feb-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-C-750	FOUNDATION LAYOUT	2	0.00	10-Feb-26	11-Feb-26	18-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	0.00	12-Feb-26	14-Feb-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-C-770	BASE PLATE LAYOUT	2	0.00	15-Feb-26	16-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00

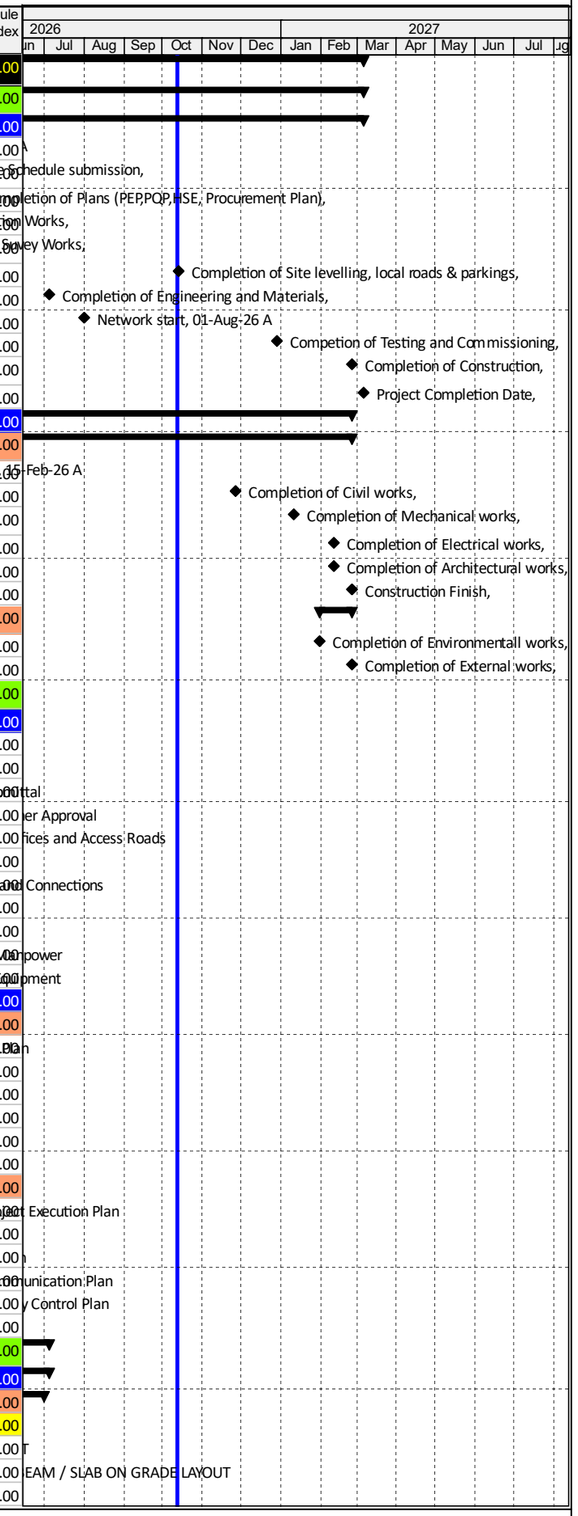

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-SS-C-780	TIE BEAM @ 4500mm EL.	2	0.00	17-Feb-26	19-Feb-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-SS-C-790	ROOF FRAMING LAYOUT	2	0.00	19-Feb-26	23-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-800	PURLINS FRAMING LAYOUT	2	0.00	23-Feb-26	25-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-810	ROOF SHEETING LAYOUT	2	0.00	25-Feb-26	28-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-820	COLUMNS AND AXIS LAYOUT	2	0.00	01-Mar-26	02-Mar-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-830	SECTIONS	2	0.00	03-Mar-26	04-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-840	EXTERNAL WALL SECTION DETAILS	2	0.00	05-Mar-26	07-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-850	BASE PLATE DETAILS	2	0.00	08-Mar-26	09-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	0.00	10-Mar-26	11-Mar-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-C-870	STRUCTURAL SCHEDULE	2	0.00	12-Mar-26	14-Mar-26	02-Jun-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	0.00	15-Mar-26	16-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	0.00	21-Mar-26	22-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
ARCHITECTURAL		75	0.00	25-Feb-26	04-Apr-26	03-Feb-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-A-830	GROUND FLOOR LAYOUT PLAN	2	0.00	25-Feb-26	28-Feb-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	0.00	01-Mar-26	02-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	0.00	03-Mar-26	04-Mar-26	02-Jun-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-A-860	ELEVATIONS (SHEET 01 0F 02)	2	0.00	05-Mar-26	07-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-1170	ELEVATIONS (SHEET 01 0F 02)	5	0.00	05-Mar-26	10-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-870	BUILDING SECTIONS	2	0.00	08-Mar-26	09-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-880	WALL SECTIONS	2	0.00	11-Mar-26	12-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-890	CEILING LAYOUT PLAN	2	0.00	14-Mar-26	15-Mar-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-900	FINISHING LAYOUT PLAN	2	0.00	16-Mar-26	21-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-910	TOILET DETAILS	2	0.00	22-Mar-26	23-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-920	DOORS & WINDOWS SCHEDULE	2	0.00	24-Mar-26	25-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-930	MISCELLANEOUS DETAILS - 01	2	0.00	26-Mar-26	28-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-940	MISCELLANEOUS DETAILS - 02	2	0.00	29-Mar-26	30-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-950	SIGNAGE LOCATION PLAN	2	0.00	31-Mar-26	01-Apr-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-SS-A-960	SIGNAGE DESIGN DETAILS	2	0.00	02-Apr-26	04-Apr-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
MECHANICAL		47	0.00	03-Mar-26	23-Apr-26	04-Feb-26	16-Apr-26	0.00	0.00	0.00
DAM3-E-SS-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	0.00	03-Mar-26	04-Mar-26	17-Mar-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	0.00	05-Mar-26	07-Mar-26	11-Mar-26	11-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-620	TYPICAL ROOF PLUMBING PLAN	2	0.00	08-Mar-26	09-Mar-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	0.00	10-Mar-26	11-Mar-26	17-Mar-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-640	TOILET DETAILS PLUMBING-WATER	2	0.00	12-Mar-26	14-Mar-26	11-Mar-26	11-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	0.00	15-Mar-26	16-Mar-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	0.00	21-Mar-26	22-Mar-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	0.00	23-Mar-26	24-Mar-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	0.00	25-Mar-26	26-Mar-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-690	SCHEDULE- PLUMBING	2	0.00	28-Mar-26	29-Mar-26	17-Mar-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-700	PUMP ROOM LAYOUT	2	0.00	30-Mar-26	31-Mar-26	16-Apr-26	16-Apr-26	0.00	0.00	0.00
DAM3-E-SS-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	0.00	01-Apr-26	02-Apr-26	16-Apr-26	16-Apr-26	0.00	0.00	0.00
DAM3-E-SS-M-720	SCHEDULES	2	0.00	04-Apr-26	05-Apr-26	17-Mar-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	0.00	06-Apr-26	07-Apr-26	26-Mar-26	26-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-740	TYPICAL ROOF HVAC PLAN	2	0.00	08-Apr-26	09-Apr-26	26-Mar-26	26-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	0.00	11-Apr-26	12-Apr-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	0.00	13-Apr-26	14-Apr-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	0.00	15-Apr-26	16-Apr-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-SS-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	0.00	18-Apr-26	19-Apr-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	0.00	20-Apr-26	21-Apr-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-SS-M-800	MISCELLANEOUS DETAILS	2	0.00	22-Apr-26	23-Apr-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
ELECTRICAL		133	0.00	05-Mar-26	05-May-26	09-Feb-26	25-Jun-26	0.00	0.00	0.00
DAM3-E-SS-E-940	GROUND FLOOR POWER PLAN	2	0.00	05-Mar-26	07-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	0.00	08-Mar-26	09-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	0.00	10-Mar-26	11-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-970	ROOF FLOOR POWER	2	0.00	12-Mar-26	14-Mar-26	08-Apr-26	09-Apr-26	0.00	0.00	0.00
DAM3-E-SS-E-980	PV SYSTEM CALCULATION	2	0.00	15-Mar-26	16-Mar-26	25-Jun-26	25-Jun-26	0.00	0.00	0.00
DAM3-E-SS-E-990	GROUND FLOOR LIGHTING PLAN	2	0.00	21-Mar-26	22-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1000	ROOF FLOOR LIGHTING PLAN	2	0.00	23-Mar-26	24-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1010	GOUND FLOOR ACCESS CONTROL	2	0.00	25-Mar-26	26-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	0.00	28-Mar-26	29-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1030	GROUND FLOOR CCTV PLAN	2	0.00	30-Mar-26	31-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	0.00	01-Apr-26	02-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00

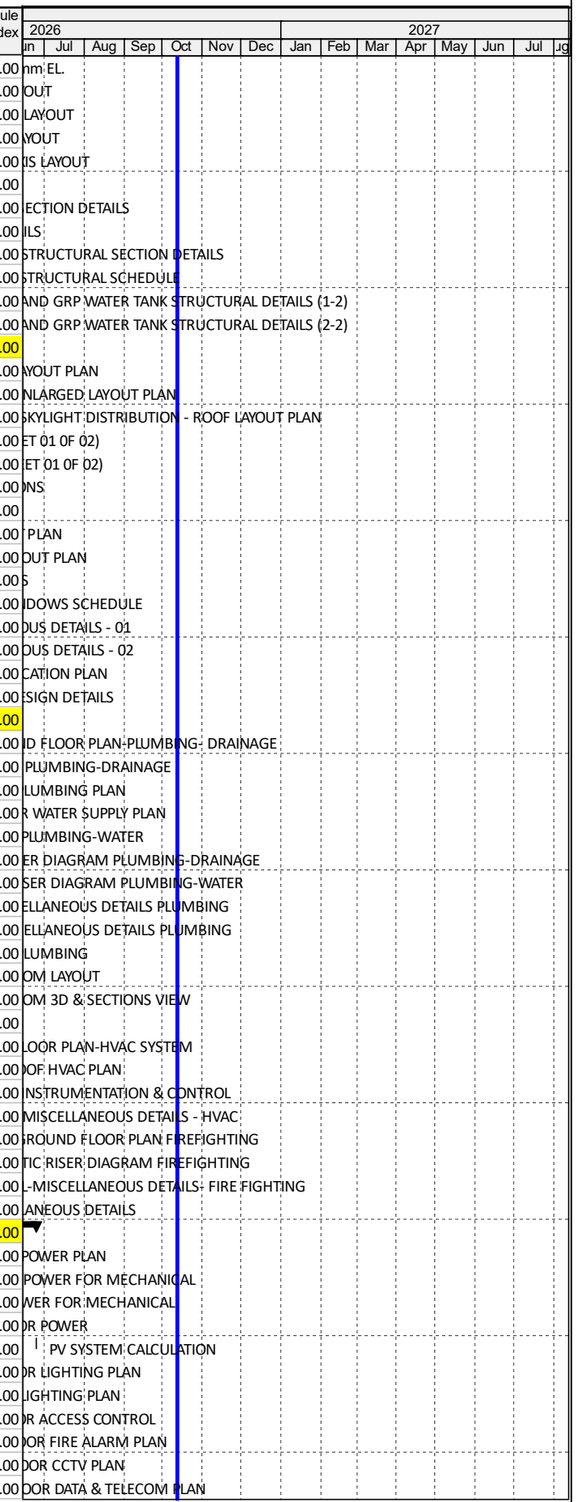

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-SS-E-1050	GROUND FLOOR GROUNDING PLAN	2	0.00	04-Apr-26	05-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1060	ROOF FLOOR LIGHTENING PLAN	2	0.00	06-Apr-26	07-Apr-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1070	POWER RISER DIAGRAM	2	0.00	08-Apr-26	09-Apr-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1080	FIRE ALARM RISER DIAGRAM	2	0.00	11-Apr-26	12-Apr-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1090	DATA & TELECOME RISER DIAGRAM	2	0.00	13-Apr-26	14-Apr-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1100	ACCESS CONTROL RISER DIAGRAM	2	0.00	15-Apr-26	16-Apr-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1110	SCHEDULES	2	0.00	18-Apr-26	19-Apr-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1120	ELECTRICAL DETAILS	2	0.00	20-Apr-26	21-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1130	GROUND FLOOR POWER PLAN	1	0.00	22-Apr-26	23-Apr-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1140	POWER FOR MECHANICAL	2	0.00	25-Apr-26	26-Apr-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1150	GROUND FLOOR LIGHTING PLAN	2	0.00	27-Apr-26	28-Apr-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SS-E-1160	GROUND FLOOR GROUNDING PLAN	2	0.00	29-Apr-26	30-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-SS-E-1170	RISER DIAGRAM	2	0.00	02-May-26	03-May-26	27-Apr-26	27-Apr-26	0.00	0.00	0.00
DAM3-E-SS-E-1180	ELECTRICAL DETAILS	2	0.00	04-May-26	05-May-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
ROAD DRAWINGS		117	0.00	27-Jan-26	29-Mar-26	20-Jan-26	01-Jul-26	0.00	0.00	0.00
DAM3-E-SS-R-730	GRADING LAYOUT PLAN	2	0.00	27-Jan-26	28-Jan-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-SS-R-740	ROAD LAYOUT PLAN	2	0.00	29-Jan-26	31-Jan-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	0.00	01-Feb-26	02-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-760	TYPICAL CROSS SECTIONS	2	0.00	03-Feb-26	04-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-770	ROAD PROFILES	2	0.00	05-Feb-26	07-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	0.00	08-Feb-26	09-Feb-26	20-Jan-26	20-Jan-26	0.00	0.00	0.00
DAM3-E-SS-R-790	ALIGNMENT & CURB SETTING OUT	2	0.00	10-Feb-26	11-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SS-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	0.00	12-Feb-26	14-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SS-R-810	ALIGNMNET GEOMETRIC DATA	2	0.00	15-Feb-26	16-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SS-R-820	SWEPT PATH LAYOUT PLAN	2	0.00	17-Feb-26	19-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SS-R-830	SIGNING & MARKING LAYOUT PLAN	2	0.00	19-Feb-26	23-Feb-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	0.00	23-Feb-26	25-Feb-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	0.00	25-Feb-26	28-Feb-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	0.00	01-Mar-26	02-Mar-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	0.00	03-Mar-26	04-Mar-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-R-880	GENERAL SITE PLAN - OVERALL	2	0.00	05-Mar-26	07-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-890	SITE SETTING-OUT PLAN - OVERALL	2	0.00	08-Mar-26	09-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-900	GENERAL LANDSCAPE LAYOUT	2	0.00	10-Mar-26	11-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-910	GENERAL HARDSCAPE LAYOUT	2	0.00	12-Mar-26	14-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-920	GENERAL SOFTSCAPE LAYOUT	2	0.00	15-Mar-26	16-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-930	PUMP ROOM DETAILS	1	0.00	21-Mar-26	22-Mar-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-940	GENERAL DETAILS	1	0.00	23-Mar-26	24-Mar-26	18-Mar-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SS-R-950	LANDSCAPE DETAILS	1	0.00	25-Mar-26	26-Mar-26	01-Jul-26	01-Jul-26	0.00	0.00	0.00
DAM3-E-SS-R-960	LANDSCAPE SCHEDULES	2	0.00	28-Mar-26	29-Mar-26	08-Mar-26	08-Mar-26	0.00	0.00	0.00
EXTERNAL		74	0.00	01-Mar-26	07-May-26	10-Feb-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-EX-690	POTABLE WATER NETWORK	2	0.00	01-Mar-26	02-Mar-26	11-May-26	11-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-700	FIRE FIGHTING WATER NETWORK	2	0.00	03-Mar-26	04-Mar-26	11-May-26	11-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-710	POTABLE WATER NETWORK PROFILES	2	0.00	05-Mar-26	07-Mar-26	11-May-26	11-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-720	FIRE FIGHTING NETWORK PROFILE	2	0.00	08-Mar-26	09-Mar-26	11-May-26	11-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-730	PIPE TRENCH DETAILS	2	0.00	10-Mar-26	11-Mar-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-740	BURIED GATE VALVE DETAILS	2	0.00	12-Mar-26	14-Mar-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-750	SINGLE VALVE CHAMBER DETAILS	2	0.00	15-Mar-26	16-Mar-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	0.00	21-Mar-26	22-Mar-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-EX-770	WASHOUT CHAMBER DETAILS	2	0.00	23-Mar-26	24-Mar-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	0.00	25-Mar-26	26-Mar-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-790	FLOW METER DETAILS	2	0.00	28-Mar-26	29-Mar-26	02-Jun-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-EX-800	FLOW METER REINFORCEMENT DETAILS	2	0.00	30-Mar-26	31-Mar-26	02-Jun-26	02-Jun-26	0.00	0.00	0.00
DAM3-E-SS-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	0.00	01-Apr-26	02-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	0.00	01-Apr-26	02-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	0.00	01-Apr-26	02-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	0.00	01-Apr-26	02-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-850	SEWAGE NETWORK	2	0.00	04-Apr-26	05-Apr-26	14-May-26	14-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-860	SEWAGE NETWORK PROFILES	2	0.00	06-Apr-26	07-Apr-26	14-May-26	14-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-870	GENERAL NOTES	2	0.00	08-Apr-26	09-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-880	PIPE TRENCHES DETAILS (1)	2	0.00	11-Apr-26	12-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-890	PIPE TRENCHES DETAILS (2)	2	0.00	13-Apr-26	14-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	0.00	15-Apr-26	16-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00

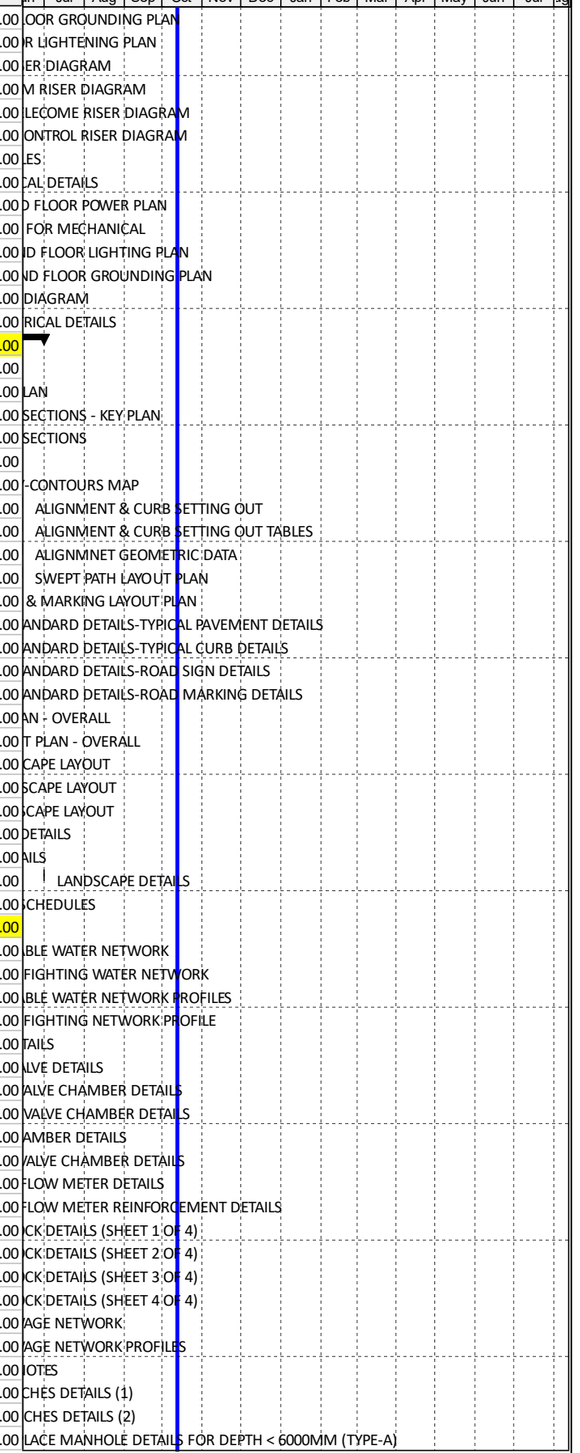

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation


44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-SS-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	0.00	15-Apr-26	16-Apr-26	12-Feb-26	12-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	0.00	15-Apr-26	16-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM	2	0.00	15-Apr-26	16-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-940	PRECAST MANHOLE DETAILS	2	0.00	18-Apr-26	19-Apr-26	15-Apr-26	15-Apr-26	0.00	0.00	0.00
DAM3-E-SS-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	0.00	20-Apr-26	21-Apr-26	12-May-26	12-May-26	0.00	0.00	0.00
DAM3-E-SS-EX-960	PIPE TRENCH DETAILS	2	0.00	22-Apr-26	23-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-970	BURIED GATE VALVE DETAILS	2	0.00	25-Apr-26	26-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-980	SINGLE VALVE CHAMBER DETAILS	2	0.00	27-Apr-26	28-Apr-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	0.00	29-Apr-26	30-Apr-26	21-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-SS-EX-1000	WASHOUT CHAMBER DETAILS	2	0.00	02-May-26	03-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	0.00	04-May-26	05-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	0.00	06-May-26	07-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	0.00	06-May-26	07-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	0.00	06-May-26	07-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SS-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	0.00	06-May-26	07-May-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
REVIEW AND APPROVAL		117	0.00	29-Jan-26	17-May-26	20-Jan-26	05-Jul-26	0.00	0.00	0.00
STRUCTURAL		87	0.00	12-Feb-26	24-Mar-26	03-Feb-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-C-750	FOUNDATION LAYOUT	2	0.00	12-Feb-26	14-Feb-26	18-Feb-26	07-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-760	GRADE BEAM / SLAB ON GRADE LAYOUT	2	0.00	15-Feb-26	16-Feb-26	21-Apr-26	03-May-26	0.00	0.00	0.00
DAM3-E-SA-C-770	BASE PLATE LAYOUT	2	0.00	17-Feb-26	19-Feb-26	07-Feb-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-780	TIE BEAM @ 4500mm EL.	2	0.00	19-Feb-26	23-Feb-26	01-Mar-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-C-790	ROOF FRAMING LAYOUT	2	0.00	23-Feb-26	25-Feb-26	07-Feb-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-800	PURLINS FRAMING LAYOUT	2	0.00	25-Feb-26	28-Feb-26	07-Feb-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-810	ROOF SHEETING LAYOUT	2	0.00	01-Mar-26	02-Mar-26	07-Feb-26	17-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-820	COLUMNS AND AXIS LAYOUT	2	0.00	03-Mar-26	04-Mar-26	07-Feb-26	07-Mar-26	0.00	0.00	0.00
DAM3-E-SA-C-830	SECTIONS	2	0.00	05-Mar-26	07-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-C-840	EXTERNAL WALL SECTION DETAILS	2	0.00	08-Mar-26	09-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-C-850	BASE PLATE DETAILS	2	0.00	10-Mar-26	11-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-C-860	TYPICAL STRUCTURAL SECTION DETAILS	2	0.00	12-Mar-26	14-Mar-26	21-Apr-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-C-870	STRUCTURAL SCHEDULE	2	0.00	15-Mar-26	16-Mar-26	02-Jun-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-C-880	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (1-2)	2	0.00	21-Mar-26	22-Mar-26	29-Mar-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-C-890	PUMP SHED AND GRP WATER TANK STRUCTURAL DETAILS (2-2)	2	0.00	23-Mar-26	24-Mar-26	29-Mar-26	17-May-26	0.00	0.00	0.00
ARCHITECTURAL		75	0.00	01-Mar-26	06-Apr-26	03-Feb-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-A-830	GROUND FLOOR LAYOUT PLAN	2	0.00	01-Mar-26	02-Mar-26	03-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-840	GROUND FLOOR ENLARGED LAYOUT PLAN	2	0.00	03-Mar-26	04-Mar-26	03-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-850	SKYLIGHT DISTRIBUTION - ROOF LAYOUT PLAN	2	0.00	05-Mar-26	07-Mar-26	02-Jun-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-A-860	ELEVATIONS (SHEET 01 0F 02)	2	0.00	08-Mar-26	09-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-870	ELEVATIONS (SHEET 01 0F 02)	2	0.00	10-Mar-26	11-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-1170	BUILDING SECTIONS	5	0.00	12-Mar-26	21-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-880	WALL SECTIONS	2	0.00	14-Mar-26	15-Mar-26	03-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-890	CEILING LAYOUT PLAN	2	0.00	16-Mar-26	21-Mar-26	05-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-900	FINISHING LAYOUT PLAN	2	0.00	22-Mar-26	23-Mar-26	09-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-910	TOILET DETAILS	2	0.00	24-Mar-26	25-Mar-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-920	DOORS & WINDOWS SCHEDULE	2	0.00	26-Mar-26	28-Mar-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-930	MISCELLANEOUS DETAILS - 01	2	0.00	29-Mar-26	30-Mar-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-940	MISCELLANEOUS DETAILS - 02	2	0.00	31-Mar-26	01-Apr-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-950	SIGNAGE LOCATION PLAN	2	0.00	02-Apr-26	04-Apr-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
DAM3-E-SA-A-960	SIGNAGE DESIGN DETAILS	2	0.00	05-Apr-26	06-Apr-26	11-Feb-26	25-Feb-26	0.00	0.00	0.00
MECHANICAL		51	0.00	05-Mar-26	26-Apr-26	04-Feb-26	09-Jun-26	0.00	0.00	0.00
DAM3-E-SA-M-600	TYPICAL GROUND FLOOR PLAN-PLUMBING- DRAINAGE	2	0.00	05-Mar-26	07-Mar-26	17-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-610	TOILETS DETAILS PLUMBING-DRAINAGE	2	0.00	08-Mar-26	09-Mar-26	11-Mar-26	10-May-26	0.00	0.00	0.00
DAM3-E-SA-M-620	TYPICAL ROOF PLUMBING PLAN	2	0.00	10-Mar-26	11-Mar-26	16-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-630	GROUND FLOOR WATER SUPPLY PLAN	2	0.00	12-Mar-26	14-Mar-26	17-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-640	TOILET DETAILS PLUMBING-WATER	2	0.00	15-Mar-26	16-Mar-26	11-Mar-26	10-May-26	0.00	0.00	0.00
DAM3-E-SA-M-650	SCHEMATIC RISER DIAGRAM PLUMBING-DRAINAGE	2	0.00	21-Mar-26	22-Mar-26	04-Feb-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-M-660	SCHEMATIC RISER DIAGRAM PLUMBING-WATER	2	0.00	23-Mar-26	24-Mar-26	04-Feb-26	13-Apr-26	0.00	0.00	0.00
DAM3-E-SA-M-670	GENERAL MISELLANEOUS DETAILS PLUMBING	2	0.00	25-Mar-26	26-Mar-26	04-Feb-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-M-680	GENERAL MISELLANEOUS DETAILS PLUMBING	2	0.00	28-Mar-26	29-Mar-26	04-Feb-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-M-690	SCHEDULE- PLUMBING	2	0.00	30-Mar-26	31-Mar-26	17-Mar-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-M-700	PUMP ROOM LAYOUT	2	0.00	01-Apr-26	02-Apr-26	16-Apr-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-M-710	PUMP ROOM 3D & SECTIONS VIEW	2	0.00	04-Apr-26	05-Apr-26	21-Apr-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-M-720	SCHEDULES	2	0.00	06-Apr-26	07-Apr-26	17-Mar-26	11-May-26	0.00	0.00	0.00

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-SA-M-730	GROUND FLOOR PLAN-HVAC SYSTEM	2	0.00	08-Apr-26	09-Apr-26	26-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-740	TYPICAL ROOF HVAC PLAN	2	0.00	11-Apr-26	12-Apr-26	26-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-750	GENERAL-INSTRUMENTATION & CONTROL	2	0.00	13-Apr-26	14-Apr-26	04-Feb-26	09-Jun-26	0.00	0.00	0.00
DAM3-E-SA-M-760	GENERAL MISCELLANEOUS DETAILS - HVAC	2	0.00	15-Apr-26	16-Apr-26	05-Feb-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-M-770	TYPICAL GROUND FLOOR PLAN FIREFIGHTING	2	0.00	18-Apr-26	19-Apr-26	14-Mar-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-M-780	SCHEMATIC RISER DIAGRAM FIREFIGHTING	2	0.00	20-Apr-26	21-Apr-26	04-Feb-26	09-Jun-26	0.00	0.00	0.00
DAM3-E-SA-M-790	GENERAL-MISCELLANEOUS DETAILS- FIRE FIGHTING	2	0.00	22-Apr-26	23-Apr-26	04-Feb-26	09-Jun-26	0.00	0.00	0.00
DAM3-E-SA-M-800	MISCELLANEOUS DETAILS	2	0.00	25-Apr-26	26-Apr-26	04-Feb-26	03-Mar-26	0.00	0.00	0.00
ELECTRICAL		99	0.00	08-Mar-26	07-May-26	09-Feb-26	28-Jun-26	0.00	0.00	0.00
DAM3-E-SA-E-940	GROUND FLOOR POWER PLAN	2	0.00	08-Mar-26	09-Mar-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-950	GROUND FLOOR POWER FOR MECHANICAL	2	0.00	10-Mar-26	11-Mar-26	09-Feb-26	18-Apr-26	0.00	0.00	0.00
DAM3-E-SA-E-960	ROOF FLOOR POWER FOR MECHANICAL	2	0.00	12-Mar-26	14-Mar-26	09-Feb-26	15-Apr-26	0.00	0.00	0.00
DAM3-E-SA-E-970	ROOF FLOOR POWER	2	0.00	15-Mar-26	16-Mar-26	08-Apr-26	09-Apr-26	0.00	0.00	0.00
DAM3-E-SA-E-980	PV SYSTEM CALCULATION	2	0.00	21-Mar-26	22-Mar-26	25-Jun-26	28-Jun-26	0.00	0.00	0.00
DAM3-E-SA-E-990	GROUND FLOOR LIGHTING PLAN	2	0.00	23-Mar-26	24-Mar-26	09-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1000	ROOF FLOOR LIGHTING PLAN	2	0.00	25-Mar-26	26-Mar-26	09-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1010	GOUND FLOOR ACCESS CONTROL	2	0.00	28-Mar-26	29-Mar-26	29-Mar-26	18-Apr-26	0.00	0.00	0.00
DAM3-E-SA-E-1020	GROUND FLOOR FIRE ALARM PLAN	2	0.00	30-Mar-26	31-Mar-26	29-Mar-26	15-Apr-26	0.00	0.00	0.00
DAM3-E-SA-E-1030	GROUND FLOOR CCTV PLAN	2	0.00	01-Apr-26	02-Apr-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1040	GROUND FLOOR DATA & TELECOM PLAN	2	0.00	04-Apr-26	05-Apr-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1050	GROUND FLOOR GROUNDING PLAN	2	0.00	06-Apr-26	07-Apr-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1060	ROOF FLOOR LIGHTENING PLAN	2	0.00	08-Apr-26	09-Apr-26	09-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1070	POWER RISER DIAGRAM	2	0.00	11-Apr-26	12-Apr-26	29-Mar-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-SA-E-1080	FIRE ALARM RISER DIAGRAM	2	0.00	13-Apr-26	14-Apr-26	29-Mar-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-E-1090	DATA & TELECOME RISER DIAGRAM	2	0.00	15-Apr-26	16-Apr-26	29-Mar-26	30-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1100	ACCESS CONTROL RISER DIAGRAM	2	0.00	18-Apr-26	19-Apr-26	29-Mar-26	30-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1110	SCHEDULES	2	0.00	20-Apr-26	21-Apr-26	29-Mar-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-SA-E-1120	ELECTRICAL DETAILS	2	0.00	22-Apr-26	23-Apr-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1130	GROUND FLOOR POWER PLAN	2	0.00	25-Apr-26	26-Apr-26	09-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1140	POWER FOR MECHANICAL	2	0.00	27-Apr-26	28-Apr-26	09-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1150	GROUND FLOOR LIGHTING PLAN	2	0.00	29-Apr-26	30-Apr-26	09-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-SA-E-1160	GROUND FLOOR GROUNDING PLAN	2	0.00	02-May-26	03-May-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-SA-E-1170	RISER DIAGRAM	2	0.00	04-May-26	05-May-26	27-Apr-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-SA-E-1180	ELECTRICAL DETAILS	2	0.00	06-May-26	07-May-26	01-Mar-26	03-Mar-26	0.00	0.00	0.00
ROAD DRAWINGS		117	0.00	29-Jan-26	31-Mar-26	20-Jan-26	05-Jul-26	0.00	0.00	0.00
DAM3-E-SA-R-730	GRADING LAYOUT PLAN	2	0.00	29-Jan-26	31-Jan-26	03-Feb-26	03-May-26	0.00	0.00	0.00
DAM3-E-SA-R-740	ROAD LAYOUT PLAN	2	0.00	01-Feb-26	02-Feb-26	16-Mar-26	29-Apr-26	0.00	0.00	0.00
DAM3-E-SA-R-750	TYPICAL CROSS SECTIONS - KEY PLAN	2	0.00	03-Feb-26	04-Feb-26	16-Mar-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-760	TYPICAL CROSS SECTIONS	2	0.00	05-Feb-26	07-Feb-26	16-Mar-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-770	ROAD PROFILES	2	0.00	08-Feb-26	09-Feb-26	16-Mar-26	29-Apr-26	0.00	0.00	0.00
DAM3-E-SA-R-780	TOPOGRAPHIC SURVEY-CONTOURS MAP	2	0.00	10-Feb-26	11-Feb-26	20-Jan-26	22-Jan-26	0.00	0.00	0.00
DAM3-E-SA-R-790	ALIGNMENT & CURB SETTING OUT	2	0.00	12-Feb-26	14-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SA-R-800	ALIGNMENT & CURB SETTING OUT TABLES	2	0.00	15-Feb-26	16-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SA-R-810	ALIGNMINET GEOMETRIC DATA	2	0.00	17-Feb-26	19-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SA-R-820	SWEPT PATH LAYOUT PLAN	2	0.00	19-Feb-26	23-Feb-26	14-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-E-SA-R-830	SIGNING & MARKING LAYOUT PLAN	2	0.00	23-Feb-26	25-Feb-26	21-Apr-26	29-Apr-26	0.00	0.00	0.00
DAM3-E-SA-R-840	ROAD STANDARD DETAILS-TYPICAL PAVEMENT DETAILS	2	0.00	25-Feb-26	28-Feb-26	21-Apr-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-850	ROAD STANDARD DETAILS-TYPICAL CURB DETAILS	2	0.00	01-Mar-26	02-Mar-26	21-Apr-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-860	ROAD STANDARD DETAILS-ROAD SIGN DETAILS	2	0.00	03-Mar-26	04-Mar-26	21-Apr-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-870	ROAD STANDARD DETAILS-ROAD MARKING DETAILS	2	0.00	05-Mar-26	07-Mar-26	21-Apr-26	04-May-26	0.00	0.00	0.00
DAM3-E-SA-R-880	GENERAL SITE PLAN - OVERALL	2	0.00	08-Mar-26	09-Mar-26	08-Mar-26	20-May-26	0.00	0.00	0.00
DAM3-E-SA-R-890	SITE SETTING-OUT PLAN - OVERALL	2	0.00	10-Mar-26	11-Mar-26	08-Mar-26	03-May-26	0.00	0.00	0.00
DAM3-E-SA-R-900	GENERAL LANDSCAPE LAYOUT	2	0.00	12-Mar-26	14-Mar-26	08-Mar-26	06-May-26	0.00	0.00	0.00
DAM3-E-SA-R-910	GENERAL HARDSCAPE LAYOUT	2	0.00	15-Mar-26	16-Mar-26	08-Mar-26	07-May-26	0.00	0.00	0.00
DAM3-E-SA-R-920	GENERAL SOFTSCAPE LAYOUT	2	0.00	21-Mar-26	22-Mar-26	08-Mar-26	09-May-26	0.00	0.00	0.00
DAM3-E-SA-R-930	PUMP ROOM DETAILS	2	0.00	23-Mar-26	24-Mar-26	14-Mar-26	06-May-26	0.00	0.00	0.00
DAM3-E-SA-R-940	GENERAL DETAILS	2	0.00	25-Mar-26	26-Mar-26	18-Mar-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-R-950	LANDSCAPE DETAILS	2	0.00	28-Mar-26	29-Mar-26	01-Jul-26	05-Jul-26	0.00	0.00	0.00
DAM3-E-SA-R-960	LANDSCAPE SCHEDULES	2	0.00	30-Mar-26	31-Mar-26	08-Mar-26	06-May-26	0.00	0.00	0.00
EXTERNAL		78	0.00	03-Mar-26	17-May-26	10-Feb-26	08-Jun-26	0.00	0.00	0.00
DAM3-E-SA-EX-690	POTABLE WATER NETWORK	2	0.00	03-Mar-26	04-Mar-26	11-May-26	01-Jun-26	0.00	0.00	0.00
DAM3-E-SA-EX-700	FIRE FIGHTING WATER NETWORK	2	0.00	05-Mar-26	07-Mar-26	11-May-26	12-May-26	0.00	0.00	0.00

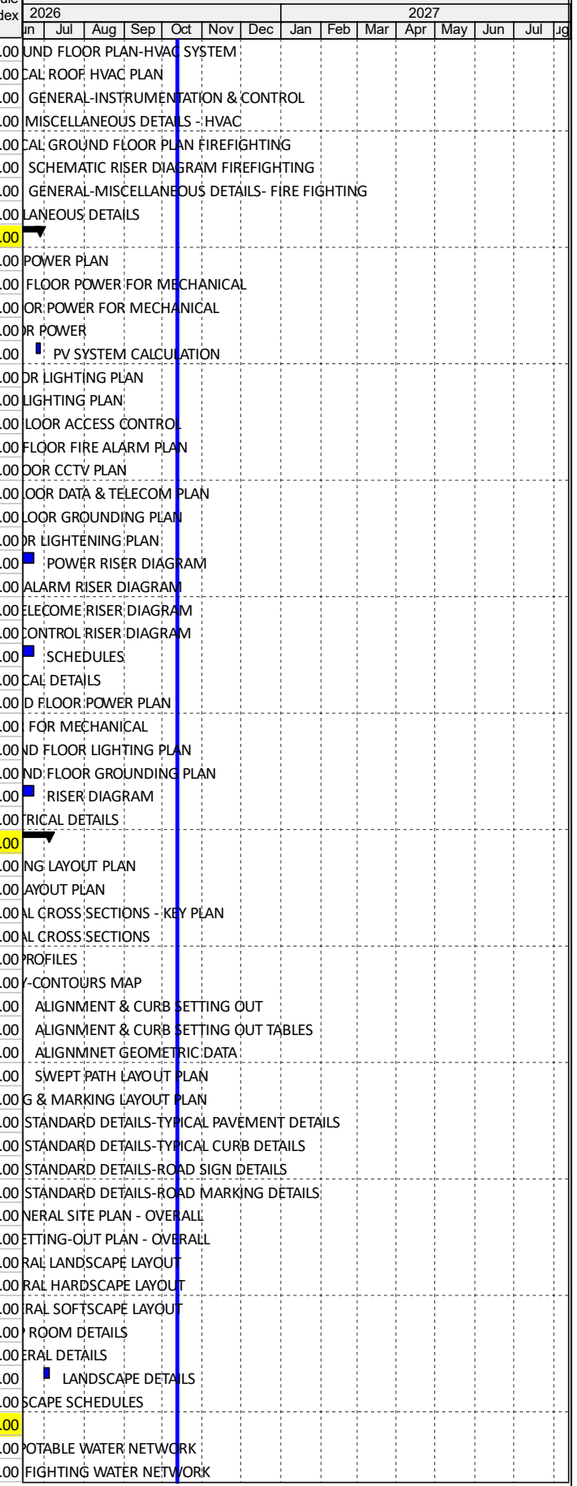

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-SA-EX-710	POTABLE WATER NETWORK PROFILES	2	0.00	08-Mar-26	09-Mar-26	11-May-26	25-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-720	FIRE FIGHTING NETWORK PROFILE	2	0.00	10-Mar-26	11-Mar-26	11-May-26	12-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-730	PIPE TRENCH DETAILS	2	0.00	12-Mar-26	14-Mar-26	10-Feb-26	10-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-740	BURIED GATE VALVE DETAILS	2	0.00	15-Mar-26	16-Mar-26	10-Feb-26	31-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-750	SINGLE VALVE CHAMBER DETAILS	2	0.00	21-Mar-26	22-Mar-26	21-Apr-26	27-Apr-26	0.00	0.00	0.00
DAM3-E-SA-EX-760	DOUBLE VALVE CHAMBER DETAILS	2	0.00	23-Mar-26	24-Mar-26	21-Apr-26	27-Apr-26	0.00	0.00	0.00
DAM3-E-SA-EX-770	WASHOUT CHAMBER DETAILS	2	0.00	25-Mar-26	26-Mar-26	10-Feb-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-780	AIR RELEASE VALVE CHAMBER DETAILS	2	0.00	28-Mar-26	29-Mar-26	10-Feb-26	25-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-790	FLOW METER DETAILS	2	0.00	30-Mar-26	31-Mar-26	02-Jun-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-EX-800	FLOW METER REINFORCEMENT DETAILS	2	0.00	01-Apr-26	02-Apr-26	02-Jun-26	03-Jun-26	0.00	0.00	0.00
DAM3-E-SA-EX-830	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	0.00	04-Apr-26	05-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-840	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	0.00	04-Apr-26	05-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-810	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	0.00	04-Apr-26	05-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-850	SEWAGE NETWORK	2	0.00	06-Apr-26	07-Apr-26	14-May-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-820	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	0.00	06-Apr-26	07-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-860	SEWAGE NETWORK PROFILES	2	0.00	08-Apr-26	09-Apr-26	14-May-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-870	GENERAL NOTES	2	0.00	11-Apr-26	12-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-880	PIPE TRENCHES DETAILS (1)	2	0.00	13-Apr-26	14-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-890	PIPE TRENCHES DETAILS (2)	2	0.00	15-Apr-26	16-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-900	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-A)	2	0.00	18-Apr-26	19-Apr-26	10-Feb-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-910	CAST IN PLACE MANHOLE DETAILS FOR DEPTH < 6000MM (TYPE-B)	2	0.00	18-Apr-26	19-Apr-26	12-Feb-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-920	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH FROM 3000MM	2	0.00	18-Apr-26	19-Apr-26	10-Feb-26	19-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-930	BACKDROP DETAIL OF PRECAST MANHOLE DEPTH < 3000MM	2	0.00	18-Apr-26	19-Apr-26	10-Feb-26	19-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-940	PRECAST MANHOLE DETAILS	2	0.00	20-Apr-26	21-Apr-26	15-Apr-26	08-Jun-26	0.00	0.00	0.00
DAM3-E-SA-EX-950	IRRIGATION NETWORK LAYOUT SHEET 1 OF 1	2	0.00	22-Apr-26	23-Apr-26	12-May-26	17-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-960	PIPE TRENCH DETAILS	2	0.00	25-Apr-26	26-Apr-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-970	BURIED GATE VALVE DETAILS	2	0.00	27-Apr-26	28-Apr-26	10-Feb-26	31-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-980	SINGLE VALVE CHAMBER DETAILS	2	0.00	29-Apr-26	30-Apr-26	21-Apr-26	27-Apr-26	0.00	0.00	0.00
DAM3-E-SA-EX-990	DOUBLE VALVE CHAMBER DETAILS	2	0.00	02-May-26	03-May-26	21-Apr-26	27-Apr-26	0.00	0.00	0.00
DAM3-E-SA-EX-1000	WASHOUT CHAMBER DETAILS	2	0.00	04-May-26	05-May-26	10-Feb-26	11-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-1010	AIR RELEASE VALVE CHAMBER DETAILS	2	0.00	06-May-26	07-May-26	10-Feb-26	25-May-26	0.00	0.00	0.00
DAM3-E-SA-EX-1020	THRUST BLOCK DETAILS (SHEET 1 OF 4)	2	0.00	09-May-26	10-May-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-1030	THRUST BLOCK DETAILS (SHEET 2 OF 4)	2	0.00	11-May-26	12-May-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-1040	THRUST BLOCK DETAILS (SHEET 3 OF 4)	2	0.00	13-May-26	14-May-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-SA-EX-1050	THRUST BLOCK DETAILS (SHEET 4 OF 4)	2	0.00	16-May-26	17-May-26	10-Feb-26	18-Mar-26	0.00	0.00	0.00
PRE QUALIFACTION FOR MATERIALS		138	0.00	22-Jan-26	12-Apr-26	15-Jan-26	11-Jun-26	0.00	0.00	0.00
PREPARATION AND SUBMITTAL		108	0.00	22-Jan-26	09-Apr-26	15-Jan-26	10-Jun-26	0.00	0.00	0.00
STRUCTURAL		10	0.00	22-Jan-26	02-Feb-26	15-Jan-26	19-Jan-26	0.00	0.00	0.00
DAM3-E-PS-C-0010	Anti termite	2	0.00	22-Jan-26	24-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
DAM3-E-PS-C-0020	Concrete mix	2	0.00	25-Jan-26	26-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
DAM3-E-PS-C-0030	Polyethylene sheet	2	0.00	27-Jan-26	28-Jan-26	19-Jan-26	19-Jan-26	0.00	0.00	0.00
DAM3-E-PS-C-0040	Bitumen paint	2	0.00	29-Jan-26	31-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
DAM3-E-PS-C-0050	Rebar	2	0.00	01-Feb-26	02-Feb-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
ARCHITECTURAL		100	0.00	25-Jan-26	02-Mar-26	08-Feb-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-A-0020	PES -Steel Structure	2	0.00	25-Jan-26	26-Jan-26	19-Feb-26	23-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0040	Concrete masonry unit (CMU)	2	0.00	27-Jan-26	28-Jan-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0050	Steel ladder	2	0.00	29-Jan-26	31-Jan-26	25-Feb-26	28-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0060	Steel gratings	2	0.00	01-Feb-26	02-Feb-26	19-May-26	19-May-26	0.00	0.00	0.00
DAM3-E-PS-A-0070	Steel rails	2	0.00	03-Feb-26	04-Feb-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-A-0120	Doors	2	0.00	05-Feb-26	07-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0130	Windows	2	0.00	08-Feb-26	09-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0140	Ceramic tiles	2	0.00	10-Feb-26	11-Feb-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
DAM3-E-PS-A-0150	Granite strip	2	0.00	12-Feb-26	14-Feb-26	03-May-26	03-May-26	0.00	0.00	0.00
DAM3-E-PS-A-0170	Epoxy paint	2	0.00	15-Feb-26	16-Feb-26	20-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PS-A-0180	Internl paint	2	0.00	17-Feb-26	19-Feb-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
DAM3-E-PS-A-0190	Gypsum board	2	0.00	19-Feb-26	23-Feb-26	24-Feb-26	24-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0200	Aluminum Composite Panel	2	0.00	23-Feb-26	25-Feb-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PS-A-0230	Steel fence and gates	2	0.00	25-Feb-26	28-Feb-26	20-May-26	20-May-26	0.00	0.00	0.00
DAM3-E-PS-A-0240	Identification sign; ID01 & ID02	2	0.00	01-Mar-26	02-Mar-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
MECHANICAL		98	0.00	27-Jan-26	09-Apr-26	24-Jan-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-M-0010	Seamless black steel or ERW pipes	2	0.00	27-Jan-26	28-Jan-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0030	PPR pipes	2	0.00	29-Jan-26	31-Jan-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00

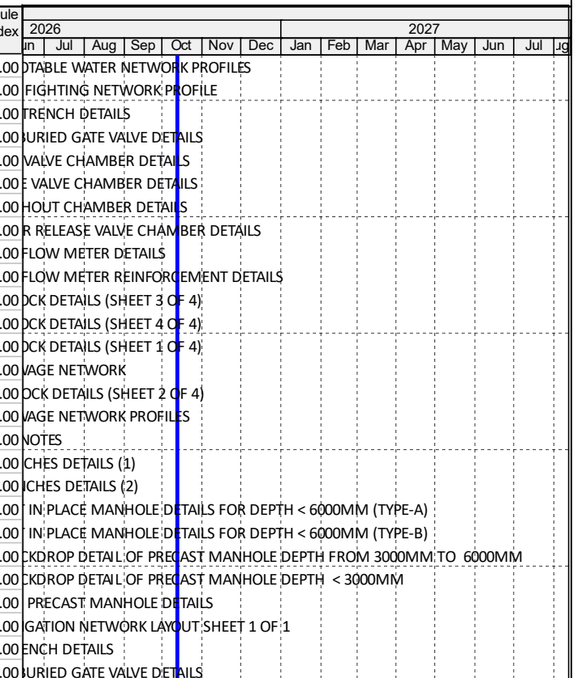

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-PS-M-0040	HVAC duct	2	0.00	01-Feb-26	02-Feb-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0050	Flexible duct	2	0.00	03-Feb-26	04-Feb-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0060	Exhaust diffuser	2	0.00	05-Feb-26	07-Feb-26	27-May-26	27-May-26	0.00	0.00	0.00
DAM3-E-PS-M-0070	U/G HDPE pipes	2	0.00	08-Feb-26	09-Feb-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0080	Warning tapes	2	0.00	08-Feb-26	09-Feb-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0090	Fire hose cabinet	2	0.00	10-Feb-26	11-Feb-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0100	Automatic air release valve	2	0.00	12-Feb-26	14-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0110	OS & Y gate valve	2	0.00	15-Feb-26	16-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0120	Fire alarm check valve	2	0.00	17-Feb-26	19-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0140	Ball valve	2	0.00	19-Feb-26	23-Feb-26	11-Feb-26	12-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0150	Capped connection	2	0.00	23-Feb-26	25-Feb-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-M-0160	UPVC pipes	2	0.00	25-Feb-26	28-Feb-26	04-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0170	Roof vent caps	2	0.00	01-Mar-26	02-Mar-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0180	Floor drain	2	0.00	03-Mar-26	04-Mar-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0190	Gully trap	2	0.00	05-Mar-26	07-Mar-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0200	Electric water heater	2	0.00	08-Mar-26	09-Mar-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0210	Western water closet	2	0.00	10-Mar-26	11-Mar-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0220	Bib tap	2	0.00	12-Mar-26	14-Mar-26	04-Apr-26	05-Apr-26	0.00	0.00	0.00
DAM3-E-PS-M-0230	Toilet Fittings	2	0.00	15-Mar-26	16-Mar-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0240	Lavatory / wash basin	2	0.00	21-Mar-26	22-Mar-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0250	Inline exhaust fans	2	0.00	23-Mar-26	24-Mar-26	02-Feb-26	02-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0260	Wall propeller type exhaust fans	2	0.00	25-Mar-26	26-Mar-26	02-Feb-26	02-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0270	Fire pumps	2	0.00	28-Mar-26	29-Mar-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0280	Fire fighting valves	2	0.00	30-Mar-26	31-Mar-26	02-Feb-26	02-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0320	Booster pump	2	0.00	01-Apr-26	02-Apr-26	03-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0330	GRP tank	2	0.00	04-Apr-26	05-Apr-26	24-Jan-26	28-Jan-26	0.00	0.00	0.00
DAM3-E-PS-M-0340	Water supply valves	2	0.00	06-Apr-26	07-Apr-26	02-Feb-26	02-Feb-26	0.00	0.00	0.00
DAM3-E-PS-M-0350	Water tap	2	0.00	08-Apr-26	09-Apr-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
ELECTRICAL		85	0.00	29-Jan-26	05-Apr-26	07-Feb-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0010	PVC conduits	2	0.00	29-Jan-26	31-Jan-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PS-E-0020	Wires	2	0.00	01-Feb-26	02-Feb-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0030	Cable Tray	2	0.00	03-Feb-26	04-Feb-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0040	Grounding system	2	0.00	05-Feb-26	07-Feb-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0050	Wiring devices	2	0.00	08-Feb-26	09-Feb-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0060	HDPE ducts	2	0.00	10-Feb-26	11-Feb-26	20-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0070	Low Voltage cables	2	0.00	12-Feb-26	14-Feb-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0080	Main distribution board (MDB)	2	0.00	15-Feb-26	16-Feb-26	19-Apr-26	19-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0090	Lighting panel board	2	0.00	17-Feb-26	19-Feb-26	19-Apr-26	19-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0100	PP-AC panel	2	0.00	19-Feb-26	23-Feb-26	19-Apr-26	19-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0110	Disconnect switches	2	0.00	23-Feb-26	25-Feb-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0120	Suspended High Bay LED lights	2	0.00	25-Feb-26	28-Feb-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0130	Flood lights	2	0.00	01-Mar-26	02-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0140	Recessed mounted LED downlight	2	0.00	03-Mar-26	04-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0150	LED Emergency Lights wall mounted	2	0.00	05-Mar-26	07-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0160	LED Emergency Exit Light	2	0.00	08-Mar-26	09-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0170	Wall mounted, duplex, telephone and data outlet	2	0.00	10-Mar-26	11-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-PS-E-0180	Fire alarm system	2	0.00	12-Mar-26	14-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PS-E-0200	Street Lighting poles	1	0.00	15-Mar-26	16-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0210	Distribution board for pump room	1	0.00	21-Mar-26	22-Mar-26	19-Apr-26	19-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0220	Surface mounted lights	2	0.00	23-Mar-26	24-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0230	CCTV System	2	0.00	25-Mar-26	26-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-PS-E-0240	Access control system	2	0.00	28-Mar-26	29-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PS-E-0250	Solar system	2	0.00	30-Mar-26	31-Mar-26	24-Feb-26	01-Mar-26	0.00	0.00	0.00
DAM3-E-PS-E-0260	Main program system & controller	2	0.00	01-Apr-26	02-Apr-26	20-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PS-E-0270	PLC controller	2	0.00	04-Apr-26	05-Apr-26	20-Apr-26	20-Apr-26	0.00	0.00	0.00
EXTERNAL		14	0.00	25-Mar-26	09-Apr-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0010	Asphalt works	2	0.00	25-Mar-26	26-Mar-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0020	Concrete parking bumper	2	0.00	28-Mar-26	29-Mar-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0030	Road markings	2	0.00	30-Mar-26	31-Mar-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0040	Road signs	2	0.00	01-Apr-26	02-Apr-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0060	Interlock tiles	2	0.00	04-Apr-26	05-Apr-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PS-EX-0070	Curbstones	2	0.00	06-Apr-26	07-Apr-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00

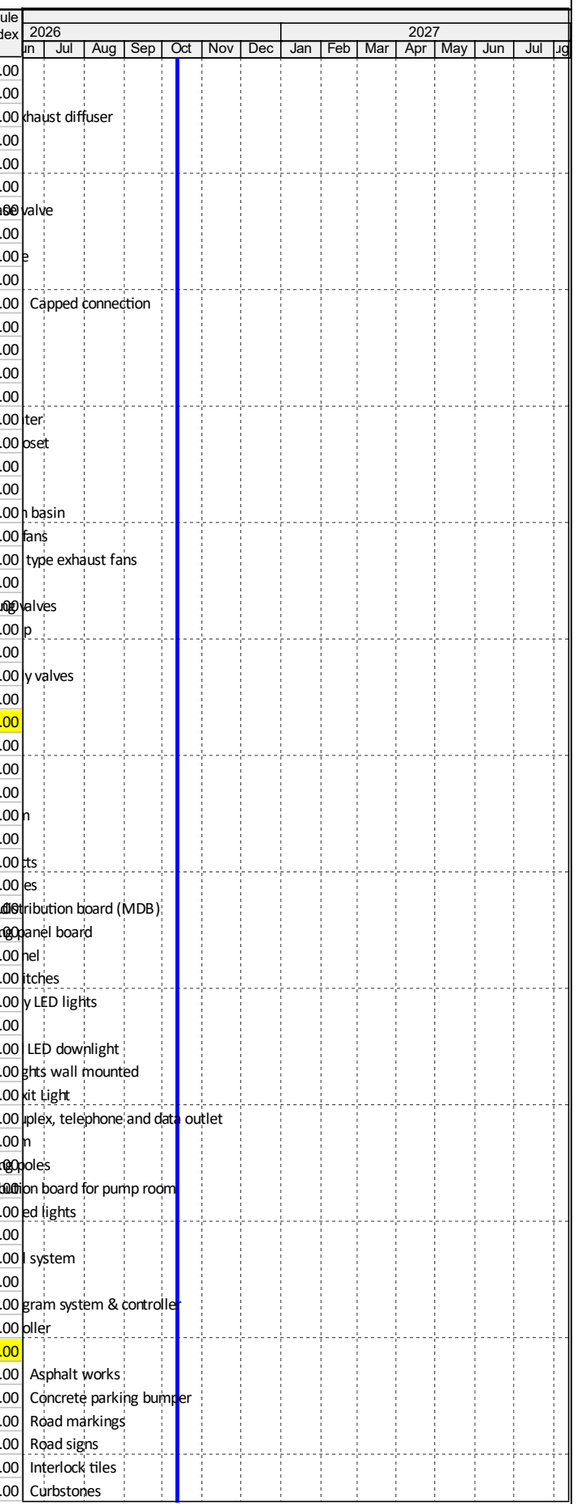

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-PS-EX-0080	Gravel bedding	2	0.00	08-Apr-26	09-Apr-26	10-Jun-26	10-Jun-26	0.00	0.00	0.00
ENVIRONMETAL		75	0.00	29-Jan-26	16-Feb-26	03-Feb-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-PS-EN-0010	HDPE pipes for fire system	2	0.00	29-Jan-26	31-Jan-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0020	Directly buried gate valve for fire system	2	0.00	01-Feb-26	02-Feb-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0030	HDPE pipes for water supply system	2	0.00	03-Feb-26	04-Feb-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0040	Directly buried gate valve for water system	2	0.00	05-Feb-26	07-Feb-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0050	Air valve	2	0.00	08-Feb-26	09-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0060	Washout valve	2	0.00	10-Feb-26	11-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0070	Gate valve	2	0.00	12-Feb-26	14-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-PS-EN-0080	UPVC pipes	2	0.00	15-Feb-26	16-Feb-26	03-Feb-26	03-Mar-26	0.00	0.00	0.00
REVIEW AND APPROVAL		138	0.00	25-Jan-26	12-Apr-26	15-Jan-26	11-Jun-26	0.00	0.00	0.00
STRUCTURAL		34	0.00	25-Jan-26	04-Feb-26	15-Jan-26	21-Jan-26	0.00	0.00	0.00
DAM3-E-PA-C-0010	Anti termite	2	0.00	25-Jan-26	26-Jan-26	15-Jan-26	20-Jan-26	0.00	0.00	0.00
DAM3-E-PA-C-0020	Concrete mix	2	0.00	27-Jan-26	28-Jan-26	15-Jan-26	20-Jan-26	0.00	0.00	0.00
DAM3-E-PA-C-0030	Polyethylene sheet	5	0.00	29-Jan-26	31-Jan-26	19-Jan-26	21-Jan-26	0.00	0.00	0.00
DAM3-E-PA-C-0040	Bitumen paint	2	0.00	01-Feb-26	02-Feb-26	15-Jan-26	20-Jan-26	0.00	0.00	0.00
DAM3-E-PA-C-0050	Rebar	2	0.00	03-Feb-26	04-Feb-26	15-Jan-26	20-Jan-26	0.00	0.00	0.00
ARCHITECTURAL		104	0.00	27-Jan-26	04-Mar-26	08-Feb-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-PA-A-0020	PES -Steel Structure	2	0.00	27-Jan-26	28-Jan-26	17-Feb-26	19-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0040	Concrete masonry unit (CMU)	2	0.00	29-Jan-26	31-Jan-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0050	Steel ladder	2	0.00	01-Feb-26	02-Feb-26	17-Feb-26	19-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0060	Steel gratings	2	0.00	03-Feb-26	04-Feb-26	19-May-26	20-May-26	0.00	0.00	0.00
DAM3-E-PA-A-0070	Steel rails	2	0.00	05-Feb-26	07-Feb-26	10-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-PA-A-0120	Doors	2	0.00	08-Feb-26	09-Feb-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0130	Windows	2	0.00	10-Feb-26	11-Feb-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0140	Ceramic tiles	2	0.00	12-Feb-26	14-Feb-26	25-Mar-26	26-Mar-26	0.00	0.00	0.00
DAM3-E-PA-A-0150	Granite strip	2	0.00	15-Feb-26	16-Feb-26	03-May-26	04-May-26	0.00	0.00	0.00
DAM3-E-PA-A-0170	Epoxy paint	2	0.00	17-Feb-26	19-Feb-26	20-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-PA-A-0180	Internl paint	2	0.00	19-Feb-26	23-Feb-26	25-Mar-26	26-Mar-26	0.00	0.00	0.00
DAM3-E-PA-A-0190	Gypsum board	2	0.00	23-Feb-26	25-Feb-26	24-Feb-26	12-Apr-26	0.00	0.00	0.00
DAM3-E-PA-A-0200	Aluminum Composite Panel	2	0.00	25-Feb-26	28-Feb-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PA-A-0230	Steel fence and gates	2	0.00	01-Mar-26	02-Mar-26	20-May-26	21-May-26	0.00	0.00	0.00
DAM3-E-PA-A-0240	Identification sign; ID01 & ID02	2	0.00	03-Mar-26	04-Mar-26	10-Jun-26	11-Jun-26	0.00	0.00	0.00
MECHANICAL		98	0.00	29-Jan-26	12-Apr-26	24-Jan-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-PA-M-0010	Seamless black steel or ERW pipes	2	0.00	29-Jan-26	31-Jan-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0030	PPR pipes	2	0.00	01-Feb-26	02-Feb-26	03-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0040	HVAC duct	2	0.00	03-Feb-26	04-Feb-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0050	Flexible duct	2	0.00	05-Feb-26	07-Feb-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0060	Exhaust diffuser	2	0.00	08-Feb-26	09-Feb-26	27-May-26	28-May-26	0.00	0.00	0.00
DAM3-E-PA-M-0070	U/G HDPE pipes	2	0.00	10-Feb-26	11-Feb-26	04-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0080	Warning tapes	2	0.00	10-Feb-26	11-Feb-26	14-Feb-26	15-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0090	Fire hose cabinet	2	0.00	12-Feb-26	14-Feb-26	04-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0100	Automatic air release valve	2	0.00	15-Feb-26	16-Feb-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0110	OS & Y gate valve	2	0.00	17-Feb-26	19-Feb-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0120	Fire alarm check valve	2	0.00	19-Feb-26	23-Feb-26	08-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0140	Ball valve	2	0.00	23-Feb-26	25-Feb-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0150	Capped connection	2	0.00	25-Feb-26	28-Feb-26	10-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-PA-M-0160	UPVC pipes	2	0.00	01-Mar-26	02-Mar-26	04-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0170	Roof vent caps	2	0.00	03-Mar-26	04-Mar-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0180	Floor drain	2	0.00	05-Mar-26	07-Mar-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0190	Gully trap	2	0.00	08-Mar-26	09-Mar-26	07-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0200	Electric water heater	2	0.00	10-Mar-26	11-Mar-26	05-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0210	Western water closet	2	0.00	12-Mar-26	14-Mar-26	05-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0220	Bib tap	2	0.00	15-Mar-26	16-Mar-26	06-Apr-26	07-Apr-26	0.00	0.00	0.00
DAM3-E-PA-M-0230	Toilet Fittings	2	0.00	21-Mar-26	22-Mar-26	07-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0240	Lavatory / wash basin	2	0.00	23-Mar-26	24-Mar-26	05-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0250	Inline exhaust fans	2	0.00	25-Mar-26	26-Mar-26	02-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0260	Wall propeller type exhaust fans	2	0.00	28-Mar-26	29-Mar-26	02-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0270	Fire pumps	2	0.00	30-Mar-26	31-Mar-26	03-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0280	Fire fighting valves	2	0.00	01-Apr-26	02-Apr-26	02-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0330	Booster pump	2	0.00	04-Apr-26	05-Apr-26	03-Feb-26	04-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0340	GRP tank	2	0.00	06-Apr-26	07-Apr-26	24-Jan-26	16-Feb-26	0.00	0.00	0.00

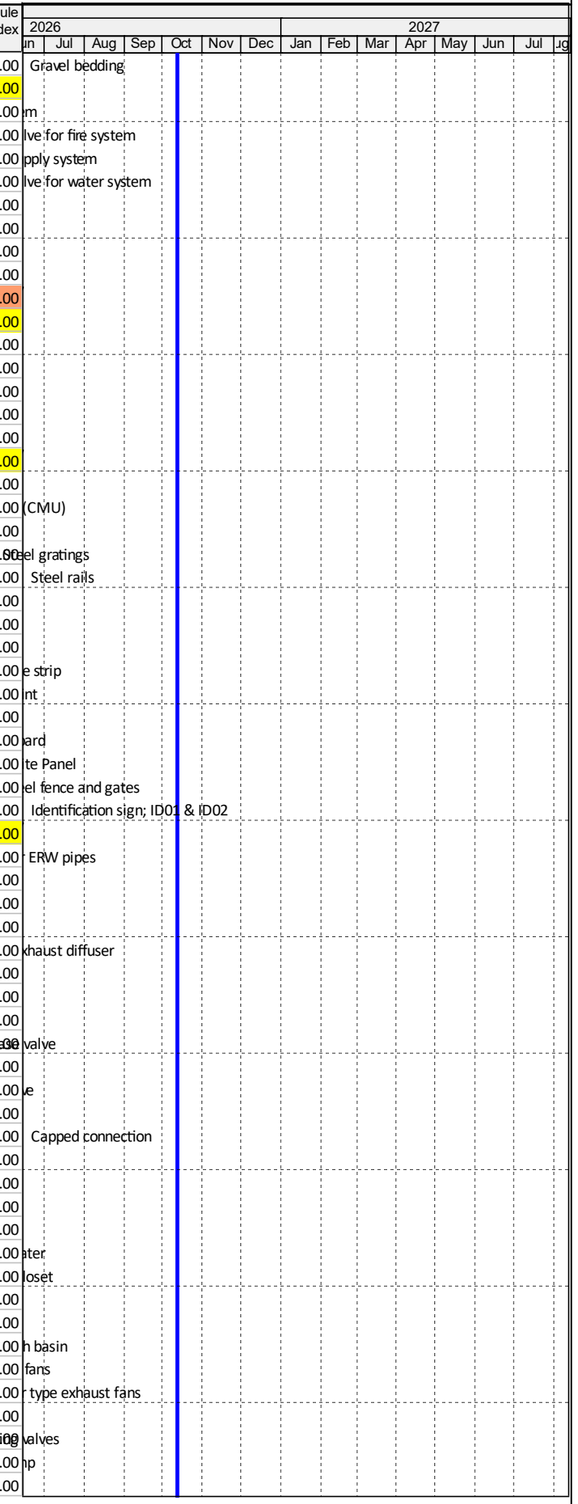

Actual Level of Effort
Actual Work
Critical Remaining Work
Primary Baseline
Remaining Work
Milestone

TASK filter: All Activities

© Oracle Corporation


44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-PA-M-0350	Water supply valves	2	0.00	08-Apr-26	09-Apr-26	02-Feb-26	03-Feb-26	0.00	0.00	0.00
DAM3-E-PA-M-0320	Water tap	2	0.00	11-Apr-26	12-Apr-26	11-Feb-26	12-Feb-26	0.00	0.00	0.00
ELECTRICAL		85	0.00	01-Feb-26	07-Apr-26	07-Feb-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0010	PVC conduits	2	0.00	01-Feb-26	02-Feb-26	07-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-PA-E-0020	Wires	2	0.00	03-Feb-26	04-Feb-26	14-Mar-26	15-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0030	Cable Tray	2	0.00	05-Feb-26	07-Feb-26	03-Mar-26	04-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0040	Grounding system	2	0.00	08-Feb-26	09-Feb-26	14-Mar-26	15-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0050	Wiring devices	2	0.00	10-Feb-26	11-Feb-26	03-Mar-26	04-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0060	HDPE ducts	2	0.00	12-Feb-26	14-Feb-26	20-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0070	Low Voltage cables	2	0.00	15-Feb-26	16-Feb-26	14-Mar-26	15-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0080	Main distribution board (MDB)	2	0.00	17-Feb-26	19-Feb-26	19-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0090	Lighting panel board	2	0.00	19-Feb-26	23-Feb-26	19-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0100	PP-AC panel	2	0.00	23-Feb-26	25-Feb-26	19-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0110	Disconnect switches	2	0.00	25-Feb-26	28-Feb-26	25-Mar-26	26-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0120	Suspended High Bay LED lights	2	0.00	01-Mar-26	02-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0130	Flood lights	2	0.00	03-Mar-26	04-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0140	Recessed mounted LED downlight	2	0.00	05-Mar-26	07-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0150	LED Emergency Lights wall mounted	2	0.00	08-Mar-26	09-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0160	LED Emergency Exit Light	2	0.00	10-Mar-26	11-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0170	Wall mounted, duplex, telephone and data outlet	2	0.00	12-Mar-26	14-Mar-26	11-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-PA-E-0180	Fire alarm system	2	0.00	15-Mar-26	16-Mar-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PA-E-0200	Street Lighting poles	2	0.00	21-Mar-26	22-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0210	Distribution board for pump room	2	0.00	23-Mar-26	24-Mar-26	19-Apr-26	20-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0220	Surface mounted lights	2	0.00	25-Mar-26	26-Mar-26	01-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0230	CCTV System	2	0.00	28-Mar-26	29-Mar-26	11-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-PA-E-0240	Access control system	2	0.00	30-Mar-26	31-Mar-26	09-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-PA-E-0250	Solar system	2	0.00	01-Apr-26	02-Apr-26	24-Feb-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-PA-E-0260	Main program system & controller	2	0.00	04-Apr-26	05-Apr-26	20-Apr-26	21-Apr-26	0.00	0.00	0.00
DAM3-E-PA-E-0270	PLC controller	2	0.00	06-Apr-26	07-Apr-26	20-Apr-26	21-Apr-26	0.00	0.00	0.00
EXTERNAL		14	0.00	28-Mar-26	12-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0010	Asphalt works	2	0.00	28-Mar-26	29-Mar-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0020	Concrete parking bumper	2	0.00	30-Mar-26	31-Mar-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0030	Road markings	2	0.00	01-Apr-26	02-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0040	Road signs	2	0.00	04-Apr-26	05-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0060	Interlock tiles	2	0.00	06-Apr-26	07-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0070	Curbstones	2	0.00	08-Apr-26	09-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
DAM3-E-PA-EX-0080	Gravel bedding	2	0.00	11-Apr-26	12-Apr-26	09-Jun-26	10-Jun-26	0.00	0.00	0.00
ENVIRONMETAL		73	0.00	01-Feb-26	19-Feb-26	03-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0010	HDPE pipes for fire system	2	0.00	01-Feb-26	02-Feb-26	05-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0020	Directly buried gate valve for fire system	2	0.00	03-Feb-26	04-Feb-26	14-Feb-26	15-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0030	HDPE pipes for water supply system	2	0.00	05-Feb-26	07-Feb-26	05-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0040	Directly buried gate valve for water system	2	0.00	08-Feb-26	09-Feb-26	14-Feb-26	15-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0050	Air valve	2	0.00	10-Feb-26	11-Feb-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0060	Washout valve	2	0.00	12-Feb-26	14-Feb-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0070	Gate valve	2	0.00	15-Feb-26	16-Feb-26	16-Feb-26	17-Feb-26	0.00	0.00	0.00
DAM3-E-PA-EN-0080	UPVC pipes	2	0.00	17-Feb-26	19-Feb-26	03-Feb-26	04-Feb-26	0.00	0.00	0.00
MATERIAL SUBMITTAL		108	2,879,895.75	27-Jan-26	20-Apr-26	15-Jan-26	14-Jun-26	2,879,895.75	2,879,895.75	1.00
PREPARATION AND SUBMITTAL		108	0.00	27-Jan-26	14-Apr-26	15-Jan-26	13-Jun-26	0.00	0.00	0.00
STRUCTURAL		10	0.00	27-Jan-26	07-Feb-26	15-Jan-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-MS-C-0010	Anti termite	2	0.00	27-Jan-26	28-Jan-26	14-Mar-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-MS-C-0020	Concrete mix	2	0.00	29-Jan-26	31-Jan-26	15-Jan-26	15-Jan-26	0.00	0.00	0.00
DAM3-E-MS-C-0030	Polyethylene sheet	2	0.00	01-Feb-26	02-Feb-26	22-Jan-26	22-Jan-26	0.00	0.00	0.00
DAM3-E-MS-C-0040	Bitumen paint	2	0.00	03-Feb-26	04-Feb-26	22-Jan-26	22-Jan-26	0.00	0.00	0.00
DAM3-E-MS-C-0050	Rebar	2	0.00	05-Feb-26	07-Feb-26	22-Jan-26	22-Jan-26	0.00	0.00	0.00
ARCHITECTURAL		100	0.00	29-Jan-26	07-Mar-26	07-Feb-26	13-Jun-26	0.00	0.00	0.00
DAM3-E-MS-A-1700	PES -Steel Structure	2	0.00	29-Jan-26	31-Jan-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-MS-A-0020	Concrete masonry unit (CMU)	2	0.00	01-Feb-26	02-Feb-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-MS-A-0030	Steel ladder	2	0.00	03-Feb-26	04-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-MS-A-0040	Steel gratings	2	0.00	05-Feb-26	07-Feb-26	21-May-26	21-May-26	0.00	0.00	0.00
DAM3-E-MS-A-0050	Steel rails	2	0.00	08-Feb-26	09-Feb-26	13-Jun-26	13-Jun-26	0.00	0.00	0.00
DAM3-E-MS-A-0100	Doors	2	0.00	10-Feb-26	11-Feb-26	19-Feb-26	19-Feb-26	0.00	0.00	0.00
DAM3-E-MS-A-0110	Windows	2	0.00	12-Feb-26	14-Feb-26	19-Feb-26	19-Feb-26	0.00	0.00	0.00

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-MS-A-0120	Ceramic tiles	2	0.00	15-Feb-26	16-Feb-26	30-Mar-26	30-Mar-26	0.00	0.00	0.00
DAM3-E-MS-A-0130	Granite strip	2	0.00	17-Feb-26	19-Feb-26	09-May-26	09-May-26	0.00	0.00	0.00
DAM3-E-MS-A-0150	Epoxy paint	2	0.00	19-Feb-26	23-Feb-26	29-Apr-26	29-Apr-26	0.00	0.00	0.00
DAM3-E-MS-A-0160	Internl paint	2	0.00	23-Feb-26	25-Feb-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-MS-A-0170	Gypsum board	2	0.00	25-Feb-26	28-Feb-26	19-Apr-26	19-Apr-26	0.00	0.00	0.00
DAM3-E-MS-A-1720	Aluminum Composite Panel	2	0.00	01-Mar-26	02-Mar-26	19-Feb-26	19-Feb-26	0.00	0.00	0.00
DAM3-E-MS-A-1750	Steel fence and gates	2	0.00	03-Mar-26	04-Mar-26	23-May-26	23-May-26	0.00	0.00	0.00
DAM3-E-MS-A-1760	Identification sign; ID01 & ID02	2	0.00	05-Mar-26	07-Mar-26	13-Jun-26	13-Jun-26	0.00	0.00	0.00
MECHANICAL		98	0.00	01-Feb-26	14-Apr-26	05-Feb-26	13-Jun-26	0.00	0.00	0.00
DAM3-E-MS-M-0020	Seamless black steel or ERW pipes	2	0.00	01-Feb-26	02-Feb-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0080	PPR pipes	2	0.00	03-Feb-26	04-Feb-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0220	HVAC duct	2	0.00	05-Feb-26	07-Feb-26	04-Mar-26	04-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0230	Flexible duct	2	0.00	08-Feb-26	09-Feb-26	04-Mar-26	04-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0240	Exhaust diffuser	2	0.00	10-Feb-26	11-Feb-26	01-Jun-26	01-Jun-26	0.00	0.00	0.00
DAM3-E-MS-M-0010	U/G HDPE pipes	2	0.00	12-Feb-26	14-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0340	Warning tapes	2	0.00	12-Feb-26	14-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0030	Fire hose cabinet	2	0.00	15-Feb-26	16-Feb-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0040	Automatic air release valve	2	0.00	17-Feb-26	19-Feb-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0050	OS & Y gate valve	2	0.00	19-Feb-26	23-Feb-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0060	Fire alarm check valve	2	0.00	23-Feb-26	25-Feb-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0090	Ball valve	2	0.00	25-Feb-26	28-Feb-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0100	Capped connection	2	0.00	01-Mar-26	02-Mar-26	13-Jun-26	13-Jun-26	0.00	0.00	0.00
DAM3-E-MS-M-0110	UPVC pipes	2	0.00	03-Mar-26	04-Mar-26	07-Feb-26	07-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0120	Roof vent caps	2	0.00	05-Mar-26	07-Mar-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0130	Floor drain	2	0.00	08-Mar-26	09-Mar-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0140	Gully trap	2	0.00	10-Mar-26	11-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0150	Electric water heater	2	0.00	12-Mar-26	14-Mar-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0160	Western water closet	2	0.00	15-Mar-26	16-Mar-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0170	Bib tap	2	0.00	21-Mar-26	22-Mar-26	14-Feb-26	14-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0180	Toilet Fittings	2	0.00	23-Mar-26	24-Mar-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0190	Lavatory / wash basin	2	0.00	25-Mar-26	26-Mar-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0200	Inline exhaust fans	2	0.00	28-Mar-26	29-Mar-26	18-Mar-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0210	Wall propeller type exhaust fans	2	0.00	30-Mar-26	31-Mar-26	18-Mar-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0250	Fire pumps	2	0.00	01-Apr-26	02-Apr-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0270	Fire fighting valves	2	0.00	04-Apr-26	05-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0310	Booster pump	2	0.00	06-Apr-26	07-Apr-26	05-Feb-26	05-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-0320	GRP tank	2	0.00	08-Apr-26	09-Apr-26	02-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-E-MS-M-0330	Water supply valves	2	0.00	11-Apr-26	12-Apr-26	10-Feb-26	10-Feb-26	0.00	0.00	0.00
DAM3-E-MS-M-3410	Water tap	2	0.00	13-Apr-26	14-Apr-26	14-Feb-26	14-Feb-26	0.00	0.00	0.00
ELECTRICAL		69	0.00	03-Feb-26	09-Apr-26	09-Feb-26	30-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-0040	PVC conduits	2	0.00	03-Feb-26	04-Feb-26	09-Feb-26	09-Feb-26	0.00	0.00	0.00
DAM3-E-MS-E-0050	Wires	2	0.00	05-Feb-26	07-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-210	Cable Tray	2	0.00	08-Feb-26	09-Feb-26	07-Mar-26	07-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0120	Grounding system	2	0.00	10-Feb-26	11-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0140	Wiring devices	2	0.00	12-Feb-26	14-Feb-26	07-Mar-26	07-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0160	HDPE ducts	2	0.00	15-Feb-26	16-Feb-26	30-Apr-26	30-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-0010	Low Voltage cables	2	0.00	17-Feb-26	19-Feb-26	16-Mar-26	16-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0020	Main distribution board (MDB)	2	0.00	19-Feb-26	23-Feb-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-190	Lighting panel board	2	0.00	23-Feb-26	25-Feb-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-200	PP-AC panel	2	0.00	25-Feb-26	28-Feb-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-0030	Disconnect switches	2	0.00	01-Mar-26	02-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0060	Suspended High Bay LED lights	2	0.00	03-Mar-26	04-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0070	Flood lights	2	0.00	05-Mar-26	07-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0080	Recessed mounted LED downlight	2	0.00	08-Mar-26	09-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0090	LED Emergency Lights wall mounted	2	0.00	10-Mar-26	11-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0100	LED Emergency Exit Light	2	0.00	12-Mar-26	14-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0110	Wall mounted, duplex, telephone and data outlet	1	0.00	15-Mar-26	16-Mar-26	29-Mar-26	29-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0130	Fire alarm system	2	0.00	21-Mar-26	22-Mar-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-MS-E-0170	Street Lighting poles	2	0.00	23-Mar-26	24-Mar-26	04-Mar-26	04-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0180	Distribution board for pump room	2	0.00	25-Mar-26	26-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-0190	Surface mounted lights	2	0.00	28-Mar-26	29-Mar-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0230	CCTV System	2	0.00	30-Mar-26	31-Mar-26	28-Mar-26	28-Mar-26	0.00	0.00	0.00

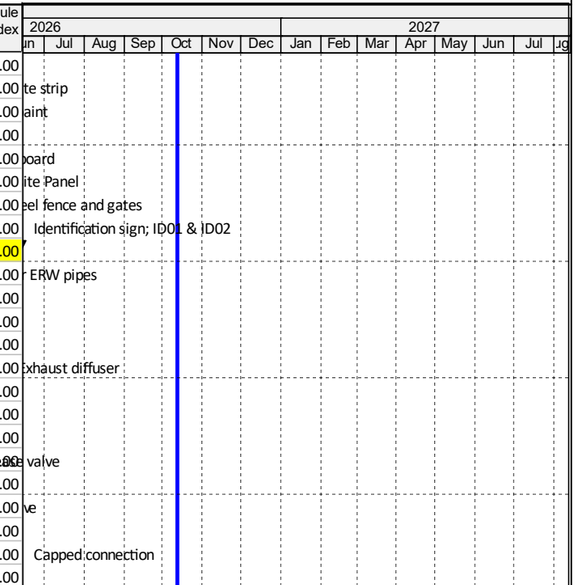

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-MS-E-0240	Access control system	2	0.00	01-Apr-26	02-Apr-26	11-Feb-26	11-Feb-26	0.00	0.00	0.00
DAM3-E-MS-E-0250	Solar system	2	0.00	04-Apr-26	05-Apr-26	03-Mar-26	03-Mar-26	0.00	0.00	0.00
DAM3-E-MS-E-0260	Main program system & controller	2	0.00	06-Apr-26	07-Apr-26	30-Apr-26	30-Apr-26	0.00	0.00	0.00
DAM3-E-MS-E-0270	PLC controller	2	0.00	08-Apr-26	09-Apr-26	30-Apr-26	30-Apr-26	0.00	0.00	0.00
EXTERNAL		14	0.00	30-Mar-26	14-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0010	Asphalt works	2	0.00	30-Mar-26	31-Mar-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0020	Concrete parking bumper	2	0.00	01-Apr-26	02-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0030	Road markings	2	0.00	04-Apr-26	05-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0040	Road signs	2	0.00	06-Apr-26	07-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0060	Interlock tiles	2	0.00	08-Apr-26	09-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0070	Curbstones	2	0.00	11-Apr-26	12-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
DAM3-E-MS-EX-0080	Gravel bedding	2	0.00	13-Apr-26	14-Apr-26	11-Jun-26	11-Jun-26	0.00	0.00	0.00
ENVIRONMETAL		55	0.00	03-Feb-26	23-Feb-26	08-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0010	HDPE pipes for fire system	2	0.00	03-Feb-26	04-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0020	Directly buried gate valve for fire system	2	0.00	05-Feb-26	07-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0030	HDPE pipes for water supply system	2	0.00	08-Feb-26	09-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0040	Directly buried gate valve for water system	2	0.00	10-Feb-26	11-Feb-26	16-Feb-26	16-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0050	Air valve	2	0.00	12-Feb-26	14-Feb-26	18-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0060	Washout valve	2	0.00	15-Feb-26	16-Feb-26	18-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0070	Gate valve	2	0.00	17-Feb-26	19-Feb-26	18-Feb-26	18-Feb-26	0.00	0.00	0.00
DAM3-E-MS-EN-0080	UPVC pipes	2	0.00	19-Feb-26	23-Feb-26	08-Feb-26	08-Feb-26	0.00	0.00	0.00
REVIEW AND APPROVAL		104	2,879,895.75	29-Jan-26	20-Apr-26	20-Jan-26	14-Jun-26	2,879,895.75	2,879,895.75	1.00
STRUCTURAL		20	481,112.68	29-Jan-26	12-Feb-26	20-Jan-26	07-Apr-26	481,112.68	481,112.68	1.00
DAM3-E-MA-C-0010	Anti termite	5	19,546.44	29-Jan-26	03-Feb-26	14-Mar-26	07-Apr-26	19,546.44	19,546.44	1.00
DAM3-E-MA-C-0020	Concrete mix	5	251,751.70	01-Feb-26	05-Feb-26	20-Jan-26	20-Jan-26	251,751.70	251,751.70	1.00
DAM3-E-MA-C-0030	Polyethylene sheet	5	13,035.98	03-Feb-26	08-Feb-26	22-Jan-26	29-Jan-26	13,035.98	13,035.98	1.00
DAM3-E-MA-C-0040	Bitumen paint	5	28,944.10	05-Feb-26	10-Feb-26	22-Jan-26	29-Jan-26	28,944.10	28,944.10	1.00
DAM3-E-MA-C-0050	Rebar	5	167,834.46	08-Feb-26	12-Feb-26	22-Jan-26	29-Jan-26	167,834.46	167,834.46	1.00
ARCHITECTURAL		93	1,232,403.28	03-Feb-26	12-Mar-26	07-Feb-26	14-Jun-26	1,232,403.28	1,232,403.28	1.00
DAM3-E-MA-A-0020	Concrete masonry unit (CMU)	5	62,820.36	03-Feb-26	08-Feb-26	26-Apr-26	29-Apr-26	62,820.36	62,820.36	1.00
DAM3-E-MA-A-0030	Steel ladder	5	4,846.16	05-Feb-26	10-Feb-26	07-Feb-26	10-Feb-26	4,846.16	4,846.16	1.00
DAM3-E-MA-A-0040	Steel gratings	5	3,179.40	08-Feb-26	12-Feb-26	21-May-26	24-May-26	3,179.40	3,179.40	1.00
DAM3-E-MA-A-0050	Steel rails	5	755.54	10-Feb-26	15-Feb-26	13-Jun-26	14-Jun-26	755.54	755.54	1.00
DAM3-E-MA-A-0100	Doors	5	75,386.56	12-Feb-26	17-Feb-26	19-Feb-26	25-Feb-26	75,386.56	75,386.56	1.00
DAM3-E-MA-A-1700	PES -Steel Structure	5	799,834.94	12-Feb-26	17-Feb-26	07-Feb-26	17-Mar-26	799,834.94	799,834.94	1.00
DAM3-E-MA-A-0110	Windows	5	52,525.19	15-Feb-26	21-Feb-26	19-Feb-26	25-Feb-26	52,525.19	52,525.19	1.00
DAM3-E-MA-A-0120	Ceramic tiles	5	36,151.26	17-Feb-26	24-Feb-26	30-Mar-26	04-May-26	36,151.26	36,151.26	1.00
DAM3-E-MA-A-0130	Granite strip	5	330.55	19-Feb-26	26-Feb-26	09-May-26	17-May-26	330.55	330.55	1.00
DAM3-E-MA-A-0150	Epoxy paint	5	56,848.54	23-Feb-26	01-Mar-26	21-Apr-26	26-Apr-26	56,848.54	56,848.54	1.00
DAM3-E-MA-A-0160	Internl paint	5	21,754.04	25-Feb-26	03-Mar-26	29-Mar-26	03-May-26	21,754.04	21,754.04	1.00
DAM3-E-MA-A-0170	Gypsum board	5	23,046.95	01-Mar-26	05-Mar-26	19-Apr-26	14-Jun-26	23,046.95	23,046.95	1.00
DAM3-E-MA-A-1720	Aluminum Composite Panel	5	86,631.78	03-Mar-26	08-Mar-26	21-Apr-26	26-Apr-26	86,631.78	86,631.78	1.00
DAM3-E-MA-A-1750	Steel fence and gates	5	3,548.60	05-Mar-26	10-Mar-26	23-May-26	25-May-26	3,548.60	3,548.60	1.00
DAM3-E-MA-A-1760	Identification sign; ID01 & ID02	5	4,743.41	08-Mar-26	12-Mar-26	08-Jun-26	13-Jun-26	4,743.41	4,743.41	1.00
MECHANICAL		101	303,435.06	03-Feb-26	20-Apr-26	05-Feb-26	14-Jun-26	303,435.06	303,435.06	1.00
DAM3-E-MA-M-0020	Seamless black steel or ERW pipes	5	35,657.12	03-Feb-26	08-Feb-26	10-Feb-26	26-Feb-26	35,657.12	35,657.12	1.00
DAM3-E-MA-M-0080	PPR pipes	5	11,485.19	05-Feb-26	10-Feb-26	05-Feb-26	11-May-26	11,485.19	11,485.19	1.00
DAM3-E-MA-M-0220	HVAC duct	5	73,629.07	08-Feb-26	12-Feb-26	04-Mar-26	12-May-26	73,629.07	73,629.07	1.00
DAM3-E-MA-M-0230	Flexible duct	5	10,444.45	10-Feb-26	15-Feb-26	04-Mar-26	12-May-26	10,444.45	10,444.45	1.00
DAM3-E-MA-M-0240	Exhaust diffuser	5	1,056.00	12-Feb-26	17-Feb-26	01-Jun-26	04-Jun-26	1,056.00	1,056.00	1.00
DAM3-E-MA-M-0010	U/G HDPE pipes	5	7,495.73	15-Feb-26	21-Feb-26	07-Feb-26	08-Mar-26	7,495.73	7,495.73	1.00
DAM3-E-MA-M-0340	Warning tapes	5	2,111.55	15-Feb-26	21-Feb-26	16-Feb-26	03-Mar-26	2,111.55	2,111.55	1.00
DAM3-E-MA-M-0030	Fire hose cabinet	5	7,466.16	17-Feb-26	24-Feb-26	07-Feb-26	01-Mar-26	7,466.16	7,466.16	1.00
DAM3-E-MA-M-0040	Automatic air release valve	5	265.43	19-Feb-26	26-Feb-26	10-Feb-26	26-Feb-26	265.43	265.43	1.00
DAM3-E-MA-M-0050	OS & Y gate valve	5	1,744.73	23-Feb-26	01-Mar-26	10-Feb-26	26-Feb-26	1,744.73	1,744.73	1.00
DAM3-E-MA-M-0060	Fire alarm check valve	5	3,998.51	25-Feb-26	03-Mar-26	10-Feb-26	26-Feb-26	3,998.51	3,998.51	1.00
DAM3-E-MA-M-0090	Ball valve	5	2,134.82	01-Mar-26	05-Mar-26	14-Feb-26	16-Apr-26	2,134.82	2,134.82	1.00
DAM3-E-MA-M-0100	Capped connection	5	136.99	03-Mar-26	08-Mar-26	13-Jun-26	14-Jun-26	136.99	136.99	1.00
DAM3-E-MA-M-0110	UPVC pipes	5	19,003.97	05-Mar-26	10-Mar-26	07-Feb-26	12-Apr-26	19,003.97	19,003.97	1.00
DAM3-E-MA-M-0120	Roof vent caps	5	456.64	08-Mar-26	12-Mar-26	16-Feb-26	14-Jun-26	456.64	456.64	1.00
DAM3-E-MA-M-0130	Floor drain	5	11,113.99	10-Mar-26	15-Mar-26	16-Feb-26	04-Jun-26	11,113.99	11,113.99	1.00
DAM3-E-MA-M-0140	Gully trap	5	2,397.38	12-Mar-26	21-Mar-26	09-Feb-26	26-Feb-26	2,397.38	2,397.38	1.00

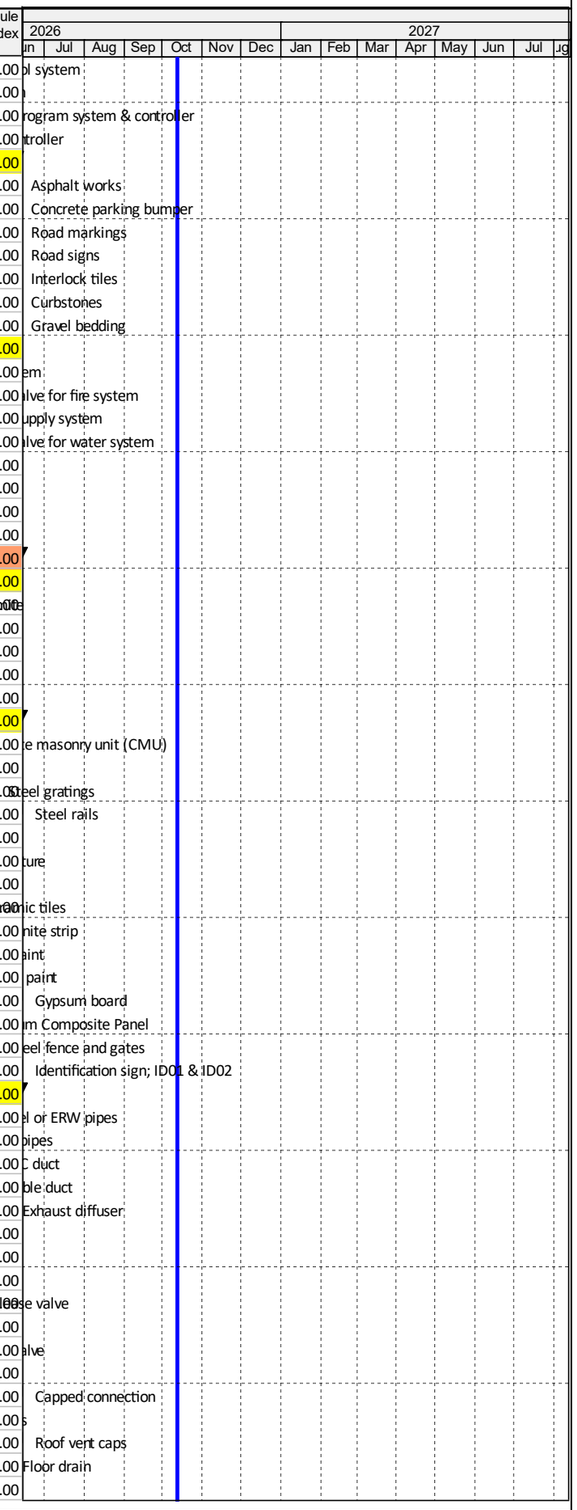

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-MA-M-0150	Electric water heater	5	896.17	15-Mar-26	23-Mar-26	08-Feb-26	01-Mar-26	896.17	896.17	1.00
DAM3-E-MA-M-0160	Western water closet	5	9,812.19	21-Mar-26	25-Mar-26	08-Feb-26	17-May-26	9,812.19	9,812.19	1.00
DAM3-E-MA-M-0170	Bib tap	5	936.14	23-Mar-26	28-Mar-26	14-Feb-26	16-Apr-26	936.14	936.14	1.00
DAM3-E-MA-M-0180	Toilet Fittings	5	11,319.13	25-Mar-26	30-Mar-26	09-Feb-26	01-Jun-26	11,319.13	11,319.13	1.00
DAM3-E-MA-M-0190	Lavatory / wash basin	5	10,548.52	28-Mar-26	01-Apr-26	08-Feb-26	17-May-26	10,548.52	10,548.52	1.00
DAM3-E-MA-M-0200	Inline exhaust fans	5	4,121.24	30-Mar-26	04-Apr-26	18-Mar-26	19-Apr-26	4,121.24	4,121.24	1.00
DAM3-E-MA-M-0210	Wall propeller type exhaust fans	5	23,066.33	01-Apr-26	06-Apr-26	18-Mar-26	19-Apr-26	23,066.33	23,066.33	1.00
DAM3-E-MA-M-0250	Fire pumps	5	15,505.34	04-Apr-26	08-Apr-26	05-Feb-26	24-Feb-26	15,505.34	15,505.34	1.00
DAM3-E-MA-M-0270	Fire fighting valves	5	1,332.84	06-Apr-26	11-Apr-26	10-Feb-26	26-Mar-26	1,332.84	1,332.84	1.00
DAM3-E-MA-M-0310	Booster pump	5	1,938.67	08-Apr-26	13-Apr-26	05-Feb-26	11-Feb-26	1,938.67	1,938.67	1.00
DAM3-E-MA-M-0320	GRP tank	5	31,477.96	11-Apr-26	15-Apr-26	02-Mar-26	07-Apr-26	31,477.96	31,477.96	1.00
DAM3-E-MA-M-0330	Water supply valves	5	467.18	13-Apr-26	18-Apr-26	10-Feb-26	26-Mar-26	467.18	467.18	1.00
DAM3-E-MA-M-3410	Water tap	5	1,415.62	15-Apr-26	20-Apr-26	14-Feb-26	16-Apr-26	1,415.62	1,415.62	1.00
ELECTRICAL		74	472,829.48	05-Feb-26	15-Apr-26	09-Feb-26	14-Jun-26	472,829.48	472,829.48	1.00
DAM3-E-MA-E-0040	PVC conduits	5	2,360.80	05-Feb-26	10-Feb-26	09-Feb-26	01-Mar-26	2,360.80	2,360.80	1.00
DAM3-E-MA-E-0050	Wires	5	1,106.91	08-Feb-26	12-Feb-26	16-Mar-26	29-Mar-26	1,106.91	1,106.91	1.00
DAM3-E-MA-E-210	Cable Tray	5	159.57	10-Feb-26	15-Feb-26	07-Mar-26	08-Mar-26	159.57	159.57	1.00
DAM3-E-MA-E-0120	Grounding system	5	9,771.19	12-Feb-26	17-Feb-26	16-Mar-26	29-Mar-26	9,771.19	9,771.19	1.00
DAM3-E-MA-E-0140	Wiring devices	5	9,962.15	15-Feb-26	21-Feb-26	07-Mar-26	08-Mar-26	9,962.15	9,962.15	1.00
DAM3-E-MA-E-0160	HDPE ducts	5	26,402.96	17-Feb-26	24-Feb-26	30-Apr-26	03-May-26	26,402.96	26,402.96	1.00
DAM3-E-MA-E-0010	Low Voltage cables	5	44,855.17	19-Feb-26	26-Feb-26	16-Mar-26	29-Mar-26	44,855.17	44,855.17	1.00
DAM3-E-MA-E-0020	Main distribution board (MDB)	5	15,994.03	23-Feb-26	01-Mar-26	26-Apr-26	12-May-26	15,994.03	15,994.03	1.00
DAM3-E-MA-E-190	Lighting panel board	5	9,064.43	25-Feb-26	03-Mar-26	26-Apr-26	12-May-26	9,064.43	9,064.43	1.00
DAM3-E-MA-E-200	PP-AC panel	5	10,662.68	01-Mar-26	05-Mar-26	26-Apr-26	12-May-26	10,662.68	10,662.68	1.00
DAM3-E-MA-E-0030	Disconnect switches	5	15,086.41	03-Mar-26	08-Mar-26	29-Mar-26	14-Jun-26	15,086.41	15,086.41	1.00
DAM3-E-MA-E-0060	Suspended High Bay LED lights	5	14,938.02	05-Mar-26	10-Mar-26	03-Mar-26	07-Mar-26	14,938.02	14,938.02	1.00
DAM3-E-MA-E-0070	Flood lights	5	2,268.18	08-Mar-26	12-Mar-26	03-Mar-26	07-Mar-26	2,268.18	2,268.18	1.00
DAM3-E-MA-E-0080	Recessed mounted LED downlight	5	20,081.13	10-Mar-26	15-Mar-26	03-Mar-26	07-Mar-26	20,081.13	20,081.13	1.00
DAM3-E-MA-E-0090	LED Emergency Lights wall mounted	5	4,144.06	12-Mar-26	21-Mar-26	03-Mar-26	07-Mar-26	4,144.06	4,144.06	1.00
DAM3-E-MA-E-0100	LED Emergency Exit Light	5	1,145.13	15-Mar-26	23-Mar-26	03-Mar-26	07-Mar-26	1,145.13	1,145.13	1.00
DAM3-E-MA-E-0110	Wall mounted, duplex, telephone and data outlet	4	13,294.12	21-Mar-26	25-Mar-26	29-Mar-26	13-Apr-26	13,294.12	13,294.12	1.00
DAM3-E-MA-E-0130	Fire alarm system	5	41,920.11	23-Mar-26	28-Mar-26	11-Feb-26	30-Mar-26	41,920.11	41,920.11	1.00
DAM3-E-MA-E-0170	Street Lighting poles	4	10,525.31	25-Mar-26	30-Mar-26	04-Mar-26	20-May-26	10,525.31	10,525.31	1.00
DAM3-E-MA-E-0180	Distribution board for pump room	4	11,002.71	28-Mar-26	01-Apr-26	26-Apr-26	12-May-26	11,002.71	11,002.71	1.00
DAM3-E-MA-E-0190	Surface mounted lights	5	11,068.82	30-Mar-26	04-Apr-26	03-Mar-26	07-Mar-26	11,068.82	11,068.82	1.00
DAM3-E-MA-E-0230	CCTV System	4	37,604.85	01-Apr-26	06-Apr-26	28-Mar-26	13-Apr-26	37,604.85	37,604.85	1.00
DAM3-E-MA-E-0240	Access control system	5	13,602.34	04-Apr-26	08-Apr-26	11-Feb-26	07-Mar-26	13,602.34	13,602.34	1.00
DAM3-E-MA-E-0250	Solar system	4	124,744.29	06-Apr-26	11-Apr-26	03-Mar-26	25-Apr-26	124,744.29	124,744.29	1.00
DAM3-E-MA-E-0260	Main program system & controller	5	12,578.11	08-Apr-26	13-Apr-26	30-Apr-26	12-May-26	12,578.11	12,578.11	1.00
DAM3-E-MA-E-0270	PLC controller	5	8,486.00	11-Apr-26	15-Apr-26	30-Apr-26	12-May-26	8,486.00	8,486.00	1.00
EXTERNAL		29	332,383.67	01-Apr-26	20-Apr-26	11-Jun-26	13-Jun-26	332,383.67	332,383.67	1.00
DAM3-E-MA-EX-0010	Asphalt works	5	280,347.76	01-Apr-26	06-Apr-26	11-Jun-26	13-Jun-26	280,347.76	280,347.76	1.00
DAM3-E-MA-EX-0020	Concrete parking bumper	5	1,433.72	04-Apr-26	08-Apr-26	11-Jun-26	13-Jun-26	1,433.72	1,433.72	1.00
DAM3-E-MA-EX-0030	Road markings	5	1,696.34	06-Apr-26	11-Apr-26	11-Jun-26	13-Jun-26	1,696.34	1,696.34	1.00
DAM3-E-MA-EX-0040	Road signs	5	4,654.29	08-Apr-26	13-Apr-26	11-Jun-26	13-Jun-26	4,654.29	4,654.29	1.00
DAM3-E-MA-EX-0060	Interlock tiles	5	21,297.02	11-Apr-26	15-Apr-26	11-Jun-26	13-Jun-26	21,297.02	21,297.02	1.00
DAM3-E-MA-EX-0070	Curbstones	5	13,036.86	13-Apr-26	18-Apr-26	11-Jun-26	13-Jun-26	13,036.86	13,036.86	1.00
DAM3-E-MA-EX-0080	Gravel bedding	5	9,917.68	15-Apr-26	20-Apr-26	11-Jun-26	13-Jun-26	9,917.68	9,917.68	1.00
ENVIRONMETAL		59	57,731.58	05-Feb-26	01-Mar-26	08-Feb-26	14-Jun-26	57,731.58	57,731.58	1.00
DAM3-E-MA-EN-0010	HDPE pipes for fire system	5	21,745.93	05-Feb-26	10-Feb-26	08-Feb-26	26-Feb-26	21,745.93	21,745.93	1.00
DAM3-E-MA-EN-0020	Directly buried gate valve for fire system	5	1,090.50	08-Feb-26	12-Feb-26	16-Feb-26	25-May-26	1,090.50	1,090.50	1.00
DAM3-E-MA-EN-0030	HDPE pipes for water supply system	5	1,598.26	10-Feb-26	15-Feb-26	08-Feb-26	26-Feb-26	1,598.26	1,598.26	1.00
DAM3-E-MA-EN-0040	Directly buried gate valve for water system	5	2,414.78	12-Feb-26	17-Feb-26	16-Feb-26	25-May-26	2,414.78	2,414.78	1.00
DAM3-E-MA-EN-0050	Air valve	5	1,963.06	15-Feb-26	21-Feb-26	18-Feb-26	26-Feb-26	1,963.06	1,963.06	1.00
DAM3-E-MA-EN-0060	Washout valve	5	2,302.04	17-Feb-26	24-Feb-26	18-Feb-26	14-Jun-26	2,302.04	2,302.04	1.00
DAM3-E-MA-EN-0070	Gate valve	5	6,398.75	19-Feb-26	26-Feb-26	18-Feb-26	14-Jun-26	6,398.75	6,398.75	1.00
DAM3-E-MA-EN-0080	UPVC pipes	5	20,218.26	23-Feb-26	01-Mar-26	08-Feb-26	26-Feb-26	20,218.26	20,218.26	1.00
METHOD STATEMENTS		125	0.00	29-Jan-26	23-Apr-26	07-Feb-26	23-Jun-26	0.00	0.00	0.00
PREPARATION AND SUBMITTAL		112	0.00	29-Jan-26	25-Mar-26	07-Feb-26	22-Jun-26	0.00	0.00	0.00
DAM3-E-MT-C-0010	Method Statement for Structural Works	7	0.00	29-Jan-26	05-Feb-26	07-Feb-26	22-Jun-26	0.00	0.00	0.00
DAM3-E-MT-A-0020	Method Statement for Architectural Works	7	0.00	07-Feb-26	14-Feb-26	05-Mar-26	22-Jun-26	0.00	0.00	0.00
DAM3-E-MT-M-0030	Method Statement for Mechanical Works	7	0.00	15-Feb-26	24-Feb-26	10-May-26	22-Jun-26	0.00	0.00	0.00

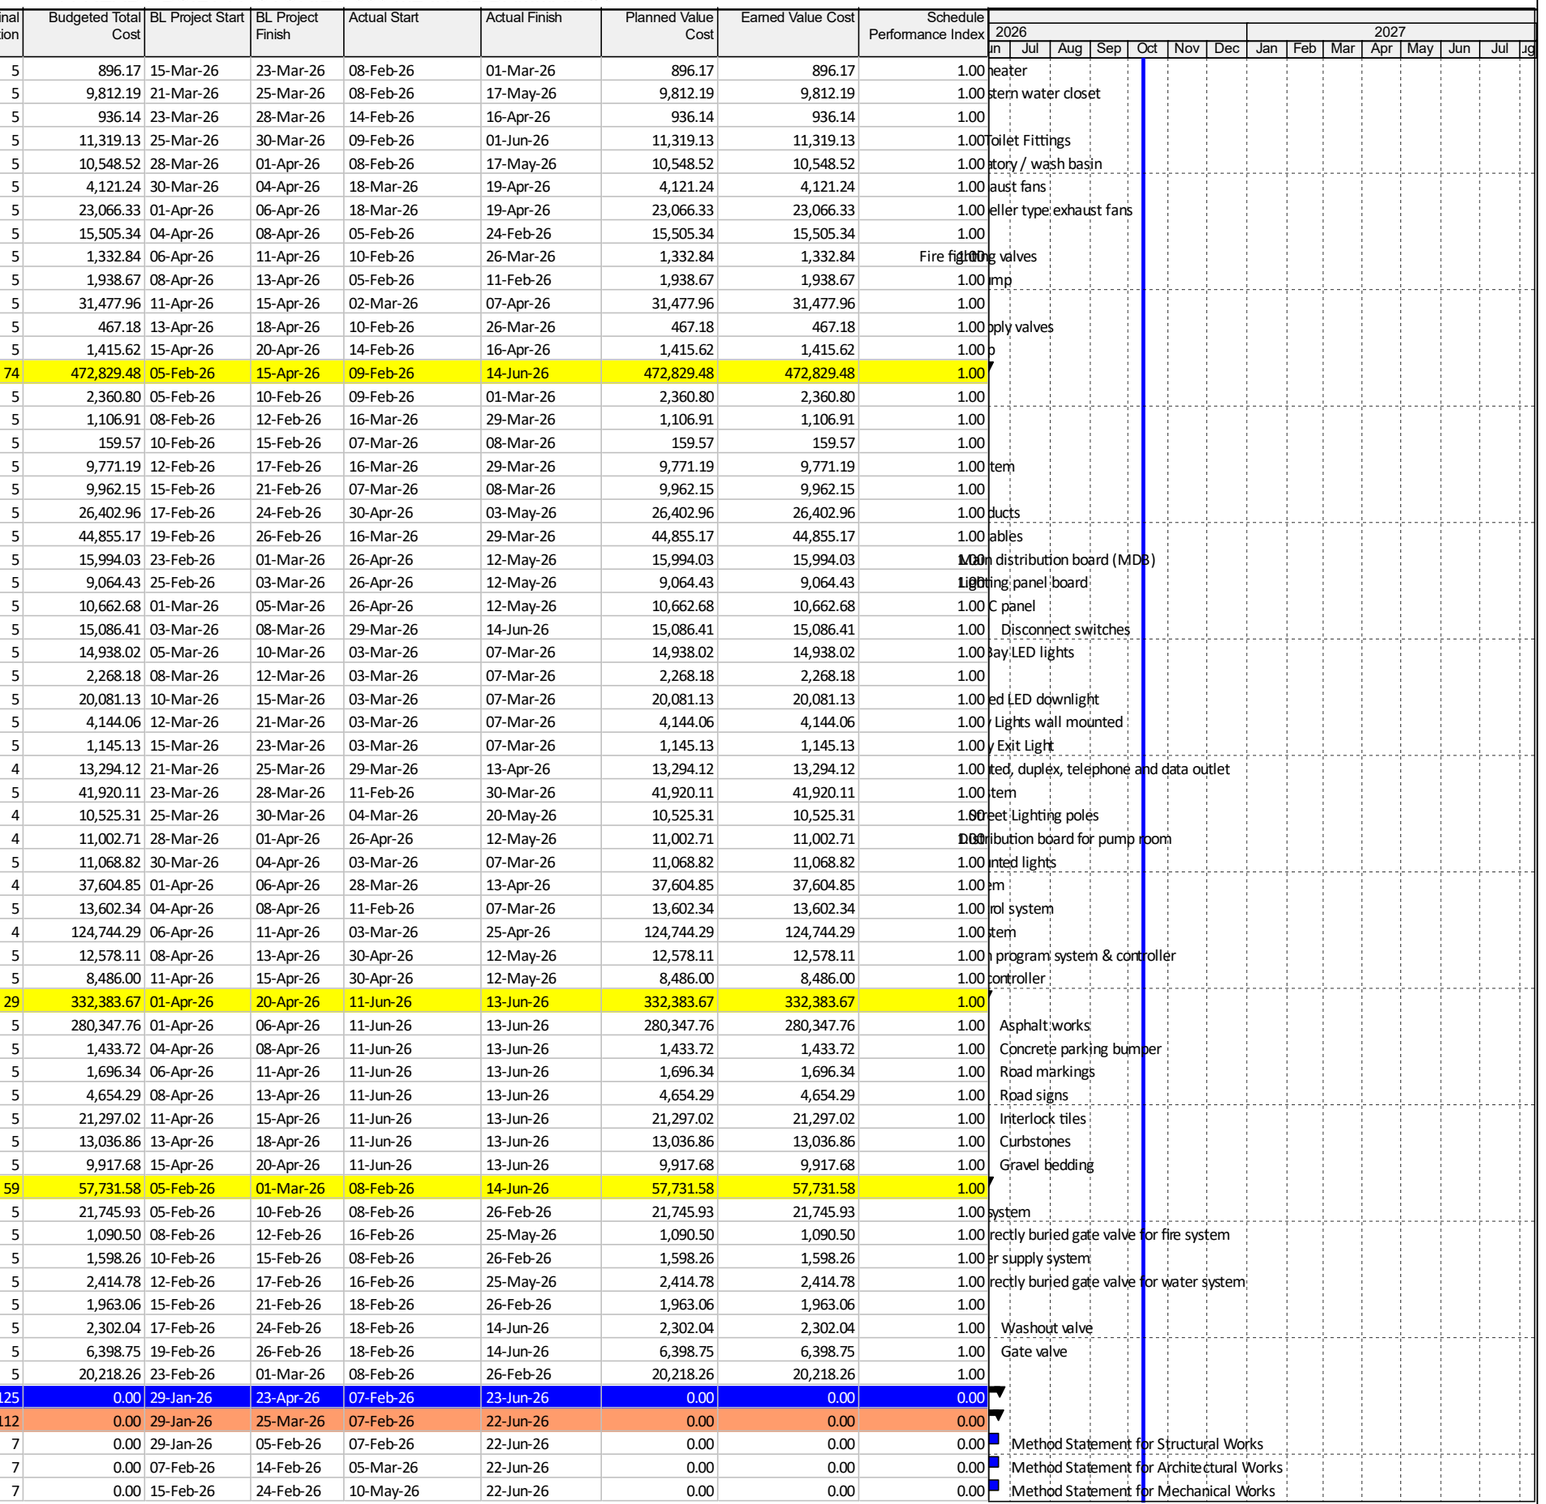

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-E-MT-E-0040	Method Statement for Electrical Works	7	0.00	24-Feb-26	04-Mar-26	10-May-26	22-Jun-26	0.00	0.00	0.00
DAM3-E-MT-EX-0050	Method Statement for External Works	7	0.00	05-Mar-26	12-Mar-26	21-Jun-26	22-Jun-26	0.00	0.00	0.00
DAM3-E-MT-ENV-0060	Method Statement for Environmental Works	8	0.00	14-Mar-26	25-Mar-26	21-Jun-26	22-Jun-26	0.00	0.00	0.00
REVIEW AND APPROVAL		51	0.00	07-Feb-26	22-Apr-26	07-Feb-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-C-1010	Method Statement for Structural Works	10	0.00	07-Feb-26	17-Feb-26	07-Feb-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-A-1020	Method Statement for Architectural Works	10	0.00	18-Feb-26	03-Mar-26	05-Mar-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-M-1030	Method Statement for Mechanical Works	10	0.00	04-Mar-26	15-Mar-26	10-May-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-E-1040	Method Statement for Electrical Works	10	0.00	16-Mar-26	30-Mar-26	10-May-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-EX-1050	Method Statement for External Works	10	0.00	31-Mar-26	11-Apr-26	21-Jun-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-ENV-1060	Method Statement for Environmental Works	10	0.00	12-Apr-26	22-Apr-26	21-Jun-26	23-Jun-26	0.00	0.00	0.00
STAGING		42	0.00	18-Feb-26	23-Apr-26	09-Feb-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-C-2010	Method Statement for Structural Works	1	0.00	18-Feb-26	19-Feb-26	09-Feb-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-A-2020	Method Statement for Architectural Works	4	0.00	04-Mar-26	08-Mar-26	21-Jun-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-M-2030	Method Statement for Mechanical Works	1	0.00	16-Mar-26	16-Mar-26	10-May-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-E-2040	Method Statement for Electrical Works	1	0.00	31-Mar-26	31-Mar-26	10-May-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-EX-2050	Method Statement for External Works	1	0.00	12-Apr-26	12-Apr-26	21-Jun-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MT-ENV-2060	Method Statement for Environmental Works	1	0.00	23-Apr-26	23-Apr-26	21-Jun-26	23-Jun-26	0.00	0.00	0.00
PROCUREMENT (20%)		258	19,199,305.00	04-Feb-26	15-Nov-26	14-Jan-26	27-Sep-26	18,149,515.44	19,199,305.00	1.06
LONG LEAD MATERIALS		245	9,350,010.31	09-Feb-26	15-Nov-26	14-Jan-26	27-Sep-26	8,300,220.75	9,350,010.31	1.13
ARCHITECTURAL		145	6,184,977.93	18-Feb-26	06-Jul-26	14-Jan-26	20-Aug-26	6,184,977.93	6,184,977.93	1.00
PO ISSUE		90	0.00	18-Feb-26	28-Feb-26	14-Jan-26	22-Mar-26	0.00	0.00	0.00
DAM3-P-PO-A-180	Doors	5	0.00	18-Feb-26	25-Feb-26	18-Mar-26	18-Mar-26	0.00	0.00	0.00
DAM3-E-PO-A-1700	PES -Steel Structure	5	0.00	18-Feb-26	25-Feb-26	14-Jan-26	14-Jan-26	0.00	0.00	0.00
DAM3-P-PO-A-190	Windows	5	0.00	21-Feb-26	28-Feb-26	22-Mar-26	22-Mar-26	0.00	0.00	0.00
MANUFACTURING		99	0.00	25-Feb-26	20-Jun-26	14-Jan-26	23-Jun-26	0.00	0.00	0.00
DAM3-P-MF-A-180	Doors	90	0.00	25-Feb-26	17-Jun-26	21-Mar-26	23-Jun-26	0.00	0.00	0.00
DAM3-E-MF-A-1700	PES -Steel Structure	45	0.00	25-Feb-26	22-Apr-26	14-Jan-26	25-May-26	0.00	0.00	0.00
DAM3-P-MF-A-190	Windows	90	0.00	01-Mar-26	20-Jun-26	25-Mar-26	23-Jun-26	0.00	0.00	0.00
DELIVERY TO SITE		59	6,184,977.93	23-Apr-26	04-Jul-26	31-May-26	20-Aug-26	6,184,977.93	6,184,977.93	1.00
DAM3-P-DL-A-1700	PES -Steel Structure -1	7	2,369,269.97	23-Apr-26	30-Apr-26	31-May-26	31-May-26	2,369,269.97	2,369,269.97	1.00
DAM3-P-DL-A-1770	PES -Steel Structure -2	7	740,740.74	02-May-26	09-May-26	10-Jun-26	14-Jun-26	740,740.74	740,740.74	1.00
DAM3-P-DL-A-180	Doors	7	502,577.07	18-Jun-26	25-Jun-26	18-Aug-26	20-Aug-26	502,577.07	502,577.07	1.00
DAM3-P-DL-A-1780	PES -Steel Structure -3	7	740,740.74	18-Jun-26	25-Jun-26	14-Jun-26	14-Jul-26	740,740.74	740,740.74	1.00
DAM3-P-DL-A-190	Windows	7	350,167.93	21-Jun-26	28-Jun-26	19-Aug-26	20-Aug-26	350,167.93	350,167.93	1.00
DAM3-P-DL-A-1790	PES -Steel Structure -4	7	1,481,481.48	27-Jun-26	04-Jul-26	01-Jul-26	01-Jul-26	1,481,481.48	1,481,481.48	1.00
STAGING TIME		38	0.00	02-May-26	06-Jul-26	21-Jul-26	20-Aug-26	0.00	0.00	0.00
DAM3-E-ST-A-1700	PES -Steel Structure	2	0.00	02-May-26	03-May-26	21-Jul-26	22-Jul-26	0.00	0.00	0.00
DAM3-P-ST-A-180	Doors	7	0.00	27-Jun-26	04-Jul-26	18-Aug-26	20-Aug-26	0.00	0.00	0.00
DAM3-P-ST-A-190	Windows	7	0.00	29-Jun-26	06-Jul-26	19-Aug-26	20-Aug-26	0.00	0.00	0.00
ELECTRICAL		187	2,332,207.26	01-Mar-26	15-Nov-26	24-Mar-26	27-Sep-26	1,282,417.69	2,332,207.26	1.82
PO ISSUE		60	0.00	01-Mar-26	14-May-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-190	Main distribution board (MDB)	5	0.00	01-Mar-26	07-Mar-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-190	Lighting panel board	5	0.00	07-Mar-26	12-Mar-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-200	PP-AC panel	5	0.00	12-Mar-26	22-Mar-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-200	Suspended High Bay LED lights	5	0.00	24-Mar-26	29-Mar-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-210	Flood lights	5	0.00	30-Mar-26	04-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-220	Recessed mounted LED downlight	5	0.00	05-Apr-26	09-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-0230	CCTV System	5	0.00	07-Apr-26	12-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-0240	Access control system	5	0.00	09-Apr-26	14-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-230	LED Emergency Lights wall mounted	5	0.00	11-Apr-26	15-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-0250	Solar system	5	0.00	12-Apr-26	16-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-0260	Main program system & controller	5	0.00	14-Apr-26	19-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-240	LED Emergency Exit Light	5	0.00	16-Apr-26	21-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-E-PO-E-0270	PLC controller	5	0.00	16-Apr-26	21-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-250	Fire alarm system	5	0.00	22-Apr-26	27-Apr-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-260	Street Lighting poles	5	0.00	28-Apr-26	03-May-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-270	Distribution board for pump room	5	0.00	04-May-26	09-May-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-280	Surface mounted lights	5	0.00	10-May-26	14-May-26	24-Mar-26	24-Mar-26	0.00	0.00	0.00
MANUFACTURING		187	0.00	07-Mar-26	29-Oct-26	01-Apr-26	27-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-190	Main distribution board (MDB)	90	0.00	07-Mar-26	27-Jun-26	01-Apr-26	22-Aug-26	0.00	0.00	0.00
DAM3-E-MF-E-190	Lighting panel board	90	0.00	12-Mar-26	02-Jul-26	07-Apr-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-200	PP-AC panel	90	0.00	22-Mar-26	08-Jul-26	13-Apr-26	20-Sep-26	0.00	0.00	0.00

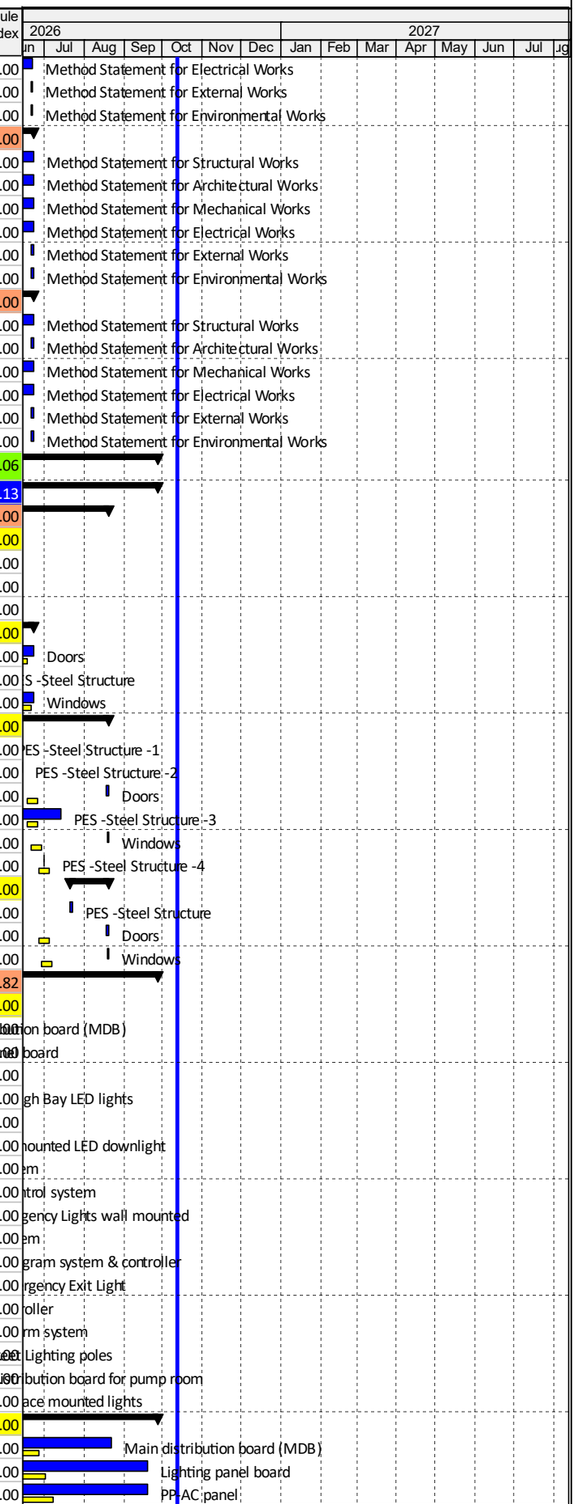

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-MF-E-200	Suspended High Bay LED lights	90	0.00	30-Mar-26	15-Jul-26	20-Apr-26	27-Aug-26	0.00	0.00	0.00
DAM3-P-MF-E-210	Flood lights	90	0.00	05-Apr-26	21-Jul-26	28-Apr-26	27-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-220	Recessed mounted LED downlight	90	0.00	11-Apr-26	27-Jul-26	04-May-26	27-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-0230	CCTV System	120	0.00	13-Apr-26	02-Sep-26	25-Apr-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-0240	Access control system	150	0.00	15-Apr-26	11-Oct-26	16-Apr-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-230	LED Emergency Lights wall mounted	90	0.00	16-Apr-26	02-Aug-26	10-May-26	27-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-0250	Solar system	150	0.00	18-Apr-26	13-Oct-26	25-Apr-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-0260	Main program system & controller	155	0.00	20-Apr-26	21-Oct-26	29-Apr-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-240	LED Emergency Exit Light	90	0.00	22-Apr-26	08-Aug-26	16-May-26	27-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-0270	PLC controller	160	0.00	22-Apr-26	29-Oct-26	02-May-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-250	Fire alarm system	130	0.00	28-Apr-26	30-Sep-26	21-May-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-260	Street Lighting poles	90	0.00	04-May-26	19-Aug-26	31-May-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-MF-E-270	Distribution board for pump room	90	0.00	10-May-26	25-Aug-26	06-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-MF-E-280	Surface mounted lights	90	0.00	16-May-26	31-Aug-26	11-Jun-26	21-Jun-26	0.00	0.00	0.00
DELIVERY TO SITE		33	2,332,207.26	27-Jun-26	07-Nov-26	24-Aug-26	21-Sep-26	1,282,417.69	2,332,207.26	1.82
DAM3-P-DL-E-190	Main distribution board (MDB)	7	106,626.87	27-Jun-26	05-Jul-26	24-Aug-26	24-Aug-26	106,626.87	106,626.87	1.00
DAM3-P-DL-E-1900	Lighting panel board	7	60,429.51	02-Jul-26	11-Jul-26	01-Sep-26	21-Sep-26	60,429.51	60,429.51	1.00
DAM3-P-DL-E-2000	PP-AC panel	7	71,084.56	08-Jul-26	16-Jul-26	01-Sep-26	21-Sep-26	71,084.56	71,084.56	1.00
DAM3-P-DL-E-200	Suspended High Bay LED lights	7	99,586.79	16-Jul-26	23-Jul-26	29-Aug-26	29-Aug-26	99,586.79	99,586.79	1.00
DAM3-P-DL-E-210	Flood lights	7	15,121.21	22-Jul-26	29-Jul-26	29-Aug-26	29-Aug-26	15,121.21	15,121.21	1.00
DAM3-P-DL-E-220	Recessed mounted LED downlight	7	133,874.22	28-Jul-26	04-Aug-26	29-Aug-26	29-Aug-26	133,874.22	133,874.22	1.00
DAM3-P-DL-E-230	LED Emergency Lights wall mounted	7	27,627.07	03-Aug-26	10-Aug-26	29-Aug-26	29-Aug-26	27,627.07	27,627.07	1.00
DAM3-P-DL-E-240	LED Emergency Exit Light	7	7,634.17	09-Aug-26	16-Aug-26	29-Aug-26	29-Aug-26	7,634.17	7,634.17	1.00
DAM3-P-DL-E-260	Street Lighting poles	7	70,168.75	20-Aug-26	27-Aug-26	19-Sep-26	21-Sep-26	70,168.75	70,168.75	1.00
DAM3-P-DL-E-270	Distribution board for pump room	7	73,351.39	26-Aug-26	02-Sep-26	19-Sep-26	20-Sep-26	73,351.39	73,351.39	1.00
DAM3-P-DL-E-280	Surface mounted lights	7	73,792.16	01-Sep-26	08-Sep-26	29-Aug-26	29-Aug-26	73,792.16	73,792.16	1.00
DAM3-P-DL-E-0230	CCTV System	7	250,698.98	03-Sep-26	10-Sep-26	06-Sep-26	21-Sep-26	250,698.98	250,698.98	1.00
DAM3-P-DL-E-250	Fire alarm system	7	279,467.41	01-Oct-26	08-Oct-26	02-Sep-26	21-Sep-26	279,467.41	279,467.41	1.00
DAM3-P-DL-E-0240	Access control system	7	90,682.24	12-Oct-26	19-Oct-26	19-Sep-26	21-Sep-26	12,954.61	90,682.24	7.00
DAM3-P-DL-E-0250	Solar system	7	831,628.60	14-Oct-26	21-Oct-26	09-Sep-26	21-Sep-26	0.00	831,628.60	0.00
DAM3-P-DL-E-0260	Main program system & controller	7	83,856.79	22-Oct-26	29-Oct-26	06-Sep-26	21-Sep-26	0.00	83,856.79	0.00
DAM3-P-DL-E-0270	PLC controller	7	56,576.55	31-Oct-26	07-Nov-26	07-Sep-26	21-Sep-26	0.00	56,576.55	0.00
STAGING TIME		38	0.00	05-Jul-26	15-Nov-26	24-Aug-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-190	Main distribution board (MDB)	7	0.00	05-Jul-26	13-Jul-26	24-Aug-26	24-Aug-26	0.00	0.00	0.00
DAM3-E-ST-E-190	Lighting panel board	7	0.00	11-Jul-26	19-Jul-26	01-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-200	PP-AC panel	7	0.00	16-Jul-26	25-Jul-26	01-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-200	Suspended High Bay LED lights	7	0.00	25-Jul-26	01-Aug-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-P-ST-E-210	Flood lights	7	0.00	30-Jul-26	06-Aug-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-P-ST-E-220	Recessed mounted LED downlight	7	0.00	05-Aug-26	12-Aug-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-P-ST-E-230	LED Emergency Lights wall mounted	7	0.00	11-Aug-26	18-Aug-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-P-ST-E-240	LED Emergency Exit Light	7	0.00	17-Aug-26	24-Aug-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-P-ST-E-260	Street Lighting poles	7	0.00	29-Aug-26	05-Sep-26	19-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-270	Distribution board for pump room	7	0.00	03-Sep-26	10-Sep-26	19-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-280	Surface mounted lights	7	0.00	09-Sep-26	16-Sep-26	29-Aug-26	29-Aug-26	0.00	0.00	0.00
DAM3-E-ST-E-0230	CCTV System	7	0.00	12-Sep-26	19-Sep-26	06-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-250	Fire alarm system	7	0.00	10-Oct-26	17-Oct-26	02-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-0240	Access control system	7	0.00	20-Oct-26	27-Oct-26	19-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-0250	Solar system	7	0.00	22-Oct-26	29-Oct-26	09-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-0260	Main program system & controller	7	0.00	31-Oct-26	07-Nov-26	06-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-0270	PLC controller	7	0.00	08-Nov-26	15-Nov-26	07-Sep-26	21-Sep-26	0.00	0.00	0.00
MECHANICAL		216	832,825.12	09-Feb-26	13-Oct-26	01-Mar-26	20-Sep-26	832,825.12	832,825.12	1.00
PO ISSUE		84	0.00	09-Feb-26	29-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-340	Seamless black steel or ERW pipes	5	0.00	09-Feb-26	14-Feb-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-350	Fire hose cabinet	5	0.00	24-Feb-26	02-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-360	Western water closet	5	0.00	25-Mar-26	31-Mar-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-370	Wall propeller type exhaust fans	5	0.00	06-Apr-26	12-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-380	Fire pumps	5	0.00	12-Apr-26	18-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-400	Booster pump	5	0.00	18-Apr-26	23-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-M-410	GRP tank	5	0.00	23-Apr-26	29-Apr-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
MANUFACTURING		211	0.00	15-Feb-26	27-Sep-26	02-Mar-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-340	Seamless black steel or ERW pipes	120	0.00	15-Feb-26	13-Jul-26	02-Mar-26	29-Jun-26	0.00	0.00	0.00
DAM3-P-MF-M-350	Fire hose cabinet	120	0.00	03-Mar-26	27-Jul-26	02-Mar-26	19-Sep-26	0.00	0.00	0.00

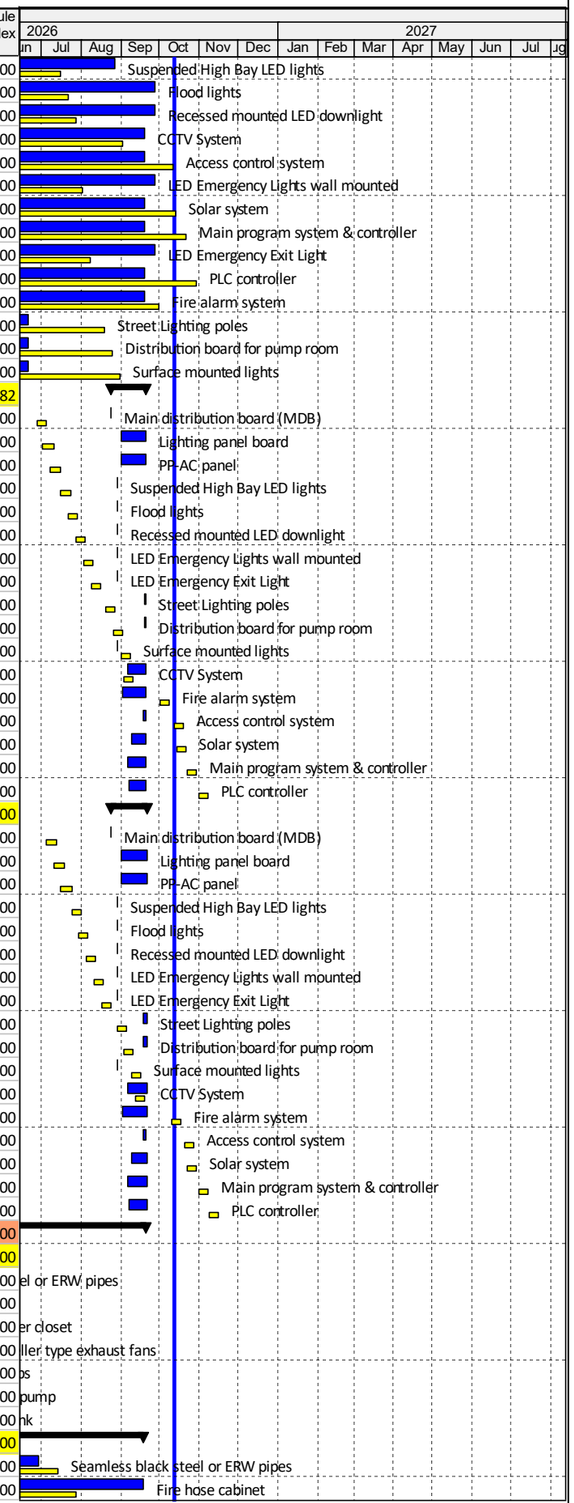


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-MF-M-360	Western water closet	150	0.00	31-Mar-26	27-Sep-26	02-Mar-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-370	Wall propeller type exhaust fans	100	0.00	12-Apr-26	10-Aug-26	02-Mar-26	09-Aug-26	0.00	0.00	0.00
DAM3-P-MF-M-380	Fire pumps	120	0.00	18-Apr-26	08-Sep-26	02-Mar-26	17-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-400	Booster pump	110	0.00	23-Apr-26	02-Sep-26	02-Mar-26	06-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-410	GRP tank	100	0.00	29-Apr-26	27-Aug-26	02-Mar-26	25-Aug-26	0.00	0.00	0.00
DELIVERY TO SITE		72	832,825.12	14-Jul-26	05-Oct-26	01-Jul-26	20-Sep-26	832,825.12	832,825.12	1.00
DAM3-P-DL-M-340	Seamless black steel or ERW pipes	7	237,714.11	14-Jul-26	21-Jul-26	01-Jul-26	11-Aug-26	237,714.11	237,714.11	1.00
DAM3-P-DL-M-350	Fire hose cabinet	7	49,774.39	28-Jul-26	04-Aug-26	19-Sep-26	20-Sep-26	49,774.39	49,774.39	1.00
DAM3-P-DL-M-370	Wall propeller type exhaust fans	7	153,775.51	10-Aug-26	18-Aug-26	10-Aug-26	20-Sep-26	153,775.51	153,775.51	1.00
DAM3-P-DL-M-410	GRP tank	7	209,853.09	27-Aug-26	05-Sep-26	29-Aug-26	31-Aug-26	209,853.09	209,853.09	1.00
DAM3-P-DL-M-400	Booster pump	7	12,924.47	02-Sep-26	10-Sep-26	07-Sep-26	07-Sep-26	12,924.47	12,924.47	1.00
DAM3-P-DL-M-380	Fire pumps	7	103,368.93	08-Sep-26	16-Sep-26	20-Sep-26	20-Sep-26	103,368.93	103,368.93	1.00
DAM3-P-DL-M-360	Western water closet	7	65,414.62	27-Sep-26	05-Oct-26	19-Sep-26	20-Sep-26	65,414.62	65,414.62	1.00
STAGING TIME		86	0.00	22-Jul-26	13-Oct-26	01-Jul-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-340	Seamless black steel or ERW pipes	7	0.00	22-Jul-26	29-Jul-26	01-Jul-26	11-Aug-26	0.00	0.00	0.00
DAM3-P-ST-M-350	Fire hose cabinet	7	0.00	05-Aug-26	12-Aug-26	19-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-370	Wall propeller type exhaust fans	7	0.00	18-Aug-26	26-Aug-26	10-Aug-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-410	GRP tank	7	0.00	05-Sep-26	13-Sep-26	29-Aug-26	31-Aug-26	0.00	0.00	0.00
DAM3-P-ST-M-400	Booster pump	7	0.00	10-Sep-26	19-Sep-26	07-Sep-26	07-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-380	Fire pumps	7	0.00	16-Sep-26	26-Sep-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-360	Western water closet	7	0.00	05-Oct-26	13-Oct-26	19-Sep-26	20-Sep-26	0.00	0.00	0.00
SHORT LEAD MATERIALS		258	9,849,294.69	04-Feb-26	14-Oct-26	14-Jan-26	21-Sep-26	9,849,294.69	9,849,294.69	1.00
STRUCTURAL		74	3,207,417.90	04-Feb-26	15-Apr-26	20-Jan-26	29-Apr-26	3,207,417.90	3,207,417.90	1.00
PO ISSUE		28	0.00	04-Feb-26	15-Feb-26	20-Jan-26	25-Mar-26	0.00	0.00	0.00
DAM3-P-PO-C-50	Anti termite	2	0.00	04-Feb-26	05-Feb-26	25-Mar-26	25-Mar-26	0.00	0.00	0.00
DAM3-P-PO-C-60	Concrete mix	2	0.00	07-Feb-26	08-Feb-26	20-Jan-26	20-Jan-26	0.00	0.00	0.00
DAM3-P-PO-C-70	Polyethylene sheet	2	0.00	09-Feb-26	10-Feb-26	01-Mar-26	01-Mar-26	0.00	0.00	0.00
DAM3-P-PO-C-80	Bitumen paint	2	0.00	11-Feb-26	12-Feb-26	09-Mar-26	09-Mar-26	0.00	0.00	0.00
DAM3-P-PO-C-90	Rebar	2	0.00	14-Feb-26	15-Feb-26	01-Feb-26	01-Feb-26	0.00	0.00	0.00
MANUFACTURING		38	0.00	07-Feb-26	02-Mar-26	21-Jan-26	07-Apr-26	0.00	0.00	0.00
DAM3-P-MF-C-50	Anti termite	12	0.00	07-Feb-26	21-Feb-26	26-Mar-26	07-Apr-26	0.00	0.00	Anti termite 0.00
DAM3-P-MF-C-60	Concrete mix	17	0.00	09-Feb-26	02-Mar-26	21-Jan-26	01-Feb-26	0.00	0.00	0.00
DAM3-P-MF-C-70	Polyethylene sheet	10	0.00	09-Feb-26	21-Feb-26	02-Mar-26	10-Mar-26	0.00	0.00	0.00 t
DAM3-P-MF-C-80	Bitumen paint	10	0.00	14-Feb-26	26-Feb-26	10-Mar-26	07-Apr-26	0.00	0.00	0.00 nt
DAM3-P-MF-C-90	Rebar	7	0.00	16-Feb-26	25-Feb-26	02-Feb-26	15-Feb-26	0.00	0.00	0.00
DELIVERY		59	3,207,417.90	21-Feb-26	15-Apr-26	12-Mar-26	29-Apr-26	3,207,417.90	3,207,417.90	1.00
DAM3-P-DL-C-50	Anti termite	2	130,309.59	21-Feb-26	24-Feb-26	12-Mar-26	29-Apr-26	130,309.59	130,309.59	Anti termite 1.00
DAM3-P-DL-C-70	Polyethylene sheet	2	86,906.55	21-Feb-26	24-Feb-26	12-Mar-26	29-Apr-26	86,906.55	86,906.55	1.00 ylene sheet
DAM3-P-DL-C-90	Rebar-1	2	218,896.43	25-Feb-26	28-Feb-26	31-Mar-26	29-Apr-26	218,896.43	218,896.43	1.00
DAM3-P-DL-C-80	Bitumen paint	2	192,960.68	26-Feb-26	01-Mar-26	31-Mar-26	29-Apr-26	192,960.68	192,960.68	1.00 n paint
DAM3-P-DL-C-60	Concrete mix -1	2	196,863.16	03-Mar-26	04-Mar-26	12-Mar-26	14-Apr-26	196,863.16	196,863.16	1.00 mix -1
DAM3-P-DL-C-100	Concrete mix -2	2	740,740.74	12-Apr-26	13-Apr-26	16-Apr-26	29-Apr-26	740,740.74	740,740.74	1.00 te mix -2
DAM3-P-DL-C-120	Rebar-2	2	450,000.00	12-Apr-26	13-Apr-26	16-Apr-26	29-Apr-26	450,000.00	450,000.00	1.00
DAM3-P-DL-C-110	Concrete mix -3	2	740,740.74	14-Apr-26	15-Apr-26	16-Apr-26	29-Apr-26	740,740.74	740,740.74	1.00 te mix -3
DAM3-P-DL-C-130	Rebar-3	2	450,000.00	14-Apr-26	15-Apr-26	16-Apr-26	29-Apr-26	450,000.00	450,000.00	1.00
STAGING TIME		16	0.00	24-Feb-26	05-Mar-26	12-Mar-26	29-Apr-26	0.00	0.00	0.00
DAM3-P-ST-C-50	Anti termite	1	0.00	24-Feb-26	25-Feb-26	12-Mar-26	29-Apr-26	0.00	0.00	Anti termite 0.00
DAM3-P-ST-C-70	Polyethylene sheet	1	0.00	24-Feb-26	25-Feb-26	12-Mar-26	29-Apr-26	0.00	0.00	0.00 ylene sheet
DAM3-P-ST-C-90	Rebar	1	0.00	01-Mar-26	01-Mar-26	31-Mar-26	29-Apr-26	0.00	0.00	0.00
DAM3-P-ST-C-80	Bitumen paint	1	0.00	02-Mar-26	02-Mar-26	31-Mar-26	29-Apr-26	0.00	0.00	0.00 n paint
DAM3-P-ST-C-60	Concrete mix	1	0.00	05-Mar-26	05-Mar-26	12-Mar-26	29-Apr-26	0.00	0.00	0.00 te mix
ARCHITECTURAL		107	2,031,043.96	09-Feb-26	19-Jul-26	14-Jan-26	20-Sep-26	2,031,043.96	2,031,043.96	1.00
PO ISSUE		86	0.00	09-Feb-26	28-Mar-26	14-Jan-26	24-May-26	0.00	0.00	0.00
DAM3-P-PO-A-200	Concrete masonry unit (CMU)	5	0.00	09-Feb-26	14-Feb-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00 sonry unit (CMU)
DAM3-P-PO-A-210	Steel ladder	5	0.00	15-Feb-26	21-Feb-26	14-Jan-26	18-Jan-26	0.00	0.00	0.00
DAM3-P-PO-A-220	Steel gratings	5	0.00	21-Feb-26	28-Feb-26	02-Apr-26	02-Apr-26	0.00	0.00	Steel gratings 0.00
DAM3-P-PO-A-280	Ceramic tiles	5	0.00	24-Feb-26	02-Mar-26	07-Apr-26	07-Apr-26	0.00	0.00	Ceramic tiles 0.00
DAM3-P-PO-A-230	Steel rails	5	0.00	01-Mar-26	05-Mar-26	24-May-26	24-May-26	0.00	0.00	0.00 eel rails
DAM3-P-PO-A-310	Epoxy paint	5	0.00	01-Mar-26	07-Mar-26	24-May-26	24-May-26	0.00	0.00	0.00 oxy paint
DAM3-P-PO-A-290	Granite strip	5	0.00	03-Mar-26	08-Mar-26	12-May-26	12-May-26	0.00	0.00	0.00 ite strip
DAM3-P-PO-A-320	Internl paint	5	0.00	07-Mar-26	12-Mar-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
DAM3-E-PO-A-1750	Steel fence and gates	5	0.00	11-Mar-26	16-Mar-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00 nd gates

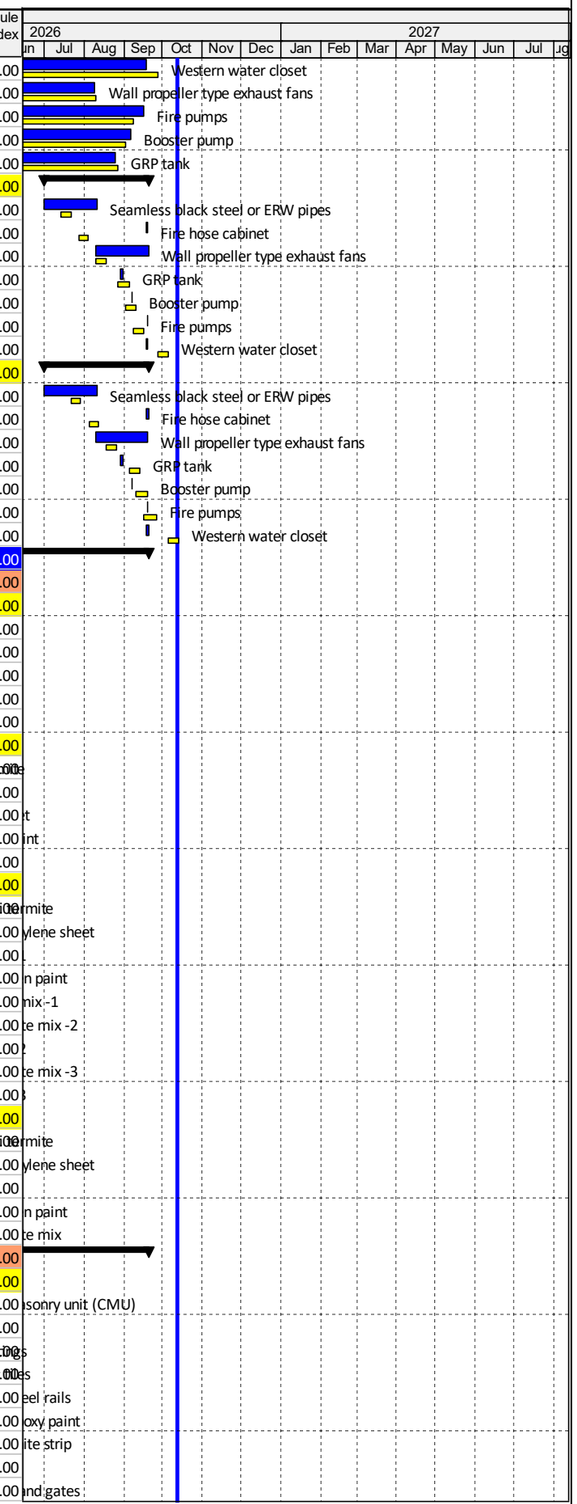

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-PO-A-330	Gypsum board	5	0.00	12-Mar-26	22-Mar-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
DAM3-E-PO-A-1760	Identification sign; ID01 & ID02	5	0.00	21-Mar-26	25-Mar-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
DAM3-E-PO-A-1720	Aluminum Composite Panel	5	0.00	22-Mar-26	28-Mar-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
MANUFACTURING		100	0.00	15-Feb-26	02-Jul-26	14-Jan-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-A-200	Concrete masonry unit (CMU)	50	0.00	15-Feb-26	19-Apr-26	06-Apr-26	08-Jun-26	0.00	0.00	0.00
DAM3-P-MF-A-210	Steel ladder	80	0.00	21-Feb-26	02-Jun-26	14-Jan-26	22-Jul-26	0.00	0.00	0.00
DAM3-P-MF-A-220	Steel gratings	80	0.00	01-Mar-26	08-Jun-26	06-Apr-26	02-Jul-26	0.00	0.00	0.00
DAM3-P-MF-A-280	Ceramic tiles	80	0.00	03-Mar-26	10-Jun-26	06-Apr-26	09-Jun-26	0.00	0.00	0.00
DAM3-P-MF-A-230	Steel rails	80	0.00	07-Mar-26	14-Jun-26	06-Apr-26	02-Jul-26	0.00	0.00	0.00
DAM3-P-MF-A-310	Epoxy paint	80	0.00	07-Mar-26	15-Jun-26	06-Apr-26	20-Jul-26	0.00	0.00	0.00
DAM3-P-MF-A-290	Granite strip	80	0.00	09-Mar-26	16-Jun-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-A-320	Internl paint	80	0.00	12-Mar-26	21-Jun-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-E-MF-A-1750	Steel fence and gates	80	0.00	21-Mar-26	24-Jun-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-A-330	Gypsum board	80	0.00	22-Mar-26	27-Jun-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-E-MF-A-1760	Identification sign; ID01 & ID02	80	0.00	26-Mar-26	30-Jun-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-E-MF-A-1720	Aluminum Composite Panel	80	0.00	28-Mar-26	02-Jul-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DELIVERY		59	2,031,043.96	20-Apr-26	11-Jul-26	10-Jun-26	20-Sep-26	2,031,043.96	2,031,043.96	1.00
DAM3-P-DL-A-200	Concrete masonry unit (CMU)	7	418,802.40	20-Apr-26	27-Apr-26	10-Jun-26	14-Jun-26	418,802.40	418,802.40	1.00
DAM3-P-DL-A-210	Steel ladder	7	32,307.70	03-Jun-26	10-Jun-26	28-Jul-26	28-Jul-26	32,307.70	32,307.70	1.00
DAM3-P-DL-A-220	Steel gratings	7	21,196.03	09-Jun-26	16-Jun-26	05-Jul-26	05-Jul-26	21,196.03	21,196.03	1.00
DAM3-P-DL-A-280	Ceramic tiles	7	241,008.42	11-Jun-26	18-Jun-26	11-Jun-26	15-Jun-26	241,008.42	241,008.42	1.00
DAM3-P-DL-A-230	Steel rails	7	5,036.93	15-Jun-26	22-Jun-26	28-Jul-26	28-Jul-26	5,036.93	5,036.93	1.00
DAM3-P-DL-A-310	Epoxy paint	7	378,990.27	15-Jun-26	23-Jun-26	23-Jul-26	25-Jul-26	378,990.27	378,990.27	1.00
DAM3-P-DL-A-290	Granite strip	7	2,203.66	17-Jun-26	24-Jun-26	20-Sep-26	20-Sep-26	2,203.66	2,203.66	1.00
DAM3-P-DL-A-320	Internl paint	7	145,026.96	21-Jun-26	29-Jun-26	02-Sep-26	20-Sep-26	145,026.96	145,026.96	1.00
DAM3-P-DL-A-1750	Steel fence and gates	7	23,657.36	25-Jun-26	02-Jul-26	20-Sep-26	20-Sep-26	23,657.36	23,657.36	1.00
DAM3-P-DL-A-330	Gypsum board	7	153,646.35	27-Jun-26	05-Jul-26	14-Sep-26	20-Sep-26	153,646.35	153,646.35	1.00
DAM3-P-DL-A-1760	Identification sign; ID01 & ID02	7	31,622.71	01-Jul-26	08-Jul-26	20-Sep-26	20-Sep-26	31,622.71	31,622.71	1.00
DAM3-P-DL-A-1720	Aluminum Composite Panel	7	577,545.17	02-Jul-26	11-Jul-26	07-Sep-26	20-Sep-26	577,545.17	577,545.17	1.00
STAGING TIME		58	0.00	28-Apr-26	19-Jul-26	15-Jun-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-A-200	Concrete masonry unit (CMU)	7	0.00	28-Apr-26	05-May-26	15-Jun-26	15-Jun-26	0.00	0.00	0.00
DAM3-P-ST-A-210	Steel ladder	7	0.00	11-Jun-26	18-Jun-26	28-Jul-26	28-Jul-26	0.00	0.00	0.00
DAM3-P-ST-A-220	Steel gratings	7	0.00	17-Jun-26	24-Jun-26	05-Jul-26	05-Jul-26	0.00	0.00	0.00
DAM3-P-ST-A-280	Ceramic tiles	7	0.00	20-Jun-26	27-Jun-26	15-Jun-26	15-Jun-26	0.00	0.00	0.00
DAM3-P-ST-A-230	Steel rails	7	0.00	23-Jun-26	30-Jun-26	28-Jul-26	28-Jul-26	0.00	0.00	0.00
DAM3-P-ST-A-310	Epoxy paint	7	0.00	23-Jun-26	01-Jul-26	23-Jul-26	25-Jul-26	0.00	0.00	0.00
DAM3-P-ST-A-290	Granite strip	7	0.00	25-Jun-26	02-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-A-320	Internl paint	7	0.00	29-Jun-26	07-Jul-26	02-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-ST-A-1750	Steel fence and gates	7	0.00	04-Jul-26	11-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-A-330	Gypsum board	7	0.00	05-Jul-26	13-Jul-26	14-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-ST-A-1760	Identification sign; ID01 & ID02	7	0.00	09-Jul-26	16-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-ST-A-1720	Aluminum Composite Panel	7	0.00	11-Jul-26	19-Jul-26	07-Sep-26	20-Sep-26	0.00	0.00	0.00
MECHANICAL		174	1,190,075.32	11-Feb-26	14-Oct-26	05-Apr-26	20-Sep-26	1,190,075.32	1,190,075.32	1.00
PO ISSUE		60	0.00	11-Feb-26	12-May-26	05-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-480	PPR pipes	5	0.00	11-Feb-26	16-Feb-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-600	HVAC duct	5	0.00	17-Feb-26	24-Feb-26	05-Apr-26	05-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-610	Flexible duct	5	0.00	24-Feb-26	02-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-620	Exhaust diffuser	5	0.00	03-Mar-26	08-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-490	Ball valve	5	0.00	07-Mar-26	11-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-430	U/G HDPE pipes	5	0.00	09-Mar-26	14-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-500	Capped connection	5	0.00	12-Mar-26	21-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-660	Warning tapes	5	0.00	15-Mar-26	23-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-510	UPVC pipes	5	0.00	22-Mar-26	26-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-440	Automatic air release valve	5	0.00	24-Mar-26	29-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-520	Roof vent caps	5	0.00	28-Mar-26	01-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-450	OS & Y gate valve	5	0.00	30-Mar-26	04-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-570	Toilet Fittings	5	0.00	30-Mar-26	05-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-530	Floor drain	5	0.00	02-Apr-26	07-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-460	Fire alarm check valve	5	0.00	05-Apr-26	09-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-540	Gully trap	5	0.00	08-Apr-26	13-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-550	Electric water heater	5	0.00	14-Apr-26	19-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-420	Water supply valves	5	0.00	18-Apr-26	23-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00

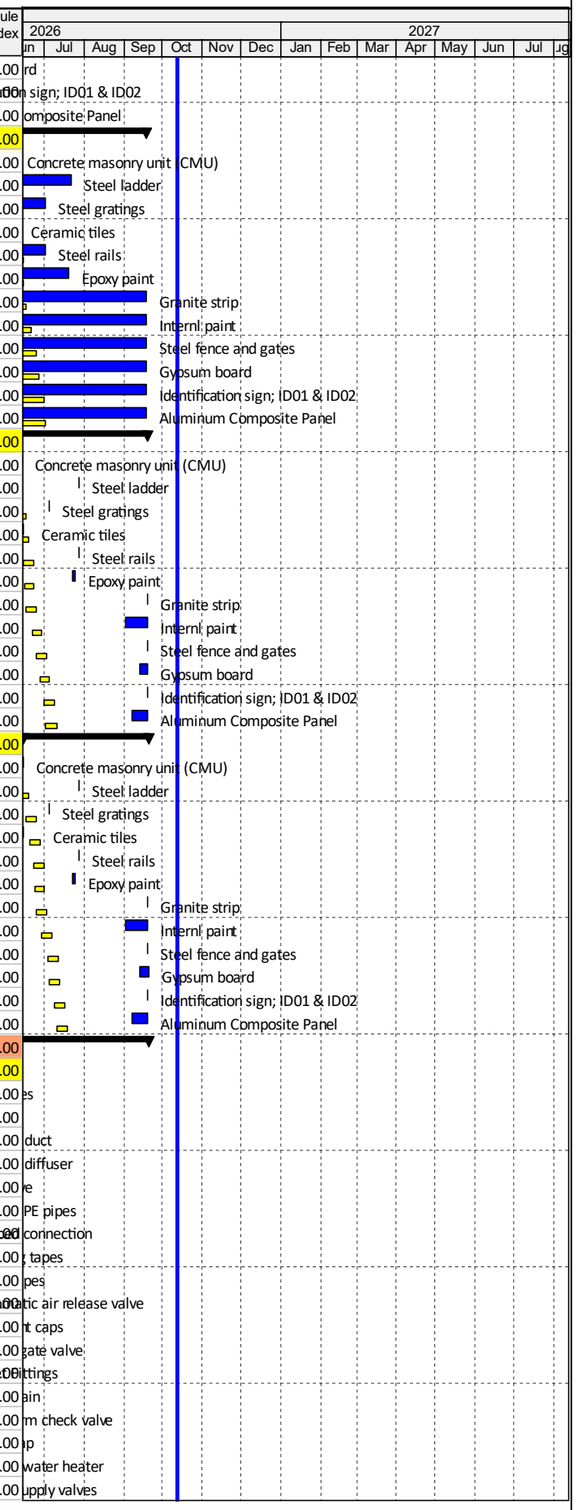

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-PO-M-560	Bib tap	5	0.00	20-Apr-26	25-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-E-PO-M-3410	Water tap	5	0.00	21-Apr-26	26-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-580	Lavatory / wash basin	5	0.00	26-Apr-26	30-Apr-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-590	Inline exhaust fans	5	0.00	02-May-26	06-May-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-M-390	Fire fighting valves	5	0.00	07-May-26	12-May-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
MANUFACTURING		169	0.00	17-Feb-26	28-Sep-26	06-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-480	PPR pipes	80	0.00	17-Feb-26	30-May-26	27-Apr-26	03-Aug-26	0.00	0.00	0.00
DAM3-P-MF-M-600	HVAC duct	80	0.00	24-Feb-26	04-Jun-26	06-Apr-26	01-Jun-26	0.00	0.00	0.00
DAM3-P-MF-M-610	Flexible duct	80	0.00	03-Mar-26	10-Jun-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-620	Exhaust diffuser	80	0.00	09-Mar-26	16-Jun-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-490	Ball valve	80	0.00	12-Mar-26	20-Jun-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-430	U/G HDPE pipes	80	0.00	15-Mar-26	22-Jun-26	27-Apr-26	02-Aug-26	0.00	0.00	0.00
DAM3-P-MF-M-500	Capped connection	80	0.00	22-Mar-26	25-Jun-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-660	Warning tapes	80	0.00	24-Mar-26	28-Jun-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-510	UPVC pipes	80	0.00	28-Mar-26	01-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-440	Automatic air release valve	80	0.00	30-Mar-26	04-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-520	Roof vent caps	80	0.00	02-Apr-26	07-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-450	OS & Y gate valve	80	0.00	05-Apr-26	09-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-570	Toilet Fittings	5	0.00	05-Apr-26	11-Apr-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-530	Floor drain	80	0.00	08-Apr-26	13-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-460	Fire alarm check valve	80	0.00	11-Apr-26	15-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-540	Gully trap	80	0.00	14-Apr-26	19-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-550	Electric water heater	120	0.00	20-Apr-26	09-Sep-26	27-Apr-26	13-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-420	Water supply valves	80	0.00	23-Apr-26	29-Jul-26	27-Apr-26	02-Aug-26	0.00	0.00	0.00
DAM3-P-MF-M-560	Bib tap	80	0.00	26-Apr-26	30-Jul-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-E-MF-M-3410	Water tap	80	0.00	27-Apr-26	01-Aug-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-580	Lavatory / wash basin	80	0.00	02-May-26	05-Aug-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-590	Inline exhaust fans	120	0.00	07-May-26	28-Sep-26	27-Apr-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-M-390	Fire fighting valves	80	0.00	13-May-26	17-Aug-26	27-Apr-26	09-Aug-26	0.00	0.00	0.00
DELIVERY		60	1,190,075.32	11-Apr-26	06-Oct-26	10-May-26	20-Sep-26	1,190,075.32	1,190,075.32	1.00
DAM3-P-DL-M-570	Toilet Fittings	5	75,460.88	11-Apr-26	16-Apr-26	15-Sep-26	20-Sep-26	75,460.88	75,460.88	1.00
DAM3-P-DL-M-480	PPR pipes	7	76,567.93	31-May-26	07-Jun-26	05-Jul-26	15-Sep-26	76,567.93	76,567.93	1.00
DAM3-P-DL-M-600	HVAC duct	7	490,860.48	06-Jun-26	13-Jun-26	04-Jun-26	14-Jun-26	490,860.48	490,860.48	1.00
DAM3-P-DL-M-610	Flexible duct	7	69,629.67	11-Jun-26	18-Jun-26	16-Sep-26	20-Sep-26	69,629.67	69,629.67	1.00
DAM3-P-DL-M-620	Exhaust diffuser	7	7,040.00	17-Jun-26	24-Jun-26	20-Sep-26	20-Sep-26	7,040.00	7,040.00	1.00
DAM3-P-DL-M-490	Ball valve	7	14,232.16	21-Jun-26	28-Jun-26	18-Jul-26	18-Jul-26	14,232.16	14,232.16	1.00
DAM3-P-DL-M-430	U/G HDPE pipes	7	49,971.54	23-Jun-26	30-Jun-26	01-Aug-26	20-Sep-26	49,971.54	49,971.54	1.00
DAM3-P-DL-M-500	Capped connection	7	913.27	27-Jun-26	04-Jul-26	05-Jul-26	14-Sep-26	913.27	913.27	1.00
DAM3-P-DL-M-660	Warning tapes	7	14,077.01	29-Jun-26	06-Jul-26	05-Jul-26	05-Jul-26	14,077.01	14,077.01	1.00
DAM3-P-DL-M-510	UPVC pipes	7	126,693.12	02-Jul-26	09-Jul-26	10-May-26	19-May-26	126,693.12	126,693.12	1.00
DAM3-P-DL-M-440	Automatic air release valve	7	1,769.50	05-Jul-26	12-Jul-26	20-Sep-26	20-Sep-26	1,769.50	1,769.50	1.00
DAM3-P-DL-M-520	Roof vent caps	7	3,044.27	08-Jul-26	15-Jul-26	20-Sep-26	20-Sep-26	3,044.27	3,044.27	1.00
DAM3-P-DL-M-450	OS & Y gate valve	7	11,631.51	11-Jul-26	18-Jul-26	15-Jul-26	20-Sep-26	11,631.51	11,631.51	1.00
DAM3-P-DL-M-530	Floor drain	7	74,093.27	14-Jul-26	21-Jul-26	16-Sep-26	20-Sep-26	74,093.27	74,093.27	1.00
DAM3-P-DL-M-460	Fire alarm check valve	7	26,656.72	16-Jul-26	23-Jul-26	20-Sep-26	20-Sep-26	26,656.72	26,656.72	1.00
DAM3-P-DL-M-540	Gully trap	7	15,982.56	20-Jul-26	27-Jul-26	06-Sep-26	20-Sep-26	15,982.56	15,982.56	1.00
DAM3-P-DL-M-420	Water supply valves	7	3,114.56	29-Jul-26	06-Aug-26	05-Jul-26	15-Sep-26	3,114.56	3,114.56	1.00
DAM3-P-DL-M-560	Bib tap	7	6,240.96	01-Aug-26	08-Aug-26	20-Sep-26	20-Sep-26	6,240.96	6,240.96	1.00
DAM3-P-DL-M-3410	Water tap	7	9,437.47	02-Aug-26	09-Aug-26	20-Sep-26	20-Sep-26	9,437.47	9,437.47	1.00
DAM3-P-DL-M-580	Lavatory / wash basin	7	70,323.44	06-Aug-26	13-Aug-26	16-Sep-26	20-Sep-26	70,323.44	70,323.44	1.00
DAM3-P-DL-M-390	Fire fighting valves	7	8,885.58	18-Aug-26	25-Aug-26	10-Aug-26	10-Aug-26	8,885.58	8,885.58	1.00
DAM3-P-DL-M-550	Electric water heater	7	5,974.50	10-Sep-26	17-Sep-26	16-Sep-26	16-Sep-26	5,974.50	5,974.50	1.00
DAM3-P-DL-M-590	Inline exhaust fans	7	27,474.92	29-Sep-26	06-Oct-26	05-Sep-26	20-Sep-26	27,474.92	27,474.92	1.00
STAGING TIME		67	0.00	16-Apr-26	14-Oct-26	10-May-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-570	Toilet Fittings	5	0.00	16-Apr-26	22-Apr-26	15-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-480	PPR pipes	7	0.00	08-Jun-26	15-Jun-26	05-Jul-26	15-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-600	HVAC duct	7	0.00	14-Jun-26	21-Jun-26	04-Jun-26	14-Jun-26	0.00	0.00	0.00
DAM3-P-ST-M-610	Flexible duct	7	0.00	20-Jun-26	27-Jun-26	16-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-620	Exhaust diffuser	7	0.00	25-Jun-26	02-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-490	Ball valve	7	0.00	29-Jun-26	06-Jul-26	18-Jul-26	18-Jul-26	0.00	0.00	0.00
DAM3-P-ST-M-430	U/G HDPE pipes	7	0.00	01-Jul-26	08-Jul-26	01-Aug-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-500	Capped connection	7	0.00	05-Jul-26	12-Jul-26	05-Jul-26	14-Sep-26	0.00	0.00	0.00

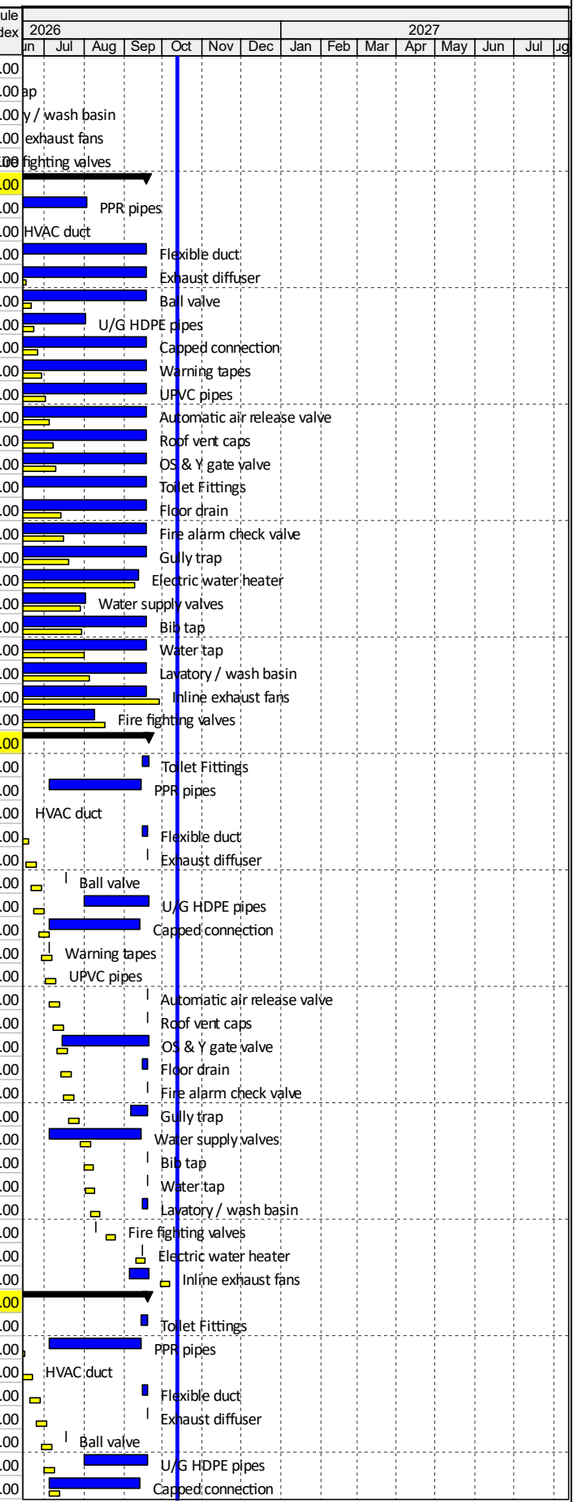


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-ST-M-660	Warning tapes	7	0.00	07-Jul-26	14-Jul-26	05-Jul-26	05-Jul-26	0.00	0.00	0.00
DAM3-P-ST-M-510	UPVC pipes	7	0.00	11-Jul-26	18-Jul-26	10-May-26	19-May-26	0.00	0.00	0.00
DAM3-P-ST-M-440	Automatic air release valve	7	0.00	13-Jul-26	20-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-520	Roof vent caps	7	0.00	16-Jul-26	23-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-450	OS & Y gate valve	7	0.00	19-Jul-26	26-Jul-26	15-Jul-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-530	Floor drain	7	0.00	22-Jul-26	29-Jul-26	16-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-460	Fire alarm check valve	7	0.00	25-Jul-26	01-Aug-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-540	Gully trap	7	0.00	28-Jul-26	04-Aug-26	06-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-420	Water supply valves	7	0.00	06-Aug-26	15-Aug-26	05-Jul-26	15-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-560	Bib tap	7	0.00	09-Aug-26	16-Aug-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-ST-M-3410	Water tap	7	0.00	10-Aug-26	17-Aug-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-580	Lavatory / wash basin	7	0.00	15-Aug-26	22-Aug-26	16-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-390	Fire fighting valves	7	0.00	26-Aug-26	02-Sep-26	10-Aug-26	10-Aug-26	0.00	0.00	0.00
DAM3-P-ST-M-550	Electric water heater	7	0.00	19-Sep-26	27-Sep-26	16-Sep-26	16-Sep-26	0.00	0.00	0.00
DAM3-P-ST-M-590	Inline exhaust fans	7	0.00	07-Oct-26	14-Oct-26	05-Sep-26	20-Sep-26	0.00	0.00	0.00
ELECTRICAL		147	819,995.13	11-Feb-26	01-Aug-26	10-Mar-26	20-Sep-26	819,995.13	819,995.13	1.00
PO ISSUE		68	0.00	11-Feb-26	09-Apr-26	10-Mar-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-E-310	PVC conduits	5	0.00	11-Feb-26	16-Feb-26	10-Mar-26	10-Mar-26	0.00	0.00	0.00
DAM3-P-PO-E-320	Wires	5	0.00	17-Feb-26	24-Feb-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-E-PO-E-210	Cable Tray	5	0.00	24-Feb-26	02-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-E-340	Grounding system	5	0.00	03-Mar-26	08-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-E-350	Wiring devices	5	0.00	09-Mar-26	14-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-E-370	HDPE ducts	5	0.00	15-Mar-26	23-Mar-26	26-Apr-26	26-Apr-26	0.00	0.00	0.00
DAM3-P-PO-E-290	Low Voltage cables	5	0.00	24-Mar-26	29-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-E-300	Disconnect switches	5	0.00	30-Mar-26	04-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-E-330	Wall mounted, duplex, telephone and data outlet	5	0.00	05-Apr-26	09-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
MANUFACTURING		142	0.00	17-Feb-26	15-Jul-26	11-Mar-26	16-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-310	PVC conduits	60	0.00	17-Feb-26	03-May-26	11-Mar-26	02-May-26	0.00	0.00	0.00
DAM3-P-MF-E-320	Wires	80	0.00	24-Feb-26	04-Jun-26	28-Jun-26	16-Sep-26	0.00	0.00	0.00
DAM3-E-MF-E-210	Cable Tray	80	0.00	03-Mar-26	10-Jun-26	04-Jul-26	16-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-340	Grounding system	80	0.00	09-Mar-26	16-Jun-26	27-Apr-26	03-May-26	0.00	0.00	0.00
DAM3-P-MF-E-350	Wiring devices	80	0.00	15-Mar-26	22-Jun-26	09-Jul-26	16-Sep-26	0.00	0.00	0.00
DAM3-P-MF-E-370	HDPE ducts	80	0.00	24-Mar-26	28-Jun-26	27-Apr-26	03-May-26	0.00	0.00	0.00
DAM3-P-MF-E-290	Low Voltage cables	80	0.00	30-Mar-26	04-Jul-26	15-Jul-26	22-Jul-26	0.00	0.00	0.00
DAM3-P-MF-E-300	Disconnect switches	80	0.00	05-Apr-26	09-Jul-26	21-Jul-26	22-Jul-26	0.00	0.00	0.00
DAM3-P-MF-E-330	Wall mounted, duplex, telephone and data outlet	80	0.00	11-Apr-26	15-Jul-26	27-Jul-26	16-Sep-26	0.00	0.00	0.00
DELIVERY		65	819,995.13	04-May-26	23-Jul-26	03-May-26	20-Sep-26	819,995.13	819,995.13	1.00
DAM3-P-DL-E-310	PVC conduits	7	15,738.66	04-May-26	11-May-26	03-May-26	20-May-26	15,738.66	15,738.66	1.00
DAM3-P-DL-E-320	Wires	7	7,379.37	06-Jun-26	13-Jun-26	20-Sep-26	20-Sep-26	7,379.37	7,379.37	1.00
DAM3-P-DL-E-2100	Cable Tray	7	1,063.80	11-Jun-26	18-Jun-26	20-Sep-26	20-Sep-26	1,063.80	1,063.80	1.00
DAM3-P-DL-E-340	Grounding system	7	65,141.26	17-Jun-26	24-Jun-26	10-May-26	19-May-26	65,141.26	65,141.26	1.00
DAM3-P-DL-E-350	Wiring devices	7	66,414.34	23-Jun-26	30-Jun-26	17-Sep-26	20-Sep-26	66,414.34	66,414.34	1.00
DAM3-P-DL-E-370	HDPE ducts	7	176,019.75	29-Jun-26	06-Jul-26	10-May-26	19-May-26	176,019.75	176,019.75	1.00
DAM3-P-DL-E-290	Low Voltage cables	7	299,034.47	05-Jul-26	12-Jul-26	23-Jul-26	25-Jul-26	299,034.47	299,034.47	1.00
DAM3-P-DL-E-300	Disconnect switches	7	100,576.04	11-Jul-26	18-Jul-26	23-Jul-26	25-Jul-26	100,576.04	100,576.04	1.00
DAM3-P-DL-E-330	Wall mounted, duplex, telephone and data outlet	7	88,627.44	16-Jul-26	23-Jul-26	17-Sep-26	20-Sep-26	88,627.44	88,627.44	1.00
STAGING TIME		75	0.00	12-May-26	01-Aug-26	03-May-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-310	PVC conduits	7	0.00	12-May-26	19-May-26	03-May-26	20-May-26	0.00	0.00	0.00
DAM3-P-ST-E-320	Wires	7	0.00	14-Jun-26	21-Jun-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-E-ST-E-210	Cable Tray	7	0.00	20-Jun-26	27-Jun-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-340	Grounding system	7	0.00	25-Jun-26	02-Jul-26	10-May-26	19-May-26	0.00	0.00	0.00
DAM3-P-ST-E-350	Wiring devices	7	0.00	01-Jul-26	08-Jul-26	17-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-E-370	HDPE ducts	7	0.00	07-Jul-26	14-Jul-26	10-May-26	19-May-26	0.00	0.00	0.00
DAM3-P-ST-E-290	Low Voltage cables	7	0.00	13-Jul-26	20-Jul-26	25-Jul-26	25-Jul-26	0.00	0.00	0.00
DAM3-P-ST-E-300	Disconnect switches	7	0.00	19-Jul-26	26-Jul-26	25-Jul-26	25-Jul-26	0.00	0.00	0.00
DAM3-P-ST-E-330	Wall mounted, duplex, telephone and data outlet	7	0.00	25-Jul-26	01-Aug-26	17-Sep-26	20-Sep-26	0.00	0.00	0.00
EXTERNAL		119	2,215,885.18	07-Apr-26	03-Sep-26	02-Mar-26	21-Sep-26	2,215,885.18	2,215,885.18	1.00
PO ISSUE		23	0.00	07-Apr-26	28-Apr-26	02-Mar-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EX-80	Asphalt works	5	0.00	07-Apr-26	12-Apr-26	02-Mar-26	02-Mar-26	0.00	0.00	0.00
DAM3-P-PO-EX-90	Concrete parking bumper	5	0.00	08-Apr-26	14-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EX-100	Road markings	5	0.00	11-Apr-26	16-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EX-110	Road signs	5	0.00	13-Apr-26	19-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00

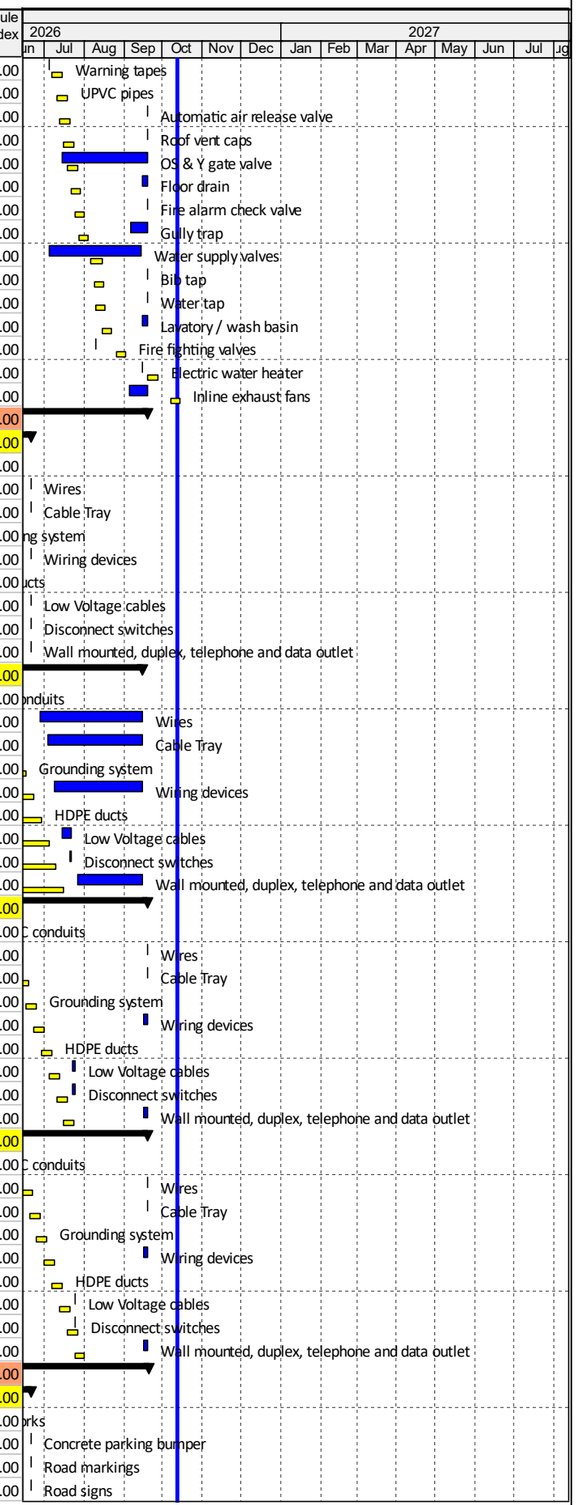

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-PO-EX-140	Curbstones	5	0.00	18-Apr-26	23-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EX-150	Gravel bedding	5	0.00	21-Apr-26	26-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EX-130	Interlock tiles	5	0.00	22-Apr-26	28-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
MANUFACTURING		111	0.00	13-Apr-26	15-Aug-26	03-Mar-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-80	Asphalt works	100	0.00	13-Apr-26	10-Aug-26	03-Mar-26	07-Jun-26	0.00	0.00	0.00
DAM3-P-MF-EX-90	Concrete parking bumper	90	0.00	14-Apr-26	01-Aug-26	28-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-100	Road markings	90	0.00	16-Apr-26	03-Aug-26	28-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-110	Road signs	90	0.00	19-Apr-26	05-Aug-26	28-Jun-26	17-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-140	Curbstones	90	0.00	23-Apr-26	10-Aug-26	28-Jun-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-150	Gravel bedding	90	0.00	27-Apr-26	12-Aug-26	28-Jun-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EX-130	Interlock tiles	90	0.00	28-Apr-26	15-Aug-26	21-Jul-26	20-Sep-26	0.00	0.00	0.00
DELIVERY		27	2,215,885.18	01-Aug-26	23-Aug-26	08-Jun-26	21-Sep-26	2,215,885.18	2,215,885.18	1.00
DAM3-P-DL-EX-90	Concrete parking bumper	7	9,558.14	01-Aug-26	09-Aug-26	21-Sep-26	21-Sep-26	9,558.14	9,558.14	1.00
DAM3-P-DL-EX-100	Road markings	7	11,308.91	03-Aug-26	11-Aug-26	21-Sep-26	21-Sep-26	11,308.91	11,308.91	1.00
DAM3-P-DL-EX-110	Road signs	7	31,028.59	05-Aug-26	13-Aug-26	20-Sep-26	20-Sep-26	31,028.59	31,028.59	1.00
DAM3-P-DL-EX-140	Curbstones	7	86,912.40	10-Aug-26	18-Aug-26	17-Sep-26	20-Sep-26	86,912.40	86,912.40	1.00
DAM3-P-DL-EX-80	Asphalt works	7	1,868,985.04	11-Aug-26	18-Aug-26	08-Jun-26	17-Jun-26	1,868,985.04	1,868,985.04	1.00
DAM3-P-DL-EX-150	Gravel bedding	7	66,111.93	13-Aug-26	20-Aug-26	17-Sep-26	21-Sep-26	66,111.93	66,111.93	1.00
DAM3-P-DL-EX-130	Interlock tiles	7	141,980.16	15-Aug-26	23-Aug-26	17-Sep-26	20-Sep-26	141,980.16	141,980.16	1.00
STAGING TIME		41	0.00	09-Aug-26	03-Sep-26	08-Jun-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-90	Concrete parking bumper	7	0.00	09-Aug-26	17-Aug-26	21-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-100	Road markings	7	0.00	11-Aug-26	19-Aug-26	21-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-110	Road signs	7	0.00	13-Aug-26	22-Aug-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-80	Asphalt works	7	0.00	19-Aug-26	26-Aug-26	08-Jun-26	08-Jun-26	0.00	0.00	0.00
DAM3-P-ST-EX-150	Gravel bedding	7	0.00	22-Aug-26	29-Aug-26	17-Sep-26	21-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-130	Interlock tiles	7	0.00	23-Aug-26	31-Aug-26	17-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EX-140	Curbstones	7	0.00	27-Aug-26	03-Sep-26	17-Sep-26	20-Sep-26	0.00	0.00	0.00
ENVIRONMENTAL		151	384,877.22	11-Feb-26	06-Aug-26	21-Jun-26	20-Sep-26	384,877.22	384,877.22	1.00
PO ISSUE		40	0.00	11-Feb-26	04-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-100	HDPE pipes for fire system	5	0.00	11-Feb-26	16-Feb-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-110	Directly buried gate valve for fire system	5	0.00	17-Feb-26	24-Feb-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-120	HDPE pipes for water supply system	5	0.00	24-Feb-26	02-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-130	Directly buried gate valve for water system	5	0.00	03-Mar-26	08-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-140	Air valve	5	0.00	09-Mar-26	14-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-150	Washout valve	5	0.00	15-Mar-26	23-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-160	Gate valve	5	0.00	24-Mar-26	29-Mar-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
DAM3-P-PO-EN-170	UPVC pipes	5	0.00	30-Mar-26	04-Apr-26	21-Jun-26	21-Jun-26	0.00	0.00	0.00
MANUFACTURING		133	0.00	17-Feb-26	21-Jul-26	22-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-100	HDPE pipes for fire system	90	0.00	17-Feb-26	10-Jun-26	28-Jun-26	23-Jul-26	0.00	0.00	0.00
DAM3-P-MF-EN-110	Directly buried gate valve for fire system	90	0.00	24-Feb-26	16-Jun-26	04-Jul-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-120	HDPE pipes for water supply system	90	0.00	03-Mar-26	22-Jun-26	22-Jun-26	15-Aug-26	0.00	0.00	0.00
DAM3-P-MF-EN-130	Directly buried gate valve for water system	90	0.00	09-Mar-26	28-Jun-26	22-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-140	Air valve	90	0.00	15-Mar-26	04-Jul-26	22-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-150	Washout valve	90	0.00	24-Mar-26	09-Jul-26	22-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-160	Gate valve	90	0.00	30-Mar-26	15-Jul-26	22-Jun-26	19-Sep-26	0.00	0.00	0.00
DAM3-P-MF-EN-170	UPVC pipes	90	0.00	05-Apr-26	21-Jul-26	22-Jun-26	25-Jul-26	0.00	0.00	0.00
DELIVERY		107	384,877.22	11-Jun-26	29-Jul-26	25-Jul-26	20-Sep-26	384,877.22	384,877.22	1.00
DAM3-P-DL-EN-100	HDPE pipes for fire system	7	144,972.85	11-Jun-26	18-Jun-26	25-Jul-26	26-Jul-26	144,972.85	144,972.85	1.00
DAM3-P-DL-EN-110	Directly buried gate valve for fire system	7	7,270.01	17-Jun-26	24-Jun-26	20-Sep-26	20-Sep-26	7,270.01	7,270.01	1.00
DAM3-P-DL-EN-120	HDPE pipes for water supply system	7	10,655.04	23-Jun-26	30-Jun-26	17-Aug-26	17-Aug-26	10,655.04	10,655.04	1.00
DAM3-P-DL-EN-130	Directly buried gate valve for water system	7	16,098.52	29-Jun-26	06-Jul-26	20-Sep-26	20-Sep-26	16,098.52	16,098.52	1.00
DAM3-P-DL-EN-140	Air valve	7	13,087.07	05-Jul-26	12-Jul-26	20-Sep-26	20-Sep-26	13,087.07	13,087.07	1.00
DAM3-P-DL-EN-150	Washout valve	7	15,346.94	11-Jul-26	18-Jul-26	20-Sep-26	20-Sep-26	15,346.94	15,346.94	1.00
DAM3-P-DL-EN-160	Gate valve	7	42,658.36	16-Jul-26	23-Jul-26	05-Sep-26	20-Sep-26	42,658.36	42,658.36	1.00
DAM3-P-DL-EN-170	UPVC pipes	7	134,788.44	22-Jul-26	29-Jul-26	26-Jul-26	26-Jul-26	134,788.44	134,788.44	1.00
STAGING TIME		107	0.00	20-Jun-26	06-Aug-26	25-Jul-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EN-100	HDPE pipes for fire system	7	0.00	20-Jun-26	27-Jun-26	25-Jul-26	26-Jul-26	0.00	0.00	0.00
DAM3-P-ST-EN-110	Directly buried gate valve for fire system	7	0.00	25-Jun-26	02-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EN-120	HDPE pipes for water supply system	7	0.00	01-Jul-26	08-Jul-26	17-Aug-26	17-Aug-26	0.00	0.00	0.00
DAM3-P-ST-EN-130	Directly buried gate valve for water system	7	0.00	07-Jul-26	14-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EN-140	Air valve	7	0.00	13-Jul-26	20-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EN-150	Washout valve	7	0.00	19-Jul-26	26-Jul-26	20-Sep-26	20-Sep-26	0.00	0.00	0.00

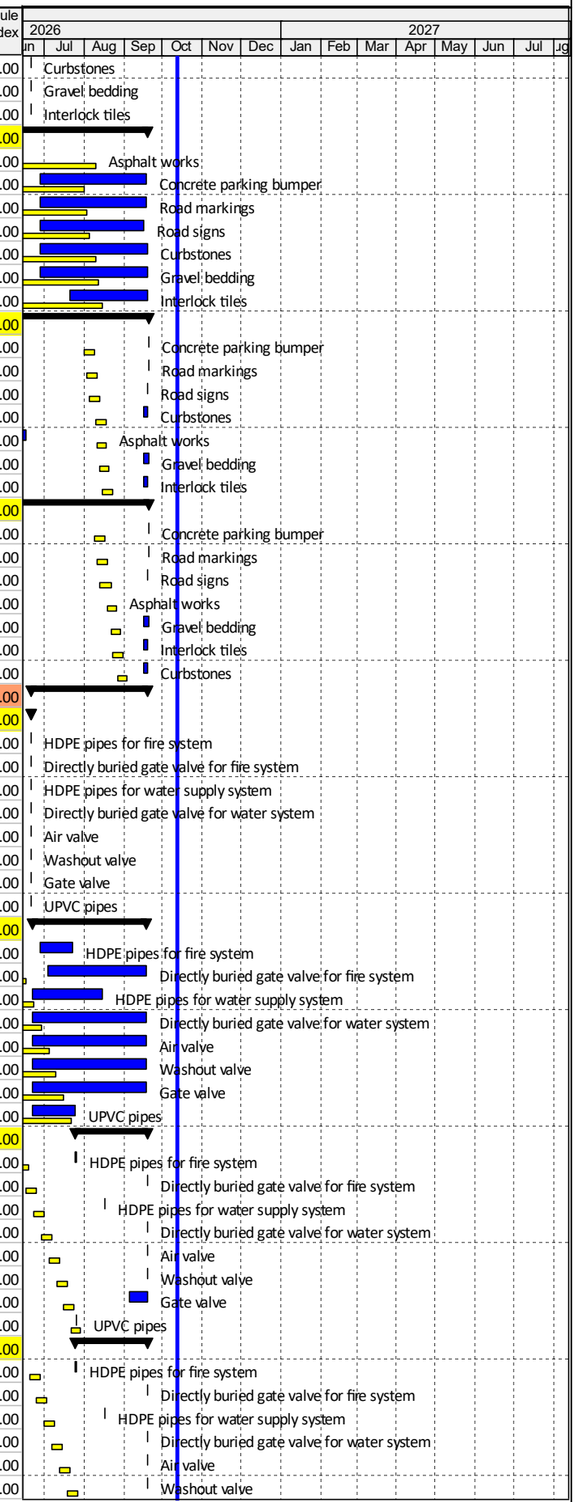


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-P-ST-EN-160	Gate valve	7	0.00	25-Jul-26	01-Aug-26	05-Sep-26	20-Sep-26	0.00	0.00	0.00
DAM3-P-ST-EN-170	UPVC pipes	7	0.00	30-Jul-26	06-Aug-26	26-Jul-26	26-Jul-26	0.00	0.00	0.00
CONSTRUCTION (67%)		321	64,317,671.75	27-Jan-26	21-Feb-27	14-Jan-26		39,294,851.69	38,293,779.50	0.97
RBF 900 SQM FACTORIES		321	55,841,646.40	27-Jan-26	16-Feb-27	14-Jan-26		37,550,480.14	35,662,672.84	0.95
SITE WORKS		16	10,892.39	27-Jan-26	25-Feb-26	14-Jan-26	31-Jan-26	10,892.39	10,892.39	1.00
DAM3-C-GEN-10	Initial Site Survey and Setting out	12	0.00	27-Jan-26	09-Feb-26	19-Jan-26	24-Jan-26	0.00	0.00	1.00
DAM3-C-GEN-88	Demolition of the existing pavement	12	10,892.39	10-Feb-26	25-Feb-26	14-Jan-26	31-Jan-26	10,892.39	10,892.39	1.00
BLOCK B6		266	5,075,523.09	10-Feb-26	23-Nov-26	15-Feb-26		3,874,467.80	3,112,647.57	0.80
STRUCTURAL		195	1,389,042.53	10-Feb-26	07-Jul-26	15-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		74	597,655.16	10-Feb-26	25-Mar-26	15-Feb-26	10-May-26	597,655.16	597,655.16	1.00
DAM3-C-B6-S-160	Excavation for footings	8	89,859.61	10-Feb-26	19-Feb-26	15-Feb-26	24-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B6-S-6143	Soil replacement - rock fill	6	179,061.91	19-Feb-26	28-Feb-26	02-Apr-26	04-Apr-26	179,061.91	179,061.91	1.00
DAM3-C-B6-S-6153	Engineering fill	6	46,046.19	01-Mar-26	07-Mar-26	12-Apr-26	13-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B6-S-777	Anti Termite Below Footings	1	11,905.55	08-Mar-26	08-Mar-26	22-Apr-26	22-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B6-S-687	Vapour Barrier for Footings	1	7,940.10	09-Mar-26	09-Mar-26	22-Apr-26	22-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B6-S-537	Lean Concrete Below Footings	2	8,229.34	10-Mar-26	11-Mar-26	22-Apr-26	22-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B6-S-587	Rebar for Footings	4	101,844.98	12-Mar-26	16-Mar-26	02-May-26	05-May-26	101,844.98	101,844.98	1.00
DAM3-C-B6-S-597	Formwork for Footings	4	25,461.25	21-Mar-26	24-Mar-26	04-May-26	09-May-26	25,461.25	25,461.25	1.00
DAM3-C-B6-S-547	Pouring Concrete for Footings	1	127,306.23	25-Mar-26	25-Mar-26	10-May-26	10-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		12	120,554.54	26-Mar-26	11-Apr-26	05-May-26	01-Jun-26	120,554.54	120,554.54	1.00
DAM3-C-B6-S-637	Rebar for column neck	2	14,919.19	26-Mar-26	28-Mar-26	05-May-26	09-May-26	14,919.19	14,919.19	1.00
DAM3-C-B6-S-647	Formwork for column neck	2	9,946.13	29-Mar-26	30-Mar-26	12-May-26	16-May-26	9,946.13	9,946.13	1.00
DAM3-C-B6-S-627	Pouring Concrete for column neck	1	24,865.31	31-Mar-26	31-Mar-26	17-May-26	17-May-26	24,865.31	24,865.31	1.00
DAM3-C-B6-S-677	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	01-Apr-26	02-Apr-26	18-May-26	19-May-26	24,777.73	24,777.73	1.00
DAM3-C-B6-S-737	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	04-Apr-26	11-Apr-26	24-May-26	01-Jun-26	46,046.19	46,046.19	1.00
GRADE BEAM		17	171,632.86	12-Apr-26	28-Apr-26	04-Jun-26	22-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B6-S-787	Anti Termite Below Grade Beams	1	11,905.55	12-Apr-26	12-Apr-26	04-Jun-26	04-Jun-26	11,905.55	11,905.55	1.00
DAM3-C-B6-S-707	Vapour barrier for Grade Beams	2	5,293.40	13-Apr-26	14-Apr-26	04-Jun-26	04-Jun-26	5,293.40	5,293.40	1.00
DAM3-C-B6-S-557	Lean Concrete Below Grade Beams	2	4,431.19	15-Apr-26	16-Apr-26	04-Jun-26	04-Jun-26	4,431.19	4,431.19	1.00
DAM3-C-B6-S-607	Rebar for Grade Beams	5	27,194.46	18-Apr-26	22-Apr-26	08-Jun-26	09-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B6-S-617	Formwork for Grade Beams	2	6,798.61	23-Apr-26	25-Apr-26	10-Jun-26	14-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B6-S-767	Anchor bolts installation	2	57,238.83	23-Apr-26	25-Apr-26	11-Jun-26	13-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B6-S-567	Pouring Concrete for Grade Beams	1	33,993.09	26-Apr-26	26-Apr-26	15-Jun-26	15-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B6-S-717	Damp proof /Bitumin paint on Grade Beams	2	24,777.73	27-Apr-26	28-Apr-26	20-Jun-26	22-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		94	397,232.98	29-Apr-26	07-Jul-26	28-Jun-26		397,232.98	396,325.87	1.00
DAM3-C-B6-S-747	Backfilling / Compaction for Slab on Grade	7	23,023.09	29-Apr-26	06-May-26	28-Jun-26	06-Jul-26	23,023.09	23,023.09	1.00
DAM3-C-B6-S-697	Anti Termite Treatment below Ground Slab	1	15,874.08	07-May-26	07-May-26	18-Aug-26	23-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B6-S-727	Vapour barrier for below Ground Slab	2	13,233.49	09-May-26	10-May-26	18-Aug-26	23-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B6-S-577	Pouring Concrete for Ground Slab	4	344,195.21	11-May-26	14-May-26	18-Aug-26	23-Aug-26	344,195.21	344,195.21	1.00
DAM3-C-B6-S-757	Concrete pad	7	907.11	30-Jun-26	07-Jul-26			907.11	0.00	0.00
COLUMNS & BEAMS		65	101,966.98	07-May-26	07-Jun-26	08-Jun-26	06-Oct-26	101,966.98	101,966.98	1.00
DAM3-C-B6-S-5101	Rebar for column	5	20,144.05	07-May-26	12-May-26	18-Jul-26	20-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B6-S-5102	Formwork for column	4	5,036.01	13-May-26	17-May-26	23-Jul-26	11-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B6-S-5103	Pouring Concrete for column	1	25,180.06	18-May-26	18-May-26	26-Jul-26	13-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B6-S-6101	Rebar for Tie Beams	4	7,263.64	19-May-26	23-May-26	08-Jun-26	13-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B6-S-6102	Formwork for Tie Beams	2	1,815.91	24-May-26	25-May-26	11-Jun-26	14-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B6-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	30-May-26	30-May-26	15-Jun-26	15-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B6-S-6113	Rebar for Beams	4	13,379.11	31-May-26	03-Jun-26	21-Sep-26	22-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B6-S-6123	Formwork for Beams	2	3,344.77	04-Jun-26	06-Jun-26	28-Sep-26	04-Oct-26	3,344.77	3,344.77	1.00
DAM3-C-B6-S-6133	Pouring Concrete for Beams	1	16,723.88	07-Jun-26	07-Jun-26	01-Oct-26	06-Oct-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		81	1,566,668.48	16-May-26	12-Jul-26	06-Jul-26		1,566,668.48	1,539,773.29	0.98
DAM3-C-B6-SS-150	Installation of columns	3	217,507.55	16-May-26	18-May-26	06-Jul-26	06-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B6-SS-160	Installation of raft and purlins	5	326,261.32	19-May-26	24-May-26	06-Jul-26	07-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B6-SS-1020	Intumescent paint to steel works	7	317,759.56	25-May-26	04-Jun-26	25-Jul-26	17-Aug-26	317,759.56	317,759.56	1.00
DAM3-C-B6-SS-1030	Steel members for office area	7	115,805.20	25-May-26	04-Jun-26	11-Oct-26	12-Oct-26	115,805.20	115,805.20	1.00
DAM3-C-B6-SS-1040	Epoxy paint to steel members at office area	7	23,161.04	06-Jun-26	13-Jun-26			23,161.04	0.00	0.00
DAM3-C-B6-SS-1050	Steel members for external platform	7	18,670.78	08-Jun-26	15-Jun-26	30-Aug-26	31-Aug-26	18,670.78	18,670.78	1.00
DAM3-C-B6-SS-1060	Epoxy paint for external platform	5	3,734.16	16-Jun-26	21-Jun-26			3,734.16	0.00	0.00
DAM3-C-B6-SS-180	Installation of wall sandwich panel	5	326,261.32	30-Jun-26	05-Jul-26	11-Oct-26	13-Oct-26	326,261.32	326,261.32	1.00
DAM3-C-B6-SS-190	Installation of roof sheet	5	217,507.55	07-Jul-26	12-Jul-26	24-Aug-26	30-Aug-26	217,507.55	217,507.55	1.00
ARCHITECTURAL		101	900,244.66	25-May-26	03-Nov-26	15-Aug-26		698,111.33	85,409.37	0.12
MASONARY WORKS		35	78,954.21	25-May-26	07-Jul-26	29-Aug-26	15-Sep-26	78,954.21	78,954.21	1.00

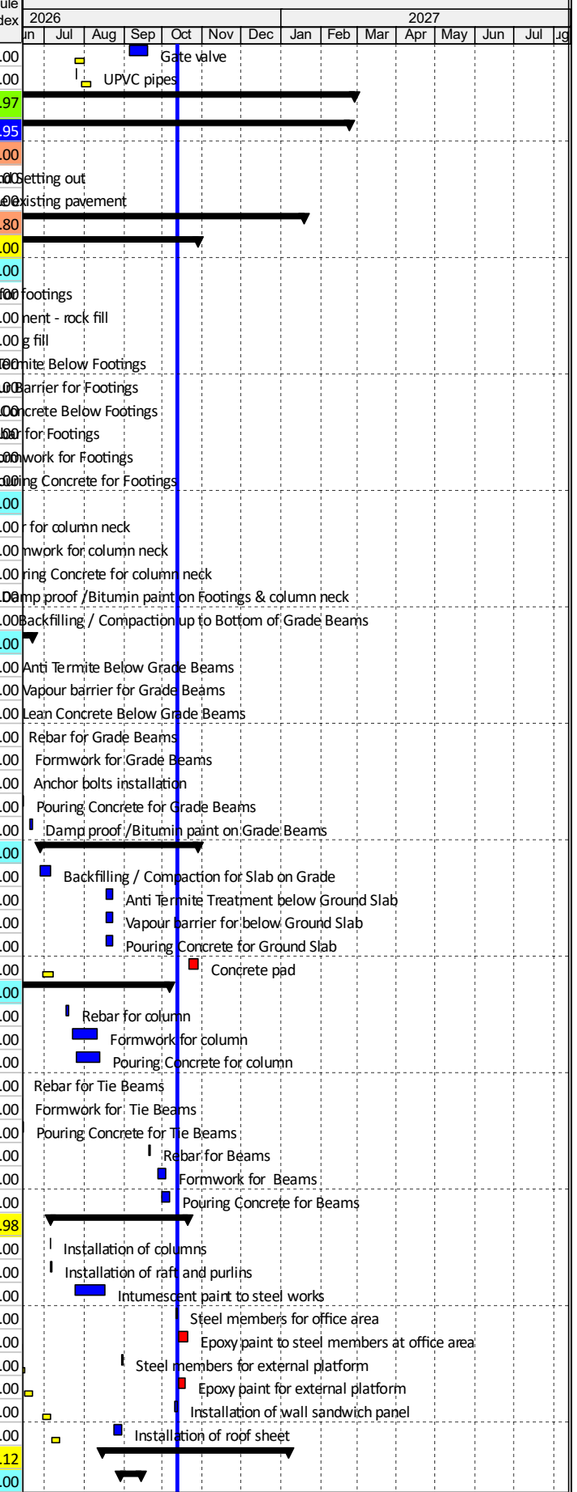

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B6-A-170	Block work at factory area	10	58,338.72	25-May-26	08-Jun-26	29-Aug-26	07-Sep-26	58,338.72	58,338.72	1.00
DAM3-C-B6-A-200	Block work at office area	7	6,179.18	22-Jun-26	29-Jun-26	30-Aug-26	09-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B6-A-620	Block work at toilet area	7	14,436.31	30-Jun-26	07-Jul-26	31-Aug-26	15-Sep-26	14,436.31	14,436.31	1.00
WALL FINISHES		40	92,757.47	08-Jul-26	06-Oct-26			92,757.47	0.00	0.00
DAM3-C-B6-A-630	Internal Wall Plaster	15	48,590.16	08-Jul-26	25-Jul-26			48,590.16	0.00	0.00
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	44,167.30	29-Sep-26	06-Oct-26			44,167.30	0.00	0.00
CIELING FINISHES		5	46,792.30	20-Sep-26	26-Sep-26			46,792.30	0.00	0.00
DAM3-C-B6-A-690	Installation of Ceiling Gypsum Board	5	46,792.30	20-Sep-26	26-Sep-26			46,792.30	0.00	0.00
FLOOR FINISHES		41	189,488.90	13-Aug-26	03-Nov-26			74,069.14	0.00	0.00
DAM3-C-B6-A-670	Tiles for Toilet	7	46,530.71	13-Aug-26	20-Aug-26			46,530.71	0.00	0.00
DAM3-C-B6-A-700	Tiles for Office Area	2	26,867.31	27-Sep-26	28-Sep-26			26,867.31	0.00	0.00
DAM3-C-B6-A-830	Granite strip	2	671.12	29-Sep-26	30-Sep-26			671.12	0.00	0.00
DAM3-C-B6-A-850	Epoxy paint	5	115,419.76	27-Oct-26	03-Nov-26			0.00	0.00	0.00
DOORS & WINDOWS		16	248,575.06	07-Jul-26	08-Aug-26			248,575.06	0.00	0.00
DAM3-C-B6-A-1010	Window (CW1)	7	94,173.21	07-Jul-26	14-Jul-26			94,173.21	0.00	0.00
DAM3-C-B6-A-640	Roll up Shutter Door	1	68,619.20	15-Jul-26	15-Jul-26			68,619.20	0.00	0.00
DAM3-C-B6-A-650	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	16-Jul-26	16-Jul-26			16,016.16	0.00	0.00
DAM3-C-B6-A-710	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	18-Jul-26	18-Jul-26			22,737.85	0.00	0.00
DAM3-C-B6-A-720	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	19-Jul-26	19-Jul-26			7,811.07	0.00	0.00
DAM3-C-B6-A-940	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	20-Jul-26	20-Jul-26			16,016.16	0.00	0.00
DAM3-C-B6-A-950	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	30-Jul-26	30-Jul-26			16,711.52	0.00	0.00
DAM3-C-B6-A-960	Skylight fixtures installation	3	6,489.89	01-Aug-26	08-Aug-26			6,489.89	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	09-Aug-26	12-Aug-26			4,879.02	0.00	0.00
DAM3-C-B6-A-810	Waterproofing membrane for toilets	4	4,879.02	09-Aug-26	12-Aug-26			4,879.02	0.00	0.00
METAL WORKS		21	193,717.06	01-Oct-26	15-Oct-26	15-Aug-26		152,084.14	6,455.16	0.04
DAM3-C-B6-A-740	Steel Ladder	2	9,839.16	01-Oct-26	03-Oct-26			9,839.16	0.00	0.00
DAM3-C-B6-A-840	Steel railing works	4	1,533.98	04-Oct-26	07-Oct-26			1,533.98	0.00	0.00
DAM3-C-B6-A-760	Aluminium composite panel	5	175,888.76	08-Oct-26	13-Oct-26			140,711.01	0.00	0.00
DAM3-C-B6-A-750	Galvanised Steel Gratings	2	6,455.16	14-Oct-26	15-Oct-26	15-Aug-26	15-Aug-26	0.00	6,455.16	0.00
SPECIALTIES		9	45,080.66	17-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B6-A-770	Installation of fittings	5	22,981.27	17-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B6-A-1000	Identification sign; ID01 & ID02	3	9,630.56	22-Oct-26	25-Oct-26			0.00	0.00	0.00
DAM3-C-B6-A-790	Furniture Installation	1	12,468.83	26-Oct-26	26-Oct-26			0.00	0.00	0.00
MECHANICAL		138	467,522.66	29-Apr-26	03-Nov-26	14-Jul-26		127,135.50	71,686.63	0.56
HVAC		17	233,183.33	15-Oct-26	31-Oct-26			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	22-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-450	Installation of HVAC Ducts	2	149,489.33	22-Oct-26	24-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-480	Installation of Duct insulation	2	21,205.40	25-Oct-26	26-Oct-26			0.00	0.00	0.00
SECOND STAGE		17	62,488.60	15-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-440	Installation of Exhaust Fans	2	7,938.56	15-Oct-26	17-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-470	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	18-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-460	Installation of Diffuser	2	2,144.00	27-Oct-26	28-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-650	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	29-Oct-26	31-Oct-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		20	102,458.78	07-Oct-26	03-Nov-26			51,710.54	0.00	0.00
FIRST STAGE		12	84,594.16	07-Oct-26	20-Oct-26			51,710.54	0.00	0.00
DAM3-C-B6-M-610	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	07-Oct-26	14-Oct-26			51,710.54	0.00	0.00
DAM3-C-B6-M-620	Installation of Fire Fighting Valve	5	12,199.40	15-Oct-26	20-Oct-26			0.00	0.00	0.00
SECOND STAGE		8	17,864.62	21-Oct-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B6-M-630	Installation of Fire Hose Cabinet	3	15,158.56	21-Oct-26	24-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-680	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	01-Nov-26	03-Nov-26			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		120	90,009.74	29-Apr-26	27-Oct-26	14-Jul-26		42,969.41	30,093.94	0.70
FIRST STAGE		106	41,149.90	29-Apr-26	29-Aug-26	14-Jul-26		41,149.90	30,093.94	0.73
DAM3-C-B6-M-510	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	29-Apr-26	03-May-26	14-Jul-26	18-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B6-M-530	Installation of Floor Drain	2	11,055.96	22-Aug-26	23-Aug-26			11,055.96	0.00	0.00
DAM3-C-B6-M-690	Installation of Trench drain	5	11,508.80	24-Aug-26	29-Aug-26	15-Jul-26	18-Jul-26	11,508.80	11,508.80	1.00
SECOND STAGE		14	48,859.84	28-Sep-26	27-Oct-26			1,819.51	0.00	0.00
DAM3-C-B6-M-490	Installation of Electric Water Heater	2	1,819.51	28-Sep-26	29-Sep-26			1,819.51	0.00	0.00
DAM3-C-B6-M-500	Installation of Sanitary Fixture and Accessories	4	19,921.72	13-Oct-26	18-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-520	Installation of Lavotary /Wash Basin	2	21,416.68	18-Oct-26	20-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-580	Installation of Bib Tap	2	1,900.66	20-Oct-26	22-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-540	Installation of Water Tap	2	2,874.14	22-Oct-26	25-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-550	Installation of Roof Vent Cap	2	927.12	25-Oct-26	27-Oct-26			0.00	0.00	0.00

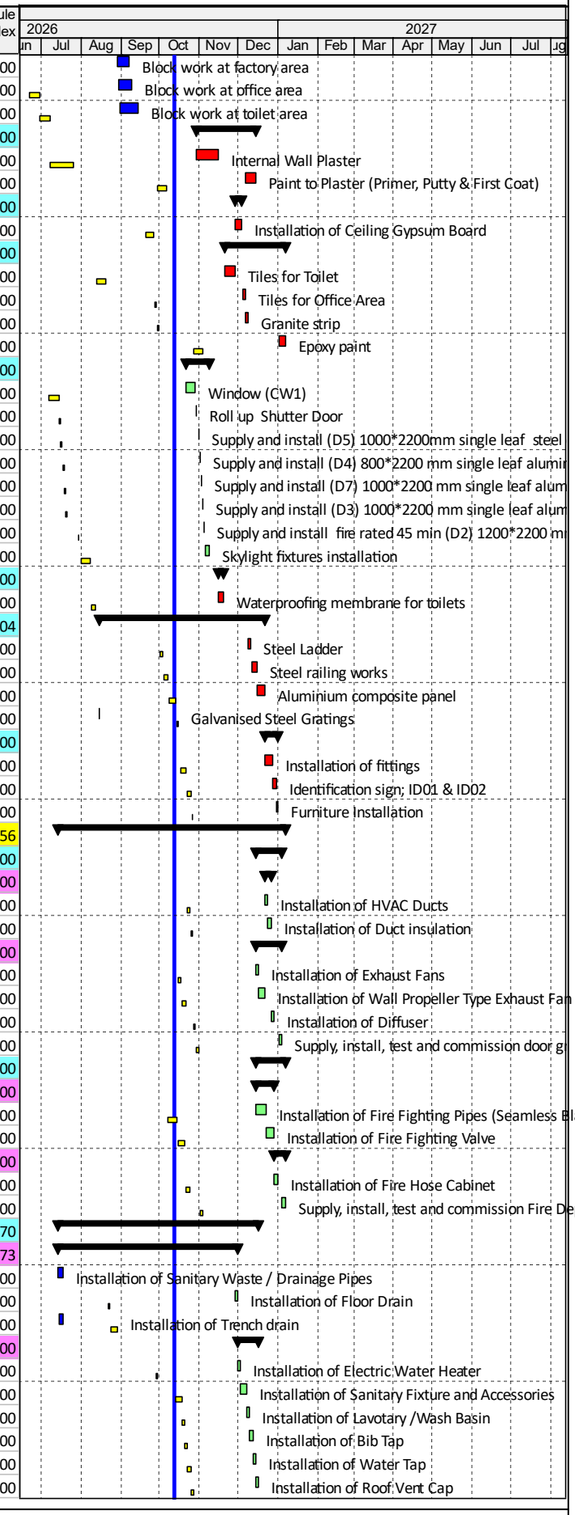


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
WATER SUPPLY SYSTEM		8	41,870.81	07-Oct-26	19-Oct-26	03-Oct-26		32,455.55	41,592.68	1.28
FIRST STAGE		6	41,592.68	07-Oct-26	13-Oct-26	03-Oct-26	07-Oct-26	32,455.55	41,592.68	1.28
DAM3-C-B6-M-600	Installation of Water Supply Pipes	4	23,318.41	07-Oct-26	11-Oct-26	03-Oct-26	07-Oct-26	23,318.41	23,318.41	1.00
DAM3-C-B6-M-590	Installation of Water Supply Valve	2	18,274.27	12-Oct-26	13-Oct-26	03-Oct-26	07-Oct-26	9,137.14	18,274.27	2.00
SECOND STAGE		3	278.13	14-Oct-26	19-Oct-26			0.00	0.00	0.00
DAM3-C-B6-M-640	Capped connection	3	278.13	14-Oct-26	19-Oct-26			0.00	0.00	0.00
ELECTRICAL		167	752,044.76	20-May-26	23-Nov-26	08-Jun-26		93,509.96	27,642.87	0.30
FIRST STAGE		161	86,114.12	20-May-26	05-Nov-26	08-Jun-26		58,956.90	27,642.87	0.47
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	2,920.45	20-May-26	01-Jun-26	08-Jun-26		2,920.45	1,460.23	0.50
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	19,646.47	04-Jul-26	07-Jul-26	08-Jun-26		19,646.47	17,681.82	0.90
DAM3-C-B6-E-453	Installation of LV Cables	4	36,389.98	21-Jul-26	25-Jul-26			36,389.98	0.00	0.00
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	14-Oct-26	18-Oct-26	09-Jun-26		0.00	884.15	0.00
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	8,462.97	28-Oct-26	01-Nov-26	01-Oct-26		0.00	7,616.67	0.00
DAM3-C-B6-E-463	Installation of Wires	4	16,925.94	02-Nov-26	05-Nov-26			0.00	0.00	0.00
SECOND STAGE		84	665,930.64	07-Oct-26	23-Nov-26			34,553.07	0.00	0.00
DAM3-C-B6-E-403	Installation of Wiring Devices	4	19,435.09	07-Oct-26	11-Oct-26			19,435.09	0.00	0.00
DAM3-C-B6-E-433	Installation of Disconnect Switches	2	30,235.95	12-Oct-26	13-Oct-26			15,117.97	0.00	0.00
DAM3-C-B6-E-353	Installation of Fire Alarm Control Panel	3	19,451.37	19-Oct-26	22-Oct-26			0.00	0.00	0.00
DAM3-C-B6-E-363	Installation of Fire Detectors & Accessories	4	56,740.37	24-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B6-E-503	Installation of Access Control System	4	27,616.86	28-Oct-26	01-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-730	Installation of Solar power plant	7	253,268.71	31-Oct-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	3,882.38	02-Nov-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	185.40	04-Nov-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	04-Nov-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-383	Installation of Lighting fixtures	2	76,166.74	07-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-423	Installation of Main Distribution Board	2	32,472.73	11-Nov-26	12-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-473	Installation of LP-1 Panel	2	18,403.54	14-Nov-26	15-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-483	Installation of PP-AC panel	2	21,648.48	16-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-443	Installation of Telephone Cabinet	2	26,991.08	18-Nov-26	19-Nov-26			0.00	0.00	0.00
DAM3-C-B6-E-720	Installation of CCTV System	3	76,349.24	18-Nov-26	23-Nov-26			0.00	0.00	0.00
BLOCK B5		242	5,075,523.09	19-Feb-26	23-Nov-26	16-Feb-26		4,772,376.51	3,271,214.05	0.69
STRUCTURAL		182	1,389,042.53	19-Feb-26	25-Jul-26	16-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		44	597,655.16	19-Feb-26	25-Mar-26	16-Feb-26	05-May-26	597,655.16	597,655.16	1.00
DAM3-C-B5-S-250	Excavation for footings	4	89,859.61	19-Feb-26	25-Feb-26	16-Feb-26	18-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B5-S-6163	Soil replacement - rock fill	4	179,061.91	25-Feb-26	02-Mar-26	30-Mar-26	02-Apr-26	179,061.91	179,061.91	1.00
DAM3-C-B5-S-6173	Engineering fill	4	46,046.19	03-Mar-26	07-Mar-26	07-Apr-26	13-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B5-S-1297	Anti Termite Below Footings	1	11,905.55	08-Mar-26	08-Mar-26	21-Apr-26	21-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B5-S-1207	Vapour Barrier for Footings	1	7,940.10	09-Mar-26	09-Mar-26	21-Apr-26	21-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B5-S-1057	Lean Concrete Below Footings	2	8,229.34	10-Mar-26	11-Mar-26	21-Apr-26	21-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B5-S-1107	Rebar for Footings	4	101,844.98	12-Mar-26	16-Mar-26	28-Apr-26	29-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B5-S-1117	Formwork for Footings	4	25,461.25	21-Mar-26	24-Mar-26	02-May-26	03-May-26	25,461.25	25,461.25	1.00
DAM3-C-B5-S-1067	Pouring Concrete for Footings	1	127,306.23	25-Mar-26	25-Mar-26	05-May-26	05-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		20	120,554.54	26-Mar-26	11-Apr-26	03-May-26	24-May-26	120,554.54	120,554.54	1.00
DAM3-C-B5-S-1157	Rebar for column neck	2	14,919.19	26-Mar-26	28-Mar-26	03-May-26	05-May-26	14,919.19	14,919.19	1.00
DAM3-C-B5-S-1167	Formwork for column neck	2	9,946.13	29-Mar-26	30-Mar-26	06-May-26	09-May-26	9,946.13	9,946.13	1.00
DAM3-C-B5-S-1147	Pouring Concrete for column neck	1	24,865.31	31-Mar-26	31-Mar-26	10-May-26	10-May-26	24,865.31	24,865.31	1.00
DAM3-C-B5-S-1197	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	01-Apr-26	02-Apr-26	11-May-26	12-May-26	24,777.73	24,777.73	1.00
DAM3-C-B5-S-1257	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	04-Apr-26	11-Apr-26	20-May-26	24-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		13	171,632.86	12-Apr-26	28-Apr-26	01-Jun-26	18-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B5-S-1307	Anti Termite Below Grade Beams	1	11,905.55	12-Apr-26	12-Apr-26	01-Jun-26	01-Jun-26	11,905.55	11,905.55	1.00
DAM3-C-B5-S-1227	Vapour barrier for Grade Beams	2	5,293.40	13-Apr-26	14-Apr-26	01-Jun-26	01-Jun-26	5,293.40	5,293.40	1.00
DAM3-C-B5-S-1077	Lean Concrete Below Grade Beams	2	4,431.19	15-Apr-26	16-Apr-26	01-Jun-26	01-Jun-26	4,431.19	4,431.19	1.00
DAM3-C-B5-S-1127	Rebar for Grade Beams	5	27,194.46	18-Apr-26	22-Apr-26	03-Jun-26	04-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B5-S-1137	Formwork for Grade Beams	2	6,798.61	23-Apr-26	25-Apr-26	03-Jun-26	07-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B5-S-1287	Anchor bolts installation	2	57,238.83	23-Apr-26	25-Apr-26	02-Jun-26	04-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B5-S-1087	Pouring Concrete for Grade Beams	1	33,993.09	26-Apr-26	26-Apr-26	11-Jun-26	11-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B5-S-1237	Damp proof /Bitumin paint on Grade Beams	2	24,777.73	27-Apr-26	28-Apr-26	14-Jun-26	18-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		103	397,232.98	29-Apr-26	29-Jun-26	21-Jun-26		397,232.98	396,325.87	1.00
DAM3-C-B5-S-1267	Backfilling / Compaction for Slab on Grade	7	23,023.09	29-Apr-26	06-May-26	21-Jun-26	24-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B5-S-1217	Anti Termite Treatment below Ground Slab	1	15,874.08	07-May-26	07-May-26	01-Aug-26	04-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B5-S-1247	Vapour barrier for below Ground Slab	2	13,233.49	09-May-26	10-May-26	01-Aug-26	04-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B5-S-1097	Pouring Concrete for Ground Slab	4	344,195.21	11-May-26	14-May-26	01-Aug-26	04-Aug-26	344,195.21	344,195.21	1.00

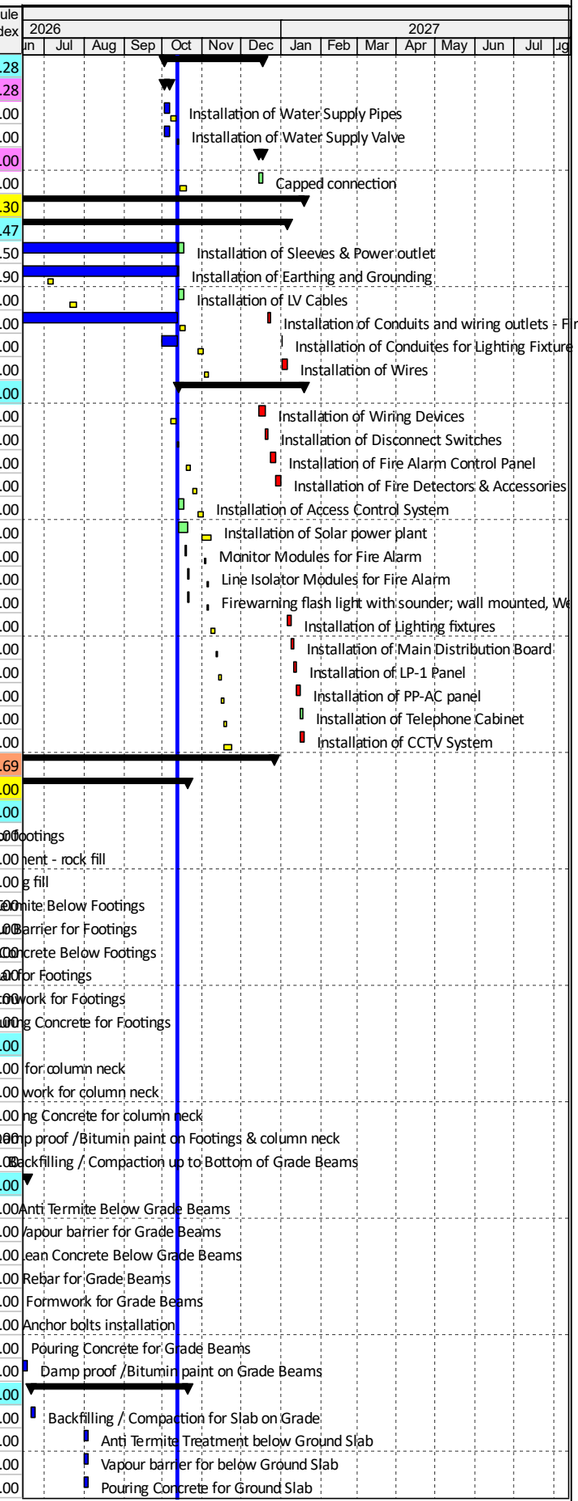

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B5-S-1277	Concrete pad	7	907.11	22-Jun-26	29-Jun-26			907.11	0.00	0.00
COLUMNS & BEAMS		77	101,966.98	07-May-26	25-Jul-26	03-Jun-26	22-Sep-26	101,966.98	101,966.98	1.00
DAM3-C-B5-S-5101	Rebar for column	5	20,144.05	07-May-26	12-May-26	14-Jul-26	16-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B5-S-5102	Formwork for column	4	5,036.01	13-May-26	17-May-26	16-Jul-26	20-Jul-26	5,036.01	5,036.01	1.00
DAM3-C-B5-S-5103	Pouring Concrete for column	1	25,180.06	18-May-26	18-May-26	18-Jul-26	21-Jul-26	25,180.06	25,180.06	1.00
DAM3-C-B5-S-6101	Rebar for Tie Beams	4	7,263.64	19-May-26	23-May-26	03-Jun-26	09-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B5-S-6102	Formwork for Tie Beams	2	1,815.91	24-May-26	25-May-26	04-Jun-26	10-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B5-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	30-May-26	30-May-26	11-Jun-26	11-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B5-S-6113	Rebar for Beams	4	13,379.11	16-Jul-26	21-Jul-26	07-Sep-26	15-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B5-S-6123	Formwork for Beams	2	3,344.77	21-Jul-26	23-Jul-26	15-Sep-26	20-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B5-S-6133	Pouring Concrete for Beams	1	16,723.88	23-Jul-26	25-Jul-26	17-Sep-26	22-Sep-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		87	1,566,668.48	16-May-26	30-Jul-26	02-Jul-26		1,566,668.48	1,539,773.29	0.98
DAM3-C-B5-SS-270	Installation of columns	3	217,507.55	16-May-26	18-May-26	02-Jul-26	05-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B5-SS-280	Installation of raft and purlins	5	326,261.32	19-May-26	24-May-26	02-Jul-26	06-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B5-SS-1840	Intumescent paint to steel works	7	317,759.56	25-May-26	04-Jun-26	12-Jul-26	20-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B5-SS-1850	Steel members for office area	7	115,805.20	06-Jun-26	13-Jun-26	05-Oct-26	06-Oct-26	115,805.20	115,805.20	1.00
DAM3-C-B5-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	14-Jun-26	21-Jun-26			23,161.04	0.00	0.00
DAM3-C-B5-SS-1030	Steel members for external platform	7	18,670.78	14-Jun-26	21-Jun-26	31-Aug-26	01-Sep-26	18,670.78	18,670.78	1.00
DAM3-C-B5-SS-300	Installation of wall sandwich panel	5	326,261.32	22-Jun-26	27-Jun-26	04-Oct-26	08-Oct-26	326,261.32	326,261.32	1.00
DAM3-C-B5-SS-1040	Epoxy paint for external platform	5	3,734.16	22-Jun-26	27-Jun-26			3,734.16	0.00	0.00
DAM3-C-B5-SS-310	Installation of roof sheet	5	217,507.55	25-Jul-26	30-Jul-26	29-Jul-26	08-Aug-26	217,507.55	217,507.55	1.00
ARCHITECTURAL		97	900,244.66	25-May-26	21-Sep-26	08-Aug-26		900,244.66	180,530.24	0.20
MASONARY WORKS		26	78,954.21	25-May-26	29-Jun-26	09-Aug-26	09-Sep-26	78,954.21	78,954.21	1.00
DAM3-C-B5-A-290	Block work at factory area	10	58,338.72	25-May-26	08-Jun-26	09-Aug-26	12-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B5-A-320	Block work at office area	7	6,179.18	14-Jun-26	21-Jun-26	13-Aug-26	09-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B5-A-1440	Block work at toilet area	7	14,436.31	22-Jun-26	29-Jun-26	15-Aug-26	09-Sep-26	14,436.31	14,436.31	1.00
WALL FINISHES		24	92,757.47	09-Jul-26	24-Aug-26	26-Sep-26		92,757.47	48,590.16	0.52
DAM3-C-B5-A-1450	Internal Wall Plaster	15	48,590.16	09-Jul-26	26-Jul-26	26-Sep-26	11-Oct-26	48,590.16	48,590.16	1.00
DAM3-C-B5-A-1500	Paint to Plaster (Primer, Putty & First Coat)	7	44,167.30	17-Aug-26	24-Aug-26			44,167.30	0.00	0.00
CIELING FINISHES		5	46,792.30	09-Aug-26	13-Aug-26			46,792.30	0.00	0.00
DAM3-C-B5-A-1510	Installation of Ceiling Gypsum Board	5	46,792.30	09-Aug-26	13-Aug-26			46,792.30	0.00	0.00
FLOOR FINISHES		35	189,488.90	01-Aug-26	21-Sep-26	11-Oct-26		189,488.90	46,530.71	0.25
DAM3-C-B5-A-1490	Tiles for Toilet	7	46,530.71	01-Aug-26	08-Aug-26	11-Oct-26	13-Oct-26	46,530.71	46,530.71	1.00
DAM3-C-B5-A-1520	Tiles for Office Area	2	26,867.31	15-Aug-26	16-Aug-26			26,867.31	0.00	0.00
DAM3-C-B5-A-1650	Granite strip	2	671.12	17-Aug-26	18-Aug-26			671.12	0.00	0.00
DAM3-C-B5-A-1670	Epoxy paint	7	115,419.76	14-Sep-26	21-Sep-26			115,419.76	0.00	0.00
DOORS & WINDOWS		14	248,575.06	28-Jun-26	13-Jul-26			248,575.06	0.00	0.00
DAM3-C-B5-A-1830	Window (CW1)	7	94,173.21	28-Jun-26	05-Jul-26			94,173.21	0.00	0.00
DAM3-C-B5-A-1460	Roll up Shutter Door	1	68,619.20	06-Jul-26	06-Jul-26			68,619.20	0.00	0.00
DAM3-C-B5-A-1470	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	07-Jul-26	07-Jul-26			16,016.16	0.00	0.00
DAM3-C-B5-A-1530	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	08-Jul-26	08-Jul-26			22,737.85	0.00	0.00
DAM3-C-B5-A-1540	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	09-Jul-26	09-Jul-26			7,811.07	0.00	0.00
DAM3-C-B5-A-1760	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	11-Jul-26	11-Jul-26			16,016.16	0.00	0.00
DAM3-C-B5-A-1770	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	12-Jul-26	12-Jul-26			16,711.52	0.00	0.00
DAM3-C-B5-A-1780	Skylight fixtures installation	1	6,489.89	13-Jul-26	13-Jul-26			6,489.89	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	27-Jul-26	30-Jul-26			4,879.02	0.00	0.00
DAM3-C-B5-A-1630	Waterproofing membrane for toilets	4	4,879.02	27-Jul-26	30-Jul-26			4,879.02	0.00	0.00
METAL WORKS		13	193,717.06	19-Aug-26	02-Sep-26	08-Aug-26		193,717.06	6,455.16	0.03
DAM3-C-B5-A-1560	Steel Ladder	2	9,839.16	19-Aug-26	20-Aug-26			9,839.16	0.00	0.00
DAM3-C-B5-A-1660	Steel railing works	4	1,533.98	22-Aug-26	25-Aug-26			1,533.98	0.00	0.00
DAM3-C-B5-A-1580	Aluminium composite panel	5	175,888.76	26-Aug-26	31-Aug-26			175,888.76	0.00	0.00
DAM3-C-B5-A-1570	Galvanised Steel Gratings	2	6,455.16	01-Sep-26	02-Sep-26	08-Aug-26	08-Aug-26	6,455.16	6,455.16	1.00
SPECIALTIES		9	45,080.66	03-Sep-26	13-Sep-26			45,080.66	0.00	0.00
DAM3-C-B5-A-1590	Installation of fittings	5	22,981.27	03-Sep-26	08-Sep-26			22,981.27	0.00	0.00
DAM3-C-B5-A-1820	Identification sign; ID01 & ID02	3	9,630.56	09-Sep-26	12-Sep-26			9,630.56	0.00	0.00
DAM3-C-B5-A-1610	Furniture Installation	1	12,468.83	13-Sep-26	13-Sep-26			12,468.83	0.00	0.00
MECHANICAL		119	467,522.66	29-Apr-26	13-Sep-26	08-Jul-26		467,522.66	135,132.24	0.29
HVAC		14	233,183.33	25-Aug-26	09-Sep-26			233,183.33	0.00	0.00
FIRST STAGE		4	170,694.73	01-Sep-26	05-Sep-26			170,694.73	0.00	0.00
DAM3-C-B5-M-1070	Installation of HVAC Ducts	2	149,489.33	01-Sep-26	02-Sep-26			149,489.33	0.00	0.00
DAM3-C-B5-M-1100	Installation of Duct insulation	2	21,205.40	03-Sep-26	05-Sep-26			21,205.40	0.00	0.00
SECOND STAGE		14	62,488.60	25-Aug-26	09-Sep-26			62,488.60	0.00	0.00

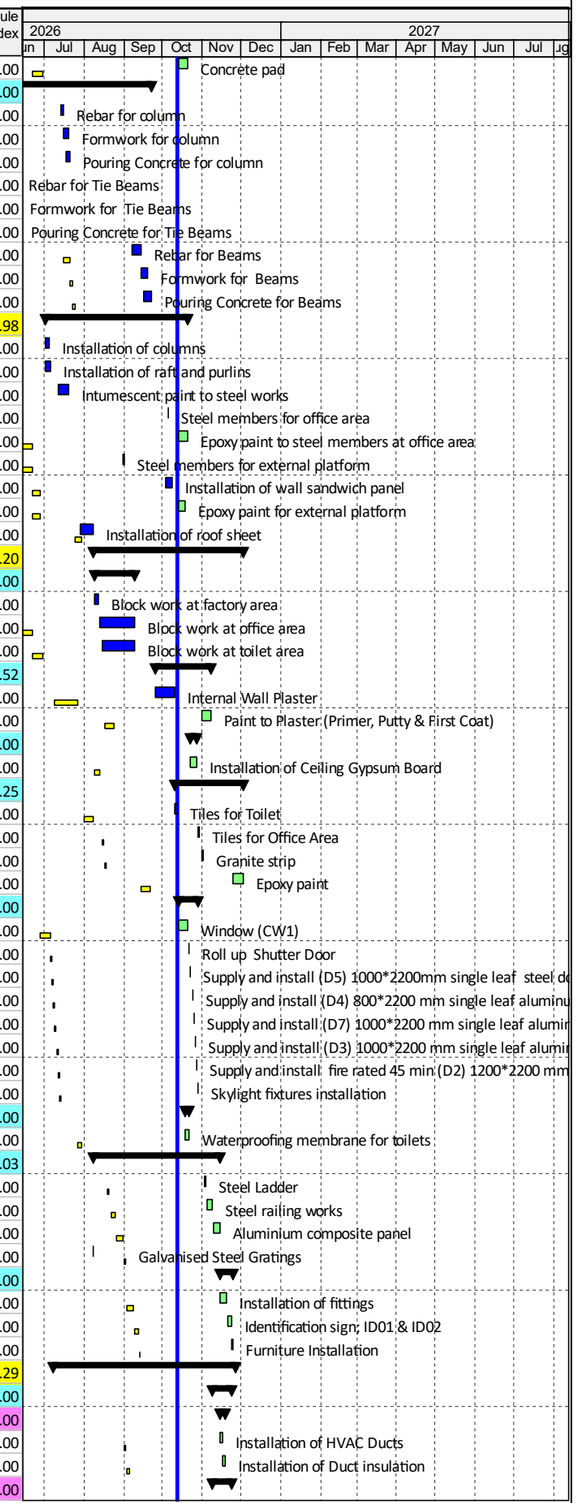

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B5-M-1060	Installation of Exhaust Fans	2	7,938.56	25-Aug-26	26-Aug-26			7,938.56	0.00	0.00
DAM3-C-B5-M-1090	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	27-Aug-26	31-Aug-26			46,831.64	0.00	0.00
DAM3-C-B5-M-1080	Installation of Diffuser	2	2,144.00	06-Sep-26	07-Sep-26			2,144.00	0.00	0.00
DAM3-C-B5-M-1270	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	08-Sep-26	09-Sep-26			5,574.40	0.00	0.00
FIRE FIGHTING SYSTEM		15	102,458.78	25-Aug-26	13-Sep-26	11-Oct-26		102,458.78	63,445.62	0.62
FIRST STAGE		12	84,594.16	25-Aug-26	07-Sep-26	11-Oct-26		84,594.16	63,445.62	0.75
DAM3-C-B5-M-1230	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	25-Aug-26	01-Sep-26	11-Oct-26		72,394.75	54,296.06	0.75
DAM3-C-B5-M-1240	Installation of Fire Fighting Valve	5	12,199.40	02-Sep-26	07-Sep-26	11-Oct-26		12,199.40	9,149.55	0.75
SECOND STAGE		14	17,864.62	08-Sep-26	13-Sep-26			17,864.62	0.00	0.00
DAM3-C-B5-M-1250	Installation of Fire Hose Cabinet	3	15,158.56	08-Sep-26	10-Sep-26			15,158.56	0.00	0.00
DAM3-C-B5-M-1300	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	10-Sep-26	13-Sep-26			2,706.06	0.00	0.00
SEWER AND DRAINAGE SYSTEM		98	90,009.74	29-Apr-26	01-Sep-26	08-Jul-26		90,009.74	30,093.94	0.33
FIRST STAGE		84	41,149.90	29-Apr-26	16-Aug-26	08-Jul-26		41,149.90	30,093.94	0.73
DAM3-C-B5-M-1130	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	29-Apr-26	03-May-26	08-Jul-26	12-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B5-M-1150	Installation of Floor Drain	2	11,055.96	09-Aug-26	10-Aug-26			11,055.96	0.00	0.00
DAM3-C-B5-M-1310	Installation of Trench drain	5	11,508.80	11-Aug-26	16-Aug-26	11-Jul-26	14-Jul-26	11,508.80	11,508.80	1.00
SECOND STAGE		14	48,859.84	17-Aug-26	01-Sep-26			48,859.84	0.00	0.00
DAM3-C-B5-M-1110	Installation of Electric Water Heater	2	1,819.51	17-Aug-26	18-Aug-26			1,819.51	0.00	0.00
DAM3-C-B5-M-1120	Installation of Sanitary Fixture and Accessories	4	19,921.72	19-Aug-26	23-Aug-26			19,921.72	0.00	0.00
DAM3-C-B5-M-1140	Installation of Lavotary /Wash Basin	2	21,416.68	24-Aug-26	25-Aug-26			21,416.68	0.00	0.00
DAM3-C-B5-M-1200	Installation of Bib Tap	2	1,900.66	26-Aug-26	27-Aug-26			1,900.66	0.00	0.00
DAM3-C-B5-M-1160	Installation of Water Tap	2	2,874.14	29-Aug-26	30-Aug-26			2,874.14	0.00	0.00
DAM3-C-B5-M-1170	Installation of Roof Vent Cap	2	927.12	31-Aug-26	01-Sep-26			927.12	0.00	0.00
WATER SUPPLY SYSTEM		23	41,870.81	25-Aug-26	06-Sep-26	29-Sep-26		41,870.81	41,592.68	0.99
FIRST STAGE		6	41,592.68	25-Aug-26	31-Aug-26	29-Sep-26	03-Oct-26	41,592.68	41,592.68	1.00
DAM3-C-B5-M-1220	Installation of Water Supply Pipes	4	23,318.41	25-Aug-26	29-Aug-26	29-Sep-26	03-Oct-26	23,318.41	23,318.41	1.00
DAM3-C-B5-M-1210	Installation of Water Supply Valve	2	18,274.27	30-Aug-26	31-Aug-26	29-Sep-26	03-Oct-26	18,274.27	18,274.27	1.00
SECOND STAGE		5	278.13	01-Sep-26	06-Sep-26			278.13	0.00	0.00
DAM3-C-B5-M-1260	Capped connection	5	278.13	01-Sep-26	06-Sep-26			278.13	0.00	0.00
ELECTRICAL		118	752,044.76	30-Jun-26	23-Nov-26	04-Jun-26		448,898.18	27,642.87	0.06
FIRST STAGE		118	86,114.12	30-Jun-26	13-Oct-26	04-Jun-26		72,105.01	27,642.87	0.38
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	2,920.45	30-Jun-26	08-Jul-26	04-Jun-26		2,920.45	1,460.23	0.50
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	01-Sep-26	05-Sep-26	04-Jun-26		1,768.31	884.15	0.50
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	8,462.97	15-Sep-26	19-Sep-26	20-Sep-26		8,462.97	7,616.67	0.90
DAM3-C-B5-E-923	Installation of Wires	4	16,925.94	20-Sep-26	24-Sep-26			16,925.94	0.00	0.00
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	19,646.47	10-Oct-26	13-Oct-26	04-Jun-26		14,734.85	17,681.82	1.20
DAM3-C-B5-E-913	Installation of LV Cables	4	36,389.98	10-Oct-26	13-Oct-26			27,292.48	0.00	0.00
SECOND STAGE		57	665,930.64	25-Aug-26	23-Nov-26			376,793.18	0.00	0.00
DAM3-C-B5-E-863	Installation of Wiring Devices	4	19,435.09	25-Aug-26	29-Aug-26			19,435.09	0.00	0.00
DAM3-C-B5-E-893	Installation of Disconnect Switches	2	30,235.95	30-Aug-26	31-Aug-26			30,235.95	0.00	0.00
DAM3-C-B5-E-813	Installation of Fire Alarm Control Panel	4	19,451.37	06-Sep-26	09-Sep-26			19,451.37	0.00	0.00
DAM3-C-B5-E-823	Installation of Fire Detectors & Accessories	4	56,740.37	10-Sep-26	14-Sep-26			56,740.37	0.00	0.00
DAM3-C-B5-E-843	Installation of Lighting fixtures	4	76,166.74	26-Sep-26	29-Sep-26			76,166.74	0.00	0.00
DAM3-C-B5-E-883	Installation of Main Distribution Board	2	32,472.73	30-Sep-26	01-Oct-26			32,472.73	0.00	0.00
DAM3-C-B5-E-933	Installation of LP-1 Panel	2	18,403.54	03-Oct-26	04-Oct-26			18,403.54	0.00	0.00
DAM3-C-B5-E-943	Installation of PP-AC panel	2	21,648.48	05-Oct-26	06-Oct-26			21,648.48	0.00	0.00
DAM3-C-B5-E-903	Installation of Telephone Cabinet	2	26,991.08	07-Oct-26	08-Oct-26			26,991.08	0.00	0.00
DAM3-C-B5-E-1340	Installation of CCTV System	7	76,349.24	07-Oct-26	14-Oct-26			54,535.17	0.00	0.00
DAM3-C-B5-E-963	Installation of Access Control System	4	27,616.86	10-Oct-26	13-Oct-26			20,712.65	0.00	0.00
DAM3-C-B5-E-973	Monitor Modules for Fire Alarm	2	3,882.38	14-Oct-26	15-Oct-26			0.00	0.00	0.00
DAM3-C-B5-E-983	Line Isolator Modules for Fire Alarm	2	185.40	17-Oct-26	18-Oct-26			0.00	0.00	0.00
DAM3-C-B5-E-993	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	19-Oct-26	20-Oct-26			0.00	0.00	0.00
DAM3-C-B5-E-1350	Installation of Solar power plant	14	253,268.71	08-Nov-26	23-Nov-26			0.00	0.00	0.00
BLOCK B4		242	5,075,523.09	25-Feb-26	01-Dec-26	17-Feb-26		4,418,632.19	3,336,529.90	0.76
STRUCTURAL		192	1,389,042.53	25-Feb-26	21-Jul-26	17-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		36	597,655.16	25-Feb-26	30-Mar-26	17-Feb-26	30-Apr-26	597,655.16	597,655.16	1.00
DAM3-C-B4-S-210	Excavation for footings	4	89,859.61	25-Feb-26	02-Mar-26	17-Feb-26	24-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B4-S-6183	Soil replacement - rock fill	4	179,061.91	03-Mar-26	07-Mar-26	26-Mar-26	29-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B4-S-6193	Engineering fill	4	46,046.19	08-Mar-26	11-Mar-26	02-Apr-26	05-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B4-S-1037	Anti Termite Below Footings	1	11,905.55	12-Mar-26	12-Mar-26	15-Apr-26	15-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B4-S-947	Vapour Barrier for Footings	1	7,940.10	14-Mar-26	14-Mar-26	15-Apr-26	15-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B4-S-797	Lean Concrete Below Footings	2	8,229.34	15-Mar-26	16-Mar-26	15-Apr-26	15-Apr-26	8,229.34	8,229.34	1.00

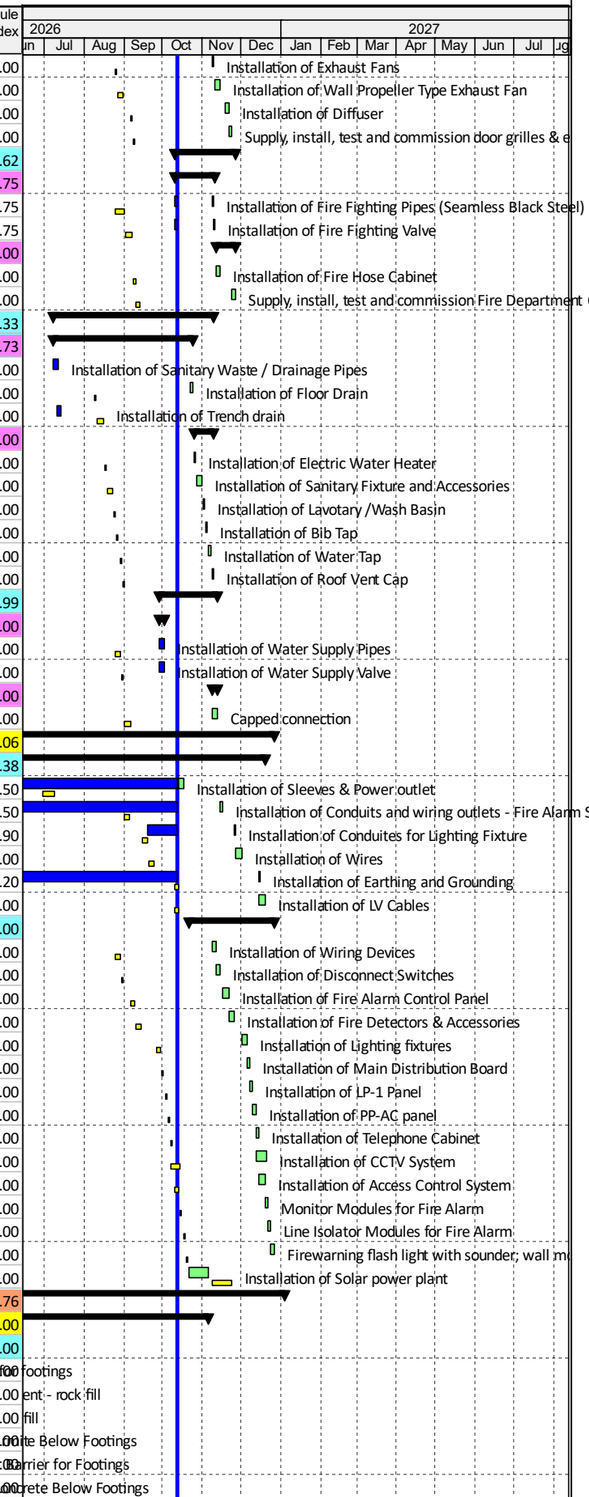

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B4-S-847	Rebar for Footings	4	101,844.98	21-Mar-26	24-Mar-26	23-Apr-26	28-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B4-S-857	Formwork for Footings	4	25,461.25	25-Mar-26	29-Mar-26	20-Apr-26	22-Apr-26	25,461.25	25,461.25	1.00
DAM3-C-B4-S-807	Pouring Concrete for Footings	1	127,306.23	30-Mar-26	30-Mar-26	30-Apr-26	30-Apr-26	127,306.23	127,306.23	1.00
COLUMN NECK		17	120,554.54	31-Mar-26	15-Apr-26	23-Apr-26	19-May-26	120,554.54	120,554.54	1.00
DAM3-C-B4-S-897	Rebar for column neck	2	14,919.19	31-Mar-26	01-Apr-26	23-Apr-26	28-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B4-S-907	Formwork for column neck	2	9,946.13	02-Apr-26	04-Apr-26	03-May-26	05-May-26	9,946.13	9,946.13	1.00
DAM3-C-B4-S-887	Pouring Concrete for column neck	1	24,865.31	05-Apr-26	05-Apr-26	05-May-26	05-May-26	24,865.31	24,865.31	1.00
DAM3-C-B4-S-937	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	06-Apr-26	07-Apr-26	07-May-26	10-May-26	24,777.73	24,777.73	1.00
DAM3-C-B4-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	08-Apr-26	15-Apr-26	13-May-26	19-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		17	171,632.86	16-Apr-26	06-May-26	20-May-26	09-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B4-S-1047	Anti Termite Below Grade Beams	1	11,905.55	16-Apr-26	16-Apr-26	20-May-26	20-May-26	11,905.55	11,905.55	1.00
DAM3-C-B4-S-967	Vapour barrier for Grade Beams	2	5,293.40	18-Apr-26	19-Apr-26	20-May-26	20-May-26	5,293.40	5,293.40	1.00
DAM3-C-B4-S-817	Lean Concrete Below Grade Beams	2	4,431.19	20-Apr-26	21-Apr-26	20-May-26	20-May-26	4,431.19	4,431.19	1.00
DAM3-C-B4-S-867	Rebar for Grade Beams	5	27,194.46	22-Apr-26	27-Apr-26	21-May-26	24-May-26	27,194.46	27,194.46	1.00
DAM3-C-B4-S-877	Formwork for Grade Beams	2	6,798.61	28-Apr-26	29-Apr-26	24-May-26	02-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B4-S-1027	Anchor bolts installation	2	57,238.83	28-Apr-26	29-Apr-26	31-May-26	01-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B4-S-827	Pouring Concrete for Grade Beams	1	33,993.09	30-Apr-26	30-Apr-26	03-Jun-26	03-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B4-S-977	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	02-May-26	06-May-26	07-Jun-26	09-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		122	397,232.98	07-May-26	21-Jul-26	14-Jun-26		397,232.98	396,325.87	1.00
DAM3-C-B4-S-1007	Backfilling / Compaction for Slab on Grade	7	23,023.09	07-May-26	14-May-26	14-Jun-26	22-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B4-S-957	Anti Termite Treatment below Ground Slab	1	15,874.08	16-May-26	16-May-26	29-Jul-26	01-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B4-S-987	Vapour barrier for below Ground Slab	2	13,233.49	17-May-26	18-May-26	29-Jul-26	01-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B4-S-837	Pouring Concrete for Ground Slab	4	344,195.21	19-May-26	23-May-26	29-Jul-26	01-Aug-26	344,195.21	344,195.21	1.00
DAM3-C-B4-S-1017	Concrete pad	7	907.11	14-Jul-26	21-Jul-26			907.11	0.00	0.00
COLUMNS & BEAMS		61	101,966.98	16-May-26	15-Jun-26	21-May-26	14-Sep-26	101,966.98	101,966.98	1.00
DAM3-C-B4-S-5101	Rebar for column	5	20,144.05	16-May-26	20-May-26	22-Jun-26	02-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B4-S-5102	Formwork for column	4	5,036.01	21-May-26	25-May-26	29-Jun-26	05-Jul-26	5,036.01	5,036.01	1.00
DAM3-C-B4-S-5103	Pouring Concrete for column	1	25,180.06	30-May-26	30-May-26	09-Jul-26	12-Jul-26	25,180.06	25,180.06	1.00
DAM3-C-B4-S-6101	Rebar for Tie Beams	4	7,263.64	31-May-26	03-Jun-26	21-May-26	24-May-26	7,263.64	7,263.64	1.00
DAM3-C-B4-S-6102	Formwork for Tie Beams	2	1,815.91	04-Jun-26	06-Jun-26	24-May-26	02-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B4-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	07-Jun-26	07-Jun-26	03-Jun-26	03-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B4-S-6113	Rebar for Beams	4	13,379.11	08-Jun-26	11-Jun-26	30-Aug-26	01-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B4-S-6123	Formwork for Beams	2	3,344.77	13-Jun-26	14-Jun-26	02-Sep-26	08-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B4-S-6133	Pouring Concrete for Beams	1	16,723.88	15-Jun-26	15-Jun-26	08-Sep-26	14-Sep-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		94	1,566,668.48	25-May-26	19-Jul-26	24-Jun-26		1,566,668.48	1,539,773.29	0.98
DAM3-C-B4-A-210	Installation of columns	3	217,507.55	25-May-26	31-May-26	24-Jun-26	24-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B4-A-220	Installation of raft and purlins	5	326,261.32	01-Jun-26	06-Jun-26	25-Jun-26	25-Jun-26	326,261.32	326,261.32	1.00
DAM3-C-B4-A-1430	Intumescent paint to steel works	7	317,759.56	07-Jun-26	14-Jun-26	08-Jul-26	14-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B4-A-1440	Steel members for office area	7	115,805.20	15-Jun-26	22-Jun-26	01-Oct-26	04-Oct-26	115,805.20	115,805.20	1.00
DAM3-C-B4-A-250	Installation of roof sheet	5	217,507.55	21-Jun-26	25-Jun-26	26-Jul-26	30-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B4-SS-1030	Steel members for external platform	7	18,670.78	23-Jun-26	30-Jun-26	01-Sep-26	02-Sep-26	18,670.78	18,670.78	1.00
DAM3-C-B4-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	28-Jun-26	05-Jul-26			23,161.04	0.00	0.00
DAM3-C-B4-SS-1040	Epoxy paint for external platform	5	3,734.16	01-Jul-26	06-Jul-26			3,734.16	0.00	0.00
DAM3-C-B4-A-240	Installation of wall sandwich panel	5	326,261.32	14-Jul-26	19-Jul-26	03-Oct-26	28-Oct-26	326,261.32	326,261.32	1.00
ARCHITECTURAL		111	900,244.66	09-Jun-26	17-Oct-26	03-Aug-26		834,290.51	224,697.54	0.27
MASONARY WORKS		30	78,954.21	09-Jun-26	21-Jul-26	05-Aug-26	01-Sep-26	78,954.21	78,954.21	1.00
DAM3-C-B4-A-230	Block work at factory area	10	58,338.72	09-Jun-26	20-Jun-26	05-Aug-26	10-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B4-A-260	Block work at office area	7	6,179.18	06-Jul-26	13-Jul-26	05-Aug-26	01-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B4-A-1030	Block work at toilet area	7	14,436.31	14-Jul-26	21-Jul-26	05-Aug-26	24-Aug-26	14,436.31	14,436.31	1.00
WALL FINISHES		28	92,757.47	01-Aug-26	15-Sep-26	24-Sep-26	13-Oct-26	92,757.47	92,757.47	1.00
DAM3-C-B4-A-1040	Internal Wall Plaster	10	48,590.16	01-Aug-26	17-Aug-26	24-Sep-26	06-Oct-26	48,590.16	48,590.16	1.00
DAM3-C-B4-A-1090	Paint to Plaster (Primer, Putty & First Coat)	7	44,167.30	08-Sep-26	15-Sep-26	07-Oct-26	13-Oct-26	44,167.30	44,167.30	1.00
CIELING FINISHES		5	46,792.30	31-Aug-26	05-Sep-26			46,792.30	0.00	0.00
DAM3-C-B4-A-1100	Installation of Ceiling Gypsum Board	5	46,792.30	31-Aug-26	05-Sep-26			46,792.30	0.00	0.00
FLOOR FINISHES		41	189,488.90	23-Aug-26	17-Oct-26	05-Oct-26		123,534.75	46,530.71	0.38
DAM3-C-B4-A-1080	Tiles for Toilet	7	46,530.71	23-Aug-26	30-Aug-26	05-Oct-26	10-Oct-26	46,530.71	46,530.71	1.00
DAM3-C-B4-A-1110	Tiles for Office Area	2	26,867.31	06-Sep-26	07-Sep-26			26,867.31	0.00	0.00
DAM3-C-B4-A-1240	Granite strip	2	671.12	08-Sep-26	09-Sep-26			671.12	0.00	0.00
DAM3-C-B4-A-1260	Epoxy paint	7	115,419.76	10-Oct-26	17-Oct-26			49,465.61	0.00	0.00
DOORS & WINDOWS		14	248,575.06	20-Jul-26	04-Aug-26			248,575.06	0.00	0.00
DAM3-C-B4-A-1420	Window (CW1)	7	94,173.21	20-Jul-26	27-Jul-26			94,173.21	0.00	0.00
DAM3-C-B4-A-1050	Roll up Shutter Door	1	68,619.20	28-Jul-26	28-Jul-26			68,619.20	0.00	0.00

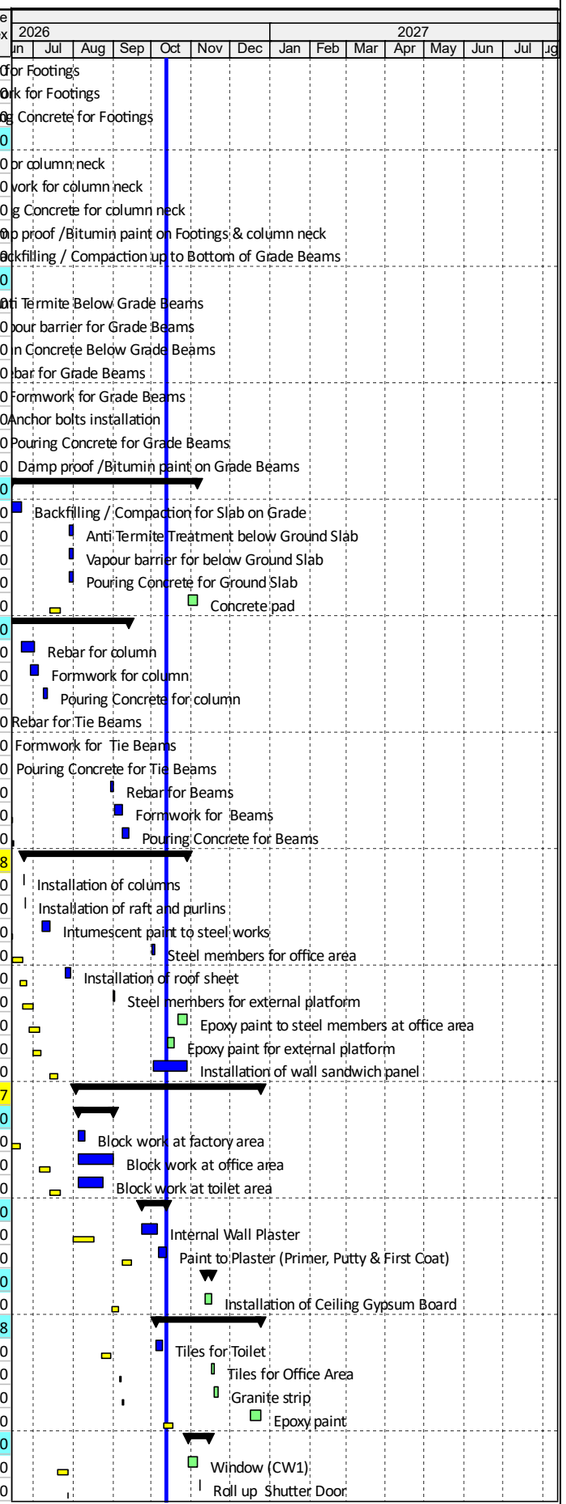

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B4-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	29-Jul-26	29-Jul-26			16,016.16	0.00	0.00
DAM3-C-B4-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	30-Jul-26	30-Jul-26			22,737.85	0.00	0.00
DAM3-C-B4-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	01-Aug-26	01-Aug-26			7,811.07	0.00	0.00
DAM3-C-B4-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	02-Aug-26	02-Aug-26			16,016.16	0.00	0.00
DAM3-C-B4-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	03-Aug-26	03-Aug-26			16,711.52	0.00	0.00
DAM3-C-B4-A-1370	Skylight fixtures installation	1	6,489.89	04-Aug-26	04-Aug-26			6,489.89	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	18-Aug-26	22-Aug-26			4,879.02	0.00	0.00
DAM3-C-B4-A-1220	Waterproofing membrane for toilets	4	4,879.02	18-Aug-26	22-Aug-26			4,879.02	0.00	0.00
METAL WORKS		18	193,717.06	10-Sep-26	26-Sep-26	03-Aug-26		193,717.06	6,455.16	0.03
DAM3-C-B4-A-1150	Steel Ladder	2	9,839.16	10-Sep-26	12-Sep-26			9,839.16	0.00	0.00
DAM3-C-B4-A-1250	Steel railing works	4	1,533.98	13-Sep-26	16-Sep-26			1,533.98	0.00	0.00
DAM3-C-B4-A-1170	Aluminium composite panel	5	175,888.76	17-Sep-26	22-Sep-26			175,888.76	0.00	0.00
DAM3-C-B4-A-1160	Galvanised Steel Gratings	2	6,455.16	24-Sep-26	26-Sep-26	03-Aug-26	03-Aug-26	6,455.16	6,455.16	1.00
SPECIALTIES		11	45,080.66	27-Sep-26	08-Oct-26			45,080.66	0.00	0.00
DAM3-C-B4-A-1180	Installation of fittings	7	22,981.27	27-Sep-26	04-Oct-26			22,981.27	0.00	0.00
DAM3-C-B4-A-1410	Identification sign; ID01 & ID02	3	9,630.56	05-Oct-26	07-Oct-26			9,630.56	0.00	0.00
DAM3-C-B4-A-1200	Furniture Installation	1	12,468.83	08-Oct-26	08-Oct-26			12,468.83	0.00	0.00
MECHANICAL		150	467,522.66	07-May-26	06-Oct-26	25-Jun-26		467,522.66	156,280.78	0.33
HVAC		14	233,183.33	16-Sep-26	03-Oct-26			233,183.33	0.00	0.00
FIRST STAGE		4	170,694.73	24-Sep-26	28-Sep-26			170,694.73	0.00	0.00
DAM3-C-B4-M-760	Installation of HVAC Ducts	2	149,489.33	24-Sep-26	26-Sep-26			149,489.33	0.00	0.00
DAM3-C-B4-M-790	Installation of Duct insulation	2	21,205.40	27-Sep-26	28-Sep-26			21,205.40	0.00	0.00
SECOND STAGE		14	62,488.60	16-Sep-26	03-Oct-26			62,488.60	0.00	0.00
DAM3-C-B4-M-750	Installation of Exhaust Fans	2	7,938.56	16-Sep-26	17-Sep-26			7,938.56	0.00	0.00
DAM3-C-B4-M-780	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	19-Sep-26	22-Sep-26			46,831.64	0.00	0.00
DAM3-C-B4-M-770	Installation of Diffuser	2	2,144.00	29-Sep-26	30-Sep-26			2,144.00	0.00	0.00
DAM3-C-B4-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	01-Oct-26	03-Oct-26			5,574.40	0.00	0.00
FIRE FIGHTING SYSTEM		28	102,458.78	16-Sep-26	06-Oct-26	30-Sep-26		102,458.78	84,594.16	0.83
FIRST STAGE		12	84,594.16	16-Sep-26	30-Sep-26	30-Sep-26	04-Oct-26	84,594.16	84,594.16	1.00
DAM3-C-B4-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	16-Sep-26	24-Sep-26	30-Sep-26	04-Oct-26	72,394.75	72,394.75	1.00
DAM3-C-B4-M-930	Installation of Fire Fighting Valve	5	12,199.40	26-Sep-26	30-Sep-26	30-Sep-26	04-Oct-26	12,199.40	12,199.40	1.00
SECOND STAGE		17	17,864.62	01-Oct-26	06-Oct-26			17,864.62	0.00	0.00
DAM3-C-B4-M-940	Installation of Fire Hose Cabinet	3	15,158.56	01-Oct-26	04-Oct-26			15,158.56	0.00	0.00
DAM3-C-B4-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	04-Oct-26	06-Oct-26			2,706.06	0.00	0.00
SEWER AND DRAINAGE SYSTEM		131	90,009.74	07-May-26	24-Sep-26	25-Jun-26		90,009.74	30,093.94	0.33
FIRST STAGE		117	41,149.90	07-May-26	07-Sep-26	25-Jun-26		41,149.90	30,093.94	0.73
DAM3-C-B4-M-820	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	07-May-26	11-May-26	27-Jun-26	29-Jun-26	18,585.14	18,585.14	1.00
DAM3-C-B4-M-840	Installation of Floor Drain	2	11,055.96	31-Aug-26	01-Sep-26			11,055.96	0.00	0.00
DAM3-C-B4-M-1000	Installation of Trench drain	5	11,508.80	02-Sep-26	07-Sep-26	25-Jun-26	28-Jun-26	11,508.80	11,508.80	1.00
SECOND STAGE		14	48,859.84	08-Sep-26	24-Sep-26			48,859.84	0.00	0.00
DAM3-C-B4-M-800	Installation of Electric Water Heater	2	1,819.51	08-Sep-26	09-Sep-26			1,819.51	0.00	0.00
DAM3-C-B4-M-810	Installation of Sanitary Fixture and Accessories	4	19,921.72	10-Sep-26	14-Sep-26			19,921.72	0.00	0.00
DAM3-C-B4-M-830	Installation of Lavotary /Wash Basin	2	21,416.68	15-Sep-26	16-Sep-26			21,416.68	0.00	0.00
DAM3-C-B4-M-890	Installation of Bib Tap	2	1,900.66	17-Sep-26	19-Sep-26			1,900.66	0.00	0.00
DAM3-C-B4-M-850	Installation of Water Tap	2	2,874.14	20-Sep-26	21-Sep-26			2,874.14	0.00	0.00
DAM3-C-B4-M-860	Installation of Roof Vent Cap	2	927.12	22-Sep-26	24-Sep-26			927.12	0.00	0.00
WATER SUPPLY SYSTEM		21	41,870.81	16-Sep-26	29-Sep-26	22-Sep-26		41,870.81	41,592.68	0.99
FIRST STAGE		7	41,592.68	16-Sep-26	22-Sep-26	22-Sep-26	29-Sep-26	41,592.68	41,592.68	1.00
DAM3-C-B4-M-910	Installation of Water Supply Pipes	4	23,318.41	16-Sep-26	20-Sep-26	22-Sep-26	29-Sep-26	23,318.41	23,318.41	1.00
DAM3-C-B4-M-900	Installation of Water Supply Valve	2	18,274.27	21-Sep-26	22-Sep-26	24-Sep-26	29-Sep-26	18,274.27	18,274.27	1.00
SECOND STAGE		5	278.13	24-Sep-26	29-Sep-26			278.13	0.00	0.00
DAM3-C-B4-M-950	Capped connection	5	278.13	24-Sep-26	29-Sep-26			278.13	0.00	0.00
ELECTRICAL		100	752,044.76	22-Jul-26	01-Dec-26	24-May-26		161,108.01	27,642.87	0.17
FIRST STAGE		99	86,114.12	22-Jul-26	28-Oct-26	24-May-26		13,151.73	27,642.87	2.10
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	2,920.45	22-Jul-26	30-Jul-26	24-May-26		2,920.45	1,460.23	0.50
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	24-Sep-26	28-Sep-26	24-May-26		1,768.31	884.15	0.50
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	8,462.97	08-Oct-26	12-Oct-26	12-Sep-26		8,462.97	7,616.67	0.90
DAM3-C-B4-E-693	Installation of Wires	4	16,925.94	13-Oct-26	17-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	19,646.47	25-Oct-26	28-Oct-26	24-May-26		0.00	17,681.82	0.00
DAM3-C-B4-E-683	Installation of LV Cables	4	36,389.98	25-Oct-26	28-Oct-26			0.00	0.00	0.00
SECOND STAGE		50	665,930.64	16-Sep-26	01-Dec-26			147,956.27	0.00	0.00
DAM3-C-B4-E-633	Installation of Wiring Devices	4	19,435.09	16-Sep-26	20-Sep-26			19,435.09	0.00	0.00

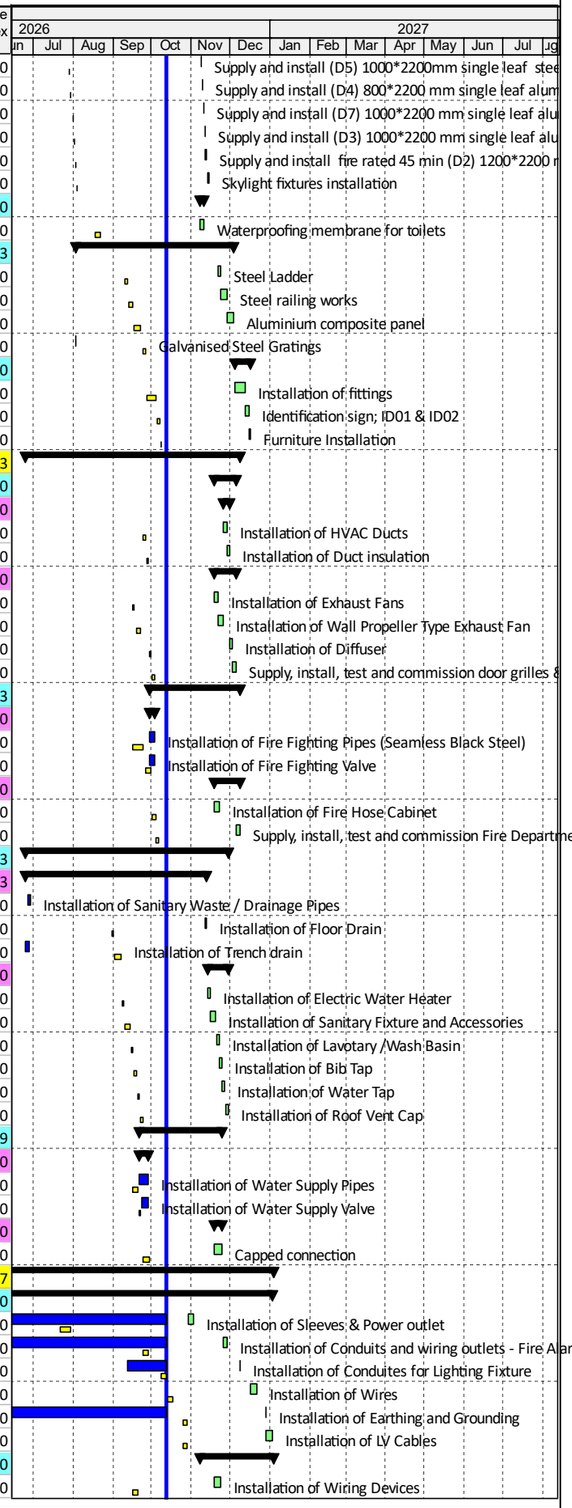

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B4-E-663	Installation of Disconnect Switches	2	30,235.95	21-Sep-26	22-Sep-26			30,235.95	0.00	0.00
DAM3-C-B4-E-583	Installation of Fire Alarm Control Panel	4	19,451.37	29-Sep-26	03-Oct-26			19,451.37	0.00	0.00
DAM3-C-B4-E-593	Installation of Fire Detectors & Accessories	4	56,740.37	04-Oct-26	07-Oct-26			56,740.37	0.00	0.00
DAM3-C-B4-E-733	Installation of Access Control System	5	27,616.86	08-Oct-26	13-Oct-26			22,093.49	0.00	0.00
DAM3-C-B4-E-743	Monitor Modules for Fire Alarm	2	3,882.38	14-Oct-26	15-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-753	Line Isolator Modules for Fire Alarm	2	185.40	17-Oct-26	18-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-613	Installation of Lighting fixtures	4	76,166.74	18-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-653	Installation of Main Distribution Board	2	32,472.73	18-Oct-26	19-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	19-Oct-26	20-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-703	Installation of LP-1 Panel	2	18,403.54	20-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-1030	Installation of CCTV System	7	76,349.24	22-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-713	Installation of PP-AC panel	2	21,648.48	22-Oct-26	24-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-673	Installation of Telephone Cabinet	2	26,991.08	25-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B4-E-1040	Installation of Solar power plant	7	253,268.71	24-Nov-26	01-Dec-26			0.00	0.00	0.00
BLOCK B3		303	5,075,523.09	03-Mar-26	28-Dec-26	17-Feb-26		3,476,170.36	2,969,685.22	0.85
STRUCTURAL		178	1,389,042.53	03-Mar-26	18-Jul-26	17-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		46	597,655.16	03-Mar-26	04-Apr-26	17-Feb-26	17-May-26	597,655.16	597,655.16	1.00
DAM3-C-B3-S-210	Excavation for footings	4	89,859.61	03-Mar-26	07-Mar-26	17-Feb-26	12-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B3-S-6203	Soil replacement - rock fill	4	179,061.91	08-Mar-26	11-Mar-26	17-Mar-26	24-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B3-S-6213	Engineering fill	4	46,046.19	12-Mar-26	16-Mar-26	28-Mar-26	07-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B3-S-1037	Anti Termite Below Footings	1	11,905.55	21-Mar-26	21-Mar-26	11-Apr-26	11-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B3-S-947	Vapour Barrier for Footings	1	7,940.10	22-Mar-26	22-Mar-26	11-Apr-26	11-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B3-S-797	Lean Concrete Below Footings	2	8,229.34	23-Mar-26	24-Mar-26	11-Apr-26	11-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B3-S-847	Rebar for Footings	4	101,844.98	25-Mar-26	29-Mar-26	06-May-26	11-May-26	101,844.98	101,844.98	1.00
DAM3-C-B3-S-857	Formwork for Footings	4	25,461.25	30-Mar-26	02-Apr-26	11-May-26	13-May-26	25,461.25	25,461.25	1.00
DAM3-C-B3-S-807	Pouring Concrete for Footings	1	127,306.23	04-Apr-26	04-Apr-26	17-May-26	17-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		12	120,554.54	05-Apr-26	20-Apr-26	11-May-26	09-Jun-26	120,554.54	120,554.54	1.00
DAM3-C-B3-S-897	Rebar for column neck	2	14,919.19	05-Apr-26	06-Apr-26	11-May-26	14-May-26	14,919.19	14,919.19	1.00
DAM3-C-B3-S-907	Formwork for column neck	2	9,946.13	07-Apr-26	08-Apr-26	21-May-26	23-May-26	9,946.13	9,946.13	1.00
DAM3-C-B3-S-887	Pouring Concrete for column neck	1	24,865.31	09-Apr-26	09-Apr-26	20-May-26	20-May-26	24,865.31	24,865.31	1.00
DAM3-C-B3-S-937	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	11-Apr-26	12-Apr-26	20-May-26	23-May-26	24,777.73	24,777.73	1.00
DAM3-C-B3-S-997	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	13-Apr-26	20-Apr-26	24-May-26	09-Jun-26	46,046.19	46,046.19	1.00
GRADE BEAM		15	171,632.86	21-Apr-26	11-May-26	14-Jun-26	30-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B3-S-1047	Anti Termite Below Grade Beams	1	11,905.55	21-Apr-26	21-Apr-26	14-Jun-26	14-Jun-26	11,905.55	11,905.55	1.00
DAM3-C-B3-S-967	Vapour barrier for Grade Beams	2	5,293.40	22-Apr-26	23-Apr-26	14-Jun-26	14-Jun-26	5,293.40	5,293.40	1.00
DAM3-C-B3-S-817	Lean Concrete Below Grade Beams	2	4,431.19	25-Apr-26	26-Apr-26	14-Jun-26	14-Jun-26	4,431.19	4,431.19	1.00
DAM3-C-B3-S-867	Rebar for Grade Beams	5	27,194.46	27-Apr-26	02-May-26	16-Jun-26	20-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B3-S-877	Formwork for Grade Beams	2	6,798.61	03-May-26	04-May-26	18-Jun-26	22-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B3-S-1027	Anchor bolts installation	2	57,238.83	03-May-26	04-May-26	18-Jun-26	20-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B3-S-827	Pouring Concrete for Grade Beams	1	33,993.09	05-May-26	05-May-26	24-Jun-26	24-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B3-S-977	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	06-May-26	11-May-26	27-Jun-26	30-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		95	397,232.98	12-May-26	18-Jul-26	06-Jul-26		397,232.98	396,325.87	1.00
DAM3-C-B3-S-1007	Backfilling / Compaction for Slab on Grade	7	23,023.09	12-May-26	19-May-26	06-Jul-26	09-Jul-26	23,023.09	23,023.09	1.00
DAM3-C-B3-S-957	Anti Termite Treatment below Ground Slab	1	15,874.08	20-May-26	20-May-26	11-Aug-26	15-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B3-S-987	Vapour barrier for below Ground Slab	2	13,233.49	21-May-26	23-May-26	11-Aug-26	15-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B3-S-837	Pouring Concrete for Ground Slab	4	344,195.21	24-May-26	31-May-26	11-Aug-26	15-Aug-26	344,195.21	344,195.21	1.00
DAM3-C-B3-S-1017	Concrete pad	7	907.11	11-Jul-26	18-Jul-26			907.11	0.00	0.00
COLUMNS & BEAMS		59	101,966.98	20-May-26	20-Jun-26	16-Jun-26	05-Oct-26	101,966.98	101,966.98	1.00
DAM3-C-B3-S-5101	Rebar for column	5	20,144.05	20-May-26	25-May-26	22-Jul-26	25-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B3-S-5102	Formwork for column	4	5,036.01	30-May-26	02-Jun-26	27-Jul-26	02-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B3-S-5103	Pouring Concrete for column	1	25,180.06	03-Jun-26	03-Jun-26	29-Jul-26	03-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B3-S-6101	Rebar for Tie Beams	4	7,263.64	04-Jun-26	08-Jun-26	16-Jun-26	20-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B3-S-6102	Formwork for Tie Beams	2	1,815.91	09-Jun-26	10-Jun-26	18-Jun-26	22-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B3-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	11-Jun-26	11-Jun-26	24-Jun-26	24-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B3-S-6113	Rebar for Beams	4	13,379.11	13-Jun-26	16-Jun-26	08-Sep-26	15-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B3-S-6123	Formwork for Beams	2	3,344.77	17-Jun-26	18-Jun-26	23-Sep-26	29-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B3-S-6133	Pouring Concrete for Beams	1	16,723.88	20-Jun-26	20-Jun-26	26-Sep-26	05-Oct-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		84	1,566,668.48	07-Jun-26	15-Jul-26	15-Jul-26		1,566,668.48	1,300,069.25	0.83
DAM3-C-B3-A-210	Installation of columns	3	217,507.55	07-Jun-26	09-Jun-26	15-Jul-26	15-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B3-A-220	Installation of raft and purlins	5	326,261.32	10-Jun-26	15-Jun-26	15-Jul-26	16-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B3-A-1430	Intumescent paint to steel works	7	317,759.56	16-Jun-26	23-Jun-26	25-Jul-26	29-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B3-A-1440	Steel members for office area	7	115,805.20	24-Jun-26	01-Jul-26	07-Oct-26		115,805.20	57,902.60	0.50

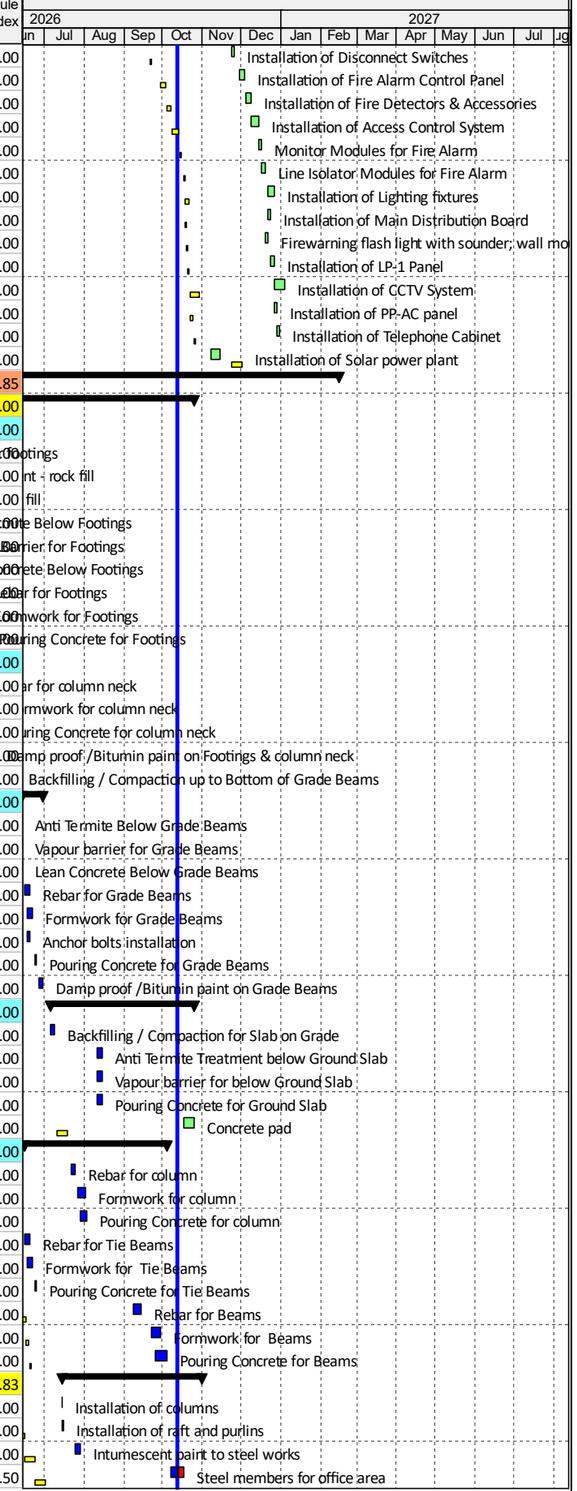

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B3-A-250	Installation of roof sheet	5	217,507.55	02-Jul-26	07-Jul-26	16-Aug-26	23-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B3-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	02-Jul-26	09-Jul-26			23,161.04	0.00	0.00
DAM3-C-B3-SS-1030	Steel members for external platform	7	18,670.78	02-Jul-26	09-Jul-26			18,670.78	0.00	0.00
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	326,261.32	11-Jul-26	15-Jul-26	12-Oct-26		326,261.32	163,130.66	0.50
DAM3-C-B3-SS-1040	Epoxy paint for external platform	5	3,734.16	11-Jul-26	15-Jul-26			3,734.16	0.00	0.00
ARCHITECTURAL		145	900,244.66	21-Jun-26	20-Dec-26	18-Aug-26		427,529.16	97,556.91	0.23
MASONARY WORKS		25	78,954.21	21-Jun-26	18-Jul-26	24-Aug-26	09-Sep-26	78,954.21	78,954.21	1.00
DAM3-C-B3-A-230	Block work at factory area	10	58,338.72	21-Jun-26	01-Jul-26	24-Aug-26	01-Sep-26	58,338.72	58,338.72	1.00
DAM3-C-B3-A-260	Block work at office area	7	6,179.18	02-Jul-26	09-Jul-26	25-Aug-26	09-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B3-A-1030	Block work at toilet area	7	14,436.31	11-Jul-26	18-Jul-26	25-Aug-26	03-Sep-26	14,436.31	14,436.31	1.00
WALL FINISHES		70	92,757.47	28-Jul-26	19-Nov-26	12-Oct-26		48,590.16	12,147.54	0.25
DAM3-C-B3-A-1040	Internal Wall Plaster	10	48,590.16	28-Jul-26	13-Aug-26	12-Oct-26		48,590.16	12,147.54	0.25
DAM3-C-B3-A-1090	Paint to Plaster (Primer, Putty & First Coat)	2	44,167.30	12-Nov-26	19-Nov-26			0.00	0.00	0.00
CIELING FINISHES		5	46,792.30	04-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1100	Installation of Ceiling Gypsum Board	5	46,792.30	04-Nov-26	09-Nov-26			0.00	0.00	0.00
FLOOR FINISHES		80	189,488.90	19-Aug-26	20-Dec-26			46,530.71	0.00	0.00
DAM3-C-B3-A-1080	Tiles for Toilet	7	46,530.71	19-Aug-26	26-Aug-26			46,530.71	0.00	0.00
DAM3-C-B3-A-1110	Tiles for Office Area	2	26,867.31	10-Nov-26	11-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1240	Granite strip	2	671.12	12-Nov-26	14-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1260	Epoxy paint	3	115,419.76	13-Dec-26	20-Dec-26			0.00	0.00	0.00
DOORS & WINDOWS		14	248,575.06	16-Jul-26	01-Aug-26			248,575.06	0.00	0.00
DAM3-C-B3-A-1420	Window (CW1)	7	94,173.21	16-Jul-26	23-Jul-26			94,173.21	0.00	0.00
DAM3-C-B3-A-1050	Roll up Shutter Door	1	68,619.20	25-Jul-26	25-Jul-26			68,619.20	0.00	0.00
DAM3-C-B3-A-1060	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	26-Jul-26	26-Jul-26			16,016.16	0.00	0.00
DAM3-C-B3-A-1120	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	27-Jul-26	27-Jul-26			22,737.85	0.00	0.00
DAM3-C-B3-A-1130	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	28-Jul-26	28-Jul-26			7,811.07	0.00	0.00
DAM3-C-B3-A-1350	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	29-Jul-26	29-Jul-26			16,016.16	0.00	0.00
DAM3-C-B3-A-1360	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	30-Jul-26	30-Jul-26			16,711.52	0.00	0.00
DAM3-C-B3-A-1370	Skylight fixtures installation	1	6,489.89	01-Aug-26	01-Aug-26			6,489.89	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	15-Aug-26	18-Aug-26			4,879.02	0.00	0.00
DAM3-C-B3-A-1220	Waterproofing membrane for toilets	4	4,879.02	15-Aug-26	18-Aug-26			4,879.02	0.00	0.00
METAL WORKS		21	193,717.06	15-Nov-26	29-Nov-26	18-Aug-26		0.00	6,455.16	0.00
DAM3-C-B3-A-1150	Steel Ladder	2	9,839.16	15-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1250	Steel railing works	4	1,533.98	17-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1170	Aluminium composite panel	5	175,888.76	22-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B3-A-1160	Galvanised Steel Gratings	2	6,455.16	28-Nov-26	29-Nov-26	18-Aug-26	18-Aug-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	30-Nov-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-B3-A-1180	Installation of fittings	3	22,981.27	30-Nov-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B3-A-1410	Identification sign; ID01 & ID02	3	9,630.56	08-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B3-A-1200	Furniture Installation	1	12,468.83	12-Dec-26	12-Dec-26			0.00	0.00	0.00
MECHANICAL		162	467,522.66	12-May-26	09-Dec-26	30-Jul-26		90,009.74	156,280.78	1.74
HVAC		14	233,183.33	21-Nov-26	06-Dec-26			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	28-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-760	Installation of HVAC Ducts	2	149,489.33	28-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B3-M-790	Installation of Duct insulation	2	21,205.40	30-Nov-26	01-Dec-26			0.00	0.00	0.00
SECOND STAGE		14	62,488.60	21-Nov-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-750	Installation of Exhaust Fans	2	7,938.56	21-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-B3-M-780	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	23-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B3-M-770	Installation of Diffuser	2	2,144.00	02-Dec-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-960	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	05-Dec-26	06-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		25	102,458.78	21-Nov-26	09-Dec-26	21-Sep-26		0.00	84,594.16	0.00
FIRST STAGE		12	84,594.16	21-Nov-26	03-Dec-26	21-Sep-26	28-Sep-26	0.00	84,594.16	0.00
DAM3-C-B3-M-920	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	21-Nov-26	28-Nov-26	21-Sep-26	28-Sep-26	0.00	72,394.75	0.00
DAM3-C-B3-M-930	Installation of Fire Fighting Valve	5	12,199.40	29-Nov-26	03-Dec-26	22-Sep-26	28-Sep-26	0.00	12,199.40	0.00
SECOND STAGE		17	17,864.62	05-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-940	Installation of Fire Hose Cabinet	3	15,158.56	05-Dec-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-990	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	07-Dec-26	09-Dec-26			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		110	90,009.74	12-May-26	20-Sep-26	30-Jul-26		90,009.74	30,093.94	0.33
FIRST STAGE		96	41,149.90	12-May-26	03-Sep-26	30-Jul-26		41,149.90	30,093.94	0.73
DAM3-C-B3-M-820	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	12-May-26	16-May-26	30-Jul-26	03-Aug-26	18,585.14	18,585.14	1.00
DAM3-C-B3-M-840	Installation of Floor Drain	2	11,055.96	27-Aug-26	29-Aug-26			11,055.96	0.00	0.00
DAM3-C-B3-M-1000	Installation of Trench drain	5	11,508.80	30-Aug-26	03-Sep-26	08-Aug-26	09-Aug-26	11,508.80	11,508.80	1.00

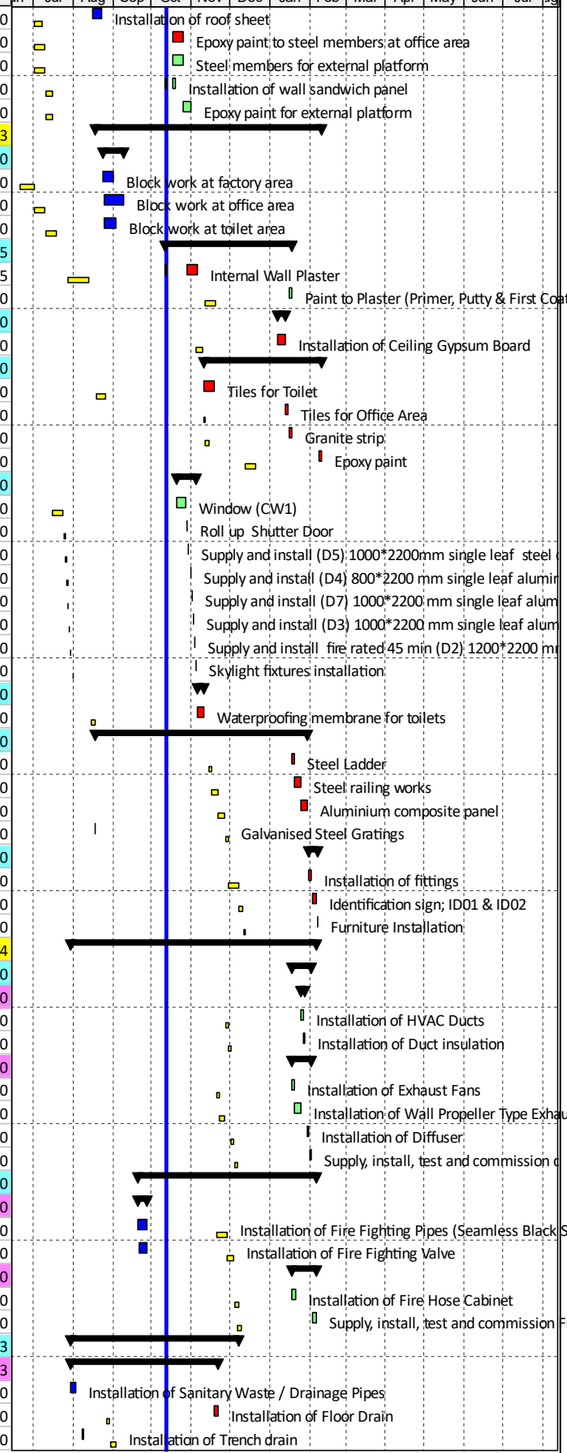


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
SECOND STAGE		14	48,859.84	05-Sep-26	20-Sep-26			48,859.84	0.00	0.00
DAM3-C-B3-M-800	Installation of Electric Water Heater	2	1,819.51	05-Sep-26	06-Sep-26			1,819.51	0.00	0.00
DAM3-C-B3-M-810	Installation of Sanitary Fixture and Accessories	4	19,921.72	07-Sep-26	10-Sep-26			19,921.72	0.00	0.00
DAM3-C-B3-M-830	Installation of Lavotary /Wash Basin	2	21,416.68	12-Sep-26	13-Sep-26			21,416.68	0.00	0.00
DAM3-C-B3-M-890	Installation of Bib Tap	2	1,900.66	14-Sep-26	15-Sep-26			1,900.66	0.00	0.00
DAM3-C-B3-M-850	Installation of Water Tap	2	2,874.14	16-Sep-26	17-Sep-26			2,874.14	0.00	0.00
DAM3-C-B3-M-860	Installation of Roof Vent Cap	2	927.12	19-Sep-26	20-Sep-26			927.12	0.00	0.00
WATER SUPPLY SYSTEM		7	41,870.81	21-Nov-26	02-Dec-26	01-Oct-26		0.00	41,592.68	0.00
FIRST STAGE		6	41,592.68	21-Nov-26	26-Nov-26	01-Oct-26	04-Oct-26	0.00	41,592.68	0.00
DAM3-C-B3-M-910	Installation of Water Supply Pipes	4	23,318.41	21-Nov-26	24-Nov-26	01-Oct-26	04-Oct-26	0.00	23,318.41	0.00
DAM3-C-B3-M-900	Installation of Water Supply Valve	2	18,274.27	25-Nov-26	26-Nov-26	01-Oct-26	04-Oct-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	28-Nov-26	02-Dec-26			0.00	0.00	0.00
DAM3-C-B3-M-950	Capped connection	5	278.13	28-Nov-26	02-Dec-26			0.00	0.00	0.00
ELECTRICAL		166	752,044.76	19-Jul-26	28-Dec-26	17-Jun-26		2,920.45	27,642.87	9.47
FIRST STAGE		166	86,114.12	19-Jul-26	24-Dec-26	17-Jun-26		2,920.45	27,642.87	9.47
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	2,920.45	19-Jul-26	27-Jul-26	17-Jun-26		2,920.45	1,460.23	0.50
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	28-Nov-26	01-Dec-26	21-Jul-26		0.00	884.15	0.00
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	8,462.97	12-Dec-26	15-Dec-26	23-Sep-26		0.00	7,616.67	0.00
DAM3-C-B3-E-693	Installation of Wires	2	16,925.94	16-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	19,646.47	21-Dec-26	24-Dec-26	17-Jun-26		0.00	17,681.82	0.00
DAM3-C-B3-E-683	Installation of LV Cables	4	36,389.98	21-Dec-26	24-Dec-26			0.00	0.00	0.00
SECOND STAGE		80	665,930.64	21-Nov-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-633	Installation of Wiring Devices	4	19,435.09	21-Nov-26	24-Nov-26			0.00	0.00	0.00
DAM3-C-B3-E-663	Installation of Disconnect Switches	2	30,235.95	25-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B3-E-583	Installation of Fire Alarm Control Panel	4	19,451.37	02-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-1040	Installation of Solar power plant	7	253,268.71	02-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-593	Installation of Fire Detectors & Accessories	4	56,740.37	07-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-733	Installation of Access Control System	3	27,616.86	12-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-743	Monitor Modules for Fire Alarm	2	3,882.38	17-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-753	Line Isolator Modules for Fire Alarm	2	185.40	20-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-613	Installation of Lighting fixtures	4	76,166.74	21-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-653	Installation of Main Distribution Board	2	32,472.73	21-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-763	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	22-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-1030	Installation of CCTV System	3	76,349.24	23-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-703	Installation of LP-1 Panel	2	18,403.54	23-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-713	Installation of PP-AC panel	2	21,648.48	23-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B3-E-673	Installation of Telephone Cabinet	2	26,991.08	26-Dec-26	27-Dec-26			0.00	0.00	0.00
BLOCK B2		273	5,075,523.09	08-Mar-26	02-Jan-27	17-Feb-26		3,318,512.94	2,772,947.04	0.84
STRUCTURAL		199	1,389,042.53	08-Mar-26	29-Sep-26	17-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		43	597,655.16	08-Mar-26	08-Apr-26	17-Feb-26	13-May-26	597,655.16	597,655.16	1.00
DAM3-C-B2-S-150	Excavation for footings	4	89,859.61	08-Mar-26	11-Mar-26	17-Feb-26	24-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B2-S-6223	Soil replacement - rock fill	4	179,061.91	12-Mar-26	16-Mar-26	17-Mar-26	24-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B2-S-6233	Engineering fill	4	46,046.19	21-Mar-26	24-Mar-26	28-Mar-26	06-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B2-S-101	Anti Termite Below Footings	1	11,905.55	25-Mar-26	25-Mar-26	13-Apr-26	13-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B2-S-102	Vapour Barrier for Footings	1	7,940.10	26-Mar-26	26-Mar-26	13-Apr-26	13-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B2-S-103	Lean Concrete Below Footings	2	8,229.34	28-Mar-26	29-Mar-26	13-Apr-26	13-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B2-S-104	Rebar for Footings	4	101,844.98	30-Mar-26	02-Apr-26	06-May-26	11-May-26	101,844.98	101,844.98	1.00
DAM3-C-B2-S-105	Formwork for Footings	4	25,461.25	04-Apr-26	07-Apr-26	10-May-26	12-May-26	25,461.25	25,461.25	1.00
DAM3-C-B2-S-106	Pouring Concrete for Footings	1	127,306.23	08-Apr-26	08-Apr-26	13-May-26	13-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		16	120,554.54	09-Apr-26	27-Apr-26	10-May-26	09-Jun-26	120,554.54	120,554.54	1.00
DAM3-C-B2-S-257	Rebar for column neck	4	14,919.19	09-Apr-26	13-Apr-26	10-May-26	12-May-26	14,919.19	14,919.19	1.00
DAM3-C-B2-S-267	Formwork for column neck	2	9,946.13	14-Apr-26	15-Apr-26	14-May-26	16-May-26	9,946.13	9,946.13	1.00
DAM3-C-B2-S-297	Pouring Concrete for column neck	1	24,865.31	16-Apr-26	16-Apr-26	17-May-26	18-May-26	24,865.31	24,865.31	1.00
DAM3-C-B2-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	18-Apr-26	19-Apr-26	19-May-26	20-May-26	24,777.73	24,777.73	1.00
DAM3-C-B2-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	20-Apr-26	27-Apr-26	24-May-26	09-Jun-26	46,046.19	46,046.19	1.00
GRADE BEAM		16	171,632.86	28-Apr-26	18-May-26	13-Jun-26	25-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B2-S-527	Anti Termite Below Grade Beams	1	11,905.55	28-Apr-26	28-Apr-26	13-Jun-26	13-Jun-26	11,905.55	11,905.55	1.00
DAM3-C-B2-S-337	Vapour barrier for Grade Beams	2	5,293.40	29-Apr-26	30-Apr-26	13-Jun-26	13-Jun-26	5,293.40	5,293.40	1.00
DAM3-C-B2-S-338	Lean Concrete Below Grade Beams	2	4,431.19	02-May-26	03-May-26	13-Jun-26	13-Jun-26	4,431.19	4,431.19	1.00
DAM3-C-B2-S-339	Rebar for Grade Beams	5	27,194.46	04-May-26	09-May-26	15-Jun-26	18-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B2-S-340	Formwork for Grade Beams	2	6,798.61	10-May-26	11-May-26	17-Jun-26	21-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B2-S-341	Anchor bolts installation	2	57,238.83	10-May-26	11-May-26	18-Jun-26	20-Jun-26	57,238.83	57,238.83	1.00

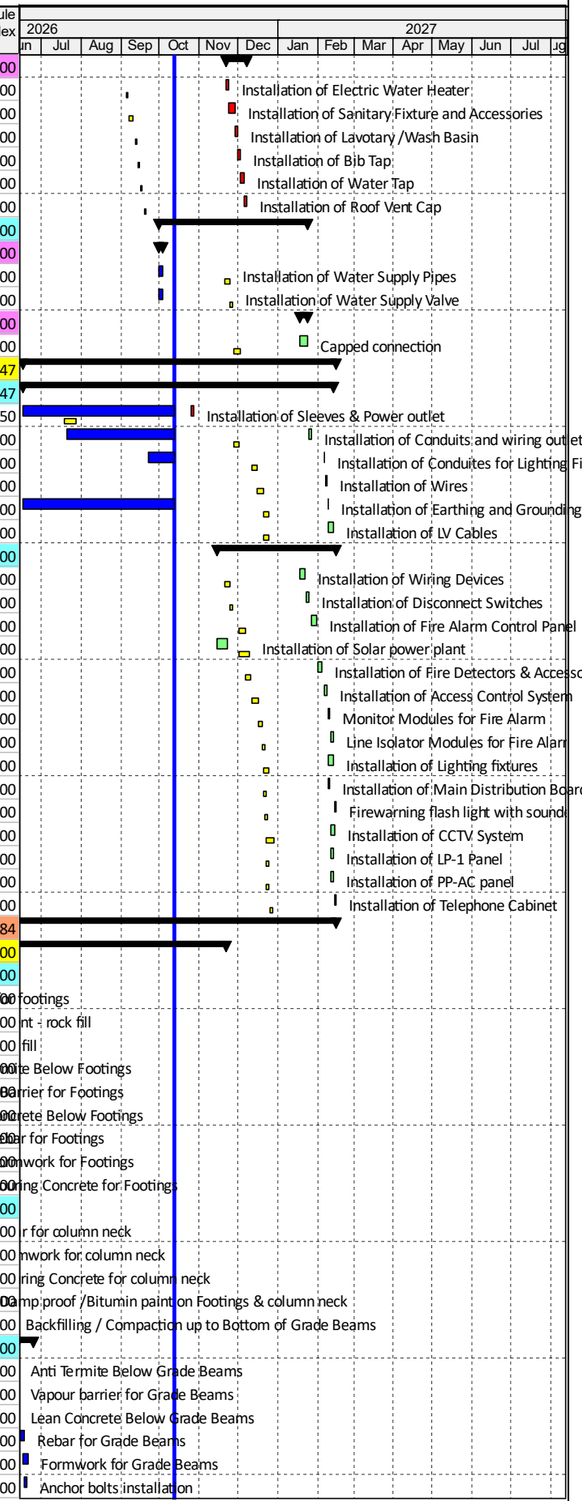

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B2-S-342	Pouring Concrete for Grade Beams	1	33,993.09	12-May-26	12-May-26	22-Jun-26	22-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B2-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	13-May-26	18-May-26	24-Jun-26	25-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		120	397,232.98	19-May-26	29-Sep-26	02-Jul-26		397,232.98	396,325.87	1.00
DAM3-C-B2-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	19-May-26	30-May-26	02-Jul-26	06-Jul-26	23,023.09	23,023.09	1.00
DAM3-C-B2-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	04-Jun-26	04-Jun-26	09-Aug-26	10-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B2-S-379	Vapour barrier for below Ground Slab	2	13,233.49	06-Jun-26	07-Jun-26	09-Aug-26	10-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B2-S-382	Pouring Concrete for Ground Slab	4	344,195.21	25-Jul-26	29-Jul-26	09-Aug-26	10-Aug-26	344,195.21	344,195.21	1.00
DAM3-C-B2-S-517	Concrete pad	7	907.11	20-Sep-26	29-Sep-26			907.11	0.00	0.00
COLUMNS & BEAMS		66	101,966.98	31-May-26	29-Jun-26	15-Jun-26	04-Oct-26	101,966.98	101,966.98	1.00
DAM3-C-B2-S-5101	Rebar for column	5	20,144.05	31-May-26	04-Jun-26	22-Jul-26	30-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B2-S-5102	Formwork for column	4	5,036.01	06-Jun-26	09-Jun-26	11-Aug-26	18-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B2-S-5103	Pouring Concrete for column	1	25,180.06	10-Jun-26	10-Jun-26	13-Aug-26	22-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B2-S-6101	Rebar for Tie Beams	4	7,263.64	11-Jun-26	15-Jun-26	15-Jun-26	18-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B2-S-6102	Formwork for Tie Beams	2	1,815.91	16-Jun-26	17-Jun-26	17-Jun-26	21-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B2-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	21-Jun-26	21-Jun-26	22-Jun-26	22-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B2-S-6113	Rebar for Beams	4	13,379.11	22-Jun-26	25-Jun-26	17-Sep-26	20-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B2-S-6123	Formwork for Beams	2	3,344.77	27-Jun-26	28-Jun-26	28-Sep-26	01-Oct-26	3,344.77	3,344.77	1.00
DAM3-C-B2-S-6133	Pouring Concrete for Beams	1	16,723.88	29-Jun-26	29-Jun-26	03-Oct-26	04-Oct-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		57	1,566,668.48	08-Aug-26	01-Oct-26	12-Jul-26		1,566,668.48	1,079,035.98	0.69
DAM3-C-B2-SS-0100	Installation of columns	3	217,507.55	08-Aug-26	10-Aug-26	12-Jul-26	13-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B2-SS-0110	Installation of raft and purlins	5	326,261.32	11-Aug-26	16-Aug-26	12-Jul-26	14-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B2-SS-610	Intumescent paint to steel works	7	317,759.56	26-Aug-26	03-Sep-26	30-Jul-26	01-Aug-26	317,759.56	317,759.56	1.00
DAM3-C-B2-SS-0140	Installation of roof sheet	5	217,507.55	03-Sep-26	09-Sep-26	06-Aug-26	13-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B2-SS-620	Steel members for office area	7	115,805.20	03-Sep-26	12-Sep-26			115,805.20	0.00	0.00
DAM3-C-B2-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	12-Sep-26	20-Sep-26			23,161.04	0.00	0.00
DAM3-C-B2-SS-1030	Steel members for external platform	7	18,670.78	12-Sep-26	20-Sep-26			18,670.78	0.00	0.00
DAM3-C-B2-SS-1040	Epoxy paint for external platform	5	3,734.16	20-Sep-26	27-Sep-26			3,734.16	0.00	0.00
DAM3-C-B2-SS-0130	Installation of wall sandwich panel	5	326,261.32	26-Sep-26	01-Oct-26			326,261.32	0.00	0.00
ARCHITECTURAL		97	900,244.66	17-Aug-26	02-Jan-27	12-Aug-26		273,975.11	121,851.99	0.44
MASONARY WORKS		19	78,954.21	17-Aug-26	29-Sep-26	22-Aug-26	27-Sep-26	78,954.21	78,954.21	1.00
DAM3-C-B2-A-0120	Block work at factory area	8	58,338.72	17-Aug-26	27-Aug-26	22-Aug-26	25-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B2-A-0150	Block work at office area	7	6,179.18	12-Sep-26	20-Sep-26	22-Aug-26	08-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B2-A-170	Block work at toilet area	7	14,436.31	20-Sep-26	29-Sep-26	22-Aug-26	27-Sep-26	14,436.31	14,436.31	1.00
WALL FINISHES		22	92,757.47	08-Oct-26	24-Nov-26	04-Oct-26		10,527.87	36,442.62	3.46
DAM3-C-B2-A-180	Internal Wall Plaster	15	48,590.16	08-Oct-26	26-Oct-26	04-Oct-26		10,527.87	36,442.62	3.46
DAM3-C-B2-A-230	Paint to Plaster (Primer, Putty & First Coat)	7	44,167.30	16-Nov-26	24-Nov-26			0.00	0.00	0.00
CIELING FINISHES		5	46,792.30	08-Nov-26	14-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-240	Installation of Ceiling Gypsum Board	5	46,792.30	08-Nov-26	14-Nov-26			0.00	0.00	0.00
FLOOR FINISHES		69	189,488.90	31-Oct-26	02-Jan-27			0.00	0.00	0.00
DAM3-C-B2-A-220	Tiles for Toilet	7	46,530.71	31-Oct-26	08-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-250	Tiles for Office Area	2	26,867.31	14-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-390	Granite strip	2	671.12	16-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-420	Epoxy paint	3	115,419.76	22-Dec-26	02-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		12	248,575.06	01-Oct-26	18-Oct-26			184,493.03	0.00	0.00
DAM3-C-B2-A-552	Window (CW1)	5	94,173.21	01-Oct-26	10-Oct-26			94,173.21	0.00	0.00
DAM3-C-B2-A-553	Roll up Shutter Door	1	68,619.20	10-Oct-26	11-Oct-26			68,619.20	0.00	0.00
DAM3-C-B2-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	11-Oct-26	12-Oct-26			16,016.16	0.00	0.00
DAM3-C-B2-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	12-Oct-26	13-Oct-26			5,684.46	0.00	0.00
DAM3-C-B2-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	13-Oct-26	14-Oct-26			0.00	0.00	0.00
DAM3-C-B2-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	14-Oct-26	15-Oct-26			0.00	0.00	0.00
DAM3-C-B2-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	15-Oct-26	17-Oct-26			0.00	0.00	0.00
DAM3-C-B2-A-558	Skylight fixtures installation	1	6,489.89	17-Oct-26	18-Oct-26			0.00	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	26-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B2-A-370	Waterproofing membrane for toilets	4	4,879.02	26-Oct-26	31-Oct-26			0.00	0.00	0.00
METAL WORKS		30	193,717.06	18-Nov-26	03-Dec-26	12-Aug-26		0.00	6,455.16	0.00
DAM3-C-B2-A-290	Steel Ladder	2	9,839.16	18-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-291	Steel railing works	4	1,533.98	21-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-B2-A-292	Aluminium composite panel	5	175,888.76	25-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B2-A-300	Galvanised Steel Gratings	2	6,455.16	01-Dec-26	03-Dec-26	12-Aug-26	12-Aug-26	0.00	6,455.16	0.00
SPECIALTIES		39	45,080.66	03-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B2-A-320	Installation of fittings	5	22,981.27	03-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B2-A-570	Identification sign; ID01 & ID02	3	9,630.56	09-Dec-26	13-Dec-26			0.00	0.00	0.00

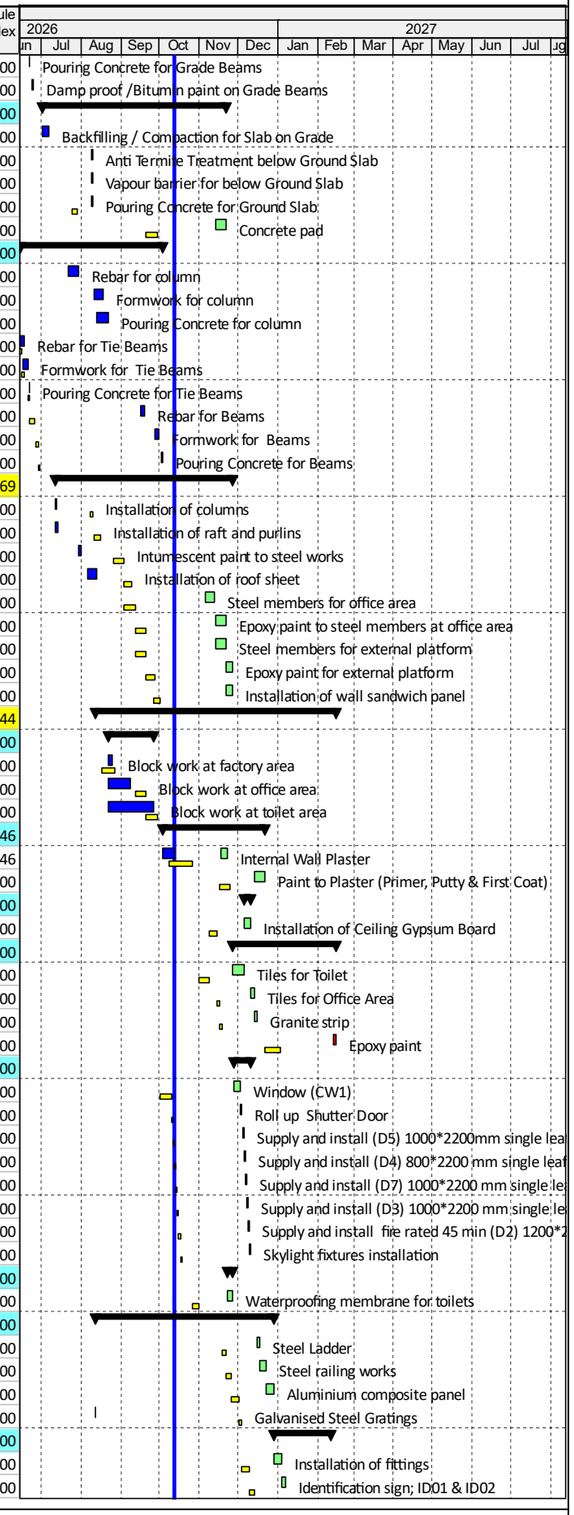


Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

TASK filter: All Activities

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B2-A-340	Furniture Installation	1	12,468.83	21-Dec-26	21-Dec-26			0.00	0.00	0.00
MECHANICAL		147	467,522.66	19-May-26	14-Dec-26	23-Jul-26		18,585.14	156,280.78	8.41
HVAC		14	233,183.33	24-Nov-26	10-Dec-26			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	01-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-140	Installation of HVAC Ducts	2	149,489.33	01-Dec-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-170	Installation of Duct insulation	2	21,205.40	03-Dec-26	06-Dec-26			0.00	0.00	0.00
SECOND STAGE		14	62,488.60	24-Nov-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-130	Installation of Exhaust Fans	2	7,938.56	24-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-160	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	26-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-339	Installation of Diffuser	2	2,144.00	06-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	08-Dec-26	10-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		19	102,458.78	24-Nov-26	14-Dec-26	10-Sep-26		0.00	84,594.16	0.00
FIRST STAGE		12	84,594.16	24-Nov-26	08-Dec-26	10-Sep-26	21-Sep-26	0.00	84,594.16	0.00
DAM3-C-B2-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	24-Nov-26	02-Dec-26	10-Sep-26	21-Sep-26	0.00	72,394.75	0.00
DAM3-C-B2-M-310	Installation of Fire Fighting Valve	5	12,199.40	02-Dec-26	08-Dec-26	10-Sep-26	21-Sep-26	0.00	12,199.40	0.00
SECOND STAGE		17	17,864.62	08-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-320	Installation of Fire Hose Cabinet	3	15,158.56	08-Dec-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	10-Dec-26	14-Dec-26			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		130	90,009.74	19-May-26	02-Dec-26	23-Jul-26		18,585.14	30,093.94	1.62
FIRST STAGE		127	41,149.90	19-May-26	16-Nov-26	23-Jul-26		18,585.14	30,093.94	1.62
DAM3-C-B2-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	19-May-26	23-May-26	23-Jul-26	27-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B2-M-220	Installation of Floor Drain	2	11,055.96	08-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-380	Installation of Trench drain	5	11,508.80	10-Nov-26	16-Nov-26	03-Aug-26	04-Aug-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	16-Nov-26	02-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-180	Installation of Electric Water Heater	2	1,819.51	16-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	18-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	23-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-270	Installation of Bib Tap	2	1,900.66	25-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-428	Installation of Water Tap	2	2,874.14	28-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-B2-M-429	Installation of Roof Vent Cap	2	927.12	30-Nov-26	02-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		19	41,870.81	24-Nov-26	07-Dec-26	01-Oct-26		0.00	41,592.68	0.00
FIRST STAGE		6	41,592.68	24-Nov-26	01-Dec-26	01-Oct-26	04-Oct-26	0.00	41,592.68	0.00
DAM3-C-B2-M-290	Installation of Water Supply Pipes	4	23,318.41	24-Nov-26	29-Nov-26	01-Oct-26	04-Oct-26	0.00	23,318.41	0.00
DAM3-C-B2-M-280	Installation of Water Supply Valve	2	18,274.27	29-Nov-26	01-Dec-26	01-Oct-26	04-Oct-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	01-Dec-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B2-M-330	Capped connection	5	278.13	01-Dec-26	07-Dec-26			0.00	0.00	0.00
ELECTRICAL		65	752,044.76	29-Sep-26	21-Dec-26	17-Jun-26		70,241.68	27,642.87	0.39
FIRST STAGE		47	86,114.12	29-Sep-26	11-Nov-26	17-Jun-26		4,688.76	27,642.87	5.90
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	29-Sep-26	04-Oct-26	17-Jun-26		1,768.31	884.15	0.50
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	2,920.45	29-Sep-26	08-Oct-26	18-Jun-26		2,920.45	1,460.23	0.50
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	13-Oct-26	18-Oct-26	29-Sep-26		0.00	7,616.67	0.00
DAM3-C-B2-E-233	Installation of Wires	4	16,925.94	18-Oct-26	22-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-223	Installation of LV Cables	4	36,389.98	01-Nov-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	19,646.47	05-Nov-26	11-Nov-26	18-Jun-26		0.00	17,681.82	0.00
SECOND STAGE		49	665,930.64	04-Oct-26	21-Dec-26			65,552.92	0.00	0.00
DAM3-C-B2-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	04-Oct-26	08-Oct-26			19,451.37	0.00	0.00
DAM3-C-B2-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	08-Oct-26	13-Oct-26			46,101.55	0.00	0.00
DAM3-C-B2-E-153	Installation of Lighting fixtures	4	76,166.74	22-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-193	Installation of Main Distribution Board	2	32,472.73	22-Oct-26	25-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-410	Installation of CCTV System	6	76,349.24	22-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-243	Installation of LP-1 Panel	2	18,403.54	25-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-253	Installation of PP-AC panel	2	21,648.48	27-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B2-E-213	Installation of Telephone Cabinet	2	26,991.08	29-Oct-26	01-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-273	Installation of Access Control System	5	27,616.86	31-Oct-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-283	Monitor Modules for Fire Alarm	2	3,882.38	05-Nov-26	08-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-293	Line Isolator Modules for Fire Alarm	2	185.40	08-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	10-Nov-26	12-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-173	Installation of Wiring Devices	4	19,435.09	24-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B2-E-203	Installation of Disconnect Switches	2	30,235.95	29-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B2-E-420	Installation of Solar power plant	10	253,268.71	10-Dec-26	21-Dec-26			0.00	0.00	0.00
BLOCK B1		274	5,075,523.09	12-Mar-26	03-Jan-27	17-Mar-26		3,298,564.06	2,705,309.91	0.82
STRUCTURAL		198	1,389,042.53	12-Mar-26	21-Sep-26	17-Mar-26		1,389,042.53	1,388,135.41	1.00

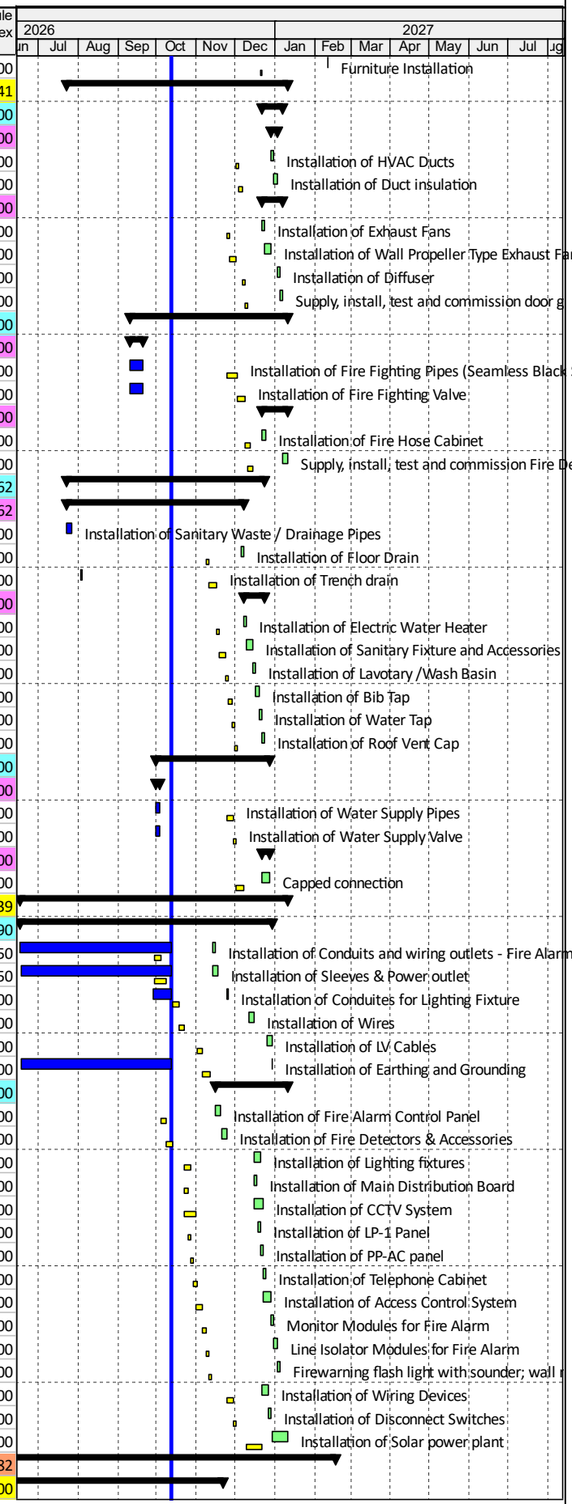

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
FOOTING		101	597,655.16	12-Mar-26	29-Apr-26	17-Mar-26	07-May-26	597,655.16	597,655.16	1.00
DAM3-C-B1-S-150	Excavation for footings	4	89,859.61	12-Mar-26	16-Mar-26	17-Mar-26	24-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B1-S-6243	Soil replacement - rock fill	4	179,061.91	21-Mar-26	24-Mar-26	17-Mar-26	24-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B1-S-6253	Engineering fill	4	46,046.19	25-Mar-26	29-Mar-26	07-Apr-26	13-Apr-26	46,046.19	46,046.19	1.00
DAM3-C-B1-S-101	Anti Termite Below Footings	1	11,905.55	30-Mar-26	30-Mar-26	25-Apr-26	25-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B1-S-102	Vapour Barrier for Footings	1	7,940.10	31-Mar-26	31-Mar-26	25-Apr-26	25-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B1-S-103	Lean Concrete Below Footings	2	8,229.34	13-Apr-26	14-Apr-26	25-Apr-26	25-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B1-S-104	Rebar for Footings	4	101,844.98	20-Apr-26	23-Apr-26	02-May-26	05-May-26	101,844.98	101,844.98	1.00
DAM3-C-B1-S-105	Formwork for Footings	4	25,461.25	25-Apr-26	28-Apr-26	05-May-26	06-May-26	25,461.25	25,461.25	1.00
DAM3-C-B1-S-106	Pouring Concrete for Footings	1	127,306.23	29-Apr-26	29-Apr-26	07-May-26	07-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		10	120,554.54	30-Apr-26	18-May-26	05-May-26	01-Jun-26	120,554.54	120,554.54	1.00
DAM3-C-B1-S-257	Rebar for column neck	4	14,919.19	30-Apr-26	04-May-26	05-May-26	06-May-26	14,919.19	14,919.19	1.00
DAM3-C-B1-S-267	Formwork for column neck	2	9,946.13	05-May-26	06-May-26	11-May-26	12-May-26	9,946.13	9,946.13	1.00
DAM3-C-B1-S-297	Pouring Concrete for column neck	1	24,865.31	07-May-26	07-May-26	13-May-26	13-May-26	24,865.31	24,865.31	1.00
DAM3-C-B1-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	09-May-26	10-May-26	16-May-26	17-May-26	24,777.73	24,777.73	1.00
DAM3-C-B1-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	11-May-26	18-May-26	21-May-26	01-Jun-26	46,046.19	46,046.19	1.00
GRADE BEAM		11	171,632.86	19-May-26	11-Jun-26	06-Jun-26	25-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B1-S-527	Anti Termite Below Grade Beams	1	11,905.55	19-May-26	19-May-26	06-Jun-26	06-Jun-26	11,905.55	11,905.55	1.00
DAM3-C-B1-S-337	Vapour barrier for Grade Beams	2	5,293.40	20-May-26	21-May-26	06-Jun-26	06-Jun-26	5,293.40	5,293.40	1.00
DAM3-C-B1-S-338	Lean Concrete Below Grade Beams	2	4,431.19	23-May-26	24-May-26	06-Jun-26	06-Jun-26	4,431.19	4,431.19	1.00
DAM3-C-B1-S-339	Rebar for Grade Beams	5	27,194.46	25-May-26	02-Jun-26	08-Jun-26	09-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B1-S-340	Formwork for Grade Beams	2	6,798.61	03-Jun-26	04-Jun-26	11-Jun-26	15-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B1-S-341	Anchor bolts installation	2	57,238.83	03-Jun-26	04-Jun-26	11-Jun-26	13-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B1-S-342	Pouring Concrete for Grade Beams	1	33,993.09	06-Jun-26	06-Jun-26	17-Jun-26	17-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B1-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	07-Jun-26	11-Jun-26	23-Jun-26	25-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		113	397,232.98	13-Jun-26	21-Sep-26	27-Jun-26		397,232.98	396,325.87	1.00
DAM3-C-B1-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	13-Jun-26	20-Jun-26	27-Jun-26	05-Jul-26	23,023.09	23,023.09	1.00
DAM3-C-B1-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	21-Jun-26	21-Jun-26	06-Aug-26	08-Aug-26	15,874.08	15,874.08	1.00
DAM3-C-B1-S-379	Vapour barrier for below Ground Slab	2	13,233.49	22-Jun-26	23-Jun-26	06-Aug-26	08-Aug-26	13,233.49	13,233.49	1.00
DAM3-C-B1-S-382	Pouring Concrete for Ground Slab	4	344,195.21	24-Jun-26	28-Jun-26	06-Aug-26	08-Aug-26	344,195.21	344,195.21	1.00
DAM3-C-B1-S-517	Concrete pad	7	907.11	14-Sep-26	21-Sep-26			907.11	0.00	0.00
COLUMNS & BEAMS		63	101,966.98	21-Jun-26	18-Jul-26	08-Jun-26	10-Oct-26	101,966.98	101,966.98	1.00
DAM3-C-B1-S-5101	Rebar for column	5	20,144.05	21-Jun-26	25-Jun-26	26-Jul-26	28-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B1-S-5102	Formwork for column	4	5,036.01	27-Jun-26	30-Jun-26	22-Aug-26	27-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B1-S-5103	Pouring Concrete for column	1	25,180.06	01-Jul-26	01-Jul-26	25-Aug-26	29-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B1-S-6101	Rebar for Tie Beams	4	7,263.64	02-Jul-26	06-Jul-26	08-Jun-26	09-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B1-S-6102	Formwork for Tie Beams	2	1,815.91	07-Jul-26	08-Jul-26	11-Jun-26	15-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B1-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	09-Jul-26	09-Jul-26	17-Jun-26	17-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B1-S-6113	Rebar for Beams	4	13,379.11	11-Jul-26	14-Jul-26	27-Sep-26	04-Oct-26	13,379.11	13,379.11	1.00
DAM3-C-B1-S-6123	Formwork for Beams	2	3,344.77	15-Jul-26	16-Jul-26	29-Sep-26	06-Oct-26	3,344.77	3,344.77	1.00
DAM3-C-B1-S-6133	Pouring Concrete for Beams	1	16,723.88	18-Jul-26	18-Jul-26	07-Oct-26	10-Oct-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		54	1,566,668.48	11-Aug-26	19-Sep-26	11-Jul-26		1,566,668.48	1,079,035.98	0.69
DAM3-C-B1-SS-0100	Installation of columns	3	217,507.55	11-Aug-26	13-Aug-26	11-Jul-26	11-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B1-SS-0110	Installation of raft and purlins	5	326,261.32	15-Aug-26	19-Aug-26	11-Jul-26	13-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B1-SS-610	Intumescent paint to steel works	7	317,759.56	20-Aug-26	27-Aug-26	25-Jul-26	28-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B1-SS-620	Steel members for office area	7	115,805.20	29-Aug-26	05-Sep-26			115,805.20	0.00	0.00
DAM3-C-B1-SS-0140	Installation of roof sheet	5	217,507.55	01-Sep-26	06-Sep-26	04-Aug-26	11-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B1-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	06-Sep-26	13-Sep-26			23,161.04	0.00	0.00
DAM3-C-B1-SS-1030	Steel members for external platform	7	18,670.78	06-Sep-26	13-Sep-26			18,670.78	0.00	0.00
DAM3-C-B1-SS-0130	Installation of wall sandwich panel	5	326,261.32	14-Sep-26	19-Sep-26			326,261.32	0.00	0.00
DAM3-C-B1-SS-1040	Epoxy paint for external platform	5	3,734.16	14-Sep-26	19-Sep-26			3,734.16	0.00	0.00
ARCHITECTURAL		96	900,244.66	20-Aug-26	03-Jan-27	10-Aug-26		321,039.38	85,409.37	0.27
MASONARY WORKS		28	78,954.21	20-Aug-26	07-Oct-26	15-Aug-26	07-Sep-26	78,954.21	78,954.21	1.00
DAM3-C-B1-A-0120	Block work at factory area	10	58,338.72	20-Aug-26	31-Aug-26	15-Aug-26	23-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B1-A-0150	Block work at office area	7	6,179.18	06-Sep-26	13-Sep-26	23-Aug-26	06-Sep-26	6,179.18	6,179.18	1.00
DAM3-C-B1-A-170	Block work at toilet area	7	14,436.31	30-Sep-26	07-Oct-26	02-Sep-26	07-Sep-26	14,436.31	14,436.31	1.00
WALL FINISHES		41	92,757.47	18-Oct-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-180	Internal Wall Plaster	10	48,590.16	18-Oct-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-230	Paint to Plaster (Primer, Putty & First Coat)	3	44,167.30	29-Nov-26	06-Dec-26			0.00	0.00	0.00
CIELING FINISHES		3	46,792.30	21-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-240	Installation of Ceiling Gypsum Board	3	46,792.30	21-Nov-26	25-Nov-26			0.00	0.00	0.00
FLOOR FINISHES		47	189,488.90	11-Nov-26	03-Jan-27			0.00	0.00	0.00

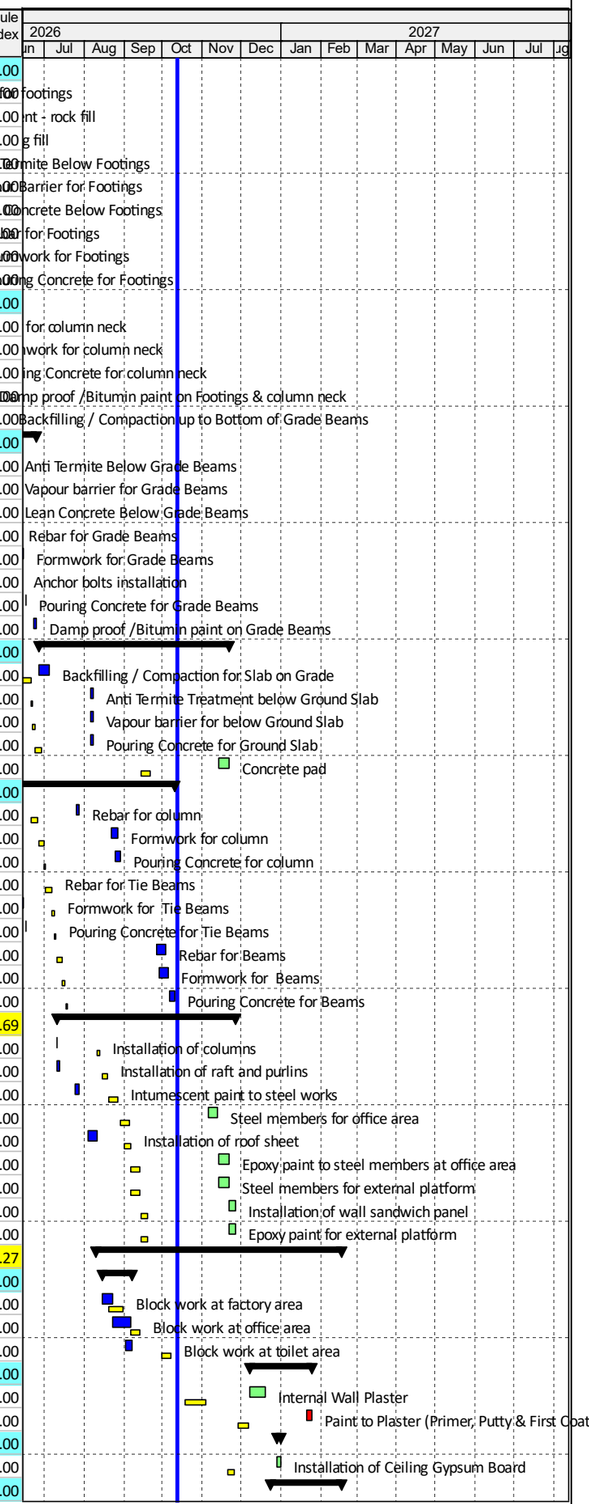

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B1-A-220	Tiles for Toilet	4	46,530.71	11-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-250	Tiles for Office Area	2	26,867.31	26-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-390	Granite strip	2	671.12	29-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-420	Epoxy paint	7	115,419.76	27-Dec-26	03-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		18	248,575.06	20-Sep-26	28-Oct-26			242,085.17	0.00	0.00
DAM3-C-B1-A-552	Window (CW1)	5	94,173.21	20-Sep-26	28-Sep-26			94,173.21	0.00	0.00
DAM3-C-B1-A-553	Roll up Shutter Door	1	68,619.20	29-Sep-26	29-Sep-26			68,619.20	0.00	0.00
DAM3-C-B1-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	30-Sep-26	30-Sep-26			16,016.16	0.00	0.00
DAM3-C-B1-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	01-Oct-26	01-Oct-26			22,737.85	0.00	0.00
DAM3-C-B1-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	03-Oct-26	03-Oct-26			7,811.07	0.00	0.00
DAM3-C-B1-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	04-Oct-26	04-Oct-26			16,016.16	0.00	0.00
DAM3-C-B1-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	05-Oct-26	05-Oct-26			16,711.52	0.00	0.00
DAM3-C-B1-A-558	Skylight fixtures installation	1	6,489.89	27-Oct-26	28-Oct-26			0.00	0.00	0.00
WATER PROOFING WORKS		4	4,879.02	07-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B1-A-370	Waterproofing membrane for toilets	4	4,879.02	07-Nov-26	10-Nov-26			0.00	0.00	0.00
METAL WORKS		8	193,717.06	01-Dec-26	15-Dec-26	10-Aug-26		0.00	6,455.16	0.00
DAM3-C-B1-A-290	Steel Ladder	2	9,839.16	01-Dec-26	02-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-291	Steel railing works	2	1,533.98	03-Dec-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-292	Aluminium composite panel	3	175,888.76	08-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-300	Galvanised Steel Gratings	2	6,455.16	14-Dec-26	15-Dec-26	10-Aug-26	10-Aug-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	16-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-320	Installation of fittings	3	22,981.27	16-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-570	Identification sign; ID01 & ID02	3	9,630.56	22-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B1-A-340	Furniture Installation	1	12,468.83	26-Dec-26	26-Dec-26			0.00	0.00	0.00
MECHANICAL		175	467,522.66	13-Jun-26	26-Dec-26	18-Jul-26		18,585.14	125,086.27	6.73
HVAC		12	233,183.33	07-Dec-26	22-Dec-26			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	14-Dec-26	17-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-140	Installation of HVAC Ducts	2	149,489.33	14-Dec-26	15-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-170	Installation of Duct insulation	2	21,205.40	16-Dec-26	17-Dec-26			0.00	0.00	0.00
SECOND STAGE		12	62,488.60	07-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-130	Installation of Exhaust Fans	2	7,938.56	07-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-160	Installation of Wall Propeller Type Exhaust Fan	2	46,831.64	09-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-339	Installation of Diffuser	2	2,144.00	19-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	21-Dec-26	22-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		18	102,458.78	07-Dec-26	26-Dec-26	06-Sep-26		0.00	84,594.16	0.00
FIRST STAGE		10	84,594.16	07-Dec-26	20-Dec-26	06-Sep-26	09-Sep-26	0.00	84,594.16	0.00
DAM3-C-B1-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	07-Dec-26	14-Dec-26	06-Sep-26	09-Sep-26	0.00	72,394.75	0.00
DAM3-C-B1-M-310	Installation of Fire Fighting Valve	5	12,199.40	15-Dec-26	20-Dec-26	08-Sep-26	09-Sep-26	0.00	12,199.40	0.00
SECOND STAGE		15	17,864.62	21-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-320	Installation of Fire Hose Cabinet	3	15,158.56	21-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	23-Dec-26	26-Dec-26			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		153	90,009.74	13-Jun-26	13-Dec-26	18-Jul-26		18,585.14	30,093.94	1.62
FIRST STAGE		139	41,149.90	13-Jun-26	26-Nov-26	18-Jul-26		18,585.14	30,093.94	1.62
DAM3-C-B1-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	13-Jun-26	16-Jun-26	18-Jul-26	25-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B1-M-220	Installation of Floor Drain	2	11,055.96	19-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B1-M-380	Installation of Trench drain	5	11,508.80	22-Nov-26	26-Nov-26	19-Jul-26	25-Jul-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	28-Nov-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-180	Installation of Electric Water Heater	2	1,819.51	28-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B1-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	30-Nov-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	05-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-270	Installation of Bib Tap	2	1,900.66	07-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-428	Installation of Water Tap	2	2,874.14	09-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-429	Installation of Roof Vent Cap	2	927.12	12-Dec-26	13-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		10	41,870.81	07-Dec-26	19-Dec-26	13-Oct-26		0.00	10,398.17	0.00
FIRST STAGE		6	41,592.68	07-Dec-26	13-Dec-26	13-Oct-26		0.00	10,398.17	0.00
DAM3-C-B1-M-290	Installation of Water Supply Pipes	4	23,318.41	07-Dec-26	10-Dec-26	13-Oct-26		0.00	5,829.60	0.00
DAM3-C-B1-M-280	Installation of Water Supply Valve	2	18,274.27	12-Dec-26	13-Dec-26	13-Oct-26		0.00	4,568.57	0.00
SECOND STAGE		5	278.13	14-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B1-M-330	Capped connection	5	278.13	14-Dec-26	19-Dec-26			0.00	0.00	0.00
ELECTRICAL		73	752,044.76	08-Oct-26	29-Dec-26	08-Jun-26		3,228.53	27,642.87	8.56
FIRST STAGE		51	86,114.12	08-Oct-26	22-Nov-26	08-Jun-26		3,228.53	27,642.87	8.56
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	08-Oct-26	12-Oct-26	09-Jun-26		1,768.31	884.15	0.50

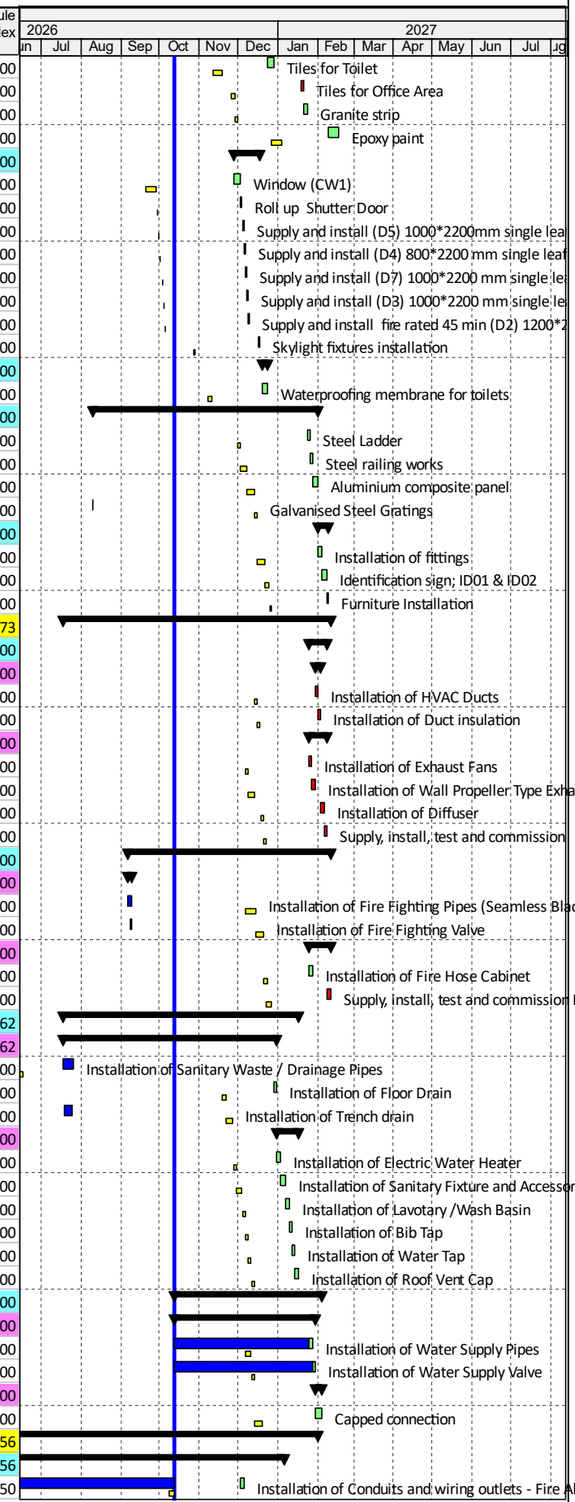

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	2,920.45	08-Oct-26	17-Oct-26	08-Jun-26		1,460.23	1,460.23	1.00
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	22-Oct-26	26-Oct-26	01-Oct-26		0.00	7,616.67	0.00
DAM3-C-B1-E-233	Installation of Wires	4	16,925.94	28-Oct-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-223	Installation of LV Cables	4	36,389.98	11-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	19,646.47	16-Nov-26	22-Nov-26	08-Jun-26		0.00	17,681.82	0.00
SECOND STAGE		49	665,930.64	13-Oct-26	29-Dec-26			0.00	0.00	0.00
DAM3-C-B1-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	13-Oct-26	17-Oct-26			0.00	0.00	0.00
DAM3-C-B1-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	18-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B1-E-153	Installation of Lighting fixtures	4	76,166.74	02-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-193	Installation of Main Distribution Board	2	32,472.73	02-Nov-26	04-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-410	Installation of CCTV System	7	76,349.24	02-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-243	Installation of LP-1 Panel	2	18,403.54	04-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-253	Installation of PP-AC panel	2	21,648.48	07-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-213	Installation of Telephone Cabinet	2	26,991.08	09-Nov-26	11-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-273	Installation of Access Control System	5	27,616.86	10-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-283	Monitor Modules for Fire Alarm	2	3,882.38	16-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-293	Line Isolator Modules for Fire Alarm	2	185.40	18-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	21-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B1-E-173	Installation of Wiring Devices	4	19,435.09	07-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B1-E-203	Installation of Disconnect Switches	2	30,235.95	12-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B1-E-420	Installation of Solar power plant	7	253,268.71	22-Dec-26	29-Dec-26			0.00	0.00	0.00
BLOCK B7		273	5,075,523.09	10-Feb-26	06-Jan-27	16-Feb-26		3,406,373.47	4,009,150.78	1.18
STRUCTURAL		206	1,389,042.53	10-Feb-26	26-Sep-26	16-Feb-26		1,389,042.53	1,388,135.41	1.00
FOOTING		32	597,655.16	10-Feb-26	25-Mar-26	16-Feb-26	11-Apr-26	597,655.16	597,655.16	1.00
DAM3-C-B7-S-150	Excavation for footings	8	89,859.61	10-Feb-26	19-Feb-26	16-Feb-26	19-Feb-26	89,859.61	89,859.61	1.00
DAM3-C-B7-S-6263	Soil replacement - rock fill	6	179,061.91	19-Feb-26	28-Feb-26	21-Feb-26	26-Feb-26	179,061.91	179,061.91	1.00
DAM3-C-B7-S-6273	Engineering fill	6	46,046.19	01-Mar-26	07-Mar-26	05-Mar-26	11-Mar-26	46,046.19	46,046.19	1.00
DAM3-C-B7-S-101	Anti Termite Below Footings	1	11,905.55	08-Mar-26	08-Mar-26	25-Mar-26	25-Mar-26	11,905.55	11,905.55	1.00
DAM3-C-B7-S-102	Vapour Barrier for Footings	1	7,940.10	09-Mar-26	09-Mar-26	25-Mar-26	25-Mar-26	7,940.10	7,940.10	1.00
DAM3-C-B7-S-103	Lean Concrete Below Footings	2	8,229.34	10-Mar-26	11-Mar-26	25-Mar-26	25-Mar-26	8,229.34	8,229.34	1.00
DAM3-C-B7-S-104	Rebar for Footings	4	101,844.98	12-Mar-26	16-Mar-26	05-Apr-26	09-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B7-S-105	Formwork for Footings	4	25,461.25	21-Mar-26	24-Mar-26	06-Apr-26	09-Apr-26	25,461.25	25,461.25	1.00
DAM3-C-B7-S-106	Pouring Concrete for Footings	1	127,306.23	25-Mar-26	25-Mar-26	11-Apr-26	11-Apr-26	127,306.23	127,306.23	1.00
COLUMN NECK		19	120,554.54	26-Mar-26	13-Apr-26	09-Apr-26	10-May-26	120,554.54	120,554.54	1.00
DAM3-C-B7-S-257	Rebar for column neck	4	14,919.19	26-Mar-26	30-Mar-26	09-Apr-26	11-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B7-S-267	Formwork for column neck	2	9,946.13	31-Mar-26	01-Apr-26	15-Apr-26	15-Apr-26	9,946.13	9,946.13	1.00
DAM3-C-B7-S-297	Pouring Concrete for column neck	1	24,865.31	02-Apr-26	02-Apr-26	16-Apr-26	16-Apr-26	24,865.31	24,865.31	1.00
DAM3-C-B7-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	04-Apr-26	05-Apr-26	20-Apr-26	23-Apr-26	24,777.73	24,777.73	1.00
DAM3-C-B7-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	06-Apr-26	13-Apr-26	02-May-26	10-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		14	171,632.86	14-Apr-26	04-May-26	13-May-26	31-May-26	171,632.86	171,632.86	1.00
DAM3-C-B7-S-527	Anti Termite Below Grade Beams	1	11,905.55	14-Apr-26	14-Apr-26	13-May-26	13-May-26	11,905.55	11,905.55	1.00
DAM3-C-B7-S-337	Vapour barrier for Grade Beams	2	5,293.40	15-Apr-26	16-Apr-26	13-May-26	13-May-26	5,293.40	5,293.40	1.00
DAM3-C-B7-S-338	Lean Concrete Below Grade Beams	2	4,431.19	18-Apr-26	19-Apr-26	13-May-26	13-May-26	4,431.19	4,431.19	1.00
DAM3-C-B7-S-339	Rebar for Grade Beams	5	27,194.46	20-Apr-26	25-Apr-26	16-May-26	18-May-26	27,194.46	27,194.46	1.00
DAM3-C-B7-S-340	Formwork for Grade Beams	2	6,798.61	26-Apr-26	27-Apr-26	18-May-26	19-May-26	6,798.61	6,798.61	1.00
DAM3-C-B7-S-341	Anchor bolts installation	2	57,238.83	26-Apr-26	27-Apr-26	16-May-26	18-May-26	57,238.83	57,238.83	1.00
DAM3-C-B7-S-342	Pouring Concrete for Grade Beams	1	33,993.09	28-Apr-26	28-Apr-26	20-May-26	20-May-26	33,993.09	33,993.09	1.00
DAM3-C-B7-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	29-Apr-26	04-May-26	23-May-26	31-May-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		137	397,232.98	05-May-26	26-Sep-26	01-Jun-26		397,232.98	396,325.87	1.00
DAM3-C-B7-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	05-May-26	12-May-26	01-Jun-26	08-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B7-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	13-May-26	13-May-26	08-Jul-26	12-Jul-26	15,874.08	15,874.08	1.00
DAM3-C-B7-S-379	Vapour barrier for below Ground Slab	2	13,233.49	14-May-26	16-May-26	08-Jul-26	12-Jul-26	13,233.49	13,233.49	1.00
DAM3-C-B7-S-382	Pouring Concrete for Ground Slab	4	344,195.21	17-May-26	20-May-26	08-Jul-26	12-Jul-26	344,195.21	344,195.21	1.00
DAM3-C-B7-S-517	Concrete pad	7	907.11	17-Sep-26	26-Sep-26			907.11	0.00	0.00
COLUMNS & BEAMS		58	101,966.98	13-May-26	13-Jun-26	11-May-26	29-Aug-26	101,966.98	101,966.98	1.00
DAM3-C-B7-S-5101	Rebar for column	5	20,144.05	13-May-26	18-May-26	25-Jun-26	02-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B7-S-5102	Formwork for column	4	5,036.01	19-May-26	23-May-26	01-Jun-26	07-Jul-26	5,036.01	5,036.01	1.00
DAM3-C-B7-S-5103	Pouring Concrete for column	1	25,180.06	24-May-26	24-May-26	05-Jul-26	22-Jul-26	25,180.06	25,180.06	1.00
DAM3-C-B7-S-6101	Rebar for Tie Beams	4	7,263.64	25-May-26	01-Jun-26	11-May-26	12-May-26	7,263.64	7,263.64	1.00
DAM3-C-B7-S-6102	Formwork for Tie Beams	2	1,815.91	02-Jun-26	03-Jun-26	13-May-26	13-May-26	1,815.91	1,815.91	1.00
DAM3-C-B7-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	04-Jun-26	04-Jun-26	14-May-26	14-May-26	9,079.54	9,079.54	1.00
DAM3-C-B7-S-6113	Rebar for Beams	4	13,379.11	06-Jun-26	09-Jun-26	16-Aug-26	19-Aug-26	13,379.11	13,379.11	1.00

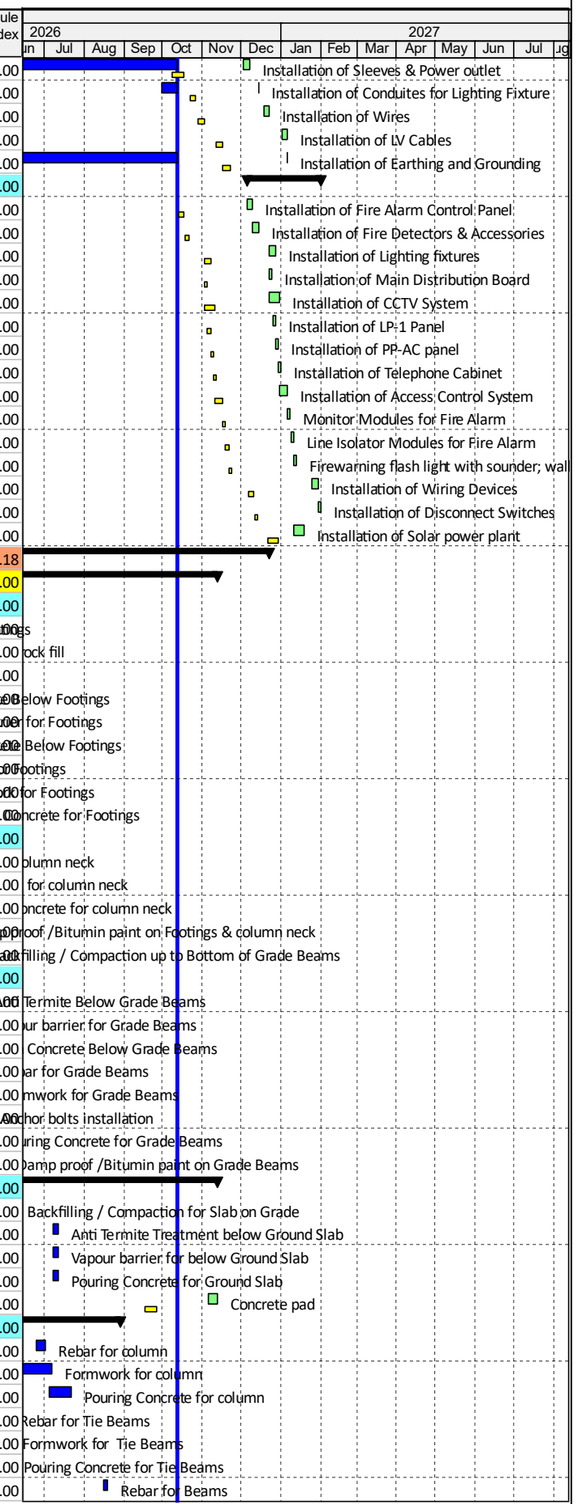

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B7-S-6123	Formwork for Beams	2	3,344.77	10-Jun-26	11-Jun-26	20-Aug-26	26-Aug-26	3,344.77	3,344.77	1.00
DAM3-C-B7-S-6133	Pouring Concrete for Beams	1	16,723.88	13-Jun-26	13-Jun-26	26-Aug-26	29-Aug-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		41	1,566,668.48	15-Aug-26	22-Sep-26	13-Jun-26		1,566,668.48	1,539,773.29	0.98
DAM3-C-B7-SS-0100	Installation of columns	3	217,507.55	15-Aug-26	17-Aug-26	13-Jun-26	13-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B7-SS-0110	Installation of raft and purlins	5	326,261.32	18-Aug-26	23-Aug-26	14-Jun-26	15-Jun-26	326,261.32	326,261.32	1.00
DAM3-C-B7-SS-610	Intumescent paint to steel works	7	317,759.56	24-Aug-26	31-Aug-26	14-Jun-26	21-Jun-26	317,759.56	317,759.56	1.00
DAM3-C-B7-SS-620	Steel members for office area	7	115,805.20	01-Sep-26	08-Sep-26	21-Sep-26	24-Sep-26	115,805.20	115,805.20	1.00
DAM3-C-B7-SS-0140	Installation of roof sheet	5	217,507.55	05-Sep-26	09-Sep-26	07-Jul-26	25-Jul-26	217,507.55	217,507.55	1.00
DAM3-C-B7-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	09-Sep-26	16-Sep-26			23,161.04	0.00	0.00
DAM3-C-B7-SS-1030	Steel members for external platform	7	18,670.78	09-Sep-26	16-Sep-26	24-Aug-26	19-Sep-26	18,670.78	18,670.78	1.00
DAM3-C-B7-SS-0130	Installation of wall sandwich panel	5	326,261.32	17-Sep-26	22-Sep-26	01-Sep-26	24-Sep-26	326,261.32	326,261.32	1.00
DAM3-C-B7-SS-1040	Epoxy paint for external platform	5	3,734.16	17-Sep-26	22-Sep-26			3,734.16	0.00	0.00
ARCHITECTURAL		75	900,244.66	24-Aug-26	19-Dec-26	01-Jul-26		346,965.33	450,504.96	1.30
MASONARY WORKS		23	78,954.21	24-Aug-26	26-Sep-26	22-Jul-26	17-Aug-26	78,954.21	78,954.21	1.00
DAM3-C-B7-A-0120	Block work at factory area	10	58,338.72	24-Aug-26	03-Sep-26	22-Jul-26	26-Jul-26	58,338.72	58,338.72	1.00
DAM3-C-B7-A-0150	Block work at office area	7	6,179.18	09-Sep-26	16-Sep-26	25-Jul-26	17-Aug-26	6,179.18	6,179.18	1.00
DAM3-C-B7-A-170	Block work at toilet area	7	14,436.31	17-Sep-26	26-Sep-26	26-Jul-26	17-Aug-26	14,436.31	14,436.31	1.00
WALL FINISHES		15	92,757.47	06-Oct-26	21-Nov-26	03-Sep-26		19,436.07	86,132.37	4.43
DAM3-C-B7-A-180	Internal Wall Plaster	15	48,590.16	06-Oct-26	22-Oct-26	03-Sep-26	24-Sep-26	19,436.07	48,590.16	2.50
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	44,167.30	14-Nov-26	21-Nov-26	28-Sep-26		0.00	37,542.21	0.00
CIELING FINISHES		5	46,792.30	05-Nov-26	10-Nov-26	04-Oct-26		0.00	23,396.15	0.00
DAM3-C-B7-A-240	Installation of Ceiling Gypsum Board	5	46,792.30	05-Nov-26	10-Nov-26	04-Oct-26		0.00	23,396.15	0.00
FLOOR FINISHES		27	189,488.90	28-Oct-26	19-Dec-26	19-Sep-26		0.00	46,530.71	0.00
DAM3-C-B7-A-220	Tiles for Toilet	7	46,530.71	28-Oct-26	04-Nov-26	19-Sep-26	28-Sep-26	0.00	46,530.71	0.00
DAM3-C-B7-A-250	Tiles for Office Area	2	26,867.31	11-Nov-26	12-Nov-26			0.00	0.00	0.00
DAM3-C-B7-A-390	Granite strip	2	671.12	14-Nov-26	15-Nov-26			0.00	0.00	0.00
DAM3-C-B7-A-420	Epoxy paint	7	115,419.76	12-Dec-26	19-Dec-26			0.00	0.00	0.00
DOORS & WINDOWS		12	248,575.06	24-Sep-26	10-Oct-26	21-Sep-26		248,575.06	77,119.80	0.31
DAM3-C-B7-A-552	Window (CW1)	7	94,173.21	24-Sep-26	01-Oct-26	05-Oct-26		94,173.21	70,629.91	0.75
DAM3-C-B7-A-553	Roll up Shutter Door	1	68,619.20	03-Oct-26	03-Oct-26			68,619.20	0.00	0.00
DAM3-C-B7-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	04-Oct-26	04-Oct-26			16,016.16	0.00	0.00
DAM3-C-B7-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	05-Oct-26	05-Oct-26			22,737.85	0.00	0.00
DAM3-C-B7-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	06-Oct-26	06-Oct-26			7,811.07	0.00	0.00
DAM3-C-B7-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	07-Oct-26	07-Oct-26			16,016.16	0.00	0.00
DAM3-C-B7-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	08-Oct-26	08-Oct-26			16,711.52	0.00	0.00
DAM3-C-B7-A-558	Skylight fixtures installation	1	6,489.89	10-Oct-26	10-Oct-26	21-Sep-26	26-Sep-26	6,489.89	6,489.89	1.00
WATER PROOFING WORKS		4	4,879.02	24-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B7-A-370	Waterproofing membrane for toilets	4	4,879.02	24-Oct-26	27-Oct-26			0.00	0.00	0.00
METAL WORKS		29	193,717.06	16-Nov-26	30-Nov-26	01-Jul-26		0.00	138,371.73	0.00
DAM3-C-B7-A-290	Steel Ladder	2	9,839.16	16-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B7-A-291	Steel railing works	4	1,533.98	18-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-B7-A-292	Aluminium composite panel	5	175,888.76	23-Nov-26	28-Nov-26	30-Sep-26		0.00	131,916.57	0.00
DAM3-C-B7-A-300	Galvanised Steel Gratings	2	6,455.16	29-Nov-26	30-Nov-26	01-Jul-26	01-Jul-26	0.00	6,455.16	0.00
SPECIALTIES		9	45,080.66	01-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B7-A-320	Installation of fittings	5	22,981.27	01-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B7-A-570	Identification sign; ID01 & ID02	3	9,630.56	07-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B7-A-340	Furniture Installation	1	12,468.83	10-Dec-26	10-Dec-26			0.00	0.00	0.00
MECHANICAL		178	467,522.66	05-May-26	10-Dec-26	10-Jun-26		18,585.14	326,975.51	17.59
HVAC		20	233,183.33	22-Nov-26	07-Dec-26	05-Oct-26		0.00	170,694.73	0.00
FIRST STAGE		6	170,694.73	29-Nov-26	02-Dec-26	05-Oct-26	11-Oct-26	0.00	170,694.73	0.00
DAM3-C-B7-M-140	Installation of HVAC Ducts	2	149,489.33	29-Nov-26	30-Nov-26	05-Oct-26	11-Oct-26	0.00	149,489.33	0.00
DAM3-C-B7-M-170	Installation of Duct insulation	2	21,205.40	01-Dec-26	02-Dec-26	06-Oct-26	11-Oct-26	0.00	21,205.40	0.00
SECOND STAGE		9	62,488.60	22-Nov-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B7-M-130	Installation of Exhaust Fans	2	7,938.56	22-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-160	Installation of Wall Propeller Type Exhaust Fan	3	46,831.64	24-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-339	Installation of Diffuser	2	2,144.00	03-Dec-26	05-Dec-26			0.00	0.00	0.00
DAM3-C-B7-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	06-Dec-26	07-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		38	102,458.78	22-Nov-26	10-Dec-26	29-Jul-26		0.00	84,594.16	0.00
FIRST STAGE		17	84,594.16	22-Nov-26	05-Dec-26	29-Jul-26	12-Aug-26	0.00	84,594.16	0.00
DAM3-C-B7-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	22-Nov-26	29-Nov-26	29-Jul-26	10-Aug-26	0.00	72,394.75	0.00
DAM3-C-B7-M-310	Installation of Fire Fighting Valve	5	12,199.40	30-Nov-26	05-Dec-26	09-Aug-26	12-Aug-26	0.00	12,199.40	0.00
SECOND STAGE		12	17,864.62	06-Dec-26	10-Dec-26			0.00	0.00	0.00

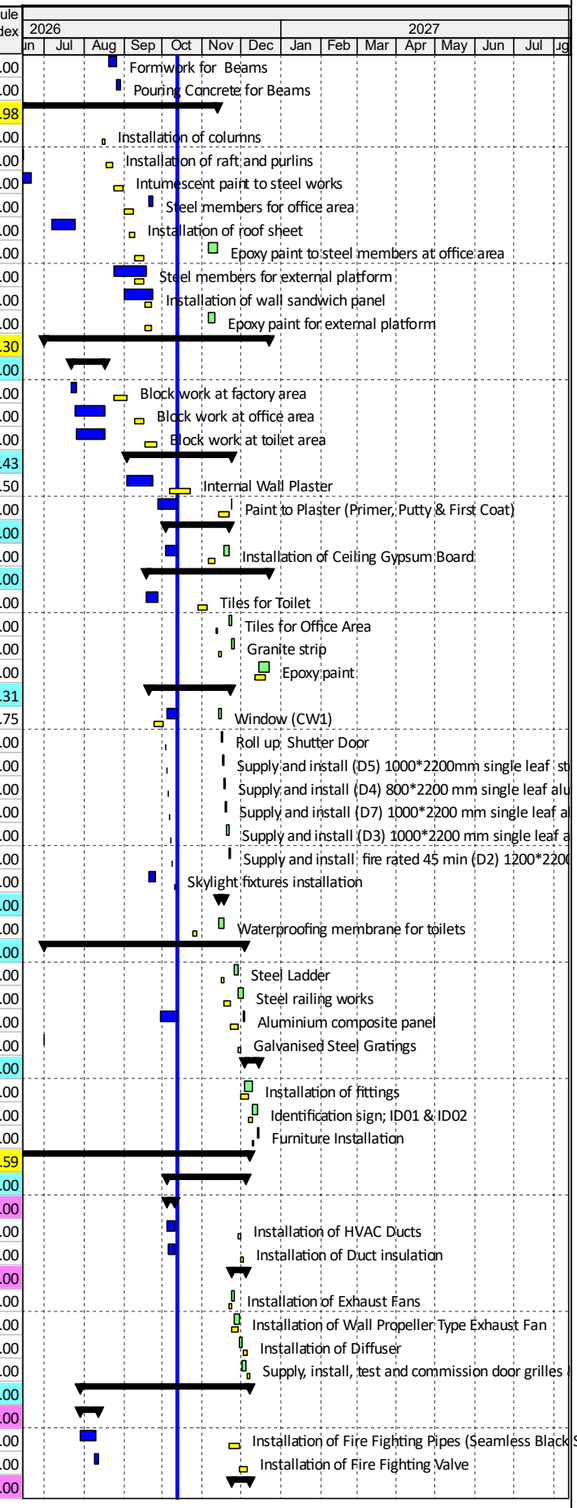

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B7-M-320	Installation of Fire Hose Cabinet	3	15,158.56	06-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B7-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	08-Dec-26	10-Dec-26			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		153	90,009.74	05-May-26	29-Nov-26	10-Jun-26		18,585.14	30,093.94	1.62
FIRST STAGE		153	41,149.90	05-May-26	12-Nov-26	10-Jun-26		18,585.14	30,093.94	1.62
DAM3-C-B7-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	05-May-26	09-May-26	10-Jun-26	14-Jun-26	18,585.14	18,585.14	1.00
DAM3-C-B7-M-220	Installation of Floor Drain	2	11,055.96	05-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-380	Installation of Trench drain	5	11,508.80	08-Nov-26	12-Nov-26	16-Jun-26	18-Jun-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	14-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-180	Installation of Electric Water Heater	2	1,819.51	14-Nov-26	15-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	16-Nov-26	19-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	21-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-270	Installation of Bib Tap	2	1,900.66	23-Nov-26	24-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-428	Installation of Water Tap	2	2,874.14	25-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B7-M-429	Installation of Roof Vent Cap	2	927.12	28-Nov-26	29-Nov-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		42	41,870.81	22-Nov-26	03-Dec-26	30-Aug-26		0.00	41,592.68	0.00
FIRST STAGE		9	41,592.68	22-Nov-26	28-Nov-26	30-Aug-26	03-Sep-26	0.00	41,592.68	0.00
DAM3-C-B7-M-290	Installation of Water Supply Pipes	4	23,318.41	22-Nov-26	25-Nov-26	30-Aug-26	03-Sep-26	0.00	23,318.41	0.00
DAM3-C-B7-M-280	Installation of Water Supply Valve	2	18,274.27	26-Nov-26	28-Nov-26	31-Aug-26	03-Sep-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	29-Nov-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B7-M-330	Capped connection	5	278.13	29-Nov-26	03-Dec-26			0.00	0.00	0.00
ELECTRICAL		73	752,044.76	27-Sep-26	06-Jan-27	16-May-26		85,111.99	303,761.61	3.57
FIRST STAGE		63	86,114.12	27-Sep-26	08-Nov-26	16-May-26		8,920.25	27,642.87	3.10
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	27-Sep-26	30-Sep-26	16-May-26		1,768.31	884.15	0.50
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	2,920.45	27-Sep-26	05-Oct-26	18-May-26		2,920.45	1,460.23	0.50
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	11-Oct-26	14-Oct-26	06-Sep-26		4,231.49	7,616.67	1.80
DAM3-C-B7-E-233	Installation of Wires	4	16,925.94	15-Oct-26	19-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-223	Installation of LV Cables	4	36,389.98	29-Oct-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	19,646.47	03-Nov-26	08-Nov-26	16-May-26		0.00	17,681.82	0.00
SECOND STAGE		73	665,930.64	01-Oct-26	06-Jan-27	21-Sep-26		76,191.74	276,118.73	3.62
DAM3-C-B7-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	01-Oct-26	05-Oct-26			19,451.37	0.00	0.00
DAM3-C-B7-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	06-Oct-26	10-Oct-26			56,740.37	0.00	0.00
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	76,166.74	20-Oct-26	24-Oct-26	21-Sep-26		0.00	22,850.02	0.00
DAM3-C-B7-E-193	Installation of Main Distribution Board	2	32,472.73	20-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-410	Installation of CCTV System	7	76,349.24	20-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-243	Installation of LP-1 Panel	2	18,403.54	22-Oct-26	24-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-253	Installation of PP-AC panel	2	21,648.48	25-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-213	Installation of Telephone Cabinet	2	26,991.08	27-Oct-26	28-Oct-26			0.00	0.00	0.00
DAM3-C-B7-E-273	Installation of Access Control System	5	27,616.86	28-Oct-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-283	Monitor Modules for Fire Alarm	2	3,882.38	03-Nov-26	04-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-293	Line Isolator Modules for Fire Alarm	2	185.40	05-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	08-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-173	Installation of Wiring Devices	4	19,435.09	22-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-203	Installation of Disconnect Switches	2	30,235.95	26-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B7-E-420	Installation of Solar power plant	7	253,268.71	30-Dec-26	06-Jan-27	04-Oct-26	06-Oct-26	0.00	253,268.71	0.00
BLOCK B8		288	5,075,523.09	19-Feb-26	14-Jan-27	17-Feb-26		2,912,484.49	3,545,138.59	1.22
STRUCTURAL		208	1,389,042.53	19-Feb-26	17-Oct-26	17-Feb-26		1,388,524.18	1,388,135.41	1.00
FOOTING		58	597,655.16	19-Feb-26	13-May-26	17-Feb-26	16-Apr-26	597,655.16	597,655.16	1.00
DAM3-C-B8-S-150	Excavation for footings	4	89,859.61	19-Feb-26	25-Feb-26	17-Feb-26	21-Feb-26	89,859.61	89,859.61	1.00
DAM3-C-B8-S-6283	Soil replacement - rock fill	4	179,061.91	25-Feb-26	02-Mar-26	28-Feb-26	02-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B8-S-6293	Engineering fill	4	46,046.19	03-Mar-26	07-Mar-26	08-Mar-26	16-Mar-26	46,046.19	46,046.19	1.00
DAM3-C-B8-S-101	Anti Termite Below Footings	1	11,905.55	08-Mar-26	08-Mar-26	28-Mar-26	28-Mar-26	11,905.55	11,905.55	1.00
DAM3-C-B8-S-102	Vapour Barrier for Footings	1	7,940.10	09-Mar-26	09-Mar-26	28-Mar-26	28-Mar-26	7,940.10	7,940.10	1.00
DAM3-C-B8-S-103	Lean Concrete Below Footings	2	8,229.34	10-Mar-26	11-Mar-26	28-Mar-26	28-Mar-26	8,229.34	8,229.34	1.00
DAM3-C-B8-S-104	Rebar for Footings	4	101,844.98	12-Mar-26	16-Mar-26	11-Apr-26	13-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B8-S-105	Formwork for Footings	4	25,461.25	09-May-26	12-May-26	13-Apr-26	14-Apr-26	25,461.25	25,461.25	1.00
DAM3-C-B8-S-106	Pouring Concrete for Footings	1	127,306.23	13-May-26	13-May-26	16-Apr-26	16-Apr-26	127,306.23	127,306.23	1.00
COLUMN NECK		17	120,554.54	14-May-26	04-Jun-26	14-Apr-26	12-May-26	120,554.54	120,554.54	1.00
DAM3-C-B8-S-257	Rebar for column neck	4	14,919.19	14-May-26	18-May-26	14-Apr-26	15-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B8-S-267	Formwork for column neck	2	9,946.13	19-May-26	20-May-26	22-Apr-26	25-Apr-26	9,946.13	9,946.13	1.00
DAM3-C-B8-S-297	Pouring Concrete for column neck	1	24,865.31	21-May-26	21-May-26	23-Apr-26	25-Apr-26	24,865.31	24,865.31	1.00
DAM3-C-B8-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	23-May-26	24-May-26	27-Apr-26	30-Apr-26	24,777.73	24,777.73	1.00
DAM3-C-B8-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	25-May-26	04-Jun-26	05-May-26	12-May-26	46,046.19	46,046.19	1.00

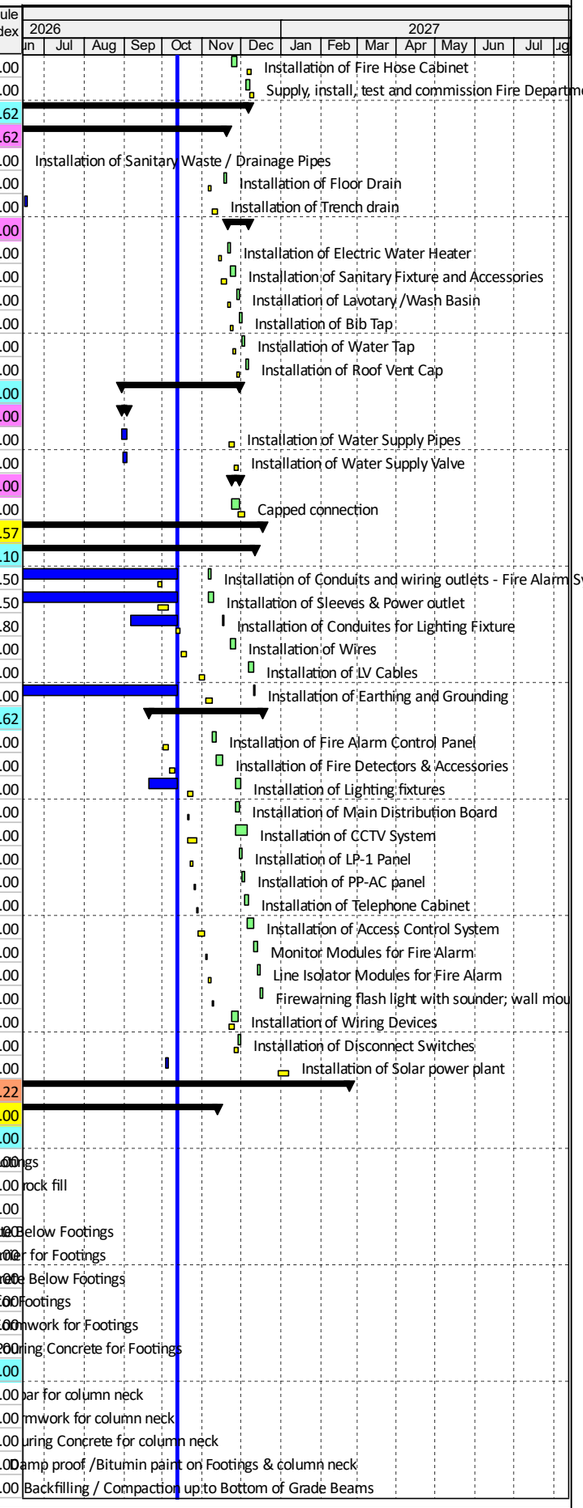

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
GRADE BEAM		24	171,632.86	20-Jun-26	09-Jul-26	13-May-26	03-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B8-S-527	Anti Termite Below Grade Beams	1	11,905.55	20-Jun-26	20-Jun-26	13-May-26	13-May-26	11,905.55	11,905.55	1.00
DAM3-C-B8-S-337	Vapour barrier for Grade Beams	2	5,293.40	21-Jun-26	22-Jun-26	13-May-26	13-May-26	5,293.40	5,293.40	1.00
DAM3-C-B8-S-338	Lean Concrete Below Grade Beams	2	4,431.19	23-Jun-26	24-Jun-26	13-May-26	13-May-26	4,431.19	4,431.19	1.00
DAM3-C-B8-S-339	Rebar for Grade Beams	5	27,194.46	25-Jun-26	30-Jun-26	16-May-26	20-May-26	27,194.46	27,194.46	1.00
DAM3-C-B8-S-340	Formwork for Grade Beams	2	6,798.61	01-Jul-26	02-Jul-26	20-May-26	23-May-26	6,798.61	6,798.61	1.00
DAM3-C-B8-S-341	Anchor bolts installation	2	57,238.83	01-Jul-26	02-Jul-26	17-May-26	20-May-26	57,238.83	57,238.83	1.00
DAM3-C-B8-S-342	Pouring Concrete for Grade Beams	1	33,993.09	04-Jul-26	04-Jul-26	24-May-26	25-May-26	33,993.09	33,993.09	1.00
DAM3-C-B8-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	05-Jul-26	09-Jul-26	31-May-26	03-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		25	397,232.98	11-Jul-26	17-Oct-26	04-Jun-26		396,714.63	396,325.87	1.00
DAM3-C-B8-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	11-Jul-26	18-Jul-26	04-Jun-26	09-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B8-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	19-Jul-26	19-Jul-26	13-Jul-26	16-Jul-26	15,874.08	15,874.08	1.00
DAM3-C-B8-S-379	Vapour barrier for below Ground Slab	2	13,233.49	20-Jul-26	21-Jul-26	13-Jul-26	16-Jul-26	13,233.49	13,233.49	1.00
DAM3-C-B8-S-382	Pouring Concrete for Ground Slab	4	344,195.21	22-Jul-26	26-Jul-26	13-Jul-26	16-Jul-26	344,195.21	344,195.21	1.00
DAM3-C-B8-S-517	Concrete pad	7	907.11	10-Oct-26	17-Oct-26			388.76	0.00	0.00
COLUMNS & BEAMS		34	101,966.98	27-Jul-26	29-Aug-26	16-May-26	03-Sep-26	101,966.98	101,966.98	1.00
DAM3-C-B8-S-5101	Rebar for column	5	20,144.05	27-Jul-26	01-Aug-26	02-Jul-26	11-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B8-S-5102	Formwork for column	4	5,036.01	02-Aug-26	05-Aug-26	07-Jul-26	25-Jul-26	5,036.01	5,036.01	1.00
DAM3-C-B8-S-5103	Pouring Concrete for column	1	25,180.06	08-Aug-26	08-Aug-26	13-Jul-26	26-Jul-26	25,180.06	25,180.06	1.00
DAM3-C-B8-S-6101	Rebar for Tie Beams	4	7,263.64	09-Aug-26	12-Aug-26	16-May-26	23-May-26	7,263.64	7,263.64	1.00
DAM3-C-B8-S-6102	Formwork for Tie Beams	2	1,815.91	13-Aug-26	15-Aug-26	16-May-26	24-May-26	1,815.91	1,815.91	1.00
DAM3-C-B8-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	19-Aug-26	20-Aug-26	16-May-26	25-May-26	9,079.54	9,079.54	1.00
DAM3-C-B8-S-6113	Rebar for Beams	4	13,379.11	20-Aug-26	25-Aug-26	23-Aug-26	26-Aug-26	13,379.11	13,379.11	1.00
DAM3-C-B8-S-6123	Formwork for Beams	2	3,344.77	25-Aug-26	27-Aug-26	29-Aug-26	01-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B8-S-6133	Pouring Concrete for Beams	1	16,723.88	27-Aug-26	29-Aug-26	01-Sep-26	03-Sep-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		44	1,566,668.48	05-Sep-26	14-Oct-26	14-Jun-26		1,434,670.29	1,539,773.29	1.07
DAM3-C-B8-SS-0100	Installation of columns	3	217,507.55	05-Sep-26	07-Sep-26	14-Jun-26	15-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B8-SS-0110	Installation of raft and purlins	5	326,261.32	08-Sep-26	13-Sep-26	15-Jun-26	16-Jun-26	326,261.32	326,261.32	1.00
DAM3-C-B8-SS-610	Intumescent paint to steel works	7	317,759.56	14-Sep-26	21-Sep-26	17-Jun-26	24-Jun-26	317,759.56	317,759.56	1.00
DAM3-C-B8-SS-620	Steel members for office area	4	115,805.20	22-Sep-26	30-Sep-26	26-Sep-26	28-Sep-26	115,805.20	115,805.20	1.00
DAM3-C-B8-SS-0140	Installation of roof sheet	5	217,507.55	27-Sep-26	01-Oct-26	19-Jul-26	01-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B8-SS-1020	Epoxy paint to steel members at office area	4	23,161.04	01-Oct-26	08-Oct-26			23,161.04	0.00	0.00
DAM3-C-B8-SS-1030	Steel members for external platform	4	18,670.78	01-Oct-26	08-Oct-26	20-Sep-26	21-Sep-26	18,670.78	18,670.78	1.00
DAM3-C-B8-SS-0130	Installation of wall sandwich panel	5	326,261.32	10-Oct-26	14-Oct-26	02-Sep-26	22-Sep-26	195,756.79	326,261.32	1.67
DAM3-C-B8-SS-1040	Epoxy paint for external platform	3	3,734.16	10-Oct-26	14-Oct-26			2,240.49	0.00	0.00
ARCHITECTURAL		92	900,244.66	14-Sep-26	13-Jan-27	18-Jul-26		70,704.89	347,958.87	4.92
MASONARY WORKS		18	78,954.21	14-Sep-26	17-Oct-26	23-Jul-26	23-Aug-26	70,704.89	78,954.21	1.12
DAM3-C-B8-A-0120	Block work at factory area	5	58,338.72	14-Sep-26	26-Sep-26	23-Jul-26	27-Jul-26	58,338.72	58,338.72	1.00
DAM3-C-B8-A-0150	Block work at office area	5	6,179.18	01-Oct-26	08-Oct-26	23-Jul-26	23-Aug-26	6,179.18	6,179.18	1.00
DAM3-C-B8-A-170	Block work at toilet area	3	14,436.31	10-Oct-26	17-Oct-26	27-Jul-26	22-Aug-26	6,186.99	14,436.31	2.33
WALL FINISHES		59	92,757.47	27-Oct-26	12-Dec-26	10-Sep-26		0.00	86,132.37	0.00
DAM3-C-B8-A-180	Internal Wall Plaster	10	48,590.16	27-Oct-26	12-Nov-26	10-Sep-26	28-Sep-26	0.00	48,590.16	0.00
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	44,167.30	05-Dec-26	12-Dec-26	01-Oct-26		0.00	37,542.21	0.00
CIELING FINISHES		3	46,792.30	26-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-240	Installation of Ceiling Gypsum Board	3	46,792.30	26-Nov-26	01-Dec-26			0.00	0.00	0.00
FLOOR FINISHES		42	189,488.90	18-Nov-26	13-Jan-27	30-Sep-26		0.00	46,530.71	0.00
DAM3-C-B8-A-220	Tiles for Toilet	4	46,530.71	18-Nov-26	25-Nov-26	30-Sep-26	04-Oct-26	0.00	46,530.71	0.00
DAM3-C-B8-A-250	Tiles for Office Area	2	26,867.31	02-Dec-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-390	Granite strip	2	671.12	05-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-420	Epoxy paint	2	115,419.76	06-Jan-27	13-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		14	248,575.06	15-Oct-26	31-Oct-26	27-Sep-26		0.00	77,119.80	0.00
DAM3-C-B8-A-552	Window (CW1)	7	94,173.21	15-Oct-26	22-Oct-26	08-Oct-26		0.00	70,629.91	0.00
DAM3-C-B8-A-553	Roll up Shutter Door	1	68,619.20	24-Oct-26	24-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	25-Oct-26	25-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	26-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	27-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	28-Oct-26	28-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	29-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B8-A-558	Skylight fixtures installation	1	6,489.89	31-Oct-26	31-Oct-26	27-Sep-26	30-Sep-26	0.00	6,489.89	0.00
WATER PROOFING WORKS		4	4,879.02	14-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B8-A-370	Waterproofing membrane for toilets	4	4,879.02	14-Nov-26	17-Nov-26			0.00	0.00	0.00
METAL WORKS		32	193,717.06	07-Dec-26	21-Dec-26	18-Jul-26		0.00	59,221.79	0.00

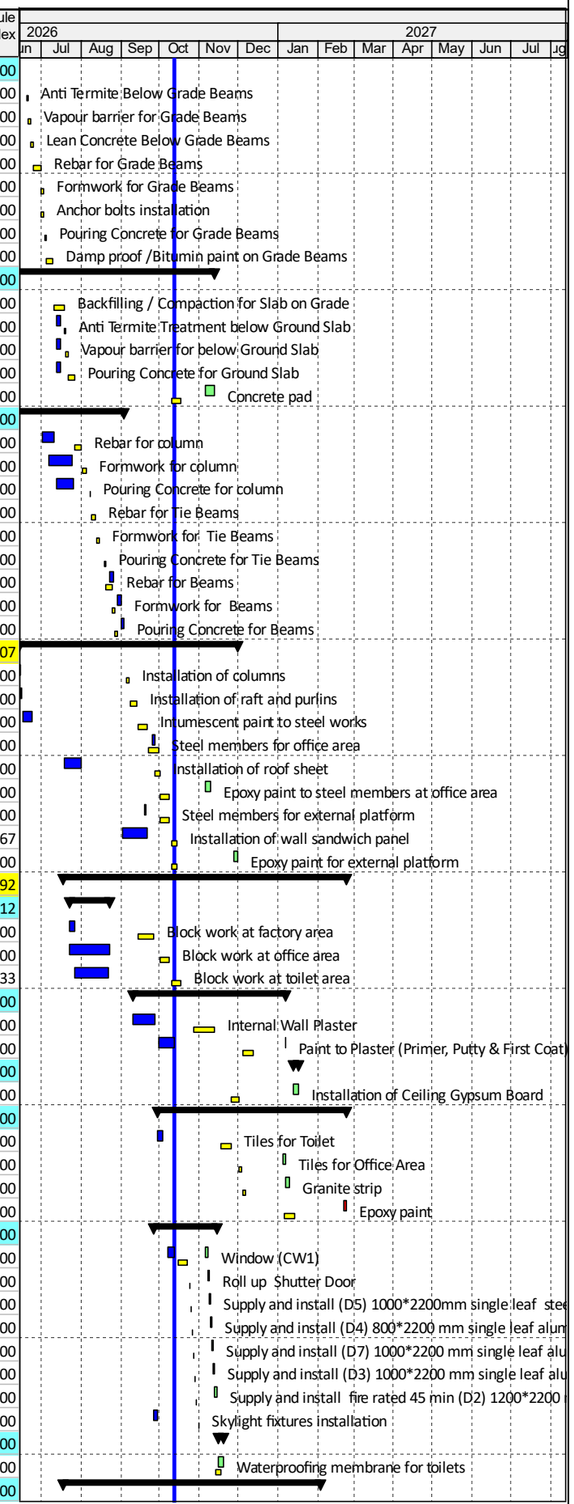

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B8-A-290	Steel Ladder	2	9,839.16	07-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-291	Steel railing works	4	1,533.98	09-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-292	Aluminium composite panel	3	175,888.76	14-Dec-26	19-Dec-26	06-Oct-26		0.00	52,766.63	0.00
DAM3-C-B8-A-300	Galvanised Steel Gratings	2	6,455.16	20-Dec-26	21-Dec-26	18-Jul-26	18-Jul-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	27-Dec-26	05-Jan-27			0.00	0.00	0.00
DAM3-C-B8-A-320	Installation of fittings	3	22,981.27	27-Dec-26	31-Dec-26			0.00	0.00	0.00
DAM3-C-B8-A-570	Identification sign; ID01 & ID02	3	9,630.56	02-Jan-27	04-Jan-27			0.00	0.00	0.00
DAM3-C-B8-A-340	Furniture Installation	1	12,468.83	05-Jan-27	05-Jan-27			0.00	0.00	0.00
MECHANICAL		107	467,522.66	11-Jul-26	05-Jan-27	15-Jun-26		18,585.14	241,628.15	13.00
HVAC		12	233,183.33	13-Dec-26	28-Dec-26	11-Oct-26		0.00	85,347.36	0.00
FIRST STAGE		4	170,694.73	20-Dec-26	23-Dec-26	11-Oct-26		0.00	85,347.36	0.00
DAM3-C-B8-M-140	Installation of HVAC Ducts	2	149,489.33	20-Dec-26	21-Dec-26	11-Oct-26		0.00	74,744.66	0.00
DAM3-C-B8-M-170	Installation of Duct insulation	2	21,205.40	22-Dec-26	23-Dec-26	11-Oct-26		0.00	10,602.70	0.00
SECOND STAGE		12	62,488.60	13-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-130	Installation of Exhaust Fans	2	7,938.56	13-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-160	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	15-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-339	Installation of Diffuser	2	2,144.00	24-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	27-Dec-26	28-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		24	102,458.78	13-Dec-26	05-Jan-27	12-Aug-26		0.00	84,594.16	0.00
FIRST STAGE		11	84,594.16	13-Dec-26	26-Dec-26	12-Aug-26	16-Aug-26	0.00	84,594.16	0.00
DAM3-C-B8-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	4	72,394.75	13-Dec-26	20-Dec-26	12-Aug-26	16-Aug-26	0.00	72,394.75	0.00
DAM3-C-B8-M-310	Installation of Fire Fighting Valve	5	12,199.40	21-Dec-26	26-Dec-26	15-Aug-26	16-Aug-26	0.00	12,199.40	0.00
SECOND STAGE		24	17,864.62	29-Dec-26	05-Jan-27			0.00	0.00	0.00
DAM3-C-B8-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	29-Dec-26	31-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-320	Installation of Fire Hose Cabinet	3	15,158.56	03-Jan-27	05-Jan-27			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		91	90,009.74	11-Jul-26	20-Dec-26	15-Jun-26		18,585.14	30,093.94	1.62
FIRST STAGE		91	41,149.90	11-Jul-26	03-Dec-26	15-Jun-26		18,585.14	30,093.94	1.62
DAM3-C-B8-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	11-Jul-26	14-Jul-26	15-Jun-26	20-Jun-26	18,585.14	18,585.14	1.00
DAM3-C-B8-M-220	Installation of Floor Drain	2	11,055.96	26-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B8-M-380	Installation of Trench drain	5	11,508.80	29-Nov-26	03-Dec-26	20-Jun-26	21-Jun-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	05-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-180	Installation of Electric Water Heater	2	1,819.51	05-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	07-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	12-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-270	Installation of Bib Tap	2	1,900.66	14-Dec-26	15-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-428	Installation of Water Tap	2	2,874.14	16-Dec-26	17-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-429	Installation of Roof Vent Cap	2	927.12	19-Dec-26	20-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		8	41,870.81	13-Dec-26	24-Dec-26	05-Sep-26		0.00	41,592.68	0.00
FIRST STAGE		8	41,592.68	13-Dec-26	19-Dec-26	05-Sep-26	09-Sep-26	0.00	41,592.68	0.00
DAM3-C-B8-M-290	Installation of Water Supply Pipes	4	23,318.41	13-Dec-26	16-Dec-26	05-Sep-26	08-Sep-26	0.00	23,318.41	0.00
DAM3-C-B8-M-280	Installation of Water Supply Valve	2	18,274.27	17-Dec-26	19-Dec-26	06-Sep-26	09-Sep-26	0.00	18,274.27	0.00
SECOND STAGE		3	278.13	20-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B8-M-330	Capped connection	3	278.13	20-Dec-26	24-Dec-26			0.00	0.00	0.00
ELECTRICAL		63	752,044.76	18-Oct-26	14-Jan-27	19-May-26		0.00	27,642.87	0.00
FIRST STAGE		61	86,114.12	18-Oct-26	29-Nov-26	19-May-26		0.00	27,642.87	0.00
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	18-Oct-26	21-Oct-26	20-May-26		0.00	884.15	0.00
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	2,920.45	18-Oct-26	26-Oct-26	20-May-26		0.00	1,460.23	0.00
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	01-Nov-26	04-Nov-26	07-Sep-26		0.00	7,616.67	0.00
DAM3-C-B8-E-233	Installation of Wires	4	16,925.94	05-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-223	Installation of LV Cables	2	36,389.98	19-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	19,646.47	24-Nov-26	29-Nov-26	19-May-26		0.00	17,681.82	0.00
SECOND STAGE		48	665,930.64	22-Oct-26	14-Jan-27			0.00	0.00	0.00
DAM3-C-B8-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	22-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B8-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	27-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B8-E-153	Installation of Lighting fixtures	4	76,166.74	10-Nov-26	14-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-193	Installation of Main Distribution Board	2	32,472.73	10-Nov-26	11-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-410	Installation of CCTV System	3	76,349.24	10-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-243	Installation of LP-1 Panel	2	18,403.54	12-Nov-26	14-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-253	Installation of PP-AC panel	2	21,648.48	15-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-213	Installation of Telephone Cabinet	2	26,991.08	17-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-273	Installation of Access Control System	3	27,616.86	18-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-283	Monitor Modules for Fire Alarm	2	3,882.38	24-Nov-26	25-Nov-26			0.00	0.00	0.00

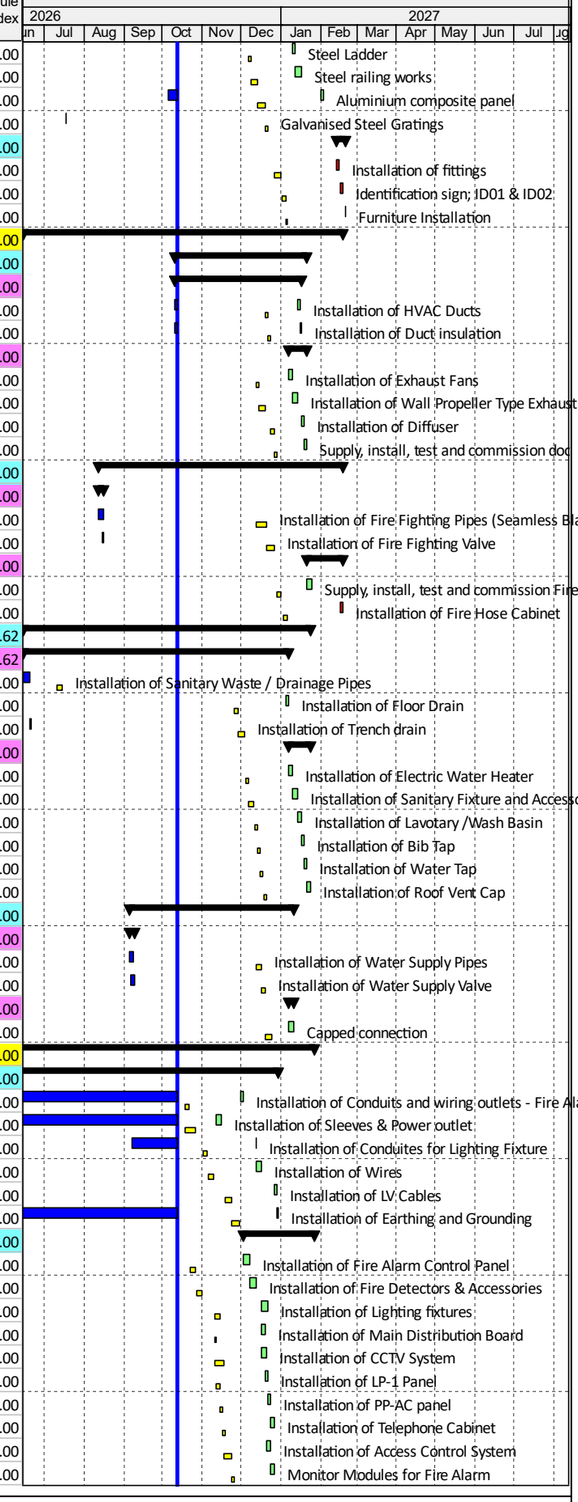

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B8-E-293	Line Isolator Modules for Fire Alarm	2	185.40	26-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	29-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-B8-E-173	Installation of Wiring Devices	3	19,435.09	13-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B8-E-203	Installation of Disconnect Switches	2	30,235.95	17-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B8-E-420	Installation of Solar power plant	7	253,268.71	07-Jan-27	14-Jan-27			0.00	0.00	0.00
BLOCK B9		287	5,075,523.09	25-Feb-26	31-Jan-27	17-Feb-26		2,707,911.45	3,422,130.70	1.26
STRUCTURAL		206	1,389,042.53	25-Feb-26	20-Oct-26	17-Feb-26		1,388,135.41	1,388,135.41	1.00
FOOTING		96	597,655.16	25-Feb-26	13-May-26	17-Feb-26	23-Apr-26	597,655.16	597,655.16	1.00
DAM3-C-B9-S-150	Excavation for footings	4	89,859.61	25-Feb-26	02-Mar-26	17-Feb-26	21-Feb-26	89,859.61	89,859.61	1.00
DAM3-C-B9-S-6303	Soil replacement - rock fill	4	179,061.91	03-Mar-26	07-Mar-26	03-Mar-26	07-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B9-S-6313	Engineering fill	4	46,046.19	08-Mar-26	11-Mar-26	09-Mar-26	17-Mar-26	46,046.19	46,046.19	1.00
DAM3-C-B9-S-101	Anti Termite Below Footings	1	11,905.55	12-Mar-26	12-Mar-26	29-Mar-26	29-Mar-26	11,905.55	11,905.55	1.00
DAM3-C-B9-S-102	Vapour Barrier for Footings	1	7,940.10	14-Mar-26	14-Mar-26	29-Mar-26	29-Mar-26	7,940.10	7,940.10	1.00
DAM3-C-B9-S-103	Lean Concrete Below Footings	2	8,229.34	15-Mar-26	16-Mar-26	30-Mar-26	30-Mar-26	8,229.34	8,229.34	1.00
DAM3-C-B9-S-104	Rebar for Footings	4	101,844.98	04-May-26	07-May-26	18-Apr-26	20-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B9-S-105	Formwork for Footings	4	25,461.25	09-May-26	12-May-26	19-Apr-26	21-Apr-26	25,461.25	25,461.25	1.00
DAM3-C-B9-S-106	Pouring Concrete for Footings	1	127,306.23	13-May-26	13-May-26	23-Apr-26	23-Apr-26	127,306.23	127,306.23	1.00
COLUMN NECK		14	120,554.54	14-May-26	04-Jun-26	21-Apr-26	14-May-26	120,554.54	120,554.54	1.00
DAM3-C-B9-S-257	Rebar for column neck	4	14,919.19	14-May-26	18-May-26	21-Apr-26	22-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B9-S-267	Formwork for column neck	2	9,946.13	19-May-26	20-May-26	22-Apr-26	23-Apr-26	9,946.13	9,946.13	1.00
DAM3-C-B9-S-297	Pouring Concrete for column neck	1	24,865.31	21-May-26	21-May-26	28-Apr-26	28-Apr-26	24,865.31	24,865.31	1.00
DAM3-C-B9-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	23-May-26	24-May-26	02-May-26	02-May-26	24,777.73	24,777.73	1.00
DAM3-C-B9-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	25-May-26	04-Jun-26	09-May-26	14-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		41	171,632.86	06-Jun-26	01-Jul-26	18-May-26	07-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B9-S-527	Anti Termite Below Grade Beams	1	11,905.55	06-Jun-26	06-Jun-26	18-May-26	18-May-26	11,905.55	11,905.55	1.00
DAM3-C-B9-S-337	Vapour barrier for Grade Beams	2	5,293.40	07-Jun-26	08-Jun-26	18-May-26	18-May-26	5,293.40	5,293.40	1.00
DAM3-C-B9-S-338	Lean Concrete Below Grade Beams	2	4,431.19	09-Jun-26	10-Jun-26	18-May-26	18-May-26	4,431.19	4,431.19	1.00
DAM3-C-B9-S-339	Rebar for Grade Beams	5	27,194.46	17-Jun-26	22-Jun-26	20-May-26	21-May-26	27,194.46	27,194.46	1.00
DAM3-C-B9-S-340	Formwork for Grade Beams	2	6,798.61	23-Jun-26	24-Jun-26	21-May-26	24-May-26	6,798.61	6,798.61	1.00
DAM3-C-B9-S-341	Anchor bolts installation	2	57,238.83	23-Jun-26	24-Jun-26	20-May-26	23-May-26	57,238.83	57,238.83	1.00
DAM3-C-B9-S-342	Pouring Concrete for Grade Beams	1	33,993.09	25-Jun-26	25-Jun-26	25-May-26	25-May-26	33,993.09	33,993.09	1.00
DAM3-C-B9-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	27-Jun-26	01-Jul-26	02-Jun-26	07-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		75	397,232.98	15-Jul-26	20-Oct-26	09-Jun-26		396,325.87	396,325.87	1.00
DAM3-C-B9-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	15-Jul-26	22-Jul-26	09-Jun-26	13-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B9-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	23-Jul-26	23-Jul-26	22-Jul-26	25-Jul-26	15,874.08	15,874.08	1.00
DAM3-C-B9-S-379	Vapour barrier for below Ground Slab	2	13,233.49	25-Jul-26	26-Jul-26	22-Jul-26	25-Jul-26	13,233.49	13,233.49	1.00
DAM3-C-B9-S-382	Pouring Concrete for Ground Slab	4	344,195.21	27-Jul-26	30-Jul-26	22-Jul-26	25-Jul-26	344,195.21	344,195.21	1.00
DAM3-C-B9-S-517	Concrete pad	7	907.11	13-Oct-26	20-Oct-26			0.00	0.00	0.00
COLUMNS & BEAMS		74	101,966.98	23-Jul-26	19-Aug-26	21-May-26	12-Sep-26	101,966.98	101,966.98	1.00
DAM3-C-B9-S-5101	Rebar for column	5	20,144.05	23-Jul-26	28-Jul-26	11-Jul-26	14-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B9-S-5102	Formwork for column	4	5,036.01	29-Jul-26	02-Aug-26	14-Jul-26	28-Jul-26	5,036.01	5,036.01	1.00
DAM3-C-B9-S-5103	Pouring Concrete for column	1	25,180.06	03-Aug-26	03-Aug-26	15-Jul-26	29-Jul-26	25,180.06	25,180.06	1.00
DAM3-C-B9-S-6101	Rebar for Tie Beams	4	7,263.64	04-Aug-26	08-Aug-26	21-May-26	07-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B9-S-6102	Formwork for Tie Beams	2	1,815.91	09-Aug-26	10-Aug-26	23-May-26	08-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B9-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	11-Aug-26	11-Aug-26	25-May-26	09-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B9-S-6113	Rebar for Beams	4	13,379.11	12-Aug-26	16-Aug-26	23-Aug-26	26-Aug-26	13,379.11	13,379.11	1.00
DAM3-C-B9-S-6123	Formwork for Beams	2	3,344.77	17-Aug-26	18-Aug-26	01-Sep-26	05-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B9-S-6133	Pouring Concrete for Beams	1	16,723.88	19-Aug-26	19-Aug-26	08-Sep-26	12-Sep-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		48	1,566,668.48	08-Sep-26	18-Oct-26	16-Jun-26		1,236,673.00	1,539,773.29	1.25
DAM3-C-B9-SS-0100	Installation of columns	3	217,507.55	08-Sep-26	10-Sep-26	16-Jun-26	17-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B9-SS-0110	Installation of raft and purlins	5	326,261.32	12-Sep-26	16-Sep-26	18-Jun-26	22-Jun-26	326,261.32	326,261.32	1.00
DAM3-C-B9-SS-610	Intumescent paint to steel works	7	317,759.56	17-Sep-26	26-Sep-26	05-Jul-26	07-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B9-SS-620	Steel members for office area	2	115,805.20	27-Sep-26	04-Oct-26	27-Sep-26	29-Sep-26	115,805.20	115,805.20	1.00
DAM3-C-B9-SS-0140	Installation of roof sheet	5	217,507.55	30-Sep-26	05-Oct-26	22-Jul-26	01-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B9-SS-1020	Epoxy paint to steel members at office area	7	23,161.04	05-Oct-26	12-Oct-26			23,161.04	0.00	0.00
DAM3-C-B9-SS-1030	Steel members for external platform	7	18,670.78	05-Oct-26	12-Oct-26	21-Sep-26	26-Sep-26	18,670.78	18,670.78	1.00
DAM3-C-B9-SS-0130	Installation of wall sandwich panel	5	326,261.32	13-Oct-26	18-Oct-26	03-Sep-26	05-Oct-26	0.00	326,261.32	0.00
DAM3-C-B9-SS-1040	Epoxy paint for external platform	5	3,734.16	13-Oct-26	18-Oct-26			0.00	0.00	0.00
ARCHITECTURAL		89	900,244.66	17-Sep-26	12-Jan-27	27-Jul-26		64,517.90	310,298.35	4.81
MASONARY WORKS		19	78,954.21	17-Sep-26	20-Oct-26	28-Jul-26	29-Aug-26	64,517.90	78,954.21	1.22
DAM3-C-B9-A-0120	Block work at factory area	10	58,338.72	17-Sep-26	29-Sep-26	28-Jul-26	30-Jul-26	58,338.72	58,338.72	1.00
DAM3-C-B9-A-0150	Block work at office area	5	6,179.18	05-Oct-26	12-Oct-26	30-Jul-26	27-Aug-26	6,179.18	6,179.18	1.00

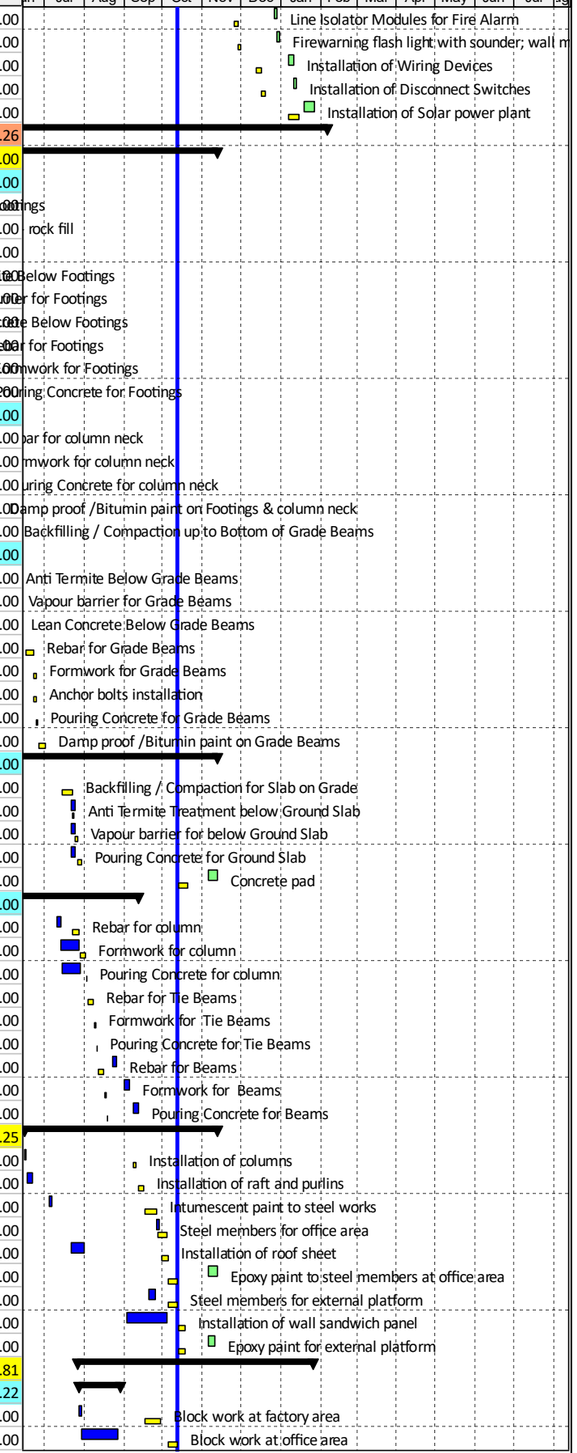

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B9-A-170	Block work at toilet area	5	14,436.31	13-Oct-26	20-Oct-26	02-Aug-26	29-Aug-26	0.00	14,436.31	0.00
WALL FINISHES		27	92,757.47	31-Oct-26	15-Dec-26	17-Sep-26		0.00	83,924.01	0.00
DAM3-C-B9-A-180	Internal Wall Plaster	5	48,590.16	31-Oct-26	16-Nov-26	17-Sep-26	05-Oct-26	0.00	48,590.16	0.00
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	44,167.30	08-Dec-26	15-Dec-26	03-Oct-26		0.00	35,333.84	0.00
CIELING FINISHES		3	46,792.30	30-Nov-26	05-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-240	Installation of Ceiling Gypsum Board	3	46,792.30	30-Nov-26	05-Dec-26			0.00	0.00	0.00
FLOOR FINISHES		51	189,488.90	22-Nov-26	12-Jan-27	01-Oct-26		0.00	46,530.71	0.00
DAM3-C-B9-A-220	Tiles for Toilet	4	46,530.71	22-Nov-26	29-Nov-26	01-Oct-26	07-Oct-26	0.00	46,530.71	0.00
DAM3-C-B9-A-250	Tiles for Office Area	2	26,867.31	06-Dec-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-390	Granite strip	2	671.12	08-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-420	Epoxy paint	4	115,419.76	05-Jan-27	12-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		19	248,575.06	19-Oct-26	03-Nov-26	30-Sep-26		0.00	6,489.89	0.00
DAM3-C-B9-A-552	Window (CW1)	7	94,173.21	19-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-B9-A-553	Roll up Shutter Door	1	68,619.20	27-Oct-26	27-Oct-26			0.00	0.00	0.00
DAM3-C-B9-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	28-Oct-26	28-Oct-26			0.00	0.00	0.00
DAM3-C-B9-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	29-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B9-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	31-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B9-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	01-Nov-26	01-Nov-26			0.00	0.00	0.00
DAM3-C-B9-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	02-Nov-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B9-A-558	Skylight fixtures installation	1	6,489.89	03-Nov-26	03-Nov-26	30-Sep-26	04-Oct-26	0.00	6,489.89	0.00
WATER PROOFING WORKS		4	4,879.02	17-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B9-A-370	Waterproofing membrane for toilets	4	4,879.02	17-Nov-26	21-Nov-26			0.00	0.00	0.00
METAL WORKS		65	193,717.06	10-Dec-26	24-Dec-26	27-Jul-26		0.00	94,399.54	0.00
DAM3-C-B9-A-290	Steel Ladder	2	9,839.16	10-Dec-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-291	Steel railing works	3	1,533.98	13-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-292	Aluminium composite panel	3	175,888.76	17-Dec-26	22-Dec-26	29-Sep-26		0.00	87,944.38	0.00
DAM3-C-B9-A-300	Galvanised Steel Gratings	2	6,455.16	23-Dec-26	24-Dec-26	27-Jul-26	27-Jul-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	26-Dec-26	04-Jan-27			0.00	0.00	0.00
DAM3-C-B9-A-320	Installation of fittings	3	22,981.27	26-Dec-26	30-Dec-26			0.00	0.00	0.00
DAM3-C-B9-A-570	Identification sign; ID01 & ID02	3	9,630.56	31-Dec-26	03-Jan-27			0.00	0.00	0.00
DAM3-C-B9-A-340	Furniture Installation	1	12,468.83	04-Jan-27	04-Jan-27			0.00	0.00	0.00
MECHANICAL		158	467,522.66	02-Jul-26	04-Jan-27	21-Jun-26		18,585.14	156,280.78	8.41
HVAC		14	233,183.33	16-Dec-26	31-Dec-26			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	23-Dec-26	27-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-140	Installation of HVAC Ducts	2	149,489.33	23-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-170	Installation of Duct insulation	2	21,205.40	26-Dec-26	27-Dec-26			0.00	0.00	0.00
SECOND STAGE		14	62,488.60	16-Dec-26	31-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-130	Installation of Exhaust Fans	2	7,938.56	16-Dec-26	17-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-160	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	19-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-339	Installation of Diffuser	2	2,144.00	28-Dec-26	29-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	30-Dec-26	31-Dec-26			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		18	102,458.78	16-Dec-26	04-Jan-27	17-Aug-26		0.00	84,594.16	0.00
FIRST STAGE		10	84,594.16	16-Dec-26	29-Dec-26	17-Aug-26	23-Aug-26	0.00	84,594.16	0.00
DAM3-C-B9-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	72,394.75	16-Dec-26	23-Dec-26	17-Aug-26	22-Aug-26	0.00	72,394.75	0.00
DAM3-C-B9-M-310	Installation of Fire Fighting Valve	5	12,199.40	24-Dec-26	29-Dec-26	17-Aug-26	23-Aug-26	0.00	12,199.40	0.00
SECOND STAGE		17	17,864.62	30-Dec-26	04-Jan-27			0.00	0.00	0.00
DAM3-C-B9-M-320	Installation of Fire Hose Cabinet	3	15,158.56	30-Dec-26	02-Jan-27			0.00	0.00	0.00
DAM3-C-B9-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	02-Jan-27	04-Jan-27			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		158	90,009.74	02-Jul-26	23-Dec-26	21-Jun-26		18,585.14	30,093.94	1.62
FIRST STAGE		158	41,149.90	02-Jul-26	07-Dec-26	21-Jun-26		18,585.14	30,093.94	1.62
DAM3-C-B9-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	02-Jul-26	06-Jul-26	21-Jun-26	24-Jun-26	18,585.14	18,585.14	1.00
DAM3-C-B9-M-220	Installation of Floor Drain	2	11,055.96	30-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-380	Installation of Trench drain	5	11,508.80	02-Dec-26	07-Dec-26	22-Jun-26	24-Jun-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	08-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-180	Installation of Electric Water Heater	2	1,819.51	08-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	10-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	15-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-270	Installation of Bib Tap	2	1,900.66	17-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-428	Installation of Water Tap	2	2,874.14	20-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-429	Installation of Roof Vent Cap	2	927.12	22-Dec-26	23-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		12	41,870.81	16-Dec-26	28-Dec-26	14-Sep-26		0.00	41,592.68	0.00
FIRST STAGE		4	41,592.68	16-Dec-26	22-Dec-26	14-Sep-26	19-Sep-26	0.00	41,592.68	0.00

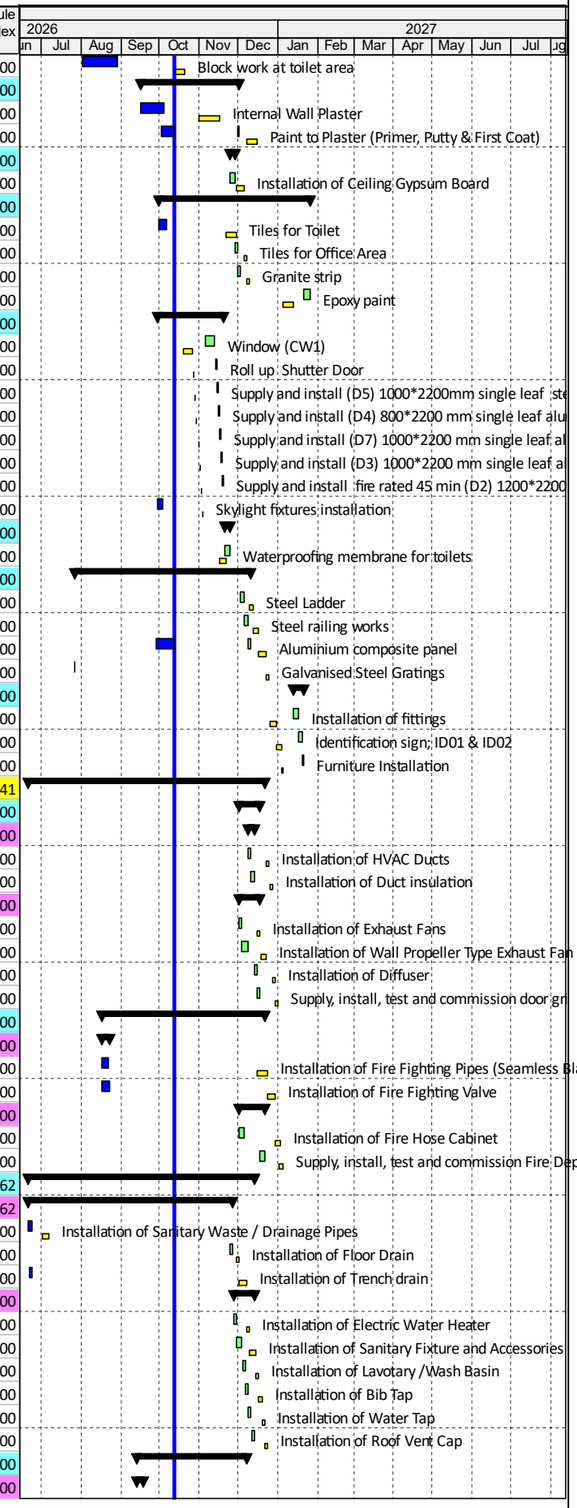

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B9-M-290	Installation of Water Supply Pipes	4	23,318.41	16-Dec-26	20-Dec-26	14-Sep-26	19-Sep-26	0.00	23,318.41	0.00
DAM3-C-B9-M-280	Installation of Water Supply Valve	2	18,274.27	21-Dec-26	22-Dec-26	15-Sep-26	19-Sep-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	23-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B9-M-330	Capped connection	5	278.13	23-Dec-26	28-Dec-26			0.00	0.00	0.00
ELECTRICAL		81	752,044.76	21-Oct-26	31-Jan-27	20-May-26		0.00	27,642.87	0.00
FIRST STAGE		77	86,114.12	21-Oct-26	02-Dec-26	20-May-26		0.00	27,642.87	0.00
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	21-Oct-26	25-Oct-26	21-May-26		0.00	884.15	0.00
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	2,920.45	21-Oct-26	29-Oct-26	21-May-26		0.00	1,460.23	0.00
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	04-Nov-26	08-Nov-26	08-Sep-26		0.00	7,616.67	0.00
DAM3-C-B9-E-233	Installation of Wires	4	16,925.94	09-Nov-26	12-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-223	Installation of LV Cables	4	36,389.98	23-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	19,646.47	28-Nov-26	02-Dec-26	20-May-26		0.00	17,681.82	0.00
SECOND STAGE		71	665,930.64	26-Oct-26	31-Jan-27			0.00	0.00	0.00
DAM3-C-B9-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	26-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B9-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	31-Oct-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-153	Installation of Lighting fixtures	4	76,166.74	14-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-193	Installation of Main Distribution Board	2	32,472.73	14-Nov-26	15-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-410	Installation of CCTV System	5	76,349.24	14-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-243	Installation of LP-1 Panel	2	18,403.54	16-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-253	Installation of PP-AC panel	2	21,648.48	18-Nov-26	19-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-213	Installation of Telephone Cabinet	2	26,991.08	21-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-273	Installation of Access Control System	5	27,616.86	22-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-283	Monitor Modules for Fire Alarm	2	3,882.38	28-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B9-E-293	Line Isolator Modules for Fire Alarm	2	185.40	30-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-B9-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	02-Dec-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B9-E-173	Installation of Wiring Devices	4	19,435.09	16-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B9-E-203	Installation of Disconnect Switches	2	30,235.95	21-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-B9-E-420	Installation of Solar power plant	8	253,268.71	16-Jan-27	31-Jan-27			0.00	0.00	0.00
BLOCK B10		293	5,075,523.09	03-Mar-26	08-Feb-27	18-Feb-26		2,687,335.31	3,297,670.78	1.23
STRUCTURAL		202	1,389,042.53	03-Mar-26	24-Oct-26	18-Feb-26		1,388,135.41	1,388,135.41	1.00
FOOTING		55	597,655.16	03-Mar-26	04-Apr-26	18-Feb-26	28-Apr-26	597,655.16	597,655.16	1.00
DAM3-C-B10-S-150	Excavation for footings	4	89,859.61	03-Mar-26	07-Mar-26	18-Feb-26	03-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B10-S-6323	Soil replacement - rock fill	4	179,061.91	08-Mar-26	11-Mar-26	07-Mar-26	11-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B10-S-6333	Engineering fill	4	46,046.19	12-Mar-26	16-Mar-26	18-Mar-26	31-Mar-26	46,046.19	46,046.19	1.00
DAM3-C-B10-S-101	Anti Termite Below Footings	1	11,905.55	21-Mar-26	21-Mar-26	01-Apr-26	01-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B10-S-102	Vapour Barrier for Footings	1	7,940.10	22-Mar-26	22-Mar-26	01-Apr-26	01-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B10-S-103	Lean Concrete Below Footings	2	8,229.34	23-Mar-26	24-Mar-26	01-Apr-26	01-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B10-S-104	Rebar for Footings	4	101,844.98	25-Mar-26	29-Mar-26	23-Apr-26	23-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B10-S-105	Formwork for Footings	4	25,461.25	30-Mar-26	02-Apr-26	23-Apr-26	25-Apr-26	25,461.25	25,461.25	1.00
DAM3-C-B10-S-106	Pouring Concrete for Footings	1	127,306.23	04-Apr-26	04-Apr-26	28-Apr-26	28-Apr-26	127,306.23	127,306.23	1.00
COLUMN NECK		17	120,554.54	05-Apr-26	22-Apr-26	26-Apr-26	20-May-26	120,554.54	120,554.54	1.00
DAM3-C-B10-S-257	Rebar for column neck	4	14,919.19	05-Apr-26	08-Apr-26	26-Apr-26	27-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B10-S-267	Formwork for column neck	2	9,946.13	09-Apr-26	11-Apr-26	27-Apr-26	04-May-26	9,946.13	9,946.13	1.00
DAM3-C-B10-S-297	Pouring Concrete for column neck	1	24,865.31	12-Apr-26	12-Apr-26	02-May-26	05-May-26	24,865.31	24,865.31	1.00
DAM3-C-B10-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	13-Apr-26	14-Apr-26	05-May-26	09-May-26	24,777.73	24,777.73	1.00
DAM3-C-B10-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	15-Apr-26	22-Apr-26	13-May-26	20-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		16	171,632.86	23-Apr-26	13-May-26	25-May-26	15-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B10-S-527	Anti Termite Below Grade Beams	1	11,905.55	23-Apr-26	23-Apr-26	25-May-26	25-May-26	11,905.55	11,905.55	1.00
DAM3-C-B10-S-337	Vapour barrier for Grade Beams	2	5,293.40	25-Apr-26	26-Apr-26	25-May-26	25-May-26	5,293.40	5,293.40	1.00
DAM3-C-B10-S-338	Lean Concrete Below Grade Beams	2	4,431.19	27-Apr-26	28-Apr-26	25-May-26	25-May-26	4,431.19	4,431.19	1.00
DAM3-C-B10-S-339	Rebar for Grade Beams	5	27,194.46	29-Apr-26	04-May-26	31-May-26	03-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B10-S-340	Formwork for Grade Beams	2	6,798.61	05-May-26	06-May-26	07-Jun-26	09-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B10-S-341	Anchor bolts installation	2	57,238.83	05-May-26	06-May-26	02-Jun-26	03-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B10-S-342	Pouring Concrete for Grade Beams	1	33,993.09	07-May-26	07-May-26	09-Jun-26	09-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B10-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	09-May-26	13-May-26	14-Jun-26	15-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		115	397,232.98	14-May-26	24-Oct-26	16-Jun-26		396,325.87	396,325.87	1.00
DAM3-C-B10-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	14-May-26	21-May-26	16-Jun-26	22-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B10-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	23-May-26	23-May-26	18-Jul-26	21-Jul-26	15,874.08	15,874.08	1.00
DAM3-C-B10-S-379	Vapour barrier for below Ground Slab	2	13,233.49	24-May-26	25-May-26	18-Jul-26	21-Jul-26	13,233.49	13,233.49	1.00
DAM3-C-B10-S-382	Pouring Concrete for Ground Slab	4	344,195.21	30-May-26	02-Jun-26	18-Jul-26	21-Jul-26	344,195.21	344,195.21	1.00
DAM3-C-B10-S-517	Concrete pad	7	907.11	17-Oct-26	24-Oct-26			0.00	0.00	0.00
COLUMNS & BEAMS		55	101,966.98	23-May-26	22-Jun-26	01-Jun-26	16-Sep-26	101,966.98	101,966.98	1.00

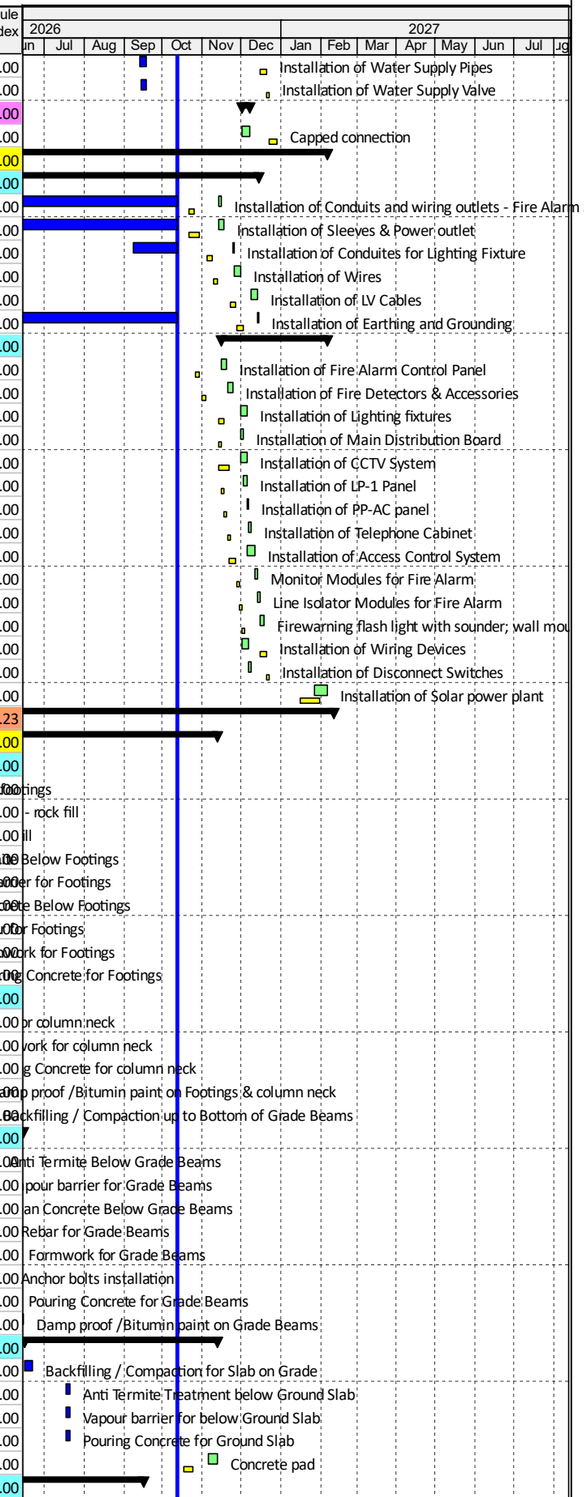

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B10-S-5101	Rebar for column	5	20,144.05	23-May-26	31-May-26	12-Jul-26	16-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B10-S-5102	Formwork for column	4	5,036.01	01-Jun-26	04-Jun-26	04-Aug-26	06-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B10-S-5103	Pouring Concrete for column	1	25,180.06	06-Jun-26	06-Jun-26	05-Aug-26	09-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B10-S-6101	Rebar for Tie Beams	4	7,263.64	07-Jun-26	10-Jun-26	01-Jun-26	03-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B10-S-6102	Formwork for Tie Beams	2	1,815.91	11-Jun-26	13-Jun-26	07-Jun-26	08-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B10-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	14-Jun-26	14-Jun-26	09-Jun-26	09-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B10-S-6113	Rebar for Beams	4	13,379.11	15-Jun-26	18-Jun-26	31-Aug-26	02-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B10-S-6123	Formwork for Beams	2	3,344.77	20-Jun-26	21-Jun-26	08-Sep-26	15-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B10-S-6133	Pouring Concrete for Beams	1	16,723.88	22-Jun-26	22-Jun-26	12-Sep-26	16-Sep-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		48	1,566,668.48	12-Sep-26	21-Oct-26	25-Jun-26		1,218,745.08	1,539,773.29	1.26
DAM3-C-B10-SS-0100	Installation of columns	3	217,507.55	12-Sep-26	14-Sep-26	25-Jun-26	25-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B10-SS-0110	Installation of raft and purlins	5	326,261.32	15-Sep-26	20-Sep-26	25-Jun-26	28-Jun-26	326,261.32	326,261.32	1.00
DAM3-C-B10-SS-610	Intumescent paint to steel works	7	317,759.56	21-Sep-26	29-Sep-26	07-Jul-26	11-Aug-26	317,759.56	317,759.56	1.00
DAM3-C-B10-SS-620	Steel members for office area	4	115,805.20	30-Sep-26	07-Oct-26	29-Sep-26	30-Sep-26	115,805.20	115,805.20	1.00
DAM3-C-B10-SS-0140	Installation of roof sheet	3	217,507.55	04-Oct-26	08-Oct-26	13-Aug-26	16-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B10-SS-1020	Epoxy paint to steel members at office area	4	23,161.04	08-Oct-26	15-Oct-26			13,234.88	0.00	0.00
DAM3-C-B10-SS-1030	Steel members for external platform	7	18,670.78	08-Oct-26	15-Oct-26	26-Sep-26	06-Oct-26	10,669.02	18,670.78	1.75
DAM3-C-B10-SS-0130	Installation of wall sandwich panel	5	326,261.32	17-Oct-26	21-Oct-26	03-Sep-26	30-Sep-26	0.00	326,261.32	0.00
DAM3-C-B10-SS-1040	Epoxy paint for external platform	5	3,734.16	17-Oct-26	21-Oct-26			0.00	0.00	0.00
ARCHITECTURAL		87	900,244.66	21-Sep-26	16-Jan-27	23-Jul-26		61,869.68	185,838.42	3.00
MASONARY WORKS		20	78,954.21	21-Sep-26	24-Oct-26	02-Aug-26	03-Sep-26	61,869.68	78,954.21	1.28
DAM3-C-B10-A-0120	Block work at factory area	3	58,338.72	21-Sep-26	03-Oct-26	02-Aug-26	23-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B10-A-0150	Block work at office area	4	6,179.18	08-Oct-26	15-Oct-26	08-Aug-26	01-Sep-26	3,530.96	6,179.18	1.75
DAM3-C-B10-A-170	Block work at toilet area	5	14,436.31	17-Oct-26	24-Oct-26	11-Aug-26	03-Sep-26	0.00	14,436.31	0.00
WALL FINISHES		31	92,757.47	03-Nov-26	19-Dec-26	21-Sep-26		0.00	70,673.82	0.00
DAM3-C-B10-A-180	Internal Wall Plaster	5	48,590.16	03-Nov-26	19-Nov-26	21-Sep-26	12-Oct-26	0.00	48,590.16	0.00
DAM3-C-B10-A-230	Paint to Plaster (Primer, Putty & First Coat)	5	44,167.30	12-Dec-26	19-Dec-26	08-Oct-26		0.00	22,083.65	0.00
CIELING FINISHES		4	46,792.30	03-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-240	Installation of Ceiling Gypsum Board	4	46,792.30	03-Dec-26	08-Dec-26			0.00	0.00	0.00
FLOOR FINISHES		25	189,488.90	25-Nov-26	16-Jan-27	11-Oct-26		0.00	23,265.35	0.00
DAM3-C-B10-A-220	Tiles for Toilet	5	46,530.71	25-Nov-26	02-Dec-26	11-Oct-26		0.00	23,265.35	0.00
DAM3-C-B10-A-250	Tiles for Office Area	2	26,867.31	09-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-390	Granite strip	2	671.12	12-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-420	Epoxy paint	3	115,419.76	09-Jan-27	16-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		21	248,575.06	22-Oct-26	07-Nov-26	04-Oct-26		0.00	6,489.89	0.00
DAM3-C-B10-A-552	Window (CW1)	7	94,173.21	22-Oct-26	29-Oct-26			0.00	0.00	0.00
DAM3-C-B10-A-553	Roll up Shutter Door	1	68,619.20	31-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-B10-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	01-Nov-26	01-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	02-Nov-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	03-Nov-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	04-Nov-26	04-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	05-Nov-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-558	Skylight fixtures installation	1	6,489.89	07-Nov-26	07-Nov-26	04-Oct-26	06-Oct-26	0.00	6,489.89	0.00
WATER PROOFING WORKS		4	4,879.02	21-Nov-26	24-Nov-26			0.00	0.00	0.00
DAM3-C-B10-A-370	Waterproofing membrane for toilets	4	4,879.02	21-Nov-26	24-Nov-26			0.00	0.00	0.00
METAL WORKS		64	193,717.06	14-Dec-26	28-Dec-26	23-Jul-26		0.00	6,455.16	0.00
DAM3-C-B10-A-290	Steel Ladder	2	9,839.16	14-Dec-26	15-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-291	Steel railing works	3	1,533.98	16-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-292	Aluminium composite panel	3	175,888.76	21-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B10-A-300	Galvanised Steel Gratings	2	6,455.16	27-Dec-26	28-Dec-26	23-Jul-26	23-Jul-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	29-Dec-26	07-Jan-27			0.00	0.00	0.00
DAM3-C-B10-A-320	Installation of fittings	3	22,981.27	29-Dec-26	03-Jan-27			0.00	0.00	0.00
DAM3-C-B10-A-570	Identification sign; ID01 & ID02	3	9,630.56	04-Jan-27	06-Jan-27			0.00	0.00	0.00
DAM3-C-B10-A-340	Furniture Installation	1	12,468.83	07-Jan-27	07-Jan-27			0.00	0.00	0.00
MECHANICAL		168	467,522.66	14-May-26	07-Jan-27	01-Jul-26		18,585.14	156,280.78	8.41
HVAC		14	233,183.33	20-Dec-26	04-Jan-27			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	27-Dec-26	30-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-140	Installation of HVAC Ducts	2	149,489.33	27-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-170	Installation of Duct insulation	2	21,205.40	29-Dec-26	30-Dec-26			0.00	0.00	0.00
SECOND STAGE		14	62,488.60	20-Dec-26	04-Jan-27			0.00	0.00	0.00
DAM3-C-B10-M-130	Installation of Exhaust Fans	2	7,938.56	20-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-160	Installation of Wall Propeller Type Exhaust Fan	4	46,831.64	22-Dec-26	26-Dec-26			0.00	0.00	0.00

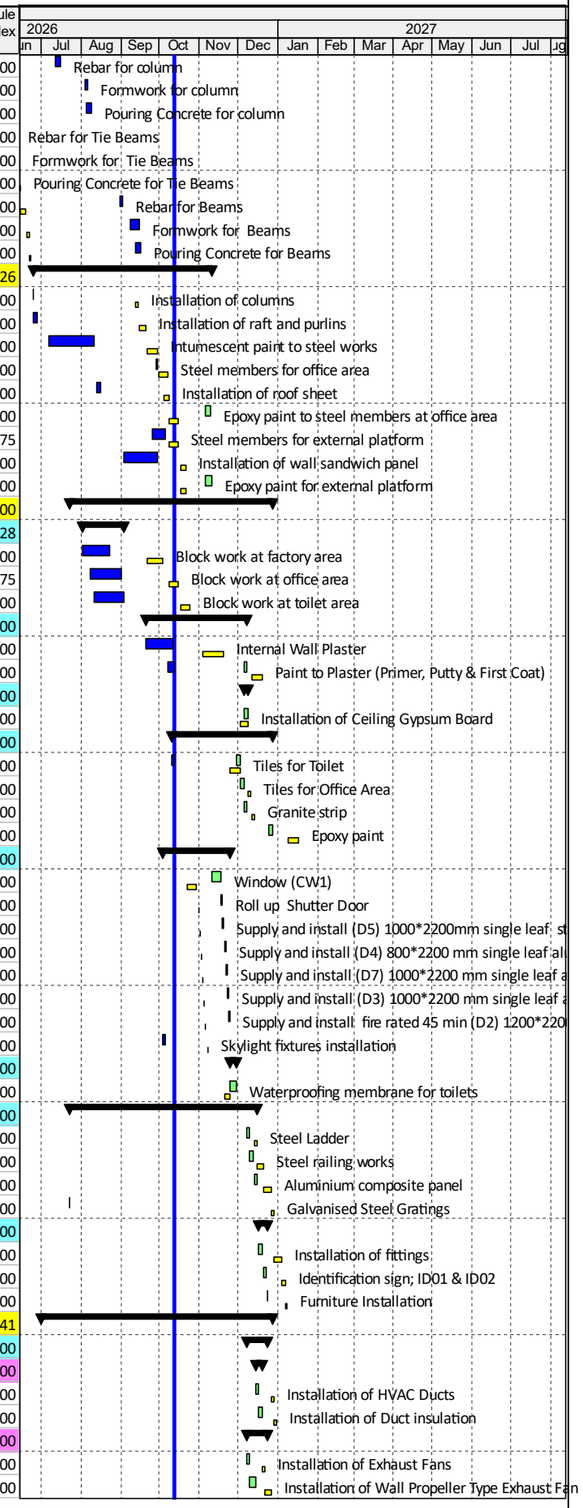

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B10-M-339	Installation of Diffuser	2	2,144.00	31-Dec-26	02-Jan-27			0.00	0.00	0.00
DAM3-C-B10-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	03-Jan-27	04-Jan-27			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		17	102,458.78	20-Dec-26	07-Jan-27	23-Aug-26		0.00	84,594.16	0.00
FIRST STAGE		8	84,594.16	20-Dec-26	02-Jan-27	23-Aug-26	29-Aug-26	0.00	84,594.16	0.00
DAM3-C-B10-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	72,394.75	20-Dec-26	27-Dec-26	23-Aug-26	27-Aug-26	0.00	72,394.75	0.00
DAM3-C-B10-M-310	Installation of Fire Fighting Valve	3	12,199.40	28-Dec-26	02-Jan-27	25-Aug-26	29-Aug-26	0.00	12,199.40	0.00
SECOND STAGE		17	17,864.62	03-Jan-27	07-Jan-27			0.00	0.00	0.00
DAM3-C-B10-M-320	Installation of Fire Hose Cabinet	3	15,158.56	03-Jan-27	05-Jan-27			0.00	0.00	0.00
DAM3-C-B10-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	05-Jan-27	07-Jan-27			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		168	90,009.74	14-May-26	27-Dec-26	01-Jul-26		18,585.14	30,093.94	1.62
FIRST STAGE		168	41,149.90	14-May-26	10-Dec-26	01-Jul-26		18,585.14	30,093.94	1.62
DAM3-C-B10-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	14-May-26	18-May-26	01-Jul-26	06-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B10-M-220	Installation of Floor Drain	2	11,055.96	03-Dec-26	05-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-380	Installation of Trench drain	5	11,508.80	06-Dec-26	10-Dec-26	07-Jul-26	09-Jul-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	12-Dec-26	27-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-180	Installation of Electric Water Heater	2	1,819.51	12-Dec-26	13-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	14-Dec-26	17-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	19-Dec-26	20-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-270	Installation of Bib Tap	2	1,900.66	21-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-428	Installation of Water Tap	2	2,874.14	23-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-429	Installation of Roof Vent Cap	2	927.12	26-Dec-26	27-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		15	41,870.81	20-Dec-26	31-Dec-26	17-Sep-26		0.00	41,592.68	0.00
FIRST STAGE		6	41,592.68	20-Dec-26	26-Dec-26	17-Sep-26	21-Sep-26	0.00	41,592.68	0.00
DAM3-C-B10-M-290	Installation of Water Supply Pipes	4	23,318.41	20-Dec-26	23-Dec-26	17-Sep-26	21-Sep-26	0.00	23,318.41	0.00
DAM3-C-B10-M-280	Installation of Water Supply Valve	2	18,274.27	24-Dec-26	26-Dec-26	17-Sep-26	21-Sep-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	27-Dec-26	31-Dec-26			0.00	0.00	0.00
DAM3-C-B10-M-330	Capped connection	5	278.13	27-Dec-26	31-Dec-26			0.00	0.00	0.00
ELECTRICAL		96	752,044.76	25-Oct-26	08-Feb-27	02-Jun-26		0.00	27,642.87	0.00
FIRST STAGE		88	86,114.12	25-Oct-26	06-Dec-26	02-Jun-26		0.00	27,642.87	0.00
DAM3-C-B10-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	25-Oct-26	28-Oct-26	03-Jun-26		0.00	884.15	0.00
DAM3-C-B10-E-183	Installation of Sleeves & Power outlet	4	2,920.45	25-Oct-26	02-Nov-26	03-Jun-26		0.00	1,460.23	0.00
DAM3-C-B10-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	08-Nov-26	11-Nov-26	21-Sep-26		0.00	7,616.67	0.00
DAM3-C-B10-E-233	Installation of Wires	4	16,925.94	12-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-223	Installation of LV Cables	4	36,389.98	26-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-113	Installation of Earthing and Grounding	5	19,646.47	01-Dec-26	06-Dec-26	02-Jun-26		0.00	17,681.82	0.00
SECOND STAGE		83	665,930.64	29-Oct-26	08-Feb-27			0.00	0.00	0.00
DAM3-C-B10-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	29-Oct-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	03-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-153	Installation of Lighting fixtures	4	76,166.74	17-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-193	Installation of Main Distribution Board	2	32,472.73	17-Nov-26	18-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-410	Installation of CCTV System	7	76,349.24	17-Nov-26	24-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-243	Installation of LP-1 Panel	2	18,403.54	19-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-253	Installation of PP-AC panel	2	21,648.48	22-Nov-26	23-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-213	Installation of Telephone Cabinet	2	26,991.08	24-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-273	Installation of Access Control System	5	27,616.86	25-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-B10-E-283	Monitor Modules for Fire Alarm	2	3,882.38	01-Dec-26	02-Dec-26			0.00	0.00	0.00
DAM3-C-B10-E-293	Line Isolator Modules for Fire Alarm	2	185.40	03-Dec-26	05-Dec-26			0.00	0.00	0.00
DAM3-C-B10-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	06-Dec-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-B10-E-173	Installation of Wiring Devices	4	19,435.09	20-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B10-E-203	Installation of Disconnect Switches	2	30,235.95	24-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B10-E-420	Installation of Solar power plant	5	253,268.71	01-Feb-27	08-Feb-27			0.00	0.00	0.00
BLOCK B11		288	5,075,523.09	08-Mar-26	16-Feb-27	18-Feb-26		2,666,759.17	3,209,355.91	1.20
STRUCTURAL		196	1,389,042.53	08-Mar-26	27-Oct-26	18-Feb-26		1,388,135.41	1,388,135.41	1.00
FOOTING		36	597,655.16	08-Mar-26	08-Apr-26	18-Feb-26	02-May-26	597,655.16	597,655.16	1.00
DAM3-C-B11-S-150	Excavation for footings	4	89,859.61	08-Mar-26	11-Mar-26	18-Feb-26	08-Mar-26	89,859.61	89,859.61	1.00
DAM3-C-B11-S-6343	Soil replacement - rock fill	4	179,061.91	12-Mar-26	16-Mar-26	08-Mar-26	16-Mar-26	179,061.91	179,061.91	1.00
DAM3-C-B11-S-6353	Engineering fill	4	46,046.19	21-Mar-26	24-Mar-26	26-Mar-26	31-Mar-26	46,046.19	46,046.19	1.00
DAM3-C-B11-S-101	Anti Termite Below Footings	1	11,905.55	25-Mar-26	25-Mar-26	02-Apr-26	02-Apr-26	11,905.55	11,905.55	1.00
DAM3-C-B11-S-102	Vapour Barrier for Footings	1	7,940.10	26-Mar-26	26-Mar-26	02-Apr-26	02-Apr-26	7,940.10	7,940.10	1.00
DAM3-C-B11-S-103	Lean Concrete Below Footings	2	8,229.34	28-Mar-26	29-Mar-26	02-Apr-26	02-Apr-26	8,229.34	8,229.34	1.00
DAM3-C-B11-S-104	Rebar for Footings	4	101,844.98	30-Mar-26	02-Apr-26	25-Apr-26	28-Apr-26	101,844.98	101,844.98	1.00
DAM3-C-B11-S-105	Formwork for Footings	4	25,461.25	04-Apr-26	07-Apr-26	28-Apr-26	29-Apr-26	25,461.25	25,461.25	1.00

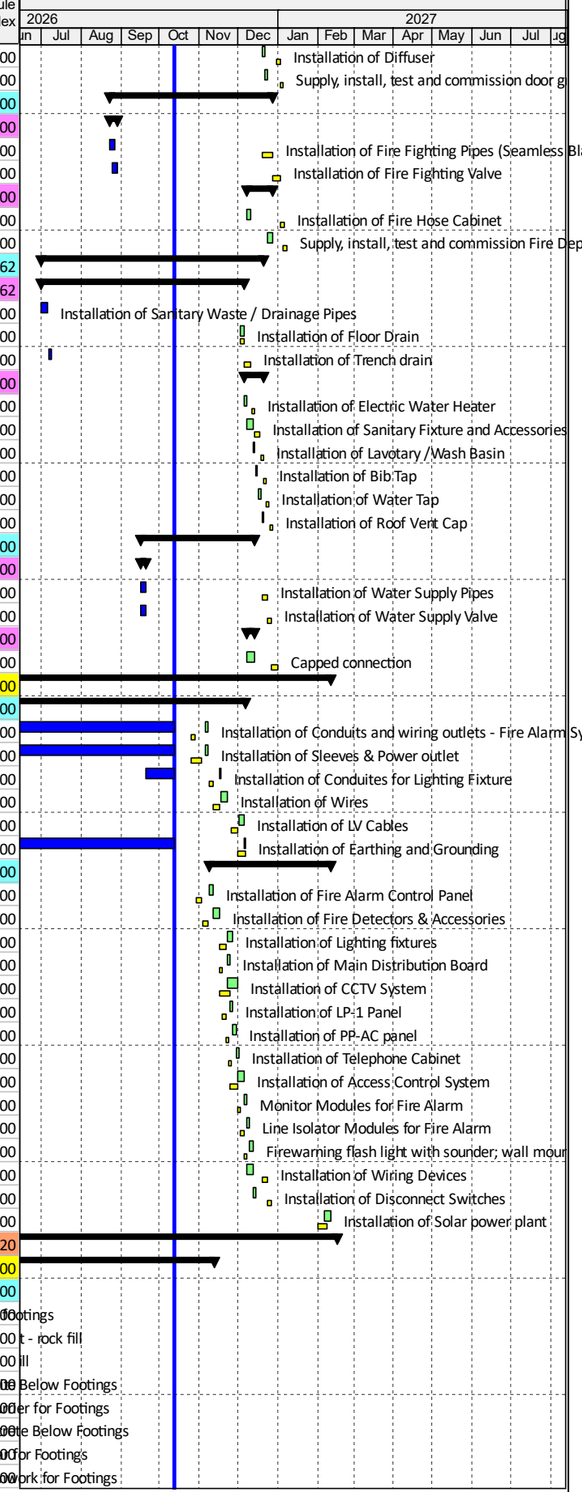

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B11-S-106	Pouring Concrete for Footings	1	127,306.23	08-Apr-26	08-Apr-26	02-May-26	02-May-26	127,306.23	127,306.23	1.00
COLUMN NECK		19	120,554.54	09-Apr-26	27-Apr-26	27-Apr-26	20-May-26	120,554.54	120,554.54	1.00
DAM3-C-B11-S-257	Rebar for column neck	4	14,919.19	09-Apr-26	13-Apr-26	27-Apr-26	28-Apr-26	14,919.19	14,919.19	1.00
DAM3-C-B11-S-267	Formwork for column neck	2	9,946.13	14-Apr-26	15-Apr-26	05-May-26	06-May-26	9,946.13	9,946.13	1.00
DAM3-C-B11-S-297	Pouring Concrete for column neck	1	24,865.31	16-Apr-26	16-Apr-26	07-May-26	07-May-26	24,865.31	24,865.31	1.00
DAM3-C-B11-S-307	Damp proof /Bitumin paint on Footings & column neck	2	24,777.73	18-Apr-26	19-Apr-26	11-May-26	13-May-26	24,777.73	24,777.73	1.00
DAM3-C-B11-S-367	Backfilling / Compaction up to Bottom of Grade Beams	7	46,046.19	20-Apr-26	27-Apr-26	17-May-26	20-May-26	46,046.19	46,046.19	1.00
GRADE BEAM		18	171,632.86	28-Apr-26	18-May-26	24-May-26	13-Jun-26	171,632.86	171,632.86	1.00
DAM3-C-B11-S-527	Anti Termite Below Grade Beams	1	11,905.55	28-Apr-26	28-Apr-26	24-May-26	24-May-26	11,905.55	11,905.55	1.00
DAM3-C-B11-S-337	Vapour barrier for Grade Beams	2	5,293.40	29-Apr-26	30-Apr-26	24-May-26	24-May-26	5,293.40	5,293.40	1.00
DAM3-C-B11-S-338	Lean Concrete Below Grade Beams	2	4,431.19	02-May-26	03-May-26	24-May-26	24-May-26	4,431.19	4,431.19	1.00
DAM3-C-B11-S-339	Rebar for Grade Beams	5	27,194.46	04-May-26	09-May-26	01-Jun-26	03-Jun-26	27,194.46	27,194.46	1.00
DAM3-C-B11-S-340	Formwork for Grade Beams	2	6,798.61	10-May-26	11-May-26	02-Jun-26	06-Jun-26	6,798.61	6,798.61	1.00
DAM3-C-B11-S-341	Anchor bolts installation	2	57,238.83	10-May-26	11-May-26	02-Jun-26	03-Jun-26	57,238.83	57,238.83	1.00
DAM3-C-B11-S-342	Pouring Concrete for Grade Beams	1	33,993.09	12-May-26	12-May-26	06-Jun-26	06-Jun-26	33,993.09	33,993.09	1.00
DAM3-C-B11-S-347	Damp proof /Bitumin paint on Grade Beams	5	24,777.73	13-May-26	18-May-26	11-Jun-26	13-Jun-26	24,777.73	24,777.73	1.00
SLAB ON GRADE		128	397,232.98	19-May-26	27-Oct-26	15-Jun-26		396,325.87	396,325.87	1.00
DAM3-C-B11-S-377	Backfilling / Compaction for Slab on Grade	7	23,023.09	19-May-26	30-May-26	15-Jun-26	21-Jun-26	23,023.09	23,023.09	1.00
DAM3-C-B11-S-378	Anti Termite Treatment below Ground Slab	1	15,874.08	31-May-26	31-May-26	26-Jul-26	28-Jul-26	15,874.08	15,874.08	1.00
DAM3-C-B11-S-379	Vapour barrier for below Ground Slab	2	13,233.49	01-Jun-26	02-Jun-26	26-Jul-26	28-Jul-26	13,233.49	13,233.49	1.00
DAM3-C-B11-S-382	Pouring Concrete for Ground Slab	4	344,195.21	03-Jun-26	07-Jun-26	26-Jul-26	28-Jul-26	344,195.21	344,195.21	1.00
DAM3-C-B11-S-517	Concrete pad	7	907.11	20-Oct-26	27-Oct-26			0.00	0.00	0.00
COLUMNS & BEAMS		81	101,966.98	31-May-26	27-Jun-26	02-Jun-26	01-Oct-26	101,966.98	101,966.98	1.00
DAM3-C-B11-S-5101	Rebar for column	5	20,144.05	31-May-26	04-Jun-26	13-Jul-26	16-Jul-26	20,144.05	20,144.05	1.00
DAM3-C-B11-S-5102	Formwork for column	4	5,036.01	06-Jun-26	09-Jun-26	08-Aug-26	11-Aug-26	5,036.01	5,036.01	1.00
DAM3-C-B11-S-5103	Pouring Concrete for column	1	25,180.06	10-Jun-26	10-Jun-26	09-Aug-26	12-Aug-26	25,180.06	25,180.06	1.00
DAM3-C-B11-S-6101	Rebar for Tie Beams	4	7,263.64	11-Jun-26	15-Jun-26	02-Jun-26	08-Jun-26	7,263.64	7,263.64	1.00
DAM3-C-B11-S-6102	Formwork for Tie Beams	2	1,815.91	16-Jun-26	17-Jun-26	03-Jun-26	08-Jun-26	1,815.91	1,815.91	1.00
DAM3-C-B11-S-6103	Pouring Concrete for Tie Beams	1	9,079.54	18-Jun-26	18-Jun-26	06-Jun-26	09-Jun-26	9,079.54	9,079.54	1.00
DAM3-C-B11-S-6113	Rebar for Beams	4	13,379.11	20-Jun-26	23-Jun-26	01-Sep-26	03-Sep-26	13,379.11	13,379.11	1.00
DAM3-C-B11-S-6123	Formwork for Beams	2	3,344.77	24-Jun-26	25-Jun-26	21-Sep-26	26-Sep-26	3,344.77	3,344.77	1.00
DAM3-C-B11-S-6133	Pouring Concrete for Beams	1	16,723.88	27-Jun-26	27-Jun-26	28-Sep-26	01-Oct-26	16,723.88	16,723.88	1.00
STRUCTURAL STEEL		45	1,566,668.48	15-Sep-26	25-Oct-26	25-Jun-26		1,200,817.16	1,521,102.51	1.27
DAM3-C-B11-SS-0100	Installation of columns	3	217,507.55	15-Sep-26	17-Sep-26	25-Jun-26	28-Jun-26	217,507.55	217,507.55	1.00
DAM3-C-B11-SS-0110	Installation of raft and purlins	5	326,261.32	19-Sep-26	24-Sep-26	30-Jun-26	01-Jul-26	326,261.32	326,261.32	1.00
DAM3-C-B11-SS-610	Intumescent paint to steel works	7	317,759.56	26-Sep-26	03-Oct-26	19-Jul-26	25-Jul-26	317,759.56	317,759.56	1.00
DAM3-C-B11-SS-620	Steel members for office area	7	115,805.20	04-Oct-26	11-Oct-26	27-Sep-26	30-Sep-26	115,805.20	115,805.20	1.00
DAM3-C-B11-SS-0140	Installation of roof sheet	5	217,507.55	07-Oct-26	12-Oct-26	01-Aug-26	08-Aug-26	217,507.55	217,507.55	1.00
DAM3-C-B11-SS-1020	Epoxy paint to steel members at office area	4	23,161.04	12-Oct-26	19-Oct-26			3,308.72	0.00	0.00
DAM3-C-B11-SS-1030	Steel members for external platform	7	18,670.78	12-Oct-26	19-Oct-26			2,667.25	0.00	0.00
DAM3-C-B11-SS-0130	Installation of wall sandwich panel	5	326,261.32	20-Oct-26	25-Oct-26	03-Sep-26	30-Sep-26	0.00	326,261.32	0.00
DAM3-C-B11-SS-1040	Epoxy paint for external platform	5	3,734.16	20-Oct-26	25-Oct-26			0.00	0.00	0.00
ARCHITECTURAL		94	900,244.66	26-Sep-26	19-Jan-27	30-Jul-26		59,221.46	116,194.34	1.96
MASONARY WORKS		21	78,954.21	26-Sep-26	27-Oct-26	06-Aug-26	06-Sep-26	59,221.46	78,954.21	1.33
DAM3-C-B11-A-0120	Block work at factory area	5	58,338.72	26-Sep-26	06-Oct-26	06-Aug-26	11-Aug-26	58,338.72	58,338.72	1.00
DAM3-C-B11-A-0150	Block work at office area	3	6,179.18	12-Oct-26	19-Oct-26	10-Aug-26	06-Sep-26	882.74	6,179.18	7.00
DAM3-C-B11-A-170	Block work at toilet area	4	14,436.31	20-Oct-26	27-Oct-26	13-Aug-26	06-Sep-26	0.00	14,436.31	0.00
WALL FINISHES		14	92,757.47	07-Nov-26	22-Dec-26	27-Sep-26		0.00	24,295.08	0.00
DAM3-C-B11-A-180	Internal Wall Plaster	10	48,590.16	07-Nov-26	23-Nov-26	27-Sep-26		0.00	24,295.08	0.00
DAM3-C-B11-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	44,167.30	15-Dec-26	22-Dec-26			0.00	0.00	0.00
CIELING FINISHES		5	46,792.30	07-Dec-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-240	Installation of Ceiling Gypsum Board	5	46,792.30	07-Dec-26	12-Dec-26			0.00	0.00	0.00
FLOOR FINISHES		17	189,488.90	29-Nov-26	19-Jan-27			0.00	0.00	0.00
DAM3-C-B11-A-220	Tiles for Toilet	5	46,530.71	29-Nov-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-250	Tiles for Office Area	2	26,867.31	13-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-390	Granite strip	2	671.12	15-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-420	Epoxy paint	7	115,419.76	12-Jan-27	19-Jan-27			0.00	0.00	0.00
DOORS & WINDOWS		22	248,575.06	26-Oct-26	10-Nov-26	06-Oct-26		0.00	6,489.89	0.00
DAM3-C-B11-A-552	Window (CW1)	7	94,173.21	26-Oct-26	02-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-553	Roll up Shutter Door	1	68,619.20	03-Nov-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-200	Supply and install (D5) 1000*2200mm single leaf steel door with do	1	16,016.16	04-Nov-26	04-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-554	Supply and install (D4) 800*2200 mm single leaf aluminum door wit	1	22,737.85	05-Nov-26	05-Nov-26			0.00	0.00	0.00

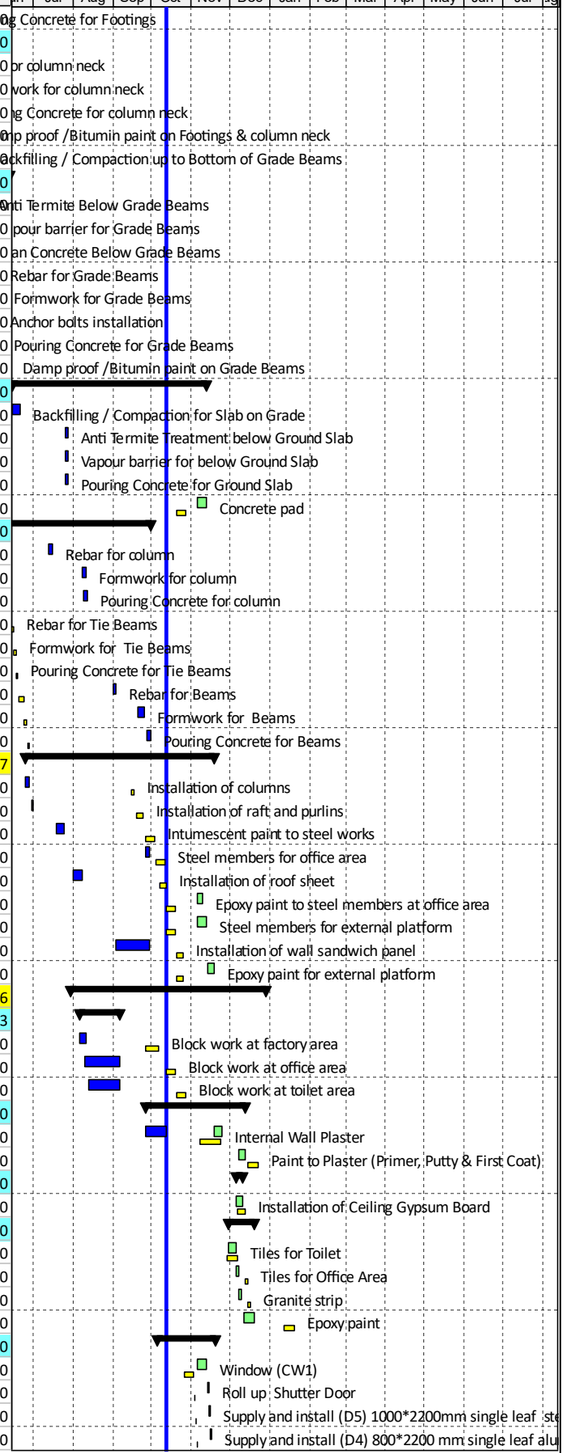

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B11-A-555	Supply and install (D7) 1000*2200 mm single leaf aluminum door wi	1	7,811.07	07-Nov-26	07-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-556	Supply and install (D3) 1000*2200 mm single leaf aluminum door wi	1	16,016.16	08-Nov-26	08-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-557	Supply and install fire rated 45 min (D2) 1200*2200 mm single leaf	1	16,711.52	09-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-558	Skylight fixtures installation	1	6,489.89	10-Nov-26	10-Nov-26	06-Oct-26	08-Oct-26	0.00	6,489.89	0.00
WATER PROOFING WORKS		4	4,879.02	24-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B11-A-370	Waterproofing membrane for toilets	4	4,879.02	24-Nov-26	28-Nov-26			0.00	0.00	0.00
METAL WORKS		64	193,717.06	17-Dec-26	31-Dec-26	30-Jul-26		0.00	6,455.16	0.00
DAM3-C-B11-A-290	Steel Ladder	2	9,839.16	17-Dec-26	19-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-291	Steel railing works	4	1,533.98	20-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-292	Aluminium composite panel	3	175,888.76	24-Dec-26	29-Dec-26			0.00	0.00	0.00
DAM3-C-B11-A-300	Galvanised Steel Gratings	2	6,455.16	30-Dec-26	31-Dec-26	30-Jul-26	30-Jul-26	0.00	6,455.16	0.00
SPECIALTIES		7	45,080.66	02-Jan-27	11-Jan-27			0.00	0.00	0.00
DAM3-C-B11-A-320	Installation of fittings	3	22,981.27	02-Jan-27	06-Jan-27			0.00	0.00	0.00
DAM3-C-B11-A-570	Identification sign; ID01 & ID02	3	9,630.56	07-Jan-27	10-Jan-27			0.00	0.00	0.00
DAM3-C-B11-A-340	Furniture Installation	1	12,468.83	11-Jan-27	11-Jan-27			0.00	0.00	0.00
MECHANICAL		182	467,522.66	19-May-26	11-Jan-27	05-Jul-26		18,585.14	156,280.78	8.41
HVAC		13	233,183.33	23-Dec-26	07-Jan-27			0.00	0.00	0.00
FIRST STAGE		4	170,694.73	30-Dec-26	03-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-140	Installation of HVAC Ducts	2	149,489.33	30-Dec-26	31-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-170	Installation of Duct insulation	2	21,205.40	02-Jan-27	03-Jan-27			0.00	0.00	0.00
SECOND STAGE		13	62,488.60	23-Dec-26	07-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-130	Installation of Exhaust Fans	2	7,938.56	23-Dec-26	24-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-160	Installation of Wall Propeller Type Exhaust Fan	3	46,831.64	26-Dec-26	29-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-339	Installation of Diffuser	2	2,144.00	04-Jan-27	05-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-340	Supply, install, test and commission door grilles & exhaust louvers	2	5,574.40	06-Jan-27	07-Jan-27			0.00	0.00	0.00
FIRE FIGHTING SYSTEM		17	102,458.78	23-Dec-26	11-Jan-27	29-Aug-26		0.00	84,594.16	0.00
FIRST STAGE		8	84,594.16	23-Dec-26	05-Jan-27	29-Aug-26	07-Sep-26	0.00	84,594.16	0.00
DAM3-C-B11-M-300	Installation of Fire Fighting Pipes (Seamless Black Steel)	5	72,394.75	23-Dec-26	30-Dec-26	29-Aug-26	05-Sep-26	0.00	72,394.75	0.00
DAM3-C-B11-M-310	Installation of Fire Fighting Valve	3	12,199.40	31-Dec-26	05-Jan-27	30-Aug-26	07-Sep-26	0.00	12,199.40	0.00
SECOND STAGE		16	17,864.62	06-Jan-27	11-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-320	Installation of Fire Hose Cabinet	3	15,158.56	06-Jan-27	09-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-370	Supply, install, test and commission Fire Department Connection(FDC)	3	2,706.06	09-Jan-27	11-Jan-27			0.00	0.00	0.00
SEWER AND DRAINAGE SYSTEM		182	90,009.74	19-May-26	30-Dec-26	05-Jul-26		18,585.14	30,093.94	1.62
FIRST STAGE		182	41,149.90	19-May-26	14-Dec-26	05-Jul-26		18,585.14	30,093.94	1.62
DAM3-C-B11-M-200	Installation of Sanitary Waste / Drainage Pipes	4	18,585.14	19-May-26	23-May-26	05-Jul-26	08-Jul-26	18,585.14	18,585.14	1.00
DAM3-C-B11-M-220	Installation of Floor Drain	2	11,055.96	07-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-380	Installation of Trench drain	5	11,508.80	09-Dec-26	14-Dec-26	06-Jul-26	08-Jul-26	0.00	11,508.80	0.00
SECOND STAGE		14	48,859.84	15-Dec-26	30-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-180	Installation of Electric Water Heater	2	1,819.51	15-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-190	Installation of Sanitary Fixture and Accessories	4	19,921.72	17-Dec-26	21-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-210	Installation of Lavotary /Wash Basin	2	21,416.68	22-Dec-26	23-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-270	Installation of Bib Tap	2	1,900.66	24-Dec-26	26-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-428	Installation of Water Tap	2	2,874.14	27-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-B11-M-429	Installation of Roof Vent Cap	2	927.12	29-Dec-26	30-Dec-26			0.00	0.00	0.00
WATER SUPPLY SYSTEM		17	41,870.81	23-Dec-26	04-Jan-27	01-Oct-26		0.00	41,592.68	0.00
FIRST STAGE		6	41,592.68	23-Dec-26	29-Dec-26	01-Oct-26	05-Oct-26	0.00	41,592.68	0.00
DAM3-C-B11-M-290	Installation of Water Supply Pipes	4	23,318.41	23-Dec-26	27-Dec-26	01-Oct-26	05-Oct-26	0.00	23,318.41	0.00
DAM3-C-B11-M-280	Installation of Water Supply Valve	2	18,274.27	28-Dec-26	29-Dec-26	01-Oct-26	05-Oct-26	0.00	18,274.27	0.00
SECOND STAGE		5	278.13	30-Dec-26	04-Jan-27			0.00	0.00	0.00
DAM3-C-B11-M-330	Capped connection	5	278.13	30-Dec-26	04-Jan-27			0.00	0.00	0.00
ELECTRICAL		93	752,044.76	28-Oct-26	16-Feb-27	01-Jun-26		0.00	27,642.87	0.00
FIRST STAGE		85	86,114.12	28-Oct-26	09-Dec-26	01-Jun-26		0.00	27,642.87	0.00
DAM3-C-B11-E-143	Installation of Conduits and wiring outlets - Fire Alarm System	4	1,768.31	28-Oct-26	01-Nov-26	02-Jun-26		0.00	884.15	0.00
DAM3-C-B11-E-183	Installation of Sleeves & Power outlet	8	2,920.45	28-Oct-26	05-Nov-26	02-Jun-26		0.00	1,460.23	0.00
DAM3-C-B11-E-163	Installation of Conduites for Lighting Fixture	4	8,462.97	11-Nov-26	15-Nov-26	27-Sep-26		0.00	7,616.67	0.00
DAM3-C-B11-E-233	Installation of Wires	4	16,925.94	16-Nov-26	19-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-223	Installation of LV Cables	4	36,389.98	30-Nov-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-113	Installation of Earthing and Grounding	3	19,646.47	05-Dec-26	09-Dec-26	01-Jun-26		0.00	17,681.82	0.00
SECOND STAGE		83	665,930.64	02-Nov-26	16-Feb-27			0.00	0.00	0.00
DAM3-C-B11-E-123	Installation of Fire Alarm Control Panel	4	19,451.37	02-Nov-26	05-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-133	Installation of Fire Detectors & Accessories	4	56,740.37	07-Nov-26	10-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-153	Installation of Lighting fixtures	4	76,166.74	21-Nov-26	24-Nov-26			0.00	0.00	0.00

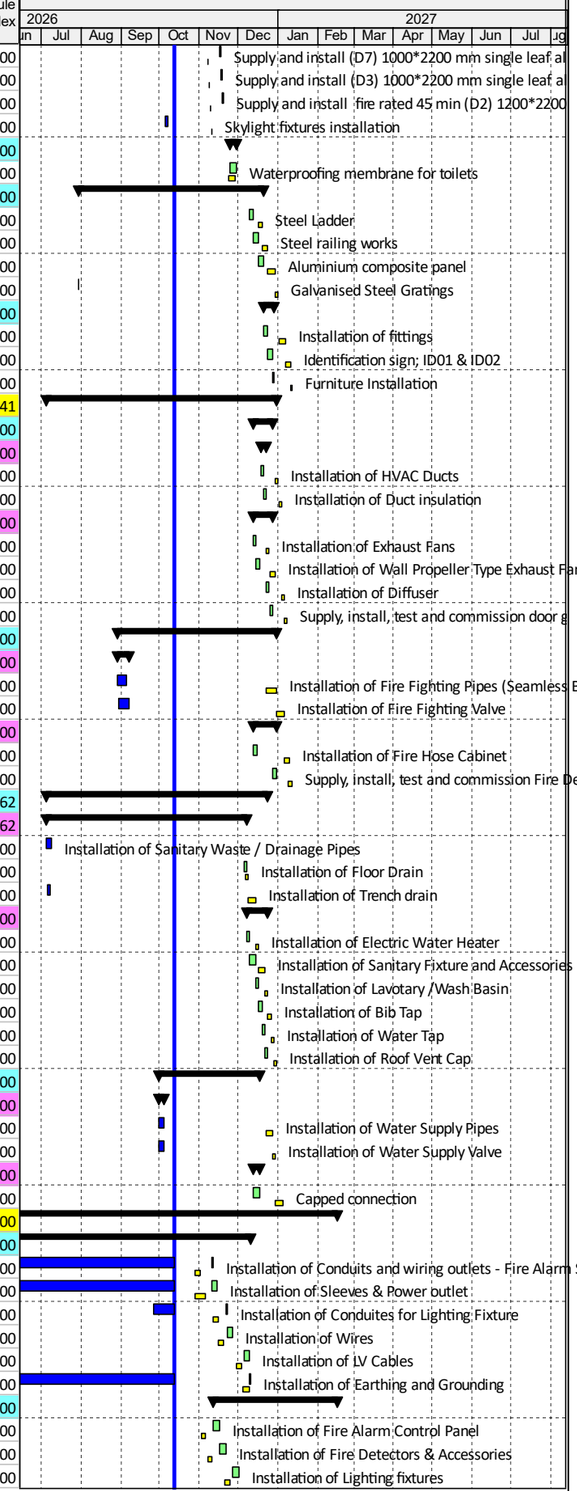

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-B11-E-193	Installation of Main Distribution Board	2	32,472.73	21-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-410	Installation of CCTV System	5	76,349.24	21-Nov-26	28-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-243	Installation of LP-1 Panel	2	18,403.54	23-Nov-26	24-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-253	Installation of PP-AC panel	2	21,648.48	25-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-213	Installation of Telephone Cabinet	2	26,991.08	28-Nov-26	29-Nov-26			0.00	0.00	0.00
DAM3-C-B11-E-273	Installation of Access Control System	5	27,616.86	29-Nov-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-283	Monitor Modules for Fire Alarm	2	3,882.38	05-Dec-26	06-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-293	Line Isolator Modules for Fire Alarm	2	185.40	07-Dec-26	08-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-303	Firewarning flash light with sounder; wall mounted, Weather proof	2	3,082.69	09-Dec-26	10-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-173	Installation of Wiring Devices	4	19,435.09	23-Dec-26	27-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-203	Installation of Disconnect Switches	2	30,235.95	28-Dec-26	29-Dec-26			0.00	0.00	0.00
DAM3-C-B11-E-420	Installation of Solar power plant	4	253,268.71	09-Feb-27	16-Feb-27			0.00	0.00	0.00
SITE INFRASTRUCTURE		290	8,476,025.35	10-Feb-26	21-Feb-27	19-Jan-26		1,744,371.54	2,631,106.65	1.51
SITE WORKS		23	197,690.88	10-Feb-26	10-Mar-26	19-Jan-26	28-Feb-26	197,690.88	197,690.88	1.00
DAM3-C-GEN-180	Initial Site Survey and Setting out	3	0.00	10-Feb-26	12-Feb-26	19-Jan-26	24-Jan-26	0.00	0.00	0.00
DAM3-C-GEN-190	Excavation to the target grading level	20	197,690.88	14-Feb-26	10-Mar-26	10-Feb-26	28-Feb-26	197,690.88	197,690.88	1.00
NETWORKS		89	1,901,944.63	07-Sep-26	23-Dec-26	01-Aug-26		727,424.65	1,180,962.82	1.62
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UNITS)		42	571,716.96	07-Sep-26	21-Oct-26	01-Aug-26		548,590.34	497,845.16	0.91
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	40,471.58	07-Sep-26	14-Sep-26	01-Aug-26		40,471.58	36,424.43	0.90
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	364,244.28	15-Sep-26	27-Sep-26	02-Aug-26		364,244.28	327,819.85	0.90
DAM3-C-ENV-F-202	Warning Tapes	2	40,471.58	28-Sep-26	29-Sep-26	03-Aug-26		40,471.58	32,377.27	0.80
DAM3-C-ENV-F-192	Installation of Valves	5	86,057.93	30-Sep-26	05-Oct-26	02-Aug-26		86,057.93	68,846.34	0.80
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	40,471.58	06-Oct-26	21-Oct-26	05-Aug-26		17,344.96	32,377.27	1.87
WATER SUPPLY SYSTEM		56	290,579.64	15-Sep-26	23-Dec-26			154,344.59	0.00	0.00
DAM3-C-ENV-WS-786	Excavation for Water Suppy Works	7	13,950.39	15-Sep-26	22-Sep-26			13,950.39	0.00	0.00
DAM3-C-ENV-WS-746	Installation of HDPE PN16 Pipes for Cold Water Supply	7	125,553.50	24-Sep-26	05-Oct-26			125,553.50	0.00	0.00
DAM3-C-ENV-WS-806	Construction of Washout Chamber	7	17,314.15	06-Oct-26	13-Oct-26			14,840.70	0.00	0.00
DAM3-C-ENV-WS-776	Warning Tape	2	13,950.39	14-Oct-26	15-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-WS-846	Construction of Air Valve Chamber	7	16,236.37	14-Oct-26	21-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-WS-766	Installation of Valves	5	53,930.05	16-Nov-26	21-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-WS-796	Backfilling for Water Supply	14	13,950.39	22-Nov-26	07-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-WS-826	Supply and install Service connection -HDPE	14	35,694.38	08-Dec-26	23-Dec-26			0.00	0.00	0.00
SEWER & DRAINAGE SYSTEM		36	772,226.27	06-Oct-26	08-Dec-26	22-Aug-26		19,081.67	683,117.66	35.80
DAM3-C-ENV-SW-516	Excavation for Sewer Works	7	22,261.94	06-Oct-26	13-Oct-26	22-Aug-26	04-Oct-26	19,081.67	22,261.94	1.17
DAM3-C-ENV-SW-486	Installation of UPVC Pipes for Sewer	4	222,619.45	14-Oct-26	25-Oct-26	16-Sep-26	05-Oct-26	0.00	222,619.45	0.00
DAM3-C-ENV-SW-536	Construction of Manhole	7	166,049.07	26-Oct-26	02-Nov-26	22-Aug-26	10-Sep-26	0.00	166,049.07	0.00
DAM3-C-ENV-SW-496	Construction of inspection chambers	7	249,925.25	03-Nov-26	10-Nov-26	22-Aug-26	03-Oct-26	0.00	249,925.25	0.00
DAM3-C-ENV-SW-526	Backfilling for Sewer Drainage	14	22,261.94	03-Nov-26	18-Nov-26	17-Sep-26	06-Oct-26	0.00	22,261.94	0.00
DAM3-C-ENV-SW-506	Gully trap	10	53,541.58	19-Nov-26	30-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-SW-546	UPVC pipe service connection	7	35,567.03	01-Dec-26	08-Dec-26			0.00	0.00	0.00
IRRIGATION SYSTEM		48	267,421.77	06-Oct-26	22-Dec-26			5,408.05	0.00	0.00
DAM3-C-ENV-SW-556	Excavation for HDPE pipes	7	6,309.39	06-Oct-26	13-Oct-26			5,408.05	0.00	0.00
DAM3-C-ENV-SW-566	Installation of HDPE Pipes	10	63,093.94	14-Oct-26	25-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-SW-586	Construction of Washout valve chamber	5	3,247.85	26-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-SW-576	Construction of Air valve chamber	5	3,786.75	26-Oct-26	31-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-SW-596	Backfilling for HDPE pipes	14	6,309.39	01-Nov-26	16-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-SW-606	Installation of valves	5	84,556.00	09-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-SW-616	Main program system and controller for irrigation system	7	100,118.45	15-Dec-26	22-Dec-26			0.00	0.00	0.00
EXTERNAL WORKS		84	3,338,525.71	15-Sep-26	25-Jan-27	01-Jul-26		819,256.01	1,252,452.95	1.53
MECHANICAL		34	1,375,655.38	26-Oct-26	10-Jan-27	01-Jul-26		0.00	1,252,452.95	0.00
DAM3-C-ENV-M-1371	Installation of GRP Tanks	10	585,839.88	30-Nov-26	10-Dec-26	08-Aug-26	08-Oct-26	0.00	585,839.88	0.00
DAM3-C-ENV-M-1381	Valves for GRP Tank	3	58,583.98	12-Dec-26	14-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-M-1391	Access Ladder for GRP Tank	2	58,583.98	15-Dec-26	16-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-M-1341	Installation of Booster Pump	5	38,967.27	26-Dec-26	30-Dec-26	07-Oct-26	07-Oct-26	0.00	38,967.27	0.00
DAM3-C-ENV-M-1301	Installation of Fire Fighting Pump	4	345,880.31	31-Dec-26	04-Jan-27	22-Sep-26	22-Sep-26	0.00	345,880.31	0.00
DAM3-C-ENV-M-1351	Valves for Water Supply Pump	2	4,329.70	03-Jan-27	04-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-M-1311	CO2 fire extinguisher	1	217.29	05-Jan-27	05-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-M-1361	Powder fire extinguisher	1	188.33	06-Jan-27	06-Jan-27			0.00	0.00	0.00
GRP Tank Foundation		31	180,037.46	31-Oct-26	29-Nov-26	27-Jul-26	27-Aug-26	0.00	180,037.46	0.00
DAM3-C-GRP-S-0101	Excavation for Foundation	4	9,001.87	31-Oct-26	03-Nov-26	27-Jul-26	27-Jul-26	0.00	9,001.87	0.00
DAM3-C-GRP-S-0102	Vapour Barrier for Foundation	2	9,001.87	04-Nov-26	05-Nov-26	06-Aug-26	06-Aug-26	0.00	9,001.87	0.00
DAM3-C-GRP-S-0103	Lean Concrete Below Foundation	2	18,003.75	07-Nov-26	08-Nov-26	06-Aug-26	06-Aug-26	0.00	18,003.75	0.00

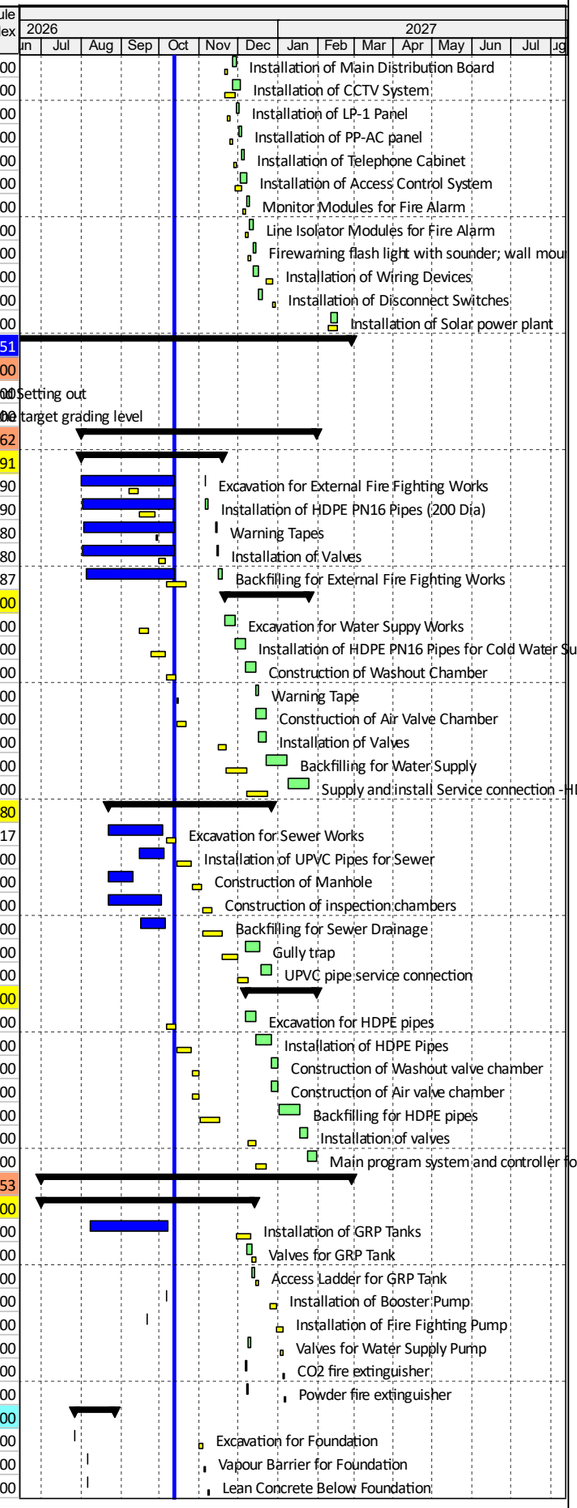

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-GRP-S-0104	Rebar for Foundation	4	36,007.49	09-Nov-26	12-Nov-26	11-Aug-26	16-Aug-26	0.00	36,007.49	0.00
DAM3-C-GRP-S-0105	Formwork for Foundation	4	18,003.75	14-Nov-26	17-Nov-26	12-Aug-26	23-Aug-26	0.00	18,003.75	0.00
DAM3-C-GRP-S-0106	Pouring Concrete for Foundation	1	63,013.11	18-Nov-26	18-Nov-26	18-Aug-26	23-Aug-26	0.00	63,013.11	0.00
DAM3-C-GRP-S-0107	Damp proof /Bitumin paint on Foundation	2	9,001.87	19-Nov-26	21-Nov-26	24-Aug-26	25-Aug-26	0.00	9,001.87	0.00
DAM3-C-GRP-S-0108	Backfilling / Compaction Around Foundation	7	18,003.75	22-Nov-26	29-Nov-26	26-Aug-26	27-Aug-26	0.00	18,003.75	0.00
Pump Shed		34	103,027.17	26-Oct-26	10-Jan-27	01-Jul-26		0.00	101,728.03	0.00
DAM3-C-PR-S-108	Excavation for Footings	4	649.57	26-Oct-26	29-Oct-26	01-Jul-26	02-Jul-26	0.00	649.57	0.00
DAM3-C-PR-S-308	Vapour Barrier for Footings	2	649.57	31-Oct-26	01-Nov-26	23-Jul-26	23-Jul-26	0.00	649.57	0.00
DAM3-C-PR-S-138	Lean Concrete Below Footings	2	649.57	02-Nov-26	03-Nov-26	23-Jul-26	23-Jul-26	0.00	649.57	0.00
DAM3-C-PR-S-198	Rebar for Footings	4	1,299.14	04-Nov-26	08-Nov-26	25-Jul-26	25-Jul-26	0.00	1,299.14	0.00
DAM3-C-PR-S-208	Formwork for Footings	4	649.57	09-Nov-26	12-Nov-26	25-Jul-26	25-Jul-26	0.00	649.57	0.00
DAM3-C-PR-S-148	Pouring Concrete for Footings	1	5,846.13	14-Nov-26	14-Nov-26	26-Jul-26	26-Jul-26	0.00	5,846.13	0.00
DAM3-C-PR-S-298	Damp proof /Bitumin paint on Footing Sides	2	649.57	15-Nov-26	16-Nov-26	28-Jul-26	28-Jul-26	0.00	649.57	0.00
DAM3-C-PR-S-378	Backfilling / Compaction Around Footings to Bottom of Grade Beams	5	1,299.14	17-Nov-26	22-Nov-26	29-Jul-26	03-Aug-26	0.00	1,299.14	0.00
DAM3-C-PR-S-328	Vapour barrier for Grade Beams	2	649.57	23-Nov-26	24-Nov-26	04-Aug-26	04-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-158	Lean Concrete Below Grade Beams	2	649.57	25-Nov-26	26-Nov-26	04-Aug-26	04-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-218	Rebar for Grade Beams	2	1,299.14	28-Nov-26	29-Nov-26	15-Aug-26	15-Aug-26	0.00	1,299.14	0.00
DAM3-C-PR-S-188	Pedestal including anchor bolts	1	1,299.14	30-Nov-26	30-Nov-26	17-Aug-26	17-Aug-26	0.00	1,299.14	0.00
DAM3-C-PR-S-228	Formwork for Grade Beams	2	649.57	30-Nov-26	01-Dec-26	16-Aug-26	17-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-168	Pouring Concrete for Grade Beams	1	3,247.85	02-Dec-26	02-Dec-26	18-Aug-26	18-Aug-26	0.00	3,247.85	0.00
DAM3-C-PR-S-338	Damp proof /Bitumin paint on Grade Beams	2	649.57	03-Dec-26	05-Dec-26	20-Aug-26	22-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-388	Backfilling / Compaction for Slab on Grade	5	1,299.14	06-Dec-26	10-Dec-26	23-Aug-26	24-Aug-26	0.00	1,299.14	0.00
DAM3-C-PR-S-318	Anti Termite Treatment below Ground Slab	1	649.57	12-Dec-26	12-Dec-26	24-Aug-26	24-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-348	Vapour barrier for below Ground Slab	2	649.57	13-Dec-26	14-Dec-26	24-Aug-26	24-Aug-26	0.00	649.57	0.00
DAM3-C-PR-S-268	Rebar for Ground Slab	4	12,070.63	15-Dec-26	19-Dec-26	25-Aug-26	26-Aug-26	0.00	12,070.63	0.00
DAM3-C-PR-S-278	Formwork for Ground Slab	4	8,263.60	20-Dec-26	23-Dec-26	26-Aug-26	26-Aug-26	0.00	8,263.60	0.00
DAM3-C-PR-S-178	Pouring Concrete for Ground Slab	1	20,334.24	24-Dec-26	24-Dec-26	27-Aug-26	27-Aug-26	0.00	20,334.24	0.00
DAM3-C-PR-S-288	Concrete Pad	5	1,299.14	26-Dec-26	30-Dec-26			0.00	0.00	0.00
DAM3-C-PR-S-128	Installation of Columns	3	7,794.85	31-Dec-26	03-Jan-27	30-Aug-26	30-Aug-26	0.00	7,794.85	0.00
DAM3-C-PR-S-358	Installation of Raft & Purlins	4	11,042.69	04-Jan-27	07-Jan-27	30-Aug-26	30-Aug-26	0.00	11,042.69	0.00
DAM3-C-PR-S-368	Installation of Roof Sheet	2	19,487.12	09-Jan-27	10-Jan-27	31-Aug-26	31-Aug-26	0.00	19,487.12	0.00
ELECTRICAL		17	236,867.32	31-Dec-26	25-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-176	Installation of Main MCC	2	13,498.43	31-Dec-26	02-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-186	Installation of Earthing and Grounding	3	1,399.38	03-Jan-27	07-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-236	Installation of panel boards	2	5,953.91	05-Jan-27	06-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-1321	Installation of wiring devices	5	5,632.31	07-Jan-27	12-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-1341	Installation of Cable tray	5	3,563.73	07-Jan-27	12-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-206	Installation of Conduites for Lighting Fixture	4	798.20	09-Jan-27	12-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-216	Installation of LV Cables	5	7,709.71	13-Jan-27	18-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-226	Installation of Wires	2	1,596.40	13-Jan-27	14-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-196	Installation of Lighting fixtures	2	7,183.81	16-Jan-27	17-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-E-1331	Installation of Programmable Logis Controller	4	189,531.43	18-Jan-27	25-Jan-27			0.00	0.00	0.00
EXTERNAL ELECTRICAL WORKS		66	1,711,707.92	15-Sep-26	01-Dec-26			819,256.01	0.00	0.00
DAM3-C-ENV-E-400	Installation of UPVC Pipe	5	76,356.22	15-Sep-26	20-Sep-26			76,356.22	0.00	0.00
DAM3-C-ENV-E-410	Construction of Concrete encased duct bank	8	687,205.97	21-Sep-26	03-Oct-26			687,205.97	0.00	0.00
DAM3-C-ENV-E-420	Installation of Sleeves for lighting poles	5	19,588.78	04-Oct-26	08-Oct-26			19,588.78	0.00	0.00
DAM3-C-ENV-E-390	Installation of Telecom manhole	4	120,350.16	10-Oct-26	20-Oct-26			36,105.05	0.00	0.00
DAM3-C-ENV-E-450	Foundation for Lighting poles	5	19,588.78	21-Oct-26	26-Oct-26			0.00	0.00	0.00
DAM3-C-ENV-E-440	Installation of Lighting poles	5	156,710.21	27-Oct-26	03-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-E-430	Installation of Lighting Fixture	5	39,177.55	04-Nov-26	09-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-E-380	Installation of LV Cables	7	98,914.91	10-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-E-460	Electrical Manhole	7	253,329.40	18-Nov-26	25-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-E-470	Installation of Earthing and Grounding	5	19,643.55	26-Nov-26	01-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-E-480	Installation of Street Lighting Feeder pillars & KWH meter	5	220,842.40	26-Nov-26	01-Dec-26			0.00	0.00	0.00
FENCES AND GATES		37	14,295.10	10-Nov-26	10-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-S-1374	Excavation for Fence	2	597.56	10-Nov-26	17-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-S-1354	Vapour Barrier for Fence	4	298.78	18-Nov-26	22-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-S-1274	Lean Concrete Below Fence	4	597.56	23-Nov-26	26-Nov-26			0.00	0.00	0.00
DAM3-C-ENV-S-1304	Rebar for Footings	7	1,195.12	28-Nov-26	05-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-S-1314	Formwork for Footings	4	597.56	06-Dec-26	09-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-S-1284	Pouring Concrete for Footings	2	1,792.67	10-Dec-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-S-1344	Damp proof /Bitumin paint on Footing Sides	2	298.78	13-Dec-26	14-Dec-26			0.00	0.00	0.00

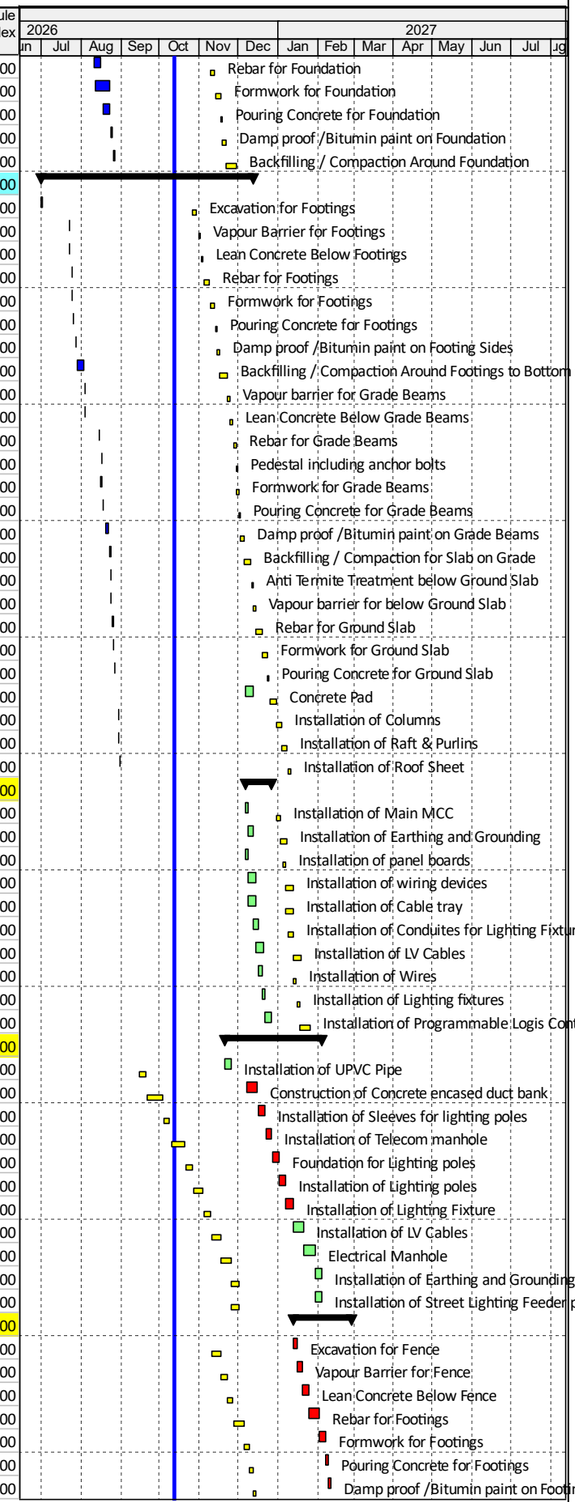

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
DAM3-C-ENV-S-1364	Backfilling / Compaction Around Footings	4	597.56	15-Dec-26	22-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-S-1334	Installation of base plate	2	1,195.12	23-Dec-26	28-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-S-1324	Installation of steel members	2	2,390.24	29-Dec-26	05-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-S-1294	Installation of steel fence	2	2,390.24	06-Jan-27	07-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-S-1384	Installation of steel gates	2	2,343.91	09-Jan-27	10-Jan-27			0.00	0.00	0.00
ROAD WORKS		34	2,873,764.57	23-Nov-26	21-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1390	SubGrade Preparation & Compaction	5	319,796.23	23-Nov-26	03-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-R-1400	Aggregate Base Course Layer	5	262,382.32	05-Dec-26	12-Dec-26			0.00	0.00	0.00
DAM3-C-ENV-R-1460	Curb Stones	4	291,156.54	13-Dec-26	04-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-R-1480	Interlock Tiles	3	475,633.54	05-Jan-27	27-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-R-890	Supply and install geotextile sheet	2	47,639.01	28-Jan-27	30-Jan-27			0.00	0.00	0.00
DAM3-C-ENV-R-1490	Gravel Bedding	2	57,375.45	31-Jan-27	01-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1500	Road Signs	3	103,945.80	02-Feb-27	07-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1450	Prime Coat	1	71,708.03	08-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1410	Asphalt Concrete Base Course Layer	2	645,372.33	09-Feb-27	10-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1470	Tack Coat	1	52,885.08	11-Feb-27	11-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1420	Asphalt Concrete Wearing Course Layer	2	475,965.66	13-Feb-27	14-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1430	Retroreflective Thermoplastic White Traffic lines	2	37,884.84	15-Feb-27	16-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1440	Installation of Concrete wheel bumper	2	32,019.76	17-Feb-27	21-Feb-27			0.00	0.00	0.00
LANDSCAPING		12	164,099.55	02-Feb-27	15-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1510	Planting of trees	5	110,131.54	02-Feb-27	07-Feb-27			0.00	0.00	0.00
DAM3-C-ENV-R-1520	Planting of shrubs	7	53,968.01	08-Feb-27	15-Feb-27			0.00	0.00	0.00
TESTING AND COMMISSIONING (10%)		183	9,599,652.50	24-May-26	18-Feb-27	17-Jun-26		7,217,926.94	7,189,496.10	1.00
TESTING AND COMMISSIONING 900 Sq.m-2		183	1,943,587.85	24-May-26	18-Feb-27	28-Jun-26		63,346.56	63,346.56	1.00
MECHANICAL		182	617,124.79	24-May-26	17-Jan-27	28-Jun-26		63,346.56	63,346.56	1.00
P001-C-TC-M-3406	Testing & Commissioning of Sewer & Drainage Pipes	7	63,346.56	24-May-26	03-Jun-26	28-Jun-26	08-Oct-26	63,346.56	63,346.56	1.00
P001-C-TC-M-3416	Testing and Commissioning of Electric Water Heater	7	2,987.25	18-Nov-26	26-Nov-26			0.00	0.00	0.00
P001-C-TC-M-3426	Testing and Commissioning of Sanitary Fixtures	7	32,707.31	23-Nov-26	01-Dec-26			0.00	0.00	0.00
P001-C-TC-M3446	Testing and Commissioning of Exhaust Fan	7	13,737.46	26-Nov-26	05-Dec-26			0.00	0.00	0.00
P001-C-TC-M-3396	Testing & Commissioning of Water Supply Pipes	7	38,283.97	29-Nov-26	07-Dec-26			0.00	0.00	0.00
P001-C-TC-M-3456	Testing and Commissioning of Wall propeller type exhaust fans	7	76,887.76	01-Dec-26	09-Dec-26			0.00	0.00	0.00
P001-C-TC-M-3376	Testing and Commissioning of Fire Fighting Pipes	7	118,857.06	02-Dec-26	10-Dec-26			0.00	0.00	0.00
P001-C-TC-M-3436	Testing and Commissioning of HVAC Duct	7	245,430.24	03-Dec-26	12-Dec-26			0.00	0.00	0.00
P001-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	24,887.19	10-Jan-27	17-Jan-27			0.00	0.00	0.00
ELECTRICAL		28	1,326,463.06	29-Nov-26	18-Feb-27			0.00	0.00	0.00
P001-C-TC-E-3506	Testing and Commissioning of Wiring Devices	7	33,207.17	29-Nov-26	07-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3496	Testing and Commissioning of Fire Alarm System	2	139,733.70	07-Dec-26	08-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3546	Testing and Commissioning of Access Control System	2	45,341.12	17-Dec-26	19-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3456	Testing and Commissioning of Main Distribution Board	3	53,313.44	23-Dec-26	30-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3446	Testing and Commissioning of LV cables	2	149,517.23	26-Dec-26	27-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3486	Testing and Commissioning of Grounding	2	32,570.63	26-Dec-26	27-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3526	Testing and Commissioning of PP-AC panel	2	35,542.28	26-Dec-26	30-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3536	Testing and Commissioning of Telephone and data system	2	44,313.72	28-Dec-26	02-Jan-27			0.00	0.00	0.00
P001-C-TC-E-3566	Testing and Commissioning of CCTV System	2	125,349.49	29-Dec-26	30-Dec-26			0.00	0.00	0.00
P001-C-TC-E-3466	Testing and Commissioning of Disconnect Switches	7	50,288.02	30-Dec-26	06-Jan-27			0.00	0.00	0.00
P001-C-TC-E-3516	Testing and Commissioning of LP panel board	2	30,214.76	31-Dec-26	02-Jan-27			0.00	0.00	0.00
P001-C-TC-E-3476	Testing and Commissioning of Lighting Fixtures	1	171,257.21	18-Jan-27	18-Jan-27			0.00	0.00	0.00
P001-C-TC-E-3556	Testing and Commissioning of Solar power plant	2	415,814.30	17-Feb-27	18-Feb-27			0.00	0.00	0.00
TESTING AND COMMISSIONING SITE INFRASTRUCTURE		85	530,478.84	06-Oct-26	06-Feb-27	13-Oct-26		28,994.57	125,892.59	4.34
PUMP ROOM SHED		19	306,247.54	12-Dec-26	06-Feb-27			0.00	0.00	0.00
S001-C-TC-M-3596	Testing & Commissioning of GRP tank	3	104,926.55	12-Dec-26	14-Dec-26			0.00	0.00	0.00
S001-C-TC-M-3586	Testing & Commissioning of Booster pump	7	6,462.23	31-Dec-26	07-Jan-27			0.00	0.00	0.00
S001-C-TC-M-3576	Testing & Commissioning of Fire Fighting pump	5	51,684.47	05-Jan-27	10-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3616	Testing and Commissioning of Panel Board	2	36,675.69	07-Jan-27	09-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3636	Testing and Commissioning of Grounding	5	208.86	09-Jan-27	13-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3646	Testing and Commissioning of Wiring devices	2	193.73	13-Jan-27	14-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3626	Testing and Commissioning of Lighting Fixtures	2	1,429.61	18-Jan-27	19-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3621	Testing and Commissioning of LV cables	3	76,378.12	19-Jan-27	24-Jan-27			0.00	0.00	0.00
S001-C-TC-E-3656	Testing and Commissioning of Programmable Logic Controller	2	28,288.27	26-Jan-27	06-Feb-27			0.00	0.00	0.00
EXTERNAL		26	52,779.67	18-Nov-26	09-Dec-26			0.00	0.00	0.00
S001-C-TC-EX-E-3626	Testing and Commissioning of LV cables	7	14,763.42	18-Nov-26	25-Nov-26			0.00	0.00	0.00
S001-C-TC-EX-E-3646	Testing and Commissioning of Street Lighting pole	15	35,084.37	22-Nov-26	08-Dec-26			0.00	0.00	0.00

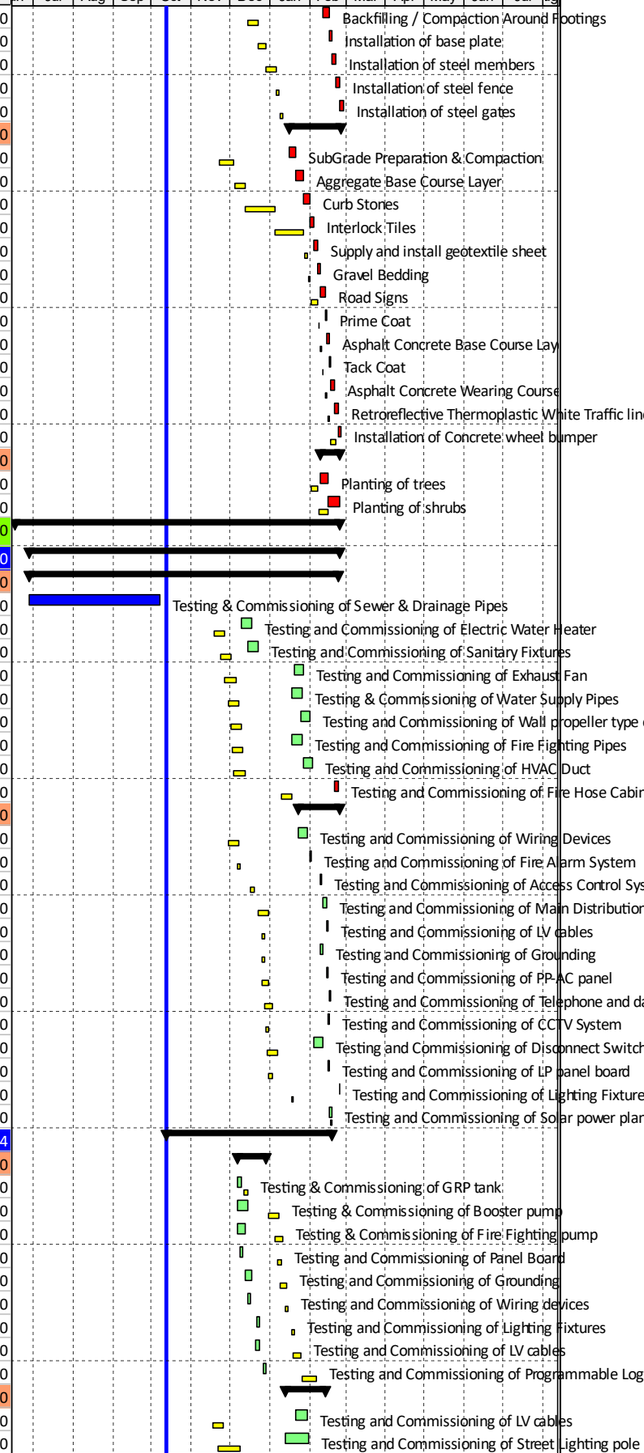

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3


Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
S001-C-TC-EX-E-3656	Testing and Commissioning of Grounding	7	2,931.87	02-Dec-26	09-Dec-26			0.00	0.00	0.00
ENVIRONMENTAL		85	171,451.64	06-Oct-26	19-Jan-27	13-Oct-26		28,994.57	125,892.59	4.34
S001-C-TC-ENV-F-1051	Testing & Commissioning of External Fire Fighting System 200 Dia	15	72,486.43	06-Oct-26	22-Oct-26	13-Oct-26		28,994.57	65,237.78	2.25
S001-C-TC-ENV-WS-11	Testing & Commissioning of Water Supply System	15	5,327.52	22-Nov-26	08-Dec-26			0.00	0.00	0.00
S001-C-TC-ENV-SW-70	Testing & Commissioning of Irrigaiton System	15	11,300.41	15-Dec-26	31-Dec-26			0.00	0.00	0.00
S001-C-TC-ENV-3666	Testing and Commissioning of Main program system & controller	10	14,943.05	23-Dec-26	09-Jan-27			0.00	0.00	0.00
S001-C-TC-ENV-SW-60	Testing & Commissioning of Sewer & Drainage System	3	67,394.23	03-Jan-27	19-Jan-27	13-Oct-26		0.00	60,654.81	0.00
SNAGG WORKS		79	7,125,585.81	10-Jun-26	16-Jul-26	17-Jun-26		7,125,585.81	7,000,256.95	0.98
S001-C-TC-M-100	Mechanical Snagg works	5	1,206,604.05	10-Jun-26	15-Jun-26	05-Jul-26	06-Jul-26	1,206,604.05	1,206,604.05	1.00
S001-C-TC-E-3676	External Snagg works	5	3,231,301.32	02-Jul-26	07-Jul-26	22-Jun-26	05-Jul-26	3,231,301.32	3,231,301.32	1.00
S001-C-TC-C-80	Civil & Architectural Snagg works-1	5	1,520,575.29	05-Jul-26	11-Jul-26	17-Jun-26	20-Jun-26	1,520,575.29	1,520,575.29	1.00
S001-C-TC-E-3606	Electrical Snagg works	5	167,105.15	08-Jul-26	13-Jul-26	05-Jul-26		167,105.15	41,776.29	0.25
S001-C-TC-A-90	Civil & Architectural Snagg works-2	5	1,000,000.00	11-Jul-26	16-Jul-26	21-Jun-26	22-Jun-26	1,000,000.00	1,000,000.00	1.00
PREOJECT CLOSEOUT		20	0.00	02-Feb-27	06-Mar-27			0.00	0.00	0.00
ENGINEERING		8	0.00	02-Feb-27	10-Feb-27			0.00	0.00	0.00
AS BUILT DRAWINGS		6	0.00	02-Feb-27	08-Feb-27			0.00	0.00	0.00
CIVIL DRAWINGS		2	0.00	02-Feb-27	03-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	02-Feb-27	03-Feb-27			0.00	0.00	0.00
DAM3-AB-1010	Civil drawings	2	0.00	02-Feb-27	03-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVALS		2	0.00	02-Feb-27	03-Feb-27			0.00	0.00	0.00
DAM3-AB-1053	Civil drawings	2	0.00	02-Feb-27	03-Feb-27			0.00	0.00	0.00
ARCHITECTURAL DRAWINGS		4	0.00	04-Feb-27	08-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
DAM3-AB-1011	Architectural drawings	2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVALS		2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-AB-1023	Architectural drawings	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
MECHANICAL DRAWINGS		4	0.00	04-Feb-27	08-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
DAM3-AB-1013	Mechanical drawings	2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVALS		2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-AB-1033	Mechanical drawings	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
ELECTRICAL DRAWINGS		4	0.00	04-Feb-27	08-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
DAM3-AB-1012	Electrical drawings	2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVALS		2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-AB-1043	Electrical drawings	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
EXTERNAL WORKS DRAWINGS		4	0.00	04-Feb-27	08-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
DAM3-AB-1054	External works drawings	2	0.00	04-Feb-27	06-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVALS		2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-AB-1055	External works drawings	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
WARRANTIES AND GUARANTEES		4	0.00	07-Feb-27	10-Feb-27			0.00	0.00	0.00
SYSTEM		4	0.00	07-Feb-27	10-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-WG-1010	Warraties and Guarantees For Mechanical Equipments	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
DAM3-WG-1011	Warraties and Guarantees For Electrical Systems	2	0.00	07-Feb-27	08-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVAL		2	0.00	09-Feb-27	10-Feb-27			0.00	0.00	0.00
DAM3-WG-1012	Warraties and Guarantees For Mechanical Equipments	2	0.00	09-Feb-27	10-Feb-27			0.00	0.00	0.00
DAM3-WG-1013	Warraties and Guarantees For Electrical Systems	2	0.00	09-Feb-27	10-Feb-27			0.00	0.00	0.00
TRAINING AND MANUALS		10	0.00	11-Feb-27	23-Feb-27			0.00	0.00	0.00
TRAINING		6	0.00	11-Feb-27	17-Feb-27			0.00	0.00	0.00
SYSTEM		6	0.00	11-Feb-27	17-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	11-Feb-27	13-Feb-27			0.00	0.00	0.00
DAM3-WG-1014	The Proposed Coursework For Mechanical Equipment	2	0.00	11-Feb-27	13-Feb-27			0.00	0.00	0.00
DAM3-WG-1015	The Proposed Coursework For Electircal systems	2	0.00	11-Feb-27	13-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVAL		2	0.00	14-Feb-27	15-Feb-27			0.00	0.00	0.00
DAM3-WG-1016	The Proposed Coursework For Mechanical Equipment	2	0.00	14-Feb-27	15-Feb-27			0.00	0.00	0.00
DAM3-WG-1017	The Proposed Coursework For Electircal systems	2	0.00	14-Feb-27	15-Feb-27			0.00	0.00	0.00
DELIVERY		2	0.00	16-Feb-27	17-Feb-27			0.00	0.00	0.00
DAM3-WG-1018	The Proposed Coursework For Mechanical Equipment	2	0.00	16-Feb-27	17-Feb-27			0.00	0.00	0.00
DAM3-WG-1019	The Proposed Coursework For Electircal systems	2	0.00	16-Feb-27	17-Feb-27			0.00	0.00	0.00
MANUALS		4	0.00	18-Feb-27	23-Feb-27			0.00	0.00	0.00

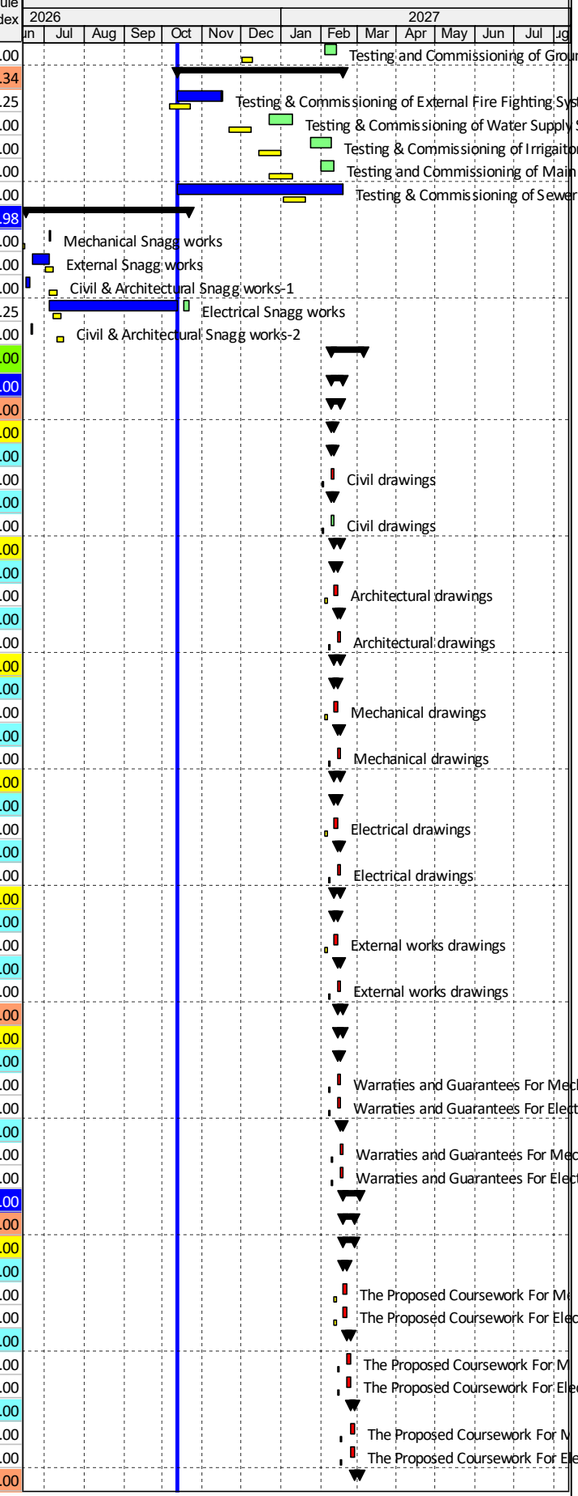

© Oracle Corporation

44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3

Activity ID	Activity Name	Original Duration	Budgeted Total Cost	BL Project Start	BL Project Finish	Actual Start	Actual Finish	Planned Value Cost	Earned Value Cost	Schedule Performance Index
SYSTEM		4	0.00	18-Feb-27	23-Feb-27			0.00	0.00	0.00
PREPARATION AND SUBMITTALS		2	0.00	18-Feb-27	20-Feb-27			0.00	0.00	0.00
DAM3-WG-1020	Manual and Catalogue For Mechanical Equipment	2	0.00	18-Feb-27	20-Feb-27			0.00	0.00	0.00
DAM3-WG-1021	Manual and Catalogue For For Electircal systems	2	0.00	18-Feb-27	20-Feb-27			0.00	0.00	0.00
REVIEW AND APPROVAL		2	0.00	21-Feb-27	23-Feb-27			0.00	0.00	0.00
DAM3-WG-1022	Manual and Catalogue For Mechanical Equipment	2	0.00	21-Feb-27	23-Feb-27			0.00	0.00	0.00
DAM3-WG-1023	Manual and Catalogue For For Electircal systems	2	0.00	21-Feb-27	23-Feb-27			0.00	0.00	0.00
DEMOBILIZATION		13	0.00	09-Feb-27	24-Feb-27			0.00	0.00	0.00
DAM3-D.MOB-1013	Demobilization of manpower	2	0.00	09-Feb-27	10-Feb-27			0.00	0.00	0.00
DAM3-D.MOB-1020	Demobilization of equipment	2	0.00	11-Feb-27	13-Feb-27			0.00	0.00	0.00
DAM3-D.MOB-1010	Dismantling and removal offices	1	0.00	24-Feb-27	24-Feb-27			0.00	0.00	0.00
FINAL HANDOVER		6	0.00	23-Feb-27	06-Mar-27			0.00	0.00	0.00
DAM3-FH-1000	Snag List Rectification	3	0.00	23-Feb-27	03-Mar-27			0.00	0.00	0.00
DAM3-FH-1010	Handover Letter	1	0.00	04-Mar-27	04-Mar-27			0.00	0.00	0.00
DAM3-FH-1020	Intial Handingover	1	0.00	06-Mar-27	06-Mar-27			0.00	0.00	0.00

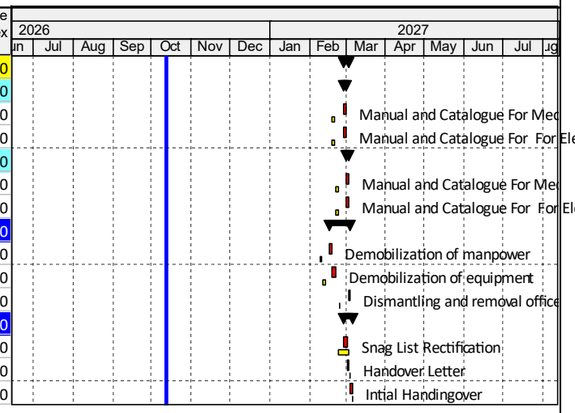

© Oracle Corporation
