

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		219	12-Feb-26	24-Dec-26	4,516,095.66	2,448,901.70	2,228,566.70	54.23%	49.35%
PROJECT MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
CONTRACTUAL MILESTONES		0	12-Feb-26	12-Feb-26	0.00	0.00	0.00	0%	0%
DAM3-PMS-MMS-007	Completion of Site levelling, local roads & parkings	0		12-Feb-26	0.00	0.00	0.00	100%	0%
CONSTRUCTION (67%)		219	20-May-26	24-Dec-26	4,348,990.51	2,281,796.55	2,186,790.41	52.47%	50.28%
RBF 900 SQM FACTORIES		219	20-May-26	24-Dec-26	3,777,273.55	1,733,206.21	1,688,945.25	45.89%	44.71%
BLOCK B6		161	20-May-26	07-Nov-26	479,199.75	180,932.42	27,642.87	37.76%	5.77%
STRUCTURAL		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	06-Jun-26	21-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B6-SS-104	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B6-SS-106	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DOORS & WINDOWS		7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B6-A-101	Window (CW1)	7	07-Jul-26	14-Jul-26	94,173.21	94,173.21	0.00	100%	0%
ELECTRICAL		161	20-May-26	07-Nov-26	357,224.22	58,956.90	27,642.87	16.5%	7.74%
FIRST STAGE		161	20-May-26	01-Nov-26	69,188.18	58,956.90	27,642.87	85.21%	39.95%
DAM3-C-B6-E-343	Installation of Earthing and Grounding	4	04-Jul-26	07-Jul-26	19,646.47	19,646.47	17,681.82	100%	90%
DAM3-C-B6-E-413	Installation of Sleeves & Power outlet	8	20-May-26	01-Jun-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	14-Oct-26	18-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	8,462.97	0.00	7,616.67	0%	90%
DAM3-C-B6-E-453	Installation of LV Cables	4	21-Jul-26	25-Jul-26	36,389.98	36,389.98	0.00	100%	0%
SECOND STAGE		8	28-Oct-26	07-Nov-26	288,036.05	0.00	0.00	0%	0%
DAM3-C-B6-E-730	Installation of Solar power plant	7	31-Oct-26	07-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B6-E-503	Installation of Access Control System	4	28-Oct-26	01-Nov-26	27,616.86	0.00	0.00	0%	0%
DAM3-C-B6-E-513	Monitor Modules for Fire Alarm	2	02-Nov-26	03-Nov-26	3,882.38	0.00	0.00	0%	0%
DAM3-C-B6-E-523	Line Isolator Modules for Fire Alarm	2	04-Nov-26	05-Nov-26	185.40	0.00	0.00	0%	0%
DAM3-C-B6-E-533	Firewarning flash light with sounder; wall mounted, Weathe	2	04-Nov-26	05-Nov-26	3,082.69	0.00	0.00	0%	0%
BLOCK B5		118	14-Jun-26	23-Nov-26	688,383.81	430,203.48	91,088.49	62.49%	13.23%
STRUCTURAL		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
DAM3-C-B5-S-127	Concrete pad	7	22-Jun-26	29-Jun-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		7	14-Jun-26	27-Jun-26	26,895.20	26,895.20	0.00	100%	0%
DAM3-C-B5-SS-102	Epoxy paint to steel members at office area	7	14-Jun-26	21-Jun-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B5-SS-104	Epoxy paint for external platform	5	22-Jun-26	27-Jun-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		13	28-Jun-26	13-Aug-26	277,044.97	277,044.97	0.00	100%	0%
CIELING FINISHES		5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DAM3-C-B5-A-151	Installation of Ceiling Gypsum Board	5	09-Aug-26	13-Aug-26	46,792.30	46,792.30	0.00	100%	0%
DOORS & WINDOWS		12	28-Jun-26	11-Jul-26	225,373.65	225,373.65	0.00	100%	0%
DAM3-C-B5-A-183	Window (CW1)	7	28-Jun-26	05-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B5-A-146	Roll up Shutter Door	1	06-Jul-26	06-Jul-26	68,619.20	68,619.20	0.00	100%	0%
DAM3-C-B5-A-147	Supply and install (D5) 1000*2200mm single leaf steel doc	1	07-Jul-26	07-Jul-26	16,016.16	16,016.16	0.00	100%	0%
DAM3-C-B5-A-153	Supply and install (D4) 800*2200 mm single leaf aluminum	1	08-Jul-26	08-Jul-26	22,737.85	22,737.85	0.00	100%	0%
DAM3-C-B5-A-154	Supply and install (D7) 1000*2200 mm single leaf aluminur	1	09-Jul-26	09-Jul-26	7,811.07	7,811.07	0.00	100%	0%
DAM3-C-B5-A-176	Supply and install (D3) 1000*2200 mm single leaf aluminur	1	11-Jul-26	11-Jul-26	16,016.16	16,016.16	0.00	100%	0%
WATER PROOFING WORKS		4	27-Jul-26	30-Jul-26	4,879.02	4,879.02	0.00	100%	0%
DAM3-C-B5-A-163	Waterproofing membrane for toilets	4	27-Jul-26	30-Jul-26	4,879.02	4,879.02	0.00	100%	0%

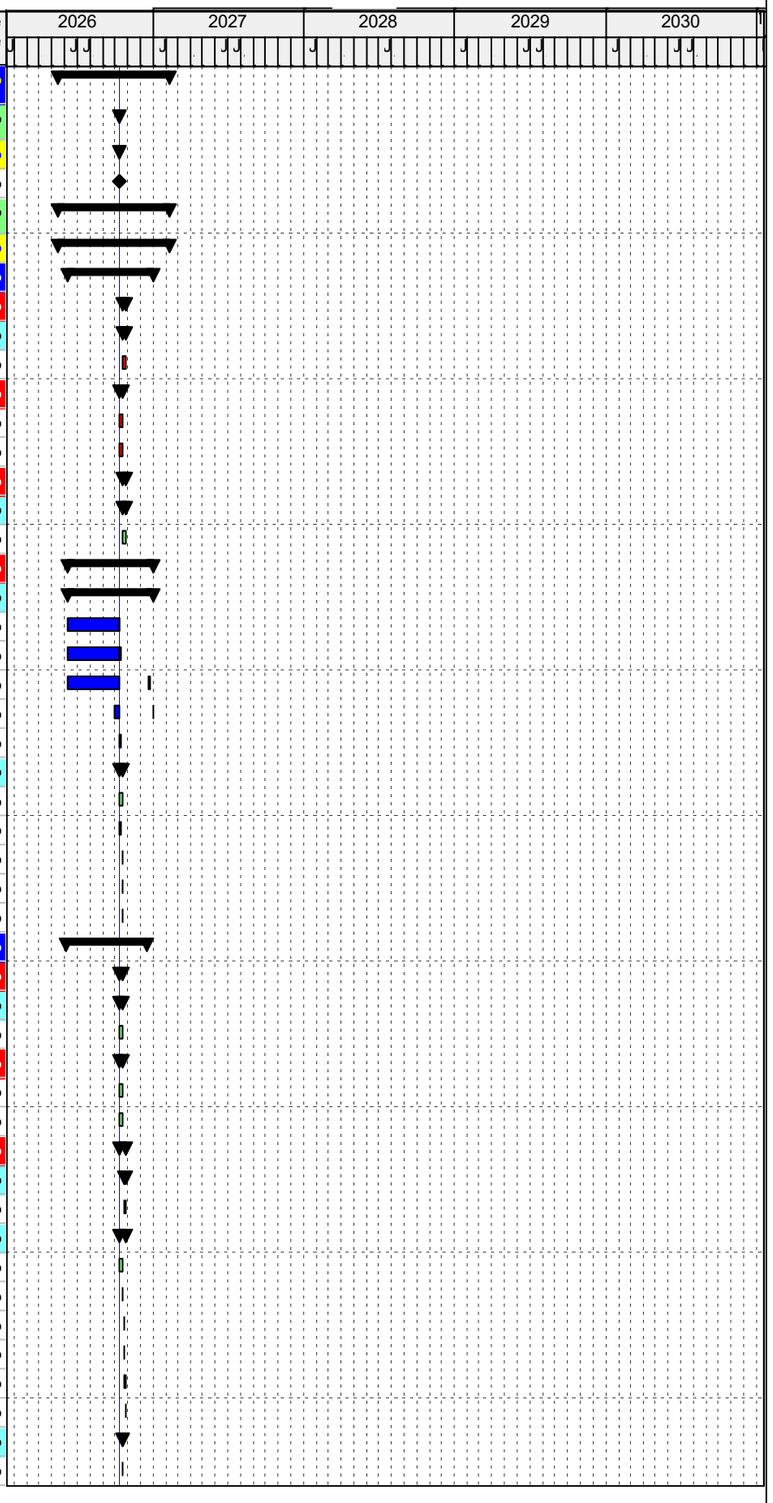

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
MECHANICAL		28	09-Aug-26	07-Sep-26	97,469.62	97,469.62	63,445.62	100%	65.09%
FIRE FIGHTING SYSTEM		12	25-Aug-26	07-Sep-26	84,594.16	84,594.16	63,445.62	100%	75%
FIRST STAGE		12	25-Aug-26	07-Sep-26	84,594.16	84,594.16	63,445.62	100%	75%
DAM3-C-B5-M-12	Installation of Fire Fighting Pipes (Seamless Black Steel)	7	25-Aug-26	01-Sep-26	72,394.75	72,394.75	54,296.06	100%	75%
DAM3-C-B5-M-12	Installation of Fire Fighting Valve	5	02-Sep-26	07-Sep-26	12,199.40	12,199.40	9,149.55	100%	75%
SEWER AND DRAINAGE SYSTEM		4	09-Aug-26	18-Aug-26	12,875.47	12,875.47	0.00	100%	0%
FIRST STAGE		2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Floor Drain	2	09-Aug-26	10-Aug-26	11,055.96	11,055.96	0.00	100%	0%
SECOND STAGE		2	17-Aug-26	18-Aug-26	1,819.51	1,819.51	0.00	100%	0%
DAM3-C-B5-M-11	Installation of Electric Water Heater	2	17-Aug-26	18-Aug-26	1,819.51	1,819.51	0.00	100%	0%
ELECTRICAL		118	30-Jun-26	23-Nov-26	286,066.91	27,886.58	27,642.87	9.75%	9.66%
FIRST STAGE		118	30-Jun-26	13-Oct-26	32,798.20	27,886.58	27,642.87	85.02%	84.28%
DAM3-C-B5-E-803	Installation of Earthing and Grounding	4	10-Oct-26	13-Oct-26	19,646.47	14,734.85	17,681.82	75%	90%
DAM3-C-B5-E-833	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	01-Sep-26	05-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B5-E-873	Installation of Sleeves & Power outlet	8	30-Jun-26	08-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B5-E-853	Installation of Conduites for Lighting Fixture	4	15-Sep-26	19-Sep-26	8,462.97	8,462.97	7,616.67	100%	90%
SECOND STAGE		14	08-Nov-26	23-Nov-26	253,268.71	0.00	0.00	0%	0%
DAM3-C-B5-E-135	Installation of Solar power plant	14	08-Nov-26	23-Nov-26	253,268.71	0.00	0.00	0%	0%
BLOCK B4		94	28-Jun-26	28-Oct-26	385,954.72	366,308.25	353,904.20	94.91%	91.7%
STRUCTURAL STEEL		16	28-Jun-26	19-Jul-26	353,156.52	353,156.52	326,261.32	100%	92.38%
DAM3-C-B4-A-240	Installation of wall sandwich panel	5	14-Jul-26	19-Jul-26	326,261.32	326,261.32	326,261.32	100%	100%
DAM3-C-B4-SS-10	Epoxy paint for external platform	5	01-Jul-26	06-Jul-26	3,734.16	3,734.16	0.00	100%	0%
DAM3-C-B4-SS-10	Epoxy paint to steel members at office area	7	28-Jun-26	05-Jul-26	23,161.04	23,161.04	0.00	100%	0%
ELECTRICAL		94	22-Jul-26	28-Oct-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
FIRST STAGE		94	22-Jul-26	28-Oct-26	32,798.20	13,151.73	27,642.87	40.1%	84.28%
DAM3-C-B4-E-573	Installation of Earthing and Grounding	4	25-Oct-26	28-Oct-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B4-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	24-Sep-26	28-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B4-E-643	Installation of Sleeves & Power outlet	8	22-Jul-26	30-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B4-E-623	Installation of Conduites for Lighting Fixture	4	08-Oct-26	12-Oct-26	8,462.97	8,462.97	7,616.67	100%	90%
BLOCK B3		166	24-Jun-26	24-Dec-26	664,101.19	634,223.44	260,823.68	95.5%	39.27%
STRUCTURAL		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
SLAB ON GRADE		7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
DAM3-C-B3-S-101	Concrete pad	7	11-Jul-26	18-Jul-26	907.11	907.11	0.00	100%	0%
STRUCTURAL STEEL		21	24-Jun-26	15-Jul-26	487,632.50	487,632.50	221,033.26	100%	45.33%
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	115,805.20	115,805.20	57,902.60	100%	50%
DAM3-C-B3-A-240	Installation of wall sandwich panel	5	11-Jul-26	15-Jul-26	326,261.32	326,261.32	163,130.66	100%	50%
DAM3-C-B3-SS-10	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	23,161.04	23,161.04	0.00	100%	0%
DAM3-C-B3-SS-10	Steel members for external platform	7	02-Jul-26	09-Jul-26	18,670.78	18,670.78	0.00	100%	0%
DAM3-C-B3-SS-10	Epoxy paint for external platform	5	11-Jul-26	15-Jul-26	3,734.16	3,734.16	0.00	100%	0%
ARCHITECTURAL		17	16-Jul-26	13-Aug-26	142,763.38	142,763.38	12,147.54	100%	8.51%
WALL FINISHES		10	28-Jul-26	13-Aug-26	48,590.16	48,590.16	12,147.54	100%	25%
DAM3-C-B3-A-104	Internal Wall Plaster	10	28-Jul-26	13-Aug-26	48,590.16	48,590.16	12,147.54	100%	25%
DOORS & WINDOWS		7	16-Jul-26	23-Jul-26	94,173.21	94,173.21	0.00	100%	0%
DAM3-C-B3-A-142	Window (CW1)	7	16-Jul-26	23-Jul-26	94,173.21	94,173.21	0.00	100%	0%
ELECTRICAL		166	19-Jul-26	24-Dec-26	32,798.20	2,920.45	27,642.87	8.9%	84.28%
FIRST STAGE		166	19-Jul-26	24-Dec-26	32,798.20	2,920.45	27,642.87	8.9%	84.28%
DAM3-C-B3-E-573	Installation of Earthing and Grounding	4	21-Dec-26	24-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B3-E-603	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Nov-26	01-Dec-26	1,768.31	0.00	884.15	0%	50%

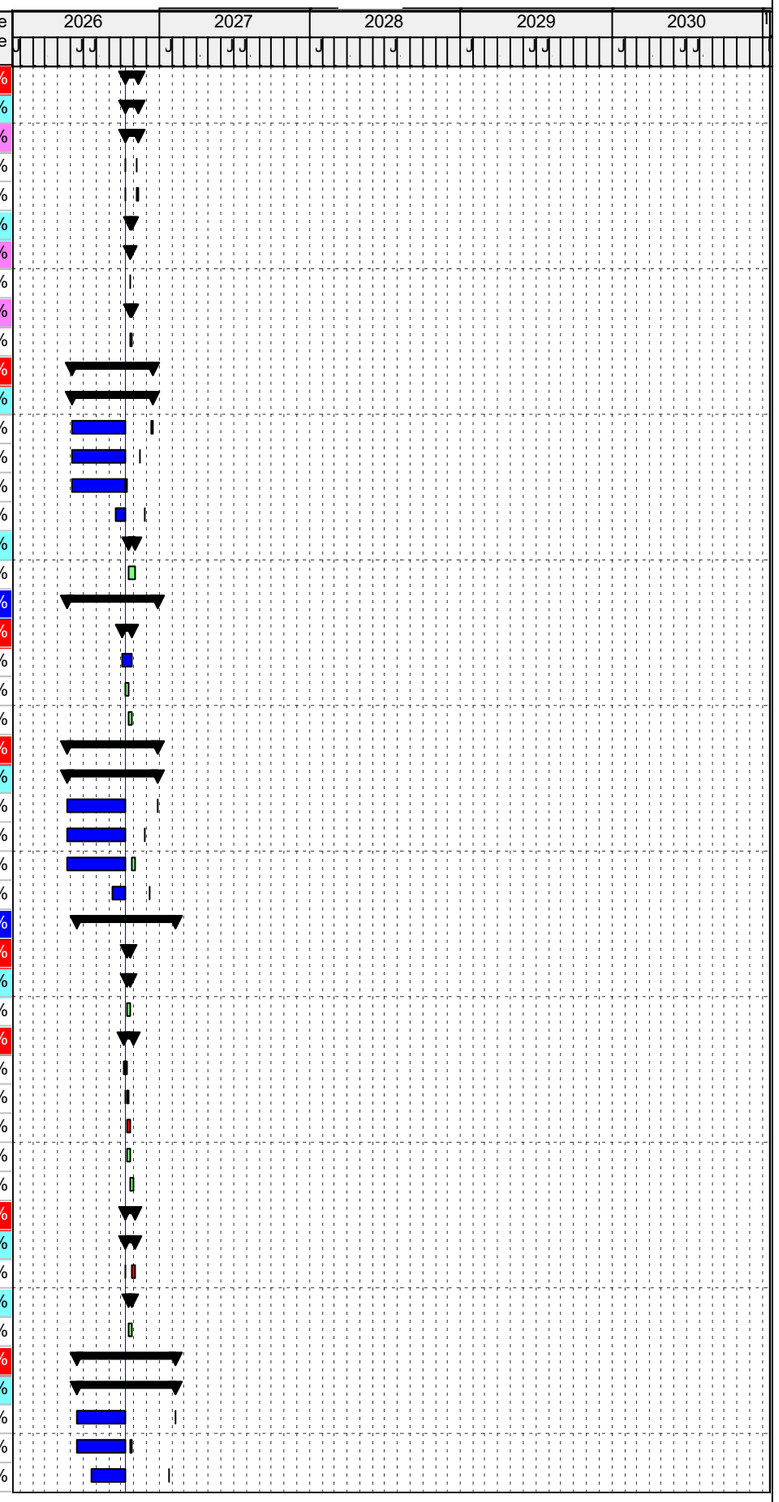

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
DAM3-C-B3-E-623	Installation of Conduites for Lighting Fixture	4	12-Dec-26	15-Dec-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B2		56	29-Sep-26	11-Nov-26	81,388.36	15,216.63	64,085.50	18.7%	78.74%
ARCHITECTURAL		15	08-Oct-26	26-Oct-26	48,590.16	10,527.87	36,442.62	21.67%	75%
WALL FINISHES		15	08-Oct-26	26-Oct-26	48,590.16	10,527.87	36,442.62	21.67%	75%
DAM3-C-B2-A-180	Internal Wall Plaster	15	08-Oct-26	26-Oct-26	48,590.16	10,527.87	36,442.62	21.67%	75%
ELECTRICAL		47	29-Sep-26	11-Nov-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
FIRST STAGE		47	29-Sep-26	11-Nov-26	32,798.20	4,688.76	27,642.87	14.3%	84.28%
DAM3-C-B2-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	29-Sep-26	04-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B2-E-113	Installation of Earthing and Grounding	5	05-Nov-26	11-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B2-E-183	Installation of Sleeves & Power outlet	8	29-Sep-26	08-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B2-E-163	Installation of Conduites for Lighting Fixture	4	13-Oct-26	18-Oct-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B1		41	08-Oct-26	22-Nov-26	32,798.20	3,228.53	27,642.87	9.84%	84.28%
ELECTRICAL		41	08-Oct-26	22-Nov-26	32,798.20	3,228.53	27,642.87	9.84%	84.28%
FIRST STAGE		41	08-Oct-26	22-Nov-26	32,798.20	3,228.53	27,642.87	9.84%	84.28%
DAM3-C-B1-E-113	Installation of Earthing and Grounding	5	16-Nov-26	22-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B1-E-183	Installation of Sleeves & Power outlet	8	08-Oct-26	17-Oct-26	2,920.45	1,460.23	1,460.23	50%	50%
DAM3-C-B1-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	08-Oct-26	12-Oct-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B1-E-163	Installation of Conduites for Lighting Fixture	4	22-Oct-26	26-Oct-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B7		63	24-Sep-26	28-Nov-26	469,986.51	103,093.46	313,977.73	21.94%	66.81%
ARCHITECTURAL		26	24-Sep-26	28-Nov-26	361,021.57	94,173.21	263,484.83	26.09%	72.98%
WALL FINISHES		4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B7-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	14-Nov-26	21-Nov-26	44,167.30	0.00	37,542.21	0%	85%
CIELING FINISHES		5	05-Nov-26	10-Nov-26	46,792.30	0.00	23,396.15	0%	50%
DAM3-C-B7-A-240	Installation of Ceiling Gypsum Board	5	05-Nov-26	10-Nov-26	46,792.30	0.00	23,396.15	0%	50%
DOORS & WINDOWS		7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	70,629.91	100%	75%
DAM3-C-B7-A-552	Window (CW1)	7	24-Sep-26	01-Oct-26	94,173.21	94,173.21	70,629.91	100%	75%
METAL WORKS		5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
DAM3-C-B7-A-292	Aluminium composite panel	5	23-Nov-26	28-Nov-26	175,888.76	0.00	131,916.57	0%	75%
ELECTRICAL		63	27-Sep-26	08-Nov-26	108,964.94	8,920.25	50,492.90	8.19%	46.34%
FIRST STAGE		63	27-Sep-26	08-Nov-26	32,798.20	8,920.25	27,642.87	27.2%	84.28%
DAM3-C-B7-E-113	Installation of Earthing and Grounding	5	03-Nov-26	08-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B7-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	27-Sep-26	30-Sep-26	1,768.31	1,768.31	884.15	100%	50%
DAM3-C-B7-E-183	Installation of Sleeves & Power outlet	8	27-Sep-26	05-Oct-26	2,920.45	2,920.45	1,460.23	100%	50%
DAM3-C-B7-E-163	Installation of Conduites for Lighting Fixture	4	11-Oct-26	14-Oct-26	8,462.97	4,231.49	7,616.67	50%	90%
SECOND STAGE		4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
DAM3-C-B7-E-153	Installation of Lighting fixtures	4	20-Oct-26	24-Oct-26	76,166.74	0.00	22,850.02	0%	30%
BLOCK B8		78	15-Oct-26	23-Dec-26	517,722.20	0.00	273,928.98	0%	52.91%
ARCHITECTURAL		75	15-Oct-26	19-Dec-26	314,229.27	0.00	160,938.75	0%	51.22%
WALL FINISHES		4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DAM3-C-B8-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	05-Dec-26	12-Dec-26	44,167.30	0.00	37,542.21	0%	85%
DOORS & WINDOWS		7	15-Oct-26	22-Oct-26	94,173.21	0.00	70,629.91	0%	75%
DAM3-C-B8-A-552	Window (CW1)	7	15-Oct-26	22-Oct-26	94,173.21	0.00	70,629.91	0%	75%
METAL WORKS		3	14-Dec-26	19-Dec-26	175,888.76	0.00	52,766.63	0%	30%
DAM3-C-B8-A-292	Aluminium composite panel	3	14-Dec-26	19-Dec-26	175,888.76	0.00	52,766.63	0%	30%
MECHANICAL		4	20-Dec-26	23-Dec-26	170,694.73	0.00	85,347.36	0%	50%
HVAC		4	20-Dec-26	23-Dec-26	170,694.73	0.00	85,347.36	0%	50%
FIRST STAGE		4	20-Dec-26	23-Dec-26	170,694.73	0.00	85,347.36	0%	50%
DAM3-C-B8-M-14	Installation of HVAC Ducts	2	20-Dec-26	21-Dec-26	149,489.33	0.00	74,744.66	0%	50%
DAM3-C-B8-M-17	Installation of Duct insulation	2	22-Dec-26	23-Dec-26	21,205.40	0.00	10,602.70	0%	50%

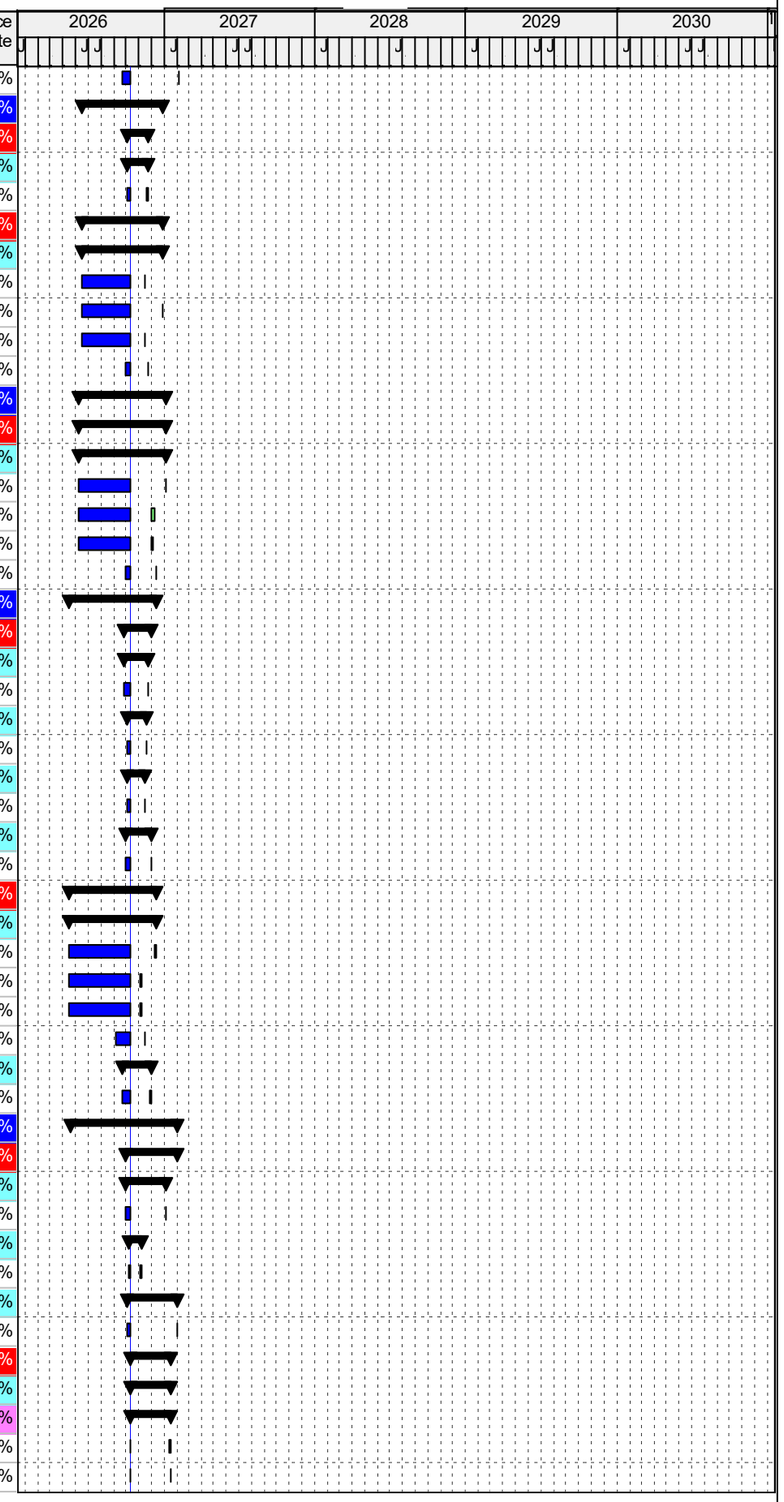

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-25	2 Weeks look ahead		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
ELECTRICAL		61	18-Oct-26	29-Nov-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		61	18-Oct-26	29-Nov-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B8-E-113	Installation of Earthing and Grounding	3	24-Nov-26	29-Nov-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B8-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	18-Oct-26	21-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B8-E-183	Installation of Sleeves & Power outlet	8	18-Oct-26	26-Oct-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B8-E-163	Installation of Conduites for Lighting Fixture	4	01-Nov-26	04-Nov-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B9		77	21-Oct-26	22-Dec-26	252,854.26	0.00	150,921.10	0%	59.69%
ARCHITECTURAL		9	08-Dec-26	22-Dec-26	220,056.06	0.00	123,278.22	0%	56.02%
WALL FINISHES		4	08-Dec-26	15-Dec-26	44,167.30	0.00	35,333.84	0%	80%
DAM3-C-B9-A-230	Paint to Plaster (Primer, Putty & First Coat)	4	08-Dec-26	15-Dec-26	44,167.30	0.00	35,333.84	0%	80%
METAL WORKS		3	17-Dec-26	22-Dec-26	175,888.76	0.00	87,944.38	0%	50%
DAM3-C-B9-A-292	Aluminium composite panel	3	17-Dec-26	22-Dec-26	175,888.76	0.00	87,944.38	0%	50%
ELECTRICAL		77	21-Oct-26	02-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		77	21-Oct-26	02-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B9-E-113	Installation of Earthing and Grounding	3	28-Nov-26	02-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B9-E-143	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	21-Oct-26	25-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B9-E-183	Installation of Sleeves & Power outlet	8	21-Oct-26	29-Oct-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B9-E-163	Installation of Conduites for Lighting Fixture	4	04-Nov-26	08-Nov-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B10		78	25-Oct-26	19-Dec-26	123,496.21	0.00	72,991.88	0%	59.1%
ARCHITECTURAL		21	25-Nov-26	19-Dec-26	90,698.01	0.00	45,349.01	0%	50%
WALL FINISHES		5	12-Dec-26	19-Dec-26	44,167.30	0.00	22,083.65	0%	50%
DAM3-C-B10-A-23	Paint to Plaster (Primer, Putty & First Coat)	5	12-Dec-26	19-Dec-26	44,167.30	0.00	22,083.65	0%	50%
FLOOR FINISHES		5	25-Nov-26	02-Dec-26	46,530.71	0.00	23,265.35	0%	50%
DAM3-C-B10-A-22	Tiles for Toilet	5	25-Nov-26	02-Dec-26	46,530.71	0.00	23,265.35	0%	50%
ELECTRICAL		78	25-Oct-26	06-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		78	25-Oct-26	06-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B10-E-11	Installation of Earthing and Grounding	5	01-Dec-26	06-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B10-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	25-Oct-26	28-Oct-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B10-E-18	Installation of Sleeves & Power outlet	4	25-Oct-26	02-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B10-E-16	Installation of Conduites for Lighting Fixture	4	08-Nov-26	11-Nov-26	8,462.97	0.00	7,616.67	0%	90%
BLOCK B11		81	28-Oct-26	09-Dec-26	81,388.36	0.00	51,937.96	0%	63.81%
ARCHITECTURAL		10	07-Nov-26	23-Nov-26	48,590.16	0.00	24,295.08	0%	50%
WALL FINISHES		10	07-Nov-26	23-Nov-26	48,590.16	0.00	24,295.08	0%	50%
DAM3-C-B11-A-18	Internal Wall Plaster	10	07-Nov-26	23-Nov-26	48,590.16	0.00	24,295.08	0%	50%
ELECTRICAL		75	28-Oct-26	09-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
FIRST STAGE		75	28-Oct-26	09-Dec-26	32,798.20	0.00	27,642.87	0%	84.28%
DAM3-C-B11-E-11	Installation of Earthing and Grounding	3	05-Dec-26	09-Dec-26	19,646.47	0.00	17,681.82	0%	90%
DAM3-C-B11-E-14	Installation of Conduits and wiring outlets - Fire Alarm Syste	4	28-Oct-26	01-Nov-26	1,768.31	0.00	884.15	0%	50%
DAM3-C-B11-E-18	Installation of Sleeves & Power outlet	8	28-Oct-26	05-Nov-26	2,920.45	0.00	1,460.23	0%	50%
DAM3-C-B11-E-16	Installation of Conduites for Lighting Fixture	4	11-Nov-26	15-Nov-26	8,462.97	0.00	7,616.67	0%	90%
SITE INFRASTRUCTURE		42	07-Sep-26	21-Oct-26	571,716.96	548,590.34	497,845.16	95.95%	87.08%
NETWORKS		42	07-Sep-26	21-Oct-26	571,716.96	548,590.34	497,845.16	95.95%	87.08%
INTERNAL FIRE FIGHTING WATER SUPPLY SYSTEM (OUTSIDE BUILDING UI		42	07-Sep-26	21-Oct-26	571,716.96	548,590.34	497,845.16	95.95%	87.08%
DAM3-C-ENV-F-212	Excavation for External Fire Fighting Works	7	07-Sep-26	14-Sep-26	40,471.58	40,471.58	36,424.43	100%	90%
DAM3-C-ENV-F-172	Installation of HDPE PN16 Pipes (200 Dia)	10	15-Sep-26	27-Sep-26	364,244.28	364,244.28	327,819.85	100%	90%
DAM3-C-ENV-F-192	Installation of Valves	5	30-Sep-26	05-Oct-26	86,057.93	86,057.93	68,846.34	100%	80%
DAM3-C-ENV-F-202	Warning Tapes	2	28-Sep-26	29-Sep-26	40,471.58	40,471.58	32,377.27	100%	80%
DAM3-C-ENV-F-222	Backfilling for External Fire Fighting Works	14	06-Oct-26	21-Oct-26	40,471.58	17,344.96	32,377.27	42.86%	80%
TESTING AND COMMISSIONING (10%)		5	08-Jul-26	13-Jul-26	167,105.15	167,105.15	41,776.29	100%	25%

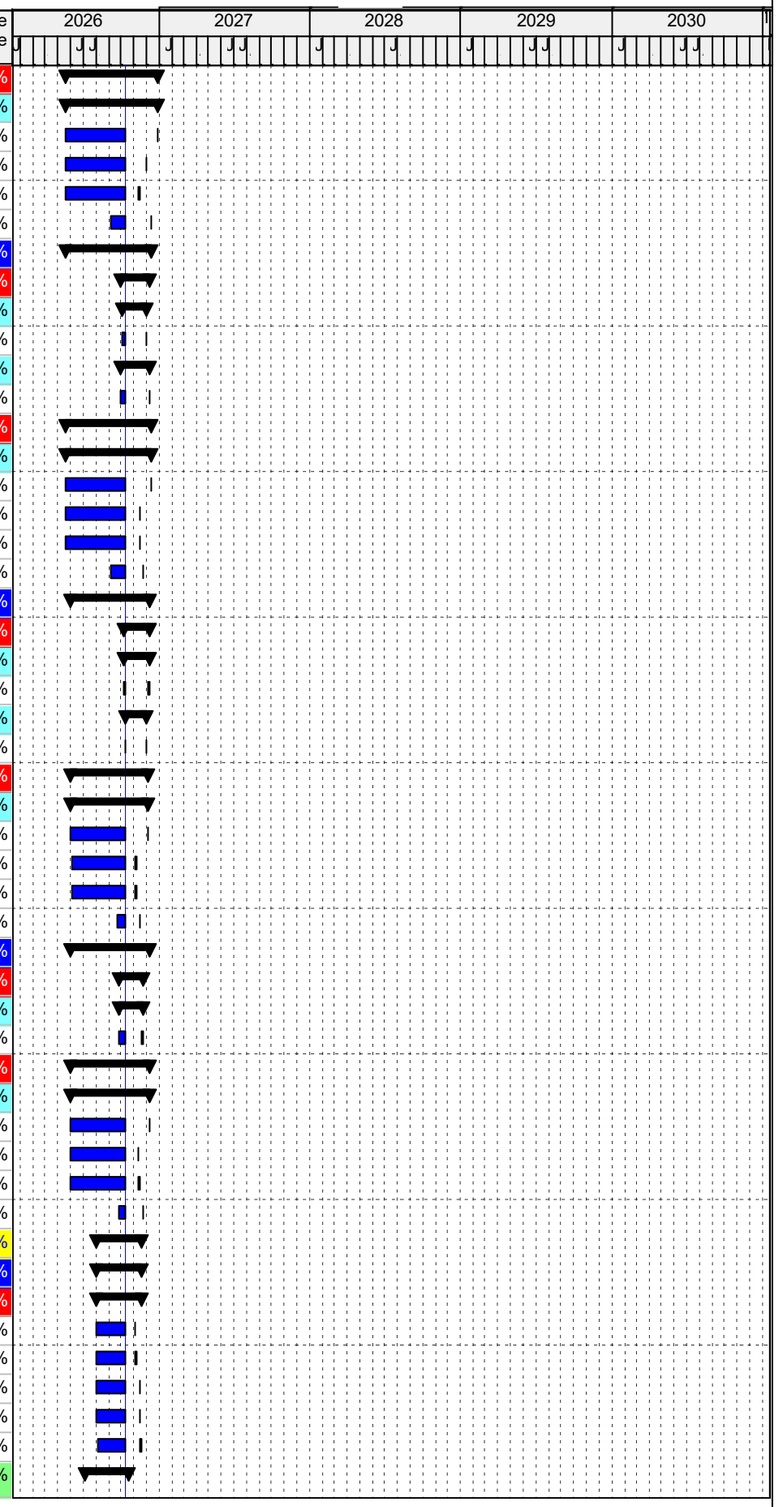

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-25	2 Weeks look ahead		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Budgeted Total Cost	Planned Value Cost	Earned Value Cost	Schedule % Complete	Performance % Complete
SNAGG WORKS		5	08-Jul-26	13-Jul-26	167,105.15	167,105.15	41,776.29	100%	25%
S001-C-TC-E-3606	Electrical Snagg works	5	08-Jul-26	13-Jul-26	167,105.15	167,105.15	41,776.29	100%	25%



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-25	2 Weeks look ahead		
