

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
44 READY BUILT FACTORIES 900 m2 IN AL DAMMAM #3		153	12-Feb-26	06-Mar-27	09-Jun-26 A	06-Mar-27	136
PROJECT MILESTONES		123	12-Feb-26	06-Mar-27	13-Oct-26	06-Mar-27	4
CONTRACTUAL MILESTONES		123	12-Feb-26	06-Mar-27	13-Oct-26	06-Mar-27	2
DAM3-PMS-MMS-0100	Project Completion Date	0		06-Mar-27		06-Mar-27	1
DAM3-PMS-MMS-0070	Completion of Site levelling, local roads & parkings	0		12-Feb-26		13-Oct-26	1
DISCIPLINE MILESTONES		0	21-Feb-27	21-Feb-27	25-Feb-27	25-Feb-27	2
900 SQM FACTORIES		0	21-Feb-27	21-Feb-27	25-Feb-27	25-Feb-27	1
DAM3-PMS-DMS-2370	Construction Finish	0		21-Feb-27		25-Feb-27	1
SITE INFRASTRUCTURE		0	21-Feb-27	21-Feb-27	25-Feb-27	25-Feb-27	1
DAM3-PMS-DMS-2450	Completion of External works	0		21-Feb-27		25-Feb-27	1
CONSTRUCTION (67%)		147	06-Jun-26	21-Feb-27	09-Jun-26 A	27-Feb-27	101
RBF 900 SQM FACTORIES		144	06-Jun-26	13-Jan-27	09-Jun-26 A	23-Feb-27	68
BLOCK B6		84	06-Jun-26	23-Nov-26	09-Jun-26 A	19-Jan-27	29
STRUCTURAL		7	30-Jun-26	07-Jul-26	21-Oct-26	28-Oct-26	1
SLAB ON GRADE		7	30-Jun-26	07-Jul-26	21-Oct-26	28-Oct-26	1
DAM3-C-B6-S-757	Concrete pad	7	30-Jun-26	07-Jul-26	21-Oct-26	28-Oct-26	1
STRUCTURAL STEEL		7	06-Jun-26	21-Jun-26	13-Oct-26	20-Oct-26	2
DAM3-C-B6-SS-1040	Epoxy paint to steel members at office area	7	06-Jun-26	13-Jun-26	13-Oct-26	20-Oct-26	1
DAM3-C-B6-SS-1060	Epoxy paint for external platform	5	16-Jun-26	21-Jun-26	13-Oct-26	18-Oct-26	1
ARCHITECTURAL		60	08-Jul-26	03-Nov-26	29-Oct-26	06-Jan-27	14
WALL FINISHES		40	08-Jul-26	06-Oct-26	29-Oct-26	14-Dec-26	2
DAM3-C-B6-A-630	Internal Wall Plaster	15	08-Jul-26	25-Jul-26	29-Oct-26	15-Nov-26	1
DAM3-C-B6-A-680	Paint to Plaster (Primer, Putty & First Coat)	7	29-Sep-26	06-Oct-26	07-Dec-26	14-Dec-26	1
CIELING FINISHES		5	20-Sep-26	26-Sep-26	29-Nov-26	03-Dec-26	1
DAM3-C-B6-A-690	Installation of Ceiling Gypsum Board	5	20-Sep-26	26-Sep-26	29-Nov-26	03-Dec-26	1
FLOOR FINISHES		41	13-Aug-26	03-Nov-26	21-Nov-26	06-Jan-27	4
DAM3-C-B6-A-670	Tiles for Toilet	7	13-Aug-26	20-Aug-26	21-Nov-26	28-Nov-26	1
DAM3-C-B6-A-700	Tiles for Office Area	2	27-Sep-26	28-Sep-26	05-Dec-26	06-Dec-26	1
DAM3-C-B6-A-830	Granite strip	2	29-Sep-26	30-Sep-26	07-Dec-26	08-Dec-26	1
DAM3-C-B6-A-850	Epoxy paint	5	27-Oct-26	03-Nov-26	02-Jan-27	06-Jan-27	1
WATER PROOFING WORKS		4	09-Aug-26	12-Aug-26	16-Nov-26	19-Nov-26	1
DAM3-C-B6-A-810	Waterproofing membrane for toilets	4	09-Aug-26	12-Aug-26	16-Nov-26	19-Nov-26	1
METAL WORKS		11	01-Oct-26	13-Oct-26	09-Dec-26	21-Dec-26	3
DAM3-C-B6-A-740	Steel Ladder	2	01-Oct-26	03-Oct-26	09-Dec-26	10-Dec-26	1
DAM3-C-B6-A-760	Aluminium composite panel	5	08-Oct-26	13-Oct-26	16-Dec-26	21-Dec-26	1
DAM3-C-B6-A-840	Steel railing works	4	04-Oct-26	07-Oct-26	12-Dec-26	15-Dec-26	1
SPECIALTIES		9	17-Oct-26	26-Oct-26	22-Dec-26	31-Dec-26	3
DAM3-C-B6-A-770	Installation of fittings	5	17-Oct-26	21-Oct-26	22-Dec-26	27-Dec-26	1
DAM3-C-B6-A-790	Furniture Installation	1	26-Oct-26	26-Oct-26	31-Dec-26	31-Dec-26	1
DAM3-C-B6-A-1000	Identification sign; ID01 & ID02	3	22-Oct-26	25-Oct-26	28-Dec-26	30-Dec-26	1
ELECTRICAL		49	07-Oct-26	23-Nov-26	09-Jun-26 A	19-Jan-27	12
FIRST STAGE		43	14-Oct-26	05-Nov-26	09-Jun-26 A	06-Jan-27	3
DAM3-C-B6-E-463	Installation of Wires	4	02-Nov-26	05-Nov-26	02-Jan-27	06-Jan-27	1
DAM3-C-B6-E-373	Installation of Conduits and wiring outlets - Fire Alarm System	4	14-Oct-26	18-Oct-26	09-Jun-26 A	23-Dec-26	1
DAM3-C-B6-E-393	Installation of Conduites for Lighting Fixture	4	28-Oct-26	01-Nov-26	01-Oct-26 A	02-Jan-27	1
SECOND STAGE		30	07-Oct-26	23-Nov-26	15-Dec-26	19-Jan-27	9
DAM3-C-B6-E-353	Installation of Fire Alarm Control Panel	3	19-Oct-26	22-Oct-26	24-Dec-26	27-Dec-26	1
DAM3-C-B6-E-363	Installation of Fire Detectors & Accessories	4	24-Oct-26	27-Oct-26	28-Dec-26	31-Dec-26	1

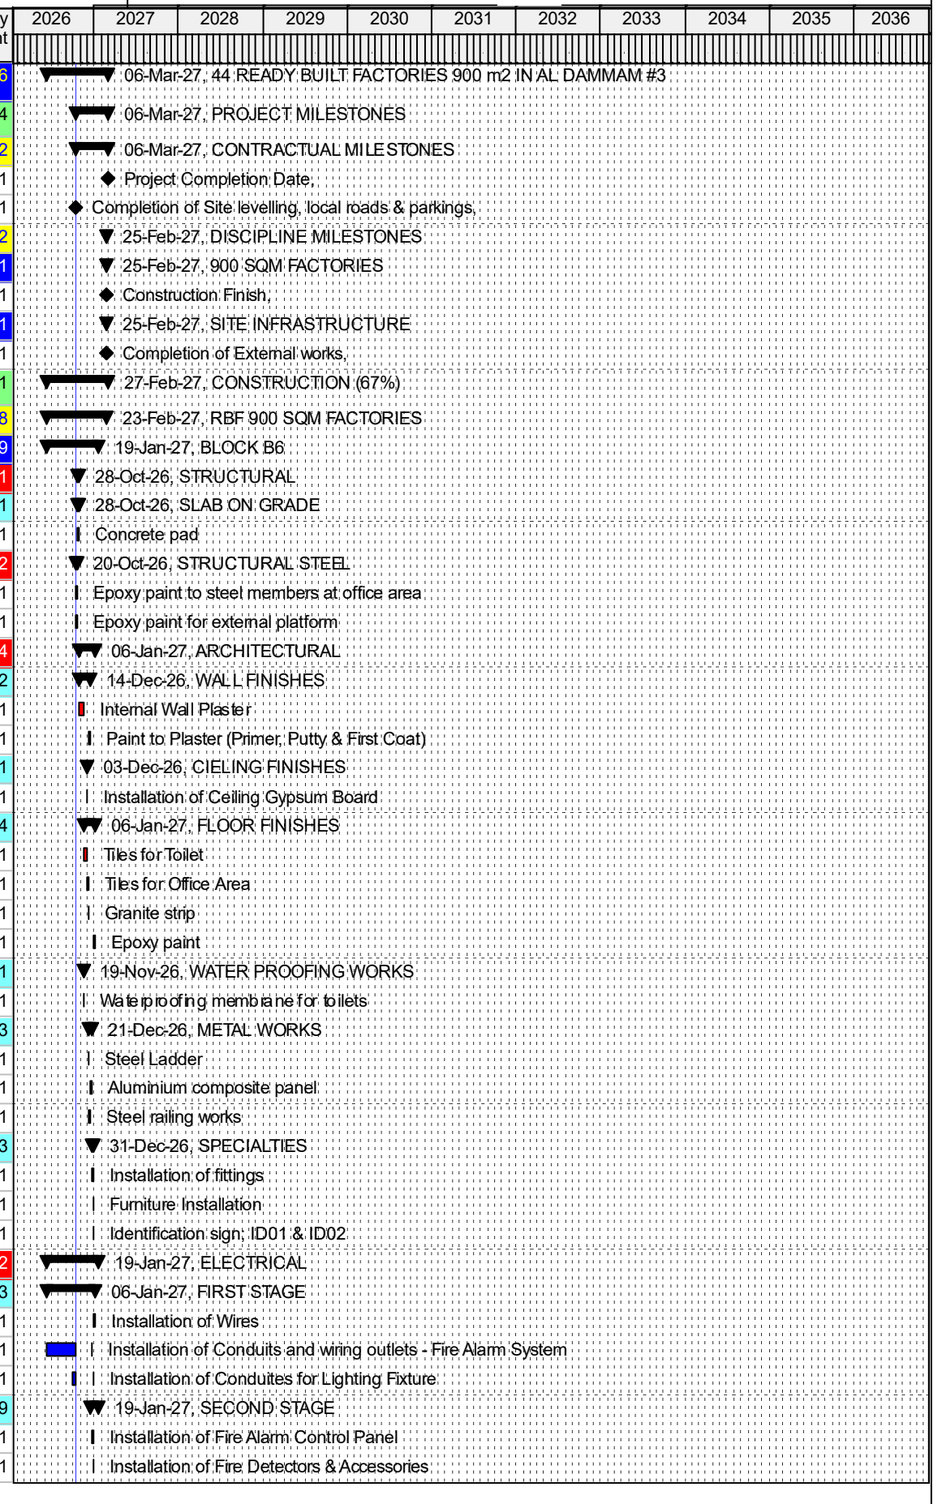

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-26	WEEKLY REPORT#34		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
DAM3-C-B6-E-383	Installation of Lighting fixtures	2	07-Nov-26	10-Nov-26	06-Jan-27	09-Jan-27	1
DAM3-C-B6-E-403	Installation of Wiring Devices	4	07-Oct-26	11-Oct-26	15-Dec-26	19-Dec-26	1
DAM3-C-B6-E-423	Installation of Main Distribution Board	2	11-Nov-26	12-Nov-26	09-Jan-27	11-Jan-27	1
DAM3-C-B6-E-433	Installation of Disconnect Switches	2	12-Oct-26	13-Oct-26	20-Dec-26	21-Dec-26	1
DAM3-C-B6-E-720	Installation of CCTV System	3	18-Nov-26	23-Nov-26	16-Jan-27	19-Jan-27	1
DAM3-C-B6-E-473	Installation of LP-1 Panel	2	14-Nov-26	15-Nov-26	11-Jan-27	13-Jan-27	1
DAM3-C-B6-E-483	Installation of PP-AC panel	2	16-Nov-26	17-Nov-26	13-Jan-27	16-Jan-27	1
BLOCK B3		134	24-Jun-26	20-Dec-26	17-Jun-26 A	10-Feb-27	23
STRUCTURAL STEEL		16	24-Jun-26	09-Jul-26	07-Oct-26 A	25-Oct-26	2
DAM3-C-B3-SS-1020	Epoxy paint to steel members at office area	7	02-Jul-26	09-Jul-26	17-Oct-26	25-Oct-26	1
DAM3-C-B3-A-1440	Steel members for office area	7	24-Jun-26	01-Jul-26	07-Oct-26 A	17-Oct-26	1
ARCHITECTURAL		91	28-Jul-26	20-Dec-26	12-Oct-26 A	10-Feb-27	13
WALL FINISHES		10	28-Jul-26	13-Aug-26	12-Oct-26 A	05-Nov-26	1
DAM3-C-B3-A-1040	Internal Wall Plaster	10	28-Jul-26	13-Aug-26	12-Oct-26 A	05-Nov-26	1
CIELING FINISHES		5	04-Nov-26	09-Nov-26	07-Jan-27	12-Jan-27	1
DAM3-C-B3-A-1100	Installation of Ceiling Gypsum Board	5	04-Nov-26	09-Nov-26	07-Jan-27	12-Jan-27	1
FLOOR FINISHES		80	19-Aug-26	20-Dec-26	10-Nov-26	10-Feb-27	4
DAM3-C-B3-A-1080	Tiles for Toilet	7	19-Aug-26	26-Aug-26	10-Nov-26	18-Nov-26	1
DAM3-C-B3-A-1110	Tiles for Office Area	2	10-Nov-26	11-Nov-26	13-Jan-27	14-Jan-27	1
DAM3-C-B3-A-1240	Granite strip	2	12-Nov-26	14-Nov-26	16-Jan-27	17-Jan-27	1
DAM3-C-B3-A-1260	Epoxy paint	3	13-Dec-26	20-Dec-26	08-Feb-27	10-Feb-27	1
WATER PROOFING WORKS		4	15-Aug-26	18-Aug-26	05-Nov-26	10-Nov-26	1
DAM3-C-B3-A-1220	Waterproofing membrane for toilets	4	15-Aug-26	18-Aug-26	05-Nov-26	10-Nov-26	1
METAL WORKS		11	15-Nov-26	26-Nov-26	18-Jan-27	30-Jan-27	3
DAM3-C-B3-A-1150	Steel Ladder	2	15-Nov-26	16-Nov-26	18-Jan-27	19-Jan-27	1
DAM3-C-B3-A-1170	Aluminium composite panel	5	22-Nov-26	26-Nov-26	25-Jan-27	30-Jan-27	1
DAM3-C-B3-A-1250	Steel railing works	4	17-Nov-26	21-Nov-26	20-Jan-27	24-Jan-27	1
SPECIALTIES		7	30-Nov-26	12-Dec-26	31-Jan-27	07-Feb-27	3
DAM3-C-B3-A-1180	Installation of fittings	3	30-Nov-26	07-Dec-26	31-Jan-27	02-Feb-27	1
DAM3-C-B3-A-1200	Furniture Installation	1	12-Dec-26	12-Dec-26	07-Feb-27	07-Feb-27	1
DAM3-C-B3-A-1410	Identification sign; ID01 & ID02	3	08-Dec-26	10-Dec-26	03-Feb-27	06-Feb-27	1
MECHANICAL		16	27-Aug-26	20-Sep-26	18-Nov-26	07-Dec-26	7
SEWER AND DRAINAGE SYSTEM		16	27-Aug-26	20-Sep-26	18-Nov-26	07-Dec-26	7
FIRST STAGE		2	27-Aug-26	29-Aug-26	18-Nov-26	21-Nov-26	1
DAM3-C-B3-M-840	Installation of Floor Drain	2	27-Aug-26	29-Aug-26	18-Nov-26	21-Nov-26	1
SECOND STAGE		14	05-Sep-26	20-Sep-26	21-Nov-26	07-Dec-26	6
DAM3-C-B3-M-800	Installation of Electric Water Heater	2	05-Sep-26	06-Sep-26	21-Nov-26	23-Nov-26	1
DAM3-C-B3-M-810	Installation of Sanitary Fixture and Accessories	4	07-Sep-26	10-Sep-26	23-Nov-26	28-Nov-26	1
DAM3-C-B3-M-830	Installation of Lavotary /Wash Basin	2	12-Sep-26	13-Sep-26	28-Nov-26	30-Nov-26	1
DAM3-C-B3-M-850	Installation of Water Tap	2	16-Sep-26	17-Sep-26	02-Dec-26	05-Dec-26	1
DAM3-C-B3-M-860	Installation of Roof Vent Cap	2	19-Sep-26	20-Sep-26	05-Dec-26	07-Dec-26	1
DAM3-C-B3-M-890	Installation of Bib Tap	2	14-Sep-26	15-Sep-26	30-Nov-26	02-Dec-26	1
ELECTRICAL		5	19-Jul-26	27-Jul-26	17-Jun-26 A	27-Oct-26	1
FIRST STAGE		5	19-Jul-26	27-Jul-26	17-Jun-26 A	27-Oct-26	1
DAM3-C-B3-E-643	Installation of Sleeves & Power outlet	5	19-Jul-26	27-Jul-26	17-Jun-26 A	27-Oct-26	1
BLOCK B2		4	21-Dec-26	02-Jan-27	11-Feb-27	15-Feb-27	2
ARCHITECTURAL		4	21-Dec-26	02-Jan-27	11-Feb-27	15-Feb-27	2
FLOOR FINISHES		3	22-Dec-26	02-Jan-27	13-Feb-27	15-Feb-27	1
DAM3-C-B2-A-420	Epoxy paint	3	22-Dec-26	02-Jan-27	13-Feb-27	15-Feb-27	1

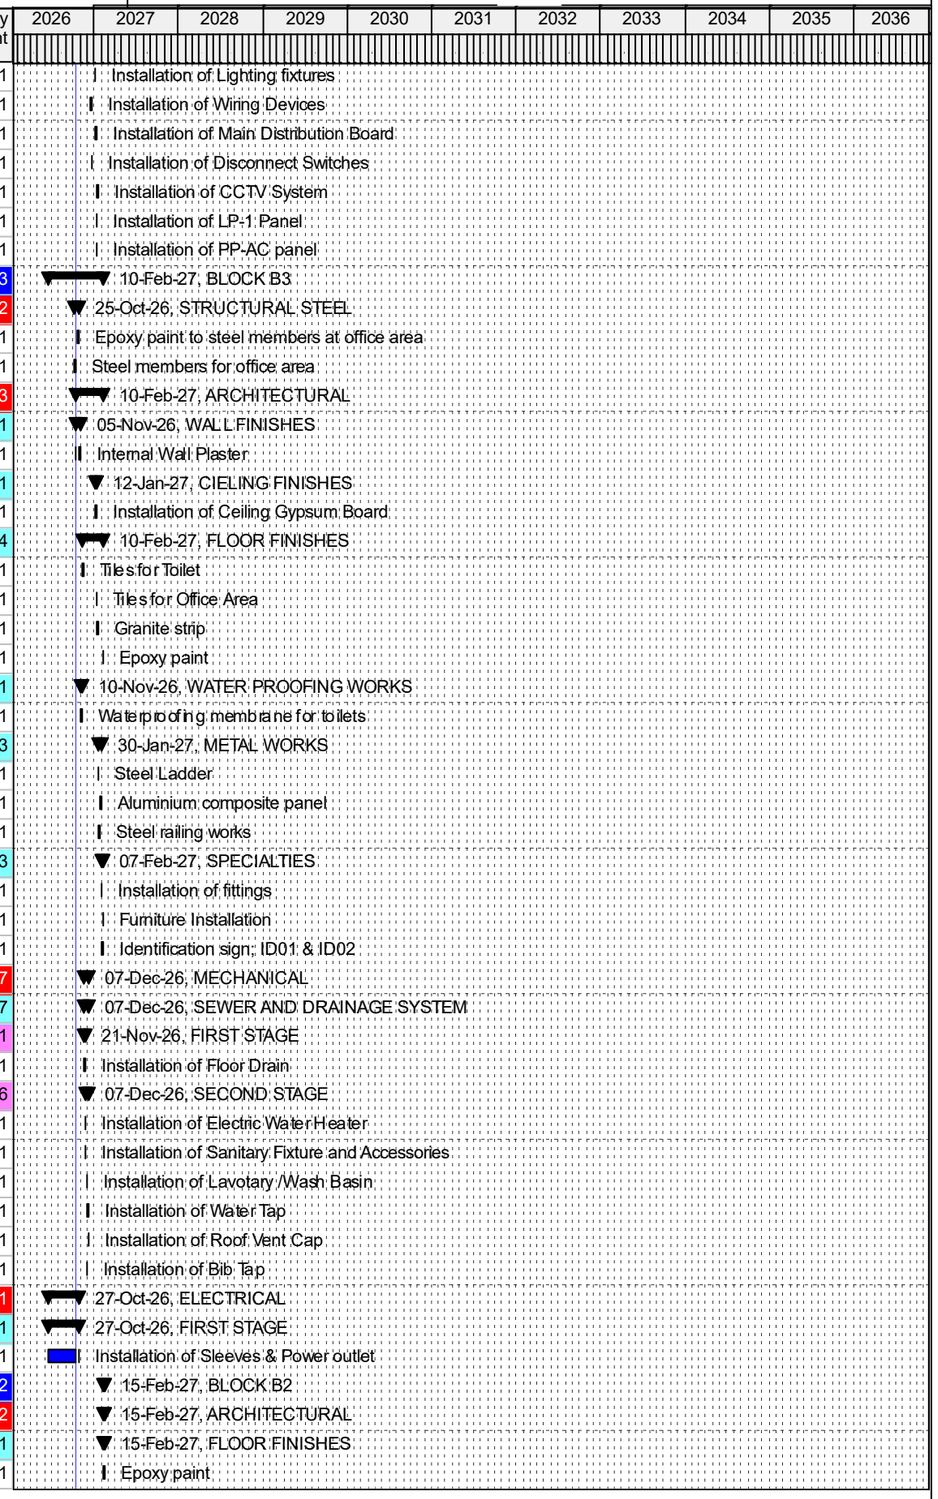

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-26	WEEKLY REPORT#34		


Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
SPECIALTIES		1	21-Dec-26	21-Dec-26	11-Feb-27	11-Feb-27	1
DAM3-C-B2-A-340	Furniture Installation	1	21-Dec-26	21-Dec-26	11-Feb-27	11-Feb-27	1
BLOCK B1		20	26-Nov-26	26-Dec-26	19-Jan-27	11-Feb-27	9
ARCHITECTURAL		5	26-Nov-26	06-Dec-26	19-Jan-27	25-Jan-27	2
WALL FINISHES		3	29-Nov-26	06-Dec-26	21-Jan-27	25-Jan-27	1
DAM3-C-B1-A-230	Paint to Plaster (Primer, Putty & First Coat)	3	29-Nov-26	06-Dec-26	21-Jan-27	25-Jan-27	1
FLOOR FINISHES		2	26-Nov-26	28-Nov-26	19-Jan-27	21-Jan-27	1
DAM3-C-B1-A-250	Tiles for Office Area	2	26-Nov-26	28-Nov-26	19-Jan-27	21-Jan-27	1
MECHANICAL		15	07-Dec-26	26-Dec-26	25-Jan-27	11-Feb-27	7
HVAC		12	07-Dec-26	22-Dec-26	25-Jan-27	08-Feb-27	6
FIRST STAGE		4	14-Dec-26	17-Dec-26	30-Jan-27	03-Feb-27	2
DAM3-C-B1-M-140	Installation of HVAC Ducts	2	14-Dec-26	15-Dec-26	30-Jan-27	01-Feb-27	1
DAM3-C-B1-M-170	Installation of Duct insulation	2	16-Dec-26	17-Dec-26	01-Feb-27	03-Feb-27	1
SECOND STAGE		12	07-Dec-26	22-Dec-26	25-Jan-27	08-Feb-27	4
DAM3-C-B1-M-130	Installation of Exhaust Fans	2	07-Dec-26	08-Dec-26	25-Jan-27	27-Jan-27	1
DAM3-C-B1-M-339	Installation of Diffuser	2	19-Dec-26	20-Dec-26	03-Feb-27	06-Feb-27	1
DAM3-C-B1-M-160	Installation of Wall Propeller Type Exhaust Fan	2	09-Dec-26	13-Dec-26	27-Jan-27	30-Jan-27	1
DAM3-C-B1-M-340	Supply, install, test and commission door grilles & exhaust lou	2	21-Dec-26	22-Dec-26	06-Feb-27	08-Feb-27	1
FIRE FIGHTING SYSTEM		3	23-Dec-26	26-Dec-26	08-Feb-27	11-Feb-27	1
SECOND STAGE		3	23-Dec-26	26-Dec-26	08-Feb-27	11-Feb-27	1
DAM3-C-B1-M-370	Supply, install, test and commission Fire Department Connect	3	23-Dec-26	26-Dec-26	08-Feb-27	11-Feb-27	1
BLOCK B8		9	27-Dec-26	13-Jan-27	13-Feb-27	23-Feb-27	5
ARCHITECTURAL		9	27-Dec-26	13-Jan-27	13-Feb-27	23-Feb-27	4
FLOOR FINISHES		2	06-Jan-27	13-Jan-27	21-Feb-27	23-Feb-27	1
DAM3-C-B8-A-420	Epoxy paint	2	06-Jan-27	13-Jan-27	21-Feb-27	23-Feb-27	1
SPECIALTIES		7	27-Dec-26	05-Jan-27	13-Feb-27	20-Feb-27	3
DAM3-C-B8-A-320	Installation of fittings	3	27-Dec-26	31-Dec-26	13-Feb-27	15-Feb-27	1
DAM3-C-B8-A-340	Furniture Installation	1	05-Jan-27	05-Jan-27	20-Feb-27	20-Feb-27	1
DAM3-C-B8-A-570	Identification sign; ID01 & ID02	3	02-Jan-27	04-Jan-27	16-Feb-27	18-Feb-27	1
MECHANICAL		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
FIRE FIGHTING SYSTEM		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
SECOND STAGE		3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
DAM3-C-B8-M-320	Installation of Fire Hose Cabinet	3	03-Jan-27	05-Jan-27	16-Feb-27	18-Feb-27	1
SITE INFRASTRUCTURE		69	21-Sep-26	21-Feb-27	07-Dec-26	27-Feb-27	33
EXTERNAL WORKS		69	21-Sep-26	10-Jan-27	07-Dec-26	27-Feb-27	18
EXTERNAL ELECTRICAL WORKS		32	21-Sep-26	09-Nov-26	07-Dec-26	13-Jan-27	6
DAM3-C-ENV-E-390	Installation of Telecom manhole	4	10-Oct-26	20-Oct-26	22-Dec-26	27-Dec-26	1
DAM3-C-ENV-E-410	Construction of Concrete encased duct bank	8	21-Sep-26	03-Oct-26	07-Dec-26	16-Dec-26	1
DAM3-C-ENV-E-420	Installation of Sleeves for lighting poles	5	04-Oct-26	08-Oct-26	16-Dec-26	22-Dec-26	1
DAM3-C-ENV-E-430	Installation of Lighting Fixture	5	04-Nov-26	09-Nov-26	07-Jan-27	13-Jan-27	1
DAM3-C-ENV-E-440	Installation of Lighting poles	5	27-Oct-26	03-Nov-26	02-Jan-27	07-Jan-27	1
DAM3-C-ENV-E-450	Foundation for Lighting poles	5	21-Oct-26	26-Oct-26	27-Dec-26	02-Jan-27	1
FENCES AND GATES		37	10-Nov-26	10-Jan-27	13-Jan-27	27-Feb-27	12
DAM3-C-ENV-S-1274	Lean Concrete Below Fence	4	23-Nov-26	26-Nov-26	20-Jan-27	25-Jan-27	1
DAM3-C-ENV-S-1284	Pouring Concrete for Footings	2	10-Dec-26	12-Dec-26	07-Feb-27	09-Feb-27	1
DAM3-C-ENV-S-1294	Installation of steel fence	2	06-Jan-27	07-Jan-27	21-Feb-27	24-Feb-27	1
DAM3-C-ENV-S-1304	Rebar for Footings	7	28-Nov-26	05-Dec-26	25-Jan-27	02-Feb-27	1
DAM3-C-ENV-S-1314	Formwork for Footings	4	06-Dec-26	09-Dec-26	02-Feb-27	07-Feb-27	1
DAM3-C-ENV-S-1324	Installation of steel members	2	29-Dec-26	05-Jan-27	18-Feb-27	21-Feb-27	1

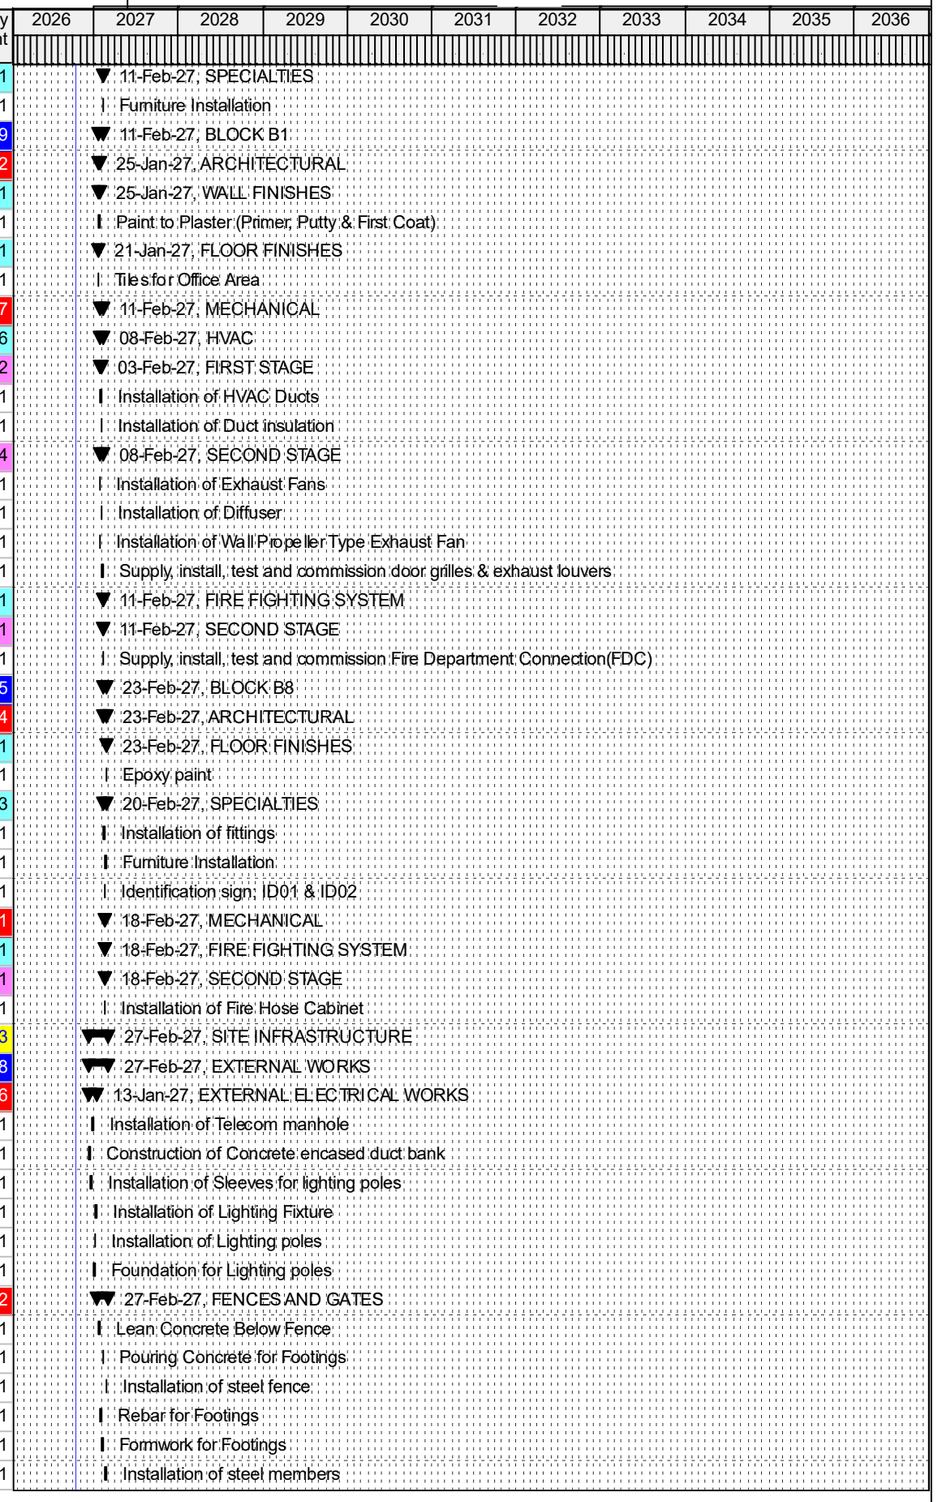

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-26	WEEKLY REPORT#34		

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Activity Count
DAM3-C-ENV-S-1334	Installation of base plate	2	23-Dec-26	28-Dec-26	16-Feb-27	18-Feb-27	1
DAM3-C-ENV-S-1344	Damp proof /Bitumin paint on Footing Sides	2	13-Dec-26	14-Dec-26	09-Feb-27	11-Feb-27	1
DAM3-C-ENV-S-1354	Vapour Barrier for Fence	4	18-Nov-26	22-Nov-26	16-Jan-27	20-Jan-27	1
DAM3-C-ENV-S-1364	Backfilling / Compaction Around Footings	4	15-Dec-26	22-Dec-26	11-Feb-27	16-Feb-27	1
DAM3-C-ENV-S-1374	Excavation for Fence	2	10-Nov-26	17-Nov-26	13-Jan-27	16-Jan-27	1
DAM3-C-ENV-S-1384	Installation of steel gates	2	09-Jan-27	10-Jan-27	24-Feb-27	27-Feb-27	1
ROAD WORKS		34	23-Nov-26	21-Feb-27	16-Jan-27	25-Feb-27	13
DAM3-C-ENV-R-890	Supply and install geotextile sheet	2	28-Jan-27	30-Jan-27	04-Feb-27	07-Feb-27	1
DAM3-C-ENV-R-1390	SubGrade Preparation & Compaction	5	23-Nov-26	03-Dec-26	16-Jan-27	21-Jan-27	1
DAM3-C-ENV-R-1400	Aggregate Base Course Layer	5	05-Dec-26	12-Dec-26	21-Jan-27	27-Jan-27	1
DAM3-C-ENV-R-1410	Asphalt Concrete Base Course Layer	2	09-Feb-27	10-Feb-27	14-Feb-27	16-Feb-27	1
DAM3-C-ENV-R-1420	Asphalt Concrete Wearing Course Layer	2	13-Feb-27	14-Feb-27	17-Feb-27	20-Feb-27	1
DAM3-C-ENV-R-1430	Retroreflective Thermoplastic White Traffic lines	2	15-Feb-27	16-Feb-27	20-Feb-27	23-Feb-27	1
DAM3-C-ENV-R-1440	Installation of Concrete wheel bumper	2	17-Feb-27	21-Feb-27	23-Feb-27	25-Feb-27	1
DAM3-C-ENV-R-1450	Prime Coat	1	08-Feb-27	08-Feb-27	13-Feb-27	14-Feb-27	1
DAM3-C-ENV-R-1460	Curb Stones	4	13-Dec-26	04-Jan-27	27-Jan-27	01-Feb-27	1
DAM3-C-ENV-R-1470	Tack Coat	1	11-Feb-27	11-Feb-27	16-Feb-27	17-Feb-27	1
DAM3-C-ENV-R-1480	Interlock Tiles	3	05-Jan-27	27-Jan-27	01-Feb-27	04-Feb-27	1
DAM3-C-ENV-R-1490	Gravel Bedding	2	31-Jan-27	01-Feb-27	07-Feb-27	09-Feb-27	1
DAM3-C-ENV-R-1500	Road Signs	3	02-Feb-27	07-Feb-27	09-Feb-27	13-Feb-27	1
LANDSCAPING		12	02-Feb-27	15-Feb-27	09-Feb-27	24-Feb-27	2
DAM3-C-ENV-R-1510	Planting of trees	5	02-Feb-27	07-Feb-27	09-Feb-27	15-Feb-27	1
DAM3-C-ENV-R-1520	Planting of shrubs	7	08-Feb-27	15-Feb-27	15-Feb-27	24-Feb-27	1
TESTING AND COMMISSIONING (10%)		4	10-Jan-27	18-Jan-27	20-Feb-27	24-Feb-27	2
TESTING AND COMMISSIONING 900 Sq.m-2		4	10-Jan-27	18-Jan-27	20-Feb-27	24-Feb-27	2
MECHANICAL		3	10-Jan-27	17-Jan-27	20-Feb-27	23-Feb-27	1
P001-C-TC-M-3386	Testing and Commissioning of Fire Hose Cabinet	3	10-Jan-27	17-Jan-27	20-Feb-27	23-Feb-27	1
ELECTRICAL		1	18-Jan-27	18-Jan-27	24-Feb-27	24-Feb-27	1
P001-C-TC-E-3476	Testing and Commissioning of Lighting Fixtures	1	18-Jan-27	18-Jan-27	24-Feb-27	24-Feb-27	1
PREOJECT CLOSEOUT		20	02-Feb-27	06-Mar-27	09-Feb-27	06-Mar-27	29

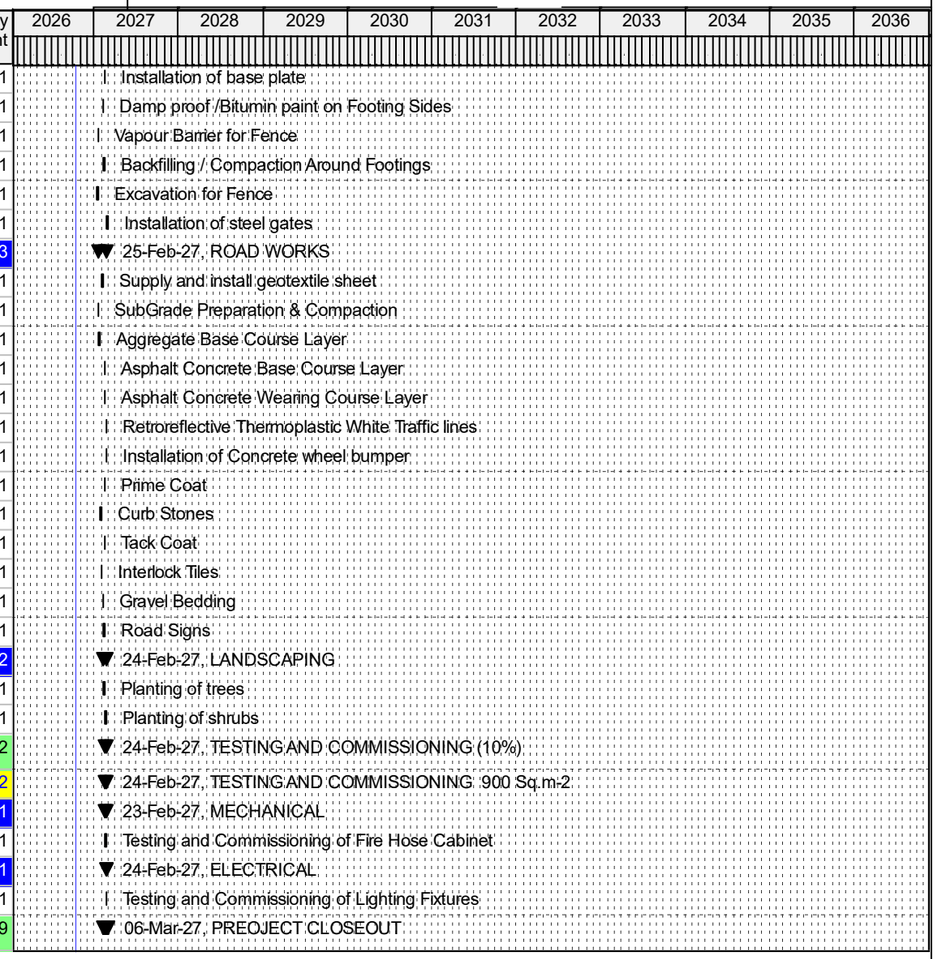

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

Date	Revision	Checked	Approved
13-Oct-26	WEEKLY REPORT#34		
