Completion of Infrastructure Works, Second Industrial City in Makkah

استكمال شبكات البنية التحتية بالمدينة الصناعية الثانية بمكة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Engr. Abdallah Aljulaifi	15-Feb-2026	14-Aug-2027

Scope: road works, box culverts, open drain channels and dike walls, street lighting and low-voltage cables, and concrete ducts at road crossings. Contract value 52,025,516 SAR excluding VAT, 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 81.3% against 51.1% planned, the project is 30.2% ahead of plan. This week it gained 1.23% against 1.13% planned, slightly above the weekly plan.

PHYSICAL % COMPLETE
81.3% / 51.1% plan
▲ SPI 1.59 +30.2%

PROGRESS THIS WEEK
+1.23% / +1.13% plan
▲ 0.10% above the weekly plan

CONTRACT TIME ELAPSED
46.6% · day 254 of 545
▼ Forecast finish 05-Sep-2027

INVOICED TO DATE (GROSS)
57.3% · 29.8M SAR
7 invoices, all paid; last period ends 26-Sep-2026

Well ahead of plan, but the forecast finish slipped to 22 days after the contract date.

The weekly report and the P6 update (UP 34, data date 27-Oct-2026) both forecast completion on 05-Sep-2027, 22 days after the contract completion date of 14-Aug-2027 and six days later than last week. Total float fell from –14 to –19 days. The negative float now runs through the open drain channels, the Ramp 2-In electrical works, the asphalt and finishing works on the connection to the 5th Ring Road, testing and commissioning, and close-out. Additional scope on Collector 9 and Road 52 is still open.

Site photos this week

Four photos from the Weekly Photos sheet of the 27-Oct-2026 weekly report, time-stamped 22 to 25-Oct-2026 where a stamp is visible. The photos carry no GPS stamp and are small in the source workbook (about 600 px wide). Select a photo to view it larger, then use the arrows to move between photos.



Cutting works, Collector 9

Excavator loading cut rock into dump trucks. No time stamp.



Aggregate base course, Non-Muslim Road

Roller and paver working along the road. Stamped 24-Oct-2026, 08:57.



Curbstone installation, Arterial Road 4

Curb line laid, with concrete mixers on site. Stamped 22-Oct-2026, 10:44.




Riprap works, Dike Wall 1

Riprap placed along the dike wall. Stamped 25-Oct-2026.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

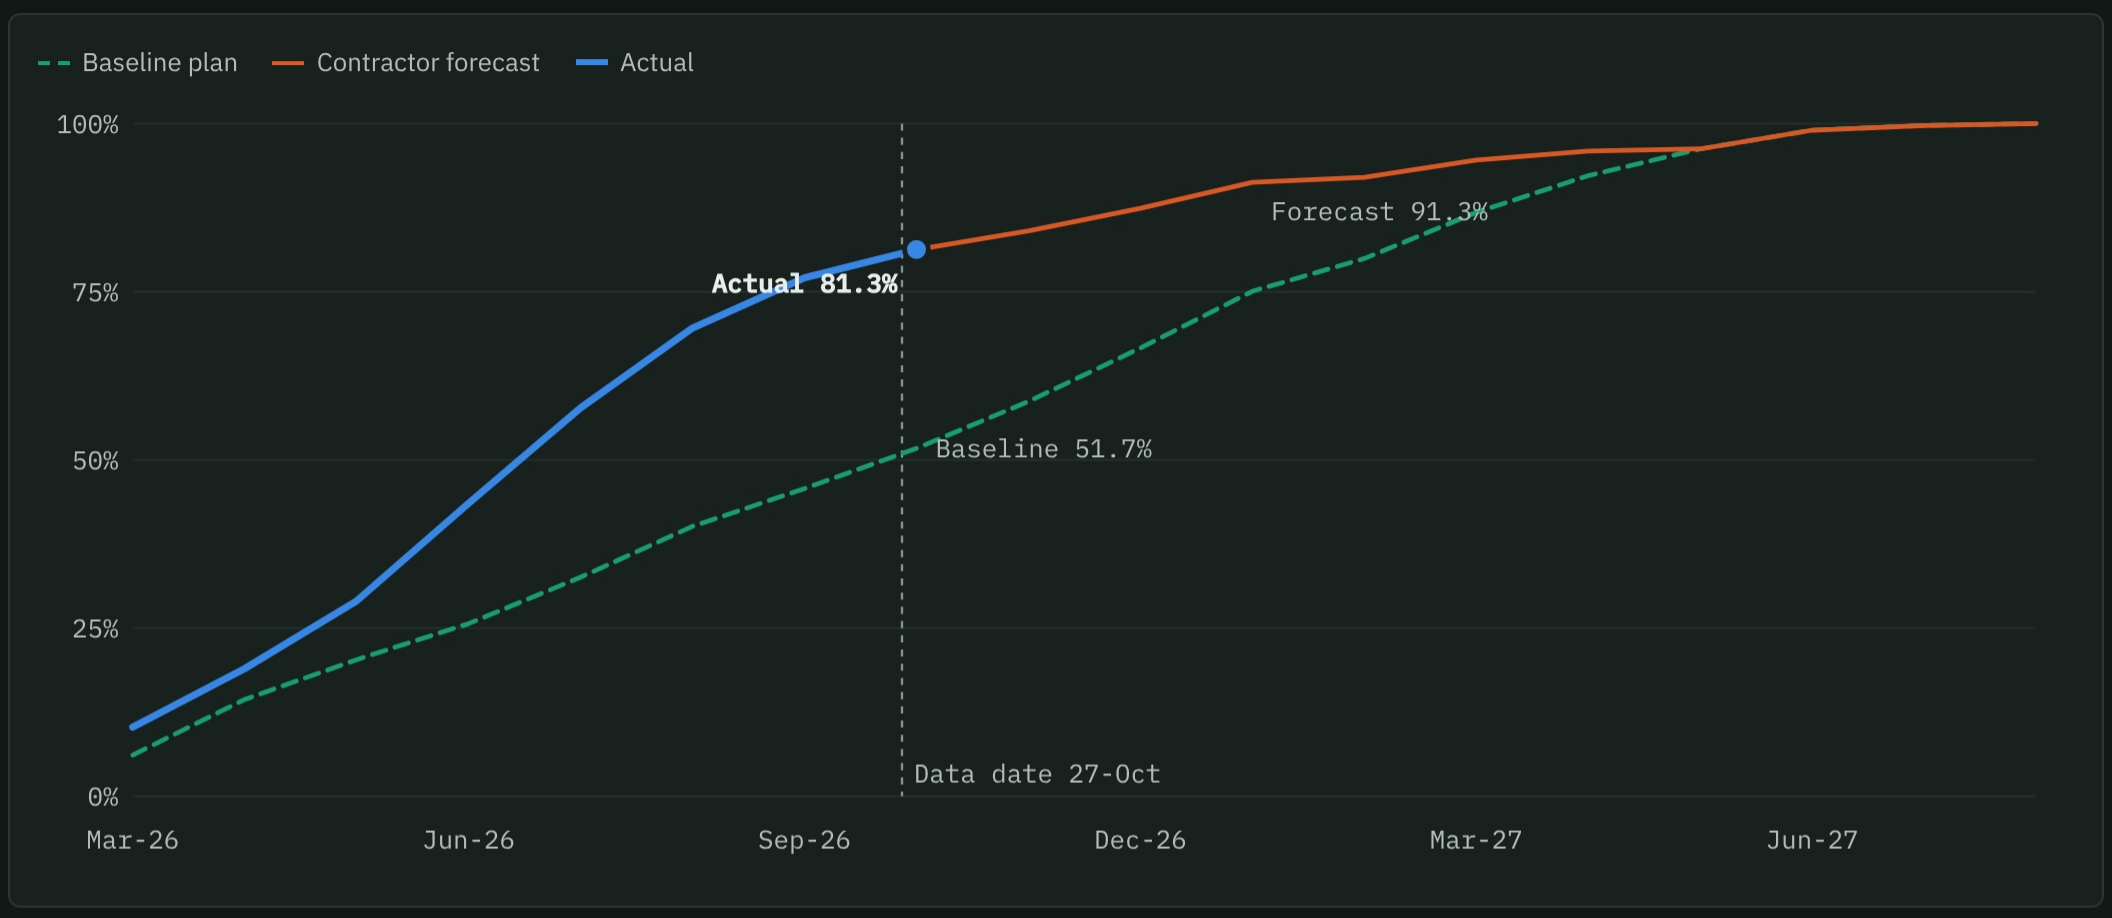

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	48.66	79.31	+30.65	—	1.63
20-Oct-2026	49.99	80.05	+30.06	+0.74	1.60
27-Oct-2026	**51.12**	**81.28**	**+30.16**	**+1.23**	**1.59**

Physical % complete from the man-hour totals in the 20-Oct-2026 and 27-Oct-2026 reports; the 20-Oct report also gives the 13-Oct cumulative values. The revised plan in the source is identical to the baseline, so the orange line shows the contractor's forecast: actual to September, then the forecast from October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	12.0%	100.0%	92.8%	−7.2%	0.93	▼ Behind
Road works	24.0%	50.2%	64.6%	+14.4%	1.29	▲ Ahead
Electrical works	8.3%	28.6%	71.8%	+43.1%	2.51	▲ Ahead
Demolition	1.3%	100.0%	67.6%	−32.4%	0.68	▼ Behind
Box culverts	3.5%	100.0%	100.0%	0.0%	1.00	✓ Complete
Open drain channels	37.6%	31.7%	96.2%	+64.5%	3.03	▲ Ahead
Testing & commissioning	3.0%	0.0%	5.6%	+5.6%	–	▲ Started early
Close-out & demobilisation	2.0%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**51.1%**	**81.3%**	**+30.2%**	**1.59**	▲ Ahead

The P6 update UP 34 (data date 27-Oct-2026) has 399 activities: 315 completed, 30 in progress and 54 not started. Its scheduled finish is 05-Sep-2027, 22 days after the contract date. There are 42 critical-path activities (43 last week). Testing of the electrical networks started on 20-Oct-2026.

Scope of work: quantities

Total, finished and remaining quantity for each network and major item. Network totals come from the Progress Summary sheet and item quantities from the Major Quantities sheet of the 27-Oct-2026 report. "This week" is this week's finished quantity minus the 20-Oct-2026 report's.

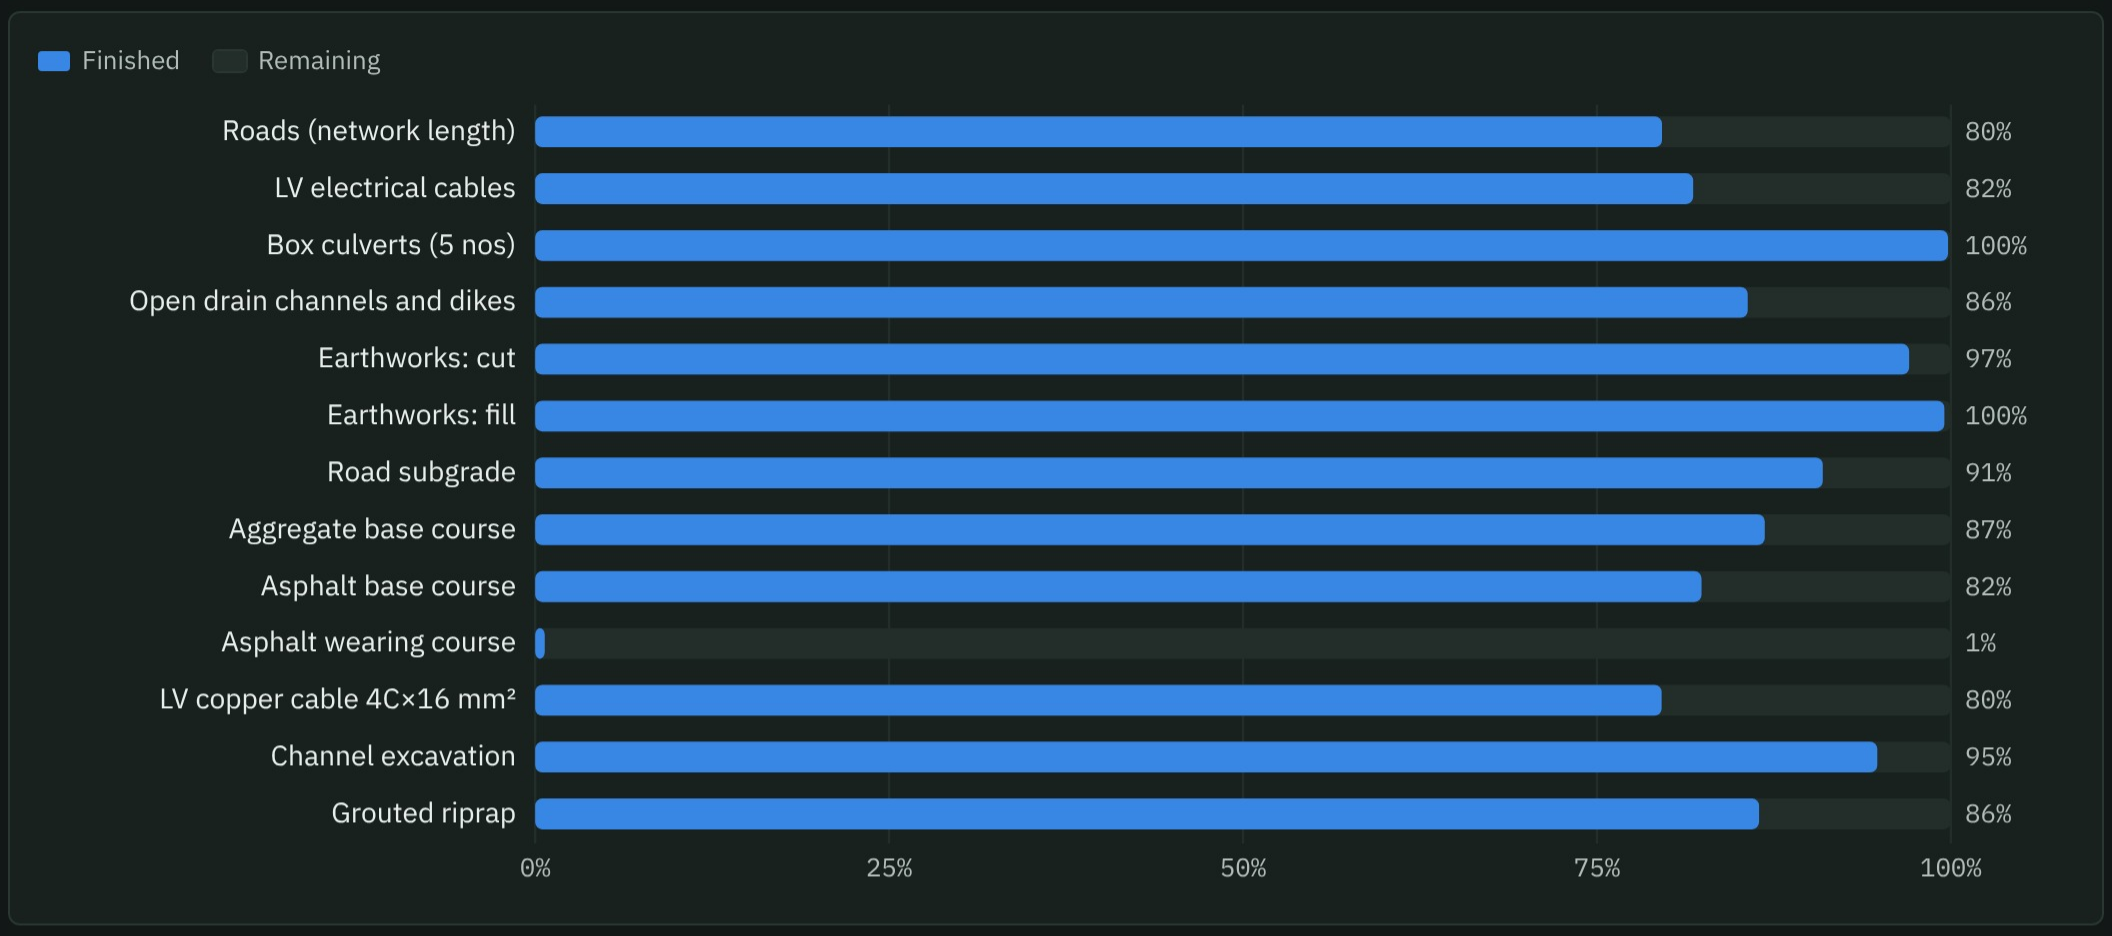

SCOPE ITEM	SOURCE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Roads (network length)	Progress Summary	LM	3,754	2,988	+189	766	79.6%
LV electrical cables	Progress Summary	LM	8,464	6,923	0	1,541	81.8%
Box culverts (5 nos)	Progress Summary	%	100	99.8	0	0.2	99.8%
Open drain channels and dikes	Progress Summary	LM	3,921	3,358	+279.1	562.6	85.6%
Earthworks: cut	B1.31 22 00.01	m³	537,044	521,210	+1,863	15,834	97.1%
Earthworks: fill	B1.31 22 00.02	m³	438,397	436,376	+474.7	2,020	99.5%
Road subgrade	B1.31 22 00.03	m³	37,334	33,956	+834.1	3,378	91.0%
Aggregate base course	B1.32 11 23.01	m³	24,889	21,617	+689.2	3,272	86.9%
Asphalt base course	B1.32 11 26.01	m³	11,676	9,619	+320.8	2,056	82.4%
Asphalt wearing course	B1.32 12 16.01	m³	5,253	35.6	0	5,218	0.7%
LV copper cable 4C×16 mm²	B2.26 05 19.01	m	8,007	6,371	0	1,636	79.6%
Channel excavation	B6.31 22 00.04	m³	115,262	109,271	0	5,991	94.8%
Grouted riprap	B6.31 25 00.02	m²	49,594	42,875	+3,018	6,719	86.5%

Box culverts and open channels

The five box culverts are 99.8% complete. Open drain channels and dikes reached 85.7% of their length (+279 m this week), and grouted riprap 86.5% after 3,018 m² this week on Open Channel 3C and Dike Wall 1.

Not yet started or barely started

The asphalt wearing course is still at 0.7% (35.6 of 5,253 m³), and the LV copper cable and channel excavation did not move this week. The summary sheets also list 471 m² of interlock paving on Arterial Road 4, but the report has no current total for interlock.

Milestones

Baseline and forecast dates from the weekly report's milestone sheet, with the forecast and float from the P6 update UP 34.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	15-Feb-2026	15-Feb-2026	15-Feb-2026 (actual)	–	✓ Done
Baseline programme approval	14-Mar-2026	01-Mar-2026	01-Mar-2026 (actual)	–	✓ Done
Completion of mobilisation	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Prequalification and material approval	14-Mar-2026	06-Jun-2026 (+84 d)	06-Jun-2026 (actual)	–	✓ Done
Long-lead materials delivered	16-Aug-2026	29-Aug-2026 (+13 d)	29-Aug-2026 (actual)	–	✓ Done
Completion of road works	14-Dec-2026	18-Jan-2027 (+35 d)	18-Jan-2027	39	▼ Later than baseline
Completion of open drain channels	14-Jun-2027	06-Jul-2027 (+22 d)	06-Jul-2027	−3	▼ Late
Completion of all works	14-Aug-2027	05-Sep-2027 (+22 d)	05-Sep-2027	−19	▼ Late
Final handover	14-Aug-2027	05-Sep-2027 (+22 d)	05-Sep-2027	−19	▼ Late

The weekly report and the P6 update agree on every forecast date, and all three open milestones slipped this week.

Completion of all works and final handover moved from 30-Aug to 05-Sep-2027, 22 calendar days after the contract date (P6 float −19 days). Road works moved from 11-Jan to 18-Jan-2027, 35 days after baseline, and the open drain channels from 29-Jun to 06-Jul-2027; their float fell from 3 to −3 days.

Procurement of key materials

Share of the required quantity procured, per material. Source: Procurement Log, weekly report 27-Oct-2026.



Pavement markings: no purchase order


5,712 m² required, 0% procured, although the material was required on site from 17-May-2026.

Asphalt and kerbs still being supplied

Bituminous base and wearing course is 57% procured (9,655 of 16,929 m³) and precast kerbs 82% (17,894 of 21,915 m). The report shows 17 of 18 planned materials on site, with the last road-works material due by 10-Nov-2026.

Manpower

Monthly average head count on site, manual and non-manual combined, planned vs actual.
Source: Manpower sheet.

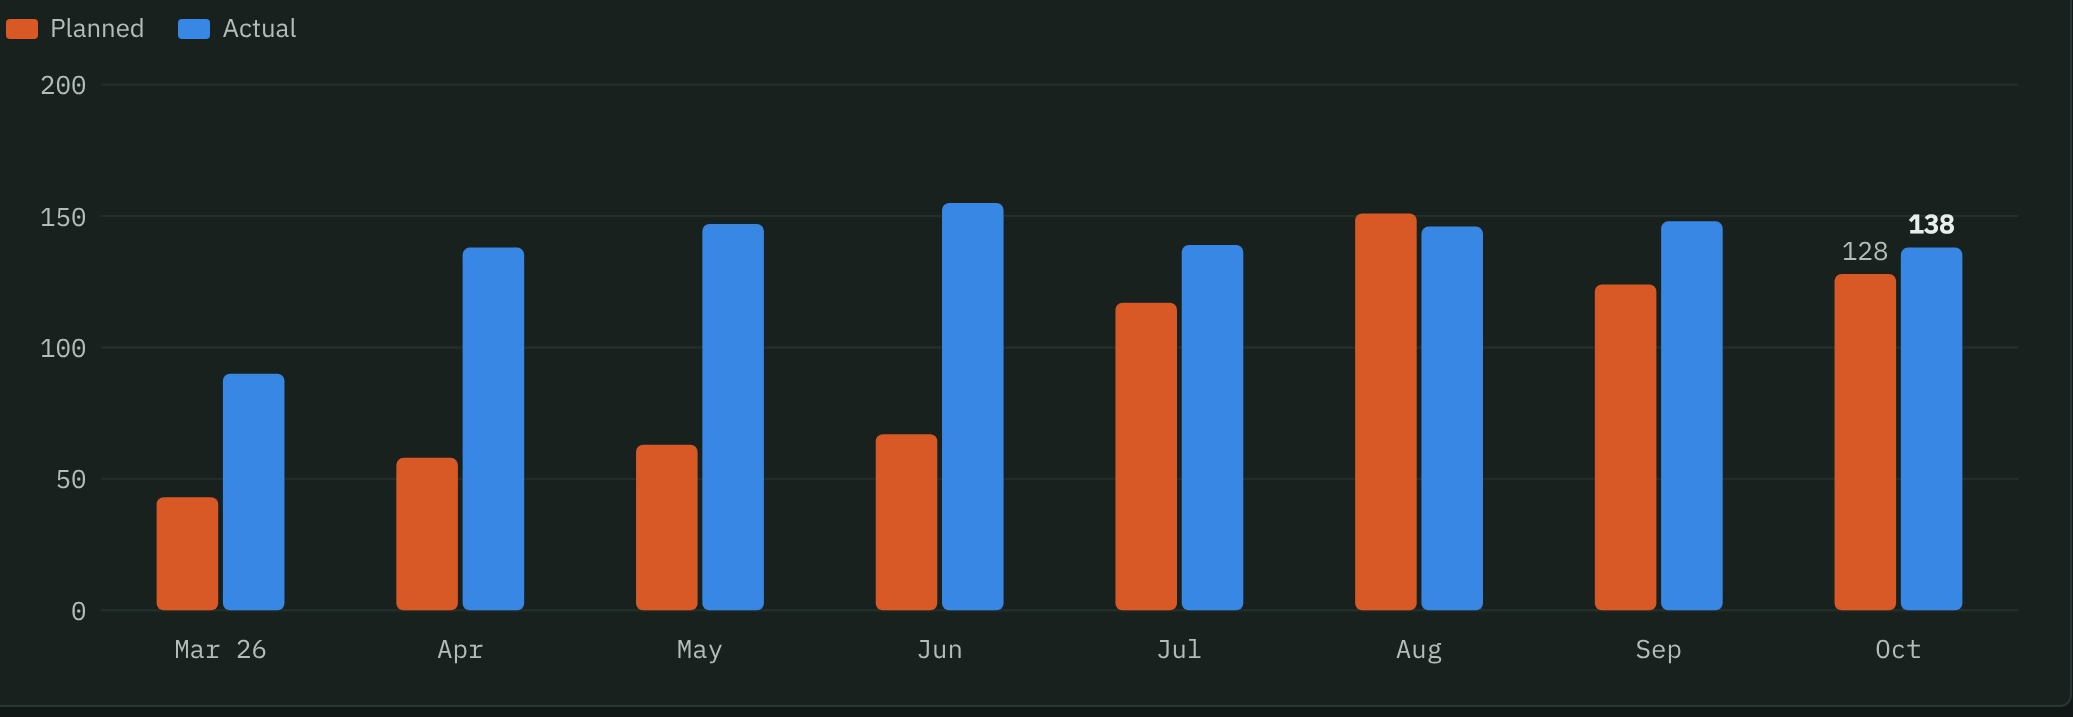

October head count averages 138 against 128 planned: 113 manual (116 planned) and 24.5 staff (12 planned). Equipment on site averages 64 units against 49 planned. The manual plan peaks at 161 in January 2027.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	52,025,516
Contract value incl. 15% VAT	59,829,343
Change orders	0
Potential changes	0
Estimate at completion	52,025,516
FIR value to date	41,145,140

All values in SAR. No change orders are registered.

Invoices

Invoices submitted	7
Gross value	29,797,667
Deductions and penalties	2,000
Net incl. VAT	34,269,317
Paid (7 invoices)	34,269,317
Approved, awaiting payment	0

Invoicing is 57.3% of the contract value against 81.3% physical progress. Invoice 7 (24-Aug to 26-Sep-2026) was paid on 25-Oct-2026, so no invoice is pending. No new invoice was submitted this week, and no retention or advance payment is recorded.

Health, safety and quality

Safety Score 87.5%

Safe man-hours (cumulative)	201,220
Man-hours this week	4,560
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses (cumulative)	1
Property damage	0
Inductions / toolbox talks	12 / 52

Consultant HSE inspection, 27-Oct-2026. Average score to date 85.3%.

Quality Score 90.1%

FIRs issued / closed	953 / 932
FIRs pending	21
NCRs issued / closed	2 / 2
Site instructions issued / closed	25 / 25
MIRs issued / closed	31 / 31
Shop drawings approved / submitted	36 / 36
Material submittals approved / submitted	63 / 65

Cumulative to 27-Oct-2026. Consultant quality inspection score 90.12% this week; average to date 84.9%. FIRs rose by 43 this week.

Open issues and risks

ISSUE	OWNER	DETAIL
Additional works, Collector 9	Contractor / MODON	Scope change adding works on Collector 9. Open in the risk register, target date 14-Nov-2026.
New Road 52	Contractor / MODON	Scope change to build Road 52, rated very high (score 25 after treatment). Open, target date 28-Dec-2026.
New Al Gloud Road	Contractor / MODON	Listed as a project challenge in the Progress Summary. The risk register shows it open; the risk log shows it closed, target date 01-Dec-2026.
Open drain channels and Ramp 2-In electrical works	Contractor	Both now carry –19 days of float in P6 UP 34 and, with close-out, set the project finish date. The open drain channel milestone moved to 06-Jul-2027, 22 days after baseline.
Connection to the 5th Ring Road	Contractor	Asphalt works started 08-Oct-2026 and are 35.0% complete by man-hours (3,792 of 10,830); with the finishing works they carry –18 days of float.

The weekly report's issue log and top-five issues table are empty this week, and the risk log (file 17) is unchanged from last week. Other register entries (design of Open Channel 3A, culvert 3, Hajj-period permits) are closed.

Data notes

- The two summary sheets (files 15 and 16) label a cost-based progress figure as "actual" and give a cost-based planned figure. This report uses physical % complete (man-hour weighted) only.
- Files 15 and 16 give this week's progress change with opposite signs (negative in file 15, positive in file 16).
- File 15 names the MODON PM as عبد الله الجليفي and file 16 as عبد الله الشنيفي. File 16 also gives project start 24-Nov-2025 and contract end 23-May-2026, against site handover 15-Feb-2026 and completion 14-Aug-2027 everywhere else.
- This week's quantities in the summary sheets (files 15 and 16) differ from the change in the Major Quantities sheet for fill (972 m³ against +474.7 m³) and aggregate base course (595 m³ against +689.2 m³); the summaries also omit the +320.8 m³ of asphalt base course. The report uses the Major Quantities change. The weekly table has no gain for 13-Oct-2026 because earlier reports were not used.
- The revised plan in the Physical-Chart Data sheet is identical to the baseline.
- The Major Quantities sheet has an older block of items at zero (subgrade 21,604 m³, base course 14,403 m³, kerbs 23,250 "m³", 15 kV cable 5,632 "m²", substation, RMU, 7 m lighting poles and others) next to the current items with progress. Only the current items are used.
- LV cable: the Major Quantities sheet gives 6,371 of 8,007 m installed; the Progress Summary gives 6,923 of 8,463.65 m.
- Luminaires are 264 in the Procurement sheet and 247 in the Progress Summary; earthing units 17 and 15. Procurement is 92.8% complete by man-hours although 17 of 18 materials are reported on site.
- The invoice summary shows 0 submitted invoices although 7 are logged, and a submitted value (34,267,317) 2,000 SAR below the approved and paid value (34,269,317). The revised contract value and EAC cells also hold 21,100,000 and 20,900,000 next to 52,025,516.
- General Information dates baseline schedule approval 01-Mar-2025, before contract award; the milestone sheet and P6 give 01-Mar-2026. The FIR summary for 21–27 Oct lists FIRs dated 17 to 20-Oct-2026, before the period, and still labels its previous total "up to 29-09-2026".
- Manual head count in October is 113.25 (116 planned) in the Manpower sheet, but the trade breakdown in the Weekly Progress Report sheet shows 105 planned and 108 actual.
- The risk dashboard (file 17) shows 240 open risks and 133 open issues but zero in every category; the log lists 8 risks, 3 of them open. Culvert 4 and Al Gloud Road are open in the weekly report's risk register but closed in file 17.
- The P6 milestone table inside the Milestones sheet (for example mobilisation 02-Apr-2026) is out of date; milestone forecasts and float are taken from the P6 file UP 34.

- The weekly report measures the delay as 22 calendar days; P6 gives –19 days of float. The Testing sheet shows testing of the electrical networks started on 20-Oct-2026 (20%), against a planned start of 08-May-2027.

Compiled 01-Nov-2026 from the weekly report of 27-Oct-2026 (report no. 37) and its P6 update UP 34, with the 20-Oct-2026 report for this week's changes.
