
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026		297	17-Feb-26	16-Dec-26	17-Feb-26 A	10-Feb-27	27,323,137.93	23,227,345.38	35,709,993.00	76.88%	65.36%	-47
MILESTONES		297	17-Feb-2	16-Dec-26	17-Feb-26 A	10-Feb-27	0.00	0.00	0.00	0%	0%	-47
GENERAL MILESTONES		297	17-Feb-2	16-Dec-26	17-Feb-26 A	10-Feb-27	0.00	0.00	0.00	0%	0%	-47
CONTRACUAL MILESTONES		235	05-May-2	16-Dec-26	05-May-26 A	10-Feb-27	0.00	0.00	0.00	0%	0%	-47
QASSIM		289	17-Feb-2	16-Dec-26	17-Feb-26 A	31-Jan-27	13,745,803.07	11,669,636.63	17,537,540.00	79.15%	67.2%	-39
MOBILIZATION		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
SITE OFFICES		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
GENERAL REQUIEREMENTS		57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
ENGINEERING		199	17-Feb-2	16-Aug-26	17-Feb-26 A	11-Oct-26	526,126.20	526,126.20	526,126.20	100%	100%	-47
SHOP DRAWINGS SUBMITTALS		168	17-Feb-2	04-Aug-26	17-Feb-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-57
STRUCTURAL DRAWINGS		125	17-Feb-2	06-Jul-26	17-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	25-Jun-26	06-Jul-26	01-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	1
TOILET BUILDING		43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-2	23-Jul-26	19-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-2	15-Apr-26	19-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-9
LANDSCAPE DRAWINGS		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		143	28-Feb-2	15-Jul-26	28-Feb-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-74
WATER SUPPLY SYSTEM		32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-44
ELECTRICAL DRAWINGS		102	11-May-2	04-Aug-26	11-May-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-57
POWER AND LIGHTING SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	11-Oct-26	0.00	0.00	0.00	0%	0%	-45
SHOP DRAWINGS APPROVALS		172	19-Feb-2	16-Aug-26	19-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
STRUCTURAL DRAWINGS		130	19-Feb-2	14-Jul-26	19-Feb-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-2	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		9	11-May-2	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		9	05-Jul-26	14-Jul-26	06-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	3
TOILET BUILDING		44	19-Feb-2	18-Apr-26	19-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		3	11-May-2	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-2	01-Aug-26	25-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-20
LANDSCAPE DRAWINGS		39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		154	09-Mar-2	27-Jul-26	09-Mar-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
WATER SUPPLY SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	12-Mar-2	14-Apr-26	12-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
ELECTRICAL DRAWINGS		100	20-May-2	16-Aug-26	20-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	28-Jul-26	16-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-10
MATERIAL SUBMITTALS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
CONCRETE WORK		43	04-Mar-2	28-Apr-26	04-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
SHORT LEAD ITEMS		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-2	15-Mar-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
HVAC WORK		19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		17	25-Feb-2	17-Mar-26	25-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
FIRE FIGHTING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0

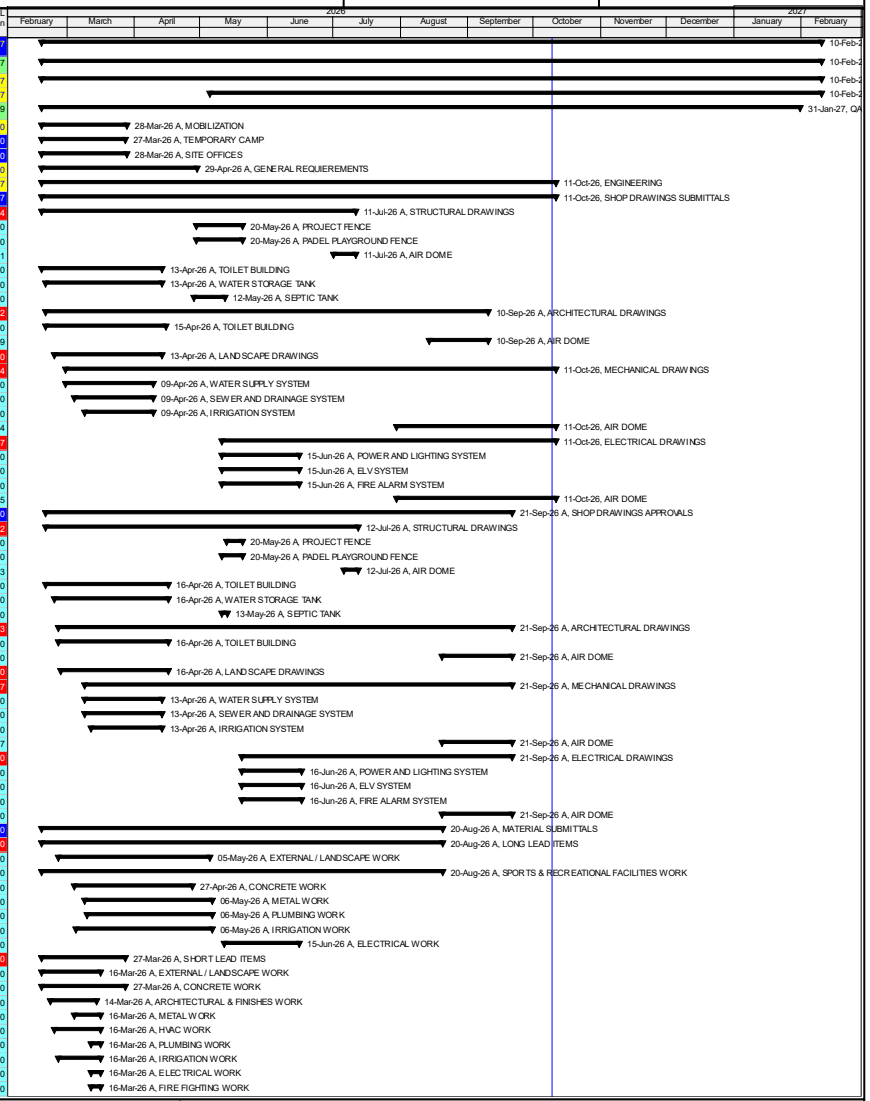


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
MATERIAL APPROVALS		196	21-Feb-2	18-Jul-26	21-Feb-26 A	01-Oct-26 A	526,126.20	526,126.20	526,126.20	100%	100%	-64
LONG LEAD ITEMS		189	02-Mar-2	18-Jul-26	02-Mar-26 A	01-Oct-26 A	358,885.26	358,885.26	358,885.26	100%	100%	-64
EXTERNAL / LANDSCAPE WORK		2	11-May-2	12-May-26	11-May-26 A	12-May-26 A	19,812.18	19,812.18	19,812.18	100%	100%	0
SPORTS & RECREATIONAL FACILITIES WORK		110	02-Mar-2	30-Jun-26	02-Mar-26 A	19-Sep-26 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
CONCRETE WORK		40	09-Mar-2	28-Apr-26	09-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
METAL WORK		112	09-Jun-26	18-Jul-26	09-Jun-26 A	01-Oct-26 A	889.23	889.23	889.23	100%	100%	-64
PLUMBING WORK		48	09-Jun-26	18-Jul-26	20-May-26 A	24-Jun-26 A	3,553.95	3,553.95	3,553.95	100%	100%	7
IRRIGATION WORK		45	11-Mar-2	06-May-26	11-Mar-26 A	06-May-26 A	24,486.75	24,486.75	24,486.75	100%	100%	0
ELECTRICAL WORK		96	12-May-2	02-Jul-26	12-May-26 A	16-Sep-26 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
SHORT LEAD ITEMS		25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	167,240.94	167,240.94	167,240.94	100%	100%	0
EXTERNAL / LANDSCAPE WORK		25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	139,867.29	139,867.29	139,867.29	100%	100%	0
CONCRETE WORK		24	23-Feb-2	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
ARCHITECTURAL & FINISHES WORK		17	25-Feb-2	16-Mar-26	25-Feb-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
METAL WORK		12	09-Mar-2	26-Mar-26	09-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
HVAC WORK		20	28-Feb-2	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
PLUMBING WORK		2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
IRRIGATION WORK		17	03-Mar-2	26-Mar-26	03-Mar-26 A	26-Mar-26 A	13,170.12	13,170.12	13,170.12	100%	100%	0
ELECTRICAL WORK		2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
FIRE FIGHTING WORK		2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
PROCUREMENT		220	03-Mar-2	27-Aug-26	03-Mar-26 A	24-Nov-26	4,735,135.80	3,896,713.20	4,735,135.80	100%	82.29%	-75
LONG LEAD ITEMS		207	18-Mar-2	27-Aug-26	18-Mar-26 A	24-Nov-26	3,229,967.34	2,438,081.97	3,229,967.34	100%	75.48%	-75
PURCHASE ORDER		147	18-Mar-2	12-Jul-26	18-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
EXTERNAL / LANDSCAPE WORK		5	06-May-2	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0%	0%	0
SPORTS & RECREATIONAL FACILITIES WORK		101	26-Mar-2	09-Jul-26	26-Mar-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		39	18-Mar-2	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		36	26-Mar-2	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		34	29-Mar-2	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		37	25-Mar-2	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		103	13-May-2	12-Jul-26	13-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
MANUFACTURE / FABRICATION		155	05-May-2	11-Aug-26	05-May-26 A	07-Nov-26	0.00	0.00	0.00	0%	0%	-74
EXTERNAL / LANDSCAPE WORK		109	05-May-2	23-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
SPORTS & RECREATIONAL FACILITIES WORK		123	05-May-2	11-Aug-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
CONCRETE WORK		69	05-May-2	12-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	15
METAL WORK		155	05-May-2	23-Jul-26	05-May-26 A	07-Nov-26	0.00	0.00	0.00	0%	0%	-90
PLUMBING WORK		79	05-May-2	23-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	25
IRRIGATION WORK		82	05-May-2	06-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-62
ELECTRICAL WORK		129	12-May-2	10-Aug-26	12-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-32
DELIVERY TO SITE		169	06-May-2	27-Aug-26	06-May-26 A	24-Nov-26	3,229,967.34	2,438,081.97	3,229,967.34	100%	75.48%	-75
EXTERNAL / LANDSCAPE WORK		123	06-May-2	10-Aug-26	06-May-26 A	11-Oct-26	178,309.62	176,866.75	178,309.62	100%	99.19%	-52
SPORTS & RECREATIONAL FACILITIES WORK		127	06-May-2	23-Aug-26	06-May-26 A	15-Oct-26	2,461,702.86	1,698,207.88	2,461,702.86	100%	68.99%	-45
CONCRETE WORK		78	06-May-2	23-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	16
METAL WORK		169	06-May-2	10-Aug-26	06-May-26 A	24-Nov-26	8,003.07	4,575.42	8,003.07	100%	57.17%	-90
PLUMBING WORK		104	06-May-2	10-Aug-26	06-May-26 A	10-Oct-26	31,985.55	31,595.03	31,985.55	100%	98.78%	-51
IRRIGATION WORK		102	06-May-2	15-Jul-26	06-May-26 A	10-Oct-26	220,380.75	219,357.96	220,380.75	100%	99.54%	-72
ELECTRICAL WORK		143	13-May-2	27-Aug-26	13-May-26 A	11-Oct-26	316,827.99	294,721.44	316,827.99	100%	93.02%	-37
SHORT LEAD ITEMS		183	03-Mar-2	12-Jul-26	03-Mar-26 A	15-Oct-26	1,505,168.46	1,458,631.23	1,505,168.46	100%	96.91%	-81
PURCHASE ORDER		64	03-Mar-2	21-May-26	03-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		57	03-Mar-2	13-May-26	03-Mar-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		39	04-Mar-2	23-Apr-26	04-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL & FINISHES WORK		48	07-Mar-2	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		36	25-Mar-2	06-May-26	25-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
HVAC WORK		46	09-Mar-2	06-May-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		33	29-Mar-2	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		43	12-Mar-2	06-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		8	12-May-2	21-May-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
FIRE FIGHTING WORK		30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
DELIVERY TO SITE		181	05-Mar-2	12-Jul-26	05-Mar-26 A	15-Oct-26	1,505,168.46	1,458,631.23	1,505,168.46	100%	96.91%	-81
EXTERNAL / LANDSCAPE WORK		155	05-Mar-2	08-Jul-26	05-Mar-26 A	14-Oct-26	1,258,805.61	1,235,050.47	1,258,805.61	100%	98.11%	-83
CONCRETE WORK		50	12-Mar-2	13-May-26	12-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
ARCHITECTURAL & FINISHES WORK		7	06-May-2	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
METAL WORK		129	06-May-2	08-Jul-26	06-May-26 A	13-Oct-26	4,310.01	3,792.81	4,310.01	100%	88%	-82
HVAC WORK		106	06-May-2	08-Jul-26	06-May-26 A	02-Oct-26 A	5,457.24	5,457.24	5,457.24	100%	100%	-72
PLUMBING WORK		7	06-May-2	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
IRRIGATION WORK		101	06-May-2	08-Jul-26	06-May-26 A	13-Oct-26	118,531.08	97,195.49	118,531.08	100%	82%	-82
ELECTRICAL WORK		128	11-May-2	12-Jul-26	11-May-26 A	15-Oct-26	3,667.68	2,787.44	3,667.68	100%	76%	-81
FIRE FIGHTING WORK		129	06-May-2	08-Jul-26	06-May-26 A	14-Oct-26	204.39	155.34	204.39	100%	76%	-83
CONSTRUCTION STAGE		258	24-Mar-2	16-Dec-26	24-Mar-26 A	25-Jan-27	8,431,928.45	6,922,352.74	10,522,524.00	81.46%	66.88%	-33
PLAYGROUND AND LANDSCAPING WORKS		258	24-Mar-2	16-Dec-26	24-Mar-26 A	25-Jan-27	5,108,188.92	5,163,264.28	6,019,638.42	87.35%	88.29%	-33
CUT AND FILL		38	24-Mar-2	06-May-26	24-Mar-26 A	06-May-26 A	729,000.00	729,000.00	900,600.00	100%	100%	0
PLAYGROUND WORKS		198	21-Apr-26	02-Dec-26	21-Apr-26 A	14-Dec-26	1,098,075.94	1,220,136.71	1,318,471.20	83.28%	92.54%	-9
FOOTBALL PLAYGROUND WORKS		164	21-Apr-26	17-Nov-26	21-Apr-26 A	03-Nov-26	564,254.70	571,303.60	611,282.16	92.31%	93.46%	12
BASKETBALL PLAYGROUND WORKS		163	30-Apr-26	17-Nov-26	30-Apr-26 A	03-Nov-26	367,838.34	372,446.93	381,705.12	96.37%	97.57%	13
PADEL PLAYGROUND WORKS		185	06-May-2	02-Dec-26	06-May-26 A	14-Dec-26	165,982.89	276,386.18	325,483.92	51%	84.92%	-9

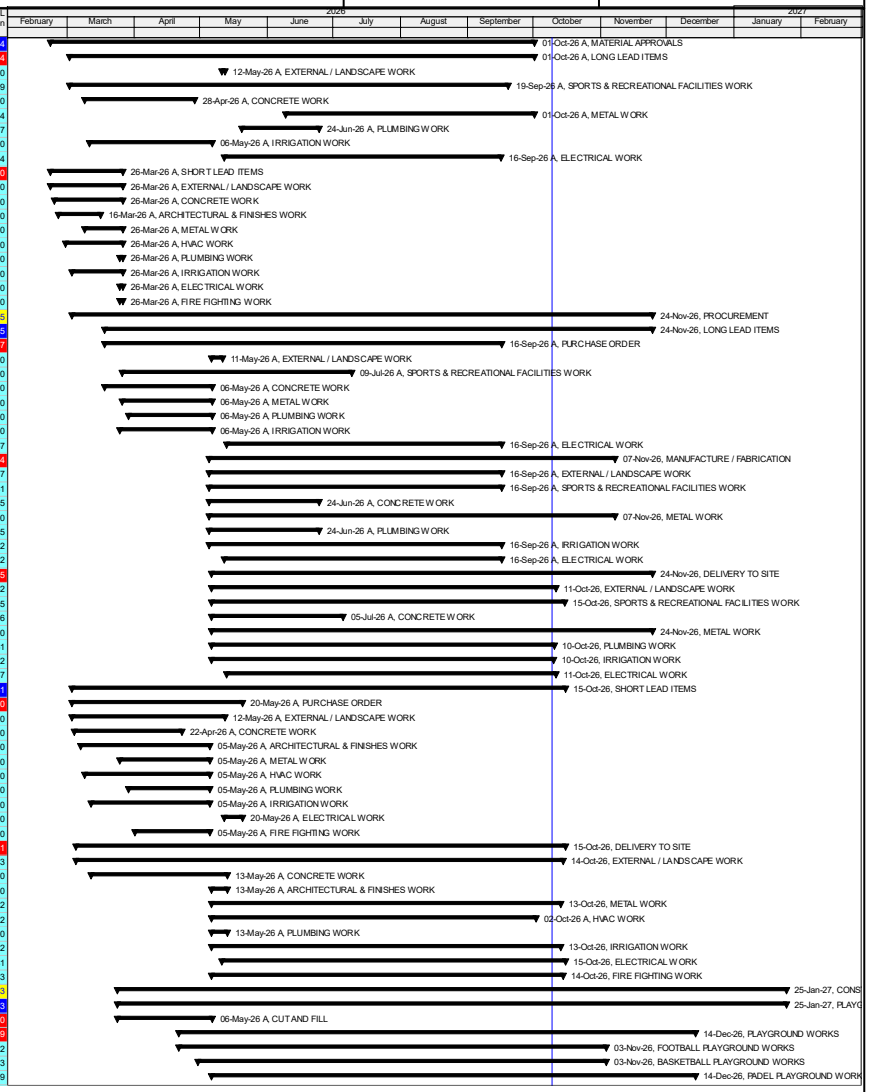


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	GENERAL SITE WORKS	238	16-Apr-26	16-Dec-26	16-Apr-26 A	25-Jan-27	1,494,285.96	1,303,724.63	1,617,941.82	92.36%	80.58%	-33
	FENCE WORKS	167	16-Apr-26	13-Sep-26	16-Apr-26 A	02-Nov-26	32,909.40	21,391.11	32,909.40	100%	65%	-42
	MECHANICAL WORK	149	12-May-26	18-Aug-26	12-May-26 A	08-Nov-26	780,707.34	670,165.14	780,707.34	100%	85.84%	-68
	STORM WATER AND UTILITY WORK	147	12-May-26	16-Aug-26	12-May-26 A	05-Nov-26	27,252.00	18,086.40	27,252.00	100%	66.37%	-68
	IRRIGATION SYSTEM WORKS	86	17-Jun-26	09-Aug-26	17-Jun-26 A	29-Oct-26	753,137.40	652,078.74	753,137.40	100%	86.58%	-68
	FIRE PROTECTION SYSTEM	2	17-Aug-26	18-Aug-26	05-Nov-26	08-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	192	20-May-26	01-Nov-26	20-May-26 A	05-Jan-27	660,770.22	519,487.58	693,965.28	95.22%	74.86%	-55
	POWER, LIGHTING & GROUNDING	157	20-May-26	20-Sep-26	20-May-26 A	25-Nov-26	636,895.08	519,487.58	636,895.08	100%	81.57%	-55
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	21-Sep-26	20-Oct-26	25-Nov-26	24-Dec-26	20,569.14	0.00	43,146.00	47.67%	0%	0
	FIRE ALARM SYSTEM	32	26-Sep-26	01-Nov-26	29-Nov-26	05-Jan-27	3,306.00	0.00	13,924.20	23.74%	0%	0
	PARKING WORK	172	17-Jun-26	09-Nov-26	17-Jun-26 A	05-Jan-27	19,899.00	88,440.00	102,919.80	19.33%	85.93%	-48
	SERVICE CONNECTION	56	10-Nov-26	16-Dec-26	12-Jul-26 A	25-Jan-27	0.00	4,240.80	7,440.00	0%	57%	-136
	LANDSCAPING WORKS	166	31-May-26	14-Dec-26	30-May-26 A	12-Dec-26	1,738,536.62	1,886,825.54	2,134,335.00	81.46%	88.87%	3
	HARDSCAPE WORK	166	31-May-26	14-Dec-26	30-May-26 A	12-Dec-26	1,623,036.62	1,688,925.54	1,712,409.00	94.78%	98.63%	3
	SOFTSCAPE WORK	145	10-Jun-26	21-Nov-26	10-Jun-26 A	28-Nov-26	115,500.00	207,900.00	421,926.00	27.37%	49.27%	-5
	TANK WORKS	132	13-May-26	19-Aug-26	13-May-26 A	19-Oct-26	48,290.40	13,577.40	48,290.40	100%	28.12%	-51
	SEPTIC TANK	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	7,475.22	7,475.22	7,475.22	100%	100%	0
	WATER STORAGE TANK	132	13-May-26	19-Aug-26	13-May-26 A	19-Oct-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-51
	AIR DOME CONSTRUCTION	204	13-May-26	26-Nov-26	13-May-26 A	11-Jan-27	3,075,439.54	1,461,181.68	4,178,041.20	73.61%	34.97%	-39
	CIVIL WORK	143	13-May-26	10-Sep-26	13-May-26 A	01-Nov-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-43
	ARCHITECTURAL WORK	33	27-Oct-26	26-Nov-26	27-Aug-26 A	11-Jan-27	0.00	125,244.14	712,953.22	0%	17.57%	-90
	MECHANICAL WORK	16	12-Sep-26	30-Sep-26	01-Nov-26	19-Nov-26	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	78	17-Aug-26	26-Oct-26	27-Aug-26 A	15-Dec-26	695,800.80	125,244.14	1,085,449.25	64.1%	11.54%	-34
	TOILET BUILDING WORKS	171	06-May-26	20-Oct-26	06-May-26 A	28-Nov-26	248,300.00	297,906.77	324,844.38	76.44%	91.71%	-33
	CIVIL WORK	171	06-May-26	19-Oct-26	06-May-26 A	26-Nov-26	150,709.46	207,912.72	227,117.58	66.36%	91.54%	-33
	STRUCTURAL WORK	85	06-May-26	04-Aug-26	06-May-26 A	10-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	22
	ARCHITECTURAL WORK	116	05-Aug-26	19-Oct-26	12-Jul-26 A	26-Nov-26	112,729.46	169,932.72	189,137.58	59.6%	89.85%	-54
	GENERAL FINISHES	107	05-Aug-26	19-Oct-26	12-Jul-26 A	26-Nov-26	59,414.61	77,117.22	84,120.00	70.63%	91.68%	-54
	WET AREA FINISHES	59	20-Aug-26	14-Oct-26	06-Aug-26 A	19-Oct-26	44,077.85	79,515.30	81,123.78	54.33%	98.02%	-16
	ROOF FINISHES	38	01-Oct-26	19-Oct-26	20-Aug-26 A	26-Nov-26	9,237.00	13,300.20	23,893.80	38.66%	55.66%	-68
	MEP WORK	132	16-Jun-26	20-Oct-26	16-Jun-26 A	28-Nov-26	97,590.54	89,994.05	97,726.80	99.86%	92.09%	-33
	MECANICAL WORKS	132	16-Jun-26	20-Oct-26	16-Jun-26 A	28-Nov-26	79,343.22	71,746.73	79,479.48	99.83%	90.27%	-33
	FIRE FIGHTING SYSTEM	1	20-Oct-26	20-Oct-26	01-Oct-26 A	28-Nov-26	0.00	40.88	136.26	0%	30%	-49
	SEWER AND DRAINAGE SYSTEM	103	16-Jun-26	02-Sep-26	16-Jun-26 A	18-Oct-26	11,290.02	9,032.02	11,290.02	100%	80%	-37
	HVAC SYSTEM	26	12-Aug-26	23-Aug-26	13-Aug-26 A	12-Oct-26	12,127.20	6,747.84	12,127.20	100%	55.64%	-40
	WATER SUPPLY SYSTEM	80	16-Jun-26	31-Aug-26	16-Jun-26 A	07-Sep-26 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
	ELECTRICAL WORKS	47	13-Jul-26	15-Sep-26	22-Jul-26 A	08-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	14
	PROJECT CLOSOUT	213	23-May-26	16-Dec-26	22-May-26 A	31-Jan-27	52,612.62	324,444.49	1,753,754.00	3%	18.5%	-39
	HAIL	278	17-Feb-26	16-Dec-26	17-Feb-26 A	21-Jan-27	5,566,215.15	5,267,934.80	6,814,652.00	81.68%	77.3%	-31
	MOBILIZATION	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	51	17-Feb-26	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	168	17-Feb-26	14-Jul-26	17-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	SHOP DRAWINGS SUBMITTALS	93	17-Feb-26	16-Jun-26	17-Feb-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	17-Feb-26	05-May-26	17-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	57	17-Feb-26	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	55	25-Feb-26	05-May-26	25-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	24-Feb-26	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	52	01-Mar-26	05-May-26	01-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	31	01-Mar-26	11-Apr-26	01-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	05-Mar-26	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	10-Mar-26	05-May-26	10-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	SHOP DRAWINGS APPROVALS	92	19-Feb-26	17-Jun-26	19-Feb-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	19-Feb-26	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	55	19-Feb-26	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	42	23-Feb-26	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-26	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-26	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	46	10-Mar-26	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0

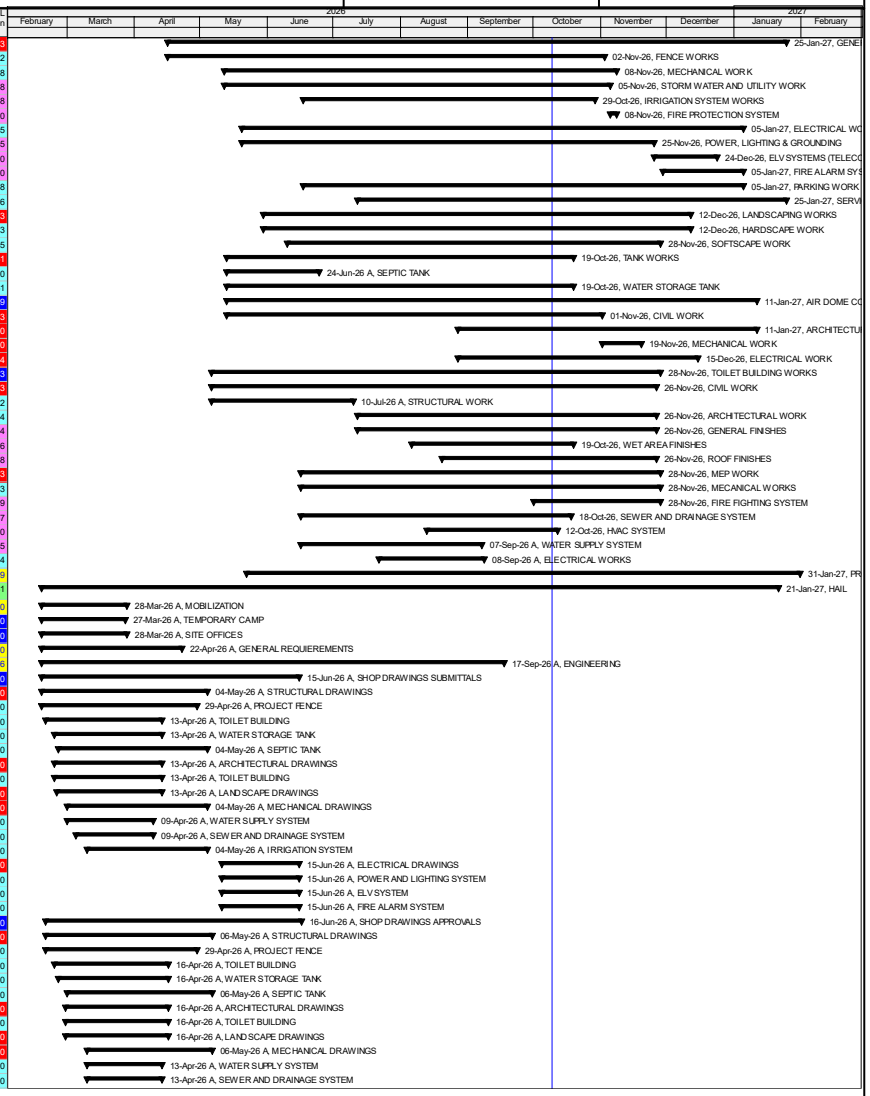


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	IRRIGATION SYSTEM	43	14-Mar-26	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL SUBMITTALS	166	17-Feb-26	06-Jul-26	17-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	LONG LEAD ITEMS	163	21-Feb-26	06-Jul-26	21-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-26	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	47	08-Mar-26	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	41	07-Mar-26	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	60	21-Feb-26	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	99	12-May-26	06-Jul-26	12-May-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	SHORT LEAD ITEMS	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	165	21-Feb-26	14-Jul-26	21-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	LONG LEAD ITEMS	162	25-Feb-26	14-Jul-26	25-Feb-26 A	17-Sep-26 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-26	06-May-26	25-Feb-26 A	06-May-26 A	26,079.63	26,079.63	26,079.63	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	43	14-Mar-26	06-May-26	14-Mar-26 A	06-May-26 A	38,839.50	38,839.50	38,839.50	100%	100%	0
	CONCRETE WORK	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	12,818.25	12,818.25	12,818.25	100%	100%	0
	ELECTRICAL WORK	101	12-May-26	14-Jul-26	12-May-26 A	17-Sep-26 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	93,374.07	93,374.07	93,374.07	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	72,133.44	72,133.44	72,133.44	100%	100%	0
	CONCRETE WORK	24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	8,114.01	8,114.01	8,114.01	100%	100%	0
	METAL WORK	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	6,854.64	6,854.64	6,854.64	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	209	26-Feb-26	26-Aug-26	26-Feb-26 A	10-Nov-26	1,839,956.04	1,787,818.60	1,839,956.04	100%	97.17%	-63
	LONG LEAD ITEMS	203	05-Mar-26	26-Aug-26	05-Mar-26 A	10-Nov-26	999,589.41	982,156.13	999,589.41	100%	96.26%	-63
	PURCHASE ORDER	162	05-Mar-26	22-Jul-26	05-Mar-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	109	11-May-26	22-Jul-26	11-May-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	MANUFACTURE / FABRICATION	184	01-Apr-26	12-Aug-26	01-Apr-26 A	07-Nov-26	0.00	0.00	0.00	0%	0%	-73
	EXTERNAL / LANDSCAPE WORK	103	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	SPORTS & RECREATIONAL FACILITIES WORK	97	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	93	01-Apr-26	06-Jul-26	01-Apr-26 A	27-Jun-26 A	0.00	0.00	0.00	0%	0%	8
	METAL WORK	155	05-May-26	23-Jul-26	05-May-26 A	07-Nov-26	0.00	0.00	0.00	0%	0%	-90
	PLUMBING WORK	120	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	IRRIGATION WORK	107	05-May-26	08-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-54
	ELECTRICAL WORK	131	12-May-26	12-Aug-26	12-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-25
	DELIVERY TO SITE	147	07-May-26	26-Aug-26	06-May-26 A	10-Nov-26	999,589.41	962,156.13	999,589.41	100%	96.26%	-63
	EXTERNAL / LANDSCAPE WORK	118	07-May-26	06-Aug-26	06-May-26 A	11-Oct-26	234,716.67	229,646.97	234,716.67	100%	97.84%	-54
	SPORTS & RECREATIONAL FACILITIES WORK	106	07-May-26	06-Aug-26	06-May-26 A	11-Oct-26	349,555.50	336,394.01	349,555.50	100%	96.23%	-54
	CONCRETE WORK	67	07-May-26	12-Jul-26	06-May-26 A	07-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	4
	METAL WORK	130	07-May-26	06-Aug-26	06-May-26 A	10-Nov-26	8,003.07	7,042.70	8,003.07	100%	88%	-80
	PLUMBING WORK	130	07-May-26	06-Aug-26	06-May-26 A	11-Oct-26	31,985.55	31,048.30	31,985.55	100%	97.07%	-54
	IRRIGATION WORK	108	07-May-26	18-Jul-26	06-May-26 A	04-Sep-26 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
	ELECTRICAL WORK	142	13-May-26	26-Aug-26	13-May-26 A	11-Oct-26	247,206.87	229,902.39	247,206.87	100%	93%	-37
	SHORT LEAD ITEMS	196	26-Feb-26	16-Jul-26	26-Feb-26 A	20-Oct-26	840,366.63	825,662.48	840,366.63	100%	98.25%	-81
	PURCHASE ORDER	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0

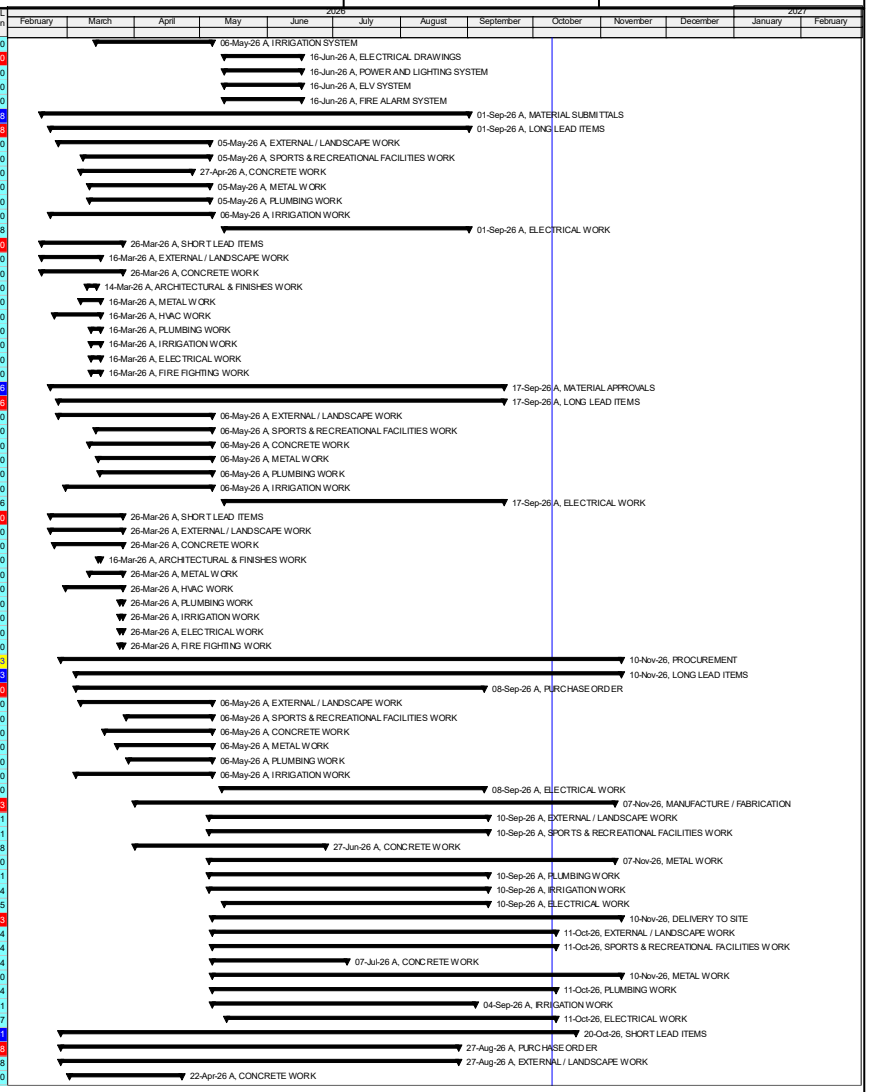


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	102	05-May-26	02-Jul-26	05-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	ELECTRICAL WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	DELIVERY TO SITE	194	01-Mar-26	16-Jul-26	01-Mar-26 A	20-Oct-26	840,366.63	825,662.48	840,366.63	100%	98.25%	-81
	EXTERNAL / LANDSCAPE WORK	166	01-Mar-26	16-Jul-26	01-Mar-26 A	11-Oct-26	649,200.96	640,265.10	649,200.96	100%	98.62%	-73
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	73,026.09	73,026.09	73,026.09	100%	100%	0
	METAL WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	4,310.01	4,310.01	4,310.01	100%	100%	0
	HVAC WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	113	06-May-26	16-Jul-26	06-May-26 A	11-Oct-26	61,691.76	57,064.88	61,691.76	100%	92.5%	-73
	ELECTRICAL WORK	117	20-May-26	16-Jul-26	20-May-26 A	14-Oct-26	3,667.68	2,640.73	3,667.68	100%	72%	-76
	FIRE FIGHTING WORK	129	20-May-26	16-Jul-26	20-May-26 A	20-Oct-26	204.39	89.93	204.39	100%	44%	-81
	CONSTRUCTION STAGE	243	05-Apr-26	26-Nov-26	05-Apr-26 A	21-Jan-27	3,501,375.59	3,200,034.00	4,088,791.20	85.63%	78.26%	-48
	PLAYGROUND AND LANDSCAPING WORKS	243	05-Apr-26	26-Nov-26	05-Apr-26 A	21-Jan-27	3,182,875.72	2,939,079.82	3,760,297.62	84.64%	78.16%	-48
	CUT AND FILL	28	05-Apr-26	06-May-26	05-Apr-26 A	06-May-26 A	453,900.00	453,900.00	453,900.00	100%	100%	0
	PLAYGROUND WORKS	171	19-Apr-26	17-Nov-26	19-Apr-26 A	09-Nov-26	728,545.73	687,924.15	781,940.40	93.17%	87.98%	7
	FOOTBALL PLAYGROUND WORKS	171	19-Apr-26	17-Nov-26	19-Apr-26 A	09-Nov-26	728,545.73	687,924.15	781,940.40	93.17%	87.98%	7
	GENERAL SITE WORKS	233	16-Apr-26	26-Nov-26	16-Apr-26 A	21-Jan-27	1,061,769.12	716,076.06	1,224,114.42	86.74%	58.5%	-48
	FENCE WORKS	153	16-Apr-26	16-Aug-26	16-Apr-26 A	17-Oct-26	65,818.80	48,705.91	65,818.80	100%	74%	-52
	MECHANICAL WORK	146	12-May-26	06-Aug-26	12-May-26 A	04-Nov-26	421,027.74	237,097.86	421,027.74	100%	56.31%	-75
	STORM WATER AND UTILITY WORK	144	12-May-26	04-Aug-26	12-May-26 A	02-Nov-26	27,252.00	9,133.20	27,252.00	100%	33.51%	-75
	IRRIGATION SYSTEM WORKS	126	02-Jun-26	30-Jul-26	02-Jun-26 A	28-Oct-26	393,457.80	227,964.66	393,457.80	100%	57.94%	-75
	FIRE PROTECTION SYSTEM	2	05-Aug-26	06-Aug-26	02-Nov-26	04-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	194	20-May-26	20-Oct-26	20-May-26 A	07-Jan-27	536,029.08	273,997.79	539,251.68	99.4%	50.81%	-67
	POWER, LIGHTING & GROUNDING	159	20-May-26	08-Sep-26	20-May-26 A	28-Nov-26	482,181.48	273,997.79	482,181.48	100%	56.82%	-67
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	09-Sep-26	08-Oct-26	28-Nov-26	27-Dec-26	43,146.00	0.00	43,146.00	100%	0%	0
	FIRE ALARM SYSTEM	32	13-Sep-26	20-Oct-26	01-Dec-26	07-Jan-27	10,701.60	0.00	13,924.20	76.86%	0%	0
	PARKING WORK	174	17-Jun-26	20-Oct-26	17-Jun-26 A	07-Jan-27	38,893.50	151,252.50	190,576.20	20.41%	79.37%	-67
	SERVICE CONNECTION	46	21-Oct-26	26-Nov-26	30-Jul-26 A	21-Jan-27	0.00	5,022.00	7,440.00	0%	67.5%	-118
	LANDSCAPING WORKS	164	31-May-26	09-Nov-26	30-May-26 A	08-Dec-26	890,370.47	1,069,353.85	1,252,052.40	71.11%	85.41%	-25
	HARDSCAPE WORK	164	31-May-26	09-Nov-26	30-May-26 A	08-Dec-26	806,778.77	971,073.85	1,046,213.40	77.11%	92.82%	-25
	SOFTSCAPE WORK	155	03-Jun-26	09-Nov-26	03-Jun-26 A	08-Dec-26	83,591.70	98,280.00	205,839.00	40.61%	47.75%	-25
	TANK WORKS	148	13-May-26	19-Sep-26	13-May-26 A	07-Nov-26	48,290.40	11,825.77	48,290.40	100%	24.49%	-41
	SEPTIC TANK	143	13-May-26	31-Aug-26	13-May-26 A	01-Nov-26	7,475.22	5,723.59	7,475.22	100%	76.57%	-52
	WATER STORAGE TANK	148	13-May-26	19-Sep-26	13-May-26 A	07-Nov-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-41
	TOILET BUILDING WORKS	165	12-May-26	12-Oct-26	12-May-26 A	16-Nov-26	318,499.87	260,954.18	328,493.58	96.96%	79.44%	-30
	CIVIL WORK	165	12-May-26	12-Oct-26	12-May-26 A	15-Nov-26	220,773.07	179,859.90	230,766.78	95.67%	77.94%	-29
	STRUCTURAL WORK	59	12-May-26	22-Jul-26	12-May-26 A	23-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
	ARCHITECTURAL WORK	99	23-Jul-26	12-Oct-26	31-Jul-26 A	15-Nov-26	182,793.07	141,879.90	192,786.78	94.82%	73.59%	-22
	GENERAL FINISHES	99	23-Jul-26	12-Oct-26	31-Jul-26 A	15-Nov-26	86,510.60	50,911.80	87,769.20	98.57%	58.01%	-22
	WET AREA FINISHES	61	12-Aug-26	11-Oct-26	07-Aug-26 A	18-Oct-26	72,388.67	79,515.30	81,123.78	89.23%	98.02%	-9
	ROOF FINISHES	47	19-Sep-26	05-Oct-26	20-Aug-26 A	15-Nov-26	23,893.80	11,452.80	23,893.80	100%	47.93%	-60
	MEP WORK	84	28-Jul-26	06-Oct-26	22-Jul-26 A	16-Nov-26	97,726.80	81,094.28	97,726.80	100%	82.98%	-40
	MECANICAL WORKS	84	28-Jul-26	06-Oct-26	22-Jul-26 A	16-Nov-26	79,479.48	65,286.52	79,479.48	100%	82.14%	-40
	FIRE FIGHTING SYSTEM	1	06-Oct-26	06-Oct-26	15-Nov-26	16-Nov-26	136.26	0.00	136.26	100%	0%	0
	SEWER AND DRAINAGE SYSTEM	53	03-Aug-26	23-Aug-26	22-Jul-26 A	13-Oct-26	11,290.02	7,580.44	11,290.02	100%	67.14%	-53
	HVAC SYSTEM	31	28-Jul-26	15-Aug-26	13-Aug-26 A	11-Oct-26	12,127.20	9,053.28	12,127.20	100%	74.65%	-33
	WATER SUPPLY SYSTEM	56	01-Aug-26	20-Aug-26	30-Jul-26 A	11-Oct-26	55,926.00	48,652.80	55,926.00	100%	86.99%	-44
	ELECTRICAL WORKS	40	05-Aug-26	08-Sep-26	12-Aug-26 A	15-Oct-26	18,247.32	15,807.76	18,247.32	100%	86.63%	-24
	PROJECT CLOSOUT	193	25-May-26	16-Dec-26	25-May-26 A	10-Jan-27	20,443.96	75,642.64	681,465.20	3%	11.1%	-22
	TABUK	297	17-Feb-26	16-Dec-26	17-Feb-26 A	10-Feb-27	8,011,119.71	6,289,773.95	11,357,801.00	70.53%	55.38%	-47
	MOBILIZATION	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	43	17-Feb-26	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	171	17-Feb-26	12-Aug-26	17-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
	SHOP DRAWINGS SUBMITTALS	163	17-Feb-26	04-Aug-26	17-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	STRUCTURAL DRAWINGS	135	17-Feb-26	18-Jul-26	17-Feb-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	13
	PROJECT FENCE	63	17-Feb-26	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	63	17-Feb-26	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	20	25-Jun-26	18-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	18
	TOILET BUILDING	41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	57	25-Feb-26	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	150	23-Feb-26	04-Aug-26	23-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	TOILET BUILDING	40	23-Feb-26	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-16
	LANDSCAPE DRAWINGS	40	23-Feb-26	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0

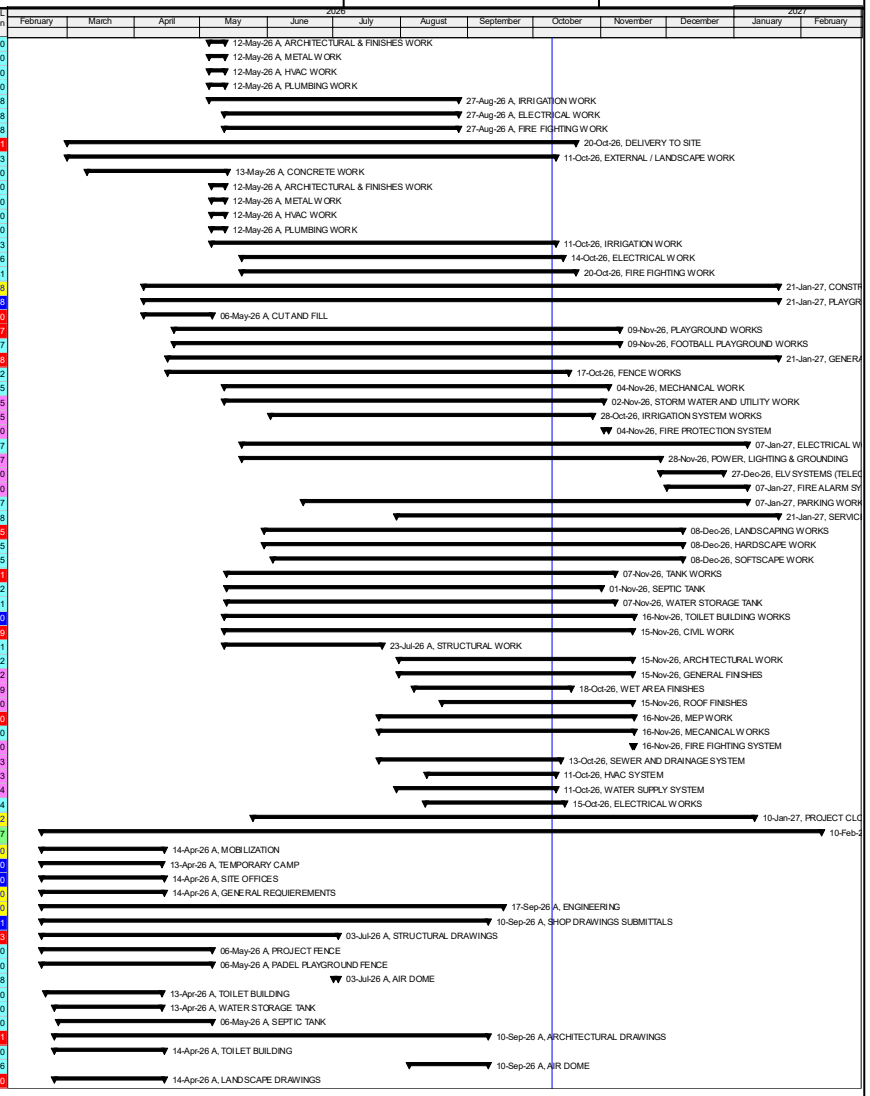


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	MECHANICAL DRAWINGS	140	28-Feb-2	12-Jul-26	28-Feb-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	-1
	WATER SUPPLY SYSTEM	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	25-Jun-26	12-Jul-26	02-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	98	10-May-2	29-Jul-26	10-May-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	15
	POWER AND LIGHTING SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	30	25-Jun-26	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	26
	SHOP DRAWINGS APPROVALS	169	19-Feb-2	12-Aug-26	19-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	STRUCTURAL DRAWINGS	138	19-Feb-2	23-Jul-26	19-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	12
	PROJECT FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	07-Jul-26	23-Jul-26	05-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
	TOILET BUILDING	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	153	28-Feb-2	12-Aug-26	28-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	TOILET BUILDING	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
	LANDSCAPE DRAWINGS	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	142	09-Mar-2	23-Jul-26	09-Mar-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	WATER SUPPLY SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	10	13-Jul-26	23-Jul-26	13-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	105	11-May-2	08-Aug-26	11-May-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	POWER AND LIGHTING SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	23	13-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	MATERIAL SUBMITTALS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	LONG LEAD ITEMS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	124	17-Feb-2	05-Jul-26	17-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	100	11-May-2	11-Jul-26	11-May-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	SHORT LEAD ITEMS	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	160	21-Feb-2	13-Jul-26	21-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-56
	LONG LEAD ITEMS	157	25-Feb-2	13-Jul-26	25-Feb-26 A	17-Sep-26 A	284,659.98	284,659.98	284,659.98	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-2	05-May-26	25-Feb-26 A	05-May-26 A	15,425.28	15,425.28	15,425.28	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	02-Mar-2	11-Jul-26	02-Mar-26 A	03-Sep-26 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
	CONCRETE WORK	38	11-Mar-2	28-Apr-26	11-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	45	11-Mar-2	06-May-26	11-Mar-26 A	06-May-26 A	6,802.65	6,802.65	6,802.65	100%	100%	0
	ELECTRICAL WORK	96	12-May-2	13-Jul-26	12-May-26 A	17-Sep-26 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	56,074.05	56,074.05	56,074.05	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	38,542.29	38,542.29	38,542.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-2	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-2	16-Mar-26	15-Mar-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	10	11-Mar-2	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-2	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,328.23	3,328.23	3,328.23	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	201	26-Feb-2	27-Aug-26	26-Feb-26 A	26-Oct-26	3,066,606.27	2,285,139.72	3,066,606.27	100%	74.52%	-48
	LONG LEAD ITEMS	194	07-Mar-2	27-Aug-26	07-Mar-26 A	26-Oct-26	2,561,939.82	1,784,927.49	2,561,939.82	100%	69.67%	-49
	PURCHASE ORDER	157	07-Mar-2	16-Jul-26	07-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48

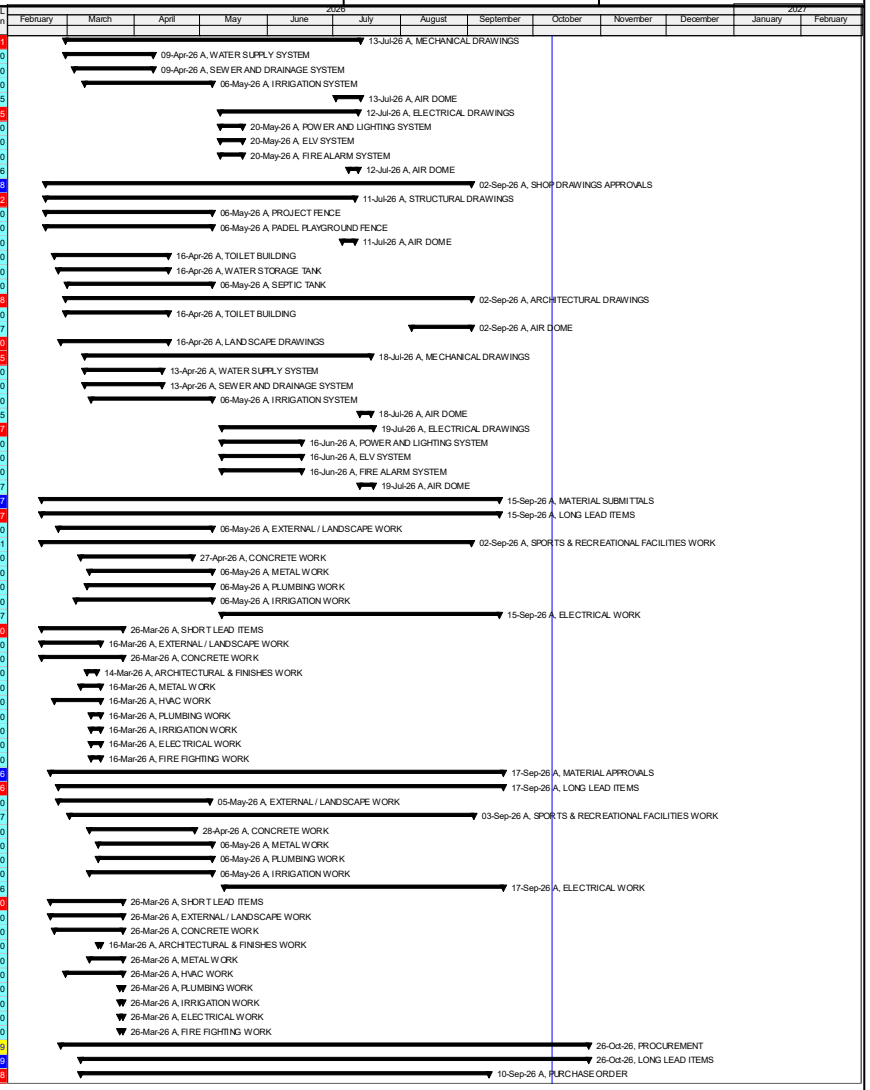


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	26-Mar-26	16-Jul-26	26-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	40	17-Mar-26	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	105	11-May-26	16-Jul-26	11-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
	MANUFACTURE / FABRICATION	140	29-Apr-26	16-Aug-26	29-Apr-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-55
	EXTERNAL / LANDSCAPE WORK	102	06-May-26	23-Jul-26	06-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
	SPORTS & RECREATIONAL FACILITIES WORK	124	06-May-26	16-Aug-26	06-May-26 A	21-Oct-26	0.00	0.00	0.00	0%	0%	-55
	CONCRETE WORK	64	29-Apr-26	30-Jun-26	29-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	0%	0%	-2
	METAL WORK	119	06-May-26	23-Jul-26	06-May-26 A	27-Sep-26 A	0.00	0.00	0.00	0%	0%	-55
	PLUMBING WORK	102	06-May-26	23-Jul-26	06-May-26 A	14-Sep-26 A	0.00	0.00	0.00	0%	0%	-45
	IRRIGATION WORK	99	06-May-26	01-Jul-26	06-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-70
	ELECTRICAL WORK	129	12-May-26	10-Aug-26	12-May-26 A	30-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
	DELIVERY TO SITE	146	06-May-26	27-Aug-26	06-May-26 A	26-Oct-26	2,561,939.82	1,784,927.49	2,561,939.82	100%	69.67%	-49
	EXTERNAL / LANDSCAPE WORK	114	06-May-26	06-Aug-26	06-May-26 A	11-Oct-26	138,827.52	137,434.65	138,827.52	100%	99%	-54
	SPORTS & RECREATIONAL FACILITIES WORK	129	06-May-26	27-Aug-26	06-May-26 A	26-Oct-26	2,148,961.86	1,383,982.01	2,148,961.86	100%	64.4%	-49
	CONCRETE WORK	63	06-May-26	06-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	1
	METAL WORK	131	06-May-26	06-Aug-26	06-May-26 A	14-Oct-26	8,003.07	6,574.62	8,003.07	100%	82.15%	-58
	PLUMBING WORK	108	06-May-26	06-Aug-26	06-May-26 A	11-Oct-26	31,985.55	31,360.72	31,985.55	100%	98.05%	-54
	IRRIGATION WORK	98	06-May-26	06-Jul-26	06-May-26 A	10-Oct-26	61,223.85	59,587.38	61,223.85	100%	97.33%	-81
	ELECTRICAL WORK	140	13-May-26	24-Aug-26	13-May-26 A	11-Oct-26	160,180.47	153,230.61	160,180.47	100%	95.66%	-40
	SHORT LEAD ITEMS	190	26-Feb-26	22-Jul-26	26-Feb-26 A	14-Oct-26	504,666.45	500,212.22	504,666.45	100%	99.12%	-71
	PURCHASE ORDER	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	EXTERNAL / LANDSCAPE WORK	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	97	11-May-26	02-Jul-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	94	11-May-26	29-Jun-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-51
	DELIVERY TO SITE	188	01-Mar-26	22-Jul-26	01-Mar-26 A	14-Oct-26	504,666.45	500,212.22	504,666.45	100%	99.12%	-71
	EXTERNAL / LANDSCAPE WORK	171	01-Mar-26	22-Jul-26	01-Mar-26 A	10-Oct-26	346,880.61	344,882.80	346,880.61	100%	99.42%	-67
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	135	06-May-26	08-Jul-26	06-May-26 A	14-Oct-26	4,310.01	3,620.41	4,310.01	100%	84%	-83
	HVAC WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	97	06-May-26	05-Jul-26	06-May-26 A	10-Oct-26	29,954.07	28,456.37	29,954.07	100%	95%	-82
	ELECTRICAL WORK	118	13-May-26	16-Jul-26	13-May-26 A	11-Oct-26	3,667.68	3,447.62	3,667.68	100%	94%	-72
	FIRE FIGHTING WORK	126	13-May-26	09-Jul-26	13-May-26 A	13-Oct-26	204.39	155.34	204.39	100%	76%	-81
	CONSTRUCTION STAGE	261	24-Mar-26	14-Dec-26	24-Mar-26 A	28-Jan-27	4,569,706.01	3,453,780.89	6,814,680.60	67.06%	50.68%	-38
	PLAYGROUND AND LANDSCAPING WORKS	255	24-Mar-26	14-Dec-26	24-Mar-26 A	21-Jan-27	1,821,855.51	1,944,937.50	2,311,795.02	78.81%	84.13%	-32
	CUT AND FILL	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	228,240.00	228,240.00	228,240.00	100%	100%	0
	PLAYGROUND WORKS	182	23-Apr-26	07-Dec-26	23-Apr-26 A	29-Nov-26	498,041.34	531,610.46	623,491.20	79.88%	85.26%	7
	FOOTBALL PLAYGROUND WORKS	159	23-Apr-26	17-Nov-26	23-Apr-26 A	31-Oct-26	279,162.60	296,090.33	333,290.16	83.76%	88.84%	15
	BASKETBALL PLAYGROUND WORKS	153	06-May-26	17-Nov-26	06-May-26 A	09-Nov-26	157,714.68	154,829.41	173,211.12	91.05%	89.39%	7
	PADEL PLAYGROUND WORKS	171	06-May-26	07-Dec-26	06-May-26 A	29-Nov-26	61,164.06	80,690.72	116,989.92	52.28%	68.97%	7
	GENERAL SITE WORKS	235	16-Apr-26	14-Dec-26	16-Apr-26 A	21-Jan-27	565,038.87	470,510.34	656,604.42	86.05%	71.66%	-32
	FENCE WORKS	154	16-Apr-26	17-Aug-26	16-Apr-26 A	18-Oct-26	32,909.40	24,352.96	32,909.40	100%	74%	-52
	MECHANICAL WORK	143	12-May-26	10-Aug-26	12-May-26 A	01-Nov-26	230,187.54	192,496.27	230,187.54	100%	83.63%	-69
	STORM WATER AND UTILITY WORK	138	12-May-26	04-Aug-26	12-May-26 A	26-Oct-26	27,252.00	15,732.00	27,252.00	100%	57.73%	-69
	IRRIGATION SYSTEM WORKS	96	02-Jun-26	30-Jul-26	02-Jun-26 A	21-Oct-26	202,617.60	176,764.27	202,617.60	100%	87.24%	-69
	FIRE PROTECTION SYSTEM	5	05-Aug-26	10-Aug-26	26-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	176	08-Jun-26	07-Nov-26	08-Jun-26 A	31-Dec-26	295,483.53	225,733.52	345,859.68	85.43%	65.27%	-46
	POWER, LIGHTING & GROUNDING	144	08-Jun-26	27-Sep-26	08-Jun-26 A	22-Nov-26	288,789.48	212,789.72	288,789.48	100%	73.68%	-47
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	28-Sep-26	26-Oct-26	22-Sep-26 A	12-Dec-26	4,958.40	12,943.80	43,146.00	11.49%	30%	-44
	FIRE ALARM SYSTEM	32	01-Oct-26	07-Nov-26	24-Nov-26	31-Dec-26	1,735.65	0.00	13,924.20	12.46%	0%	0
	PARKING WORK	168	17-Jun-26	11-Nov-26	17-Jun-26 A	31-Dec-26	5,788.80	23,798.40	40,207.80	14.4%	59.19%	-42
	SERVICE CONNECTION	192	10-Jun-26	14-Dec-26	10-Jun-26 A	21-Jan-27	669.60	4,129.20	7,440.00	9%	55.5%	-32
	LANDSCAPING WORKS	156	31-May-26	22-Nov-26	30-May-26 A	28-Nov-26	482,244.90	704,953.89	755,169.00	63.86%	93.35%	-4
	HARDSCAPE WORK	156	31-May-26	22-Nov-26	30-May-26 A	28-Nov-26	457,884.90	626,473.89	648,147.00	70.65%	96.66%	-4
	SOFTSCAPE WORK	143	10-Jun-26	22-Nov-26	10-Jun-26 A	28-Nov-26	24,360.00	78,480.00	107,022.00	22.76%	73.33%	-4
	TANK WORKS	153	13-May-26	27-Sep-26	13-May-26 A	12-Nov-26	48,290.40	9,622.80	48,290.40	100%	19.93%	-40
	SEPTIC TANK	148	13-May-26	03-Sep-26	13-May-26 A	07-Nov-26	7,475.22	3,520.62	7,475.22	100%	47.1%	-54
	WATER STORAGE TANK	153	13-May-26	27-Sep-26	13-May-26 A	12-Nov-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-40
	AIR DOME CONSTRUCTION	218	13-May-26	03-Dec-26	13-May-26 A	28-Jan-27	2,573,468.96	1,210,693.39	4,178,041.20	61.6%	28.98%	-47
	CIVIL WORK	150	13-May-26	14-Sep-26	13-May-26 A	10-Nov-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-47
	ARCHITECTURAL WORK	25	05-Nov-26	03-Dec-26	30-Dec-26	28-Jan-27	0.00	0.00	712,953.22	0%	0%	0
	MECHANICAL WORK	23	15-Sep-26	12-Oct-26	10-Nov-26	07-Dec-26	563,598.65	0.00	667,968.77	84.38%	0%	0

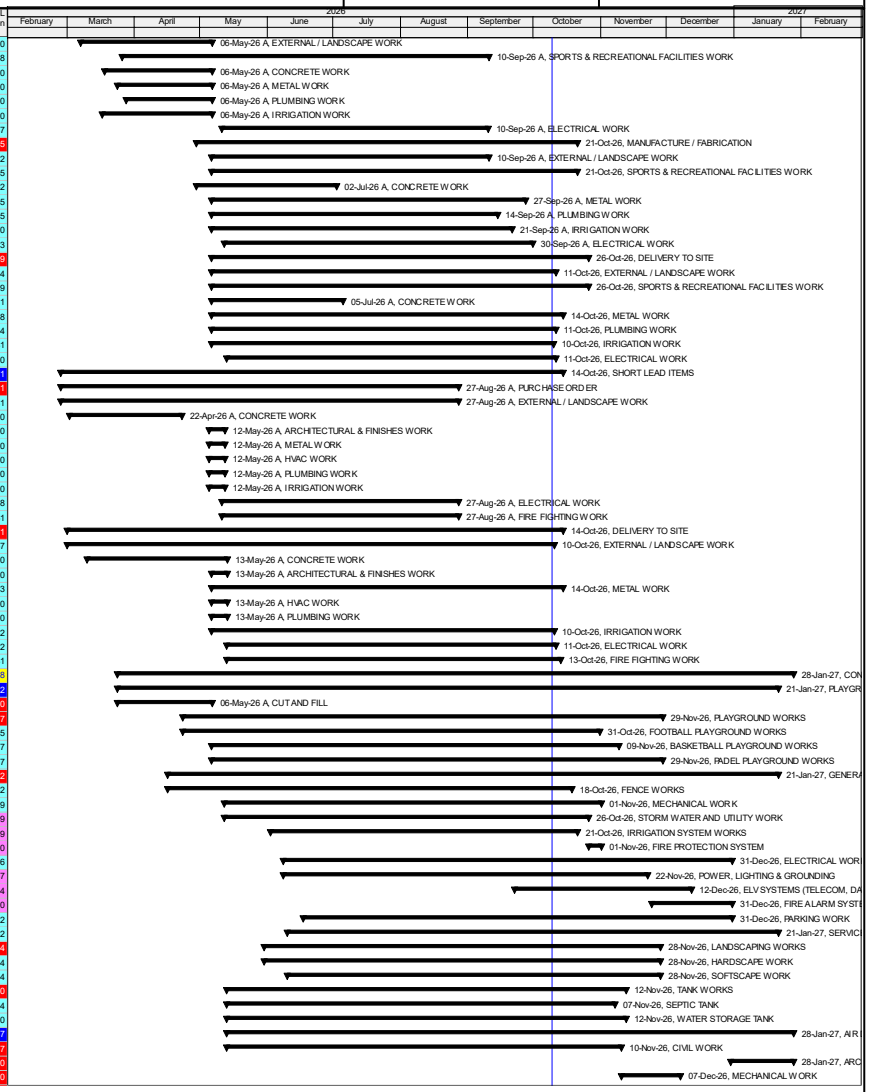


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 11-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELECTRICAL WORK	33	28-Sep-26	04-Nov-26	22-Nov-26	30-Dec-26	298,200.34	0.00	1,085,449.25	27.47%	0%	0
	TOILET BUILDING WORKS	143	12-May-26	28-Oct-26	12-May-26 A	18-Oct-26	174,381.54	298,150.00	324,844.38	53.68%	91.78%	10
	CIVIL WORK	143	12-May-26	26-Oct-26	12-May-26 A	17-Oct-26	84,475.80	220,184.04	227,117.58	37.19%	96.95%	9
	STRUCTURAL WORK	59	12-May-26	01-Aug-26	12-May-26 A	12-Aug-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
	ARCHITECTURAL WORK	76	02-Aug-26	26-Oct-26	01-Aug-26 A	17-Oct-26	46,495.80	182,204.04	189,137.58	24.58%	96.33%	8
	GENERAL FINISHES	76	02-Aug-26	21-Oct-26	01-Aug-26 A	07-Sep-26 A	11,016.60	84,120.00	84,120.00	13.1%	100%	37
	WET AREA FINISHES	37	26-Aug-26	13-Oct-26	06-Aug-26 A	13-Oct-26	34,291.20	78,979.14	81,123.78	42.27%	97.36%	-17
	ROOF FINISHES	46	07-Oct-26	26-Oct-26	14-Aug-26 A	17-Oct-26	1,188.00	19,104.90	23,893.80	4.97%	79.96%	-36
	MEP WORK	103	16-Jun-26	28-Oct-26	16-Jun-26 A	18-Oct-26	89,903.74	77,965.96	97,726.80	92%	79.78%	10
	MECANICAL WORKS	103	16-Jun-26	28-Oct-26	16-Jun-26 A	18-Oct-26	71,658.42	59,718.64	79,479.48	90.16%	75.14%	10
	FIRE FIGHTING SYSTEM	2	27-Oct-26	28-Oct-26	23-Sep-26 A	18-Oct-26	0.00	54.50	136.26	0%	40%	-19
	SEWER AND DRAINAGE SYSTEM	92	16-Jun-26	05-Sep-26	16-Jun-26 A	13-Oct-26	11,290.02	9,999.73	11,290.02	100%	88.57%	-31
	HVAC SYSTEM	42	09-Aug-26	12-Oct-26	13-Aug-26 A	14-Oct-26	4,442.40	8,284.80	12,127.20	36.63%	68.32%	3
	WATER SUPPLY SYSTEM	45	12-Aug-26	02-Sep-26	22-Jul-26 A	12-Oct-26	55,926.00	41,379.60	55,926.00	100%	73.99%	-50
	ELECTRICAL WORKS	38	15-Aug-26	17-Sep-26	22-Jul-26 A	16-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
	PROJECT CLOSOUT	219	25-May-26	16-Dec-26	25-May-26 A	10-Feb-27	34,073.40	210,119.32	1,135,780.10	3%	18.5%	-47

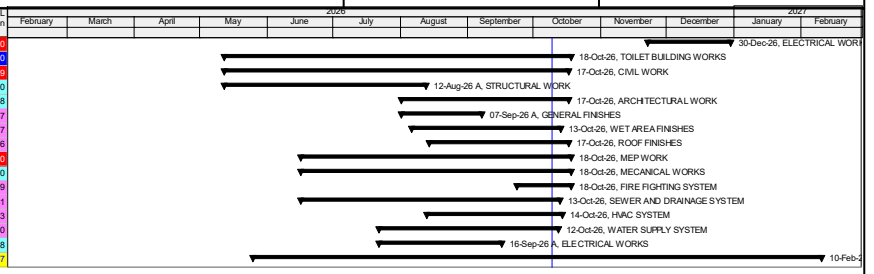

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
