Infrastructure Network Development, Sudair City for Industry and Business

تطوير شبكات البنية التحتية بالمنطقة الصناعية بسدير المرحلة الثالثة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Eng. Zyad Al Shabat	06-Jan-2026	05-Jul-2027

Scope: roads and paving, potable water, TSE, sewer, storm water, irrigation and landscaping, electrical (medium voltage, telecom, street lighting) and CCTV networks in Zones A and G, over 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 19-Oct-2026 the project is 45.4% complete against 40.7% planned, 4.8% ahead (SPI 1.12). This week it gained 0.64% against 1.56% planned, so the lead narrowed from 5.7% to 4.8%. Road works and the storm and sewer networks are ahead; procurement and engineering are behind.

PHYSICAL % COMPLETE

45.4% / 40.7% plan

▲ SPI 1.12 +4.8%

PROGRESS THIS WEEK

+0.64% / +1.56% plan

▼ 0.92% below the weekly plan

CONTRACT TIME ELAPSED

52.5% · day 286 of 545

● P6 finish 05-Jul-2027

INVOICED TO DATE (GROSS)

14.6% · 24.6M SAR

4 invoices, last period ends 30-Sep-2026

Ahead overall, but the lead is shrinking and procurement is behind.

This week's progress (0.64%) was well under the weekly plan (1.56%). Procurement is at 60.1% against 99.2% planned (SPI 0.61): MV cables (0 of 51,500 m), unit substations, street lighting poles and lighting panels are not yet delivered, and the final substation location is still pending between the Client and SEC. The P6 update finishes the project on the contract date, 05-Jul-2027, with zero float.

Site photos this week

Six photos from the "Weekly Progress Photos" sheet of the 19-Oct-2026 weekly report. Only the curbstone photo carries a camera stamp (17-Oct-2026). Road works dominate the week: base course grading, prime coat, asphalt base course and curbstone in Zones A and G. Select a photo to view it larger, then use the arrows to move between photos.



Asphalt base course, MC20 Zone A

First asphalt layer of the base course laid.



Base course grading, MC10 Zone A

Grading of the first base course layer on the arterial road.



Prime coat (MC1), MC20 Zone A

MC1 sprayed on the base course layer.



Curbstone concrete, MCZ0 Zone G

Concrete pouring for curbstone. Camera-stamped 17-Oct-2026, 10:38.



Asphalt compaction, MCE0 Zone G

Roller compacting the asphalt base course.




Asphalt paving, MCE0 Zone G

Paver laying the first asphalt layer of the base course.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly points dated the 6th of each month. Source: Physical-Chart Data sheet. There is no revised plan.

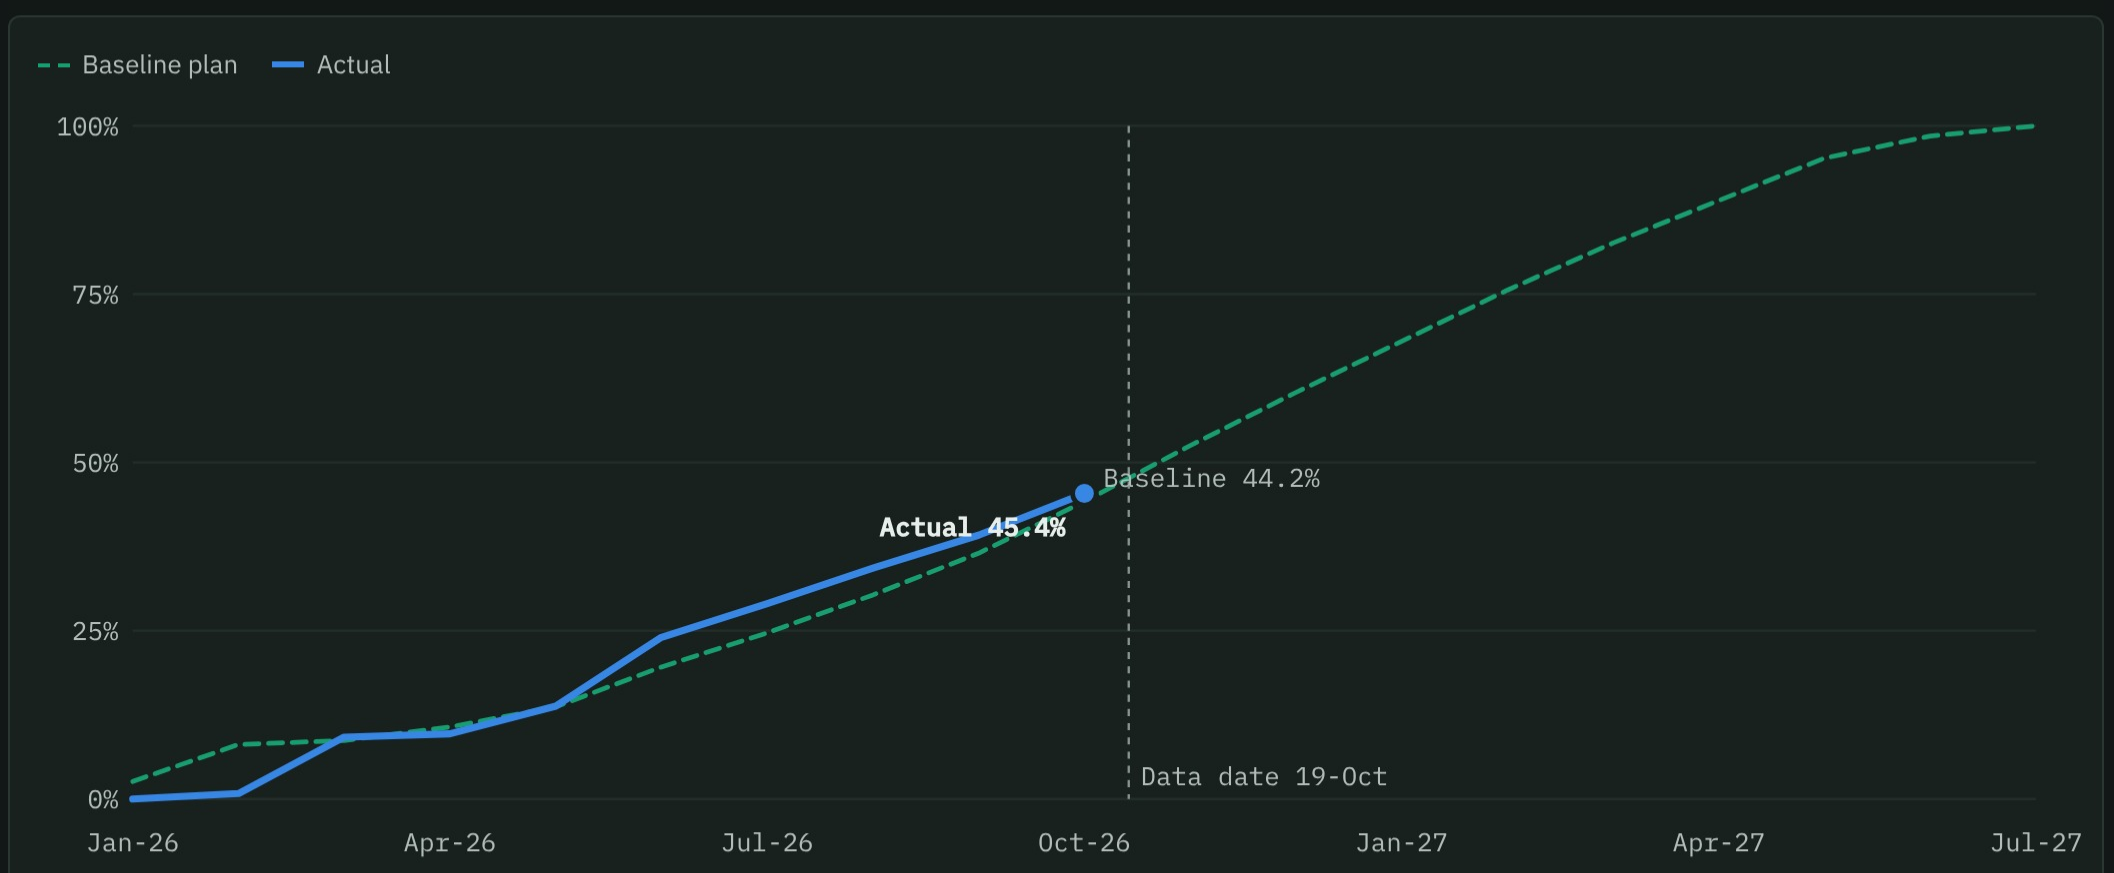

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	39.10	44.79	+5.69	–	1.15
19-Oct-2026	**40.66**	**45.43**	**+4.77**	**+0.64**	**1.12**

Only the 19-Oct-2026 report was used. The 12-Oct-2026 row is the previous-week value in that report (to date minus this week); earlier weeks are not shown. The chart's October point (44.2% planned) is dated 06-Oct, while the weekly report plans 40.7% to 19-Oct; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Network rows are part of Construction; their weights are shares of the whole project. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5%	100.0%	93.4%	−6.6%	0.93	▼ Behind
Procurement	13%	99.2%	60.1%	−39.1%	0.61	▼ Behind
Construction	75%	26.4%	39.9%	+13.6%	1.51	▲ Ahead
· Road works	16.4%	72.2%	80.6%	+8.3%	1.12	▲ Ahead
· Storm water drainage	16.5%	20.7%	44.0%	+23.3%	2.13	▲ Ahead
· Sewerage	5.5%	5.8%	72.6%	+66.8%	12.50	▲ Ahead
· TSE	7.7%	0.0%	6.1%	+6.1%	–	▲ Started early
· Potable water	12.3%	0.0%	14.2%	+14.2%	–	▲ Started early
· Electrical works	8.7%	43.8%	33.2%	−10.6%	0.76	▼ Behind
· Landscape & irrigation	6.8%	0.0%	4.7%	+4.7%	–	▲ Started early
· CCTV	1.2%	34.0%	12.2%	−21.8%	0.36	▼ Behind
Testing & commissioning	2%	0.0%	0.0%	0.0%	–	● Not yet due
Close-out	2%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**40.7%**	**45.4%**	**+4.8%**	**1.12**	▲ Ahead

The P6 update (data date 19-Oct-2026) has 2,115 activities: 787 completed, 300 in progress and 1,028 not started. Its scheduled finish is 05-Jul-2027, the contract completion date.

Scope of work: quantities

Quantity executed on site for the major items, from the Major Quantities sheet of the 19-Oct-2026 weekly report. The report gives no zone split and no previous-week figure, so the "This week" column shows "–". The scope table on the report's summary page shows 0 executed for every network and was not used.

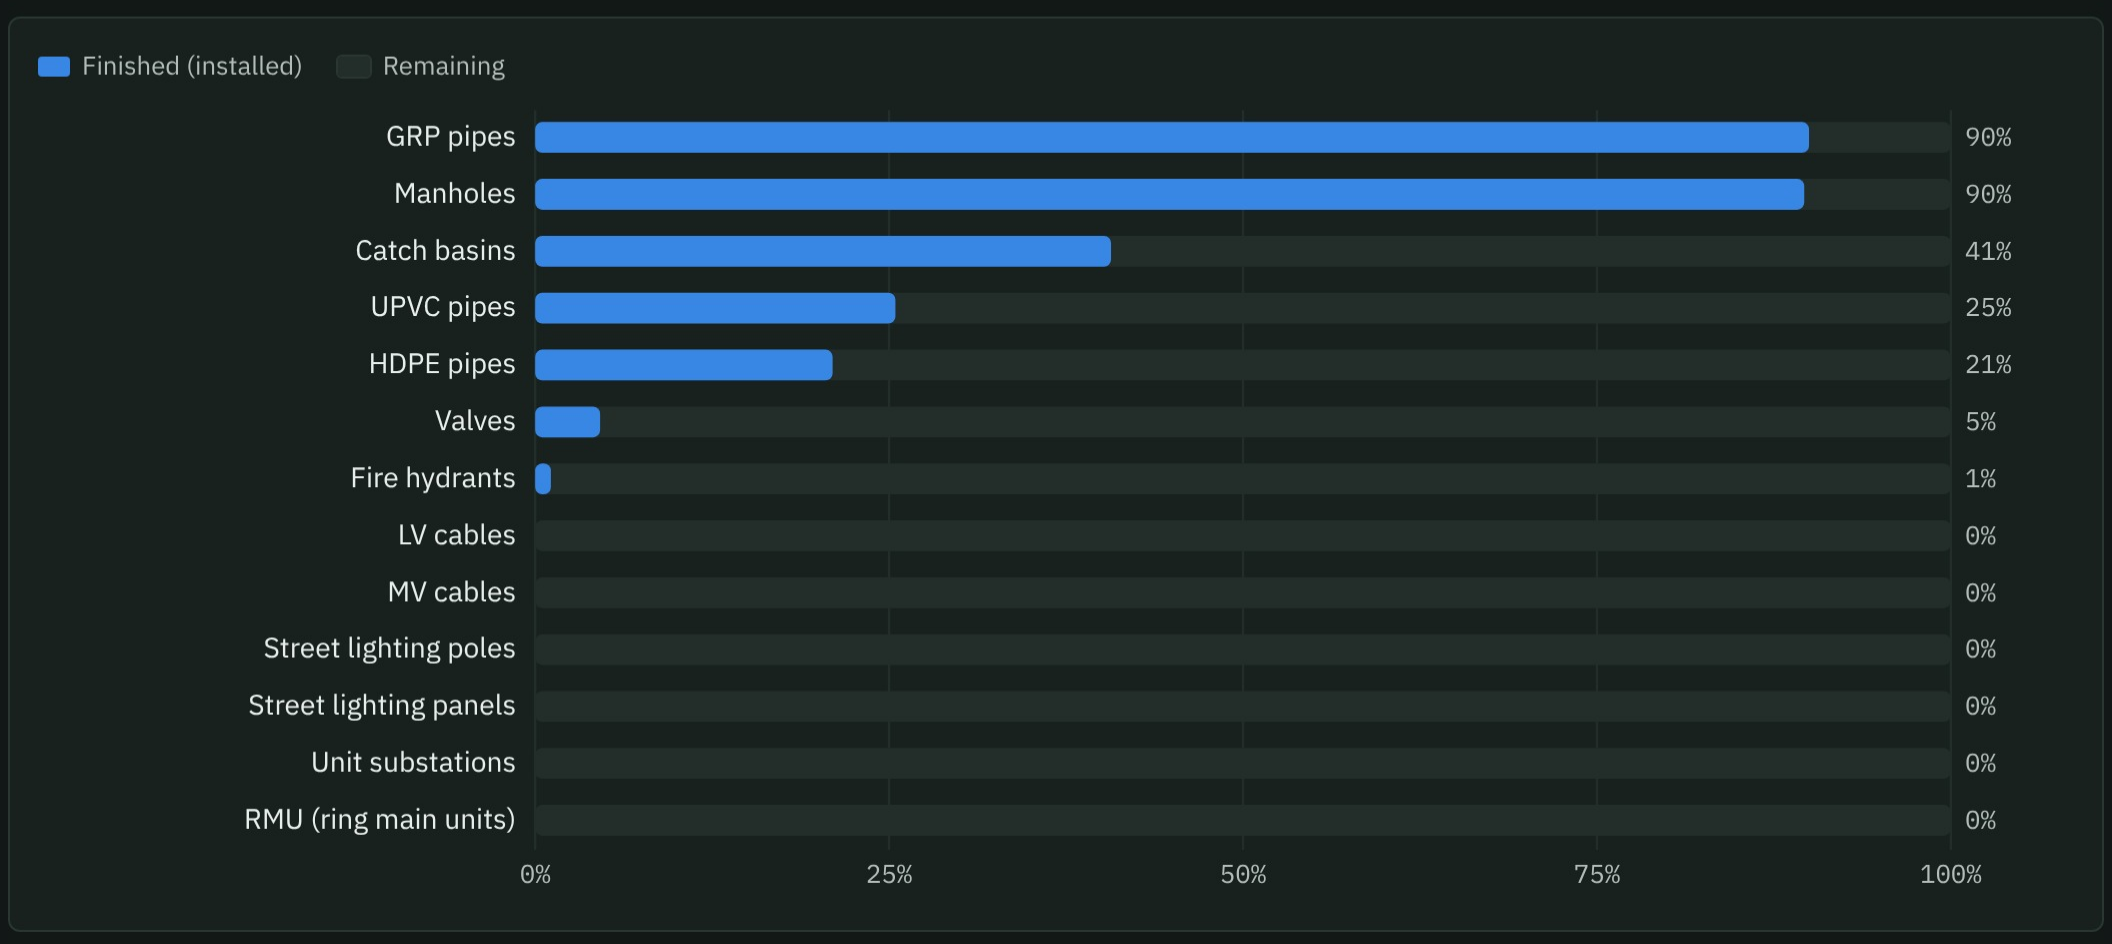

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
GRP pipes	All zones	m	18,337	16,500	–	1,837	90.0%	–
Manholes	All zones	EA	251	225	–	26	89.6%	–
Catch basins	All zones	EA	295	120	–	175	40.7%	–
UPVC pipes	All zones	m	4,716	1,200	–	3,516	25.4%	–
HDPE pipes	All zones	m	28,557	6,000	–	22,557	21.0%	–
Valves	All zones	EA	218	10	–	208	4.6%	–
Fire hydrants	All zones	EA	90	1	–	89	1.1%	–
LV cables	All zones	m	68,400	0	–	68,400	0.0%	–
MV cables	All zones	m	51,500	0	–	51,500	0.0%	–
Street lighting poles	All zones	EA	592	0	–	592	0.0%	–
Street lighting panels	All zones	EA	52	0	–	52	0.0%	–
Unit substations	All zones	EA	5	0	–	5	0.0%	–
RMU (ring main units)	All zones	EA	11	0	–	11	0.0%	–

Wet networks well advanced

GRP pipes are 90% installed (16,500 of 18,337 m) and manholes 90% (225 of 251). Catch basins are at 41%, UPVC pipes 25% and HDPE pipes 21%.

Not yet started or barely started

Fire hydrants (1 of 90) and valves (10 of 218) have barely started. No LV or MV cable, street lighting pole, lighting panel, unit substation or RMU is installed yet.

Milestones

The weekly report and the P6 schedule update give different dates for several milestones. Both are shown so the difference can be resolved with the contractor. Baselines for the last four contractual milestones are from the approved baseline schedule.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	06-Jan-2026	06-Jan-2026	06-Jan-2026 (actual)	–	✓ Done
Mobilisation finish	05-Feb-2026	05-Feb-2026	06-Apr-2026 (actual)	–	✓ Done
Baseline submission	05-Feb-2026	06-Apr-2026 (+60 d)	06-Apr-2026 (actual)	–	✓ Done
Quality lab	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
RBF	05-Feb-2026	16-Feb-2026 (+11 d)	–	–	✓ Done
Technical submittals (plans and materials)	05-Mar-2026	16-Aug-2026 (+164 d)	25-Jul-2026 (actual)	–	✓ Done late
Engineering phase finish	05-Mar-2026	28-Sep-2026 (+207 d)	19-Oct-2026	83	▼ Late
Procurement phase finish	23-Jan-2027	17-Jan-2027	22-Dec-2026	36	● On track
Medium voltage works complete	21-Jan-2027	–	18-Feb-2027	27	▼ At risk
All network works complete	04-May-2027	–	14-Apr-2027	65	● On track
Road works complete	14-Apr-2027	–	17-Apr-2027	18	● Float available
Finishing works complete	05-Jul-2027	–	27-Jun-2027	7.7	● On track
Project finish (all works)	05-Jul-2027	05-Jul-2027	05-Jul-2027	0	● On time

The weekly report and the P6 update disagree on four milestone dates.

Mobilisation finished on 05-Feb-2026 in the weekly report but on 06-Apr-2026 in P6. Technical submittals finished on 16-Aug-2026 in the weekly report but on 25-Jul-2026 in P6. The weekly report forecasts the engineering phase to finish on 28-Sep-2026, while P6 still has it open on 19-Oct-2026. Procurement finishes on 17-Jan-2027 in the weekly report and 22-Dec-2026 in P6. The MV works finish 28 days after their baseline, and project finish has no float left.

Procurement of key materials

Share of total quantity delivered to site. Source: Major Quantities sheet; asphalt, interlock and kerbstone from the completion rate in the Procurement sheet, weekly report 19-Oct-2026.

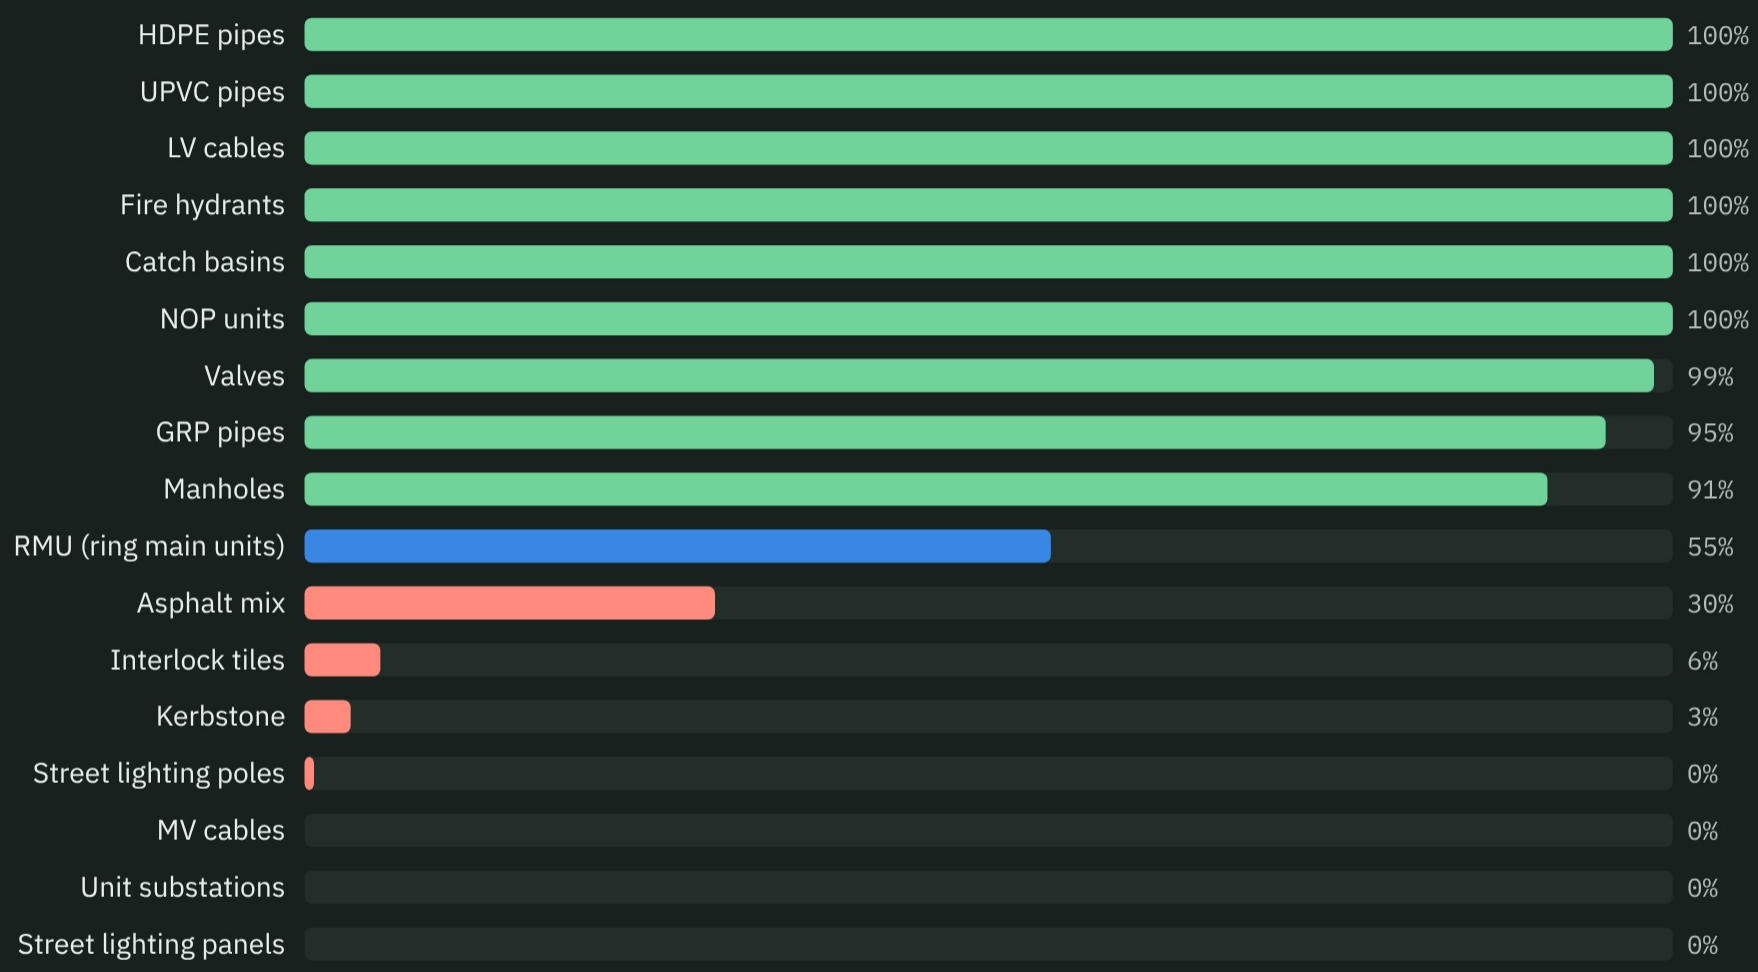

MV cables: nothing delivered


0 of 51,500 m. The Procurement sheet lists the material approval as not submitted, with the cables required on site by 31-May-2026. The risk register says the cables have been procured and that the final substation location is still pending between the Client and SEC.

Street lighting, substations and paving materials

Street lighting poles 1 of 592 delivered, lighting panels 0 of 52 and unit substations 0 of 5 (approval not submitted). Kerbstone is 3.4% delivered, interlock tiles 5.5% and asphalt mix 30%.

Manpower

Monthly head count on site (manual plus non-manual), planned vs actual. Source: Manpower sheet.

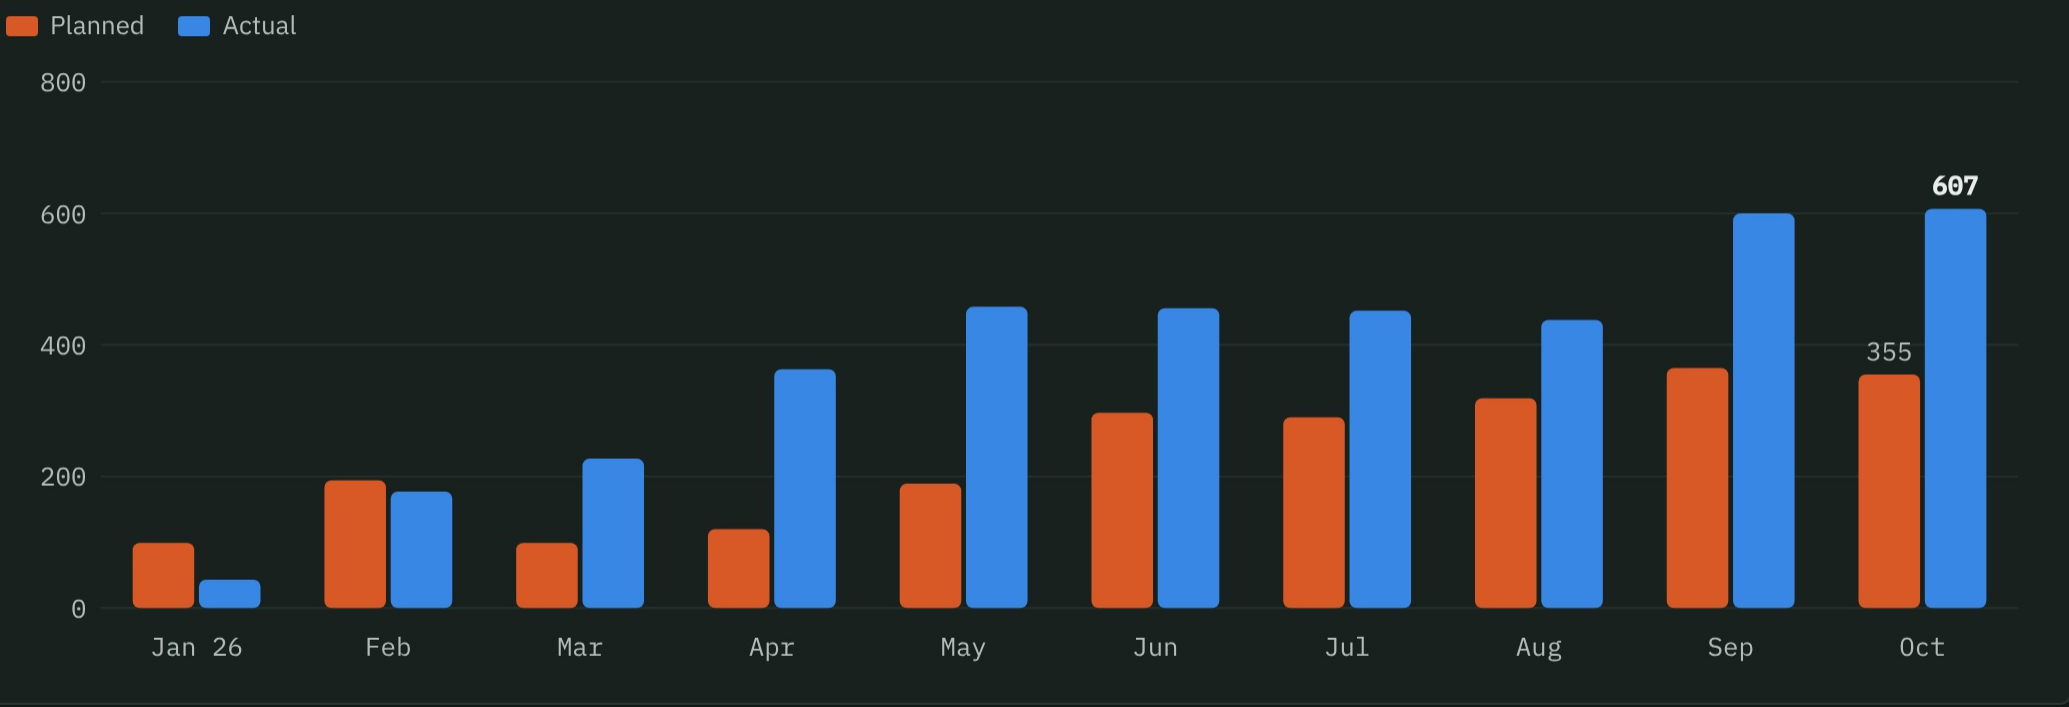

October head count is 607 (540 manual, 67 non-manual) against 355 planned (+71%). Actual head count has been above plan every month since February. The site also has 332 pieces of equipment against 200 planned.

Cost and invoicing

Contract value

Road works	88,002,863
Storm water drainage network	25,405,198
Electrical works	20,082,302
CCTV works	9,305,708
Potable water network	7,779,405
Sewer network	7,071,027
Landscape & irrigation	6,835,461
TSE network	4,147,557
BOQ total (excl. VAT)	**168,629,520**
Contract value incl. 15% VAT	193,923,948
Change orders	0

All values in SAR. The BOQ total plus 15% VAT matches the contract value. No change orders are registered.

Invoices

Invoices submitted	4
Gross value	24,575,402
Advance payment recovery (10%)	−2,457,540
Retention	0
Deductions and penalties	−34,000
VAT	3,317,679
Net incl. VAT	25,401,542
PM-approved / paid	0 / 0
Advance payment (10%)	16,862,952

Invoicing is 14.6% of the contract value against 45.4% physical progress. The invoice log shows none of the four invoices approved by the PM or paid yet; the first covers work up to 28-Jun-2026.

Health, safety and quality

Safety Score 81.8%

Safe man-hours (cumulative)	900,536
Man-hours this week	36,720
Man-hours this month	98,080
Internal trainings (cumulative)	55
Toolbox talks (cumulative)	41
Consultant safety inspection score	80.7%
Safety observations logged / closed	13 / 13

All man-hours are reported as safe. The report does not state incident counts clearly.

Quality Score 81.3%

NCRs issued / closed / open	21 / 16 / 5
Site instructions issued / open	7 / 2
MIRs issued / open	235 / 1
FIRs issued / open	3,781 / 61
Shop drawings submitted / processed	420 / 339
Shop drawings pending with consultant	21
Material submittals processed	60 of 64

Open issues and risks

ISSUE	OWNER	DETAIL
Substation location (MV)	Client / SEC	The final substation location is still pending confirmation between the Client and SEC. The MV cable size was settled by RFI (answered 09-Feb-2026) and the contractor is building MV road-crossing ducts at its own risk. Further delay may affect testing, energization and handover. Rated high (5 × 5).
Landscape proposal approval	Client	The landscape proposal (RFI-0036, 23-Aug-2026) awaits Client approval, which is needed to finalise the landscape shop drawings and procure the materials. Rated medium.
Procurement behind plan	Contractor	Procurement is at 60.1% against 99.2% planned. Approval of MV cables, unit substations, KWH meters, the fence for electrical works and road marking is not yet submitted.
Engineering not closed	Contractor	Engineering is at 93.4% against 100% planned, with 21 shop drawings pending with the consultant and 5 NCRs open.

All 13 safety observations in the issue log (08-Sep to 17-Oct-2026) and 16 of the 18 risks in the register are closed.

Data notes

- The uploaded files name the project "Phase Two – Part Two" (SUD1-02-011), while the repository folder and the project tracker call it Phase 3 (المرحلة الثالثة).
- The summary sheet labels cost-based progress as "Plan" and "Actual". This report uses physical progress (man-hour weighted) only: 40.66% planned and 45.43% actual.
- The Physical-Chart Data sheet plans 44.2% at its October point (06-Oct), more than the 40.66% planned to 19-Oct on the front sheet, and it shows the 19-Oct actual (45.43%) on the 06-Oct point.
- The front sheet leaves physical progress for electrical, landscape and CCTV works blank; the man-hours in the Progress sheet were used. Its BOQ values for CCTV Zone A and Zone G read 46,056 and 2 SAR instead of 6,513,996 and 2,791,854.
- Activity counts differ: the P6 update has 787 completed, 300 in progress and 1,028 not started; the schedule panel of the weekly report has 711, 352 and 1,052 (the front sheet shows 144 in progress).
- The weekly report puts the procurement phase baseline at 23-Jan-2027; the approved baseline schedule has 21-Nov-2026.
- The summary page's scope table shows 0 executed for every network, and its totals differ from the hidden Conclusion sheet (for example roads 15,234 m vs 18,252 m). Manholes are labelled "m" in the Major Quantities sheet but are counted in units.

- Procurement figures disagree: street lighting poles are 590 units and 10% complete in the Procurement sheet but 592 units with 1 delivered in Major Quantities; LV cables are 29,700 m vs 68,400 m. MV cables are "not submitted" in procurement, while the risk register says they have been procured.
- October planned head count is 355 in the monthly table (327 manual, 28 non-manual) but 335 in the head-count panel (300 manual, 35 non-manual).
- Several cells show #REF ! errors (EAC, risk scores, safety score in the status score). The substation risk carries a value of 6,835,460.61 SAR, which is the landscape BOQ value.
- Only the 19-Oct-2026 report was used. Weekly gains for earlier weeks and this-week quantities are not stated in it, so they show "–". The report week is the contract week the report states (41 of 78); whole weeks since handover give 40.

Compiled 28-Oct-2026 from the weekly report for the week ending 19-Oct-2026, with the P6 update and baseline schedule uploaded with it.
