Infrastructure Development for Industrial City 1 in Jeddah

تطوير البنية التحتية بالمدينة الصناعية الأولى بجدة (1كم2)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Company for Trading and Contracting	EGIS	Eng. Abdallah Aljulayfi	19-Nov-2025	18-Nov-2027

Scope: road works, storm, sewer, potable water and TSE networks, electrical works, fence and gates, a bridge and landscaping. Contract value 86.8M SAR, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 72.6% against a plan of 47.0%, the project is 25.6% ahead (SPI 1.55). This week it gained 0.27% against 0.78% planned, so the lead narrowed slightly. Yet the schedule forecasts completion 184 days after the contract date.

PHYSICAL % COMPLETE

72.6% / 47.0% plan

▲ SPI 1.55 +25.6%

PROGRESS THIS WEEK

+0.27 % / +0.78% plan

▼ 0.51% below the weekly plan

CONTRACT TIME ELAPSED

46.0% · day 335 of 729

▼ Forecast finish 20-May-2028

INVOICED TO DATE (GROSS)

51.7% · 44.9M SAR

7 invoices in the log, last period ends 29-Sep-2026

Well ahead on progress, but the forecast finish is six months late.

Both the weekly report and the P6 update forecast completion on 20-May-2028, 184 days after the contract completion date of 18-Nov-2027, with −157 days of total float. Every open milestone is forecast 7 days later than the latest plan date in the Milestones sheet. Roads and medium voltage, the WBS that is behind plan (73.5% against 100%), depends on the MV network, which is waiting for the MODON–SEC agreement; MV cable, ring main units and lighting substations have not been ordered.

Site photos this week

Six photos from the Weekly Photos sheet of the 20-Oct-2026 weekly report, camera-stamped 17 to 19 Oct 2026. Telecom ducts, curbs, interlock paving and street lighting are in progress. Select a photo to view it larger, then use the arrows to move between photos.



Telecom pipes, local road L01

Duct pipes laid in the trench. Stamped 19-Oct-2026, 11:08.



Curbstone works

Curb machine and crew along the road edge. Stamped 19-Oct-2026, 08:59.



Telecom pipe backfilling, L01

Warning tape laid before backfill. Stamped 19-Oct-2026, 06:55.



Interlock works

Paving blocks laid on the walkway. Stamped 19-Oct-2026, 08:53.



Street-light fuse box, local road 1

GPS-stamped 19-Oct-2026, 06:12, 21° 23′ 56″ N, 39° 14′ 9″ E.




Installation of light poles

Crane truck setting a pole. GPS-stamped 17-Oct-2026, 09:05, 21° 24′ 3″ N, 39° 14′ 11″ E.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet. The revised plan in the sheet is identical to the baseline, so only the baseline is drawn.

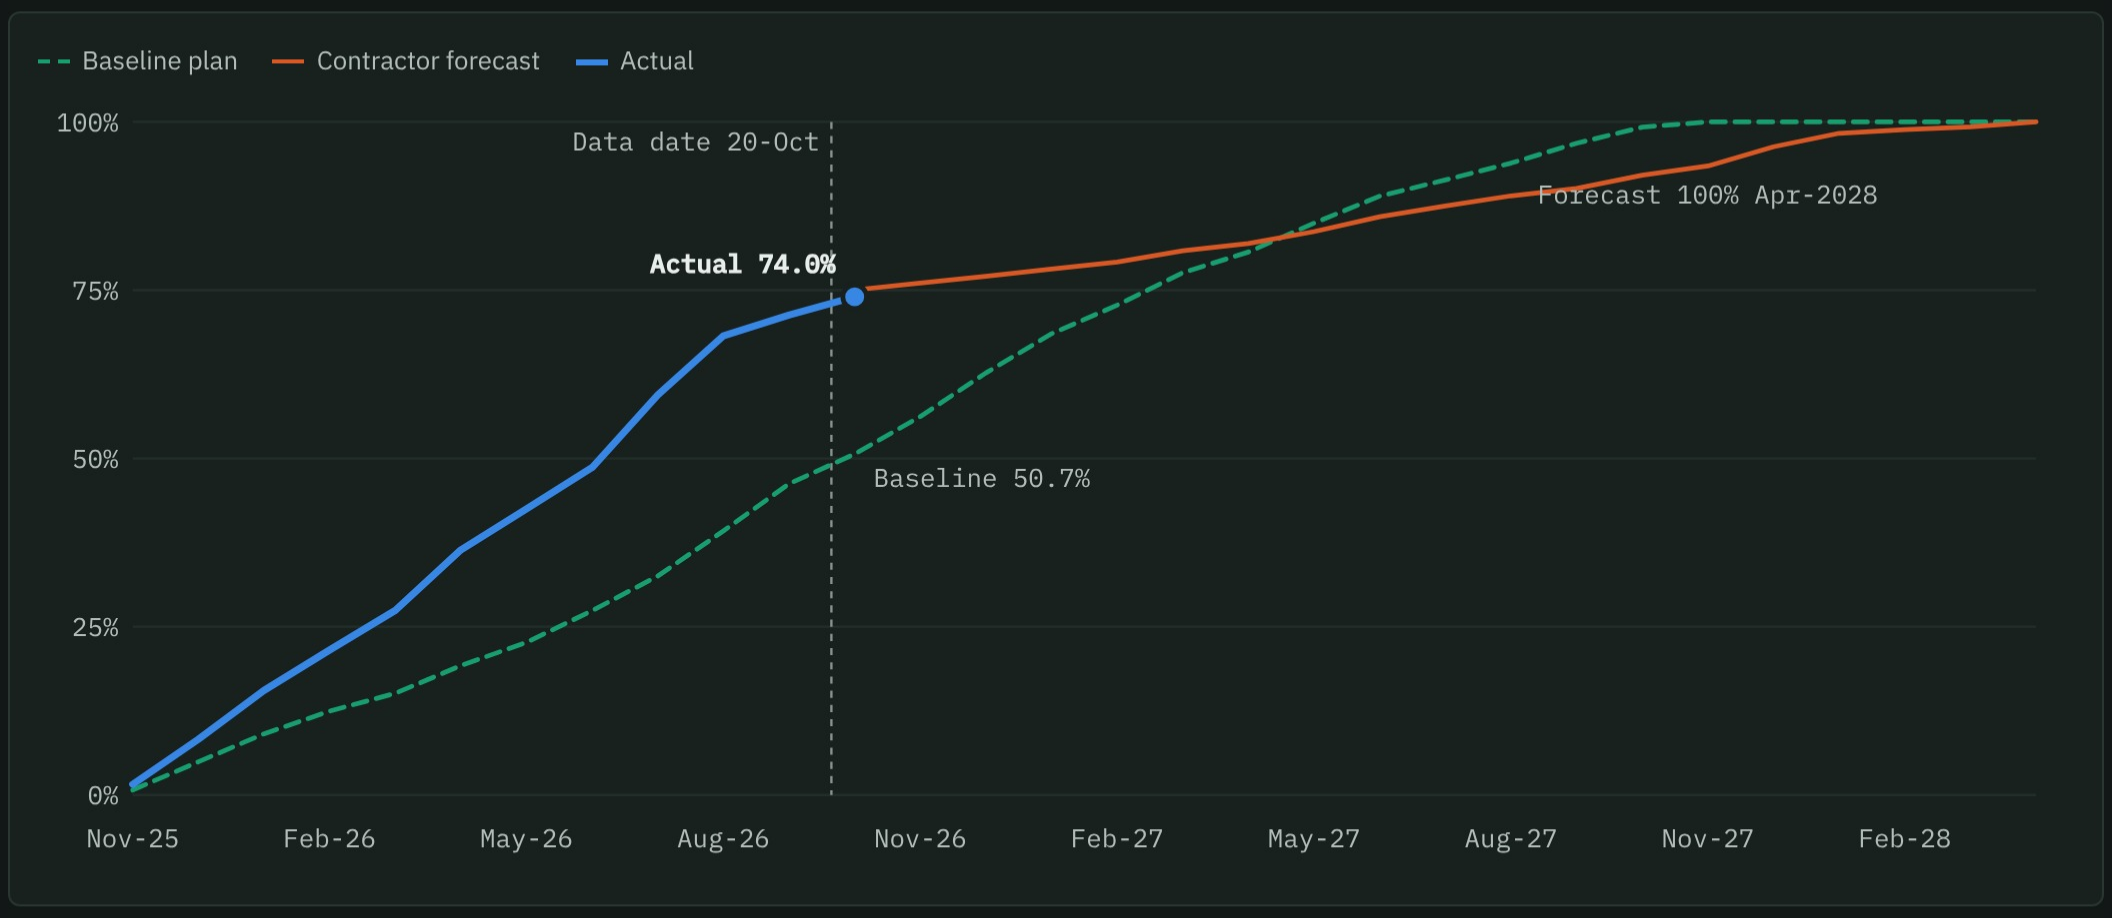

WEEK	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
Previous week	46.20	72.35	+26.14	—	1.57
20-Oct-2026	**46.99**	**72.61**	**+25.63**	**+0.27**	**1.55**

Only this week and the previous week are available, both from the 20-Oct-2026 report (Progress sheet, "last week" columns). The gain for the previous week is not stated in it. The chart's October actual (74.0%) comes from the P6 export and is higher than the 72.6% on the report dashboard; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Construction sub-phases are listed under Construction.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	2.8%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.7%	100.0%	98.8%	−1.2%	0.99	▼ Slightly behind
Procurement	11.5%	43.5%	78.9%	+35.4%	1.81	▲ Ahead
Construction	76.3%	45.2%	71.5%	+26.4%	1.58	▲ Ahead
· Site demolition	1.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Roads & medium voltage	14.0%	100.0%	73.5%	−26.5%	0.73	▼ Behind
· Deep infrastructure network	7.6%	100.0%	95.9%	−4.1%	0.96	▼ Slightly behind
· Shallow infrastructure network	27.8%	21.8%	77.9%	+56.2%	3.58	▲ Ahead
· Bridge	2.0%	55.1%	87.1%	+32.0%	1.58	▲ Ahead
· Outside boundary area (tie-in lines)	2.8%	49.8%	99.7%	+49.9%	2.00	▲ Ahead
· Roads finishing	9.2%	0.0%	68.4%	+68.4%	–	▲ Ahead
· Fence and gate	6.1%	55.0%	58.2%	+3.2%	1.06	▲ On track
· Roundabout & landscape	5.8%	0.0%	0.0%	0.0%	–	● Not yet due
Testing & commissioning	2.8%	0.0%	53.1%	+53.1%	–	▲ Ahead
Project close-out	1.9%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**47.0%**	**72.6%**	**+25.6%**	**1.55**	▲ Ahead

The P6 update (data date 20-Oct-2026) has 1,905 activities: 1,278 completed, 204 in progress and 423 not started. Of the 204 active activities, 91 are ahead and 113 behind. Critical-path activities fell from 460 to 457, and failed starts rose from 107 to 113.

Scope of work: quantities

Total, finished and remaining quantity for the major BOQ items, from the Major Quantities sheet of the 20-Oct-2026 weekly report. The report gives no zone split, no backfilled quantity and no previous-week quantity, so "This week" shows —.

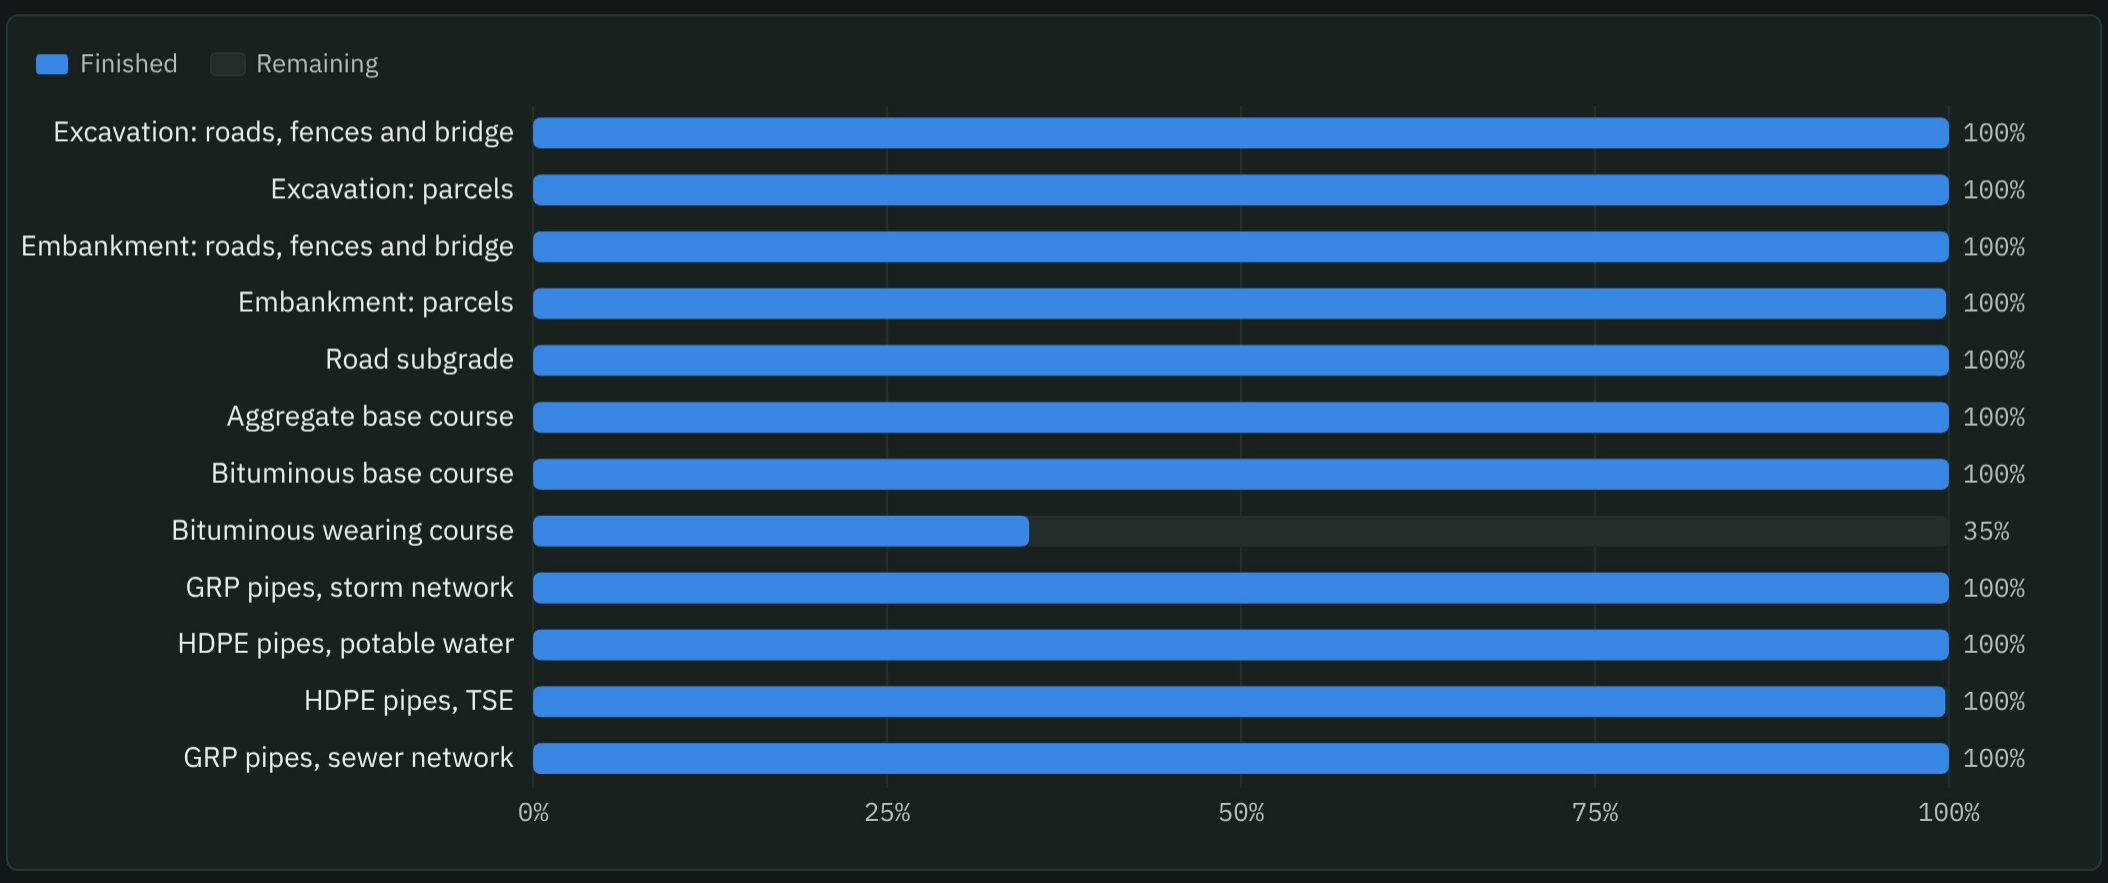

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation: roads, fences and bridge	All	m³	116,177	116,177	–	0	100.0%	–
Excavation: parcels	All	m³	123,555	123,555	–	0	100.0%	–
Embankment: roads, fences and bridge	All	m³	80,920	80,920	–	0	100.0%	–
Embankment: parcels	All	m³	94,645	94,456	–	189.3	99.8%	–
Road subgrade	All	m³	34,694	34,694	–	0	100.0%	–
Aggregate base course	All	m³	23,129	23,129	–	0	100.0%	–
Bituminous base course	All	m³	8,290	8,290	–	0	100.0%	–
Bituminous wearing course	All	m³	5,920	2,074	–	3,846	35.0%	–
GRP pipes, storm network	All	LM	5,650	5,650	–	0	100.0%	–
HDPE pipes, potable water	All	LM	12,075	12,075	–	0.3	100.0%	–
HDPE pipes, TSE	All	LM	8,722	8,700	–	22	99.7%	–
GRP pipes, sewer network	All	LM	6,244	6,244	–	0	100.0%	–

Asphalt wearing course is the main open road item

2,074 of 5,920 m³ is laid (35.0%). All other earthworks, base course and pipe items are complete or within 0.3% of their totals.

Milestones

Baseline dates and forecasts from the Milestones sheet of the weekly report, and forecasts and total float from the P6 export in the same workbook.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	19-Nov-2025	19-Nov-2025	19-Nov-2025 (actual)	–	✓ Done
Baseline time schedule	18-Dec-2025	18-Dec-2025	18-Dec-2025 (actual)	–	✓ Done
Finish mobilization	18-Dec-2025	04-Mar-2026	04-Mar-2026 (actual)	–	✓ Done late
Shop drawings, method statements and materials approved	19-Jan-2026	07-Nov-2026	07-Nov-2026	−55	▼ Late
All purchase orders issued	19-Jan-2026	01-Nov-2026	01-Nov-2026	−49	▼ Late
Roads & medium voltage complete	17-Sep-2026	18-Jan-2027	19-Jun-2027	−106	▼ Late
Deep infrastructure network complete	18-Nov-2026	19-Jun-2027	18-Jan-2027	43	? Conflicts with P6
Shallow infrastructure network complete	18-Mar-2027	03-Oct-2027	03-Oct-2027	−42	▼ Late
Completion of all works	18-Nov-2027	20-May-2028	20-May-2028	−157	▼ Late

The two sources swap the dates of two milestones.

The weekly report forecasts roads and medium voltage on 18-Jan-2027 and the deep network on 19-Jun-2027; the P6 export gives the same two dates the other way round. All other forecasts agree. Every open forecast is 7 days later than the latest plan date in the same sheet (Days Change −7).

Procurement of key materials

Share of the revised BOQ quantity delivered to site. Source: Material Monitoring sheet, weekly report 20-Oct-2026.

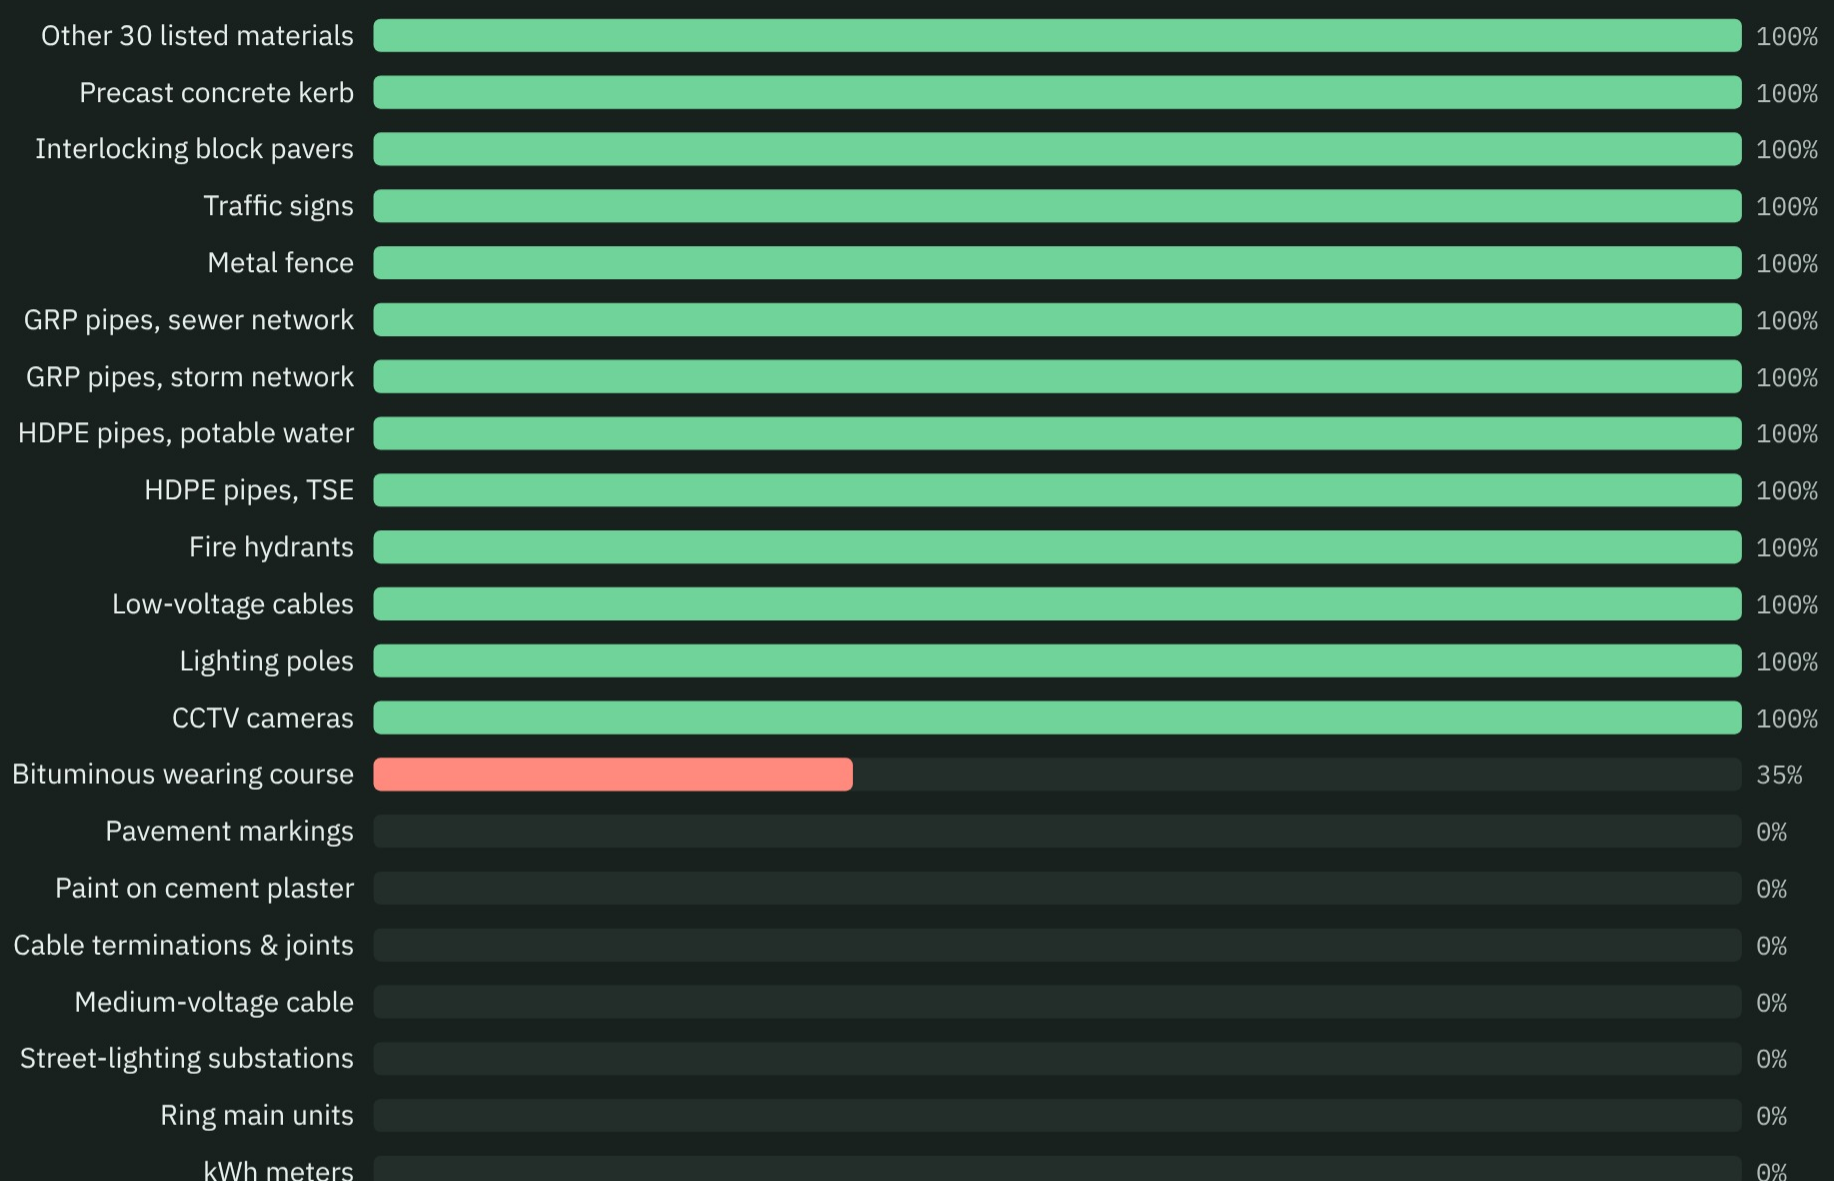

Medium-voltage materials: nothing ordered


MV cable (14,500 m), ring main units (4), street-lighting substations (4), kWh meters (4) and cable terminations (64) are not delivered. The Procurement Log shows the MV cable and substation orders on hold until the MODON–SEC electricity agreement is completed, with delivery now expected 30-Nov-2026.

Road finishing items

Asphalt wearing course 2,074 of 5,920 m³ delivered (35%). Pavement markings (3,780 m²) and paint on cement plaster (4,062 m²) not yet delivered. Overall, 108 of 113 purchase orders are issued and 105 of 113 materials are on site.

Manpower

Monthly manual (direct) head count on site, planned vs actual. Source: Manpower sheet.

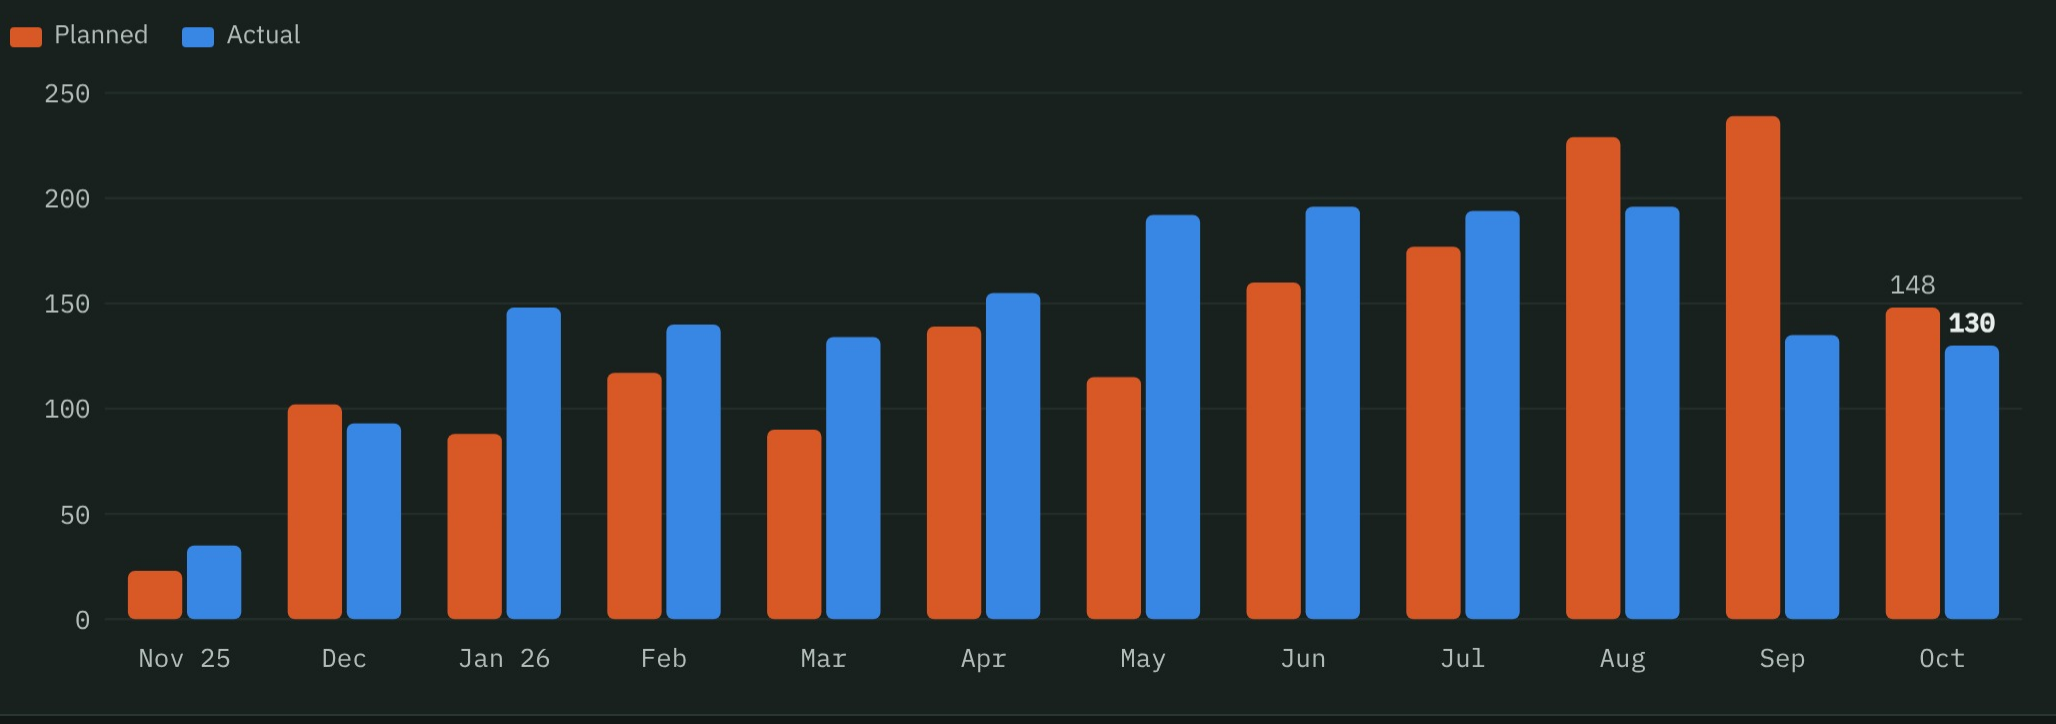

October manual head count is 130 against 148 planned (–12%). Non-manual staff are 48 against 22 planned. Equipment on site is 48 against 60 planned. The plan rises to 187 manual workers in November.

Cost and invoicing

Contract value

Original contract value	86,782,345
Revised contract value	86,782,345
Estimate at completion	86,782,345
Change orders	0

All values in SAR. No change orders are registered (CCO sheet).

Invoices

Invoices in the log	7
Gross value	44,851,849
Approved by PM (7, incl. VAT)	51,579,627
Paid (6, incl. VAT)	48,055,958
Retention / deductions	0 / 0
Advance payment	0

Gross invoicing is 51.7% of the contract value against 72.6% physical progress. Invoice 7 (period to 29-Sep-2026, 3,523,669 incl. VAT) is approved by the PM and was sent to accounts on 06-Oct-2026; it is not yet paid.

Health, safety and quality

Safety Score 0.77

Safe man-hours (cumulative)	465,010
Man-hours this week	9,216
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks (cumulative)	63 / 88

MODON HSE inspection 20-Oct-2026: 8 topics good, 13 need improvement and 2 failed (HSE communications and meetings, project leadership site tours).

Quality Score 0.85

Field inspection requests issued / closed	5,477 / 5,427
FIRs with the consultant	45
Material inspections issued / closed	100 / 100
NCRs issued / closed	16 / 16
Site instructions issued / closed	21 / 21
Shop drawings pending	65

Consultant quality score 0.85 this week; average 0.83 across all audits.

Open issues and risks

ISSUE	OWNER	DETAIL
MODON–SEC agreement for medium voltage	Owner	Open since 15-Dec-2025, target closure 30-Dec-2025. MODON is following up with SEC for the electricity source; the contractor is waiting for a reply to letter 2818 of 13-Jan-2026.
MV materials on hold	Owner / Contractor	Orders for MV cable, ring main units and street-lighting substations wait for the agreement. The ring main unit order is marked "PO in delay"; it was required on site by 20-Oct-2026.
Completion forecast	Contractor	The schedule forecasts completion on 20-May-2028 with –157 days of float, 184 days after the contract date, although physical progress is 25.6% ahead of plan.

The other two issues in the log are closed: tie-in permits from SEC, STC and NWC (closed 10-Feb-2026) and supplier prequalification for post-tensioning, bearings and expansion joints.

Data notes

Built only from the 20-Oct-2026 weekly upload (W3); earlier weeks were not used.

- Week number: the report states week 47.86 (whole weeks since site handover: 47); the file reference is WPR-048.
- Physical progress differs between sheets: the dashboard shows 72.6% (518,858 of 714,561 man-hours), while the P6 export, the Physical-Chart Data sheet and Progress Certificate #01 show 74.0–74.1% (528,823 man-hours).
- The weekly summary file (works executed this week) and the Look Ahead and Conclusion sheets label cost-based progress as "actual"; this report uses physical % complete (man-hours) only. The weekly summary file also gives project code JDH3-03-011, contract value 86,742,345 and an expected finish of 30-Nov-2026; the Look Ahead sheet also shows 30-Nov-2026. The dashboard and P6 forecast 20-May-2028.
- MODON PM: Eng. Abdallah Aljulayfi in the General Information sheet; م. رضا المنشاوي in the Look Ahead sheet and the weekly summary file.
- Milestones: the dashboard panel's "Original (Baseline)" column shows latest-plan dates (e.g. project finish 13-May-2028), and the Milestones sheet gives finish mobilization a baseline of 11-Nov-2025, before project start; the P6 baseline (18-Dec-2025) is used here. P6 and the weekly report swap the roads/MV and deep-network dates.
- Invoices: the summary says 6 submitted invoices, but the log lists 7 and the 44,851,849 total includes the seventh. Approved and paid amounts include 15% VAT, while the submitted total is gross; the Conclusion sheet labels the same contract value (86,782,345) as both including and excluding VAT.
- HDPE pipes: the Major Quantities sheet does not name the network; potable water and TSE are inferred from quantities. Installed quantities differ from the Material Monitoring sheet (potable 12,075 vs 12,045 m; TSE 8,700 vs 8,772 m), and TSE delivery (8,722 m) exceeds its revised BOQ (8,502 m).
- Equipment cumulative actual stays at 564 from July although monthly counts continue. Several dashboard cells show #REF! errors (milestone panel, safety and quality scores in the Codes sheet).
- Procurement sheet: some purchase-order dates fall after delivery (e.g. fiberglass manholes PO 29-Dec-2026, UPVC pipes PO 18-Dec-2026), which look like year typos.

Compiled 28-Oct-2026 from the weekly report uploaded for the week ending 20-Oct-2026 (W3).
