Additional Development and Network Completion, Tabuk Industrial City

تطوير اضافي و استكمال شبكات في تبوك

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ASAS for Developing & Operating Industrial Cities	EGIS	Eng. Yazeed Alragabah	04-Sep-2025	03-Sep-2027

Scope: roads, the Pond A storm-water outfall, storm, sewerage, potable water and fire-fighting, TSE irrigation, road lighting, telecom and CCTV networks in three zones of Tabuk Industrial City. Contract value 140.5M SAR excl. VAT.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 50.7% against 35.2% planned under the revised plan, 15.5% ahead (SPI 1.44), after gaining 0.8% this week against 0.6% planned.

PHYSICAL % COMPLETE
50.7% / 35.2% plan
▲ SPI 1.44 +15.5%

PROGRESS THIS WEEK
+0.8% / +0.6% plan
▲ 0.2% above the weekly plan

CONTRACT TIME ELAPSED
56.2% · day 410 of 729
▼ Forecast finish 07-Oct-2027

INVOICED TO DATE (GROSS)
32.9% · 46.2M SAR
14 invoices, last period ends 15-Oct-2026

Well ahead of the revised plan, but the forecast finish is 34 days after the contract date.

The weekly report and the P6 update (data date 19-Oct-2026) both forecast project handover on 07-Oct-2027, 34 days after the contract completion date of 03-Sep-2027. The P6 project finish has –29.3 days of float, and 220 open activities have negative float, mostly in electrical (82), CCTV (61) and telecom (43) works. Against the original baseline, which called for 64.2% by the end of October, the project is behind.

Site photos this week

The two site photos in the 19-Oct-2026 weekly report that are large enough to show; they carry no date or GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.



Aggregate base course

ABC laid on the road formation, with the next lane prepared alongside. Weekly report 19-Oct-2026.



Manhole testing

Fibreglass manhole under test, with forced ventilation from a generator-driven blower.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet, weekly report 19-Oct-2026.



WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	34.6	49.9	+15.3	–	1.44
19-Oct-2026	**35.2**	**50.7**	**+15.5**	**+0.8**	**1.44**

The latest report gives only this week and the previous week (Progress sheet, "this week" and "last week" columns), so earlier weeks are not shown. Its weekly table uses 354,339 budgeted man-hours; the S-curve sheet and the P6 progress certificate use 373,967 and show 48.0% actual at the same date.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.5%	100.0%	100.0%	0.0	1.00	✓ Complete
Construction works	98.0%	35.5%	51.3%	+15.8	1.45	▲ Ahead
Zone 1	21.1%	39.6%	58.2%	+18.6	1.47	▲ Ahead
Zone 2	25.3%	46.6%	71.4%	+24.8	1.53	▲ Ahead
Zone 3	51.6%	28.3%	38.5%	+10.2	1.36	▲ Ahead
Close-out	1.6%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**35.2%**	**50.7%**	**+15.5**	**1.44**	▲ Ahead

Engineering and procurement carry no man-hours in this measure, so they are not shown. The P6 update has 1,492 activities: 587 completed, 203 in progress and 702 not started.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 19-Oct-2026 weekly report. The sheet gives project totals only, with no split by zone, no previous-week figures and no backfill figures, so "This week" shows —.

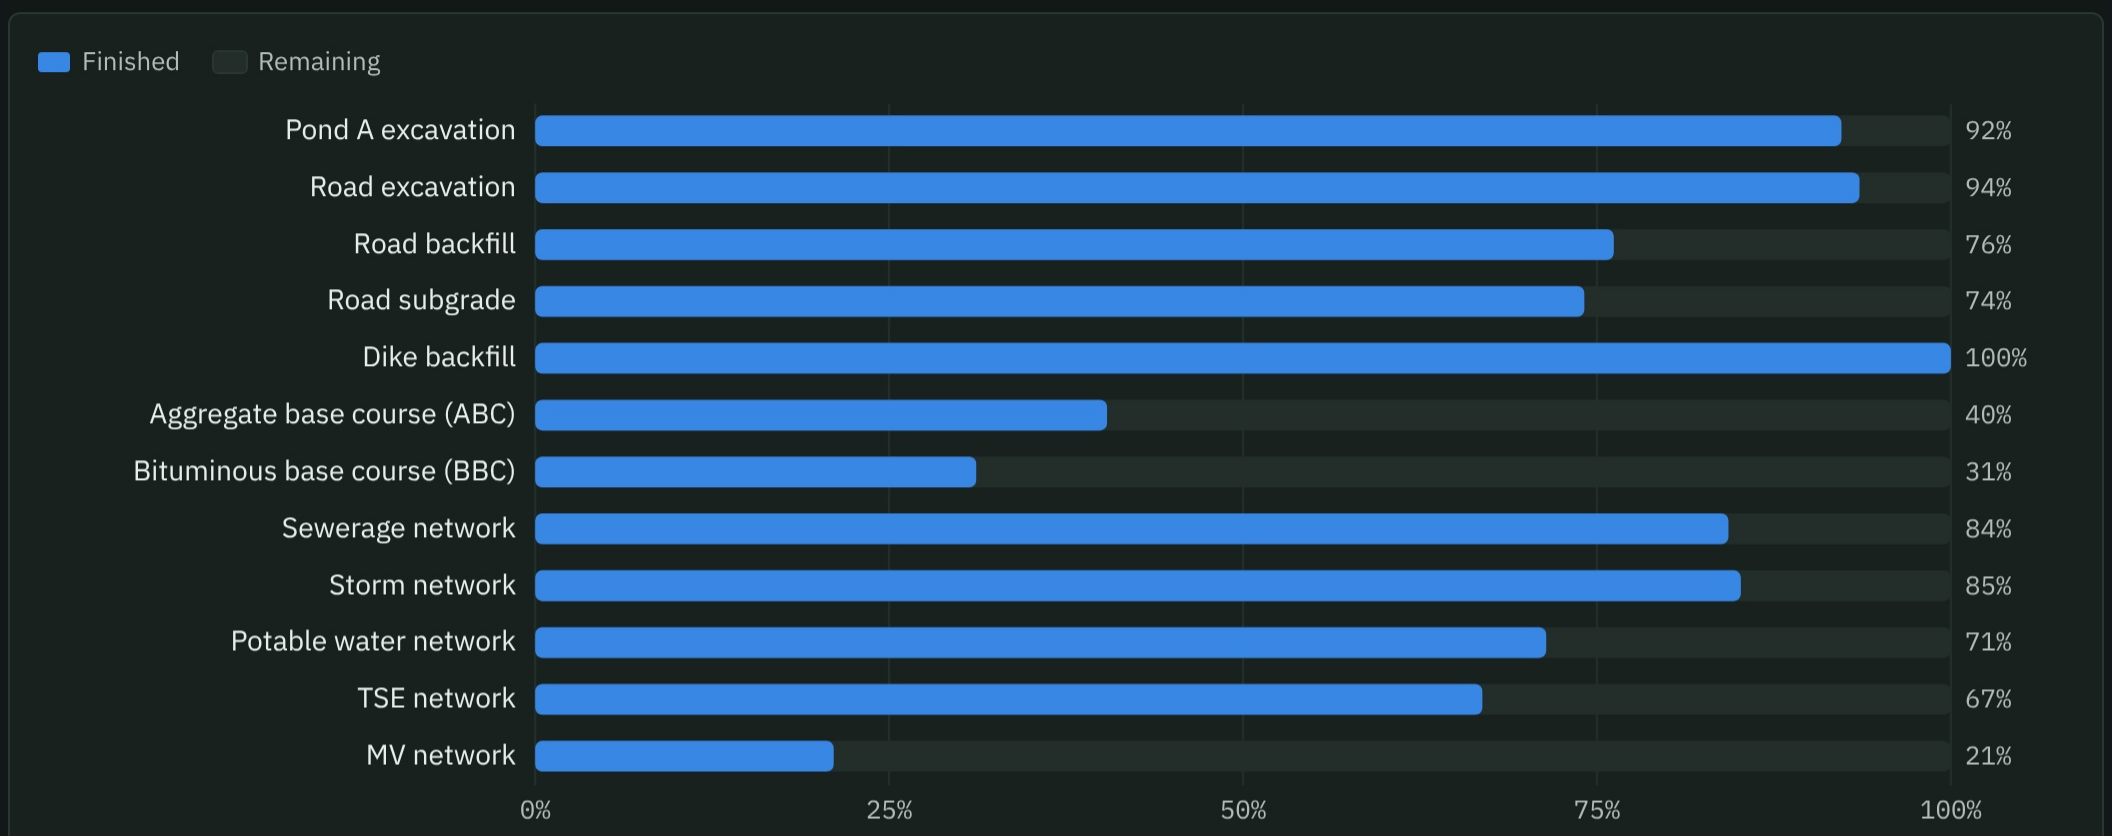

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Pond A excavation	All zones	m³	321,070	296,255	–	24,815	92.3%	–
Road excavation	All zones	m³	99,925	93,475	–	6,450	93.5%	–
Road backfill	All zones	m³	107,100	81,600	–	25,500	76.2%	–
Road subgrade	All zones	m³	72,730	53,900	–	18,830	74.1%	–
Dike backfill	All zones	m³	3,865	3,865	–	0	100.0%	–
Aggregate base course (ABC)	All zones	m³	48,485	19,586	–	28,899	40.4%	–
Bituminous base course (BBC)	All zones	m³	27,310	8,508	–	18,802	31.2%	–
Sewerage network	All zones	LM	8,370	7,055	–	1,315	84.3%	–
Storm network	All zones	LM	15,638	13,318	–	2,320	85.2%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Potable water network	All zones	LM	13,221	9,442	–	3,779	71.4%	–
TSE network	All zones	LM	12,223	8,178	–	4,045	66.9%	–
MV network	All zones	LM	23,700	4,998	–	18,702	21.1%	–

Wet networks well advanced

Sewerage is 84% laid, storm 85%, potable water 71% and TSE 67%. Pond A excavation is 92% done and the dike backfill is complete.

Road layers and MV behind

Aggregate base course is at 40% and bituminous base course at 31%. The MV network is at 21%; its connection to the substation is still an open issue.

Milestones

Baseline and forecast from the Milestones sheet of the weekly report; P6 forecast and total float from the P6 update (data date 19-Oct-2026). For the network finishes the baseline is the P6 baseline from the progress tracker, and the weekly report gives no forecast.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	04-Sep-2025	04-Sep-2025	04-Sep-2025 (actual)	–	✓ Done
Complete preliminary submittals	06-Dec-2025	17-Nov-2026 (+346 d)	–	–	▼ Late
Complete Zone 1	09-Feb-2027	04-Oct-2027 (+237 d)	30-Jun-2027	+56.9	? Conflicts with P6
Complete Zone 2	02-Aug-2027	30-Aug-2027 (+28 d)	24-Jul-2027	+11.8	? Conflicts with P6
Complete Zone 3	02-Aug-2027	29-Sep-2027 (+58 d)	05-Jun-2027	+78.0	? Conflicts with P6
Sewerage network	14-Aug-2027	–	27-Mar-2027	+138.7	● Float available
Potable water network	21-Aug-2027	–	10-Jun-2027	+73.0	● Float available
TSE network	21-Jul-2027	–	16-Jun-2027	+68.6	● Float available
Storm network	14-Aug-2027	–	12-Aug-2027	+20.0	● Float available
Telecom network	16-Aug-2027	–	08-Sep-2027	−4.3	▼ At risk
CCTV network	03-Sep-2027	–	18-Sep-2027	−12.6	▼ Late
Road works	02-Sep-2027	–	04-Oct-2027	−26.1	▼ Late
Electrical works	03-Sep-2027	–	04-Oct-2027	−26.8	▼ Late
Complete delivery of all materials	03-Aug-2027	04-Oct-2027 (+62 d)	–	–	▼ Late
All works complete, ready for initial handover	10-Aug-2027	19-Sep-2027 (+40 d)	–	–	▼ Late
Project handover	03-Sep-2027	07-Oct-2027 (+34 d)	07-Oct-2027	−29.3	▼ Late

The weekly report and P6 disagree on the zone completion dates.

The weekly report forecasts Zones 1, 2 and 3 to finish between 30-Aug-2027 and 04-Oct-2027, while the P6 update finishes them between 05-Jun-2027 and 24-Jul-2027 with positive float. Both agree on project handover, 07-Oct-2027. The late items in P6 are road works, electrical, CCTV and telecom.

Procurement of key materials

Completion rate of delivery per material. Source: Procurement sheet, weekly report 19-Oct-2026.

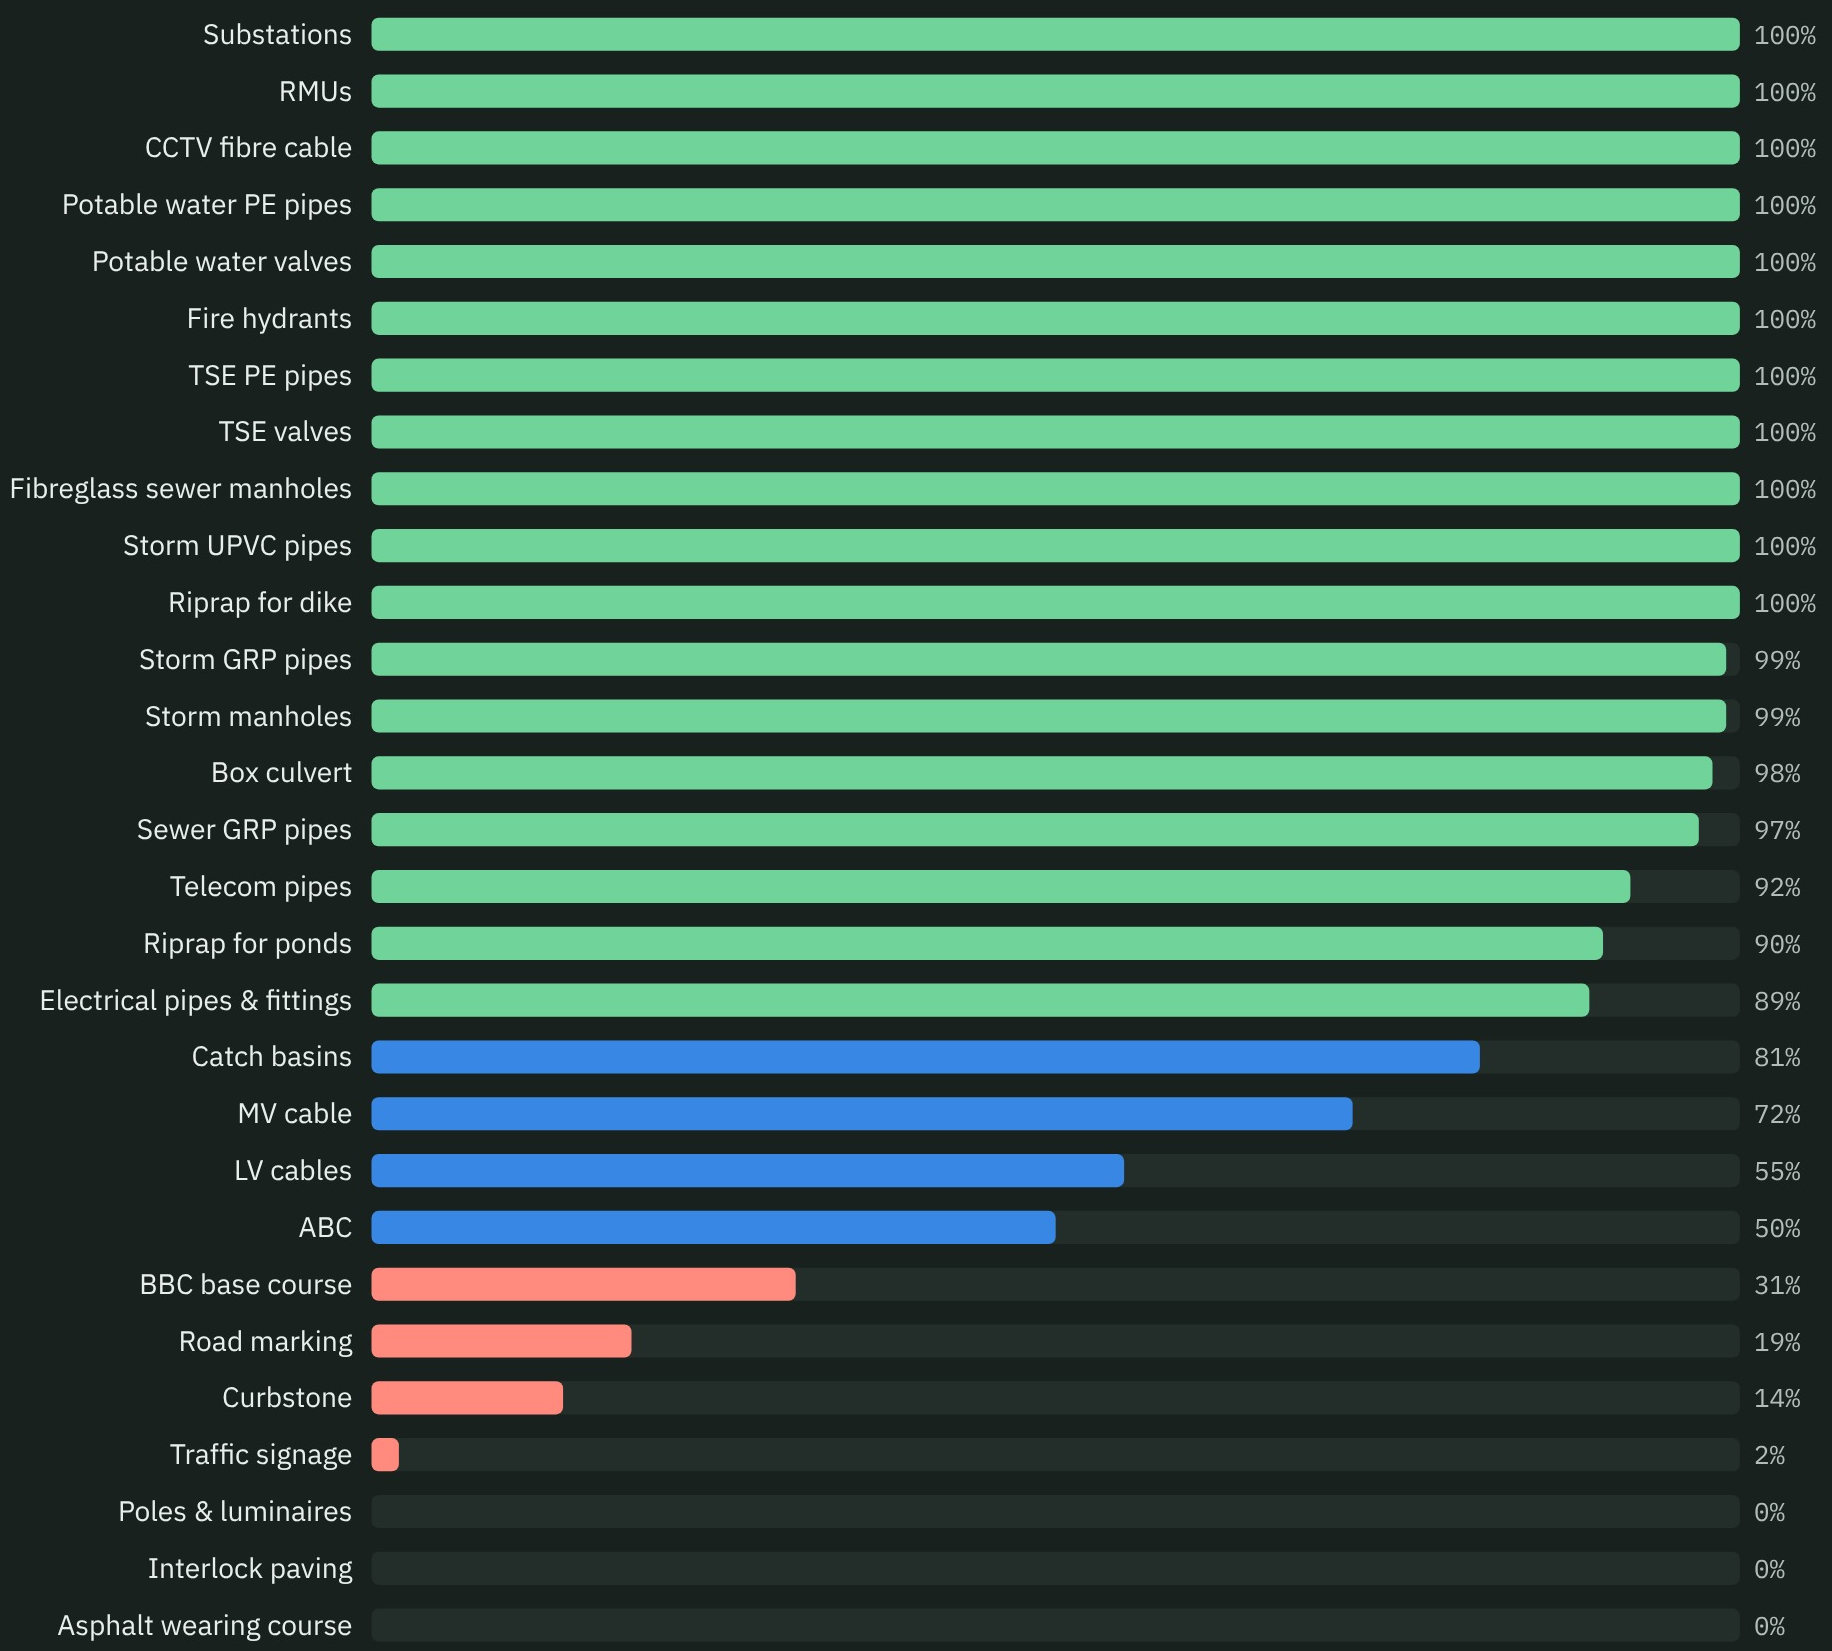

Nothing delivered yet for street lighting poles, interlock and asphalt wearing course


Purchase orders are issued for 957 poles and luminaires (08-Sep-2026), 62,075 m² of interlock (05-Jul-2026), pole foundations and CCTV cameras, but no delivery is recorded. Curbstone is at 14% and traffic signage at 2%.

Electrical cables part-delivered

MV cable is at 72% of 115,400 m and LV cables at 55%. Substations and RMUs are fully delivered. Pipes, valves, hydrants and manholes for the wet networks are complete or nearly so.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

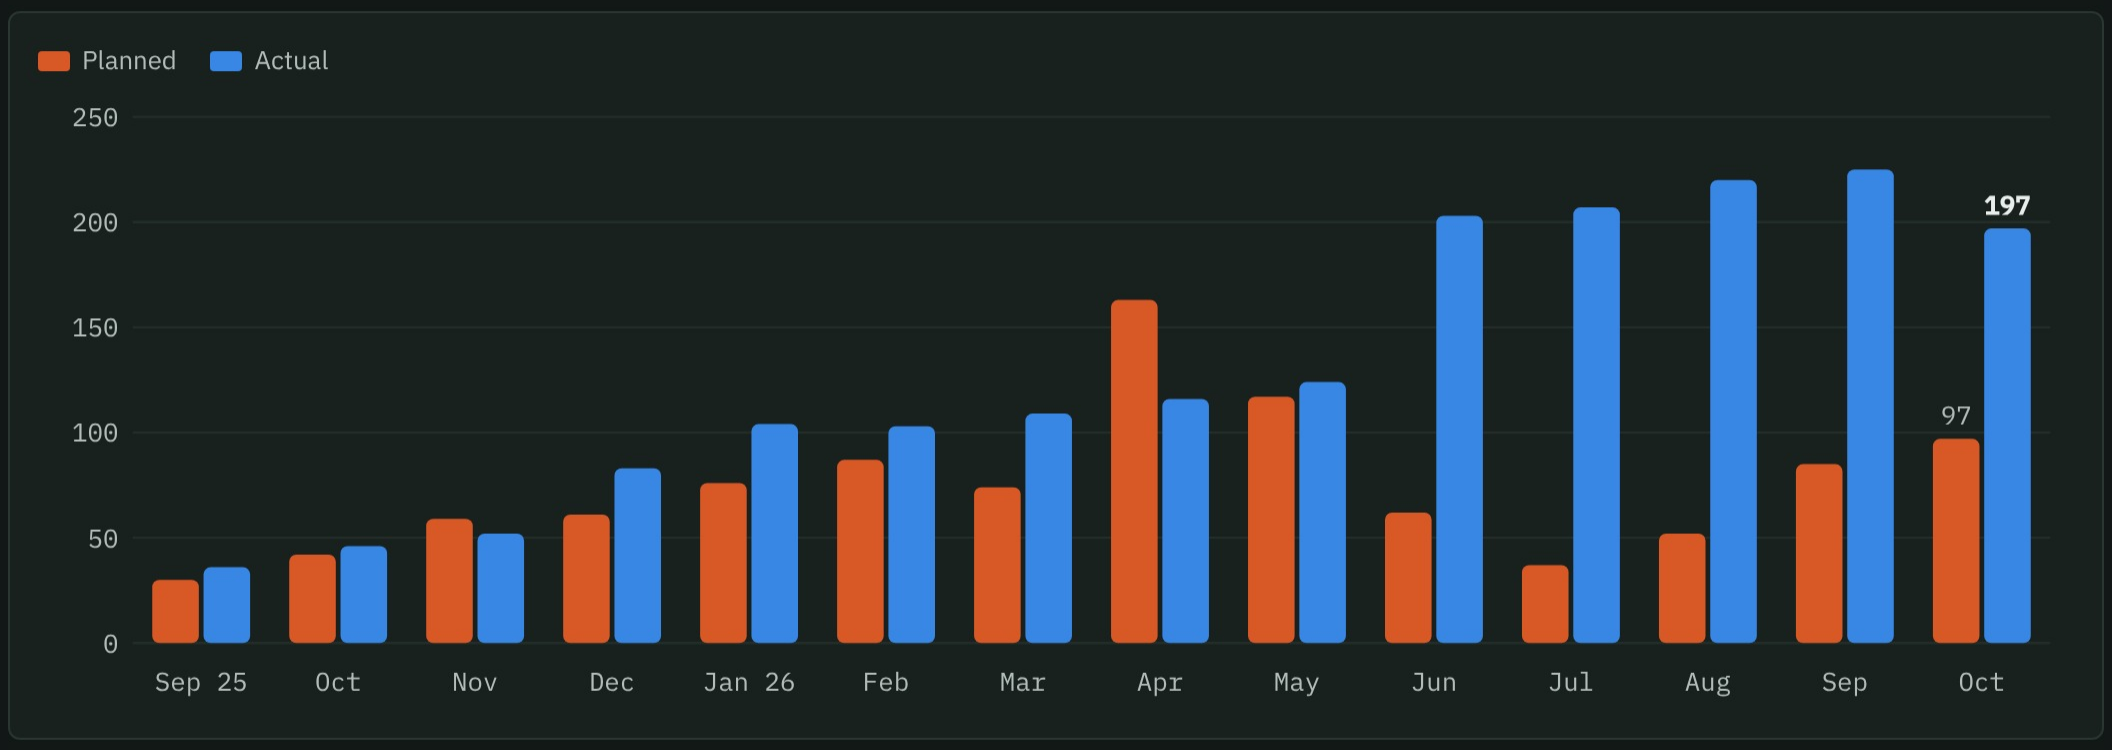

October head count is 197 (35 non-manual, 162 manual) against 97 planned, down from 225 in September. The plan rises to a peak of 229 in March 2027. Equipment on site in October: 59 against 32 planned.

Cost and invoicing

Contract value

Roads	55,700,828
Storm water network	42,542,241
Electrical	21,956,853
Potable water network	7,176,559
TSE network	6,656,378
Sewerage network	6,435,003
Contract value (excl. VAT)	**140,467,862**
Change orders	0

All values in SAR, from the BOQ summary in the weekly report. The parts add up to the contract value. No change orders are registered.

Invoices

Invoices in the log	14
Gross value submitted	46,212,660
PM-approved (13 invoices)	43,497,867
Paid incl. VAT (13 invoices)	50,080,548
Deductions and penalties	76,000
Advance payment (10%)	14,046,786
Retention	0
FIR value to date	53,952,272

Invoicing is 32.9% of the contract value against 50.7% physical progress. Invoice 14 (1–15 Oct 2026) is waiting for PM approval.

Health, safety and quality

Safety Score 0.95

Safe man-hours (cumulative)	381,284
Man-hours this week	9,660
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	8 / 36

Quality Score 0.93

FIRs issued / pending	7,068 / 137
MIRs issued / pending	242 / 2
NCRs issued / closed	11 / 11
Site instructions issued / closed	20 / 20
Shop drawing submittals	428
Material submittals approved	48 / 52

Cumulative to 19-Oct-2026. The consultant's weekly audit on 17-Oct-2026 scored quality 0.98 and safety 0.95.

Open issues and risks

ISSUE	OWNER	DETAIL
MV connection to the substation	MODON	Open since 15-Jun-2026. The start of the MV network connection to the station is waiting for the station's response; target 30-Oct-2026.
Shop drawings to Code A	Contractor	Open since 29-Jun-2026. Drawings are being submitted for upgrade to Code A; target 30-Oct-2026.
Fence blocking electrical works	MODON	Open since 06-Jul-2026. A Shinko fence obstructs the electrical works; referred to the consultant, target 26-Oct-2026.
More telecom manholes	Contractor	Open since 05-Oct-2026. The number of telecom manholes has increased; waiting for the shop drawing, target 26-Oct-2026.
Deep excavation	Contractor	Open safety risk: collapse of excavation sides. Barriers and warning signs are in place and equipment is kept away from the edges.

The project challenges named in this week's MODON summary are the Code A drawing approval and the MV connection to the substation.

Data notes

- Physical progress appears with two values. The weekly report's summary and Progress sheet give 50.69% (179,604 of 354,339 budgeted man-hours), while the Physical-Chart Data sheet and the P6 progress certificate give 48.03% (of 373,967). The headline uses the report's own summary figure.
- The MODON weekly summary file and the P6 progress tracker label cost-weighted progress as "actual" and "planned". This report uses physical % complete (man-hour weighted) only.
- The project ID differs between files: TAB1-02-003 in the weekly report, TAB1-01-009 in the MODON summary file and the older procurement sheet, and TAB1-02-005 to TAB1-02-008 in the risk register.
- Report week: the Milestones sheet states contract week 59 of 108, and the consultant's audits label 17-Oct-2026 as Week-59. Counting whole weeks from site handover gives 58. The report uses the stated week 59.
- Zone milestones disagree three ways: the weekly report's baseline (Zone 1 09-Feb-2027), the P6 baseline in the progress tracker (Zone 1 05-Jun-2027), and the forecasts in the weekly report and P6; see Milestones. The "Complete mobilization" milestone has a baseline of 10-Aug-2027, which looks wrong.
- The P6 project finish of 07-Oct-2027 is 34 calendar days after the contract date, but its total float is −29.3 days.
- The invoice log lists 14 invoices totalling 46,212,660 SAR, while its summary says 13 submitted and 14 approved by the CM.
- The "Resources at site" panel (28/32 non-manual, 57/192 manual) shows the September figures, not October's (28/35 and 69/162). Cumulative actual equipment has stayed at 269 since March 2026.
- The summary panel shows 6,360 safe man-hours this week, while the HSE statistics sheet shows 9,660.
- The workbook has two procurement sheets. "Procurement (2)" is an older version with lower rates (for example ABC 32% against 50%); the report uses "Procurement". Some items have no quantity or delivery rate.
- All 14 risk register entries are marked "Open", although 10 of them have their treatment closed.
- Scope quantities have no zone split and no previous-week values, so the this-week column is empty. Only two photos in the report are large enough to use; the other two are 382 and 546 px wide.
