Playground Initiative for Western Region (Asir, Jazan, Jeddah)

مبادرة الملاعب بالمنطقة الغربية (عسير, جازان, واحة جدة)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Profast Company Ltd.	EGIS	Eng. Yazeed Al Ragabh	26-Mar-2026	25-Jan-2027

Scope: sports grounds (padel, basketball and football), a service and toilet building, landscape works, bike and walking paths, and parking at three sites in Asir, Jazan and Jeddah.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 42.4% against 51.0% planned, 8.6% behind (SPI 0.83). It gained 3.4% this week against 4.1% planned, so the gap widened from 8.0% last week. Jazan is furthest behind at 24.3% against 44.5% planned; Jeddah is ahead of its plan.

PHYSICAL % COMPLETE
42.4% / 51.0% plan
▼ SPI 0.83 −8.6%

PROGRESS THIS WEEK
+3.4% / +4.1% plan
▼ 0.6% below the weekly plan

CONTRACT TIME ELAPSED
67.9% · day 207 of 305
▼ Forecast finish 09-May-2027

INVOICED TO DATE (GROSS)
14.6% · 4.94M SAR
5 invoices, last period ends 08-Oct-2026

Project completion is forecast 104 days late.

The weekly report and the P6 update (data date 19-Oct-2026) both forecast completion on 09-May-2027, against the contract completion date of 25-Jan-2027. P6 shows −85 days of float on project completion and 330 open activities with negative float. The most critical path runs through the steel tension cables and the PVC membrane approval (−85 days), and supply of the air dome is the challenge named in the weekly summary. The original baseline called for 75.1% by mid-October.

Site photos this week

Six photos from the Weekly Photos sheet of the 19-Oct-2026 weekly report, two from each site, all time-stamped 18-Oct-2026. Select a photo to view it larger, then use the arrows to move between photos.




Roof waterproofing, Jazan

Waterproofing on the service building roof. Stamped 18-Oct-2026, 11:28, Abu Arish.



Door works, Jazan

Metal door fitted in the service building. Stamped 18-Oct-2026, 11:01, Abu Arish.

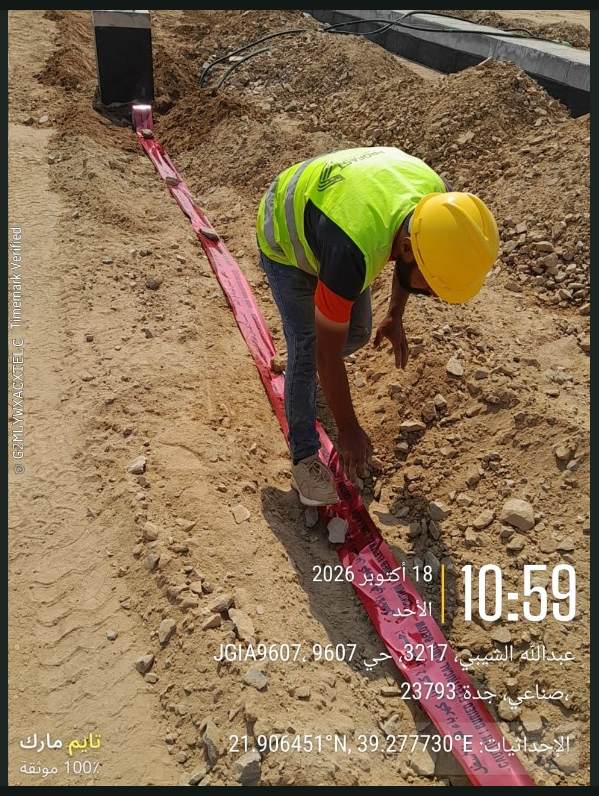

Cable warning tape, Jeddah

Warning tape laid over the cable trench. Stamped 18-Oct-2026, 10:59, GPS 21.906451°N, 39.277730°E.



Lighting pole cables and foundations, Jeddah

Backfilling along the pole foundations. Stamped 18-Oct-2026, 11:39, GPS 21.906437°N, 39.277696°E.



Wet-area waterproofing, Asir

Bituminous coat around pipe sleeves. Stamped 18-Oct-2026, 10:15, GPS 18.3361059°N, 42.6567205°E.




Air dome entrance raft, Asir

Steel fixing for the raft. Stamped 18-Oct-2026, 08:24, Khamis Mushait.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly, plotted at mid-month. Source: Physical-Chart Data sheet, weekly report 19-Oct-2026.

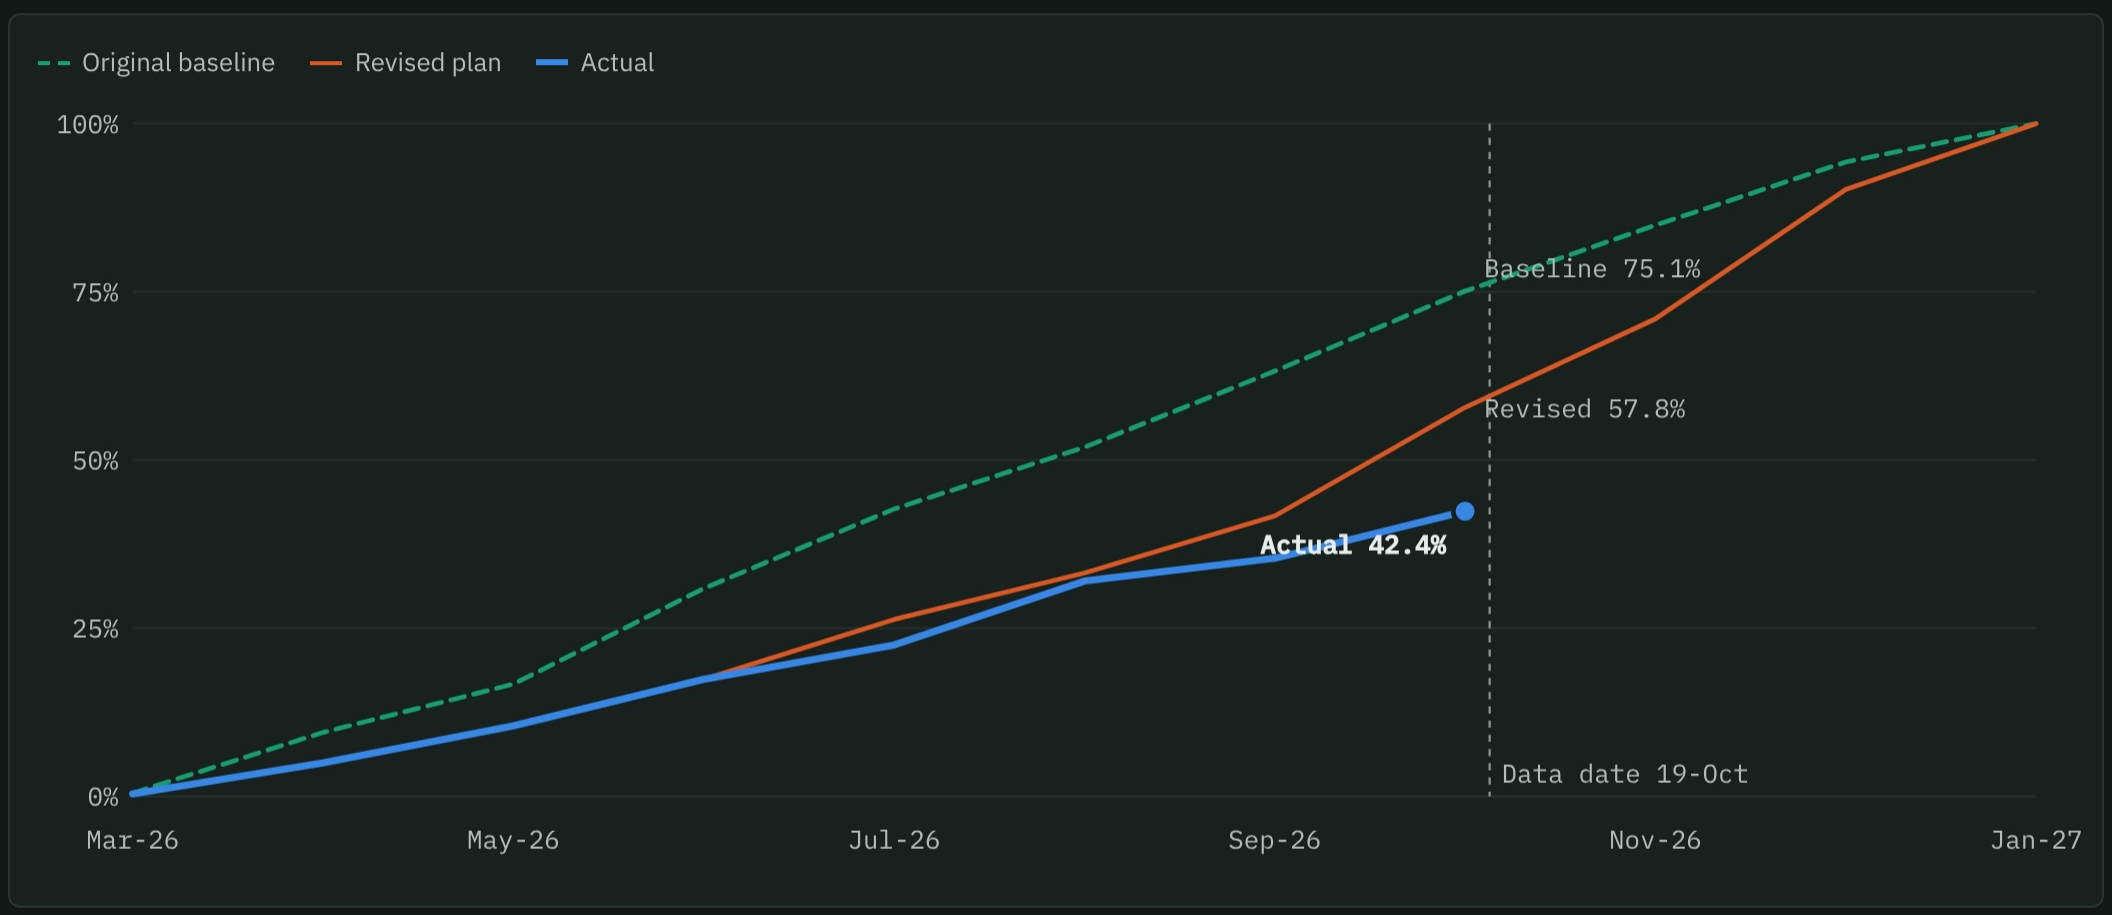

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	47.0	39.0	-8.0	—	0.83
19-Oct-2026	**51.0**	**42.4**	**-8.6**	**+3.4**	**0.83**

Only the latest weekly report was used. It gives this week's and last week's cumulative values (Progress sheet), so the table has two rows and last week's gain is not available. This week's planned gain was +4.1%.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Construction is split into the three sites.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.1%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	5.2%	100.0%	98.6%	−1.4	0.99	▼ Slightly behind
Procurement	12.6%	98.9%	62.2%	−36.8	0.63	▼ Behind
Construction	73.8%	40.9%	35.6%	−5.3	0.87	▼ Behind
Construction: Jazan	25.2%	44.5%	24.3%	−20.2	0.55	▼ Behind
Construction: Asir	23.8%	41.8%	40.9%	−0.9	0.98	● On track
Construction: Jeddah	24.8%	36.4%	42.1%	+5.7	1.16	▲ Ahead
Testing & commissioning	3.2%	0.0%	0.0%	0.0	–	○ Not yet due
Close-out	2.1%	0.0%	0.0%	0.0	–	○ Not yet due
Total	100%	**51.0%**	**42.4%**	**−8.6**	**0.83**	▼ Behind

Site weights are shares of the whole project. The P6 update (data date 19-Oct-2026) has 2,134 activities: 1,728 completed, 21 in progress and 385 not started. Its scheduled finish is 09-May-2027, against a must-finish date of 25-Jan-2027.

Scope of work: quantities

Major quantities for the three sites combined, from the Major Quantities sheet of the 19-Oct-2026 weekly report. The sheet has no previous-week values, so the "This week" column shows "–". Backfilling does not apply to these items.

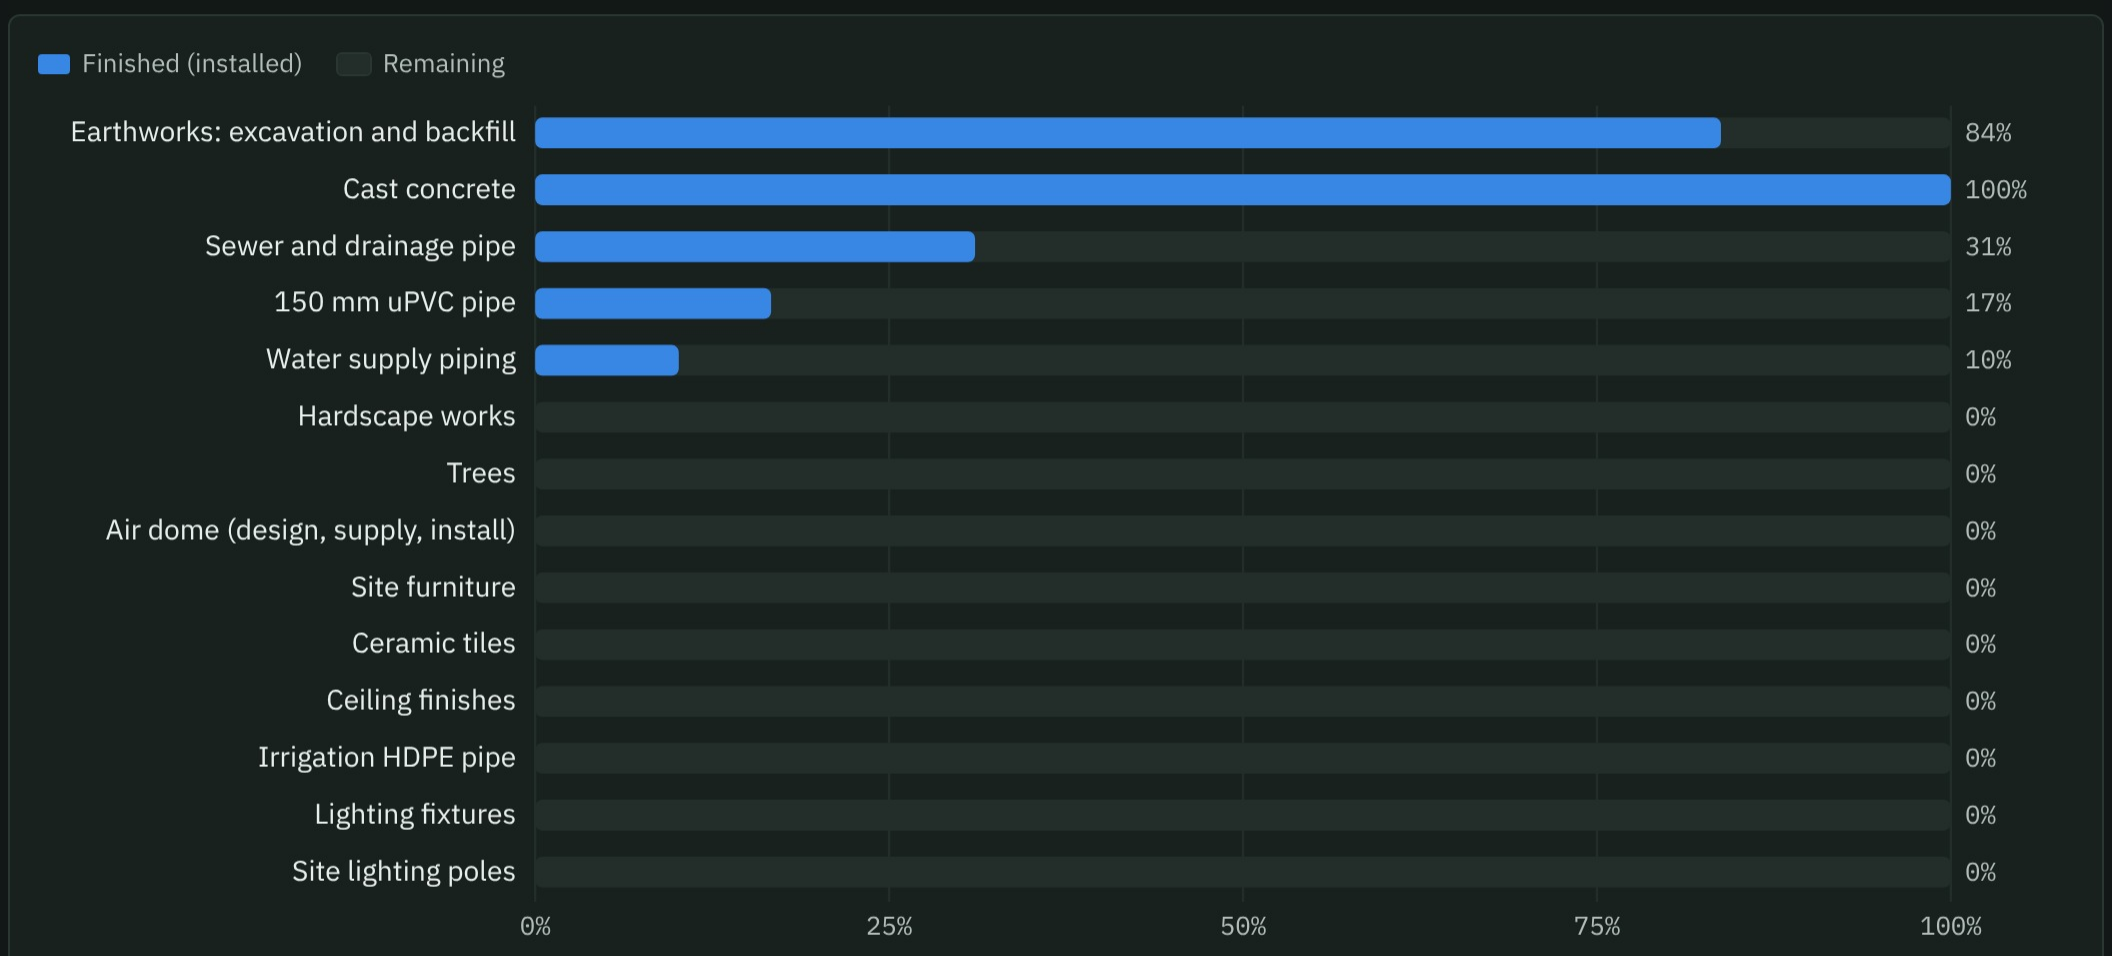

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Earthworks: excavation and backfill	All sites	m³	68,052	57,000	–	11,052	83.8%	–
Cast concrete	All sites	m³	145	145	–	0	100.0%	–
Sewer and drainage pipe	All sites	LM	177	55	–	122	31.1%	–
150 mm uPVC pipe	All sites	LM	300	50	–	250	16.7%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Water supply piping	All sites	LM	138	14	–	124	10.1%	–
Hardscape works	All sites	m²	30,380	0	–	30,380	0.0%	–
Trees	All sites	EA	895	0	–	895	0.0%	–
Air dome (design, supply, install)	All sites	item	3	0	–	3	0.0%	–
Site furniture	All sites	EA	248	0	–	248	0.0%	–
Ceramic tiles	All sites	m²	219	0	–	219	0.0%	–
Ceiling finishes	All sites	m²	207	0	–	207	0.0%	–
Irrigation HDPE pipe	All sites	LM	7,150	0	–	7,150	0.0%	–
Lighting fixtures	All sites	EA	129	0	–	129	0.0%	–
Site lighting poles	All sites	EA	322	0	–	322	0.0%	–

Work done this week

Ground slab cast for the football and basketball courts in Asir. Air dome foundations cast, with glazed-façade steelwork under way, at all sites. Irrigation pipes finished in Asir and Jeddah, and curbs around the courts finished in Jeddah. Stone cladding finished on the Asir toilets. Water-tank tie beam cast in Jazan. Toilet ceramics, roof insulation, lighting cables and pole foundations, and walkway backfilling continue.

Quantities behind the plan to date

Sewer and drainage pipe is at 55 LM against 177 LM planned to date, 150 mm uPVC pipe at 50 LM against 150 LM, and earthworks at 57,000 m³ against 57,844 m³. Water supply piping is ahead, at 14 LM with none planned yet. Hardscape, trees, the air dome, irrigation pipe and lighting have not started.

Milestones

The weekly report and the P6 update give the same forecast dates for every milestone; the delays are against the baseline. The day counts in brackets are the change from baseline given in the weekly report.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	26-Mar-2026	26-Mar-2026	26-Mar-2026 (actual)	–	✓ Done
Baseline programme approval	29-Apr-2026	29-Apr-2026	29-Apr-2026 (actual)	–	✓ Done
Complete mobilisation	02-Jun-2026	02-Jun-2026	02-Jun-2026 (actual)	–	✓ Done
Levelling works	22-Jul-2026	20-Oct-2026 (+90 d)	20-Oct-2026	−13	▼ Late
Engineering	19-Jan-2027	05-Nov-2026 (−75 d)	05-Nov-2026	69	● Ahead of baseline
Toilet building	09-Aug-2026	04-Jan-2027 (+148 d)	04-Jan-2027	18	▼ Late
Playground area	30-Nov-2026	29-Apr-2027 (+150 d)	29-Apr-2027	−77	▼ Late
Asir works	13-Dec-2026	29-Mar-2027 (+106 d)	29-Mar-2027	−50	▼ Late
Natural landscape works	16-Jan-2027	08-Mar-2027 (+51 d)	08-Mar-2027	−53	▼ Late
Jazan works	19-Jan-2027	09-May-2027 (+110 d)	09-May-2027	−85	▼ Late
Jeddah works	25-Jan-2027	25-Mar-2027 (+59 d)	25-Mar-2027	−47	▼ Late
Testing & commissioning	29-Apr-2026 *	11-Apr-2027 (+347 d)	11-Apr-2027	−61	▼ Late
Project finish	25-Jan-2027	09-May-2027 (+104 d)	09-May-2027	−85	▼ Late

Jazan sets the finish date.

Jazan works and project completion share the latest forecast, 09-May-2027, at −85 days of float. Open activities with negative float are led by furniture (19), electrical works (15), fixtures (14), air lock doors (12), steel tension cables (11), emergency doors (11) and the padel and basketball grounds (10 each). * The testing and commissioning baseline of 29-Apr-2026 is as given in the Milestones sheet and appears to be wrong.

Procurement of key materials

Share of total quantity delivered to site. Source: supply tracking file (ملف التوريدات) dated 19-Oct-2026.

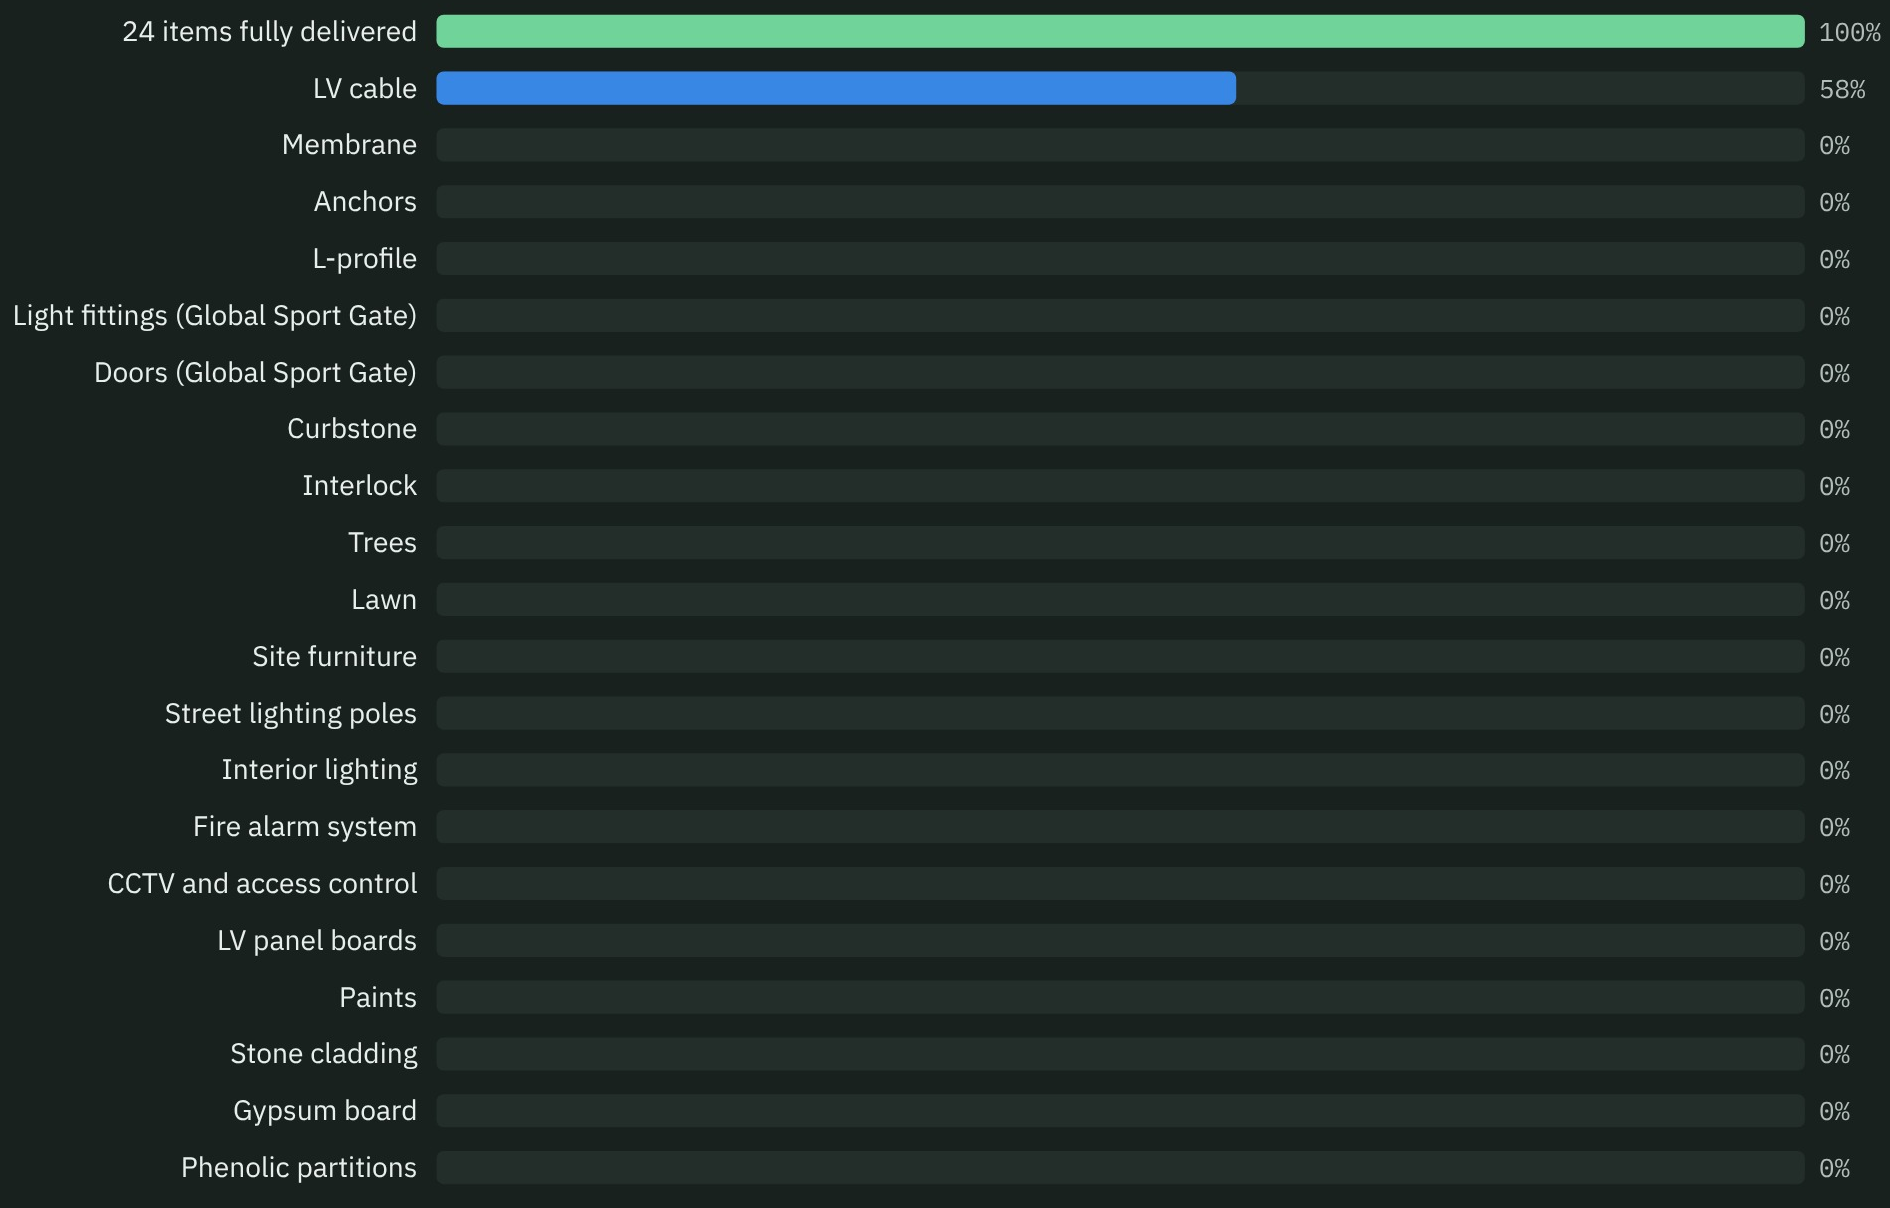

Twelve Global Sport Gate items: nothing delivered


Membrane (18,019 m²), 1,521 anchors, 1,488 LM of L-profile, 162 light fittings, 24 doors, generators, ATS units, electric panels, ventilation and insulation are all in manufacture, with supply due between 01-Nov and 25-Dec-2026. Supply of the air dome is the challenge named in the weekly summary, and the risk register rates air-dome delivery delay High.

Paving, planting and electrical fit-out

Curbstone (8,868 LM) and interlock (8,173 m²) are being supplied with nothing on site yet. Trees, lawn, site furniture, street lighting poles, interior lighting, fire alarm, CCTV and LV panel boards are also at 0. LV cable is at 4,500 of 7,700 LM. In total 37 tracked items have nothing delivered. The weekly report counts 117 materials planned, 35 purchase orders issued and 22 materials on site.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

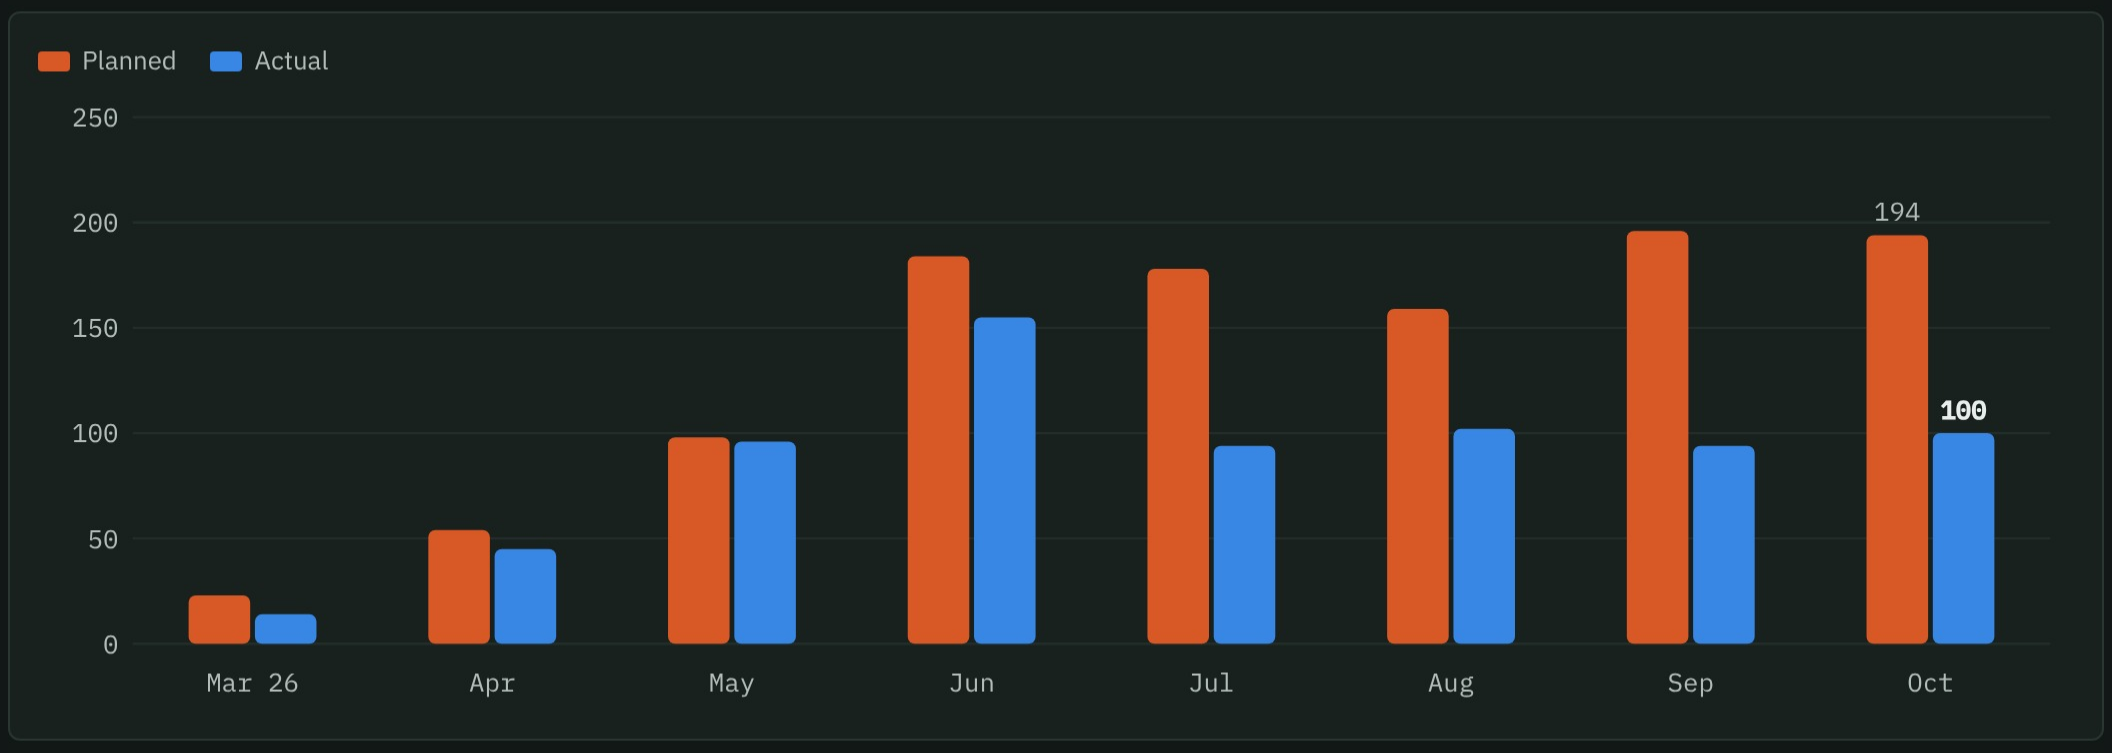

October head count is 100 against 194 planned (−48%): 70 workers against 175 planned and 30 staff against 19. Equipment on site is 21 against 27 planned.

Cost and invoicing

Contract value

Original contract value	33,997,787
Potential changes	−204,183
Revised contract value	33,793,604
Estimate at completion	33,997,787
Change orders	0

All values in SAR. The Conclusion sheet gives 33,997,787 as including VAT. No change orders are registered.

Invoices

Invoices submitted	5
Gross value	4,943,711
Deductions and penalties	11,000
Net incl. VAT	5,674,267
Approved by MODON PM / paid	0 / 0
FIR value to date	6,416,144

Invoicing is 14.6% of the revised contract value against 42.4% physical progress. All five invoices are approved by the consultant, but none is recorded as approved by the MODON PM or paid.

Health, safety and quality

Safety Score 0.84

Safe man-hours (cumulative)	132,050
Man-hours this week	6,480
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	160 / 156

MODON HSE site inspection 13-Oct-2026 (report no. 13).

Quality Score 0.86

FIRs issued / closed	657 / 634
FIRs pending	22
MIRs issued / closed	102 / 99
NCRs issued / closed	20 / 20
Site instructions issued / closed	25 / 25
Shop drawing submittals processed	137 of 141
Material submittals processed	130 of 147

QC observations checklist no. 25, inspection day 19-Oct-2026.

Open issues and risks

ISSUE	OWNER	DETAIL
MV cables on the excavation route	Owner	Raised 10-Oct-2026 (Jazan, per the risk and issue log). Medium-voltage cables conflict with the excavation route; coordination with the relevant parties on mitigation is ongoing and the contractor is waiting for the owner's permission.
Air dome supply	Contractor	Named as the project challenge in the weekly summary. The risk register rates delay in air-dome material delivery High (score 20); mitigation is close follow-up with MODON to speed up approval of the air dome design, target 15-Nov-2026.

The risk register has 9 open risks. Six are rated High: air-dome delivery delay, air quality in confined spaces, equipment maintenance and certification, fall protection, heat stress, and separation of public traffic. Two are Medium (unauthorised site entry, unsafe material storage) and one is Low (defective tools). The seven earlier issues in the issue log are closed.

Data notes

- Only the latest weekly upload (W3, data date 19-Oct-2026) was used. "This week" values come from the report's own last-week columns; the quantity table has none, so its this-week column is blank.
- The report week is the project week counted from site handover (26-Mar-2026 to 19-Oct-2026 is 207 days, week 29). The files carry the serial WPR-25 but state no week number.
- The weekly summary sheets (files 15 and 16), the Conclusion sheet and the look-ahead sheet label a cost-based progress figure as "actual". This report uses physical progress (man-hour weighted) only.
- File 16 names a different contractor (شركة الانجاز للتجارة والمقاولات), project manager (عبد الله الشنيفي), sector (القطاع الأوسط), start date 24-Nov-2025 and contract end 23-May-2026. File 15 and the weekly report give Profast, Eng. Yazeed Al Ragabh, 26-Mar-2026 and 25-Jan-2027.
- The Physical-Chart Data sheet puts the revised plan at 57.8% for mid-October, above the 51.0% planned to 19-Oct in the Progress sheet. The baseline curve totals 427,120 man-hours against 406,255 in the revised plan and the Progress sheet.
- The Milestones sheet's baseline dates for programme approval (02-Jun-2026), mobilisation (25-Jan-2027) and testing and commissioning (29-Apr-2026) look shifted; the summary on the report's first sheet gives 29-Apr and 02-Jun for the first two. The Conclusion sheet dates project end as 25-Jan-2026 and playground completion as 16-Jan-2026.
- The major-quantity panel on the report's first sheet has shifted columns (for example, trees: 895 total, 30,380 remaining), so quantities were taken from the Major Quantities sheet.
- The invoice log counts 47 consultant-approved invoices although only 5 were submitted.
- The HSE statistics sheet covers 06–13 Oct 2026 and gives 137,270 cumulative man-hours and 159 toolbox talks; the report summary gives 132,050 and 156.
- The procurement log shows street lighting poles as delivered to site, while the supply file shows 0 of 322 delivered. In the supply file the remarks and unit columns look shifted for several rows.
- Several cells on the report's first sheet show #REF ! errors (EAC and the milestone panel).

Compiled 28-Oct-2026 from the weekly report uploaded for the week ending 19-Oct-2026.
