Construction of Industrial Units for Artisans in Najran

مبادرة الحرفيين (الصناعات منخفضة العمليات التصنيعية بنجران)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Labenat Al Bena	EGIS	Eng. Ahmed Kotbi	03-Mar-2026	02-Jan-2027

Scope: the Low Process RBF unit, an outside mosque, a pump shed and a GRP water tank, with site works, concrete, masonry, finishes, pre-engineered structures, and mechanical and electrical systems including fire fighting, fire alarm and solar power.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is 98.5% complete against 82.4% planned, 16.1% ahead of the baseline (SPI 1.195). This week's progress was 2.0%, below the 3.8% planned for the week.

PHYSICAL % COMPLETE
98.5% / 82.4% plan
▲ SPI 1.195 +16.1%

PROGRESS THIS WEEK
+2.0% / +3.8% plan
▼ 1.8% below the weekly plan

CONTRACT TIME ELAPSED
76.1% · day 232 of 305
● Forecast finish 15-Oct-2026 has passed

INVOICED TO DATE (GROSS)
83.1% · 7.94M SAR
6 invoices, last period ends 30-Sep-2026

The works are nearly finished, but the reported completion forecast is out of date.

The weekly report forecasts completion of all works on 15-Oct-2026, six days before its own data date, while close-out is 67.2% and electrical works 98.5% complete. Testing and commissioning is still planned for 09-Dec-2026 to 19-Dec-2026, and the contract completion date is 02-Jan-2027. The forecast needs to be updated.

Site photos this week

Two photos from the "Weekly Photos" sheet of the 21-Oct-2026 weekly report (pump room works), both stamped 21-Oct-2026, Najran Region. Select a photo to view it larger, then use the arrows to move between photos.



Fire pump shed

Fire pumps and fire-fighting pipework under the pump shed canopy. Stamped 21-Oct-2026, 09:23.




Pump shed and GRP water tank

Pump shed next to the GRP water tank, with workers on site. Stamped 21-Oct-2026, 09:24.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly; the October value is to 21-Oct-2026. Source: Physical-Chart Data sheet.

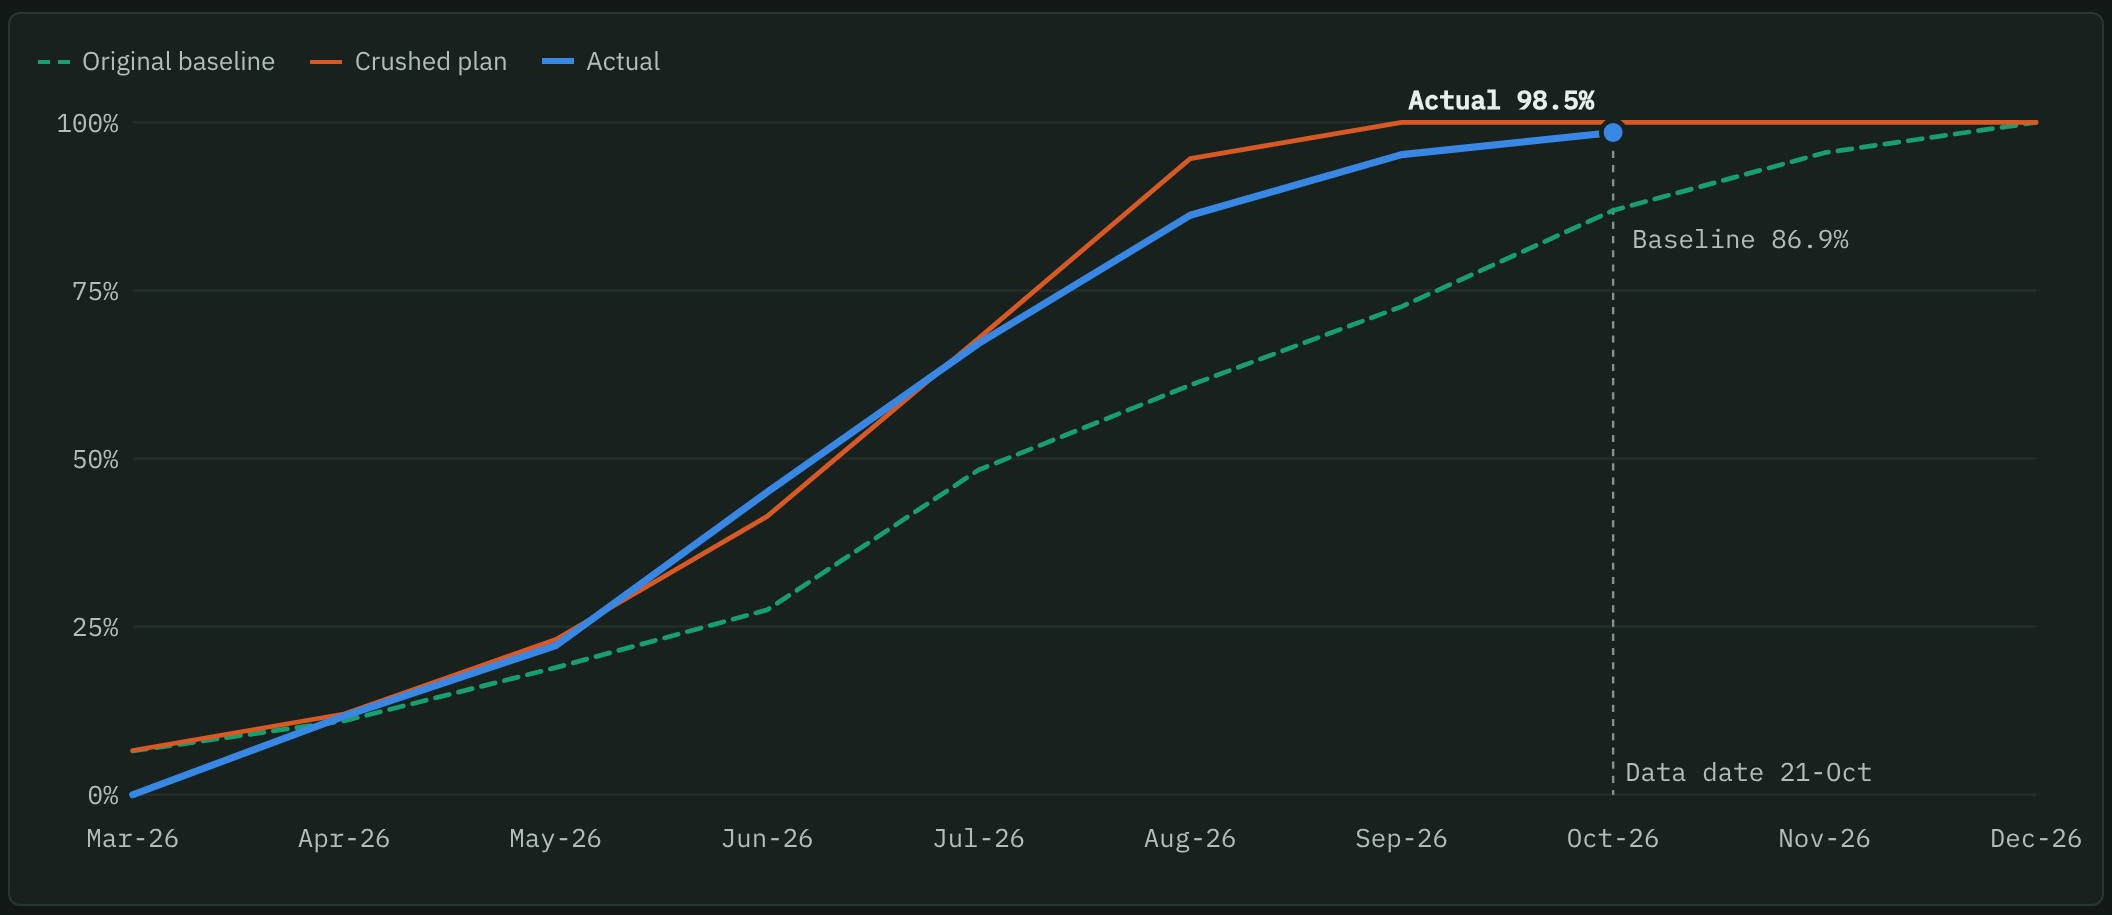

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
21-Oct-2026	**82.4**	**98.5**	**+16.1**	**+2.0**	**1.195**

Only this week's report was used, so earlier weeks are not shown. The gain this week (+2.0%, against +3.8% planned) is the weekly progress stated in the report.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report and Progress sheets.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	4.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	12.0%	98.2%	100.0%	+1.8%	1.02	✓ Complete
Construction	**76.3%**	**82.1%**	**99.6%**	**+17.5%**	**1.21**	▲ Ahead
· Site works	4.7%	66.9%	100.0%	+33.1%	1.49	✓ Complete
· Concrete	17.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Masonry	2.2%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Metal works	0.6%	41.6%	100.0%	+58.4%	2.40	✓ Complete
· Thermal and moisture protection	2.7%	92.9%	100.0%	+7.1%	1.08	✓ Complete
· Doors and windows	3.6%	56.1%	100.0%	+43.9%	1.78	✓ Complete
· Finishes	5.0%	29.4%	100.0%	+70.6%	3.41	✓ Complete
· Specialties	0.6%	0.0%	100.0%	+100.0%	–	✓ Complete
· Pre-engineered structure	8.1%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Mechanical works	13.1%	87.8%	100.0%	+12.2%	1.14	✓ Complete
· Electrical works	18.3%	76.9%	98.5%	+21.6%	1.28	▲ Ahead

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Close-out	3.7%	0.0%	67.2%	+67.2%	–	▲ Ahead
Total	100%	**82.4%**	**98.5%**	**+16.1%**	**1.195**	▲ Ahead

The P6 schedule status in the report lists 1,462 activities: 1,430 completed, 17 in progress and 15 not started (97.8% complete by count). No activities are on the critical path.

Scope of work: quantities

Total and installed quantity for each major item, from the Major Quantities sheet of the 21-Oct-2026 weekly report. "This week" is shown as "–" because the report gives no previous-week quantities.

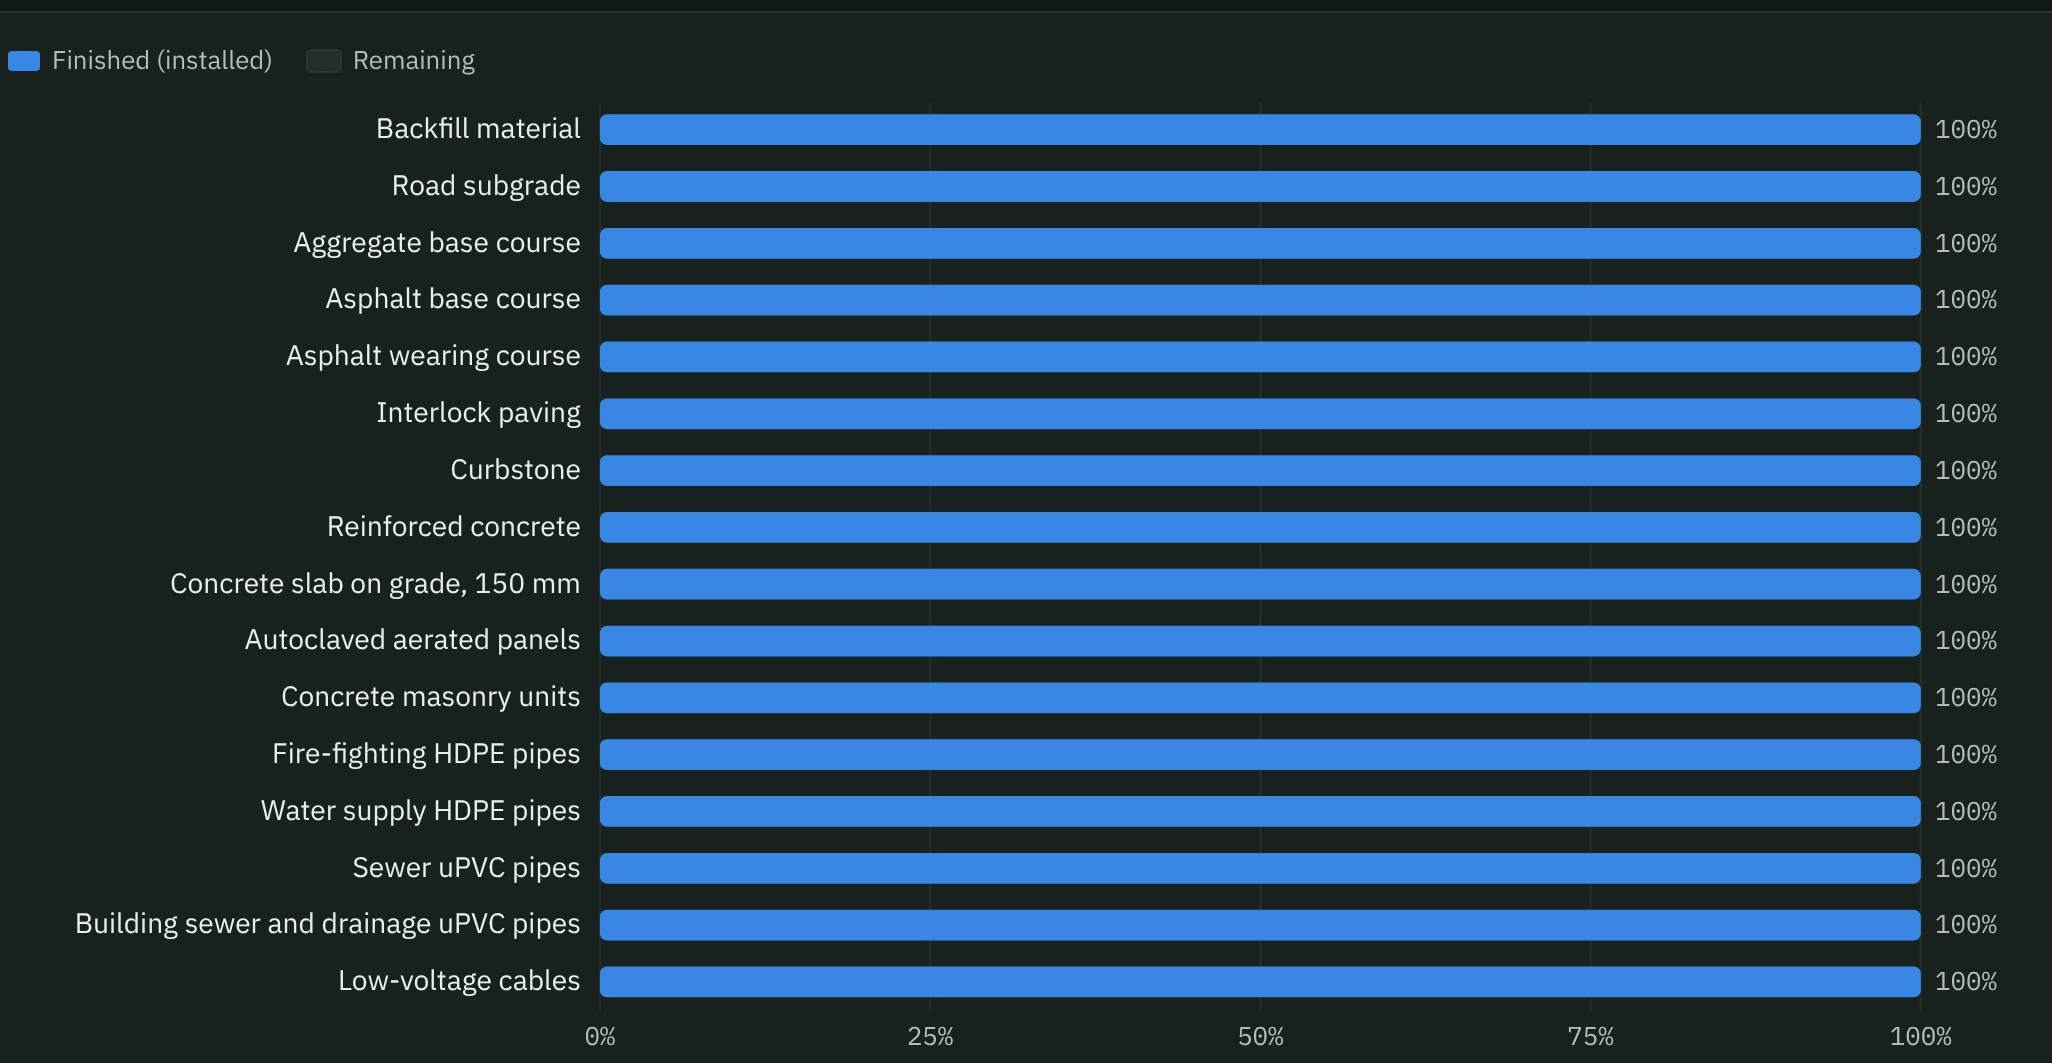

SCOPE ITEM	BOQ ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Backfill material	2.1.6	m³	2,615	2,615	–	0	100.0%
Road subgrade	2.2.4	m³	1,300	1,300	–	0	100.0%
Aggregate base course	2.2.3	m³	867	867	–	0	100.0%
Asphalt base course	2.2.2	m³	304	304	–	0	100.0%
Asphalt wearing course	2.2.1	m³	217	217	–	0	100.0%
Interlock paving	2.2.7.1	m²	1,326	1,326	–	0	100.0%
Curbstone	2.3.8	LM	1,294	1,294	–	0	100.0%
Reinforced concrete	3.2	m³	449	449	–	0	100.0%
Concrete slab on grade, 150 mm	3.3	m³	307	307	–	0	100.0%
Autoclaved aerated panels	3.4	m²	55	55	–	0	100.0%
Concrete masonry units	4.1	m²	444	444	–	0	100.0%
Fire-fighting HDPE pipes	15.1.2.1 · 200 mm	LM	48	48	–	0	100.0%
	15.1.2.2 · 150 mm	LM	200	200	–	0	100.0%

SCOPE ITEM	BOQ ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
	15.4.1.1 · 8 in	LM	15	15	–	0	100.0%
	Total	LM	**263**	**263**	**–**	**0**	**100.0%**
Water supply HDPE pipes	15.2.2.1 · 100 mm	LM	20	20	–	0	100.0%
	15.2.2.2 · 90 mm	LM	235	235	–	0	100.0%
	15.2.2.3 · 63 mm	LM	8	8	–	0	100.0%
	15.2.2.4 · 50 mm	LM	40	40	–	0	100.0%
	15.5.1.1 · 63 mm	LM	40	40	–	0	100.0%
	Total	LM	**343**	**343**	**–**	**0**	**100.0%**
Sewer uPVC pipes	15.3.2.1 · 110 mm	LM	105	105	–	0	100.0%
	15.3.2.2 · 160 mm	LM	75	75	–	0	100.0%
	Total	LM	**180**	**180**	**–**	**0**	**100.0%**
Building sewer and drainage uPVC pipes	15.6.1.1 · 4 in	LM	168	168	–	0	100.0%
	15.6.1.2 · 3 in	LM	30	30	–	0	100.0%
	15.6.1.3 · 2 in	LM	132	132	–	0	100.0%
	15.6.1.4 · 1 in	LM	180	180	–	0	100.0%
	Total	LM	**510**	**510**	**–**	**0**	**100.0%**
Low-voltage cables	16.6.1 · 4C×185 mm²	LM	120	120	–	0	100.0%
	16.6.2 · 4C×120 mm²	LM	75	75	–	0	100.0%
	Total	LM	**195**	**195**	**–**	**0**	**100.0%**

Asphalt status disagrees between sheets

The Major Quantities sheet reports both asphalt layers and the interlock paving as fully installed, but the Procurement sheet lists both asphalt layers as "Ready for delivery" and the site layout on the Project Summary sheet marks the wearing course as "Not Started".

Milestones

Baseline, latest plan and forecast dates from the Milestones sheet. Change is the number of days the forecast is earlier than the baseline, as stated in the sheet.

MILESTONE	BASELINE	LATEST PLAN	FORECAST	CHANGE (DAYS)	STATUS
Contract award	25-Jan-2026	25-Jan-2026	25-Jan-2026	0	✓ Done
Contract signature	12-Feb-2026	12-Feb-2026	12-Feb-2026	0	✓ Done
Site handover	03-Mar-2026	03-Mar-2026	03-Mar-2026	0	✓ Done
Complete mobilisation	31-Mar-2025	31-Mar-2025	31-Mar-2025	0	✓ Done
Existing condition survey and final reports	31-Mar-2025	31-Mar-2025	31-Mar-2025	0	✓ Done
Long-lead procurement and delivery	27-Oct-2026	27-Oct-2026	27-Oct-2026	0	? Actual date after data date
Short-lead procurement and delivery	29-Oct-2026	05-Sep-2026	05-Sep-2026	0	✓ Done

MILESTONE	BASELINE	LATEST PLAN	FORECAST	CHANGE (DAYS)	STATUS
All warehouse works	29-Nov-2026	03-Oct-2026	03-Oct-2026	0	✓ Done
Outside mosque (prayer room)	05-Dec-2026	30-Sep-2026	30-Sep-2026	0	✓ Done
GRP water tank and pump shed	24-Aug-2026	24-Aug-2026	24-Aug-2026	0	? Forecast date has passed
All external works	25-Nov-2026	25-Nov-2026	30-Sep-2026	56	? Forecast date has passed
All works incl. testing, commissioning and close-out (initial handover)	02-Jan-2027	02-Jan-2027	15-Oct-2026	79	? Forecast date has passed
Demobilisation	02-Jan-2027	02-Jan-2027	15-Oct-2026	79	? Forecast date has passed

Four milestones are still forecasts although their dates have passed.

The GRP water tank and pump shed, external works, completion of all works and demobilisation are marked as forecasts dated between 24-Aug-2026 and 15-Oct-2026, all before the 21-Oct-2026 data date. Close-out is 67.2% complete and testing and commissioning is planned for December 2026, so they need either actual dates or new forecasts.

Procurement of key materials

Share of material items delivered to site, by discipline. Source: Procurement sheet, weekly report 21-Oct-2026 (86 of 108 items delivered).



Finishes: 5 of 11 items delivered


Granite tiles, marble strip and wood skirting are "Ready for delivery"; marble chips and phenolic partitions are "Contractor ready"; carpet is "Locally available".

Other items not yet delivered

Both asphalt layers and road paint (ready for delivery), HVAC fans, ductwork, diffusers and grilles (contractor ready), roof deck waterproofing (delivery ongoing), aluminium cladding, galvanized steel fence and fence gate, water sprinklers, a Corian countertop, and toilet and mosque signage and MODON logos.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

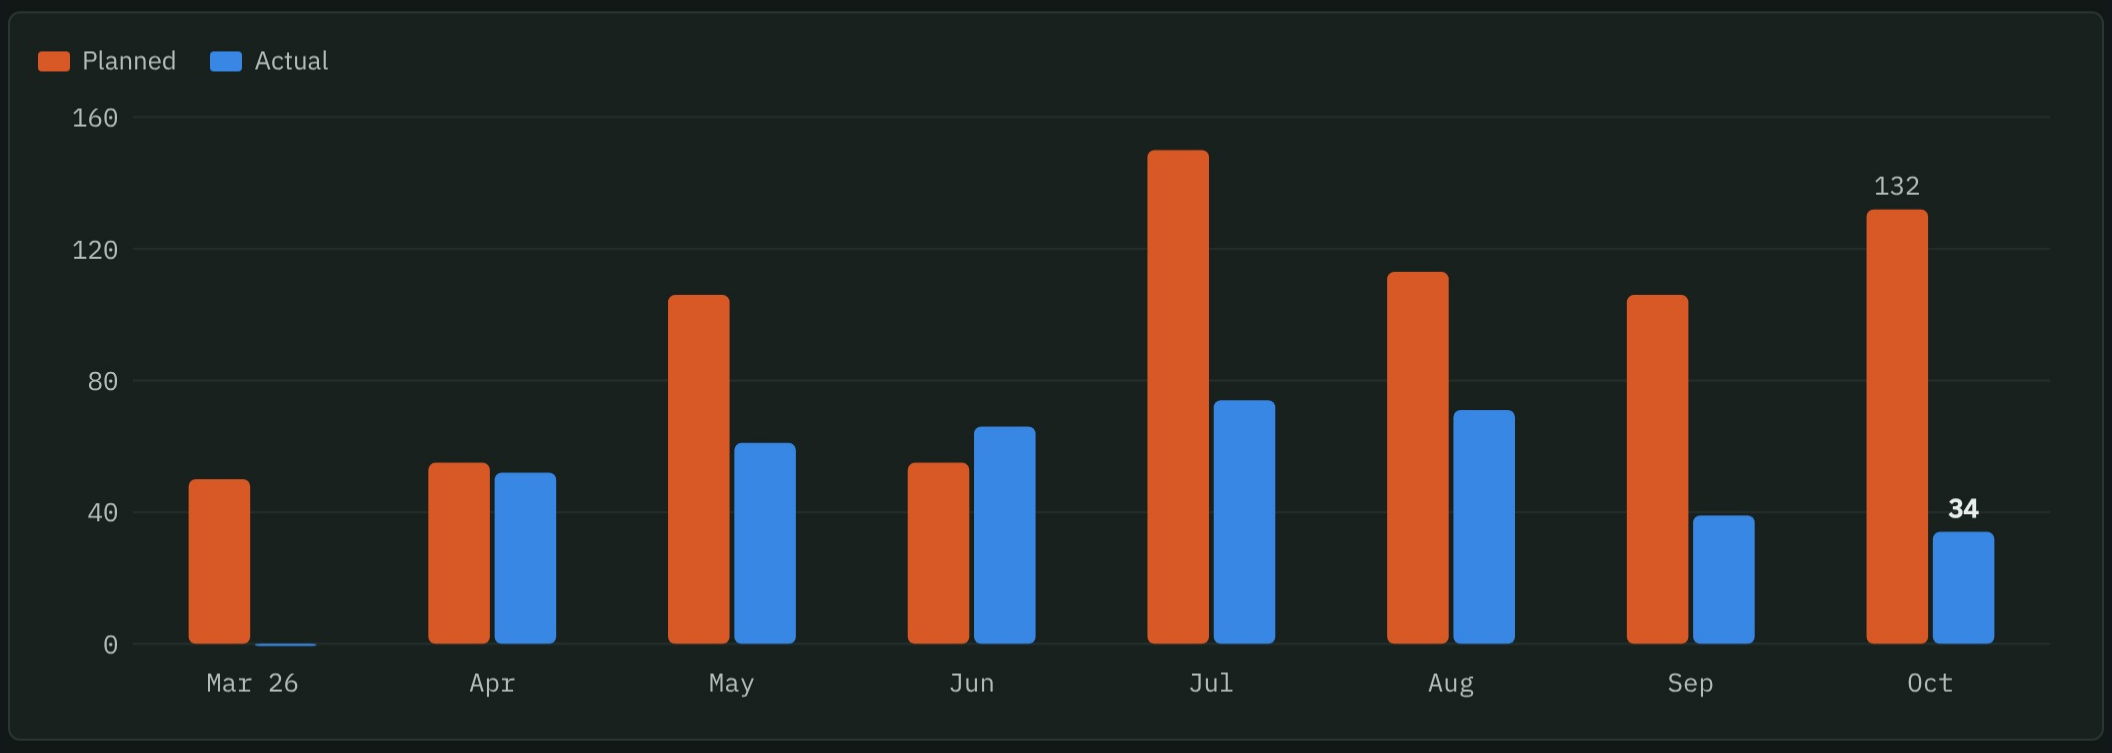

October head count is 34 (13 non-manual, 21 manual) against 132 planned (−74%). Equipment on site is 8 against 34 planned.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	9,554,134
Revised contract value	9,554,134
Contract value incl. 15% VAT	10,987,254
Change orders	0

All values in SAR. The change order log is empty.

Invoices

Invoices submitted / PM approved	6 / 6
Gross value	7,935,744
Invoices paid	4
Paid value	4,460,610
Retention	0
Deductions and penalties	−20,000
Net incl. VAT	9,106,107
FIR value to date	9,332,210

Invoicing is 83.1% of the contract value against 98.5% physical progress. Invoices 5 and 6 (3,475,134 SAR gross) are approved but not yet paid.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	83,990
Man-hours this week	1,824
Lost-time injuries	0
Fatalities	0
First-aid cases	2
Near misses (year to date)	9
Fire incidents	0
Inductions / toolbox talks	40 / 28

From the HSE-Stat sheet; the summary panel differs, see Data notes.

Quality Score 0.89

FIRs issued / closed	407 / 407
MIRs issued / closed	64 / 64
NCRs issued / closed	17 / 17
Site instructions issued / closed	18 / 18
Approved shop drawings	93 / 93
Approved material submittals	95 / 95
FIR value this period (SAR)	65,380

FIR period: 12-Oct-2026 to 18-Oct-2026.

Data notes

- The forecast completion of all works (15-Oct-2026) is before the report's data date of 21-Oct-2026, while close-out is 67.2% complete and the Testing sheet plans testing and commissioning for 09-Dec-2026 to 19-Dec-2026.
- Milestones: mobilisation and the existing condition survey have baseline dates of 31-Mar-2025, before the contract award of 25-Jan-2026. Long-lead procurement is marked actual with a date of 27-Oct-2026, after the data date; the summary panel gives its latest plan as 03-Oct-2026 while the Milestones sheet gives 27-Oct-2026. The change column shows 0 days for short-lead procurement, the warehouse and the mosque, although their forecasts are 54 to 66 days before baseline.
- S-curve: the Physical-Chart Data sheet divides earned man-hours by 241,519.85 (the crushed plan total) for April to September but by 224,320 for October. This report uses 224,320, the budget in the Progress sheet, for every month; with the sheet's own percentages September would be 88.4% instead of 95.2%.
- Only the latest weekly report was used. This-week quantities are shown as "–" because the report has no previous-week figures, and the S-curve table has only this week.
- Asphalt: the Major Quantities sheet and the Lookahead sheet report the base and wearing courses as 100% installed, but the Procurement sheet lists both as "Ready for delivery" and the Project Summary layout marks the wearing course as "Not Started". Their Plan to Date cells are blank and the variance column shows the full quantity.
- Procurement: the Procurement sheet shows 86 of 108 items delivered, but the summary panel shows 95 of 95 materials on site. The sheet header still reads "as of 26-Jul-2026". Finishes and Specialties are reported 100% physically complete although 6 of 11 finishes items and 2 of 3 specialties items are not delivered.
- Manpower: October non-manual actual is 13 in the monthly table, 16 in the Manpower sheet summary and 14 in the weekly report panel.
- HSE: the weekly report panel shows 1 first-aid case, 2 near misses and 1 fire incident; the HSE-Stat sheet shows 2 first-aid cases, 9 near misses year to date (0 cumulative) and no fire incidents.
- The hidden PV-PH and PV sheets hold planned-value data for another project (HAL1-05-1, Civil Defense Fire Station in Hail Industrial City, 2024–2025). They were not used.
- The Invoice Log shows a revised contract value of 21,100,000, an estimate at completion of 20,900,000 and potential changes of 200,000 next to the 9,554,134 contract value. Invoice 1 and the Lookahead sheet use project ID NJR1-01-007, and the Lookahead names Mohammed Alharbi as project manager.
- The Project Summary sheet splits the contract value by component differently from the Progress sheet (for example Site Works 1,067,430 against 682,299), though both total 9,554,134. It also labels a cost-based progress figure as planned progress; this report uses physical (man-hour) progress only.
- The Issues log and the Risk Register are empty, so the issues and risks section is left out. The weekly quality score is 0.8878 in every week since April. Several summary cells show #REF!.
- The file is "Weekly Report #29"; this report uses project week 33 (days since site handover divided by 7), which matches "Current Contract Weeks: 33 of 44" in the Milestones sheet.

Compiled 28-Oct-2026 from the weekly report uploaded for 21-Oct-2026 (Weekly Report #29).
