
egis ENJAZCO شركة الانجاز للتجارة والمقاولات ALEnjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 13 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-R-UP-Land Developmen		147	23-Mar-26	05-May-27	16-May-26 A	06-Jan-27	0.00	5,065,913.39	8,694,503.10	0%	58.27%	98
Key Milestones		0	23-Mar-26	22-Sep-26	13-Oct-26	13-Oct-26	0.00	0.00	0.00	0%	0%	-17
Contractual Milestone		0	23-Mar-26	22-Sep-26	13-Oct-26	13-Oct-26	0.00	0.00	0.00	0%	0%	-17
Construction		0	23-Mar-26	22-Sep-26	13-Oct-26	13-Oct-26	0.00	0.00	0.00	0%	0%	-17
JDH4-02-007-M	Completion of Road Works	0		22-Sep-26		13-Oct-26	0.00	0.00	0.00	100%	0%	-17
JDH4-02-007-M	Completion of Earthworks & Site Gra	0		23-Mar-26		13-Oct-26	0.00	0.00	0.00	100%	0%	-171
Construction		147	02-Nov-26	02-May-27	16-May-26 A	03-Jan-27	0.00	4,288,211.52	6,238,602.48	0%	68.74%	98
Roads		37	02-Nov-26	23-Nov-26	23-Sep-26 A	01-Nov-26	0.00	45,603.33	99,050.01	0%	46.04%	19
Road 01		37	02-Nov-26	23-Nov-26	23-Sep-26 A	01-Nov-26	0.00	45,603.33	99,050.01	0%	46.04%	19
Road Works (Roundabout)		37	02-Nov-26	23-Nov-26	23-Sep-26 A	01-Nov-26	0.00	45,603.33	99,050.01	0%	46.04%	19
Finishing Works		37	02-Nov-26	23-Nov-26	23-Sep-26 A	01-Nov-26	0.00	45,603.33	99,050.01	0%	46.04%	19
Precast Interlocking block pavers		4	02-Nov-26	05-Nov-26	23-Sep-26 A	18-Oct-26	0.00	45,603.33	57,004.16	0%	80%	16
JDH4-02-00	Installation of Interlocking block pave	4	02-Nov-26	05-Nov-26	23-Sep-26 A	18-Oct-26	0.00	45,603.33	57,004.16	0%	80%	16
Pavement Markings		4	05-Nov-26	09-Nov-26	14-Oct-26	18-Oct-26	0.00	0.00	16,149.78	0%	0%	19
JDH4-02-00	Pavement markings [Road 01]	4	05-Nov-26	09-Nov-26	14-Oct-26	18-Oct-26	0.00	0.00	16,149.78	0%	0%	19
Traffic Signage		12	10-Nov-26	23-Nov-26	19-Oct-26	01-Nov-26	0.00	0.00	25,896.07	0%	0%	19
JDH4-02-00	Installation of Traffic Signs [Road 01]	12	10-Nov-26	23-Nov-26	19-Oct-26	01-Nov-26	0.00	0.00	25,896.07	0%	0%	19
Sewage Lift Station		147	12-Dec-26	02-May-27	17-Sep-26 A	03-Jan-27	0.00	828,409.34	1,824,698.63	0%	45.4%	98
Mechanical Works		66	12-Dec-26	10-Jan-27	23-Sep-26 A	25-Oct-26	0.00	564,837.89	1,116,429.99	0%	50.59%	66
Anti Water Hammer Equipment		4	12-Dec-26	15-Dec-26	01-Oct-26 A	18-Oct-26	0.00	529,831.18	883,051.97	0%	60%	50
JDH4-02-007-	Installation of Anti-Water Hammer Ec	4	12-Dec-26	15-Dec-26	01-Oct-26 A	18-Oct-26	0.00	529,831.18	883,051.97	0%	60%	50
Pumps		6	04-Jan-27	10-Jan-27	23-Sep-26 A	25-Oct-26	0.00	35,006.70	233,378.02	0%	15%	66
JDH4-02-007-	Installation of Submersible pump [Se	6	04-Jan-27	10-Jan-27	23-Sep-26 A	25-Oct-26	0.00	35,006.70	233,378.02	0%	15%	66
Electrical Works		141	12-Dec-26	02-May-27	17-Sep-26 A	03-Jan-27	0.00	263,571.46	708,268.64	0%	37.21%	98
Main Distribution Board		14	12-Dec-26	27-Dec-26	03-Oct-26 A	29-Oct-26	0.00	52,036.99	104,073.98	0%	50%	50
JDH4-02-007-	Installation of Panel Board [Sewage I	7	20-Dec-26	27-Dec-26	03-Oct-26 A	29-Oct-26	0.00	14,191.91	28,383.81	0%	50%	50
JDH4-02-007-	Installation of Main Distribution Board	7	12-Dec-26	19-Dec-26	03-Oct-26 A	21-Oct-26	0.00	37,845.09	75,690.17	0%	50%	50
Local Control Panel		25	20-Dec-26	27-Jan-27	04-Oct-26 A	14-Nov-26	0.00	53,613.87	107,227.74	0%	50%	64
JDH4-02-007-	Installation of MCP-LP-01 [Sewage L	10	20-Dec-26	30-Dec-26	04-Oct-26 A	02-Nov-26	0.00	12,615.03	25,230.06	0%	50%	50
JDH4-02-007-	Installation of FP-CP [Sewage Lift Sta	5	23-Jan-27	27-Jan-27	04-Oct-26 A	14-Nov-26	0.00	14,191.91	28,383.81	0%	50%	64
JDH4-02-007-	Installation of OD-CP [Sewage Lift St	5	06-Jan-27	11-Jan-27	04-Oct-26 A	09-Nov-26	0.00	14,191.91	28,383.81	0%	50%	55
JDH4-02-007-	Installation of MCP-LP-02 [Sewage L	5	31-Dec-26	05-Jan-27	04-Oct-26 A	08-Nov-26	0.00	12,615.03	25,230.06	0%	50%	50
Power Factor Correction Capacitor Bank		7	12-Jan-27	19-Jan-27	05-Oct-26 A	10-Nov-26	0.00	11,038.15	22,076.30	0%	50%	60
JDH4-02-007-	Installation of Power Factor Correctio	7	12-Jan-27	19-Jan-27	05-Oct-26 A	10-Nov-26	0.00	11,038.15	22,076.30	0%	50%	60
Low-Voltage Electrical Power Conductors and Cable		9	20-Jan-27	30-Jan-27	29-Sep-26 A	21-Nov-26	0.00	5,260.56	17,535.20	0%	30%	60
JDH4-02-007-	Installation of Low Voltage Cables [Se	9	20-Jan-27	30-Jan-27	29-Sep-26 A	21-Nov-26	0.00	5,260.56	17,535.20	0%	30%	60
ICT (Data& telephone System)		10	08-Feb-27	18-Feb-27	05-Oct-26 A	02-Dec-26	0.00	11,038.15	22,076.30	0%	50%	67
JDH4-02-007-	Installation of IDF Cabinet 9U (for dat	10	08-Feb-27	18-Feb-27	05-Oct-26 A	02-Dec-26	0.00	11,038.15	22,076.30	0%	50%	67
Programmable Logic Controllers		14	31-Mar-27	15-Apr-27	04-Oct-26 A	24-Dec-26	0.00	75,690.17	252,300.56	0%	30%	92
JDH4-02-007-	Installation of Programmable Logic C	14	31-Mar-27	15-Apr-27	04-Oct-26 A	24-Dec-26	0.00	75,690.17	252,300.56	0%	30%	92
Instrumentation for Process Systems		8	21-Apr-27	02-May-27	17-Sep-26 A	03-Jan-27	0.00	54,893.57	182,978.56	0%	30%	98
JDH4-02-007-	Installation of Process System [Sewa	8	21-Apr-27	02-May-27	17-Sep-26 A	03-Jan-27	0.00	54,893.57	182,978.56	0%	30%	98
Plot Backfilling 2		20	14-Jan-27	06-Feb-27	25-Jul-26 A	26-Oct-26	0.00	1,469,876.05	2,027,415.24	0%	72.5%	88
JDH4-02-007-CI	Plots backfilling Stage 7 [Plots]	10	26-Jan-27	06-Feb-27	30-Jul-26 A	26-Oct-26	0.00	608,224.57	1,013,707.62	0%	60%	88
JDH4-02-007-CI	Plots backfilling Stage 6 [Plots]	10	14-Jan-27	25-Jan-27	25-Jul-26 A	20-Oct-26	0.00	861,651.48	1,013,707.62	0%	85%	84
Additional Works		30	25-Mar-27	24-Apr-27	16-May-26 A	01-Nov-26	0.00	1,944,322.81	2,287,438.60	0%	85%	146
JDH4-02-007-CI	Road Work	25	27-Mar-27	24-Apr-27	16-May-26 A	26-Oct-26	0.00	972,161.40	1,143,719.30	0%	85%	151
JDH4-02-007-CI	Electrical Works	25	25-Mar-27	22-Apr-27	28-Jun-26 A	01-Nov-26	0.00	972,161.40	1,143,719.30	0%	85%	145
Testing & Commissioning		78	20-Dec-26	05-May-27	09-Jun-26 A	06-Jan-27	0.00	777,701.86	2,455,900.62	0%	31.67%	98
JDH4-02-007-TC	Test for Road Works	3	30-Mar-27	01-Apr-27	09-Jun-26 A	04-Nov-26	0.00	450,248.45	818,633.54	0%	55%	123

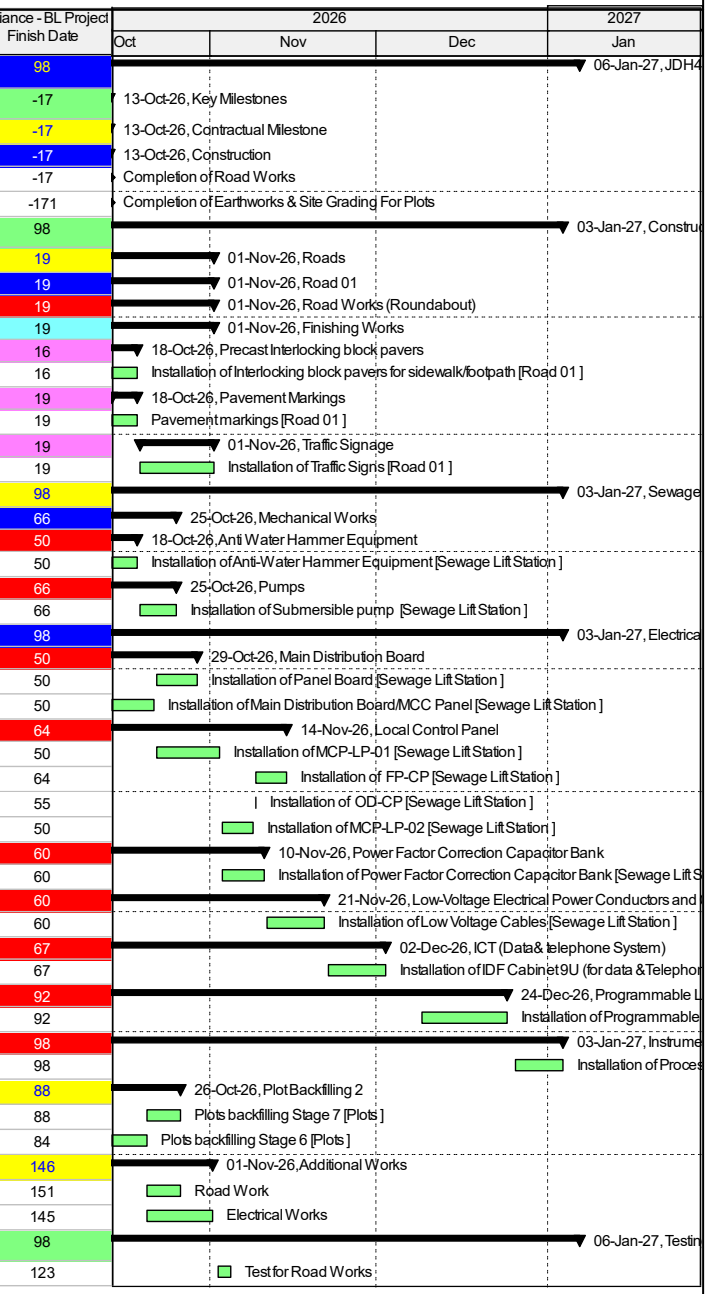

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved

egis ENJAZCO شركة الانجاز للتجارة والمقاولات AL Enjaz Company For Trading And Contracting

JDH4-02-007-R-UP-Land Development of Jeddah Oasis- 13 Oct 2026
2 Week Look Ahead

MODON

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Finish Date
JDH4-02-007-TC·	Test for Sewage Lift Station	3	03-May-27	05-May-27	17-Jun-26 A	06-Jan-27	0.00	163,726.71	818,633.54	0%	20%	98
JDH4-02-007-TC·	Test for Electrical Network	3	20-Dec-26	22-Dec-26	08-Sep-26 A	04-Nov-26	0.00	163,726.71	818,633.54	0%	20%	41

2026			2027
Oct	Nov	Dec	Jan
	Test for Electrical Network		Test for Sewage L

Actual Work
Remaining Work
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
