3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Total		185.89	1549	21-May-26	17-Dec-26	21-May-26 A	13-Jan-27	62,933,859.68
Development of Infrastructure for phase 1 of the Logistics area - Acceleration Pl		185.89	1549	21-May-26	17-Dec-26	21-May-26 A	13-Jan-27	62,933,859.68
Milestones		2.00	2	05-Oct-26	09-Nov-26	22-Nov-26	24-Nov-26	0.00
Contractual Milestones		0.00	1	05-Oct-26	05-Oct-26	22-Nov-26	22-Nov-26	0.00
DMM-Mil-4	Engineering - Finish	0.00	1		05-Oct-26		22-Nov-26	0.00
Control Milestones		0.00	1	09-Nov-26	09-Nov-26	24-Nov-26	24-Nov-26	0.00
Zonewise Milestones		0.00	1	09-Nov-26	09-Nov-26	24-Nov-26	24-Nov-26	0.00
DMM-Mil-13	Zone 01 - Finish	0.00	1		09-Nov-26		24-Nov-26	0.00
Engineering		16.00	23	16-Sep-26	05-Oct-26	04-Nov-26	22-Nov-26	0.00
Prequalifications & Materials Submissions		16.00	23	16-Sep-26	05-Oct-26	04-Nov-26	22-Nov-26	0.00
Submittals		6.00	8	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
Wet Networks & Stations		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Potable Water Pump Station		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Mechanical		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
DMM2-Eng-PQ-0127	Prepare & Submit for Hose Bibb Materials	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Guard Rooms		6.00	7	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
Mechanical		6.00	5	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-044	Prepare & Submit for Clean out Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Eng-PQ-046	Prepare & Submit for Electrical Water Heater Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Eng-PQ-048	Prepare & Submit for Shower Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Eng-PQ-049	Prepare & Submit for Toilet Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Eng-PQ-050	Prepare & Submit for Semi Pedestal Sink Materials	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	0.00
Electrical		2.00	2	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Eng-PQ-062	Prepare & Submit for PC Workstation Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Eng-PQ-063	Prepare & Submit for 50 inch Screen Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
Approvals		16.00	15	16-Sep-26	05-Oct-26	04-Nov-26	22-Nov-26	0.00
Wet Networks & Stations		3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	0.00
Potable Water Pump Station		3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	0.00
Mechanical		3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-578	Review & Approval for Hose Bibb Materials	3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	0.00
Guard Rooms		16.00	14	16-Sep-26	05-Oct-26	04-Nov-26	22-Nov-26	0.00
Mechanical		14.00	7	19-Sep-26	05-Oct-26	07-Nov-26	22-Nov-26	0.00
DMM2-Eng-PQ-1408	Review & Approval for DX Wall Mounted Split/AC Materials	6.00	1	19-Sep-26	26-Sep-26	07-Nov-26	12-Nov-26	0.00
DMM2-Eng-PQ-1428	Review & Approval for Clean out Materials	4.00	1	19-Sep-26	22-Sep-26	07-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-1468	Review & Approval for Shower Materials	6.00	1	19-Sep-26	26-Sep-26	07-Nov-26	12-Nov-26	0.00
DMM2-Eng-PQ-1478	Review & Approval for Toilet Materials	6.00	1	21-Sep-26	28-Sep-26	09-Nov-26	15-Nov-26	0.00
DMM2-Eng-PQ-1438	Review & Approval for Floor Drain Materials	4.00	1	24-Sep-26	28-Sep-26	11-Nov-26	15-Nov-26	0.00
DMM2-Eng-PQ-1488	Review & Approval for Semi Pedestal Sink Materials	6.00	1	24-Sep-26	30-Sep-26	11-Nov-26	17-Nov-26	0.00
DMM2-Eng-PQ-1448	Review & Approval for Electrical Water Heater Materials	6.00	1	29-Sep-26	05-Oct-26	16-Nov-26	22-Nov-26	0.00
Electrical		8.00	7	16-Sep-26	26-Sep-26	04-Nov-26	12-Nov-26	0.00
DMM2-Eng-PQ-1538	Review & Approval for Wiring Devices Materials	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-1548	Review & Approval for Ground Wires, Rods, Pits, Clamping Materials	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-1578	Review & Approval for Data and Voice System Materials	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-1588	Review & Approval for Data Cabinet Materials	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Eng-PQ-1598	Review & Approval for Data/ Voice RJ45 Outlet Materials	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00



Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Eng-PQ-1608	Review & Approval for PC Workstation Materials	6.00	1	19-Sep-26	26-Sep-26	07-Nov-26	12-Nov-26	0.00
DMM2-Eng-PQ-1618	Review & Approval for 50 inch Screen Materials	6.00	1	19-Sep-26	26-Sep-26	07-Nov-26	12-Nov-26	0.00
Procurement		89.00	258	16-Sep-26	09-Dec-26	22-Aug-26 A	24-Nov-26	0.00
PR & PO		18.00	61	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	0.00
Earth & Road Works		18.00	3	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	0.00
DMM2-Proc-PO-09	PR & PO for Traffic Signs Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-07	PR & PO for Pavement Markings Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-010	PR & PO for ground Mounted Information Signs Materials	2.00	1	06-Oct-26	07-Oct-26	23-Nov-26	24-Nov-26	0.00
Wet Networks & Stations		14.00	25	16-Sep-26	03-Oct-26	04-Nov-26	19-Nov-26	0.00
Sewerage Network		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-019	PR & PO for Discharge Chamber Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
Potable Water Pump Station		14.00	18	16-Sep-26	03-Oct-26	04-Nov-26	19-Nov-26	0.00
Civil & Architecture		8.00	6	16-Sep-26	26-Sep-26	04-Nov-26	12-Nov-26	0.00
DMM2-Proc-PO-030	PR & PO for Stairs Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-035	PR & PO for Gravel Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-032	PR & PO for Stainless Steel Ladder Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-034	PR & PO for Metal Railing Materials	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	0.00
DMM2-Proc-PO-036	PR & PO for Handrail Materials	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	0.00
DMM2-Proc-PO-033	PR & PO for Steel shutter Door Materials	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	0.00
Mechanical		14.00	11	16-Sep-26	03-Oct-26	04-Nov-26	19-Nov-26	0.00
DMM2-Proc-PO-042	PR & PO for Sand Trap Louver Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-188	PR & PO for Fans Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-198	PR & PO for Louvers Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-050	PR & PO for Trench Drain Materials	2.00	1	22-Sep-26	24-Sep-26	04-Nov-26	07-Nov-26	0.00
DMM2-Proc-PO-041	PR & PO for Strainers Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-045	PR & PO for Exhaust Fans Materials	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	0.00
DMM2-Proc-PO-044	PR & PO for Hose Bibb Materials	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	0.00
DMM2-Proc-PO-046	PR & PO for Chlorine Cylinder Racks Materials	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	0.00
DMM2-Proc-PO-047	PR & PO for Chlorinators Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-048	PR & PO for Discharge Line Analyzer Materials	2.00	1	29-Sep-26	30-Sep-26	16-Nov-26	17-Nov-26	0.00
DMM2-Proc-PO-049	PR & PO for Emergency shower Materials	2.00	1	01-Oct-26	03-Oct-26	18-Nov-26	19-Nov-26	0.00
Electrical		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-051	PR & PO for Switches and Circuit Breakers Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
Sewer Lift Station		6.00	6	16-Sep-26	28-Sep-26	04-Nov-26	10-Nov-26	0.00
Civil & Architecture		6.00	4	16-Sep-26	28-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Proc-PO-052	PR & PO for Metal Ladders Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-054	PR & PO for Internal painting (Acrylic) Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-055	PR & PO for Signages Materials	2.00	1	24-Sep-26	26-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-053	PR & PO for Metal Covers Materials	2.00	1	27-Sep-26	28-Sep-26	09-Nov-26	10-Nov-26	0.00
Mechanical		2.00	1	19-Sep-26	20-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-067	PR & PO for Scupper Materials	2.00	1	19-Sep-26	20-Sep-26	04-Nov-26	05-Nov-26	0.00
Electrical		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-078	PR & PO for Surfaced Mounted Light (LED) Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
Landscape Works		2.00	4	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0103	PR & PO for Fences (ZATCA HCIS) Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0104	PR & PO Prepare & Submit for Fences (MODON) Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00

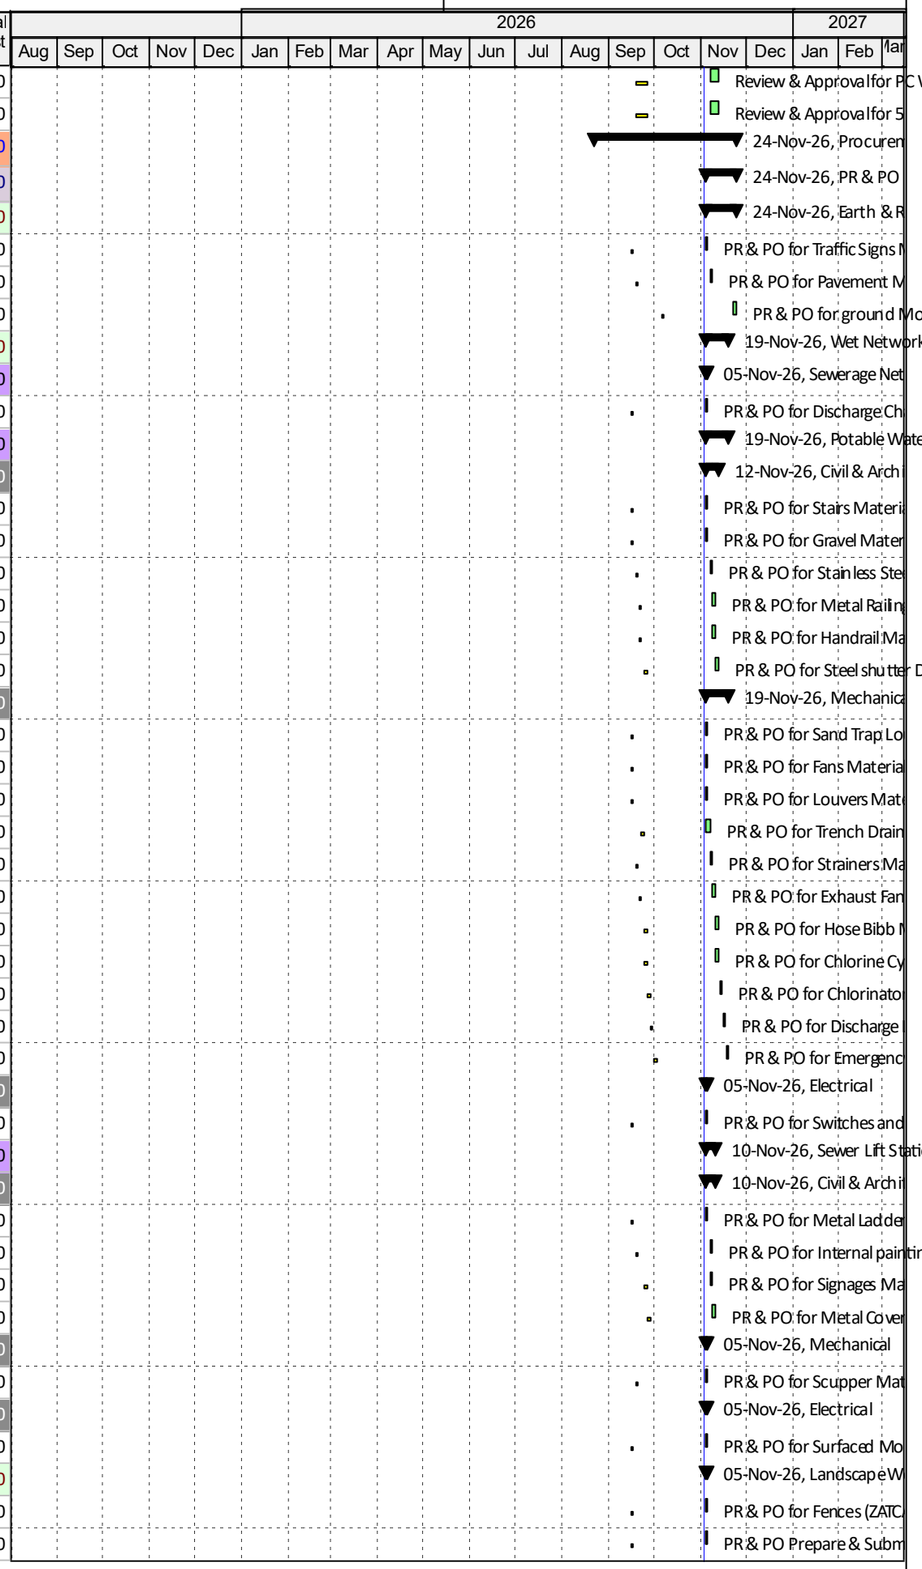

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Proc-PO-0105	PR & PO for Vehicle Steel Gate Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0106	PR & PO for Vehicle and Pedestrian Steel Gate Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
Guard Rooms		18.00	29	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	0.00
Civil & Architecture		6.00	11	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	0.00
DMM2-Proc-PO-0108	PR & PO for Stone Coping Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0114	PR & PO for Fluid-Applied Water Proofing Paint Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0117	PR & PO for Porcelain Flooring Tiles Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0118	PR & PO for gypsum Board Suspended Ceiling Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0119	PR & PO for Painting Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0120	PR & PO for Raised Floor System Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0121	PR & PO for Steel Doors Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0122	PR & PO for Wood Doors Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0123	PR & PO for Aluminum Windows Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0111	PR & PO for Reinforced Concrete Materials	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	0.00
DMM2-Proc-PO-0113	PR & PO for Board Insulation Materials	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	0.00
Mechanical		18.00	9	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	0.00
DMM2-Proc-PO-0124	PR & PO for Exhaust Axial Fans Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0126	PR & PO for PPR Pipes Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0128	PR & PO for Scupper Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0129	PR & PO for Clean out Materials	1.00	1	24-Sep-26	24-Sep-26	11-Nov-26	11-Nov-26	0.00
DMM2-Proc-PO-0127	PR & PO for DX Wall Mounted Split/AC Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-0133	PR & PO for Shower Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-0134	PR & PO for Toilet Materials	2.00	1	29-Sep-26	30-Sep-26	16-Nov-26	17-Nov-26	0.00
DMM2-Proc-PO-0135	PR & PO for Semi Pedestal Sink Materials	2.00	1	01-Oct-26	03-Oct-26	18-Nov-26	19-Nov-26	0.00
DMM2-Proc-PO-0131	PR & PO for Electrical Water Heater Materials	2.00	1	06-Oct-26	07-Oct-26	23-Nov-26	24-Nov-26	0.00
Electrical		10.00	9	16-Sep-26	28-Sep-26	04-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-0137	PR & PO for Panelboards Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0139	PR & PO for Lighting Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0142	PR & PO for Enclosed Switches and Circuit Breakers Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0143	PR & PO for Fire Alarm System Materials	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	0.00
DMM2-Proc-PO-0140	PR & PO for Wiring Devices Materials	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	0.00
DMM2-Proc-PO-0145	PR & PO for Data Cabinet Materials	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	0.00
DMM2-Proc-PO-0146	PR & PO for Data/ Voice RJ45 Outlet Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-0147	PR & PO for PC Workstation Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
DMM2-Proc-PO-0148	PR & PO for 50 inch Screen Materials	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	0.00
Manufacturing & Delivery		89.00	197	16-Sep-26	09-Dec-26	22-Aug-26 A	24-Nov-26	0.00
Long Lead Items		59.00	53	16-Sep-26	07-Nov-26	29-Aug-26 A	14-Nov-26	0.00
Zone 01		39.00	2	21-Sep-26	14-Oct-26	15-Sep-26 A	07-Nov-26	0.00
Wet Networks & Stations		20.00	1	21-Sep-26	14-Oct-26	15-Sep-26 A	05-Nov-26	0.00
TSE Network		20.00	1	21-Sep-26	14-Oct-26	15-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-64	Manuf. & Delivery for Solenoid Primary Control Valves Materials	20.00	1	21-Sep-26	14-Oct-26	15-Sep-26 A	05-Nov-26	0.00
Dry Networks		4.00	1	07-Oct-26	11-Oct-26	19-Sep-26 A	07-Nov-26	0.00
Street Lighting		4.00	1	07-Oct-26	11-Oct-26	19-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-13	Manuf. & Delivery for SL Luminares Materials(Rem)	4.00	1	07-Oct-26	11-Oct-26	19-Sep-26 A	07-Nov-26	0.00
Zone 02		59.00	19	16-Sep-26	07-Nov-26	29-Aug-26 A	08-Nov-26	0.00
Wet Networks & Stations		42.00	15	16-Sep-26	07-Nov-26	29-Aug-26 A	08-Nov-26	0.00

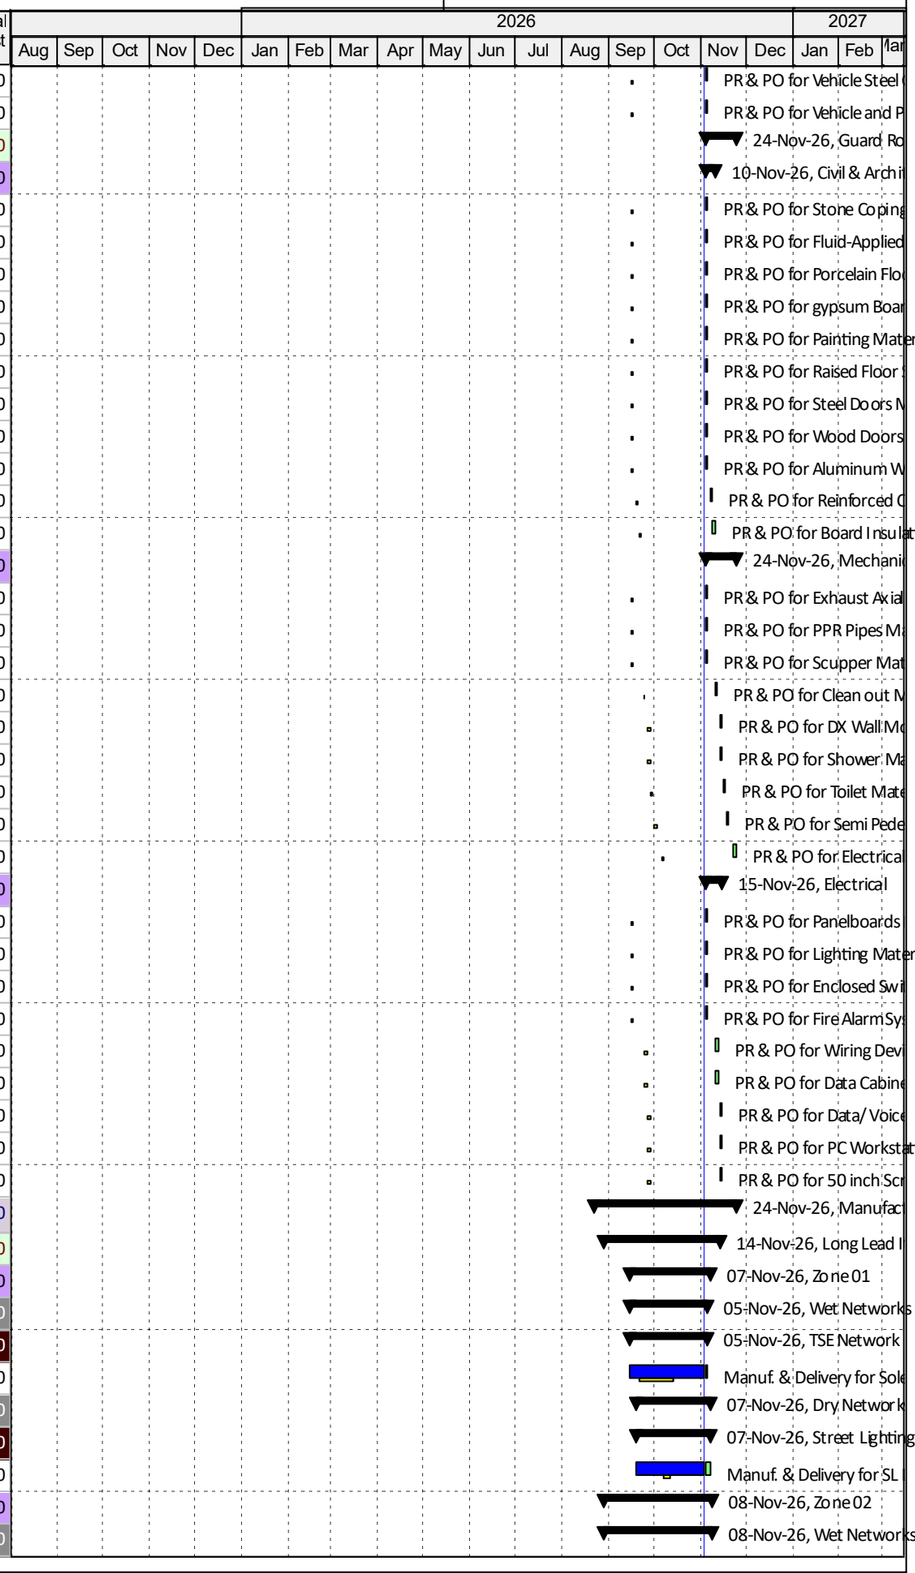

Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Potable Network		4.00	2	16-Sep-26	20-Sep-26	29-Aug-26 A	04-Nov-26	0.00
DMM2-Eng-PQ-050	Manuf. & Delivery for Flow Meter Materials	4.00	1	16-Sep-26	20-Sep-26	29-Aug-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-36	Manuf. & Delivery for Flow Meter Chamber Materials	4.00	1	16-Sep-26	20-Sep-26	10-Sep-26 A	04-Nov-26	0.00
TSE Network		20.00	1	15-Oct-26	07-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-23	Manuf. & Delivery for Solenoid Primary Control Valves Materials	20.00	1	15-Oct-26	07-Nov-26	25-Sep-26 A	07-Nov-26	0.00
Potable Water Pump Station		34.00	12	16-Sep-26	26-Oct-26	02-Sep-26 A	08-Nov-26	0.00
Mechanical		25.00	5	16-Sep-26	15-Oct-26	02-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Electromagnetic Flow Meters Materials(Rem)	14.00	1	16-Sep-26	03-Oct-26	02-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Surge Tank Materials	25.00	1	16-Sep-26	15-Oct-26	03-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-2	Manuf. & Delivery for Butterfly Valve Materials(Rem)	14.00	1	16-Sep-26	03-Oct-26	03-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for DI Pipes Materials(Rem)	6.00	1	16-Sep-26	22-Sep-26	17-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-2	Manuf. & Delivery for OverHead Crane Materials(Rem)	12.00	1	16-Sep-26	30-Sep-26	01-Oct-26 A	07-Nov-26	0.00
Electrical		34.00	7	16-Sep-26	26-Oct-26	12-Sep-26 A	08-Nov-26	0.00
DMM2-Proc-Delv-2	Manuf. & Delivery for LV Cables Materials(Rem)	5.00	1	16-Sep-26	21-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Automatic Transfer Switch ATS panel Materials	19.00	1	16-Sep-26	08-Oct-26	13-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Addressable Fire Alarm System Materials	25.00	1	16-Sep-26	15-Oct-26	15-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Motor Control Center (MCC) Materials(Rem)	9.00	1	16-Sep-26	27-Sep-26	17-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Local Control Panel Materials(Rem)	4.20	1	16-Sep-26	21-Sep-26	20-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for PLC System Materials(Rem)	12.00	1	16-Sep-26	30-Sep-26	20-Sep-26 A	08-Nov-26	0.00
DMM2-Proc-Delv-3	Manuf. & Delivery for Panelboards Materials	16.00	1	08-Oct-26	26-Oct-26	25-Sep-26 A	07-Nov-26	0.00
Dry Networks		37.00	4	16-Sep-26	11-Oct-26	06-Sep-26 A	07-Nov-26	0.00
Medium Voltage Network		10.00	2	16-Sep-26	28-Sep-26	06-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-29	Manuf. & Delivery for Unit Substation Materials(Rem)	10.00	1	16-Sep-26	28-Sep-26	06-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-29	Manuf. & Delivery for RMU Materials(Rem)	10.00	1	16-Sep-26	28-Sep-26	17-Sep-26 A	05-Nov-26	0.00
Street Lighting		37.00	2	16-Sep-26	11-Oct-26	12-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-30	Manuf. & Delivery for SL Pillars Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	12-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-30	Manuf. & Delivery for SL Luminares Materials(Rem)	4.00	1	07-Oct-26	11-Oct-26	22-Sep-26 A	07-Nov-26	0.00
Zone 03		42.00	24	16-Sep-26	07-Nov-26	29-Aug-26 A	12-Nov-26	0.00
Wet Networks & Stations		42.00	16	16-Sep-26	07-Nov-26	29-Aug-26 A	12-Nov-26	0.00
TSE Network		10.00	1	27-Oct-26	07-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-41	Manuf. & Delivery for Solenoid Primary Control Valves Materials	10.00	1	27-Oct-26	07-Nov-26	25-Sep-26 A	07-Nov-26	0.00
Sewer Lift Station		30.00	15	16-Sep-26	21-Oct-26	29-Aug-26 A	12-Nov-26	0.00
Mechanical		30.00	8	16-Sep-26	21-Oct-26	01-Sep-26 A	12-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Surge Tank Materials	30.00	1	16-Sep-26	21-Oct-26	01-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Basket Screens Materials	20.00	1	16-Sep-26	10-Oct-26	12-Sep-26 A	08-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Double Flanged DI Pipes Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	12-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Submersible Pumps Materials	13.00	1	27-Sep-26	11-Oct-26	13-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Non Return Valve (Flap) Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	13-Sep-26 A	10-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for JIB Crane Materials(Rem)	15.00	1	16-Sep-26	04-Oct-26	19-Sep-26 A	12-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Buried Flanged DI Pipes Materials	2.00	1	11-Oct-26	12-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Odor Control Unit Materials	3.00	1	11-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Electrical		24.00	7	16-Sep-26	14-Oct-26	29-Aug-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Low Voltage Cables Materials(Rem)	15.00	1	16-Sep-26	04-Oct-26	29-Aug-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Motor Control Center (MCC) Materials	3.00	1	19-Sep-26	21-Sep-26	02-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Automatic Transfer (Switch ATS) Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Fuel Pump Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	15-Sep-26 A	05-Nov-26	0.00

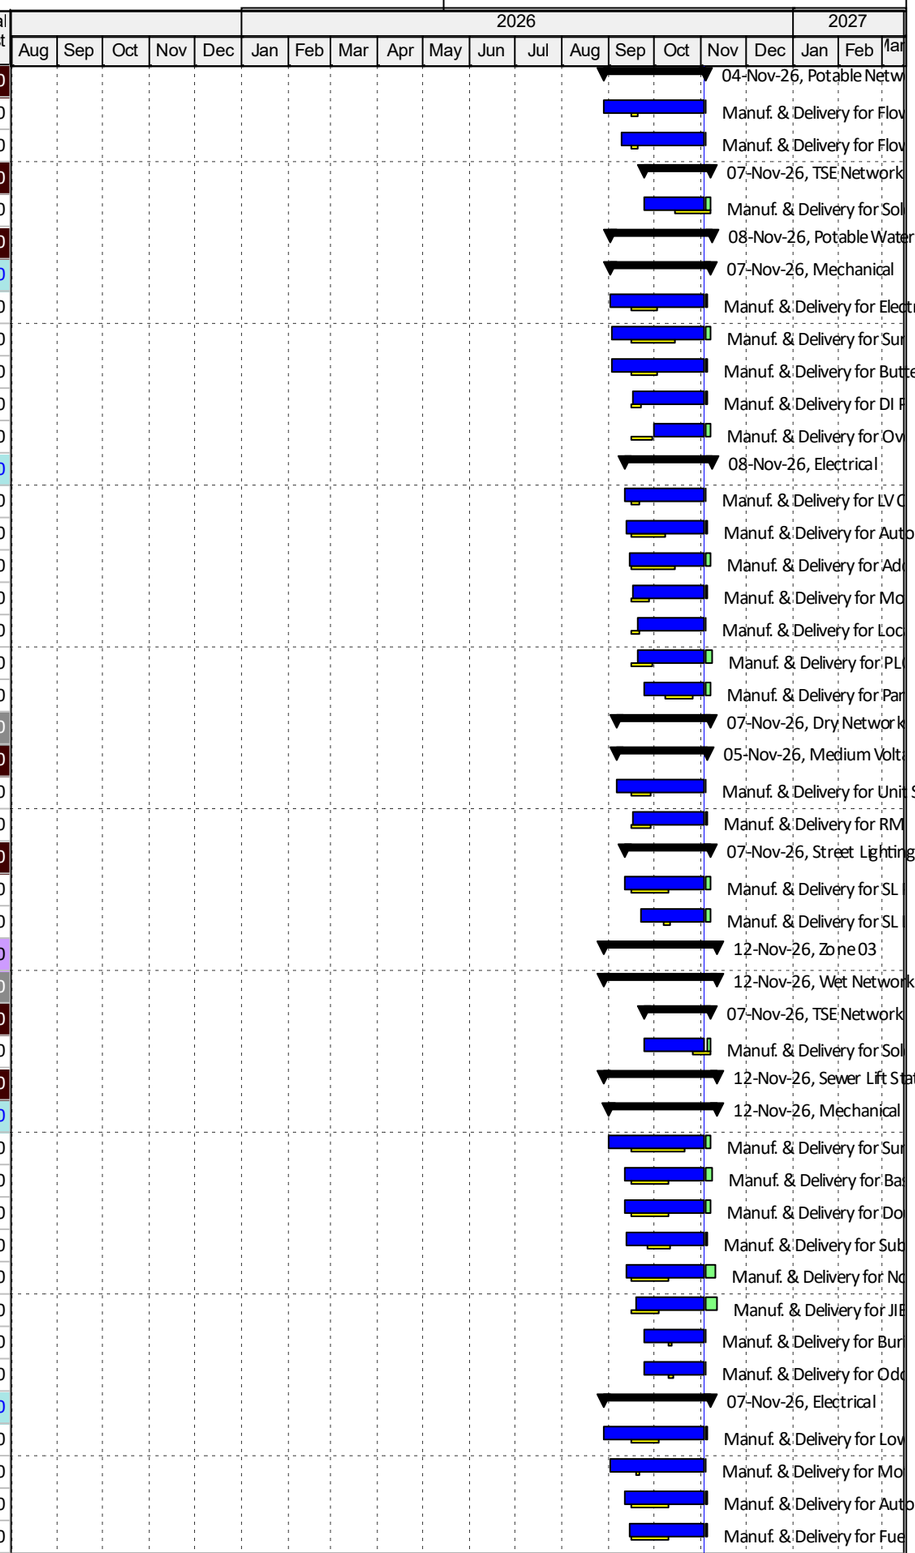

Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Proc-Delv-4	Manuf. & Delivery for Displacement Rotary Type Pump Materials(Rem)	24.00	1	16-Sep-26	14-Oct-26	19-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for PLC System Materials(Rem)	15.00	1	16-Sep-26	04-Oct-26	19-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-4	Manuf. & Delivery for Local Control Panel Materials	3.00	1	11-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Dry Networks		20.00	8	16-Sep-26	18-Oct-26	30-Aug-26 A	10-Nov-26	0.00
Medium Voltage Network		20.00	2	16-Sep-26	10-Oct-26	13-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for RMU Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	13-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for Unit Substation Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	14-Sep-26 A	05-Nov-26	0.00
Low Voltage Network		20.00	2	16-Sep-26	10-Oct-26	16-Sep-26 A	10-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for LV Pillars Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	16-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-71	Manuf. & Delivery for LV Panels Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	17-Sep-26 A	10-Nov-26	0.00
Street Lighting		20.00	4	16-Sep-26	18-Oct-26	30-Aug-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-48	Manuf. & Delivery for SL Luminares Materials(Rem)	10.00	1	07-Oct-26	18-Oct-26	30-Aug-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for SL Cables Materials(Rem)	10.00	1	16-Sep-26	28-Sep-26	13-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for SL Poles Materials(Rem)	10.00	1	16-Sep-26	28-Sep-26	19-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-47	Manuf. & Delivery for SL Pillars Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	21-Sep-26 A	05-Nov-26	0.00
Zone 04		30.00	8	16-Sep-26	21-Oct-26	02-Sep-26 A	14-Nov-26	0.00
Wet Networks & Stations		25.00	3	16-Sep-26	15-Oct-26	02-Sep-26 A	14-Nov-26	0.00
TSE Network		25.00	3	16-Sep-26	15-Oct-26	02-Sep-26 A	14-Nov-26	0.00
DMM2-Proc-Delv-58	Manuf. & Delivery for Valves Materials(Rem)	2.00	1	16-Sep-26	17-Sep-26	02-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-58	Manuf. & Delivery for HDPE Pipes Materials(Rem)	2.00	1	16-Sep-26	17-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-58	Manuf. & Delivery for Solenoid Primary Control Valves Materials	25.00	1	16-Sep-26	15-Oct-26	17-Sep-26 A	14-Nov-26	0.00
Dry Networks		30.00	5	16-Sep-26	21-Oct-26	12-Sep-26 A	10-Nov-26	0.00
Medium Voltage Network		30.00	2	16-Sep-26	21-Oct-26	12-Sep-26 A	10-Nov-26	0.00
DMM2-Proc-Delv-64	Manuf. & Delivery for Unit Substation Materials(Rem)	20.00	1	29-Sep-26	21-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-64	Manuf. & Delivery for RMU Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	19-Sep-26 A	10-Nov-26	0.00
Street Lighting		20.00	3	16-Sep-26	18-Oct-26	12-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-65	Manuf. & Delivery for SL Pillars Materials(Rem)	20.00	1	16-Sep-26	10-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-65	Manuf. & Delivery for SL Poles Materials(Rem)	10.00	1	16-Sep-26	28-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-65	Manuf. & Delivery for SL Luminares Materials(Rem)	10.00	1	07-Oct-26	18-Oct-26	17-Sep-26 A	07-Nov-26	0.00
Short Lead Items		89.00	144	16-Sep-26	09-Dec-26	22-Aug-26 A	24-Nov-26	0.00
Zone 01		89.00	25	16-Sep-26	09-Dec-26	22-Aug-26 A	24-Nov-26	0.00
Earth & Road Works		50.50	8	16-Sep-26	03-Nov-26	01-Sep-26 A	24-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Pavement Markings Materials	10.00	1	05-Oct-26	15-Oct-26	01-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Curbstone Materials(Rem)	13.00	1	19-Sep-26	04-Oct-26	19-Sep-26 A	12-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Wheels Stopper (precast concrete) Materials	2.00	1	02-Nov-26	03-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Traffic Signs Materials	10.00	1	17-Oct-26	27-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for ground Mounted Information Signs Materials	10.00	1	08-Oct-26	19-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Agg. Base Coarse(Rem)	31.00	1	16-Sep-26	22-Oct-26	27-Sep-26 A	22-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Asphalt Materials(Rem)	35.00	1	16-Sep-26	27-Oct-26	29-Sep-26 A	24-Nov-26	0.00
DMM2-Proc-Delv-72C	Manuf. & Delivery for Interlock Materials	15.00	1	16-Sep-26	04-Oct-26	30-Sep-26 A	12-Nov-26	0.00
Wet Networks & Stations		15.00	4	01-Oct-26	18-Oct-26	22-Aug-26 A	09-Nov-26	0.00
TSE Network		15.00	4	01-Oct-26	18-Oct-26	22-Aug-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for Bubbler Materials	15.00	1	01-Oct-26	18-Oct-26	22-Aug-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for Pull Box Materials	15.00	1	01-Oct-26	18-Oct-26	26-Aug-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for Dripper Materials	15.00	1	01-Oct-26	18-Oct-26	29-Aug-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for Two Wire Decoder Cable 12 awgMaterials	15.00	1	01-Oct-26	18-Oct-26	12-Sep-26 A	09-Nov-26	0.00

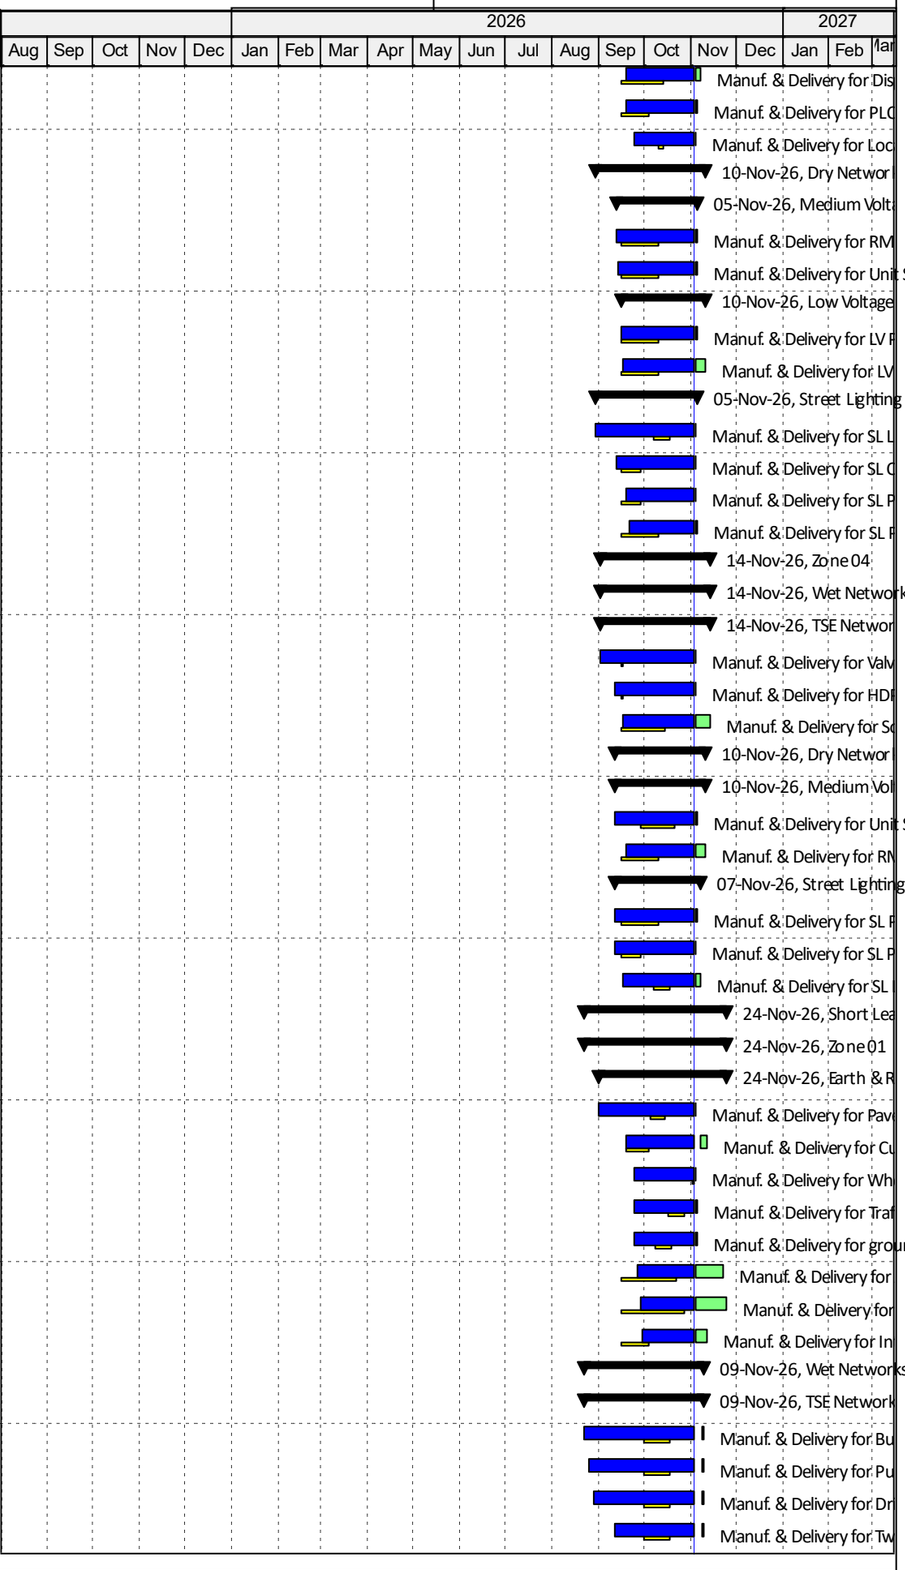

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Dry Networks		8.00	2	29-Sep-26	07-Oct-26	27-Aug-26 A	04-Nov-26	0.00
Street Lighting		8.00	2	29-Sep-26	07-Oct-26	27-Aug-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for SL Earthing Materials	5.00	1	29-Sep-26	04-Oct-26	27-Aug-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-72	Manuf. & Delivery for SL Drawpits Materials	4.00	1	04-Oct-26	07-Oct-26	29-Aug-26 A	04-Nov-26	0.00
Landscape Works		72.00	11	16-Sep-26	09-Dec-26	27-Aug-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Trees Materials	30.00	1	16-Sep-26	21-Oct-26	27-Aug-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Gravel/Stone Mulch Materials	20.00	1	16-Sep-26	10-Oct-26	02-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-725	Manuf. & Delivery for Vehicle and Pedestrian Steel Gate Materials	30.00	1	19-Sep-26	24-Oct-26	02-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Large Shrubs Materials	12.00	1	16-Sep-26	30-Sep-26	12-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Geotextile Layers Materials	30.00	1	16-Sep-26	21-Oct-26	13-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Ornamental Grasses Materials	10.00	1	29-Nov-26	09-Dec-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Plastic edge Materials	10.00	1	31-Oct-26	10-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Plants Materials	15.00	1	11-Nov-26	28-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-724	Manuf. & Delivery for Fences (ZATCA HCIS) Materials	10.00	1	17-Nov-26	28-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-725	Manuf. & Delivery Prepare & Submit for Fences (MODON) Materials	10.00	1	05-Nov-26	16-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-725	Manuf. & Delivery for Vehicle Steel Gate Materials	10.00	1	25-Oct-26	04-Nov-26	25-Sep-26 A	05-Nov-26	0.00
Zone 02		84.00	78	16-Sep-26	03-Dec-26	29-Aug-26 A	24-Nov-26	0.00
Earth & Road Works		55.00	8	16-Sep-26	08-Nov-26	17-Sep-26 A	24-Nov-26	0.00
DMM2-Proc-Delv-726	Manuf. & Delivery for Asphalt Materials	10.00	1	17-Oct-26	27-Oct-26	17-Sep-26 A	24-Nov-26	0.00
DMM2-Proc-Delv-726	Manuf. & Delivery for Agg. Base Coarse(Rem)	7.00	1	16-Sep-26	24-Sep-26	23-Sep-26 A	08-Nov-26	0.00
DMM2-Proc-Delv-726	Manuf. & Delivery for Pavement Markings Materials	10.00	1	17-Oct-26	27-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-727	Manuf. & Delivery for Wheels Stopper (precast concrete) Materials	2.00	1	02-Nov-26	03-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-727	Manuf. & Delivery for Traffic Signs Materials	10.00	1	28-Oct-26	08-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-727	Manuf. & Delivery for ground Mounted Information Signs Materials	10.00	1	20-Oct-26	31-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-726	Manuf. & Delivery for Curbstone Materials	8.00	1	05-Oct-26	13-Oct-26	05-Oct-26 A	08-Nov-26	0.00
DMM2-Proc-Delv-726	Manuf. & Delivery for Interlock Materials	15.00	1	05-Oct-26	21-Oct-26	05-Oct-26 A	12-Nov-26	0.00
Wet Networks & Stations		37.00	23	19-Sep-26	01-Nov-26	29-Aug-26 A	09-Nov-26	0.00
TSE Network		10.00	4	07-Oct-26	18-Oct-26	25-Sep-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Dripper Materials	7.00	1	11-Oct-26	18-Oct-26	25-Sep-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Bubbler Materials	7.00	1	11-Oct-26	18-Oct-26	25-Sep-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Pull Box Materials	10.00	1	07-Oct-26	18-Oct-26	25-Sep-26 A	09-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Two Wire Decoder Cable 12 awg Materials	10.00	1	07-Oct-26	18-Oct-26	25-Sep-26 A	09-Nov-26	0.00
Potable Water Pump Station		37.00	19	19-Sep-26	01-Nov-26	29-Aug-26 A	07-Nov-26	0.00
Civil & Architecture		27.00	6	19-Sep-26	20-Oct-26	09-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Steelshutter Door Materials	15.00	1	04-Oct-26	20-Oct-26	09-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Handrail Materials	15.00	1	24-Sep-26	11-Oct-26	13-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Stairs Materials	8.00	1	04-Oct-26	12-Oct-26	14-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Stainless Steel Ladder Materials	15.00	1	22-Sep-26	10-Oct-26	14-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Gravel Materials	2.00	1	19-Sep-26	20-Sep-26	15-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Metal Railing Materials	8.00	1	12-Oct-26	20-Oct-26	25-Sep-26 A	05-Nov-26	0.00
Mechanical		37.00	12	19-Sep-26	01-Nov-26	29-Aug-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Sand Trap Louver Materials	10.00	1	19-Sep-26	30-Sep-26	29-Aug-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Fans Materials	10.00	1	19-Sep-26	30-Sep-26	05-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Trench Drain Materials	6.00	1	26-Sep-26	01-Oct-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Emergency shower Materials	10.00	1	04-Oct-26	14-Oct-26	08-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Hose Bibb Materials	10.00	1	27-Sep-26	07-Oct-26	10-Sep-26 A	04-Nov-26	0.00

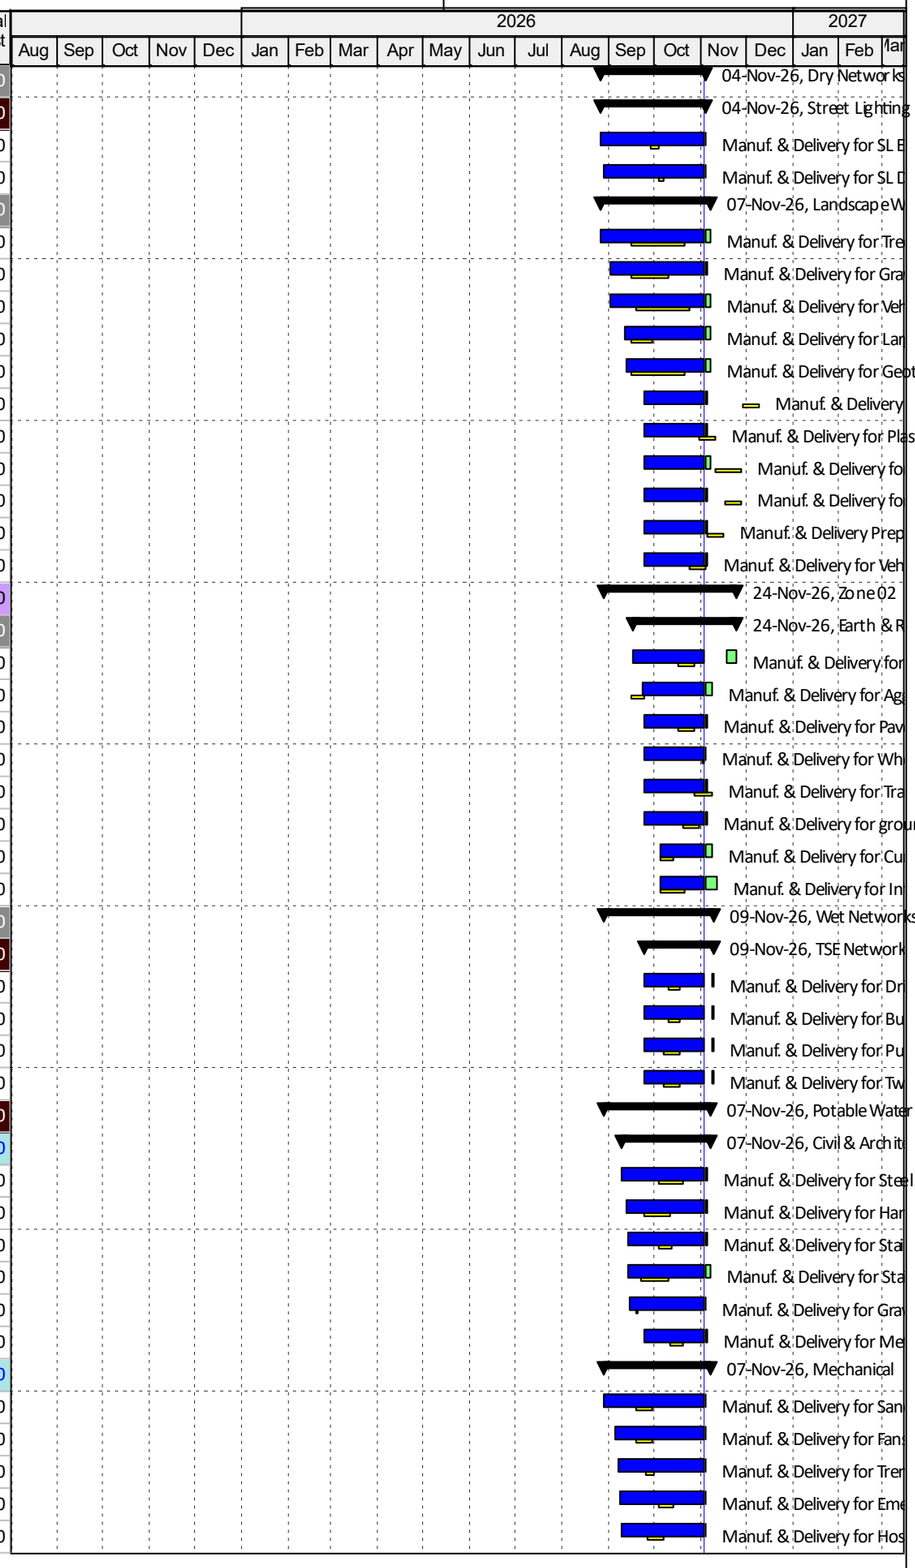


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Proc-Delv-7.	Manuf. & Delivery for Chlorinators Materials	8.00	1	29-Sep-26	07-Oct-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Discharge Line Analyzer Materials	9.00	1	01-Oct-26	11-Oct-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Louvers Materials	15.00	1	01-Oct-26	18-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Chlorine Cylinder Racks Materials	20.00	1	27-Sep-26	19-Oct-26	14-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for FM200 Supression System Materials	15.00	1	04-Oct-26	20-Oct-26	21-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Strainers Materials	10.00	1	21-Oct-26	01-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Exhaust Fans Materials	10.00	1	12-Oct-26	22-Oct-26	25-Sep-26 A	05-Nov-26	0.00
Electrical		5.00	1	19-Oct-26	24-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7.	Manuf. & Delivery for Switches and Circuit Breakers Materials	5.00	1	19-Oct-26	24-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Landscape Works		55.00	11	01-Oct-26	03-Dec-26	07-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Large Shrubs Materials	3.00	1	01-Oct-26	04-Oct-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-732	Manuf. & Delivery for Trees Materials	15.00	1	22-Oct-26	08-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-732	Manuf. & Delivery for Ornamental Grasses Materials	3.00	1	29-Nov-26	01-Dec-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Geotextile Layers Materials	10.00	1	22-Oct-26	02-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Plastic edge Materials	10.00	1	11-Nov-26	22-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Plants Materials	5.00	1	29-Nov-26	03-Dec-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Gravel/Stone Mulch Materials	7.00	1	22-Oct-26	29-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Fences (ZATCA HCIS) Materials	15.00	1	17-Nov-26	03-Dec-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Fences (MODON) Materials	15.00	1	17-Nov-26	03-Dec-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Vehicle Steel Gate Materials	10.00	1	05-Nov-26	16-Nov-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-733	Manuf. & Delivery for Vehicle and Pedestrian Steel Gate Materials	10.00	1	25-Oct-26	04-Nov-26	25-Sep-26 A	05-Nov-26	0.00
Guard Rooms		35.00	36	16-Sep-26	27-Oct-26	03-Sep-26 A	05-Nov-26	0.00
Civil & Architecture		27.00	13	16-Sep-26	18-Oct-26	07-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for gypsum Board Suspended Ceiling Materials	3.00	1	07-Oct-26	10-Oct-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Concrete Masonry Materials	5.00	1	22-Sep-26	28-Sep-26	09-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Fluid-Applied Water Proofing Paint Materials	3.00	1	19-Sep-26	21-Sep-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Stone Coping Materials	3.00	1	07-Oct-26	10-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Board Insulation Materials	7.00	1	29-Sep-26	06-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Porcelain Flooring Tiles Materials	15.00	1	19-Sep-26	06-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Raised Floor System Materials	3.00	1	07-Oct-26	10-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Aluminum Windows Materials	3.00	1	07-Oct-26	10-Oct-26	13-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Water proofing Membrane Materials	5.00	1	16-Sep-26	21-Sep-26	19-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Vapor Retarders Materials	5.00	1	07-Oct-26	12-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Painting Materials	2.00	1	11-Oct-26	12-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for SteelDoors Materials	5.00	1	07-Oct-26	12-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Wood Doors Materials	5.00	1	13-Oct-26	18-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Mechanical		27.00	12	16-Sep-26	22-Oct-26	08-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for uPVC Pipes Materials	2.00	1	16-Sep-26	17-Sep-26	08-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Scupper Materials	3.00	1	19-Sep-26	21-Sep-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Toilet Materials	3.00	1	01-Oct-26	04-Oct-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for PPR Pipes Materials	3.00	1	19-Sep-26	21-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Clean out Materials	1.00	1	26-Sep-26	26-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Floor Drain Materials	2.00	1	22-Sep-26	24-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Shower Materials	2.00	1	05-Oct-26	06-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Exhaust Axial Fans Materials	3.00	1	11-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for DX Wall Mounted Split/AC Materials	2.00	1	21-Oct-26	22-Oct-26	25-Sep-26 A	04-Nov-26	0.00

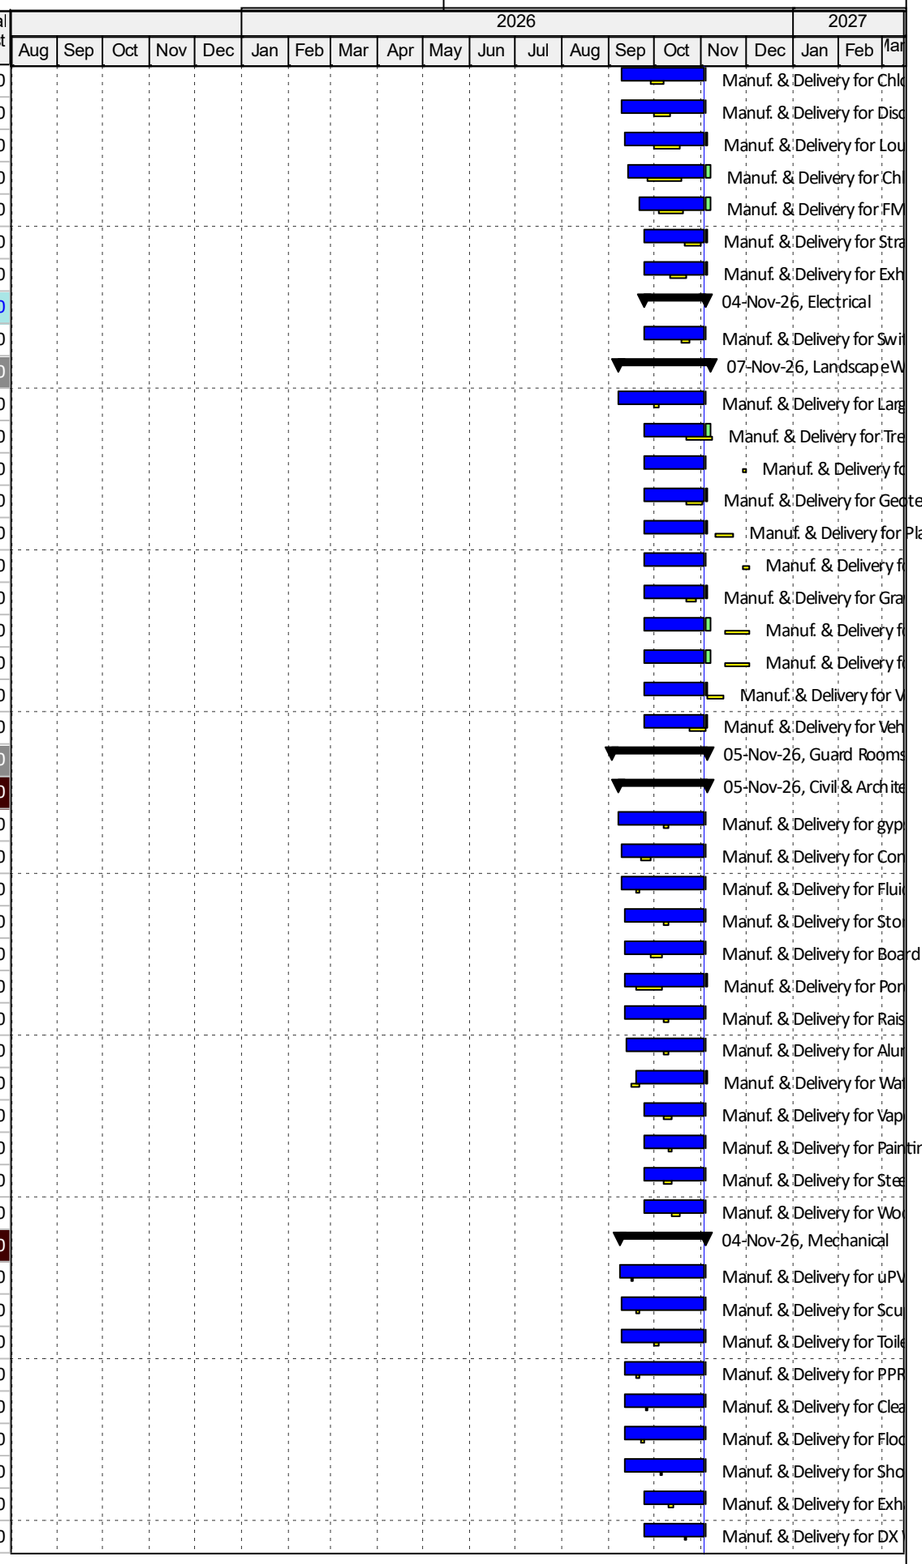


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Proc-Delv-73	Manuf. & Delivery for Electrical Water Heater Materials	5.00	1	15-Oct-26	20-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Semi Pedestal Sink Materials	2.00	1	05-Oct-26	06-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Fire Extinguishers (CO2 & Powder) Materials	3.00	1	12-Oct-26	14-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Electrical		33.00	11	19-Sep-26	27-Oct-26	03-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for PC Workstation Materials	2.00	1	04-Oct-26	05-Oct-26	03-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Wiring Devices Materials	4.00	1	29-Sep-26	03-Oct-26	09-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Fire Alarm System Materials	4.00	1	07-Oct-26	11-Oct-26	10-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Low Voltage Cable Materials	4.00	1	07-Oct-26	11-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Lighting Materials	5.00	1	29-Sep-26	04-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Ground Wires, Rods, Pits, Clamping Materials	4.00	1	29-Sep-26	03-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Enclosed Switches and Circuit Breakers Materials	3.00	1	19-Sep-26	21-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Panelboards Materials	1.00	1	27-Oct-26	27-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Data Cabinet Materials	5.00	1	15-Oct-26	20-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for Data/ Voice RJ45 Outlet Materials	3.00	1	12-Oct-26	14-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-73	Manuf. & Delivery for 50 inch Screen Materials	3.00	1	11-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Zone 03		57.50	26	16-Sep-26	11-Nov-26	07-Sep-26 A	10-Nov-26	0.00
Earth & Road Works		57.50	8	16-Sep-26	11-Nov-26	10-Sep-26 A	10-Nov-26	0.00
DMM2-Proc-Delv-74(	Manuf. & Delivery for Interlock Materials	15.00	1	16-Sep-26	04-Oct-26	10-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-74(	Manuf. & Delivery for Curbstone Materials	5.00	1	29-Sep-26	05-Oct-26	15-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-74(	Manuf. & Delivery for Agg. Base Coarse(Rem)	6.00	1	16-Sep-26	22-Sep-26	20-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-74(	Manuf. & Delivery for Asphalt Materials(Rem)	10.50	1	16-Sep-26	29-Sep-26	24-Sep-26 A	10-Nov-26	0.00
DMM2-Proc-Delv-74(	Manuf. & Delivery for Pavement Markings Materials	4.00	1	28-Oct-26	01-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-741	Manuf. & Delivery for Wheels Stopper (precast concrete) Materials	2.00	1	02-Nov-26	03-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-741	Manuf. & Delivery for Traffic Signs Materials	3.00	1	09-Nov-26	11-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-741	Manuf. & Delivery for ground Mounted Information Signs Materials	5.00	1	08-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Wet Networks & Stations		40.00	18	16-Sep-26	04-Nov-26	07-Sep-26 A	07-Nov-26	0.00
TSE Network		15.00	4	19-Oct-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Dripper Materials	7.00	1	19-Oct-26	26-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Bubbler Materials	15.00	1	19-Oct-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Pull Box Materials	15.00	1	19-Oct-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Two Wire Decoder Cable 12 awg Materials	15.00	1	19-Oct-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
Sewer Lift Station		26.00	14	16-Sep-26	17-Oct-26	07-Sep-26 A	05-Nov-26	0.00
Civil & Architecture		23.00	4	19-Sep-26	15-Oct-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Metal Ladders Materials	3.00	1	19-Sep-26	21-Sep-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Internal painting (Acrylic) Materials	4.00	1	21-Sep-26	26-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Metal Covers Materials	2.00	1	14-Oct-26	15-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Signages Materials	3.00	1	11-Oct-26	13-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Mechanical		26.00	4	16-Sep-26	17-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Geotextile Membrane Materials(Rem)	14.00	1	16-Sep-26	03-Oct-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Penstock Materials	15.00	1	16-Sep-26	04-Oct-26	15-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Scupper Materials	20.00	1	21-Sep-26	14-Oct-26	16-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Screening Container Materials	4.00	1	13-Oct-26	17-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Electrical		24.00	6	16-Sep-26	14-Oct-26	07-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Surfaced Mounted Light (LED) Materials	3.00	1	19-Sep-26	21-Sep-26	07-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Galvanized Steel Pole Materials	3.00	1	19-Sep-26	21-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Under Ground Fuel Tank Materials	20.00	1	16-Sep-26	10-Oct-26	13-Sep-26 A	05-Nov-26	0.00

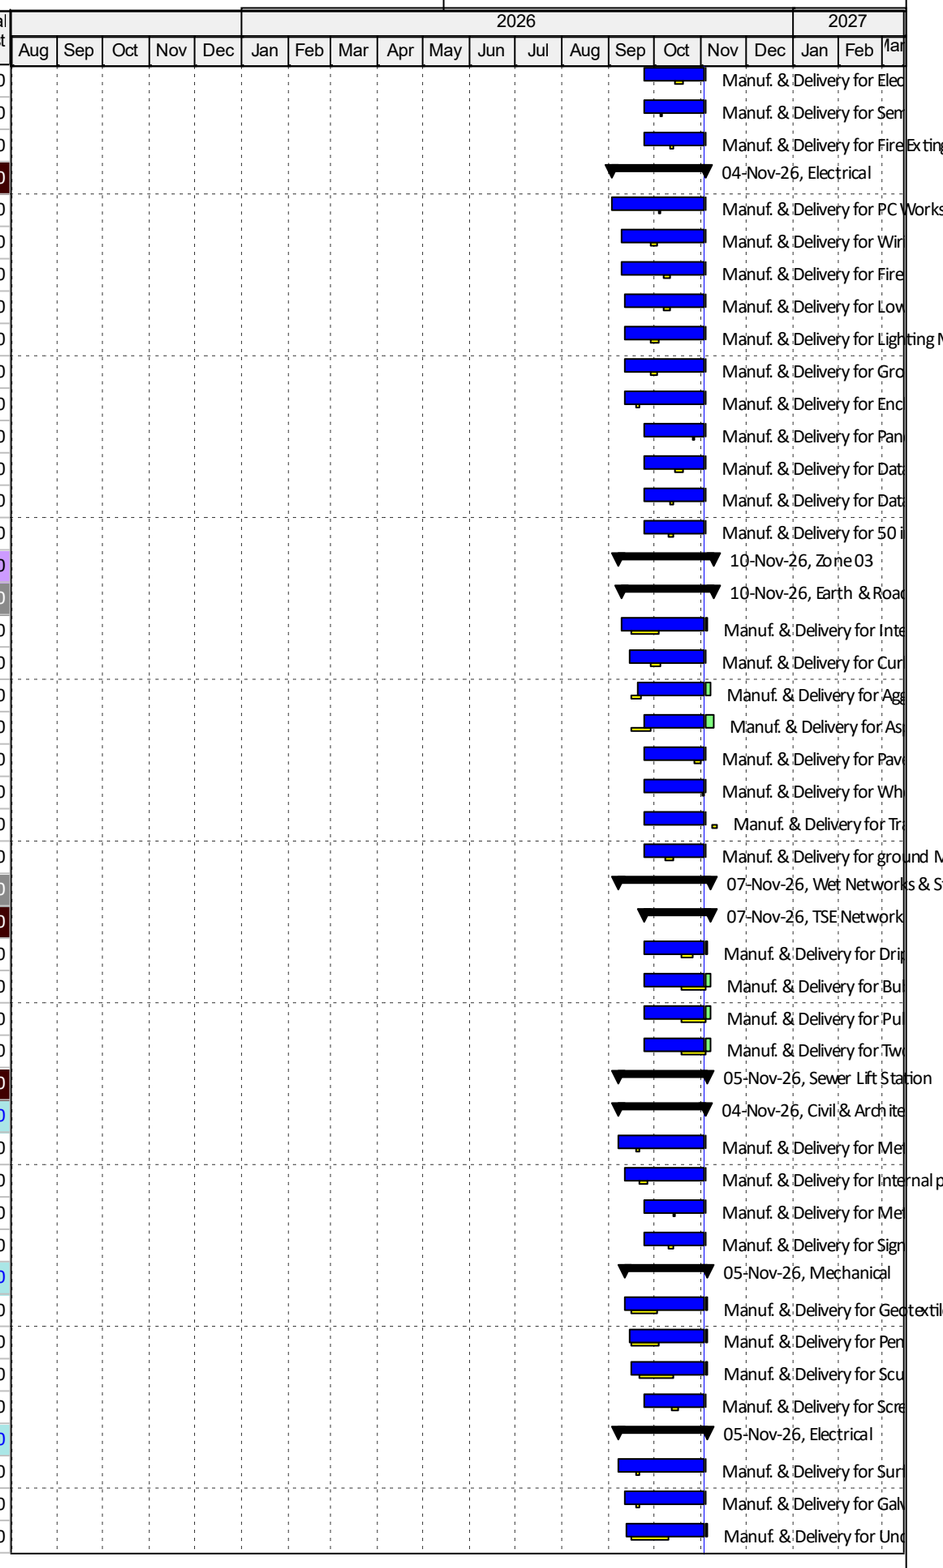

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
DMM2-Proc-Delv-7	Manuf. & Delivery for Electrical Hand Holes Materials	3.00	1	19-Sep-26	21-Sep-26	15-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Process Control Wiring Materials	2.00	1	05-Oct-26	06-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-7	Manuf. & Delivery for Instrumentation for Process Systems Materials	9.00	1	05-Oct-26	14-Oct-26	25-Sep-26 A	05-Nov-26	0.00
Zone 04		46.00	15	16-Sep-26	09-Nov-26	12-Sep-26 A	07-Nov-26	0.00
Earth & Road Works		33.50	8	16-Sep-26	03-Nov-26	12-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Asphalt Materials	7.00	1	29-Sep-26	07-Oct-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-74	Manuf. & Delivery for Agg. Base Coarse(Rem)	7.20	1	16-Sep-26	26-Sep-26	12-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Curbstone Materials	8.00	1	05-Oct-26	14-Oct-26	21-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Interlock Materials	8.00	1	07-Oct-26	17-Oct-26	25-Sep-26 A	05-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Pavement Markings Materials	2.00	1	02-Nov-26	03-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Wheels Stopper (precast concrete) Materials	2.00	1	02-Nov-26	03-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Traffic Signs Materials	3.00	1	17-Oct-26	20-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for ground Mounted Information Signs Materials	5.00	1	14-Oct-26	19-Oct-26	25-Sep-26 A	04-Nov-26	0.00
Wet Networks & Stations		5.00	3	04-Nov-26	09-Nov-26	25-Sep-26 A	07-Nov-26	0.00
TSE Network		5.00	3	04-Nov-26	09-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Bubbler Materials	1.00	1	04-Nov-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Pull Box Materials	4.00	1	05-Nov-26	09-Nov-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-75	Manuf. & Delivery for Two Wire Decoder Cable 12 awg Materials	1.00	1	04-Nov-26	04-Nov-26	25-Sep-26 A	07-Nov-26	0.00
Landscape Works		46.00	4	16-Sep-26	09-Nov-26	13-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-754	Manuf. & Delivery for Ornamental Grasses Materials	3.00	1	16-Sep-26	19-Sep-26	13-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-754	Manuf. & Delivery for Large Shrubs Materials	3.00	1	16-Sep-26	19-Sep-26	13-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-753	Manuf. & Delivery for Trees Materials	3.00	1	22-Oct-26	25-Oct-26	25-Sep-26 A	04-Nov-26	0.00
DMM2-Proc-Delv-754	Manuf. & Delivery for Geotextile Layers Materials	6.00	1	03-Nov-26	09-Nov-26	25-Sep-26 A	04-Nov-26	0.00
Construction		185.89	1260	21-May-26	07-Dec-26	21-May-26 A	06-Dec-26	62,933,859.68
Zone 01		65.00	122	16-Sep-26	19-Nov-26	19-Sep-26 A	28-Nov-26	18,085,483.53
Earthworks & Site Grading		44.99	2	16-Sep-26	30-Sep-26	19-Sep-26 A	16-Nov-26	1,226,813.21
B1.1.31 23 23.22_R	Engineering Backfiling - Service Road(Rem)	12.00	1	16-Sep-26	30-Sep-26	19-Sep-26 A	16-Nov-26	1,151,074.70
B1.1.31 23 16.01_R	Excavation (all types of soil)(Rem)	3.99	1	16-Sep-26	30-Sep-26	04-Nov-26	08-Nov-26	75,738.51
Road 01		59.32	47	16-Sep-26	03-Nov-26	30-Sep-26 A	25-Nov-26	4,147,969.75
Wet Networks		17.00	12	16-Sep-26	01-Nov-26	04-Nov-26	23-Nov-26	46,856.88
TSE Network		17.00	12	16-Sep-26	01-Nov-26	04-Nov-26	23-Nov-26	46,856.88
Valves & Chambers		17.00	12	16-Sep-26	01-Nov-26	04-Nov-26	23-Nov-26	46,856.88
Gate Valves		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
Gate valves dia (250) mm		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
B3.33 14 19.01.13	Spindle & Surface Box	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
Air Valves		5.00	1	20-Sep-26	26-Sep-26	04-Nov-26	09-Nov-26	1,185.47
Air valves on less than 315 mm. (In Chamber)		5.00	1	20-Sep-26	26-Sep-26	04-Nov-26	09-Nov-26	1,185.47
B3.33 05 63.02.89	Valve & Fitting Installation	5.00	1	20-Sep-26	26-Sep-26	04-Nov-26	09-Nov-26	1,185.47
Solenoid valves		12.00	10	19-Oct-26	01-Nov-26	10-Nov-26	23-Nov-26	40,106.06
1 Solenoid valve ?1.0 inch with box		6.00	3	19-Oct-26	25-Oct-26	10-Nov-26	16-Nov-26	9,604.63
B4.32 84 13.31	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	19-Oct-26	21-Oct-26	10-Nov-26	12-Nov-26	4,917.51
B4.32 84 13.32	Solenoid Valve Box Installation	3.00	1	22-Oct-26	25-Oct-26	14-Nov-26	16-Nov-26	2,838.80
B4.32 84 13.066	Pull Box Installation	3.00	1	22-Oct-26	25-Oct-26	14-Nov-26	16-Nov-26	1,848.31
1 Solenoid valve ?1.5 inch with box		9.00	4	22-Oct-26	01-Nov-26	14-Nov-26	23-Nov-26	17,906.00
B4.32 84 13.34	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	22-Oct-26	25-Oct-26	14-Nov-26	16-Nov-26	4,917.51
B4.32 84 13.35	Solenoid Valve Box Installation	3.00	1	26-Oct-26	28-Oct-26	17-Nov-26	19-Nov-26	8,434.05

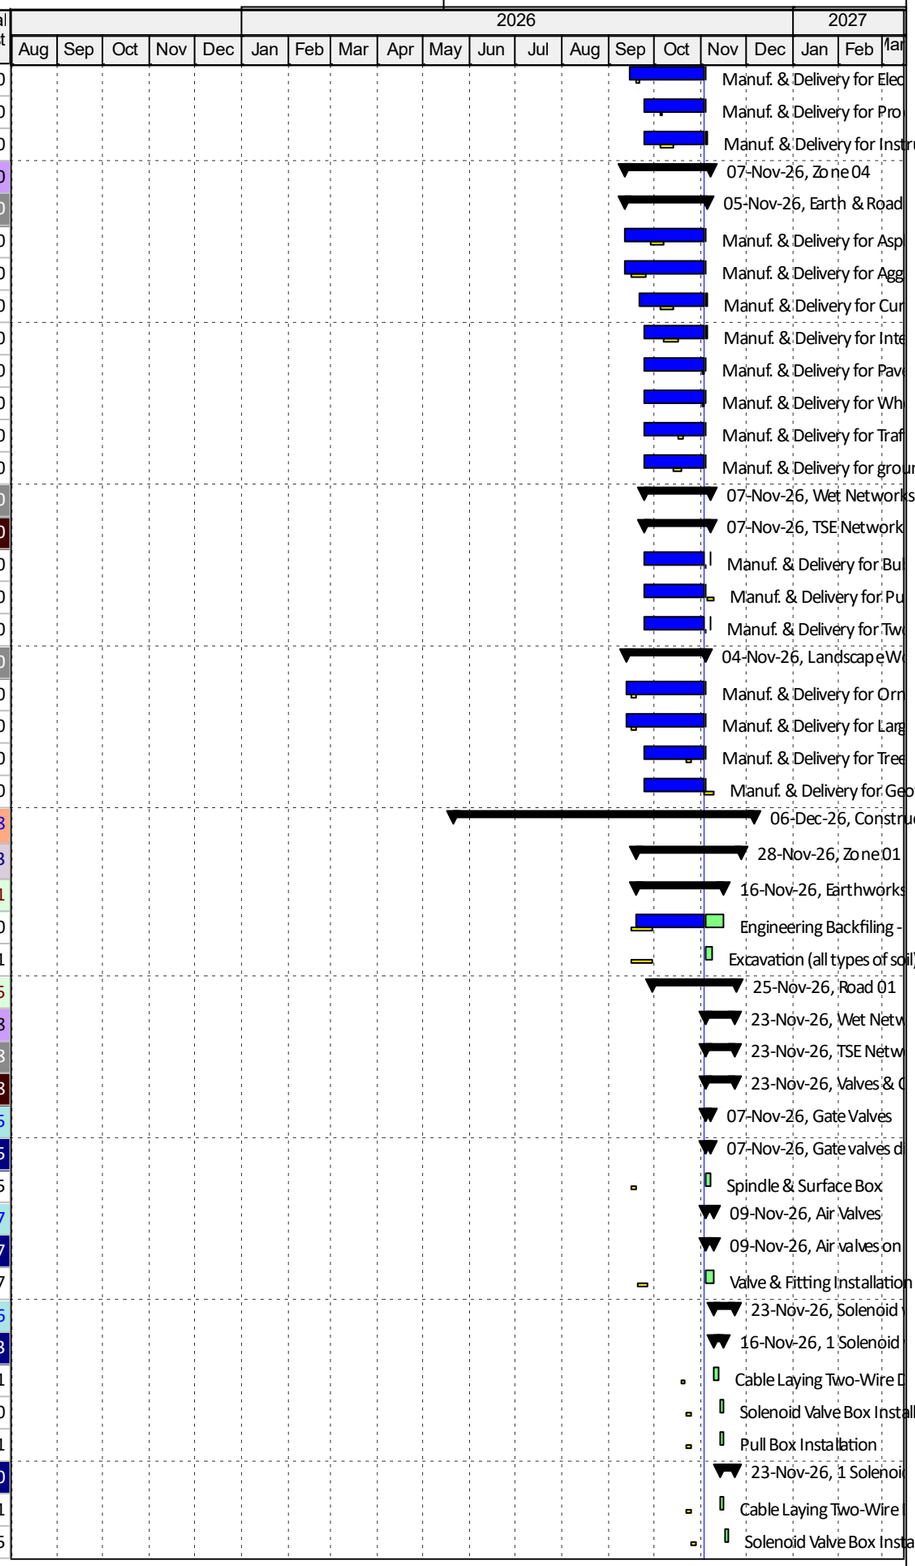


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B4.32 84 13.067	Pull Box Installation	3.00	1	26-Oct-26	28-Oct-26	17-Nov-26	19-Nov-26	1,848.31
B4.32 84 13.36	Bubblers Installation	3.00	1	29-Oct-26	01-Nov-26	21-Nov-26	23-Nov-26	2,706.13
1 Solenoid valve ?2.0 inch with box		6.00	3	26-Oct-26	01-Nov-26	17-Nov-26	23-Nov-26	12,595.43
B4.32 84 13.28	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	26-Oct-26	28-Oct-26	17-Nov-26	19-Nov-26	4,917.51
B4.32 84 13.29	Solenoid Valve Box Installation	3.00	1	29-Oct-26	01-Nov-26	21-Nov-26	23-Nov-26	5,829.60
B4.32 84 13.068	Pull Box Installation	3.00	1	29-Oct-26	01-Nov-26	21-Nov-26	23-Nov-26	1,848.31
Dry Networks		20.28	10	16-Sep-26	13-Oct-26	10-Oct-26 A	16-Nov-26	131,968.05
Medium Voltage Network		10.28	2	16-Sep-26	03-Oct-26	04-Nov-26	16-Nov-26	10,905.84
Cables		10.28	2	16-Sep-26	03-Oct-26	04-Nov-26	16-Nov-26	10,905.84
3C,500mm2		10.28	2	16-Sep-26	03-Oct-26	04-Nov-26	16-Nov-26	10,905.84
B2.33 71 49.23.02	Straight joints cables	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	7,880.95
B2.33 71 49.23.03	Cable Termination	4.00	1	29-Sep-26	03-Oct-26	11-Nov-26	16-Nov-26	3,024.89
Street Lighting		12.00	2	10-Oct-26	13-Oct-26	10-Oct-26 A	05-Nov-26	61,571.46
SL Poles		3.00	1	10-Oct-26	12-Oct-26	10-Oct-26 A	04-Nov-26	58,898.50
Pole (10 M Single Arm)		3.00	1	10-Oct-26	12-Oct-26	10-Oct-26 A	04-Nov-26	58,898.50
B2.33 71 16.025	Backfilling, Grouting & Chamfering	3.00	1	10-Oct-26	12-Oct-26	10-Oct-26 A	04-Nov-26	58,898.50
Earthing		2.00	1	12-Oct-26	13-Oct-26	04-Nov-26	05-Nov-26	2,672.96
B2.33 71 19 012	Earth Rods& Conduits	2.00	1	12-Oct-26	13-Oct-26	04-Nov-26	05-Nov-26	2,672.96
Telecommunication Network		7.00	6	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	59,490.75
Demolishing and Site Clearing		7.00	6	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	59,490.75
B2.1.02 41 00.012_R	Old Manholes Grubbing(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	792.73
B2.1.02 41 00.014_R	New Manholes Installation (Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,585.46
B2.1.02 41 00.011_R	Excavation(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	3,879.89
B2.1.02 41 00.013_R	Old Network Components Grubbing(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	6,966.57
B2.1.02 41 00.015_R	New Network Components Installation(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	13,933.63
B2.1.02 41 00.016	Backfilling & Warrning Tape	5.00	1	19-Sep-26	24-Sep-26	07-Nov-26	11-Nov-26	32,332.46
Earth & Road Works		58.32	19	20-Sep-26	02-Nov-26	30-Sep-26 A	24-Nov-26	3,590,838.97
Earth Layers		6.00	1	20-Sep-26	06-Oct-26	28-Oct-26 A	08-Nov-26	114,568.40
B1.2.32 11 23.01.1_R	Aggregate Base Course(Rem)	6.00	1	20-Sep-26	06-Oct-26	28-Oct-26 A	08-Nov-26	114,568.40
Interlock		2.00	1	21-Oct-26	27-Oct-26	11-Nov-26	14-Nov-26	313,988.14
B1.2.32 14 13.13.1	60mm thick - Interlocking Block Pavers	2.00	1	21-Oct-26	27-Oct-26	11-Nov-26	14-Nov-26	313,988.14
Curbstone		23.00	7	14-Oct-26	31-Oct-26	12-Oct-26 A	17-Nov-26	696,009.20
Pre-Installation		3.00	3	14-Oct-26	21-Oct-26	09-Nov-26	11-Nov-26	276,473.37
32 16 133_R	Haunching(Rem)	3.00	1	19-Oct-26	21-Oct-26	09-Nov-26	11-Nov-26	92,157.79
32 16 131_R	Excavation(Rem)	2.00	1	14-Oct-26	15-Oct-26	10-Nov-26	11-Nov-26	92,157.79
32 16 132_R	PCC(Rem)	2.00	1	17-Oct-26	18-Oct-26	10-Nov-26	11-Nov-26	92,157.79
Installation		23.00	3	26-Oct-26	31-Oct-26	12-Oct-26 A	17-Nov-26	337,617.14
B1.2.32 16.13.01.1_	Curb Stone, Type K1(Rem)	2.00	1	26-Oct-26	27-Oct-26	12-Oct-26 A	14-Nov-26	154,938.54
B1.2.32 16.13.03.1	Edge Curb, Type K4	2.00	1	28-Oct-26	29-Oct-26	14-Nov-26	16-Nov-26	112,529.23
B1.2.32 16.13.041	Heel Curb, Type K5	1.00	1	31-Oct-26	31-Oct-26	16-Nov-26	17-Nov-26	70,149.37
Finishing		1.00	1	31-Oct-26	31-Oct-26	16-Nov-26	17-Nov-26	81,918.69
32 16 134	Finishing, Fareface	1.00	1	31-Oct-26	31-Oct-26	16-Nov-26	17-Nov-26	81,918.69
Asphalt Layers		48.40	2	07-Oct-26	21-Oct-26	30-Sep-26 A	12-Nov-26	2,346,770.80
B1.2.32 11 26.01.1_R	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	6.00	1	07-Oct-26	13-Oct-26	30-Sep-26 A	07-Nov-26	397,093.32
B1.2.32 12 16.01.1	Bituminous concrete Wearing Course, including tack coat (RC2)	5.00	1	14-Oct-26	21-Oct-26	07-Nov-26	12-Nov-26	1,949,677.48
Pavement Marking		3.00	2	25-Oct-26	27-Oct-26	15-Nov-26	18-Nov-26	49,465.29

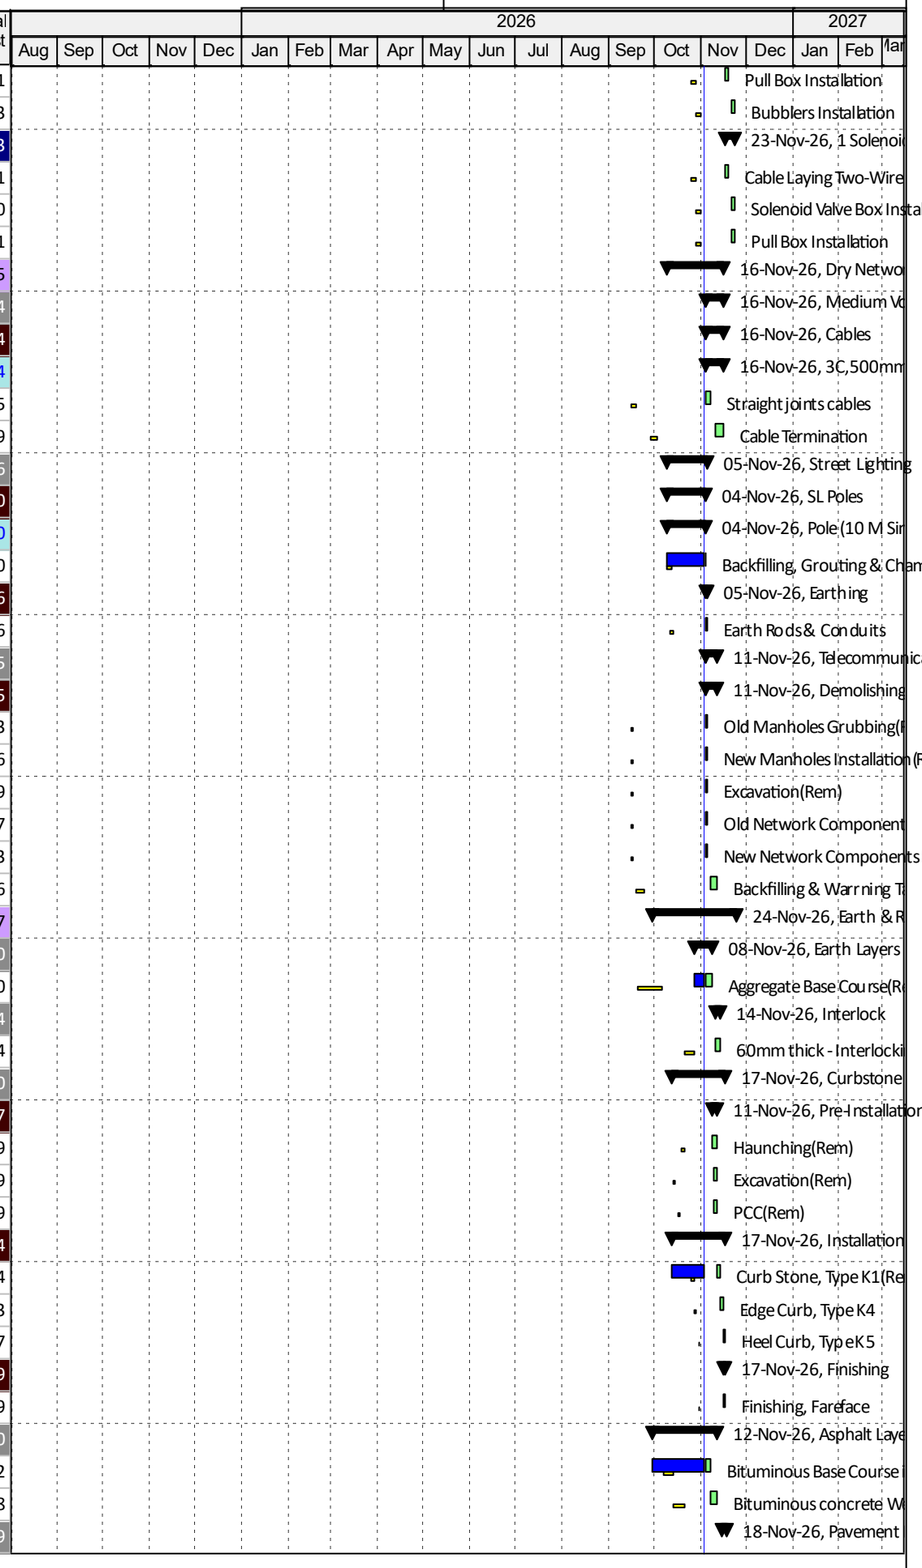


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B1.2.32 17 23.01.1	Retroreflective Thermoplastic White Traffic lines	3.00	1	25-Oct-26	27-Oct-26	15-Nov-26	18-Nov-26	33,438.58
B1.2.32 17 23.02.1	Retroreflective Thermoplastic Yellow, Traffic lines	2.00	1	25-Oct-26	26-Oct-26	15-Nov-26	17-Nov-26	16,026.71
Traffic Signs		11.00	5	21-Oct-26	02-Nov-26	11-Nov-26	24-Nov-26	45,628.68
Pre-Installation		5.00	2	21-Oct-26	26-Oct-26	11-Nov-26	17-Nov-26	19,230.98
10 14 53.1	Excavation	2.00	1	21-Oct-26	22-Oct-26	11-Nov-26	14-Nov-26	9,621.07
10 14 53.01	Foundation	3.00	1	24-Oct-26	26-Oct-26	14-Nov-26	17-Nov-26	9,609.91
Installation		6.00	3	27-Oct-26	02-Nov-26	17-Nov-26	24-Nov-26	26,397.70
B1.2.10 14 53.011	1 Sheet Alumenium, Single post	4.00	1	27-Oct-26	31-Oct-26	17-Nov-26	22-Nov-26	23,099.98
B1.2.10 14 53.021	2 Sheet Alumenium, Single post	2.00	1	01-Nov-26	02-Nov-26	22-Nov-26	24-Nov-26	2,420.91
B1.2.10 14 14.01.1	Ground mounted, 1 Sheet Alumenium, Single post	2.00	1	01-Nov-26	02-Nov-26	22-Nov-26	24-Nov-26	876.81
Miscellaneous		2.00	1	22-Oct-26	24-Oct-26	12-Nov-26	15-Nov-26	24,408.46
B1.2.32 12 19.13.01	Speed Tables	2.00	1	22-Oct-26	24-Oct-26	12-Nov-26	15-Nov-26	24,408.46
Landscape		15.00	6		03-Nov-26	08-Nov-26	25-Nov-26	378,305.84
Steel fence (MODON)		11.20	3	18-Oct-26	31-Oct-26	08-Nov-26	21-Nov-26	370,467.30
B7.32 31 26.021_R	Earthwork(Rem)	5.00	1	18-Oct-26	22-Oct-26	08-Nov-26	14-Nov-26	21,102.95
B7.32 31 26.022_R	Foundation(Rem)	4.20	1	18-Oct-26	22-Oct-26	08-Nov-26	12-Nov-26	21,100.88
B7.32 31 26.023	Fence Installation	7.00	1	22-Oct-26	31-Oct-26	12-Nov-26	21-Nov-26	328,263.48
Gates		10.00	3	24-Oct-26	03-Nov-26	14-Nov-26	25-Nov-26	7,838.54
Size (1.6x 2.7)m		10.00	2	24-Oct-26	03-Nov-26	14-Nov-26	25-Nov-26	1,501.91
B7.32 31 26.03.021	Earthwork	5.00	1	24-Oct-26	28-Oct-26	14-Nov-26	19-Nov-26	750.95
B7.32 31 26.03.022	Foundation	5.00	1	29-Oct-26	03-Nov-26	19-Nov-26	25-Nov-26	750.95
Size (4.5x 2.7)m		5.00	1	29-Oct-26	03-Nov-26	19-Nov-26	25-Nov-26	6,336.63
B7.32 31 26.03.041	Earthwork	5.00	1	29-Oct-26	03-Nov-26	19-Nov-26	25-Nov-26	6,336.63
Service Road		24.00	73	16-Sep-26	19-Nov-26	24-Oct-26 A	28-Nov-26	12,710,700.57
Wet Networks		24.00	40	08-Oct-26	19-Nov-26	24-Oct-26 A	28-Nov-26	1,035,402.72
Storm Network		24.00	40	08-Oct-26	19-Nov-26	24-Oct-26 A	28-Nov-26	1,035,402.72
GRP		22.00	17	08-Oct-26	05-Nov-26	29-Oct-26 A	26-Nov-26	727,198.04
?1300		4.00	1	12-Oct-26	15-Oct-26	31-Oct-26 A	05-Nov-26	10,080.91
Depth From 3.5m to 4.5m		4.00	1	12-Oct-26	15-Oct-26	31-Oct-26 A	05-Nov-26	10,080.91
B6.33 42 11.26.4	Embedment & Test	4.00	1	12-Oct-26	15-Oct-26	31-Oct-26 A	05-Nov-26	10,080.91
?1400		20.00	6	08-Oct-26	31-Oct-26	02-Nov-26 A	26-Nov-26	219,322.00
Depth From 3.5m to 4.5m		5.00	1	15-Oct-26	20-Oct-26	02-Nov-26 A	07-Nov-26	25,524.30
B6.33 42 11.30.4	Embedment & Test	5.00	1	15-Oct-26	20-Oct-26	02-Nov-26 A	07-Nov-26	25,524.30
Depth From 2.5m to 3.5m		20.00	5	08-Oct-26	31-Oct-26	04-Nov-26	26-Nov-26	193,797.69
B6.33 42 11.29.1	Excavation	3.00	1	08-Oct-26	11-Oct-26	04-Nov-26	07-Nov-26	38,759.54
B6.33 42 11.29.2	Sand Bedding	3.00	1	12-Oct-26	14-Oct-26	08-Nov-26	10-Nov-26	9,683.60
B6.33 42 11.29.3	Pipe Laying	3.00	1	15-Oct-26	18-Oct-26	11-Nov-26	14-Nov-26	87,202.67
B6.33 42 11.29.4	Embedment & Test	5.00	1	19-Oct-26	24-Oct-26	15-Nov-26	19-Nov-26	38,759.54
B6.33 42 11.29.5	Backfilling & Warrning Tape	6.00	1	25-Oct-26	31-Oct-26	21-Nov-26	26-Nov-26	19,392.35
?1500		22.00	10	12-Oct-26	05-Nov-26	29-Oct-26 A	07-Nov-26	497,795.14
Depth From 2.5m to 3.5m		19.00	5	12-Oct-26	02-Nov-26	29-Oct-26 A	05-Nov-26	286,472.00
B6.33 42 11.33.1	Excavation	3.00	1	12-Oct-26	14-Oct-26	29-Oct-26 A	04-Nov-26	58,672.54
B6.33 42 11.33.2	Sand Bedding	3.00	1	15-Oct-26	18-Oct-26	31-Oct-26 A	04-Nov-26	14,192.71
B6.33 42 11.33.3	Pipe Laying	3.00	1	19-Oct-26	21-Oct-26	01-Nov-26 A	04-Nov-26	127,709.86
B6.33 42 11.33.4	Embedment & Test	4.00	1	22-Oct-26	26-Oct-26	02-Nov-26 A	04-Nov-26	57,511.47
B6.33 42 11.33.5	Backfilling & Warrning Tape	6.00	1	27-Oct-26	02-Nov-26	03-Nov-26 A	05-Nov-26	28,385.43

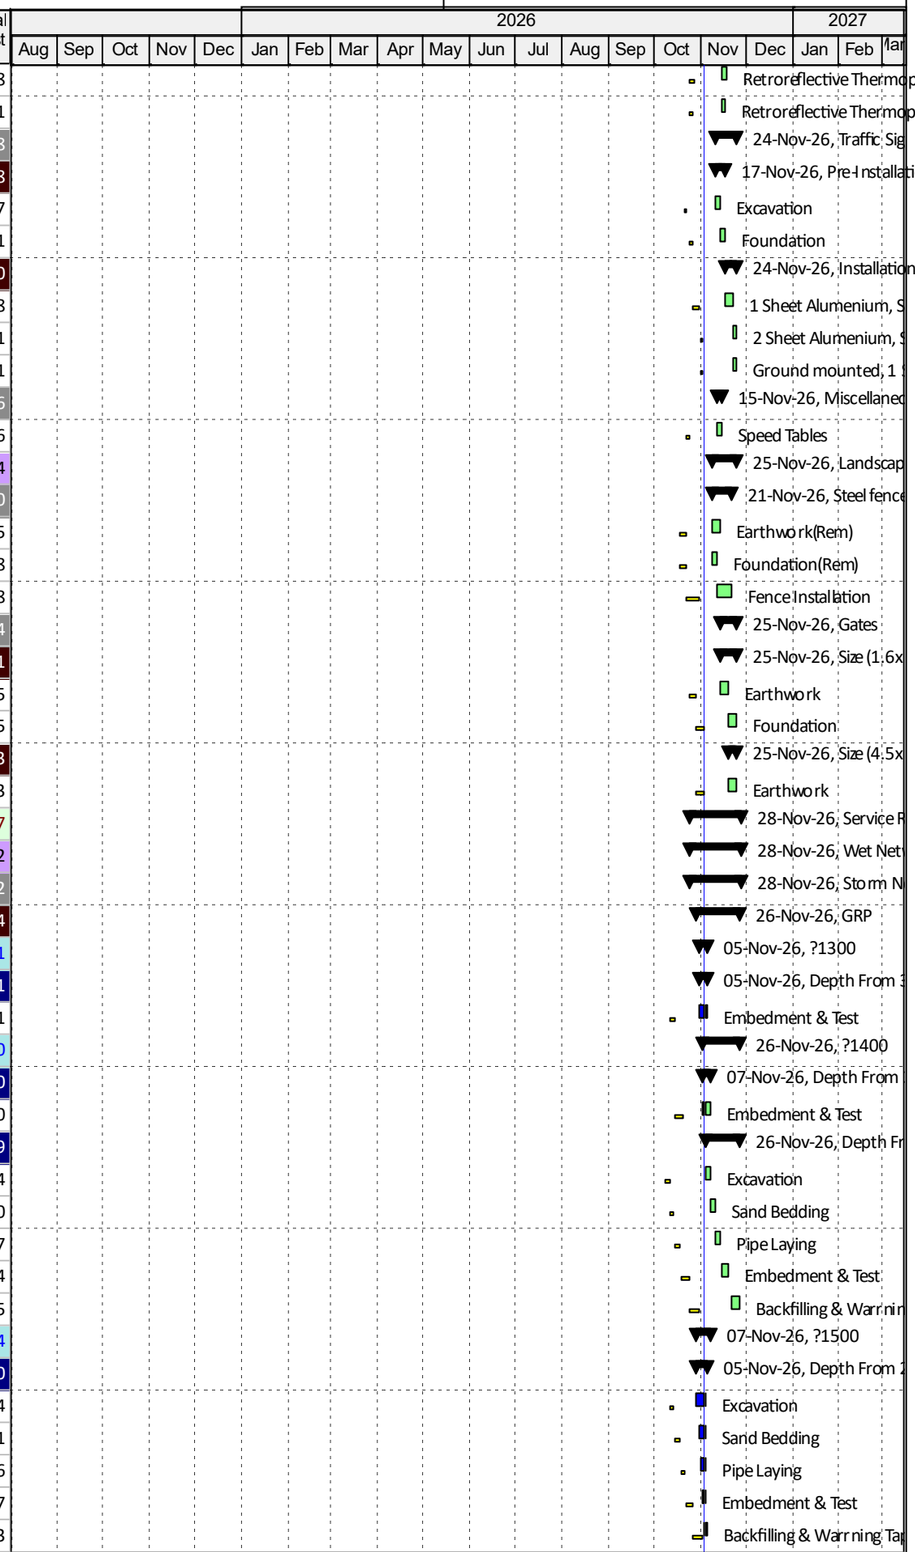

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Depth From 3.5m to 4.5m		19.00	5	15-Oct-26	05-Nov-26	31-Oct-26 A	07-Nov-26	211,323.13
B6.33 42 11.34.1	Excavation	3.00	1	15-Oct-26	18-Oct-26	31-Oct-26 A	05-Nov-26	42,283.32
B6.33 42 11.34.2	Sand Bedding	3.00	1	19-Oct-26	21-Oct-26	31-Oct-26 A	05-Nov-26	10,559.15
B6.33 42 11.34.3	Pipe Laying	3.00	1	22-Oct-26	25-Oct-26	01-Nov-26 A	05-Nov-26	95,079.06
B6.33 42 11.34.4	Embedment & Test	5.00	1	26-Oct-26	31-Oct-26	02-Nov-26 A	07-Nov-26	42,283.32
B6.33 42 11.34.5	Backfilling & Warning Tape	3.00	1	03-Nov-26	05-Nov-26	02-Nov-26 A	05-Nov-26	21,118.30
Manholes		22.50	15	19-Oct-26	12-Nov-26	24-Oct-26 A	28-Nov-26	186,284.34
?2000		22.50	15	19-Oct-26	12-Nov-26	24-Oct-26 A	28-Nov-26	186,284.34
Depth From 2.5m to 3.5m		18.00	5	19-Oct-26	08-Nov-26	24-Oct-26 A	07-Nov-26	72,866.45
B6.33 05 13.07.1	Excavation & Compaction	3.00	1	19-Oct-26	21-Oct-26	24-Oct-26 A	05-Nov-26	10,765.08
B6.33 05 13.07.2	Blinding Conc, & RC Base	4.00	1	22-Oct-26	26-Oct-26	25-Oct-26 A	05-Nov-26	7,095.17
B6.33 05 13.07.3	Manhole Installation	3.00	1	27-Oct-26	29-Oct-26	26-Oct-26 A	05-Nov-26	32,404.79
B6.33 05 13.07.5	Backfilling	3.00	1	05-Nov-26	08-Nov-26	27-Oct-26 A	05-Nov-26	15,506.25
B6.33 05 13.07.4	Test, Internal Finishing, Benching & Cover	5.00	1	31-Oct-26	04-Nov-26	28-Oct-26 A	07-Nov-26	7,095.17
Depth From 3.5m to 4.5m		16.00	5	22-Oct-26	09-Nov-26	05-Nov-26	24-Nov-26	89,845.68
B6.33 05 13.08.1	Excavation & Compaction	3.00	1	22-Oct-26	25-Oct-26	05-Nov-26	09-Nov-26	12,909.84
B6.33 05 13.08.2	Blinding Conc, & RC Base	4.00	1	26-Oct-26	29-Oct-26	09-Nov-26	14-Nov-26	8,714.14
B6.33 05 13.08.3	Manhole Installation	3.00	1	31-Oct-26	02-Nov-26	14-Nov-26	17-Nov-26	42,079.22
B6.33 05 13.08.4	Test, Internal Finishing, Benching & Cover	3.00	1	03-Nov-26	05-Nov-26	17-Nov-26	21-Nov-26	8,714.14
B6.33 05 13.08.5	Backfilling	3.00	1	07-Nov-26	09-Nov-26	21-Nov-26	24-Nov-26	17,428.33
Depth From 4.5m to 5.5m		16.00	5	26-Oct-26	12-Nov-26	09-Nov-26	28-Nov-26	23,572.21
B6.33 05 13.09.1	Excavation & Compaction	3.00	1	26-Oct-26	28-Oct-26	09-Nov-26	12-Nov-26	3,387.08
B6.33 05 13.09.2	Blinding Conc, & RC Base	4.00	1	29-Oct-26	02-Nov-26	12-Nov-26	17-Nov-26	2,370.95
B6.33 05 13.09.3	Manhole Installation	2.00	1	03-Nov-26	04-Nov-26	17-Nov-26	19-Nov-26	11,040.03
B6.33 05 13.09.4	Test, Internal Finishing, Benching & Cover	3.00	1	05-Nov-26	08-Nov-26	19-Nov-26	23-Nov-26	2,370.95
B6.33 05 13.09.5	Backfilling	3.00	1	10-Nov-26	12-Nov-26	24-Nov-26	28-Nov-26	4,403.20
Catch Basins		15.50	8	26-Oct-26	19-Nov-26	04-Nov-26	22-Nov-26	121,920.34
Single		5.50	4	26-Oct-26	19-Nov-26	08-Nov-26	14-Nov-26	86,766.55
B6.33 05 63.07.4	Backfilling, DI Frame & Grate Cover Fixing	3.00	1	17-Nov-26	19-Nov-26	08-Nov-26	10-Nov-26	26,921.76
B6.33 05 63.07.2_R	Blinding Conc.(Rem)	3.00	1	26-Oct-26	28-Oct-26	09-Nov-26	12-Nov-26	8,565.25
B6.33 05 63.07.3_R	Catch Basin Installation(Rem)	4.00	1	26-Oct-26	29-Oct-26	09-Nov-26	14-Nov-26	38,459.65
B6.33 05 63.07.1_R	Excavation, Compaction & Vapour Barrier(Rem)	3.00	1	26-Oct-26	28-Oct-26	09-Nov-26	12-Nov-26	12,819.88
Double		15.50	4	29-Oct-26	16-Nov-26	04-Nov-26	22-Nov-26	35,153.79
B6.33 05 63.08.4	Backfilling, DI Frame & Grate Cover Fixing	3.00	1	14-Nov-26	16-Nov-26	04-Nov-26	07-Nov-26	10,516.10
B6.33 05 63.08.1	Excavation, Compaction & Vapour Barrier	3.00	1	29-Oct-26	01-Nov-26	12-Nov-26	16-Nov-26	5,258.04
B6.33 05 63.08.2	Blinding Conc.	3.00	1	02-Nov-26	04-Nov-26	16-Nov-26	19-Nov-26	3,455.28
B6.33 05 63.08.3	Catch Basin Installation	2.00	1	05-Nov-26	07-Nov-26	19-Nov-26	22-Nov-26	15,924.38
Dry Networks		17.00	16	20-Oct-26	09-Nov-26	04-Nov-26	23-Nov-26	251,582.47
Street Lighting		17.00	16	20-Oct-26	09-Nov-26	04-Nov-26	23-Nov-26	251,582.47
Duct Banks		7.00	5	29-Oct-26	05-Nov-26	12-Nov-26	19-Nov-26	61,077.70
2 Way		5.00	3	29-Oct-26	03-Nov-26	12-Nov-26	17-Nov-26	46,040.68
B2.33 71 00 02 011	Excavation	2.00	1	29-Oct-26	31-Oct-26	12-Nov-26	14-Nov-26	9,208.14
B2.33 71 00 02 012	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	01-Nov-26	03-Nov-26	15-Nov-26	17-Nov-26	27,624.41
B2.33 71 00 02 013	Backfilling & Warning Tape	3.00	1	01-Nov-26	03-Nov-26	15-Nov-26	17-Nov-26	9,208.14
4 Way		5.00	2	01-Nov-26	05-Nov-26	15-Nov-26	19-Nov-26	15,037.02
B2.33 71 00 02 021	Excavation	2.00	1	01-Nov-26	02-Nov-26	15-Nov-26	16-Nov-26	3,759.25

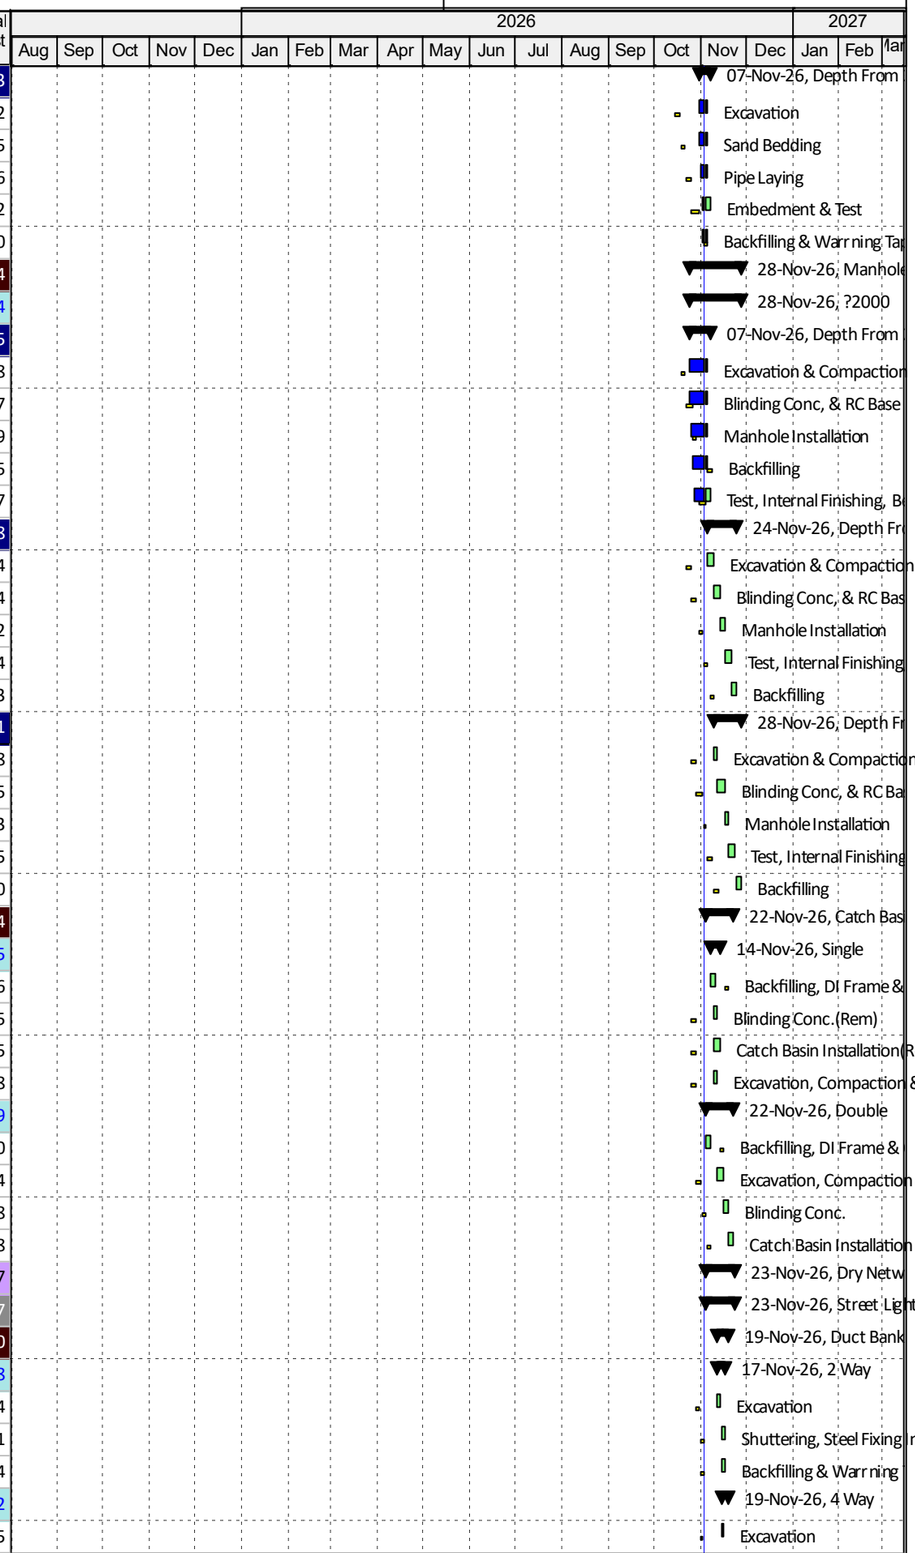


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.33 71 00 02 022	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	03-Nov-26	05-Nov-26	17-Nov-26	19-Nov-26	11,277.76
Drawpits		6.00	3	03-Nov-26	09-Nov-26	17-Nov-26	23-Nov-26	71,922.87
B2.33 71 00 02 041	Excavation	2.00	1	03-Nov-26	04-Nov-26	17-Nov-26	18-Nov-26	14,384.57
B2.33 71 00 02 042	Drawpits Installation	2.00	1	05-Nov-26	07-Nov-26	19-Nov-26	21-Nov-26	43,153.72
B2.33 71 00 02 043	Backfilling & Warning Tape	2.00	1	08-Nov-26	09-Nov-26	22-Nov-26	23-Nov-26	14,384.57
Cables		5.00	2	20-Oct-26	24-Oct-26	04-Nov-26	09-Nov-26	103,854.93
4C,10+1C,10mm2		5.00	2	20-Oct-26	24-Oct-26	04-Nov-26	09-Nov-26	103,854.93
B2.33 71 19 242	Land Adjustment		1	20-Oct-26	21-Oct-26	04-Nov-26	07-Nov-26	25,963.96
B2.33 71 49.23.202	Cable Pulling	2.00	1	22-Oct-26	24-Oct-26	08-Nov-26	09-Nov-26	77,890.96
SL Poles		7.00	3	20-Oct-26	26-Oct-26	04-Nov-26	11-Nov-26	10,245.23
Relocate Lighting Poles		7.00	3	20-Oct-26	26-Oct-26	04-Nov-26	11-Nov-26	10,245.23
B2.1.02 41 00.16	Excavation (Evacuation Around Poles)	2.00	1	20-Oct-26	21-Oct-26	04-Nov-26	05-Nov-26	1,807.98
B2.1.02 41 00.17	Old Poles Grubbing	3.00	1	22-Oct-26	24-Oct-26	07-Nov-26	09-Nov-26	3,013.30
B2.1.02 41 00.17a	Poles Transferring & Installation Incl. Foundation	2.00	1	25-Oct-26	26-Oct-26	10-Nov-26	11-Nov-26	5,423.95
Earthing		7.00	3	27-Oct-26	03-Nov-26	10-Nov-26	17-Nov-26	4,481.74
B2.33 71 19 13	Land Adjustment	2.00	1	27-Oct-26	28-Oct-26	10-Nov-26	11-Nov-26	904.39
B2.33 71 19 14	Earth Rods & Conduits	2.00	1	29-Oct-26	31-Oct-26	12-Nov-26	14-Nov-26	2,672.96
B2.33 71 19 15	Backfilling	3.00	1	01-Nov-26	03-Nov-26	15-Nov-26	17-Nov-26	904.39
Earth & Road Works		18.00	17	16-Sep-26	09-Nov-26	04-Nov-26	24-Nov-26	11,423,715.38
Earth Works		13.00	1	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	2,862,348.59
B1.2.31 23 23.01.2_R	Embankment Backfiling(Rem)	13.00	1	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	2,862,348.59
Earth Layers		3.00	2	03-Oct-26	11-Oct-26	04-Nov-26	07-Nov-26	1,110,732.09
B1.2.32 11 13.01.2_R	Subgrade(Rem)	3.00	1	03-Oct-26	05-Oct-26	04-Nov-26	07-Nov-26	275,736.68
B1.2.32 11 23.01.2_R	Aggregate Base Course(Rem)	3.00	1	08-Oct-26	11-Oct-26	04-Nov-26	07-Nov-26	834,995.41
Interlock		3.00	1	01-Nov-26	03-Nov-26	15-Nov-26	17-Nov-26	293,381.12
B1.2.32 14 13.13.2	60mm thick - Interlocking Block Pavers	3.00	1	01-Nov-26	03-Nov-26	15-Nov-26	17-Nov-26	293,381.12
Curbstone		12.00	6	12-Oct-26	05-Nov-26	08-Nov-26	21-Nov-26	675,088.16
Pre-Installation		8.00	3	12-Oct-26	20-Oct-26	08-Nov-26	16-Nov-26	344,444.28
32 16 13.0021	Excavation	2.00	1	12-Oct-26	13-Oct-26	08-Nov-26	09-Nov-26	114,814.76
32 16 13.0023	Haunching	3.00	1	14-Oct-26	17-Oct-26	10-Nov-26	12-Nov-26	114,814.76
32 16 13.0024	PCC	3.00	1	18-Oct-26	20-Oct-26	14-Nov-26	16-Nov-26	114,814.76
Installation		4.00	3	01-Nov-26	05-Nov-26	17-Nov-26	21-Nov-26	330,643.87
B1.2.32 16.13.01.2	Curb Stone, Type K1	2.00	1	01-Nov-26	02-Nov-26	17-Nov-26	18-Nov-26	160,857.65
B1.2.32 16.13.03.2	Edge Curb, Type K4	2.00	1	01-Nov-26	02-Nov-26	17-Nov-26	18-Nov-26	104,239.87
B1.2.32 16.13.042	Heel Curb, Type K 5	2.00	1	04-Nov-26	05-Nov-26	19-Nov-26	21-Nov-26	65,546.36
Asphalt Layers		18.00	2	12-Oct-26	09-Nov-26	04-Nov-26	24-Nov-26	6,459,709.57
B1.2.32 11 26.01.2_R	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	4.00	1	12-Oct-26	19-Oct-26	04-Nov-26	08-Nov-26	4,637,964.74
B1.2.32 12 16.01.2	Bituminous concrete Wearing Course, including tack coat (RC2)	5.00	1	04-Nov-26	09-Nov-26	19-Nov-26	24-Nov-26	1,821,744.83
Traffic Signs		8.00	5	14-Oct-26	22-Oct-26	10-Nov-26	18-Nov-26	22,455.85
Pre-Installation		4.00	2	14-Oct-26	18-Oct-26	10-Nov-26	14-Nov-26	20,112.34
B2.31 23 00.41	Excavation	2.00	1	14-Oct-26	15-Oct-26	10-Nov-26	11-Nov-26	10,061.75
10 14 53.02	Foundation	2.00	1	17-Oct-26	18-Oct-26	12-Nov-26	14-Nov-26	10,050.59
Installation		4.00	3	19-Oct-26	22-Oct-26	15-Nov-26	18-Nov-26	2,343.51
B1.2.10 14 53.317	1 Sheet Alumenium, Single post	2.00	1	19-Oct-26	20-Oct-26	15-Nov-26	16-Nov-26	1,249.85
B1.2.10 14 53.318	2 Sheet Alumenium, Single post	2.00	1	21-Oct-26	22-Oct-26	17-Nov-26	18-Nov-26	212.06
B1.2.10 14 14.01.18	Ground mounted, 1 Sheet Alumenium, Single post	2.00	1	21-Oct-26	22-Oct-26	17-Nov-26	18-Nov-26	881.59

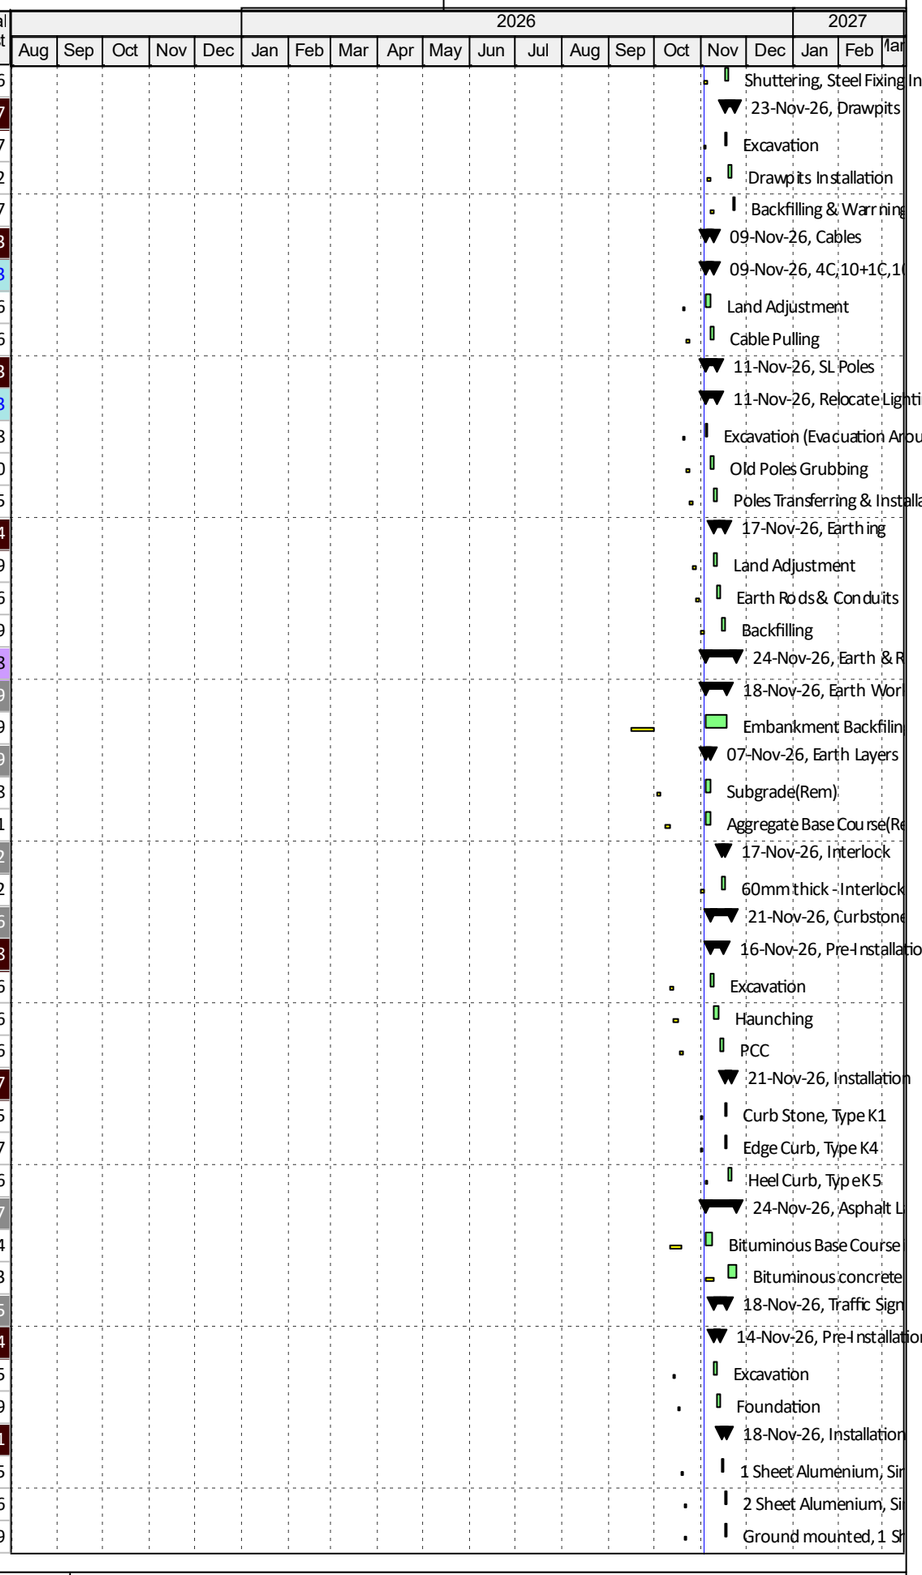


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Zone 02		65.00	550	16-Sep-26	07-Dec-26	26-Sep-26 A	01-Dec-26	25,139,690.42
Earthworks & Site Grading		6.23	1	16-Sep-26	30-Sep-26	04-Nov-26	11-Nov-26	62,386.48
B1.1.31 23 16.02_R	Excavation (all types of soil)(Rem)	6.23	1	16-Sep-26	30-Sep-26	04-Nov-26	11-Nov-26	62,386.48
Service Road		35.32	24	16-Sep-26	26-Oct-26	17-Oct-26 A	26-Nov-26	1,151,018.44
Wet Networks		24.12	17	16-Sep-26	26-Oct-26	17-Oct-26 A	09-Nov-26	208,912.98
Stormwater Network		24.12	17	16-Sep-26	26-Oct-26	17-Oct-26 A	09-Nov-26	208,912.98
GRP		10.26	8	16-Sep-26	24-Sep-26	28-Oct-26 A	09-Nov-26	87,917.39
?1500		10.26	8	16-Sep-26	24-Sep-26	28-Oct-26 A	09-Nov-26	87,917.39
Depth From 2.5m to 3.5m		3.12	4	16-Sep-26	24-Sep-26	28-Oct-26 A	04-Nov-26	32,933.81
B6.33 42 11.31-1	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	28-Oct-26 A	04-Nov-26	4,616.46
B6.33 42 11.31-1	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	29-Oct-26 A	04-Nov-26	0.00
B6.33 42 11.31-1	Embedment & Test(Rem)	2.84	1	16-Sep-26	19-Sep-26	31-Oct-26 A	04-Nov-26	19,084.42
B6.33 42 11.31-1	Backfilling & Warrning Tape(Rem)	3.12	1	20-Sep-26	24-Sep-26	02-Nov-26 A	04-Nov-26	9,232.93
Depth From 3.5m to 4.5m		4.26	4	16-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	54,983.58
B6.33 42 11.31-1	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	3,434.57
B6.33 42 11.31-1	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	30,926.37
B6.33 42 11.31-1	Embedment & Test(Rem)	2.84	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	13,753.49
B6.33 42 11.31-1	Backfilling & Warrning Tape(Rem)	2.94	1	21-Sep-26	24-Sep-26	05-Nov-26	09-Nov-26	6,869.15
Manholes		5.00	4	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	20,661.93
?1500		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	2,481.67
Depth From 2.5m to 3.5m		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	2,481.67
B6.33 05 39.01.33	Test, Internal Finishing, Benching & Cover	5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	2,481.67
?2000		5.00	3	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	18,180.26
Depth From 2.5m to 3.5m		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	7,095.17
B6.33 05 39.01.34	Test, Internal Finishing, Benching & Cover	5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	7,095.17
Depth From 3.5m to 4.5m		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	8,714.14
B6.33 05 39.01.34	Test, Internal Finishing, Benching & Cover	5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	8,714.14
Depth From 4.5m to 5.5m		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	2,370.95
B6.33 05 39.01.35	Test, Internal Finishing, Benching & Cover	5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	2,370.95
Catch Basins		24.12	5	19-Sep-26	26-Oct-26	17-Oct-26 A	07-Nov-26	100,333.66
Single		18.12	4	19-Sep-26	19-Oct-26	17-Oct-26 A	07-Nov-26	89,817.57
B6.33 05 40.01.330	Excavation, Compaction & Vapour Barrier	3.00	1	19-Sep-26	21-Sep-26	17-Oct-26 A	05-Nov-26	13,519.66
B6.33 05 40.01.340	Blinding Conc.	3.00	1	22-Sep-26	26-Sep-26	18-Oct-26 A	05-Nov-26	8,993.51
B6.33 05 40.01.350	Catch Basin Installation	4.00	1	27-Sep-26	30-Sep-26	19-Oct-26 A	05-Nov-26	40,382.64
B6.33 05 40.01.360	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	13-Oct-26	19-Oct-26	19-Oct-26 A	07-Nov-26	26,921.76
Double		6.00	1	20-Oct-26	26-Oct-26	19-Oct-26 A	07-Nov-26	10,516.10
B6.33 05 40.01.840	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	20-Oct-26	26-Oct-26	19-Oct-26 A	07-Nov-26	10,516.10
Dry Networks		5.00	3	16-Sep-26	21-Sep-26	21-Nov-26	26-Nov-26	118,701.38
Street Lighting		5.00	3	16-Sep-26	21-Sep-26	21-Nov-26	26-Nov-26	118,701.38
SL Poles		5.00	2	16-Sep-26	21-Sep-26	21-Nov-26	26-Nov-26	117,797.00
Pole (10 M Single Arm)		5.00	2	16-Sep-26	21-Sep-26	21-Nov-26	26-Nov-26	117,797.00
B2.33 71 16.63	Excavation	2.00	1	16-Sep-26	17-Sep-26	21-Nov-26	23-Nov-26	58,898.50
B2.33 71 16.64	PC & RC Foundation	3.00	1	19-Sep-26	21-Sep-26	23-Nov-26	26-Nov-26	58,898.50
Earthing		2.00	1	19-Sep-26	20-Sep-26	23-Nov-26	25-Nov-26	904.39
B2.33 71 19 32	Land Adjustment	2.00	1	19-Sep-26	20-Sep-26	23-Nov-26	25-Nov-26	904.39
Earth & Road Works		11.00	4	28-Sep-26	17-Oct-26	08-Nov-26	21-Nov-26	823,404.07

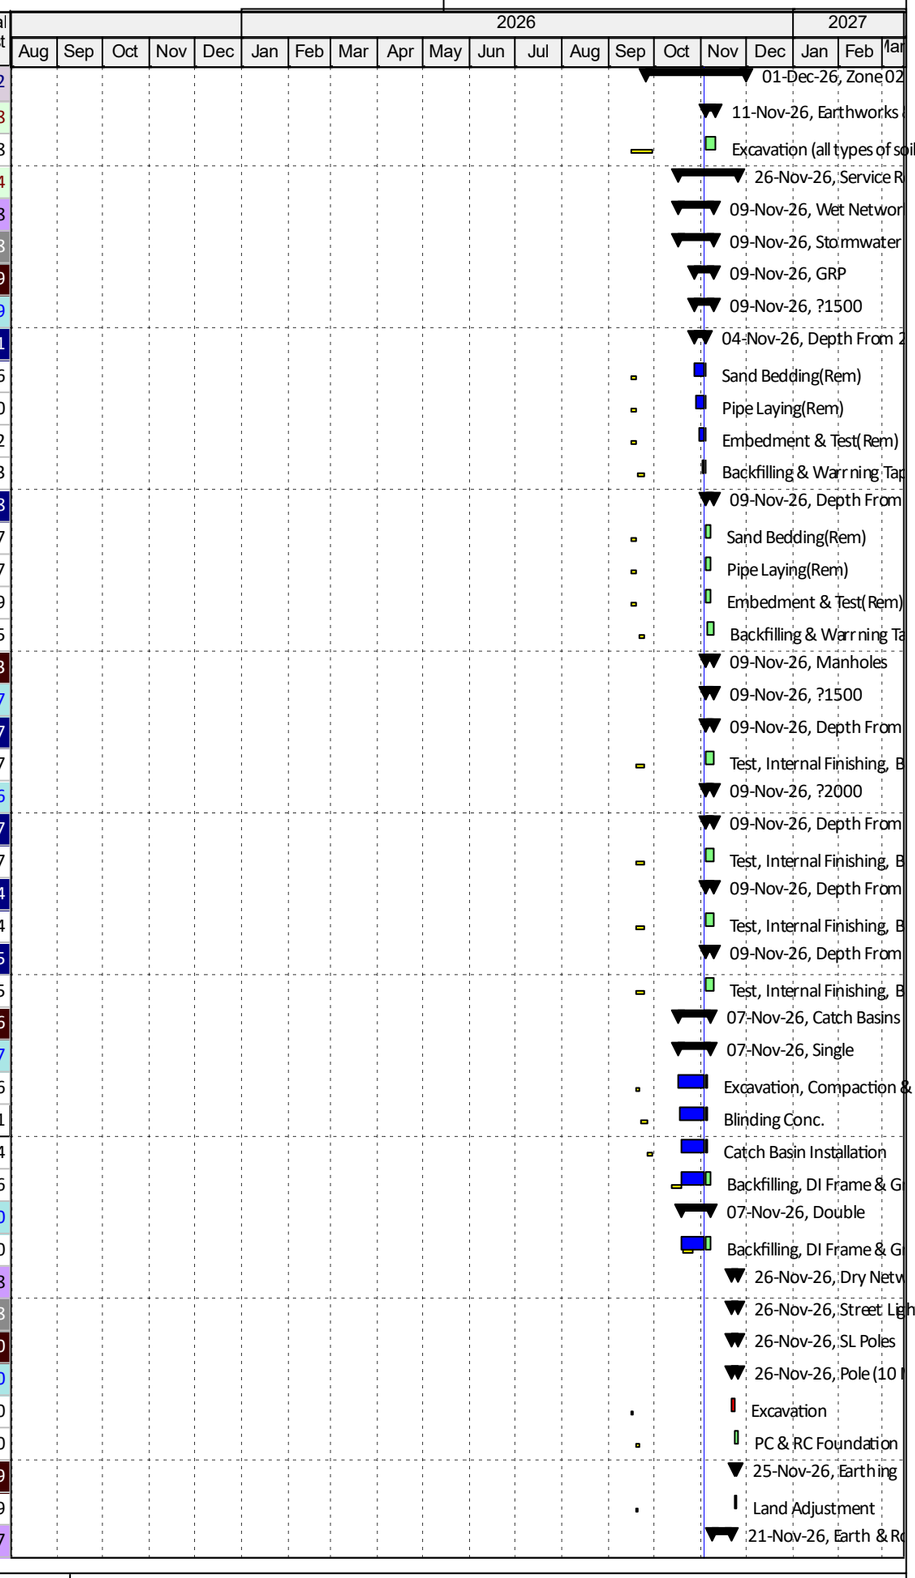


Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Earth Works		2.00	1	28-Sep-26	01-Oct-26	08-Nov-26	10-Nov-26	273,448.67
B1.2.31 23 16.01.9	Roadway Excavation	2.00	1	28-Sep-26	01-Oct-26	08-Nov-26	10-Nov-26	273,448.67
Earth Layers		4.00	2	01-Oct-26	06-Oct-26	10-Nov-26	15-Nov-26	142,496.14
B1.2.32 11 13.01.9	Subgrade	2.00	1	01-Oct-26	04-Oct-26	10-Nov-26	12-Nov-26	48,448.61
B1.2.32 11 23.01.9	Aggregate Base Course	2.00	1	04-Oct-26	06-Oct-26	12-Nov-26	15-Nov-26	94,047.54
Asphalt Layers		5.00	1	06-Oct-26	17-Oct-26	15-Nov-26	21-Nov-26	407,459.26
B1.2.32 11 26.01.9	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	5.00	1	06-Oct-26	17-Oct-26	15-Nov-26	21-Nov-26	407,459.26
Entrance Road 01		44.32	31	16-Sep-26	07-Dec-26	07-Oct-26 A	28-Nov-26	994,637.23
Wet Networks		26.00	7	16-Sep-26	28-Sep-26	07-Oct-26 A	05-Nov-26	76,450.25
Sewerage Network		3.58	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	8,222.09
GRP Pipes		3.58	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	8,222.09
?200		3.58	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	8,222.09
Depth From 0.0m - 1.5m		3.58	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	8,222.09
B5.33 31 00.01.21	Embedment & Test(Rem)	3.58	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	8,222.09
Stormwater Network		26.00	6	16-Sep-26	28-Sep-26	07-Oct-26 A	05-Nov-26	68,228.17
Manholes		2.00	2	16-Sep-26	27-Sep-26	04-Nov-26	05-Nov-26	1,262.81
?1500		2.00	1	24-Sep-26	27-Sep-26	04-Nov-26	05-Nov-26	198.53
Depth From 2.5m to 3.5m		2.00	1	24-Sep-26	27-Sep-26	04-Nov-26	05-Nov-26	198.53
B6.33 05 13.05.05	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	24-Sep-26	27-Sep-26	04-Nov-26	05-Nov-26	198.53
?2000		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,064.27
Depth From 2.5m to 3.5m		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,064.27
B6.33 05 13.07.05	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,064.27
Catch Basins		2.09	4	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	66,965.36
UPVC		2.09	4	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	66,965.36
?300 From 0.0 to 1.5m		2.09	2	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	60,708.40
B6.33 42 11.35-10	Catch Basin Opening Prep.(Rem)	2.09	1	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	4,636.48
B6.33 42 11.35-10	Fittings & Pipe Installation(Rem)	2.00	1	24-Sep-26	27-Sep-26	07-Oct-26 A	04-Nov-26	56,071.92
?400 From 0.0 to 1.5m		2.09	2	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	6,256.96
B6.33 42 11.36-11	Catch Basin Opening Prep.(Rem)	2.09	1	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	1,251.39
B6.33 42 11.36-11	Fittings & Pipe Installation(Rem)	2.09	1	24-Sep-26	28-Sep-26	07-Oct-26 A	04-Nov-26	5,005.57
Dry Networks		20.00	5	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	254,848.76
Medium Voltage Network		20.00	5	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	254,848.76
Duct Banks		10.00	2	16-Sep-26	28-Sep-26	04-Nov-26	15-Nov-26	9,850.97
4 Way		10.00	2	16-Sep-26	28-Sep-26	04-Nov-26	15-Nov-26	9,850.97
B2.31 23 00.602	Excavation	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	3,411.59
B2.33 71 00.212	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	7.00	1	20-Sep-26	28-Sep-26	08-Nov-26	15-Nov-26	6,439.38
Cables		10.00	3	29-Sep-26	10-Oct-26	16-Nov-26	26-Nov-26	244,997.79
3C,500mm2		10.00	3	29-Sep-26	10-Oct-26	16-Nov-26	26-Nov-26	244,997.79
B2.33 71 49.23.68	Cable 13.8 kV Unarmored	4.00	1	29-Sep-26	03-Oct-26	16-Nov-26	19-Nov-26	234,058.34
B2.33 71 49.23.69	Straight joints cables	3.00	1	04-Oct-26	06-Oct-26	21-Nov-26	23-Nov-26	7,880.95
B2.33 71 49.23.70	Cable Termination	3.00	1	07-Oct-26	10-Oct-26	24-Nov-26	26-Nov-26	3,058.50
Earth & Road Works		28.32	13	05-Oct-26	07-Nov-26	25-Oct-26 A	26-Nov-26	484,035.55
Earth Layers		10.23	2	05-Oct-26	12-Oct-26	25-Oct-26 A	05-Nov-26	37,900.61
B1.2.32 11 13.01.4_R	Subgrade(Rem)	1.05	1	05-Oct-26	07-Oct-26	25-Oct-26 A	04-Nov-26	11,576.45
B1.2.32 11 23.01.4_R	Aggregate Base Course(Rem)	1.23	1	08-Oct-26	12-Oct-26	04-Nov-26	05-Nov-26	26,324.16
Curbstone		12.00	6	06-Oct-26	19-Oct-26	12-Nov-26	26-Nov-26	55,128.31

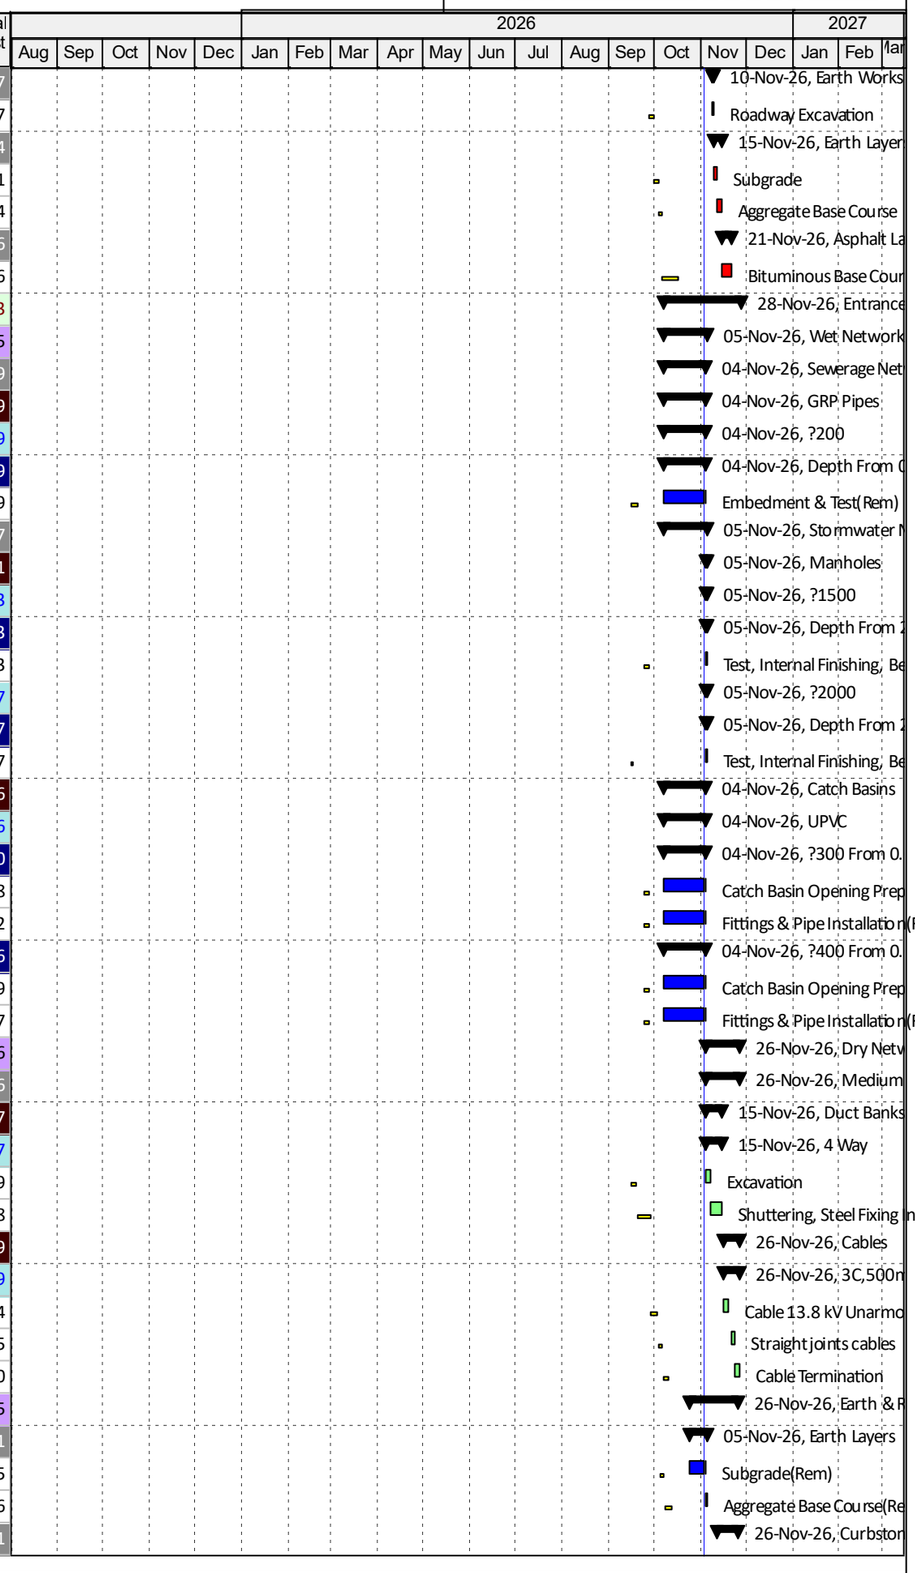

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Pre-Installation		6.00	3	06-Oct-26	12-Oct-26	12-Nov-26	19-Nov-26	29,135.01
B2.31 23 00.91	Excavation	2.00	1	06-Oct-26	07-Oct-26	12-Nov-26	15-Nov-26	9,711.67
B1.2.32 14 13.13.24	PCC	2.00	1	08-Oct-26	10-Oct-26	15-Nov-26	17-Nov-26	9,711.67
32 16 13.004	Haunching	2.00	1	11-Oct-26	12-Oct-26	17-Nov-26	19-Nov-26	9,711.67
Installation		6.00	3	13-Oct-26	19-Oct-26	19-Nov-26	26-Nov-26	25,993.29
B1.2.32 16.13.01.4	Curb Stone, Type K1	2.00	1	13-Oct-26	14-Oct-26	19-Nov-26	22-Nov-26	14,090.47
B1.2.32 16.13.03.4	Edge Curb, Type K4	2.00	1	15-Oct-26	17-Oct-26	22-Nov-26	24-Nov-26	7,079.35
B1.2.32 16.13.044	Heel Curb, Type K5	2.00	1	18-Oct-26	19-Oct-26	24-Nov-26	26-Nov-26	4,823.47
Asphalt Layers		7.00	2	22-Oct-26	02-Nov-26	09-Nov-26	16-Nov-26	387,364.09
B1.2.32 11 26.01.4	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	22-Oct-26	27-Oct-26	09-Nov-26	10-Nov-26	278,101.76
B1.2.32 12 16.01.4	Bituminous concrete Wearing Course, including tack coat (RC2)	5.00	1	28-Oct-26	02-Nov-26	11-Nov-26	16-Nov-26	109,262.33
Pavement Marking		2.00	2	03-Nov-26	07-Nov-26	17-Nov-26	18-Nov-26	2,772.10
B1.2.32 17 23.01.4	Retroreflective Thermoplastic White Traffic lines	2.00	1	03-Nov-26	04-Nov-26	17-Nov-26	18-Nov-26	1,873.94
B1.2.32 17 23.02.4	Retroreflective Thermoplastic Yellow, Traffic lines	2.00	1	05-Nov-26	07-Nov-26	17-Nov-26	18-Nov-26	898.16
Traffic Signs		2.00	1	08-Oct-26	10-Oct-26	12-Nov-26	15-Nov-26	870.43
Pre-Installation		2.00	1	08-Oct-26	10-Oct-26	12-Nov-26	15-Nov-26	870.43
B2.31 23 00.101	Excavation	2.00	1	08-Oct-26	10-Oct-26	12-Nov-26	15-Nov-26	870.43
Landscape		18.82	6	11-Oct-26	07-Dec-26	05-Nov-26	28-Nov-26	179,302.67
Fences		11.00	2	11-Oct-26	22-Oct-26	15-Nov-26	28-Nov-26	96,086.61
Steel fence (ZATCA HCIS)		5.00	1	11-Oct-26	15-Oct-26	15-Nov-26	21-Nov-26	25,743.45
B7.32 93 43.04.14	Earthwork	5.00	1	11-Oct-26	15-Oct-26	15-Nov-26	21-Nov-26	25,743.45
Steel fence (MODON)		6.00	1	17-Oct-26	22-Oct-26	21-Nov-26	28-Nov-26	70,343.16
B7.32 93 43.04.12	Earthwork	6.00	1	17-Oct-26	22-Oct-26	21-Nov-26	28-Nov-26	70,343.16
Geotextile		5.00	1	03-Nov-26	08-Nov-26	05-Nov-26	11-Nov-26	17,676.73
B7.31 32 19.23.2	Geotextile to protect trees planting soil	5.00	1	03-Nov-26	08-Nov-26	05-Nov-26	11-Nov-26	17,676.73
Trees		10.50	3	01-Dec-26	07-Dec-26	08-Nov-26	19-Nov-26	65,539.33
B7.32 93 43.01	Azadirachta indica	3.00	1	01-Dec-26	03-Dec-26	08-Nov-26	11-Nov-26	18,253.67
B7.32 93 43.04	Delonix Regia	3.00	1	05-Dec-26	07-Dec-26	17-Nov-26	19-Nov-26	19,470.55
B7.32 93 43.06	Schinus Molle	3.00	1	05-Dec-26	07-Dec-26	17-Nov-26	19-Nov-26	27,815.11
Entrance Road 02		45.00	66	16-Sep-26	08-Nov-26	07-Oct-26 A	28-Nov-26	1,554,019.96
Wet Networks		45.00	38	16-Sep-26	07-Nov-26	07-Oct-26 A	28-Nov-26	313,721.43
Sewerage Network		21.00	9	16-Sep-26	15-Oct-26	04-Nov-26	28-Nov-26	22,973.21
Manholes ?1200		2.56	2	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,543.09
Depth From 0.0m to 1.5m		2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,421.30
B5.33 05 13.01 4_R	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,421.30
Depth From 1.5m to 2.5m		2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	4,121.79
B5.33 05 13.02 4_R	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	4,121.79
Sewerage Plot Connection		12.00	2	01-Oct-26	14-Oct-26	11-Nov-26	25-Nov-26	1,287.37
B5..33 31 16.011	Excavation	10.00	1	01-Oct-26	12-Oct-26	11-Nov-26	23-Nov-26	1,029.90
B5..33 31 16.012	Sand Bedding	2.00	1	13-Oct-26	14-Oct-26	23-Nov-26	25-Nov-26	257.47
Discharge Chamber		21.00	5	16-Sep-26	15-Oct-26	04-Nov-26	28-Nov-26	16,142.75
B5.33 05 63.011	Excavation & Compaction	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,409.37
B5.33 05 63.012	Blinding Conc, & RC Base	3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	1,686.56
B5.33 05 63.013	Chamber Installation	6.00	1	29-Sep-26	05-Oct-26	11-Nov-26	17-Nov-26	7,228.10
B5.33 05 63.014	Test, Internal Finishing, Benching & Cover	4.00	1	06-Oct-26	10-Oct-26	18-Nov-26	22-Nov-26	1,686.56
B5.33 05 63.015	Backfilling	5.00	1	11-Oct-26	15-Oct-26	23-Nov-26	28-Nov-26	3,132.18

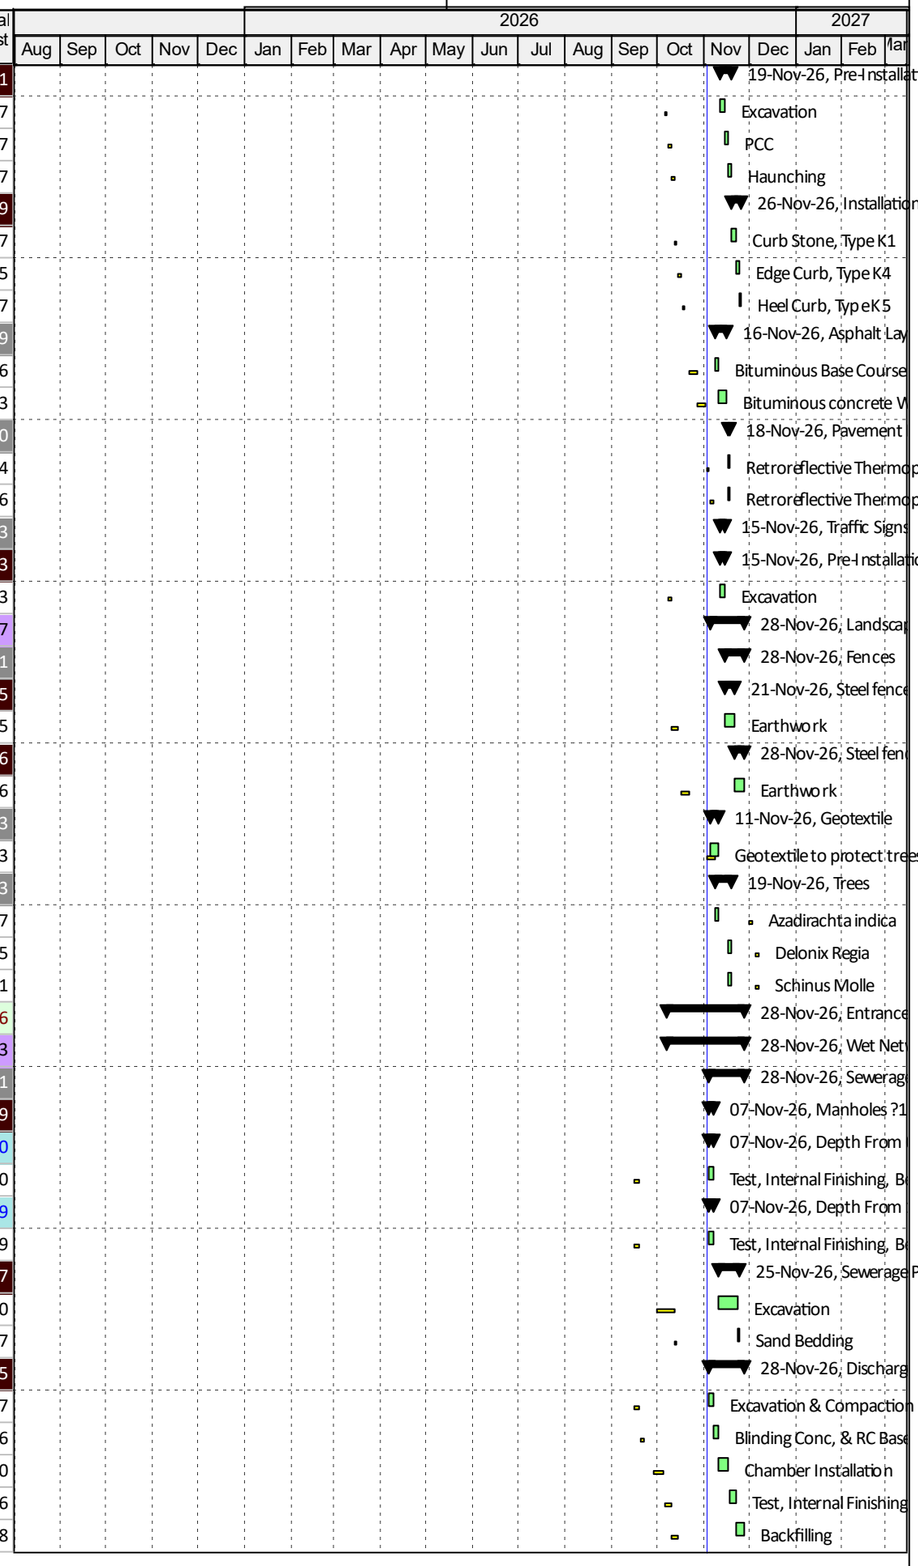

Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Stormwater Network		26.00	12	16-Sep-26	07-Oct-26	07-Oct-26 A	05-Nov-26	97,867.78
GRP		4.00	1	16-Sep-26	20-Sep-26	28-Oct-26 A	05-Nov-26	236.29
?400		4.00	1	16-Sep-26	20-Sep-26	28-Oct-26 A	05-Nov-26	236.29
Depth From 1.5m to 2.5m		4.00	1	16-Sep-26	20-Sep-26	28-Oct-26 A	05-Nov-26	236.29
B6.33 42 11.02 5_	Backfilling & Warning Tape(Rem)	4.00	1	16-Sep-26	20-Sep-26	28-Oct-26 A	05-Nov-26	236.29
Manholes		2.00	2	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,892.07
?1200		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,040.65
Depth From 1.5m to 2.5m		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,040.65
B6.33 05 13.01 4_	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,040.65
?2000		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	851.42
Depth From 2.5m to 3.5m		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	851.42
B6.33 05 13.07 4_	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	851.42
Catch Basins		18.00	9	16-Sep-26	07-Oct-26	07-Oct-26 A	05-Nov-26	94,739.42
Single		2.00	1	16-Sep-26	17-Sep-26	14-Oct-26 A	04-Nov-26	2,692.18
B6.33 05 40.01.21(	Excavation, Compaction & Vapour Barrier(Rem)	2.00	1	16-Sep-26	17-Sep-26	14-Oct-26 A	04-Nov-26	2,692.18
Double		11.28	4	19-Sep-26	07-Oct-26	14-Oct-26 A	05-Nov-26	35,153.79
B6.33 05 40.01.800	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	01-Oct-26	07-Oct-26	14-Oct-26 A	05-Nov-26	10,516.10
B6.33 05 40.01.770	Excavation, Compaction & Vapour Barrier	3.00	1	19-Sep-26	21-Sep-26	17-Oct-26 A	04-Nov-26	5,258.04
B6.33 05 40.01.780	Blinding Conc.	3.00	1	22-Sep-26	26-Sep-26	18-Oct-26 A	04-Nov-26	3,455.28
B6.33 05 40.01.790	Catch Basin Installation	4.00	1	27-Sep-26	30-Sep-26	19-Oct-26 A	04-Nov-26	15,924.38
UPVC		12.00	4	16-Sep-26	30-Sep-26	07-Oct-26 A	04-Nov-26	56,893.45
?300 From 0.0 to 1.5m		2.09	2	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	44,801.47
B6.33 42 11.35 1_	Catch Basin Opening Prep.(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	8,960.29
B6.33 42 11.35 2_	Fittings & Pipe Installation(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	35,841.17
?400 From 0.0 to 1.5m		2.00	2	29-Sep-26	30-Sep-26	10-Oct-26 A	04-Nov-26	12,091.99
B6.33 42 11.36 1_	Catch Basin Opening Prep.(Rem)	2.00	1	29-Sep-26	30-Sep-26	10-Oct-26 A	04-Nov-26	2,418.40
B6.33 42 11.36 2_	Fittings & Pipe Installation(Rem)	2.00	1	29-Sep-26	30-Sep-26	11-Oct-26 A	04-Nov-26	9,673.59
Potable Water Network		30.00	8	06-Oct-26	07-Nov-26	24-Oct-26 A	25-Nov-26	69,659.45
Plots and Buildings Crossing		10.00	2	06-Oct-26	17-Oct-26	14-Nov-26	25-Nov-26	537.34
B3.33 14 13.02.011	Earthwork	7.00	1	06-Oct-26	13-Oct-26	14-Nov-26	22-Nov-26	268.67
B3.33 14 13.02.012	Sand Bedding	3.00	1	14-Oct-26	17-Oct-26	22-Nov-26	25-Nov-26	268.67
Valves & Chambers		30.00	6	14-Oct-26	07-Nov-26	24-Oct-26 A	10-Nov-26	69,122.11
Gate Valves		3.00	1	27-Oct-26	29-Oct-26	07-Nov-26	10-Nov-26	2,550.47
Gate valves dia (110) mm		3.00	1	27-Oct-26	29-Oct-26	07-Nov-26	10-Nov-26	2,550.47
B3.33 14 19.01.1(	Spindle & Surface Box	3.00	1	27-Oct-26	29-Oct-26	07-Nov-26	10-Nov-26	2,550.47
Washout Valves		30.00	5	14-Oct-26	07-Nov-26	24-Oct-26 A	07-Nov-26	66,571.64
Washout valves on 110-400 mm. (In Chamber)		30.00	5	14-Oct-26	07-Nov-26	24-Oct-26 A	07-Nov-26	66,571.64
B3.33 05 63.01.01	Land Adjustment & Compaction	3.00	1	14-Oct-26	17-Oct-26	24-Oct-26 A	05-Nov-26	9,985.75
B3.33 05 63.01.01	Foundations	4.00	1	18-Oct-26	21-Oct-26	25-Oct-26 A	05-Nov-26	13,314.33
B3.33 05 63.01.01	Chambers Walls Conc Cast In Situ	4.00	1	22-Oct-26	26-Oct-26	29-Oct-26 A	05-Nov-26	13,314.33
B3.33 05 63.01.01	Chamber Curing, Finishing & Steel Cover	5.00	1	27-Oct-26	01-Nov-26	31-Oct-26 A	07-Nov-26	9,985.75
B3.33 05 63.01.01	Valve & Fitting Installation	5.00	1	02-Nov-26	07-Nov-26	02-Nov-26 A	07-Nov-26	19,971.49
Fire Fighting Network		20.00	9	16-Sep-26	19-Oct-26	04-Nov-26	26-Nov-26	123,221.00
Valves & Chambers		20.00	6	16-Sep-26	19-Oct-26	04-Nov-26	26-Nov-26	41,144.57
Gate Valves		12.00	2	16-Sep-26	12-Oct-26	04-Nov-26	17-Nov-26	6,070.71
Gate valves dia (250) mm		12.00	2	16-Sep-26	12-Oct-26	04-Nov-26	17-Nov-26	6,070.71

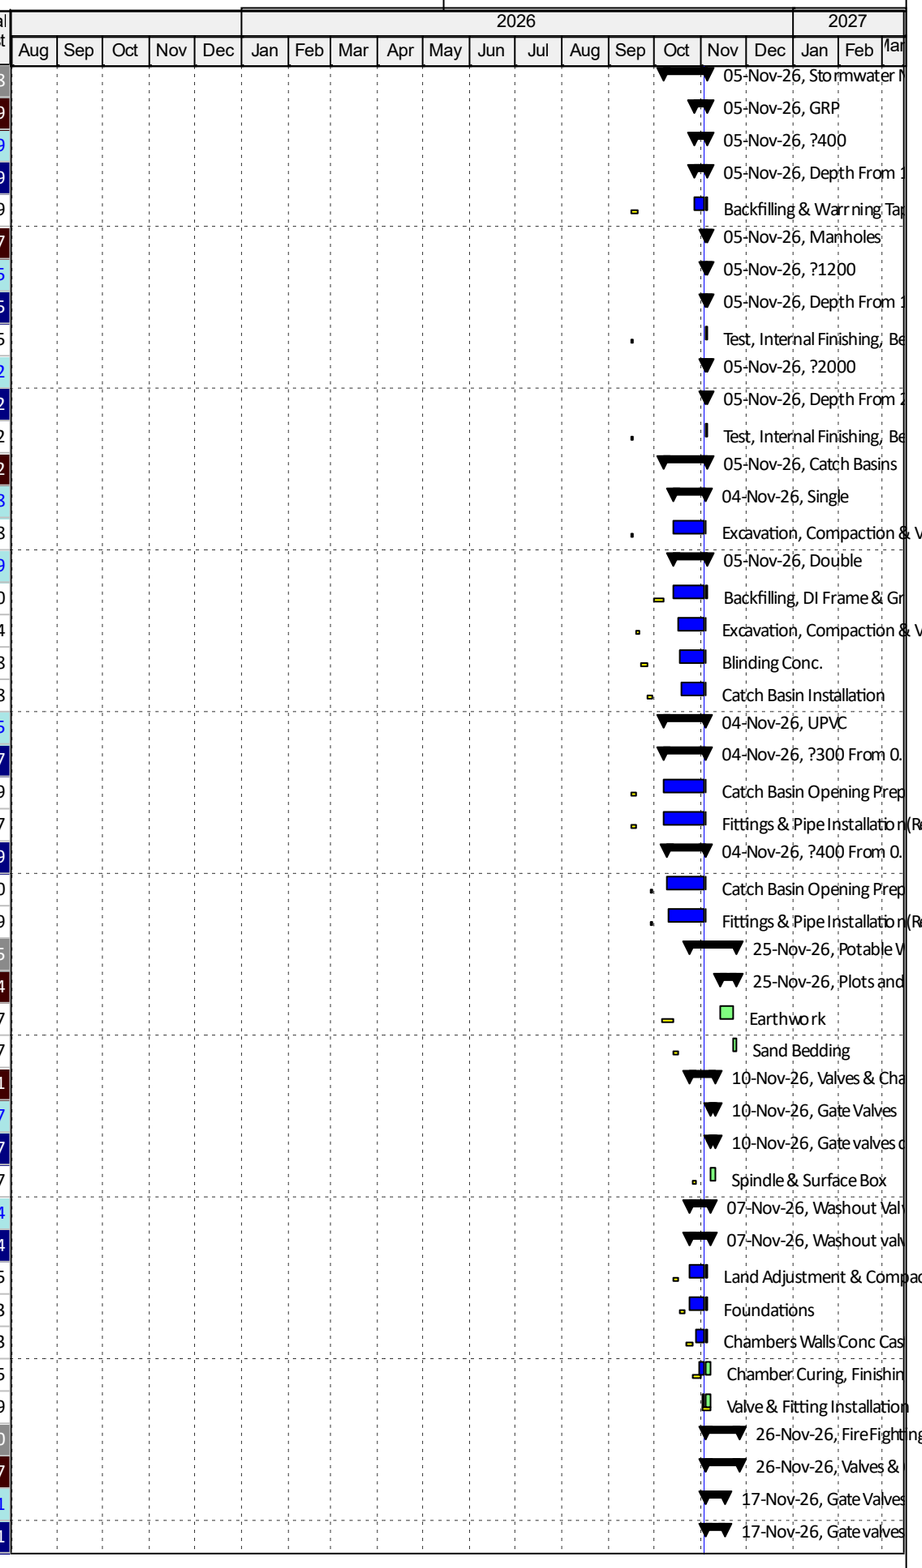


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 14 19.01.12	Burried Isolation Valve Installation(Rem)	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	1,053.59
B3.33 14 19.01.12	Spindle & Surface Box	4.00	1	08-Oct-26	12-Oct-26	14-Nov-26	17-Nov-26	5,017.11
Washout Valves		20.00	4	21-Sep-26	19-Oct-26	04-Nov-26	26-Nov-26	35,073.86
Washout valves on 110-400 mm. (In Chamber)		20.00	4	21-Sep-26	19-Oct-26	04-Nov-26	26-Nov-26	35,073.86
B3.33 05 63.01.42	Land Adjustment & Compaction	4.00	1	21-Sep-26	26-Sep-26	04-Nov-26	08-Nov-26	7,932.00
B3.33 05 63.01.40	Foundations	5.00	1	27-Sep-26	01-Oct-26	09-Nov-26	14-Nov-26	9,649.37
B3.33 05 63.01.43	Chambers Walls Conc Cast In Situ	5.00	1	03-Oct-26	07-Oct-26	15-Nov-26	19-Nov-26	9,870.62
B3.33 05 63.01.41	Chamber Curing, Finishing & Steel Cover	6.00	1	13-Oct-26	19-Oct-26	21-Nov-26	26-Nov-26	7,621.88
Fire Hydrant		16.00	3	21-Sep-26	10-Oct-26	04-Nov-26	22-Nov-26	82,076.43
B3.33 14 19.01.fh23	Riser Pipe & Flanged Fittings Installation	4.00	1	21-Sep-26	26-Sep-26	04-Nov-26	08-Nov-26	16,415.29
B3.33 14 19.01.fh22	Firehydrant Fixing/Installation	5.00	1	27-Sep-26	01-Oct-26	09-Nov-26	14-Nov-26	49,245.86
B3.33 14 19.01.fh24	Backfilling & Compaction	7.00	1	03-Oct-26	10-Oct-26	15-Nov-26	22-Nov-26	16,415.29
Dry Networks		17.50	25	08-Oct-26	08-Nov-26	05-Nov-26	25-Nov-26	774,926.94
Medium Voltage Network		17.00	3	08-Oct-26	27-Oct-26	05-Nov-26	25-Nov-26	31,882.63
Duct Banks		17.00	3	08-Oct-26	27-Oct-26	05-Nov-26	25-Nov-26	31,882.63
2 Way		17.00	3	08-Oct-26	27-Oct-26	05-Nov-26	25-Nov-26	31,882.63
B2.31 23 00.638	Excavation	4.00	1	08-Oct-26	12-Oct-26	05-Nov-26	10-Nov-26	8,056.11
B2.33 71 00.284	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	7.00	1	13-Oct-26	20-Oct-26	10-Nov-26	18-Nov-26	15,770.40
B2.33 71 00.285	Backfilling & Warrning Tape	6.00	1	21-Oct-26	27-Oct-26	18-Nov-26	25-Nov-26	8,056.11
Street Lighting		15.00	11	22-Oct-26	08-Nov-26	09-Nov-26	25-Nov-26	483,299.88
SL Poles		14.00	9	22-Oct-26	07-Nov-26	09-Nov-26	24-Nov-26	414,804.20
Pole (10 M Single Arm)		14.00	5	22-Oct-26	07-Nov-26	09-Nov-26	24-Nov-26	317,671.69
B2.33 71 16.43	Excavation	2.00	1	22-Oct-26	24-Oct-26	09-Nov-26	10-Nov-26	58,898.50
B2.33 71 16.44	PC & RC Foundation	3.00	1	25-Oct-26	27-Oct-26	11-Nov-26	14-Nov-26	58,898.50
B2.33 71 16.45	Lighting Poles Installation Incl power box, Cables	3.00	1	28-Oct-26	31-Oct-26	15-Nov-26	17-Nov-26	117,797.00
B2.26.56.19.4	Lighting Luminares Inst	3.00	1	01-Nov-26	03-Nov-26	18-Nov-26	21-Nov-26	23,179.20
B2.33 71 16.46	Backfilling, Grouting & Chamfering	3.00	1	04-Nov-26	07-Nov-26	22-Nov-26	24-Nov-26	58,898.50
Pole (10 M Double Arm)		12.00	4	25-Oct-26	07-Nov-26	11-Nov-26	24-Nov-26	97,132.51
B2.33 71 16.47	Excavation	2.00	1	25-Oct-26	26-Oct-26	11-Nov-26	12-Nov-26	18,488.33
B2.33 71 16.48	PC & RC Foundation	4.00		27-Oct-26	31-Oct-26	14-Nov-26	17-Nov-26	18,488.33
B2.33 71 16.49	Lighting Poles Installation Incl power box, Cables	3.00	1	01-Nov-26	03-Nov-26	18-Nov-26	21-Nov-26	36,976.66
B2.26.56.19.5	Lighting Luminares Inst	3.00	1	04-Nov-26	07-Nov-26	22-Nov-26	24-Nov-26	23,179.20
SL Pillars		4.00	2	04-Nov-26	08-Nov-26	22-Nov-26	25-Nov-26	68,495.68
B2.33 71 26 031	Pillars Installation (Internal Wiring)	2.00	1	04-Nov-26	05-Nov-26	22-Nov-26	23-Nov-26	16,342.35
B2.33 71 26 042	KWH meter mounting aframe installation	2.00	1	07-Nov-26	08-Nov-26	24-Nov-26	25-Nov-26	52,153.33
Telecommunication Network		8.00	11	21-Oct-26	29-Oct-26	17-Nov-26	25-Nov-26	259,744.43
Ducts		8.00	11	21-Oct-26	29-Oct-26	17-Nov-26	25-Nov-26	259,744.43
Size (6*50mm) HDPE ducts		4.00	2	21-Oct-26	25-Oct-26	17-Nov-26	21-Nov-26	141,841.38
B2.1.33 81 26.84	Excavation	2.00	1	21-Oct-26	22-Oct-26	17-Nov-26	18-Nov-26	35,460.35
B2.1.33 81 26.85	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	24-Oct-26	25-Oct-26	19-Nov-26	21-Nov-26	106,381.04
Size (6*50mm+2*32mm) HDPE ducts		6.00	3	24-Oct-26	29-Oct-26	19-Nov-26	25-Nov-26	106,245.26
B2.1.33 81 26.87	Excavation	2.00	1	24-Oct-26	25-Oct-26	19-Nov-26	21-Nov-26	21,251.23
B2.1.33 81 26.88	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	26-Oct-26	27-Oct-26	22-Nov-26	23-Nov-26	63,742.79
B2.1.33 81 26.89	Backfilling & Warrning Tape	2.00	1	28-Oct-26	29-Oct-26	24-Nov-26	25-Nov-26	21,251.23
Size (2*32mm) HDPE ducts		6.00	3	24-Oct-26	29-Oct-26	19-Nov-26	25-Nov-26	6,720.24
B2.1.33 81 26.93	Excavation	2.00	1	24-Oct-26	25-Oct-26	19-Nov-26	21-Nov-26	1,344.05

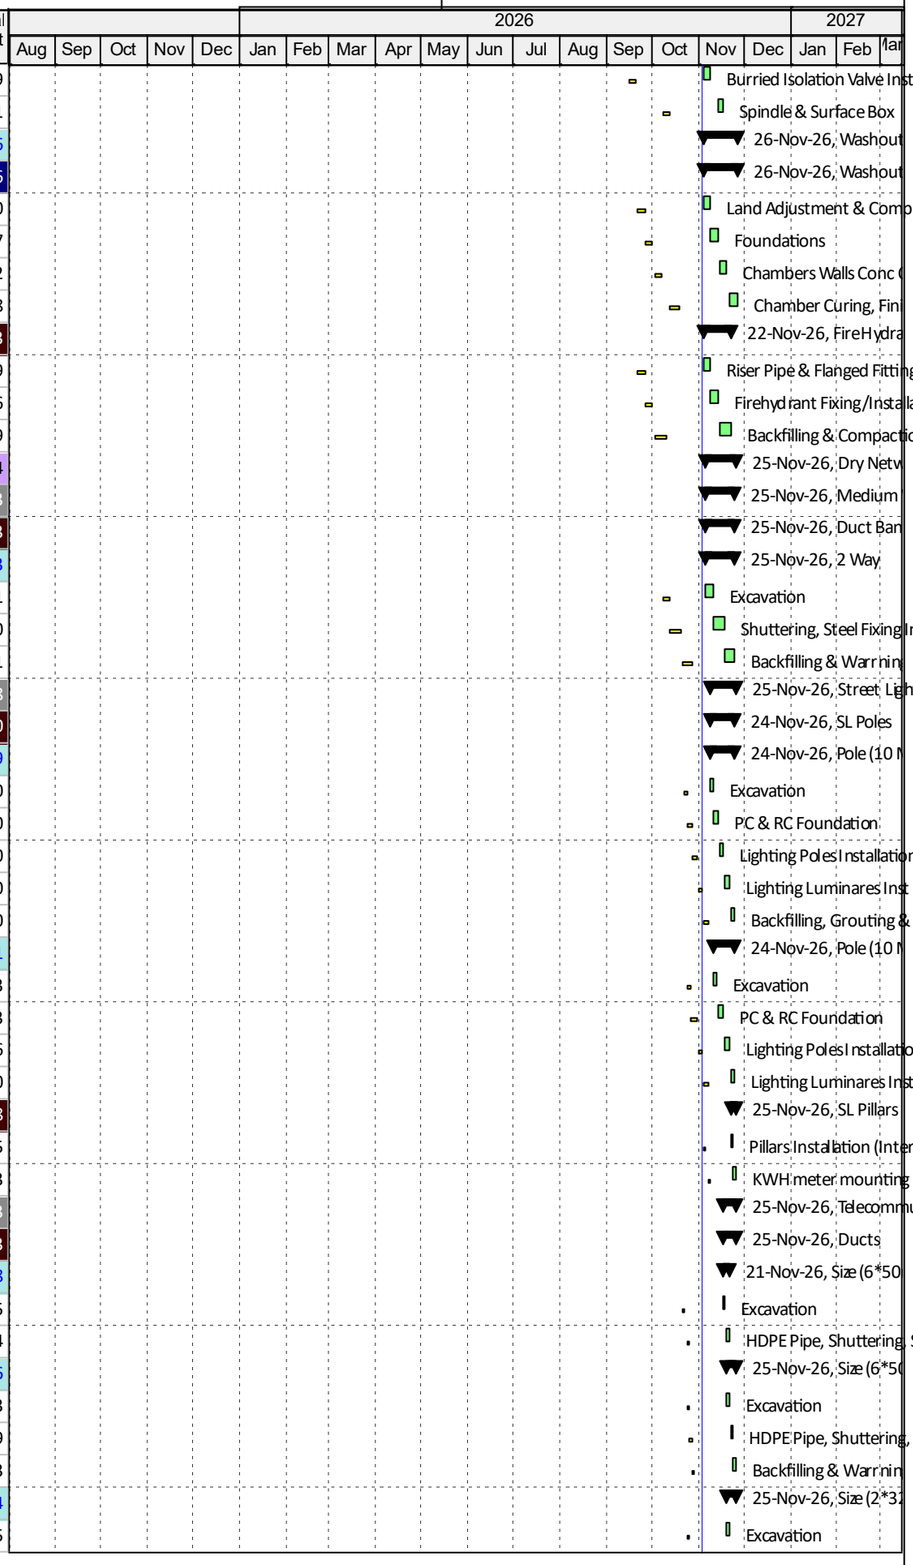

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.1.33 81 26.94	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	26-Oct-26	27-Oct-26	22-Nov-26	23-Nov-26	4,032.14
B2.1.33 81 26.95	Backfilling & Warning Tape	2.00	1	28-Oct-26	29-Oct-26	24-Nov-26	25-Nov-26	1,344.05
Size (4*32mm) HDPE ducts		4.00	2	26-Oct-26	29-Oct-26	22-Nov-26	25-Nov-26	4,398.81
B2.1.33 81 26.96	Excavation	2.00	1	26-Oct-26	27-Oct-26	22-Nov-26	23-Nov-26	1,099.70
B2.1.33 81 26.97	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	28-Oct-26	29-Oct-26	24-Nov-26	25-Nov-26	3,299.11
Size (6*50mm+6*32mm) HDPE ducts		2.00	1	28-Oct-26	29-Oct-26	24-Nov-26	25-Nov-26	538.74
B2.1.33 81 26.99	Excavation	2.00	1	28-Oct-26	29-Oct-26	24-Nov-26	25-Nov-26	538.74
Earth & Road Works		12.00	3	06-Oct-26	21-Oct-26	26-Oct-26 A	08-Nov-26	465,371.58
Earth Layers		10.00	2	06-Oct-26	15-Oct-26	26-Oct-26 A	05-Nov-26	59,104.78
B1.2.32 11 13.01.5_R	Subgrade(Rem)	2.00	1	06-Oct-26	10-Oct-26	26-Oct-26 A	04-Nov-26	16,907.39
B1.2.32 11 23.01.5_R	Aggregate Base Course(Rem)	2.00	1	11-Oct-26	15-Oct-26	04-Nov-26	05-Nov-26	42,197.40
Asphalt Layers		2.00	1	17-Oct-26	21-Oct-26	07-Nov-26	08-Nov-26	406,266.80
B1.2.32 11 26.01.5	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	17-Oct-26	21-Oct-26	07-Nov-26	08-Nov-26	406,266.80
Management Road 01		44.32	73	16-Sep-26	11-Nov-26	07-Oct-26 A	28-Nov-26	2,637,280.10
Wet Networks		44.00	47	16-Sep-26	13-Oct-26	07-Oct-26 A	26-Nov-26	1,133,618.74
Stormwater Network		26.00	11	16-Sep-26	19-Sep-26	07-Oct-26 A	05-Nov-26	125,876.41
GRP		2.84	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	4,758.57
?1100		2.84	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	4,758.57
Depth From 2.5m to 3.5m		2.84	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	4,758.57
B6.33 42 11.01-1C	Embedment & Test(Rem)	2.84	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	4,758.57
Manholes		2.00	2	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,051.36
?1500		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	223.35
Depth From 2.5m to 3.5m		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	223.35
B6.33 05 39.01.3C	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	223.35
?2000		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	828.01
Depth From 2.5m to 3.5m		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	828.01
B6.33 05 39.01.31	Test, Internal Finishing, Benching & Cover(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	828.01
Catch Basins		26.00	8	16-Sep-26	19-Sep-26	07-Oct-26 A	05-Nov-26	120,066.48
Single		2.00	4	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	8,078.29
B6.33 05 40.01.26(	Blinding Conc.(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	809.42
B6.33 05 40.01.27(	Catch Basin Installation(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	3,634.44
B6.33 05 40.01.25(	Excavation, Compaction & Vapour Barrier(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,211.48
B6.33 05 40.01.28(	Backfilling, DI Frame & Grate Cover Fixing(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,422.96
UPVC		3.00	4	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	111,988.19
?300 From 0.0 to 1.5m		2.00	2	16-Sep-26	17-Sep-26	07-Oct-26 A	04-Nov-26	70,089.90
B6.33 42 11.35-13	Catch Basin Opening Prep.(Rem)	2.00	1	16-Sep-26	17-Sep-26	07-Oct-26 A	04-Nov-26	14,017.98
B6.33 42 11.35-13	Fittings & Pipe Installation(Rem)	2.00	1	16-Sep-26	17-Sep-26	07-Oct-26 A	04-Nov-26	56,071.92
?400 From 0.0 to 1.5m		3.00	2	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	41,898.29
B6.33 42 11.36-12	Catch Basin Opening Prep.(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	4,890.82
B6.33 42 11.36-12	Fittings & Pipe Installation(Rem)	3.00	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	37,007.47
Potable Water Network		13.00	5	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	3,893.82
HDPE Pipes		2.18	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
?110mm		2.18	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth: 1.51m - 2.5m		2.18	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B3.33 14 11.01.01	Backfilling & Warning Tape(Rem)	2.18	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Plots and Buildings Crossing		13.00	3	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	1,343.34

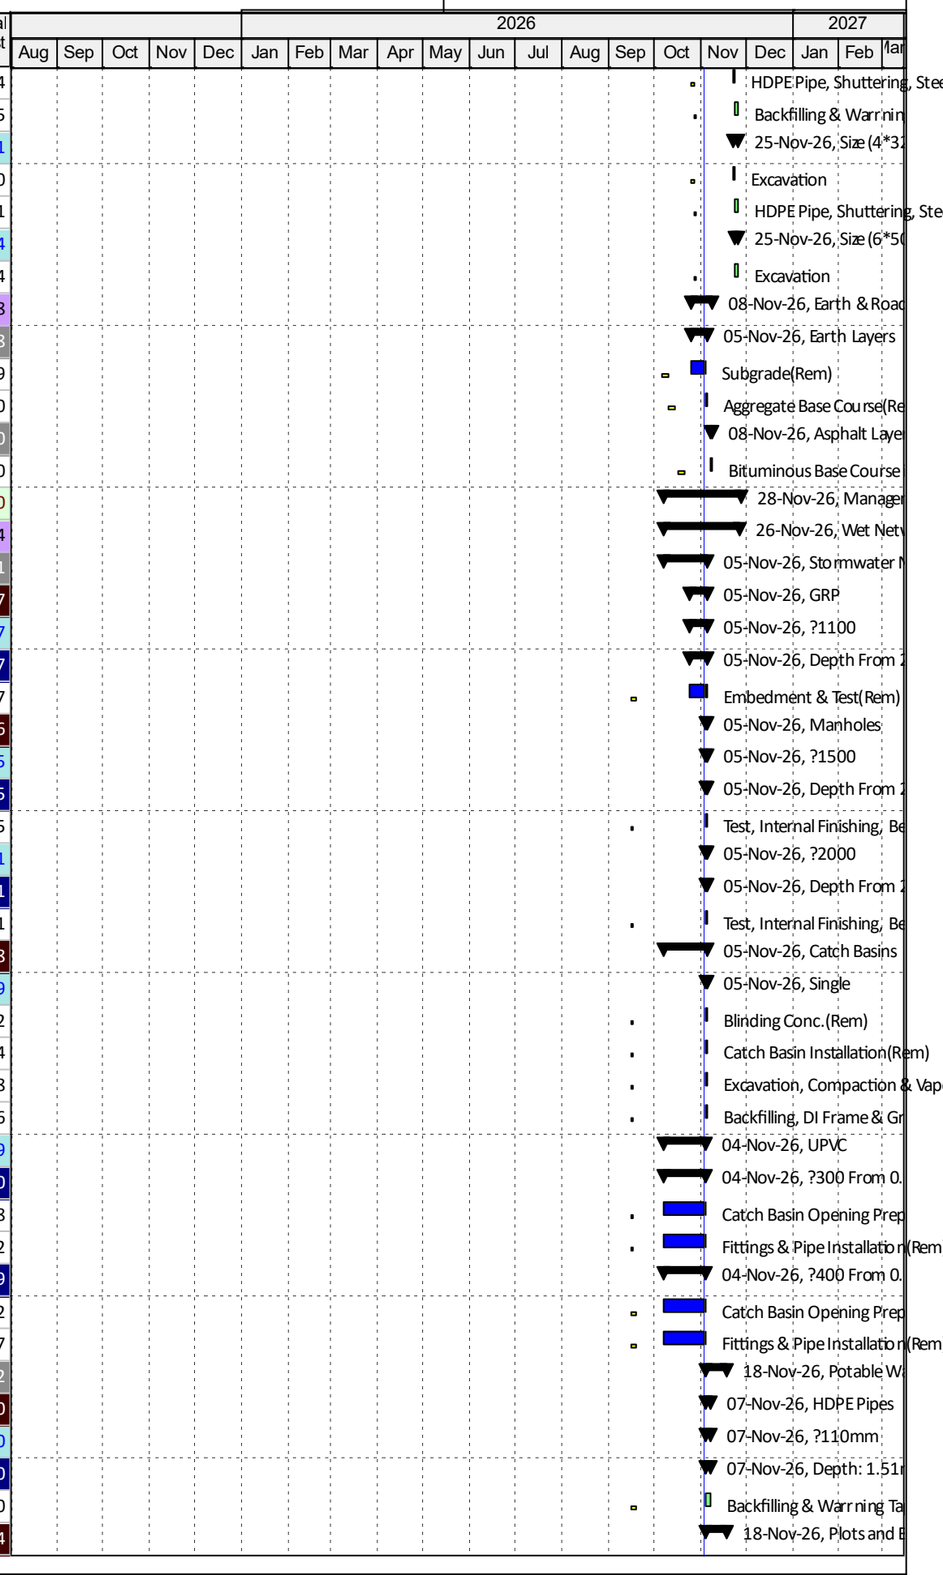


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 14 13.02.19	Earthwork	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	268.67
B3.33 14 13.02.20	Sand Bedding	3.00	1	22-Sep-26	26-Sep-26	10-Nov-26	12-Nov-26	268.67
B3.33 14 13.02.21	Tee, Pipe (Crossing) Installation & Backfilling	5.00	1	27-Sep-26	01-Oct-26	14-Nov-26	18-Nov-26	806.01
Valves & Chambers		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,550.47
Gate Valves		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,550.47
Gate valves dia (110) mm		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,550.47
B3.33 14 19.01.11	Spindle & Surface Box	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,550.47
Fire Fighting Network		12.95	9	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	101,909.65
Valves & Chambers		12.95	7	16-Sep-26	01-Oct-26	04-Nov-26	18-Nov-26	36,905.12
Gate Valves		4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,525.67
Gate valves dia (250) mm		4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,525.67
B3.33 14 19.01.12	Burried Isolation Valve Installation	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,525.67
Air Valves		9.00	5	16-Sep-26	27-Sep-26	04-Nov-26	14-Nov-26	14,578.19
Air valves on less than 315 mm. (In Chamber)		9.00	5	16-Sep-26	27-Sep-26	04-Nov-26	14-Nov-26	14,578.19
B3.33 05 63.02.50	Foundations(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,455.31
B3.33 05 63.02.51	Chamber Curing, Finishing & Steel Cover(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,161.29
B3.33 05 63.02.52	Land Adjustment & Compaction(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,121.40
B3.33 05 63.02.53	Chambers Walls Conc Cast In Situ(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,495.20
B3.33 05 63.02.54	Valve & Fitting Installation	6.00	1	20-Sep-26	27-Sep-26	08-Nov-26	14-Nov-26	9,344.99
Washout Valves		6.00	1	24-Sep-26	01-Oct-26	11-Nov-26	18-Nov-26	14,801.26
Washout valves on 110-400 mm. (In Chamber)		6.00	1	24-Sep-26	01-Oct-26	11-Nov-26	18-Nov-26	14,801.26
B3.33 05 63.01.49	Valve & Fitting Installation	6.00	1	24-Sep-26	01-Oct-26	11-Nov-26	18-Nov-26	14,801.26
Fire Hydrant		6.95	2	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	65,004.53
B3.33 14 19.01.fh25_I	Firehydrant Fixing/Installation(Rem)	4.97	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	48,753.40
B3.33 14 19.01.fh27_I	Backfilling & Compaction(Rem)	6.95	1	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	16,251.13
TSE Network		18.46	22	21-Sep-26	13-Oct-26	05-Nov-26	26-Nov-26	901,938.86
HDPE Pipes		5.93	5	21-Sep-26	29-Sep-26	05-Nov-26	12-Nov-26	51,263.76
?125mm		5.93	5	21-Sep-26	29-Sep-26	05-Nov-26	12-Nov-26	51,263.76
Depth: 0.0m - 1.5m		5.93	5	21-Sep-26	29-Sep-26	05-Nov-26	12-Nov-26	51,263.76
B4.33 14 13.0110_	Excavation(Rem)	3.46	1	21-Sep-26	26-Sep-26	05-Nov-26	09-Nov-26	10,252.50
B4.33 14 13.0112_	Sand Bedding(Rem)	2.64	1	22-Sep-26	26-Sep-26	07-Nov-26	09-Nov-26	2,563.75
B4.33 14 13.0114_	Pipe Laying(Rem)	2.64	1	22-Sep-26	26-Sep-26	07-Nov-26	09-Nov-26	23,068.76
B4.33 14 13.0116_	Embedment & Test(Rem)	4.29	1	22-Sep-26	28-Sep-26	07-Nov-26	11-Nov-26	10,252.50
B4.33 14 13.0118_	Backfilling & Warrning Tape(Rem)	5.11	1	22-Sep-26	29-Sep-26	07-Nov-26	12-Nov-26	5,126.25
Valves & Chambers		17.64	17	22-Sep-26	13-Oct-26	07-Nov-26	26-Nov-26	850,675.10
Gate Valves		5.00	4	22-Sep-26	29-Sep-26	07-Nov-26	12-Nov-26	16,591.62
Gate valves dia (100) mm		5.00	2	22-Sep-26	29-Sep-26	07-Nov-26	12-Nov-26	12,052.11
B3.33 14 19.01.14	Burried Isolation Valve Installation(Rem)	2.00	1	22-Sep-26	26-Sep-26	07-Nov-26	09-Nov-26	6,486.76
B3.33 14 19.01.14	Spindle & Surface Box	3.00	1	26-Sep-26	29-Sep-26	09-Nov-26	12-Nov-26	5,565.35
Gate valves dia (150) mm		5.00	2	22-Sep-26	29-Sep-26	07-Nov-26	12-Nov-26	4,539.51
B3.33 14 19.01.15	Burried Isolation Valve Installation(Rem)	2.00	1	22-Sep-26	26-Sep-26	07-Nov-26	09-Nov-26	2,452.38
B3.33 14 19.01.16	Spindle & Surface Box	3.00	1	26-Sep-26	29-Sep-26	09-Nov-26	12-Nov-26	2,087.13
Solenoid valves		15.00	13	27-Sep-26	13-Oct-26	10-Nov-26	26-Nov-26	834,083.48
1 Solenoid valve ?1.0 inch with box		9.00	4	30-Sep-26	10-Oct-26	14-Nov-26	23-Nov-26	14,159.07
B4.32 84 13.71	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	30-Sep-26	03-Oct-26	14-Nov-26	16-Nov-26	4,917.51
B4.32 84 13.72	Solenoid Valve Box Installation	3.00	1	04-Oct-26	06-Oct-26	17-Nov-26	19-Nov-26	2,838.80



© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B4.32 84 13.73	Bubblers Installation	3.00	1	07-Oct-26	10-Oct-26	21-Nov-26	23-Nov-26	2,706.13
B4.32 84 13.77	Pull Box Installation	3.00	1	07-Oct-26	10-Oct-26	21-Nov-26	23-Nov-26	3,696.63
1 Solenoid valve ?1.5 inch with box		15.00	5	27-Sep-26	13-Oct-26	10-Nov-26	26-Nov-26	803,698.69
B4.33 14 13.09	Extra flexible drip line with 3.0 LPH	3.00	1	27-Sep-26	29-Sep-26	10-Nov-26	12-Nov-26	135,629.40
B4.32 84 13.04	Dripper	3.00	1	30-Sep-26	03-Oct-26	14-Nov-26	16-Nov-26	651,021.11
B4.32 84 13.74	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	04-Oct-26	06-Oct-26	17-Nov-26	19-Nov-26	4,917.51
B4.32 84 13.78	Pull Box Installation	3.00	1	07-Oct-26	10-Oct-26	21-Nov-26	23-Nov-26	3,696.63
B4.32 84 13.75	Solenoid Valve Box Installation	3.00	1	11-Oct-26	13-Oct-26	24-Nov-26	26-Nov-26	8,434.05
1 Solenoid valve ?2.0 inch with box		9.00	4	27-Sep-26	06-Oct-26	10-Nov-26	19-Nov-26	16,225.71
B4.32 84 13.68	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	27-Sep-26	29-Sep-26	10-Nov-26	12-Nov-26	4,917.51
B4.32 84 13.69	Solenoid Valve Box Installation	3.00	1	30-Sep-26	03-Oct-26	14-Nov-26	16-Nov-26	5,829.60
B4.32 84 13.79	Pull Box Installation	3.00	1	30-Sep-26	03-Oct-26	14-Nov-26	16-Nov-26	2,772.47
B4.32 84 13.70	Bubblers Installation	3.00	1	04-Oct-26	06-Oct-26	17-Nov-26	19-Nov-26	2,706.13
Dry Networks		15.00	12	29-Sep-26	11-Nov-26	09-Nov-26	25-Nov-26	576,097.80
Medium Voltage Network		13.28	5	29-Sep-26	05-Nov-26	09-Nov-26	24-Nov-26	254,848.76
Duct Banks		8.00	2	29-Sep-26	08-Oct-26	12-Nov-26	22-Nov-26	9,850.97
4 Way		8.00	2	29-Sep-26	08-Oct-26	12-Nov-26	22-Nov-26	9,850.97
B2.31 23 00.639	Excavation	4.00	1	29-Sep-26	04-Oct-26	12-Nov-26	17-Nov-26	3,411.59
B2.33 71 00.286	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	4.00	1	04-Oct-26	08-Oct-26	17-Nov-26	22-Nov-26	6,439.38
Cables		13.28	3	26-Oct-26	05-Nov-26	09-Nov-26	24-Nov-26	244,997.79
3C,500mm2		13.28	3	26-Oct-26	05-Nov-26	09-Nov-26	24-Nov-26	244,997.79
B2.33 71 49.23.74	Cable 13.8 kV Unarmored	4.00	1	26-Oct-26	29-Oct-26	09-Nov-26	12-Nov-26	234,058.34
B2.33 71 49.23.75	Straight joints cables	3.00	1	31-Oct-26	02-Nov-26	14-Nov-26	16-Nov-26	7,880.95
B2.33 71 49.23.76	Cable Termination	3.00	1	03-Nov-26	05-Nov-26	21-Nov-26	24-Nov-26	3,058.50
Street Lighting		15.00	7	26-Oct-26	11-Nov-26	09-Nov-26	25-Nov-26	321,249.04
SL Poles		14.00	5	26-Oct-26	10-Nov-26	09-Nov-26	24-Nov-26	317,671.69
Pole (10 M Single Arm)		14.00	5	26-Oct-26	10-Nov-26	09-Nov-26	24-Nov-26	317,671.69
B2.33 71 16.51	Excavation	3.00	1	26-Oct-26	28-Oct-26	09-Nov-26	11-Nov-26	58,898.50
B2.33 71 16.52	PC & RC Foundation	3.00	1	29-Oct-26	01-Nov-26	12-Nov-26	15-Nov-26	58,898.50
B2.33 71 16.53	Lighting Poles Installation Incl power box, Cables	3.00	1	02-Nov-26	04-Nov-26	16-Nov-26	18-Nov-26	117,797.00
B2.26.56.19.6	Lighting Luminares Inst	2.00	1	05-Nov-26	07-Nov-26	19-Nov-26	21-Nov-26	23,179.20
B2.33 71 16.54	Backfilling, Grouting & Chamfering	3.00	1	08-Nov-26	10-Nov-26	22-Nov-26	24-Nov-26	58,898.50
Earthing		6.00	2	05-Nov-26	11-Nov-26	19-Nov-26	25-Nov-26	3,577.35
B2.33 71 19 26	Land Adjustment	3.00	1	05-Nov-26	08-Nov-26	19-Nov-26	22-Nov-26	904.39
B2.33 71 19 27	Earth Rods & Conduits	3.00	1	09-Nov-26	11-Nov-26	23-Nov-26	25-Nov-26	2,672.96
Earth & Road Works		19.32	11	04-Oct-26	27-Oct-26	04-Nov-26	26-Nov-26	713,267.78
Earth Layers		2.00	2	11-Oct-26	19-Oct-26	04-Nov-26	05-Nov-26	80,652.67
B1.2.32 11 13.01.6_R	Subgrade(Rem)	2.00	1	11-Oct-26	15-Oct-26	04-Nov-26	05-Nov-26	13,978.56
B1.2.32 11 23.01.6_R	Aggregate Base Course(Rem)	2.00	1	14-Oct-26	19-Oct-26	04-Nov-26	05-Nov-26	66,674.10
Interlock		3.00	1	25-Oct-26	27-Oct-26	04-Nov-26	08-Nov-26	21,247.50
B1.2.32 14 13.13.6	60mm thick - Interlocking Block Pavers	3.00	1	25-Oct-26	27-Oct-26	04-Nov-26	08-Nov-26	21,247.50
Curbstone		12.00	6	04-Oct-26	17-Oct-26	12-Nov-26	26-Nov-26	273,038.16
Pre-Installation		6.00	3	04-Oct-26	10-Oct-26	12-Nov-26	19-Nov-26	139,647.67
B2.31 23 00.151	Excavation	2.00	1	04-Oct-26	05-Oct-26	12-Nov-26	15-Nov-26	46,547.46
B1.2.32 14 13.13.26	PCC	2.00	1	06-Oct-26	07-Oct-26	15-Nov-26	17-Nov-26	46,552.82
32 16 13.006	Haunching	2.00	1	08-Oct-26	10-Oct-26	17-Nov-26	19-Nov-26	46,547.39

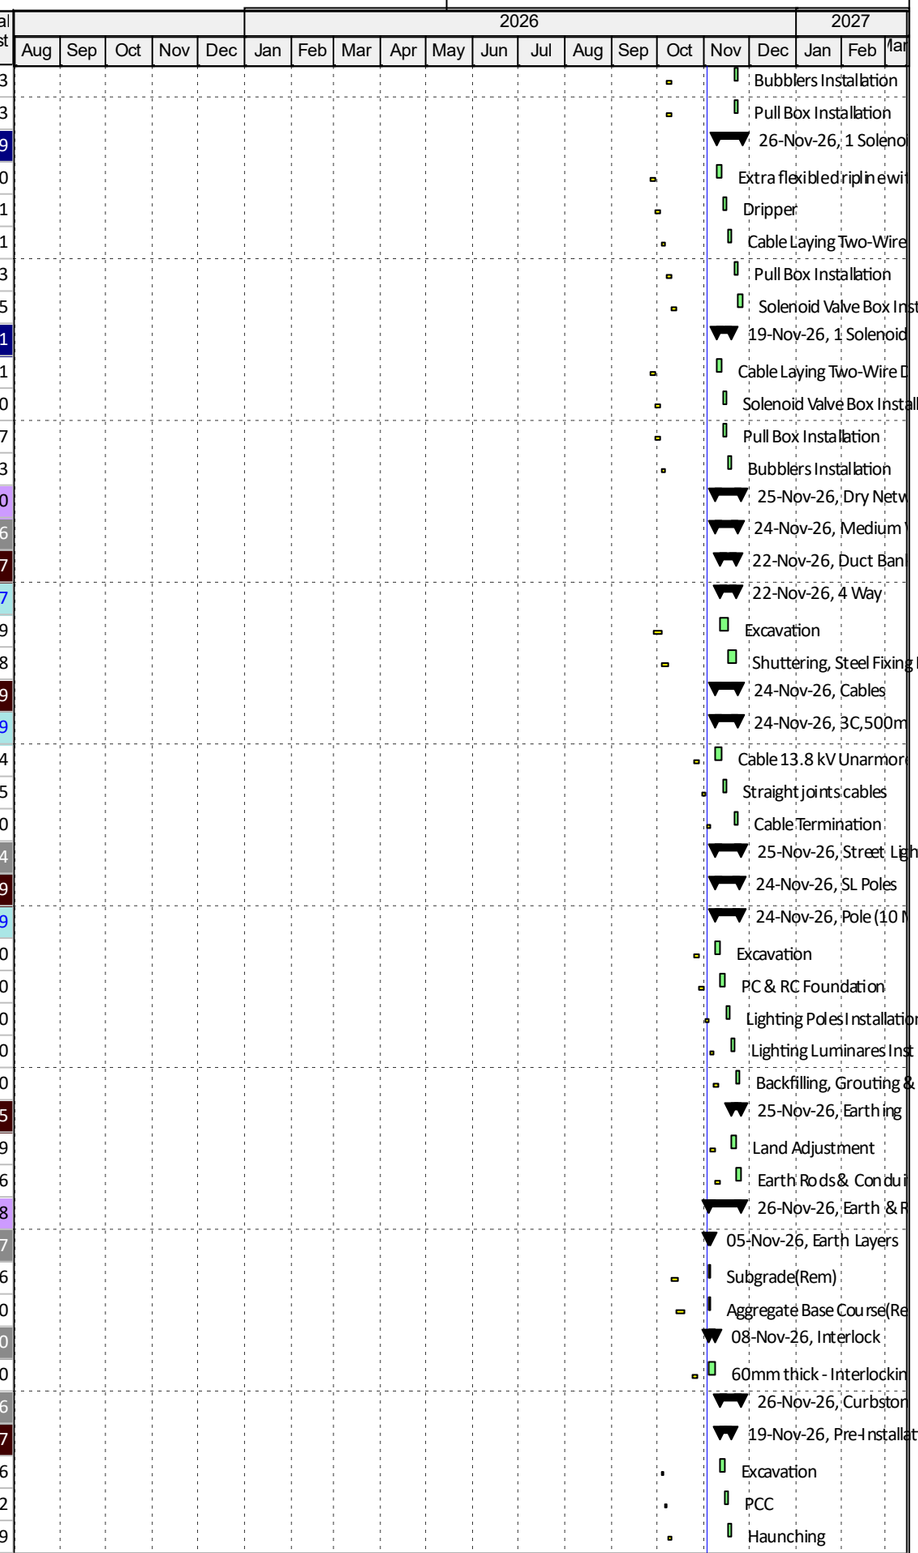

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Installation		6.00	3	11-Oct-26	17-Oct-26	19-Nov-26	26-Nov-26	133,390.49
B1.2.32 16.13.01.6	Curb Stone, Type K1	2.00	1	11-Oct-26	12-Oct-26	19-Nov-26	22-Nov-26	124,719.20
B1.2.32 16.13.02.5	Dropped Curb, Type K3	2.00	1	13-Oct-26	14-Oct-26	22-Nov-26	24-Nov-26	122.64
B1.2.32 16.13.03.6	Edge Curb, Type K4	2.00	1	15-Oct-26	17-Oct-26	24-Nov-26	26-Nov-26	8,548.64
Asphalt Layers		2.00	1	20-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	335,890.21
B1.2.32 11 26.01.6	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	20-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	335,890.21
Traffic Signs		2.00	1	06-Oct-26	07-Oct-26	12-Nov-26	15-Nov-26	2,439.24
Pre-Installation		2.00	1	06-Oct-26	07-Oct-26	12-Nov-26	15-Nov-26	2,439.24
B2.31 23 00.161	Excavation	2.00	1	06-Oct-26	07-Oct-26	12-Nov-26	15-Nov-26	2,439.24
Landscape		11.00	3	08-Oct-26	20-Oct-26	15-Nov-26	28-Nov-26	214,295.77
Fences		5.00	1	08-Oct-26	13-Oct-26	15-Nov-26	21-Nov-26	25,743.45
Steel fence (ZATCA HCIS)		5.00	1	08-Oct-26	13-Oct-26	15-Nov-26	21-Nov-26	25,743.45
B7.32 93 43.04.44.1	Earthwork	5.00	1	08-Oct-26	13-Oct-26	15-Nov-26	21-Nov-26	25,743.45
Miscellaneous		6.00	2	14-Oct-26	20-Oct-26	21-Nov-26	28-Nov-26	188,552.32
B7.32 91 00.1	Plastic edge	5.00	1	14-Oct-26	19-Oct-26	21-Nov-26	26-Nov-26	46,358.52
B7.32 91 00.02.2	Grey gravel bed - 30-50 mm diameter (G1)	6.00	1	14-Oct-26	20-Oct-26	21-Nov-26	28-Nov-26	142,193.81
Commercial Road 01		48.00	108	16-Sep-26	25-Nov-26	07-Oct-26 A	01-Dec-26	1,328,220.97
Wet Networks		48.00	80	16-Sep-26	15-Nov-26	07-Oct-26 A	01-Dec-26	504,995.33
Stormwater Network		31.00	52	16-Sep-26	07-Oct-26	07-Oct-26 A	11-Nov-26	313,984.18
GRP		14.84	45	16-Sep-26	06-Oct-26	21-Oct-26 A	07-Nov-26	227,194.97
?400		6.84	2	22-Sep-26	06-Oct-26	25-Oct-26 A	07-Nov-26	708.70
Depth From 1.5m to 2.5m		6.84	2	22-Sep-26	06-Oct-26	25-Oct-26 A	07-Nov-26	708.70
B6.33 42 11.02.4_	Embedment & Test(Rem)	2.84	1	22-Sep-26	27-Sep-26	25-Oct-26 A	07-Nov-26	472.41
B6.33 42 11.02.5_	Backfilling & Warrning Tape(Rem)	4.00	1	01-Oct-26	06-Oct-26	26-Oct-26 A	07-Nov-26	236.29
?600		2.56	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	16,822.51
Depth From 0.0m to 1.5m		2.56	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	16,822.51
B6.33 42 11.3611	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	16,822.51
?900		13.56	6	16-Sep-26	29-Sep-26	24-Oct-26 A	07-Nov-26	3,314.93
Depth From 0.0m to 1.5m		2.56	5	16-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Backfilling & Warrning Tape(Rem)	2.56	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 1.5m to 2.5m		3.12	1	26-Sep-26	29-Sep-26	24-Oct-26 A	07-Nov-26	3,314.93
B6.33 42 11.13.55	Backfilling & Warrning Tape(Rem)	3.12	1	26-Sep-26	29-Sep-26	24-Oct-26 A	07-Nov-26	3,314.93
?1000		2.56	5	16-Sep-26	28-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 0.0m to 1.5m		2.56	5	16-Sep-26	28-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Backfilling & Warrning Tape(Rem)	2.56	1	26-Sep-26	28-Sep-26	04-Nov-26	07-Nov-26	0.00
?1100		14.56	6	16-Sep-26	29-Sep-26	24-Oct-26 A	07-Nov-26	16,122.45
Depth From 0.0m to 1.5m		2.56	5	16-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00

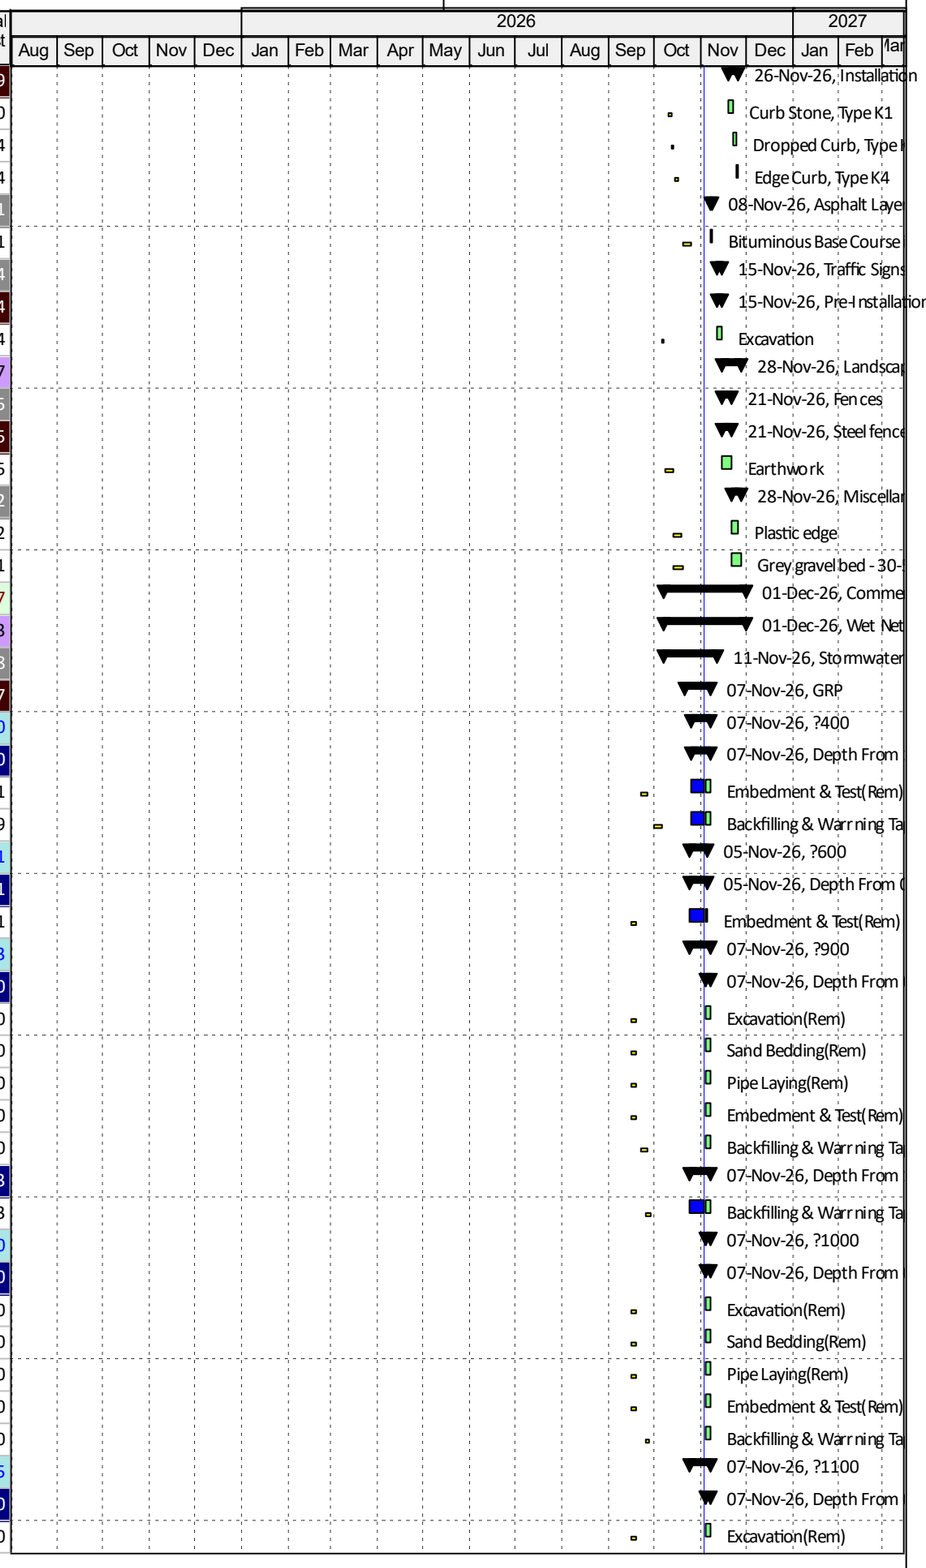


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B6.33 42 11.3612	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Backfilling & Warrning Tape(Rem)	2.56	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 1.5m to 2.5m		3.12	1	26-Sep-26	29-Sep-26	24-Oct-26 A	05-Nov-26	16,122.45
B6.33 42 11.13.10	Backfilling & Warrning Tape(Rem)	3.12	1	26-Sep-26	29-Sep-26	24-Oct-26 A	05-Nov-26	16,122.45
?1200		2.84	5	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 0.0m to 1.5m		2.84	5	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3612	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
DMM2-Eng-PQ-050	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3613	Backfilling & Warrning Tape(Rem)	2.84	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
?1300		14.84	6	16-Sep-26	19-Sep-26	25-Oct-26 A	07-Nov-26	4,805.66
Depth From 0.0m to 1.5m		2.84	5	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Backfilling & Warrning Tape(Rem)	2.84	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 1.5m to 2.5m		2.84	1	16-Sep-26	19-Sep-26	25-Oct-26 A	05-Nov-26	4,805.66
B6.33 42 11.13.19	Embedment & Test(Rem)	2.84	1	16-Sep-26	19-Sep-26	25-Oct-26 A	05-Nov-26	4,805.66
?1400		14.84	9	16-Sep-26	19-Sep-26	21-Oct-26 A	07-Nov-26	185,420.73
Depth From 0.0m to 1.5m		2.84	5	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3614	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Backfilling & Warrning Tape(Rem)	2.84	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 1.5m to 2.5m		2.84	4	16-Sep-26	19-Sep-26	21-Oct-26 A	05-Nov-26	185,420.73
B6.33 42 11.13.21	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	21-Oct-26 A	05-Nov-26	41,185.06
B6.33 42 11.13.22	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	21-Oct-26 A	05-Nov-26	10,385.71
B6.33 42 11.13.23	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	21-Oct-26 A	05-Nov-26	92,664.90
B6.33 42 11.13.24	Embedment & Test(Rem)	2.84	1	16-Sep-26	19-Sep-26	24-Oct-26 A	05-Nov-26	41,185.06
?1500		2.84	5	16-Sep-26	24-Sep-26	04-Nov-26	07-Nov-26	0.00
Depth From 0.0m to 1.5m		2.84	5	16-Sep-26	24-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Embedment & Test(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	0.00
B6.33 42 11.3615	Backfilling & Warrning Tape(Rem)	2.84	1	20-Sep-26	24-Sep-26	04-Nov-26	07-Nov-26	0.00
Catch Basins		31.00	7	16-Sep-26	07-Oct-26	07-Oct-26 A	11-Nov-26	86,789.21
Double		7.00	3	22-Sep-26	07-Oct-26	04-Nov-26	11-Nov-26	29,895.76
B6.33 05 40.01.700	Blinding Conc.	3.00	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	3,455.28
B6.33 05 40.01.720	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	01-Oct-26	07-Oct-26	04-Nov-26	11-Nov-26	10,516.10
B6.33 05 40.01.710	Catch Basin Installation	4.00	1	27-Sep-26	30-Sep-26	08-Nov-26	11-Nov-26	15,924.38

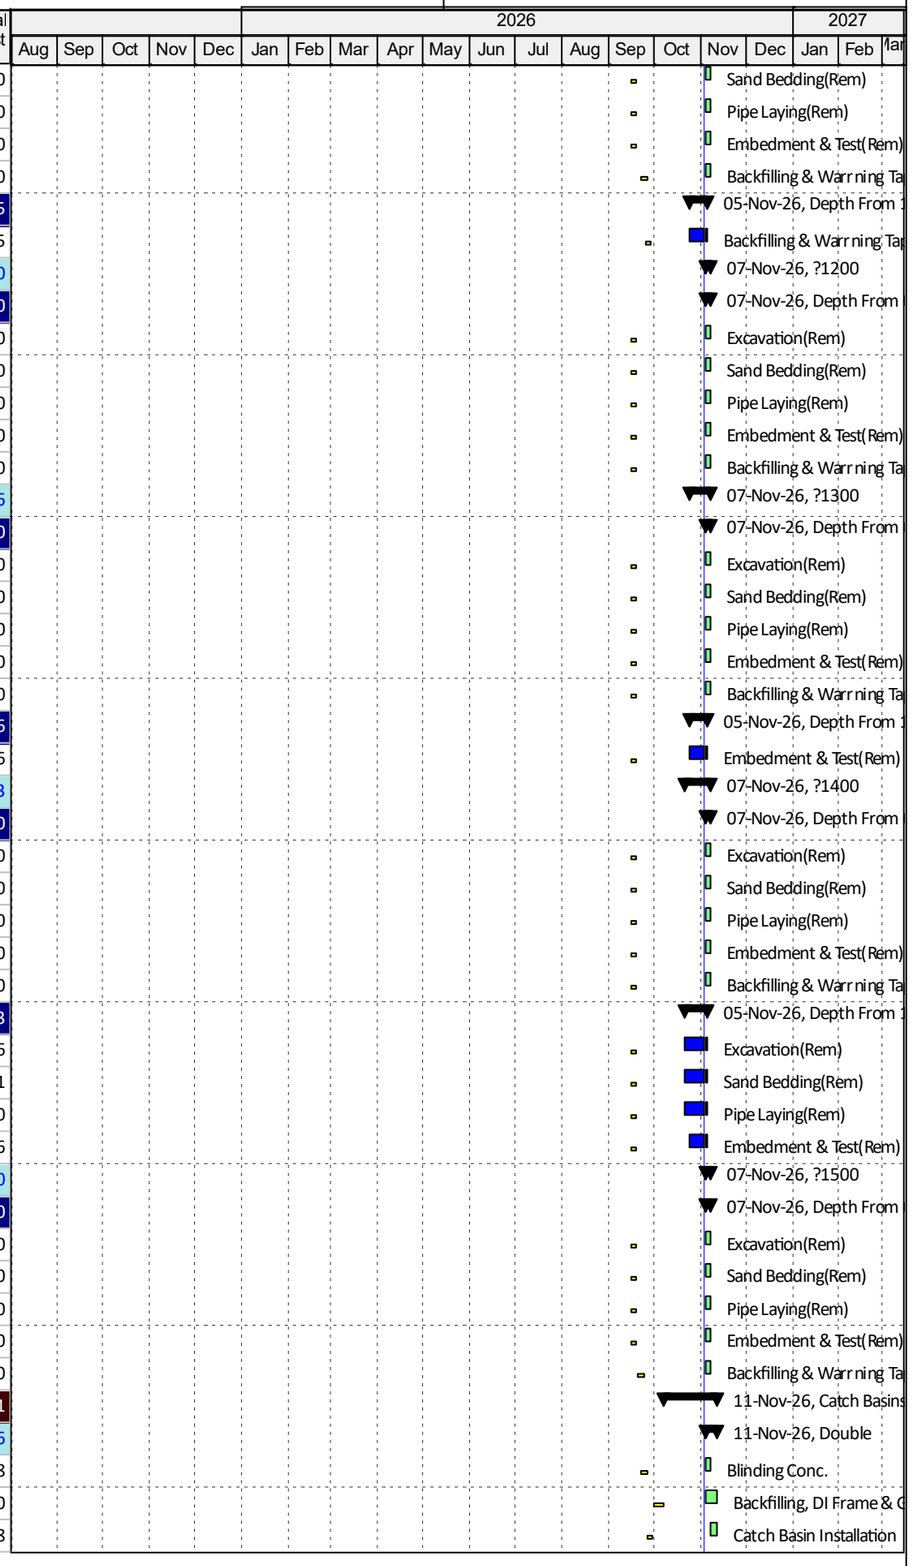


Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
UPVC		7.00	4	16-Sep-26	30-Sep-26	07-Oct-26 A	11-Nov-26	56,893.45
?300 From 0.0 to 1.5m		2.09	2	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	44,801.47
B6.33 42 11.35-11	Catch Basin Opening Prep.(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	8,960.29
B6.33 42 11.35-12	Fittings & Pipe Installation(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	35,841.17
?400 From 0.0 to 1.5m		2.00	2	29-Sep-26	30-Sep-26	08-Oct-26 A	11-Nov-26	12,091.99
B6.33 42 11.36-11	Catch Basin Opening Prep.(Rem)	2.00	1	29-Sep-26	30-Sep-26	08-Oct-26 A	11-Nov-26	2,418.40
B6.33 42 11.36-12	Fittings & Pipe Installation(Rem)	2.00	1	29-Sep-26	30-Sep-26	10-Oct-26 A	04-Nov-26	9,673.59
Potable Water Network		30.00	19	16-Sep-26	01-Nov-26	14-Oct-26 A	01-Dec-26	130,083.60
HDPE Pipes		3.00	5	16-Sep-26	19-Sep-26	28-Oct-26 A	04-Nov-26	30,694.64
?110mm		3.00	5	16-Sep-26	19-Sep-26	28-Oct-26 A	04-Nov-26	30,694.64
Depth: 0.0m - 1.5m		3.00	5	16-Sep-26	19-Sep-26	28-Oct-26 A	04-Nov-26	30,694.64
B3.33 14 13.01.01	Excavation(Rem)	3.00	1	16-Sep-26	19-Sep-26	28-Oct-26 A	04-Nov-26	6,168.01
B3.33 14 13.01.01	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	29-Oct-26 A	04-Nov-26	1,396.29
B3.33 14 13.01.01	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	31-Oct-26 A	04-Nov-26	13,878.31
B3.33 14 13.01.01	Embedment & Test(Rem)	2.10	1	16-Sep-26	19-Sep-26	31-Oct-26 A	04-Nov-26	6,168.01
B3.33 14 13.01.01	Backfilling & Warning Tape(Rem)	2.38	1	16-Sep-26	19-Sep-26	01-Nov-26 A	04-Nov-26	3,084.01
Valves & Chambers		24.00	11	20-Sep-26	26-Oct-26	14-Oct-26 A	07-Nov-26	98,045.62
Gate Valves		3.00	1	20-Sep-26	22-Sep-26	04-Nov-26	07-Nov-26	2,550.47
Gate valves dia (110) mm		3.00	1	20-Sep-26	22-Sep-26	04-Nov-26	07-Nov-26	2,550.47
B3.33 14 19.01.10	Spindle & Surface Box	3.00	1	20-Sep-26	22-Sep-26	04-Nov-26	07-Nov-26	2,550.47
Air Valves		21.00	5	20-Sep-26	14-Oct-26	15-Oct-26 A	07-Nov-26	28,923.51
Air valves on less than 315 mm. (In Chamber)		21.00	5	20-Sep-26	14-Oct-26	15-Oct-26 A	07-Nov-26	28,923.51
B3.33 05 63.02.20	Foundations	4.00	1	24-Sep-26	28-Sep-26	15-Oct-26 A	05-Nov-26	5,389.08
B3.33 05 63.02.21	Chamber Curing, Finishing & Steel Cover	5.00	1	04-Oct-26	08-Oct-26	18-Oct-26 A	07-Nov-26	4,549.72
B3.33 05 63.02.22	Land Adjustment & Compaction	3.00	1	20-Sep-26	22-Sep-26	20-Oct-26 A	05-Nov-26	4,549.72
B3.33 05 63.02.23	Chambers Walls Conc Cast In Situ	4.00	1	29-Sep-26	03-Oct-26	21-Oct-26 A	05-Nov-26	6,600.26
B3.33 05 63.02.24	Valve & Fitting Installation	5.00	1	10-Oct-26	14-Oct-26	25-Oct-26 A	07-Nov-26	7,834.72
Washout Valves		21.00	5	24-Sep-26	26-Oct-26	14-Oct-26 A	07-Nov-26	66,571.64
Washout valves on 110-400 mm. (In Chamber)		21.00	5	24-Sep-26	26-Oct-26	14-Oct-26 A	07-Nov-26	66,571.64
B3.33 05 63.01.15	Foundations	4.00	1	28-Sep-26	01-Oct-26	14-Oct-26 A	05-Nov-26	13,314.33
B3.33 05 63.01.16	Chamber Curing, Finishing & Steel Cover	5.00	1	07-Oct-26	12-Oct-26	17-Oct-26 A	07-Nov-26	9,985.75
B3.33 05 63.01.17	Land Adjustment & Compaction	3.00	1	24-Sep-26	27-Sep-26	19-Oct-26 A	05-Nov-26	9,985.75
B3.33 05 63.01.18	Chambers Walls Conc Cast In Situ	4.00	1	03-Oct-26	06-Oct-26	20-Oct-26 A	05-Nov-26	13,314.33
B3.33 05 63.01.19	Valve & Fitting Installation	5.00	1	21-Oct-26	26-Oct-26	22-Oct-26 A	07-Nov-26	19,971.49
Plots and Buildings Crossing		22.50	3	28-Sep-26	01-Nov-26	05-Nov-26	01-Dec-26	1,343.34
B3.33 14 13.02.16	Earthwork	7.00	1	28-Sep-26	05-Oct-26	05-Nov-26	14-Nov-26	268.67
B3.33 14 13.02.17	Sand Bedding	3.00	1	06-Oct-26	08-Oct-26	14-Nov-26	17-Nov-26	268.67
B3.33 14 13.02.18	Tee, Pipe (Crossing) Installation & Backfilling	7.00	1	24-Oct-26	01-Nov-26	24-Nov-26	01-Dec-26	806.01
Fire Fighting Network		23.44	9	29-Sep-26	15-Nov-26	04-Nov-26	01-Dec-26	60,927.55
Valves & Chambers		23.44	9	29-Sep-26	15-Nov-26	04-Nov-26	01-Dec-26	60,927.55
Gate Valves		8.00	2	29-Sep-26	07-Oct-26	04-Nov-26	12-Nov-26	12,542.78
Gate valves dia (250) mm		8.00	2	29-Sep-26	07-Oct-26	04-Nov-26	12-Nov-26	12,542.78
B3.33 14 19.01.12	Burried Isolation Valve Installation	4.00	1	29-Sep-26	03-Oct-26	04-Nov-26	08-Nov-26	7,525.67
B3.33 14 19.01.12	Spindle & Surface Box	4.00	1	04-Oct-26	07-Oct-26	09-Nov-26	12-Nov-26	5,017.11
Air Valves		20.00	4	07-Nov-26	15-Nov-26	08-Nov-26	01-Dec-26	20,932.79
Air valves on less than 315 mm. (In Chamber)		20.00	4	07-Nov-26	15-Nov-26	08-Nov-26	01-Dec-26	20,932.79

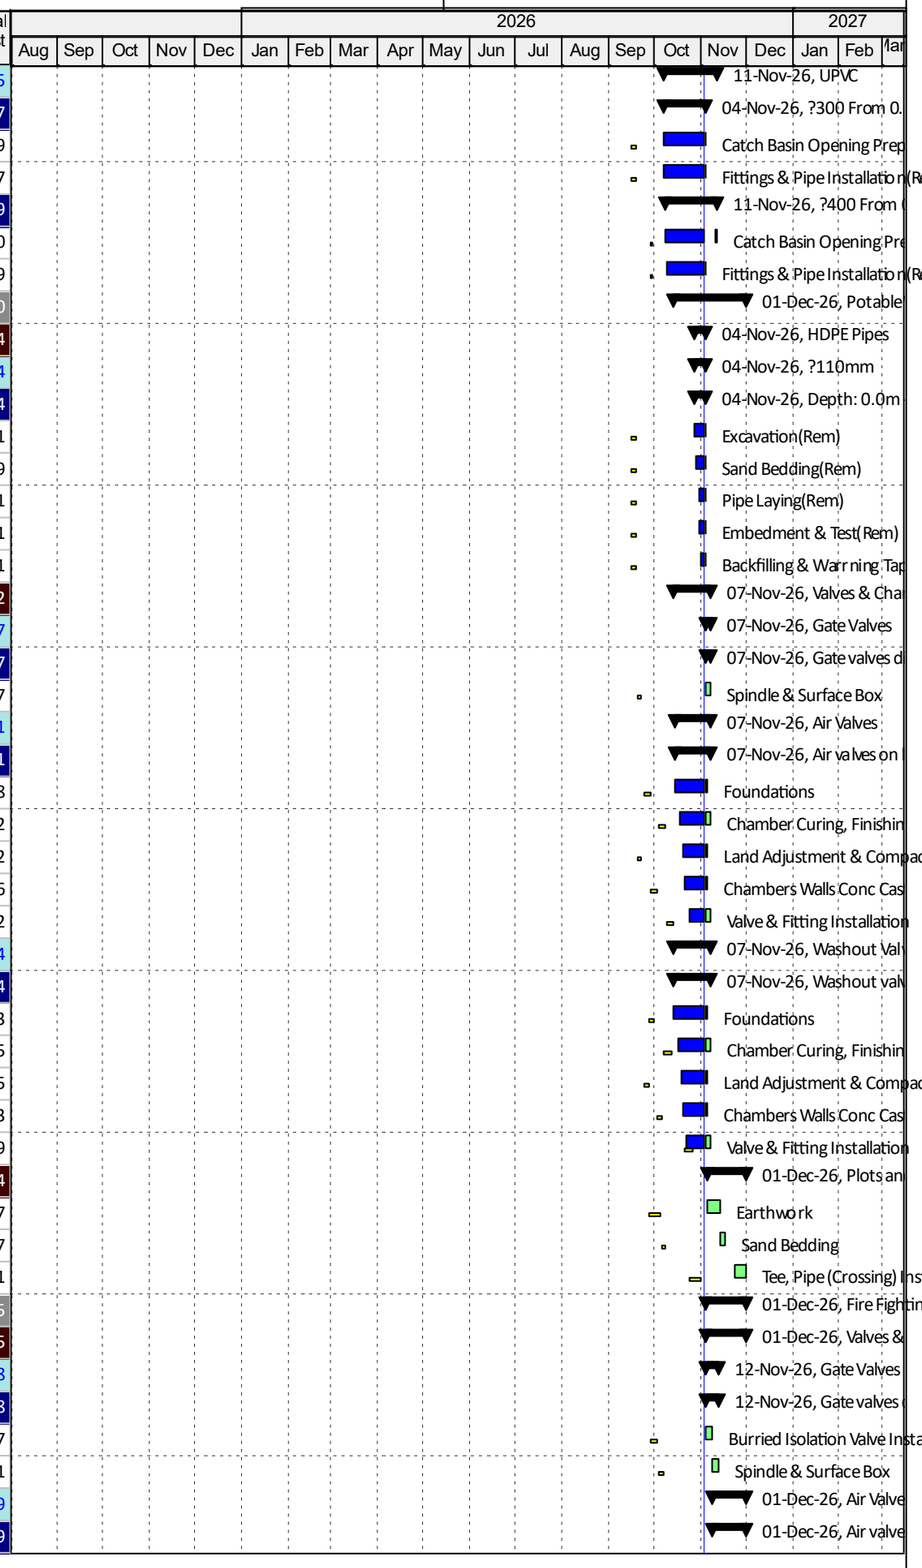

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 05 63.02.47	Land Adjustment & Compaction	4.00	1	07-Nov-26	08-Nov-26	08-Nov-26	12-Nov-26	4,485.60
B3.33 05 63.02.45	Foundations	5.00	1	09-Nov-26	10-Nov-26	12-Nov-26	18-Nov-26	5,821.24
B3.33 05 63.02.48	Chambers Walls Conc Cast In Situ	5.00	1	11-Nov-26	12-Nov-26	18-Nov-26	24-Nov-26	5,980.80
B3.33 05 63.02.46	Chamber Curing, Finishing & Steel Cover	6.00	1	14-Nov-26	15-Nov-26	24-Nov-26	01-Dec-26	4,645.16
Washout Valves		14.00	3	09-Nov-26	15-Nov-26	12-Nov-26	29-Nov-26	27,451.99
Washout valves on 110-400 mm. (In Chamber)		14.00	3	09-Nov-26	15-Nov-26	12-Nov-26	29-Nov-26	27,451.99
B3.33 05 63.01.37	Land Adjustment & Compaction	4.00	1	09-Nov-26	10-Nov-26	12-Nov-26	17-Nov-26	7,932.00
B3.33 05 63.01.35	Foundations	5.00	1	11-Nov-26	12-Nov-26	17-Nov-26	23-Nov-26	9,649.37
B3.33 05 63.01.38	Chambers Walls Conc Cast In Situ	5.00	1	14-Nov-26	15-Nov-26	23-Nov-26	29-Nov-26	9,870.62
Dry Networks		12.00	24	10-Oct-26	26-Oct-26	04-Nov-26	17-Nov-26	391,846.23
Medium Voltage Network		12.00	2	13-Oct-26	26-Oct-26	04-Nov-26	17-Nov-26	9,850.97
Duct Banks		12.00	2	13-Oct-26	26-Oct-26	04-Nov-26	17-Nov-26	9,850.97
4 Way		12.00	2	13-Oct-26	26-Oct-26	04-Nov-26	17-Nov-26	9,850.97
B2.33 71 00 02 43	Excavation	8.00	1	13-Oct-26	21-Oct-26	04-Nov-26	12-Nov-26	3,411.59
B2.33 71 00 02 44	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	4.00	1	22-Oct-26	26-Oct-26	14-Nov-26	17-Nov-26	6,439.38
Telecommunication Network		11.00	22	10-Oct-26	20-Oct-26	04-Nov-26	16-Nov-26	381,995.25
Ducts		9.00	13	10-Oct-26	15-Oct-26	04-Nov-26	14-Nov-26	310,620.33
Size (6*50mm) HDPE ducts		6.00	3	10-Oct-26	15-Oct-26	04-Nov-26	10-Nov-26	177,301.73
B2.1.33 81 26.54	Excavation	2.00	1	10-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	35,460.35
B2.1.33 81 26.55	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	106,381.04
B2.1.33 81 26.56	Backfilling & Warrning Tape	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	35,460.35
Size (6*50mm+2*32mm) HDPE ducts		4.00	2	10-Oct-26	13-Oct-26	04-Nov-26	08-Nov-26	84,994.02
B2.1.33 81 26.57	Excavation	2.00	1	10-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	21,251.23
B2.1.33 81 26.58	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	63,742.79
Size (6*50mm+4*32mm) HDPE ducts		6.00	3	10-Oct-26	15-Oct-26	04-Nov-26	10-Nov-26	37,205.53
B2.1.33 81 26.60	Excavation	2.00	1	10-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	7,441.11
B2.1.33 81 26.61	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	22,323.32
B2.1.33 81 26.62	Backfilling & Warrning Tape	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	7,441.11
Size (2*32mm) HDPE ducts		9.00	3	10-Oct-26	15-Oct-26	04-Nov-26	14-Nov-26	6,720.24
B2.1.33 81 26.63	Excavation	2.00	1	10-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	1,344.05
B2.1.33 81 26.64	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	4,032.14
B2.1.33 81 26.65	Backfilling & Warrning Tape	2.00	1	14-Oct-26	15-Oct-26	12-Nov-26	14-Nov-26	1,344.05
Size (4*32mm) HDPE ducts		4.00	2	12-Oct-26	15-Oct-26	07-Nov-26	10-Nov-26	4,398.81
B2.1.33 81 26.66	Excavation	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	1,099.70
B2.1.33 81 26.67	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	3,299.11
Manholes		6.00	6	12-Oct-26	18-Oct-26	07-Nov-26	12-Nov-26	60,270.45
Manhole Type 1		6.00	3	12-Oct-26	18-Oct-26	07-Nov-26	12-Nov-26	43,831.98
B2.31 23 00.603	Excavation	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	8,766.40
B2.33 71 00.214	Manhole Installation	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	26,299.19
B2.33 71 00.215	Backfilling & Warrning Tape	2.00	1	17-Oct-26	18-Oct-26	11-Nov-26	12-Nov-26	8,766.40
Manhole Type 2		6.00	3	12-Oct-26	18-Oct-26	07-Nov-26	12-Nov-26	16,438.47
B2.31 23 00.604	Excavation	2.00	1	12-Oct-26	13-Oct-26	07-Nov-26	08-Nov-26	3,287.69
B2.33 71 00.216	Manhole Installation	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	9,863.09
B2.33 71 00.217	Backfilling & Warrning Tape	2.00	1	17-Oct-26	18-Oct-26	11-Nov-26	12-Nov-26	3,287.69
Road Crossing Ducts		7.00	3	14-Oct-26	20-Oct-26	09-Nov-26	16-Nov-26	11,104.47
Size (6*50mm) HDPE		7.00	3	14-Oct-26	20-Oct-26	09-Nov-26	16-Nov-26	11,104.47

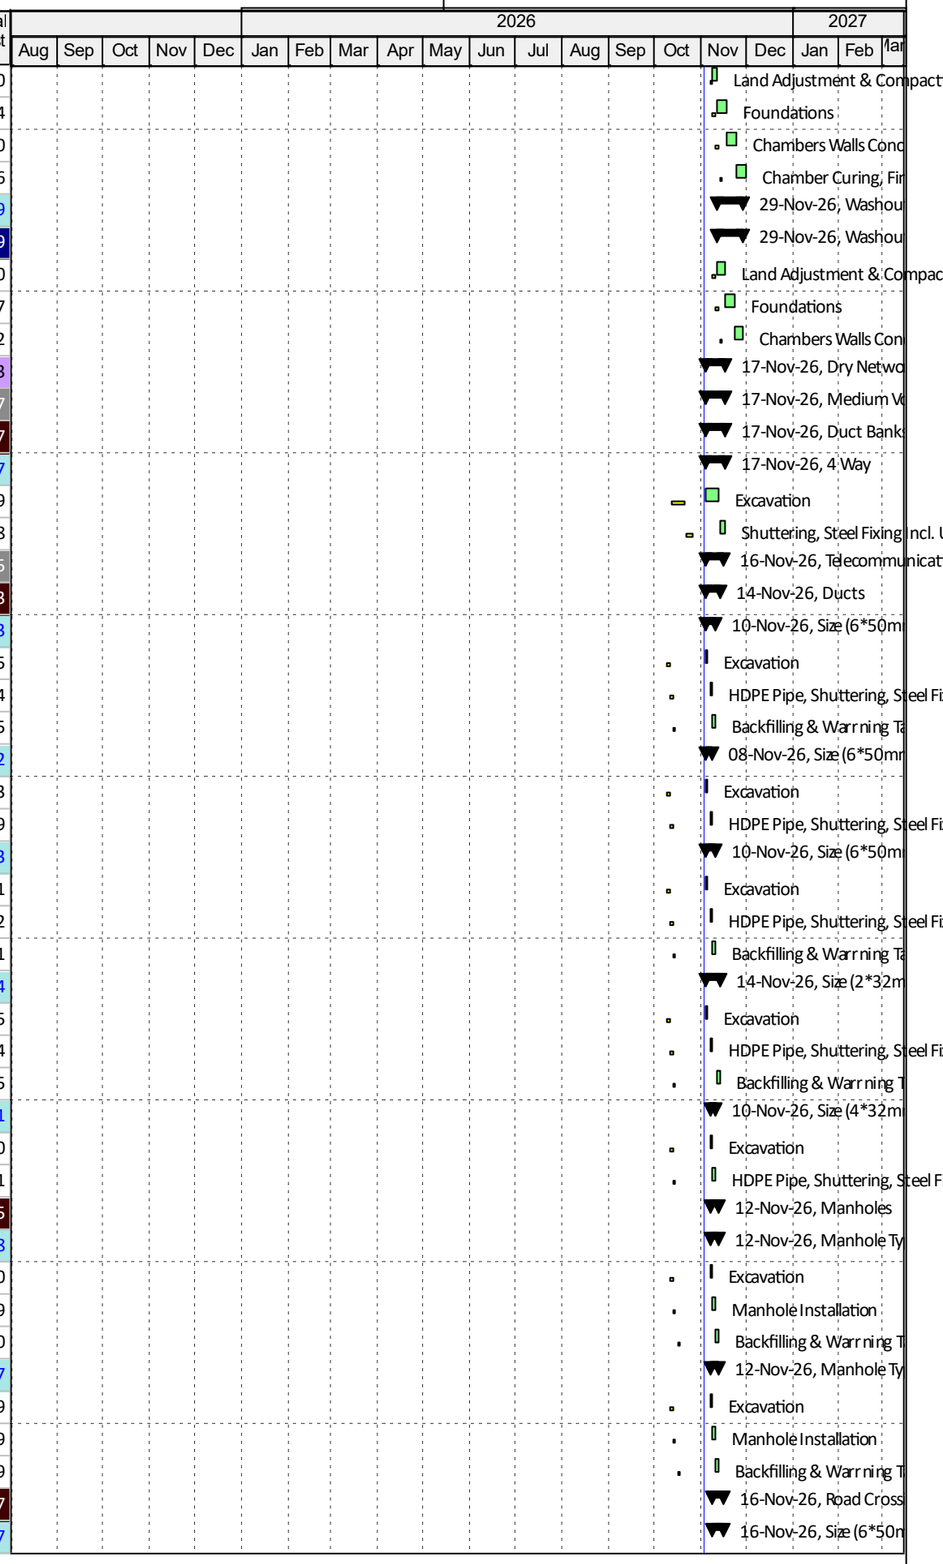


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.31 23 00.605	Excavation	2.00	1	14-Oct-26	15-Oct-26	09-Nov-26	10-Nov-26	2,221.93
B2.33 71 00.218	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	2.00	1	17-Oct-26	18-Oct-26	11-Nov-26	12-Nov-26	6,660.61
B2.33 71 00.219	Backfilling & Warrning Tape	2.00	1	19-Oct-26	20-Oct-26	15-Nov-26	16-Nov-26	2,221.93
Earth & Road Works		6.85	4	17-Oct-26	25-Nov-26	04-Nov-26	11-Nov-26	431,379.41
Earth Layers		2.00	2	17-Oct-26	29-Oct-26	04-Nov-26	05-Nov-26	68,488.12
B1.2.32 11 13.01.3_R	Subgrade(Rem)	2.00	1	17-Oct-26	22-Oct-26	04-Nov-26	05-Nov-26	11,768.83
B1.2.32 11 23.01.3_R	Aggregate Base Course(Rem)	1.44	1	24-Oct-26	29-Oct-26	04-Nov-26	05-Nov-26	56,719.29
Interlock		2.00	1	23-Nov-26	25-Nov-26	09-Nov-26	11-Nov-26	21,589.81
B1.2.32 14 13.13.3	60mm thick - Interlocking Block Pavers	2.00	1	23-Nov-26	25-Nov-26	09-Nov-26	11-Nov-26	21,589.81
Asphalt Layers		2.00	1	31-Oct-26	05-Nov-26	05-Nov-26	08-Nov-26	341,301.48
B1.2.32 11 26.01.3	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	31-Oct-26	05-Nov-26	05-Nov-26	08-Nov-26	341,301.48
Parking Roads		59.84	49	16-Sep-26	23-Nov-26	01-Oct-26 A	25-Nov-26	2,765,992.40
Wet Networks		40.84	37	16-Sep-26	10-Oct-26	07-Oct-26 A	23-Nov-26	383,947.70
Stormwater Network		29.00	24	16-Sep-26	27-Sep-26	07-Oct-26 A	09-Nov-26	238,535.31
GRP		7.28	15	16-Sep-26	27-Sep-26	28-Oct-26 A	07-Nov-26	89,296.73
?500		7.28	5	16-Sep-26	26-Sep-26	29-Oct-26 A	07-Nov-26	19,449.74
Depth From 1.5m to 2.5m		7.28	5	16-Sep-26	26-Sep-26	29-Oct-26 A	07-Nov-26	19,449.74
B6.33 42 11.03-11	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	29-Oct-26 A	05-Nov-26	3,005.66
B6.33 42 11.03-14	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	31-Oct-26 A	05-Nov-26	751.05
B6.33 42 11.03-17	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	02-Nov-26 A	05-Nov-26	6,762.38
B6.33 42 11.03-11	Embedment & Test	5.00	1	19-Sep-26	26-Sep-26	02-Nov-26 A	07-Nov-26	7,427.81
B6.33 42 11.03-11	Backfilling & Warrning Tape(Rem)	3.30	1	20-Sep-26	26-Sep-26	03-Nov-26 A	07-Nov-26	1,502.83
?600		7.28	5	16-Sep-26	26-Sep-26	28-Oct-26 A	07-Nov-26	17,767.06
Depth From 1.5m to 2.5m		7.28	5	16-Sep-26	26-Sep-26	28-Oct-26 A	07-Nov-26	17,767.06
B6.33 42 11.03-12	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	28-Oct-26 A	05-Nov-26	3,261.98
B6.33 42 11.03-15	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	01-Nov-26 A	05-Nov-26	3,261.98
B6.33 42 11.03-18	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	02-Nov-26 A	05-Nov-26	7,413.60
B6.33 42 11.03-11	Embedment & Test	5.00	1	19-Sep-26	26-Sep-26	02-Nov-26 A	07-Nov-26	2,198.52
B6.33 42 11.03-11	Backfilling & Warrning Tape(Rem)	3.12	1	21-Sep-26	26-Sep-26	03-Nov-26 A	07-Nov-26	1,630.99
?800		7.28	5	16-Sep-26	27-Sep-26	28-Oct-26 A	07-Nov-26	52,079.93
Depth From 1.5m to 2.5m		7.28	5	16-Sep-26	27-Sep-26	28-Oct-26 A	07-Nov-26	52,079.93
B6.33 42 11.03-16	Sand Bedding(Rem)	2.28	1	16-Sep-26	19-Sep-26	28-Oct-26 A	05-Nov-26	2,011.07
B6.33 42 11.03-13	Excavation(Rem)	2.28	1	16-Sep-26	19-Sep-26	29-Oct-26 A	05-Nov-26	8,048.52
B6.33 42 11.03-19	Pipe Laying(Rem)	2.28	1	16-Sep-26	19-Sep-26	02-Nov-26 A	05-Nov-26	18,108.11
B6.33 42 11.03-11	Embedment & Test	5.00	1	19-Sep-26	26-Sep-26	02-Nov-26 A	07-Nov-26	19,890.09
B6.33 42 11.03-11	Backfilling & Warrning Tape(Rem)	3.12	1	22-Sep-26	27-Sep-26	03-Nov-26 A	07-Nov-26	4,022.14
Manholes		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	9,648.47
?1200		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	9,648.47
Depth From 1.5m to 2.5m		5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	9,648.47
B6.33 05 13.04-11	Test, Internal Finishing, Benching & Cover	5.00	1	19-Sep-26	24-Sep-26	04-Nov-26	09-Nov-26	9,648.47
Catch Basins		27.00	8	16-Sep-26	19-Sep-26	07-Oct-26 A	07-Nov-26	139,590.11
Single		3.00	4	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	29,639.80
B6.33 05 40.01.30(	Blinding Conc.(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,967.86
B6.33 05 40.01.31(	Catch Basin Installation(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	13,326.27
B6.33 05 40.01.29(	Excavation, Compaction & Vapour Barrier(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	4,461.49
B6.33 05 40.01.32(	Backfilling, DI Frame & Grate Cover Fixing(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	8,884.18

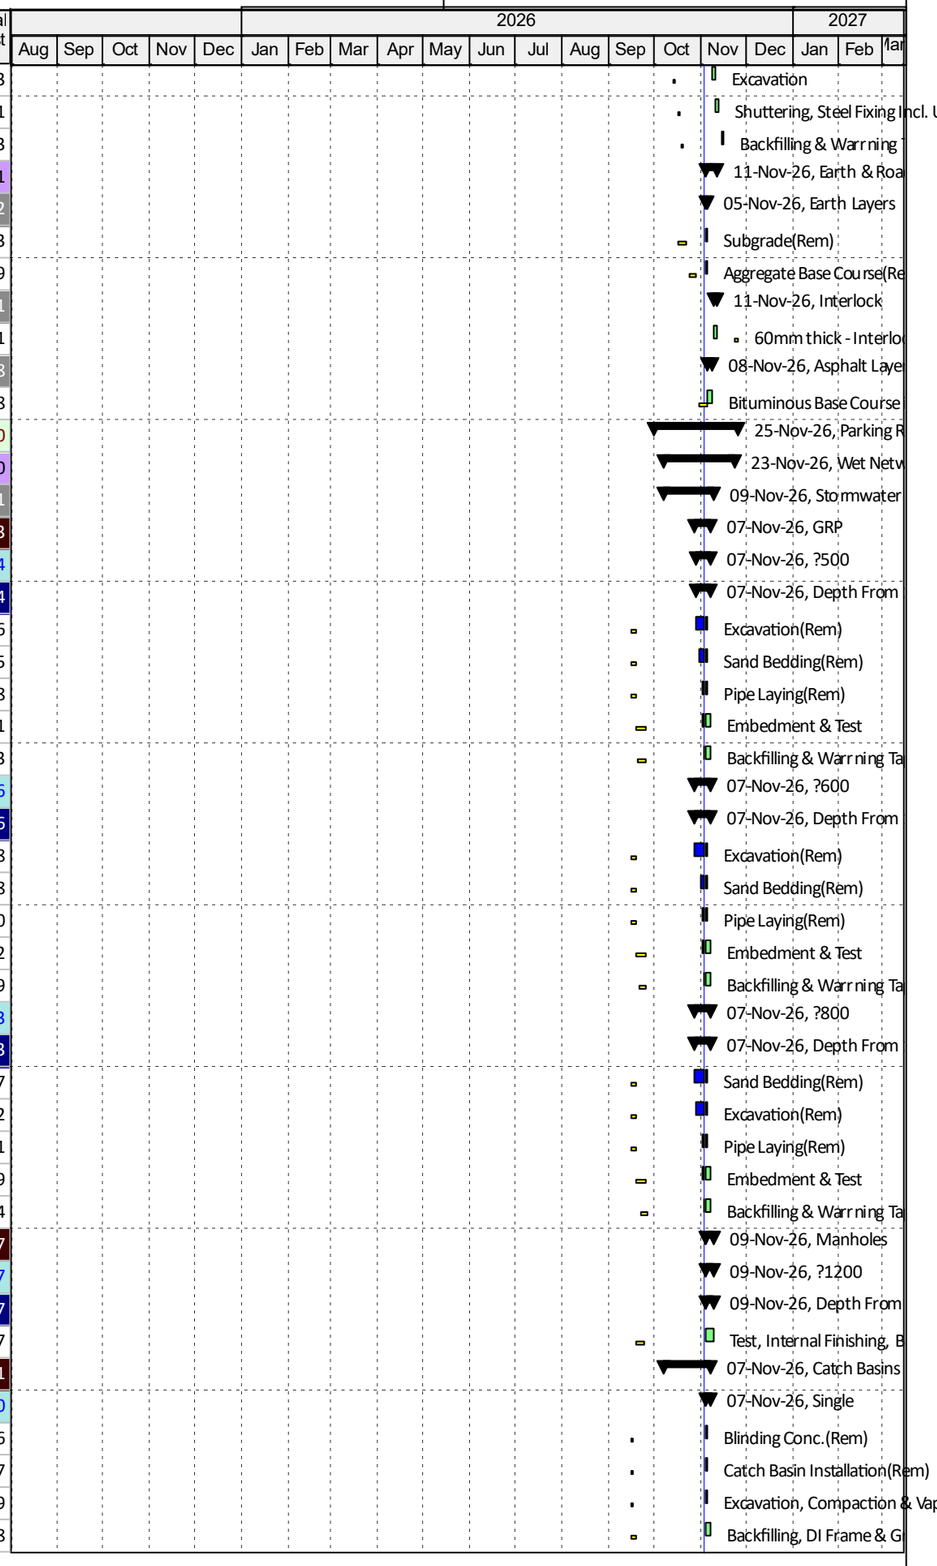

Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
UPVC		2.09	4	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	109,950.31
?300 From 0.0 to 1.5m		2.09	2	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	54,975.16
B6.33 42 11.35-1	Catch Basin Opening Prep.(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	10,995.03
B6.33 42 11.35-1	Fittings & Pipe Installation(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	43,980.12
?400 From 0.0 to 1.5m		2.09	2	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	54,975.16
B6.33 42 11.36-1	Catch Basin Opening Prep.(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	10,995.03
B6.33 42 11.36-1	Fittings & Pipe Installation(Rem)	2.09	1	16-Sep-26	19-Sep-26	07-Oct-26 A	04-Nov-26	43,980.12
Fire Fighting Network		22.84	13	16-Sep-26	10-Oct-26	15-Oct-26 A	23-Nov-26	145,412.39
HDPE Pipes		11.00	10	16-Sep-26	29-Sep-26	15-Oct-26 A	05-Nov-26	63,335.97
?250mm		11.00	10	16-Sep-26	29-Sep-26	15-Oct-26 A	05-Nov-26	63,335.97
Depth: 0.0m - 1.5m		11.00	5	16-Sep-26	29-Sep-26	15-Oct-26 A	05-Nov-26	59,148.69
B3.1. 33 14 13.01.	Excavation(Rem)	4.00	1	16-Sep-26	20-Sep-26	15-Oct-26 A	04-Nov-26	3,460.99
B3.1. 33 14 13.01.	Sand Bedding(Rem)	4.00	1	16-Sep-26	20-Sep-26	18-Oct-26 A	04-Nov-26	1,730.67
B3.1. 33 14 13.01.	Pipe Laying(Rem)	4.00	1	16-Sep-26	20-Sep-26	19-Oct-26 A	04-Nov-26	15,574.64
B3.1. 33 14 13.01.	Embedment & Test(Rem)	4.00	1	16-Sep-26	20-Sep-26	22-Oct-26 A	04-Nov-26	6,921.98
B3.1. 33 14 13.01.	Backfilling & Warrning Tape	7.00	1	21-Sep-26	29-Sep-26	26-Oct-26 A	05-Nov-26	31,460.40
Depth: 1.51m - 2.5m		11.00	5	16-Sep-26	29-Sep-26	17-Oct-26 A	05-Nov-26	4,187.28
B3.1. 33 14 13.01.	Excavation(Rem)	4.00	1	16-Sep-26	20-Sep-26	17-Oct-26 A	04-Nov-26	386.52
B3.1. 33 14 13.01.	Sand Bedding(Rem)	4.00	1	16-Sep-26	20-Sep-26	19-Oct-26 A	04-Nov-26	118.10
B3.1. 33 14 13.01.	Pipe Laying(Rem)	4.00	1	16-Sep-26	20-Sep-26	20-Oct-26 A	04-Nov-26	1,062.92
B3.1. 33 14 13.01.	Embedment & Test(Rem)	4.00	1	16-Sep-26	20-Sep-26	24-Oct-26 A	04-Nov-26	472.41
B3.1. 33 14 13.01.	Backfilling & Warrning Tape	7.00	1	21-Sep-26	29-Sep-26	29-Oct-26 A	05-Nov-26	2,147.32
Fire Hydrant		16.00	3	21-Sep-26	10-Oct-26	04-Nov-26	23-Nov-26	82,076.43
B3.33 14 19.01.fh29	Riser Pipe & Flanged Fittings Installation	4.00	1	21-Sep-26	26-Sep-26	04-Nov-26	09-Nov-26	16,415.29
B3.33 14 19.01.fh28	Firehydrant Fixing/Installation	5.00	1	27-Sep-26	01-Oct-26	09-Nov-26	15-Nov-26	49,245.86
B3.33 14 19.01.fh30	Backfilling & Compaction	7.00	1	03-Oct-26	10-Oct-26	15-Nov-26	23-Nov-26	16,415.29
Dry Networks		15.84	8	20-Sep-26	12-Oct-26	08-Nov-26	25-Nov-26	234,519.02
Low Voltage Network		2.00	1	11-Oct-26	12-Oct-26	23-Nov-26	25-Nov-26	95,723.28
Cables		2.00	1	11-Oct-26	12-Oct-26	23-Nov-26	25-Nov-26	95,723.28
4C,10+1C,10mm2		2.00	1	11-Oct-26	12-Oct-26	23-Nov-26	25-Nov-26	95,723.28
B2.33 71 00 01 10	Cable Pulling	2.00	1	11-Oct-26	12-Oct-26	23-Nov-26	25-Nov-26	95,723.28
Street Lighting		11.00	7	20-Sep-26	03-Oct-26	08-Nov-26	19-Nov-26	138,795.74
Duct Banks		7.00	4	20-Sep-26	28-Sep-26	08-Nov-26	15-Nov-26	66,872.87
2 Way		5.00	2	20-Sep-26	26-Sep-26	08-Nov-26	12-Nov-26	36,832.55
B2.33 71 00 02 64	Excavation	2.00	1	20-Sep-26	21-Sep-26	08-Nov-26	09-Nov-26	9,208.14
B2.33 71 00 02 65	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	22-Sep-26	26-Sep-26	10-Nov-26	12-Nov-26	27,624.41
6 Way		5.00	2	22-Sep-26	28-Sep-26	10-Nov-26	15-Nov-26	30,040.32
B2.33 71 00 02 67	Excavation	2.00	1	22-Sep-26	24-Sep-26	10-Nov-26	11-Nov-26	7,510.08
B2.33 71 00 02 68	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	26-Sep-26	28-Sep-26		15-Nov-26	22,530.24
Drawpits		7.00	3	26-Sep-26	03-Oct-26	12-Nov-26	19-Nov-26	71,922.87
B2.33 71 00 02 70	Excavation	2.00	1	26-Sep-26	27-Sep-26	12-Nov-26	14-Nov-26	14,384.57
B2.33 71 00 02 71	Drawpits Installation	2.00	1	28-Sep-26	29-Sep-26	15-Nov-26	16-Nov-26	43,153.72
B2.33 71 00 02 72	Backfilling & Warrning Tape	3.00	1	30-Sep-26	03-Oct-26	17-Nov-26	19-Nov-26	14,384.57
Earth & Road Works		46.00	4	24-Oct-26	23-Nov-26	01-Oct-26 A	09-Nov-26	2,147,525.69
Earth Layers		5.00	2	24-Oct-26	03-Nov-26	04-Nov-26	09-Nov-26	481,654.90
B1.2.32 11 13.01.7_R	Subgrade(Rem)	5.00	1	24-Oct-26	01-Nov-26	04-Nov-26	09-Nov-26	149,652.58

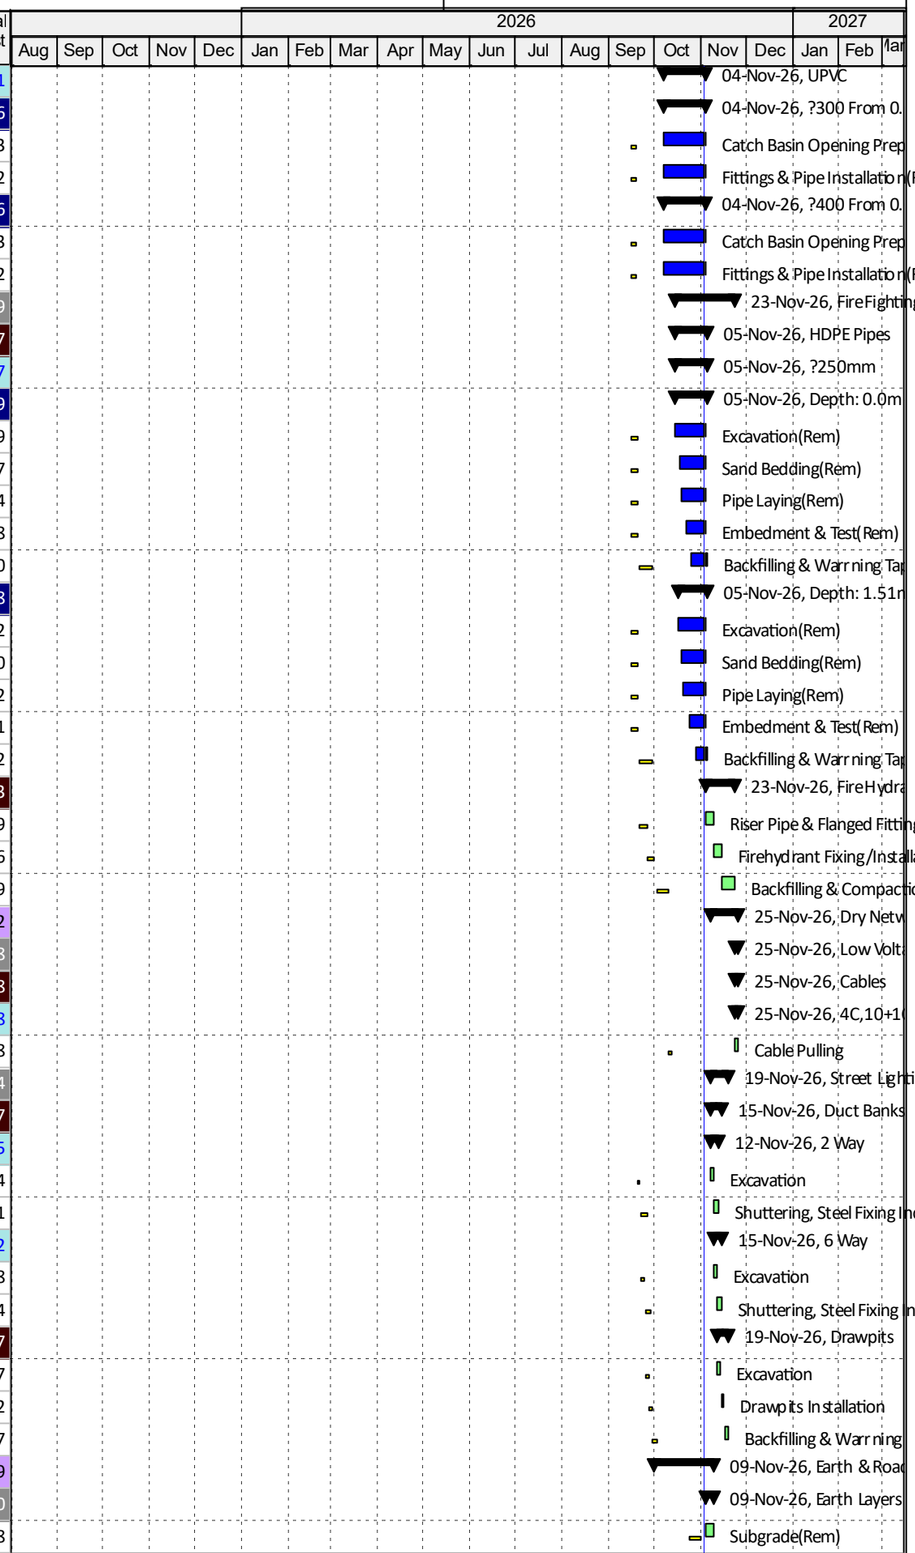


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B1.2.32 11 23.01.7_R	Aggregate Base Course(Rem)	2.00	1	29-Oct-26	03-Nov-26	04-Nov-26	05-Nov-26	332,002.32
Interlock		2.00	1	21-Nov-26	23-Nov-26	07-Nov-26	09-Nov-26	227,472.88
B1.2.32 14 13.13.7	60mm thick - Interlocking Block Pavers	2.00	1	21-Nov-26	23-Nov-26	07-Nov-26	09-Nov-26	227,472.88
Asphalt Layers		2.00	1	08-Nov-26	16-Nov-26	01-Oct-26 A	05-Nov-26	1,438,397.91
B1.2.32 11 26.01.7_R	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	08-Nov-26	16-Nov-26	01-Oct-26 A	05-Nov-26	1,438,397.91
Arterial Road		62.14	67	16-Sep-26	12-Nov-26	26-Sep-26 A	29-Nov-26	6,402,403.62
Wet Networks		58.00	35	16-Sep-26	17-Oct-26	03-Oct-26 A	23-Nov-26	1,069,034.87
Sewerage Network		38.12	7	16-Sep-26	08-Oct-26	07-Oct-26 A	21-Nov-26	36,064.67
HDPE Pipes		4.00	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	16,794.30
?160		4.00	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	16,794.30
Depth From 1.5m to 2.5m		4.00	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	16,794.30
B5.33 31 23.024_I	Embedment & Test(Rem)	4.00	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	16,794.30
Valves & Chambers		14.12	6	17-Sep-26	08-Oct-26	04-Nov-26	21-Nov-26	19,270.37
Gate Valves		4.00	2	17-Sep-26	21-Sep-26	04-Nov-26	08-Nov-26	3,127.62
B3.33 14 19.01.1_R	Burried Isolation Valve Installation(Rem)	2.00	1	17-Sep-26	19-Sep-26	04-Nov-26	05-Nov-26	2,334.05
B3.33 14 19.01.7	Spindle & Surface Box	2.00	1	20-Sep-26	21-Sep-26	07-Nov-26	08-Nov-26	793.57
Air Valves in Chambers		14.00	4	21-Sep-26	08-Oct-26	04-Nov-26	21-Nov-26	16,142.75
B3.33 14 19.01.26	Land Adjustment & Compaction	3.00	1	21-Sep-26	26-Sep-26	04-Nov-26	08-Nov-26	2,409.37
B3.33 14 19.01.28	Foundations	4.00	1	26-Sep-26	30-Sep-26	08-Nov-26	12-Nov-26	3,132.18
B3.33 14 19.01.30	Chambers Walls Conc Cast In Situ	3.00	1	30-Sep-26	04-Oct-26	12-Nov-26	16-Nov-26	7,469.03
B3.33 14 19.01.32	Chamber Curing, Finishing & Steel Cover	4.00	1	04-Oct-26	08-Oct-26	16-Nov-26	21-Nov-26	3,132.18
Stormwater Network		44.86	6	16-Sep-26	14-Oct-26	03-Oct-26 A	09-Nov-26	419,394.70
Box Cul.		44.86	6	16-Sep-26	14-Oct-26	03-Oct-26 A	09-Nov-26	419,394.70
B6. 33 42 13.015_R	Curing & Water Proofing(Rem)	4.56	1	16-Sep-26	21-Sep-26	03-Oct-26 A	04-Nov-26	144,148.92
B6. 33 42 13.016	Backfilling & Warrning Tape	6.00	1	01-Oct-26	08-Oct-26	22-Oct-26 A	09-Nov-26	242,947.61
Concrete Chambers		20.95	4	21-Sep-26	14-Oct-26	14-Oct-26 A	09-Nov-26	32,298.17
Size 1.5 x 1.5 m, depth 2.5 to 3.5		20.95	2	21-Sep-26	14-Oct-26	14-Oct-26 A	09-Nov-26	14,251.73
B6.33 05 63.054	Waterproofing Tanking Membrane & Protection	4.00	1	21-Sep-26	27-Sep-26	14-Oct-26 A	04-Nov-26	7,037.89
B6.33 05 63.053	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	5.00	1	08-Oct-26	14-Oct-26	02-Nov-26 A	09-Nov-26	7,213.84
Size 1.5 x 1.5 m, depth 3.5 to 4.5		16.95	2	27-Sep-26	14-Oct-26	19-Oct-26 A	09-Nov-26	18,046.44
B6.33 05 63.064	Waterproofing Tanking Membrane & Protection	4.00	1	27-Sep-26	01-Oct-26	19-Oct-26 A	04-Nov-26	9,023.22
B6.33 05 63.063	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	5.00	1	08-Oct-26	14-Oct-26	02-Nov-26 A	09-Nov-26	9,023.22
Potable Water Network		16.00	14	16-Sep-26	17-Oct-26	28-Oct-26 A	15-Nov-26	563,226.36
HDPE Pipes		8.80	10	08-Oct-26	17-Oct-26	28-Oct-26 A	11-Nov-26	493,683.23
?250mm		8.80	10	08-Oct-26	17-Oct-26	28-Oct-26 A	11-Nov-26	493,683.23
Depth: 0.0m - 1.5m		7.00	5	08-Oct-26	17-Oct-26	28-Oct-26 A	11-Nov-26	222,032.84
B3.33 14 11.01.01	Excavation(Rem)	3.00	1	11-Oct-26	13-Oct-26	28-Oct-26 A	07-Nov-26	44,383.29
B3.33 14 11.01.01	Sand Bedding(Rem)	3.00	1	11-Oct-26	13-Oct-26	29-Oct-26 A	07-Nov-26	11,101.16
B3.33 14 11.01.01	Pipe Laying(Rem)	3.00	1	11-Oct-26	13-Oct-26	31-Oct-26 A	07-Nov-26	99,971.32
B3.33 14 11.01.01	Embedment & Test(Rem)	5.00	1	08-Oct-26	13-Oct-26	31-Oct-26 A	09-Nov-26	44,385.42
B3.33 14 11.01.01	Backfilling & Warrning Tape(Rem)	6.00	1	11-Oct-26	17-Oct-26	01-Nov-26 A	11-Nov-26	22,191.64
Depth: 1.51m - 2.5m		8.80	5	10-Oct-26	17-Oct-26	28-Oct-26 A	10-Nov-26	271,650.39
B3.33 14 11.01.02	Excavation(Rem)	4.00	1	11-Oct-26	14-Oct-26	28-Oct-26 A	08-Nov-26	54,329.03
B3.33 14 11.01.02	Sand Bedding(Rem)	3.00	1	12-Oct-26	14-Oct-26	29-Oct-26 A	08-Nov-26	13,584.89
B3.33 14 11.01.02	Pipe Laying(Rem)	4.00	1	11-Oct-26	14-Oct-26	31-Oct-26 A	08-Nov-26	122,242.94
B3.33 14 11.01.02	Embedment & Test(Rem)	5.00	1	10-Oct-26	14-Oct-26	01-Nov-26 A	09-Nov-26	54,329.03

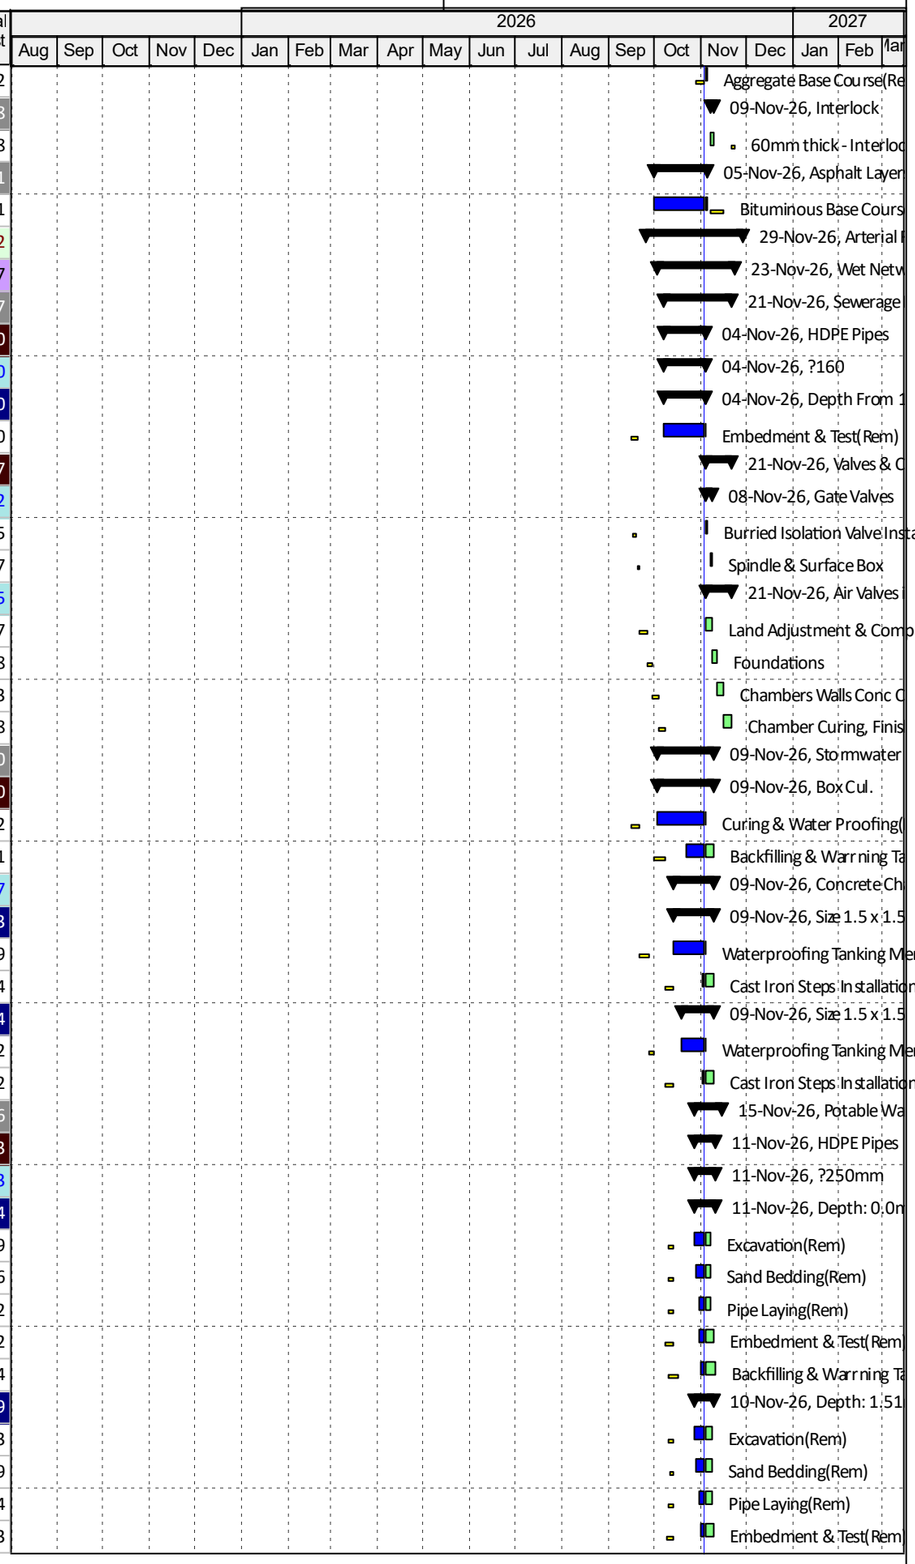

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 14 11.01.02	Backfilling & Warrning Tape(Rem)	6.00	1	11-Oct-26	17-Oct-26	03-Nov-26 A	10-Nov-26	27,164.51
Valves & Chambers		5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	7,834.72
Air Valves		5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	7,834.72
Air valves on less than 315 mm. (In Chamber)		5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	7,834.72
B3.33 05 63.02.19	Valve & Fitting Installation	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	7,834.72
Flow Meter (On Chamber)		10.00	3	16-Sep-26	28-Sep-26	04-Nov-26	15-Nov-26	61,708.41
B3.33 14 19.01.fm1(	RC Conc. Works	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	12,460.81
B3.33 14 19.01.fm1	Fixing Flange/Connections	3.00	1	21-Sep-26	24-Sep-26	09-Nov-26	11-Nov-26	12,460.81
B3.33 14 19.01.fm1	Flow Meter Installation	3.00	1	26-Sep-26	28-Sep-26	12-Nov-26	15-Nov-26	36,786.79
Fire Fighting Network		13.00	3	21-Sep-26	06-Oct-26	09-Nov-26	23-Nov-26	0.00
Flow Meter (On Chamber)		13.00	3	21-Sep-26	06-Oct-26	09-Nov-26	23-Nov-26	0.00
B3.33 14 19.01.fm5(	RC Conc. Works	5.00	1	21-Sep-26	27-Sep-26	09-Nov-26	14-Nov-26	0.00
B3.33 14 19.01.fm4	Fixing Flange/Connections	4.00	1	28-Sep-26	01-Oct-26	15-Nov-26	18-Nov-26	0.00
B3.33 14 19.01.fm5	Flow Meter Installation	4.00	1	03-Oct-26	06-Oct-26	19-Nov-26	23-Nov-26	0.00
TSE Network		10.14	5	16-Sep-26	29-Sep-26	04-Nov-26	16-Nov-26	50,349.14
HDPE Pipes		10.14	5	16-Sep-26	29-Sep-26	04-Nov-26	16-Nov-26	50,349.14
?125mm		10.14	5	16-Sep-26	29-Sep-26	04-Nov-26	16-Nov-26	50,349.14
Depth: 0.0m - 1.5m		10.14	5	16-Sep-26	29-Sep-26	04-Nov-26	16-Nov-26	50,349.14
B4.33 14 13.081_I	Excavation(Rem)	2.57	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	9,801.15
B4.33 14 13.082_I	Sand Bedding(Rem)	2.57	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,450.89
B4.33 14 13.083_I	Pipe Laying(Rem)	2.57	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	22,053.19
B4.33 14 13.084_I	Embedment & Test(Rem)	4.14	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,801.15
B4.33 14 13.085	Backfilling & Warrning Tape	6.00	1	21-Sep-26	29-Sep-26	09-Nov-26	16-Nov-26	6,242.77
Dry Networks		39.14	16	16-Sep-26	24-Oct-26	12-Oct-26 A	29-Nov-26	1,519,008.90
Medium Voltage Network		14.00	6	26-Sep-26	12-Oct-26	12-Nov-26	29-Nov-26	1,308,375.44
Cables		14.00	6	26-Sep-26	12-Oct-26	12-Nov-26	29-Nov-26	1,308,375.44
3C,500mm2		5.00	3	26-Sep-26	01-Oct-26	12-Nov-26	18-Nov-26	1,054,878.63
B2.33 71 49.23.01(	Cable Pulling(Rem)	2.60	1	26-Sep-26	28-Sep-26	12-Nov-26	15-Nov-26	93,623.33
B2.33 71 19 16_R	Land Adjustment(Rem)	3.00	1	26-Sep-26	29-Sep-26	12-Nov-26	16-Nov-26	274,644.37
B2.33 71 19 17_R	Backfilling(Rem)	5.00	1	26-Sep-26	01-Oct-26	12-Nov-26	18-Nov-26	686,610.93
Cable Replacement		11.00	3	29-Sep-26	12-Oct-26	16-Nov-26	29-Nov-26	253,496.81
B2.33 71 49.23.061	Excavation	3.00	1	29-Sep-26	03-Oct-26	16-Nov-26	19-Nov-26	63,374.20
B2.33 71 49.23.062	Old Cable Grubbing	4.00	1	03-Oct-26	07-Oct-26	19-Nov-26	24-Nov-26	126,748.40
B2.33 71 49.23.063	New Cable Installation	4.00	1	07-Oct-26	12-Oct-26	24-Nov-26	29-Nov-26	63,374.20
Street Lighting		28.32	10	16-Sep-26	24-Oct-26	12-Oct-26 A	10-Nov-26	210,633.46
Cables		5.50	3	26-Sep-26	01-Oct-26	12-Oct-26 A	04-Nov-26	
4C,10+1C,10mm2		5.50	3	26-Sep-26	01-Oct-26	12-Oct-26 A	04-Nov-26	77,891.43
B2.33 71 19 18_R	Land Adjustment(Rem)	1.50	1	26-Sep-26	27-Sep-26	12-Oct-26 A	04-Nov-26	12,981.98
B2.33 71 49.23.64_	Cable Pulling(Rem)	2.50	1	26-Sep-26	28-Sep-26	19-Oct-26 A	04-Nov-26	38,945.48
B2.33 71 19 19	Backfilling	3.00	1	28-Sep-26	01-Oct-26	31-Oct-26 A	04-Nov-26	25,963.96
SL Poles		8.00	2	16-Sep-26	26-Sep-26	14-Oct-26 A	07-Nov-26	59,764.62
Pole (12 M Single Arm)		8.00	2	16-Sep-26	26-Sep-26	14-Oct-26 A	07-Nov-26	59,764.62
B2.33 71 16.034_R	Lighting Luminares Inst(Rem)	2.00	1	16-Sep-26	17-Sep-26	14-Oct-26 A	04-Nov-26	3,751.94
B2.33 71 16.035	Backfilling, Grouting & Chamfering	6.00	1	19-Sep-26	26-Sep-26	17-Oct-26 A	07-Nov-26	56,012.68
Earthing		16.32	3	19-Sep-26	24-Oct-26	15-Oct-26 A	08-Nov-26	4,481.74
B2.33 71 19 20	Land Adjustment	3.00	1	19-Sep-26	21-Sep-26	15-Oct-26 A	04-Nov-26	904.39

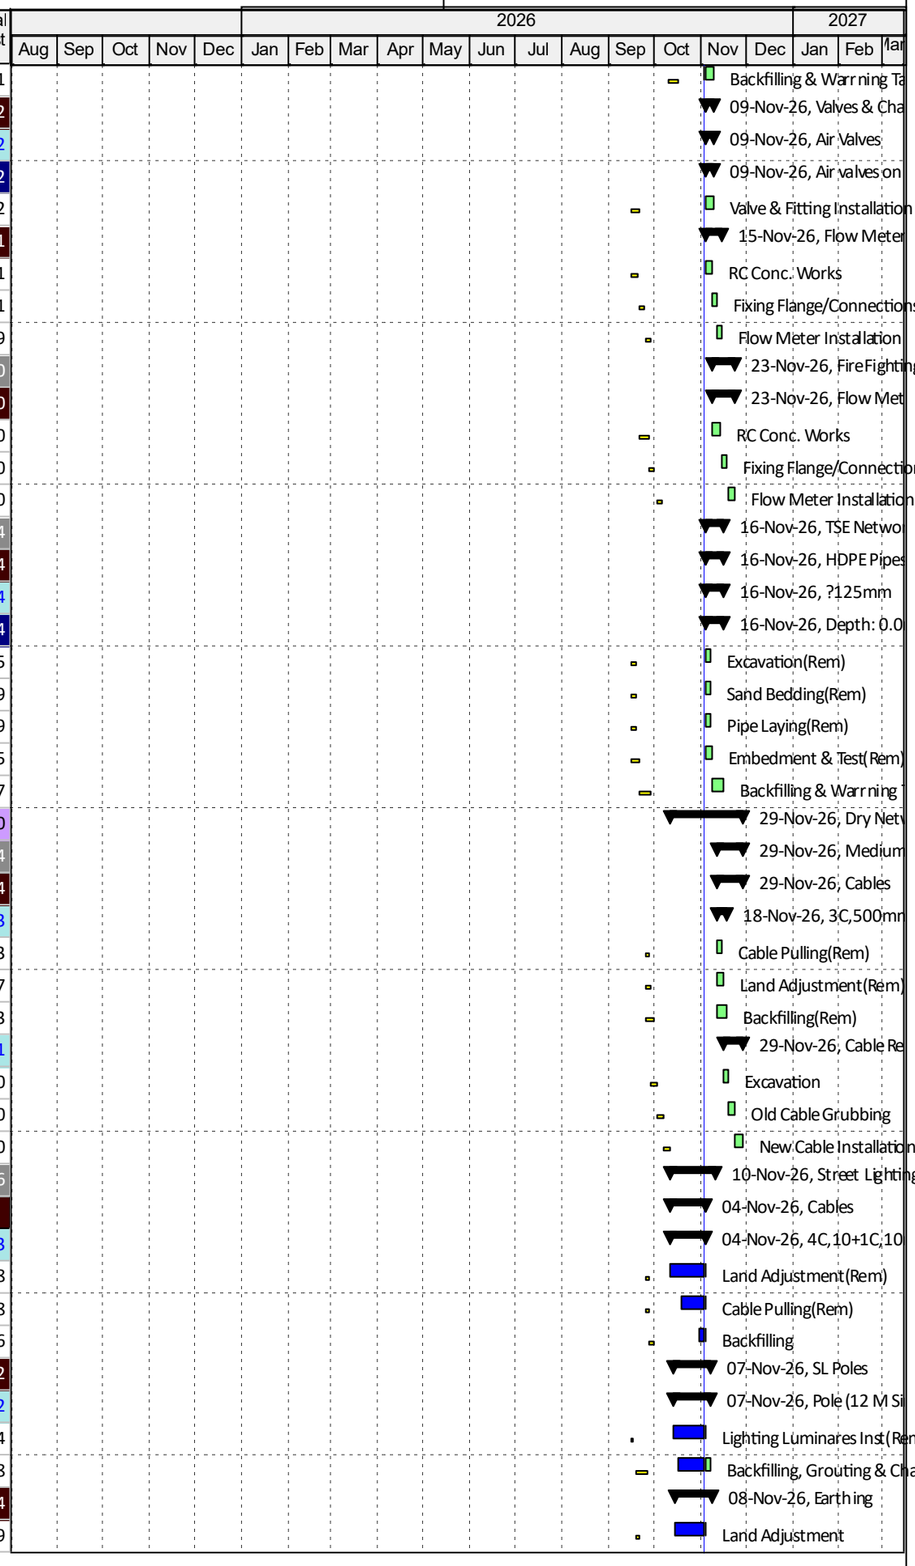


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.33 71 19 22	Backfilling	3.00	1	22-Oct-26	24-Oct-26	21-Oct-26 A	04-Nov-26	904.39
B2.33 71 19 21	Earth Rods& Conduits	3.00	1	22-Sep-26	26-Sep-26	04-Nov-26	08-Nov-26	2,672.96
SL Pillars		4.00	2	11-Oct-26	14-Oct-26	07-Nov-26	10-Nov-26	68,495.68
B2.33 71 26 03	Pillars Installation (Internal Wiring)	2.00	1	11-Oct-26	12-Oct-26	07-Nov-26	08-Nov-26	16,342.35
B2.33 71 26 041	KWH meter mounting aframe installation	2.00	1	13-Oct-26	14-Oct-26	09-Nov-26	10-Nov-26	52,153.33
Earth & Road Works		59.32	16	05-Oct-26	12-Nov-26	26-Sep-26 A	25-Nov-26	3,814,359.84
Earth Layers		42.95	2	05-Oct-26	11-Oct-26	30-Sep-26 A	10-Nov-26	502,745.29
B1.2.32 11 13.01.8_R	Subgrade(Rem)	6.00	1	05-Oct-26	08-Oct-26	30-Sep-26 A	10-Nov-26	104,166.60
B1.2.32 11 23.01.8_R	Aggregate Base Course(Rem)	1.95	1	07-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	398,578.69
Interlock		3.00	1	25-Oct-26	27-Oct-26	04-Nov-26	08-Nov-26	277,084.34
B1.2.32 14 13.13.8	60mm thick - Interlocking Block Pavers	3.00	1	25-Oct-26	27-Oct-26	04-Nov-26	08-Nov-26	277,084.34
Curbstone		2.00	5	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	23,677.07
Pre-Installation		2.00	3	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	10,656.06
32 16 13.031_R	Excavation(Rem)	2.00	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	3,551.44
32 16 13.032_R	PCC(Rem)	2.00	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	3,553.18
32 16 13.033_R	Haunching(Rem)	1.80	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	3,551.44
Installation		1.80	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	10,653.56
B1.2.32 16.13.01.8_	Curb Stone, Type K1(Rem)	1.80	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	10,653.56
Finishing		1.80	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	2,367.44
32 16 13.08_R	Finishing, Fareface(Rem)	1.80	1	24-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	2,367.44
Asphalt Layers		52.32	2	11-Oct-26	04-Nov-26	26-Sep-26 A	17-Nov-26	2,947,004.14
B1.2.32 11 26.01.8_R	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.24	1	11-Oct-26	14-Oct-26	26-Sep-26 A	05-Nov-26	1,226,477.08
B1.2.32 12 16.01.8	Bituminous concrete Wearing Course, including tack coat (RC2)	5.00	1	25-Oct-26	04-Nov-26	11-Nov-26	17-Nov-26	1,720,527.06
Pavement Marking		5.00	2	04-Nov-26	10-Nov-26	17-Nov-26	23-Nov-26	43,651.52
B1.2.32 17 23.02.8	Retroreflective Thermoplastic Yellow, Traffic lines	2.00	1	04-Nov-26	07-Nov-26	17-Nov-26	19-Nov-26	14,143.05
B1.2.32 17 23.01.8	Retroreflective Thermoplastic White Traffic lines	3.00	1	07-Nov-26	10-Nov-26	19-Nov-26	23-Nov-26	29,508.46
Traffic Signs		17.00	4	15-Oct-26	12-Nov-26	05-Nov-26	25-Nov-26	20,197.49
Pre-Installation		5.00	2	15-Oct-26	20-Oct-26	05-Nov-26	11-Nov-26	1,171.97
B2.31 23 00.221	Excavation	2.00	1	15-Oct-26	17-Oct-26	05-Nov-26	08-Nov-26	585.99
10 14 53.08	Foundation	3.00	1	18-Oct-26	20-Oct-26	08-Nov-26	11-Nov-26	585.99
Installation		5.00	2	07-Nov-26	12-Nov-26	19-Nov-26	25-Nov-26	19,025.51
B1.2.10 14 53.018	1 Sheet Alumenium, Single post	2.00	1	07-Nov-26	09-Nov-26	19-Nov-26	22-Nov-26	16,739.11
B1.2.10 14 53.028	2 Sheet Alumenium, Single post	2.00	1	10-Nov-26	12-Nov-26	23-Nov-26	25-Nov-26	2,286.40
Guard Rooms		21.00	36	21-Sep-26	08-Nov-26	01-Nov-26 A	25-Nov-26	334,947.39
Underground Utilities		8.00	4	04-Oct-26	12-Oct-26	04-Nov-26	14-Nov-26	19,423.98
B8.31 23 16.0131	Scupper ?110mm	2.00	1	04-Oct-26	05-Oct-26	04-Nov-26	07-Nov-26	11,126.00
B8.31 23 16.0133	Clean out ?110mm	2.00	1	06-Oct-26	07-Oct-26	07-Nov-26	09-Nov-26	254.62
B8.31 23 16.0135	Floor drain	2.00	1	08-Oct-26	10-Oct-26	09-Nov-26	11-Nov-26	510.12
B8.31 23 16.0137	Manhole, dimensions 600mmX600mm	2.00	1	11-Oct-26	12-Oct-26	11-Nov-26	14-Nov-26	7,533.24
Superstructure - Roof		10.00	4	21-Sep-26	30-Sep-26	01-Nov-26 A	12-Nov-26	31,732.65
B8.31 23 16.0147	Roof Slab and beams	2.00	1	21-Sep-26	22-Sep-26	01-Nov-26 A	04-Nov-26	23,170.74
B8.31 23 16.0153	Sloped screed for roof	2.00	1	24-Sep-26	26-Sep-26	07-Nov-26	08-Nov-26	1,673.60
B8.31 23 16.0187	Water proofing Membrane for roof	2.00	1	27-Sep-26	28-Sep-26	09-Nov-26	10-Nov-26	4,464.91
B8.31 23 16.01111	50mm Extruded polystyrene insulation for roof	2.00	1	29-Sep-26	30-Sep-26	11-Nov-26	12-Nov-26	2,423.41
Enclosure & Weatherproofing		12.00	5	18-Oct-26	31-Oct-26	04-Nov-26	18-Nov-26	58,765.84
B8.31 23 16.0149	Aluminum window W01 size (1.3m x 1.4m)	1.00	1	18-Oct-26	18-Oct-26	04-Nov-26	05-Nov-26	25,526.12

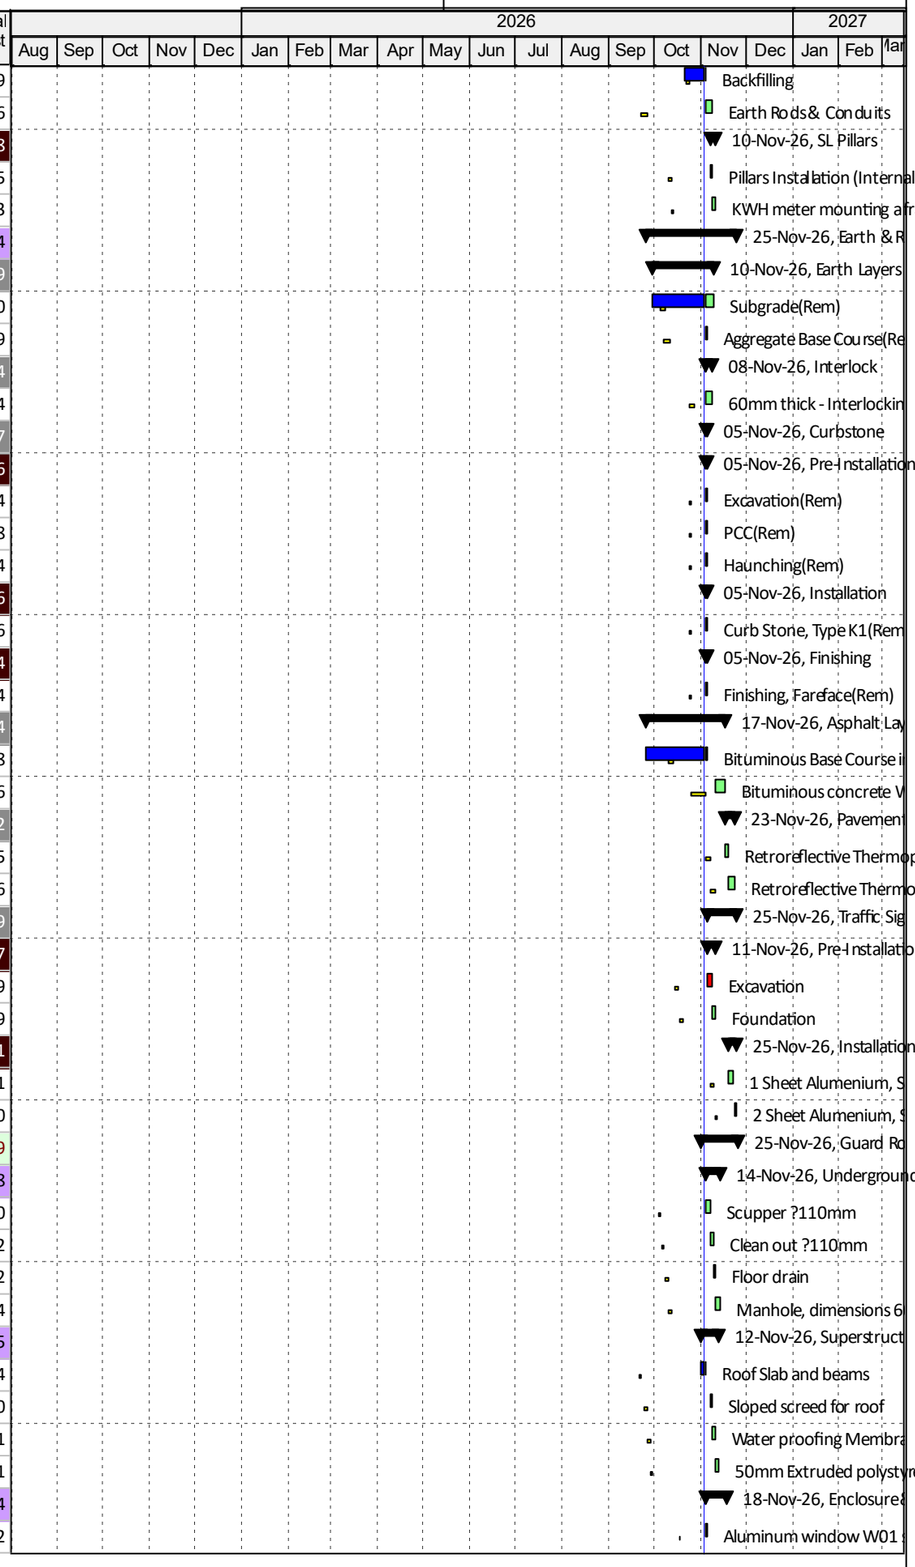


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B8.31 23 16.0155	Aluminum window W02 size (0.6m x 0.9m)	2.00	1	19-Oct-26	20-Oct-26	05-Nov-26	08-Nov-26	1,274.86
B8.31 23 16.0189	External plastering	4.00	1	21-Oct-26	25-Oct-26	08-Nov-26	12-Nov-26	11,179.44
B8.31 23 16.01113	Water proofing Membrane with 50mm screed protection	2.00	1	26-Oct-26	27-Oct-26	12-Nov-26	15-Nov-26	4,699.45
B8.31 23 16.01137	External painting	3.00	1	28-Oct-26	31-Oct-26	15-Nov-26	18-Nov-26	16,085.97
Interior & MEP		14.00	12	18-Oct-26	05-Nov-26	04-Nov-26	19-Nov-26	177,038.14
B8.31 23 16.0151	Internal plastering	2.00	1	18-Oct-26	19-Oct-26	04-Nov-26	05-Nov-26	5,604.49
B8.31 23 16.0157	Cementitious Water proofing for wet areas	2.00	1	20-Oct-26	21-Oct-26	07-Nov-26	08-Nov-26	393.68
Mechanical		4.00	2	24-Oct-26	27-Oct-26	07-Nov-26	10-Nov-26	23,469.00
B8.31 23 16.0159	DX wall mounted Split/AC	2.00	1	24-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	22,310.04
B8.31 23 16.0191	EF-01 Exhaust axial fan	2.00	1	26-Oct-26	27-Oct-26	09-Nov-26	10-Nov-26	1,158.96
Plumbing & Electrical		12.00	8	20-Oct-26	05-Nov-26	07-Nov-26	19-Nov-26	147,570.96
B8.31 23 16.0177	20A DOUBLE POLE SWITCH	2.00	1	20-Oct-26	21-Oct-26	07-Nov-26	08-Nov-26	1,269.60
B8.31 23 16.0179	13A SPUR OUTLET, For guard room 1&2	2.00	1	22-Oct-26	24-Oct-26	09-Nov-26	10-Nov-26	2,539.20
B8.31 23 16.0161	Electrical Water Heater 50L	2.00	1	28-Oct-26	29-Oct-26	11-Nov-26	12-Nov-26	799.86
B8.31 23 16.0181	13A SINGLE SWITCH SOCKET OUTLET	2.00	1	28-Oct-26	29-Oct-26	11-Nov-26	12-Nov-26	2,296.86
B8.31 23 16.0163	DB-MGR Panel	2.00	1	31-Oct-26	01-Nov-26	14-Nov-26	15-Nov-26	4,716.62
B8.31 23 16.0183	13A DOUBLE SWITCH SOCKET OUTLET	2.00	1	31-Oct-26	01-Nov-26	14-Nov-26	15-Nov-26	8,788.78
B8.31 23 16.0165	Grounding and lightning system	2.00	1	02-Nov-26	03-Nov-26	16-Nov-26	17-Nov-26	62,590.88
B8.31 23 16.0167	Fire alarm system	2.00	1	04-Nov-26	05-Nov-26	18-Nov-26	19-Nov-26	64,569.17
Interior Finishes		15.00	8	22-Oct-26	08-Nov-26	09-Nov-26	25-Nov-26	33,922.95
B8.31 23 16.0195	Porcelain flooring tiles size (600x600)	3.00	1	22-Oct-26	25-Oct-26	09-Nov-26	11-Nov-26	1,133.72
B8.31 23 16.0197	Ceramic wall tile size (300x300) mm	3.00	1	26-Oct-26	28-Oct-26	12-Nov-26	15-Nov-26	1,860.79
B8.31 23 16.01117	Raised floor finish	3.00	1	26-Oct-26	28-Oct-26	12-Nov-26	15-Nov-26	11,373.43
B8.31 23 16.0185	Internal painting	3.00	1	02-Nov-26	04-Nov-26	16-Nov-26	18-Nov-26	5,458.33
B8.31 23 16.01107	Porcelain flooring tiles size (300x300)	3.00	1	29-Oct-26	01-Nov-26	16-Nov-26	18-Nov-26	367.66
B8.31 23 16.0199	Gypsum board ceiling, including paint	2.00	1	05-Nov-26	07-Nov-26	19-Nov-26	21-Nov-26	6,816.18
B8.31 23 16.01109	Porcelain flooring tiles size (500x500)	3.00	1	02-Nov-26	04-Nov-26	19-Nov-26	22-Nov-26	4,374.64
B8.31 23 16.01115	Porcelain skirting 100 mm height	3.00	1	05-Nov-26	08-Nov-26	23-Nov-26	25-Nov-26	2,538.21
Fixtures, Equipment & Final Connections		5.70	3	01-Nov-26	07-Nov-26	18-Nov-26	24-Nov-26	14,063.83
Install Sanitary wares		2.00	1	05-Nov-26	07-Nov-26	23-Nov-26	24-Nov-26	793.71
B8.31 23 16.01119	Toilet	2.00	1	05-Nov-26	07-Nov-26	23-Nov-26	24-Nov-26	793.71
Install Final Electrical & Tech Components		5.70	2	01-Nov-26	07-Nov-26	18-Nov-26	24-Nov-26	13,270.12
B8.31 23 16.01147	WALL MOUNTED BULK HEAD OUTDOOR LED 15 WATTS, IP65	2.00	1	01-Nov-26	02-Nov-26	18-Nov-26	21-Nov-26	3,187.14
B8.31 23 16.01131	Data Cabinet including all devices 12U	2.00	1	05-Nov-26	07-Nov-26	23-Nov-26	24-Nov-26	10,082.98
Potable Water Pump Station		20.20	95	16-Sep-26	07-Nov-26	04-Nov-26	28-Nov-26	7,908,783.83
Superstructure		2.50	2	16-Sep-26	21-Sep-26	04-Nov-26	07-Nov-26	109,495.62
B3.2.32 11 23.01.39_R	Roof Slab & Beams Construction (Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	91,430.53
B3.2.32 11 23.01.27_R	CMU (Concrete Masonry Unit) Walls Construction(Rem)	2.50	1	19-Sep-26	21-Sep-26	04-Nov-26	07-Nov-26	18,065.09
Building Envelope & Waterproofing		12.00	9	16-Sep-26	30-Sep-26	04-Nov-26	17-Nov-26	452,845.57
B3.2.32 11 23.01.21	Sloped Screed for Roof	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	30,741.49
B3.2.32 11 23.01.43	External Plastering	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	43,146.36
B3.2.32 11 23.01.49	Waterproofing Membrane for Roof	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	84,892.13
B3.2.32 11 23.01.29	Geotextile Membrane for Roof	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	7,258.70
B3.2.32 11 23.01.65	Water proofing with 50mm screed protection	2.00	1	21-Sep-26	22-Sep-26	09-Nov-26	10-Nov-26	138,849.40
B3.2.32 11 23.01.41	50mm Foam Concrete for Roof	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	30,737.17
B3.2.32 11 23.01.79	Stainless steel at top of tank size of 950x950mm	2.00	1	24-Sep-26	26-Sep-26	11-Nov-26	12-Nov-26	4,172.27

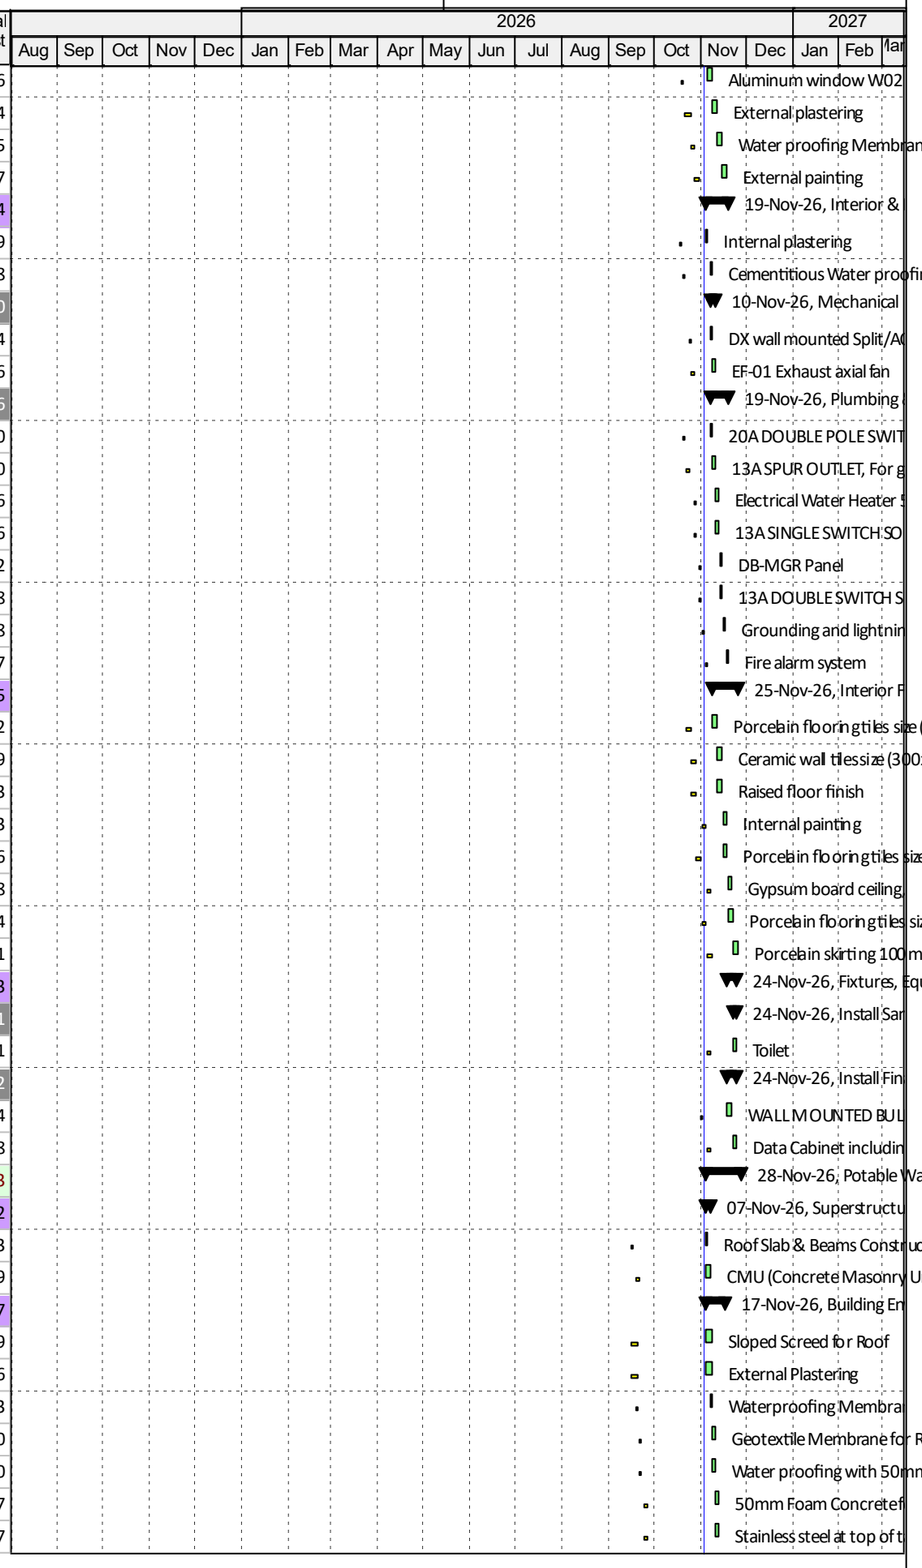

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.2.32 11 23.01.51	Gravel for Roof	2.00	1	27-Sep-26	28-Sep-26	14-Nov-26	15-Nov-26	72,661.71
B3.2.32 11 23.01.69	Stone Copping Installation	2.00	1	29-Sep-26	30-Sep-26	16-Nov-26	17-Nov-26	40,386.35
Interior Finishes & Fixed Installations		15.20	6	16-Sep-26	04-Nov-26	04-Nov-26	22-Nov-26	296,392.02
B3.2.32 11 23.01.31	Lean Concrete for Equipment Pads	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	438.12
B3.2.32 11 23.01.33	Stairs Construction	3.00	1	13-Oct-26	15-Oct-26	05-Nov-26	09-Nov-26	2,198.64
B3.2.32 11 23.01.45	Internal Plastering	3.00	1	17-Oct-26	19-Oct-26	09-Nov-26	12-Nov-26	37,934.87
B3.2.32 11 23.01.63	Water proofing Membrane with protection board	3.00	1	20-Oct-26	22-Oct-26	12-Nov-26	16-Nov-26	63,500.44
B3.2.32 11 23.01.71	Internal Painting (Acrylic/Emulsion)	2.00	1	03-Nov-26	04-Nov-26	19-Nov-26	22-Nov-26	38,106.28
B3.2.32 11 23.01.91	Epoxy Paint for Floors & Non-Toxic Epoxy for Tank	2.00	1	03-Nov-26	04-Nov-26	19-Nov-26	22-Nov-26	154,213.68
Mechanical & Piping Rough-In		19.00	48	24-Sep-26	07-Nov-26	05-Nov-26	28-Nov-26	5,875,299.88
B3.2.32 11 23.01.53	Overhead Crane Installation	2.00	1	01-Oct-26	03-Oct-26	07-Nov-26	09-Nov-26	98,511.60
B3.2.32 11 23.01.73	Surge Tank	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26	11-Nov-26	630,474.24
B3.2.32 11 23.01.93	Control Panel	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26	11-Nov-26	34,421.10
Major Equipment		8.00	12	04-Oct-26	29-Oct-26	09-Nov-26	18-Nov-26	4,721,751.92
Pumps		8.00	6	04-Oct-26	12-Oct-26	09-Nov-26	18-Nov-26	3,691,295.12
B3.2.32 11 23.01.81	Water Pump - Vertical multistage cintrifugal pump	2.00	1	04-Oct-26	05-Oct-26	09-Nov-26	11-Nov-26	522,141.80
B3.2.32 11 23.01.12	Submersible pump	3.00	1	05-Oct-26	07-Oct-26	10-Nov-26	14-Nov-26	308,283.36
B3.2.32 11 23.01.99	Fire Pump - split case cintrifugal pump	2.00	1	06-Oct-26	07-Oct-26	11-Nov-26	14-Nov-26	2,688,787.20
B3.2.32 11 23.01.11	Fire Pump - Vertical multistage cintrifugal (jockey) pump	2.00	1	06-Oct-26	07-Oct-26	11-Nov-26	14-Nov-26	160,805.70
B3.2.32 11 23.01.13	Manually Operated Fuel Pump	2.00	1	08-Oct-26	10-Oct-26	14-Nov-26	16-Nov-26	4,844.81
B3.2.32 11 23.01.14	Positive Displacement Rotary Type Pump	2.00	1	11-Oct-26	12-Oct-26	16-Nov-26	18-Nov-26	6,432.25
Chlorination System		8.00	6	20-Oct-26	29-Oct-26	09-Nov-26	18-Nov-26	1,030,456.81
B3.2.32 11 23.01.83	Chlorine Cylinder racks	2.00	1	20-Oct-26	21-Oct-26	09-Nov-26	11-Nov-26	38,245.78
B3.2.32 11 23.01.10	Chlorinators	2.00	1	22-Oct-26	24-Oct-26	11-Nov-26	14-Nov-26	580,640.45
B3.2.32 11 23.01.11	Discharge Line Analyzer	2.00	1	22-Oct-26	24-Oct-26	11-Nov-26	14-Nov-26	245,931.94
B3.2.32 11 23.01.12	Motive Water Pumps (Injection)	2.00	1	25-Oct-26	26-Oct-26	14-Nov-26	16-Nov-26	36,298.37
B3.2.32 11 23.01.12	Motive Water Pumps (Water)	2.00	1	25-Oct-26	26-Oct-26	14-Nov-26	16-Nov-26	56,093.80
B3.2.32 11 23.01.13	Control Panel	2.00	1	28-Oct-26	29-Oct-26	16-Nov-26	18-Nov-26	73,246.46
Internal Piping & Valves Installation		8.00	16	28-Oct-26	05-Nov-26	16-Nov-26	25-Nov-26	205,950.71
Pipes		8.00	7	28-Oct-26	05-Nov-26	16-Nov-26	25-Nov-26	44,448.75
Double Flanged DI Pipes		6.00	6	28-Oct-26	03-Nov-26	16-Nov-26	23-Nov-26	43,680.50
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?60 mm	2.00	1	28-Oct-26	29-Oct-26	16-Nov-26	18-Nov-26	4,302.20
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?80 mm	2.00	1	31-Oct-26	01-Nov-26	18-Nov-26	21-Nov-26	13,512.30
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?100 mm	2.00	1	31-Oct-26	01-Nov-26	18-Nov-26	21-Nov-26	5,153.90
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?200 mm	2.00	1	31-Oct-26	01-Nov-26	18-Nov-26	21-Nov-26	6,374.30
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?300 mm	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	9,192.70
B3.2.32 11 23.01.1	Double Flanged DI Pipe ?350 mm	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	5,145.10
PPR Pipes		2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	768.25
B3.2.32 11 23.01.1	PPR Pipes with ?25mm	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	768.25
Valves		8.00	8	28-Oct-26	05-Nov-26	16-Nov-26	25-Nov-26	142,437.07
Gate Valves		8.00	5	28-Oct-26	05-Nov-26	16-Nov-26	25-Nov-26	95,614.21
B3.2.32 11 23.01.1	Manually operated Gate Valve DN60	2.00	1	28-Oct-26	29-Oct-26	16-Nov-26	18-Nov-26	3,958.04
B3.2.32 11 23.01.1	Manually operated Gate Valve DN80	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	8,923.98
B3.2.32 11 23.01.1	Manually operated Gate Valve DN100	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	7,074.93
B3.2.32 11 23.01.1	Manually operated Gate Valve DN200	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	13,582.66
B3.2.32 11 23.01.1	Manually operated Gate Valve DN350	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	62,074.60

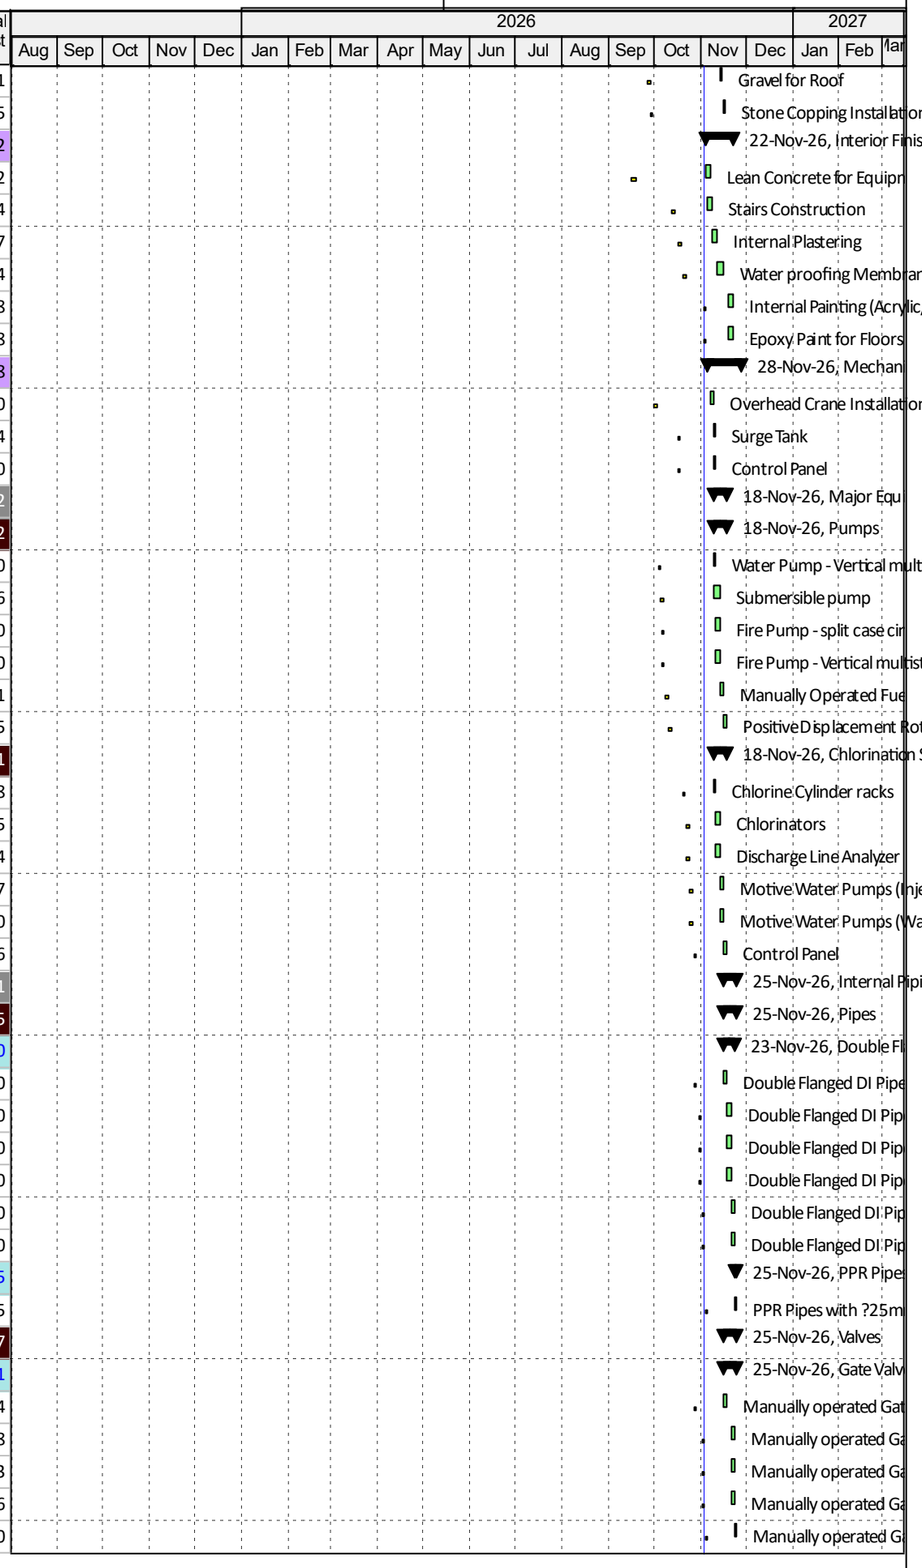

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Non Return Valves		6.00	2	31-Oct-26	05-Nov-26	18-Nov-26	25-Nov-26	38,791.80
B3.2.32 11 23.01.1	Non return Valve DN60	2.00	1	31-Oct-26	01-Nov-26	18-Nov-26	21-Nov-26	4,741.20
B3.2.32 11 23.01.1	Non return Valve DN300	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	34,050.60
Butterfly Valves		2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	8,031.06
B3.2.32 11 23.01.1	Butterfly Valve DN200	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	8,031.06
Flowmeters		2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	19,064.89
B3.2.32 11 23.01.17	Electromagnetic Flowmeter DN80, PN16	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	19,064.89
HVAC & Fire Suppression Fixture Installation		13.20	8	01-Oct-26	07-Nov-26	09-Nov-26	24-Nov-26	80,295.05
Fans		2.00	2	01-Oct-26	25-Oct-26	09-Nov-26	10-Nov-26	13,791.66
B3.2.32 11 23.01.55	Roof Mounted Fans	2.00	1	01-Oct-26	03-Oct-26	09-Nov-26	10-Nov-26	12,516.80
B3.2.32 11 23.01.85	Exhaust Axial Fan	2.00	1	24-Oct-26	25-Oct-26	09-Nov-26	10-Nov-26	1,274.86
AC Units		2.00	1	24-Oct-26	25-Oct-26	09-Nov-26	10-Nov-26	13,443.95
B3.2.32 11 23.01.10	DX wall mounted Split/AC	2.00	1	24-Oct-26	25-Oct-26	09-Nov-26	10-Nov-26	13,443.95
FM200 System		2.00	3	26-Oct-26	27-Oct-26	11-Nov-26	12-Nov-26	44,121.35
B3.2.32 11 23.01.11	FM200 system for Electrcal Room - First Fix	2.00	1	26-Oct-26	27-Oct-26	11-Nov-26	12-Nov-26	8,824.25
B3.2.32 11 23.01.1	FM200 system for Electrcal Room - Second Fix	2.00	1	26-Oct-26	27-Oct-26	11-Nov-26	12-Nov-26	1,323.64
B3.2.32 11 23.01.3	FM200 system for Electrcal Room - Final Fix	2.00	1	26-Oct-26	27-Oct-26	11-Nov-26	12-Nov-26	33,973.46
Fire Extinguishers		2.00	2	05-Nov-26	07-Nov-26	22-Nov-26	24-Nov-26	8,938.08
B3.2.32 11 23.01.27	CO2 fire extinguishers	2.00	1	05-Nov-26	07-Nov-26	22-Nov-26	24-Nov-26	5,649.96
B3.2.32 11 23.01.28	Powder fire extinguishers	2.00	1	05-Nov-26	07-Nov-26	22-Nov-26	24-Nov-26	3,288.12
External & Underground Piping		19.00	9	24-Sep-26	15-Oct-26	05-Nov-26	28-Nov-26	103,895.26
Buried Pipes		10.00	5	24-Sep-26	05-Oct-26	05-Nov-26	17-Nov-26	42,490.95
B3.2.32 11 23.01.13	Buried DI Pipe ?80 mm	2.00	1	24-Sep-26	26-Sep-26	05-Nov-26	08-Nov-26	5,689.50
B3.2.32 11 23.01.17	Buried DI Pipe ?100 mm	2.00	1	27-Sep-26	28-Sep-26	08-Nov-26	10-Nov-26	2,190.60
B3.2.32 11 23.01.23	Buried DI Pipe ?200 mm	2.00	1	29-Sep-26	30-Sep-26	10-Nov-26	12-Nov-26	8,455.20
B3.2.32 11 23.01.37	Buried DI Pipe ?300 mm	2.00	1	01-Oct-26	03-Oct-26	12-Nov-26	15-Nov-26	12,590.55
B3.2.32 11 23.01.57	Buried DI Pipe ?350 mm	2.00	1	04-Oct-26	05-Oct-26	15-Nov-26	17-Nov-26	13,565.10
uPVC		2.00	1	06-Oct-26	07-Oct-26	17-Nov-26	19-Nov-26	8,034.02
B3.2.32 11 23.01.87	uPVC Pipes ?110mm	2.00	1	06-Oct-26	07-Oct-26	17-Nov-26	19-Nov-26	8,034.02
Drains		7.00	3	08-Oct-26	15-Oct-26	19-Nov-26	28-Nov-26	53,370.29
B3.2.32 11 23.01.10	Trench drain	2.00	1	08-Oct-26	10-Oct-26	19-Nov-26	22-Nov-26	33,378.14
B3.2.32 11 23.01.11	Scupper ?110mm	2.00	1	11-Oct-26	12-Oct-26	22-Nov-26	24-Nov-26	15,646.04
B3.2.32 11 23.01.12	Manholes	3.00	1	13-Oct-26	15-Oct-26	24-Nov-26	28-Nov-26	4,346.11
Electrical & Control Systems		18.40	16	16-Sep-26	05-Nov-26	04-Nov-26	25-Nov-26	942,144.26
Primary Power Installation		9.00	4	16-Sep-26	11-Oct-26	04-Nov-26	14-Nov-26	638,234.04
Generator		5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	379,675.30
B3.2.32 11 23.01.35	Standby Diesel Generator	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	379,675.30
Fuel Tank		2.00	1	22-Sep-26	24-Sep-26	10-Nov-26	11-Nov-26	13,229.73
B3.2.32 11 23.01.47	Underground Fuel Tank	2.00	1	22-Sep-26	24-Sep-26	10-Nov-26	11-Nov-26	13,229.73
ATS		2.00	1	10-Oct-26	11-Oct-26	12-Nov-26	14-Nov-26	87,617.38
B3.2.32 11 23.01.67	Automatic Transfer Switch ATS	2.00	1	10-Oct-26	11-Oct-26	12-Nov-26	14-Nov-26	87,617.38
Motor Control Center (MCC)		2.00	1	10-Oct-26	11-Oct-26	12-Nov-26	14-Nov-26	157,711.63
B3.2.32 11 23.01.89	MCC Installation	2.00	1	10-Oct-26	11-Oct-26	12-Nov-26	14-Nov-26	157,711.63
Hand Holes		6.00	2	19-Sep-26	26-Sep-26	07-Nov-26	12-Nov-26	62,815.79
B3.2. 26 05 43 .02	Hand Hole (EHH-2) 400mm x 400mm x 600mm	3.00	1	19-Sep-26	21-Sep-26	07-Nov-26	09-Nov-26	29,205.85
B3.2. 26 05 43 .01	Hand Hole (EHH-1) 600mm x 600mm x 800mm	3.00	1	22-Sep-26	26-Sep-26	10-Nov-26	12-Nov-26	33,609.94




© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Cable Tray, Conduit Installation & Power Cable Pulling		6.00	3	31-Oct-26	05-Nov-26	18-Nov-26	25-Nov-26	109,662.20
B3.2.32 11 23.01.145	4x1Cx 630mm2 Cu/XLPE//PVC	2.00	1	31-Oct-26	01-Nov-26	18-Nov-26	21-Nov-26	102,989.40
B3.2.32 11 23.01.153	4Cx 10mm2 Cu/XLPE/SWA/PVC	2.00	1	02-Nov-26	03-Nov-26	21-Nov-26	23-Nov-26	878.00
B3.2.32 11 23.01.159	4/Cx35mm²+1Cx16mm²	2.00	1	04-Nov-26	05-Nov-26	23-Nov-26	25-Nov-26	5,794.80
Enclosed Switches and Circuit Breakers		5.00	3	17-Oct-26	21-Oct-26	09-Nov-26	15-Nov-26	19,565.37
B3.2. 26 28 16 .02	40A, 3P, 60Hz Isolator/disconnect switches IP65	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26	11-Nov-26	2,820.13
B3.2. 26 28 16 .03	20A, 1P, 60Hz Isolator/disconnect switches IP65	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26	11-Nov-26	3,387.31
B3.2. 26 28 16 .01	630A, 3P, 60Hz Isolator/disconnect switches IP65	2.00	1	20-Oct-26	21-Oct-26	12-Nov-26	15-Nov-26	13,357.93
Panelboards		6.00	3	27-Oct-26	02-Nov-26	12-Nov-26	19-Nov-26	22,448.70
B3.2. 26 24 16 .01	DB-PW Panel: 100 Ampere, 3P, IP66,60Hz	2.00	1	27-Oct-26	28-Oct-26	12-Nov-26	15-Nov-26	6,258.38
B3.2. 26 24 16 .02	DB-CL Panel: 100 Ampere, 3P, IP66,60Hz	2.00	1	29-Oct-26	31-Oct-26	15-Nov-26	17-Nov-26	6,026.59
B3.2. 26 24 16 .03	ELP Panel: phtocell , timer,40 Ampere, 3P, IP66,60Hz	2.00	1	01-Nov-26	02-Nov-26	17-Nov-26	19-Nov-26	10,163.73
Lighting		2.00	1	20-Oct-26	21-Oct-26	12-Nov-26	15-Nov-26	89,418.15
Fixtures (LEDs)		2.00	1	20-Oct-26	21-Oct-26	12-Nov-26	15-Nov-26	89,418.15
B3.2.32 11 23.01.29	Install addressable fire alarm system including smoke detector	2.00	1	20-Oct-26	21-Oct-26	12-Nov-26	15-Nov-26	89,418.15
Final Fixtures		14.00	14	11-Oct-26	26-Oct-26	09-Nov-26	24-Nov-26	232,606.48
Door & Louver Installation		9.00	7	17-Oct-26	26-Oct-26	09-Nov-26	19-Nov-26	186,670.26
B3.2.32 11 23.01.59	Steel Door SD1 For chlorination size (2000x2300)mm	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26		25,590.25
B3.2.32 11 23.01.75	Steel Door SD1 size(2000x2550)mm	2.00	1	19-Oct-26	20-Oct-26	11-Nov-26	14-Nov-26	27,815.04
B3.2.32 11 23.01.95	Steel Door SD2 size(900x2200)mm	2.00	1	20-Oct-26	21-Oct-26	12-Nov-26	15-Nov-26	12,864.49
B3.2.32 11 23.01.107	90 mins fire rated Steel Door SD3 size (1000x2200)mm	2.00	1	22-Oct-26	24-Oct-26	15-Nov-26	17-Nov-26	8,112.74
B3.2.32 11 23.01.119	Sand trap louver 1500 mm x 1500mm	2.00	1	22-Oct-26	24-Oct-26	15-Nov-26	17-Nov-26	44,160.03
B3.2.32 11 23.01.131	Louver 3400mm x 2800mm	2.00	1	25-Oct-26	26-Oct-26	17-Nov-26	19-Nov-26	38,087.74
B3.2.32 11 23.01.143	Steel shutter Door SD4 size (3200x3000)mm	2.00	1	25-Oct-26	26-Oct-26	17-Nov-26	19-Nov-26	30,039.97
Ladders		10.00	5	11-Oct-26	21-Oct-26	09-Nov-26	19-Nov-26	31,813.54
B3.2.32 11 23.01.61	5m External Galvanized Steel Ladder	2.00	1	11-Oct-26	12-Oct-26	09-Nov-26	10-Nov-26	5,215.33
B3.2.32 11 23.01.77	3m External Galvanized Steel Ladder	2.00	1	13-Oct-26	14-Oct-26	11-Nov-26	12-Nov-26	3,129.20
B3.2.32 11 23.01.97	4.3m External Galvanized Steel Ladder - Potable Water Tank	2.00	1	15-Oct-26	17-Oct-26	14-Nov-26	15-Nov-26	9,387.60
B3.2.32 11 23.01.109	4.5m External Stainless Steel A36 Ladder	2.00	1	18-Oct-26	19-Oct-26	16-Nov-26	17-Nov-26	9,387.60
B3.2.32 11 23.01.121	4.3m External Galvanized Steel Ladder - Chlorination	2.00	1	20-Oct-26	21-Oct-26	18-Nov-26	19-Nov-26	4,693.80
Handrails		2.00	1	22-Oct-26	24-Oct-26	21-Nov-26	22-Nov-26	12,094.48
B3.2.32 11 23.01.133	Handrail with approximate height 1.1m	2.00	1	22-Oct-26	24-Oct-26	21-Nov-26	22-Nov-26	12,094.48
Signage		2.00	1	25-Oct-26	26-Oct-26	23-Nov-26	24-Nov-26	2,028.21
B3.2.32 11 23.01.141	Aluminum exterior signage size (300x150)mm	2.00	1	25-Oct-26	26-Oct-26	23-Nov-26	24-Nov-26	2,028.21
Zone 03		185.89	434	21-May-26	23-Nov-26	21-May-26 A	06-Dec-26	10,416,302.78
Road 02		64.00	104	16-Sep-26	15-Nov-26	19-Sep-26 A	30-Nov-26	3,343,925.43
Wet Networks		61.00	61	16-Sep-26	11-Nov-26	22-Sep-26 A	26-Nov-26	1,334,774.90
Sewerage Network		3.52	3	16-Sep-26	20-Sep-26	22-Sep-26 A	07-Nov-26	30,390.15
Manholes ?1200		3.52	3	16-Sep-26	20-Sep-26	22-Sep-26 A	07-Nov-26	30,390.15
Depth From 4.5m to 5.5m		2.56	1	16-Sep-26	19-Sep-26	22-Sep-26 A	05-Nov-26	17,622.83
B6.33 05 39.01.607	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	22-Sep-26 A	05-Nov-26	17,622.83
Depth From 5.5m to 6.5m		3.52	2	16-Sep-26	20-Sep-26	28-Sep-26 A	07-Nov-26	12,767.32
B6.33 05 39.01.657	Test, Internal Finishing, Benching & Cover(Rem)	3.04	1	16-Sep-26	20-Sep-26	28-Sep-26 A	05-Nov-26	9,635.68
Depth From 5.5m to 6.5m Backdrop		3.52	1	16-Sep-26	20-Sep-26	30-Sep-26 A	07-Nov-26	3,131.64
B6.33 05 39.01.70	Test, Internal Finishing, Benching & Cover(Rem)	3.52	1	16-Sep-26	20-Sep-26	30-Sep-26 A	07-Nov-26	3,131.64
Stormwater Network		6.00	2	16-Sep-26	22-Sep-26	06-Oct-26 A	08-Nov-26	15,900.45

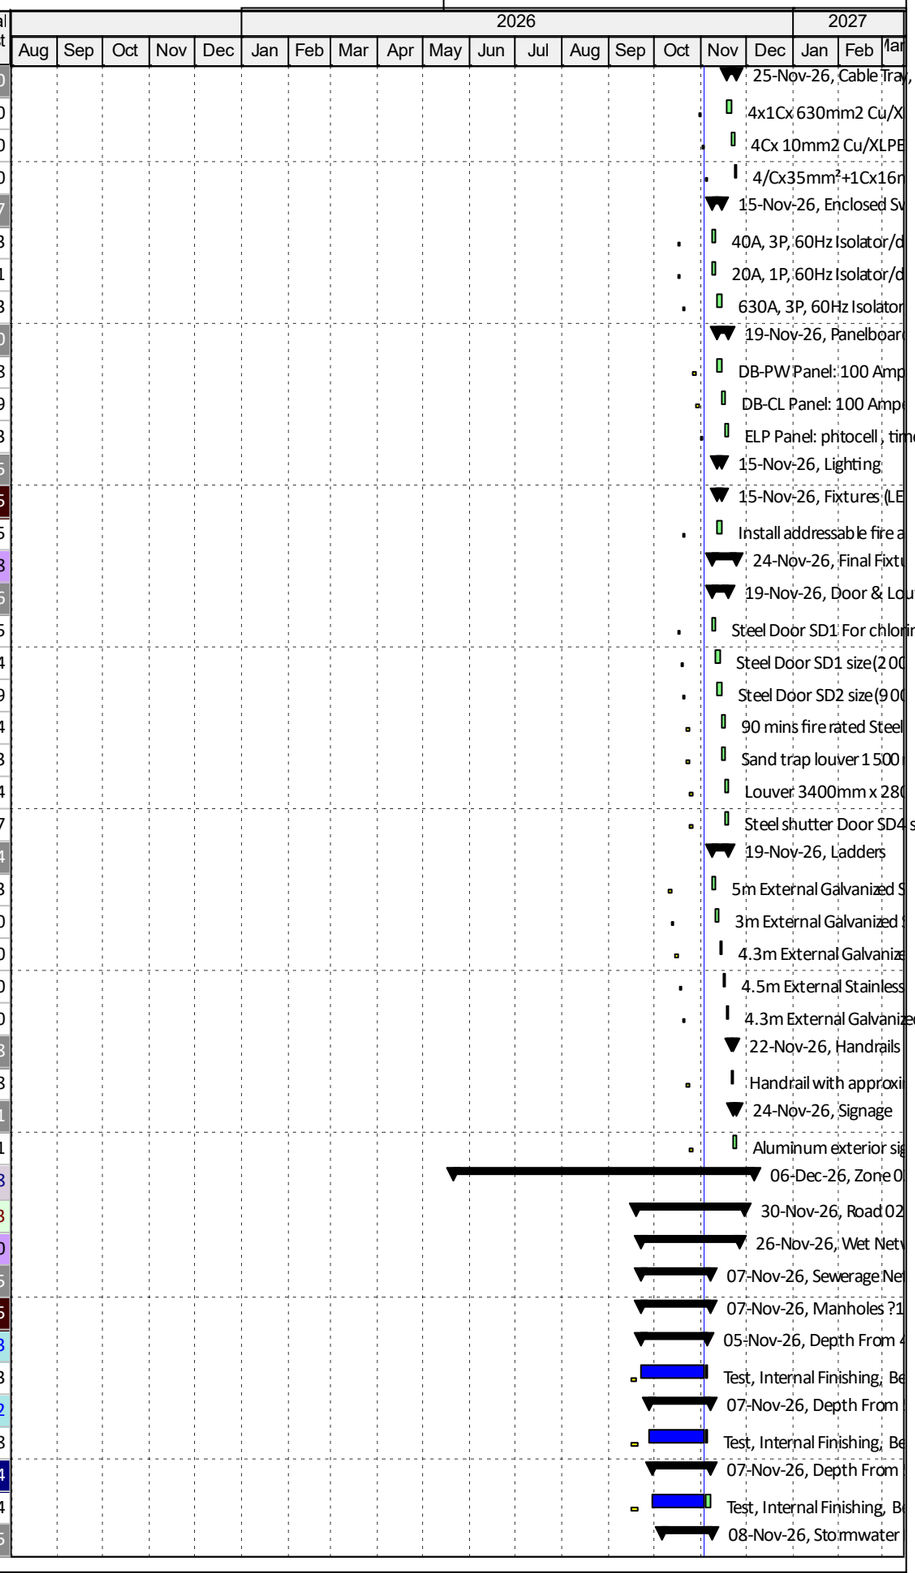

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Catch Basins		6.00	2	16-Sep-26	22-Sep-26	06-Oct-26 A	08-Nov-26	15,900.45
Single		2.00	1	16-Sep-26	17-Sep-26	06-Oct-26 A	05-Nov-26	5,384.35
B6.33 05 40.01.40(	Backfilling, DI Frame & Grate Cover Fixing(Rem)	2.00	1	16-Sep-26	17-Sep-26	06-Oct-26 A	05-Nov-26	5,384.35
Double		6.00	1	16-Sep-26	22-Sep-26	18-Oct-26 A	08-Nov-26	10,516.10
B6.33 05 40.01.880	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	16-Sep-26	22-Sep-26	18-Oct-26 A	08-Nov-26	10,516.10
Potable Water Network		10.00	2	20-Sep-26	01-Oct-26	04-Nov-26	15-Nov-26	1,074.67
Plots and Buildings Crossing		10.00	2	20-Sep-26	01-Oct-26	04-Nov-26	15-Nov-26	1,074.67
B3.33 14 13.02.23	Sand Bedding	3.00	1	20-Sep-26	22-Sep-26	04-Nov-26	07-Nov-26	268.67
B3.33 14 13.02.24	Tee, Pipe (Crossing) Installation & Backfilling	7.00	1	24-Sep-26	01-Oct-26	08-Nov-26	15-Nov-26	806.01
Fire Fighting Network		20.00	12	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	143,100.19
Valves & Chambers		20.00	9	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	61,023.76
Gate Valves		4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	5,017.11
Gate valves dia (250) mm		4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	5,017.11
B3.33 14 19.01.12	Spindle & Surface Box	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	5,017.11
Air Valves		20.00	4	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	20,932.79
Air valves on less than 315 mm. (In Chamber)		20.00	4	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	20,932.79
B3.33 05 63.02.57	Land Adjustment & Compaction	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	4,485.60
B3.33 05 63.02.55	Foundations	5.00	1	21-Sep-26	27-Sep-26	09-Nov-26	14-Nov-26	5,821.24
B3.33 05 63.02.58	Chambers Walls Conc Cast In Situ	5.00	1	28-Sep-26	03-Oct-26	15-Nov-26	19-Nov-26	5,980.60
B3.33 05 63.02.56	Chamber Curing, Finishing & Steel Cover	6.00	1	04-Oct-26	10-Oct-26	21-Nov-26	26-Nov-26	4,645.16
Washout Valves		20.00	4	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	35,073.86
Washout valves on 110-400 mm. (In Chamber)		20.00	4	16-Sep-26	10-Oct-26	04-Nov-26	26-Nov-26	35,073.86
B3.33 05 63.01.52	Land Adjustment & Compaction	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,932.00
B3.33 05 63.01.50	Foundations	5.00	1	21-Sep-26	27-Sep-26	09-Nov-26	14-Nov-26	9,649.37
B3.33 05 63.01.53	Chambers Walls Conc Cast In Situ	5.00	1	28-Sep-26	03-Oct-26	15-Nov-26	19-Nov-26	9,870.62
B3.33 05 63.01.51	Chamber Curing, Finishing & Steel Cover	6.00	1	04-Oct-26	10-Oct-26	21-Nov-26	26-Nov-26	7,621.88
Fire Hydrant		14.00	3	16-Sep-26	03-Oct-26	04-Nov-26	19-Nov-26	82,076.43
B3.33 14 19.01.fh32	Riser Pipe & Flanged Fittings Installation	4.00	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	16,415.29
B3.33 14 19.01.fh31	Firehydrant Fixing/Installation	5.00	1	21-Sep-26	27-Sep-26	09-Nov-26	14-Nov-26	49,245.86
B3.33 14 19.01.fh33	Backfilling & Compaction	5.00	1	28-Sep-26	03-Oct-26	15-Nov-26	19-Nov-26	16,415.29
TSE Network		18.00	42	16-Sep-26	11-Nov-26	04-Nov-26	24-Nov-26	1,144,309.43
HDPE Pipes		6.00	24	16-Sep-26	26-Sep-26	04-Nov-26	10-Nov-26	1,085,276.92
?110mm		5.06	2	16-Sep-26	26-Sep-26	04-Nov-26	10-Nov-26	14,619.70
Depth: 0.0m - 1.5m		5.06	2	16-Sep-26	26-Sep-26	04-Nov-26	10-Nov-26	14,619.70
B4.33 14 13.01-01	Embedment & Test(Rem)	4.25	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,746.47
B4.33 14 13.01-01	Backfilling & Warning Tape(Rem)	5.06	1	19-Sep-26	26-Sep-26	04-Nov-26	10-Nov-26	4,873.23
?25mm		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	532,517.68
Depth: 0.0m - 1.5m		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	532,517.68
B4.33 14 13.01-20	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	33,282.39
B4.33 14 13.01-21	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	299,541.54
B4.33 14 13.01-22	Embedment & Test(Rem)	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	133,129.57
B4.33 14 13.01-23	Backfilling & Warning Tape(Rem)	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	66,564.17
?32mm		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	171,251.70
Depth: 0.0m - 1.5m		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	171,251.70
B4.33 14 13.01-25	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	10,703.23
B4.33 14 13.01-26	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	96,329.08

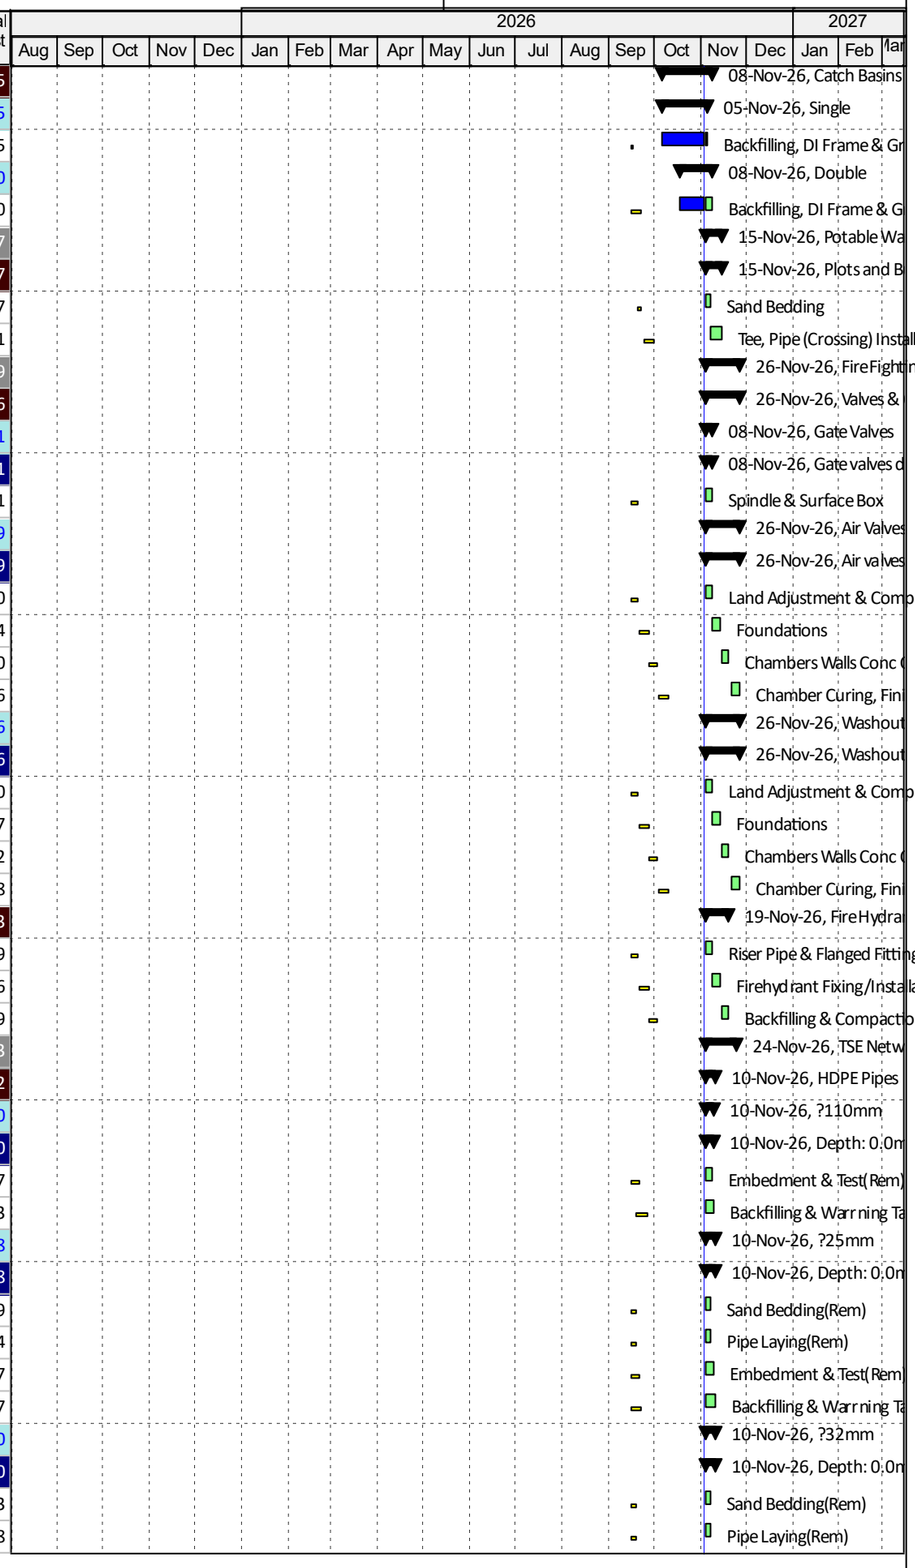

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B4.33 14 13.01-27	Embedment & Test(Rem)	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	42,812.92
B4.33 14 13.01-28	Backfilling & Warrning Tape(Rem)	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	21,406.46
?50mm		6.00	5	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	329,957.79
Depth: 0.0m - 1.5m		6.00	5	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	329,957.79
B4.33 14 13.01-29	Excavation(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	65,991.56
B4.33 14 13.01-30	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	16,497.89
B4.33 14 13.01-31	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	148,481.00
B4.33 14 13.01-32	Embedment & Test(Rem)	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	65,991.56
B4.33 14 13.01-33	Backfilling & Warrning Tape(Rem)	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	32,995.78
?63mm		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	26,031.55
Depth: 0.0m - 1.5m		6.00	4	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	26,031.55
B4.33 14 13.01-35	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	1,626.97
DMM2-Eng-PQ-05	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	14,642.75
B4.33 14 13.01-37	Embedment & Test(Rem)	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	6,507.89
B4.33 14 13.01-38	Backfilling & Warrning Tape(Rem)	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	3,253.94
?75mm		6.00	5	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	10,898.50
Depth: 0.0m - 1.5m		6.00	5	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	10,898.50
B4.33 14 13.01-39	Excavation(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	2,179.70
B4.33 14 13.01-40	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	544.93
B4.33 14 13.01-41	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	4,904.33
B4.33 14 13.01-42	Embedment & Test(Rem)	5.00	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	2,179.70
B4.33 14 13.01-43	Backfilling & Warrning Tape(Rem)	6.00	1	16-Sep-26	22-Sep-26	04-Nov-26	10-Nov-26	1,089.85
Valves & Chambers		18.00	18	16-Sep-26	11-Nov-26	04-Nov-26	24-Nov-26	59,032.52
Gate Valves		5.00	2	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	12,052.11
Gate valves dia (250) mm		5.00	2	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	12,052.11
B3.33 14 19.01.13	Burried Isolation Valve Installation(Rem)	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	6,486.76
B3.33 14 19.01.13	Spindle & Surface Box	3.00	1	19-Sep-26	21-Sep-26	07-Nov-26	09-Nov-26	5,565.35
Air Valves		14.00	4	27-Oct-26	11-Nov-26	05-Nov-26	22-Nov-26	1,462.08
Air valves on less than 315 mm. (In Chamber)		14.00	4	27-Oct-26	11-Nov-26	05-Nov-26	22-Nov-26	1,462.08
B3.33 05 63.02.92	Land Adjustment & Compaction	3.00	1	27-Oct-26	29-Oct-26	05-Nov-26	09-Nov-26	395.16
B3.33 05 63.02.90	Foundations	4.00	1	31-Oct-26	03-Nov-26	09-Nov-26	14-Nov-26	276.61
B3.33 05 63.02.93	Chambers Walls Conc Cast In Situ	4.00	1	04-Nov-26	08-Nov-26	14-Nov-26	18-Nov-26	276.61
B3.33 05 63.02.91	Chamber Curing, Finishing & Steel Cover	3.00	1	09-Nov-26	11-Nov-26	18-Nov-26	22-Nov-26	513.71
Solenoid valves		15.00	12	20-Sep-26	07-Oct-26	08-Nov-26	24-Nov-26	45,518.32
1 Solenoid valve ?1.0 inch with box		9.00	4	20-Sep-26	30-Sep-26	08-Nov-26	17-Nov-26	12,310.76
B4.32 84 13.23	Solenoid Valve Box Installation	3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	2,838.80
B4.32 84 13.065	Pull Box Installation	7.00	1	20-Sep-26	28-Sep-26	08-Nov-26	15-Nov-26	1,848.31
B4.32 84 13.22	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	24-Sep-26	27-Sep-26	11-Nov-26	14-Nov-26	4,917.51
B4.32 84 13.24	Bubblers Installation	3.00	1	28-Sep-26	30-Sep-26	15-Nov-26	17-Nov-26	2,706.13
1 Solenoid valve ?1.5 inch with box		9.00	4	24-Sep-26	04-Oct-26	11-Nov-26	21-Nov-26	17,906.00
B4.32 84 13.26	Solenoid Valve Box Installation	3.00	1	24-Sep-26	27-Sep-26	11-Nov-26	14-Nov-26	8,434.05
B4.32 84 13.25	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	28-Sep-26	30-Sep-26	15-Nov-26	17-Nov-26	4,917.51
B4.32 84 13.064	Pull Box Installation	3.00	1	29-Sep-26	01-Oct-26	16-Nov-26	18-Nov-26	1,848.31
B4.32 84 13.27	Bubblers Installation	3.00	1	01-Oct-26	04-Oct-26	18-Nov-26	21-Nov-26	2,706.13
1 Solenoid valve ?2.0 inch with box		9.00	4	28-Sep-26	07-Oct-26	15-Nov-26	24-Nov-26	15,301.56
B4.32 84 13.20	Solenoid Valve Box Installation	3.00	1	28-Sep-26	30-Sep-26	15-Nov-26	17-Nov-26	5,829.60




Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B4.32 84 13.19	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	01-Oct-26	04-Oct-26	18-Nov-26	21-Nov-26	4,917.51
B4.32 84 13.063	Pull Box Installation	3.00	1	03-Oct-26	05-Oct-26	19-Nov-26	22-Nov-26	1,848.31
B4.32 84 13.21	Bubblers Installation	3.00	1	05-Oct-26	07-Oct-26	22-Nov-26	24-Nov-26	2,706.13
Dry Networks		35.00	26	24-Sep-26	15-Nov-26	04-Oct-26 A	30-Nov-26	612,174.54
Medium Voltage Network		35.00	8	24-Sep-26	09-Nov-26	04-Oct-26 A	30-Nov-26	316,570.01
Cables		32.28	3	24-Sep-26	09-Nov-26	04-Oct-26 A	28-Nov-26	244,997.79
3C,500mm2		32.28	3	24-Sep-26	09-Nov-26	04-Oct-26 A	28-Nov-26	244,997.79
B2.33 71 49.23.77	Cable 13.8 kV Unarmored	4.00	1	24-Sep-26	28-Sep-26	04-Oct-26 A	04-Nov-26	234,058.34
B2.33 71 49.23.78	Straight joints cables	3.00	1	29-Sep-26	01-Oct-26	05-Nov-26	08-Nov-26	7,880.95
B2.33 71 49.23.79	Cable Termination	3.00	1	07-Nov-26	09-Nov-26	24-Nov-26	28-Nov-26	3,058.50
RMU		17.00	3	27-Sep-26	18-Oct-26	11-Nov-26	30-Nov-26	33,476.81
B2 33 73 00.02.81	Land Adjustment	3.00	1	27-Sep-26	29-Sep-26	11-Nov-26	14-Nov-26	8,183.22
B2 33 73 00.02.83	Foundation Works & Curing	7.00	1	30-Sep-26	07-Oct-26	15-Nov-26	22-Nov-26	8,183.22
B2 33 73 00.02.85	Installation of Ring Main Unit RMU, 13.8KV	7.00	1	11-Oct-26	18-Oct-26	23-Nov-26	30-Nov-26	17,110.37
Units Substation		14.00	2	30-Sep-26	15-Oct-26	15-Nov-26	30-Nov-26	38,095.41
B2 33 73 00.01.81	Land Adjustment	3.00	1	30-Sep-26	03-Oct-26	15-Nov-26	17-Nov-26	19,047.71
B2 33 73 00.01.83	Foundation Works & Curing	7.00	1	08-Oct-26	15-Oct-26	23-Nov-26	30-Nov-26	19,047.71
Low Voltage Network		19.00	5	29-Sep-26	11-Oct-26	04-Nov-26	25-Nov-26	133,982.14
Duct Banks		4.00	1	05-Oct-26	07-Oct-26	04-Nov-26	08-Nov-26	2,844.71
6 Way		4.00	1	05-Oct-26	07-Oct-26	04-Nov-26	08-Nov-26	2,844.71
B2.33 71 00 02 111	Backfilling & Warning Tape	4.00	1	05-Oct-26	07-Oct-26	04-Nov-26	08-Nov-26	2,844.71
Cables		2.00	1	29-Sep-26	30-Sep-26	05-Nov-26	07-Nov-26	95,723.28
4C,10+1C,10mm2		2.00	1	29-Sep-26	30-Sep-26	05-Nov-26	07-Nov-26	95,723.28
B2.33 71 00 01 11	Cable Pulling	2.00	1	29-Sep-26	30-Sep-26	05-Nov-26	07-Nov-26	95,723.28
0.6/1 KV Low Voltage Distribution Panels		2.00	1	04-Oct-26	05-Oct-26	18-Nov-26	19-Nov-26	19,047.71
B2.33 71 26 24	Land Adjustment	2.00	1	04-Oct-26	05-Oct-26	18-Nov-26	19-Nov-26	19,047.71
0.6/1 KV Low Voltage Distribution Pillars		5.00	2	06-Oct-26	11-Oct-26	21-Nov-26	25-Nov-26	16,366.44
B2.33 71 26 27	Land Adjustment	2.00	1	06-Oct-26	07-Oct-26	21-Nov-26	22-Nov-26	8,183.22
B2.33 71 26 28	Foundation Works & Curing	3.00	1	08-Oct-26	11-Oct-26	23-Nov-26	25-Nov-26	8,183.22
Street Lighting		19.00	5	08-Oct-26	15-Nov-26	20-Oct-26 A	25-Nov-26	89,344.20
Cables		3.00	1	08-Oct-26	11-Oct-26	23-Nov-26	25-Nov-26	25,963.96
4C,10+1C,10mm2		3.00	1	08-Oct-26	11-Oct-26	23-Nov-26	25-Nov-26	25,963.96
B2.33 71 19 122	Land Adjustment	3.00	1	08-Oct-26	11-Oct-26	23-Nov-26	25-Nov-26	25,963.96
SL Poles		3.00	1	01-Nov-26	03-Nov-26	20-Oct-26 A	04-Nov-26	58,898.50
Pole (10 M Single Arm)		3.00	1	01-Nov-26	03-Nov-26	20-Oct-26 A	04-Nov-26	58,898.50
B2.33 71 16.70	Backfilling, Grouting & Chamfering	3.00	1	01-Nov-26	03-Nov-26	20-Oct-26 A	04-Nov-26	58,898.50
Earthing		8.00	3	05-Nov-26	15-Nov-26	04-Nov-26	12-Nov-26	4,481.74
B2.33 71 19 35	Land Adjustment	3.00	1	05-Nov-26	09-Nov-26	04-Nov-26	07-Nov-26	904.39
B2.33 71 19 36	Earth Rods& Conduits	3.00	1	09-Nov-26	12-Nov-26	08-Nov-26	10-Nov-26	2,672.96
B2.33 71 19 37	Backfilling	2.00	1	12-Nov-26	15-Nov-26	11-Nov-26	12-Nov-26	904.39
Telecommunication Network		11.00	8	03-Oct-26	04-Nov-26	07-Oct-26 A	05-Nov-26	72,278.19
Manholes		7.00	3	03-Oct-26	10-Oct-26	07-Oct-26 A	05-Nov-26	43,831.98
Manhole Type 1		7.00	3	03-Oct-26	10-Oct-26	07-Oct-26 A	05-Nov-26	43,831.98
B2.31 23 00.620	Excavation	2.00	1	03-Oct-26	04-Oct-26	07-Oct-26 A	04-Nov-26	8,766.40
B2.33 71 00.248	Manhole Installation	2.00	1	05-Oct-26	06-Oct-26	15-Oct-26 A	04-Nov-26	26,299.19
B2.33 71 00.249	Backfilling & Warning Tape	3.00	1	07-Oct-26	10-Oct-26	22-Oct-26 A	05-Nov-26	8,766.40

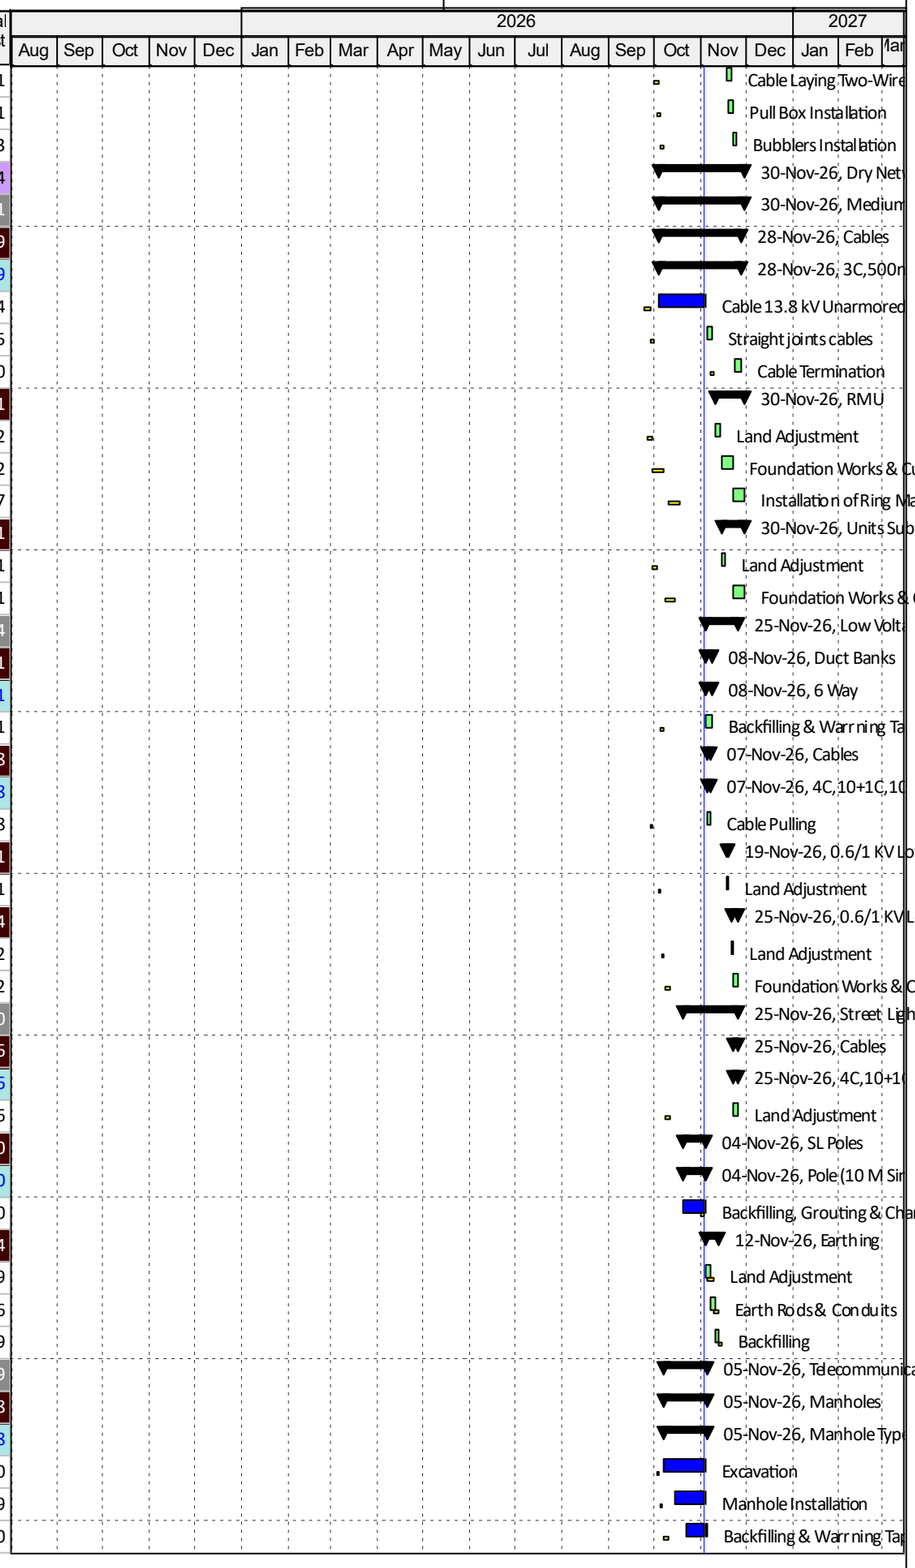


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Road Crossing Ducts		11.00	5	03-Oct-26	04-Nov-26	10-Oct-26 A	05-Nov-26	28,446.21
Size (6X50mm+4X32mm) HDPE		6.00	2	03-Oct-26	08-Oct-26	11-Oct-26 A	05-Nov-26	25,710.79
B2.33 71 00.246	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	03-Oct-26	05-Oct-26	11-Oct-26 A	05-Nov-26	19,283.10
B2.33 71 00.247	Backfilling & Warning Tape	3.00	1	06-Oct-26	08-Oct-26	21-Oct-26 A	05-Nov-26	6,427.70
Size (2*32mm) HDPE		9.00	3	05-Oct-26	04-Nov-26	10-Oct-26 A	05-Nov-26	2,735.42
B2.31 23 00.621	Excavation	2.00	1	05-Oct-26	06-Oct-26	10-Oct-26 A	04-Nov-26	547.76
B2.33 71 00.250	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	07-Oct-26	10-Oct-26	17-Oct-26 A	05-Nov-26	1,639.89
B2.33 71 00.251	Backfilling & Warning Tape	3.00	1	01-Nov-26	04-Nov-26	26-Oct-26 A	05-Nov-26	547.76
Earth & Road Works		59.50	15	04-Oct-26	12-Nov-26	19-Sep-26 A	25-Nov-26	1,345,489.10
Earth Layers		37.80	2	04-Oct-26	12-Oct-26	19-Sep-26 A	04-Nov-26	55,422.74
B1.2.32 11 13.01.10_	Subgrade(Rem)	2.10	1	04-Oct-26	08-Oct-26	19-Sep-26 A	04-Nov-26	17,220.10
B1.2.32 11 23.01.10_	Aggregate Base Course(Rem)	2.80	1	07-Oct-26	12-Oct-26	22-Oct-26 A	04-Nov-26	38,202.64
Interlock		3.00	1	07-Oct-26	10-Oct-26	08-Nov-26	11-Nov-26	26,174.66
B1.2.32 14 13.13.10	60mm thick - Interlocking Block Pavers	3.00	1	07-Oct-26	10-Oct-26	08-Nov-26	11-Nov-26	26,174.66
Curbstone		12.00	6	11-Oct-26	26-Oct-26	11-Nov-26	25-Nov-26	302,623.02
Pre-Installation		6.00	3	11-Oct-26	19-Oct-26	11-Nov-26	18-Nov-26	188,723.70
B2.31 23 00.271	Excavation	2.00	1	11-Oct-26	14-Oct-26	11-Nov-26	14-Nov-26	62,908.13
B1.2.32 14 13.13.21	PCC	2.00	1	15-Oct-26	17-Oct-26	14-Nov-26	16-Nov-26	62,907.44
32 16 13.0010	Haunching	2.00	1	18-Oct-26	19-Oct-26	16-Nov-26	18-Nov-26	62,908.13
Installation		6.00	3	20-Oct-26	26-Oct-26	18-Nov-26	25-Nov-26	113,899.33
B1.2.32 16.13.01.10	Curb Stone, Type K1	2.00	1	20-Oct-26	21-Oct-26	18-Nov-26	21-Nov-26	14,351.09
B1.2.32 16.13.02.9	Dropped Curb, Type K3	2.00	1	22-Oct-26	24-Oct-26	21-Nov-26	23-Nov-26	1,875.53
B1.2.32 16.13.03.10	Edge Curb, Type K4	2.00	1	25-Oct-26	26-Oct-26	23-Nov-26	25-Nov-26	97,672.71
Asphalt Layers		2.00	1	13-Oct-26	18-Oct-26	24-Oct-26 A	05-Nov-26	119,996.49
B1.2.32 11 26.01.10_	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	13-Oct-26	18-Oct-26	24-Oct-26 A	05-Nov-26	119,996.49
Traffic Signs		4.00	2	15-Oct-26	21-Oct-26	14-Nov-26	18-Nov-26	1,272.17
Pre-Installation		4.00	2	15-Oct-26	21-Oct-26	14-Nov-26	18-Nov-26	1,272.17
B2.31 23 00.281	Excavation	2.00	1	15-Oct-26	17-Oct-26	14-Nov-26	16-Nov-26	636.09
10 14 53.010	Foundation	2.00	1	18-Oct-26	21-Oct-26	16-Nov-26	18-Nov-26	636.09
Guard Rail		8.00	3	24-Oct-26	12-Nov-26	10-Nov-26	18-Nov-26	840,000.00
B2.31 23 00.654	Excavation	3.00	1	24-Oct-26	26-Oct-26	10-Nov-26	12-Nov-26	126,000.00
10 14 53.15	Foundation	2.00	1	26-Oct-26	27-Oct-26	12-Nov-26	14-Nov-26	210,000.00
B1.2.10 14 53.328	W-Beam Guard Rail Installation	4.00	1	28-Oct-26	12-Nov-26	15-Nov-26	18-Nov-26	504,000.00
Landscape		12.00	2	18-Oct-26	31-Oct-26	16-Nov-26	30-Nov-26	51,486.90
Fences		12.00	2	18-Oct-26	31-Oct-26	16-Nov-26	30-Nov-26	51,486.90
Steel fence (ZATCA HCIS)		12.00	2	18-Oct-26	31-Oct-26	16-Nov-26	30-Nov-26	51,486.90
B7.32 31 26.01-4	Earthwork	6.00	1	18-Oct-26	24-Oct-26	16-Nov-26	23-Nov-26	25,743.45
B7.32 31 26.01-6	Foundation	6.00	1	25-Oct-26	31-Oct-26	23-Nov-26	30-Nov-26	25,743.45
Customs Road 04 & Road 05		59.50	65	16-Sep-26	18-Nov-26	22-Sep-26 A	25-Nov-26	1,569,156.79
Wet Networks		17.59	11	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	72,657.69
TSE Network		17.59	11	16-Sep-26	07-Oct-26	04-Nov-26	24-Nov-26	72,657.69
HDPE Pipes		4.96	3	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	37,106.07
?125mm		4.96	3	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	37,106.07
Depth: 0.0m - 1.5m		4.96	3	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	37,106.07
B4.33 14 13.01-01	Pipe Laying(Rem)	2.59	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	22,263.88
B4.33 14 13.01-01	Embedment & Test(Rem)	4.17	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,894.79

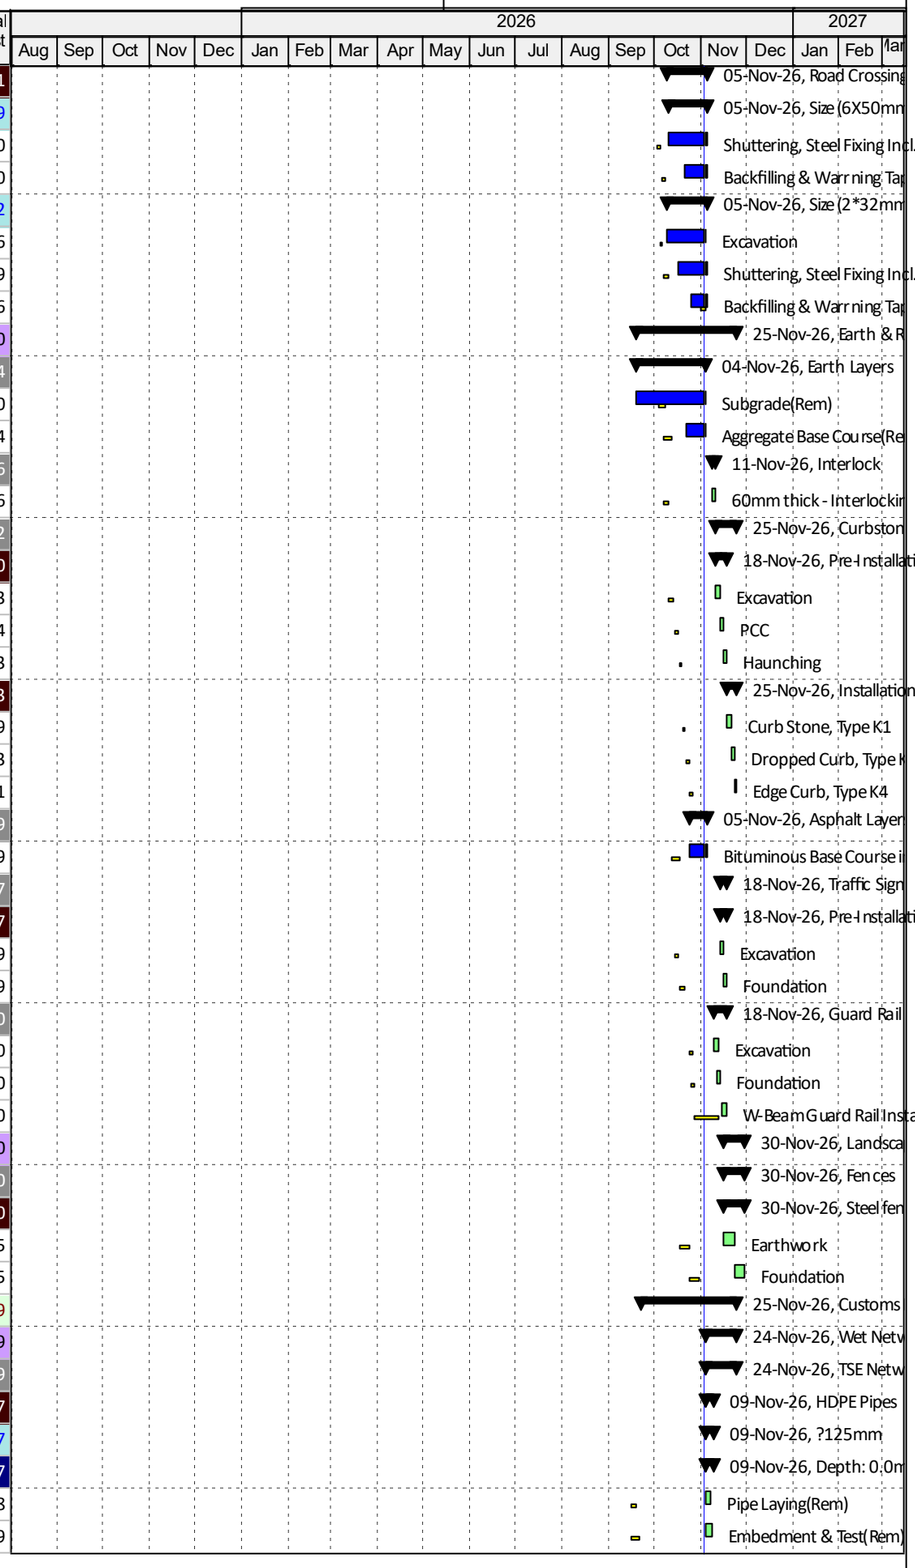

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B4.33 14 13.01-01	Backfilling & Warrning Tape(Rem)	4.96	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	4,947.40
Valves		15.00	8	19-Sep-26	07-Oct-26	07-Nov-26	24-Nov-26	35,551.62
Solenoid valves		15.00	8	19-Sep-26	07-Oct-26	07-Nov-26	24-Nov-26	35,551.62
1 Solenoid valve ?1.0 inch with box		9.00	3	19-Sep-26	30-Sep-26	07-Nov-26	17-Nov-26	9,604.63
B4.32 84 13.062	Pull Box Installation	3.00	1	19-Sep-26	22-Sep-26	07-Nov-26	10-Nov-26	1,848.31
B4.32 84 13.40	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	22-Sep-26	27-Sep-26	10-Nov-26	14-Nov-26	4,917.51
B4.32 84 13.41	Solenoid Valve Box Installation	3.00	1	27-Sep-26	30-Sep-26	14-Nov-26	17-Nov-26	2,838.80
1 Solenoid valve ?1.5 inch with box		9.00	3	22-Sep-26	04-Oct-26	10-Nov-26	21-Nov-26	15,199.87
B4.32 84 13.061	Pull Box Installation	3.00	1	22-Sep-26	27-Sep-26	10-Nov-26	14-Nov-26	1,848.31
B4.32 84 13.43	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	27-Sep-26	30-Sep-26	14-Nov-26	17-Nov-26	4,917.51
B4.32 84 13.44	Solenoid Valve Box Installation	3.00	1	30-Sep-26	04-Oct-26	17-Nov-26	21-Nov-26	8,434.05
1 Solenoid valve ?2.0 inch with box		6.00	2	30-Sep-26	07-Oct-26	17-Nov-26	24-Nov-26	10,747.11
B4.32 84 13.37	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	30-Sep-26	04-Oct-26	17-Nov-26	21-Nov-26	4,917.51
B4.32 84 13.38	Solenoid Valve Box Installation	3.00	1	04-Oct-26	07-Oct-26	21-Nov-26	24-Nov-26	5,829.60
Dry Networks		33.72	36	29-Sep-26	10-Nov-26	07-Oct-26 A	24-Nov-26	1,127,669.31
Medium Voltage Network		31.72	10	29-Sep-26	26-Oct-26	12-Oct-26 A	22-Nov-26	352,081.15
Duct Banks		19.00	3	04-Oct-26	26-Oct-26	12-Oct-26 A	05-Nov-26	38,569.64
2 Way		19.00	3	04-Oct-26	26-Oct-26	12-Oct-26 A	05-Nov-26	38,569.64
B2.31 23 00.641	Excavation	4.00	1	04-Oct-26	08-Oct-26	12-Oct-26 A	04-Nov-26	8,056.11
B2.33 71 00.290	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	8.00	1	08-Oct-26	18-Oct-26	15-Oct-26 A	05-Nov-26	20,822.61
B2.33 71 00.291	Backfilling & Warrning Tape	7.00	1	18-Oct-26	26-Oct-26	19-Oct-26 A	04-Nov-26	9,690.92
Cables		19.32	2	29-Sep-26	06-Oct-26	17-Oct-26 A	08-Nov-26	241,939.29
3C,500mm2		19.32	2	29-Sep-26	06-Oct-26	17-Oct-26 A	08-Nov-26	241,939.29
B2.33 71 49.23.86	Cable 13.8 kV Unarmored	4.00	1	29-Sep-26	03-Oct-26	17-Oct-26 A	04-Nov-26	234,058.34
B2.33 71 49.23.87	Straight joints cables	3.00	1	04-Oct-26	06-Oct-26	04-Nov-26	08-Nov-26	7,880.95
RMU		10.00	3	08-Oct-26	20-Oct-26	09-Nov-26	21-Nov-26	33,476.81
B2 33 73 00.02.15	Land Adjustment	3.00	1	08-Oct-26	12-Oct-26	09-Nov-26	12-Nov-26	8,183.22
B2 33 73 00.02.17	Foundation Works & Curing	4.00	1	12-Oct-26	17-Oct-26	12-Nov-26	17-Nov-26	8,183.22
B2 33 73 00.02.19	Installation of Ring Main Unit RMU, 13.8KV	3.00	1	17-Oct-26	20-Oct-26	17-Nov-26	21-Nov-26	17,110.37
Units Substation		8.00	2	12-Oct-26	21-Oct-26	12-Nov-26	22-Nov-26	38,095.41
B2 33 73 00.01.15	Land Adjustment	3.00	1	12-Oct-26	15-Oct-26	12-Nov-26	16-Nov-26	19,047.71
B2 33 73 00.01.17	Foundation Works & Curing	4.00	1	17-Oct-26	21-Oct-26	17-Nov-26	22-Nov-26	19,047.71
Low Voltage Network		14.44	7	04-Oct-26	17-Oct-26	04-Nov-26	21-Nov-26	171,088.61
Duct Banks		6.00	2	08-Oct-26	15-Oct-26	04-Nov-26	11-Nov-26	20,903.48
4 Way		6.00	2	08-Oct-26	15-Oct-26	04-Nov-26	11-Nov-26	20,903.48
B2.33 71 00 02 127	Excavation	3.00	1	08-Oct-26	12-Oct-26	04-Nov-26	08-Nov-26	5,225.87
B2.33 71 00 02 128	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	12-Oct-26	15-Oct-26	08-Nov-26	11-Nov-26	15,677.61
Cables		2.00	1	04-Oct-26	05-Oct-26	08-Nov-26	09-Nov-26	95,723.28
4C,10+1C,10mm2		2.00	1	04-Oct-26	05-Oct-26	08-Nov-26	09-Nov-26	95,723.28
B2.33 71 00 01 14	Cable Pulling	2.00	1	04-Oct-26	05-Oct-26	08-Nov-26	09-Nov-26	95,723.28
0.6/1 KV Low Voltage Distribution Panels		10.00	2	06-Oct-26	17-Oct-26	10-Nov-26	21-Nov-26	38,095.41
B2.33 71 26 30	Land Adjustment	2.00	1	06-Oct-26	07-Oct-26	10-Nov-26	11-Nov-26	19,047.71
B2.33 71 26 31	Foundation Works & Curing	3.00	1	14-Oct-26	17-Oct-26	18-Nov-26	21-Nov-26	19,047.71
0.6/1 KV Low Voltage Distribution Pillars		5.00	2	08-Oct-26	13-Oct-26	12-Nov-26	17-Nov-26	16,366.44
B2.33 71 26 33	Land Adjustment	2.00	1	08-Oct-26	10-Oct-26	12-Nov-26	14-Nov-26	8,183.22
B2.33 71 26 34	Foundation Works & Curing	3.00	1	11-Oct-26	13-Oct-26	15-Nov-26	17-Nov-26	8,183.22




© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Street Lighting		19.64	13	12-Oct-26	10-Nov-26	07-Oct-26 A	24-Nov-26	544,229.10
Duct Banks		10.00	3	12-Oct-26	22-Oct-26	15-Oct-26 A	07-Nov-26	46,040.68
2 Way		10.00	3	12-Oct-26	22-Oct-26	15-Oct-26 A	07-Nov-26	46,040.68
B2.33 71 00 02 73	Excavation	3.00	1	12-Oct-26	15-Oct-26	15-Oct-26 A	07-Nov-26	9,208.14
B2.33 71 00 02 74	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	15-Oct-26	19-Oct-26	18-Oct-26 A	07-Nov-26	27,624.41
B2.33 71 00 02 75	Backfilling & Warrning Tape	3.00	1	20-Oct-26	22-Oct-26	20-Oct-26 A	07-Nov-26	9,208.14
Drawpits		7.00	3	12-Oct-26	20-Oct-26	04-Nov-26	11-Nov-26	71,922.87
B2.33 71 00 02 76	Excavation	2.00	1	12-Oct-26	14-Oct-26	04-Nov-26	05-Nov-26	14,384.57
B2.33 71 00 02 77	Drawpits Installation	2.00	1	14-Oct-26	17-Oct-26	07-Nov-26	08-Nov-26	43,153.72
B2.33 71 00 02 78	Backfilling & Warrning Tape	3.00	1	17-Oct-26	20-Oct-26	09-Nov-26	11-Nov-26	14,384.57
Cables		7.00	2	02-Nov-26	10-Nov-26	16-Nov-26	24-Nov-26	103,854.93
4C,10+1C,10mm2		7.00	2	02-Nov-26	10-Nov-26	16-Nov-26	24-Nov-26	103,854.93
B2.33 71 19 162	Land Adjustment	2.00	1	02-Nov-26	04-Nov-26	16-Nov-26	18-Nov-26	25,963.96
B2.33 71 49.23.162	Cable Pulling	5.00	1	04-Nov-26	10-Nov-26	18-Nov-26	24-Nov-26	77,890.96
SL Poles		11.00	5	26-Oct-26	08-Nov-26	07-Oct-26 A	04-Nov-26	322,410.62
Pole (10 M Single Arm)		11.00	5	26-Oct-26	08-Nov-26	07-Oct-26 A	04-Nov-26	322,410.62
B2.33 71 16.87	Excavation	3.00	1	26-Oct-26	29-Oct-26	07-Oct-26 A	04-Nov-26	58,898.50
B2.33 71 16.88	PC & RC Foundation	3.00	1	29-Oct-26	02-Nov-26	13-Oct-26 A	04-Nov-26	58,898.50
B2.33 71 16.89	Lighting Poles Installation Incl power box, Cables	3.00	1	02-Nov-26	05-Nov-26	15-Oct-26 A	04-Nov-26	117,797.00
B2.26.56.19.15	Lighting Luminares Inst	2.00	1	05-Nov-26	08-Nov-26	17-Oct-26 A	04-Nov-26	27,918.13
B2.33 71 16.90	Backfilling, Grouting & Chamfering	2.00	1	05-Nov-26	08-Nov-26	19-Oct-26 A	04-Nov-26	58,898.50
Telecommunication Network		8.00	6	20-Oct-26	31-Oct-26	04-Nov-26	12-Nov-26	60,270.45
Manholes		8.00	6	20-Oct-26	31-Oct-26	04-Nov-26	12-Nov-26	60,270.45
Manhole Type 1		7.00	3	20-Oct-26	28-Oct-26	04-Nov-26	11-Nov-26	43,831.98
B2.31 23 00.627	Excavation	2.00	1	20-Oct-26	22-Oct-26	04-Nov-26	05-Nov-26	8,766.40
B2.33 71 00.262	Manhole Installation	2.00	1	22-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	26,299.19
B2.33 71 00.263	Backfilling & Warrning Tape	3.00	1	25-Oct-26	28-Oct-26	09-Nov-26	11-Nov-26	8,766.40
Manhole Type 2		6.00	3	22-Oct-26	31-Oct-26	07-Nov-26	12-Nov-26	16,438.47
B2.31 23 00.628	Excavation	2.00	1	22-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	3,287.69
B2.33 71 00.264	Manhole Installation	2.00	1	25-Oct-26	27-Oct-26	09-Nov-26	10-Nov-26	9,863.09
B2.33 71 00.265	Backfilling & Warrning Tape	2.00	1	28-Oct-26	31-Oct-26	11-Nov-26	12-Nov-26	3,287.69
Earth & Road Works		59.50	18	04-Oct-26	18-Nov-26	22-Sep-26 A	25-Nov-26	368,829.79
Earth Layers		2.00	2	04-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	51,573.06
B1.2.32 11 13.01.11_	Subgrade(Rem)	2.00	1	04-Oct-26	08-Oct-26	04-Nov-26	05-Nov-26	14,082.56
B1.2.32 11 23.01.11_	Aggregate Base Course(Rem)	2.00	1	06-Oct-26	11-Oct-26	04-Nov-26	05-Nov-26	37,490.50
Interlock		2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	21,405.58
B1.2.32 14 13.13.11	60mm thick - Interlocking Block Pavers	2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	21,405.58
Curbstone		11.00	7	05-Nov-26	18-Nov-26	12-Nov-26	25-Nov-26	45,759.81
Pre-Installation		5.00	3	05-Nov-26	11-Nov-26	12-Nov-26	18-Nov-26	24,215.75
B2.31 23 00.301	Excavation	2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	8,071.92
B1.2.32 14 13.13.21	PCC	2.00	1	07-Nov-26	09-Nov-26	14-Nov-26	16-Nov-26	8,071.92
32 16 13.0011	Haunching	2.00	1	09-Nov-26	11-Nov-26	16-Nov-26	18-Nov-26	8,071.92
Installation		6.00	4	11-Nov-26	18-Nov-26	18-Nov-26	25-Nov-26	21,544.05
B1.2.32 16.13.01.11	Curb Stone, Type K1	3.00	1	11-Nov-26	15-Nov-26	18-Nov-26	22-Nov-26	8,103.97
B1.2.32 16.13.02.10	Dropped Curb, Type K3	1.00	1	15-Nov-26	16-Nov-26	22-Nov-26	23-Nov-26	1,585.45
B1.2.32 16.13.03.11	Edge Curb, Type K4	1.00	1	16-Nov-26	17-Nov-26	23-Nov-26	24-Nov-26	6,096.19

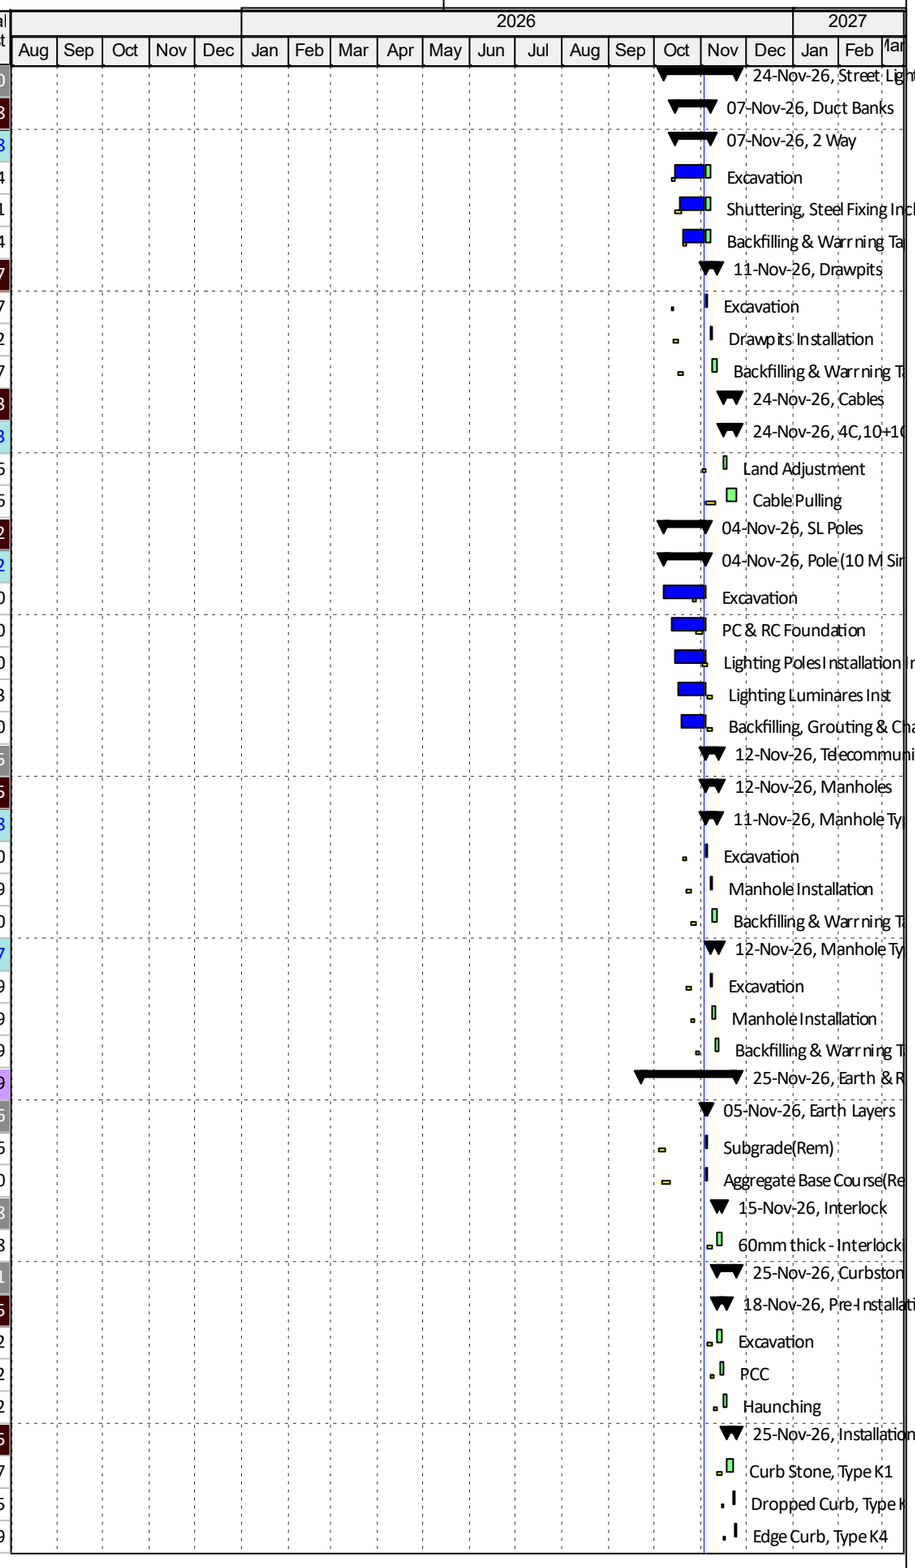


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B1.2.32 16.13.0411	Heel Curb, Type K5	1.00	1	17-Nov-26	18-Nov-26	24-Nov-26	25-Nov-26	5,758.45
Asphalt Layers		44.58	2	08-Oct-26	19-Oct-26	22-Sep-26 A	08-Nov-26	237,816.46
B1.2.32 11 26.01.11_	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	08-Oct-26	13-Oct-26	22-Sep-26 A	05-Nov-26	104,900.66
B1.2.32 12 16.01.11	Bituminous concrete Wearing Course, including tack coat (RC2)	2.00	1	14-Oct-26	19-Oct-26	05-Nov-26	08-Nov-26	132,915.80
Pavement Marking		10.82	2	20-Oct-26	29-Oct-26	08-Nov-26	21-Nov-26	3,372.20
B1.2.32 17 23.02.11	Retroreflective Thermoplastic Yellow, Traffic lines	2.00	1	20-Oct-26	25-Oct-26	08-Nov-26	10-Nov-26	1,092.59
B1.2.32 17 23.01.11	Retroreflective Thermoplastic White Traffic lines	2.00	1	28-Oct-26	29-Oct-26	18-Nov-26	21-Nov-26	2,279.62
Traffic Signs		8.90	4	05-Nov-26	12-Nov-26	12-Nov-26	23-Nov-26	8,902.67
Pre-Installation		4.00	2	05-Nov-26	10-Nov-26	12-Nov-26	17-Nov-26	3,854.31
B2.31 23 00.311	Excavation	2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	1,927.15
10 14 53.011	Foundation	2.00	1	08-Nov-26	10-Nov-26	15-Nov-26	17-Nov-26	1,927.15
Installation		2.00	2	10-Nov-26	12-Nov-26	21-Nov-26	23-Nov-26	5,048.37
B1.2.10 14 53.0111	1 Sheet Alumenium, Single post	2.00	1	10-Nov-26	12-Nov-26	21-Nov-26	23-Nov-26	1,930.58
B1.2.10 14 14.0211	Ground mounted, 1 Sheet Alumenium, Double post	2.00	1	10-Nov-26	12-Nov-26	21-Nov-26	23-Nov-26	3,117.79
Customs Road 06		89.41	50	24-Sep-26	23-Nov-26	24-Sep-26 A	28-Nov-26	1,102,357.42
Dry Networks		64.17	37	24-Sep-26	23-Nov-26	13-Oct-26 A	24-Nov-26	850,556.81
Medium Voltage Network		29.96	10	29-Sep-26	24-Oct-26	13-Oct-26 A	21-Nov-26	364,503.16
Cables		18.96	4	29-Sep-26	11-Oct-26	13-Oct-26 A	08-Nov-26	254,835.52
3C,500mm2		18.96	2	29-Sep-26	06-Oct-26	17-Oct-26 A	08-Nov-26	241,993.87
B2.33 71 49.23.92	Cable 13.8 kV Unarmored	4.00	1	29-Sep-26	03-Oct-26	17-Oct-26 A	04-Nov-26	234,112.92
B2.33 71 49.23.93	Straight joints cables	3.00	1	04-Oct-26	06-Oct-26	04-Nov-26	08-Nov-26	7,880.95
3C,50mm2		14.96	2	04-Oct-26	11-Oct-26	13-Oct-26 A	08-Nov-26	12,841.65
B2.33 71 49.23.95	Cable 13.8 kV Unarmored	4.00	1	04-Oct-26	07-Oct-26	13-Oct-26 A	04-Nov-26	4,960.70
B2.33 71 49.23.96	Straight joints cables	3.00	1	08-Oct-26	11-Oct-26	04-Nov-26	08-Nov-26	7,880.95
RMU		10.00	3	08-Oct-26	19-Oct-26	04-Nov-26	16-Nov-26	33,476.81
B2 33 73 00.02.5	Land Adjustment	3.00	1	08-Oct-26	11-Oct-26	04-Nov-26	08-Nov-26	8,183.22
B2 33 73 00.02.7	Foundation Works & Curing	4.00	1	12-Oct-26	15-Oct-26	08-Nov-26	12-Nov-26	8,183.22
B2 33 73 00.02.9	Installation of Ring Main Unit RMU, 13.8KV	3.00	1	17-Oct-26	19-Oct-26	12-Nov-26	16-Nov-26	17,110.37
Units Substation		11.00	3	12-Oct-26	24-Oct-26	08-Nov-26	21-Nov-26	76,190.82
B2 33 73 00.01.5	Land Adjustment	3.00	1	12-Oct-26	14-Oct-26	08-Nov-26	11-Nov-26	19,047.71
B2 33 73 00.01.7	Foundation Works & Curing	4.00	1	17-Oct-26	20-Oct-26	12-Nov-26	17-Nov-26	19,047.71
B2 33 73 00.01.9	Installation of Unit Substation 13.8/0.4 KV	3.00	1	21-Oct-26	24-Oct-26	17-Nov-26	21-Nov-26	38,095.41
Low Voltage Network		15.20	14	24-Sep-26	25-Oct-26	04-Nov-26	22-Nov-26	226,022.58
Duct Banks		12.00	8	24-Sep-26	07-Oct-26	04-Nov-26	17-Nov-26	38,647.32
2 Way		5.00	2	24-Sep-26	29-Sep-26	04-Nov-26	09-Nov-26	11,026.45
B2.33 71 00 02 142	Excavation	2.00	1	24-Sep-26	26-Sep-26	04-Nov-26	05-Nov-26	2,755.67
B2.33 71 00 02 143	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	27-Sep-26	29-Sep-26	07-Nov-26	09-Nov-26	8,270.78
6 Way		8.00	3	27-Sep-26	05-Oct-26	07-Nov-26	15-Nov-26	14,223.54
B2.33 71 00 02 130	Excavation	2.00	1	27-Sep-26	28-Sep-26	07-Nov-26	08-Nov-26	2,844.71
B2.33 71 00 02 131	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	29-Sep-26	01-Oct-26	09-Nov-26	11-Nov-26	8,534.12
B2.33 71 00 02 132	Backfilling & Warrning Tape	3.00	1	03-Oct-26	05-Oct-26	12-Nov-26	15-Nov-26	2,844.71
8 Way		8.00	3	29-Sep-26	07-Oct-26	09-Nov-26	17-Nov-26	13,397.33
B2.33 71 00 02 133	Excavation	2.00	1	29-Sep-26	30-Sep-26	09-Nov-26	10-Nov-26	2,680.93
B2.33 71 00 02 134	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	01-Oct-26	04-Oct-26	11-Nov-26	14-Nov-26	8,035.48
B2.33 71 00 02 135	Backfilling & Warrning Tape	3.00	1	05-Oct-26	07-Oct-26	15-Nov-26	17-Nov-26	2,680.93
Cables		4.00	2	08-Oct-26	12-Oct-26	04-Nov-26	09-Nov-26	121,556.59

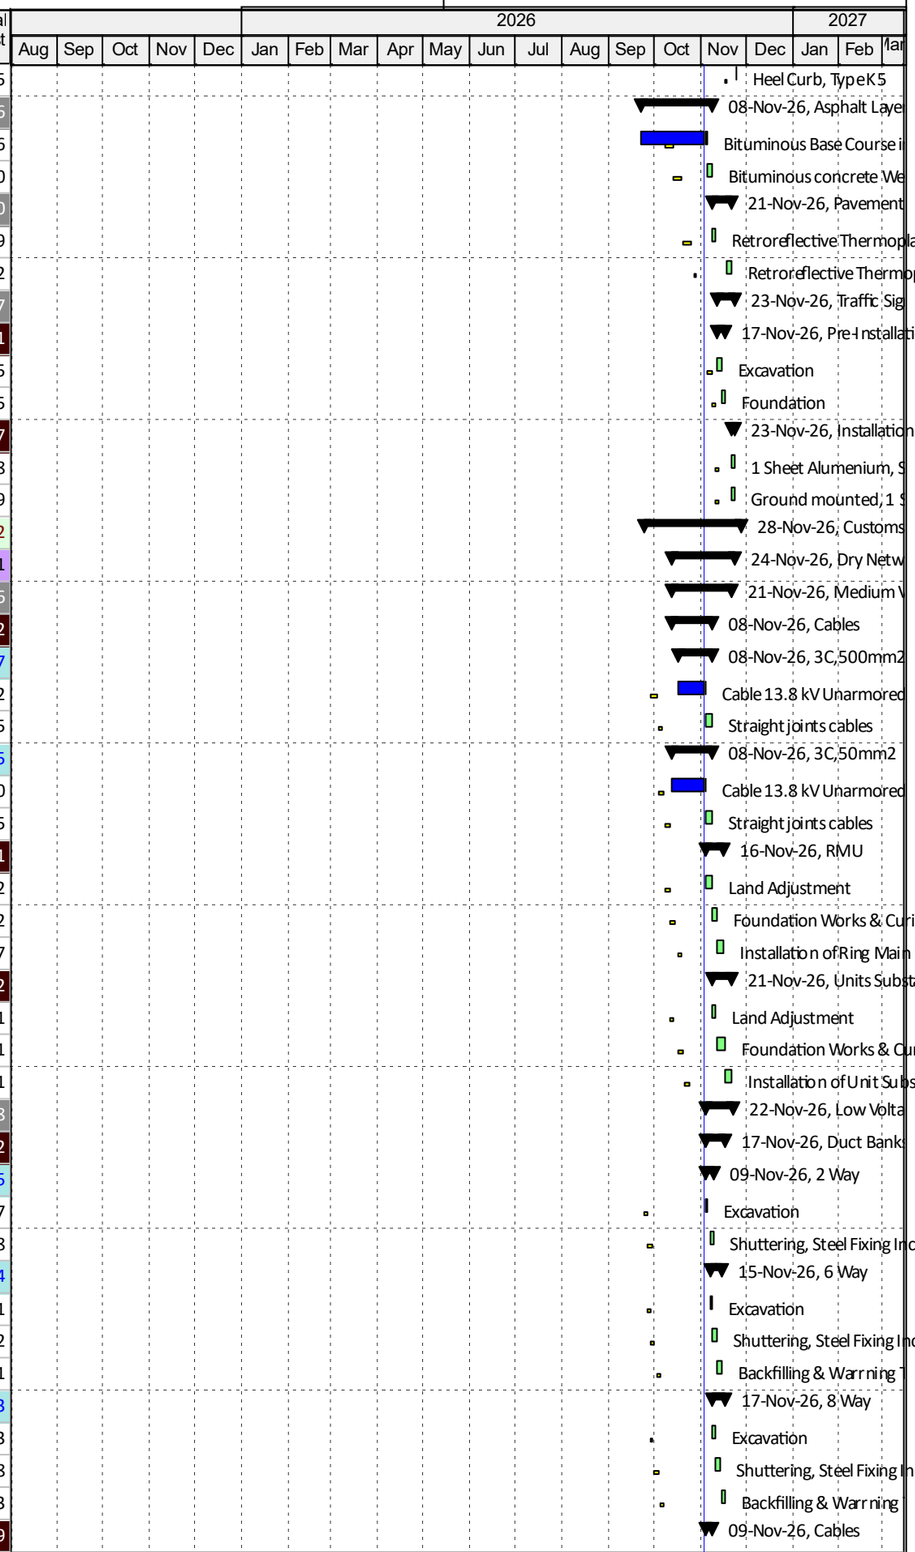


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
4C,10+1C,10mm2		2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	07-Nov-26	95,723.28
B2.33 71 00 01 17	Cable Pulling	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	07-Nov-26	95,723.28
4C,50+1C,25mm2		2.00	1	11-Oct-26	12-Oct-26	07-Nov-26	09-Nov-26	25,833.30
B2.33 71 00 01 18	Cable Pulling	2.00	1	11-Oct-26	12-Oct-26	07-Nov-26	09-Nov-26	25,833.30
0.6/1 KV Low Voltage Distribution Panels		2.00	1	15-Oct-26	17-Oct-26	11-Nov-26	14-Nov-26	19,047.71
B2.33 71 26 021	Land Adjustment	2.00	1	15-Oct-26	17-Oct-26	11-Nov-26	14-Nov-26	19,047.71
0.6/1 KV Low Voltage Distribution Pillars		7.00	3	18-Oct-26	25-Oct-26	14-Nov-26	22-Nov-26	46,770.97
B2.33 71 26 011	Land Adjustment	2.00	1	18-Oct-26	19-Oct-26	14-Nov-26	16-Nov-26	8,183.22
B2.33 71 26 012	Foundation Works & Curing	3.00	1	20-Oct-26	22-Oct-26	16-Nov-26	19-Nov-26	8,183.22
B2.33 71 26 013	Installation of 0.6/1 KV Low Voltage Distribution Pillars	2.00	1	24-Oct-26	25-Oct-26	19-Nov-26	22-Nov-26	30,404.52
Street Lighting		44.21	13	01-Oct-26	23-Nov-26	14-Oct-26 A	24-Nov-26	260,031.08
Duct Banks		8.00	3	01-Oct-26	10-Oct-26	11-Nov-26	19-Nov-26	18,796.27
4 Way		8.00	3	01-Oct-26	10-Oct-26	11-Nov-26	19-Nov-26	18,796.27
B2.33 71 00 02 154	Excavation	2.00	1	01-Oct-26	03-Oct-26	11-Nov-26	12-Nov-26	3,759.25
B2.33 71 00 02 155	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	04-Oct-26	06-Oct-26	14-Nov-26	16-Nov-26	11,277.76
B2.33 71 00 02 156	Backfilling & Warning Tape	3.00	1	07-Oct-26	10-Oct-26	17-Nov-26	19-Nov-26	3,759.25
Drawpits		4.00	2	04-Oct-26	07-Oct-26	14-Nov-26	17-Nov-26	57,538.30
B2.33 71 00 02 157	Excavation	2.00	1	04-Oct-26	05-Oct-26	14-Nov-26	15-Nov-26	14,384.57
B2.33 71 00 02 158	Drawpits Installation	2.00	1	06-Oct-26	07-Oct-26	16-Nov-26	17-Nov-26	43,153.72
Cables		6.00	2	13-Oct-26	19-Oct-26	09-Nov-26	16-Nov-26	48,183.79
4C,16+1C,16mm2		6.00	2	13-Oct-26	19-Oct-26	09-Nov-26	16-Nov-26	48,183.79
B2.33 71 19 182	Land Adjustment	3.00	1	13-Oct-26	15-Oct-26	09-Nov-26	12-Nov-26	12,045.95
B2.33 71 49.23.172	Cable Pulling	3.00	1	17-Oct-26	19-Oct-26	12-Nov-26	16-Nov-26	36,137.84
SL Poles		37.09	5	05-Nov-26	23-Nov-26	14-Oct-26 A	04-Nov-26	119,170.37
Pole (16 M Double Arm)		37.09	5	05-Nov-26	23-Nov-26	14-Oct-26 A	04-Nov-26	119,170.37
B2.33 71 16.103	Excavation	3.00	1	05-Nov-26	09-Nov-26	14-Oct-26 A	04-Nov-26	19,388.56
B2.33 71 16.104	PC & RC Foundation	3.00	1	09-Nov-26	12-Nov-26	17-Oct-26 A	04-Nov-26	19,388.56
B2.33 71 16.105	Lighting Poles Installation Incl power box, Cables	2.00	1	12-Nov-26	15-Nov-26	20-Oct-26 A	04-Nov-26	39,100.27
B2.26.56.19.19	Lighting Luminares Inst	2.00	1	22-Nov-26	23-Nov-26	21-Oct-26 A	04-Nov-26	21,904.40
B2.33 71 16.106	Backfilling, Grouting & Chamfering	3.00	1	22-Nov-26	23-Nov-26	22-Oct-26 A	04-Nov-26	19,388.56
SL Pillars		2.00	1	15-Nov-26	17-Nov-26	22-Nov-26	24-Nov-26	16,342.35
B2.33 71 26 033	Pillars Installation (Internal Wiring)	2.00	1	15-Nov-26	17-Nov-26	22-Nov-26	24-Nov-26	16,342.35
Earth & Road Works		60.50	12	14-Oct-26	21-Nov-26	24-Sep-26 A	26-Nov-26	226,057.16
Earth Layers		1.53	2	14-Oct-26	28-Oct-26	04-Nov-26	05-Nov-26	37,041.30
B1.2.32 11 13.01.14_	Subgrade(Rem)	1.05	1	14-Oct-26	25-Oct-26	04-Nov-26	05-Nov-26	9,674.99
B1.2.32 11 23.01.14_	Aggregate Base Course(Rem)	1.53	1	17-Oct-26	28-Oct-26	04-Nov-26	05-Nov-26	27,366.31
Interlock		2.00	1	15-Nov-26	21-Nov-26	04-Nov-26	07-Nov-26	14,706.05
B1.2.32 14 13.13.14	60mm thick - Interlocking Block Pavers	2.00	1	15-Nov-26	21-Nov-26	04-Nov-26	07-Nov-26	14,706.05
Curbstone		12.00	6	05-Nov-26	19-Nov-26	12-Nov-26	26-Nov-26	113,128.50
Pre-Installation		6.00	3	05-Nov-26	12-Nov-26	12-Nov-26	19-Nov-26	17,531.86
B2.31 23 00.391	Excavation	2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	5,843.95
B1.2.32 14 13.13.21	PCC	2.00	1	08-Nov-26	10-Nov-26	15-Nov-26	17-Nov-26	5,843.95
32 16 13.0014	Haunching	2.00	1	10-Nov-26	12-Nov-26	17-Nov-26	19-Nov-26	5,843.95
Installation		6.00	3	12-Nov-26	19-Nov-26	19-Nov-26	26-Nov-26	95,596.64
B1.2.32 16.13.01.14	Curb Stone, Type K1	2.00	1	12-Nov-26	15-Nov-26	19-Nov-26	22-Nov-26	8,063.06
B1.2.32 16.13.02.13	Dropped Curb, Type K3	2.00	1	15-Nov-26	17-Nov-26	22-Nov-26	24-Nov-26	

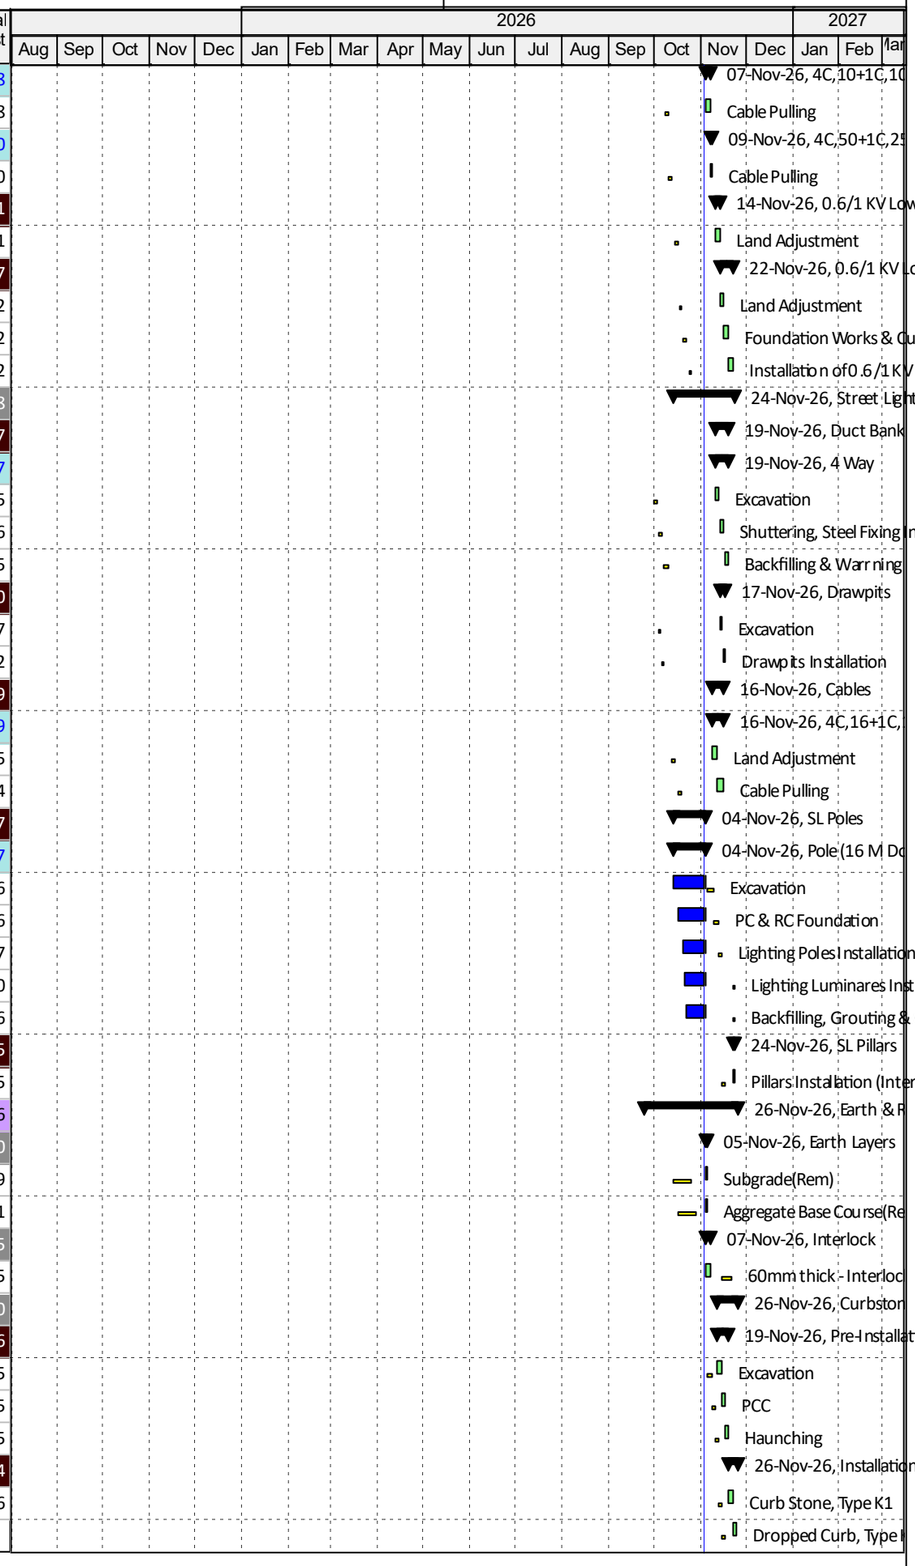


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B1.2.32 16.13.03.14	Edge Curb, Type K4	2.00	1	17-Nov-26	19-Nov-26	24-Nov-26	26-Nov-26	87,427.98
Asphalt Layers		2.00	1	26-Oct-26	05-Nov-26	24-Sep-26 A	05-Nov-26	60,444.78
B1.2.32 11 26.01.14_	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	26-Oct-26	05-Nov-26	24-Sep-26 A	05-Nov-26	60,444.78
Traffic Signs		4.00	2	05-Nov-26	10-Nov-26	12-Nov-26	17-Nov-26	736.52
Pre-Installation		4.00	2	05-Nov-26	10-Nov-26	12-Nov-26	17-Nov-26	736.52
B2.31 23 00.401	Excavation	2.00	1	05-Nov-26	08-Nov-26	12-Nov-26	15-Nov-26	379.42
10 14 53.014	Foundation	2.00	1	08-Nov-26	10-Nov-26	15-Nov-26	17-Nov-26	357.10
Landscape		6.00	1	20-Oct-26	26-Oct-26	21-Nov-26	28-Nov-26	25,743.45
Fences		6.00	1	20-Oct-26	26-Oct-26	21-Nov-26	28-Nov-26	25,743.45
Steel fence (ZATCA HCIS)		6.00	1	20-Oct-26	26-Oct-26	21-Nov-26	28-Nov-26	25,743.45
B7.32 31 26.01-190	Earthwork	6.00	1	20-Oct-26	26-Oct-26	21-Nov-26	28-Nov-26	25,743.45
Customs Road 02		62.50	98	16-Sep-26	22-Nov-26	17-Sep-26 A	29-Nov-26	1,520,063.66
Wet Networks		62.00	39	16-Sep-26	22-Nov-26	17-Sep-26 A	28-Nov-26	427,718.39
Sewerage Network		58.00	16	16-Sep-26	06-Oct-26	17-Sep-26 A	23-Nov-26	148,525.42
GRP Pipes		3.67	4	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	73,870.14
?150		3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	4,052.33
Depth From 1.5m to 2.5m		3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	4,052.33
B5.33 31 00.01.25	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	4,052.33
?200		3.67	3	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	69,817.82
Depth From 2.5m to 3.5m		3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	22,266.38
B5.33 31 00.01.27	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	22,266.38
Depth From 3.5m to 4.5m		3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	34,571.19
B5.33 31 00.01.29	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	24-Sep-26 A	04-Nov-26	34,571.19
Depth From 4.5m to 5.5m		3.67	1	16-Sep-26	20-Sep-26	26-Sep-26 A	04-Nov-26	12,980.25
B5.33 31 00.01.31	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	26-Sep-26 A	04-Nov-26	12,980.25
Manholes ?1200		13.00	5	16-Sep-26	01-Oct-26	17-Sep-26 A	07-Nov-26	42,754.10
Depth From 0.0m to 1.5m		2.56	1	16-Sep-26	19-Sep-26	04-Oct-26 A	05-Nov-26	1,545.49
B6.33 05 39.01.857	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	04-Oct-26 A	05-Nov-26	1,545.49
Depth From 1.5m to 2.5m		4.00	1	17-Sep-26	22-Sep-26	17-Sep-26 A	07-Nov-26	7,003.02
B6.33 05 39.01.907	Test, Internal Finishing, Benching & Cover	4.00	1	17-Sep-26	22-Sep-26	17-Sep-26 A	07-Nov-26	7,003.02
Depth From 2.5m to 3.5m		4.00	1	17-Sep-26	22-Sep-26	17-Sep-26 A	07-Nov-26	8,447.73
B6.33 05 39.01.957	Test, Internal Finishing, Benching & Cover	4.00	1	17-Sep-26	22-Sep-26	17-Sep-26 A	07-Nov-26	8,447.73
Depth From 4.5m to 5.5m		13.00	2	16-Sep-26	01-Oct-26	27-Sep-26 A	07-Nov-26	25,757.86
B6.33 05 39.01.100	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	29-Sep-26 A	05-Nov-26	18,898.48
Depth From 4.5m to 5.5m with back drop		5.00	1	27-Sep-26	01-Oct-26	27-Sep-26 A	07-Nov-26	6,859.38
B6.33 05 39.01.42	Test, Internal Finishing, Benching & Cover	5.00	1	27-Sep-26	01-Oct-26	27-Sep-26 A	07-Nov-26	6,859.38
Valves & Chambers		17.00	7	16-Sep-26	06-Oct-26	04-Nov-26	23-Nov-26	31,901.18
Gate Valves		4.00	2	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	3,127.62
B3.33 14 19.01.93	Burried Isolation Valve Installation	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	2,334.05
B3.33 14 19.01.103	Spindle & Surface Box	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	08-Nov-26	793.57
Washout Valves in Chambers		17.00	5	16-Sep-26	06-Oct-26	04-Nov-26	23-Nov-26	28,773.56
B3.33 14 19.01.43	Land Adjustment & Compaction	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	3,773.53
B3.33 14 19.01.53	Foundations	3.00	1	20-Sep-26	22-Sep-26	08-Nov-26	10-Nov-26	4,905.60
B3.33 14 19.01.63	Chambers Walls Conc Cast In Situ	3.00	1	24-Sep-26	27-Sep-26	11-Nov-26	14-Nov-26	11,697.96
B3.33 14 19.01.73	Chamber Curing, Finishing & Steel Cover	4.00	1	28-Sep-26	01-Oct-26	15-Nov-26	18-Nov-26	4,905.60
B3.33 14 19.01.83	Valve & Fitting Installation	4.00	1	03-Oct-26	06-Oct-26	19-Nov-26	23-Nov-26	3,490.88

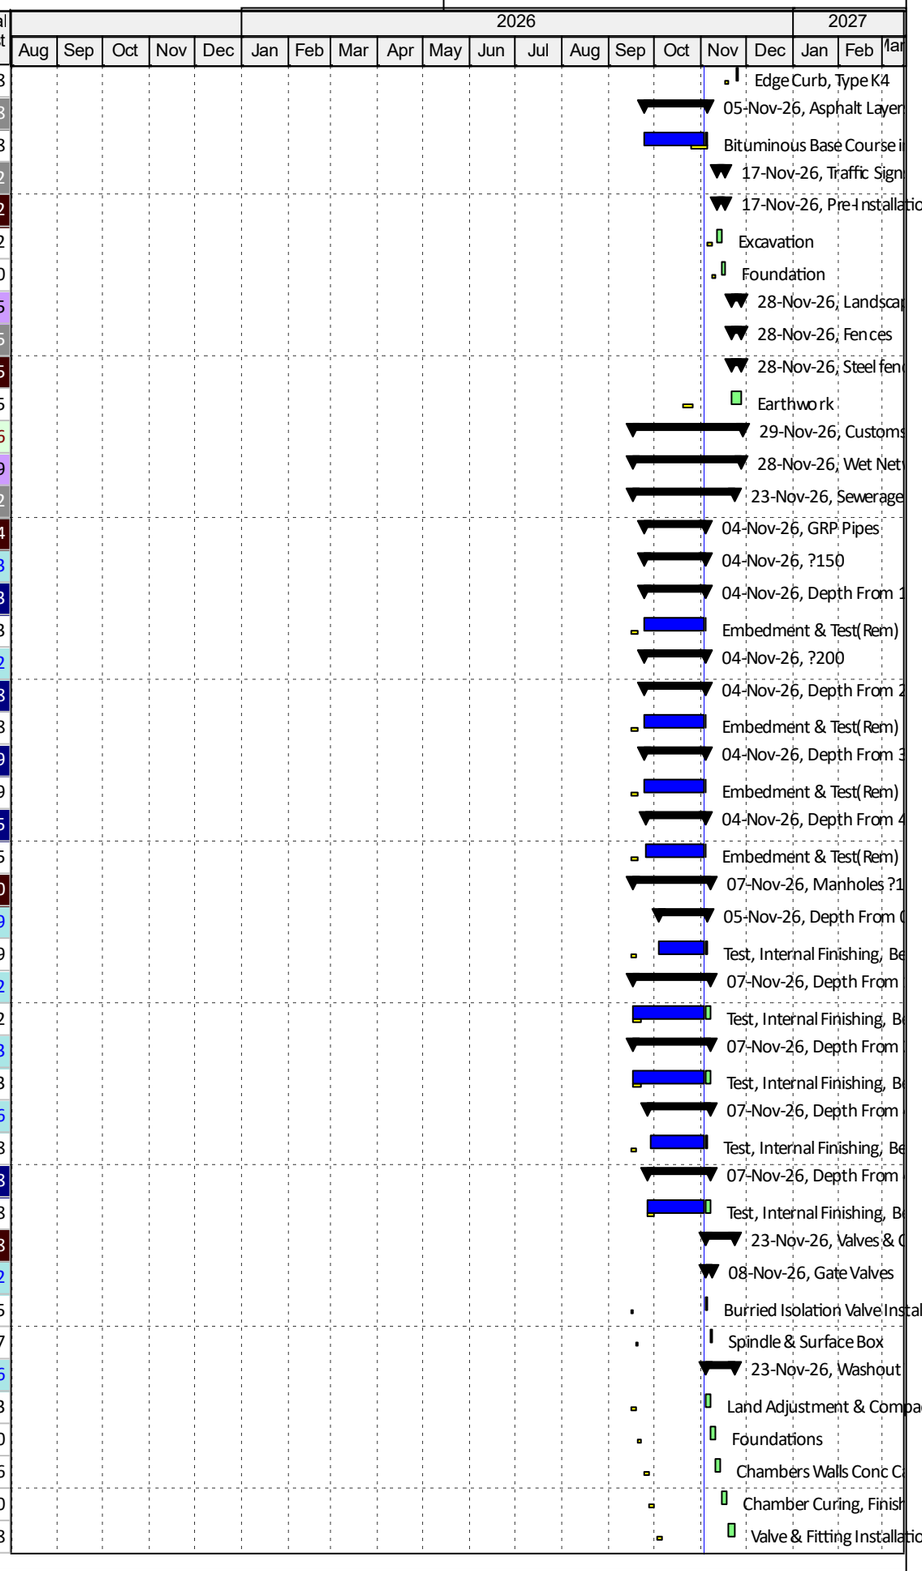

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Stormwater Network		21.84	10	16-Sep-26	30-Sep-26	14-Oct-26 A	08-Nov-26	54,705.14
GRP		3.84	2	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	1,211.99
?400		3.84	2	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	1,211.99
Depth From 1.5m to 2.5m		3.84	2	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	1,211.99
B6.33 42 11.01-1.	Embedment & Test(Rem)	3.56	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	807.90
B6.33 42 11.01-1.	Backfilling & Warning Tape(Rem)	3.84	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	404.09
Catch Basins		9.11	8	16-Sep-26	30-Sep-26	14-Oct-26 A	07-Nov-26	53,493.16
Single		3.00	4	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	33,681.59
B6.33 05 40.01.42(	Blinding Conc.(Rem)	3.00	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	3,372.57
B6.33 05 40.01.43(	Catch Basin Installation(Rem)	2.13	1	16-Sep-26	19-Sep-26	14-Oct-26 A	04-Nov-26	15,143.49
B6.33 05 40.01.41(	Excavation, Compaction & Vapour Barrier(Rem)	3.00	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	5,069.87
B6.33 05 40.01.44(	Backfilling, DI Frame & Grate Cover Fixing(Rem)	2.88	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	10,095.66
Double		9.11	4	16-Sep-26	30-Sep-26	14-Oct-26 A	07-Nov-26	19,811.57
B6.33 05 40.01.90(	Blinding Conc.(Rem)	3.00	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	1,295.73
B6.33 05 40.01.89(	Excavation, Compaction & Vapour Barrier(Rem)	3.00	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	1,971.76
B6.33 05 40.01.91(	Catch Basin Installation(Rem)	2.13	1	20-Sep-26	22-Sep-26	14-Oct-26 A	04-Nov-26	6,027.98
B6.33 05 40.01.920	Backfilling, DI Frame & Grate Cover Fixing	6.00	1	22-Sep-26	30-Sep-26	18-Oct-26 A	07-Nov-26	10,516.10
Potable Water Network		17.00	5	04-Oct-26	22-Oct-26	27-Sep-26 A	04-Nov-26	112,133.61
HDPE Pipes		17.00	5	04-Oct-26	22-Oct-26	27-Sep-26 A	04-Nov-26	112,133.61
?110mm		17.00	5	04-Oct-26	22-Oct-26	27-Sep-26 A	04-Nov-26	112,133.61
Depth: 0.51m - 1.5m		17.00	5	04-Oct-26	22-Oct-26	27-Sep-26 A	04-Nov-26	112,133.61
B3.33 14 13-191	Excavation	3.00	1	04-Oct-26	06-Oct-26	27-Sep-26 A	04-Nov-26	22,426.31
B3.33 14 13-193	Sand Bedding	3.00	1	07-Oct-26	10-Oct-26	30-Sep-26 A	04-Nov-26	5,607.60
B3.33 14 13-195	Pipe Laying	3.00	1	11-Oct-26	13-Oct-26	03-Oct-26 A	04-Nov-26	50,460.23
B3.33 14 13-197	Embedment & Test	4.00	1	14-Oct-26	18-Oct-26	07-Oct-26 A	04-Nov-26	22,426.31
B3.33 14 13-199	Backfilling & Warning Tape	4.00	1	19-Oct-26	22-Oct-26	11-Oct-26 A	04-Nov-26	11,213.16
Fire Fighting Network		21.00	8	21-Oct-26	22-Nov-26	04-Nov-26	28-Nov-26	112,354.20
Valves & Chambers		21.00	5	28-Oct-26	09-Nov-26	04-Nov-26	28-Nov-26	30,277.78
Air Valves		21.00	5	28-Oct-26	09-Nov-26	04-Nov-26	28-Nov-26	30,277.78
Air valves on less than 315 mm. (In Chamber)		21.00	5	28-Oct-26	09-Nov-26	04-Nov-26	28-Nov-26	30,277.78
B3.33 05 63.02.67	Land Adjustment & Compaction	4.00	1	28-Oct-26	29-Oct-26	04-Nov-26	08-Nov-26	4,485.60
B3.33 05 63.02.65	Foundations	4.00	1	31-Oct-26	02-Nov-26	09-Nov-26	12-Nov-26	5,821.24
B3.33 05 63.02.68	Chambers Walls Conc Cast In Situ	4.00	1	03-Nov-26	04-Nov-26	14-Nov-26	17-Nov-26	5,980.80
B3.33 05 63.02.66	Chamber Curing, Finishing & Steel Cover	5.00	1	05-Nov-26	07-Nov-26	18-Nov-26	23-Nov-26	4,645.16
B3.33 05 63.02.69	Valve & Fitting Installation	4.00	1	08-Nov-26	09-Nov-26	24-Nov-26	28-Nov-26	9,344.99
Fire Hydrant		19.00	3	21-Oct-26	22-Nov-26	04-Nov-26	25-Nov-26	82,076.43
B3.33 14 19.01.fh38	Riser Pipe & Flanged Fittings Installation	4.00	1	21-Oct-26	25-Oct-26	04-Nov-26	08-Nov-26	16,415.29
B3.33 14 19.01.fh37	Firehydrant Fixing/Installation	5.00	1	26-Oct-26	31-Oct-26	09-Nov-26	14-Nov-26	49,245.86
B3.33 14 19.01.fh39	Backfilling & Compaction	5.00	1	19-Nov-26	22-Nov-26	21-Nov-26	25-Nov-26	16,415.29
Dry Networks		20.00	43	30-Sep-26	16-Nov-26	04-Nov-26	26-Nov-26	820,833.45
Medium Voltage Network		11.94	3	30-Sep-26	13-Oct-26	07-Nov-26	21-Nov-26	244,997.79
Cables		11.94	3	30-Sep-26	13-Oct-26	07-Nov-26	21-Nov-26	244,997.79
3C,500mm2		11.94	3	30-Sep-26	13-Oct-26	07-Nov-26	21-Nov-26	244,997.79
B2.33 71 49.23.83	Cable 13.8 kV Unarmored	4.00	1	30-Sep-26		07-Nov-26	11-Nov-26	234,058.34
B2.33 71 49.23.84	Straight joints cables	3.00	1	05-Oct-26	08-Oct-26	11-Nov-26	15-Nov-26	7,880.95
B2.33 71 49.23.85	Cable Termination	4.00	1	08-Oct-26	13-Oct-26	16-Nov-26	21-Nov-26	3,058.50

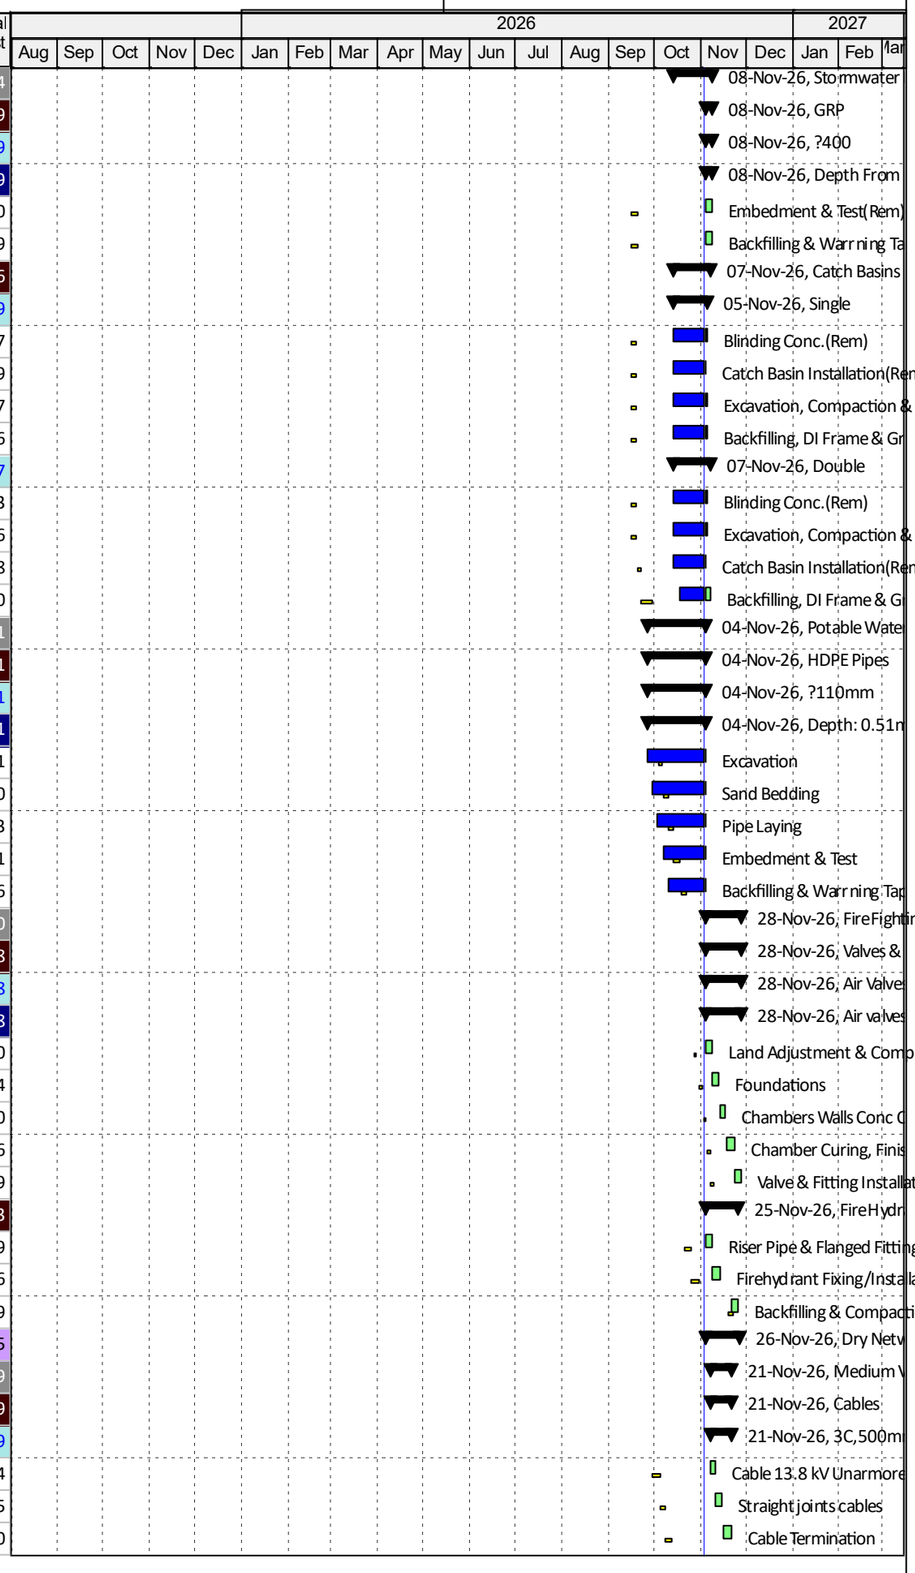


Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Low Voltage Network		11.00	8	30-Sep-26	04-Nov-26	07-Nov-26	19-Nov-26	149,177.45
Duct Banks		11.00	6	30-Sep-26	04-Nov-26	07-Nov-26	19-Nov-26	27,620.87
6 Way		8.00	3	30-Sep-26	01-Nov-26	07-Nov-26	16-Nov-26	14,223.54
B2.33 71 00 02 136	Excavation	2.00	1	30-Sep-26	03-Oct-26	07-Nov-26	09-Nov-26	2,844.71
B2.33 71 00 02 137	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	03-Oct-26	06-Oct-26	09-Nov-26	12-Nov-26	8,534.12
B2.33 71 00 02 138	Backfilling & Warning Tape	3.00	1	29-Oct-26	01-Nov-26	12-Nov-26	16-Nov-26	2,844.71
8 Way		9.00	3	03-Oct-26	04-Nov-26	09-Nov-26	19-Nov-26	13,397.33
B2.33 71 00 02 139	Excavation	2.00	1	03-Oct-26	05-Oct-26	09-Nov-26	11-Nov-26	2,680.93
B2.33 71 00 02 140	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	05-Oct-26	08-Oct-26	11-Nov-26	15-Nov-26	8,035.48
B2.33 71 00 02 141	Backfilling & Warning Tape	3.00	1	02-Nov-26	04-Nov-26	16-Nov-26	19-Nov-26	2,680.93
Cables		4.00	2	13-Oct-26	17-Oct-26	09-Nov-26	14-Nov-26	121,556.59
4C,10+1C,10mm2		2.00	1	13-Oct-26	14-Oct-26	09-Nov-26	11-Nov-26	95,723.28
B2.33 71 00 01 15	Cable Pulling	2.00	1	13-Oct-26	14-Oct-26	09-Nov-26	11-Nov-26	95,723.28
4C,50+1C,25mm2		2.00	1	15-Oct-26	17-Oct-26	11-Nov-26	14-Nov-26	25,833.30
B2.33 71 00 01 16	Cable Pulling	2.00	1	15-Oct-26	17-Oct-26	11-Nov-26	14-Nov-26	25,833.30
Street Lighting		12.00	8	03-Nov-26	16-Nov-26	14-Nov-26	26-Nov-26	196,917.89
SL Poles		12.00	8	03-Nov-26	16-Nov-26	14-Nov-26	26-Nov-26	196,917.89
Pole (10 M Double Arm)		12.00	5	03-Nov-26	16-Nov-26	14-Nov-26	26-Nov-26	119,040.49
B2.33 71 16.79	Excavation	2.00	1	03-Nov-26	04-Nov-26	14-Nov-26	15-Nov-26	18,488.33
B2.33 71 16.80	PC & RC Foundation	2.00	1	05-Nov-26	07-Nov-26	16-Nov-26	17-Nov-26	17,169.04
B2.33 71 16.81	Lighting Poles Installation Incl power box, Cables	3.00	1	08-Nov-26	10-Nov-26	18-Nov-26	21-Nov-26	36,976.66
B2.26.56.19.13	Lighting Luminares Inst	2.00	1	11-Nov-26	12-Nov-26	22-Nov-26	23-Nov-26	27,918.13
B2.33 71 16.82	Backfilling, Grouting & Chamfering	3.00	1	14-Nov-26	16-Nov-26	24-Nov-26	26-Nov-26	18,488.33
Pole (16 M Double Arm)		8.00	3	05-Nov-26	14-Nov-26	16-Nov-26	24-Nov-26	77,877.40
B2.33 71 16.83	Excavation	2.00	1	05-Nov-26	07-Nov-26	16-Nov-26	17-Nov-26	19,388.56
B2.33 71 16.84	PC & RC Foundation	3.00	1	08-Nov-26	10-Nov-26	18-Nov-26	21-Nov-26	19,388.56
B2.33 71 16.85	Lighting Poles Installation Incl power box, Cables	3.00	1	11-Nov-26	14-Nov-26	22-Nov-26	24-Nov-26	39,100.27
Telecommunication Network		18.00	24	07-Oct-26	28-Oct-26	04-Nov-26	24-Nov-26	229,740.32
Ducts		13.00	15	07-Oct-26	22-Oct-26	04-Nov-26	18-Nov-26	158,365.40
Size (6*50mm+2*32mm) HDPE ducts		9.00	3	07-Oct-26	19-Oct-26	04-Nov-26	14-Nov-26	106,245.26
B2.1.33 81 26.135	Excavation	2.00	1	07-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	21,251.23
B2.1.33 81 26.136	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	3.00	1	10-Oct-26	13-Oct-26	07-Nov-26	09-Nov-26	63,742.79
B2.1.33 81 26.137	Backfilling & Warning Tape	3.00	1	17-Oct-26	19-Oct-26	11-Nov-26	14-Nov-26	21,251.23
Size (6*50mm+4*32mm) HDPE ducts		8.00	3	10-Oct-26	19-Oct-26	07-Nov-26	15-Nov-26	37,205.53
B2.1.33 81 26.138	Excavation	2.00	1	10-Oct-26	12-Oct-26	07-Nov-26	08-Nov-26	7,441.11
B2.1.33 81 26.139	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	3.00	1	12-Oct-26	15-Oct-26	09-Nov-26	11-Nov-26	22,323.32
B2.1.33 81 26.140	Backfilling & Warning Tape	3.00	1	15-Oct-26	19-Oct-26	12-Nov-26	15-Nov-26	7,441.11
Size (2*32mm) HDPE ducts		7.00	3	12-Oct-26	20-Oct-26	09-Nov-26	16-Nov-26	6,720.24
B2.1.33 81 26.141	Excavation	2.00	1	12-Oct-26	14-Oct-26	09-Nov-26	10-Nov-26	1,344.05
B2.1.33 81 26.142	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	14-Oct-26	17-Oct-26	11-Nov-26	12-Nov-26	4,032.14
B2.1.33 81 26.143	Backfilling & Warning Tape	3.00	1	17-Oct-26	20-Oct-26	14-Nov-26	16-Nov-26	1,344.05
Size (4*32mm) HDPE ducts		7.00	3	12-Oct-26	20-Oct-26	09-Nov-26	16-Nov-26	5,498.91
B2.1.33 81 26.144	Excavation	2.00	1	12-Oct-26	14-Oct-26	09-Nov-26	10-Nov-26	1,099.70
B2.1.33 81 26.145	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	14-Oct-26	17-Oct-26	11-Nov-26	12-Nov-26	3,299.51
B2.1.33 81 26.146	Backfilling & Warning Tape	3.00	1	17-Oct-26	20-Oct-26	14-Nov-26	16-Nov-26	1,099.70
Size (6*50mm+6*32mm) HDPE ducts		7.00	3	14-Oct-26	22-Oct-26	11-Nov-26	18-Nov-26	2,695.47

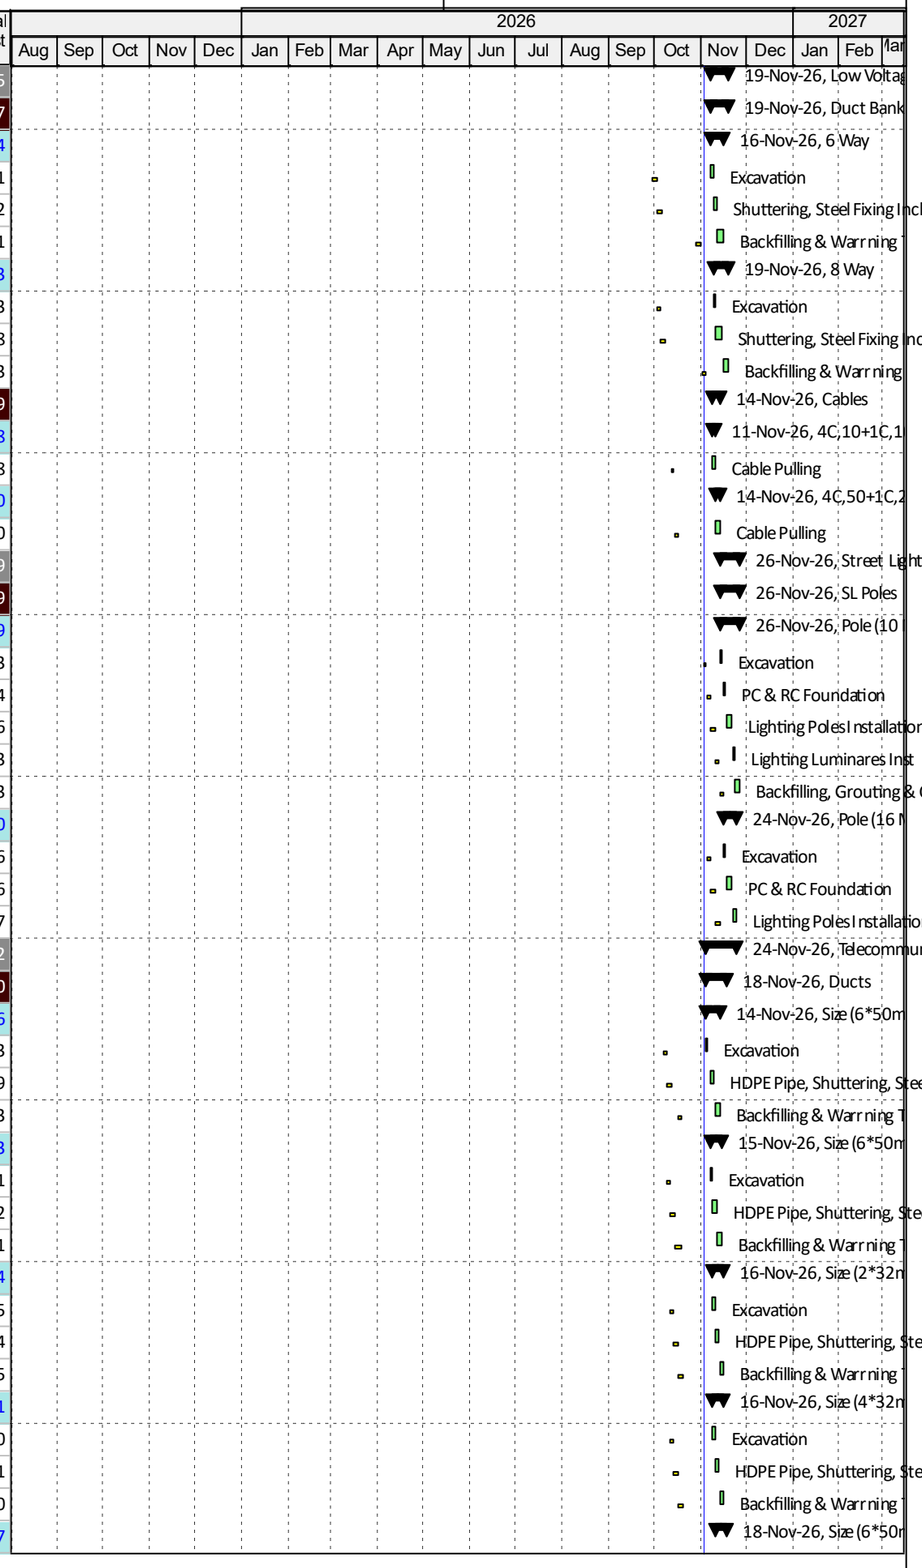


Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.1.33 81 26.147	Excavation	2.00	1	14-Oct-26	17-Oct-26	11-Nov-26	12-Nov-26	538.74
B2.1.33 81 26.148	HDPE Pipe, Shuttering, Steel Fixing & Conc. Cast	2.00	1	17-Oct-26	19-Oct-26	14-Nov-26	15-Nov-26	1,617.98
B2.1.33 81 26.149	Backfilling & Warrning Tape	3.00	1	19-Oct-26	22-Oct-26	16-Nov-26	18-Nov-26	538.74
Manholes		10.00	6	17-Oct-26	28-Oct-26	14-Nov-26	24-Nov-26	60,270.45
Manhole Type 1		7.00	3	17-Oct-26	25-Oct-26	14-Nov-26	21-Nov-26	43,831.98
B2.31 23 00.623	Excavation	2.00	1	17-Oct-26	19-Oct-26	14-Nov-26	15-Nov-26	8,766.40
B2.33 71 00.254	Manhole Installation	2.00	1	19-Oct-26	21-Oct-26	16-Nov-26	17-Nov-26	26,299.19
B2.33 71 00.255	Backfilling & Warrning Tape	3.00	1	21-Oct-26	25-Oct-26	18-Nov-26	21-Nov-26	8,766.40
Manhole Type 2		8.00	3	19-Oct-26	28-Oct-26	16-Nov-26	24-Nov-26	16,438.47
B2.31 23 00.625	Excavation	2.00	1	19-Oct-26	21-Oct-26	16-Nov-26	17-Nov-26	3,287.69
B2.33 71 00.258	Manhole Installation	3.00	1	21-Oct-26	25-Oct-26	18-Nov-26	21-Nov-26	9,863.09
B2.33 71 00.259	Backfilling & Warrning Tape	3.00	1	25-Oct-26	28-Oct-26	22-Nov-26	24-Nov-26	3,287.69
Road Crossing Ducts		7.00	3	17-Oct-26	25-Oct-26	14-Nov-26	21-Nov-26	11,104.47
Size (6X50mm) HDPE		7.00	3	17-Oct-26	25-Oct-26	14-Nov-26	21-Nov-26	11,104.47
B2.31 23 00.622	Excavation	2.00	1	17-Oct-26	19-Oct-26	14-Nov-26	15-Nov-26	2,221.93
B2.33 71 00.252	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	2.00	1	19-Oct-26	21-Oct-26	16-Nov-26	17-Nov-26	6,660.61
B2.33 71 00.253	Backfilling & Warrning Tape	3.00	1	21-Oct-26	25-Oct-26	18-Nov-26	21-Nov-26	2,221.93
Earth & Road Works		15.00	14	05-Oct-26	16-Nov-26	05-Nov-26	23-Nov-26	220,024.92
Earth Layers		2.00	2	17-Oct-26	11-Nov-26	07-Nov-26	08-Nov-26	33,045.55
B1.2.32 11 13.01.13_	Subgrade(Rem)	2.00	1	17-Oct-26	25-Oct-26	07-Nov-26	08-Nov-26	5,000.96
B1.2.32 11 23.01.13_	Aggregate Base Course(Rem)	1.04	1	26-Oct-26	11-Nov-26	07-Nov-26	08-Nov-26	28,044.59
Interlock		3.00	1	05-Oct-26	07-Oct-26	05-Nov-26	09-Nov-26	14,780.48
B1.2.32 14 13.13.13	60mm thick - Interlocking Block Pavers	3.00	1	05-Oct-26	07-Oct-26	05-Nov-26	09-Nov-26	14,780.48
Curbstone		12.00	8	08-Oct-26	21-Oct-26	09-Nov-26	23-Nov-26	37,093.57
Pre-Installation		9.00	3	08-Oct-26	18-Oct-26	09-Nov-26	19-Nov-26	17,872.62
B2.31 23 00.361	Excavation	2.00	1	08-Oct-26	10-Oct-26	09-Nov-26	11-Nov-26	5,957.54
B1.2.32 14 13.13.21	PCC	3.00	1	11-Oct-26	13-Oct-26	11-Nov-26	15-Nov-26	5,957.54
32 16 13.0013	Haunching	4.00	1	14-Oct-26	18-Oct-26	15-Nov-26	19-Nov-26	5,957.54
Installation		3.00	5	19-Oct-26	21-Oct-26	19-Nov-26	23-Nov-26	19,220.95
B1.2.32 16.13.01.13	Curb Stone, Type K1	3.00	1	19-Oct-26	21-Oct-26	19-Nov-26	23-Nov-26	8,307.55
B1.2.32 16.13.02.12	Dropped Curb, Type K3	2.00	1	20-Oct-26	21-Oct-26	21-Nov-26	23-Nov-26	149.19
B1.2.32 16.13.03.13	Edge Curb, Type K4	2.00	1	20-Oct-26	21-Oct-26	21-Nov-26	23-Nov-26	5,916.78
B1.2.32 16.13.0413	Heel Curb, Type K 5	2.00	1	20-Oct-26	21-Oct-26	21-Nov-26	23-Nov-26	4,782.31
B1.2.32 16.13.05.12	Transition Curb	2.00	1	20-Oct-26	21-Oct-26	21-Nov-26	23-Nov-26	65.12
Asphalt Layers		1.14	1	04-Nov-26	16-Nov-26	07-Nov-26	08-Nov-26	133,185.90
B1.2.32 11 26.01.13_	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	1.14	1	04-Nov-26	16-Nov-26	07-Nov-26	08-Nov-26	133,185.90
Traffic Signs		4.00	2	11-Oct-26	14-Oct-26	11-Nov-26	16-Nov-26	1,919.42
Pre-Installation		4.00	2	11-Oct-26	14-Oct-26	11-Nov-26	16-Nov-26	1,919.42
B2.31 23 00.371	Excavation	2.00	1	11-Oct-26	12-Oct-26	11-Nov-26	14-Nov-26	959.71
10 14 53.013	Foundation	2.00	1	13-Oct-26	14-Oct-26	14-Nov-26	16-Nov-26	959.71
Landscape		13.00	2	13-Oct-26	27-Oct-26	14-Nov-26	29-Nov-26	51,486.90
Fences		13.00	2	13-Oct-26	27-Oct-26	14-Nov-26	29-Nov-26	51,486.90
Steel fence (ZATCA HCIS)		13.00	2	13-Oct-26	27-Oct-26	14-Nov-26	29-Nov-26	51,486.90
B7.32 31 26.01-19	Earthwork	6.00	1	13-Oct-26	19-Oct-26	14-Nov-26	21-Nov-26	25,743.45
B7.32 31 26.01-111	Foundation	7.00	1	20-Oct-26	27-Oct-26	21-Nov-26	29-Nov-26	25,743.45
Customs Road 01		158.48	79	21-May-26	12-Nov-26	21-May-26 A	06-Dec-26	1,647,453.22

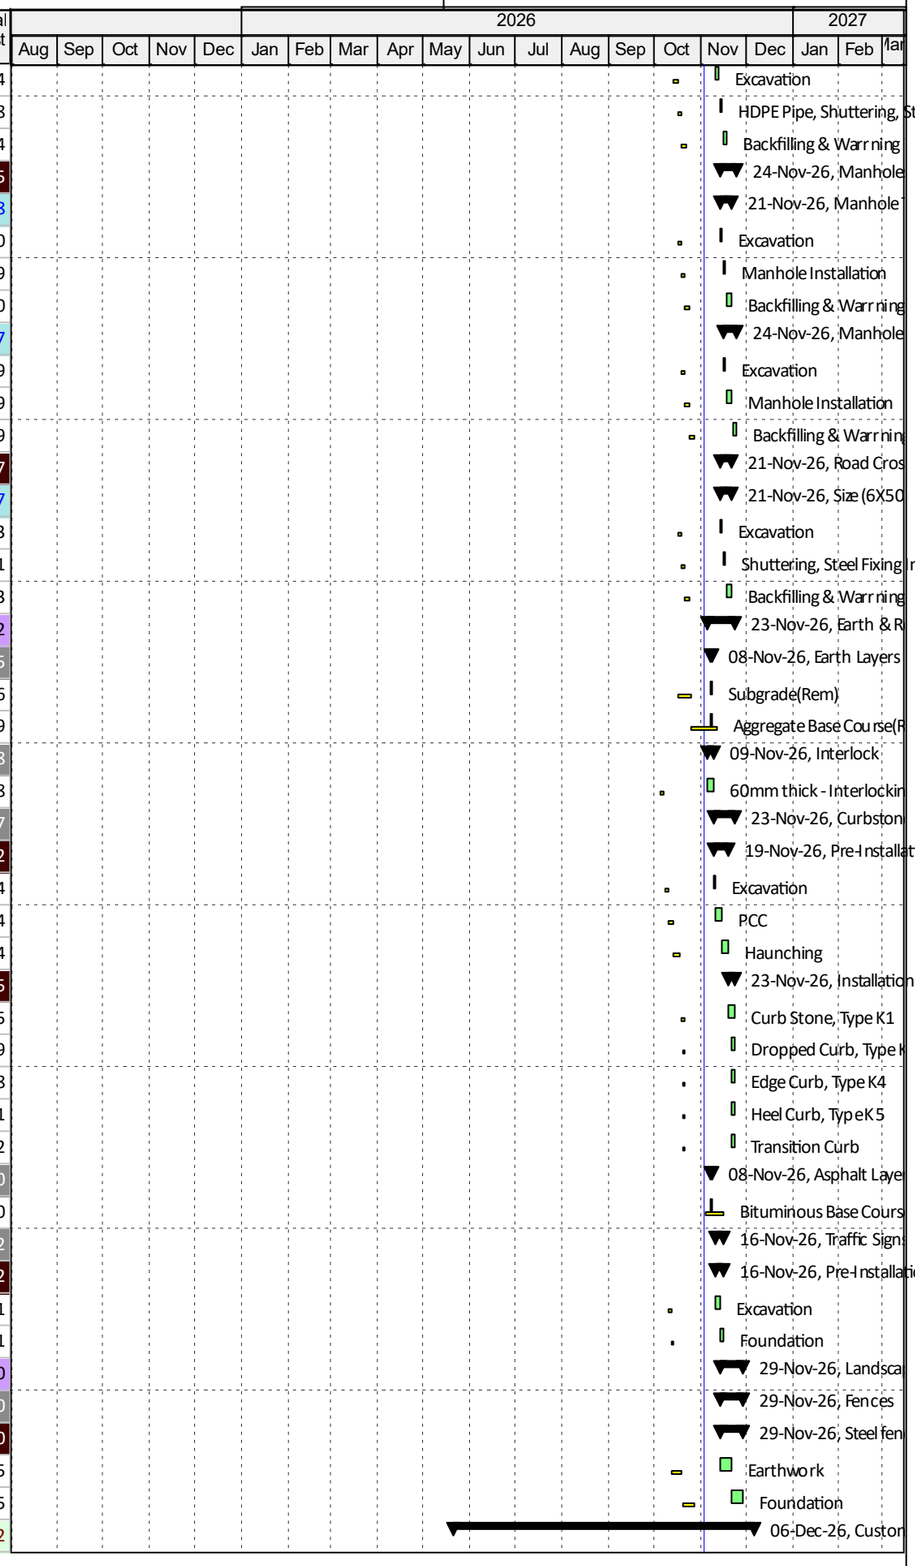

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Wet Networks		62.00	33	16-Sep-26	12-Nov-26	20-Sep-26 A	06-Dec-26	826,149.88
Sewerage Network		62.00	11	16-Sep-26	19-Oct-26	20-Sep-26 A	06-Dec-26	114,675.92
GRP Pipes		3.67	2	16-Sep-26	20-Sep-26	20-Sep-26 A	04-Nov-26	4,906.61
?150		3.67	2	16-Sep-26	20-Sep-26	20-Sep-26 A	04-Nov-26	4,906.61
Depth From 1.5m to 2.5m		3.67	1	16-Sep-26	20-Sep-26	26-Sep-26 A	04-Nov-26	4,031.30
B5.33 31 00.01.02	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	26-Sep-26 A	04-Nov-26	4,031.30
Depth From 2.5m to 3.5m		3.67	1	16-Sep-26	20-Sep-26	20-Sep-26 A	04-Nov-26	875.31
B5.33 31 00.01.02	Embedment & Test(Rem)	3.67	1	16-Sep-26	20-Sep-26	20-Sep-26 A	04-Nov-26	875.31
Manholes ?1200		28.00	5	16-Sep-26	19-Oct-26	24-Sep-26 A	06-Dec-26	37,704.12
Depth From 1.5m to 2.5m		28.00	3	16-Sep-26	19-Oct-26	26-Sep-26 A	06-Dec-26	23,823.18
B6.33 05 39.01.747	Manhole Installation (Rem)	1.52	1	16-Sep-26	17-Sep-26	26-Sep-26 A	04-Nov-26	13,845.51
B6.33 05 39.01.757	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	28-Sep-26 A	05-Nov-26	3,835.68
B6.33 05 39.01.767	Backfilling(Rem)	10.00	1	08-Oct-26	19-Oct-26	04-Oct-26 A	06-Dec-26	6,141.99
Depth From 2.5m to 3.5m		28.00	2	16-Sep-26	19-Oct-26	24-Sep-26 A	06-Dec-26	13,880.94
B6.33 05 39.01.807	Test, Internal Finishing, Benching & Cover(Rem)	2.56	1	16-Sep-26	19-Sep-26	24-Sep-26 A	05-Nov-26	4,626.97
B6.33 05 39.01.817	Backfilling(Rem)	10.00	1	08-Oct-26	19-Oct-26	01-Oct-26 A	06-Dec-26	9,253.97
HDPE Pipes		21.00	4	16-Sep-26	11-Oct-26	04-Nov-26	28-Nov-26	72,065.19
?160		21.00	4	16-Sep-26	11-Oct-26	04-Nov-26	28-Nov-26	72,065.19
Depth From 0.0m to 1.5m		21.00	4	16-Sep-26	11-Oct-26	04-Nov-26	28-Nov-26	72,065.19
B5.33 31 23.01-1..	Excavation	10.00	1	16-Sep-26	28-Sep-26	04-Nov-26	15-Nov-26	16,012.44
B5.33 31 23.01-1..	Sand Bedding	3.00	1	29-Sep-26	01-Oct-26	16-Nov-26	18-Nov-26	4,007.71
B5.33 31 23.01-1..	Pipe Laying	3.00	1	03-Oct-26	05-Oct-26	19-Nov-26	22-Nov-26	36,032.59
B5.33 31 23.01-1..	Embedment & Test	5.00	1	06-Oct-26	11-Oct-26	23-Nov-26	28-Nov-26	16,012.44
Stormwater Network		46.50	10	16-Sep-26	07-Nov-26	28-Sep-26 A	11-Nov-26	577,067.34
Box Cul.		46.50	10	16-Sep-26	07-Nov-26	28-Sep-26 A	11-Nov-26	577,067.34
B6. 33 42 13.56_R	Curing & Water Proofing(Rem)	2.50	1	16-Sep-26	19-Sep-26	28-Sep-26 A	04-Nov-26	78,207.33
B6. 33 42 13.66	Backfilling & Warrning Tape	6.00	1	19-Sep-26	27-Sep-26	21-Oct-26 A	09-Nov-26	469,243.98
Concrete Chambers		16.00	8	11-Oct-26	07-Nov-26	15-Oct-26 A	11-Nov-26	29,616.03
Size 3.0 x 3.0 m, depth 1.5 to 2.5		12.00	2	12-Oct-26	24-Oct-26	15-Oct-26 A	11-Nov-26	5,799.11
B6.33 05 63.014	Waterproofing Tanking Membrane & Protection	4.00	1	20-Oct-26	24-Oct-26	15-Oct-26 A	04-Nov-26	2,899.56
B6.33 05 63.013	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	7.00	1	12-Oct-26	19-Oct-26	28-Oct-26 A	11-Nov-26	2,899.56
Size 3.0 x 1.5 m, depth 1.5 to 2.5		6.00	2	11-Oct-26	28-Oct-26	17-Oct-26 A	09-Nov-26	4,072.19
B6.33 05 63.024	Waterproofing Tanking Membrane & Protection	4.00	1	25-Oct-26	28-Oct-26	17-Oct-26 A	04-Nov-26	2,036.10
B6.33 05 63.023	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	5.00	1	11-Oct-26	17-Oct-26	28-Oct-26 A	09-Nov-26	2,036.10
Size 2.5 x 1.5 m, depth 1.5 to 2.5		7.00	2	11-Oct-26	02-Nov-26	17-Oct-26 A	08-Nov-26	3,623.71
B6.33 05 63.034	Waterproofing Tanking Membrane & Protection	4.00	1	29-Oct-26	02-Nov-26	17-Oct-26 A	04-Nov-26	1,811.86
B6.33 05 63.033	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	4.00	1	11-Oct-26	14-Oct-26	28-Oct-26 A	08-Nov-26	1,811.86
Size 2.0 x 1.5 m, depth 2.5 to 3.5		11.00	2	11-Oct-26	07-Nov-26	18-Oct-26 A	08-Nov-26	16,121.02
B6.33 05 63.044	Waterproofing Tanking Membrane & Protection	4.00	1	03-Nov-26	07-Nov-26	18-Oct-26 A	04-Nov-26	8,060.51
B6.33 05 63.043	Cast Iron Steps Installation, Epoxy Paint & Internal Finishing	4.00	1	11-Oct-26	14-Oct-26	28-Oct-26 A	08-Nov-26	8,060.51
Potable Water Network		3.00	5	16-Sep-26	19-Sep-26	08-Oct-26 A	07-Nov-26	31,397.41
HDPE Pipes		3.00	5	16-Sep-26	19-Sep-26	08-Oct-26 A	07-Nov-26	31,397.41
?110mm		3.00	5	16-Sep-26	19-Sep-26	08-Oct-26 A	07-Nov-26	31,397.41
Depth: 0.0m - 1.5m		3.00	5	16-Sep-26	19-Sep-26	08-Oct-26 A	07-Nov-26	31,397.41
B3.33 14 13-91_R	Excavation(Rem)	3.00	1	16-Sep-26	19-Sep-26	08-Oct-26 A	07-Nov-26	6,279.37
B3.33 14 13-95_R	Sand Bedding(Rem)	3.00	1	16-Sep-26	19-Sep-26	10-Oct-26 A	07-Nov-26	1,570.13

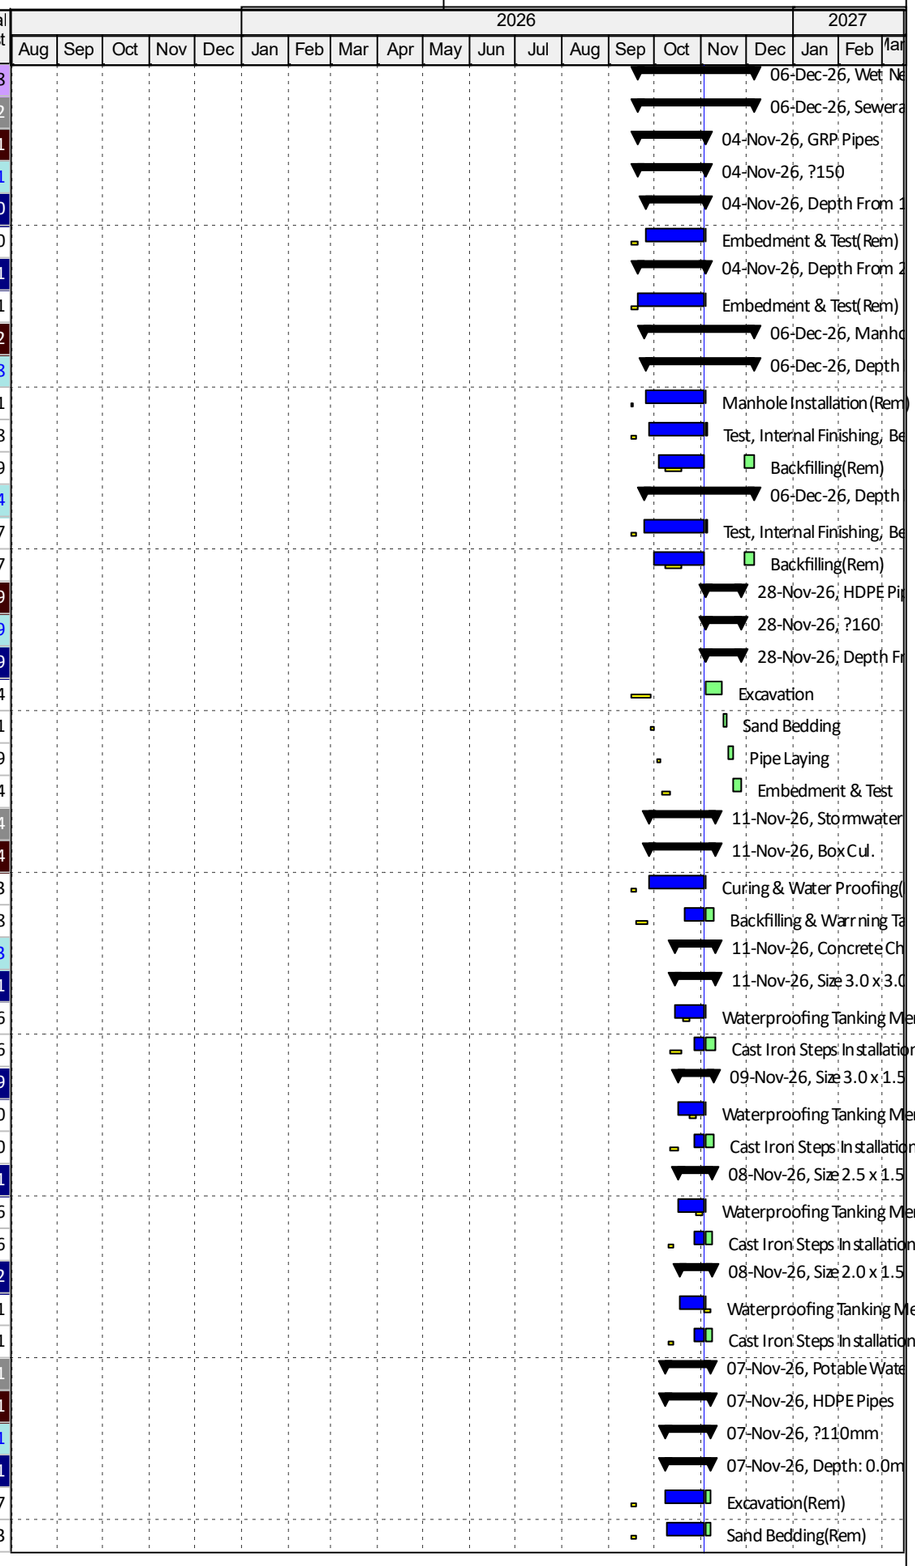


Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 14 13-99_R	Pipe Laying(Rem)	3.00	1	16-Sep-26	19-Sep-26	11-Oct-26 A	07-Nov-26	14,128.86
B3.33 14 13-103_I	Embedment & Test(Rem)	2.12	1	16-Sep-26	19-Sep-26	12-Oct-26 A	07-Nov-26	6,279.37
B3.33 14 13-107_I	Backfilling & Warrning Tape(Rem)	2.40	1	16-Sep-26	19-Sep-26	13-Oct-26 A	07-Nov-26	3,139.68
Fire Fighting Network		20.00	7	05-Oct-26	12-Nov-26	04-Nov-26	26-Nov-26	103,009.21
Valves & Chambers		20.00	4	12-Oct-26	03-Nov-26	04-Nov-26	26-Nov-26	20,932.79
Air Valves		20.00	4	12-Oct-26	03-Nov-26	04-Nov-26	26-Nov-26	20,932.79
Air valves on less than 315 mm. (In Chamber)		20.00	4	12-Oct-26	03-Nov-26	04-Nov-26	26-Nov-26	20,932.79
B3.33 05 63.02.62	Land Adjustment & Compaction	4.00	1	12-Oct-26	15-Oct-26	04-Nov-26	08-Nov-26	4,485.60
B3.33 05 63.02.60	Foundations	5.00	1	17-Oct-26	21-Oct-26	09-Nov-26	14-Nov-26	5,821.24
B3.33 05 63.02.63	Chambers Walls Conc Cast In Situ	5.00	1	22-Oct-26	27-Oct-26	15-Nov-26	19-Nov-26	5,980.80
B3.33 05 63.02.61	Chamber Curing, Finishing & Steel Cover	6.00	1	28-Oct-26	03-Nov-26	21-Nov-26	26-Nov-26	4,645.16
Fire Hydrant		14.00	3	05-Oct-26	12-Nov-26	04-Nov-26	19-Nov-26	82,076.43
B3.33 14 19.01.fh35	Riser Pipe & Flanged Fittings Installation	4.00	1	05-Oct-26	08-Oct-26	04-Nov-26	08-Nov-26	16,415.29
B3.33 14 19.01.fh34	Firehydrant Fixing/Installation	5.00	1	10-Oct-26	14-Oct-26	09-Nov-26	14-Nov-26	49,245.86
B3.33 14 19.01.fh36	Backfilling & Compaction	5.00	1	10-Nov-26	12-Nov-26	15-Nov-26	19-Nov-26	16,415.29
Dry Networks		39.68	34	16-Sep-26	29-Oct-26	10-Oct-26 A	24-Nov-26	589,528.87
Medium Voltage Network		14.00	3	05-Oct-26	20-Oct-26	04-Nov-26	19-Nov-26	38,569.64
Duct Banks		14.00	3	05-Oct-26	20-Oct-26	04-Nov-26	19-Nov-26	38,569.64
2 Way		14.00	3	05-Oct-26	20-Oct-26	04-Nov-26	19-Nov-26	38,569.64
B2.31 23 00.640	Excavation	4.00	1	05-Oct-26	08-Oct-26	04-Nov-26	08-Nov-26	8,056.11
B2.33 71 00.288	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	7.00	1	10-Oct-26	17-Oct-26	09-Nov-26	16-Nov-26	20,822.61
B2.33 71 00.289	Backfilling & Warrning Tape	3.00	1	18-Oct-26	20-Oct-26	17-Nov-26	19-Nov-26	9,690.92
Low Voltage Network		15.30	13	19-Sep-26	25-Oct-26	07-Nov-26	24-Nov-26	186,318.64
Duct Banks		14.00	11	10-Oct-26	25-Oct-26	09-Nov-26	24-Nov-26	64,762.06
2 Way		5.00	2	10-Oct-26	14-Oct-26	09-Nov-26	14-Nov-26	11,026.45
B2.33 71 00 02 112	Excavation	2.00	1	10-Oct-26	11-Oct-26	09-Nov-26	10-Nov-26	2,755.67
B2.33 71 00 02 113	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	12-Oct-26	14-Oct-26	11-Nov-26	14-Nov-26	8,270.78
4 Way		8.00	3	12-Oct-26	20-Oct-26	11-Nov-26	19-Nov-26	26,129.35
B2.33 71 00 02 115	Excavation	2.00	1	12-Oct-26	13-Oct-26	11-Nov-26	12-Nov-26	5,225.87
B2.33 71 00 02 116	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	14-Oct-26	17-Oct-26	14-Nov-26	16-Nov-26	15,677.61
B2.33 71 00 02 117	Backfilling & Warrning Tape	3.00	1	18-Oct-26	20-Oct-26	17-Nov-26	19-Nov-26	5,225.87
6 Way		8.00	3	14-Oct-26	22-Oct-26	14-Nov-26	22-Nov-26	14,223.54
B2.33 71 00 02 118	Excavation	2.00	1	14-Oct-26	15-Oct-26	14-Nov-26	15-Nov-26	2,844.71
B2.33 71 00 02 119	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	17-Oct-26	19-Oct-26	16-Nov-26	18-Nov-26	8,534.12
B2.33 71 00 02 120	Backfilling & Warrning Tape	3.00	1	20-Oct-26	22-Oct-26	19-Nov-26	22-Nov-26	2,844.71
8 Way		8.00	3	17-Oct-26	25-Oct-26	16-Nov-26	24-Nov-26	13,382.72
B2.33 71 00 02 121	Excavation	2.00	1	17-Oct-26	18-Oct-26	16-Nov-26	17-Nov-26	2,680.93
B2.33 71 00 02 122	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	3.00	1	19-Oct-26	21-Oct-26	18-Nov-26	21-Nov-26	8,035.48
B2.33 71 00 02 123	Backfilling & Warrning Tape	3.00	1	22-Oct-26	25-Oct-26	22-Nov-26	24-Nov-26	2,666.32
Cables		14.30	2	19-Sep-26	24-Oct-26	07-Nov-26	23-Nov-26	121,556.59
4C,10+1C,10mm2		2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	09-Nov-26	95,723.28
B2.33 71 00 01 12	Cable Pulling	2.00	1	19-Sep-26	20-Sep-26	07-Nov-26	09-Nov-26	95,723.28
4C,50+1C,25mm2		2.00	1	22-Oct-26	24-Oct-26	22-Nov-26	23-Nov-26	25,833.30
B2.33 71 00 01 13	Cable Pulling	2.00	1	22-Oct-26	24-Oct-26	22-Nov-26	23-Nov-26	25,833.30
Street Lighting		29.60	18	16-Sep-26	29-Oct-26	10-Oct-26 A	12-Nov-26	364,640.58
SL Poles		29.00	15	16-Sep-26	21-Oct-26	10-Oct-26 A	12-Nov-26	360,158.85

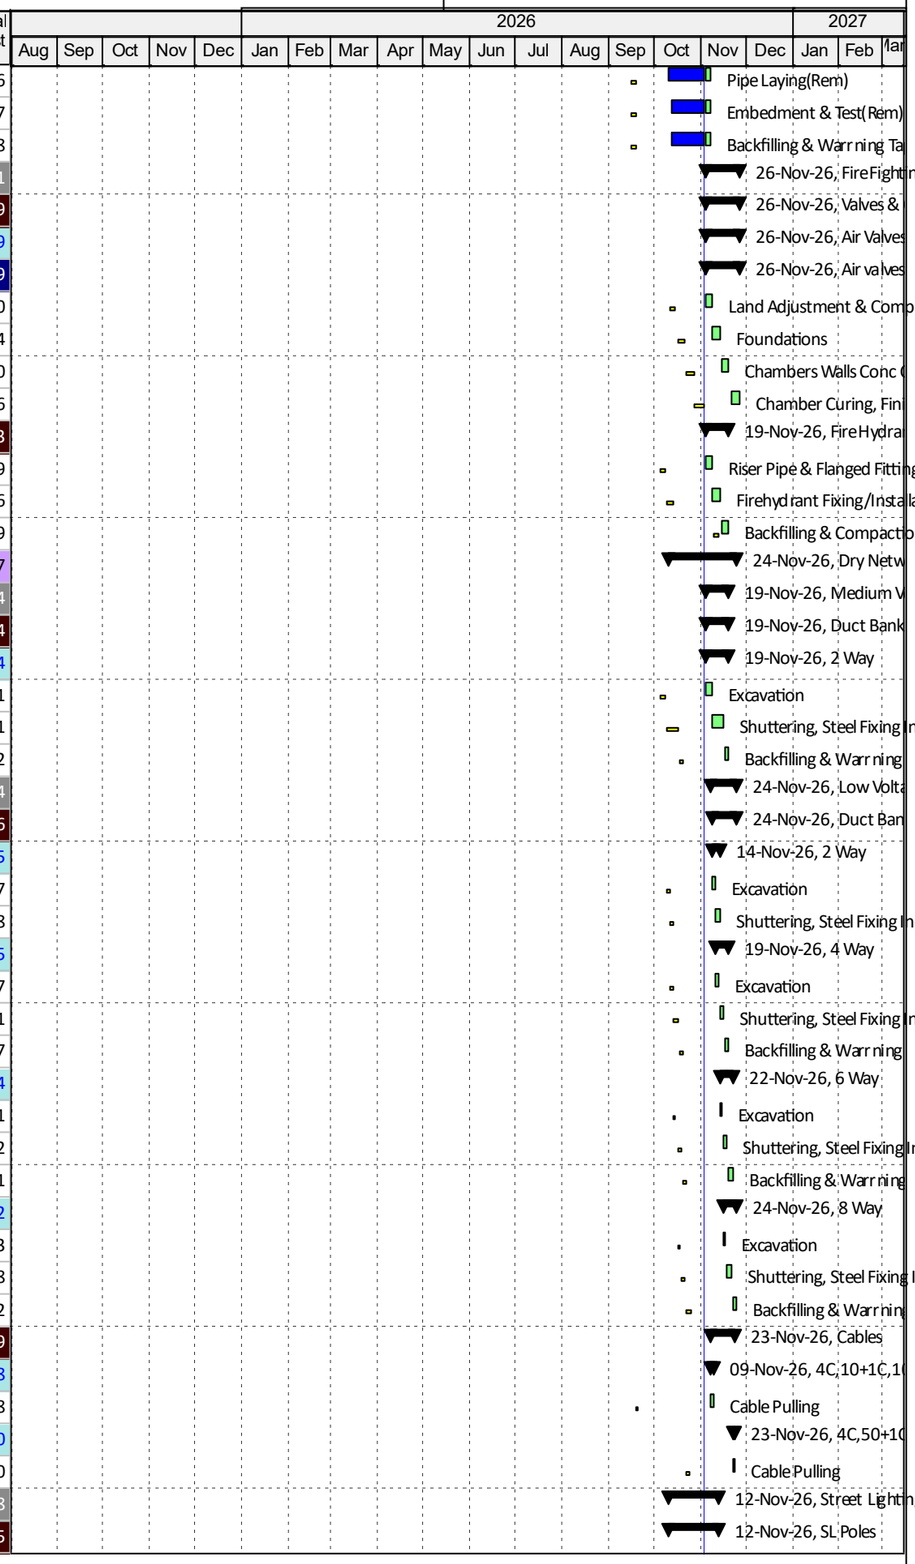

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Pole (10 M Single Arm)		14.28	5	16-Sep-26	26-Sep-26	14-Oct-26 A	05-Nov-26	147,222.93
B2.33 71 16.71_R	Excavation(Rem)	2.00	1	16-Sep-26	19-Sep-26	14-Oct-26 A	05-Nov-26	15,101.57
B2.33 71 16.72_R	PC & RC Foundation(Rem)	2.00	1	16-Sep-26	19-Sep-26	17-Oct-26 A	05-Nov-26	15,101.57
B2.33 71 16.73_R	Lighting Poles Installation Incl power box, Cables(Rem)	2.00	1	16-Sep-26	19-Sep-26	19-Oct-26 A	05-Nov-26	30,203.15
B2.33 71 16.74	Backfilling, Grouting & Chamfering	3.00	1	21-Sep-26	26-Sep-26	22-Oct-26 A	05-Nov-26	58,898.50
B2.26.56.19.11	Lighting Luminares Inst	2.00	1	19-Sep-26	21-Sep-26	29-Oct-26 A	04-Nov-26	27,918.13
Pole (10 M Double Arm)		14.76	5	01-Oct-26	08-Oct-26	10-Oct-26 A	12-Nov-26	65,368.09
B2.33 71 16.75_R	Excavation(Rem)	2.00	1	01-Oct-26	03-Oct-26	10-Oct-26 A	12-Nov-26	4,740.41
B2.33 71 16.76_R	PC & RC Foundation(Rem)	2.00	1	01-Oct-26	03-Oct-26	12-Oct-26 A	05-Nov-26	4,740.41
B2.33 71 16.77_R	Lighting Poles Installation Incl power box, Cables(Rem)	2.00	1	01-Oct-26	03-Oct-26	20-Oct-26 A	05-Nov-26	9,480.81
B2.26.56.19.12	Lighting Luminares Inst	2.00	1	04-Oct-26	05-Oct-26	29-Oct-26 A	04-Nov-26	27,918.13
B2.33 71 16.78	Backfilling, Grouting & Chamfering	3.00	1	06-Oct-26	08-Oct-26	05-Nov-26	09-Nov-26	18,488.33
Pole (12 M Single Arm)		29.00	5	14-Oct-26	21-Oct-26	10-Oct-26 A	12-Nov-26	147,567.83
B2.33 71 16.116_R	Excavation(Rem)	2.00	1	14-Oct-26	15-Oct-26	10-Oct-26 A	12-Nov-26	14,361.65
B2.33 71 16.126_R	PC & RC Foundation(Rem)	2.00	1	14-Oct-26	15-Oct-26	12-Oct-26 A	04-Nov-26	14,361.65
B2.33 71 16.136_R	Lighting Poles Installation Incl power box, Cables(Rem)	2.00	1	14-Oct-26	15-Oct-26	14-Oct-26 A	04-Nov-26	28,723.30
B2.33 71 16.146	Backfilling, Grouting & Chamfering	3.00	1	19-Oct-26	21-Oct-26	23-Oct-26 A	05-Nov-26	56,012.68
B2.26.56.19.29	Lighting Luminares Inst	2.00	1	17-Oct-26	18-Oct-26	31-Oct-26 A	04-Nov-26	34,108.54
Earthing		7.00	3	22-Oct-26	29-Oct-26	04-Nov-26	12-Nov-26	4,481.74
B2.33 71 19 38	Land Adjustment	2.00	1	22-Oct-26	24-Oct-26	04-Nov-26	07-Nov-26	904.39
B2.33 71 19 39	Earth Rods & Conduits	3.00	1	25-Oct-26	27-Oct-26	07-Nov-26	10-Nov-26	2,672.96
B2.33 71 19 40	Backfilling	2.00	1	28-Oct-26	29-Oct-26	10-Nov-26	12-Nov-26	904.39
Earth & Road Works		156.40	10	21-May-26	11-Nov-26	21-May-26 A	25-Nov-26	180,287.57
Earth Layers		139.48	2	21-May-26	21-Sep-26	21-May-26 A	05-Nov-26	65,239.56
B1.2.32 11 23.01.12	Aggregate Base Course	2.00	1	21-May-26	24-May-26	21-May-26 A	04-Nov-26	55,271.48
B1.2.32 11 13.01.12_	Subgrade(Rem)	2.00	1	16-Sep-26	21-Sep-26	04-Nov-26	05-Nov-26	9,968.09
Interlock		3.00	1	31-Oct-26	02-Nov-26	12-Nov-26	16-Nov-26	15,151.97
B1.2.32 14 13.13.12	60mm thick - Interlocking Block Pavers	3.00	1	31-Oct-26	02-Nov-26	12-Nov-26	16-Nov-26	15,151.97
Curbstone		8.00	4	03-Nov-26	11-Nov-26	16-Nov-26	25-Nov-26	36,323.95
Pre-Installation		6.00	3	03-Nov-26	09-Nov-26	16-Nov-26	23-Nov-26	24,587.66
B2.31 23 00.331	Excavation	2.00	1	03-Nov-26	04-Nov-26	16-Nov-26	18-Nov-26	8,194.59
B1.2.32 14 13.13.21	PCC	2.00	1	05-Nov-26	07-Nov-26	18-Nov-26	21-Nov-26	8,196.53
32 16 13.0012	Haunching	2.00	1	08-Nov-26	09-Nov-26	21-Nov-26	23-Nov-26	8,196.53
Installation		2.00	1	10-Nov-26	11-Nov-26	23-Nov-26	25-Nov-26	11,736.29
B1.2.32 16.13.01.12	Curb Stone, Type K1	2.00	1	10-Nov-26	11-Nov-26	23-Nov-26	25-Nov-26	11,736.29
Asphalt Layers		2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	62,277.60
B1.2.32 11 26.01.12_	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	16-Sep-26	17-Sep-26	04-Nov-26	07-Nov-26	62,277.60
Traffic Signs		2.00	2	05-Nov-26	07-Nov-26	18-Nov-26	21-Nov-26	1,294.49
Pre-Installation		2.00	2	05-Nov-26	07-Nov-26	18-Nov-26	21-Nov-26	1,294.49
B2.31 23 00.341	Excavation	1.00	1	05-Nov-26	05-Nov-26	18-Nov-26	19-Nov-26	647.25
10 14 53.012	Foundation	2.00	1	05-Nov-26	07-Nov-26	18-Nov-26	21-Nov-26	647.25
Landscape		6.00	2	01-Nov-26	07-Nov-26	14-Nov-26	21-Nov-26	51,486.90
Fences		6.00	2	01-Nov-26	07-Nov-26	14-Nov-26	21-Nov-26	51,486.90
Steel fence (ZATCA HCIS)		6.00	2	01-Nov-26	07-Nov-26	14-Nov-26	21-Nov-26	51,486.90
B7.32 31 26.01-1_R	Earthwork(Rem)	5.00	1	01-Nov-26	05-Nov-26	14-Nov-26	19-Nov-26	25,743.45
B7.32 31 26.01-3_R	Foundation(Rem)	6.00	1	01-Nov-26	07-Nov-26	14-Nov-26	21-Nov-26	25,743.45

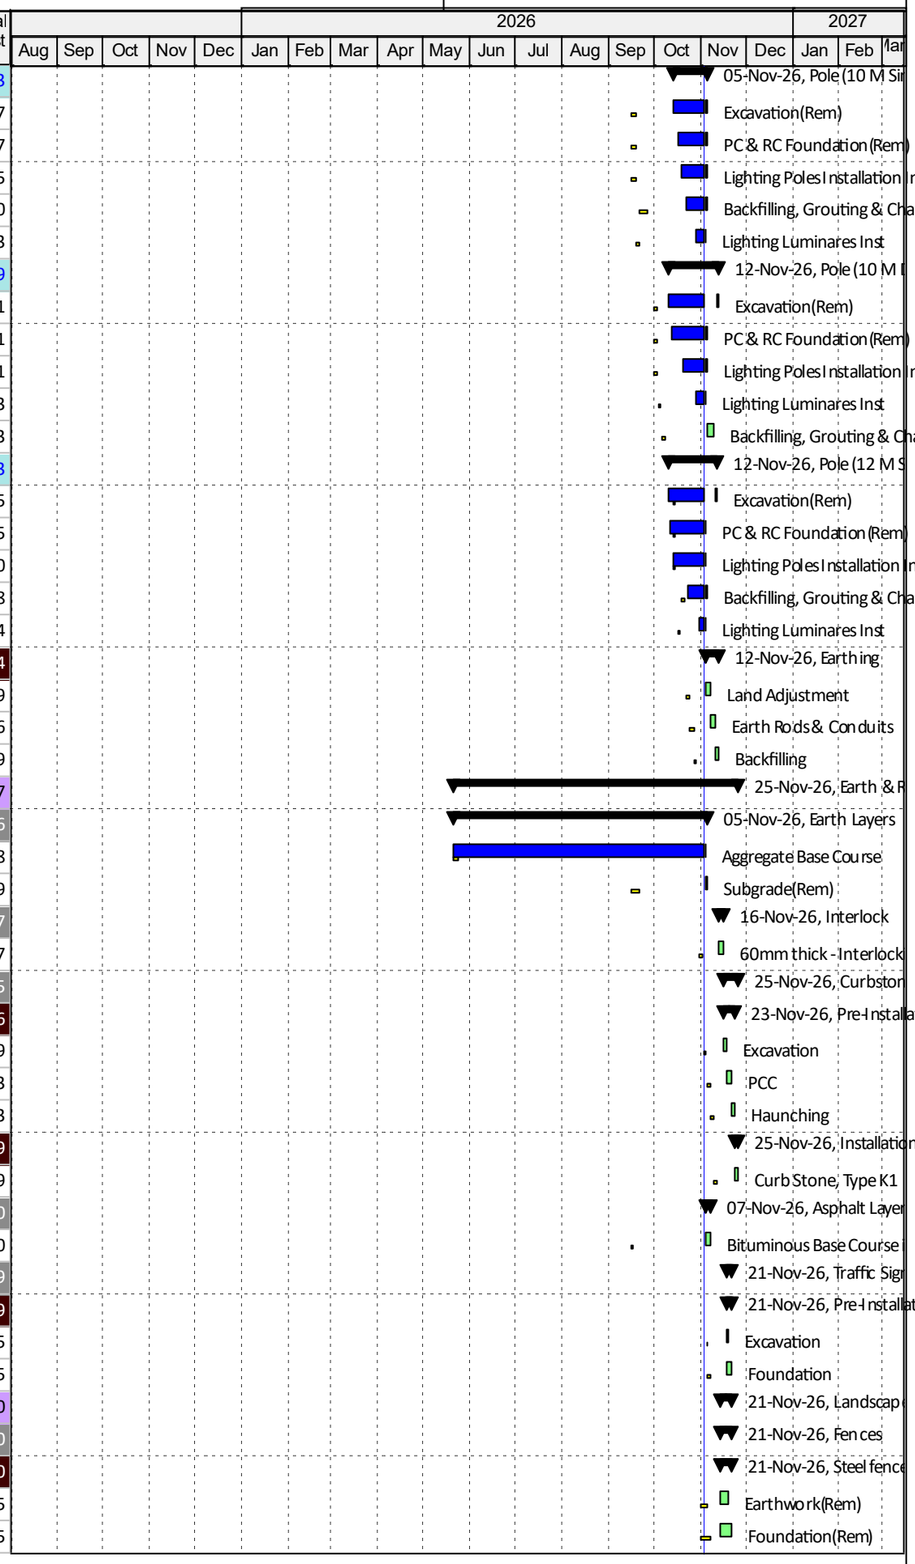


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Sewerage Lift Station		30.00	38	16-Sep-26	29-Oct-26	12-Oct-26 A	25-Nov-26	1,233,346.26
Underground Concrete Structures & Waterproofing		4.00	2	29-Sep-26	03-Oct-26	12-Oct-26 A	04-Nov-26	31,279.29
B5.1.31 23 16.01.15	Water proofing Membrane with protection board	2.00	1	29-Sep-26	30-Sep-26	12-Oct-26 A	04-Nov-26	28,830.37
B5.1.31 23 16.01.21	Backfilling around underground chambers	2.00	1	01-Oct-26	03-Oct-26	15-Oct-26 A	04-Nov-26	2,448.92
Superstructure - Control Room & Roof Slabs		10.00	3	22-Sep-26	04-Oct-26	04-Nov-26	15-Nov-26	17,892.66
B5.1.31 23 16.01.17	Reinforced Concrete Columns	3.00	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	2,317.92
B5.1.31 23 16.01.23	Concrete masonry unit (200mm) walls	3.00	1	27-Sep-26	29-Sep-26	08-Nov-26	10-Nov-26	3,834.41
B5.1.31 23 16.01.27	Roof Slab for wet well & Chambers	4.00	1	30-Sep-26	04-Oct-26	11-Nov-26	15-Nov-26	11,740.34
Waterproofing, Roofing & External Enclosure		13.00	4	30-Sep-26	14-Oct-26	11-Nov-26	25-Nov-26	2,993.01
B5.1.31 23 16.01.29	External plastering	4.00	1	30-Sep-26	04-Oct-26	11-Nov-26	15-Nov-26	2,141.28
B5.1.31 23 16.01.39	Water proofing Membrane for roof	3.00	1	05-Oct-26	07-Oct-26	16-Nov-26	18-Nov-26	733.20
B5.1.31 23 16.01.55	Vapor retarders for roof	3.00	1	08-Oct-26	11-Oct-26	19-Nov-26	22-Nov-26	55.35
B5.1.31 23 16.01.71	Geotextile membrane	3.00	1	12-Oct-26	14-Oct-26	23-Nov-26	25-Nov-26	63.18
Internal Chamber Works (Wet Well, Valve, Screening)		13.00	6	04-Oct-26	18-Oct-26	05-Nov-26	19-Nov-26	41,832.00
B5.1.31 23 16.01.31	Sloped screed for internal floors for wet well and valve chamber	2.00	1	04-Oct-26	05-Oct-26	05-Nov-26	07-Nov-26	318.67
B5.1.31 23 16.01.41	Sloped screed for internal floors for Screening chamber	3.00	1	06-Oct-26	08-Oct-26	08-Nov-26	10-Nov-26	115.88
B5.1.31 23 16.01.43	Epoxy paint for internal side and floors for wet well and valve chamber	2.00	1	06-Oct-26	07-Oct-26	08-Nov-26	09-Nov-26	4,481.77
B5.1.31 23 16.01.57	Epoxy paint for internal side and floors for Screening chamber	3.00	1	10-Oct-26	12-Oct-26	11-Nov-26	14-Nov-26	2,750.85
B5.1.31 23 16.01.73	Stainless steel A3 6 ladders for screening chamber for screening chamber,	3.00	1	13-Oct-26	15-Oct-26	15-Nov-26	17-Nov-26	18,775.21
B5.1.31 23 16.01.91	Stainless steel A3 6 covers	2.00	1	17-Oct-26	18-Oct-26	18-Nov-26	19-Nov-26	15,389.62
Control Room Internal Finishes		13.00	4	27-Sep-26	14-Oct-26	08-Nov-26	22-Nov-26	3,498.74
B5.1.31 23 16.01.19	Vapor retarders below slab on grade	2.00	1	27-Sep-26	28-Sep-26	08-Nov-26	09-Nov-26	55.35
B5.1.31 23 16.01.25	Water proofing Paint below slab on grade	3.00	1	29-Sep-26	01-Oct-26	10-Nov-26	12-Nov-26	521.55
B5.1.31 23 16.01.45	Internal plastering	3.00	1	08-Oct-26	11-Oct-26	16-Nov-26	18-Nov-26	1,251.33
B5.1.31 23 16.01.59	Internal painting (Acrylic)	3.00	1	12-Oct-26	14-Oct-26	19-Nov-26	22-Nov-26	1,670.51
Mechanical & Process Equipment Installation		18.00	7	05-Oct-26	25-Oct-26	05-Nov-26		662,902.24
B5.1.31 23 16.01.33	Buried ductile iron pipes installation	3.00	1	13-Oct-26	15-Oct-26	05-Nov-26	08-Nov-26	13,806.50
B5.1.31 23 16.01.49	Double flanged ductile iron pipe installation	2.00	1	17-Oct-26	18-Oct-26	09-Nov-26	10-Nov-26	8,283.90
B5.1.31 23 16.01.47	JIB Crane installation	3.00	1	05-Oct-26	07-Oct-26	16-Nov-26	18-Nov-26	98,511.60
B5.1.31 23 16.01.63	Submersible - wet installed pump installation	3.00	1	19-Oct-26	21-Oct-26	19-Nov-26	22-Nov-26	331,462.56
B5.1.31 23 16.01.65	Manually operated Gate Valve DN150 installation	2.00	1	19-Oct-26	20-Oct-26	19-Nov-26	21-Nov-26	7,694.82
B5.1.31 23 16.01.77	Non-return Valve DN150 installation	2.00	1	21-Oct-26	22-Oct-26	22-Nov-26	23-Nov-26	8,901.16
B5.1.31 23 16.01.79	Basket screens	3.00	1	22-Oct-26	25-Oct-26	23-Nov-26	25-Nov-26	194,241.70
Electrical & Control Systems		18.00	7	16-Sep-26	29-Oct-26	04-Nov-26	24-Nov-26	341,739.74
B5.1.31 23 16.01.5	Grounding and lightning system	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	15,605.61
B5.1.31 23 16.01.35	4Cx 95mm2 Cable from SEC/Generator to ATS and MCC-SPS	3.00	1	04-Oct-26	06-Oct-26	08-Nov-26	10-Nov-26	7,616.75
B5.1.31 23 16.01.51	Standby Diesel Generator Set installation	3.00	1	22-Oct-26	25-Oct-26	11-Nov-26	14-Nov-26	206,990.26
B5.1.31 23 16.01.67	2.084m3 capacity underground fuel tank installation	2.00	1	26-Oct-26	27-Oct-26	15-Nov-26	16-Nov-26	20,861.33
B5.1. 26 32 12 .05	Positive displacement rotary type pump installation	3.00	1	15-Oct-26	18-Oct-26	16-Nov-26	18-Nov-26	12,864.46
B5.1.31 23 16.01.83	Manually operated fuel pump installation	2.00	1	28-Oct-26	29-Oct-26	17-Nov-26	18-Nov-26	4,844.80
B5.1.31 23 16.01.81	MCC - 160AT/250AF, 400V, 3PH, 60HZ	2.00	1	15-Oct-26	17-Oct-26	23-Nov-26	24-Nov-26	72,956.53
External Works & Site Finishing		12.00	5	04-Oct-26	17-Oct-26	05-Nov-26	18-Nov-26	131,208.56
B5.1.31 23 16.01.37	Precast Concrete curbstone - Type K1	3.00	1	04-Oct-26	06-Oct-26	05-Nov-26	08-Nov-26	11,941.91
B5.1.31 23 16.01.53	Electrical Hand Hole (EHH-1) 600mm x 600mm x 800mm	3.00	1	07-Oct-26	10-Oct-26	09-Nov-26	11-Nov-26	33,609.94
B5.1.31 23 16.01.69	Precast Concrete curbstone - Type K4	2.00	1	11-Oct-26	12-Oct-26	12-Nov-26	14-Nov-26	5,645.90
B5.1.31 23 16.01.87	Electrical Hand Hole (EHH-2) 400mm x 400mm x 600mm	2.00	1	13-Oct-26	14-Oct-26	15-Nov-26	16-Nov-26	14,602.93

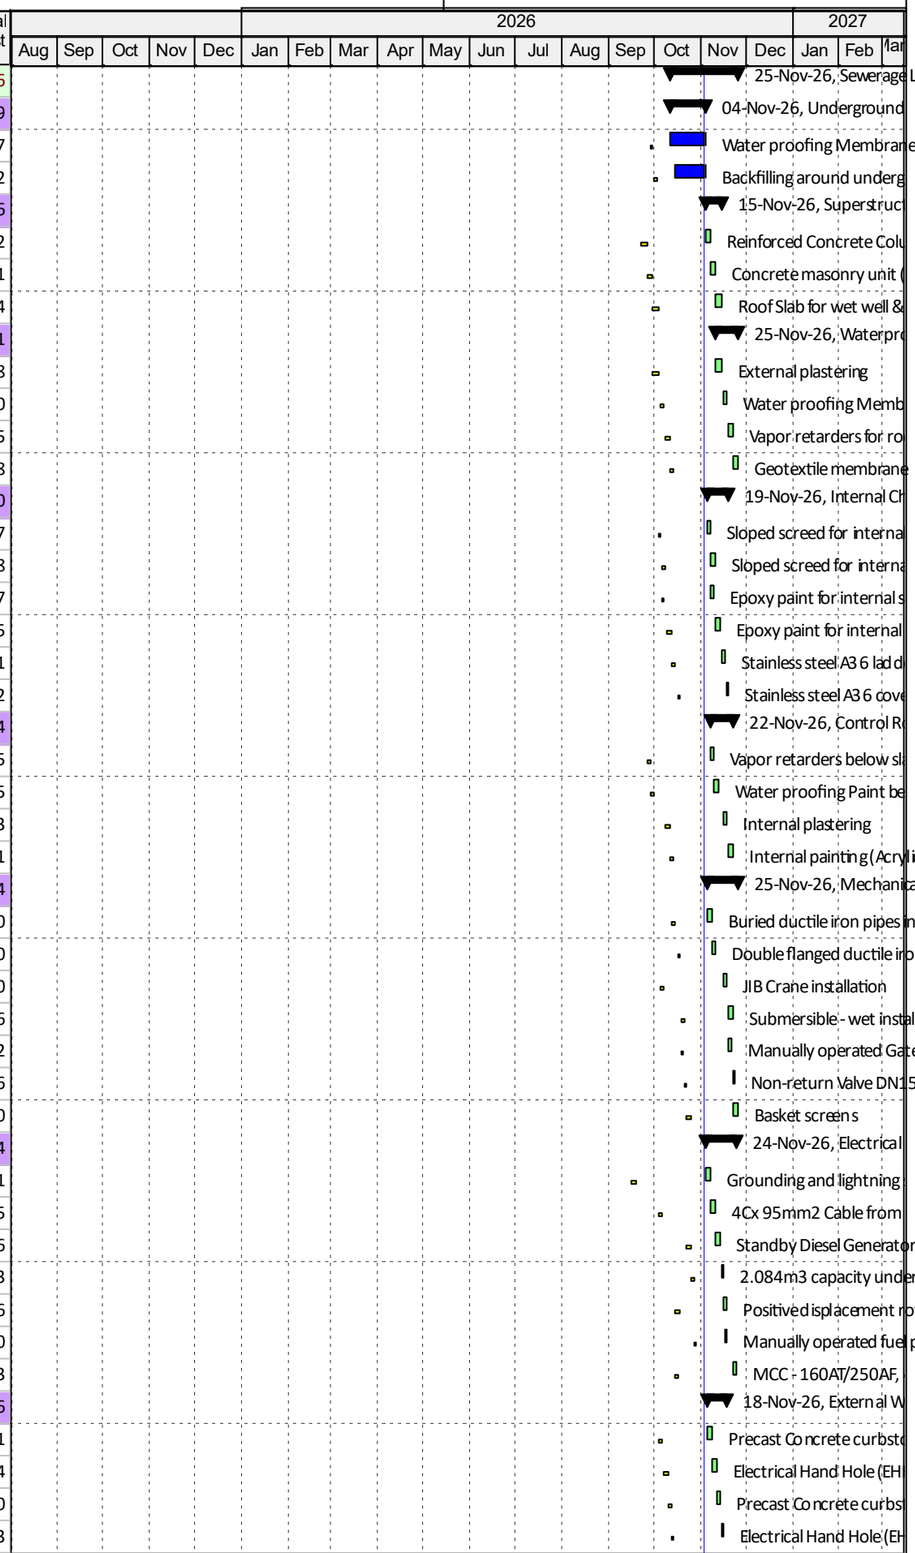


Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B5.1.31 23 16.01.85	Steel fence (ZATCA HCIS) including Steel gate size (7*2.7)m	2.00	1	15-Oct-26	17-Oct-26	17-Nov-26	18-Nov-26	65,407.89
Zone 04		65.34	154	16-Sep-26	16-Nov-26	06-Sep-26 A	03-Dec-26	9,292,382.96
Road 02		61.00	87	16-Sep-26	16-Nov-26	19-Sep-26 A	26-Nov-26	8,257,131.90
Wet Networks		61.00	41	16-Sep-26	16-Nov-26	19-Sep-26 A	26-Nov-26	220,768.39
Sewerage Network		8.71	5	16-Sep-26	27-Sep-26	19-Sep-26 A	05-Nov-26	23,091.04
Manholes ?1200		8.71	5	16-Sep-26	27-Sep-26	19-Sep-26 A	05-Nov-26	23,091.04
Depth From 0.0m to 1.5m		2.18	1	20-Sep-26	22-Sep-26	20-Sep-26 A	05-Nov-26	1,313.67
B6.33 05 39.01.14(	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	20-Sep-26	22-Sep-26	20-Sep-26 A	05-Nov-26	1,313.67
Depth From 1.5m to 2.5m		2.18	1	16-Sep-26	19-Sep-26	26-Sep-26 A	05-Nov-26	3,809.64
B6.33 05 39.01.14[	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	16-Sep-26	19-Sep-26	26-Sep-26 A	05-Nov-26	3,809.64
Depth From 2.5m to 3.5m		2.18	1	19-Sep-26	21-Sep-26	19-Sep-26 A	05-Nov-26	4,595.57
B6.33 05 39.01.15(	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	19-Sep-26	21-Sep-26	19-Sep-26 A	05-Nov-26	4,595.57
Depth From 3.5m to 4.5m		4.35	2	21-Sep-26	27-Sep-26	21-Sep-26 A	05-Nov-26	13,372.16
B6.33 05 39.01.15[	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	21-Sep-26	24-Sep-26	21-Sep-26 A	05-Nov-26	11,243.33
Depth From 3.5m to 4.5m Backdrop		2.18	1	24-Sep-26	27-Sep-26	24-Sep-26 A	05-Nov-26	2,128.83
B6.33 05 39.01.16	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	24-Sep-26	27-Sep-26	24-Sep-26 A	05-Nov-26	2,128.83
Potable Water Network		20.00	3	20-Sep-26	12-Oct-26	04-Nov-26	26-Nov-26	1,343.34
Plots and Buildings Crossing		20.00	3	20-Sep-26	12-Oct-26	04-Nov-26	26-Nov-26	1,343.34
B3.33 14 13.02.25	Earthwork	7.00	1	20-Sep-26	28-Sep-26	04-Nov-26	11-Nov-26	268.67
B3.33 14 13.02.26	Sand Bedding	5.00	1	29-Sep-26	04-Oct-26	12-Nov-26	17-Nov-26	268.67
B3.33 14 13.02.27	Tee, Pipe (Crossing) Installation & Backfilling	7.00	1	05-Oct-26	12-Oct-26	19-Nov-26	26-Nov-26	806.01
Fire Fighting Network		27.50	13	16-Sep-26	24-Oct-26	01-Oct-26 A	11-Nov-26	137,522.12
Valves & Chambers		27.50	10	16-Sep-26	24-Oct-26	01-Oct-26 A	07-Nov-26	56,266.45
Gate Valves		4.00	1	16-Sep-26	20-Sep-26	06-Oct-26 A	05-Nov-26	5,017.11
Gate valves dia (250) mm		4.00	1	16-Sep-26	20-Sep-26	06-Oct-26 A	05-Nov-26	5,017.11
B3.33 14 19.01.13	Spindle & Surface Box	4.00	1	16-Sep-26	20-Sep-26	06-Oct-26 A	05-Nov-26	5,017.11
Air Valves		26.00	5	24-Sep-26	24-Oct-26	01-Oct-26 A	07-Nov-26	30,277.78
Air valves on less than 315 mm. (In Chamber)		26.00	5	24-Sep-26	24-Oct-26	01-Oct-26 A	07-Nov-26	30,277.78
B3.33 05 63.02.72	Land Adjustment & Compaction	4.00	1	24-Sep-26	28-Sep-26	01-Oct-26 A	05-Nov-26	4,485.60
B3.33 05 63.02.70	Foundations	5.00	1	29-Sep-26	04-Oct-26	04-Oct-26 A	07-Nov-26	5,821.24
B3.33 05 63.02.73	Chambers Walls Conc Cast In Situ	5.00	1	05-Oct-26	10-Oct-26	07-Oct-26 A	07-Nov-26	5,980.80
B3.33 05 63.02.71	Chamber Curing, Finishing & Steel Cover	6.00	1	11-Oct-26	17-Oct-26	10-Oct-26 A	07-Nov-26	4,645.16
B3.33 05 63.02.74	Valve & Fitting Installation	6.00	1	18-Oct-26	24-Oct-26	12-Oct-26 A	07-Nov-26	9,344.99
Washout Valves		27.50	4	16-Sep-26	24-Oct-26	06-Oct-26 A	07-Nov-26	20,971.56
Washout valves on 110-400 mm. (In Chamber)		27.50	4	16-Sep-26	24-Oct-26	06-Oct-26 A	07-Nov-26	20,971.56
B3.33 05 63.01.55	Foundations(Rem)	3.50	1	16-Sep-26	20-Sep-26	06-Oct-26 A	05-Nov-26	4,824.68
B3.33 05 63.01.56	Chamber Curing, Finishing & Steel Cover(Rem)	4.00	1	16-Sep-26	20-Sep-26	08-Oct-26 A	05-Nov-26	3,810.94
B3.33 05 63.01.58	Chambers Walls Conc Cast In Situ(Rem)	3.50	1	16-Sep-26	20-Sep-26	11-Oct-26 A	05-Nov-26	4,935.31
B3.33 05 63.01.59	Valve & Fitting Installation(Rem)	4.00	1	20-Oct-26	24-Oct-26	13-Oct-26 A	07-Nov-26	7,400.63
Fire Hydrant		6.95	3	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	81,255.66
B3.33 14 19.01.fh40_I	Firehydrant Fixing/Installation(Rem)	4.97	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	48,753.40
B3.33 14 19.01.fh41_I	Riser Pipe & Flanged Fittings Installation(Rem)	3.98	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	16,251.13
B3.33 14 19.01.fh42_I	Backfilling & Compaction(Rem)	6.95	1	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	16,251.13
TSE Network		19.00	20	16-Sep-26	16-Nov-26	04-Nov-26	25-Nov-26	58,811.90
HDPE Pipes		4.20	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,596.28
?110mm		4.20	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,596.28

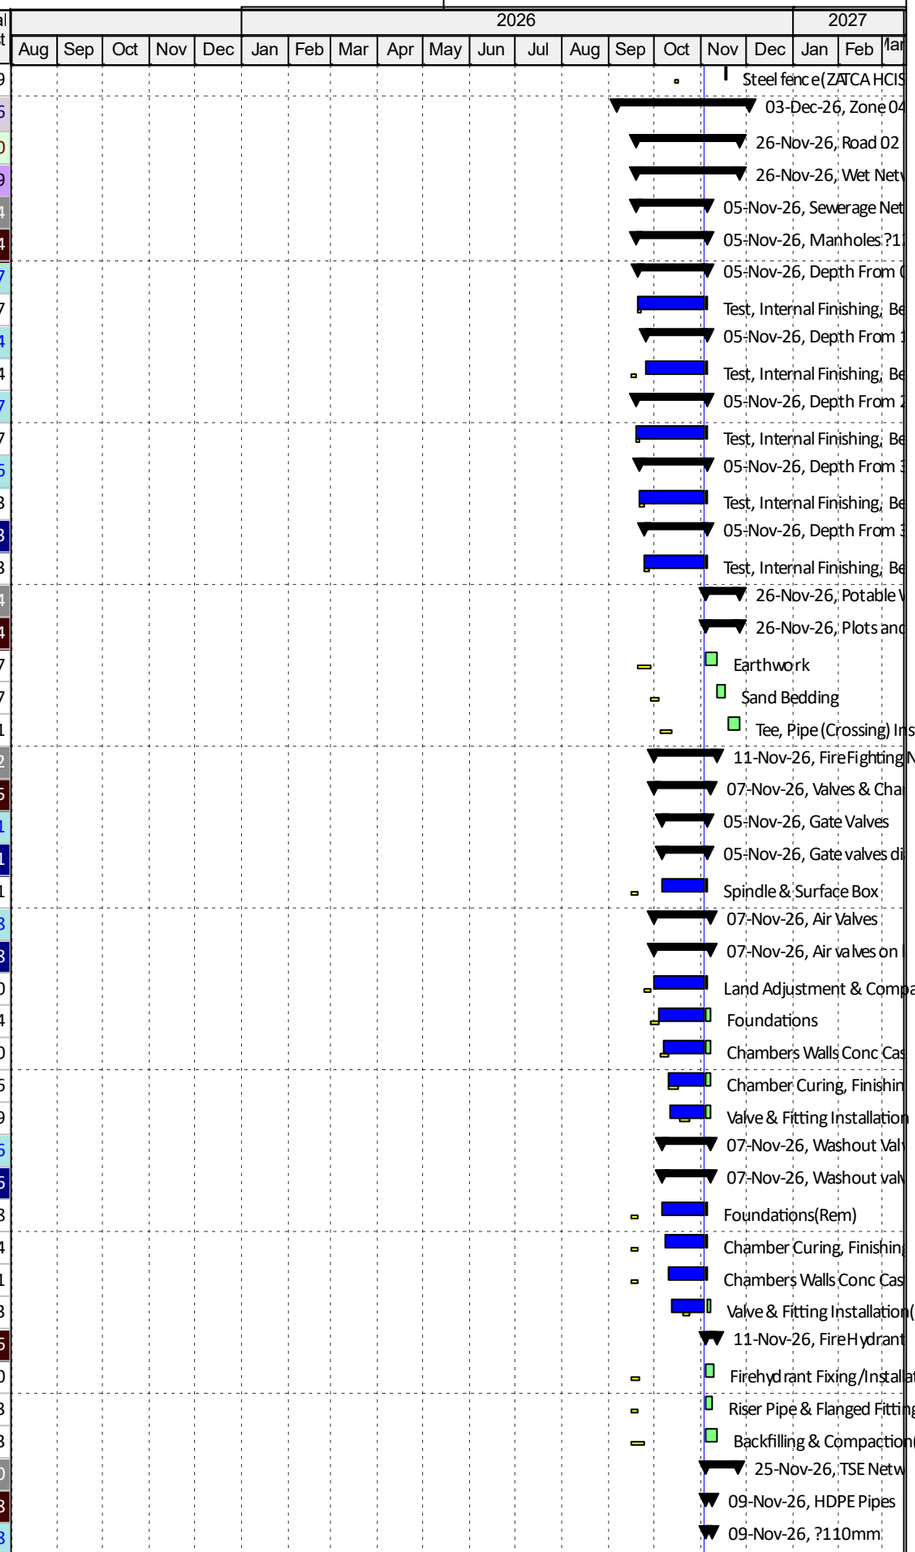

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Depth: 0.0m - 1.5m		4.20	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,596.28
B4.33 14 13.01-01	Embedment & Test(Rem)	4.20	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	9,596.28
Valves & Chambers		19.00	19	16-Sep-26	16-Nov-26	04-Nov-26	25-Nov-26	49,215.62
Gate Valves		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
Gate valves dia (250) mm		3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
B3.33 14 19.01.14	Spindle & Surface Box	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	5,565.35
Air Valves		16.00	4	06-Oct-26	24-Oct-26	04-Nov-26	22-Nov-26	1,462.08
Air valves on less than 315 mm. (In Chamber)		16.00	4	06-Oct-26	24-Oct-26	04-Nov-26	22-Nov-26	1,462.08
B3.33 05 63.02.97	Land Adjustment & Compaction	3.00	1	06-Oct-26	08-Oct-26	04-Nov-26	07-Nov-26	395.16
B3.33 05 63.02.95	Foundations	4.00	1	10-Oct-26	13-Oct-26	08-Nov-26	11-Nov-26	276.61
B3.33 05 63.02.98	Chambers Walls Conc Cast In Situ	4.00	1	14-Oct-26	18-Oct-26	12-Nov-26	16-Nov-26	276.61
B3.33 05 63.02.96	Chamber Curing, Finishing & Steel Cover	5.00	1	19-Oct-26	24-Oct-26	17-Nov-26	22-Nov-26	513.71
Washout Valves		16.00	4	10-Oct-26	27-Oct-26	08-Nov-26	25-Nov-26	2,036.02
Washout valves on 110-400 mm. (In Chamber)		16.00	4	10-Oct-26	27-Oct-26	08-Nov-26	25-Nov-26	2,036.02
B3.33 05 63.01.72	Land Adjustment & Compaction	3.00	1	10-Oct-26	12-Oct-26	08-Nov-26	10-Nov-26	550.28
B3.33 05 63.01.70	Foundations	4.00	1	13-Oct-26	17-Oct-26	11-Nov-26	15-Nov-26	385.19
B3.33 05 63.01.73	Chambers Walls Conc Cast In Situ	4.00	1	18-Oct-26	21-Oct-26	16-Nov-26	19-Nov-26	385.19
B3.33 05 63.01.71	Chamber Curing, Finishing & Steel Cover	5.00	1	22-Oct-26	27-Oct-26	21-Nov-26	25-Nov-26	715.36
Solenoid valves		13.65	10	05-Nov-26	16-Nov-26	04-Nov-26	21-Nov-26	40,152.17
1 Solenoid valve ?1.0 inch with box		13.65	4	05-Nov-26	14-Nov-26	04-Nov-26	21-Nov-26	12,310.76
B4.32 84 13.49	Pull Box Installation	3.00	1	10-Nov-26	12-Nov-26	04-Nov-26	08-Nov-26	1,848.31
B4.32 84 13.13	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	05-Nov-26	08-Nov-26	07-Nov-26	10-Nov-26	4,917.51
B4.32 84 13.14	Solenoid Valve Box Installation	3.00	1	08-Nov-26	10-Nov-26	14-Nov-26	17-Nov-26	2,838.80
B4.32 84 13.15	Bubblers Installation	3.00	1	11-Nov-26	14-Nov-26	17-Nov-26	21-Nov-26	2,706.13
1 Solenoid valve ?1.5 inch with box		10.65	3	09-Nov-26	15-Nov-26	04-Nov-26	17-Nov-26	15,199.87
B4.32 84 13.50	Pull Box Installation	3.00	1	10-Nov-26	12-Nov-26	04-Nov-26	08-Nov-26	1,848.31
B4.32 84 13.16	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	09-Nov-26	11-Nov-26	10-Nov-26	14-Nov-26	4,917.51
B4.32 84 13.17	Solenoid Valve Box Installation	3.00	1	12-Nov-26	15-Nov-26	14-Nov-26	17-Nov-26	8,434.05
1 Solenoid valve ?2.0 inch with box		7.65	3	12-Nov-26	16-Nov-26	08-Nov-26	17-Nov-26	12,641.53
B4.32 84 13.51	Pull Box Installation	3.00	1	14-Nov-26	16-Nov-26	08-Nov-26	11-Nov-26	1,848.31
B4.32 84 13.10	Cable Laying Two-Wire Decoder (12 AWG)	3.00	1	12-Nov-26	15-Nov-26	14-Nov-26	17-Nov-26	4,917.51
B4.32 84 13.03	Solenoid Valve Box Installation	3.00	1	12-Nov-26	15-Nov-26	14-Nov-26	17-Nov-26	5,875.71
Dry Networks		32.00	25	16-Sep-26	26-Oct-26	30-Sep-26 A	19-Nov-26	732,134.70
Medium Voltage Network		28.00	5	16-Sep-26	19-Oct-26	30-Sep-26 A	11-Nov-26	283,147.86
Duct Banks		14.00	2	04-Oct-26	19-Oct-26	30-Sep-26 A	04-Nov-26	38,150.07
2 Way		14.00	2	04-Oct-26	19-Oct-26	30-Sep-26 A	04-Nov-26	38,150.07
B2.33 71 00.292	Shuttering, Steel Fixing Incl. UPVC Pipe & Conc. Cast	7.00	1	04-Oct-26	11-Oct-26	30-Sep-26 A	04-Nov-26	30,093.96
B2.33 71 00.293	Backfilling & Warning Tape	7.00	1	12-Oct-26	19-Oct-26	01-Oct-26 A	04-Nov-26	8,056.11
Cables		24.28	3	16-Sep-26	28-Sep-26	07-Oct-26 A	11-Nov-26	244,997.79
3C,500mm2		24.28	3	16-Sep-26	28-Sep-26	07-Oct-26 A	11-Nov-26	244,997.79
B2.33 71 49.23.89	Cable 13.8 kV Unarmored	4.00	1	16-Sep-26	20-Sep-26	07-Oct-26 A	04-Nov-26	234,058.34
B2.33 71 49.23.90	Straight joints cables	3.00	1	21-Sep-26	24-Sep-26	04-Nov-26	08-Nov-26	7,880.95
B2.33 71 49.23.91	Cable Termination	3.00	1	26-Sep-26	28-Sep-26	08-Nov-26	11-Nov-26	3,058.50
Low Voltage Network		2.00	2	18-Oct-26	19-Oct-26	17-Oct-26 A	05-Nov-26	121,556.59
Cables		2.00	2	18-Oct-26	19-Oct-26	17-Oct-26 A	05-Nov-26	121,556.59
4C,10+1C,10mm2		2.00	1	18-Oct-26	19-Oct-26	17-Oct-26 A	05-Nov-26	95,723.28

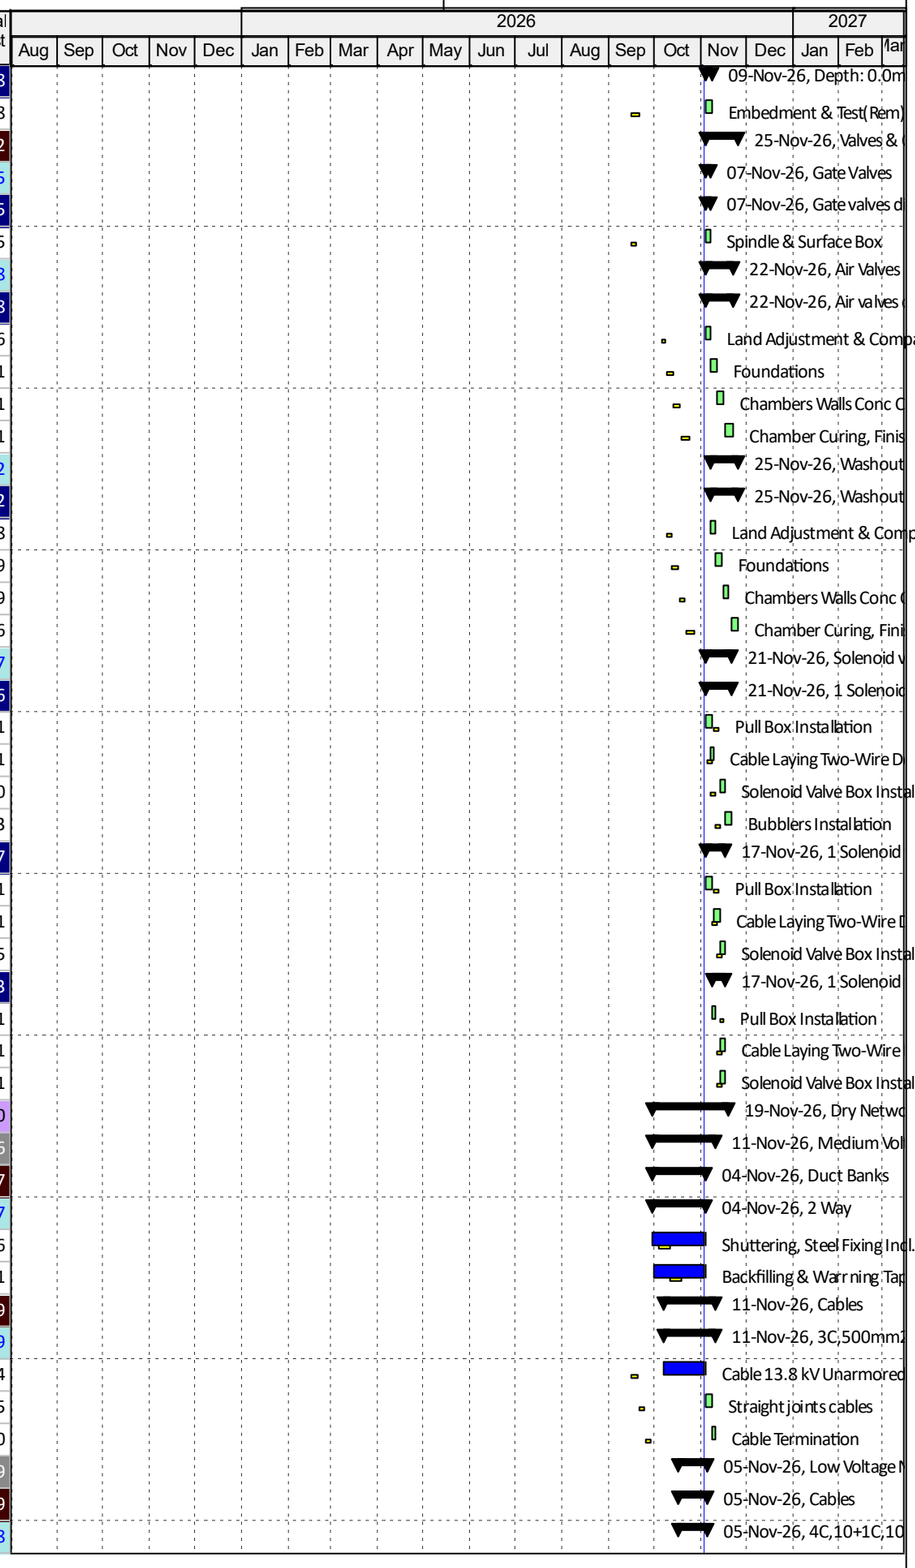


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B2.33 71 00 01 19	Cable Pulling	2.00	1	18-Oct-26	19-Oct-26	17-Oct-26 A	05-Nov-26	95,723.28
4C,50+1C,25mm2		2.00	1	18-Oct-26	19-Oct-26	18-Oct-26 A	05-Nov-26	25,833.30
B2.33 71 00 01 20	Cable Pulling	2.00	1	18-Oct-26	19-Oct-26	18-Oct-26 A	05-Nov-26	25,833.30
Street Lighting		26.00	12	24-Sep-26	26-Oct-26	20-Oct-26 A	19-Nov-26	307,541.01
Drawpits		6.00	3	01-Oct-26	07-Oct-26	04-Nov-26	10-Nov-26	71,922.87
B2.33 71 00 02 82	Excavation	2.00	1	01-Oct-26	03-Oct-26	04-Nov-26	05-Nov-26	14,384.57
B2.33 71 00 02 83	Drawpits Installation	2.00	1	04-Oct-26	05-Oct-26	07-Nov-26	08-Nov-26	43,153.72
B2.33 71 00 02 84	Backfilling & Warning Tape	2.00	1	06-Oct-26	07-Oct-26	09-Nov-26	10-Nov-26	14,384.57
Cables		6.00	3	18-Oct-26	24-Oct-26	11-Nov-26	17-Nov-26	129,818.89
4C,10+1C,10mm2		6.00	3	18-Oct-26	24-Oct-26	11-Nov-26	17-Nov-26	129,818.89
B2.33 71 19 202	Land Adjustment	2.00	1	18-Oct-26	19-Oct-26	11-Nov-26	12-Nov-26	25,963.96
B2.33 71 49.23.182	Cable Pulling	2.00	1	20-Oct-26	21-Oct-26	14-Nov-26	15-Nov-26	77,890.96
B2.33 71 19 212	Backfilling	2.00	1		24-Oct-26	16-Nov-26	17-Nov-26	25,963.96
SL Poles		2.00	1	24-Sep-26	26-Sep-26	20-Oct-26 A	04-Nov-26	58,898.50
Pole (10 M Single Arm)		2.00	1	24-Sep-26	26-Sep-26	20-Oct-26 A	04-Nov-26	58,898.50
B2.33 71 16.94	Backfilling, Grouting & Chamfering	2.00	1	24-Sep-26	26-Sep-26	20-Oct-26 A	04-Nov-26	58,898.50
SL Pillars		4.00	2	22-Oct-26	26-Oct-26	16-Nov-26	19-Nov-26	42,419.01
B2.33 71 26 034	Pillars Installation (Internal Wiring)	2.00	1	22-Oct-26	24-Oct-26	16-Nov-26	17-Nov-26	16,342.35
B2.33 71 26 045	KWH meter mounting aframe installation	2.00	1	25-Oct-26	26-Oct-26	18-Nov-26	19-Nov-26	26,076.67
Earthing		6.00	3	29-Sep-26	05-Oct-26	04-Nov-26	10-Nov-26	4,481.74
B2.33 71 19 44	Land Adjustment	2.00	1	29-Sep-26	30-Sep-26	04-Nov-26	05-Nov-26	904.39
B2.33 71 19 45	Earth Rods& Conduits	2.00	1	01-Oct-26	03-Oct-26	07-Nov-26	08-Nov-26	2,672.96
B2.33 71 19 46	Backfilling	2.00	1	04-Oct-26	05-Oct-26	09-Nov-26	10-Nov-26	904.39
Telecommunication Network		2.00	6	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	19,889.25
Manholes		2.00	6	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	19,889.25
Manhole Type 1		2.00	3	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	14,464.55
B2.31 23 00.630_R	Excavation(Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	2,892.91
B2.33 71 00.268_R	Manhole Installation (Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	8,678.73
B2.33 71 00.269_R	Backfilling & Warning Tape(Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	2,892.91
Manhole Type 2		2.00	3	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	5,424.69
B2.31 23 00.631_R	Excavation(Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	1,084.94
B2.33 71 00.270_R	Manhole Installation (Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	3,254.82
B2.33 71 00.271_R	Backfilling & Warning Tape(Rem)	2.00	1	08-Oct-26	10-Oct-26	04-Nov-26	05-Nov-26	1,084.94
Earth & Road Works		37.00	17	16-Sep-26	08-Nov-26	14-Oct-26 A	25-Nov-26	7,040,228.95
Earth Layers		3.50	2	16-Sep-26	04-Oct-26	14-Oct-26 A	05-Nov-26	709,680.56
B1.2.32 11 13.01.15_	Subgrade(Rem)	2.80	1	16-Sep-26	21-Sep-26	14-Oct-26 A	04-Nov-26	188,087.18
B1.2.32 11 23.01.15_	Aggregate Base Course(Rem)	3.50	1	22-Sep-26	04-Oct-26	14-Oct-26 A	05-Nov-26	521,593.38
Interlock		3.00	1	18-Oct-26	20-Oct-26	04-Nov-26	07-Nov-26	285,897.59
B1.2.32 14 13.13.15	60mm thick - Interlocking Block Pavers	3.00	1	18-Oct-26	20-Oct-26	04-Nov-26	07-Nov-26	285,897.59
Curbstone		16.00	8	21-Oct-26	08-Nov-26	08-Nov-26	25-Nov-26	663,229.96
Pre-Installation		6.00	3	21-Oct-26	27-Oct-26	08-Nov-26	14-Nov-26	338,514.37
B2.31 23 00.421	Excavation	2.00	1	21-Oct-26	22-Oct-26	08-Nov-26	09-Nov-26	112,838.12
B1.2.32 14 13.13.21	PCC	2.00	1	24-Oct-26	25-Oct-26	10-Nov-26	11-Nov-26	112,838.12
32 16 13.0015	Haunching	2.00	1	26-Oct-26	27-Oct-26	12-Nov-26	14-Nov-26	112,838.12
Installation		10.00	5	28-Oct-26	08-Nov-26	15-Nov-26	25-Nov-26	324,715.60
B1.2.32 16.13.01.15	Curb Stone, Type K1	2.00	1	28-Oct-26	29-Oct-26	15-Nov-26	16-Nov-26	156,752.40

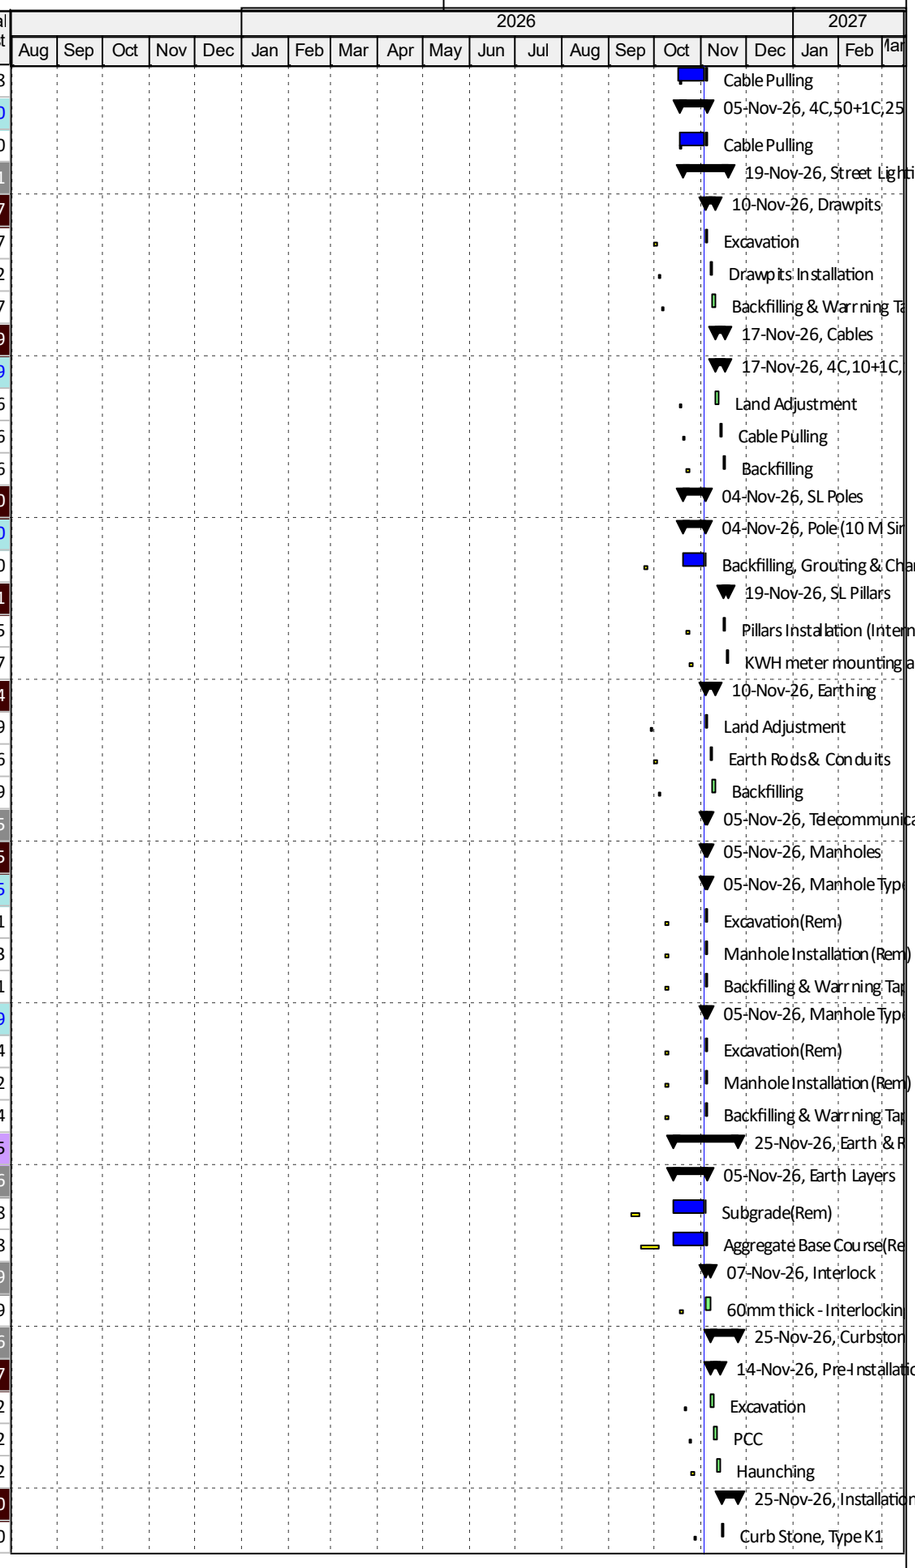


Project Baseline Bar
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B1.2.32 16.13.02.14	Dropped Curb, Type K3	2.00	1	31-Oct-26	01-Nov-26	17-Nov-26	18-Nov-26	1,992.67
B1.2.32 16.13.03.15	Edge Curb, Type K4	2.00	1	02-Nov-26	03-Nov-26	19-Nov-26	21-Nov-26	101,227.18
B1.2.32 16.13.0415	Heel Curb, Type K5	2.00	1	04-Nov-26	05-Nov-26	22-Nov-26	23-Nov-26	63,873.55
B1.2.32 16.13.05.14	Transition Curb	2.00	1	07-Nov-26	08-Nov-26	24-Nov-26	25-Nov-26	869.80
Asphalt Layers		5.00	1	07-Oct-26	13-Oct-26	05-Nov-26	11-Nov-26	4,519,600.91
B1.2.32 11 26.01.15	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	5.00	1	07-Oct-26	13-Oct-26	05-Nov-26	11-Nov-26	4,519,600.91
Traffic Signs		4.00	2	24-Oct-26	27-Oct-26	10-Nov-26	14-Nov-26	21,819.92
Pre-Installation		4.00	2	24-Oct-26	27-Oct-26	10-Nov-26	14-Nov-26	21,819.92
B2.31 23 00.431	Excavation	2.00	1	24-Oct-26	25-Oct-26	10-Nov-26	11-Nov-26	10,909.96
10 14 53.015	Foundation	2.00	1	26-Oct-26	27-Oct-26	12-Nov-26	14-Nov-26	10,909.96
Guard Rail		11.00	3	15-Oct-26	03-Nov-26	04-Nov-26	16-Nov-26	840,000.00
B2.31 23 00.664	Excavation	3.00	1	15-Oct-26	20-Oct-26	04-Nov-26	07-Nov-26	126,000.00
10 14 53.25	Foundation	2.00	1	21-Oct-26	26-Oct-26	10-Nov-26	11-Nov-26	210,000.00
B1.2.10 14 53.338	W-Beam Guard Rail Installation	4.00	1	24-Oct-26	03-Nov-26	12-Nov-26	16-Nov-26	504,000.00
Landscape		18.10	4	26-Oct-26	15-Nov-26	04-Nov-26	25-Nov-26	263,999.86
Fences		12.00	2	26-Oct-26	08-Nov-26	12-Nov-26	25-Nov-26	51,486.90
Steel fence (ZATCA HCIS)		12.00	2	26-Oct-26	08-Nov-26	12-Nov-26	25-Nov-26	51,486.90
B7.32 31 26.01-191	Earthwork	6.00	1	26-Oct-26	01-Nov-26	12-Nov-26	18-Nov-26	25,743.45
B7.32 31 26.01-193	Foundation	6.00	1	02-Nov-26	08-Nov-26	19-Nov-26	25-Nov-26	25,743.45
Geotextile		17.10	2	10-Nov-26	15-Nov-26	04-Nov-26	24-Nov-26	212,512.97
B7.31 32 19.23.6	Geotextile to protect trees planting soil	5.00	1	10-Nov-26	15-Nov-26	04-Nov-26	10-Nov-26	42,040.92
B7.31 32 19.23.7	Geotextile below gravel bed	5.00	1	10-Nov-26	15-Nov-26	19-Nov-26	24-Nov-26	170,472.04
Road 03		55.29	28	16-Sep-26	21-Oct-26	27-Sep-26 A	30-Nov-26	456,036.92
Wet Networks		55.29	10	16-Sep-26	18-Oct-26	27-Sep-26 A	30-Nov-26	73,356.51
Sewerage Network		4.35	2	27-Sep-26	03-Oct-26	27-Sep-26 A	05-Nov-26	8,405.21
Manholes ?1200		4.35	2	27-Sep-26	03-Oct-26	27-Sep-26 A	05-Nov-26	8,405.21
Depth From 1.5m to 2.5m		2.18	1	27-Sep-26	29-Sep-26	27-Sep-26 A	05-Nov-26	3,809.64
B6.33 05 39.01.165	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	27-Sep-26	29-Sep-26	27-Sep-26 A	05-Nov-26	3,809.64
Depth From 2.5m to 3.5m		2.18	1	29-Sep-26	03-Oct-26	29-Sep-26 A	05-Nov-26	4,595.57
B6.33 05 39.01.170	Test, Internal Finishing, Benching & Cover(Rem)	2.18	1	29-Sep-26	03-Oct-26	29-Sep-26 A	05-Nov-26	4,595.57
Potable Water Network		9.00	3	05-Oct-26	15-Oct-26	04-Nov-26	14-Nov-26	1,343.34
Plots and Buildings Crossing		9.00	3	05-Oct-26	15-Oct-26	04-Nov-26	14-Nov-26	1,343.34
B3.33 14 13.02.28	Earthwork	3.00	1	05-Oct-26	08-Oct-26	04-Nov-26	07-Nov-26	268.67
B3.33 14 13.02.29	Sand Bedding	3.00	1	08-Oct-26	12-Oct-26	08-Nov-26	10-Nov-26	268.67
B3.33 14 13.02.30	Tee, Pipe (Crossing) Installation & Backfilling	3.00	1	12-Oct-26	15-Oct-26	11-Nov-26	14-Nov-26	806.01
Fire Fighting Network		41.00	5	16-Sep-26	18-Oct-26	07-Oct-26 A	30-Nov-26	63,607.96
Valves & Chambers		13.00	2	16-Sep-26	01-Oct-26	07-Oct-26 A	07-Nov-26	14,362.11
Gate Valves		4.00	1	28-Sep-26	01-Oct-26	11-Oct-26 A	05-Nov-26	5,017.11
Gate valves dia (250) mm		4.00	1	28-Sep-26	01-Oct-26	11-Oct-26 A	05-Nov-26	5,017.11
B3.33 14 19.01.13	Spindle & Surface Box	4.00	1	28-Sep-26	01-Oct-26	11-Oct-26 A	05-Nov-26	5,017.11
Air Valves		6.00	1	16-Sep-26	22-Sep-26	07-Oct-26 A	07-Nov-26	9,344.99
Air valves on less than 315 mm. (In Chamber)		6.00	1	16-Sep-26	22-Sep-26	07-Oct-26 A	07-Nov-26	9,344.99
B3.33 05 63.02.79	Valve & Fitting Installation	6.00	1	16-Sep-26	22-Sep-26	07-Oct-26 A	07-Nov-26	9,344.99
Fire Hydrant		23.00	3	16-Sep-26	18-Oct-26	04-Nov-26	30-Nov-26	49,245.86
B3.33 14 19.01.fh43_I	Firehydrant Fixing/Installation(Rem)	3.50	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	24,622.93
B3.33 14 19.01.fh44_I	Riser Pipe & Flanged Fittings Installation(Rem)	3.00	1	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	8,207.64

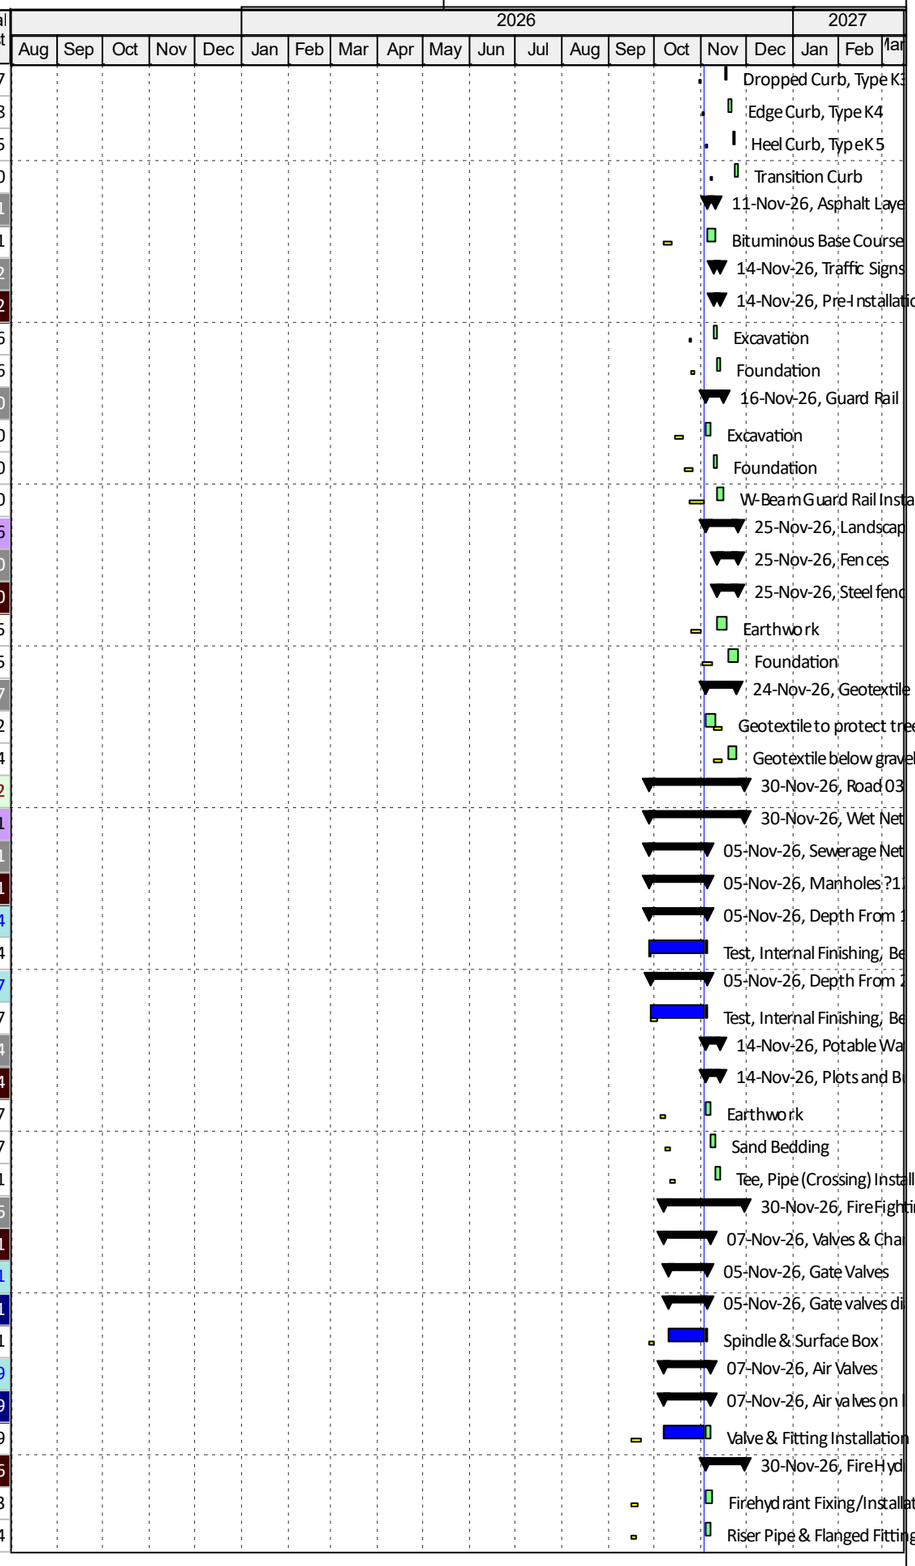


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
B3.33 14 19.01.fh45	Backfilling & Compaction	7.00	1	11-Oct-26	18-Oct-26	23-Nov-26	30-Nov-26	16,415.29
Dry Networks		8.00	8	21-Sep-26	19-Oct-26	04-Nov-26	12-Nov-26	56,005.89
Street Lighting		6.00	3	13-Oct-26	19-Oct-26	07-Nov-26	12-Nov-26	4,501.83
Earthing		6.00	3	13-Oct-26	19-Oct-26	07-Nov-26	12-Nov-26	4,501.83
B2.33 71 19 47	Land Adjustment	2.00	1	13-Oct-26	14-Oct-26	07-Nov-26	08-Nov-26	904.39
B2.33 71 19 48	Earth Rods& Conduits	2.00	1	15-Oct-26	17-Oct-26	09-Nov-26	10-Nov-26	2,693.06
B2.33 71 19 49	Backfilling	2.00	1	18-Oct-26	19-Oct-26	11-Nov-26	12-Nov-26	904.39
Telecommunication Network		8.00	5	21-Sep-26	30-Sep-26	04-Nov-26	12-Nov-26	51,504.05
Manholes		8.00	5	21-Sep-26	30-Sep-26	04-Nov-26	12-Nov-26	51,504.05
Manhole Type 1		4.00	2	21-Sep-26	26-Sep-26	04-Nov-26	08-Nov-26	35,065.58
B2.33 71 00.274	Manhole Installation	2.00	1	21-Sep-26	22-Sep-26	04-Nov-26	05-Nov-26	26,299.19
B2.33 71 00.275	Backfilling & Warrning Tape	2.00	1	24-Sep-26	26-Sep-26	07-Nov-26	08-Nov-26	8,766.40
Manhole Type 2		8.00	3	21-Sep-26	30-Sep-26	04-Nov-26	12-Nov-26	16,438.47
B2.31 23 00.634	Excavation	3.00	1	21-Sep-26	24-Sep-26	04-Nov-26	07-Nov-26	3,287.69
B2.33 71 00.276	Manhole Installation	2.00	1	26-Sep-26	27-Sep-26	08-Nov-26	09-Nov-26	9,863.09
B2.33 71 00.277	Backfilling & Warrning Tape	3.00	1	28-Sep-26	30-Sep-26	10-Nov-26	12-Nov-26	3,287.69
Earth & Road Works		34.50	10	30-Sep-26	21-Oct-26	08-Oct-26 A	24-Nov-26	326,674.52
Interlock		3.00	1	30-Sep-26	04-Oct-26	04-Nov-26	07-Nov-26	17,024.55
B1.2.32 14 13.13.16	60mm thick - Interlocking Block Pavers	3.00	1	30-Sep-26	04-Oct-26	04-Nov-26	07-Nov-26	17,024.55
Curbstone		15.00	8	04-Oct-26	21-Oct-26	08-Nov-26	24-Nov-26	40,518.07
Pre-Installation		6.00	3	04-Oct-26	11-Oct-26	08-Nov-26	14-Nov-26	20,360.24
B2.31 23 00.451	Excavation	2.00	1	04-Oct-26	06-Oct-26	08-Nov-26	09-Nov-26	6,786.75
B1.2.32 14 13.13.21	PCC	2.00	1	06-Oct-26	08-Oct-26	10-Nov-26	11-Nov-26	6,786.75
32 16 13.0016	Haunching	2.00	1	08-Oct-26	11-Oct-26	12-Nov-26	14-Nov-26	6,786.75
Installation		9.00	5	11-Oct-26	21-Oct-26	15-Nov-26	24-Nov-26	20,157.82
B1.2.32 16.13.01.16	Curb Stone, Type K1	3.00	1	11-Oct-26	14-Oct-26	15-Nov-26	17-Nov-26	9,334.25
B1.2.32 16.13.02.15	Dropped Curb, Type K3	1.00	1	14-Oct-26	15-Oct-26	18-Nov-26	18-Nov-26	118.66
B1.2.32 16.13.03.16	Edge Curb, Type K4	1.00	1	15-Oct-26	17-Oct-26	19-Nov-26	19-Nov-26	6,849.59
B1.2.32 16.13.0416	Heel Curb, Type K5	2.00	1	17-Oct-26	19-Oct-26	21-Nov-26	22-Nov-26	3,803.53
B1.2.32 16.13.05.15	Transition Curb	2.00	1	19-Oct-26	21-Oct-26	23-Nov-26	24-Nov-26	51.79
Asphalt Layers		2.00	1	30-Sep-26	06-Oct-26	08-Oct-26 A	04-Nov-26	269,131.90
B1.2.32 11 26.01.16	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	30-Sep-26	06-Oct-26	08-Oct-26 A	04-Nov-26	269,131.90
Road 04		52.28	39	16-Sep-26	07-Nov-26	06-Sep-26 A	03-Dec-26	579,214.14
Wet Networks		44.94	20	16-Sep-26	31-Oct-26	06-Sep-26 A	03-Dec-26	157,640.79
Sewerage Network		4.35	2	03-Oct-26	07-Oct-26	03-Oct-26 A	05-Nov-26	15,052.97
Manholes ?1200		4.35	2	03-Oct-26	07-Oct-26	03-Oct-26 A	05-Nov-26	15,052.97
Depth From 1.5m to 2.5m		2.18	1	03-Oct-26	05-Oct-26	03-Oct-26 A	05-Nov-26	3,809.64
B6.33 05 39.01.175	Test, Internal Finishing, Benching& Cover(Rem)	2.18	1	03-Oct-26	05-Oct-26	03-Oct-26 A	05-Nov-26	3,809.64
Depth From 3.5m to 4.5m		2.18	1	05-Oct-26	07-Oct-26	05-Oct-26 A	05-Nov-26	11,243.33
B6.33 05 39.01.185	Test, Internal Finishing, Benching& Cover(Rem)	2.18	1	05-Oct-26	07-Oct-26	05-Oct-26 A	05-Nov-26	11,243.33
Potable Water Network		17.00	3	16-Sep-26	24-Oct-26	04-Nov-26	23-Nov-26	1,343.34
Plots and Buildings Crossing		17.00	3	16-Sep-26	24-Oct-26	04-Nov-26	23-Nov-26	1,343.34
B3.33 14 13.02.31	Earthwork	7.00	1	16-Sep-26	24-Sep-26	04-Nov-26	11-Nov-26	268.67
B3.33 14 13.02.32	Sand Bedding	3.00	1	26-Sep-26	28-Sep-26	12-Nov-26	15-Nov-26	268.67
B3.33 14 13.02.33	Tee, Pipe (Crossing) Installation & Backfilling	7.00	1	15-Oct-26	24-Oct-26	16-Nov-26	23-Nov-26	806.01
Fire Fighting Network		34.00	15	16-Sep-26	31-Oct-26	06-Sep-26 A	03-Dec-26	141,244.48

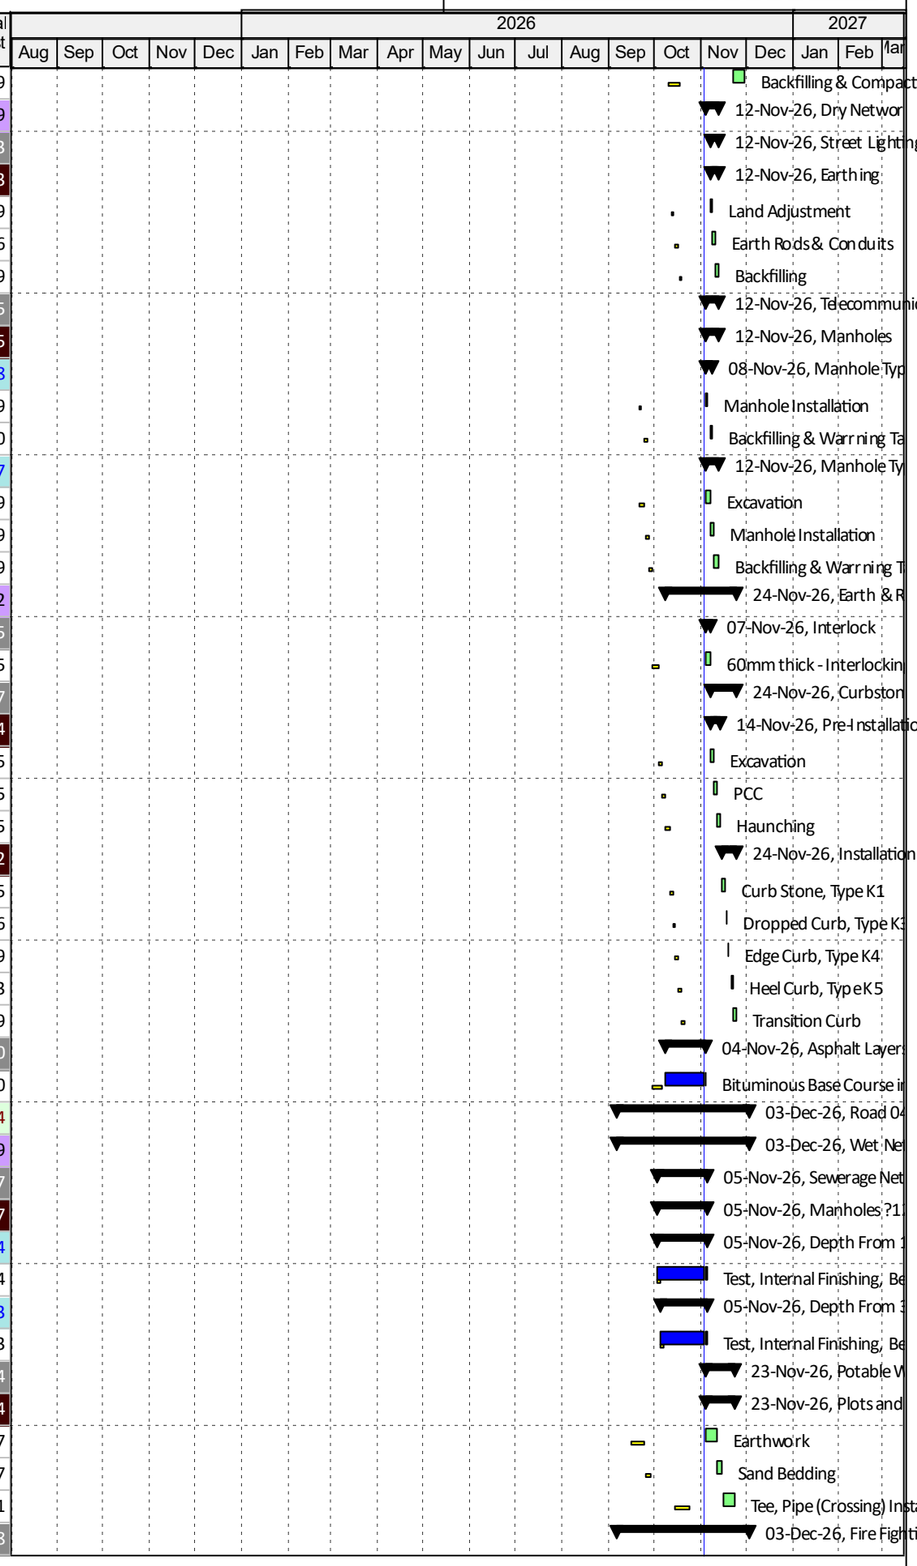

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
Valves & Chambers		34.00	12	16-Sep-26	31-Oct-26	06-Sep-26 A	03-Dec-26	59,988.82
Gate Valves		8.00	2	22-Oct-26	31-Oct-26	14-Sep-26 A	03-Dec-26	7,839.24
Gate valves dia (250) mm		8.00	2	22-Oct-26	31-Oct-26	14-Sep-26 A	03-Dec-26	7,839.24
B3.33 14 19.01.13	Burried Isolation Valve Installation(Rem)	4.00	1	22-Oct-26	26-Oct-26	14-Sep-26 A	03-Dec-26	2,822.13
B3.33 14 19.01.13	Spindle & Surface Box	4.00	1	27-Oct-26	31-Oct-26	21-Sep-26 A	05-Nov-26	5,017.11
Air Valves		10.00	5	16-Sep-26	28-Sep-26	06-Sep-26 A	07-Nov-26	19,811.39
Air valves on less than 315 mm. (In Chamber)		10.00	5	16-Sep-26	28-Sep-26	06-Sep-26 A	07-Nov-26	19,811.39
B3.33 05 63.02.82	Land Adjustment & Compaction(Rem)	3.00	1	16-Sep-26	19-Sep-26	06-Sep-26 A	05-Nov-26	2,242.80
B3.33 05 63.02.80	Foundations(Rem)	3.50	1	16-Sep-26	20-Sep-26	13-Sep-26 A	05-Nov-26	2,910.62
B3.33 05 63.02.83	Chambers Walls Conc Cast In Situ(Rem)	3.50	1	16-Sep-26	20-Sep-26	13-Sep-26 A	05-Nov-26	2,990.40
B3.33 05 63.02.81	Chamber Curing, Finishing & Steel Cover(Rem)	4.00	1	16-Sep-26	20-Sep-26	24-Sep-26 A	05-Nov-26	2,322.58
B3.33 05 63.02.84	Valve & Fitting Installation	6.00	1	21-Sep-26	28-Sep-26	28-Sep-26 A	07-Nov-26	9,344.99
Washout Valves		10.00	5	16-Sep-26	28-Sep-26	16-Sep-26 A	07-Nov-26	32,338.19
Washout valves on 110-400 mm. (In Chamber)		10.00	5	16-Sep-26	28-Sep-26	16-Sep-26 A	07-Nov-26	32,338.19
B3.33 05 63.01.62	Land Adjustment & Compaction(Rem)	3.00	1	16-Sep-26	19-Sep-26	16-Sep-26 A	05-Nov-26	3,966.00
B3.33 05 63.01.60	Foundations(Rem)	3.50	1	16-Sep-26	20-Sep-26	19-Sep-26 A	05-Nov-26	4,824.68
B3.33 05 63.01.63	Chambers Walls Conc Cast In Situ(Rem)	3.50	1	16-Sep-26	20-Sep-26	22-Sep-26 A	05-Nov-26	4,935.31
B3.33 05 63.01.61	Chamber Curing, Finishing & Steel Cover(Rem)	4.00	1	16-Sep-26	20-Sep-26	03-Oct-26 A	05-Nov-26	3,810.94
B3.33 05 63.01.64	Valve & Fitting Installation	6.00	1	21-Sep-26	28-Sep-26	07-Oct-26 A	07-Nov-26	14,801.26
Fire Hydrant		6.95	3	16-Sep-26	31-Oct-26	04-Nov-26	11-Nov-26	81,255.66
B3.33 14 19.01.fh46_I	Firehydrant Fixing/Installation(Rem)	4.97	1	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	48,753.40
B3.33 14 19.01.fh47_I	Riser Pipe & Flanged Fittings Installation(Rem)	3.98	1	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	16,251.13
B3.33 14 19.01.fh48_I	Backfilling & Compaction(Rem)	6.95	1	24-Oct-26	31-Oct-26	04-Nov-26	11-Nov-26	16,251.13
Dry Networks		20.34	9	15-Oct-26	07-Nov-26	01-Oct-26 A	15-Nov-26	64,752.18
Street Lighting		6.00	3	15-Oct-26	21-Oct-26	09-Nov-26	15-Nov-26	4,481.74
Earthing		6.00	3	15-Oct-26	21-Oct-26	09-Nov-26	15-Nov-26	4,481.74
B2.33 71 19 50	Land Adjustment	2.00	1	15-Oct-26	17-Oct-26	09-Nov-26	10-Nov-26	904.39
B2.33 71 19 51	Earth Rods& Conduits	2.00	1	18-Oct-26	19-Oct-26	11-Nov-26	12-Nov-26	2,672.96
B2.33 71 19 52	Backfilling	2.00	1	20-Oct-26	21-Oct-26	14-Nov-26	15-Nov-26	904.39
Telecommunication Network		8.34	6	20-Oct-26	07-Nov-26	01-Oct-26 A	05-Nov-26	60,270.45
Manholes		8.34	6	20-Oct-26	07-Nov-26	01-Oct-26 A	05-Nov-26	60,270.45
Manhole Type 1		8.34	3	20-Oct-26	07-Nov-26	01-Oct-26 A	05-Nov-26	43,831.98
B2.31 23 00.636	Excavation	2.00	1	20-Oct-26	21-Oct-26	01-Oct-26 A	05-Nov-26	8,766.40
B2.33 71 00.280	Manhole Installation	2.00	1	22-Oct-26	24-Oct-26	04-Oct-26 A	05-Nov-26	26,299.19
B2.33 71 00.281	Backfilling & Warrning Tape	2.00	1	04-Nov-26	07-Nov-26	06-Oct-26 A	05-Nov-26	8,766.40
Manhole Type 2		6.00	3	22-Oct-26	28-Oct-26	07-Oct-26 A	05-Nov-26	16,438.47
B2.31 23 00.637	Excavation	2.00	1	22-Oct-26	24-Oct-26	07-Oct-26 A	05-Nov-26	3,287.69
B2.33 71 00.282	Manhole Installation	2.00	1	25-Oct-26	26-Oct-26	10-Oct-26 A	05-Nov-26	9,863.09
B2.33 71 00.283	Backfilling & Warrning Tape	2.00	1	27-Oct-26	28-Oct-26	15-Oct-26 A	05-Nov-26	3,287.69
Earth & Road Works		34.70	10	22-Sep-26	13-Oct-26	06-Oct-26 A	24-Nov-26	356,821.16
Interlock		3.00	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	18,596.77
B1.2.32 14 13.13.17	60mm thick - Interlocking Block Pavers	3.00	1	22-Sep-26	26-Sep-26	04-Nov-26	07-Nov-26	18,596.77
Curbstone		15.00	8	27-Sep-26	13-Oct-26	08-Nov-26	24-Nov-26	44,238.12
Pre-Installation		7.00	3	27-Sep-26	04-Oct-26	08-Nov-26	15-Nov-26	22,218.72
B2.31 23 00.481	Excavation	2.00	1	27-Sep-26	28-Sep-26	08-Nov-26	09-Nov-26	7,405.12
B1.2.32 14 13.13.21	PCC	2.00	1	29-Sep-26	30-Sep-26	10-Nov-26	11-Nov-26	7,408.47

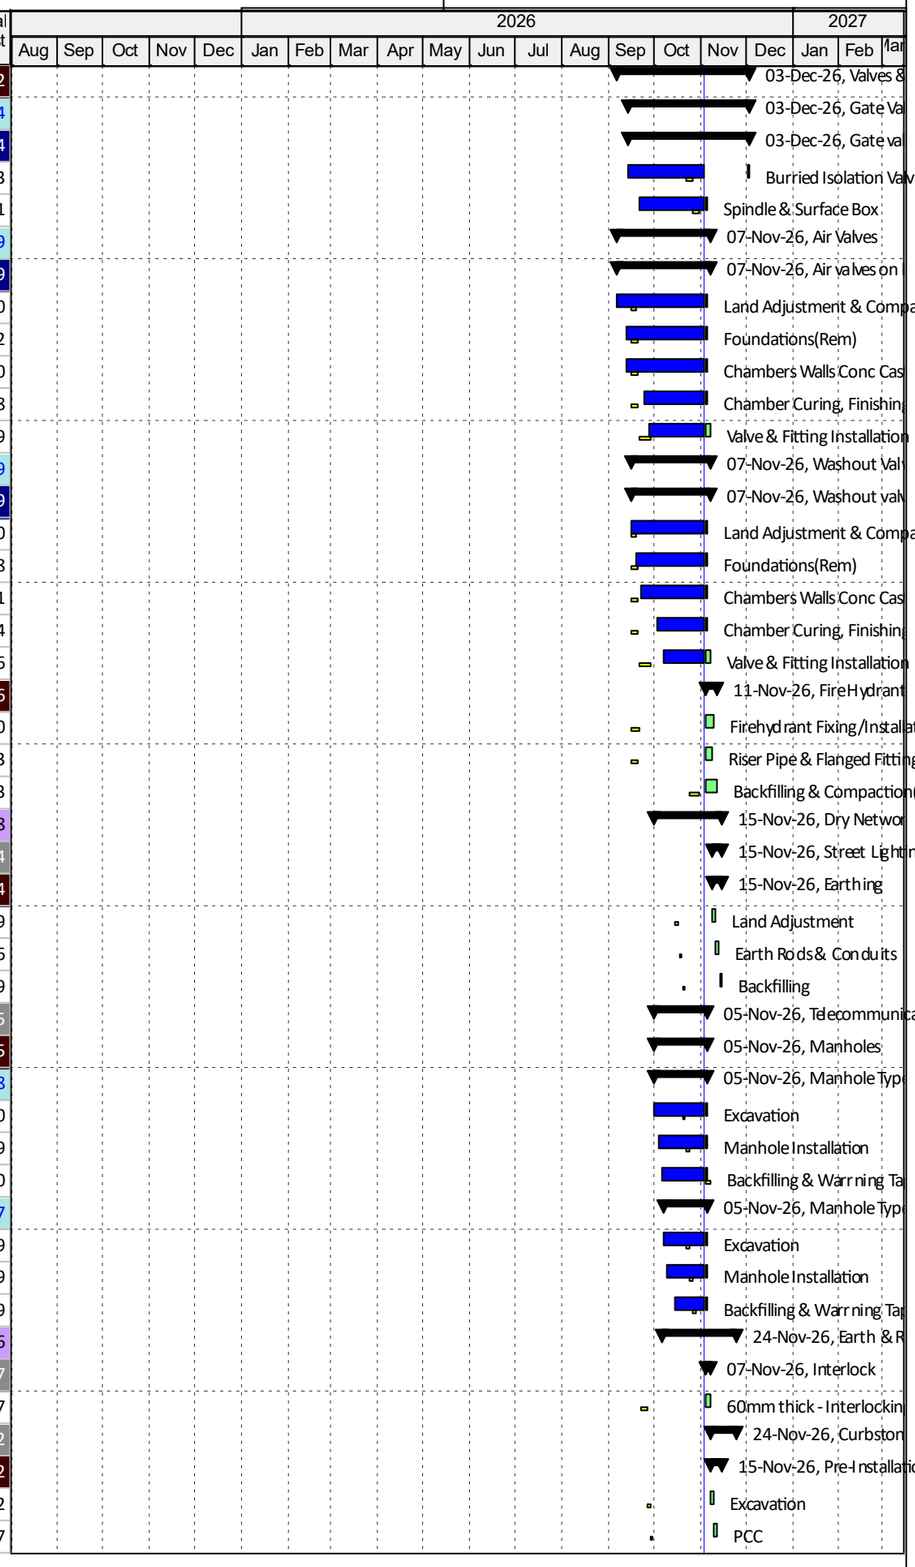

Project Baseline Bar · Actual Work · Remaining Work · Critical Remaining Work · Milestone · Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.


© Oracle Corporation

3 WEEKS LOOKAHEAD

Weekly Progress Report As of 03-Nov-26

Development of Infrastructure for phase 1 of the Logistics area at the 2nd Industrial City in Dammam

Activity ID	Activity Name	Original Duration	Activity Count	BL Project Start	BL Project Finish	Start	Finish	Budgeted Total Cost
32 16 13.0017	Haunching	3.00	1	01-Oct-26	04-Oct-26	12-Nov-26	15-Nov-26	7,405.12
Installation		8.00	5	05-Oct-26	13-Oct-26	16-Nov-26	24-Nov-26	22,019.40
B1.2.32 16.13.01.17	Curb Stone, Type K1	3.00	1	05-Oct-26	07-Oct-26	16-Nov-26	18-Nov-26	10,196.27
B1.2.32 16.13.02.16	Dropped Curb, Type K3	1.00	1	08-Oct-26	08-Oct-26	19-Nov-26	19-Nov-26	129.62
B1.2.32 16.13.03.17	Edge Curb, Type K4	2.00	1	10-Oct-26	11-Oct-26	21-Nov-26	22-Nov-26	7,482.16
B1.2.32 16.13.0417	Heel Curb, Type K5	2.00	1	10-Oct-26	11-Oct-26	21-Nov-26	22-Nov-26	4,154.78
B1.2.32 16.13.05.16	Transition Curb	2.00	1	12-Oct-26	13-Oct-26	23-Nov-26	24-Nov-26	56.58
Asphalt Layers		2.00	1	22-Sep-26	28-Sep-26	06-Oct-26 A	04-Nov-26	293,986.27
B1.2.32 11 26.01.17	Bituminous Base Course including Prime Coat (MC1) and tack coat (RC2	2.00	1	22-Sep-26	28-Sep-26	06-Oct-26 A	04-Nov-26	293,986.27
Testing & Commissioning		24.00	6	19-Nov-26	17-Dec-26	08-Sep-26 A	13-Jan-27	0.00
Zone 01		6.00	2	19-Nov-26	26-Nov-26	08-Sep-26 A	05-Jan-27	0.00
Wet Networks & Stations		6.00	2	19-Nov-26	26-Nov-26	08-Sep-26 A	05-Jan-27	0.00
Sewerage Network		6.00	1	19-Nov-26	26-Nov-26	08-Sep-26 A	05-Jan-27	0.00
T&C-Sew-01	Testing & Commissioning for Sewerage Network	6.00	1	19-Nov-26	26-Nov-26	08-Sep-26 A	05-Jan-27	0.00
Storm Network		6.00	1	19-Nov-26	26-Nov-26	12-Sep-26 A	05-Jan-27	0.00
T&C-Strm-01	Testing & Commissioning for Storm Network	6.00	1	19-Nov-26	26-Nov-26	12-Sep-26 A	05-Jan-27	0.00
Zone 03		11.00	2	28-Nov-26	10-Dec-26	12-Sep-26 A	13-Jan-27	0.00
Wet Networks & Stations		11.00	2	28-Nov-26	10-Dec-26	12-Sep-26 A	13-Jan-27	0.00
Sewerage Network		6.00	1	03-Dec-26	10-Dec-26	13-Sep-26 A	04-Nov-26	0.00
T&C-Sew-11	Testing & Commissioning for Sewerage Network	6.00	1	03-Dec-26	10-Dec-26	13-Sep-26 A	04-Nov-26	0.00
Storm Network		6.00	1	28-Nov-26	05-Dec-26	12-Sep-26 A	13-Jan-27	0.00
T&C-Strm-11	Testing & Commissioning for Storm Network	6.00	1	28-Nov-26	05-Dec-26	12-Sep-26 A	13-Jan-27	0.00
Zone 04		17.00	2	28-Nov-26	17-Dec-26	10-Sep-26 A	05-Jan-27	0.00
Wet Networks & Stations		17.00	2	28-Nov-26	17-Dec-26	10-Sep-26 A	05-Jan-27	0.00
Sewerage Network		6.00	1	10-Dec-26	17-Dec-26	10-Sep-26 A	05-Jan-27	0.00
T&C-Sew-21	Testing & Commissioning for Sewerage Network	6.00	1	10-Dec-26	17-Dec-26	10-Sep-26 A	05-Jan-27	0.00
Storm Network		6.00	1	28-Nov-26	05-Dec-26	28-Sep-26 A	04-Nov-26	0.00
T&C-Strm-21	Testing & Commissioning for Storm Network	6.00	1	28-Nov-26	05-Dec-26	28-Sep-26 A	04-Nov-26	0.00

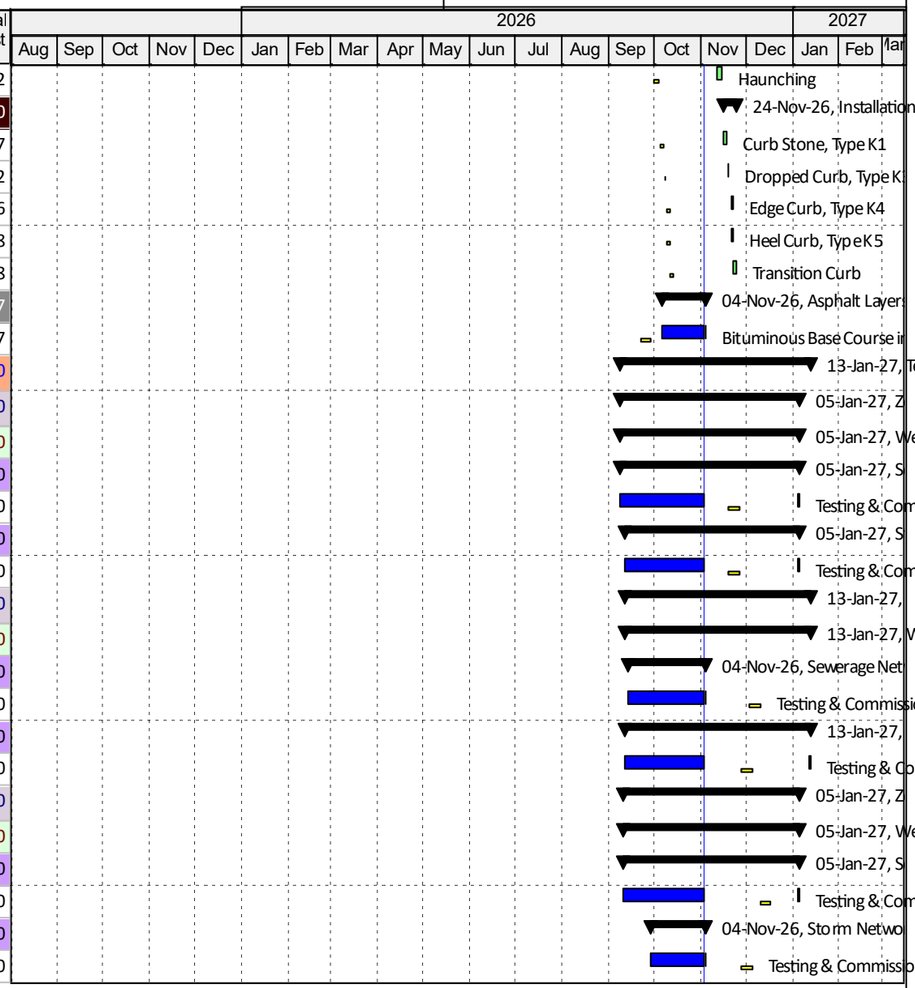

Project Baseline Bar | Actual Work | Remaining Work | Critical Remaining Work | Milestone | Summary

TASK filter: 3 WEEKS LOOKAHEAD_New.

© Oracle Corporation
