Playground Initiative for Eastern Region (Arar, Hasa Oasis, Dammam 2nd)

مبادرة الملاعب بالمنطقة الشرقية (عرعر, واحة الاحساء, الدمام الثانية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Profast Company Ltd.	EGIS	Eng. Mohamed Alisa	03-Mar-2026	02-Jan-2027

Scope: football, basketball and padel grounds, an air dome, a service and toilet building, landscape works, parking, and bike and walking paths at three sites: Hasa Oasis, the 2nd Industrial City at Arar and the 2nd Industrial City at Dammam.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 59.2% against 58.9% planned, 0.3% ahead of the current plan (SPI 1.01). It gained 3.9% this week against 5.2% planned, so the weekly plan was missed by 1.3%. The report also restated last week's figure from 53.9% to 55.3%. Hasa Oasis construction is ahead (64.5% against 53.6% planned), Arar is 1.3% behind and procurement is 18.7% behind.

PHYSICAL % COMPLETE

59.2% / 58.9% plan

▲ SPI 1.01 +0.3%

PROGRESS THIS WEEK

+3.9% / +5.2% plan

▼ 1.3% below the weekly plan

CONTRACT TIME ELAPSED

80.0% · day 244 of 305

▼ Forecast finish 27-Feb-2027

INVOICED TO DATE (GROSS)

15.0% · 4.50M SAR

6 invoices, last period ends 20-Oct-2026

Project completion is forecast 56 days late.

The weekly report and the P6 update (data date 02-Nov-2026) both forecast completion on 27-Feb-2027, against the contract completion date of 02-Jan-2027. This is 15 days earlier than last week's forecast of 14-Mar-2027. P6 shows –46 days of float on project completion and 258 open activities with negative float, against 268 last week. The three site-completion milestones are forecast between 11-Feb and 27-Feb-2027. Supply of the air dome remains the cause of delay named in the weekly summary. The original baseline called for 85.7% by the end of October and 91.5% by the end of November.

Site photos this week

Four photos from the Weekly Photos sheet of the 02-Nov-2026 weekly report. The other two photos in the sheet are under 600 px wide and are not shown. Select a photo to view it larger, then use the arrows to move between photos.



Curtain wall, service building, Arar

Glazed façade and entrance installed on the toilet and service building.



Lighting poles, Arar

Lighting poles installed across the site. Stamped 02-Nov-2026, 09:00, Arar.



Tree planting, Hasa Oasis

Trees planted in the curbed landscape beds. Location stamp Al-Hofuf, Al-Ahsa; the date is not legible.




Interlock paving, Dammam

Interlock being laid between the grounds.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values; the last actual point is the 02-Nov data date. Source: Physical-Chart Data sheet and Weekly Progress Report sheet, weekly report 02-Nov-2026.

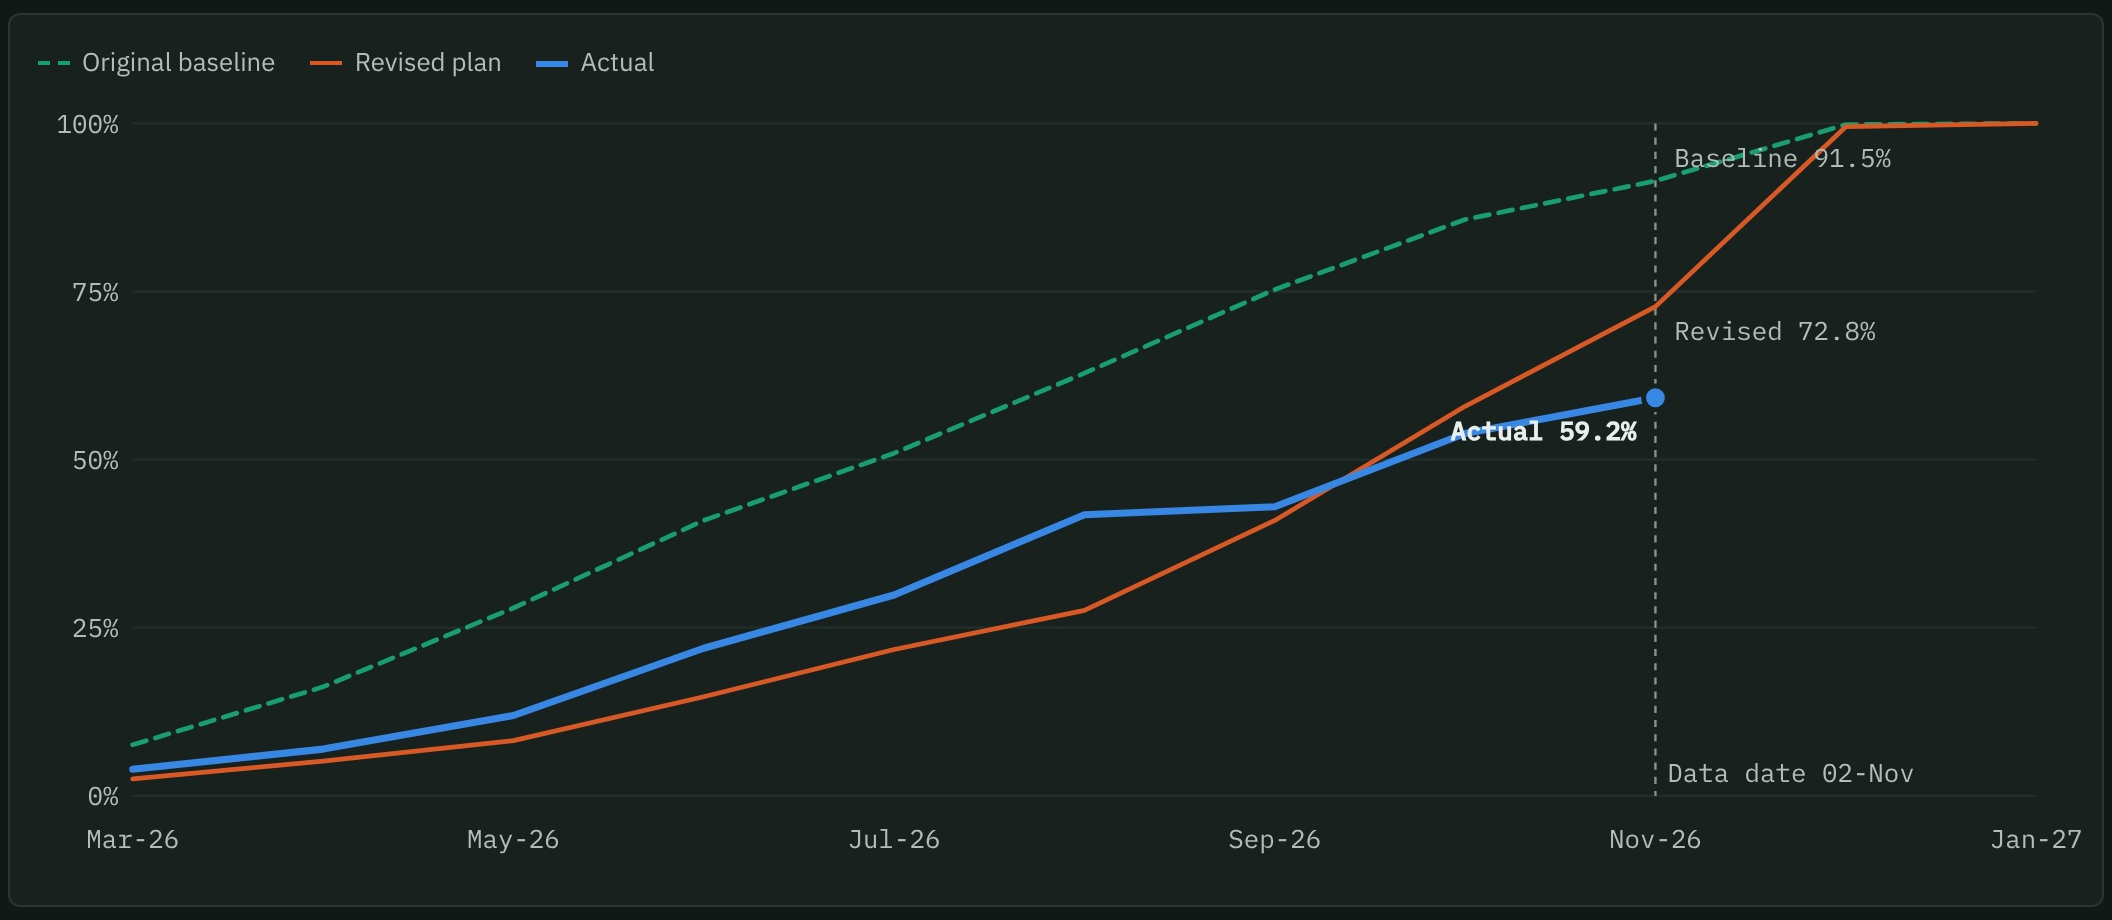

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
05-Oct-2026	–	46.0	–	+3.0	–
12-Oct-2026	–	46.9	–	+0.9	–
19-Oct-2026	50.1	50.3	+0.2	+3.4	1.00
26-Oct-2026	53.7	53.9	+0.2	+3.6	1.00
26-Oct-2026 (restated)	53.7	55.3	+1.6	–	1.03
02-Nov-2026	**58.9**	**59.2**	**+0.3**	**+3.9**	**1.01**

Rows up to 26 Oct come from last week's report (W05 MD Files). This week's to-date figure equals the P6 extract; last week's report gave 53.9% while its own P6 extract gave 55.3%, so the gain this week is measured from the restated 55.3%. Measured from the 53.9% reported last week, the change is +5.3%.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet, 02-Nov-2026.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	3.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	5.0%	97.8%	99.2%	+1.4%	1.01	▲ Ahead
Procurement	12.0%	84.0%	65.4%	−18.7%	0.78	▼ Behind
Construction	75.0%	54.5%	57.8%	+3.4%	1.06	▲ Ahead
Construction: Arar	24.9%	54.2%	53.0%	−1.3%	0.98	▼ Slightly behind
Construction: Hasa Oasis	25.0%	53.6%	64.5%	+11.0%	1.20	▲ Ahead
Construction: Dammam	25.0%	55.7%	56.0%	+0.4%	1.01	● On plan
Testing & commissioning	3.0%	0.0%	0.0%	0.0%	–	○ Not started

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Close-out	2.0%	0.0%	0.0%	0.0%	–	○ Not started
Total	100%	**58.9%**	**59.2%**	**+0.3%**	**1.01**	● On plan

By site, all phases included: Arar 56.5% against 60.1% planned, Hasa Oasis 65.3% against 60.2%, Dammam 59.4% against 59.9%. The P6 update has 2,150 activities: 1,835 completed, 30 in progress and 285 not started. Its scheduled finish is 27-Feb-2027, 56 days after the contract date.

Scope of work: quantities

Total quantity and quantity executed to date for the main BOQ items, all three sites combined, from the Major Quantities sheet of the 02-Nov-2026 weekly report. The sheet does not split quantities by site. "This week" is the change from the 26-Oct-2026 report; every quantity in the sheet is unchanged.

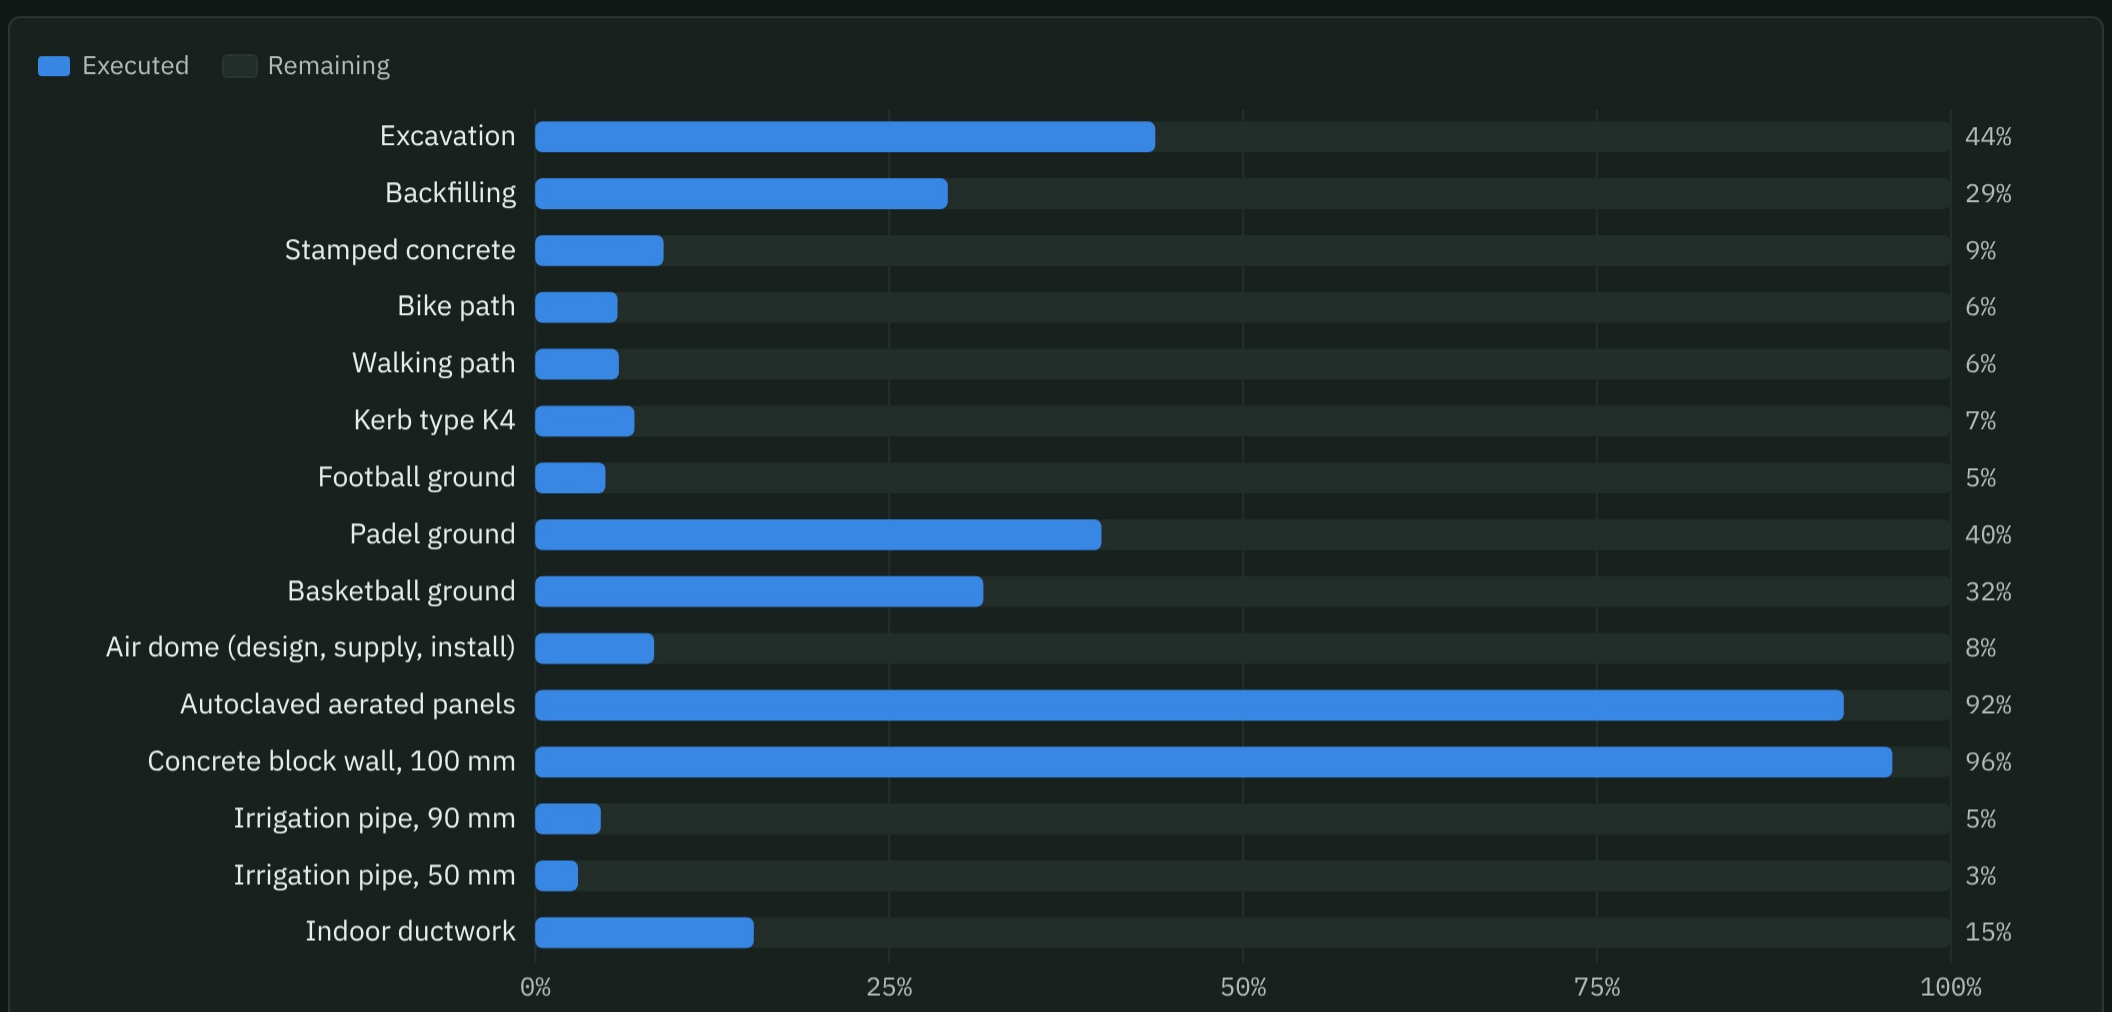

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation	All sites	m³	10,295	4,510	0	5,785	43.8%	–
Backfilling	All sites	m³	10,266	2,992	0	7,274	29.1%	–
Stamped concrete	All sites	m²	1,800	163.3	0	1,637	9.1%	–
Bike path	All sites	m²	2,300	133.8	0	2,166	5.8%	–
Walking path	All sites	m²	2,200	130.1	0	2,070	5.9%	–
Kerb type K4	All sites	LM	9,080	636.7	0	8,443	7.0%	–
Football ground	All sites	m²	3,000	148.9	0	2,851	5.0%	–
Padel ground	All sites	m²	600	240	0	360	40.0%	–
Basketball ground	All sites	m²	1,530	484.4	0	1,046	31.7%	–
Air dome (design, supply, install)	All sites	item	3	0.3	0	2.7	8.4%	–
Autoclaved aerated panels	All sites	m²	750	693.3	0	56.7	92.4%	–
Concrete block wall, 100 mm	All sites	m²	135	129.4	0	5.6	95.9%	–

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Irrigation pipe, 90 mm	All sites	LM	750	34.8	0	715.2	4.6%	–
Irrigation pipe, 50 mm	All sites	LM	350	10.6	0	339.4	3.0%	–
Indoor ductwork	All sites	kg	300	46.3	0	253.7	15.4%	–

Status by site this week

Arar: gypsum board, painting and wash basins finished in the service building, lighting cables laid and backfilled, lighting poles and fittings installed. Hasa Oasis: trees planted, switches, sockets and lighting installed in the service building, bike and walking paths being levelled for the asphalt layer. Dammam: interlock being laid between the grounds, switches and sockets installed in the service building. The glass curtain wall is installed at all three sites, and the air dome entrance steel and formwork continue at Arar and Dammam.

Quantities not updated

The Major Quantities sheet is identical to last week's, although the weekly summary reports interlock, lighting poles, trees and curtain walls installed this week. Items reported beyond their BOQ total (150 mm uPVC external wastewater pipe 126.81 of 50 m, plastering 551.07 of 471 m², foundation waterproofing 101.55 of 60 m², slab on grade 46.17 of 45 m³, polyethylene sheet and anti-termite 288.75 of 270 m²) are left out of the chart and table.

Milestones

The weekly report's Milestones sheet and the P6 update give the same forecast dates. Float is from the P6 update (data date 02-Nov-2026).

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	03-Mar-2026	03-Mar-2026	03-Mar-2026 (actual)	–	✓ Done
Baseline programme approval	01-Apr-2026	04-Apr-2026	04-Apr-2026 (actual)	–	✓ Done
Completion of mobilization	02-Apr-2026	02-Apr-2026	02-Apr-2026 (actual)	–	✓ Done
Completion of levelling works	02-Apr-2026	02-May-2026	02-May-2026 (actual)	–	✓ Done
Completion of engineering	02-May-2026	03-Jan-2027	03-Jan-2027	−4	▼ Late
Completion of toilet building	02-Aug-2026	15-Feb-2027	15-Feb-2027	−38	▼ Late
Completion of playground area	24-Aug-2026	15-Feb-2027	15-Feb-2027	−38	▼ Late
Completion of natural landscape works	02-Nov-2026	27-Feb-2027	27-Feb-2027	−46	▼ Late
Completion of Arar works	21-Dec-2026	11-Feb-2027	11-Feb-2027	−34	▼ Late
Completion of Hasa Oasis works	21-Dec-2026	15-Feb-2027	15-Feb-2027	−37	▼ Late
Completion of Dammam works	21-Dec-2026	27-Feb-2027	27-Feb-2027	−46	▼ Late
Completion of testing & commissioning	21-Dec-2026	27-Feb-2027	27-Feb-2027	−46	▼ Late
Project completion	02-Jan-2027	27-Feb-2027	27-Feb-2027	−46	▼ Late

The air dome, Dammam landscape and late purchase orders drive the finish date.

In P6 the PVC membrane deliveries run from 02-Nov to 24-Dec-2026 and membrane installation from 29-Dec-2026 to 21-Jan-2027, with −10 to −36 days of float. The most negative float (−46 days) now sits on purchase orders still to be placed (marking paint, distribution boards, power cables, CCTV), padel wire mesh delivery, benches, precast seats and trash bins, stamped concrete and MEP testing for the landscape works. Testing and commissioning of all three areas is forecast for 16-Feb to 27-Feb-2027.

Procurement of key materials

Share of total quantity delivered to site. Source: supply tracking file (ملف التوريدات) dated 26-Oct-2026, the latest uploaded; no new supply file came with this week's report.



The weekly report's procurement summary is unchanged from last week: 119 materials, 116 purchase orders issued, 3 still to issue, 99 materials on site and 20 still to arrive. Procurement physical progress rose from 51.7% to 65.4% against 84.0% planned.

Air dome: nothing delivered yet


At 26-Oct, purchase orders were issued and advance payments made for the membrane, anchors, L-profiles, lighting, ventilation, generators, ATS, doors, fire-fighting, panels and electrical material, with supply scheduled from 01-Nov to 05-Dec-2026. The 18 package units were in final approval and the entrance steel and curtain wall in manufacture. P6 now places the first membrane delivery from 02-Nov-2026.

Landscape, path and ground surfaces

Trees (298), lawn (7,030 m²), tartan floor (510 m²), bike and walking path surfaces (4,281 m²) and the football and padel ground surfaces were ordered and paid, with supply due between 29-Oct and 30-Nov-2026. Trees are now being planted at Hasa Oasis. Lighting fixtures (105) were paid and ready to supply; LV panel boards (9) were in manufacture.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet. November is the month to the 02-Nov data date.

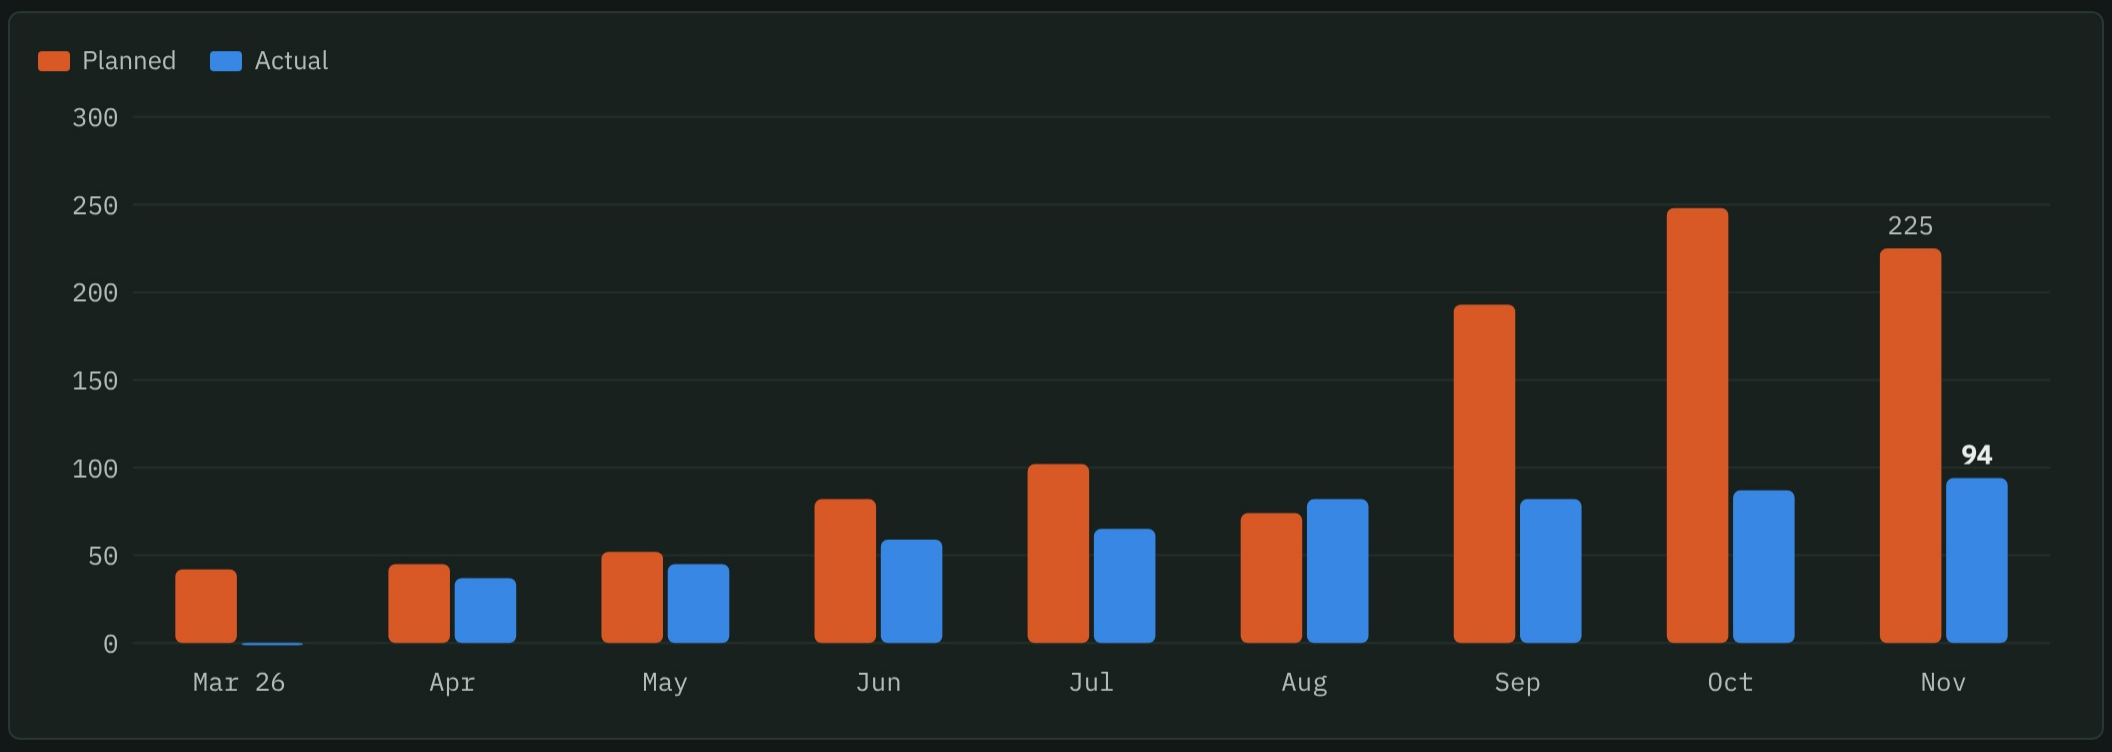

November head count is 94 against 225 planned (−58%): 75 workers against 206 planned and 19 staff as planned. Equipment on site is 12 against 35 planned. The plan rises to 380 in December 2026.

Cost and invoicing

Contract value

Playground works	20,775,269
Site works	5,722,500
Service buildings	3,500,083
Contract value (excl. VAT)	**29,997,852**
Contract value incl. 15% VAT	34,497,529
Change orders	0

All values in SAR, from the Progress Summary and Invoice Log sheets. No change orders are registered.

Invoices

Invoices submitted	6
Gross value	4,501,527
Approved by MODON PM (5 invoices)	3,673,916
Paid (3 invoices)	2,178,751
Deductions and penalties	59,000
Net incl. VAT	5,117,756
FIR value to date	5,965,729

The invoice log is unchanged from last week. Invoicing is 15.0% of the contract value against 59.2% physical progress; approved field inspections rose to 19.9%. No advance payment or retention is recorded.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	45,916
Man-hours this week	1,296
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	33 / 110
Internal audits	5

Quality Score 0.86

FIRs issued / closed / pending	983 / 973 / 10
MIRs issued / closed / pending	194 / 181 / 13
NCRs issued / closed / pending	29 / 27 / 2
Site instructions issued / closed / pending	16 / 6 / 10
Shop drawing submittals (134 planned)	159
Material submittals (119 planned)	140

Cumulative counts from the Quality-Stat sheet. This week 31 FIRs and 10 MIRs were issued and two site instructions were added. All pending items are less than 10 days old.

Open issues and risks

ISSUE	OWNER	DETAIL
Air dome supply	Contractor	Late manufacture and supply of the air dome is the cause of delay named in the weekly summary. The risk register rates late delivery of this long-lead item as high likelihood and very high impact. Membrane delivery and installation run with negative float.
Shop drawing submittals	Contractor	Open since 03-Apr-2026. The expected closure of 29-Oct-2026 has passed and the log has not been updated. Two shop drawings remain to be submitted.
Procurement behind plan	Contractor	Procurement is at 65.4% against 84.0% planned (physical). Twenty materials are not yet on site, three purchase orders are still to be issued, and P6 shows purchase orders for marking paint, distribution boards, power cables and CCTV on the most negative float.
Manpower and equipment	Contractor	75 workers on site against 206 planned for November, and 12 pieces of equipment against 35 planned, while the plan calls for 361 workers in December.
Interfaces between finishes and the air dome	Contractor	The supply file ties the final layer of the paths and grounds to the air dome finishing, to avoid damage; these surfaces were 60% paid but not delivered at 26-Oct.

No new issues were logged this week. Other open risks in the register cover site access, confined spaces, material storage, equipment certification, work at height, heat and traffic separation.

Data notes

- Week number: the Milestones sheet states "Current Contract Weeks: 27 of 44", which is again the report number (WPR-27). From site handover on 03-Mar-2026 to the 02-Nov-2026 data date is 244 days, week 34, one week after last week's report (week 33).
- Restated progress: last week's report gave 53.9% (225,576 man-hours) while its P6 extract gave 55.3% (231,540). This week's to-date figure, 247,833 man-hours (59.2%), matches the P6 extract, and the report's weekly gain of 16,292 man-hours (3.9%) is measured from 231,540. Against the 53.9% reported last week the change is 5.3%. The Physical-Chart Data sheet adds only 15,467 man-hours and shows 57.6% for November, which does not match the 59.2% headline.
- The MODON summary files (Look Ahead, الأعمال المنفذة ونسب الإنجاز, الأعمال المنفذه خلال الإسبوع) and the Progress Summary sheet label cost-based progress as actual progress. Those figures are not used here.
- The file الأعمال المنفذه خلال الإسبوع still carries details of another project: project manager عبد الله الشنيفي, contractor شركة الانجاز, start 24-Nov-2025, contract end 23-May-2026 and sector القطاع الأوسط.
- No supply file (ملف التوريدات) was uploaded this week, and the procurement log and the report's Procurement and Invoice Log sheets are identical to last week's. The procurement chart therefore still shows the 26-Oct-2026 position.
- The Major Quantities sheet is identical to last week's for every item, so the this-week column shows 0 although work on interlock, lighting poles, trees and curtain walls is reported. Several items exceed their BOQ quantity and "Plan To Date" equals the full quantity for every item.
- The milestone table on the Weekly Progress Report sheet still has its names shifted by one row against the Milestones sheet; "Completion of Playground Area" there carries the engineering dates and is marked actual although P6 forecasts 03-Jan-2027.
- Two of the six weekly photos are 598 px wide, under the 600 px minimum, and are not shown. The week folder also holds last week's Executive Summary (WPR-26) beside this week's.
- Several summary cells in the DB and Invoice Log sheets show #REF! errors.

Compiled 03-Nov-2026 from the weekly report with data date 02-Nov-2026 (WPR-27), compared with the 26-Oct-2026 report (WPR-26).
