
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026		162	25-Jun-26	15-Dec-26	01-Jul-26 A	28-Jan-27	8,849,653.81	6,538,014.17	11,765,838.88	75.21%	55.57%	-34
MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	27-Dec-26	0.00	0.00	0.00	0%	0%	-5
GENERAL MILESTONES		148	25-Jun-26	15-Dec-26	01-Jul-26 A	27-Dec-26	0.00	0.00	0.00	0%	0%	-5
PG-GN-MS-30_R	Project Durations(Remaining)	148	25-Jun-26	15-Dec-26	01-Jul-26 A	27-Dec-26	0.00	0.00	0.00	56.95%	50%	-5
QASSIM		132	25-Jun-26	02-Dec-26	30-Jul-26 A	12-Jan-27	4,306,625.82	2,939,813.05	5,682,934.93	75.78%	51.73%	-4
ENGINEERING		35	25-Jun-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-21
SHOP DRAWINGS SUBMITTALS		35	25-Jun-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-21
MECHANICAL DRAWINGS		18	25-Jun-26	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
PG-Q-EN-ME-SD-SB-100	Air Package and HVAC System Drawings	18	25-Jun-26	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-38
ELECTRICAL DRAWINGS		17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-39
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-39
PG-Q-EN-EL-SD-SB-120	Power & Lighting System Drawings	10	16-Jul-26	27-Jul-26	30-Jul-26 A	03-Oct-26	0.00	0.00	0.00	100%	90%	-45
PG-Q-EN-EL-SD-SB-130	Generators Details	15	16-Jul-26	02-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-41
PG-Q-EN-EL-SD-SB-140	Smart Dome System Drawings	17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	100%	90%	-39
PROCUREMENT		66	25-Jun-26	27-Aug-26	14-Aug-26 A	31-Oct-26	2,536,743.99	1,459,417.35	2,536,743.99	100%	57.53%	-11
LONG LEAD ITEMS		66	25-Jun-26	27-Aug-26	14-Aug-26 A	31-Oct-26	2,383,025.05	1,372,173.92	2,383,025.05	100%	57.58%	-11
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-Q-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	100%	0%	0
DELIVERY TO SITE		66	07-Jul-26	27-Aug-26	14-Aug-26 A	11-Oct-26	2,383,025.05	1,372,173.92	2,383,025.05	100%	57.58%	-4
EXTERNAL / LANDSCAPE WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-28
PG-Q-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	14,428.69	12,985.82	14,428.69	100%	90%	-28
SPORTS & RECREATIONAL FACILITIES WORK		37	13-Jul-26	23-Aug-26	14-Aug-26 A	11-Oct-26	2,119,264.56	1,155,873.24	2,119,264.56	100%	54.54%	-13
PG-Q-PR-LL-SP-DL-30_R	Padel Playground Materials (Fence, tempered glass, etc)(Remaining)	15	13-Jul-26	29-Jul-26	14-Aug-26 A	04-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-28
PG-Q-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	46,985.40	42,286.86	46,985.40	100%	90%	-28
PG-Q-PR-LL-SP-DL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-28
PG-Q-PR-LL-SP-DL-40_R	Tartan Floor(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	156,686.40	141,017.76	156,686.40	100%	90%	-28
PG-Q-PR-LL-SP-DL-50	Air Dome Materials	10	12-Aug-26	23-Aug-26	25-Aug-26 A	11-Oct-26	1,878,662.16	939,331.08	1,878,662.16	100%	50%	-30
PLUMBING WORK		15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	7,810.43	7,029.38	7,810.43	100%	90%	-28
PG-Q-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	15	25-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	7,810.43	7,029.38	7,810.43	100%	90%	-28
IRRIGATION WORK		8	07-Jul-26	15-Jul-26	20-Aug-26 A	03-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-28
PG-Q-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	8	07-Jul-26	15-Jul-26	20-Aug-26 A	03-Oct-26	20,455.88	19,433.08	20,455.88	100%	95%	-28
ELECTRICAL WORK		40	30-Jul-26	27-Aug-26	14-Aug-26 A	05-Oct-26	221,065.50	176,852.40	221,065.50	100%	80%	-19
PG-Q-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	10	30-Jul-26	10-Aug-26	14-Aug-26 A	04-Oct-26	1,785.24	1,428.19	1,785.24	100%	80%	-33
PG-Q-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	05-Oct-26	3,124.17	2,499.34	3,124.17	100%	80%	-29
PG-Q-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	05-Oct-26	182,755.44	146,204.35	182,755.44	100%	80%	-29
PG-Q-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	15	11-Aug-26	27-Aug-26	14-Aug-26 A	05-Oct-26	8,081.83	6,465.46	8,081.83	100%	80%	-29
PG-Q-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	05-Oct-26	6,326.40	5,061.12	6,326.40	100%	80%	-18
PG-Q-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	15	11-Aug-26	27-Aug-26	27-Aug-26 A	05-Oct-26	6,170.09	4,936.08	6,170.09	100%	80%	-18
PG-Q-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	05-Oct-26	7,811.37	6,249.10	7,811.37	100%	80%	-18
PG-Q-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	15	11-Aug-26	27-Aug-26	27-Aug-26 A	05-Oct-26	5,010.96	4,008.77	5,010.96	100%	80%	-18
SHORT LEAD ITEMS		49	25-Jun-26	12-Jul-26	14-Aug-26 A	11-Oct-26	153,718.94	87,243.43	153,718.94	100%	56.76%	-34
DELIVERY TO SITE		49	25-Jun-26	12-Jul-26	14-Aug-26 A	11-Oct-26	153,718.94	87,243.43	153,718.94	100%	56.76%	-34
EXTERNAL / LANDSCAPE WORK		12	25-Jun-26	08-Jul-26	27-Aug-26 A	11-Oct-26	78,553.04	38,992.68	78,553.04	100%	49.64%	-26
PG-Q-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	11-Oct-26	1,892.27	662.29	1,892.27	100%	35%	-26
PG-Q-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Oct-26	714.10	357.05	714.10	100%	50%	-24
PG-Q-PR-SL-LS-DL-70_R	Trees(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Oct-26	34,366.68	17,183.34	34,366.68	100%	50%	-24
PG-Q-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	25-Jun-26	08-Jul-26	27-Aug-26 A	08-Oct-26	41,580.00	20,790.00	41,580.00	100%	50%	-24
METAL WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	1,724.00	862.00	1,724.00	100%	50%	0
PG-Q-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	1,302.70	651.35	1,302.70	100%	50%	0
PG-Q-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	112.75	56.38	112.75	100%	50%	0
PG-Q-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	308.56	154.28	308.56	100%	50%	0
IRRIGATION WORK		18	25-Jun-26	08-Jul-26	14-Aug-26 A	07-Oct-26	71,118.65	46,227.12	71,118.65	100%	65%	-33
PG-Q-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	25-Jun-26	08-Jul-26	14-Aug-26 A	07-Oct-26	7,186.00	4,670.90	7,186.00	100%	65%	-33
PG-Q-PR-SL-IR-DL-20_R	Bubblers and Sprayers(Remaining)	12	25-Jun-26	08-Jul-26	20-Aug-26 A	07-Oct-26	63,932.65	41,556.22	63,932.65	100%	65%	-28
ELECTRICAL WORK		15	25-Jun-26	12-Jul-26	26-Sep-26 A	11-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	2
PG-Q-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	15	25-Jun-26	12-Jul-26	26-Sep-26 A	11-Oct-26	2,200.61	1,100.30	2,200.61	100%	50%	2
FIRE FIGHTING WORK		12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	122.63	61.32	122.63	100%	50%	0
PG-Q-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	25-Jun-26	08-Jul-26	26-Sep-26 A	08-Oct-26	122.63	61.32	122.63	100%	50%	0
CONSTRUCTION STAGE		110	05-Jul-26	02-Dec-26	06-Aug-26 A	30-Dec-26	1,769,881.84	1,208,563.83	2,497,301.96	70.87%	48.39%	5
PLAYGROUND AND LANDSCAPING WORKS		110	05-Jul-26	02-Dec-26	06-Aug-26 A	30-Dec-26	840,514.26	930,423.39	1,280,964.84	65.62%	72.63%	5
PLAYGROUND WORKS		95	11-Aug-26	17-Nov-26	06-Aug-26 A	05-Nov-26	83,996.71	226,095.54	297,167.22	28.27%	76.08%	7
FOOTBALL PLAYGROUND WORKS		53	19-Aug-26	17-Nov-26	14-Aug-26 A	29-Oct-26	48,027.00	69,070.08	109,254.66	43.96%	63.22%	13
PG-Q-CON-EXFB-120	Installation of Lighting System	12	19-Aug-26	01-Sep-26	20-Aug-26 A	04-Oct-26	24,360.00	20,706.00	24,360.00	100%	85%	-26
PG-Q-CON-EXFB-90	Tufing / Seeding Works	10	02-Sep-26	13-Sep-26	14-Aug-26 A	06-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-35
PG-Q-CON-EXFB-60	Goal Post Installation & Alignment	15	03-Oct-26	19-Oct-26	27-Aug-26 A	10-Oct-26	0.00	28,400.40	35,500.50	0%	80%	-22
PG-Q-CON-EXFB-110	Install Playground Benches	17	20-Oct-26	08-Nov-26	27-Aug-26 A	20-Oct-26	0.00	1,030.08	2,060.16	0%	50%	-28
PG-Q-CON-EXFB-100	Markings and Signages	8	09-Nov-26	17-Nov-26	20-Oct-26	29-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		64	31-Aug-26	17-Nov-26	20-Aug-26 A	05-Nov-26	24,013.23	33,324.48	43,200.72	55.59%	77.14%	2
PG-Q-CON-EXBB-80	Court Line Marking	15	31-Aug-26	16-Sep-26	20-Aug-26 A	07-Oct-26	13,091.76	10,473.41	13,091.76	100%	80%	-26
PG-Q-CON-EXBB-60	Basketball Pole Installation & Alignment	17	17-Sep-26	07-Oct-26	20-Aug-26 A	11-Oct-26	10,921.47	12,377.66	15,472.08	70.59%	80%	-27
PG-Q-CON-EXBB-90	Backboard & Hoop Installation	17	08-Oct-26	27-Oct-26	01-Oct-26 A	15-Oct-26	0.00	10,473.41	13,091.76	0%	80%	5

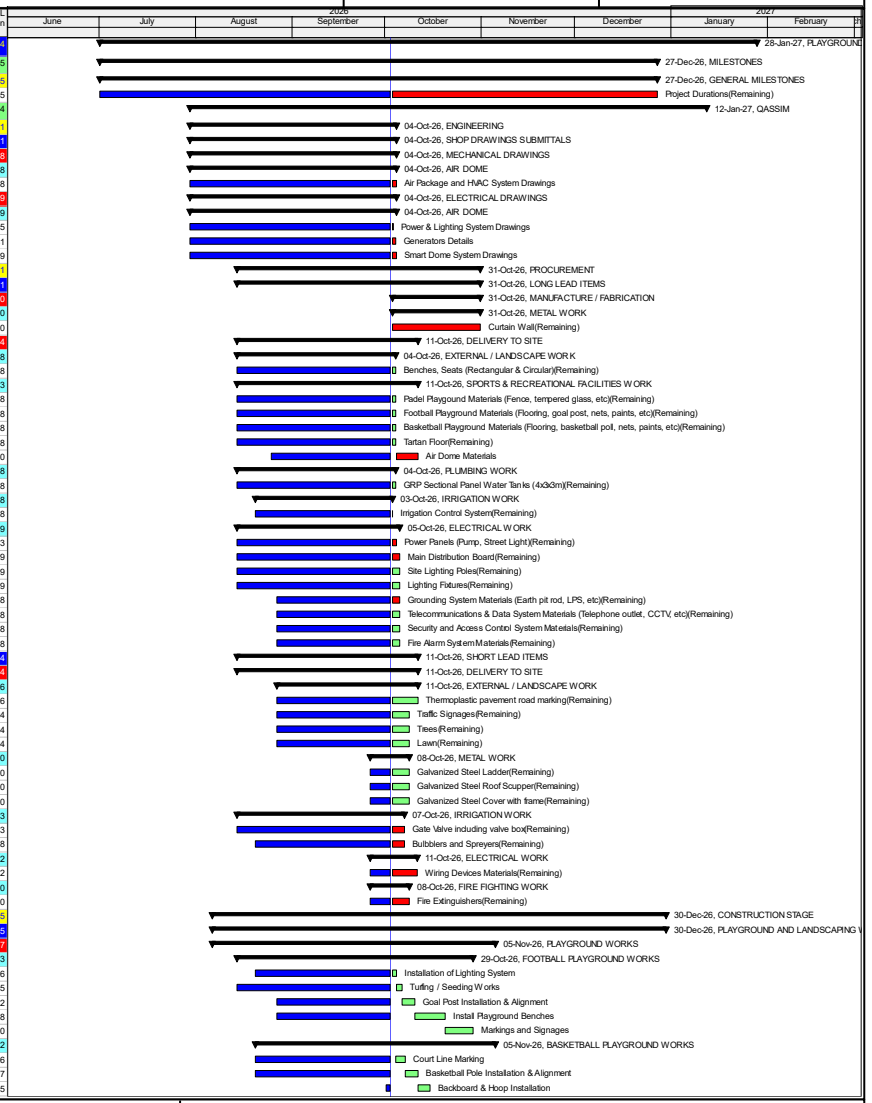

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-Q-CON-EXBB-100	Install Playground Benches	18	28-Oct-26	17-Nov-26	15-Oct-26	05-Nov-26	0.00	0.00	1,545.12	0%	0%	0
PADEL PLAYGROUND WORKS		86	11-Aug-26	28-Oct-26	06-Aug-26 A	04-Nov-26	11,956.48	123,700.98	144,711.84	8.26%	85.48%	-10
PG-Q-CON-EXPD-40	Steel Structure & Fence Supports Installation	18	11-Aug-26	31-Aug-26	20-Aug-26 A	10-Oct-26	3,534.96	2,474.47	3,534.96	100%	70%	-25
PG-Q-CON-EXPD-60	Chain Link Fence & Gates Installation	16	01-Sep-26	19-Sep-26	20-Aug-26 A	15-Oct-26	5,302.44	3,711.71	5,302.44	100%	70%	-32
PG-Q-CON-EXPD-50	Tempered Glass Installation	17	20-Sep-26	10-Oct-26	15-Oct-26	04-Nov-26	3,119.08	0.00	5,302.44	58.82%	0%	0
PG-Q-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	16	11-Oct-26	28-Oct-26	06-Aug-26 A	04-Nov-26	0.00	117,514.80	130,572.00	0%	90%	-61
GENERAL SITE WORKS		110	05-Jul-26	28-Nov-26	14-Aug-26 A	30-Dec-26	713,275.32	523,600.87	715,507.32	99.69%	73.18%	8
FENCE WORKS		58	02-Aug-26	13-Sep-26	20-Aug-26 A	29-Oct-26	19,745.64	7,240.07	19,745.64	100%	36.67%	-22
PG-Q-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	12	02-Aug-26	15-Aug-26	20-Aug-26 A	04-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-26
PG-Q-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	15	16-Aug-26	01-Sep-26	27-Sep-26 A	18-Oct-26	6,581.88	1,645.47	6,581.88	100%	25%	-2
PG-Q-CON-EXGN-FN-50	Installation of Gates	10	02-Sep-26	13-Sep-26	18-Oct-26	29-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		56	05-Jul-26	16-Aug-26	20-Aug-26 A	29-Oct-26	348,762.60	238,538.34	348,762.60	100%	68.4%	-22
STORM WATER AND UTILITY WORK		56	05-Jul-26	16-Aug-26	20-Aug-26 A	29-Oct-26	21,060.00	11,894.40	21,060.00	100%	56.48%	-22
PG-Q-CON-EXGN-M-30_R	Manhole Installation(Remaining)	6	05-Jul-26	11-Jul-26	20-Aug-26 A	04-Oct-26	4,128.00	3,302.40	4,128.00	100%	80%	-31
PG-Q-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	6	12-Jul-26	18-Jul-26	20-Aug-26 A	05-Oct-26	10,740.00	8,592.00	10,740.00	100%	80%	-32
PG-Q-CON-EXGN-M-50	Concrete Encasement	7	19-Jul-26	26-Jul-26	05-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-60	Backfilling & Compaction	6	27-Jul-26	02-Aug-26	13-Oct-26	20-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-Q-CON-EXGN-M-70	Surface Reinstatement & Civil Works	6	10-Aug-26	16-Aug-26	22-Oct-26	29-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		5	03-Aug-26	09-Aug-26	20-Aug-26 A	22-Oct-26	327,702.60	226,643.94	327,702.60	100%	69.16%	-47
PG-Q-CON-EXGN-M-90	Installation of Irrigation Control System	3	03-Aug-26	05-Aug-26	20-Aug-26 A	20-Oct-26	90,915.00	72,732.00	90,915.00	100%	80%	-49
PG-Q-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	3	06-Aug-26	09-Aug-26	27-Aug-26 A	22-Oct-26	236,787.60	153,911.94	236,787.60	100%	65%	-44
ELECTRICAL WORK		25	13-Aug-26	12-Sep-26	20-Aug-26 A	10-Nov-26	344,767.08	275,813.66	344,767.08	100%	80%	-43
POWER, LIGHTING & GROUNDING		25	13-Aug-26	12-Sep-26	20-Aug-26 A	10-Nov-26	344,767.08	275,813.66	344,767.08	100%	80%	-43
PG-Q-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	13-Aug-26	17-Aug-26	20-Aug-26 A	29-Oct-26	162,449.28	129,959.42	162,449.28	100%	80%	-56
PG-Q-CON-EXGN-E-30	Lightning Protection System (LPS)	3	29-Aug-26	31-Aug-26	27-Aug-26 A	01-Nov-26	8,265.00	6,612.00	8,265.00	100%	80%	-53
PG-Q-CON-EXGN-E-60	Site Lighting Poles Installation	3	09-Sep-26	12-Sep-26	20-Aug-26 A	10-Nov-26	174,052.80	139,242.24	174,052.80	100%	80%	-66
SERVICE CONNECTION		8	19-Nov-26	28-Nov-26	14-Aug-26 A	30-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-109
PG-Q-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	8	19-Nov-26	28-Nov-26	14-Aug-26 A	30-Dec-26	0.00	2,008.80	2,232.00	0%	90%	-109
LANDSCAPING WORKS		54	30-Sep-26	02-Dec-26	20-Aug-26 A	28-Nov-26	8,529.23	180,726.98	233,577.30	3.65%	77.37%	-29
HARDSCAPE WORK		54	30-Sep-26	02-Dec-26	20-Aug-26 A	28-Nov-26	8,529.23	94,101.98	118,077.30	7.22%	79.7%	-29
PG-Q-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	30-Sep-26	14-Oct-26	27-Aug-26 A	31-Oct-26	8,529.23	47,124.00	55,440.00	15.38%	85%	-42
PG-Q-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	22-Nov-26	02-Dec-26	20-Aug-26 A	28-Nov-26	0.00	46,977.98	62,637.30	0%	75%	-74
SOFTSCAPE WORK		15	15-Oct-26	01-Nov-26	27-Aug-26 A	04-Nov-26	0.00	86,625.00	115,500.00	0%	75%	-44
PG-Q-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	15	15-Oct-26	01-Nov-26	27-Aug-26 A	04-Nov-26	0.00	86,625.00	115,500.00	0%	75%	-44
TANK WORKS		8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
WATER STORAGE TANK		8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
PG-Q-CON-EXTW-IR-40	GRP Water Tank Installation	8	11-Aug-26	19-Aug-26	04-Oct-26	13-Oct-26	34,713.00	0.00	34,713.00	100%	0%	0
AIR DOME CONSTRUCTION		76	17-Aug-26	04-Nov-26	27-Aug-26 A	13-Dec-26	918,457.06	250,488.29	1,168,945.34	78.57%	21.43%	-24
CIVIL WORK		18	22-Aug-26	10-Sep-26	04-Oct-26	25-Oct-26	500,976.58	0.00	500,976.58	100%	0%	0
PG-Q-CON-EXAD-CL-70	Installation of Steel Cable Structural System	10	22-Aug-26	01-Sep-26	04-Oct-26	15-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-Q-CON-EXAD-CL-80	Installation of Membrane System	8	02-Sep-26	10-Sep-26	15-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
ARCHITECTURAL WORK		8	27-Oct-26	04-Nov-26	27-Aug-26 A	13-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-84
PG-Q-CON-EXAD-AR-10	Installation of Thermal Insulation System	8	27-Oct-26	04-Nov-26	27-Aug-26 A	13-Dec-26	0.00	125,244.14	250,488.29	0%	50%	-84
ELECTRICAL WORK		32	17-Aug-26	13-Sep-26	27-Aug-26 A	22-Oct-26	417,480.48	125,244.14	417,480.48	100%	30%	-24
PG-Q-CON-EXAD-EL-10	Installation of Electrical Boxes & MDBs	12	17-Aug-26	30-Aug-26	27-Aug-26 A	08-Oct-26	208,740.24	125,244.14	208,740.24	100%	60%	-24
PG-Q-CON-EXAD-EL-20	Installation of Lighting System	12	31-Aug-26	13-Sep-26	08-Oct-26	22-Oct-26	208,740.24	0.00	208,740.24	100%	0%	0
TOILET BUILDING WORKS		39	20-Aug-26	20-Oct-26	20-Aug-26 A	22-Nov-26	10,910.52	27,652.16	47,391.78	23.02%	58.35%	-27
CIVIL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	0.00	24,890.46	36,345.00	0%	68.48%	-67
ARCHITECTURAL WORK		29	06-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	0.00	24,890.46	36,345.00	0%	68.48%	-67
GENERAL FINISHES		28	08-Oct-26	19-Oct-26	27-Aug-26 A	21-Nov-26	0.00	13,067.46	20,825.40	0%	62.75%	-63
PG-Q-CON-B-AR-GF-60	Install Doors & Windows	5	08-Oct-26	13-Oct-26	27-Aug-26 A	14-Oct-26	0.00	9,291.66	13,273.80	0%	70%	-36
PG-Q-CON-B-AR-GF-70	Lockers and Furniture Installation	5	14-Oct-26	19-Oct-26	19-Sep-26 A	21-Nov-26	0.00	3,775.80	7,551.60	0%	50%	-49
WET AREA FINISHES		5	08-Oct-26	13-Oct-26	01-Oct-26 A	15-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-7
PG-Q-CON-B-AR-WF-60	Install Doors	5	08-Oct-26	13-Oct-26	01-Oct-26 A	15-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-7
ROOF FINISHES		6	06-Oct-26	12-Oct-26	20-Aug-26 A	13-Oct-26	0.00	9,142.20	10,158.00	0%	90%	-40
PG-Q-CON-B-AR-RF-20	Epoxy Flooring and Finishes	6	06-Oct-26	12-Oct-26	20-Aug-26 A	13-Oct-26	0.00	9,142.20	10,158.00	0%	90%	-40
MEP WORK		39	20-Aug-26	20-Oct-26	01-Oct-26 A	22-Nov-26	10,910.52	2,761.70	11,046.78	98.77%	25%	8
MECANICAL WORKS		39	20-Aug-26	20-Oct-26	01-Oct-26 A	22-Nov-26	10,910.52	2,761.70	11,046.78	98.77%	25%	8
FIRE FIGHTING SYSTEM		1	20-Oct-26	20-Oct-26	01-Oct-26 A	22-Nov-26	0.00	34.07	136.26	0%	25%	-43
PG-Q-CON-B-GF-FF-10	Fire Extinguisher Installation	1	20-Oct-26	20-Oct-26	01-Oct-26 A	22-Nov-26	0.00	34.07	136.26	0%	25%	-43
SEWER AND DRAINAGE SYSTEM		2	01-Sep-26	02-Sep-26	01-Oct-26 A	12-Oct-26	3,225.72	806.43	3,225.72	100%	25%	-8
PG-Q-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	01-Sep-26	02-Sep-26	01-Oct-26 A	12-Oct-26	3,225.72	806.43	3,225.72	100%	25%	-8
HVAC SYSTEM		3	20-Aug-26	23-Aug-26	01-Oct-26 A	05-Oct-26	7,684.80	1,921.20	7,684.80	100%	25%	0
PG-Q-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	20-Aug-26	23-Aug-26	01-Oct-26 A	05-Oct-26	7,684.80	1,921.20	7,684.80	100%	25%	0
PROJECT CLOSOUT		18	15-Nov-26	02-Dec-26	06-Aug-26 A	12-Jan-27	0.00	271,831.87	648,888.98	0%	41.89%	-120
PG-Q-PCL-20	As-Built Drawings	15	15-Nov-26	02-Dec-26	23-Sep-26 A	12-Jan-27	0.00	35,075.08	175,375.40	0%	20%	-79
PG-Q-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	15-Nov-26	26-Nov-26	06-Aug-26 A	04-Jan-27	0.00	236,756.79	473,513.58	0%	50%	-118
HAIL		113	25-Jun-26	26-Nov-26	09-Jul-26 A	16-Jan-27	1,601,229.16	1,621,207.24	2,300,016.12	69.62%	70.49%	-30
PROCUREMENT		59	25-Jun-26	26-Aug-26	06-Aug-26 A	03-Nov-26	516,988.47	460,355.44	516,988.47	100%	89.05%	-21
LONG LEAD ITEMS		59	25-Jun-26	26-Aug-26	06-Aug-26 A	03-Nov-26	423,859.72	388,815.26	423,859.72	100%	91.73%	-21
MANUFACTURE / FABRICATION		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
METAL WORK		25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	0%	0%	0
PG-H-PR-LL-MT-MF-20_R	Curtain Wall(Remaining)	25	25-Jun-26	23-Jul-26	03-Oct-26	31-Oct-26	0.00	0.00	0.00	100%	0%	0




Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
DELIVERY TO SITE		59	25-Jul-26	26-Aug-26	06-Aug-26 A	03-Nov-26	423,859.72	388,815.28	423,859.72	100%	91.73%	-46
EXTERNAL / LANDSCAPE WORK		29	25-Jul-26	05-Aug-26	06-Aug-26 A	04-Oct-26	72,919.30	66,425.88	72,919.30	100%	91.1%	-38
PG-H-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	05-Aug-26	20-Aug-26 A	04-Oct-26	28,474.61	24,203.41	28,474.61	100%	85%	-26
PG-H-PR-LL-LS-DL-10_R	Bike and Walk Path Materials(Remaining)	12	25-Jul-26	05-Aug-26	06-Aug-26 A	03-Oct-26	44,444.70	42,222.46	44,444.70	100%	95%	-37
SPORTS & RECREATIONAL FACILITIES WORK		12	25-Jul-26	05-Aug-26	06-Aug-26 A	04-Oct-26	163,721.25	150,559.76	163,721.25	100%	91.96%	-37
PG-H-PR-LL-SP-DL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	05-Aug-26	06-Aug-26 A	03-Oct-26	64,212.75	61,002.11	64,212.75	100%	95%	-37
PG-H-PR-LL-SP-DL-20_R	Tartan Floor(Remaining)	12	25-Jul-26	05-Aug-26	06-Aug-26 A	04-Oct-26	99,508.50	89,557.65	99,508.50	100%	90%	-37
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	4,801.84	3,841.47	4,801.84	100%	80%	-45
PG-H-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	688.66	550.93	688.66	100%	80%	-20
PG-H-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	03-Nov-26	4,113.18	3,290.54	4,113.18	100%	80%	-45
PLUMBING WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	9,372.51	7,498.01	9,372.51	100%	80%	-20
PG-H-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	05-Oct-26	9,372.51	7,498.01	9,372.51	100%	80%	-20
ELECTRICAL WORK		48	30-Jul-26	26-Aug-26	20-Aug-26 A	04-Oct-26	173,044.81	160,490.15	173,044.81	100%	92.74%	-14
PG-H-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	04-Oct-26	3,124.17	2,655.54	3,124.17	100%	85%	-23
PG-H-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	8	30-Jul-26	08-Aug-26	27-Aug-26 A	04-Oct-26	2,499.34	2,124.44	2,499.34	100%	85%	-23
PG-H-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	8	08-Aug-26	16-Aug-26	27-Aug-26 A	04-Oct-26	6,326.40	5,377.44	6,326.40	100%	85%	-23
PG-H-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	03-Oct-26	134,020.66	127,319.62	134,020.66	100%	95%	-25
PG-H-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	13-Aug-26	26-Aug-26	20-Aug-26 A	04-Oct-26	8,081.83	6,869.55	8,081.83	100%	85%	-26
PG-H-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	6,170.09	5,244.58	6,170.09	100%	85%	-20
PG-H-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	7,811.37	6,639.66	7,811.37	100%	85%	-20
PG-H-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	13-Aug-26	26-Aug-26	27-Aug-26 A	04-Oct-26	5,010.96	4,259.31	5,010.96	100%	85%	-20
SHORT LEAD ITEMS		39	04-Jul-26	16-Jul-26	20-Aug-26 A	15-Oct-26	93,128.75	71,540.16	93,128.75	100%	76.82%	-36
DELIVERY TO SITE		39	04-Jul-26	16-Jul-26	20-Aug-26 A	15-Oct-26	93,128.75	71,540.16	93,128.75	100%	76.82%	-36
EXTERNAL / LANDSCAPE WORK		12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	59,572.42	44,679.32	59,572.42	100%	75%	-21
PG-H-PR-SL-LS-DL-50_R	Thermoplastic pavement road marking(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	3,311.47	2,483.60	3,311.47	100%	75%	-21
PG-H-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	1,249.67	937.25	1,249.67	100%	75%	-21
PG-H-PR-SL-LS-DL-70_R	Trees(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	30,441.29	22,830.96	30,441.29	100%	75%	-21
PG-H-PR-SL-LS-DL-80_R	Lawn(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	05-Oct-26	24,570.00	18,427.50	24,570.00	100%	75%	-21
IRRIGATION WORK		17	04-Jul-26	16-Jul-26	20-Aug-26 A	04-Oct-26	30,845.88	26,219.00	30,845.88	100%	85%	-26
PG-H-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	12	04-Jul-26	16-Jul-26	20-Aug-26 A	04-Oct-26	3,403.35	2,892.85	3,403.35	100%	85%	-26
PG-H-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	12	04-Jul-26	16-Jul-26	27-Aug-26 A	04-Oct-26	27,442.53	23,326.15	27,442.53	100%	85%	-20
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	26-Sep-26 A	08-Oct-26	2,567.38	641.84	2,567.38	100%	25%	0
PG-H-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	26-Sep-26 A	08-Oct-26	2,567.38	641.84	2,567.38	100%	25%	0
FIRE FIGHTING WORK		12	04-Jul-26	16-Jul-26	03-Oct-26	15-Oct-26	143.07	0.00	143.07	100%	0%	0
PG-H-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	12	04-Jul-26	16-Jul-26	03-Oct-26	15-Oct-26	143.07	0.00	143.07	100%	0%	0
CONSTRUCTION STAGE		113	25-Jun-26	26-Nov-26	09-Jul-26 A	16-Jan-27	1,084,240.69	1,105,653.13	1,599,032.05	67.81%	69.15%	-30
PLAYGROUND AND LANDSCAPING WORKS		110	25-Jun-26	26-Nov-26	09-Jul-26 A	16-Jan-27	985,312.93	1,032,818.08	1,496,083.09	65.86%	69.03%	-30
PLAYGROUND WORKS		58	29-Jul-26	05-Nov-26	06-Aug-26 A	26-Oct-26	406,003.50	413,232.06	492,518.40	82.43%	83.9%	16
FOOTBALL PLAYGROUND WORKS		58	29-Jul-26	05-Nov-26	06-Aug-26 A	26-Oct-26	406,003.50	413,232.06	492,518.40	82.43%	83.9%	16
PG-H-CON-EX-FB-50	Goal Post Foundation	17	29-Jul-26	17-Aug-26	20-Aug-26 A	07-Oct-26	35,500.50	26,625.38	35,500.50	100%	75%	-23
PG-H-CON-EX-FB-120	Installation of Lighting System	13	18-Aug-26	01-Sep-26	27-Aug-26 A	12-Oct-26	48,720.00	31,668.00	48,720.00	100%	65%	-26
PG-H-CON-EX-FB-90	Turfing / Seeding Works	12	02-Sep-26	15-Sep-26	14-Aug-26 A	15-Oct-26	23,667.00	18,933.60	23,667.00	100%	80%	-40
PG-H-CON-EX-FB-40_R	Tartan flooring(Remaining)	15	16-Sep-26	04-Oct-26	06-Aug-26 A	15-Oct-26	298,116.00	309,582.00	343,980.00	86.67%	90%	-44
PG-H-CON-EX-FB-60	Goal Post Installation & Alignment	13	05-Oct-26	19-Oct-26	20-Aug-26 A	20-Oct-26	0.00	23,075.33	35,500.50	0%	65%	-39
PG-H-CON-EX-FB-110	Install Playground Benches	15	20-Oct-26	05-Nov-26	27-Aug-26 A	26-Oct-26	0.00	3,347.76	5,150.40	0%	65%	-36
GENERAL SITE WORKS		110	25-Jun-26	26-Nov-26	14-Aug-26 A	16-Jan-27	502,972.15	315,556.85	593,122.15	84.8%	53.2%	1
FENCE WORKS		37	23-Jul-26	16-Aug-26	27-Aug-26 A	13-Oct-26	39,491.28	13,163.76	39,491.28	100%	33.33%	-18
PG-H-CON-EX-GN-FN-30	Installation of Galvanized Steel Posts & Framing	9	23-Jul-26	02-Aug-26	27-Aug-26 A	04-Oct-26	13,163.76	10,531.01	13,163.76	100%	80%	-23
PG-H-CON-EX-GN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	8	03-Aug-26	11-Aug-26	27-Sep-26 A	08-Oct-26	13,163.76	2,632.75	13,163.76	100%	20%	-1
PG-H-CON-EX-GN-FN-50	Installation of Gates	4	12-Aug-26	16-Aug-26	08-Oct-26	13-Oct-26	13,163.76	0.00	13,163.76	100%	0%	0
MECHANICAL WORK		61	25-Jun-26	04-Aug-26	14-Aug-26 A	26-Oct-26	344,351.40	151,389.96	344,351.40	100%	43.96%	-27
STORM WATER AND UTILITY WORK		61	25-Jun-26	04-Aug-26	14-Aug-26 A	26-Oct-26	23,124.00	4,747.20	23,124.00	100%	20.53%	-27
PG-H-CON-EX-GN-M-20_R	Bedding preparation & level control(Remaining)	10	25-Jun-26	06-Jul-26	14-Aug-26 A	04-Oct-26	1,032.00	877.20	1,032.00	100%	85%	-33
PG-H-CON-EX-GN-M-30	Manhole Installation	5	07-Jul-26	12-Jul-26	27-Aug-26 A	05-Oct-26	5,160.00	3,870.00	5,160.00	100%	75%	-28
PG-H-CON-EX-GN-M-40	150 mm uPVC pipe laying & jointing	4	13-Jul-26	16-Jul-26	05-Oct-26	10-Oct-26	10,740.00	0.00	10,740.00	100%	0%	0
PG-H-CON-EX-GN-M-50	Concrete Encasement	3	18-Jul-26	20-Jul-26	10-Oct-26	13-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-60	Backfilling & Compaction	3	21-Jul-26	23-Jul-26	13-Oct-26	17-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-H-CON-EX-GN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	21-Oct-26	26-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		34	21-Jul-26	30-Jul-26	14-Aug-26 A	21-Oct-26	321,227.40	146,642.76	321,227.40	100%	45.65%	-50
PG-H-CON-EX-GN-M-80_R	Installation of HDPE Irrigation Pipe Network with Gate Valve and	2	21-Jul-26	23-Jul-26	14-Aug-26 A	17-Oct-26	108,345.60	92,093.76	108,345.60	100%	85%	-51
PG-H-CON-EX-GN-M-90	Installation of Irrigation Control System	3	25-Jul-26	27-Jul-26	26-Aug-26 A	18-Oct-26	90,915.00	54,549.00	90,915.00	100%	60%	-42
PG-H-CON-EX-GN-M-100	Installation of Bubblers and Sprinklers	3	28-Jul-26	30-Jul-26	18-Oct-26	21-Oct-26	121,966.80	0.00	121,966.80	100%	0%	0
ELECTRICAL WORK		4	05-Aug-26	09-Aug-26	20-Aug-26 A	27-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-55
POWER, LIGHTING & GROUNDING		4	05-Aug-26	09-Aug-26	20-Aug-26 A	27-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-55
PG-H-CON-EX-GN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	4	05-Aug-26	09-Aug-26	20-Aug-26 A	27-Oct-26	119,129.47	83,390.63	119,129.47	100%	70%	-55
PARKING WORK		5	10-Oct-26	14-Oct-26	20-Aug-26 A	22-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-100
PG-H-CON-EX-GN-PR-10	Installation of Parking Accessories	5	10-Oct-26	14-Oct-26	20-Aug-26 A	22-Dec-26	0.00	64,822.50	86,430.00	0%	75%	-100
SERVICE CONNECTION		11	31-Oct-26	26-Nov-26	20-Aug-26 A	16-Jan-27	0.00	2,790.00	3,720.00	0%	75%	-102
PG-H-CON-EX-GN-SC-20	HDPE Pipe Laying & Valve Installation	8	31-Oct-26	08-Nov-26	20-Aug-26 A	03-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-107
PG-H-CON-EX-GN-SC-40	Backfilling	8	18-Nov-26	26-Nov-26	27-Aug-26 A	16-Jan-27	0.00	892.80	1,488.00	0%	60%	-112
LANDSCAPING WORKS		43	20-Sep-26	09-Nov-26	09-Jul-26 A	07-Dec-26	70,560.00	300,409.25	404,665.26	17.44%	74.24%	-86
HARDSCAPE WORK		33	20-Sep-26	28-Oct-26	09-Jul-26 A	25-Nov-26	70,560.00	259,459.25	350,065.26	20.16%	74.12%	-86
PG-H-CON-EX-LS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	13	20-Sep-26	05-Oct-26	27-Aug-26 A	08-Nov-26	41,580.00	37,837.80	54,054.00	76.92%	70%	-48

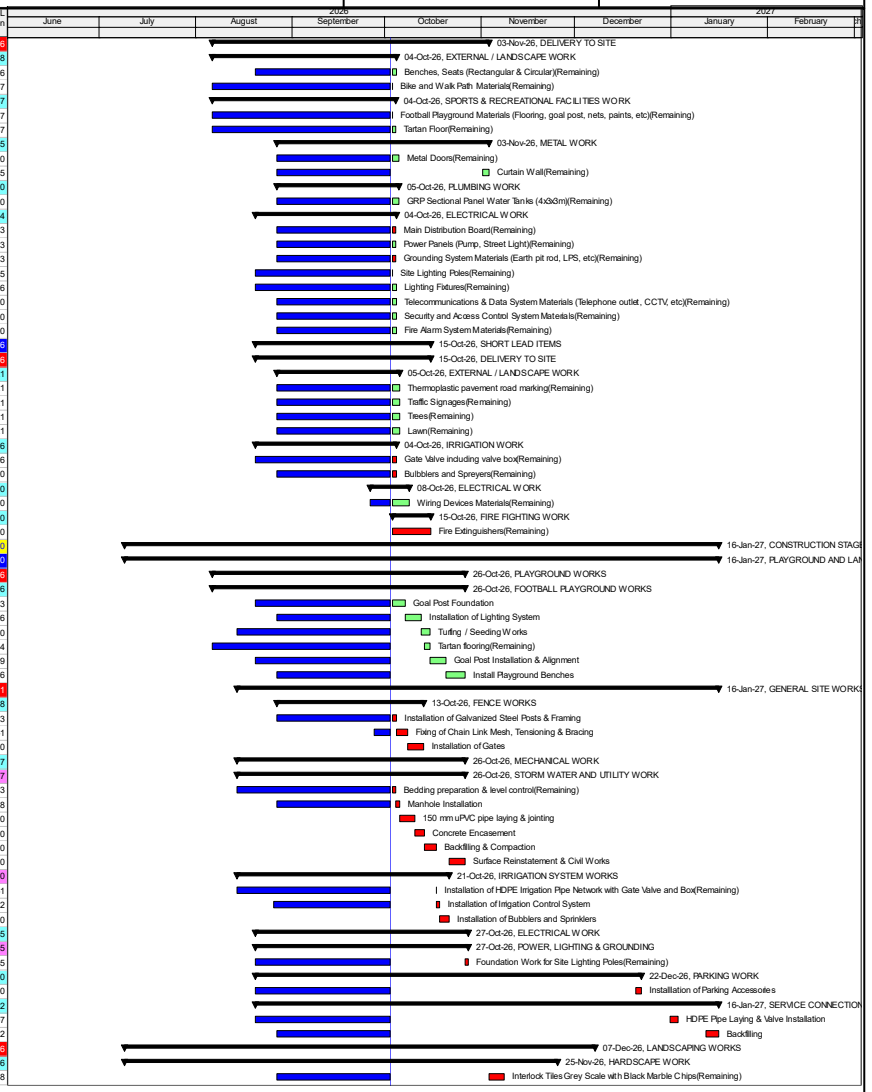


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-H-CON-EX-LS-HS-30_R	Stamped Concrete Floor(Remaining)	15	20-Sep-2	07-Oct-26	30-Jul-26 A	08-Nov-26	28,980.00	39,123.00	43,470.00	66.67%	90%	-70
PG-H-CON-EX-LS-HS-40_R	Bike Path and Walking Path Construction(Remaining)	8	08-Oct-26	17-Oct-26	09-Jul-26 A	19-Nov-26	0.00	140,741.55	148,149.00	0%	95%	-105
PG-H-CON-EX-LS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	18-Oct-26	28-Oct-26	30-Jul-26 A	25-Nov-26	0.00	41,756.90	104,392.26	0%	40%	-91
SOFTSCAPE WORK		7	02-Nov-2	09-Nov-26	27-Aug-26 A	07-Dec-26	0.00	40,950.00	54,600.00	0%	75%	-80
PG-H-CON-EX-LS-SS-20_R	Lawn Area Preparation &Planting / Turfing(Remaining)	7	02-Nov-2	09-Nov-26	27-Aug-26 A	07-Dec-26	0.00	40,950.00	54,600.00	0%	75%	-80
TANK WORKS		62	02-Jul-26	31-Aug-26	14-Aug-26 A	28-Oct-26	5,777.28	3,619.92	5,777.28	100%	62.66%	-11
SEPTIC TANK		62	02-Jul-26	31-Aug-26	14-Aug-26 A	28-Oct-26	5,777.28	3,619.92	5,777.28	100%	62.66%	-11
PG-H-CON-EX-TW-ST-40	RCC Wall	7	02-Jul-26	09-Jul-26	14-Aug-26 A	05-Oct-26	2,757.60	1,930.32	2,757.60	100%	70%	-36
PG-H-CON-EX-TW-ST-50	RCC Slab	7	11-Jul-26	18-Jul-26	27-Aug-26 A	07-Oct-26	2,599.38	1,689.60	2,599.38	100%	65%	-28
PG-H-CON-EX-TW-ST-60	Finishing Work	7	17-Aug-2	24-Aug-26	13-Oct-26	21-Oct-26	252.18	0.00	252.18	100%	0%	0
PG-H-CON-EX-TW-ST-70	Backfilling	6	25-Aug-2	31-Aug-26	21-Oct-26	28-Oct-26	168.12	0.00	168.12	100%	0%	0
TOILET BUILDING WORKS		72	03-Aug-2	05-Oct-26	30-Jul-26 A	14-Oct-26	98,927.76	72,835.04	102,948.96	96.09%	70.75%	-11
CIVIL WORK		39	09-Sep-2	05-Oct-26	20-Aug-26 A	14-Oct-26	32,161.80	25,152.12	36,183.00	88.89%	69.51%	-25
ARCHITECTURAL WORK		39	09-Sep-2	05-Oct-26	20-Aug-26 A	14-Oct-26	32,161.80	25,152.12	36,183.00	88.89%	69.51%	-25
GENERAL FINISHES		21	09-Sep-2	27-Sep-26	20-Aug-26 A	14-Oct-26	16,505.40	11,553.78	16,505.40	100%	70%	-32
PG-H-CON-B-AR-GF-40	Wall Paint	3	09-Sep-2	12-Sep-26	20-Aug-26 A	10-Oct-26	2,958.00	2,070.60	2,958.00	100%	70%	-40
PG-H-CON-B-AR-GF-50	Epoxy Flooring	7	13-Sep-2	20-Sep-26	20-Aug-26 A	12-Oct-26	273.60	191.52	273.60	100%	70%	-38
PG-H-CON-B-AR-GF-60	Install Doors & Windows	5	21-Sep-2	27-Sep-26	27-Aug-26 A	14-Oct-26	13,273.80	9,291.66	13,273.80	100%	70%	-36
WET AREA FINISHES		4	01-Oct-26	05-Oct-26	27-Aug-26 A	12-Oct-26	1,340.40	3,485.04	5,361.60	25%	65%	-34
PG-H-CON-B-AR-WF-60	Install Doors	4	01-Oct-26	05-Oct-26	27-Aug-26 A	12-Oct-26	1,340.40	3,485.04	5,361.60	25%	65%	-34
ROOF FINISHES		36	19-Sep-2	26-Sep-26	20-Aug-26 A	12-Oct-26	14,316.00	10,113.30	14,316.00	100%	70.64%	-39
PG-H-CON-B-AR-RF-10	Waterproofing on Floor	4	19-Sep-2	22-Sep-26	20-Aug-26 A	12-Oct-26	4,158.00	2,494.80	4,158.00	100%	60%	-41
PG-H-CON-B-AR-RF-20	Epoxy Flooring and Finishes	2	24-Sep-2	26-Sep-26	27-Aug-26 A	12-Oct-26	10,158.00	7,618.50	10,158.00	100%	75%	-37
MEP WORK		62	03-Aug-2	08-Sep-26	30-Jul-26 A	08-Oct-26	66,765.96	47,682.92	66,765.96	100%	71.42%	-28
MECANICAL WORKS		54	03-Aug-2	23-Aug-26	30-Jul-26 A	07-Oct-26	50,502.24	33,858.76	50,502.24	100%	67.04%	-40
SEWER AND DRAINAGE SYSTEM		47	03-Aug-2	23-Aug-26	30-Jul-26 A	07-Oct-26	6,451.44	2,741.86	6,451.44	100%	42.5%	-40
PG-H-CON-B-GF-DR-10	Sewer and Drainge System Main Lines Installation	2	03-Aug-2	04-Aug-26	30-Jul-26 A	03-Oct-26	3,225.72	2,741.86	3,225.72	100%	85%	-52
PG-H-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	22-Aug-2	23-Aug-26	05-Oct-26	07-Oct-26	3,225.72	0.00	3,225.72	100%	0%	0
HVAC SYSTEM		3	12-Aug-2	15-Aug-26	26-Sep-26 A	04-Oct-26	7,684.80	3,842.40	7,684.80	100%	50%	-5
PG-H-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	3	12-Aug-2	15-Aug-26	26-Sep-26 A	04-Oct-26	7,684.80	3,842.40	7,684.80	100%	50%	-5
WATER SUPPLY SYSTEM		3	18-Aug-2	20-Aug-26	27-Aug-26 A	05-Oct-26	36,366.00	27,274.50	36,366.00	100%	75%	-29
PG-H-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	18-Aug-2	20-Aug-26	27-Aug-26 A	05-Oct-26	36,366.00	27,274.50	36,366.00	100%	75%	-29
ELECTRICAL WORKS		11	27-Aug-2	08-Sep-26	20-Aug-26 A	08-Oct-26	16,263.72	13,824.16	16,263.72	100%	85%	-31
PG-H-CON-B-GF-EL-20	Electrical Light Fixtures Installation	2	27-Aug-2	29-Aug-26	20-Aug-26 A	07-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-39
PG-H-CON-B-GF-EL-30	Fire Alarm Devices Installation	3	30-Aug-2	01-Sep-26	20-Aug-26 A	07-Oct-26	1,983.60	1,686.06	1,983.60	100%	85%	-38
PG-H-CON-B-GF-EL-40	Telecom & CCTV Devices Installation	3	02-Sep-2	05-Sep-26	20-Aug-26 A	08-Oct-26	4,959.00	4,215.15	4,959.00	100%	85%	-38
PG-H-CON-B-GF-EL-50	Electrical & ELV Wiring Works	3	06-Sep-2	08-Sep-26	20-Aug-26 A	08-Oct-26	7,337.52	6,236.89	7,337.52	100%	85%	-39
PROJECT CLOSOUT		10	02-Nov-2	14-Nov-26	06-Aug-26 A	07-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-95
PG-H-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	10	02-Nov-2	14-Nov-26	06-Aug-26 A	07-Dec-26	0.00	55,198.68	183,995.60	0%	30%	-95
TABUK		144	25-Jun-26	09-Dec-26	12-Jul-26 A	28-Jan-27	2,941,798.83	1,976,993.88	3,782,887.82	77.77%	52.26%	-30
PROCUREMENT		63	25-Jun-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,157,429.76	1,184,097.22	2,157,429.76	100%	54.88%	-9
LONG LEAD ITEMS		54	01-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,118,427.42	1,150,173.89	2,118,427.42	100%	54.29%	-15
MANUFACTURE / FABRICATION		26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-14
SPORTS & RECREATIONAL FACILITIES WORK		26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-14
PG-T-PR-LL-SPMF-50	Air Dome Materials	26	18-Jul-26	16-Aug-26	27-Aug-26 A	14-Oct-26	0.00	0.00	0.00	100%	60%	-14
DELIVERY TO SITE		54	01-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,118,427.42	1,150,173.89	2,118,427.42	100%	54.29%	-15
EXTERNAL / LANDSCAPE WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-30
PG-T-PR-LL-LS-DL-20_R	Benches, Seats (Rectangular & Circular)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	13,928.65	12,535.79	13,928.65	100%	90%	-30
SPORTS & RECREATIONAL FACILITIES WORK		27	25-Jul-26	27-Aug-26	06-Aug-26 A	21-Oct-26	2,013,812.01	1,060,965.95	2,013,812.01	100%	52.68%	-34
PG-T-PR-LL-SPDL-10_R	Football Playground Materials (Flooring, goal post, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	58,731.75	52,858.58	58,731.75	100%	90%	-30
PG-T-PR-LL-SPDL-20_R	Basketball Playground Materials (Flooring, basketball poll, nets, paints,	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	10,152.00	9,136.80	10,152.00	100%	90%	-30
PG-T-PR-LL-SPDL-30_R	Padel Playgound Materials (Fence, tempered glass, etc)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	26,778.60	24,100.74	26,778.60	100%	90%	-30
PG-T-PR-LL-SPDL-40_R	Tartan Floor(Remaining)	12	25-Jul-26	06-Aug-26	06-Aug-26 A	04-Oct-26	39,487.50	35,538.75	39,487.50	100%	90%	-37
PG-T-PR-LL-SPDL-50	Air Dome Materials	10	17-Aug-2	27-Aug-26	20-Aug-26 A	21-Oct-26	1,878,662.16	939,331.08	1,878,662.16	100%	50%	-42
METAL WORK		12	25-Jul-26	06-Aug-26	27-Aug-26 A	08-Oct-26	4,001.54	2,401.70	4,001.54	100%	60.02%	-23
PG-T-PR-LL-MT-DL-10_R	Metal Doors(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	04-Oct-26	573.89	516.50	573.89	100%	90%	-19
PG-T-PR-LL-MT-DL-20_R	Curtain Wall(Remaining)	12	25-Jul-26	06-Aug-26	27-Aug-26 A	08-Oct-26	3,427.65	1,885.21	3,427.65	100%	55%	-23
PLUMBING WORK		12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-30
PG-T-PR-LL-PB-DL-20_R	GRP Sectional Panel Water Tanks (4x3x3m)(Remaining)	12	25-Jul-26	06-Aug-26	14-Aug-26 A	04-Oct-26	6,248.34	5,623.51	6,248.34	100%	90%	-30
IRRIGATION WORK		4	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-32
PG-T-PR-LL-IR-DL-20_R	Irrigation Control System(Remaining)	4	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	16,364.70	14,728.23	16,364.70	100%	90%	-32
ELECTRICAL WORK		54	25-Jul-26	24-Aug-26	14-Aug-26 A	05-Oct-26	64,072.19	53,918.72	64,072.19	100%	84.15%	-16
PG-T-PR-LL-EL-DL-50_R	Grounding System Materials (Earth pit rod, LPS, etc)(Remaining)	4	25-Jul-26	28-Jul-26	14-Aug-26 A	03-Oct-26	3,615.08	3,072.82	3,615.08	100%	85%	-38
PG-T-PR-LL-EL-DL-10_R	Main Distribution Board(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	1,785.24	1,517.45	1,785.24	100%	85%	-31
PG-T-PR-LL-EL-DL-20_R	Power Panels (Pump, Street Light)(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	1,428.19	1,213.96	1,428.19	100%	85%	-31
PG-T-PR-LL-EL-DL-30_R	Site Lighting Poles(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	41,772.67	35,506.77	41,772.67	100%	85%	-31
PG-T-PR-LL-EL-DL-40_R	Lighting Fixtures(Remaining)	12	11-Aug-2	24-Aug-26	14-Aug-26 A	04-Oct-26	4,618.19	3,925.46	4,618.19	100%	85%	-31
PG-T-PR-LL-EL-DL-60_R	Telecommunications & Data System Materials (Telephone outlet, CCTV,	12	11-Aug-2	24-Aug-26	27-Aug-26 A	05-Oct-26	3,525.77	2,820.61	3,525.77	100%	80%	-20
PG-T-PR-LL-EL-DL-70_R	Security and Access Control System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	05-Oct-26	4,463.64	3,570.91	4,463.64	100%	80%	-20
PG-T-PR-LL-EL-DL-80_R	Fire Alarm System Materials(Remaining)	12	11-Aug-2	24-Aug-26	27-Aug-26 A	05-Oct-26	2,863.40	2,290.72	2,863.40	100%	80%	-20
SHORT LEAD ITEMS		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	33,923.33	39,002.34	100%	86.98%	-29
DELIVERY TO SITE		52	25-Jun-26	22-Jul-26	07-Aug-26 A	08-Oct-26	39,002.34	33,923.33	39,002.34	100%	86.98%	-29
EXTERNAL / LANDSCAPE WORK		10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	19,978.06	17,980.25	19,978.06	100%	90%	-21

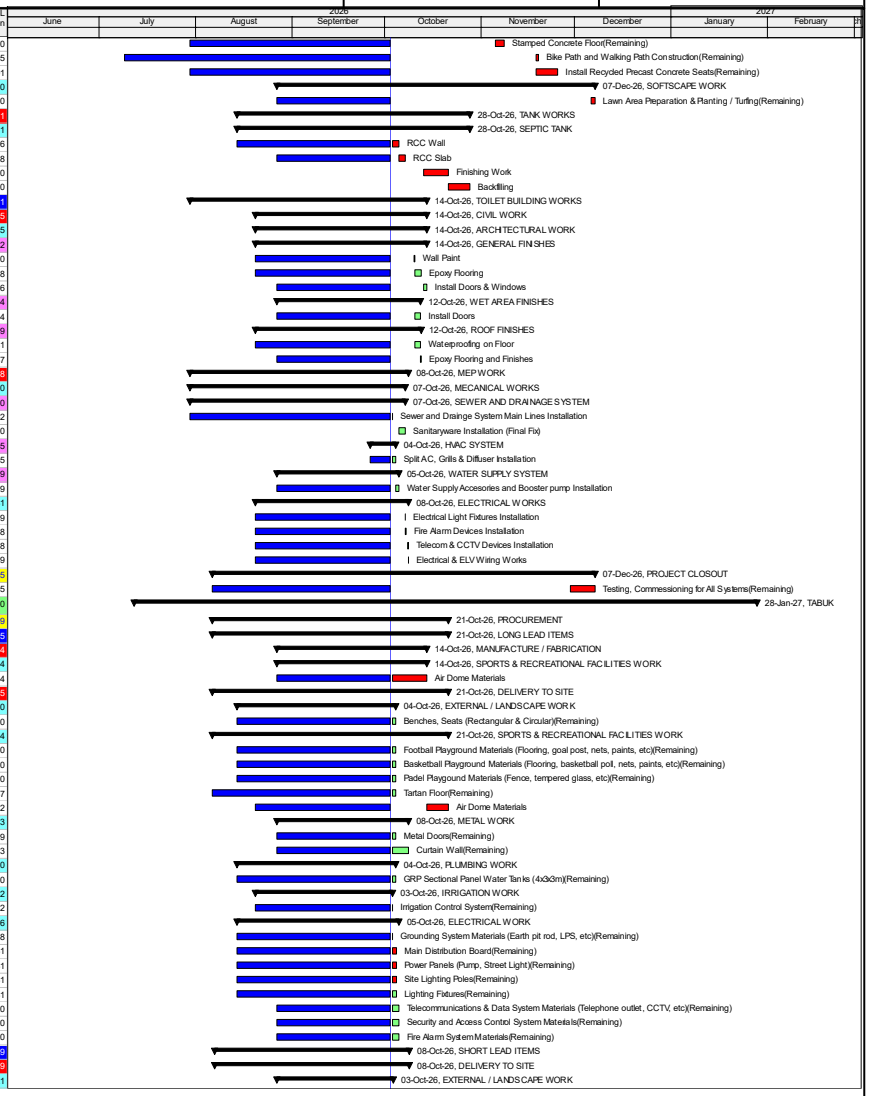


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-PR-SL-LS-DL-60_R	Traffic Signages(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	714.10	642.69	714.10	100%	90%	-21
PG-T-PR-SL-LS-DL-70_R	Trees(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	8,301.96	7,471.76	8,301.96	100%	90%	-21
PG-T-PR-SL-LS-DL-80_R	Lawn(Remaining)	10	12-Jul-26	22-Jul-26	27-Aug-26 A	03-Oct-26	10,962.00	9,865.80	10,962.00	100%	90%	-21
METAL WORK		12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Oct-26	1,724.00	862.00	1,724.00	100%	50%	-1
PG-T-PR-SL-MT-DL-10_R	Galvanized Steel Ladder(Remaining)	12	25-Jun-26	08-Jul-26	23-Sep-26 A	08-Oct-26	1,302.70	651.35	1,302.70	100%	50%	-1
PG-T-PR-SL-MT-DL-20_R	Galvanized Steel Roof Scupper(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Oct-26	112.75	56.38	112.75	100%	50%	-1
PG-T-PR-SL-MT-DL-30_R	Galvanized Steel Cover with frame(Remaining)	12	25-Jun-26	08-Jul-26	24-Sep-26 A	08-Oct-26	308.56	154.28	308.56	100%	50%	-1
IRRIGATION WORK		14	25-Jun-26	05-Jul-26	07-Aug-26 A	03-Oct-26	14,977.04	13,479.33	14,977.04	100%	90%	-39
PG-T-PR-SL-IR-DL-10_R	Gate Valve including valve box(Remaining)	9	25-Jun-26	05-Jul-26	07-Aug-26 A	03-Oct-26	1,859.76	1,673.78	1,859.76	100%	90%	-39
PG-T-PR-SL-IR-DL-20_R	Bubblers and Spreyers(Remaining)	9	25-Jun-26	05-Jul-26	20-Aug-26 A	03-Oct-26	13,117.28	11,805.55	13,117.28	100%	90%	-28
ELECTRICAL WORK		12	04-Jul-26	16-Jul-26	19-Sep-26 A	06-Oct-26	2,200.61	1,540.43	2,200.61	100%	70%	-3
PG-T-PR-SL-EL-DL-10_R	Wiring Devices Materials(Remaining)	12	04-Jul-26	16-Jul-26	19-Sep-26 A	06-Oct-26	2,200.61	1,540.43	2,200.61	100%	70%	-3
FIRE FIGHTING WORK		9	30-Jun-26	09-Jul-26	27-Sep-26 A	07-Oct-26	122.63	61.32	122.63	100%	50%	-1
PG-T-PR-SL-FF-DL-10_R	Fire Extinguishers(Remaining)	9	30-Jun-26	09-Jul-26	27-Sep-26 A	07-Oct-26	122.63	61.32	122.63	100%	50%	-1
CONSTRUCTION STAGE		132	25-Jun-26	07-Dec-26	12-Jul-26 A	03-Jan-27	784,369.06	616,850.75	1,205,219.42	65.08%	51.18%	-9
PLAYGROUND AND LANDSCAPING WORKS		132	25-Jun-26	07-Dec-26	12-Jul-26 A	03-Jan-27	494,289.06	588,291.30	892,378.96	55.39%	65.92%	-9
PLAYGROUND WORKS		68	08-Aug-26	07-Dec-26	14-Aug-26 A	23-Nov-26	82,062.54	126,192.44	194,465.34	42.2%	64.89%	18
FOOTBALL PLAYGROUND WORKS		55	19-Aug-26	17-Nov-26	14-Aug-26 A	27-Oct-26	48,027.00	68,855.79	109,254.66	43.96%	63.02%	15
PG-T-CON-EXFB-120	Installation of Lighting System	13	19-Aug-26	02-Sep-26	20-Aug-26 A	05-Oct-26	24,360.00	19,488.00	24,360.00	100%	80%	-26
PG-T-CON-EXFB-90	Turfing / Seeding Works	12	03-Sep-26	16-Sep-26	14-Aug-26 A	06-Oct-26	23,667.00	21,300.30	23,667.00	100%	90%	-33
PG-T-CON-EXFB-60	Goal Post Installation & Alignment	15	06-Oct-26	22-Oct-26	20-Aug-26 A	11-Oct-26	0.00	26,625.38	35,500.50	0%	75%	-29
PG-T-CON-EXFB-110	Install Playground Benches	12	24-Oct-26	05-Nov-26	27-Aug-26 A	15-Oct-26	0.00	1,442.11	2,060.16	0%	70%	-29
PG-T-CON-EXFB-100	Markings and Signages	10	07-Nov-26	17-Nov-26	15-Oct-26	27-Oct-26	0.00	0.00	23,667.00	0%	0%	0
BASKETBALL PLAYGROUND WORKS		51	31-Aug-26	17-Nov-26	20-Aug-26 A	02-Nov-26	22,546.92	24,819.01	43,200.72	52.19%	57.45%	4
PG-T-CON-EXBB-80	Court Line Marking	16	31-Aug-26	17-Sep-26	20-Aug-26 A	06-Oct-26	13,091.76	11,128.00	13,091.76	100%	85%	-24
PG-T-CON-EXBB-60	Basketball Pole Installation & Alignment	18	19-Sep-26	10-Oct-26	20-Aug-26 A	11-Oct-26	9,455.16	12,377.66	15,472.08	61.11%	80%	-25
PG-T-CON-EXBB-90	Backboard & Hoop Installation	17	11-Oct-26	29-Oct-26	11-Oct-26	31-Oct-26	0.00	0.00	13,091.76	0%	0%	0
PG-T-CON-EXBB-100	Install Playground Benches	16	31-Oct-26	17-Nov-26	27-Aug-26 A	02-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-41
PADEL PLAYGROUND WORKS		54	08-Aug-26	07-Dec-26	20-Aug-26 A	23-Nov-26	11,488.62	32,517.64	42,009.96	27.35%	77.4%	23
PG-T-CON-EXPD-40	Steel Structure & Fence Supports Installation	20	08-Aug-26	30-Aug-26	20-Aug-26 A	07-Oct-26	3,534.96	3,004.72	3,534.96	100%	85%	-20
PG-T-CON-EXPD-60	Chain Link Fence & Gates Installation	18	31-Aug-26	20-Sep-26	20-Aug-26 A	10-Oct-26	5,302.44	4,507.07	5,302.44	100%	85%	-25
PG-T-CON-EXPD-50	Tempered Glass Installation	18	21-Sep-26	12-Oct-26	10-Oct-26	31-Oct-26	2,651.22	0.00	5,302.44	50%	0%	0
PG-T-CON-EXPD-30_R	Tartan Flooring Layers(Remaining)	17	13-Oct-26	01-Nov-26	20-Aug-26 A	02-Nov-26	0.00	23,692.50	26,325.00	0%	90%	-46
PG-T-CON-EXPD-80	Install Playground Benches	15	21-Nov-26	07-Dec-26	27-Aug-26 A	23-Nov-26	0.00	1,313.35	1,545.12	0%	85%	-60
GENERAL SITE WORKS		132	25-Jun-26	23-Nov-26	12-Jul-26 A	03-Jan-27	382,475.94	278,888.83	439,891.54	86.95%	63.4%	-21
FENCE WORKS		45	27-Jul-26	17-Aug-26	20-Aug-26 A	14-Oct-26	19,745.64	8,227.35	19,745.64	100%	41.67%	-28
PG-T-CON-EXGN-FN-30	Installation of Galvanized Steel Posts & Framing	7	27-Jul-26	03-Aug-26	20-Aug-26 A	04-Oct-26	6,581.88	5,594.60	6,581.88	100%	85%	-30
PG-T-CON-EXGN-FN-40	Fixing of Chain Link Mesh, Tensioning & Bracing	6	04-Aug-26	10-Aug-26	20-Sep-26 A	07-Oct-26	6,581.88	2,632.75	6,581.88	100%	40%	-9
PG-T-CON-EXGN-FN-50	Installation of Gates	6	11-Aug-26	17-Aug-26	07-Oct-26	14-Oct-26	6,581.88	0.00	6,581.88	100%	0%	0
MECHANICAL WORK		72	01-Jul-26	10-Aug-26	12-Jul-26 A	25-Oct-26	206,336.28	167,571.01	206,336.28	100%	81.21%	-55
STORM WATER AND UTILITY WORK		49	01-Jul-26	04-Aug-26	20-Aug-26 A	19-Oct-26	22,092.00	9,498.00	22,092.00	100%	42.99%	-21
PG-T-CON-EXGN-M-30	Manhole Installation	5	01-Jul-26	06-Jul-26	20-Aug-26 A	03-Oct-26	5,160.00	4,128.00	5,160.00	100%	80%	-32
PG-T-CON-EXGN-M-40	150 mm uPVC pipe laying & jointing	4	07-Jul-26	11-Jul-26	20-Sep-26 A	05-Oct-26	10,740.00	5,370.00	10,740.00	100%	50%	-9
PG-T-CON-EXGN-M-50	Concrete Encasement	3	12-Jul-26	14-Jul-26	06-Oct-26	08-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-60	Backfilling & Compaction	3	15-Jul-26	18-Jul-26	10-Oct-26	12-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
PG-T-CON-EXGN-M-70	Surface Reinstatement & Civil Works	4	01-Aug-26	04-Aug-26	14-Oct-26	19-Oct-26	2,064.00	0.00	2,064.00	100%	0%	0
IRRIGATION SYSTEM WORKS		43	14-Jul-26	30-Jul-26	12-Jul-26 A	14-Oct-26	183,926.34	158,073.01	183,926.34	100%	85.94%	-66
PG-T-CON-EXGN-M-80_R	Installation of HDPE Irigation Pipe Network with Gate Valve and	4	14-Jul-26	18-Jul-26	12-Jul-26 A	12-Oct-26	34,712.34	31,241.11	34,712.34	100%	90%	-75
PG-T-CON-EXGN-M-90	Installation of Irrigation Control System	6	19-Jul-26	25-Jul-26	20-Aug-26 A	13-Oct-26	90,915.00	77,277.75	90,915.00	100%	85%	-40
PG-T-CON-EXGN-M-100	Installation of Bubblers and Sprinklers	5	26-Jul-26	30-Jul-26	20-Aug-26 A	14-Oct-26	58,299.00	49,554.15	58,299.00	100%	85%	-42
FIRE PROTECTION SYSTEM		5	05-Aug-26	10-Aug-26	19-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
PG-T-CON-EXGN-M-110	Fire Extinguisher Installation	5	05-Aug-26	10-Aug-26	19-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
ELECTRICAL WORK		99	25-Jun-26	26-Oct-26	20-Aug-26 A	17-Dec-26	156,394.02	90,258.87	198,713.62	78.7%	45.42%	4
POWER, LIGHTING & GROUNDING		64	25-Jun-26	14-Sep-26	20-Aug-26 A	12-Nov-26	155,567.62	81,629.67	155,567.62	100%	52.47%	-1
PG-T-CON-EXGN-E-20_R	Foundation Work for Site Lighting Poles(Remaining)	21	25-Jun-26	19-Jul-26	20-Aug-26 A	07-Oct-26	55,696.90	44,557.52	55,696.90	100%	80%	-19
PG-T-CON-EXGN-E-30	Lightning Protection System (LPS)	8	11-Aug-26	19-Aug-26	20-Aug-26 A	26-Oct-26	8,265.00	7,025.25	8,265.00	100%	85%	-49
PG-T-CON-EXGN-E-40	KWH Meter and MDB Installation	5	25-Aug-26	30-Aug-26	17-Sep-26 A	01-Nov-26	4,586.70	458.67	4,586.70	100%	10%	-32
PG-T-CON-EXGN-E-50	Power Panels and Distribution Boards	7	31-Aug-26	07-Sep-26	17-Sep-26 A	08-Nov-26	17,397.90	1,739.79	17,397.90	100%	10%	-37
PG-T-CON-EXGN-E-60	Site Lighting Poles Installation	6	08-Sep-26	14-Sep-26	17-Sep-26 A	12-Nov-26	69,621.12	27,848.45	69,621.12	100%	40%	-41
ELV SYSTEMS (TELECOM, DATA, AV & CCTV)		25	28-Sep-26	26-Oct-26	22-Sep-26 A	17-Dec-26	826.40	8,629.20	43,146.00	1.92%	20%	-48
PG-T-CON-EXGN-E-90	ELV Containment & Cabling Works	3	28-Sep-26	30-Sep-26	22-Sep-26 A	26-Nov-26	619.80	123.96	619.80	100%	20%	-53
PG-T-CON-EXGN-E-100	Fiber Optic Pull Box Installation	3	01-Oct-26	04-Oct-26	22-Sep-26 A	30-Nov-26	206.60	123.96	619.80	33.33%	20%	-55
PG-T-CON-EXGN-E-110	Telephone and Data Outlet Installation	4	05-Oct-26	08-Oct-26	22-Sep-26 A	03-Dec-26	0.00	743.76	3,718.80	0%	20%	-57
PG-T-CON-EXGN-E-120	Telecom Equipment and AV HDMI Installation	4	10-Oct-26	13-Oct-26	22-Sep-26 A	07-Dec-26	0.00	3,049.82	15,249.12	0%	20%	-60
PG-T-CON-EXGN-E-130	CCTV Rack / Cabinet Installation	4	14-Oct-26	18-Oct-26	22-Sep-26 A	10-Dec-26	0.00	289.30	1,446.48	0%	20%	-64
PG-T-CON-EXGN-E-140	NVR and CCTV Monitor Installation	4	19-Oct-26	22-Oct-26	22-Sep-26 A	14-Dec-26	0.00	1,322.40	6,612.00	0%	20%	-67
PG-T-CON-EXGN-E-150	IP Camera Installation	3	24-Oct-26	26-Oct-26	22-Sep-26 A	17-Dec-26	0.00	2,976.00	14,880.00	0%	20%	-70
PARKING WORK		7	27-Oct-26	03-Nov-26	20-Aug-26 A	19-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-95
PG-T-CON-EXGN-PR-10	Installation of Parking Accessories	7	27-Oct-26	03-Nov-26	20-Aug-26 A	19-Dec-26	0.00	10,934.40	12,864.00	0%	85%	-95
SERVICE CONNECTION		10	12-Nov-26	23-Nov-26	14-Aug-26 A	03-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-111
PG-T-CON-EXGN-SC-20	HDPE Pipe Laying & Valve Installation	10	12-Nov-26	23-Nov-26	14-Aug-26 A	03-Jan-27	0.00	1,897.20	2,232.00	0%	85%	-111
LANDSCAPING WORKS		38	28-Sep-26	22-Nov-26	12-Jul-26 A	02-Dec-26	24,393.60	182,106.99	252,665.10	9.65%	72.07%	-74
HARDSCAPE WORK		38	28-Sep-26	22-Nov-26	30-Jul-26 A	02-Dec-26	24,393.60	146,435.79	170,003.10	14.35%	86.14%	-58

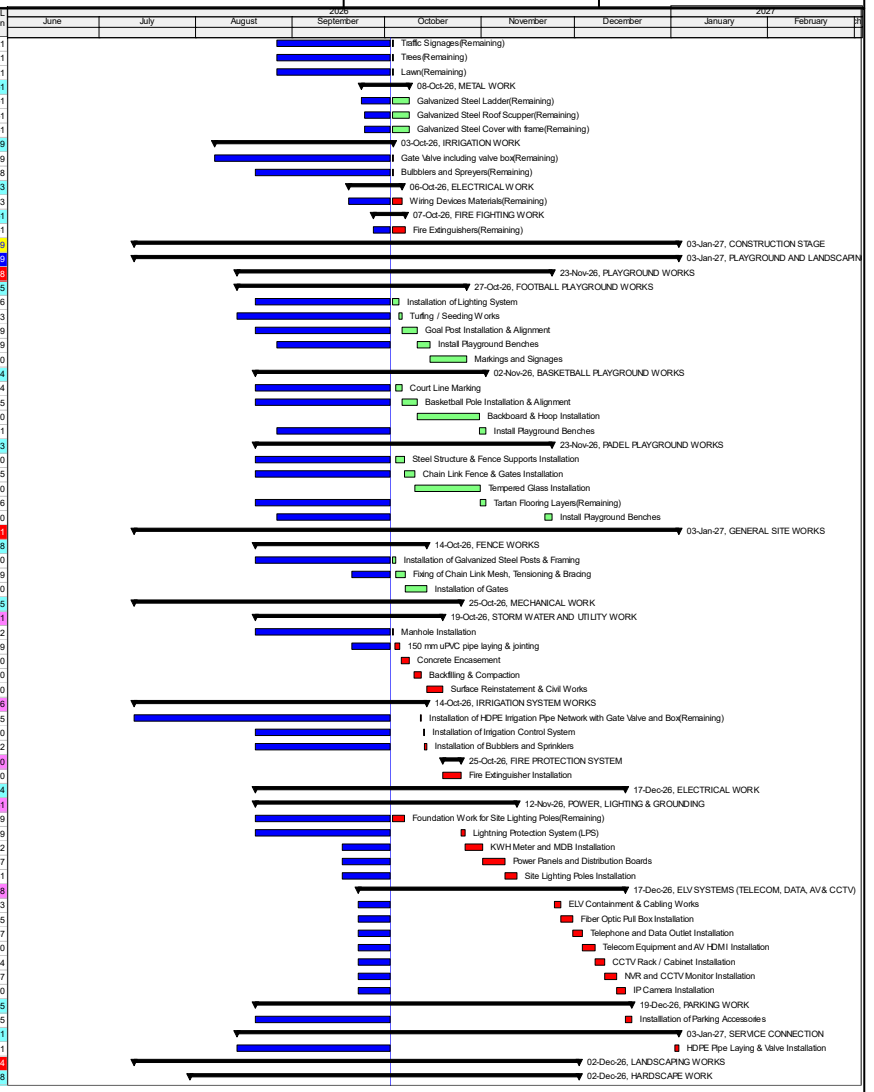

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PG-T-CON-EXLS-HS-20_R	Interlock Tiles Grey Scale with Black Marble Chips(Remaining)	10	28-Sep-26	08-Oct-26	27-Aug-26 A	09-Nov-26	24,393.60	51,836.40	60,984.00	40%	85%	-53
PG-T-CON-EXLS-HS-30_R	Stamped Concrete Floor(Remaining)	10	10-Oct-26	20-Oct-26	30-Jul-26 A	09-Nov-26	0.00	39,123.00	43,470.00	0%	90%	-77
PG-T-CON-EXLS-HS-50_R	Install Recycled Precast Concrete Seats(Remaining)	10	31-Oct-26	10-Nov-26	30-Jul-26 A	23-Nov-26	0.00	54,123.39	60,137.10	0%	90%	-89
PG-T-CON-EXLS-HS-60	Install Recycled Precast Concrete Trash Bins	10	11-Nov-26	22-Nov-26	23-Sep-26 A	02-Dec-26	0.00	1,353.00	5,412.00	0%	25%	-49
SOFTSCAPE WORK		20	10-Oct-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	35,671.20	82,662.00	0%	43.15%	-84
PG-T-CON-EXLS-SS-10	Planting Trees	12	10-Oct-26	22-Oct-26	22-Sep-26 A	22-Nov-26	0.00	4,612.20	46,122.00	0%	10%	-40
PG-T-CON-EXLS-SS-20_R	Lawn Area Preparation & Planting / Turfing(Remaining)	6	16-Nov-26	22-Nov-26	12-Jul-26 A	02-Dec-26	0.00	31,059.00	36,540.00	0%	85%	-116
TANK WORKS		58	07-Jul-26	01-Aug-26	14-Aug-26 A	24-Oct-26	5,356.98	1,103.04	5,356.98	100%	20.59%	-37
SEPTIC TANK		58	07-Jul-26	01-Aug-26	14-Aug-26 A	24-Oct-26	5,356.98	1,103.04	5,356.98	100%	20.59%	-37
PG-T-CON-EXTW-ST-40	RCC Wall	9	07-Jul-26	16-Jul-26	14-Aug-26 A	08-Oct-26	2,757.60	1,103.04	2,757.60	100%	40%	-37
PG-T-CON-EXTW-ST-50	RCC Slab	13	18-Jul-26	01-Aug-26	08-Oct-26	24-Oct-26	2,599.38	0.00	2,599.38	100%	0%	0
AIR DOME CONSTRUCTION		9	26-Aug-26	05-Sep-26	14-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
CIVIL WORK		9	26-Aug-26	05-Sep-26	14-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
PG-T-CON-EXAD-CL-70	Installation of Steel Cable Structural System	9	26-Aug-26	05-Sep-26	14-Oct-26	25-Oct-26	250,488.29	0.00	250,488.29	100%	0%	0
TOILET BUILDING WORKS		16	31-Aug-26	28-Oct-26	19-Sep-26 A	13-Oct-26	39,591.72	28,559.45	62,352.18	63.5%	45.8%	30
CIVIL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	6,033.03	14,939.40	0%	40.38%	-5
ARCHITECTURAL WORK		5	11-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	6,033.03	14,939.40	0%	40.38%	-5
WET AREA FINISHES		2	11-Oct-26	12-Oct-26	23-Sep-26 A	11-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-12
PG-T-CON-BARW-F-60	Install Doors	2	11-Oct-26	12-Oct-26	23-Sep-26 A	11-Oct-26	0.00	2,680.80	5,361.60	0%	50%	-12
ROOF FINISHES		3	24-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-16
PG-T-CON-BARRF-30	Steel ladder and Steel roof scupper Installation	3	24-Oct-26	26-Oct-26	19-Sep-26 A	12-Oct-26	0.00	3,352.23	9,577.80	0%	35%	-16
MEP WORK		16	31-Aug-26	28-Oct-26	20-Sep-26 A	13-Oct-26	39,591.72	22,526.42	47,412.78	83.5%	47.51%	31
MECANICAL WORKS		16	31-Aug-26	28-Oct-26	20-Sep-26 A	13-Oct-26	39,591.72	22,526.42	47,412.78	83.5%	47.51%	31
FIRE FIGHTING SYSTEM		2	27-Oct-26	28-Oct-26	23-Sep-26 A	13-Oct-26	0.00	40.88	136.26	0%	30%	-14
PG-T-CON-B-GF-FF-10	Fire Extinguisher Installation	2	27-Oct-26	28-Oct-26	23-Sep-26 A	13-Oct-26	0.00	40.88	136.26	0%	30%	-14
SEWER AND DRAINAGE SYSTEM		2	03-Sep-26	05-Sep-26	23-Sep-26 A	10-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-11
PG-T-CON-B-GF-DR-30	Sanitaryware Installation (Final Fix)	2	03-Sep-26	05-Sep-26	23-Sep-26 A	10-Oct-26	3,225.72	1,612.86	3,225.72	100%	50%	-11
HVAC SYSTEM		2	11-Oct-26	12-Oct-26	20-Sep-26 A	11-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-15
PG-T-CON-B-GF-AC-20	Split AC, Grills & Diffuser Installation	2	11-Oct-26	12-Oct-26	20-Sep-26 A	11-Oct-26	0.00	2,689.68	7,684.80	0%	35%	-15
WATER SUPPLY SYSTEM		3	31-Aug-26	02-Sep-26	23-Sep-26 A	08-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-9
PG-T-CON-B-GF-WS-30	Water Supply Accesories and Booster pump Installation	3	31-Aug-26	02-Sep-26	23-Sep-26 A	08-Oct-26	36,366.00	18,183.00	36,366.00	100%	50%	-9
PROJECT CLOSOUT		140	22-Nov-26	09-Dec-26	06-Aug-26 A	28-Jan-27	0.00	176,045.92	420,238.64	0%	41.89%	-135
PG-T-PCL-20	As-Built Drawings	15	22-Nov-26	09-Dec-26	23-Sep-26 A	28-Jan-27	0.00	22,715.60	113,578.01	0%	20%	-94
PG-T-PCL-10_R	Testing, Commissioning for All Systems(Remaining)	11	22-Nov-26	03-Dec-26	06-Aug-26 A	21-Jan-27	0.00	153,330.31	306,660.63	0%	50%	-133



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
