
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026		291	17-Feb-26	16-Dec-26	17-Feb-26 A	03-Feb-27	26,355,019.94	22,616,392.56	35,709,993.00	74.16%	63.64%	-41
MILESTONES		291	17-Feb-2	16-Dec-26	17-Feb-26 A	03-Feb-27	0.00	0.00	0.00	0%	0%	-41
GENERAL MILESTONES		291	17-Feb-2	16-Dec-26	17-Feb-26 A	03-Feb-27	0.00	0.00	0.00	0%	0%	-41
CONTRACUAL MILESTONES		229	05-May-2	16-Dec-26	05-May-26 A	03-Feb-27	0.00	0.00	0.00	0%	0%	-41
QASSIM		283	17-Feb-2	16-Dec-26	17-Feb-26 A	24-Jan-27	13,380,572.10	11,410,904.67	17,537,540.00	77.05%	65.71%	-33
MOBILIZATION		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
TEMPORARY CAMP		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
SITE OFFICES		29	17-Feb-2	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
GENERAL REQUIEREMENTS		57	17-Feb-2	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
ENGINEERING		199	17-Feb-2	16-Aug-26	17-Feb-26 A	04-Oct-26	526,126.20	526,126.20	526,126.20	100%	100%	-41
SHOP DRAWINGS SUBMITTALS		168	17-Feb-2	04-Aug-26	17-Feb-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-51
STRUCTURAL DRAWINGS		125	17-Feb-2	05-Jul-26	17-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	-4
PROJECT FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		19	29-Apr-26	21-May-26	29-Apr-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	25-Jun-26	06-Jul-26	01-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	1
TOILET BUILDING		43	17-Feb-2	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		41	19-Feb-2	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		13	28-Apr-26	13-May-26	28-Apr-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		158	19-Feb-2	23-Jul-26	19-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
TOILET BUILDING		42	19-Feb-2	15-Apr-26	19-Feb-26 A	15-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		15	07-Jul-26	23-Jul-26	14-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-9
LANDSCAPE DRAWINGS		39	23-Feb-2	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		143	28-Feb-2	15-Jul-26	28-Feb-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-68
WATER SUPPLY SYSTEM		32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	09-Mar-2	11-Apr-26	09-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		18	25-Jun-26	15-Jul-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-38
ELECTRICAL DRAWINGS		102	11-May-2	04-Aug-26	11-May-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-51
POWER AND LIGHTING SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		27	11-May-2	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	16-Jul-26	04-Aug-26	30-Jul-26 A	04-Oct-26	0.00	0.00	0.00	0%	0%	-39
SHOP DRAWINGS APPROVALS		172	19-Feb-2	16-Aug-26	19-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
STRUCTURAL DRAWINGS		130	19-Feb-2	14-Jul-26	19-Feb-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	2
PROJECT FENCE		7	13-May-2	21-May-26	13-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
PADEL PLAYGROUND FENCE		9	11-May-2	21-May-26	11-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		9	05-Jul-26	14-Jul-26	06-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	3
TOILET BUILDING		44	19-Feb-2	18-Apr-26	19-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
WATER STORAGE TANK		42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEPTIC TANK		3	11-May-2	14-May-26	11-May-26 A	13-May-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL DRAWINGS		166	25-Feb-2	01-Aug-26	25-Feb-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
TOILET BUILDING		40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		7	25-Jul-26	01-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-20
LANDSCAPE DRAWINGS		39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
MECHANICAL DRAWINGS		154	09-Mar-2	27-Jul-26	09-Mar-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
WATER SUPPLY SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
SEWER AND DRAINAGE SYSTEM		27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION SYSTEM		24	12-Mar-2	14-Apr-26	12-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		10	16-Jul-26	27-Jul-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
ELECTRICAL DRAWINGS		100	20-May-2	16-Aug-26	20-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-30
POWER AND LIGHTING SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
ELV SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
FIRE ALARM SYSTEM		20	20-May-2	17-Jun-26	20-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
AIR DOME		17	28-Jul-26	16-Aug-26	20-Aug-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-10
MATERIAL SUBMITTALS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
LONG LEAD ITEMS		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
EXTERNAL / LANDSCAPE WORK		56	25-Feb-2	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
SPORTS & RECREATIONAL FACILITIES WORK		134	17-Feb-2	16-Jul-26	17-Feb-26 A	20-Aug-26 A	0.00	0.00	0.00	0%	0%	-30
CONCRETE WORK		43	04-Mar-2	28-Apr-26	04-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		26	12-May-2	16-Jun-26	12-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
SHORT LEAD ITEMS		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
EXTERNAL / LANDSCAPE WORK		23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
CONCRETE WORK		28	17-Feb-2	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
ARCHITECTURAL & FINISHES WORK		18	21-Feb-2	15-Mar-26	21-Feb-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
METAL WORK		11	04-Mar-2	17-Mar-26	04-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
HVAC WORK		19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
PLUMBING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
IRRIGATION WORK		17	25-Feb-2	17-Mar-26	25-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
ELECTRICAL WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
FIRE FIGHTING WORK		4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0

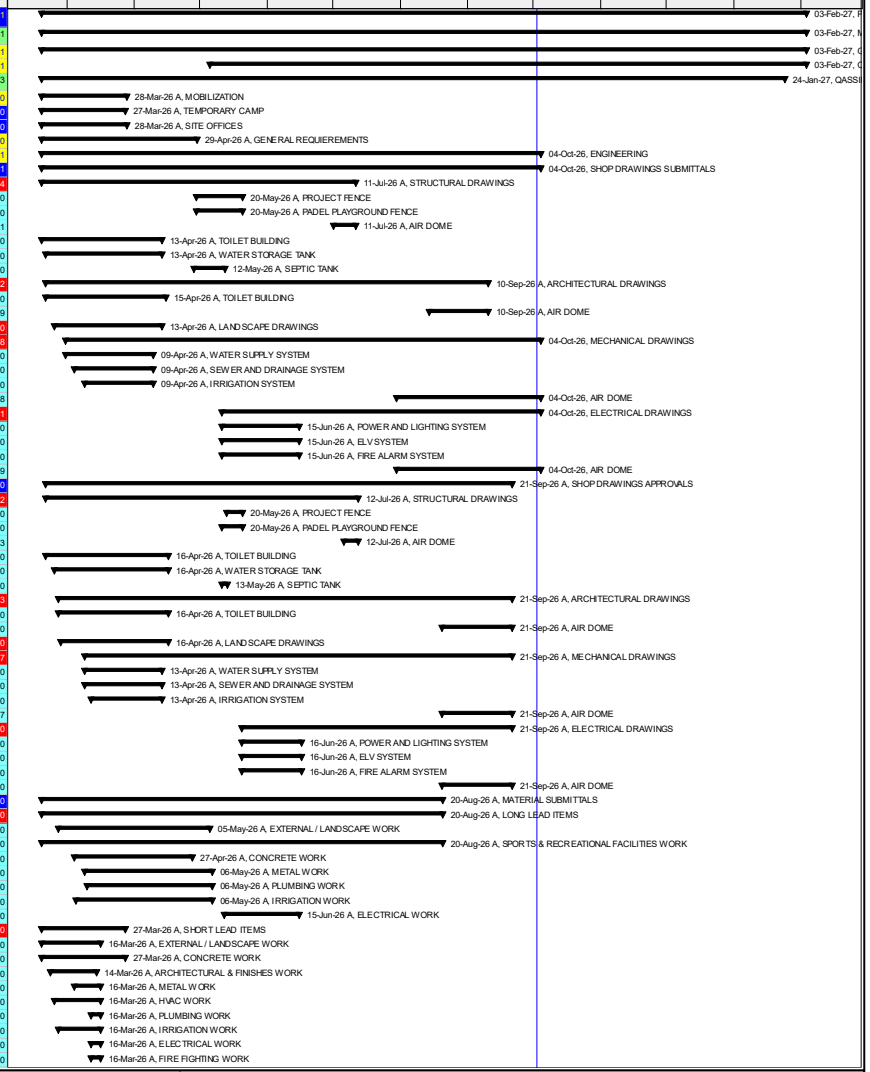


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	MATERIAL APPROVALS	196	21-Feb-26	18-Jul-26	21-Feb-26 A	01-Oct-26 A	526,126.20	526,126.20	526,126.20	100%	100%	-64
	LONG LEAD ITEMS	189	02-Mar-26	18-Jul-26	02-Mar-26 A	01-Oct-26 A	358,885.26	358,885.26	358,885.26	100%	100%	-64
	EXTERNAL / LANDSCAPE WORK	2	11-May-26	12-May-26	11-May-26 A	12-May-26 A	19,812.18	19,812.18	19,812.18	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	110	02-Mar-26	30-Jun-26	02-Mar-26 A	19-Sep-26 A	273,522.54	273,522.54	273,522.54	100%	100%	-69
	CONCRETE WORK	40	09-Mar-26	28-Apr-26	09-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	112	09-Jun-26	18-Jul-26	09-Jun-26 A	01-Oct-26 A	889.23	889.23	889.23	100%	100%	-64
	PLUMBING WORK	48	09-Jun-26	18-Jul-26	20-May-26 A	24-Jun-26 A	3,553.95	3,553.95	3,553.95	100%	100%	7
	IRRIGATION WORK	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	24,486.75	24,486.75	24,486.75	100%	100%	0
	ELECTRICAL WORK	96	12-May-26	02-Jul-26	12-May-26 A	16-Sep-26 A	35,203.11	35,203.11	35,203.11	100%	100%	-64
	SHORT LEAD ITEMS	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	167,240.94	167,240.94	167,240.94	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	139,867.29	139,867.29	139,867.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	17	25-Feb-26	16-Mar-26	25-Feb-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	12	09-Mar-26	26-Mar-26	09-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	17	03-Mar-26	26-Mar-26	03-Mar-26 A	26-Mar-26 A	13,170.12	13,170.12	13,170.12	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	214	03-Mar-26	27-Aug-26	03-Mar-26 A	17-Nov-26	4,735,135.80	3,654,381.51	4,735,135.80	100%	77.18%	-69
	LONG LEAD ITEMS	201	18-Mar-26	27-Aug-26	18-Mar-26 A	17-Nov-26	3,229,967.34	2,215,688.57	3,229,967.34	100%	68.6%	-69
	PURCHASE ORDER	147	18-Mar-26	12-Jul-26	18-Mar-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	5	06-May-26	12-May-26	06-May-26 A	11-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	101	26-Mar-26	09-Jul-26	26-Mar-26 A	09-Jul-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	26-Mar-26	07-May-26	26-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	37	25-Mar-26	07-May-26	25-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	103	13-May-26	12-Jul-26	13-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	MANUFACTURE / FABRICATION	149	05-May-26	11-Aug-26	05-May-26 A	31-Oct-26	0.00	0.00	0.00	0%	0%	-68
	EXTERNAL / LANDSCAPE WORK	109	05-May-26	23-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
	SPORTS & RECREATIONAL FACILITIES WORK	123	05-May-26	11-Aug-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	CONCRETE WORK	69	05-May-26	12-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	15
	METAL WORK	149	05-May-26	23-Jul-26	05-May-26 A	31-Oct-26	0.00	0.00	0.00	0%	0%	-84
	PLUMBING WORK	79	05-May-26	23-Jul-26	05-May-26 A	24-Jun-26 A	0.00	0.00	0.00	0%	0%	25
	IRRIGATION WORK	82	05-May-26	06-Jul-26	05-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-62
	ELECTRICAL WORK	129	12-May-26	10-Aug-26	12-May-26 A	16-Sep-26 A	0.00	0.00	0.00	0%	0%	-32
	DELIVERY TO SITE	163	06-May-26	27-Aug-26	06-May-26 A	17-Nov-26	3,229,967.34	2,215,688.57	3,229,967.34	100%	68.6%	-69
	EXTERNAL / LANDSCAPE WORK	123	06-May-26	10-Aug-26	06-May-26 A	04-Oct-26	178,309.62	176,866.75	178,309.62	100%	99.19%	-46
	SPORTS & RECREATIONAL FACILITIES WORK	127	06-May-26	23-Aug-26	06-May-26 A	11-Oct-26	2,461,702.86	1,498,311.54	2,461,702.86	100%	60.86%	-41
	CONCRETE WORK	78	06-May-26	23-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	16
	METAL WORK	163	06-May-26	10-Aug-26	06-May-26 A	17-Nov-26	8,003.07	4,575.42	8,003.07	100%	57.17%	-84
	PLUMBING WORK	104	06-May-26	10-Aug-26	06-May-26 A	04-Oct-26	31,985.55	31,204.51	31,985.55	100%	97.56%	-46
	IRRIGATION WORK	102	06-May-26	15-Jul-26	06-May-26 A	03-Oct-26	220,380.75	219,357.96	220,380.75	100%	99.54%	-66
	ELECTRICAL WORK	143	13-May-26	27-Aug-26	13-May-26 A	05-Oct-26	316,827.99	272,614.89	316,827.99	100%	86.05%	-32
	SHORT LEAD ITEMS	183	03-Mar-26	12-Jul-26	03-Mar-26 A	11-Oct-26	1,505,168.46	1,438,692.95	1,505,168.46	100%	95.58%	-77
	PURCHASE ORDER	64	03-Mar-26	21-May-26	03-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	57	03-Mar-26	13-May-26	03-Mar-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	04-Mar-26	23-Apr-26	04-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	48	07-Mar-26	06-May-26	07-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	36	25-Mar-26	06-May-26	25-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	46	09-Mar-26	06-May-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	33	29-Mar-26	06-May-26	29-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	43	12-Mar-26	06-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	8	12-May-26	21-May-26	12-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	30	01-Apr-26	06-May-26	01-Apr-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	DELIVERY TO SITE	181	05-Mar-26	12-Jul-26	05-Mar-26 A	11-Oct-26	1,505,168.46	1,438,692.95	1,505,168.46	100%	95.58%	-77
	EXTERNAL / LANDSCAPE WORK	155	05-Mar-26	08-Jul-26	05-Mar-26 A	11-Oct-26	1,258,805.61	1,219,245.25	1,258,805.61	100%	96.86%	-80
	CONCRETE WORK	50	12-Mar-26	13-May-26	12-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	129	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	4,310.01	3,448.01	4,310.01	100%	80%	-78
	HVAC WORK	106	06-May-26	08-Jul-26	06-May-26 A	02-Oct-26 A	5,457.24	5,457.24	5,457.24	100%	100%	-72
	PLUMBING WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	101	06-May-26	08-Jul-26	06-May-26 A	07-Oct-26	118,531.08	93,639.55	118,531.08	100%	79%	-76
	ELECTRICAL WORK	128	11-May-26	12-Jul-26	11-May-26 A	11-Oct-26	3,667.68	2,567.38	3,667.68	100%	70%	-77
	FIRE FIGHTING WORK	129	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	204.39	143.07	204.39	100%	70%	-78
	CONSTRUCTION STAGE	252	24-Mar-26	16-Dec-26	24-Mar-26 A	18-Jan-27	8,066,697.48	6,905,952.46	10,522,524.00	77.93%	66.72%	-27
	PLAYGROUND AND LANDSCAPING WORKS	252	24-Mar-26	16-Dec-26	24-Mar-26 A	18-Jan-27	5,042,850.12	5,149,243.83	6,019,638.42	86.23%	88.05%	-27
	CUT AND FILL	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	729,000.00	729,000.00	900,600.00	100%	100%	0
	PLAYGROUND WORKS	197	21-Apr-26	02-Dec-26	21-Apr-26 A	09-Dec-26	1,076,683.57	1,218,782.40	1,318,471.20	81.66%	92.44%	-6
	FOOTBALL PLAYGROUND WORKS	159	21-Apr-26	17-Nov-26	21-Apr-26 A	29-Oct-26	550,054.50	571,097.58	611,282.16	89.98%	93.43%	17
	BASKETBALL PLAYGROUND WORKS	157	30-Apr-26	17-Nov-26	30-Apr-26 A	05-Nov-26	362,517.63	371,828.88	381,705.12	94.97%	97.41%	11
	PADEL PLAYGROUND WORKS	184	06-May-26	02-Dec-26	06-May-26 A	09-Dec-26	164,111.44	275,855.94	325,483.92	50.42%	84.75%	-6

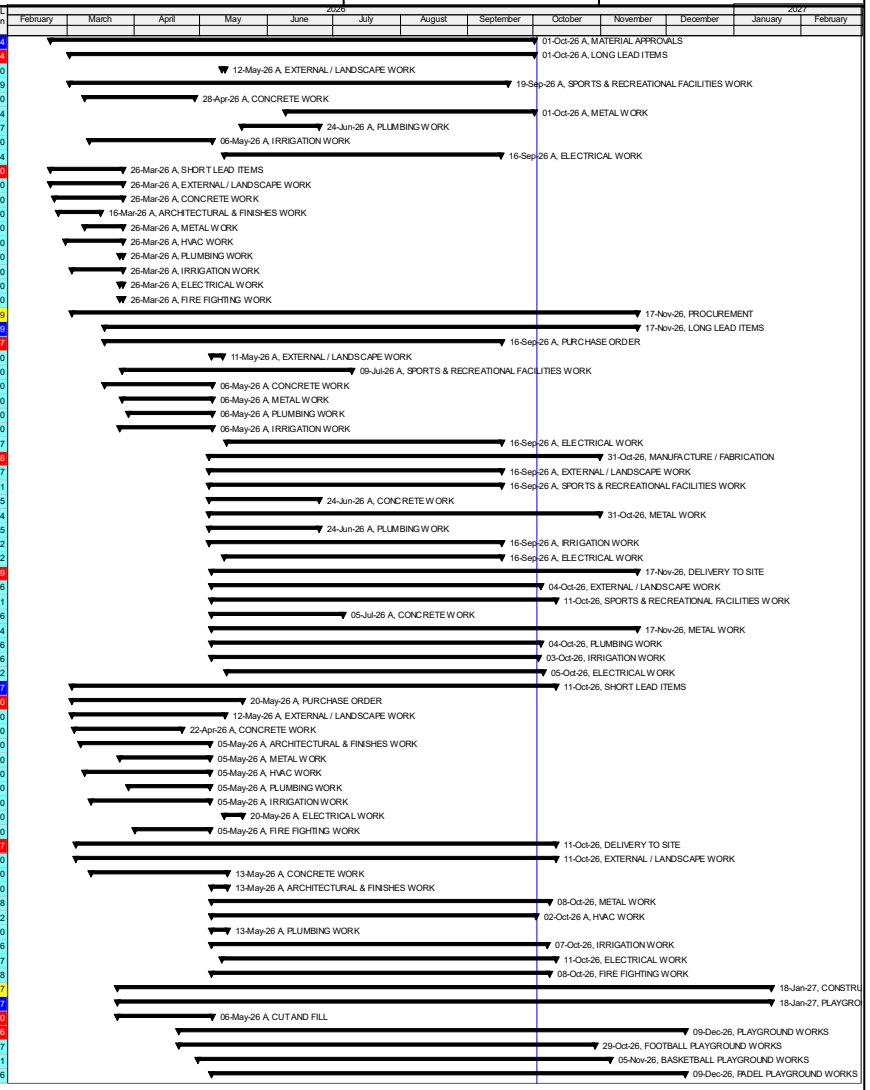

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00


PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

شركة الإنشاء المتقدم للمقاولات
Advanced Construction For Cont. Co

egis

مدن

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	GENERAL SITE WORKS	232	16-Apr-26	16-Dec-26	16-Apr-26 A	18-Jan-27	1,475,927.22	1,302,737.35	1,617,941.82	91.22%	80.52%	-27
	FENCE WORKS	163	16-Apr-26	13-Sep-26	16-Apr-26 A	29-Oct-26	32,909.40	20,403.83	32,909.40	100%	62%	-38
	MECHANICAL WORK	143	12-May-26	18-Aug-26	12-May-26 A	01-Nov-26	780,707.34	670,165.14	780,707.34	100%	85.84%	-62
	STORM WATER AND UTILITY WORK	141	12-May-26	16-Aug-26	12-May-26 A	29-Oct-26	27,252.00	18,086.40	27,252.00	100%	66.37%	-62
	IRRIGATION SYSTEM WORKS	86	17-Jun-26	09-Aug-26	17-Jun-26 A	22-Oct-26	753,137.40	652,078.74	753,137.40	100%	86.58%	-62
	FIRE PROTECTION SYSTEM	2	17-Aug-26	18-Aug-26	29-Oct-26	01-Nov-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	186	20-May-26	01-Nov-26	20-May-26 A	29-Dec-26	642,411.48	519,487.58	693,965.28	92.57%	74.86%	-49
	POWER, LIGHTING & GROUNDING	151	20-May-26	20-Sep-26	20-May-26 A	18-Nov-26	636,895.08	519,487.58	636,895.08	100%	81.57%	-49
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	21-Sep-26	20-Oct-26	18-Nov-26	17-Dec-26	4,028.70	0.00	43,146.00	9.34%	0%	0
	FIRE ALARM SYSTEM	32	26-Sep-26	01-Nov-26	22-Nov-26	29-Dec-26	1,487.70	0.00	13,924.20	10.68%	0%	0
	PARKING WORK	166	17-Jun-26	09-Nov-26	17-Jun-26 A	29-Dec-26	19,899.00	88,440.00	102,919.80	19.33%	85.93%	-42
	SERVICE CONNECTION	50	10-Nov-26	16-Dec-26	12-Jul-26 A	18-Jan-27	0.00	4,240.80	7,440.00	0%	57%	-130
	LANDSCAPING WORKS	164	31-May-26	14-Dec-26	30-May-26 A	09-Dec-26	1,712,948.93	1,885,146.68	2,134,335.00	80.26%	88.32%	5
	HARDSCAPE WORK	164	31-May-26	14-Dec-26	30-May-26 A	09-Dec-26	1,597,448.93	1,683,021.68	1,712,409.00	93.29%	98.28%	5
	SOFTSCAPE WORK	143	10-Jun-26	21-Nov-26	10-Jun-26 A	24-Nov-26	115,500.00	202,125.00	421,926.00	27.37%	47.91%	-3
	TANK WORKS	127	13-May-26	19-Aug-26	13-May-26 A	13-Oct-26	48,290.40	13,577.40	48,290.40	100%	28.12%	-46
	SEPTIC TANK	33	13-May-26	24-Jun-26	13-May-26 A	24-Jun-26 A	7,475.22	7,475.22	7,475.22	100%	100%	0
	WATER STORAGE TANK	127	13-May-26	19-Aug-26	13-May-26 A	13-Oct-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-46
	AIR DOME CONSTRUCTION	198	13-May-26	26-Nov-26	13-May-26 A	04-Jan-27	2,838,867.26	1,461,181.68	4,178,041.20	67.95%	34.97%	-33
	CIVIL WORK	137	13-May-26	10-Sep-26	13-May-26 A	25-Oct-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-37
	ARCHITECTURAL WORK	27	27-Oct-26	26-Nov-26	27-Aug-26 A	04-Jan-27	0.00	125,244.14	712,953.22	0%	17.57%	-84
	MECHANICAL WORK	16	12-Sep-26	30-Sep-26	25-Oct-26	12-Nov-26	667,968.77	0.00	667,968.77	100%	0%	0
	ELECTRICAL WORK	72	17-Aug-26	26-Oct-26	27-Aug-26 A	08-Dec-26	459,228.53	125,244.14	1,085,449.25	42.31%	11.54%	-28
	TOILET BUILDING WORKS	166	06-May-26	20-Oct-26	06-May-26 A	22-Nov-26	184,980.09	295,526.96	324,844.38	56.94%	90.97%	-27
	CIVIL WORK	166	06-May-26	19-Oct-26	06-May-26 A	21-Nov-26	87,389.55	206,085.24	227,117.58	38.48%	90.74%	-28
	STRUCTURAL WORK	85	06-May-26	04-Aug-26	06-May-26 A	10-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	22
	ARCHITECTURAL WORK	111	05-Aug-26	19-Oct-26	12-Jul-26 A	21-Nov-26	49,409.55	168,105.24	189,137.58	26.12%	88.88%	-49
	GENERAL FINISHES	107	05-Aug-26	19-Oct-26	12-Jul-26 A	21-Nov-26	17,323.35	76,362.06	84,120.00	20.59%	90.78%	-49
	WET AREA FINISHES	59	20-Aug-26	14-Oct-26	06-Aug-26 A	15-Oct-26	31,046.70	78,442.98	81,123.78	38.27%	96.7%	-13
	ROOF FINISHES	33	01-Oct-26	19-Oct-26	20-Aug-26 A	21-Nov-26	1,039.50	13,300.20	23,893.80	4.35%	55.66%	-63
	MEP WORK	132	16-Jun-26	20-Oct-26	16-Jun-26 A	22-Nov-26	97,590.54	89,441.72	97,726.80	99.86%	91.52%	-27
	MECANICAL WORKS	132	16-Jun-26	20-Oct-26	16-Jun-26 A	22-Nov-26	79,343.22	71,194.40	79,479.48	99.83%	89.58%	-27
	FIRE FIGHTING SYSTEM	1	20-Oct-26	20-Oct-26	01-Oct-26 A	22-Nov-26	0.00	34.07	136.26	0%	25%	-43
	SEWER AND DRAINAGE SYSTEM	103	16-Jun-26	02-Sep-26	16-Jun-26 A	12-Oct-26	11,290.02	8,870.73	11,290.02	100%	78.57%	-33
	HVAC SYSTEM	26	12-Aug-26	23-Aug-26	13-Aug-26 A	05-Oct-26	12,127.20	6,363.60	12,127.20	100%	52.47%	-34
	WATER SUPPLY SYSTEM	80	16-Jun-26	31-Aug-26	16-Jun-26 A	07-Sep-26 A	55,926.00	55,926.00	55,926.00	100%	100%	-5
	ELECTRICAL WORKS	47	13-Jul-26	15-Sep-26	22-Jul-26 A	08-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	14
	PROJECT CLOSOUT	207	23-May-26	16-Dec-26	22-May-26 A	24-Jan-27	52,612.62	324,444.49	1,753,754.00	3%	18.5%	-33
	HAIL	272	17-Feb-26	16-Dec-26	17-Feb-26 A	16-Jan-27	5,342,614.81	5,171,795.08	6,814,652.00	78.4%	75.89%	-26
	MOBILIZATION	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	28	17-Feb-26	28-Mar-26	17-Feb-26 A	27-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	29	17-Feb-26	29-Mar-26	17-Feb-26 A	28-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	51	17-Feb-26	23-Apr-26	17-Feb-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	168	17-Feb-26	14-Jul-26	17-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	SHOP DRAWINGS SUBMITTALS	93	17-Feb-26	16-Jun-26	17-Feb-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	17-Feb-26	05-May-26	17-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	57	17-Feb-26	30-Apr-26	17-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	55	25-Feb-26	05-May-26	25-Feb-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	24-Feb-26	14-Apr-26	24-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	52	01-Mar-26	05-May-26	01-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	31	01-Mar-26	11-Apr-26	01-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	05-Mar-26	11-Apr-26	05-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	10-Mar-26	05-May-26	10-Mar-26 A	04-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	11-May-26	16-Jun-26	11-May-26 A	15-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	SHOP DRAWINGS APPROVALS	92	19-Feb-26	17-Jun-26	19-Feb-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	STRUCTURAL DRAWINGS	61	19-Feb-26	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PROJECT FENCE	55	19-Feb-26	30-Apr-26	19-Feb-26 A	29-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	42	23-Feb-26	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-26	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-26	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TOILET BUILDING	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	LANDSCAPE DRAWINGS	38	28-Feb-26	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	46	10-Mar-26	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	WATER SUPPLY SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	26	10-Mar-26	14-Apr-26	10-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0

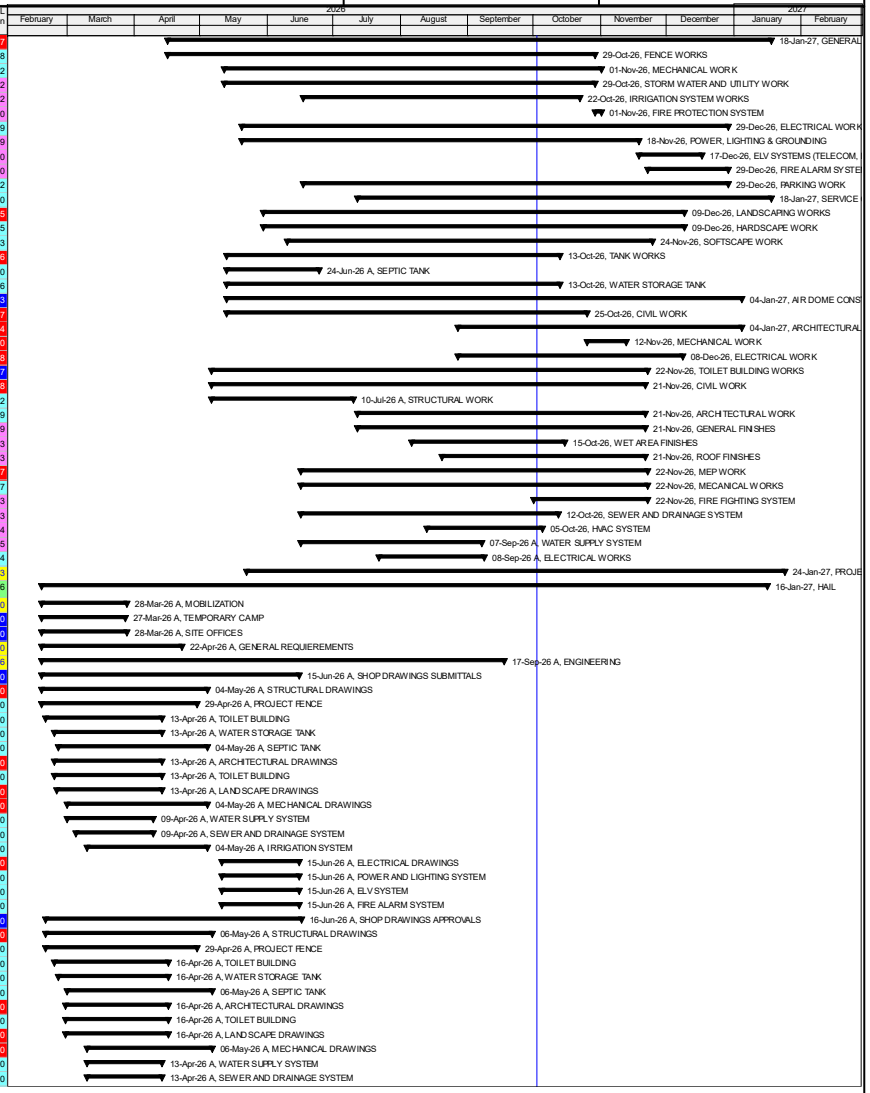


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	IRRIGATION SYSTEM	43	14-Mar-26	07-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL DRAWINGS	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	POWER AND LIGHTING SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	27	12-May-26	17-Jun-26	12-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL SUBMITTALS	166	17-Feb-26	06-Jul-26	17-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	LONG LEAD ITEMS	163	21-Feb-26	06-Jul-26	21-Feb-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-26	06-May-26	25-Feb-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	47	08-Mar-26	06-May-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	41	07-Mar-26	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	44	11-Mar-26	06-May-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	60	21-Feb-26	07-May-26	21-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	99	12-May-26	06-Jul-26	12-May-26 A	01-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	SHORT LEAD ITEMS	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-26	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-26	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-26	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-26	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-26	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-26	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	165	21-Feb-26	14-Jul-26	21-Feb-26 A	17-Sep-26 A	204,439.56	204,439.56	204,439.56	100%	100%	-56
	LONG LEAD ITEMS	162	25-Feb-26	14-Jul-26	25-Feb-26 A	17-Sep-26 A	111,065.49	111,065.49	111,065.49	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-26	06-May-26	25-Feb-26 A	06-May-26 A	26,079.63	26,079.63	26,079.63	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	43	14-Mar-26	06-May-26	14-Mar-26 A	06-May-26 A	38,839.50	38,839.50	38,839.50	100%	100%	0
	CONCRETE WORK	45	11-Mar-26	06-May-26	11-Mar-26 A	06-May-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-26	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	41	16-Mar-26	06-May-26	16-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	55	28-Feb-26	06-May-26	28-Feb-26 A	06-May-26 A	12,818.25	12,818.25	12,818.25	100%	100%	0
	ELECTRICAL WORK	101	12-May-26	14-Jul-26	12-May-26 A	17-Sep-26 A	27,467.43	27,467.43	27,467.43	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	93,374.07	93,374.07	93,374.07	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-26	26-Mar-26	21-Feb-26 A	26-Mar-26 A	72,133.44	72,133.44	72,133.44	100%	100%	0
	CONCRETE WORK	24	23-Feb-26	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-26	16-Mar-26	15-Mar-26 A	16-Mar-26 A	8,114.01	8,114.01	8,114.01	100%	100%	0
	METAL WORK	10	11-Mar-26	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-26	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	6,854.64	6,854.64	6,854.64	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-26	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	203	26-Feb-26	26-Aug-26	26-Feb-26 A	03-Nov-26	1,839,956.04	1,783,323.01	1,839,956.04	100%	96.92%	-57
	LONG LEAD ITEMS	197	05-Mar-26	26-Aug-26	05-Mar-26 A	03-Nov-26	999,589.41	964,544.97	999,589.41	100%	96.49%	-57
	PURCHASE ORDER	162	05-Mar-26	22-Jul-26	05-Mar-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	34	29-Mar-26	07-May-26	29-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-26	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	109	11-May-26	22-Jul-26	11-May-26 A	08-Sep-26 A	0.00	0.00	0.00	0%	0%	-40
	MANUFACTURE / FABRICATION	178	01-Apr-26	12-Aug-26	01-Apr-26 A	31-Oct-26	0.00	0.00	0.00	0%	0%	-67
	EXTERNAL / LANDSCAPE WORK	103	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	SPORTS & RECREATIONAL FACILITIES WORK	97	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	93	01-Apr-26	06-Jul-26	01-Apr-26 A	27-Jun-26 A	0.00	0.00	0.00	0%	0%	8
	METAL WORK	149	05-May-26	23-Jul-26	05-May-26 A	31-Oct-26	0.00	0.00	0.00	0%	0%	-84
	PLUMBING WORK	120	05-May-26	23-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-41
	IRRIGATION WORK	107	05-May-26	08-Jul-26	05-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-54
	ELECTRICAL WORK	131	12-May-26	12-Aug-26	12-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-25
	DELIVERY TO SITE	147	07-May-26	26-Aug-26	06-May-26 A	03-Nov-26	999,589.41	964,544.97	999,589.41	100%	96.49%	-57
	EXTERNAL / LANDSCAPE WORK	118	07-May-26	06-Aug-26	06-May-26 A	04-Oct-26	234,716.67	228,223.24	234,716.67	100%	97.23%	-49
	SPORTS & RECREATIONAL FACILITIES WORK	106	07-May-26	06-Aug-26	06-May-26 A	04-Oct-26	349,555.50	336,394.01	349,555.50	100%	96.23%	-48
	CONCRETE WORK	67	07-May-26	12-Jul-26	06-May-26 A	07-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	4
	METAL WORK	130	07-May-26	06-Aug-26	06-May-26 A	03-Nov-26	8,003.07	7,042.70	8,003.07	100%	88%	-74
	PLUMBING WORK	130	07-May-26	06-Aug-26	06-May-26 A	05-Oct-26	31,985.55	30,111.05	31,985.55	100%	94.14%	-49
	IRRIGATION WORK	108	07-May-26	18-Jul-26	06-May-26 A	04-Sep-26 A	115,364.25	115,364.25	115,364.25	100%	100%	-41
	ELECTRICAL WORK	142	13-May-26	26-Aug-26	13-May-26 A	04-Oct-26	247,206.87	234,652.21	247,206.87	100%	94.92%	-32
	SHORT LEAD ITEMS	190	26-Feb-26	16-Jul-26	26-Feb-26 A	15-Oct-26	840,366.63	818,778.04	840,366.63	100%	97.43%	-77
	PURCHASE ORDER	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	EXTERNAL / LANDSCAPE WORK	156	26-Feb-26	02-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0

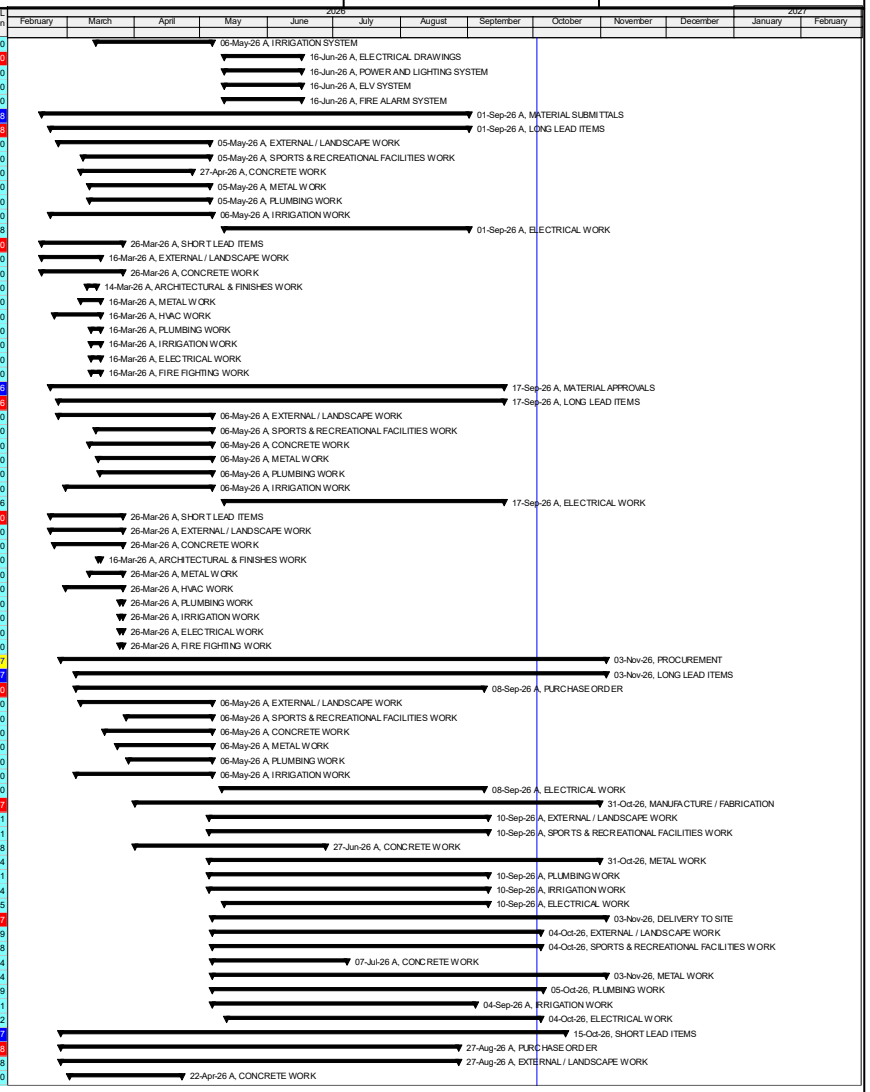


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	102	05-May-26	02-Jul-26	05-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	ELECTRICAL WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	96	12-May-26	02-Jul-26	12-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	DELIVERY TO SITE	188	01-Mar-26	16-Jul-26	01-Mar-26 A	15-Oct-26	840,366.63	818,778.04	840,366.63	100%	97.43%	-77
	EXTERNAL / LANDSCAPE WORK	166	01-Mar-26	16-Jul-26	01-Mar-26 A	05-Oct-26	649,200.96	634,307.85	649,200.96	100%	97.71%	-68
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	73,026.09	73,026.09	73,026.09	100%	100%	0
	METAL WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	4,310.01	4,310.01	4,310.01	100%	100%	0
	HVAC WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	6	06-May-26	12-May-26	06-May-26 A	12-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	113	06-May-26	16-Jul-26	06-May-26 A	04-Oct-26	61,691.76	57,064.88	61,691.76	100%	92.5%	-67
	ELECTRICAL WORK	117	20-May-26	16-Jul-26	20-May-26 A	08-Oct-26	3,667.68	1,742.15	3,667.68	100%	47.5%	-71
	FIRE FIGHTING WORK	123	20-May-26	16-Jul-26	20-May-26 A	15-Oct-26	204.39	61.32	204.39	100%	30%	-77
	CONSTRUCTION STAGE	237	05-Apr-26	26-Nov-26	05-Apr-26 A	16-Jan-27	3,277,775.25	3,108,389.87	4,088,791.20	80.16%	76.02%	-42
	PLAYGROUND AND LANDSCAPING WORKS	237	05-Apr-26	26-Nov-26	05-Apr-26 A	16-Jan-27	3,025,701.96	2,875,651.47	3,760,297.62	80.46%	76.47%	-42
	CUT AND FILL	28	05-Apr-26	06-May-26	05-Apr-26 A	06-May-26 A	453,900.00	453,900.00	453,900.00	100%	100%	0
	PLAYGROUND WORKS	169	19-Apr-26	17-Nov-26	19-Apr-26 A	07-Nov-26	671,758.50	678,987.06	781,940.40	85.91%	86.83%	9
	FOOTBALL PLAYGROUND WORKS	169	19-Apr-26	17-Nov-26	19-Apr-26 A	07-Nov-26	671,758.50	678,987.06	781,940.40	85.91%	86.83%	9
	GENERAL SITE WORKS	227	16-Apr-26	26-Nov-26	16-Apr-26 A	16-Jan-27	1,035,856.92	685,598.98	1,224,114.42	84.62%	56.01%	-42
	FENCE WORKS	149	16-Apr-26	16-Aug-26	16-Apr-26 A	13-Oct-26	65,818.80	39,491.28	65,818.80	100%	60%	-48
	MECHANICAL WORK	141	12-May-26	06-Aug-26	12-May-26 A	28-Oct-26	421,027.74	227,748.36	421,027.74	100%	54.09%	-70
	STORM WATER AND UTILITY WORK	139	12-May-26	04-Aug-26	12-May-26 A	26-Oct-26	27,252.00	8,875.20	27,252.00	100%	32.57%	-70
	IRRIGATION SYSTEM WORKS	121	02-Jun-26	30-Jul-26	02-Jun-26 A	21-Oct-26	393,457.80	218,873.16	393,457.80	100%	55.63%	-70
	FIRE PROTECTION SYSTEM	2	05-Aug-26	06-Aug-26	26-Oct-26	28-Oct-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	189	20-May-26	20-Oct-26	20-May-26 A	31-Dec-26	510,116.88	262,084.84	539,251.68	94.6%	48.6%	-62
	POWER, LIGHTING & GROUNDING	154	20-May-26	08-Sep-26	20-May-26 A	21-Nov-26	482,181.48	262,084.84	482,181.48	100%	54.35%	-62
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	09-Sep-26	08-Oct-26	21-Nov-26	20-Dec-26	23,307.00	0.00	43,146.00	54.02%	0%	0
	FIRE ALARM SYSTEM	32	13-Sep-26	20-Oct-26	24-Nov-26	31-Dec-26	4,628.40	0.00	13,924.20	33.24%	0%	0
	PARKING WORK	169	17-Jun-26	20-Oct-26	17-Jun-26 A	31-Dec-26	38,893.50	151,252.50	190,576.20	20.41%	79.37%	-62
	SERVICE CONNECTION	40	21-Oct-26	26-Nov-26	30-Jul-26 A	16-Jan-27	0.00	5,022.00	7,440.00	0%	67.5%	-112
	LANDSCAPING WORKS	163	31-May-26	09-Nov-26	30-May-26 A	07-Dec-26	815,896.14	1,045,745.39	1,252,052.40	65.16%	83.52%	-24
	HARDSCAPE WORK	163	31-May-26	09-Nov-26	30-May-26 A	07-Dec-26	761,296.14	950,195.39	1,046,213.40	72.77%	90.82%	-24
	SOFTSCAPE WORK	155	03-Jun-26	09-Nov-26	03-Jun-26 A	07-Dec-26	54,600.00	95,550.00	205,839.00	26.53%	46.42%	-24
	TANK WORKS	144	13-May-26	19-Sep-26	13-May-26 A	03-Nov-26	48,290.40	11,420.04	48,290.40	100%	23.65%	-37
	SEPTIC TANK	139	13-May-26	31-Aug-26	13-May-26 A	28-Oct-26	7,475.22	5,317.86	7,475.22	100%	71.14%	-48
	WATER STORAGE TANK	144	13-May-26	19-Sep-26	13-May-26 A	03-Nov-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-37
	TOILET BUILDING WORKS	165	12-May-26	12-Oct-26	12-May-26 A	12-Nov-26	252,073.29	232,738.40	328,493.58	76.74%	70.85%	-26
	CIVIL WORK	165	12-May-26	12-Oct-26	12-May-26 A	11-Nov-26	154,482.75	154,230.90	230,766.78	66.94%	66.83%	-25
	STRUCTURAL WORK	59	12-May-26	22-Jul-26	12-May-26 A	23-Jul-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-1
	ARCHITECTURAL WORK	99	23-Jul-26	12-Oct-26	31-Jul-26 A	11-Nov-26	116,502.75	116,250.90	192,786.78	60.43%	60.3%	-18
	GENERAL FINISHES	99	23-Jul-26	12-Oct-26	31-Jul-26 A	11-Nov-26	60,024.60	26,890.38	87,769.20	68.39%	30.64%	-18
	WET AREA FINISHES	61	12-Aug-26	11-Oct-26	07-Aug-26 A	12-Oct-26	42,162.15	79,247.22	81,123.78	51.97%	97.69%	-4
	ROOF FINISHES	44	19-Sep-26	05-Oct-26	20-Aug-26 A	11-Nov-26	14,316.00	10,113.30	23,893.80	59.92%	42.33%	-56
	MEP WORK	80	28-Jul-26	06-Oct-26	22-Jul-26 A	12-Nov-26	97,590.54	78,507.50	97,726.80	99.86%	80.33%	-36
	MECANICAL WORKS	80	28-Jul-26	06-Oct-26	22-Jul-26 A	12-Nov-26	79,343.22	62,699.74	79,479.48	99.83%	78.89%	-36
	FIRE FIGHTING SYSTEM	1	06-Oct-26	06-Oct-26	11-Nov-26	12-Nov-26	0.00	0.00	136.26	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	47	03-Aug-26	23-Aug-26	22-Jul-26 A	07-Oct-26	11,290.02	7,580.44	11,290.02	100%	67.14%	-47
	HVAC SYSTEM	31	28-Jul-26	15-Aug-26	13-Aug-26 A	04-Oct-26	12,127.20	8,284.80	12,127.20	100%	68.32%	-28
	WATER SUPPLY SYSTEM	56	01-Aug-26	20-Aug-26	30-Jul-26 A	05-Oct-26	55,926.00	46,834.50	55,926.00	100%	83.74%	-38
	ELECTRICAL WORKS	40	05-Aug-26	08-Sep-26	12-Aug-26 A	08-Oct-26	18,247.32	15,807.76	18,247.32	100%	86.63%	-19
	PROJECT CLOSOUT	192	25-May-26	16-Dec-26	25-May-26 A	09-Jan-27	20,443.96	75,642.64	681,465.20	3%	11.1%	-20
	TABUK	291	17-Feb-26	16-Dec-26	17-Feb-26 A	03-Feb-27	7,631,833.03	6,033,692.82	11,357,801.00	67.19%	53.12%	-41
	MOBILIZATION	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	TEMPORARY CAMP	43	17-Feb-26	14-Apr-26	17-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SITE OFFICES	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	GENERAL REQUIEREMENTS	44	17-Feb-26	15-Apr-26	17-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ENGINEERING	171	17-Feb-26	12-Aug-26	17-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-30
	SHOP DRAWINGS SUBMITTALS	163	17-Feb-26	04-Aug-26	17-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	STRUCTURAL DRAWINGS	135	17-Feb-26	18-Jul-26	17-Feb-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	13
	PROJECT FENCE	63	17-Feb-26	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	63	17-Feb-26	07-May-26	17-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	20	25-Jun-26	18-Jul-26	01-Jul-26 A	03-Jul-26 A	0.00	0.00	0.00	0%	0%	18
	TOILET BUILDING	41	19-Feb-26	14-Apr-26	19-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	39	23-Feb-26	14-Apr-26	23-Feb-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	57	25-Feb-26	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	150	23-Feb-26	04-Aug-26	23-Feb-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-31
	TOILET BUILDING	40	23-Feb-26	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	19-Jul-26	04-Aug-26	05-Aug-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-16
	LANDSCAPE DRAWINGS	40	23-Feb-26	15-Apr-26	23-Feb-26 A	14-Apr-26 A	0.00	0.00	0.00	0%	0%	0

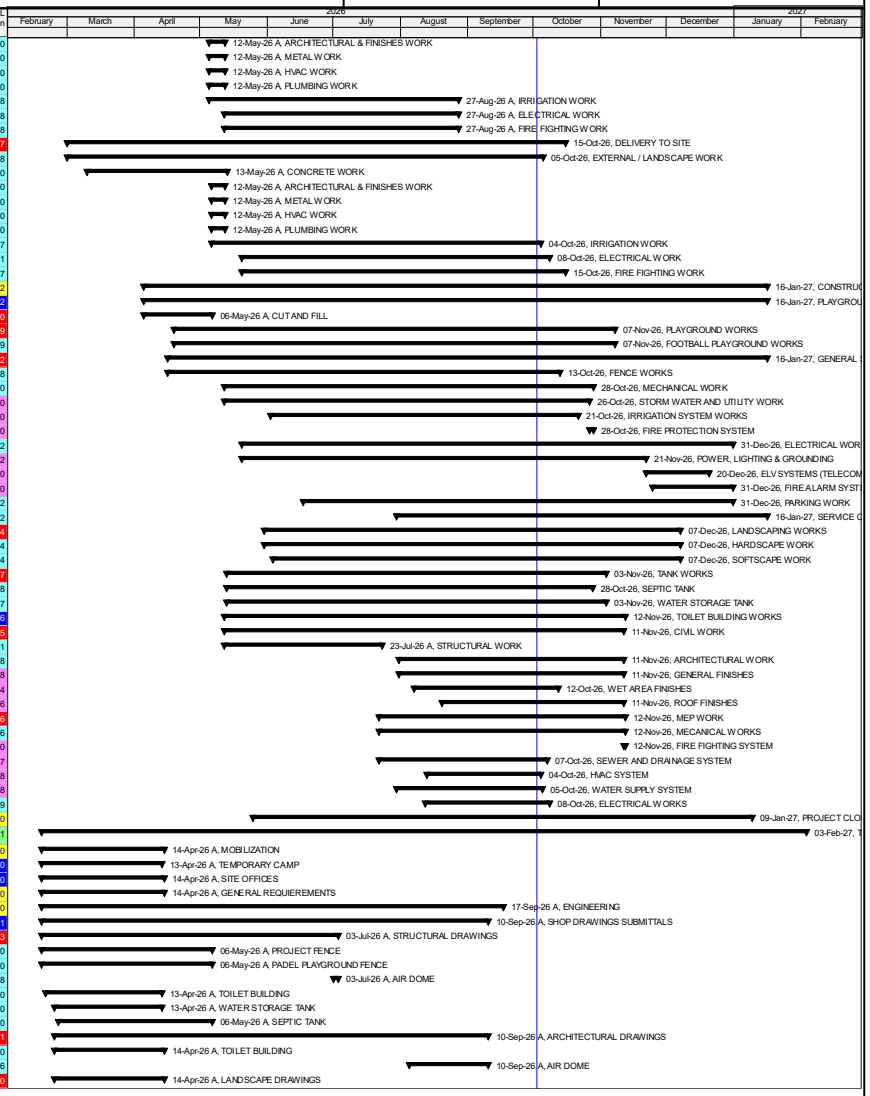


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Advanced Construction For Cont. Co

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	MECHANICAL DRAWINGS	140	28-Feb-2	12-Jul-26	28-Feb-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	-1
	WATER SUPPLY SYSTEM	32	28-Feb-2	11-Apr-26	28-Feb-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	28	04-Mar-2	11-Apr-26	04-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	47	09-Mar-2	07-May-26	09-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	25-Jun-26	12-Jul-26	02-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	98	10-May-2	29-Jul-26	10-May-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	15
	POWER AND LIGHTING SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	10	10-May-2	21-May-26	10-May-26 A	20-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	30	25-Jun-26	29-Jul-26	08-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0%	0%	26
	SHOP DRAWINGS APPROVALS	169	19-Feb-2	12-Aug-26	19-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	STRUCTURAL DRAWINGS	138	19-Feb-2	23-Jul-26	19-Feb-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	12
	PROJECT FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PADEL PLAYGROUND FENCE	61	19-Feb-2	07-May-26	19-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	15	07-Jul-26	23-Jul-26	05-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	0%	0%	10
	TOILET BUILDING	42	23-Feb-2	18-Apr-26	23-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	WATER STORAGE TANK	40	25-Feb-2	18-Apr-26	25-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEPTIC TANK	54	01-Mar-2	07-May-26	01-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL DRAWINGS	153	28-Feb-2	12-Aug-26	28-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-18
	TOILET BUILDING	38	28-Feb-2	18-Apr-26	28-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	7	05-Aug-2	12-Aug-26	06-Aug-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-17
	LANDSCAPE DRAWINGS	39	26-Feb-2	18-Apr-26	26-Feb-26 A	16-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	MECHANICAL DRAWINGS	142	09-Mar-2	23-Jul-26	09-Mar-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	WATER SUPPLY SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	SEWER AND DRAINAGE SYSTEM	27	09-Mar-2	14-Apr-26	09-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION SYSTEM	44	12-Mar-2	07-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	10	13-Jul-26	23-Jul-26	13-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	0%	0%	5
	ELECTRICAL DRAWINGS	105	11-May-2	08-Aug-26	11-May-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	POWER AND LIGHTING SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	ELV SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE ALARM SYSTEM	28	11-May-2	17-Jun-26	11-May-26 A	16-Jun-26 A	0.00	0.00	0.00	0%	0%	0
	AIR DOME	23	13-Jul-26	08-Aug-26	13-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	0%	0%	17
	MATERIAL SUBMITTALS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	LONG LEAD ITEMS	166	17-Feb-2	11-Jul-26	17-Feb-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	EXTERNAL / LANDSCAPE WORK	57	25-Feb-2	07-May-26	25-Feb-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	124	17-Feb-2	05-Jul-26	17-Feb-26 A	02-Sep-26 A	0.00	0.00	0.00	0%	0%	-51
	CONCRETE WORK	41	07-Mar-2	28-Apr-26	07-Mar-26 A	27-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	45	11-Mar-2	07-May-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	46	10-Mar-2	07-May-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	50	05-Mar-2	07-May-26	05-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	100	11-May-2	11-Jul-26	11-May-26 A	15-Sep-26 A	0.00	0.00	0.00	0%	0%	-57
	SHORT LEAD ITEMS	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	EXTERNAL / LANDSCAPE WORK	23	17-Feb-2	17-Mar-26	17-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	CONCRETE WORK	28	17-Feb-2	28-Mar-26	17-Feb-26 A	26-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	4	10-Mar-2	15-Mar-26	10-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	9	07-Mar-2	17-Mar-26	07-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	19	23-Feb-2	17-Mar-26	23-Feb-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	FIRE FIGHTING WORK	4	12-Mar-2	17-Mar-26	12-Mar-26 A	16-Mar-26 A	0.00	0.00	0.00	0%	0%	0
	MATERIAL APPROVALS	160	21-Feb-2	13-Jul-26	21-Feb-26 A	17-Sep-26 A	340,734.03	340,734.03	340,734.03	100%	100%	-56
	LONG LEAD ITEMS	157	25-Feb-2	13-Jul-26	25-Feb-26 A	17-Sep-26 A	284,659.98	284,659.98	284,659.98	100%	100%	-56
	EXTERNAL / LANDSCAPE WORK	56	25-Feb-2	05-May-26	25-Feb-26 A	05-May-26 A	15,425.28	15,425.28	15,425.28	100%	100%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	02-Mar-2	11-Jul-26	02-Mar-26 A	03-Sep-26 A	238,773.54	238,773.54	238,773.54	100%	100%	-47
	CONCRETE WORK	38	11-Mar-2	28-Apr-26	11-Mar-26 A	28-Apr-26 A	1,417.50	1,417.50	1,417.50	100%	100%	0
	METAL WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	889.23	889.23	889.23	100%	100%	0
	PLUMBING WORK	42	15-Mar-2	06-May-26	15-Mar-26 A	06-May-26 A	3,553.95	3,553.95	3,553.95	100%	100%	0
	IRRIGATION WORK	45	11-Mar-2	06-May-26	11-Mar-26 A	06-May-26 A	6,802.65	6,802.65	6,802.65	100%	100%	0
	ELECTRICAL WORK	96	12-May-2	13-Jul-26	12-May-26 A	17-Sep-26 A	17,797.83	17,797.83	17,797.83	100%	100%	-56
	SHORT LEAD ITEMS	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	56,074.05	56,074.05	56,074.05	100%	100%	0
	EXTERNAL / LANDSCAPE WORK	25	21-Feb-2	26-Mar-26	21-Feb-26 A	26-Mar-26 A	38,542.29	38,542.29	38,542.29	100%	100%	0
	CONCRETE WORK	24	23-Feb-2	26-Mar-26	23-Feb-26 A	26-Mar-26 A	1,609.47	1,609.47	1,609.47	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	2	15-Mar-2	16-Mar-26	15-Mar-26 A	16-Mar-26 A	7,931.55	7,931.55	7,931.55	100%	100%	0
	METAL WORK	10	11-Mar-2	26-Mar-26	11-Mar-26 A	26-Mar-26 A	478.89	478.89	478.89	100%	100%	0
	HVAC WORK	20	28-Feb-2	26-Mar-26	28-Feb-26 A	26-Mar-26 A	606.36	606.36	606.36	100%	100%	0
	PLUMBING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,147.03	3,147.03	3,147.03	100%	100%	0
	IRRIGATION WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	3,328.23	3,328.23	3,328.23	100%	100%	0
	ELECTRICAL WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	407.52	407.52	407.52	100%	100%	0
	FIRE FIGHTING WORK	2	25-Mar-2	26-Mar-26	25-Mar-26 A	26-Mar-26 A	22.71	22.71	22.71	100%	100%	0
	PROCUREMENT	201	26-Feb-2	27-Aug-26	26-Feb-26 A	21-Oct-26	3,066,606.27	2,093,273.73	3,066,606.27	100%	68.26%	-45
	LONG LEAD ITEMS	194	07-Mar-2	27-Aug-26	07-Mar-26 A	21-Oct-26	2,561,939.82	1,593,686.29	2,561,939.82	100%	62.21%	-45
	PURCHASE ORDER	157	07-Mar-2	16-Jul-26	07-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48

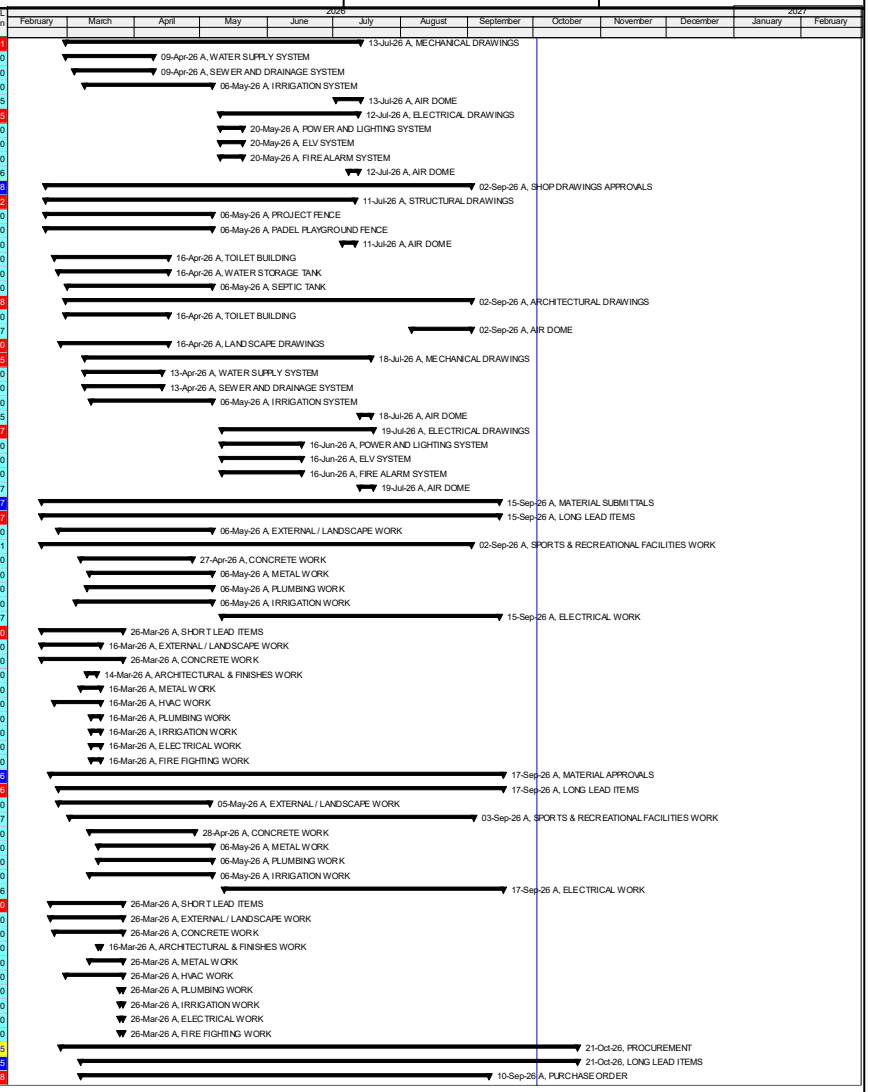


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	EXTERNAL / LANDSCAPE WORK	49	07-Mar-26	07-May-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	SPORTS & RECREATIONAL FACILITIES WORK	119	26-Mar-26	16-Jul-26	26-Mar-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-48
	CONCRETE WORK	39	18-Mar-26	07-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	38	24-Mar-26	07-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	35	28-Mar-26	07-May-26	28-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	40	17-Mar-26	07-May-26	17-Mar-26 A	06-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	105	11-May-26	16-Jul-26	11-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-47
	MANUFACTURE / FABRICATION	140	29-Apr-26	16-Aug-26	29-Apr-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-49
	EXTERNAL / LANDSCAPE WORK	102	06-May-26	23-Jul-26	06-May-26 A	10-Sep-26 A	0.00	0.00	0.00	0%	0%	-42
	SPORTS & RECREATIONAL FACILITIES WORK	124	06-May-26	16-Aug-26	06-May-26 A	14-Oct-26	0.00	0.00	0.00	0%	0%	-49
	CONCRETE WORK	64	29-Apr-26	30-Jun-26	29-Apr-26 A	02-Jul-26 A	0.00	0.00	0.00	0%	0%	-2
	METAL WORK	119	06-May-26	23-Jul-26	06-May-26 A	27-Sep-26 A	0.00	0.00	0.00	0%	0%	-55
	PLUMBING WORK	102	06-May-26	23-Jul-26	06-May-26 A	14-Sep-26 A	0.00	0.00	0.00	0%	0%	-45
	IRRIGATION WORK	99	06-May-26	01-Jul-26	06-May-26 A	21-Sep-26 A	0.00	0.00	0.00	0%	0%	-70
	ELECTRICAL WORK	129	12-May-26	10-Aug-26	12-May-26 A	30-Sep-26 A	0.00	0.00	0.00	0%	0%	-43
	DELIVERY TO SITE	146	06-May-26	27-Aug-26	06-May-26 A	21-Oct-26	2,561,939.82	1,593,686.29	2,561,939.82	100%	62.21%	-45
	EXTERNAL / LANDSCAPE WORK	114	06-May-26	06-Aug-26	06-May-26 A	04-Oct-26	138,827.52	137,434.65	138,827.52	100%	99%	-48
	SPORTS & RECREATIONAL FACILITIES WORK	129	06-May-26	27-Aug-26	06-May-26 A	21-Oct-26	2,148,961.86	1,196,115.80	2,148,961.86	100%	55.66%	-45
	CONCRETE WORK	63	06-May-26	06-Jul-26	06-May-26 A	05-Jul-26 A	12,757.50	12,757.50	12,757.50	100%	100%	1
	METAL WORK	131	06-May-26	06-Aug-26	06-May-26 A	08-Oct-26	8,003.07	6,403.24	8,003.07	100%	80.01%	-52
	PLUMBING WORK	108	06-May-26	06-Aug-26	06-May-26 A	04-Oct-26	31,985.55	31,360.72	31,985.55	100%	98.05%	-48
	IRRIGATION WORK	98	06-May-26	06-Jul-26	06-May-26 A	03-Oct-26	61,223.85	59,587.38	61,223.85	100%	97.33%	-75
	ELECTRICAL WORK	140	13-May-26	24-Aug-26	13-May-26 A	05-Oct-26	160,180.47	150,027.00	160,180.47	100%	93.66%	-34
	SHORT LEAD ITEMS	190	26-Feb-26	22-Jul-26	26-Feb-26 A	08-Oct-26	504,666.45	499,587.44	504,666.45	100%	98.99%	-66
	PURCHASE ORDER	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	EXTERNAL / LANDSCAPE WORK	163	26-Feb-26	11-Jul-26	26-Feb-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-41
	CONCRETE WORK	41	02-Mar-26	23-Apr-26	02-Mar-26 A	22-Apr-26 A	0.00	0.00	0.00	0%	0%	0
	ARCHITECTURAL & FINISHES WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	METAL WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	HVAC WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	PLUMBING WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	IRRIGATION WORK	7	05-May-26	13-May-26	05-May-26 A	12-May-26 A	0.00	0.00	0.00	0%	0%	0
	ELECTRICAL WORK	97	11-May-26	02-Jul-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-48
	FIRE FIGHTING WORK	94	11-May-26	29-Jun-26	11-May-26 A	27-Aug-26 A	0.00	0.00	0.00	0%	0%	-51
	DELIVERY TO SITE	188	01-Mar-26	22-Jul-26	01-Mar-26 A	08-Oct-26	504,666.45	499,587.44	504,666.45	100%	98.99%	-66
	EXTERNAL / LANDSCAPE WORK	171	01-Mar-26	22-Jul-26	01-Mar-26 A	03-Oct-26	346,880.61	344,882.80	346,880.61	100%	99.42%	-61
	CONCRETE WORK	52	10-Mar-26	13-May-26	10-Mar-26 A	13-May-26 A	14,485.23	14,485.23	14,485.23	100%	100%	0
	ARCHITECTURAL & FINISHES WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	71,383.95	71,383.95	71,383.95	100%	100%	0
	METAL WORK	135	06-May-26	08-Jul-26	06-May-26 A	08-Oct-26	4,310.01	3,448.01	4,310.01	100%	80%	-78
	HVAC WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	5,457.24	5,457.24	5,457.24	100%	100%	0
	PLUMBING WORK	7	06-May-26	13-May-26	06-May-26 A	13-May-26 A	28,323.27	28,323.27	28,323.27	100%	100%	0
	IRRIGATION WORK	97	06-May-26	05-Jul-26	06-May-26 A	03-Oct-26	29,954.07	28,456.37	29,954.07	100%	95%	-76
	ELECTRICAL WORK	118	13-May-26	16-Jul-26	13-May-26 A	06-Oct-26	3,667.68	3,007.50	3,667.68	100%	82%	-69
	FIRE FIGHTING WORK	126	13-May-26	09-Jul-26	13-May-26 A	07-Oct-26	204.39	143.07	204.39	100%	70%	-76
	CONSTRUCTION STAGE	258	24-Mar-26	14-Dec-26	24-Mar-26 A	24-Jan-27	4,190,419.33	3,389,565.75	6,814,680.60	61.49%	49.74%	-35
	PLAYGROUND AND LANDSCAPING WORKS	258	24-Mar-26	14-Dec-26	24-Mar-26 A	24-Jan-27	1,751,580.47	1,887,820.71	2,311,795.02	75.77%	81.66%	-35
	CUT AND FILL	38	24-Mar-26	06-May-26	24-Mar-26 A	06-May-26 A	228,240.00	228,240.00	228,240.00	100%	100%	0
	PLAYGROUND WORKS	177	23-Apr-26	07-Dec-26	23-Apr-26 A	23-Nov-26	469,976.40	528,146.30	623,491.20	75.38%	84.71%	12
	FOOTBALL PLAYGROUND WORKS	155	23-Apr-26	17-Nov-26	23-Apr-26 A	27-Oct-26	258,022.50	292,891.29	333,290.16	77.42%	87.88%	19
	BASKETBALL PLAYGROUND WORKS	147	06-May-26	17-Nov-26	06-May-26 A	02-Nov-26	152,557.32	154,829.41	173,211.12	88.08%	89.39%	13
	PADEL PLAYGROUND WORKS	166	06-May-26	07-Dec-26	06-May-26 A	23-Nov-26	59,396.58	80,425.60	116,989.92	50.77%	68.75%	12
	GENERAL SITE WORKS	238	16-Apr-26	14-Dec-26	16-Apr-26 A	24-Jan-27	559,419.17	437,752.23	656,604.42	85.2%	66.67%	-35
	FENCE WORKS	151	16-Apr-26	17-Aug-26	16-Apr-26 A	14-Oct-26	32,909.40	21,391.11	32,909.40	100%	65%	-49
	MECHANICAL WORK	138	12-May-26	10-Aug-26	12-May-26 A	25-Oct-26	230,187.54	191,422.27	230,187.54	100%	83.16%	-64
	STORM WATER AND UTILITY WORK	133	12-May-26	04-Aug-26	12-May-26 A	19-Oct-26	27,252.00	14,658.00	27,252.00	100%	53.79%	-64
	IRRIGATION SYSTEM WORKS	96	02-Jun-26	30-Jul-26	02-Jun-26 A	14-Oct-26	202,617.60	176,764.27	202,617.60	100%	87.24%	-64
	FIRE PROTECTION SYSTEM	5	05-Aug-26	10-Aug-26	19-Oct-26	25-Oct-26	317.94	0.00	317.94	100%	0%	0
	ELECTRICAL WORK	179	08-Jun-26	07-Nov-26	08-Jun-26 A	03-Jan-27	289,863.83	197,011.26	345,859.68	83.81%	56.96%	-49
	POWER, LIGHTING & GROUNDING	144	08-Jun-26	27-Sep-26	08-Jun-26 A	24-Nov-26	288,789.48	188,382.06	288,789.48	100%	65.23%	-49
	ELV SYSTEMS (TELECOM, DATA, AV & CCTV)	25	28-Sep-26	26-Oct-26	22-Sep-26 A	17-Dec-26	826.40	8,629.20	43,146.00	1.92%	20%	-48
	FIRE ALARM SYSTEM	32	01-Oct-26	07-Nov-26	26-Nov-26	03-Jan-27	247.95	0.00	13,924.20	1.78%	0%	0
	PARKING WORK	171	17-Jun-26	11-Nov-26	17-Jun-26 A	03-Jan-27	5,788.80	23,798.40	40,207.80	14.4%	59.19%	-45
	SERVICE CONNECTION	195	10-Jun-26	14-Dec-26	10-Jun-26 A	24-Jan-27	669.60	4,129.20	7,440.00	9%	55.5%	-35
	LANDSCAPING WORKS	156	31-May-26	22-Nov-26	30-May-26 A	02-Dec-26	445,654.50	684,610.89	755,169.00	59.01%	90.66%	-8
	HARDSCAPE WORK	156	31-May-26	22-Nov-26	30-May-26 A	02-Dec-26	421,294.50	624,579.69	648,147.00	65%	96.36%	-8
	SOFTSCAPE WORK	143	10-Jun-26	22-Nov-26	10-Jun-26 A	02-Dec-26	24,360.00	60,031.20	107,022.00	22.76%	56.09%	-8
	TANK WORKS	148	13-May-26	27-Sep-26	13-May-26 A	08-Nov-26	48,290.40	9,071.28	48,290.40	100%	18.78%	-35
	SEPTIC TANK	143	13-May-26	03-Sep-26	13-May-26 A	02-Nov-26	7,475.22	2,969.10	7,475.22	100%	39.72%	-49
	WATER STORAGE TANK	148	13-May-26	27-Sep-26	13-May-26 A	08-Nov-26	40,815.18	6,102.18	40,815.18	100%	14.95%	-35
	AIR DOME CONSTRUCTION	212	13-May-26	03-Dec-26	13-May-26 A	21-Jan-27	2,290,178.63	1,210,693.39	4,178,041.20	54.81%	28.98%	-41
	CIVIL WORK	144	13-May-26	14-Sep-26	13-May-26 A	03-Nov-26	1,711,669.97	1,210,693.39	1,711,669.97	100%	70.73%	-41
	ARCHITECTURAL WORK	25	05-Nov-26	03-Dec-26	23-Dec-26	21-Jan-27	0.00	0.00	712,953.22	0%	0%	0
	MECHANICAL WORK	23	15-Sep-26	12-Oct-26	03-Nov-26	30-Nov-26	459,228.53	0.00	667,968.77	68.75%	0%	0

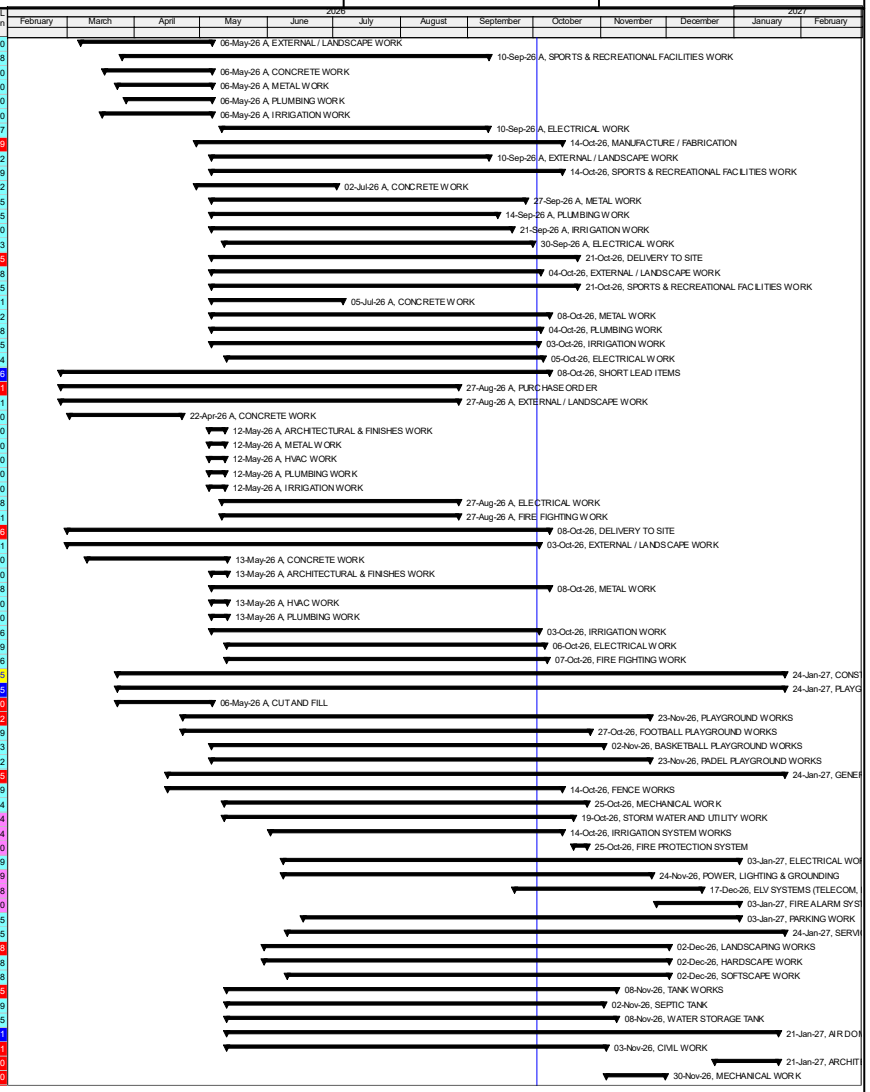


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00

PLAYGROUNDS INITIATIVE - QASSIM, HAIL & TABUK - 04-Oct-2026

Activity ID	Activity Name	O.D	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Schedule % Complete	Performance % Complete	Variance - BL Project Duration
	ELECTRICAL WORK	33	28-Sep-26	04-Nov-26	15-Nov-26	23-Dec-26	119,280.14	0.00	1,085,449.25	10.99%	0%	0
	TOILET BUILDING WORKS	143	12-May-26	28-Oct-26	12-May-26 A	13-Oct-26	148,660.23	291,051.65	324,844.38	45.76%	89.6%	14
	CIVIL WORK	143	12-May-26	26-Oct-26	12-May-26 A	12-Oct-26	58,754.49	218,211.21	227,117.58	25.87%	96.08%	13
	STRUCTURAL WORK	59	12-May-26	01-Aug-26	12-May-26 A	12-Aug-26 A	37,980.00	37,980.00	37,980.00	100%	100%	-10
	ARCHITECTURAL WORK	76	02-Aug-26	26-Oct-26	01-Aug-26 A	12-Oct-26	20,774.49	180,231.21	189,137.58	10.98%	95.29%	12
	GENERAL FINISHES	76	02-Aug-26	21-Oct-26	01-Aug-26 A	07-Sep-26 A	10,782.09	84,120.00	84,120.00	12.82%	100%	37
	WET AREA FINISHES	37	26-Aug-26	13-Oct-26	06-Aug-26 A	11-Oct-26	9,992.40	78,442.98	81,123.78	12.32%	96.7%	-14
	ROOF FINISHES	46	07-Oct-26	26-Oct-26	14-Aug-26 A	12-Oct-26	0.00	17,668.23	23,893.80	0%	73.94%	-32
	MEP WORK	103	16-Jun-26	28-Oct-26	16-Jun-26 A	13-Oct-26	89,903.74	72,840.44	97,726.80	92%	74.53%	14
	MECANICAL WORKS	103	16-Jun-26	28-Oct-26	16-Jun-26 A	13-Oct-26	71,658.42	54,593.12	79,479.48	90.16%	68.69%	14
	FIRE FIGHTING SYSTEM	2	27-Oct-26	28-Oct-26	23-Sep-26 A	13-Oct-26	0.00	40.88	136.26	0%	30%	-14
	SEWER AND DRAINAGE SYSTEM	92	16-Jun-26	05-Sep-26	16-Jun-26 A	10-Oct-26	11,290.02	9,677.16	11,290.02	100%	85.71%	-28
	HVAC SYSTEM	42	09-Aug-26	12-Oct-26	13-Aug-26 A	11-Oct-26	4,442.40	7,132.08	12,127.20	36.63%	58.81%	6
	WATER SUPPLY SYSTEM	45	12-Aug-26	02-Sep-26	22-Jul-26 A	08-Oct-26	55,926.00	37,743.00	55,926.00	100%	67.49%	-47
	ELECTRICAL WORKS	38	15-Aug-26	17-Sep-26	22-Jul-26 A	16-Sep-26 A	18,247.32	18,247.32	18,247.32	100%	100%	-18
	PROJECT CLOSOUT	213	25-May-26	16-Dec-26	25-May-26 A	03-Feb-27	34,073.40	210,119.32	1,135,780.10	3%	18.5%	-41



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining W...
Milestone
summary

Baseline Schedule Rev.00
