Additional Development and Network Completion, Tabuk Industrial City

تطوير اضافي و استكمال شبكات في تبوك

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	ASAS for Developing & Operating Industrial Cities	EGIS	Eng. Yazeed Alragabah	04-Sep-2025	03-Sep-2027

Scope: roads, the Pond A storm-water outfall, storm, sewerage, potable water and fire-fighting, TSE irrigation, road lighting, telecom and CCTV networks in three zones of Tabuk Industrial City. Contract value 140.5M SAR excl. VAT.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The project is at 54.0% against 37.8% planned under the revised plan, 16.2% ahead (SPI 1.43). This week it gained 2.1% against 1.1% planned, the largest weekly gain of the last three weeks.

PHYSICAL % COMPLETE
54.0% / 37.8% plan
▲ SPI 1.43 +16.2%

PROGRESS THIS WEEK
+2.1% / +1.1% plan
▲ 1.0% above the weekly plan

CONTRACT TIME ELAPSED
58.2% · day 424 of 729
▼ Forecast finish 06-Oct-2027


INVOICED TO DATE (GROSS)
36.2% · 50.9M SAR
15 invoices, last period ends 29-Oct-2026

Well ahead of the revised plan, but the forecast finish is still about five weeks after the contract date.

The P6 update (data date 02-Nov-2026) and the weekly report both forecast handover on 06-Oct-2027, 33 days after the contract completion date of 03-Sep-2027; the P6 project finish has −28.4 days of float. Open activities with negative float fell from 228 to 224, mostly in electrical (82), CCTV (72) and telecom (38) works. Against the original baseline, which called for 64.2% by the end of October, the project is behind.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet, weekly report 02-Nov-2026. The sheet records the latest actual in the month of the data date (November).

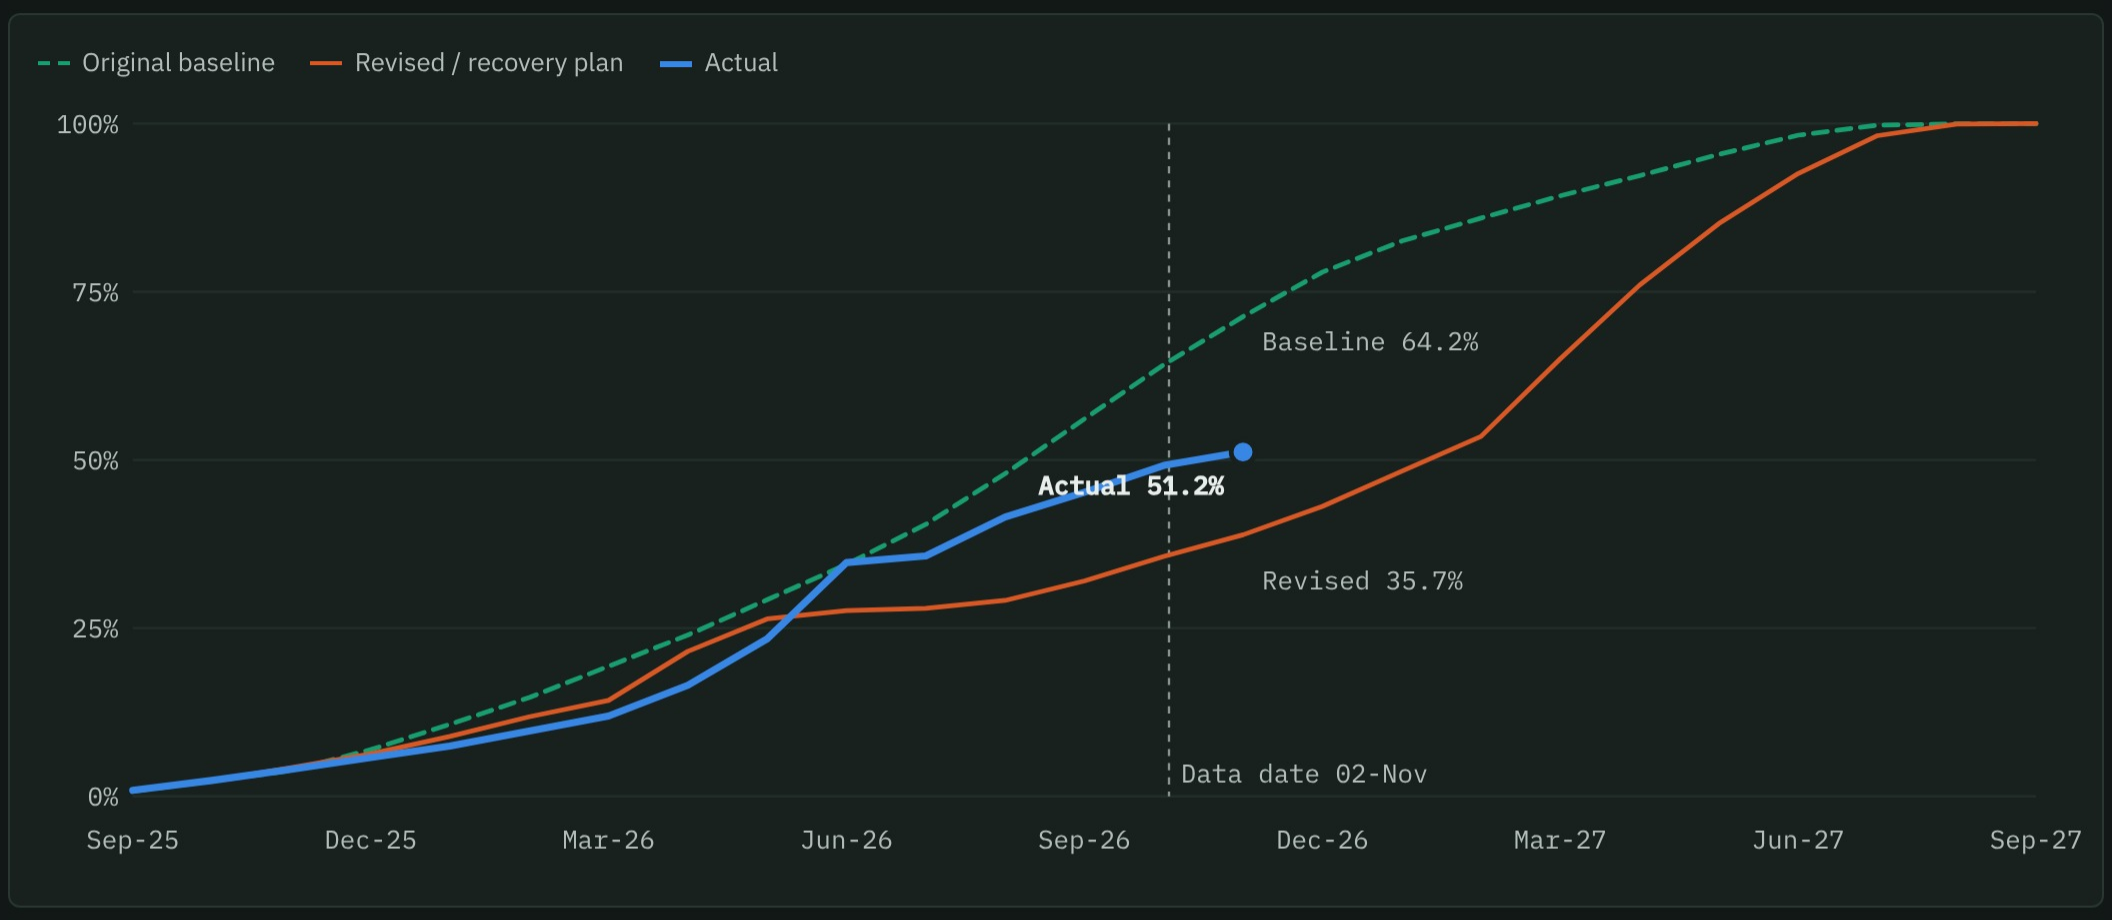

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
12-Oct-2026	34.6	49.9	+15.3	–	1.44
19-Oct-2026	35.2	50.7	+15.5	+0.8	1.44
26-Oct-2026	36.7	51.9	+15.2	+1.2	1.42
02-Nov-2026	**37.8**	**54.0**	**+16.2**	**+2.1**	**1.43**

From the Progress sheets of the 19-Oct, 26-Oct and 02-Nov weekly reports (the 12-Oct row is the "last week" column of the 19-Oct report); earlier weeks are not available. The weekly table uses 354,339 budgeted man-hours; the S-curve sheet uses 373,967 and shows 51.2% actual at the same date.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	0.5%	100.0%	100.0%	0.0	1.00	✓ Complete
Construction works	98.0%	38.1%	54.7%	+16.6	1.43	▲ Ahead
Zone 1	21.1%	42.6%	61.9%	+19.3	1.45	▲ Ahead
Zone 2	25.3%	50.7%	75.5%	+24.8	1.49	▲ Ahead
Zone 3	51.6%	30.1%	41.5%	+11.4	1.38	▲ Ahead
Close-out	1.6%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**37.8%**	**54.0%**	**+16.2**	**1.43**	▲ Ahead

Engineering and procurement carry no man-hours in this measure, so they are not shown. The P6 update has 1,492 activities: 639 completed, 195 in progress and 658 not started.

Scope of work: quantities

Total, finished and remaining quantity for the main items, from the Major Quantities sheet of the 02-Nov-2026 weekly report. "This week" is the change from the 26-Oct-2026 report. The sheet gives project totals only, with no split by zone and no backfill figures.

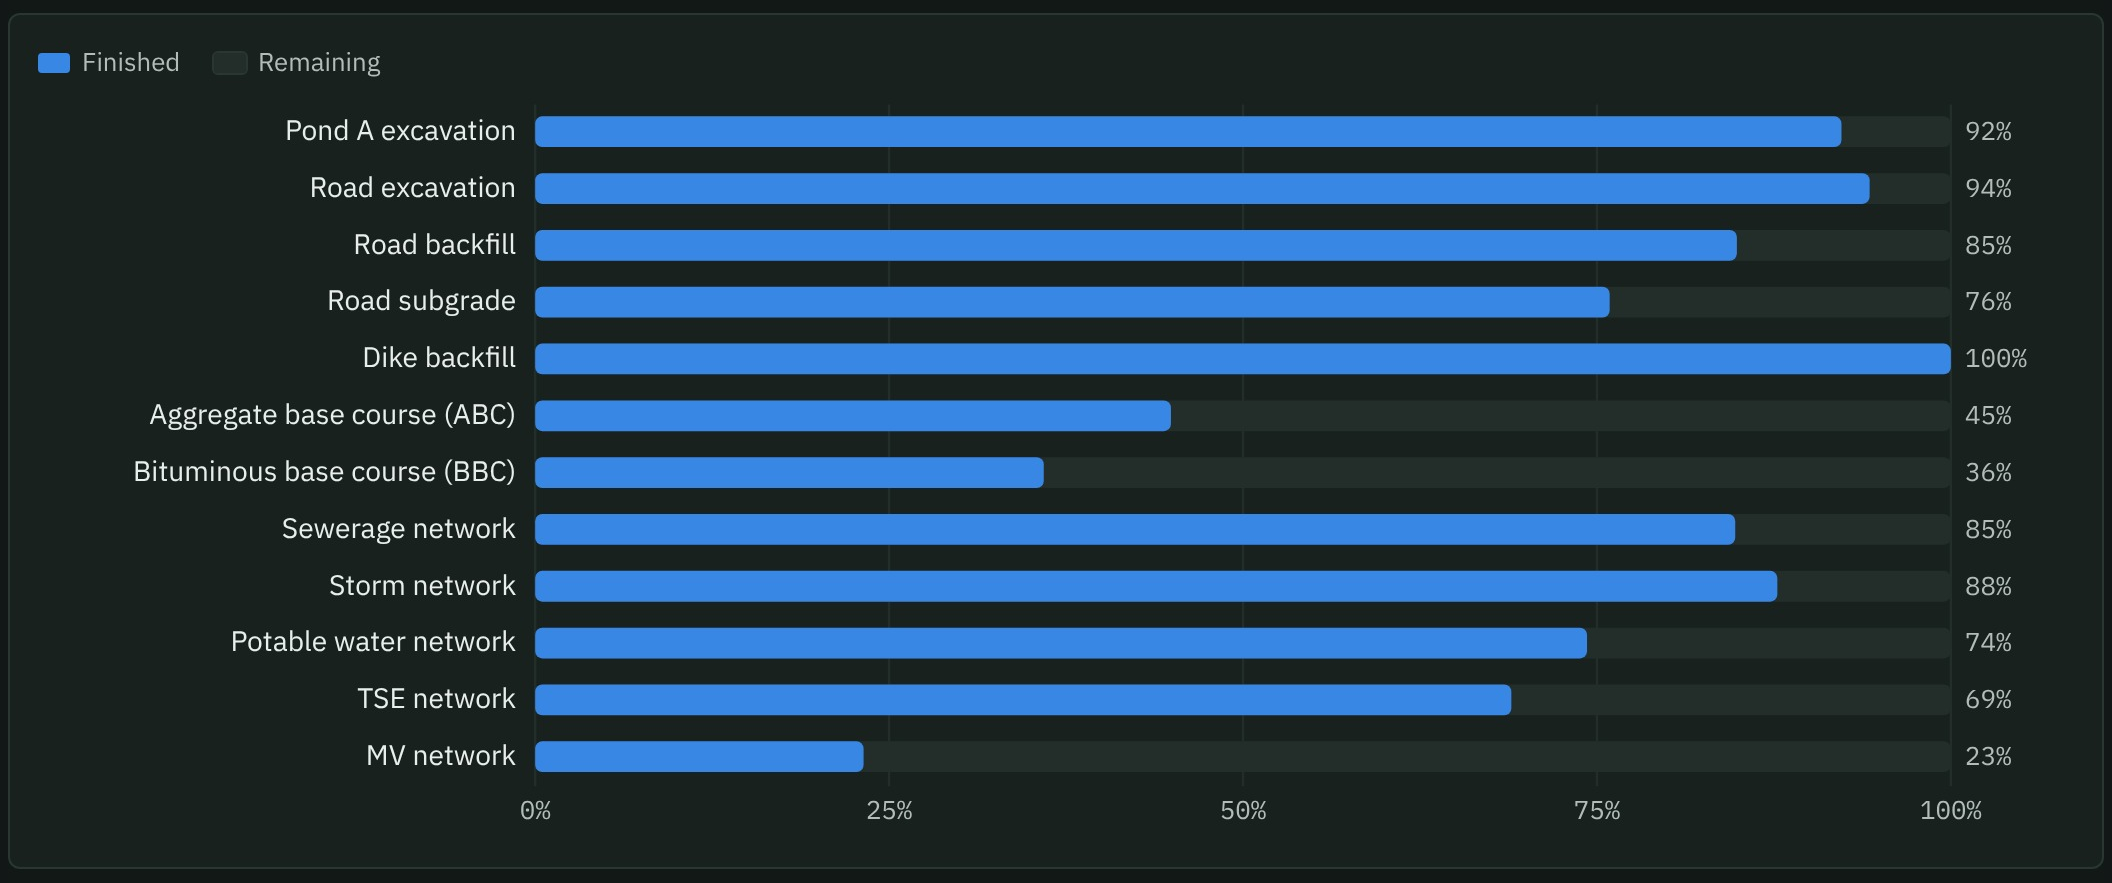

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Pond A excavation	All zones	m³	321,070	296,255	0	24,815	92.3%	–
Road excavation	All zones	m³	99,925	94,190	+715	5,735	94.3%	–
Road backfill	All zones	m³	107,100	90,910	+4,155	16,190	84.9%	–
Road subgrade	All zones	m³	72,730	55,200	+300	17,530	75.9%	–
Dike backfill	All zones	m³	3,865	3,865	0	0	100.0%	–
Aggregate base course (ABC)	All zones	m³	48,485	21,774	+871	26,711	44.9%	–
Bituminous base course (BBC)	All zones	m³	27,310	9,811	+1,303	17,499	35.9%	–
Sewerage network	All zones	LM	8,370	7,095	0	1,275	84.8%	–
Storm network	All zones	LM	15,638	13,721	+74	1,917	87.7%	–
Potable water network	All zones	LM	13,221	9,823	+311	3,398	74.3%	–
TSE network	All zones	LM	12,223	8,428	0	3,795	69.0%	–
MV network	All zones	LM	23,700	5,498	+500	18,202	23.2%	–

Wet networks well advanced

Sewerage is 85% laid, storm 88%, potable water 74% and TSE 69%. This week added 311 m of potable water and 74 m of storm pipe; sewer and TSE did not move.

Road layers and MV behind

Aggregate base course is at 45% (+871 m³) and bituminous base course at 36% (+1,303 m³). The MV network moved from 21% to 23% (+500 m); its connection to the substation is still an open issue.

Milestones

Baseline and forecast from the Milestones sheet of the weekly report; P6 forecast and total float from the P6 update (data date 02-Nov-2026). For the network finishes the baseline is the P6 baseline from the progress tracker, and the weekly report gives no forecast.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	04-Sep-2025	04-Sep-2025	04-Sep-2025 (actual)	–	✓ Done
Complete preliminary submittals	06-Dec-2025	11-Dec-2026 (+370 d)	–	–	▼ Late
Complete Zone 1	09-Feb-2027	03-Oct-2027 (+236 d)	02-Jun-2027	+80.3	? Conflicts with P6
Complete Zone 2	02-Aug-2027	12-Sep-2027 (+41 d)	22-Jun-2027	+38.2	? Conflicts with P6
Complete Zone 3	02-Aug-2027	28-Sep-2027 (+57 d)	15-Jun-2027	+69.7	? Conflicts with P6
Sewerage network	14-Aug-2027	–	14-Mar-2027	+149.6	● Float available
Potable water network	21-Aug-2027	–	21-Jun-2027	+64.7	● Float available
TSE network	21-Jul-2027	–	10-Jun-2027	+73.4	● Float available
Storm network	14-Aug-2027	–	24-Jul-2027	+36.9	● Float available
Telecom network	16-Aug-2027	–	28-Aug-2027	+6.4	● Float available
CCTV network	03-Sep-2027	–	02-Oct-2027	−24.6	▼ Late
Road works	02-Sep-2027	–	30-Sep-2027	−23.4	▼ Late
Electrical works	03-Sep-2027	–	03-Oct-2027	−25.9	▼ Late
Complete delivery of all materials	03-Aug-2027	30-Sep-2027 (+58 d)	–	–	▼ Late
All works complete, ready for initial handover	10-Aug-2027	02-Oct-2027 (+53 d)	–	–	▼ Late
Project handover	03-Sep-2027	06-Oct-2027 (+33 d)	06-Oct-2027	−28.4	▼ Late

The weekly report and P6 disagree on the zone completion dates.

The weekly report forecasts Zones 1, 2 and 3 to finish between 12-Sep-2027 and 03-Oct-2027, while the P6 update finishes them between 02-Jun-2027 and 22-Jun-2027 with positive float. Both put project handover on 06-Oct-2027. The late items in P6 are road works, electrical and CCTV; telecom now has positive float.

Procurement of key materials

Completion rate of delivery per material. Source: Procurement sheet, weekly report 02-Nov-2026.

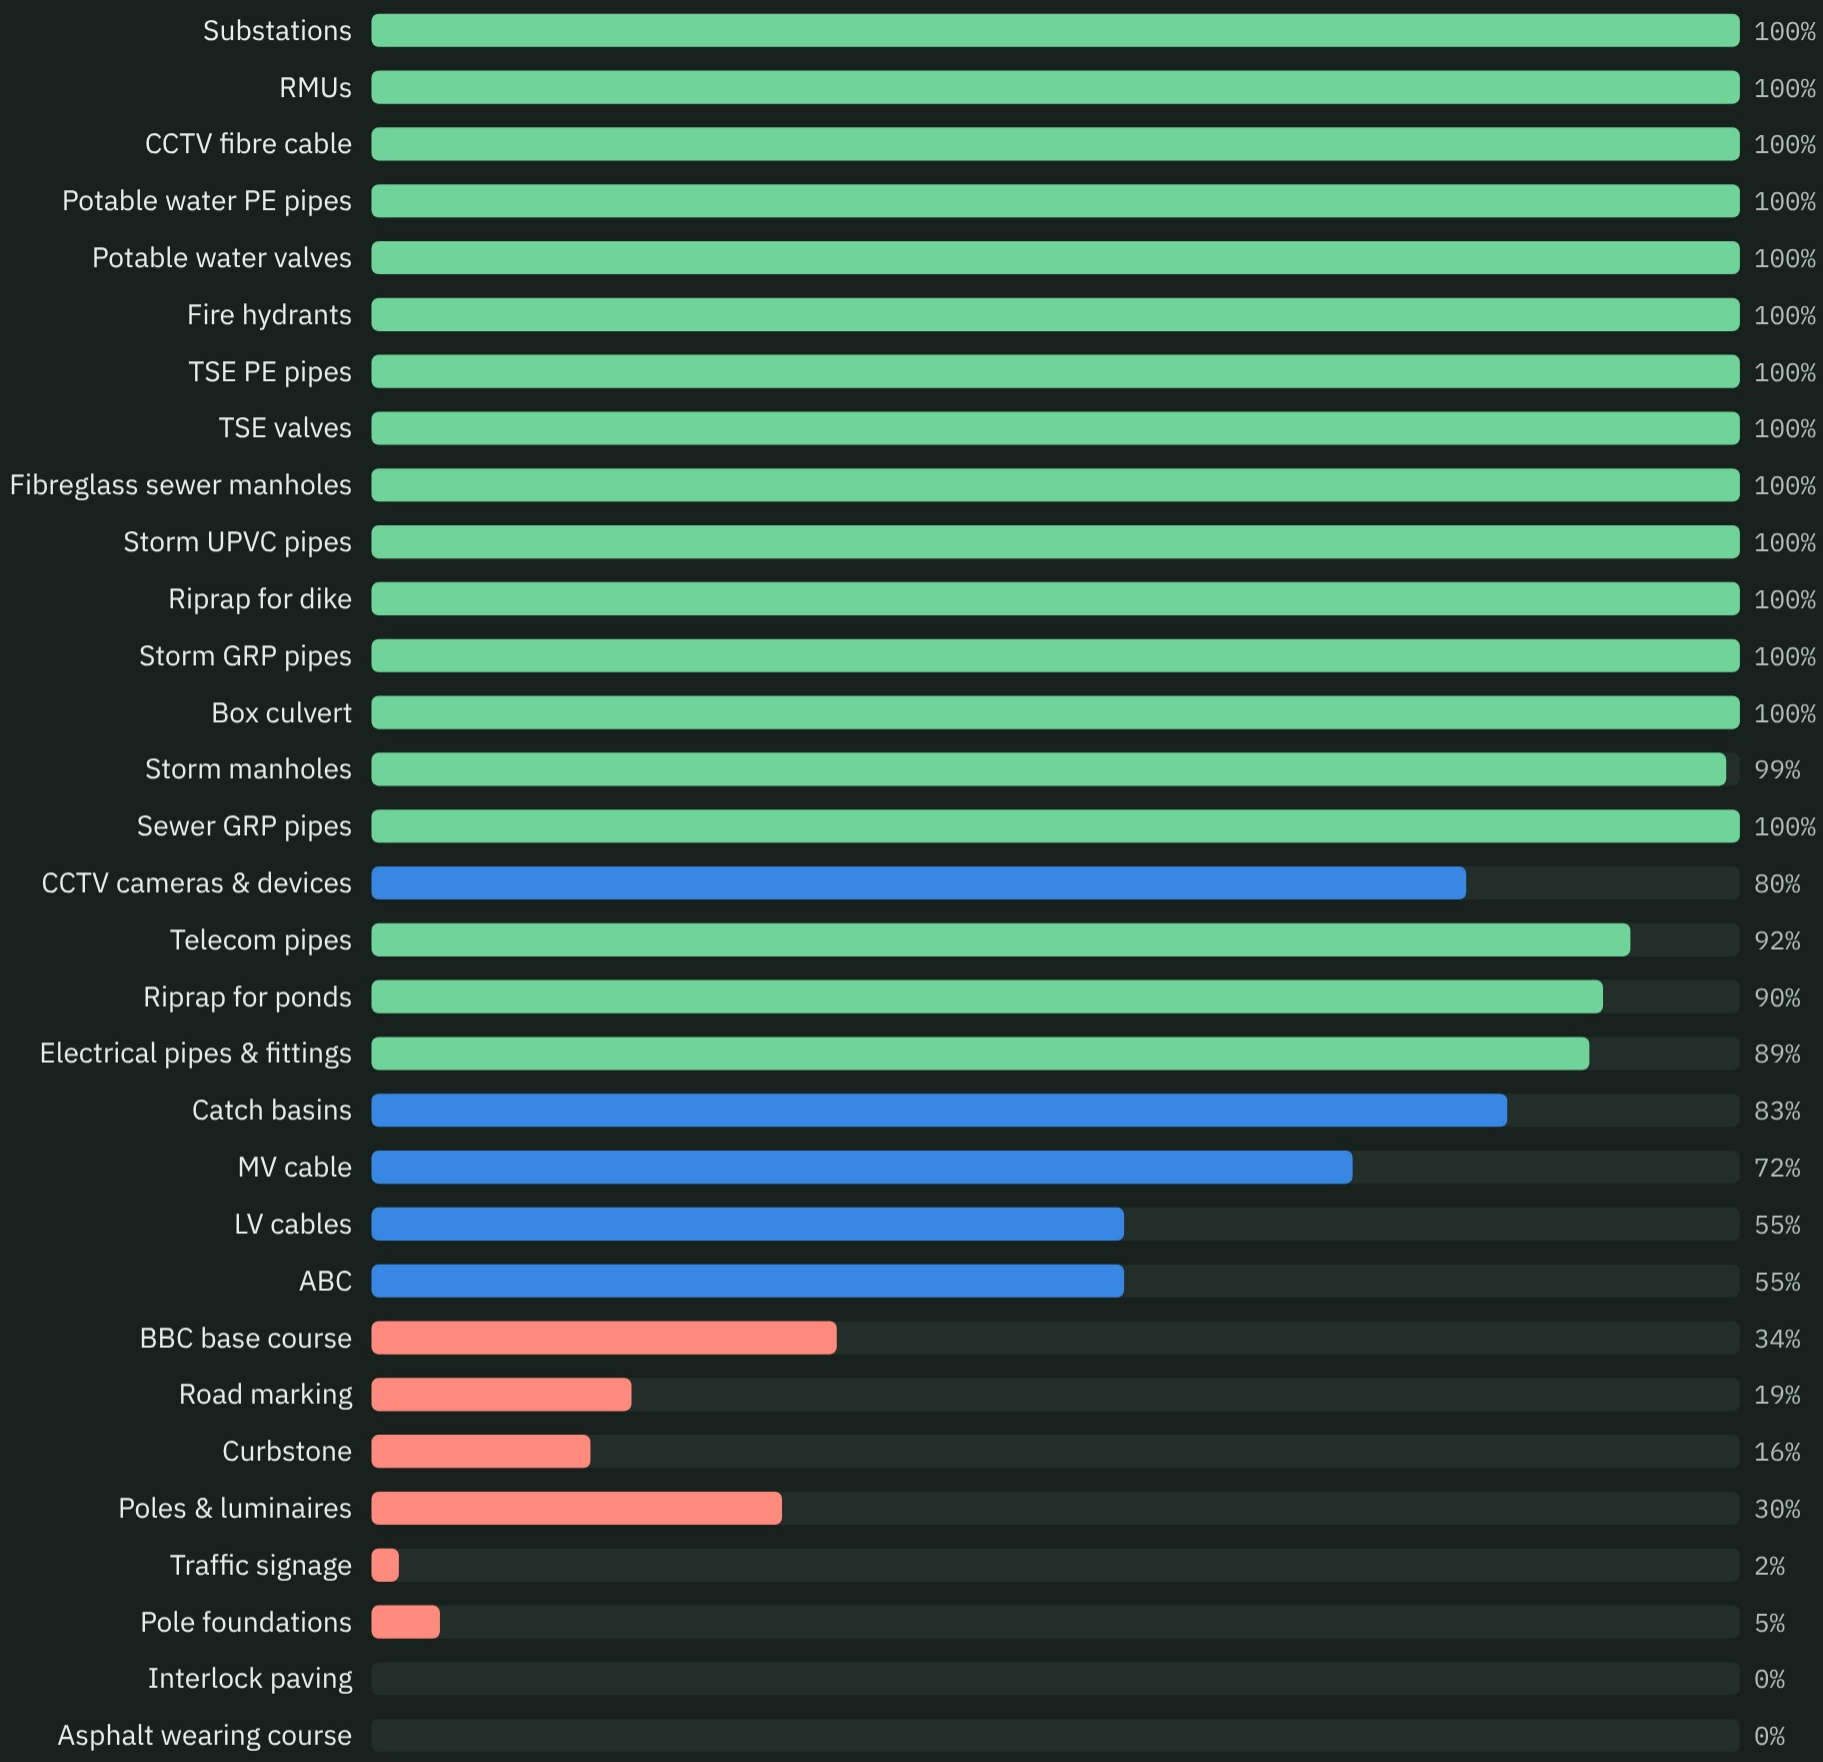

Interlock and wearing course still not delivered; street lighting at 30%


Interlock (62,075 m²) and the asphalt wearing course have purchase orders but no delivery. Poles and luminaires rose from 8% to 30% of 957 and pole foundations from 1% to 5%. Curbstone is at 16% and traffic signage at 2%.

Electrical cables part-delivered

MV cable is at 72% of 115,400 m and LV cables at 55%. Substations and RMUs are fully delivered. Sewer GRP pipes were completed this week, and CCTV cameras are 80% delivered; the other wet-network materials are complete or nearly so.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

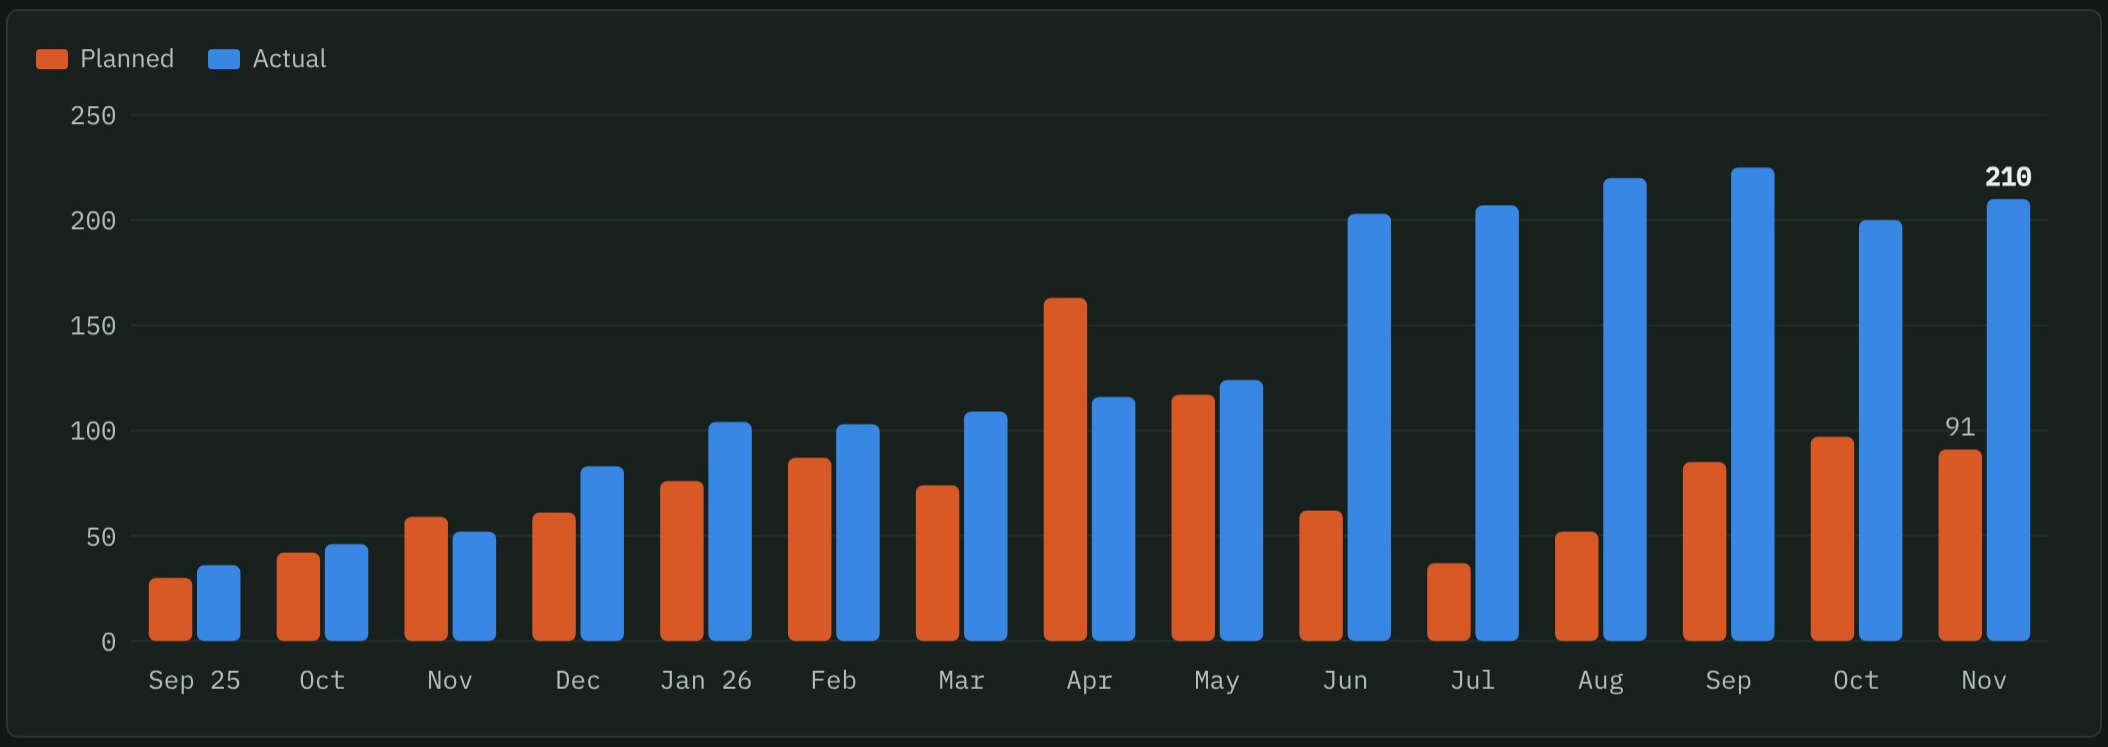

November head count is 210 (35 non-manual, 175 manual) against 91 planned, up from 200 in October. The plan rises to a peak of 229 in March 2027. Equipment on site in November: 63 against 29 planned.

Cost and invoicing

Contract value

Roads	55,700,828
Storm water network	42,542,241
Electrical	21,956,853
Potable water network	7,176,559
TSE network	6,656,378
Sewerage network	6,435,003
Contract value (excl. VAT)	**140,467,862**
Change orders	0

All values in SAR, from the BOQ summary in the weekly report. The parts add up to the contract value. No change orders are registered.

Invoices

Invoices in the log	15
Gross value submitted	50,860,088
PM-approved (13 invoices)	43,497,867
Paid incl. VAT (13 invoices)	50,080,548
Deductions and penalties	110,000
Advance payment (10%)	14,046,786
Retention	0
FIR value to date	56,302,460

Invoicing is 36.2% of the contract value against 54.0% physical progress. Invoice 15 (4,647,428 SAR, dated 29-Oct-2026) was submitted this week; invoices 14 and 15 are waiting for PM approval.

Health, safety and quality

Safety Score 0.95

Safe man-hours (cumulative)	391,334
Man-hours this week	10,050
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	8 / 36

Quality Score 0.93

FIRs issued / pending	7,605 / 138
MIRs issued / pending	249 / 1
NCRs issued / closed	12 / 12
Site instructions issued / closed	20 / 20
Shop drawing submittals	428
Material submittals approved	48 / 52

Cumulative to 02-Nov-2026. The consultant's weekly audits on 29–30 Oct 2026 scored quality 0.97 and safety 0.95. One new NCR was issued and closed this week.

Open issues and risks

ISSUE	OWNER	DETAIL
MV connection to the substation	MODON	Open since 15-Jun-2026. The start of the MV network connection to the station is waiting for the station's response; target now 10-Nov-2026.
Shop drawings to Code A	Contractor	Open since 29-Jun-2026. Drawings are being submitted for upgrade to Code A; target now 15-Nov-2026.
More telecom manholes	Contractor	Open since 05-Oct-2026. The number of telecom manholes has increased; waiting for the shop drawing, target now 10-Nov-2026.
Deep excavation	Contractor	Open safety risk: collapse of excavation sides. Barriers and warning signs are in place and equipment is kept away from the edges.

The Shinko fence that blocked the electrical works was closed in the issue log on 29-Oct-2026 (fence removal in progress). The project challenges named in this week's MODON summary are still the Code A drawing approval and the MV connection to the substation.

Data notes

- Physical progress appears with two values. The weekly report's summary and Progress sheet give 54.01% (191,388 of 354,339 budgeted man-hours), while the Physical-Chart Data sheet gives 51.18% (of 373,967). The headline uses the report's own summary figure.
- The MODON weekly summary file, the P6 progress tracker and the progress certificates label cost-weighted progress as "actual" and "planned". This report uses physical % complete (man-hour weighted) only.
- The project ID differs between files: TAB1-02-003 in the weekly report, TAB1-01-009 in the MODON summary file and the older procurement sheet, and TAB1-02-005 to TAB1-02-008 in the risk register.
- Report week: the Milestones sheet states contract week 61 of 109, and the consultant's audits label 29–30 Oct 2026 as Week-61. Counting whole weeks from site handover gives 60. The report uses the stated week 61.
- Zone milestones disagree three ways: the weekly report's baseline (Zone 1 09-Feb-2027), the P6 baseline in the progress tracker (Zone 1 05-Jun-2027), and the forecasts in the weekly report (Zone 1 03-Oct-2027) and P6 (Zone 1 02-Jun-2027); see Milestones.
- The HSE statistics now show 391,334 cumulative man-hours, exactly 10,050 (this week's hours) more than the 381,284 shown in both of the previous two reports, so one week's hours appear to be missing from the cumulative total. The summary panel shows 6,360 safe hours this week against 10,050 on the HSE sheet.
- The "Resources at site" panel (28/35 non-manual, 149/384 manual) does not match the November manpower sheet (28/35 and 63/175). Cumulative actual equipment has stayed at 269 since March 2026.
- The workbook has two procurement sheets; the report uses "Procurement", not the older "Procurement (2)". Some items have no quantity or delivery rate.
- Risk register entries are still all marked "Open", including those whose treatment is closed. Open issues keep moving their target dates (MV connection: 30-Oct, then 03-Nov, now 10-Nov-2026).
- No site photos are shown: the five images in this week's weekly report are 329 to 529 px wide, below the 600 px minimum, and the PDFs contain none.

Compiled 08-Nov-2026 from the weekly report for the week ending 02-Nov-2026, with the 26-Oct-2026 report for this-week values.
