Road Development for the Support Services Area, Second Industrial City in Makkah (Al-Akayshiyah)

تطوير الطرق لمنطقة الخدمات المساندة بالمدينة الصناعية الثانية بمكة المكرمة (العكيشية)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Trading & Contracting Co.	EGIS	Abdallah Aljulaifi	25-Jun-2026	24-Aug-2027

Scope: road works and the storm water drainage network for the support services area of the Second Industrial City in Makkah, Al-Akayshiyah. Contract value 33.04M SAR excluding VAT, 14 months from site handover.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. On 03-Nov-2026 the project is 53.3% complete against 39.2% planned, 14.1% ahead of plan. This week it gained 5.0% against 3.6% planned, the largest weekly gain in the last three reports.

PHYSICAL % COMPLETE

53.3% / 39.2% plan

▲ SPI 1.36 +14.1%

PROGRESS THIS WEEK

+5.0% / +3.6% plan

▲ 1.4% above the weekly plan

CONTRACT TIME ELAPSED

30.8% · day 131 of 425

▼ P6 finish 28-Oct-2027

INVOICED TO DATE (GROSS)

20.4% · 6.75M SAR

3 invoices, all paid; last period ends 27-Sep-2026

Progress is well ahead of plan, but the forecast finish slipped another week: now 65 days late.

The P6 update (UP 16, data date 03-Nov-2026) schedules project completion on 28-Oct-2027, 65 days after the contract completion date of 24-Aug-2027, with −55 days of total float (−49 last week). The weekly report gives the same forecast. Pavement materials still have no purchase orders; the failed-start list has moved the aggregate base order again, to 03-Nov-2026.

Site photos this week

Six photos from the Tracking Sheet presentation uploaded with the 03-Nov-2026 weekly report, with their slide captions. Five are stamped 01-Nov-2026 and one 02-Nov-2026, with time and altitude (no GPS coordinates are shown). Select a photo to view it larger, then use the arrows to move between photos.



Cutting works, Local Road 17

Stamped 01-Nov-2026, 06:35, altitude 180.2 m.



Cutting works, Local Road 11

Stamped 01-Nov-2026, 06:55, altitude 184.0 m.



Excavation for UPVC pipes, Local Road 28

Stamped 01-Nov-2026, 11:26, altitude 172.0 m.



Field density test, catch basin base, Local Road 28

Stamped 01-Nov-2026, 10:25.



Manhole works, Local Road 28

Stamped 01-Nov-2026, 10:45, altitude 178.5 m.




Kerb installation, Local Road 30

Stamped 02-Nov-2026, 10:33, altitude 167.9 m.

Progress S-curve

Cumulative physical progress (man-hour weighted), month-end values; the actual line ends at 31-Oct-2026. Source: Physical-Chart Data sheet.

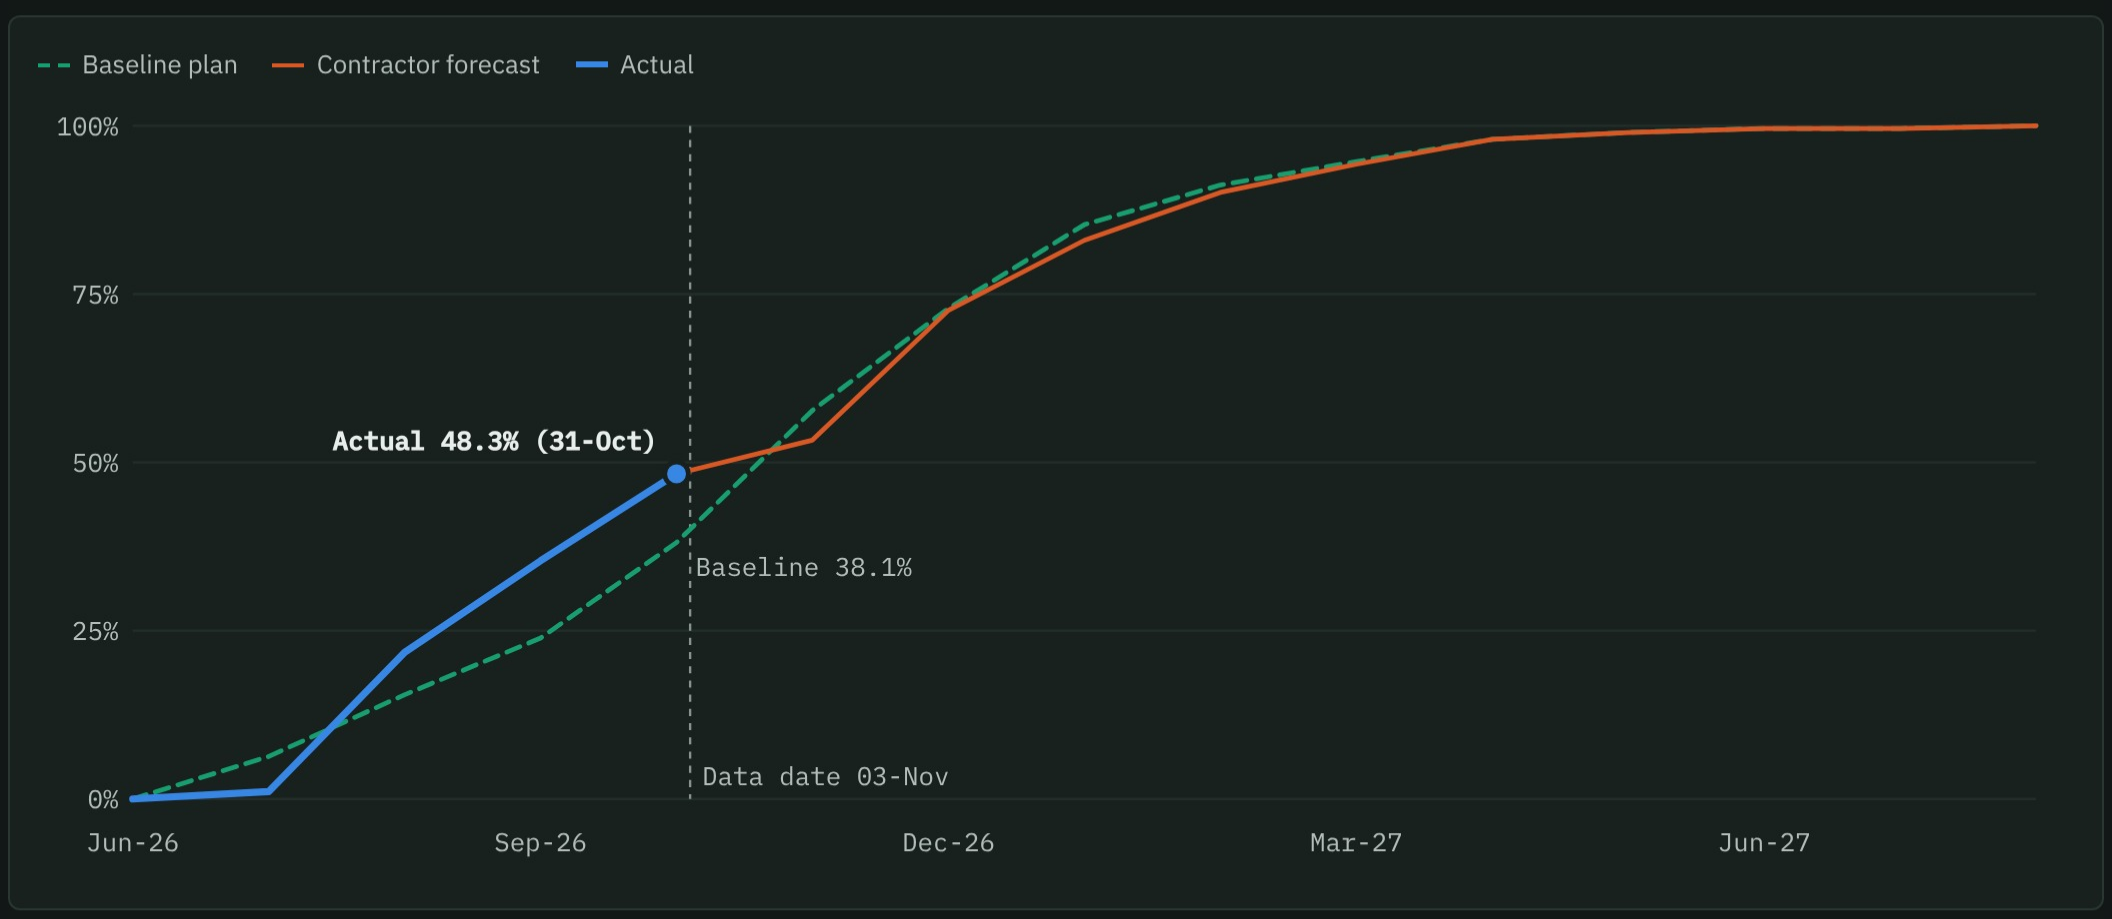

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	28.5	41.0	+12.4%	–	1.44
20-Oct-2026	32.6	45.2	+12.6%	+4.3	1.39
27-Oct-2026	35.7	48.3	+12.6%	+3.0	1.35
03-Nov-2026	**39.2**	**53.3**	**+14.1%**	**+5.0**	**1.36**

Rows from weekly reports No. 17 to No. 19. The 13-Oct-2026 row is the "CM Last Week" figure stated in report No. 17; earlier weeks were not uploaded.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (218,590 in total).
Source: Weekly Progress Report sheet and P6 update.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3.6%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	2.7%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	2.2%	90.3%	59.8%	−30.4%	0.66	▼ Behind
Road works	54.3%	38.0%	53.0%	+15.0%	1.39	▲ Ahead
Storm water drainage	35.6%	28.9%	46.7%	+17.8%	1.62	▲ Ahead
Testing & commissioning	1.1%	0.0%	25.0%	+25.0%	–	▲ Started early
Handover & close-out	0.4%	0.0%	0.0%	0.0%	–	Not due yet
Total	100%	**39.2%**	**53.3%**	**+14.1%**	**1.36**	▲ Ahead

The P6 update (UP 16, data date 03-Nov-2026) has 381 activities: 160 completed, 56 in progress and 165 not started. Its scheduled finish is 28-Oct-2027 with −55 days of total float. Critical-path activities went from 166 to 163 this week; the schedule sheet counts 33 failed starts.

Scope of work: quantities

Total scope and quantity finished for the items under way, from the Major Quantities sheet of the 03-Nov-2026 weekly report. "This week" is this week's cumulative quantity minus the 27-Oct-2026 report's.

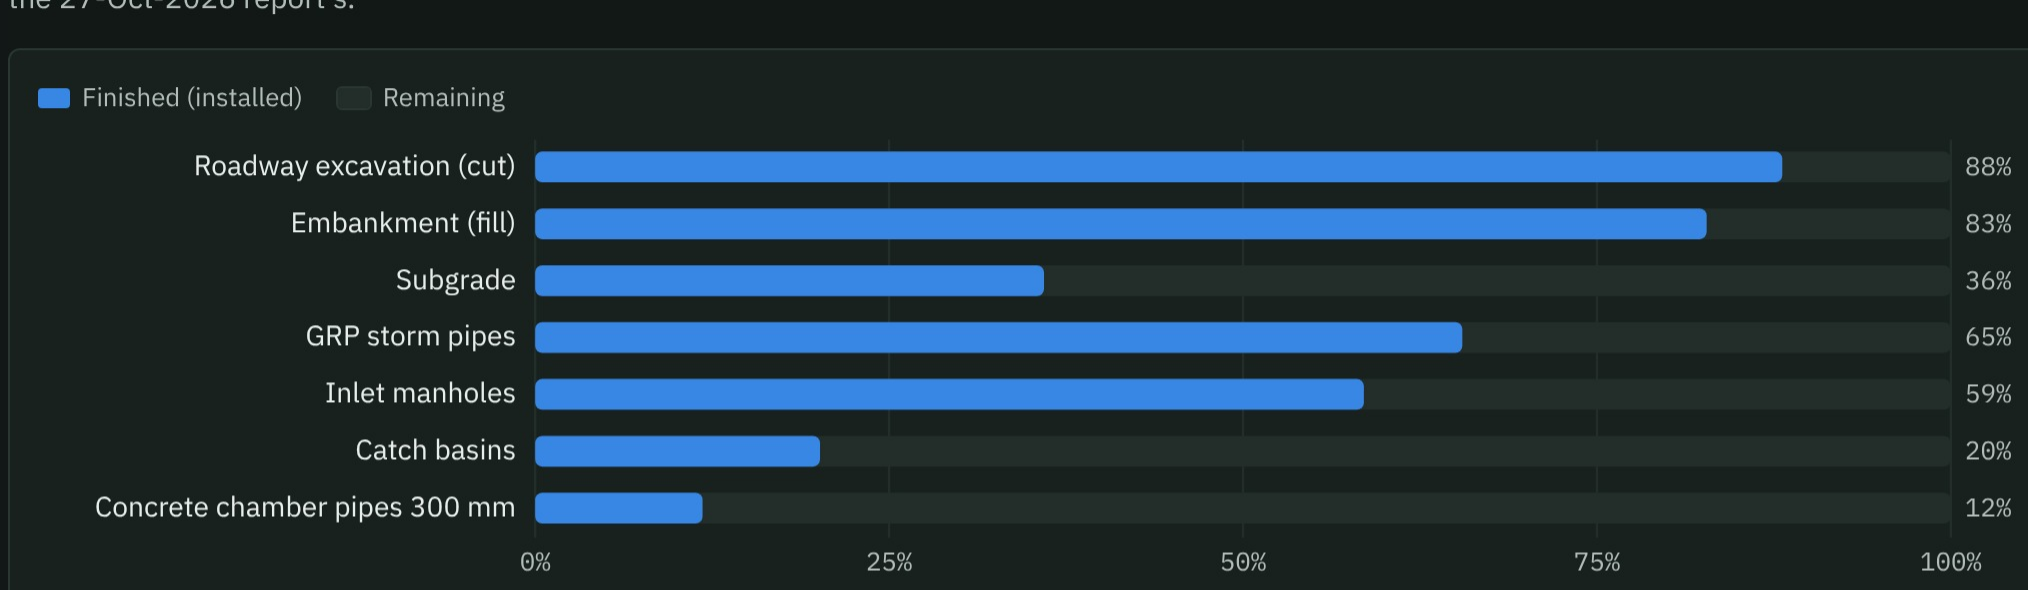

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Roadway excavation (cut)	All roads	m³	252,115	222,090	0	30,025	88.1%	–
Embankment (fill)	All roads	m³	221,841	183,569	0	38,272	82.7%	–
Subgrade	All roads	m³	39,250	14,108	+6,686	25,142	35.9%	–
GRP storm pipes	All roads	LM	5,855	3,834	+413.5	2,021	65.5%	–
Inlet manholes	All roads	EA	82	48	+10	34	58.5%	–
Catch basins	All roads	EA	164	33	+18	131	20.1%	–
Concrete chamber pipes 300 mm	All roads	LM	5,410	639.7	+464.7	4,770	11.8%	–

Subgrade and storm drainage moved this week

Subgrade nearly doubled to 14,108 m³ (36% of 39,250 m³), mostly on Local Road 11, against 3,580 m³ planned to date. Cut (222,090 m³) and fill (183,569 m³) are again unchanged, and remain well ahead of the 170,228 m³ and 149,787 m³ planned.

Not yet started

Aggregate base course, bituminous base and wearing courses, interlock paving, pavement markings and traffic signs are all at 0%. Kerbs are also at 0% in the quantities, although a tracking-sheet photo shows kerb installation on Local Road 30. The weekly works list adds 230 m of UPVC pipes, which are not in Major Quantities.

Milestones

The weekly report and the P6 update (UP 16) give the same forecast dates. The weekly report shows the slip in calendar days; the P6 column shows total float.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project commencement	25-Jun-2026	25-Jun-2026	25-Jun-2026 (actual)	–	✓ Done
Baseline programme submission	12-Jul-2026	12-Jul-2026	12-Jul-2026 (actual)	–	✓ Done
Completion of mobilisation	23-Jul-2026	15-Aug-2026 (+23 d)	15-Aug-2026 (actual)	–	✓ Done late
Approval of drawings and materials	23-Aug-2026	19-Sep-2026 (+27 d)	19-Sep-2026 (actual)	–	✓ Done late
Storm water drainage complete	24-Feb-2027	24-Apr-2027 (+59 d)	24-Apr-2027	−32	▼ Late
Road works complete	24-Apr-2027	29-Jun-2027 (+66 d)	29-Jun-2027	−38	▼ Late
Project completion	24-Aug-2027	28-Oct-2027 (+65 d)	28-Oct-2027	−55	▼ Late

All three construction milestones slipped another 7 days this week.

Storm drainage moved from 17-Apr to 24-Apr-2027, road works from 22-Jun to 29-Jun-2027 and project completion from 21-Oct to 28-Oct-2027, the third weekly slip of 7 days in a row. Negative float covers every road: Local Road 28 at −55 days, Local Road 30 at −47, Local Road 17 at −46, Local Road 11 at −44 and Local Road 29 at −41; procurement is at −7 days.

Procurement of key materials

Procurement completion rate per material. Source: Procurement Log, weekly report 03-Nov-2026 (unchanged from last week).



Pavement materials: still no purchase orders


Aggregate base course, bituminous base, precast kerbs, interlock pavers and pavement markings have no purchase order, although the required order dates (29-Aug to 17-Sep-2026) have passed. The failed-start list moved the aggregate base order from 27-Oct to 03-Nov-2026 and the bituminous base order from 02-Nov to 09-Nov-2026. Aggregate base is needed on site by 15-Nov-2026.

Storm drainage materials

GRP pipes (5,855 m), inlet manholes (82) and traffic signs (171) are fully procured. Catch basins are still at 110 of 164 (67%); the third delivery moved from 05-Nov to 12-Nov-2026.

Manpower

Monthly average head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet; November is the month to date.

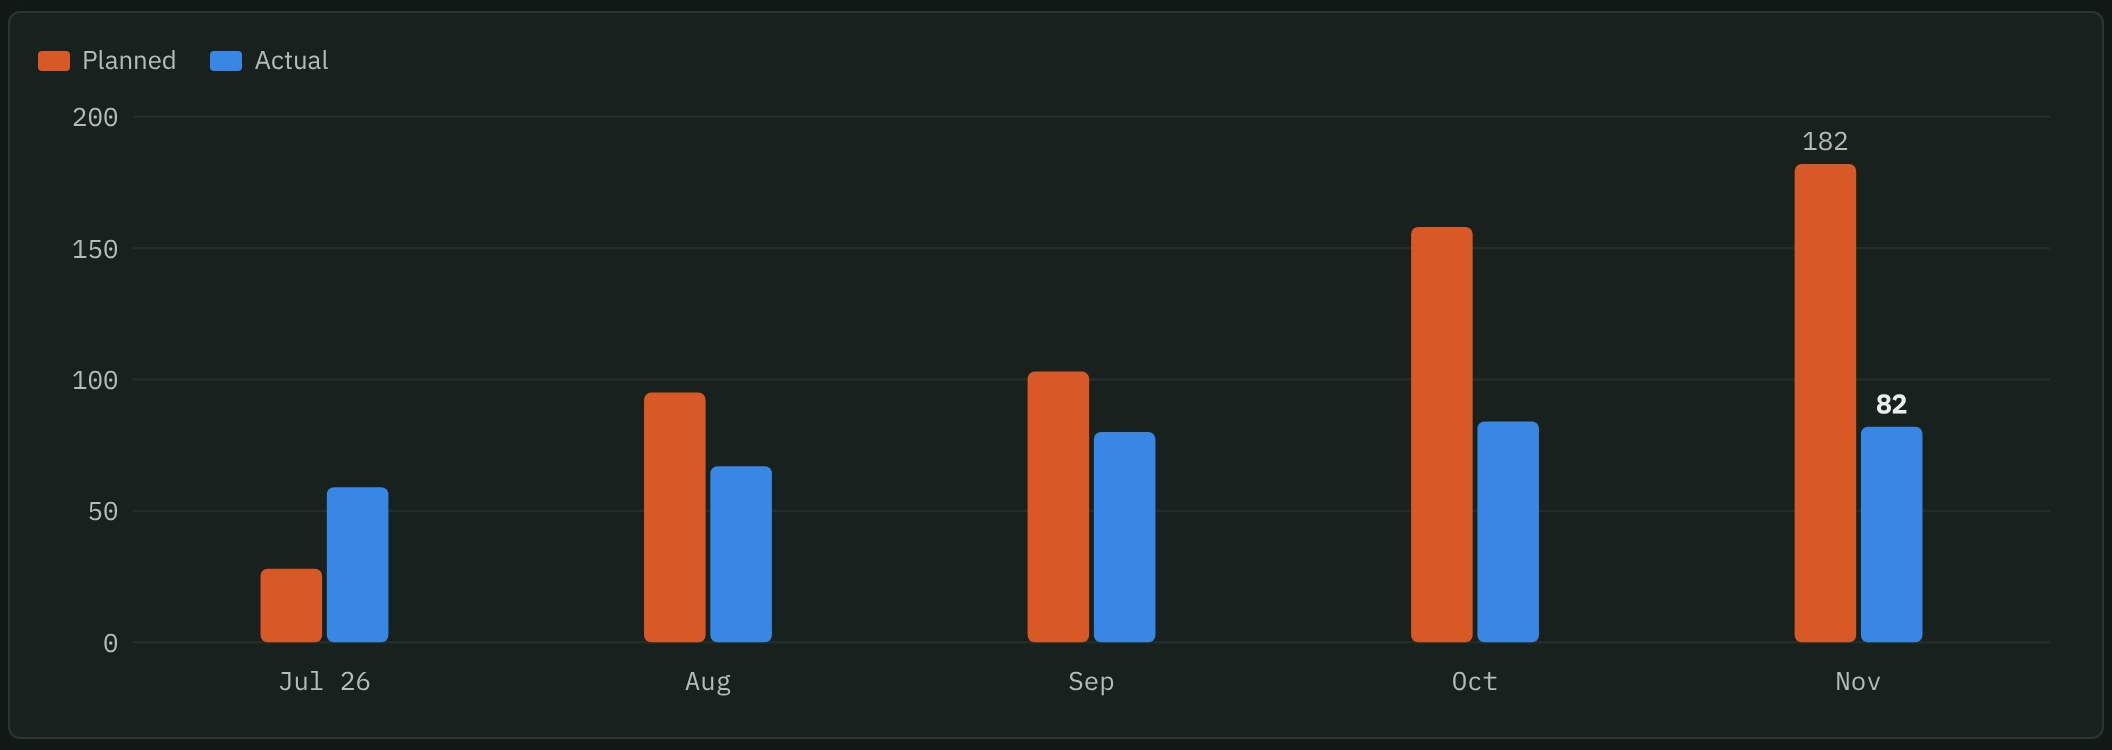

November head count so far is 82 against 182 planned (−55%): 67 manual workers against 169 planned, and 15 staff against 13. Equipment on site is 61 against 91 planned. October closed at 84 against 158.

Cost and invoicing

Contract value

Road works	19,411,954
Storm water drainage	13,628,050
BOQ total (excl. VAT)	**33,040,004**
Contract value incl. 15% VAT	37,996,005
Change orders	0

All values in SAR. Road works are 58.8% of the BOQ and storm water drainage 41.2%. No change orders are registered.

Invoices

Invoices submitted	3
Gross value	6,754,935
Deductions and penalties	2,000
Net incl. VAT	7,770,175
Paid (3 invoices)	7,770,175
FIR value to date	10,495,811

Invoicing is 20.4% of the contract value against 53.3% physical progress. All three invoices are paid. No invoice has been submitted for work after 27-Sep-2026. There is no advance payment or retention.

Health, safety and quality

Safety Score 0.89

Safe man-hours (cumulative)	42,941
Man-hours this week	2,976
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	1
Property damage	0
Inductions / toolbox talks	4 / 20

Quality Score 0.90

FIRs issued (cumulative)	296
FIRs closed / pending	254 / 42
MIRs issued / closed	42 / 42
NCRs issued	0
Site instructions (closed)	1
Shop drawings approved	22 / 23
Material submittals approved	40 / 42

Consultant quality and safety inspections of 03-Nov-2026. 44 FIRs were issued this week.

Open issues and risks

RISK	OWNER	DETAIL
Falls into excavations	Contractor	Unstable soil and missing barricades. Barricades, warning signs and a supervisor at excavations. Rated high (H20, H16 after treatment).
Traffic management	Contractor	Vehicle accidents from inadequate traffic diversion. Diversion signs, barriers and traffic marshals. Rated high (H16).
Operator competence	Contractor	Accidents from insufficient training and supervision of operators. Training, competency checks and supervision. Rated high (H16).
Oil spills	Contractor	Soil contamination from equipment leaks or poor handling of oil. Spill response plan, maintenance and containment. Rated medium (M9).

The risk register is unchanged from last week. The issue log and the top-issues panel of the weekly report are empty, and the tracking sheet's challenges box is blank.

Data notes

- The summary files (works executed and progress files, Tracking Sheet) label a cost-based figure as "actual" progress. This report uses physical (man-hour) progress only.
- The Weekly Progress Report sheet gives 53.59% earned because it counts the 600 testing and commissioning man-hours twice. The P6 update and the Physical-Chart Data sheet give 116,534 man-hours, 53.31%, which this report uses.
- The weekly physical progress panel shows 7.16% planned and 10.36% earned this week, adding rows twice; the correct figures are 3.58% and 5.04%.
- The Progress sheet now uses a budget of 218,290 man-hours (39.3% and 53.4%), while the main sheet and P6 use 218,590.
- Testing and commissioning shows 600 man-hours earned (25%) and the storm water test 50% complete, although tests were planned to start on 25-Feb-2027.
- The progress file and the works-executed file again show this week's progress with opposite signs. The works-executed file is dated 03-10-2026 in its name and still gives a contract of 24-Nov-2025 to 23-May-2026.
- The MODON PM is written as الجليفي in the progress file and as الشنيفي in the works-executed file.
- Week number: the report states contract week 19 of 61 (Milestones sheet). Whole weeks from site handover to the data date give 18.
- Cut and fill to date are unchanged in Major Quantities for the second week, while the works list again reports 4,260 m³ of cut on Local Road 17.
- The works list and Major Quantities differ for this week's work: GRP pipes 644 m against 414 m, catch basins 13 against 18. The 230 m of UPVC pipes in the works list are not in Major Quantities.
- A tracking-sheet photo shows kerb installation on Local Road 30, while kerbs are at 0 in Major Quantities and have no purchase order.
- The schedule sheet counts 31 failed starts last week and 33 this week, while last week's report counted 35. The Failed Start List still carries the title and date of project MKH2-02-003.
- The Progress Summary gives 2,763 m of storm drainage pipe against 3,834 m of GRP pipe in Major Quantities, and still lists 156 catch basins against 164.
- The forecast in the Physical-Chart Data sheet reaches 100% on 31-Aug-2027, but P6 finishes on 28-Oct-2027.
- The baseline schedule approval is dated 13-Jul-2025, before the contract award of 11-May-2026.
- Major Quantities lists several items twice with different totals and includes electrical items that are not in this project's scope.
- The manpower summary panel shows 28 planned and 94 actual, while the Manpower sheet gives 182 planned and 82 actual for November.
- The invoice summary shows 0 submitted invoices, while the invoice log lists 3. Potential changes are 0 in the summary and 200,000 SAR in the invoice log.

- The risk register marks the four project risks as Closed while their treatment status is Open; it also holds rows for project MKH2-02-003.
- Several summary panels in the weekly report workbook show #REF! errors.
- The site photos come from the Tracking Sheet presentation (1,200 to 1,296 px wide). The four photos embedded in the workbook are under 600 px wide and were not used.

Compiled 04-Nov-2026 from weekly report No. 19 (data date 03-Nov-2026), with report No. 18 for the previous week.
