
Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
26-10-2026		440d	20-May-26 A	13-Nov-27	104d	31,773,489	22,027,910	84,452,014
JDH3-02-009-Al-Khorayef Factory Road		69d	27-Oct-26	14-Jan-27	354d	54,099	0	455,535
Construction		69d	27-Oct-26	14-Jan-27	354d	54,099	0	455,535
JDH3-02-009-KF-Sewage Network- SW		29d	13-Dec-26	14-Jan-27	284d	0	0	35,363
JDH3-02-009-R151-(SW)-GRP Pipes-150 mm diameter depth from 0 to		11d	13-Dec-26	24-Dec-26	177d	0	0	452
JDH	Backfilling and warning tape Works for GRP Pipe Line 150 mm	11d	13-Dec-26	24-Dec-26	177d	0	0	452
JDH3-02-009-R151-(SW)-GRP Pipes-150 mm diameter depth from 1.5		18d	26-Dec-26	14-Jan-27	177d	0	0	27,405
JDH	Excavation Works for GRP Pipe Line 200 mm - depth from 0 to	6d	26-Dec-26	31-Dec-26	177d	0	0	6,851
JDH	Bedding Works for GRP Pipe Line 200 mm - depth from 0 to 1.5	6d	02-Jan-27	07-Jan-27	177d	0	0	1,713
JDH	Installing for GRP Pipe Line 200 mm - depth from 0 to 1.5 m- (E	6d	09-Jan-27	14-Jan-27	177d	0	0	18,841
JDH3-02-009-R151-(SW)-MH Works depth from 0 to 1.50 Diam 1200 m		9d	26-Dec-26	04-Jan-27	293d	0	0	7,506
JDH	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	9d	26-Dec-26	04-Jan-27	293d	0	0	7,506
JDH3-02-009-KF-Storm Network - ST		18d	27-Oct-26	16-Nov-26	405d	54,099	0	54,099
JDH3-02-009-KF-(ST)-MH Works (1200) mm diameter depth from 1.50		4d	08-Nov-26	11-Nov-26	177d	1,052	0	1,052
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	08-Nov-26	09-Nov-26	177d	701	0	701
JDH	Steel Coverfor MH 1200 mm - depth from 1.50 to 2.0 m- (B6.33	2d	10-Nov-26	11-Nov-26	177d	351	0	351
JDH3-02-009-KF-(ST)-MH Works (1200) mm diameter depth from 2.01		4d	10-Nov-26	14-Nov-26	177d	3,217	0	3,217
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	10-Nov-26	11-Nov-26	177d	2,144	0	2,144
JDH	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.5 m- (B6.33	2d	12-Nov-26	14-Nov-26	177d	1,072	0	1,072
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 2.01		4d	27-Oct-26	31-Oct-26	411d	4,513	0	4,513
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	177d	3,009	0	3,009
JDH	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	411d	1,504	0	1,504
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 2.51		4d	29-Oct-26	02-Nov-26	411d	13,509	0	13,509
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	29-Oct-26	31-Oct-26	177d	9,006	0	9,006
JDH	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2d	01-Nov-26	02-Nov-26	411d	4,503	0	4,503
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 3.01		4d	12-Nov-26	16-Nov-26	177d	1,819	0	1,819
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	12-Nov-26	14-Nov-26	177d	1,213	0	1,213
JDH	Steel Coverfor MH 1500 mm - depth from 3.01 to 3.5 m- (B6.33	2d	15-Nov-26	16-Nov-26	177d	606	0	606
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 2.01		2d	15-Nov-26	16-Nov-26	177d	1,367	0	1,367
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	15-Nov-26	16-Nov-26	177d	1,367	0	1,367
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 2.51		4d	01-Nov-26	04-Nov-26	411d	15,605	0	15,605
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	01-Nov-26	02-Nov-26	177d	10,403	0	10,403
JDH	Steel Coverfor MH 2000 mm - depth from 2.51 to 3.00 m- (B6.3	2d	03-Nov-26	04-Nov-26	411d	5,202	0	5,202
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 3.01		4d	05-Nov-26	09-Nov-26	411d	2,400	0	2,400
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	05-Nov-26	07-Nov-26	177d	1,600	0	1,600
JDH	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2d	08-Nov-26	09-Nov-26	411d	800	0	800
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 4.01		4d	03-Nov-26	07-Nov-26	411d	10,617	0	10,617
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	03-Nov-26	04-Nov-26	177d	7,078	0	7,078
JDH	Steel Coverfor MH 2000 mm - depth from 4.01 to 4.50 m- (B6.3	2d	05-Nov-26	07-Nov-26	411d	3,539	0	3,539
JDH3-02-009-KF-Potable Water Network - WT		23d	28-Nov-26	23-Dec-26	371d	0	0	229,174
JDH3-02-009-R16-(WT)-HDPE Pipes-160 mm diameter depth from 0 to		22d	29-Nov-26	23-Dec-26	371d	0	0	119,823
JDH	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m- (	10d	29-Nov-26	09-Dec-26	371d	0	0	87,870
JDH	Primary Test for HDPE Pipe Line 160 mm - depth from 0 to 1.5	6d	10-Dec-26	16-Dec-26	371d	0	0	15,976
JDH	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	6d	17-Dec-26	23-Dec-26	371d	0	0	15,976
JDH3-02-009-R16-(WT)-Gate Valve-150 mm on pipe dia (160) mm		4d	10-Dec-26	14-Dec-26	371d	0	0	17,265
JDH	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B3.33	2d	10-Dec-26	12-Dec-26	371d	0	0	15,539
JDH	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 mi	2d	13-Dec-26	14-Dec-26	371d	0	0	1,727
JDH3-02-009-R08-(WT)-Wash-Out Valve-100 mm on pipe dia (160) mm		2d	15-Dec-26	16-Dec-26	371d	0	0	752
JDH	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	15-Dec-26	16-Dec-26	371d	0	0	752
JDH3-02-009-R08-(WT)-Wash-Out Valve-100 mm on pipe dia (225) mm		19d	28-Nov-26	19-Dec-26	371d	0	0	7,673
JDH	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2d	28-Nov-26	29-Nov-26	384d	0	0	6,906
JDH	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	17-Dec-26	19-Dec-26	371d	0	0	767

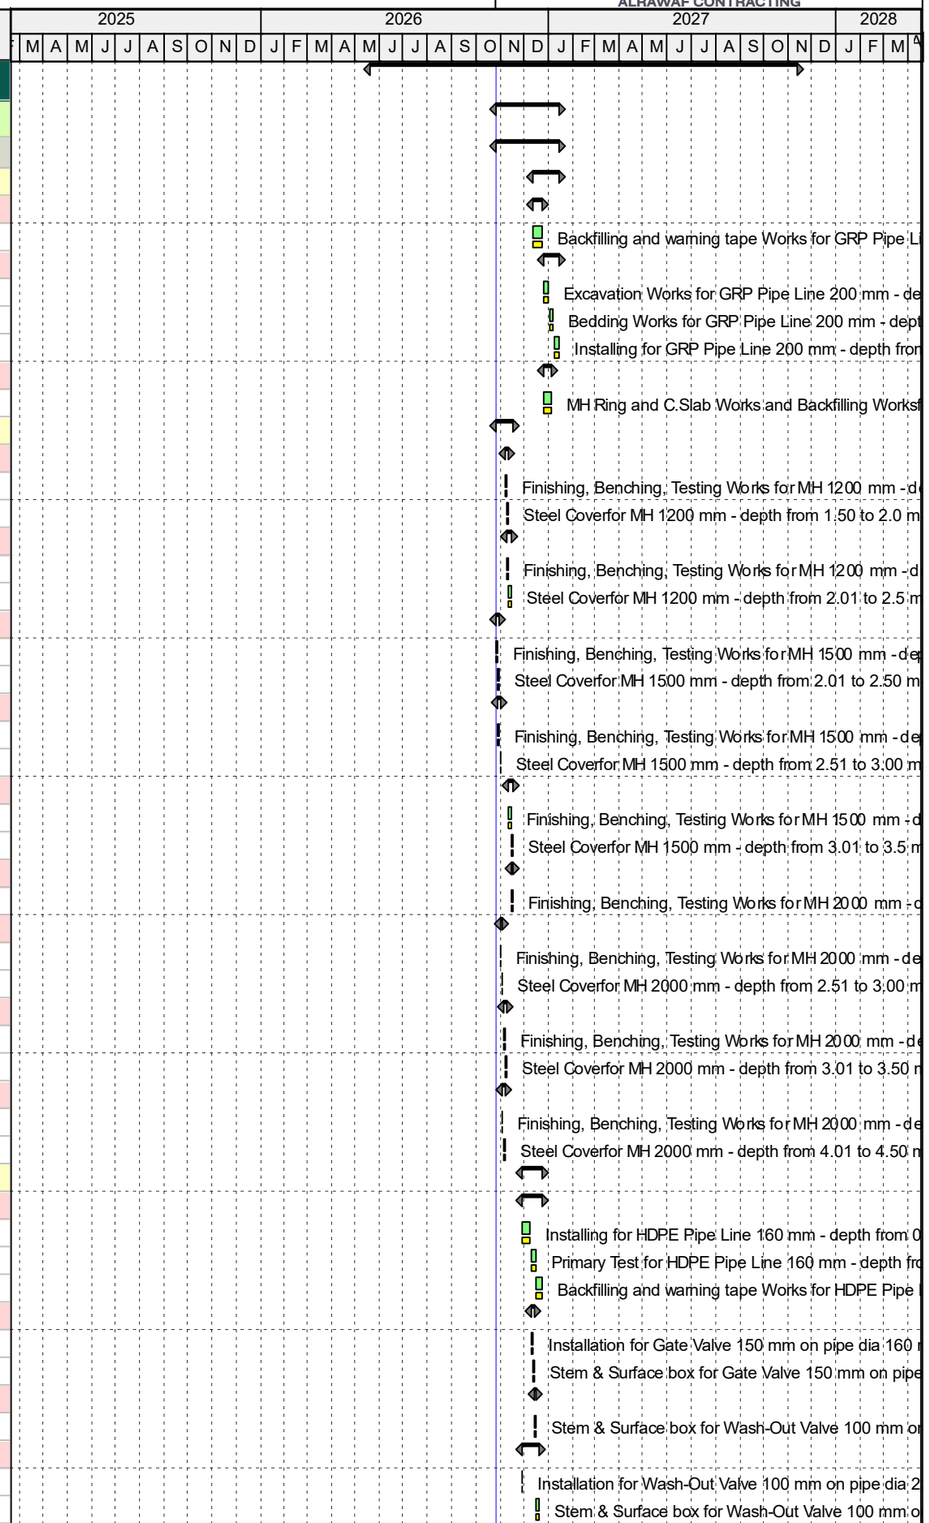


Actual Level of Effort · Remaining Work
Primary Baseline · Critical Remaining Work
Actual Work · Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R08-(WT)-Wash-Out Chamber on 160 mm dia pipeline d	2d	28-Nov-26	29-Nov-26	388d	0	0	11,475
JDI	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	28-Nov-26	29-Nov-26	388d	0	0	11,475
	JDH3-02-009-R08-(WT)-Wash-Out Chamber on 225 mm dia pipeline d	4d	28-Nov-26	01-Dec-26	388d	0	0	13,561
JDI	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2d	28-Nov-26	29-Nov-26	388d	0	0	2,086
JDI	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	30-Nov-26	01-Dec-26	388d	0	0	11,475
	JDH3-02-009-R08-(WT)-Fire Hydrant	6d	13-Dec-26	19-Dec-26	373d	0	0	58,625
JDI	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	13-Dec-26	14-Dec-26	373d	0	0	9,771
JDI	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-WT	2d	15-Dec-26	16-Dec-26	373d	0	0	19,542
JDI	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-WT	2d	17-Dec-26	19-Dec-26	373d	0	0	29,312
	JDH3-02-009-KF-TSE Network - TSE	13d	26-Nov-26	10-Dec-26	366d	0	0	136,898
	JDH3-02-009-R151-(TSE)-HDPE Pipes-160 mm diameter depth from 1.	13d	26-Nov-26	10-Dec-26	366d	0	0	133,862
JDI	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51 t	3d	26-Nov-26	29-Nov-26	366d	0	0	11,155
JDI	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5	10d	30-Nov-26	10-Dec-26	366d	0	0	122,707
	JDH3-02-009-R152-(TSE)-HDPE Pipes-110 mm diameter depth from 0	8d	26-Nov-26	05-Dec-26	357d	0	0	3,037
JDI	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	4d	26-Nov-26	30-Nov-26	357d	0	0	2,429
JDI	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4d	01-Dec-26	05-Dec-26	357d	0	0	607
JDH3-02-009-New Roads - NR		144d	03-Sep-26 A	18-Feb-27	324d	983,156	75,694	1,619,519
A-MCG		99d	27-Oct-26	18-Feb-27	316d	24,793	0	457,884
	JDH3-02-009-AMCG-Storm Network- ST	12d	27-Oct-26	09-Nov-26	367d	24,793	0	32,515
	JDH3-02-009-AMCG-(ST)-MH Works (1500) mm diameter depth from 2	4d	27-Oct-26	31-Oct-26	367d	1,560	0	1,560
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	367d	1,003	0	1,003
JDI	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	367d	557	0	557
	JDH3-02-009-AMCG-(ST)-MH Works (1200) mm diameter depth from 2	4d	29-Oct-26	02-Nov-26	367d	1,112	0	1,112
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	29-Oct-26	31-Oct-26	367d	715	0	715
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	367d	397	0	397
	JDH3-02-009-AMCG-(ST)-MH Works (1500) mm diameter depth from 2	4d	01-Nov-26	04-Nov-26	367d	1,751	0	1,751
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	01-Nov-26	02-Nov-26	367d	1,126	0	1,126
JDI	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2d	03-Nov-26	04-Nov-26	367d	625	0	625
	JDH3-02-009-AMCG-(ST)-MH Works (2000) mm diameter depth from 3	4d	03-Nov-26	07-Nov-26	367d	2,489	0	2,489
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	03-Nov-26	04-Nov-26	367d	1,600	0	1,600
JDI	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2d	05-Nov-26	07-Nov-26	367d	889	0	889
	JDH3-02-009-AMCG-(ST)-MH Works (2000) mm diameter depth from 3	4d	05-Nov-26	09-Nov-26	367d	17,881	0	25,603
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	05-Nov-26	07-Nov-26	367d	17,068	0	17,068
JDI	Steel Coverfor MH 2000 mm - depth from 3.51 to 4.0- (B6.33 0	2d	08-Nov-26	09-Nov-26	367d	813	0	8,534
	JDH3-02-009-AMCG-Road Works - RD	16d	01-Feb-27	18-Feb-27	316d	0	0	425,370
JDH3(	Supply and installation Traffic signs 1 Sheet with Single post - (E	7d	11-Feb-27	18-Feb-27	316d	0	0	6,540
	JDH3-02-009-AMCG-(RD)-Bituminous concrete wearing course 50 mn	6d	04-Feb-27	10-Feb-27	316d	0	0	415,000
JDI	Supply, lay and compaction Asphaltic wearing course 50 mm in	6d	04-Feb-27	10-Feb-27	316d	0	0	415,000
	JDH3-02-009-AMCG-(RD)-Precast Concrete Curb	3d	01-Feb-27	03-Feb-27	293d	0	0	3,830
JDI	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3d	01-Feb-27	03-Feb-27	293d	0	0	3,830
A-MCH		89d	27-Oct-26	07-Feb-27	334d	3,742	0	14,342
	JDH3-02-009-AMCH-Earthworks - EW	2d	27-Oct-26	28-Oct-26	378d	38	0	38
JDH3(	Backfill Layers with Imported Material Side Walk for Road - (B1.3	2d	27-Oct-26	28-Oct-26	378d	38	0	38
	JDH3-02-009-AMCH-Storm Network - ST	6d	27-Oct-26	02-Nov-26	417d	3,704	0	3,704
	JDH3-02-009-AMCH-(ST)-MH Works (1500) mm diameter depth from 2	4d	27-Oct-26	31-Oct-26	417d	1,560	0	1,560
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	417d	1,003	0	1,003
JDI	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	417d	557	0	557
	JDH3-02-009-AMCH-(ST)-MH Works (1200) mm diameter depth from 2	4d	29-Oct-26	02-Nov-26	417d	2,144	0	2,144
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	29-Oct-26	31-Oct-26	417d	1,430	0	1,430
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	417d	715	0	715
	JDH3-02-009-AMCH-Road Works - RD	2d	16-Jan-27	17-Jan-27	334d	0	0	286
	JDH3-02-009-AMCH-(RD)-Pavement Marking	2d	16-Jan-27	17-Jan-27	334d	0	0	286

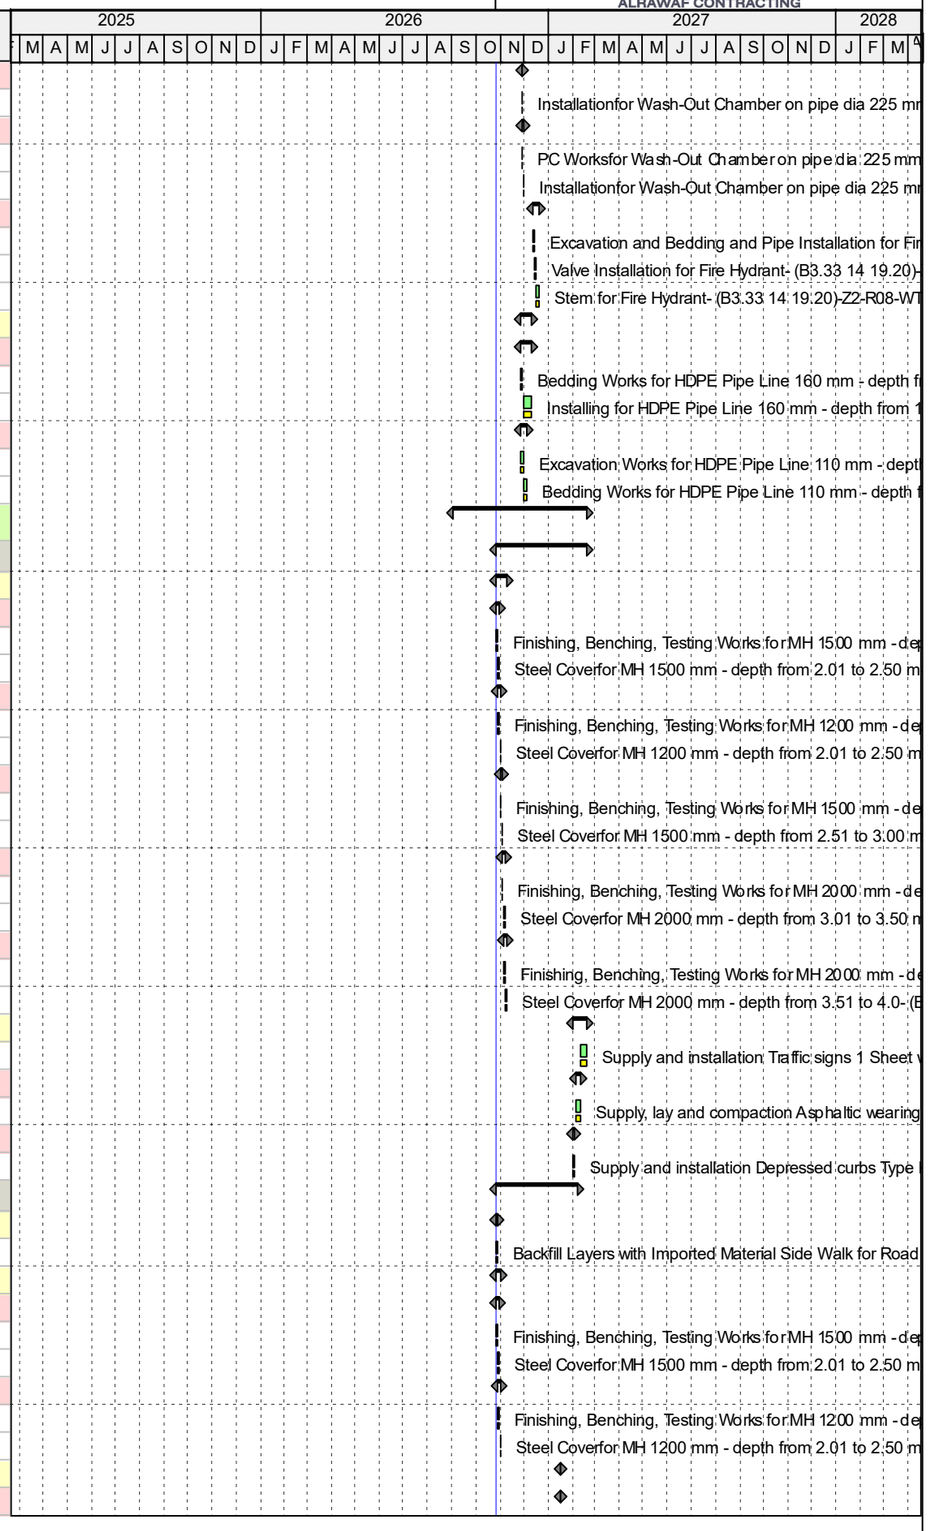

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.(	2d	16-Jan-27	17-Jan-27	334d	0	0	286
JDH3-02-009-AMCH-Landscape Works - LS		18d	18-Jan-27	07-Feb-27	334d	0	0	10,314
JDH3-02-009-AMCH-(LS)-Miscellaneous Landscaping Items		18d	18-Jan-27	07-Feb-27	334d	0	0	10,314
JDH	Concrete heel kerb - PV6- (B7.32 93 34.07)-Z3-R20-LS	18d	18-Jan-27	07-Feb-27	334d	0	0	10,314
A-MCA		134d	03-Sep-26 A	07-Feb-27	334d	748,133	75,694	938,231
JDH3-02-009-AMCA-Sewage Network - SW		65d	03-Sep-26 A	18-Nov-26	403d	234,292	75,694	236,115
JDH3-02-009-AMCA-(SW)-GRP Pipes-150 mm diameter depth from 1.!		20d	27-Oct-26	18-Nov-26	379d	25,222	0	25,222
JDH	Excavation Works for GRP Pipe Line 150 mm - depth from 1.51	2d	27-Oct-26	28-Oct-26	371d	5,044	0	5,044
JDH	Bedding Works for GRP Pipe Line 150 mm - depth from 1.51 to	3d	29-Oct-26	01-Nov-26	371d	1,261	0	1,261
JDH	Installing for GRP Pipe Line 150 mm - depth from 1.51 to 2.5 m	3d	02-Nov-26	04-Nov-26	371d	13,872	0	13,872
JDH	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	6d	05-Nov-26	11-Nov-26	371d	2,522	0	2,522
JDH	Backfilling and warning tape Works for GRP Pipe Line 150 mm	6d	12-Nov-26	18-Nov-26	379d	2,522	0	2,522
JDH3-02-009-AMCA-(SW)-GRP Pipes-150 mm diameter depth from 2.!		5d	12-Nov-26	17-Nov-26	371d	5,308	0	5,308
JDH	Excavation Works for GRP Pipe Line 150 mm - depth from 2.51	2d	12-Nov-26	14-Nov-26	371d	4,246	0	4,246
JDH	Bedding Works for GRP Pipe Line 150 mm - depth from 2.51 to	3d	15-Nov-26	17-Nov-26	371d	1,062	0	1,062
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 1.!		6d	27-Oct-26	02-Nov-26	399d	8,738	0	8,738
JDH	Primary Test for GRP Pipe Line 200 mm - depth from 1.51 to 2.	6d	27-Oct-26	02-Nov-26	399d	8,738	0	8,738
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 2.!		6d	27-Oct-26	02-Nov-26	399d	11,329	0	11,329
JDH	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	6d	27-Oct-26	02-Nov-26	399d	11,329	0	11,329
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 3.!		6d	27-Oct-26	02-Nov-26	399d	8,831	0	8,831
JDH	Primary Test for GRP Pipe Line 200 mm - depth from 3.51 to 4.	6d	27-Oct-26	02-Nov-26	399d	8,831	0	8,831
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 4.!		6d	27-Oct-26	02-Nov-26	399d	1,823	0	3,647
JDH	Primary Test for GRP Pipe Line 200 mm - depth from 4.51 to 5.	6d	27-Oct-26	02-Nov-26	399d	1,823	0	3,647
JDH3-02-009-AMCA-(SW)-MH Works depth from 1.51 to 2.5 Diam 120		46d	08-Sep-26 A	01-Nov-26	412d	113,723	48,332	113,723
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	28-Oct-26	29-Oct-26	412d	11,372	0	11,372
JDH	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	2d	31-Oct-26	01-Nov-26	412d	5,686	0	5,686
JDH	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	2d	16-Sep-26 A	27-Oct-26	412d	39,803	19,902	39,803
JDH	Excavation and PC Blinding Works for MH 1200 mm - depth fro	2d	08-Sep-26 A	27-Oct-26	412d	28,431	14,215	28,431
JDH	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	2d	10-Sep-26 A	27-Oct-26	412d	28,431	14,215	28,431
JDH3-02-009-AMCA-(SW)-MH Works depth from 2.51 to 3.5 Diam 120		52d	03-Sep-26 A	03-Nov-26	412d	48,773	27,362	48,773
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	31-Oct-26	01-Nov-26	412d	4,877	0	4,877
JDH	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3	2d	02-Nov-26	03-Nov-26	412d	2,439	0	2,439
JDH	Excavation and PC Blinding Works for MH 1200 mm - depth fro	2d	03-Sep-26 A	27-Oct-26	414d	12,193	8,048	12,193
JDH	Installation of Basefor MH 1200 mm - depth from 2.51 to 3.5 m	2d	06-Sep-26 A	27-Oct-26	414d	12,193	8,048	12,193
JDH	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	2d	16-Sep-26 A	27-Oct-26	414d	17,071	11,267	17,071
JDH3-02-009-AMCA-(SW)-MH Works depth from 3.51 to 4.5 Diam 120		4d	02-Nov-26	05-Nov-26	412d	5,027	0	5,027
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	02-Nov-26	03-Nov-26	412d	3,351	0	3,351
JDH	Steel Coverfor MH 1200 mm - depth from 3.51 to 4.5 m- (B5.33	2d	04-Nov-26	05-Nov-26	412d	1,676	0	1,676
JDH3-02-009-AMCA-(SW)-MH Works depth from 4.51 to 5.5 Diam 120		4d	04-Nov-26	08-Nov-26	412d	5,518	0	5,518
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	04-Nov-26	05-Nov-26	412d	3,679	0	3,679
JDH	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	2d	07-Nov-26	08-Nov-26	412d	1,839	0	1,839
JDH3-02-009-AMCA-Storm Network- ST		12d	27-Oct-26	09-Nov-26	383d	59,914	0	59,914
JDH3-02-009-AMCA-(ST)-MH Works (1200) mm diameter depth from 3		4d	27-Oct-26	31-Oct-26	383d	1,358	0	1,358
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	383d	873	0	873
JDH	Steel Coverfor MH 1200 mm - depth from 3.01 to 3.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	383d	485	0	485
JDH3-02-009-AMCA-(ST)-MH Works (1500) mm diameter depth from 2		4d	29-Oct-26	02-Nov-26	383d	5,129	0	5,129
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	29-Oct-26	31-Oct-26	383d	3,377	0	3,377
JDH	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2d	01-Nov-26	02-Nov-26	383d	1,751	0	1,751
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 3		4d	01-Nov-26	04-Nov-26	383d	12,088	0	12,088
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	01-Nov-26	02-Nov-26	383d	8,000	0	8,000
JDH	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2d	03-Nov-26	04-Nov-26	383d	4,089	0	4,089
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 3		4d	03-Nov-26	07-Nov-26	383d	30,723	0	30,723
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	03-Nov-26	04-Nov-26	383d	20,482	0	20,482

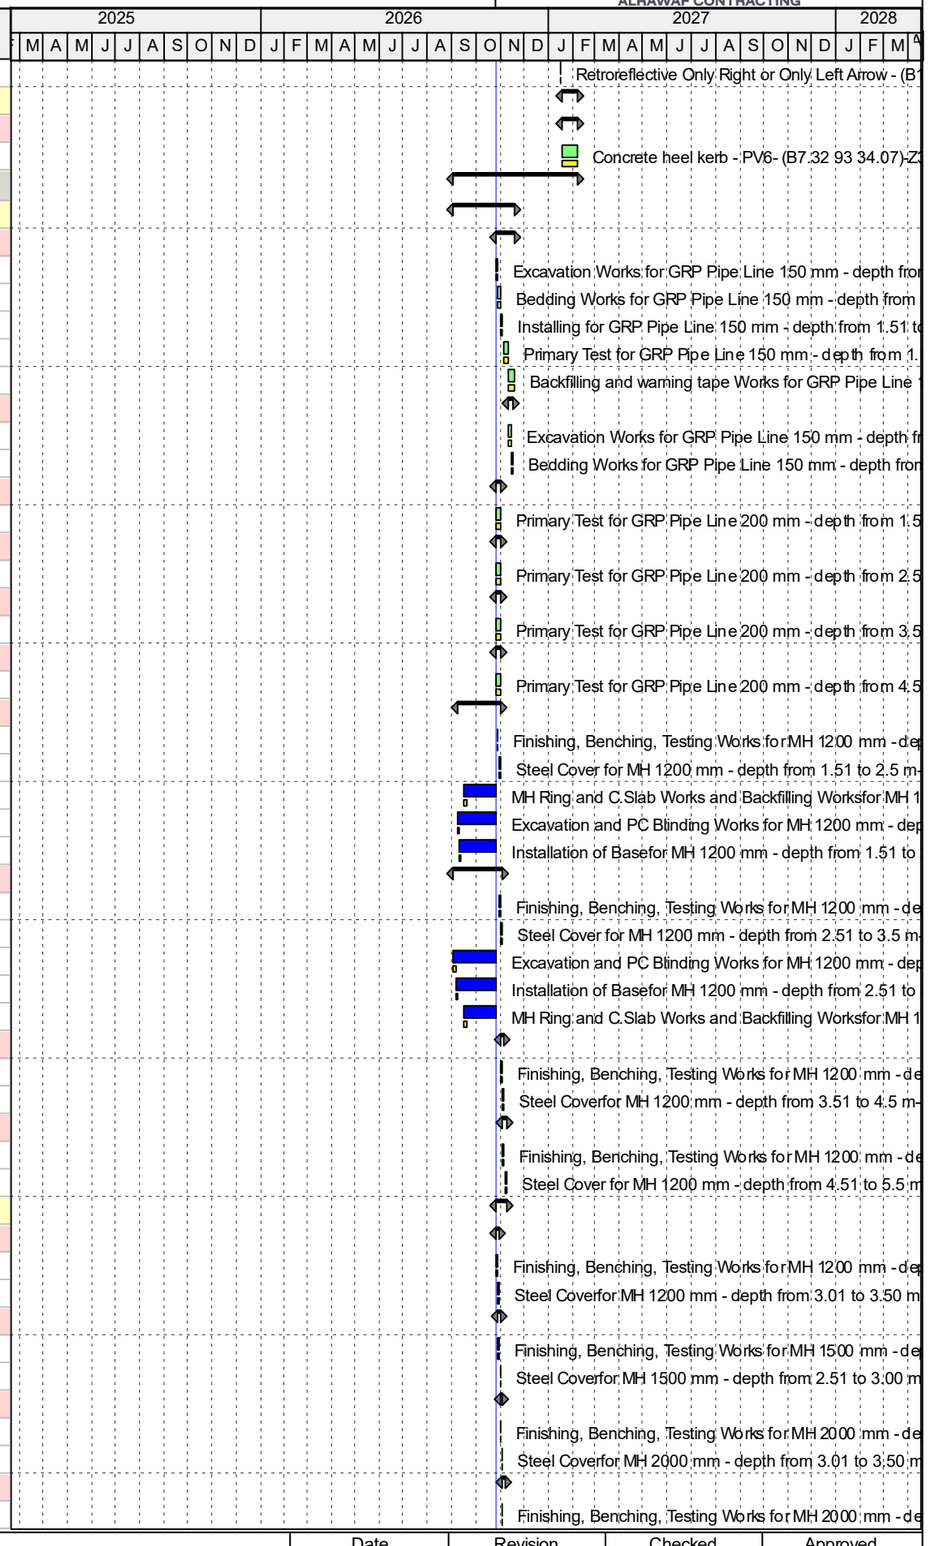


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Steel Coverfor MH 2000 mm - depth from 3.51 to 4.0- (B6.33 0	2d	05-Nov-26	07-Nov-26	383d	10,241	0	10,241
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 4		4d	05-Nov-26	09-Nov-26	383d	10,617	0	10,617
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	05-Nov-26	07-Nov-26	383d	7,078	0	7,078
JDH	Steel Coverfor MH 2000 mm - depth from 4.01 to 4.5- (B6.33 0	2d	08-Nov-26	09-Nov-26	383d	3,539	0	3,539
JDH3-02-009-AMCA-Road Works - RD		18d	18-Jan-27	07-Feb-27	303d	0	0	25,487
JDH3-02-009-AMCA-(RD)-Precast Concrete Curb		18d	18-Jan-27	07-Feb-27	303d	0	0	25,487
JDH	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	18d	18-Jan-27	07-Feb-27	303d	0	0	25,487
JDH3-02-009-AMCA-Landscape Works - LS		18d	16-Jan-27	04-Feb-27	336d	0	0	162,787
JDH3-02-009-AMCA-(LS)-Miscellaneous Landscaping Items		18d	16-Jan-27	04-Feb-27	336d	0	0	162,787
JDH	Concrete heel kerb - PV6- (B7.32 93 34.07)-Z3-R20-LS	18d	16-Jan-27	04-Feb-27	336d	0	0	162,787
JDH3-02-009-AMCA-Potable Water Network- WT		19d	27-Oct-26	17-Nov-26	404d	246,797	0	246,797
(WT)-HDPE Pipes-160 mm diameter depth from 0 to 1.5 m		12d	27-Oct-26	09-Nov-26	411d	5,004	0	5,004
JDH	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	2d	27-Oct-26	28-Oct-26	398d	1,001	0	1,001
JDH	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	2d	29-Oct-26	31-Oct-26	398d	250	0	250
JDH	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m- (	4d	01-Nov-26	04-Nov-26	398d	2,752	0	2,752
JDH	Primary Test for HDPE Pipe Line 160 mm - depth from 0 to 1.5	2d	05-Nov-26	07-Nov-26	398d	500	0	500
JDH	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	2d	08-Nov-26	09-Nov-26	411d	500	0	500
(WT)-HDPE Pipes-225 mm diameter depth from 0 to 1.5 m		8d	08-Nov-26	16-Nov-26	401d	189,595	0	189,595
JDH	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 t	2d	08-Nov-26	09-Nov-26	401d	47,399	0	47,399
JDH	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	2d	10-Nov-26	11-Nov-26	401d	11,850	0	11,850
JDH	Installing for HDPE Pipe Line 225 mm - depth from 0 to 1.5 m- (	4d	12-Nov-26	16-Nov-26	401d	130,347	0	130,347
(WT)-Gate Valve-150 mm on pipe dia (160) mm		4d	08-Nov-26	11-Nov-26	398d	3,453	0	3,453
JDH	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B3.33	2d	08-Nov-26	09-Nov-26	398d	3,108	0	3,108
JDH	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 m	2d	10-Nov-26	11-Nov-26	398d	345	0	345
(WT)-Gate Valve-200 mm on pipe dia (225) mm		4d	27-Oct-26	31-Oct-26	419d	10,638	0	10,638
JDH	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B3.33	2d	27-Oct-26	28-Oct-26	419d	9,574	0	9,574
JDH	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 m	2d	29-Oct-26	31-Oct-26	419d	1,064	0	1,064
(WT)-Fire Hydrant		5d	12-Nov-26	17-Nov-26	398d	38,106	0	38,106
JDH	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	12-Nov-26	14-Nov-26	398d	12,702	0	12,702
JDH	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-NR-AMCA-V	3d	15-Nov-26	17-Nov-26	398d	25,404	0	25,404
JDH3-02-009-AMCA-TSE Network - TSE		18d	27-Oct-26	16-Nov-26	405d	207,130	0	207,130
JDH3-02-009-AMCA-(TSE)-HDPE Pipes-110 mm diameter depth from (		18d	27-Oct-26	16-Nov-26	401d	9,808	0	9,808
JDH	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	3d	27-Oct-26	29-Oct-26	401d	2,180	0	2,180
JDH	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	3d	31-Oct-26	02-Nov-26	401d	545	0	545
JDH	Installing for HDPE Pipe Line 110 mm - depth from 0 to 1.5 m- (	8d	03-Nov-26	11-Nov-26	401d	5,994	0	5,994
JDH	Primary Test for HDPE Pipe Line 110 mm - depth from 0 to 1.5	4d	12-Nov-26	16-Nov-26	401d	1,090	0	1,090
JDH3-02-009-AMCA-(TSE)-HDPE Pipes-160 mm diameter depth from		10d	27-Oct-26	07-Nov-26	413d	174,460	0	174,460
JDH	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	2d	27-Oct-26	28-Oct-26	413d	34,892	0	34,892
JDH	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51	2d	29-Oct-26	31-Oct-26	413d	8,723	0	8,723
JDH	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5	2d	01-Nov-26	02-Nov-26	413d	95,953	0	95,953
JDH	Primary Test for HDPE Pipe Line 160 mm - depth from 1.51 to 2	2d	03-Nov-26	04-Nov-26	413d	17,446	0	17,446
JDH	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	2d	05-Nov-26	07-Nov-26	413d	17,446	0	17,446
JDH3-02-009-AMCA-(TSE)-Gate Valve-100 mm on pipe dia (110) mm		4d	12-Nov-26	16-Nov-26	403d	10,147	0	10,147
JDH	Installation for Gate Valve 100 mm on pipe dia 110 mm- (B4.33	2d	12-Nov-26	14-Nov-26	403d	9,132	0	9,132
JDH	Stem & Surface box for Gate Valve 100 mm on pipe dia 110 m	2d	15-Nov-26	16-Nov-26	403d	1,015	0	1,015
JDH3-02-009-AMCA-(TSE)-Gate Valve-150 mm on pipe dia (160) mm		2d	15-Nov-26	16-Nov-26	403d	12,715	0	12,715
JDH	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B4.33	2d	15-Nov-26	16-Nov-26	403d	12,715	0	12,715
D-MCA		75d	27-Oct-26	21-Jan-27	348d	1,112	0	3,687
JDH3-02-009-DMCA-Storm Network- ST		4d	27-Oct-26	31-Oct-26	419d	1,112	0	1,112
JDH3-02-009-DMCA-(ST)-MH Works (1200) mm diameter depth from 2		4d	27-Oct-26	31-Oct-26	419d	1,112	0	1,112
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	419d	715	0	715
JDH	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	419d	397	0	397
JDH3-02-009-DMCA-Road Works - RD		6d	16-Jan-27	21-Jan-27	348d	0	0	2,575

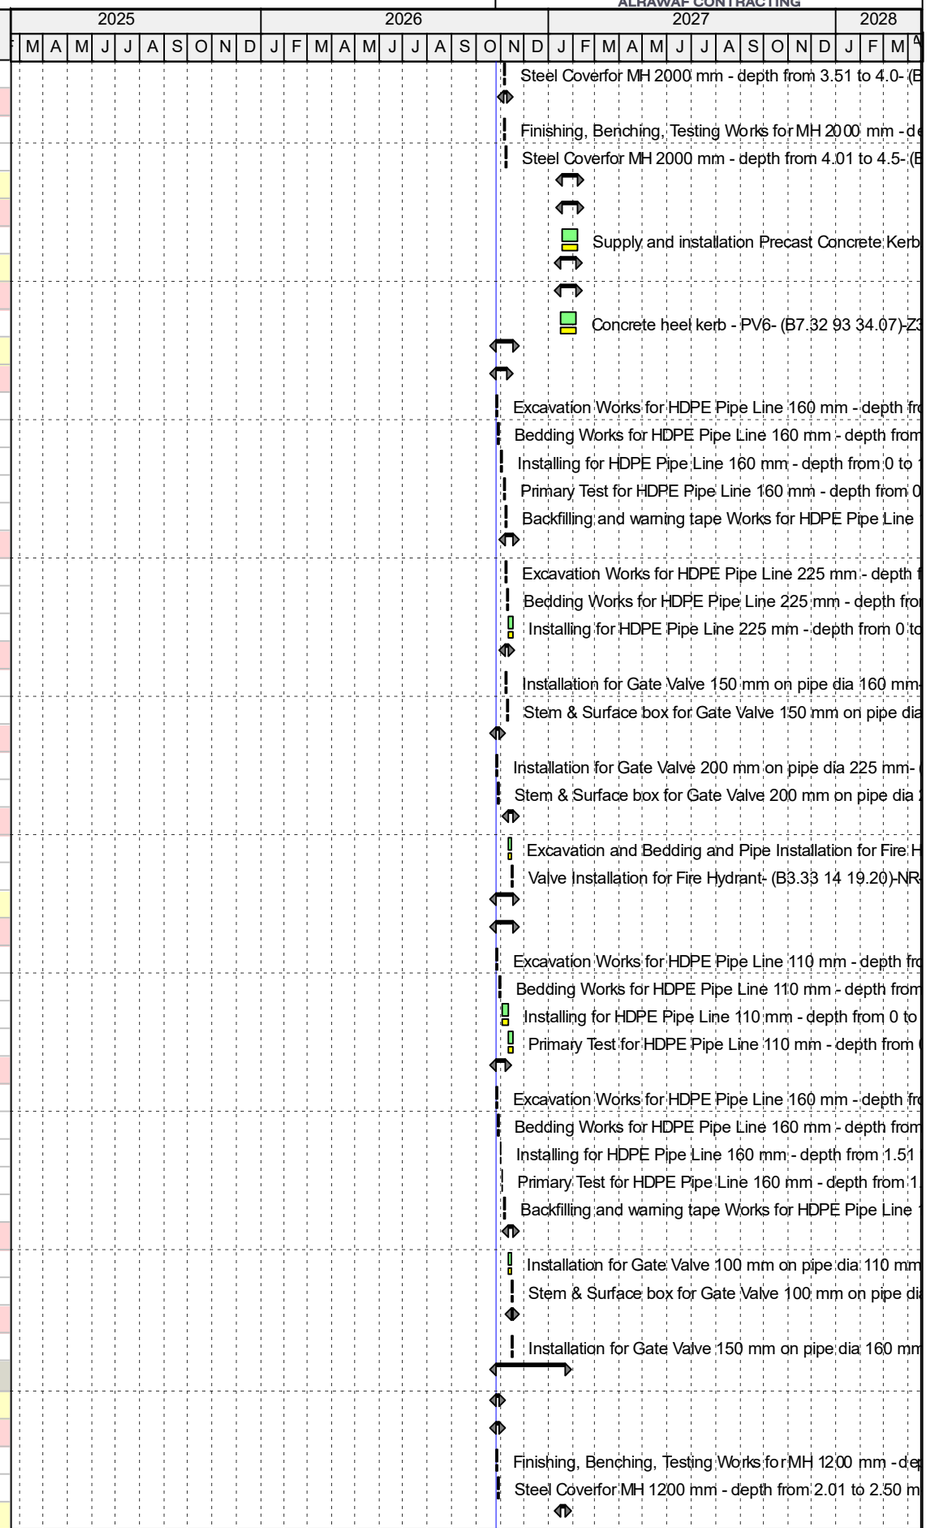

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-DMCA-(RD)-Pavement Marking	6d	16-Jan-27	21-Jan-27	348d	0	0	2,575
JDI	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-NR-DMCA-R	2d	16-Jan-27	17-Jan-27	348d	0	0	1,717
JDI	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2d	18-Jan-27	19-Jan-27	348d	0	0	572
JDI	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.(	2d	20-Jan-27	21-Jan-27	348d	0	0	286
D-MCE		20d	27-Oct-26	18-Nov-26	403d	109,340	0	109,340
	JDH3-02-009-DMCE-Storm Network - ST	6d	27-Oct-26	02-Nov-26	417d	19,366	0	19,366
	JDH3-02-009-DMCE-(ST)-MH Works (2000) mm diameter depth from 3	4d	27-Oct-26	31-Oct-26	417d	12,088	0	12,088
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	27-Oct-26	28-Oct-26	417d	8,000	0	8,000
JDI	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	417d	4,089	0	4,089
	JDH3-02-009-DMCE-(ST)-MH Works (1500) mm diameter depth from 3	4d	29-Oct-26	02-Nov-26	417d	7,278	0	7,278
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	29-Oct-26	31-Oct-26	417d	4,852	0	4,852
JDI	Steel Coverfor MH 1500 mm - depth from 3.01 to 3.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	417d	2,426	0	2,426
	JDH3-02-009-DMCE-Road Works - RD	20d	27-Oct-26	18-Nov-26	293d	89,974	0	89,974
	JDH3-02-009-DMCE-(RD)-Precast Concrete Curb	20d	27-Oct-26	18-Nov-26	293d	89,974	0	89,974
JDI	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8d	27-Oct-26	04-Nov-26	293d	68,785	0	68,785
JDI	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	12d	05-Nov-26	18-Nov-26	293d	21,189	0	21,189
C-MCA		8d	27-Oct-26	04-Nov-26	415d	9,418	0	9,418
	JDH3-02-009-CMCA-Storm Network- ST	8d	27-Oct-26	04-Nov-26	415d	9,418	0	9,418
	JDH3-02-009-CMCA-(ST)-MH Works (1200) mm diameter depth from 1	4d	27-Oct-26	31-Oct-26	415d	5,298	0	5,298
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	415d	3,506	0	3,506
JDI	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2d	29-Oct-26	31-Oct-26	415d	1,792	0	1,792
	JDH3-02-009-CMCA-(ST)-MH Works (1200) mm diameter depth from 2	6d	27-Oct-26	02-Nov-26	415d	1,112	0	1,112
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	417d	715	0	715
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	415d	397	0	397
	JDH3-02-009-CMCA-(ST)-MH Works (1500) mm diameter depth from 2	8d	27-Oct-26	04-Nov-26	415d	3,009	0	3,009
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	419d	2,006	0	2,006
JDI	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	03-Nov-26	04-Nov-26	415d	1,003	0	1,003
C-MCB		18d	27-Oct-26	16-Nov-26	393d	86,617	0	86,617
	JDH3-02-009-CMCB-Storm Network - ST	18d	27-Oct-26	16-Nov-26	393d	86,617	0	86,617
	JDH3-02-009-CMCB-(ST)-GRP Pipes-400 mm diameter depth from 1.5	15d	27-Oct-26	12-Nov-26	393d	82,666	0	82,666
JDI	Excavation Works for GRP Pipe Line 400 mm - depth from 1.51	3d	27-Oct-26	29-Oct-26	393d	16,533	0	16,533
JDI	Bedding Works for GRP Pipe Line 400 mm - depth from 1.51 to	3d	31-Oct-26	02-Nov-26	393d	4,133	0	4,133
JDI	Installing for GRP Pipe Line 400 mm - depth from 1.51 to 2.00	3d	03-Nov-26	05-Nov-26	393d	45,466	0	45,466
JDI	Primary Test for GRP Pipe Line 400 mm - depth from 1.51 to 2.	3d	07-Nov-26	09-Nov-26	393d	8,267	0	8,267
JDI	Backfilling and warning tape Works for GRP Pipe Line 400 mm	3d	10-Nov-26	12-Nov-26	393d	8,267	0	8,267
	JDH3-02-009-CMCB-(ST)-GRP Pipes-500 mm diameter depth from 2.5	3d	14-Nov-26	16-Nov-26	393d	3,952	0	3,952
JDI	Excavation Works for GRP Pipe Line 500 mm - depth from 2.51	3d	14-Nov-26	16-Nov-26	393d	3,952	0	3,952
JDH3-02-009-Infrastructure Networks		440d	20-May-26 A	02-Oct-27	140d	27,933,370	13,143,569	49,588,501
	JDH3-02-009-Milestone	33d	08-Nov-26	16-Dec-26	379d	0	0	0
	Network Milestones	4d	08-Nov-26	12-Nov-26	408d	0	0	0
JDH3S	Finish of Sewage Network - SS - .FMI-SS	0d		12-Nov-26	408d	0	0	0
JDH3S	Finish of Storm Network - ST - .FMI-ST	0d		08-Nov-26	412d	0	0	0
	Zones Millestones	30d	11-Nov-26	16-Dec-26	379d	0	0	0
JDH3(	Finish Z3	0d		16-Dec-26	379d	0	0	0
JDH3(	Finish EX	0d		11-Nov-26	409d	0	0	0
	JDH3-02-009-Engineering - EN	2d	27-Oct-26	28-Oct-26	421d	0	0	0
	JDH3-02-009-Prequalification and Material	2d	27-Oct-26	28-Oct-26	421d	0	0	0
	JDH3-02-009-Submittals of Material and Prequalifications - SUB	2d	27-Oct-26	28-Oct-26	421d	0	0	0
	JDH3-02-009-Submittals of Material and Prequalifications - SUB-La	2d	27-Oct-26	28-Oct-26	421d	0	0	0
	Prepare Material Submittal for Landscape and Irrigation - PR-LS	2d	27-Oct-26	28-Oct-26	421d	0	0	0
	JDH3-02-009-Procurement - PR	44d	15-Sep-26 A	17-Nov-26	402d	369,797	0	369,797
	Long Lead Items	10d	27-Oct-26	05-Nov-26	498d	369,797	0	369,797

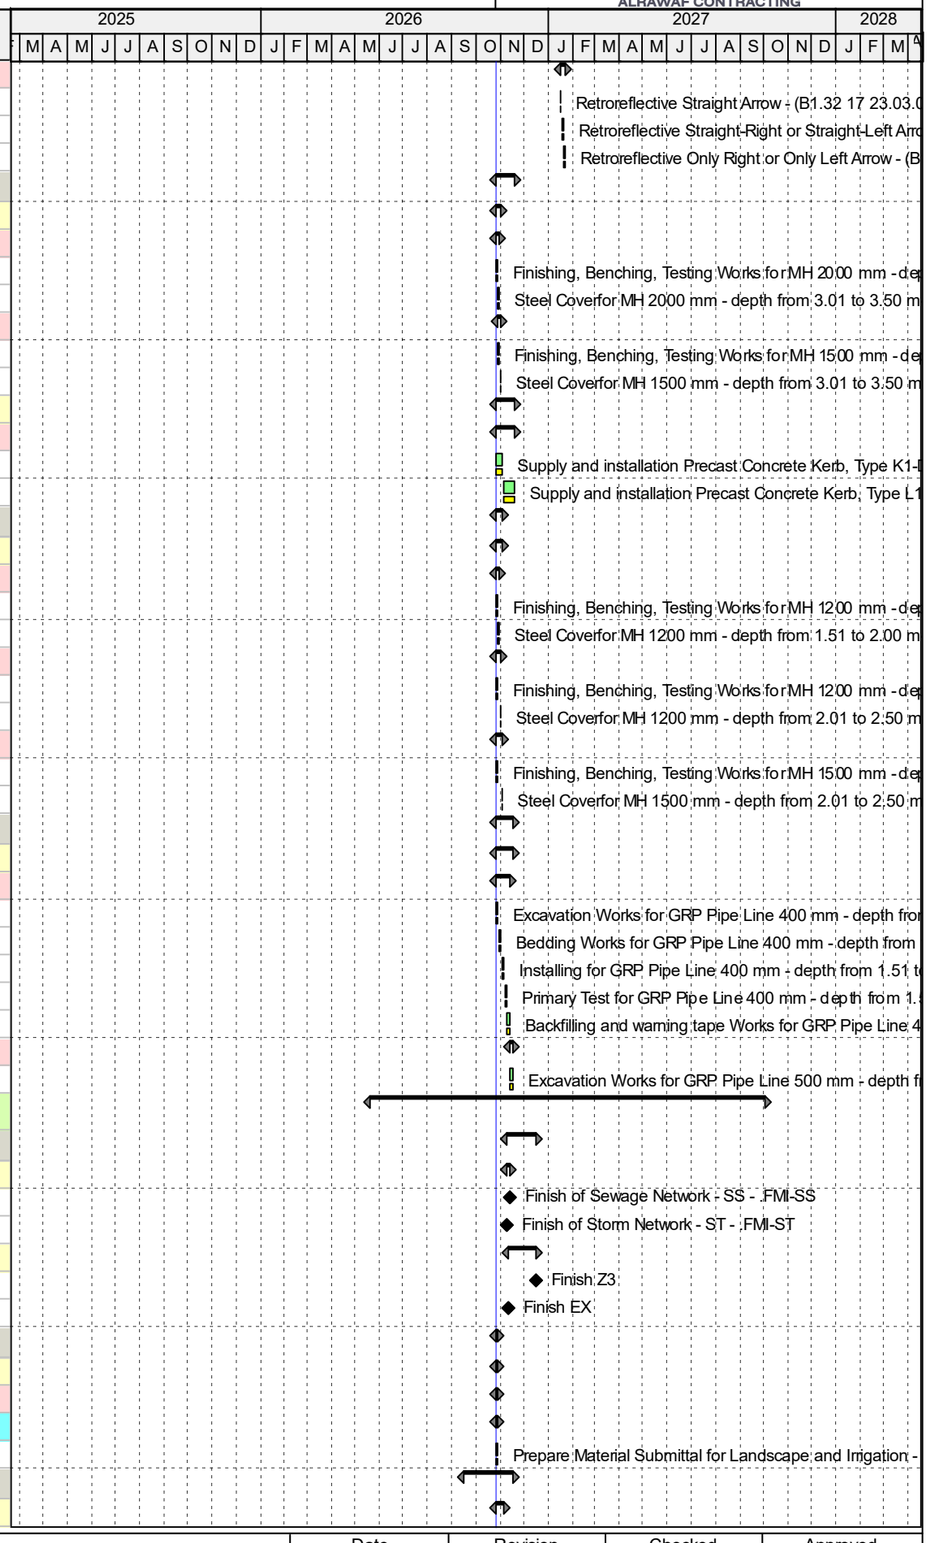


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-Material Delivery and staging on Site - DOS	10d	27-Oct-26	05-Nov-26	498d	369,797	0	369,797
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z03	10d	27-Oct-26	05-Nov-26	240d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10d	27-Oct-26	05-Nov-26	240d	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z03-DOS	10d	27-Oct-26	05-Nov-26	240d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z01	10d	27-Oct-26	05-Nov-26	398d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10d	27-Oct-26	05-Nov-26	398d	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z01-DOS	10d	27-Oct-26	05-Nov-26	398d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z02	10d	27-Oct-26	05-Nov-26	440d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10d	27-Oct-26	05-Nov-26	440d	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z02-DOS	10d	27-Oct-26	05-Nov-26	440d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z04	10d	27-Oct-26	05-Nov-26	498d	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10d	27-Oct-26	05-Nov-26	498d	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z04-DOS	10d	27-Oct-26	05-Nov-26	498d	92,449	0	92,449
	Short Lead items	21d	15-Sep-26 A	17-Nov-26	119d	0	0	0
	JDH3-02-009-Material Purchase Order - PO	21d	15-Sep-26 A	17-Nov-26	119d	0	0	0
	JDH3-Material Purchase Order - PO-Landscape and Irrigation- LS	21d	15-Sep-26 A	17-Nov-26	119d	0	0	0
	Material Purchase Order for Landscape and Irrigation - PR-LS-P	21d	15-Sep-26 A	17-Nov-26	119d	0	0	0
	JDH3-02-009-Execution	440d	20-May-26 A	19-Jul-27	203d	27,563,573	10,139,238	43,329,822
	JDH3-02-009-XX-Execution	3d	27-Oct-26	29-Oct-26	420d	11,854	0	11,854
	Z2	3d	27-Oct-26	29-Oct-26	420d	8,413	0	8,413
	R102	3d	27-Oct-26	29-Oct-26	420d	8,413	0	8,413
	JDH3-02-009-XX-R102-Potable Water Network - WT	3d	27-Oct-26	29-Oct-26	420d	8,413	0	8,413
	JDH3-02-009-XX-R102-(WT)-HDPE Pipes-800 mm diameter d	3d	27-Oct-26	29-Oct-26	420d	8,413	0	8,413
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	3d	27-Oct-26	29-Oct-26	420d	8,413	0	8,413
	Z3	2d	27-Oct-26	28-Oct-26	421d	3,442	0	3,442
	R103	2d	27-Oct-26	28-Oct-26	421d	3,442	0	3,442
	JDH3-02-009-XX-R103-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	3,442	0	3,442
	JDH3-02-009-XX-R103-(WT)-HDPE Pipes-800 mm diameter d	2d	27-Oct-26	28-Oct-26	421d	3,442	0	3,442
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	2d	27-Oct-26	28-Oct-26	421d	3,442	0	3,442
	Pond - PS	123d	27-Oct-26	23-Mar-27	300d	405,364	0	2,959,693
	JDH3-02-009-ST1-Pond 1 - ST	17d	27-Oct-26	15-Nov-26	379d	0	0	627,213
	JDH3-02-009-ST3-Stage (3) - Pond 1	5d	27-Oct-26	01-Nov-26	379d	0	0	313,607
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5d	27-Oct-26	01-Nov-26	379d	0	0	313,607
	JDH3-02-009-ST4-Stage (4) - Pond 1	12d	02-Nov-26	15-Nov-26	379d	0	0	313,607
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	02-Nov-26	15-Nov-26	379d	0	0	313,607
	JDH3-02-009-ST1-Pond 2 - ST	24d	27-Oct-26	23-Nov-26	399d	0	0	326,099
	JDH3-02-009-ST3-Stage (3) - Pond 2	12d	27-Oct-26	09-Nov-26	399d	0	0	163,050
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	27-Oct-26	09-Nov-26	399d	0	0	163,050
	JDH3-02-009-ST4-Stage (4) - Pond 2	12d	10-Nov-26	23-Nov-26	399d	0	0	163,050
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	10-Nov-26	23-Nov-26	399d	0	0	163,050
	JDH3-02-009-ST1-Pond 3 - ST	24d	27-Oct-26	23-Nov-26	399d	0	0	812,429
	JDH3-02-009-ST2-Stage (2) - Pond 3	15d	27-Oct-26	12-Nov-26	408d	0	0	282,543
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	27-Oct-26	09-Nov-26	408d	0	0	264,943
	Access Ramp for Pond 3- (B6.31 22 00.05)-PS-PN3-ST2	3d	10-Nov-26	12-Nov-26	408d	0	0	17,600
	JDH3-02-009-ST3-Stage (3) - Pond 3	12d	27-Oct-26	09-Nov-26	399d	0	0	264,943
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	27-Oct-26	09-Nov-26	399d	0	0	264,943
	JDH3-02-009-ST4-Stage (4) - Pond 3	12d	10-Nov-26	23-Nov-26	399d	0	0	264,943
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12d	10-Nov-26	23-Nov-26	399d	0	0	264,943
	JDH3-02-009-ST1-Pond 6 - ST	19d	27-Oct-26	17-Nov-26	404d	121,471	0	247,820
	JDH3-02-009-ST1-Stage (1) - Pond 6	8d	27-Oct-26	04-Nov-26	415d	0	0	126,349
	Chain Link Fence for Pond 6- (B6.31 22 00.04)-PS-PN6-ST1	8d	27-Oct-26	04-Nov-26	415d	0	0	126,349
	JDH3-02-009-PN6-Landscape Works - LS	19d	27-Oct-26	17-Nov-26	263d	121,471	0	121,471
	JDH3-02-009-PN6-(LS)-Trees	19d	27-Oct-26	17-Nov-26	263d	121,471	0	121,471

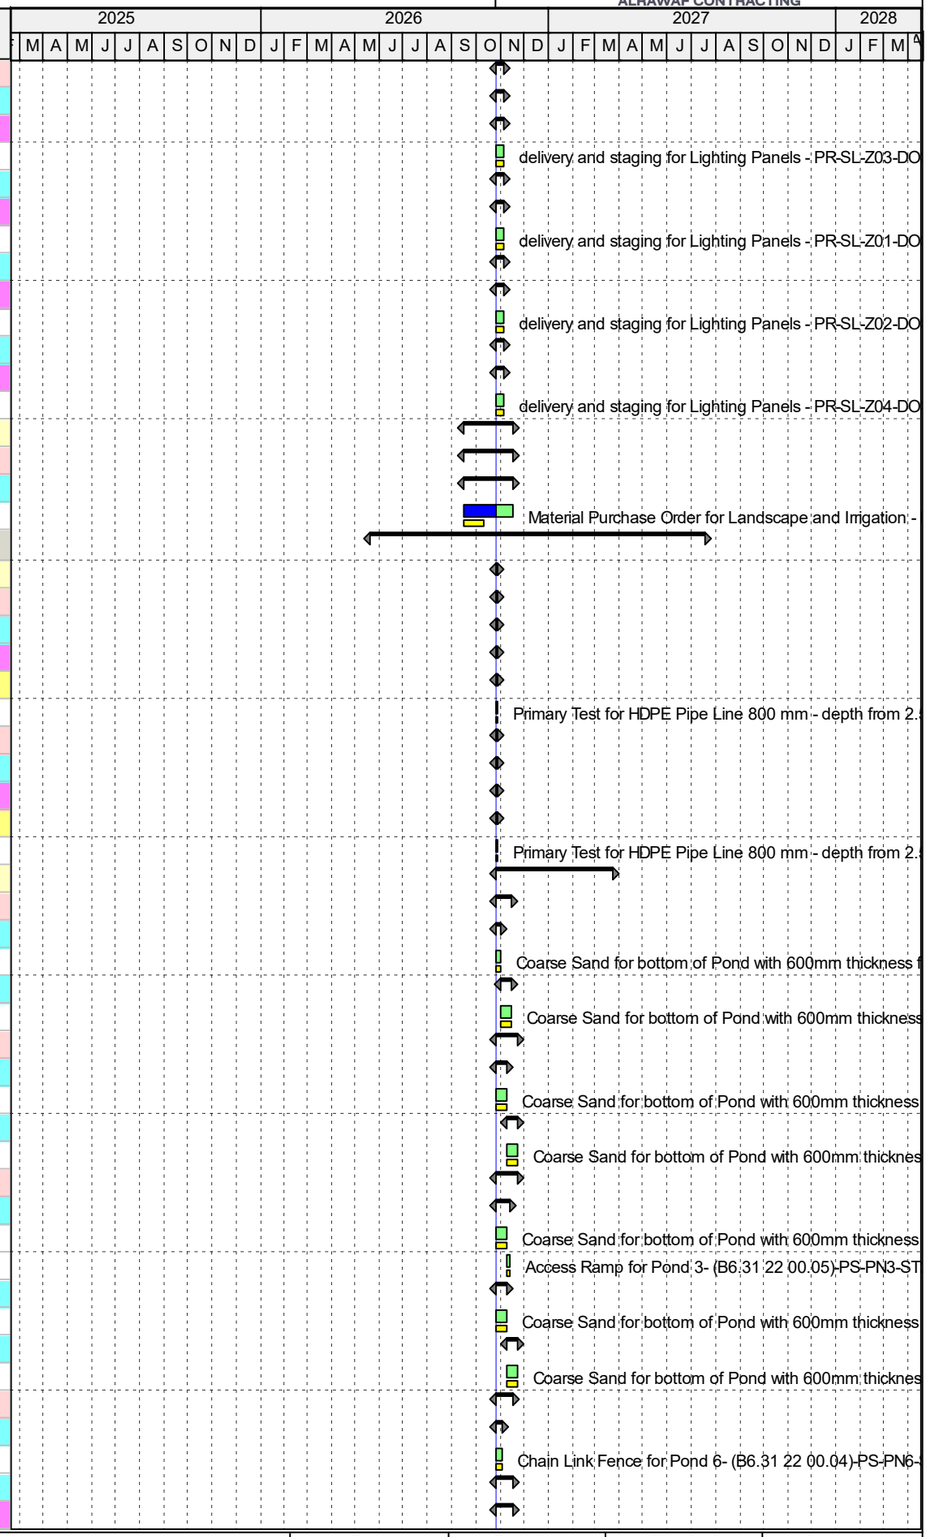


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Ref. ACA AMP (Acacia Ampliceps) - (B7.32 93 00.01)-PS-PN6-L:	4d	27-Oct-26	31-Oct-26	263d	20,683	0	20,683
	Ref. AZA INC (Azadirachta Indica) - (B7.32 93 00.03)-PS-PN6-L:	2d	01-Nov-26	02-Nov-26	271d	9,192	0	9,192
	Ref. COR SEB (Cordia Sebestena) - (B7.32 93 00.05)-PS-PN6-I	5d	12-Nov-26	17-Nov-26	263d	32,502	0	32,502
	Ref. DEL REG (Delonix Regia) - (B7.32 93 00.07)-PS-PN6-LS	6d	05-Nov-26	11-Nov-26	263d	30,204	0	30,204
	Ref. FIC REL (Ficus Religiosa) - (B7.32 93 00.08)-PS-PN6-LS	4d	01-Nov-26	04-Nov-26	263d	28,890	0	28,890
JDH3-02-009-ST1-Pond 9 - ST		123d	27-Oct-26	23-Mar-27	263d	0	0	655,281
JDH3-02-009-ST1-Stage (1) - Pond 9		18d	27-Oct-26	16-Nov-26	345d	0	0	594,951
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	18d	27-Oct-26	16-Nov-26	345d	0	0	594,951
JDH3-02-009-PN9-Landscape Works - LS		16d	02-Mar-27	23-Mar-27	263d	0	0	60,330
JDH3-02-009-PN9-(LS)-Trees		12d	02-Mar-27	18-Mar-27	263d	0	0	59,751
	Ref. ACA AMP (Acacia Ampliceps) - (B7.32 93 00.01)-PS-PN9-L:	7d	08-Mar-27	18-Mar-27	263d	0	0	29,547
	Ref. DEL REG (Delonix Regia) - (B7.32 93 00.07)-PS-PN9-LS	5d	02-Mar-27	07-Mar-27	263d	0	0	30,204
JDH3-02-009-PN9-(LS)-Design, Delive, install, wiring, control, pr		4d	20-Mar-27	23-Mar-27	263d	0	0	580
	Online pressure compensating emitters with - - (B7.32.80.00.0	4d	20-Mar-27	23-Mar-27	263d	0	0	580
JDH3-02-009-ST1-Pond 4 - ST		3d	27-Oct-26	29-Oct-26	420d	283,893	0	290,850
JDH3-02-009-BW-Backfilling Works		3d	27-Oct-26	29-Oct-26	420d	283,893	0	290,850
	Backfill Layers Works Imported Material for Pond 4 - (B1.31 22 (	3d	27-Oct-26	29-Oct-26	420d	283,893	0	290,850
Earthworks - EW		335d	25-May-26 A	19-Jul-27	203d	714,729	1,605,924	3,146,786
JDH3-02-009-Block 01-Block Works - BW		20d	25-May-26 A	19-Jul-27	203d	0	131,875	146,528
Z1		20d	25-May-26 A	19-Jul-27	203d	0	131,875	146,528
JDH3-02-009-Block Works - BWZ1-Block 01		20d	25-May-26 A	19-Jul-27	203d	0	131,875	146,528
	Excavation Works for Block 01 - (B1.31 22 00.05)-Z1-B01-BW	20d	25-May-26 A	19-Jul-27	203d	0	131,875	146,528
JDH3-02-009-R01-Road Works - RW		57d	21-Jul-26 A	31-Dec-26	315d	714,729	1,474,049	3,000,258
Z1		17d	21-Jul-26 A	19-Nov-26	352d	0	621,753	690,837
JDH3-02-009-Road Works - RWZ1-R101		8d	21-Jul-26 A	19-Nov-26	318d	0	241,236	268,040
	Backfill Layers with Imported Material Side Walk for Road - (B1.:	8d	21-Jul-26 A	19-Nov-26	318d	0	241,236	268,040
JDH3-02-009-Road Works - RWZ1-R06		12d	01-Sep-26 A	28-Oct-26	371d	0	380,517	422,797
	Backfill Layers with Imported Material Side Walk for Road - (B1.:	12d	01-Sep-26 A	28-Oct-26	371d	0	380,517	422,797
Z2		43d	17-Sep-26 A	31-Dec-26	302d	714,729	852,296	2,309,421
JDH3-02-009-Road Works - RWZ2-R102		19d	17-Sep-26 A	03-Dec-26	327d	0	637,877	1,594,692
	Backfill Layers with Imported Material Side Walk for Road - (B1.:	19d	17-Sep-26 A	03-Dec-26	327d	0	637,877	1,594,692
JDH3-02-009-Road Works - RWZ2-R14		15d	24-Sep-26 A	31-Dec-26	289d	714,729	214,419	714,729
	Backfill Layers with Imported Material Side Walk for Road - (B1.:	15d	24-Sep-26 A	31-Dec-26	289d	714,729	214,419	714,729
Z3		186d	20-May-26 A	12-Jan-27	356d	4,087,230	938,996	4,625,399
R152		142d	22-Jul-26 A	12-Jan-27	356d	404,473	143,222	439,588
JDH3-02-009-R152-Potable Water Network - WT		2d	27-Oct-26	28-Oct-26	421d	5,862	0	5,862
JDH3-02-009-R152-(WT)-Fire Hydrant		2d	27-Oct-26	28-Oct-26	421d	5,862	0	5,862
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R152-W	2d	27-Oct-26	28-Oct-26	421d	5,862	0	5,862
JDH3-02-009-R152-Electrical Network - EL		16d	22-Jul-26 A	04-Nov-26	397d	186,075	93,037	186,075
JDH3-02-009-R152-(EL)-MV cable trench size 1.5m wide and 80		16d	22-Jul-26 A	04-Nov-26	397d	8,712	4,356	8,712
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	5d	22-Jul-26 A	04-Nov-26	370d	5,227	2,614	5,227
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5d	26-Jul-26 A	04-Nov-26	397d	3,485	1,742	3,485
JDH3-02-009-R152-(EL)-MV cables AL/XLPE/LLDPE Unarmored		6d	23-Jul-26 A	04-Nov-26	397d	177,363	88,681	177,363
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4d	23-Jul-26 A	04-Nov-26	397d	168,662	84,331	168,662
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	25-Jul-26 A	04-Nov-26	397d	8,701	4,351	8,701
JDH3-02-009-R152-Street Lighting Network -SL		20d	27-Oct-26	18-Nov-26	397d	50,625	0	50,625
JDH3-02-009-R152-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP		12d	05-Nov-26	18-Nov-26	397d	46,686	0	46,686
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	05-Nov-26	09-Nov-26	397d	5,187	0	5,187
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	4d	10-Nov-26	14-Nov-26	397d	38,905	0	38,905
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	15-Nov-26	18-Nov-26	397d	2,594	0	2,594
JDH3-02-009-R152-(SL)-Lighting Pole with single arm 12 m heig		5d	27-Oct-26	01-Nov-26	412d	3,940	0	3,940
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	5d	27-Oct-26	01-Nov-26	412d	3,940	0	3,940
JDH3-02-009-R152-Road Works - RD		114d	01-Sep-26 A	12-Jan-27	356d	161,910	50,185	175,069

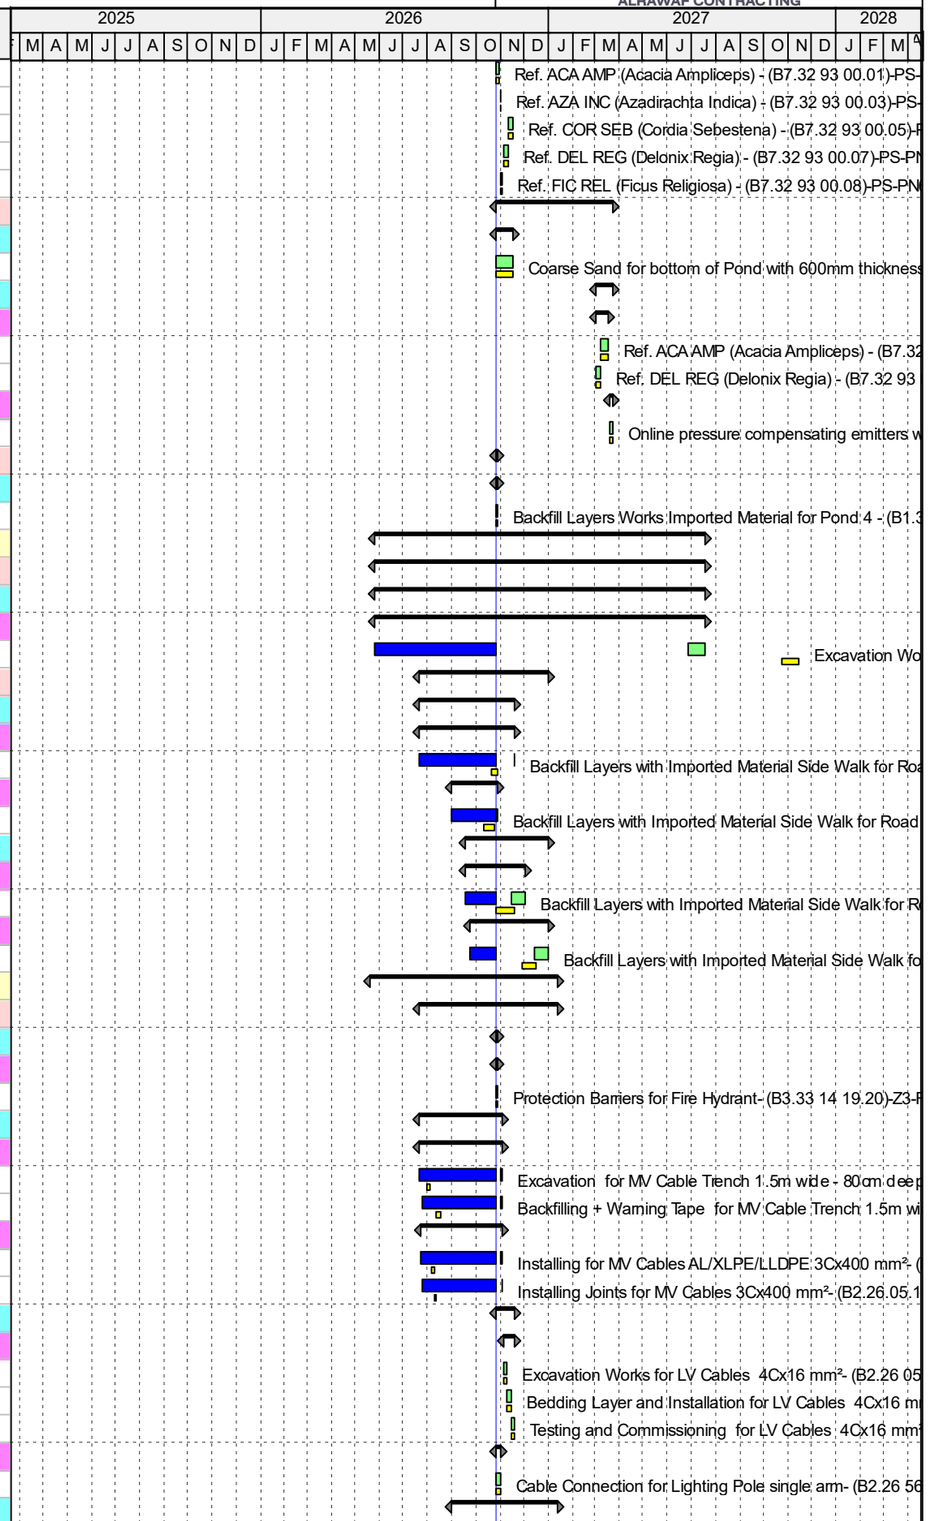


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R152-(RD)-Precast Concrete Curb	67d	01-Sep-26 A	18-Nov-26	339d	161,910	50,185	161,910
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5d	01-Nov-26	05-Nov-26	339d	37,429	0	37,429
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	11d	07-Nov-26	18-Nov-26	339d	69,333	0	69,333
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8d	01-Sep-26 A	31-Oct-26	339d	55,148	50,185	55,148
	JDH3-02-009-R152-(RD)-Pavement Marking	12d	30-Dec-26	12-Jan-27	356d	0	0	6,428
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2d	30-Dec-26	31-Dec-26	356d	0	0	1,417
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	02-Jan-27	03-Jan-27	356d	0	0	1,234
	Thermoplastic intermittent 500 mm wide White yield line - (B1.3	2d	04-Jan-27	05-Jan-27	356d	0	0	630
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z3-R152-RD	2d	06-Jan-27	07-Jan-27	356d	0	0	2,289
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2d	09-Jan-27	10-Jan-27	356d	0	0	572
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.0	2d	11-Jan-27	12-Jan-27	356d	0	0	286
	JDH3-02-009-R152-(RD)-Traffic Signage	2d	31-Dec-26	02-Jan-27	363d	0	0	6,730
	Supply and installation Traffic signs with Double post - (B1.10 14	2d	31-Dec-26	02-Jan-27	363d	0	0	6,730
	JDH3-02-009-R152-Landscape Works - LS	7d	03-Jan-27	10-Jan-27	110d	0	0	21,957
	JDH3-02-009-R152-(LS)-HDPE for Secondary Network	7d	03-Jan-27	10-Jan-27	110d	0	0	21,957
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	7d	03-Jan-27	10-Jan-27	110d	0	0	21,957
R16		171d	20-May-26 A	26-Dec-26	371d	342,099	157,895	359,958
	JDH3-02-009-R16-Potable Water Network - WT	2d	12-Nov-26	14-Nov-26	405d	2,931	0	2,931
	JDH3-02-009-R16-(WT)-Fire Hydrant	2d	12-Nov-26	14-Nov-26	405d	2,931	0	2,931
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R16-W	2d	12-Nov-26	14-Nov-26	405d	2,931	0	2,931
	JDH3-02-009-R16-Electrical Network - EL	78d	20-May-26 A	27-Oct-26	419d	166,206	157,895	166,206
	JDH3-02-009-R16-(EL)-MV cable trench size 1.5m wide and 80c	5d	09-Jun-26 A	27-Oct-26	419d	3,347	3,180	3,347
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5d	09-Jun-26 A	27-Oct-26	419d	3,347	3,180	3,347
	JDH3-02-009-R16-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	64d	20-May-26 A	27-Oct-26	419d	162,859	154,716	162,859
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	25-Jun-26 A	27-Oct-26	419d	5,801	5,511	5,801
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4d	20-May-26 A	27-Oct-26	419d	157,058	149,205	157,058
	JDH3-02-009-R16-Street Lighting Network -SL	4d	27-Oct-26	01-Nov-26	419d	3,534	0	3,534
	JDH3-02-009-R16-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	4d	27-Oct-26	01-Nov-26	419d	2,682	0	2,682
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	27-Oct-26	01-Nov-26	419d	2,682	0	2,682
	JDH3-02-009-R16-(SL)-Earthing System for Streetlighting feede	2d	27-Oct-26	28-Oct-26	421d	852	0	852
	Supply, construct, connect and test earthing pits for Street Light	2d	27-Oct-26	28-Oct-26	421d	852	0	852
	JDH3-02-009-R16-Road Works - RD	22d	27-Oct-26	21-Nov-26	110d	169,428	0	169,428
	JDH3-02-009-R16-(RD)-Precast Concrete Curb	10d	27-Oct-26	07-Nov-26	110d	55,210	0	55,210
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	110d	4,724	0	4,724
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8d	29-Oct-26	07-Nov-26	110d	50,487	0	50,487
	JDH3-02-009-R16-(RD)-Precast Interlocking Block Pavers	12d	08-Nov-26	21-Nov-26	110d	114,218	0	114,218
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12d	08-Nov-26	21-Nov-26	110d	114,218	0	114,218
	JDH3-02-009-R16-Landscape Works - LS	6d	20-Dec-26	26-Dec-26	110d	0	0	17,860
	JDH3-02-009-R16-(LS)-HDPE for Secondary Network	6d	20-Dec-26	26-Dec-26	110d	0	0	17,860
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	6d	20-Dec-26	26-Dec-26	110d	0	0	17,860
R17		44d	27-Oct-26	16-Dec-26	379d	267,207	0	285,066
	JDH3-02-009-R17-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	417d	3,908	0	3,908
	JDH3-02-009-R17-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	417d	3,908	0	3,908
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R17-W	2d	27-Oct-26	28-Oct-26	417d	3,908	0	3,908
	JDH3-02-009-R17-Electrical Network - EL	6d	27-Oct-26	02-Nov-26	417d	68,946	0	68,946
	JDH3-02-009-R17-(EL)-RMU 33 KV	6d	27-Oct-26	02-Nov-26	417d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z3-R17-EL	2d	27-Oct-26	28-Oct-26	417d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z3-R17-EL	2d	29-Oct-26	31-Oct-26	417d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z3-R1	2d	01-Nov-26	02-Nov-26	417d	4,925	0	4,925
	JDH3-02-009-R17-Street Lighting Network -SL	11d	27-Oct-26	08-Nov-26	412d	20,231	0	20,231
	JDH3-02-009-R17-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	4d	27-Oct-26	31-Oct-26	419d	4,828	0	4,828
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	27-Oct-26	28-Oct-26	419d	1,609	0	1,609
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	29-Oct-26	31-Oct-26	419d	3,219	0	3,219

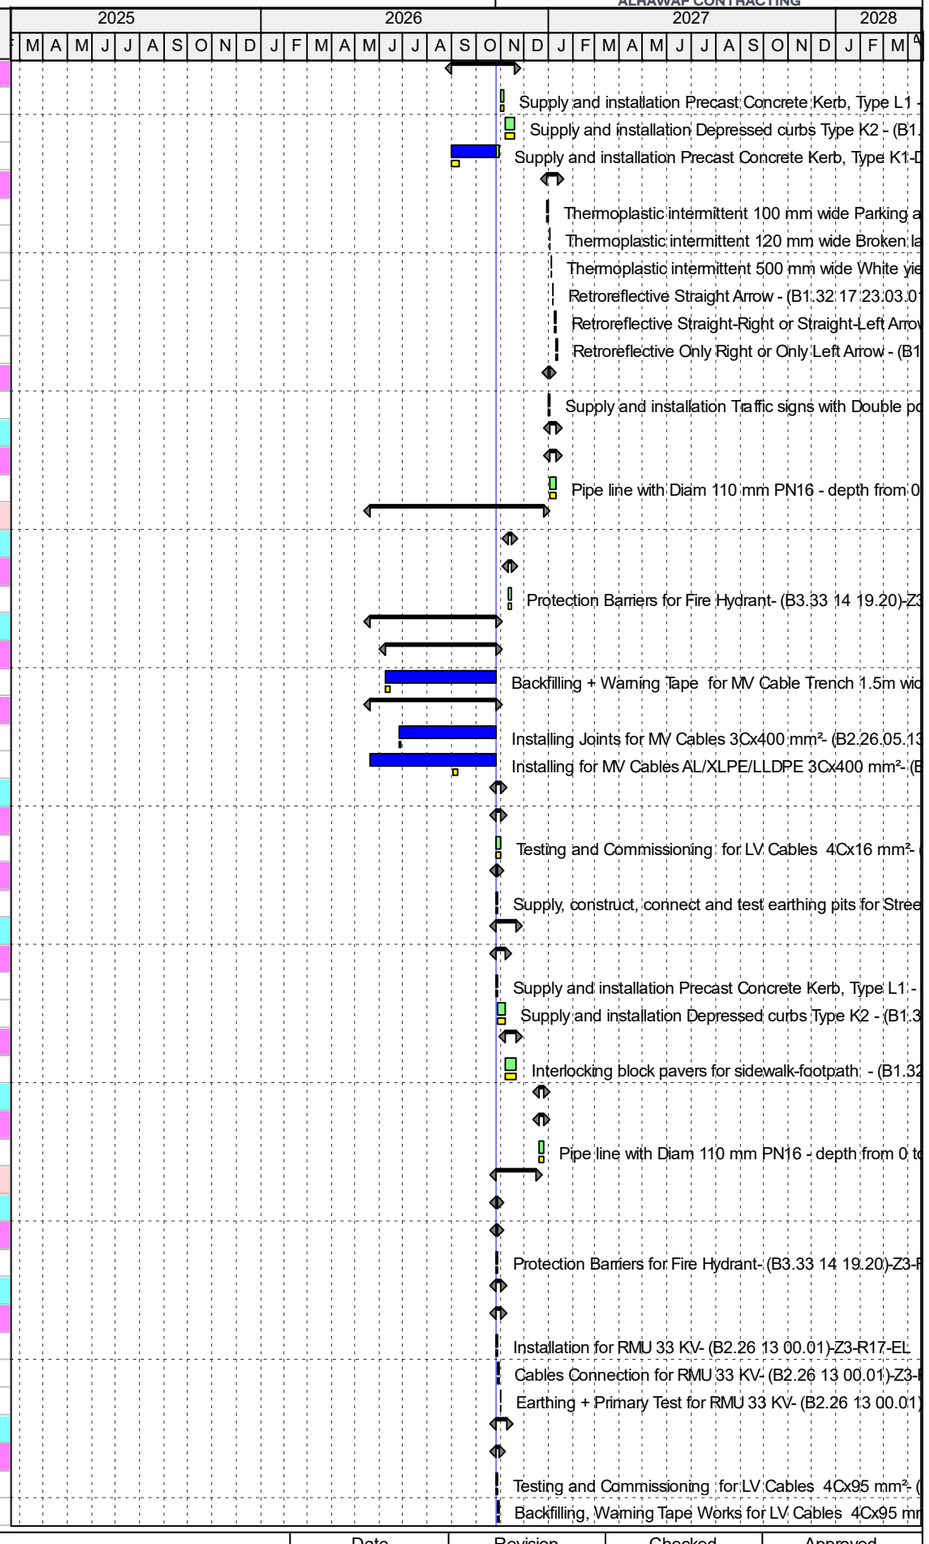


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R17-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	5d	27-Oct-26	01-Nov-26	418d	3,946	0	3,946
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	27-Oct-26	01-Nov-26	418d	3,946	0	3,946
	JDH3-02-009-R17-(SL)-Earthing System for Distribution panels,S	2d	27-Oct-26	28-Oct-26	421d	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	27-Oct-26	28-Oct-26	421d	1,126	0	1,126
	JDH3-02-009-R17-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	412d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R17-S	2d	27-Oct-26	28-Oct-26	417d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2d	29-Oct-26	31-Oct-26	417d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R17-S	2d	07-Nov-26	08-Nov-26	412d	7,232	0	7,232
	JDH3-02-009-R17-Road Works - RD	22d	27-Oct-26	21-Nov-26	377d	174,121	0	174,121
	JDH3-02-009-R17-(RD)-Precast Concrete Curb	10d	27-Oct-26	07-Nov-26	377d	59,977	0	59,977
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	377d	9,490	0	9,490
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8d	29-Oct-26	07-Nov-26	377d	50,487	0	50,487
	JDH3-02-009-R17-(RD)-Precast Interlocking Block Pavers	12d	08-Nov-26	21-Nov-26	377d	114,145	0	114,145
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12d	08-Nov-26	21-Nov-26	377d	114,145	0	114,145
	JDH3-02-009-R17-Landscape Works - LS	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
	JDH3-02-009-R17-(LS)-HDPE for Secondary Network	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
R18		131d	23-Jul-26 A	23-Dec-26	373d	515,050	122,550	945,000
	JDH3-02-009-R18-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R18-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R18-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R18-Street Lighting Network -SL	95d	23-Jul-26 A	11-Nov-26	409d	192,403	68,163	192,403
	JDH3-02-009-R18-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8d	27-Oct-26	04-Nov-26	415d	96,924	0	96,924
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	27-Oct-26	28-Oct-26	340d	9,692	0	9,692
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	29-Oct-26	31-Oct-26	415d	72,693	0	72,693
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	01-Nov-26	02-Nov-26	415d	4,846	0	4,846
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	03-Nov-26	04-Nov-26	415d	9,692	0	9,692
	JDH3-02-009-R18-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	88d	23-Jul-26 A	03-Nov-26	340d	75,672	64,699	75,672
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	29-Oct-26	03-Nov-26	340d	3,784	0	3,784
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	23-Jul-26 A	28-Oct-26	340d	7,567	6,810	7,567
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	23-Jul-26 A	28-Oct-26	340d	56,754	51,078	56,754
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	06-Aug-26 A	03-Nov-26	340d	7,567	6,810	7,567
	JDH3-02-009-R18-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2d	28-Jul-26 A	27-Oct-26	423d	3,849	3,464	3,849
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2d	28-Jul-26 A	27-Oct-26	423d	3,849	3,464	3,849
	JDH3-02-009-R18-(SL)-Earthing System for Distribution panels,S	3d	09-Nov-26	11-Nov-26	336d	5,628	0	5,628
	Supply, construct, connect and test earthing pits for Street Light	3d	09-Nov-26	11-Nov-26	336d	5,628	0	5,628
	JDH3-02-009-R18-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	336d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R18-S	2d	27-Oct-26	28-Oct-26	341d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2d	29-Oct-26	31-Oct-26	341d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R18-S	2d	07-Nov-26	08-Nov-26	336d	7,232	0	7,232
	JDH3-02-009-R18-Road Works - RD	89d	25-Aug-26 A	23-Dec-26	371d	317,761	54,386	729,852
	JDH3-02-009-R18-(RD)-Bituminous concrete wearing course 50	2d	02-Dec-26	05-Dec-26	365d	0	0	353,427
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2d	02-Dec-26	05-Dec-26	365d	0	0	353,427
	JDH3-02-009-R18-(RD)-Precast Concrete Curb	53d	25-Aug-26 A	11-Nov-26	365d	146,698	54,386	146,698
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3d	27-Oct-26	31-Oct-26	365d	21,085	0	21,085
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10d	31-Oct-26	11-Nov-26	365d	65,183	0	65,183
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9d	25-Aug-26 A	27-Oct-26	365d	60,429	54,386	60,429
	JDH3-02-009-R18-(RD)-Precast Interlocking Block Pavers	18d	11-Nov-26	02-Dec-26	365d	171,063	0	181,126
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18d	11-Nov-26	02-Dec-26	365d	171,063	0	181,126
	JDH3-02-009-R18-(RD)-Pavement Marking	16d	05-Dec-26	23-Dec-26	365d	0	0	15,387
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	05-Dec-26	07-Dec-26	365d	0	0	4,869
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	07-Dec-26	09-Dec-26	365d	0	0	477
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	09-Dec-26	12-Dec-26	365d	0	0	3,579

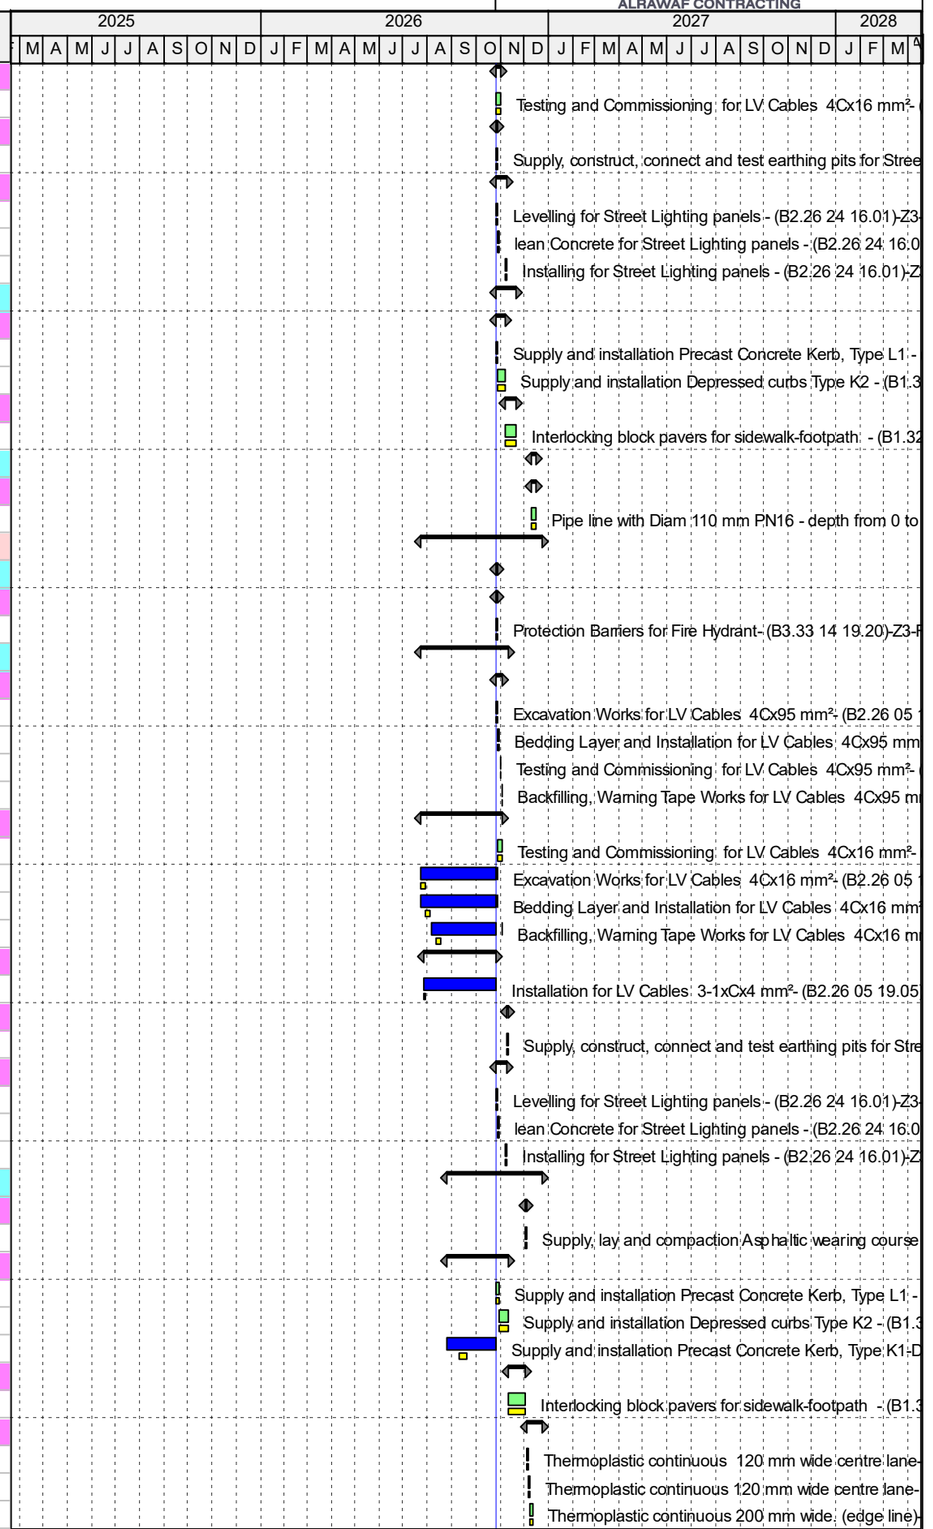


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Thermoplastic continuous 100 mm wide (parking separator line)	2d	12-Dec-26	14-Dec-26	365d	0	0	1,323
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	14-Dec-26	16-Dec-26	365d	0	0	1,901
	Thermoplastic continuous Chevron hatching - white (round abou	2d	16-Dec-26	19-Dec-26	365d	0	0	309
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2d	19-Dec-26	21-Dec-26	365d	0	0	1,579
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	21-Dec-26	23-Dec-26	365d	0	0	1,349
	JDH3-02-009-R18-(RD)-Traffic Signage	10d	05-Dec-26	16-Dec-26	377d	0	0	33,214
	Supply and installation Traffic signs 1 Sheet with Single post - (E	4d	05-Dec-26	09-Dec-26	377d	0	0	13,080
	Supply and installation Traffic signs 2 Sheet with Single post - (E	4d	09-Dec-26	14-Dec-26	377d	0	0	16,769
	Supply and installation Traffic signs with Double post - (B1.10 14	2d	14-Dec-26	16-Dec-26	377d	0	0	3,365
	JDH3-02-009-R18-Landscape Works - LS	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
	JDH3-02-009-R18-(LS)-HDPE for Secondary Network	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	6d	10-Dec-26	16-Dec-26	379d	0	0	17,860
R19		80d	01-Sep-26 A	03-Dec-26	391d	451,183	47,667	455,232
	JDH3-02-009-R19-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R19-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R19-W	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R19-Street Lighting Network -SL	19d	27-Oct-26	17-Nov-26	404d	138,367	0	142,416
	JDH3-02-009-R19-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	12d	27-Oct-26	09-Nov-26	409d	47,612	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2d	27-Oct-26	28-Oct-26	415d	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2d	29-Oct-26	31-Oct-26	415d	3,401	0	3,401
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2d	08-Nov-26	09-Nov-26	409d	3,401	0	3,401
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	10d	27-Oct-26	07-Nov-26	409d	2,224	0	2,224
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	27-Oct-26	28-Oct-26	415d	741	0	741
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	05-Nov-26	07-Nov-26	409d	1,483	0	1,483
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 3x1Cx50mm²,Cu/XL	2d	29-Oct-26	31-Oct-26	417d	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z3-F	2d	29-Oct-26	31-Oct-26	417d	1,520	0	1,520
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	4d	27-Oct-26	31-Oct-26	419d	2,477	0	2,477
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	27-Oct-26	31-Oct-26	419d	2,477	0	2,477
	JDH3-02-009-R19-(SL)-Earthing System for Distribution panels,S	2d	14-Nov-26	15-Nov-26	402d	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	14-Nov-26	15-Nov-26	402d	0	0	1,126
	JDH3-02-009-R19-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	402d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R19-S	2d	27-Oct-26	28-Oct-26	407d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2d	29-Oct-26	31-Oct-26	407d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R19-S	2d	07-Nov-26	08-Nov-26	402d	7,232	0	7,232
	JDH3-02-009-R19-(SL)- LV Distribution Panel Main: 100A, MCCB	11d	29-Oct-26	10-Nov-26	402d	18,369	0	18,369
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z3-R19-S	2d	29-Oct-26	31-Oct-26	407d	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z3-F	2d	01-Nov-26	02-Nov-26	407d	3,674	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z3-R19-S	2d	09-Nov-26	10-Nov-26	402d	12,858	0	12,858
	JDH3-02-009-R19-(SL)-KWH meter mounting frame	2d	11-Nov-26	12-Nov-26	402d	0	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z3-R19-SL	2d	11-Nov-26	12-Nov-26	402d	0	0	2,072
	JDH3-02-009-R19-(SL)-Earthing System for Streetlighting feede	2d	16-Nov-26	17-Nov-26	402d	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2d	16-Nov-26	17-Nov-26	402d	0	0	852
	JDH3-02-009-R19-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL/	8d	27-Oct-26	04-Nov-26	409d	1,212	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2d	27-Oct-26	28-Oct-26	407d	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2d	29-Oct-26	31-Oct-26	409d	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2	2d	01-Nov-26	02-Nov-26	409d	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2d	03-Nov-26	04-Nov-26	409d	121	0	121
	JDH3-02-009-R19-(SL)-RMU 33 KV	4d	27-Oct-26	31-Oct-26	417d	54,621	0	54,621
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z3-R19-SL	2d	27-Oct-26	28-Oct-26	417d	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z3-R19-SL	2d	29-Oct-26	31-Oct-26	417d	4,202	0	4,202
JDH3-02-009-R19-Road Works - RD		80d	01-Sep-26 A	03-Dec-26	360d	308,419	47,667	308,419
	JDH3-02-009-R19-(RD)-Precast Concrete Curb	62d	01-Sep-26 A	12-Nov-26	360d	122,546	47,667	122,546
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	31-Oct-26	02-Nov-26	360d	15,078	0	15,078

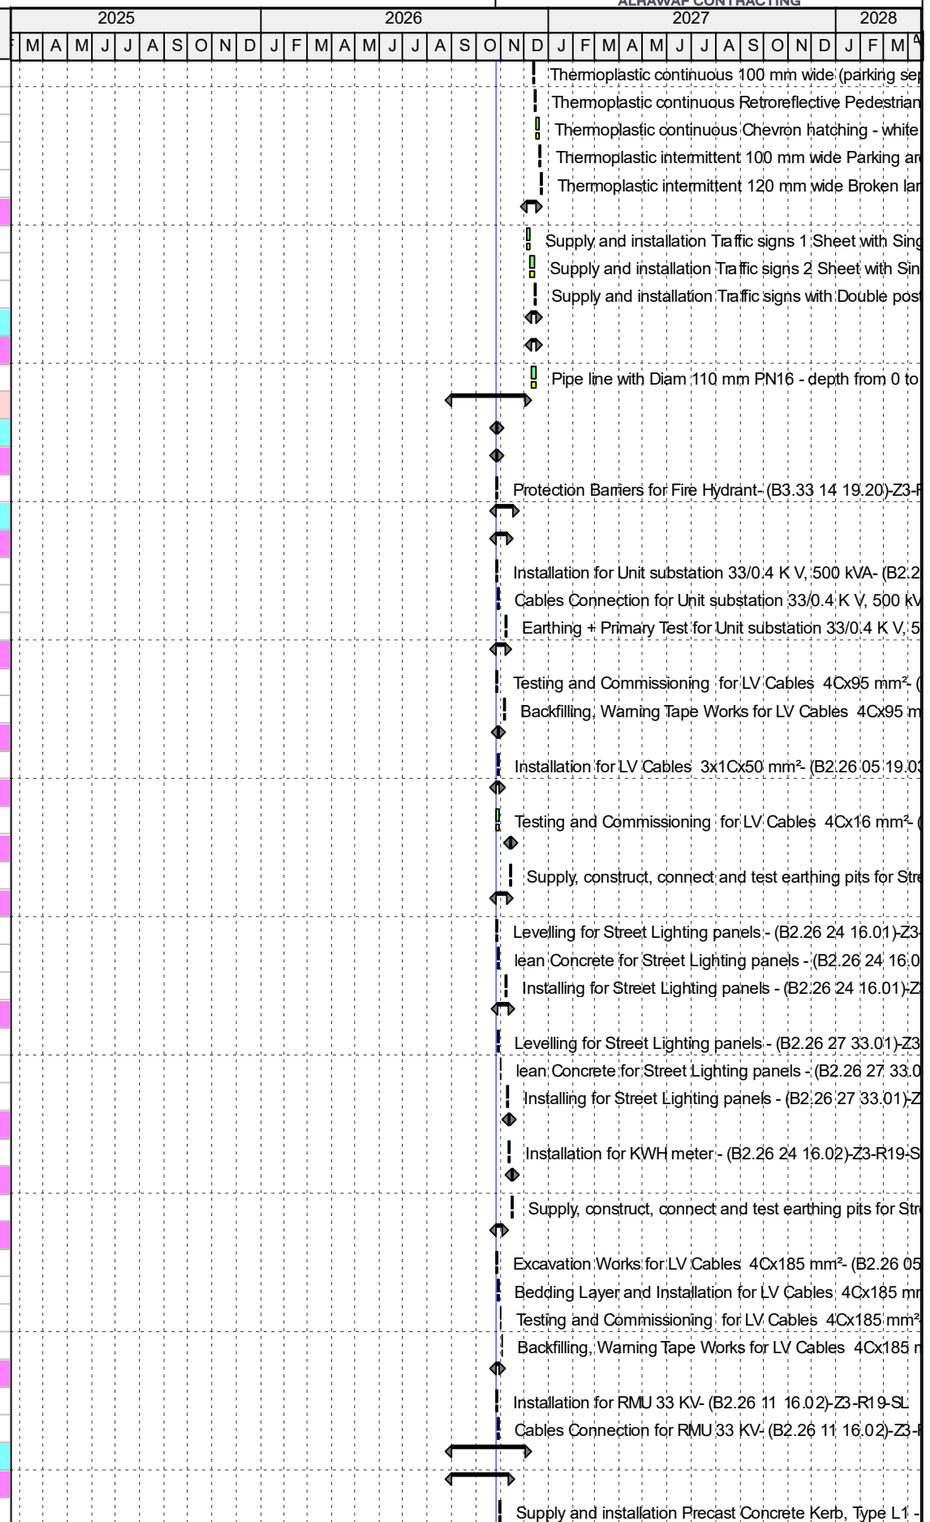

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9d	02-Nov-26	12-Nov-26	360d	55,656	0	55,656
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	7d	01-Sep-26 A	31-Oct-26	360d	51,811	47,667	51,811
	JDH3-02-009-R19-(RD)-Precast Interlocking Block Pavers	18d	12-Nov-26	03-Dec-26	360d	185,873	0	185,873
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18d	12-Nov-26	03-Dec-26	360d	185,873	0	185,873
R20		82d	28-Jul-26 A	06-Dec-26	388d	1,600,407	344,321	1,622,817
JDH3-02-009-R20-TSE Network - TSE		48d	03-Sep-26 A	31-Oct-26	420d	84,994	25,206	84,994
JDH3-02-009-R20-(TSE)-Butterfly Valve-300 mm on pipe dia (315		9d	15-Sep-26 A	28-Oct-26	421d	48,390	15,969	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2d	15-Sep-26 A	28-Oct-26	422d	43,551	14,372	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	24-Sep-26 A	28-Oct-26	421d	4,839	1,597	4,839
JDH3-02-009-R20-(TSE)-Valve Chamber on 315 mm dia pipeline		48d	03-Sep-26 A	31-Oct-26	420d	36,604	9,237	36,604
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	28-Oct-26	31-Oct-26	420d	8,613	0	8,613
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	16-Sep-26 A	28-Oct-26	420d	23,685	7,816	23,685
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	03-Sep-26 A	28-Oct-26	420d	4,306	1,421	4,306
JDH3-02-009-R20-Potable Water Network - WT		49d	01-Sep-26 A	09-Nov-26	411d	399,301	138,505	399,301
JDH3-02-009-R20-(WT)-Wash-Out Valve-150 mm on pipe dia (63		4d	27-Oct-26	31-Oct-26	415d	19,542	0	19,542
	Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E	2d	27-Oct-26	28-Oct-26	411d	17,588	0	17,588
	Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6	2d	29-Oct-26	31-Oct-26	415d	1,954	0	1,954
JDH3-02-009-R20-(WT)-Wash-Out Chamber on 630 mm dia pipe		8d	29-Oct-26	07-Nov-26	411d	27,211	0	27,211
	Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m	2d	29-Oct-26	31-Oct-26	411d	4,082	0	4,082
	PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fr	2d	01-Nov-26	02-Nov-26	411d	2,721	0	2,721
	Installationfor Wash-Out Chamber on pipe dia 630 mm - depth	2d	03-Nov-26	04-Nov-26	411d	14,966	0	14,966
	Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm - c	2d	05-Nov-26	07-Nov-26	411d	5,442	0	5,442
JDH3-02-009-R20-(WT)-Butterfly Valve-600 mm on pipe dia (630)		6d	16-Sep-26 A	07-Nov-26	413d	246,581	98,633	246,581
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2d	16-Sep-26 A	07-Nov-26	413d	221,923	88,769	221,923
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 630	2d	22-Sep-26 A	07-Nov-26	413d	24,658	9,863	24,658
JDH3-02-009-R20-(WT)-Valve Chamber on 630 mm dia pipeline		49d	01-Sep-26 A	09-Nov-26	411d	91,796	36,718	91,796
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2d	08-Nov-26	09-Nov-26	411d	18,359	0	18,359
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2d	16-Sep-26 A	07-Nov-26	411d	50,488	20,195	50,488
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2d	03-Sep-26 A	07-Nov-26	411d	9,180	5,508	9,180
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2d	01-Sep-26 A	07-Nov-26	411d	13,769	11,015	13,769
JDH3-02-009-R20-(WT)-Fire Hydrant		2d	27-Oct-26	28-Oct-26	421d	3,420	0	3,420
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R20-W	2d	27-Oct-26	28-Oct-26	421d	3,420	0	3,420
JDH3-02-009-R20-(WT)-Valve Chamber on 400 mm dia pipeline		45d	12-Sep-26 A	09-Nov-26	411d	10,752	3,154	10,752
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	07-Nov-26	09-Nov-26	411d	2,867	0	2,867
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	12-Sep-26 A	07-Nov-26	411d	7,885	3,154	7,885
JDH3-02-009-R20-Electrical Network - EL		10d	05-Nov-26	16-Nov-26	370d	216,274	0	216,274
JDH3-02-009-R20-(EL)-MV cable trench size 1.5m wide and 80c		5d	05-Nov-26	10-Nov-26	370d	3,356	0	3,356
	Excavation for MV Cable Trench 1.5m wide - 80 cm deep- (B2.3	5d	05-Nov-26	10-Nov-26	370d	3,356	0	3,356
JDH3-02-009-R20-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(		5d	11-Nov-26	16-Nov-26	370d	212,919	0	212,919
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	11-Nov-26	16-Nov-26	370d	212,919	0	212,919
JDH3-02-009-R20-Street Lighting Network -SL		44d	28-Jul-26 A	01-Dec-26	389d	167,540	145,394	167,540
JDH3-02-009-R20-(SL)-Lighting Pole with double arms 16 m hei		10d	28-Jul-26 A	22-Nov-26	397d	79,730	75,146	79,730
	Excavation for RC foundation for Lighting Pole double arms- (B2	2d	28-Jul-26 A	22-Nov-26	370d	7,973	7,574	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2d	29-Jul-26 A	22-Nov-26	393d	7,973	7,574	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2.	2d	30-Jul-26 A	22-Nov-26	393d	7,973	7,574	7,973
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	4d	01-Aug-26 A	22-Nov-26	393d	51,825	49,233	51,825
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	4d	05-Aug-26 A	22-Nov-26	397d	3,987	3,189	3,987
JDH3-02-009-R20-(SL)-Street Lighting(LED) Luminaire complet		6d	01-Aug-26 A	22-Nov-26	397d	20,198	16,159	20,198
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.'	3d	01-Aug-26 A	22-Nov-26	397d	16,159	12,927	16,159
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3d	01-Aug-26 A	22-Nov-26	397d	4,040	3,232	4,040
JDH3-02-009-R20-(SL)- LV Cables - Single Core Copper, 3-1xC 4		2d	16-Sep-26 A	22-Nov-26	393d	3,849	3,079	3,849
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2d	16-Sep-26 A	22-Nov-26	393d	3,849	3,079	3,849
JDH3-02-009-R20-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE		23d	04-Aug-26 A	01-Dec-26	370d	63,763	51,010	63,763

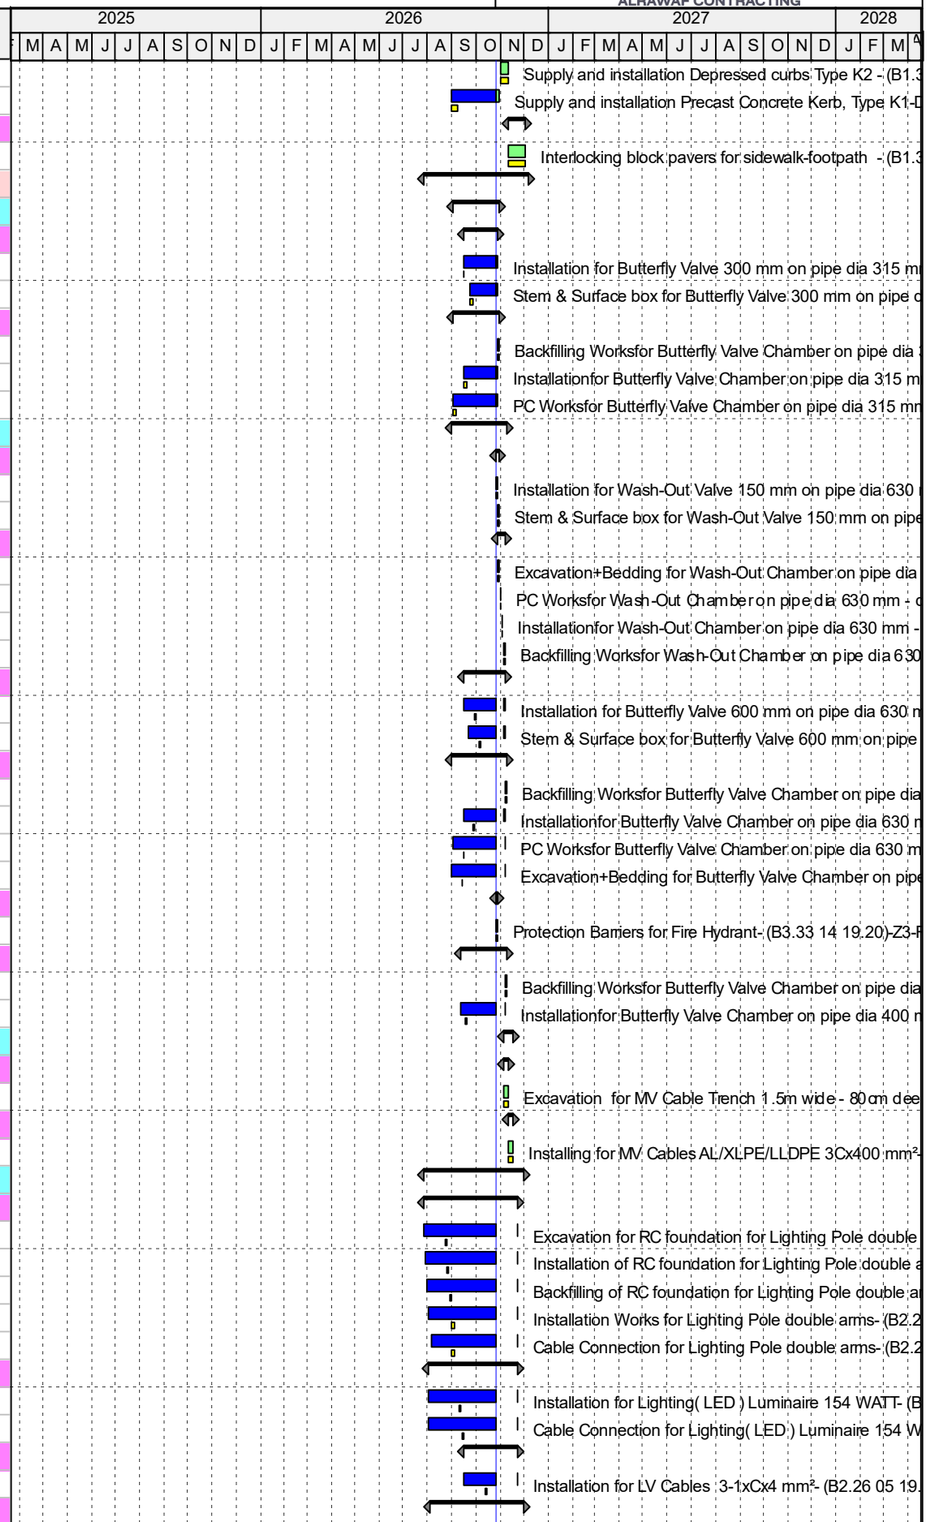


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	05-Aug-26 A	24-Nov-26	371d	50,339	40,271	50,339
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	19-Aug-26 A	01-Dec-26	370d	6,712	5,370	6,712
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	04-Aug-26 A	24-Nov-26	371d	6,712	5,370	6,712
	JDH3-02-009-R20-Road Works - RD	44d	05-Sep-26 A	06-Dec-26	388d	732,297	35,217	754,708
	JDH3-02-009-R20-(RD)-Bituminous concrete wearing course 50	5d	27-Oct-26	01-Nov-26	395d	494,057	0	494,057
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	27-Oct-26	01-Nov-26	395d	494,057	0	494,057
	JDH3-02-009-R20-(RD)-Precast Concrete Curb	6d	05-Sep-26 A	06-Dec-26	370d	176,083	35,217	176,083
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	6d	05-Sep-26 A	06-Dec-26	370d	176,083	35,217	176,083
	JDH3-02-009-R20-(RD)-Pavement Marking	23d	02-Nov-26	28-Nov-26	395d	30,625	0	38,026
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	02-Nov-26	03-Nov-26	395d	857	0	857
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	5d	04-Nov-26	09-Nov-26	395d	26,832	0	26,832
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2d	10-Nov-26	11-Nov-26	395d	1,034	0	1,034
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	12-Nov-26	14-Nov-26	395d	1,901	0	3,802
	Thermoplastic continuous Painted rumble strips marking (300m	2d	15-Nov-26	16-Nov-26	395d	0	0	702
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	17-Nov-26	18-Nov-26	395d	0	0	1,889
	Thermoplastic intermittent 200 mm wide Broken edge line - (B1	2d	19-Nov-26	21-Nov-26	395d	0	0	1,687
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2d	22-Nov-26	23-Nov-26	395d	0	0	429
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.0	2d	24-Nov-26	25-Nov-26	395d	0	0	715
	Thermoplastic continuous Chevron hatching - white (round abou	2d	26-Nov-26	28-Nov-26	395d	0	0	78
	JDH3-02-009-R20-(RD)-Traffic Signage	16d	02-Nov-26	19-Nov-26	400d	31,533	0	46,541
	Supply and installation Traffic signs 1 Sheet with Single post - (E	14d	02-Nov-26	17-Nov-26	400d	31,533	0	44,146
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2d	18-Nov-26	19-Nov-26	400d	0	0	2,396
	R151	125d	04-Aug-26 A	30-Dec-26	367d	506,812	123,341	517,738
	JDH3-02-009-R151-Potable Water Network - WT	2d	15-Nov-26	16-Nov-26	405d	4,885	0	4,885
	JDH3-02-009-R151-(WT)-Fire Hydrant	2d	15-Nov-26	16-Nov-26	405d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R151-W	2d	15-Nov-26	16-Nov-26	405d	4,885	0	4,885
	JDH3-02-009-R151-Street Lighting Network -SL	82d	04-Aug-26 A	10-Nov-26	410d	180,735	63,744	180,735
	JDH3-02-009-R151-(SL)- LV Cables - Copper, 4 Cx 95 mm², Cu/XLP	8d	27-Oct-26	04-Nov-26	411d	80,468	0	80,468
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	27-Oct-26	28-Oct-26	411d	8,047	0	8,047
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	29-Oct-26	31-Oct-26	411d	60,351	0	60,351
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	01-Nov-26	02-Nov-26	411d	4,023	0	4,023
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	03-Nov-26	04-Nov-26	411d	8,047	0	8,047
	JDH3-02-009-R151-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP	76d	06-Aug-26 A	04-Nov-26	411d	77,159	58,641	77,159
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	29-Oct-26	03-Nov-26	412d	3,858	0	3,858
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	06-Aug-26 A	28-Oct-26	412d	7,716	6,173	7,716
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	08-Aug-26 A	28-Oct-26	412d	57,869	46,295	57,869
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	11-Aug-26 A	04-Nov-26	411d	7,716	6,173	7,716
	JDH3-02-009-R151-(SL)-Earthing System for Streetlighting feed	2d	05-Nov-26	07-Nov-26	411d	426	0	426
	Supply, construct, connect and test earthing pits for Street Light	2d	05-Nov-26	07-Nov-26	411d	426	0	426
	JDH3-02-009-R151-(SL)-Earthing System for Distribution panels	2d	09-Nov-26	10-Nov-26	410d	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	09-Nov-26	10-Nov-26	410d	1,126	0	1,126
	JDH3-02-009-R151-(SL)- Street Lighting Panels	10d	28-Oct-26	08-Nov-26	410d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R151-	2d	28-Oct-26	29-Oct-26	414d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2d	31-Oct-26	01-Nov-26	414d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R151-	2d	07-Nov-26	08-Nov-26	410d	7,232	0	7,232
	JDH3-02-009-R151-(SL)-Lighting Pole with single arm 12 m heig	7d	04-Aug-26 A	04-Nov-26	411d	6,378	5,103	6,378
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	7d	04-Aug-26 A	04-Nov-26	411d	6,378	5,103	6,378
	JDH3-02-009-R151-(SL)- LV Cables - Single Core Copper, 3 -1x C	2d	27-Oct-26	28-Oct-26	417d	4,847	0	4,847
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2d	27-Oct-26	28-Oct-26	417d	4,847	0	4,847
	JDH3-02-009-R151-Road Works - RD	83d	25-Aug-26 A	01-Dec-26	360d	321,192	59,597	321,192
	JDH3-02-009-R151-(RD)-Precast Concrete Curb	65d	25-Aug-26 A	10-Nov-26	360d	144,497	59,597	144,497
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	29-Oct-26	360d	16,813	0	16,813
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10d	29-Oct-26	10-Nov-26	360d	64,950	0	64,950

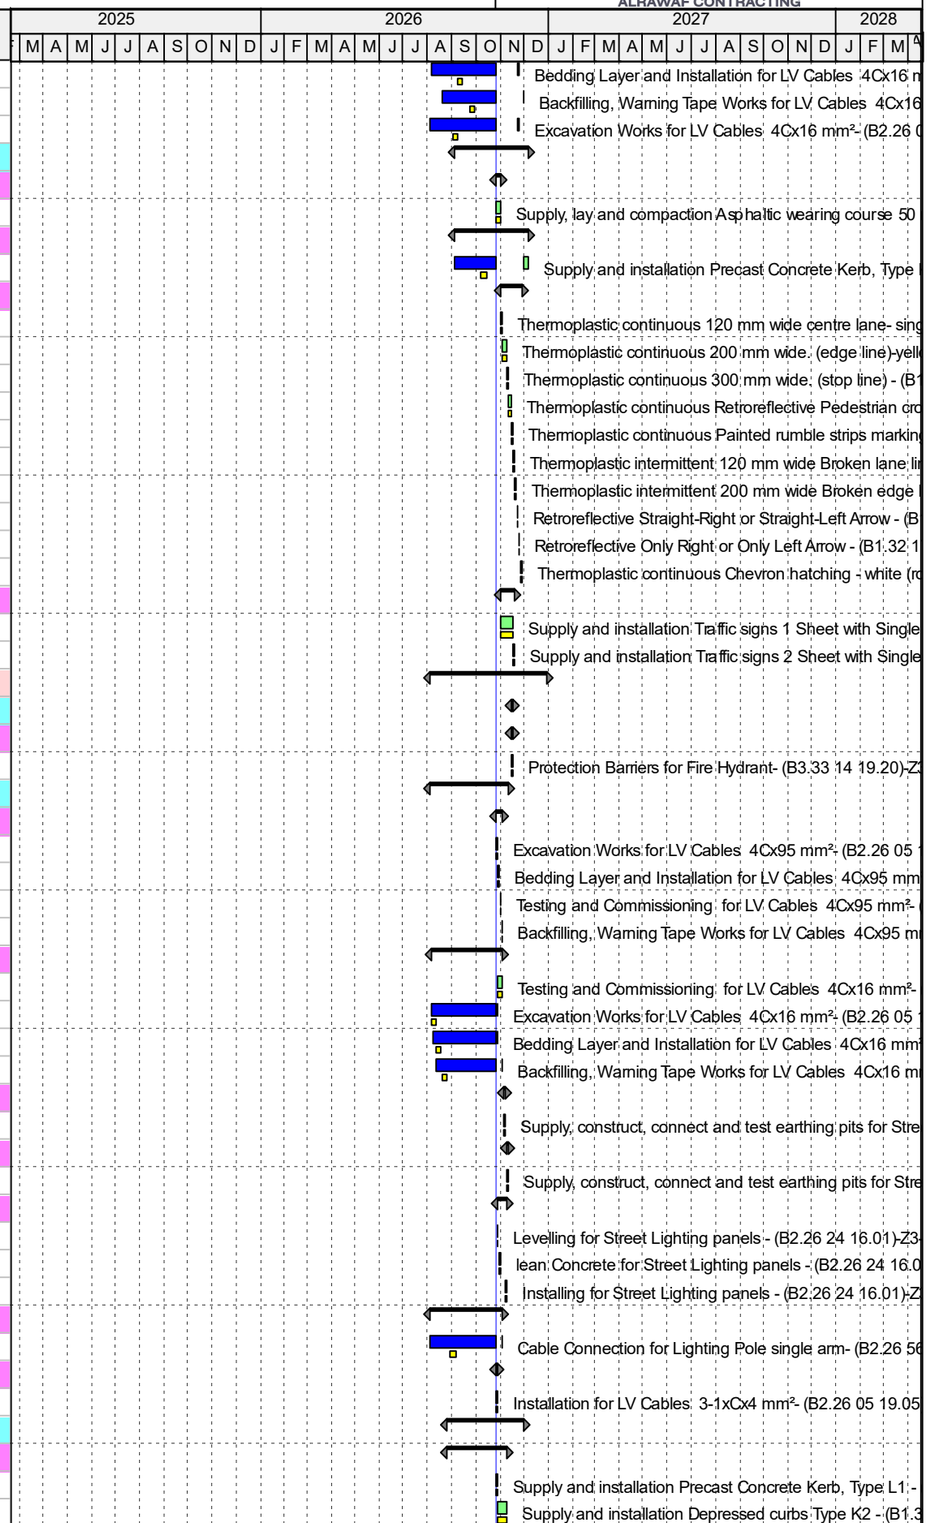


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9d	25-Aug-26 A	27-Oct-26	360d	62,734	59,597	62,734
	JDH3-02-009-R151-(RD)-Precast Interlocking Block Pavers	18d	10-Nov-26	01-Dec-26	360d	176,695	0	176,695
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18d	10-Nov-26	01-Dec-26	360d	176,695	0	176,695
	JDH3-02-009-R151-Landscape Works - LS	4d	27-Dec-26	30-Dec-26	110d	0	0	10,926
	JDH3-02-009-R151-(LS)-HDPE for Secondary Network	4d	27-Dec-26	30-Dec-26	110d	0	0	10,926
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	4d	27-Dec-26	30-Dec-26	110d	0	0	10,926
Z2		239d	02-Jun-26 A	05-Apr-27	289d	8,138,560	1,756,686	9,603,012
R07		47d	08-Sep-26 A	03-Dec-26	390d	232,536	47,846	1,044,897
	JDH3-02-009-R07-TSE Network - TSE	4d	27-Oct-26	31-Oct-26	419d	31,010	0	31,010
	JDH3-02-009-R07-(TSE)-Wash-Out Valve-100 mm on pipe dia (2	4d	27-Oct-26	31-Oct-26	419d	15,346	0	15,346
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2d	27-Oct-26	28-Oct-26	419d	13,811	0	13,811
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	29-Oct-26	31-Oct-26	419d	1,535	0	1,535
	JDH3-02-009-R07-(TSE)-Wash-Out Chamber on 225 mm dia pip	4d	27-Oct-26	31-Oct-26	419d	15,665	0	15,665
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	27-Oct-26	28-Oct-26	419d	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - (	2d	29-Oct-26	31-Oct-26	419d	4,177	0	4,177
	JDH3-02-009-R07-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
	JDH3-02-009-R07-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R07-W	2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
	JDH3-02-009-R07-Electrical Network - EL	13d	03-Nov-26	17-Nov-26	384d	196,152	0	196,152
	JDH3-02-009-R07-(EL)-MV cable trench size 1.5m wide and 80c	6d	03-Nov-26	09-Nov-26	384d	5,903	0	5,903
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	03-Nov-26	09-Nov-26	384d	5,903	0	5,903
	JDH3-02-009-R07-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7d	10-Nov-26	17-Nov-26	384d	190,249	0	190,249
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	10-Nov-26	15-Nov-26	384d	184,448	0	184,448
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	16-Nov-26	17-Nov-26	384d	5,801	0	5,801
	JDH3-02-009-R07-Street Lighting Network -SL	47d	08-Sep-26 A	03-Dec-26	390d	0	47,846	141,180
	JDH3-02-009-R07-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8d	25-Nov-26	03-Dec-26	390d	0	0	51,536
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	25-Nov-26	26-Nov-26	384d	0	0	5,154
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.:	2d	28-Nov-26	29-Nov-26	390d	0	0	38,652
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	30-Nov-26	01-Dec-26	390d	0	0	2,577
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	02-Dec-26	03-Dec-26	390d	0	0	5,154
	JDH3-02-009-R07-(SL)-Lighting Pole with single arm 12 m heigh	7d	27-Oct-26	03-Nov-26	414d	0	0	5,816
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	7d	27-Oct-26	03-Nov-26	414d	0	0	5,816
	JDH3-02-009-R07-(SL)-Earthing System for Distribution panels,S	2d	27-Oct-26	28-Oct-26	419d	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	27-Oct-26	28-Oct-26	419d	0	0	1,126
	JDH3-02-009-R07-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	412d	0	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R07-S	2d	27-Oct-26	28-Oct-26	417d	0	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2d	29-Oct-26	31-Oct-26	417d	0	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R07-S	2d	07-Nov-26	08-Nov-26	412d	0	0	7,232
	JDH3-02-009-R07-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	46d	08-Sep-26 A	02-Dec-26	384d	0	47,846	72,371
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	28-Nov-26	02-Dec-26	384d	0	0	4,021
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	08-Sep-26 A	26-Nov-26	384d	0	5,629	8,041
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	5d	10-Sep-26 A	26-Nov-26	384d	0	42,217	60,309
	JDH3-02-009-R07-Telecommunications Network - TEL	9d	27-Oct-26	05-Nov-26	414d	0	0	25,728
	JDH3-02-009-R07-(TEL)-Ducts	9d	27-Oct-26	05-Nov-26	414d	0	0	25,728
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2d	27-Oct-26	28-Oct-26	414d	0	0	3,859
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	5d	29-Oct-26	03-Nov-26	414d	0	0	19,296
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2d	04-Nov-26	05-Nov-26	414d	0	0	2,573
	JDH3-02-009-R07-Road Works - RD	20d	27-Oct-26	18-Nov-26	375d	0	0	645,453
	JDH3-02-009-R07-(RD)-Bituminous concrete wearing course 50	6d	08-Nov-26	14-Nov-26	375d	0	0	369,411
	Supply, lay and compaction Asphaltic wearing course 50 mm in	6d	08-Nov-26	14-Nov-26	375d	0	0	369,411
	JDH3-02-009-R07-(RD)-Precast Concrete Curb	5d	27-Oct-26	01-Nov-26	375d	0	0	80,561
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	375d	0	0	12,577
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3d	29-Oct-26	01-Nov-26	375d	0	0	67,984

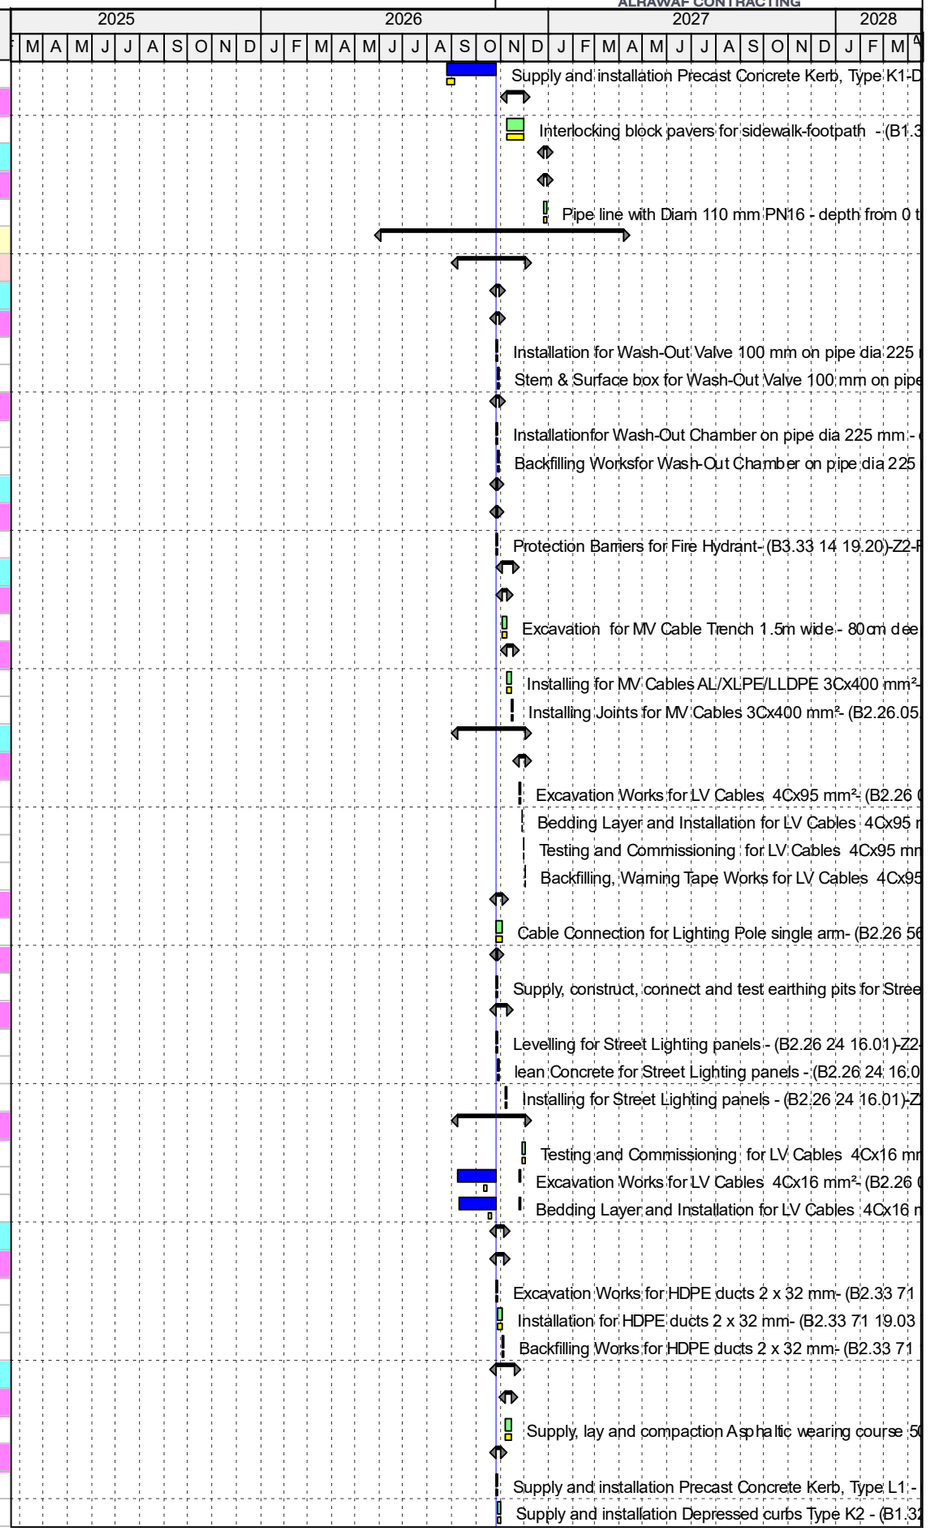


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R07-(RD)-Precast Interlocking Block Pavers	5d	02-Nov-26	07-Nov-26	375d	0	0	178,985
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	5d	02-Nov-26	07-Nov-26	375d	0	0	178,985
	JDH3-02-009-R07-(RD)-Pavement Marking	2d	15-Nov-26	16-Nov-26	375d	0	0	5,051
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	15-Nov-26	16-Nov-26	375d	0	0	5,051
	JDH3-02-009-R07-(RD)-Traffic Signage	4d	15-Nov-26	18-Nov-26	375d	0	0	11,445
	Supply and installation Traffic signs 1 Sheet with Single post - (E	4d	15-Nov-26	18-Nov-26	375d	0	0	11,445
R08		23d	27-Oct-26	22-Nov-26	400d	748,338	0	748,338
	JDH3-02-009-R08-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	396d	4,397	0	4,397
	JDH3-02-009-R08-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	396d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-W	2d	27-Oct-26	28-Oct-26	396d	4,397	0	4,397
	JDH3-02-009-R08-Electrical Network - EL	17d	29-Oct-26	17-Nov-26	396d	164,372	0	164,372
	JDH3-02-009-R08-(EL)-MV cable trench size 1.5m wide and 80c	17d	29-Oct-26	17-Nov-26	396d	8,260	0	8,260
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	29-Oct-26	04-Nov-26	396d	4,956	0	4,956
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5d	12-Nov-26	17-Nov-26	396d	3,304	0	3,304
	JDH3-02-009-R08-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	6d	05-Nov-26	11-Nov-26	396d	156,112	0	156,112
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4d	05-Nov-26	09-Nov-26	396d	150,311	0	150,311
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	10-Nov-26	11-Nov-26	396d	5,801	0	5,801
	JDH3-02-009-R08-Street Lighting Network -SL	13d	27-Oct-26	10-Nov-26	410d	21,511	0	21,511
	JDH3-02-009-R08-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	10d	27-Oct-26	07-Nov-26	413d	10,054	0	10,054
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	27-Oct-26	01-Nov-26	413d	3,351	0	3,351
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	02-Nov-26	07-Nov-26	413d	6,703	0	6,703
	JDH3-02-009-R08-(SL)-Earthing System for Distribution panels,S	2d	09-Nov-26	10-Nov-26	390d	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	09-Nov-26	10-Nov-26	390d	1,126	0	1,126
	JDH3-02-009-R08-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	412d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R08-S	2d	27-Oct-26	28-Oct-26	421d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2d	27-Oct-26	28-Oct-26	397d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R08-S	2d	07-Nov-26	08-Nov-26	390d	7,232	0	7,232
	JDH3-02-009-R08-Telecommunications Network - TEL	23d	27-Oct-26	22-Nov-26	390d	88,414	0	88,414
	JDH3-02-009-R08-(TEL)-Reinforced Concrete Duct 6-ways ducts	8d	27-Oct-26	04-Nov-26	393d	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2d	27-Oct-26	28-Oct-26	393d	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2d	29-Oct-26	31-Oct-26	393d	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2d	01-Nov-26	02-Nov-26	393d	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2d	03-Nov-26	04-Nov-26	393d	191	0	191
	JDH3-02-009-R08-(TEL)-Unreinforced Concrete Duct 6-ways duc	10d	11-Nov-26	22-Nov-26	390d	86,508	0	86,508
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3d	11-Nov-26	14-Nov-26	390d	18,537	0	18,537
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	7d	15-Nov-26	22-Nov-26	390d	67,970	0	67,970
	JDH3-02-009-R08-Road Works - RD	18d	27-Oct-26	16-Nov-26	378d	469,644	0	469,644
	JDH3-02-009-R08-(RD)-Bituminous concrete wearing course 50	5d	11-Nov-26	16-Nov-26	378d	285,288	0	285,288
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	5d	11-Nov-26	16-Nov-26	378d	285,288	0	285,288
	JDH3-02-009-R08-(RD)-Precast Concrete Curb	11d	27-Oct-26	08-Nov-26	378d	62,795	0	62,795
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	378d	9,001	0	9,001
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9d	29-Oct-26	08-Nov-26	378d	53,795	0	53,795
	JDH3-02-009-R08-(RD)-Precast Interlocking Block Pavers	2d	09-Nov-26	10-Nov-26	378d	121,560	0	121,560
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	2d	09-Nov-26	10-Nov-26	378d	121,560	0	121,560
R09		142d	11-Aug-26 A	24-Jan-27	347d	407,552	117,626	483,545
	JDH3-02-009-R09-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R09-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R09-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R09-Electrical Network - EL	76d	11-Aug-26 A	08-Nov-26	259d	200,109	49,062	200,109
	JDH3-02-009-R09-(EL)-MV cable trench size 1.5m wide and 80c	76d	11-Aug-26 A	08-Nov-26	259d	9,658	1,449	9,658
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6d	01-Nov-26	08-Nov-26	259d	3,863	0	3,863
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	11-Aug-26 A	01-Nov-26	259d	5,795	1,449	5,795
	JDH3-02-009-R09-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7d	12-Aug-26 A	01-Nov-26	259d	190,451	47,613	190,451

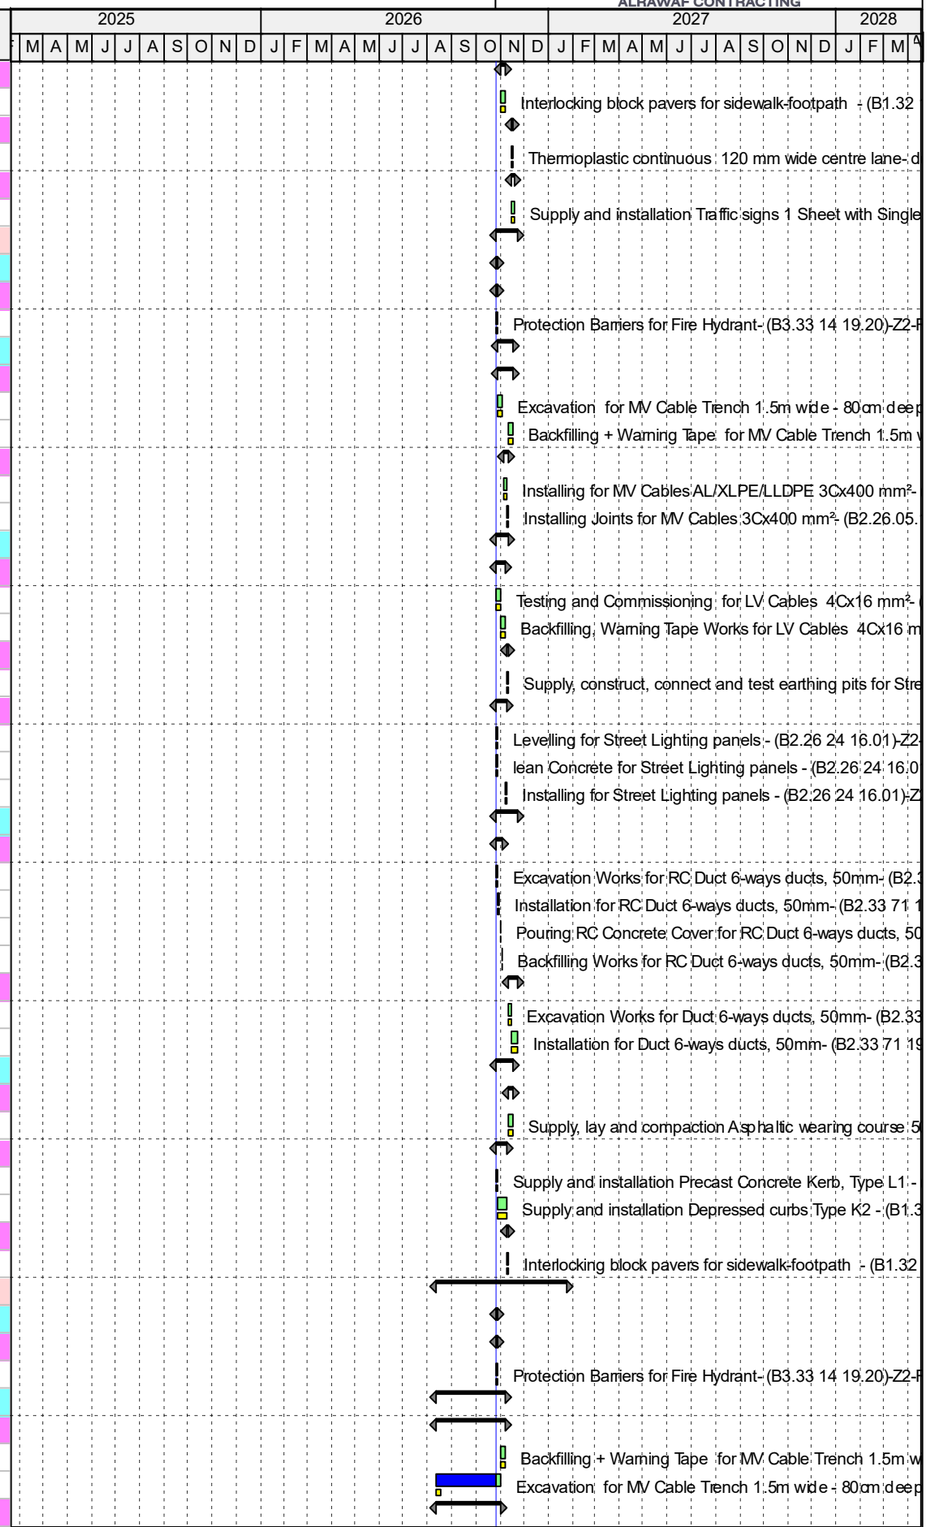

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	13-Aug-26 A	01-Nov-26	259d	8,701	2,175	8,701
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	12-Aug-26 A	01-Nov-26	259d	181,750	45,437	181,750
	JDH3-02-009-R09-Street Lighting Network -SL	40d	22-Sep-26 A	17-Nov-26	405d	63,630	32,890	63,630
	JDH3-02-009-R09-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	37d	22-Sep-26 A	17-Nov-26	332d	58,752	29,964	58,752
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	08-Nov-26	12-Nov-26	332d	2,938	0	2,938
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4d	12-Nov-26	17-Nov-26	332d	5,875	0	5,875
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4d	23-Sep-26 A	08-Nov-26	259d	44,064	26,439	44,064
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	22-Sep-26 A	08-Nov-26	259d	5,875	3,525	5,875
	JDH3-02-009-R09-(SL)-Lighting Pole with single arm 12 m heigh	8d	27-Sep-26 A	04-Nov-26	415d	4,878	2,927	4,878
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	8d	27-Sep-26 A	04-Nov-26	415d	4,878	2,927	4,878
	JDH3-02-009-R09-Telecommunications Network - TEL	12d	03-Nov-26	17-Nov-26	405d	99,289	0	99,289
	JDH3-02-009-R09-(TEL)-Unreinforced Concrete Duct 6-ways duc	12d	03-Nov-26	17-Nov-26	259d	73,561	0	73,561
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	2d	03-Nov-26	05-Nov-26	259d	11,034	0	11,034
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	4d	05-Nov-26	10-Nov-26	259d	40,458	0	40,458
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	4d	10-Nov-26	15-Nov-26	259d	14,712	0	14,712
	Backfilling Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.0	2d	15-Nov-26	17-Nov-26	259d	7,356	0	7,356
	JDH3-02-009-R09-(TEL)-Ducts	9d	05-Nov-26	16-Nov-26	406d	25,728	0	25,728
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2d	05-Nov-26	08-Nov-26	406d	3,859	0	3,859
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	5d	08-Nov-26	14-Nov-26	406d	19,296	0	19,296
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2d	14-Nov-26	16-Nov-26	406d	2,573	0	2,573
	JDH3-02-009-R09-Road Works - RD	80d	03-Sep-26 A	24-Jan-27	262d	39,638	35,674	115,631
	JDH3-02-009-R09-(RD)-Precast Concrete Curb	6d	03-Sep-26 A	17-Nov-26	259d	39,638	35,674	39,638
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	6d	03-Sep-26 A	17-Nov-26	259d	39,638	35,674	39,638
	JDH3-02-009-R09-(RD)-Pavement Marking	12d	05-Jan-27	19-Jan-27	266d	0	0	16,067
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	05-Jan-27	07-Jan-27	266d	0	0	2,830
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	07-Jan-27	10-Jan-27	266d	0	0	909
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	10-Jan-27	12-Jan-27	266d	0	0	6,596
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2d	12-Jan-27	14-Jan-27	266d	0	0	609
	Thermoplastic continuous 100 mm wide (parking separator line)	2d	14-Jan-27	17-Jan-27	266d	0	0	369
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	17-Jan-27	19-Jan-27	266d	0	0	4,753
	JDH3-02-009-R09-(RD)-Traffic Signage	16d	05-Jan-27	24-Jan-27	259d	0	0	59,926
	Supply and installation Traffic signs 1 Sheet with Single post - (E	11d	05-Jan-27	18-Jan-27	259d	0	0	35,971
	Supply and installation Traffic signs 2 Sheet with Single post - (E	5d	18-Jan-27	24-Jan-27	259d	0	0	23,955
	R11	128d	13-Jun-26 A	22-Nov-26	400d	610,091	128,351	647,881
	JDH3-02-009-R11-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R11-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R11-W	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R11-Electrical Network - EL	112d	13-Jun-26 A	03-Nov-26	417d	238,478	123,279	238,478
	JDH3-02-009-R11-(EL)-MV cable trench size 1.5m wide and 80c	17d	13-Jun-26 A	28-Oct-26	420d	8,260	6,195	8,260
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	13-Jun-26 A	28-Oct-26	417d	4,956	3,717	4,956
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3d	04-Jul-26 A	28-Oct-26	420d	3,304	2,478	3,304
	JDH3-02-009-R11-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	97d	27-Jun-26 A	31-Oct-26	418d	161,272	117,084	161,272
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	28-Oct-26	31-Oct-26	418d	5,160	0	5,160
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4d	27-Jun-26 A	28-Oct-26	417d	150,311	112,733	150,311
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	02-Jul-26 A	28-Oct-26	418d	5,801	4,351	5,801
	JDH3-02-009-R11-(EL)-RMU 33 KV	6d	27-Oct-26	03-Nov-26	417d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z2-R11-EL	2d	27-Oct-26	29-Oct-26	417d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z2-R11-EL	2d	29-Oct-26	01-Nov-26	417d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z2-R1	2d	01-Nov-26	03-Nov-26	417d	4,925	0	4,925
	JDH3-02-009-R11-Street Lighting Network -SL	61d	25-Aug-26 A	15-Nov-26	406d	178,972	5,072	198,224
	JDH3-02-009-R11-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	10d	27-Oct-26	07-Nov-26	409d	45,911	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2d	27-Oct-26	28-Oct-26	413d	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2d	29-Oct-26	31-Oct-26	413d	3,401	0	3,401

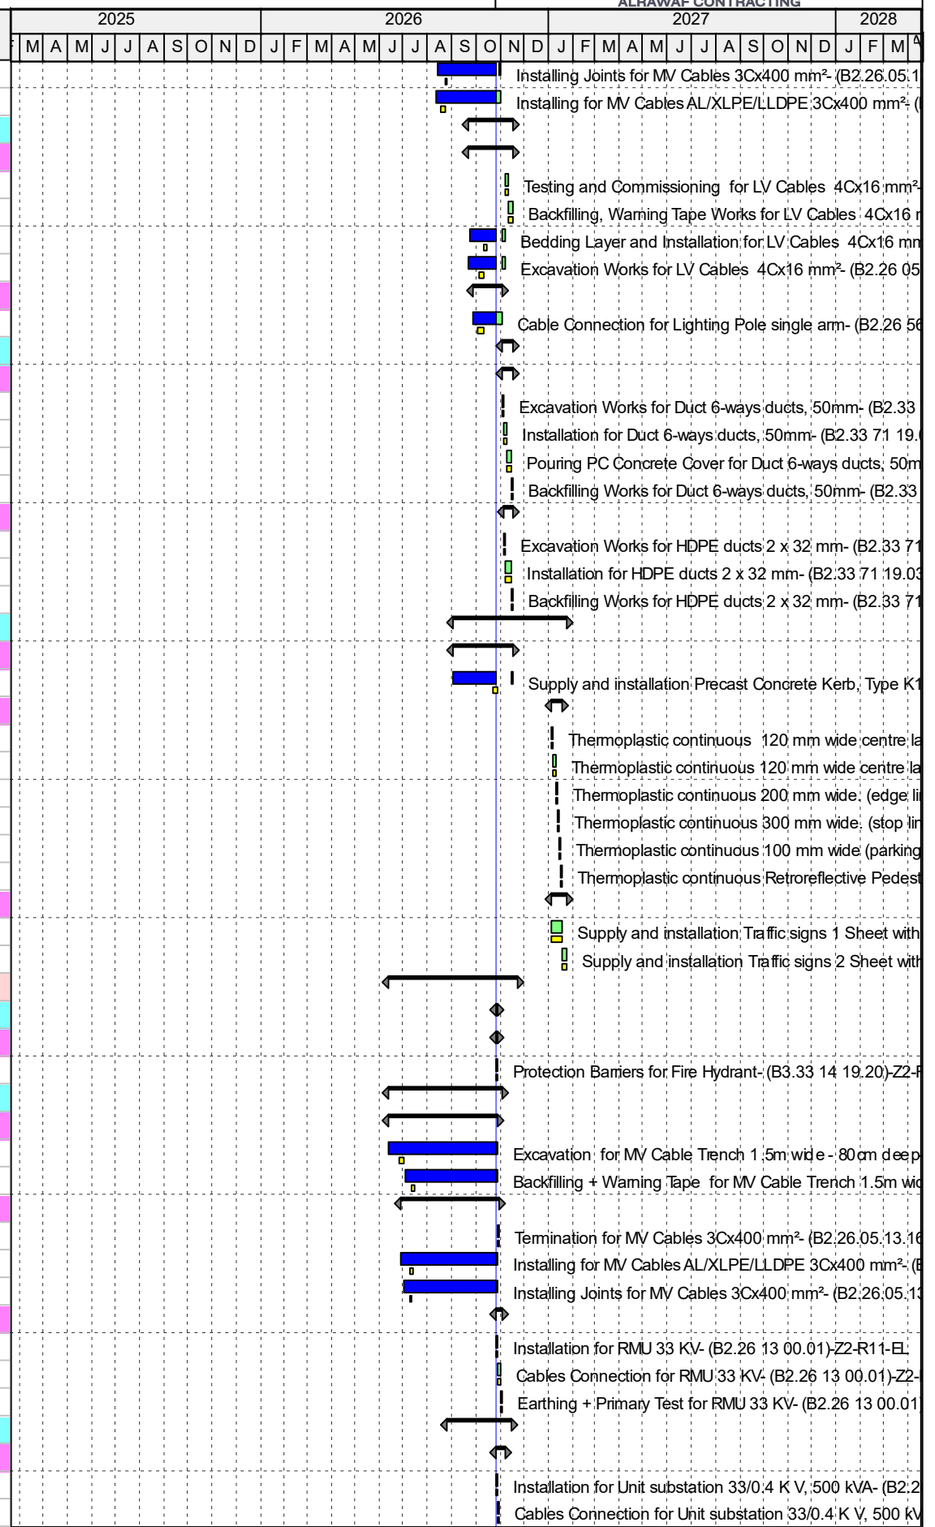


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2d	05-Nov-26	07-Nov-26	409d	1,700	0	3,401
	JDH3-02-009-R11-(SL)-RMU 33 KV	14d	27-Oct-26	11-Nov-26	409d	54,621	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z2-R11-SL	2d	27-Oct-26	28-Oct-26	417d	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z2-R11-SL	2d	29-Oct-26	31-Oct-26	417d	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z2-R1	2d	10-Nov-26	11-Nov-26	409d	0	0	4,202
	JDH3-02-009-R11-(SL)- LV Cables -Aluminium, 4Cx185mm²,AL/	8d	27-Oct-26	04-Nov-26	409d	1,212	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2d	27-Oct-26	28-Oct-26	409d	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2d	29-Oct-26	31-Oct-26	409d	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2	2d	01-Nov-26	02-Nov-26	409d	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2d	03-Nov-26	04-Nov-26	409d	121	0	121
	JDH3-02-009-R11-(SL)- LV Cables -Copper, 4Cx95mm²,Cu/XLPE	10d	29-Oct-26	09-Nov-26	409d	42,314	0	47,015
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	29-Oct-26	31-Oct-26	411d	4,702	0	4,702
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	01-Nov-26	02-Nov-26	411d	35,261	0	35,261
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	03-Nov-26	04-Nov-26	411d	2,351	0	2,351
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	08-Nov-26	09-Nov-26	409d	0	0	4,702
	JDH3-02-009-R11-(SL)- LV Cables -Copper, 3x1Cx50mm²,Cu/XL	2d	01-Nov-26	02-Nov-26	415d	760	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z2-F	2d	01-Nov-26	02-Nov-26	415d	760	0	1,520
	JDH3-02-009-R11-(SL)- LV Cables -Copper, 4Cx16mm²,Cu/XLPE	49d	25-Aug-26 A	01-Nov-26	396d	3,382	5,072	10,145
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	27-Oct-26	01-Nov-26	396d	3,382	0	3,382
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	25-Aug-26 A	01-Nov-26	396d	0	5,072	6,763
	JDH3-02-009-R11-(SL)-Earthing System for Distribution panels,S	2d	14-Nov-26	15-Nov-26	386d	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	14-Nov-26	15-Nov-26	386d	0	0	1,126
	JDH3-02-009-R11-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	386d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R11-S	2d	27-Oct-26	28-Oct-26	391d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2d	29-Oct-26	31-Oct-26	391d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R11-S	2d	07-Nov-26	08-Nov-26	386d	7,232	0	7,232
	JDH3-02-009-R11-(SL)- LV Distribution Panel Main: 100A, MCCB	11d	29-Oct-26	10-Nov-26	386d	18,369	0	18,369
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z2-R11-S	2d	29-Oct-26	31-Oct-26	391d	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z2-F	2d	01-Nov-26	02-Nov-26	391d	3,674	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z2-R11-S	2d	09-Nov-26	10-Nov-26	386d	12,858	0	12,858
	JDH3-02-009-R11-(SL)-KWH meter mounting frame	2d	11-Nov-26	12-Nov-26	386d	2,072	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z2-R11-SL	2d	11-Nov-26	12-Nov-26	386d	2,072	0	2,072
	JDH3-02-009-R11-Telecommunications Network -TEL	12d	05-Nov-26	18-Nov-26	400d	1,907	0	20,444
	JDH3-02-009-R11-(TEL)-Reinforced Concrete Duct 6-ways ducts	8d	05-Nov-26	14-Nov-26	404d	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2d	05-Nov-26	07-Nov-26	393d	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2d	08-Nov-26	09-Nov-26	404d	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2d	10-Nov-26	11-Nov-26	404d	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2d	12-Nov-26	14-Nov-26	404d	191	0	191
	JDH3-02-009-R11-(TEL)-Unreinforced Concrete Duct 6-ways duc	3d	16-Nov-26	18-Nov-26	386d	0	0	18,537
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3d	16-Nov-26	18-Nov-26	386d	0	0	18,537
	JDH3-02-009-R11-Road Works - RD	23d	27-Oct-26	22-Nov-26	363d	186,337	0	186,337
	JDH3-02-009-R11-(RD)-Precast Concrete Curb	11d	27-Oct-26	08-Nov-26	363d	63,413	0	63,413
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	363d	9,604	0	9,604
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9d	29-Oct-26	08-Nov-26	363d	53,809	0	53,809
	JDH3-02-009-R11-(RD)-Precast Interlocking Block Pavers	12d	09-Nov-26	22-Nov-26	363d	122,925	0	122,925
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12d	09-Nov-26	22-Nov-26	363d	122,925	0	122,925
	R12	19d	27-Oct-26	17-Nov-26	404d	614,585	0	614,585
	JDH3-02-009-R12-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R12-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R12-W	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R12-Street Lighting Network -SL	5d	27-Oct-26	01-Nov-26	418d	6,141	0	6,141
	JDH3-02-009-R12-(SL)-Earthing System for Streetlighting feede	3d	27-Oct-26	29-Oct-26	420d	2,555	0	2,555
	Supply, construct, connect and test earthing pits for Street Light	3d	27-Oct-26	29-Oct-26	420d	2,555	0	2,555

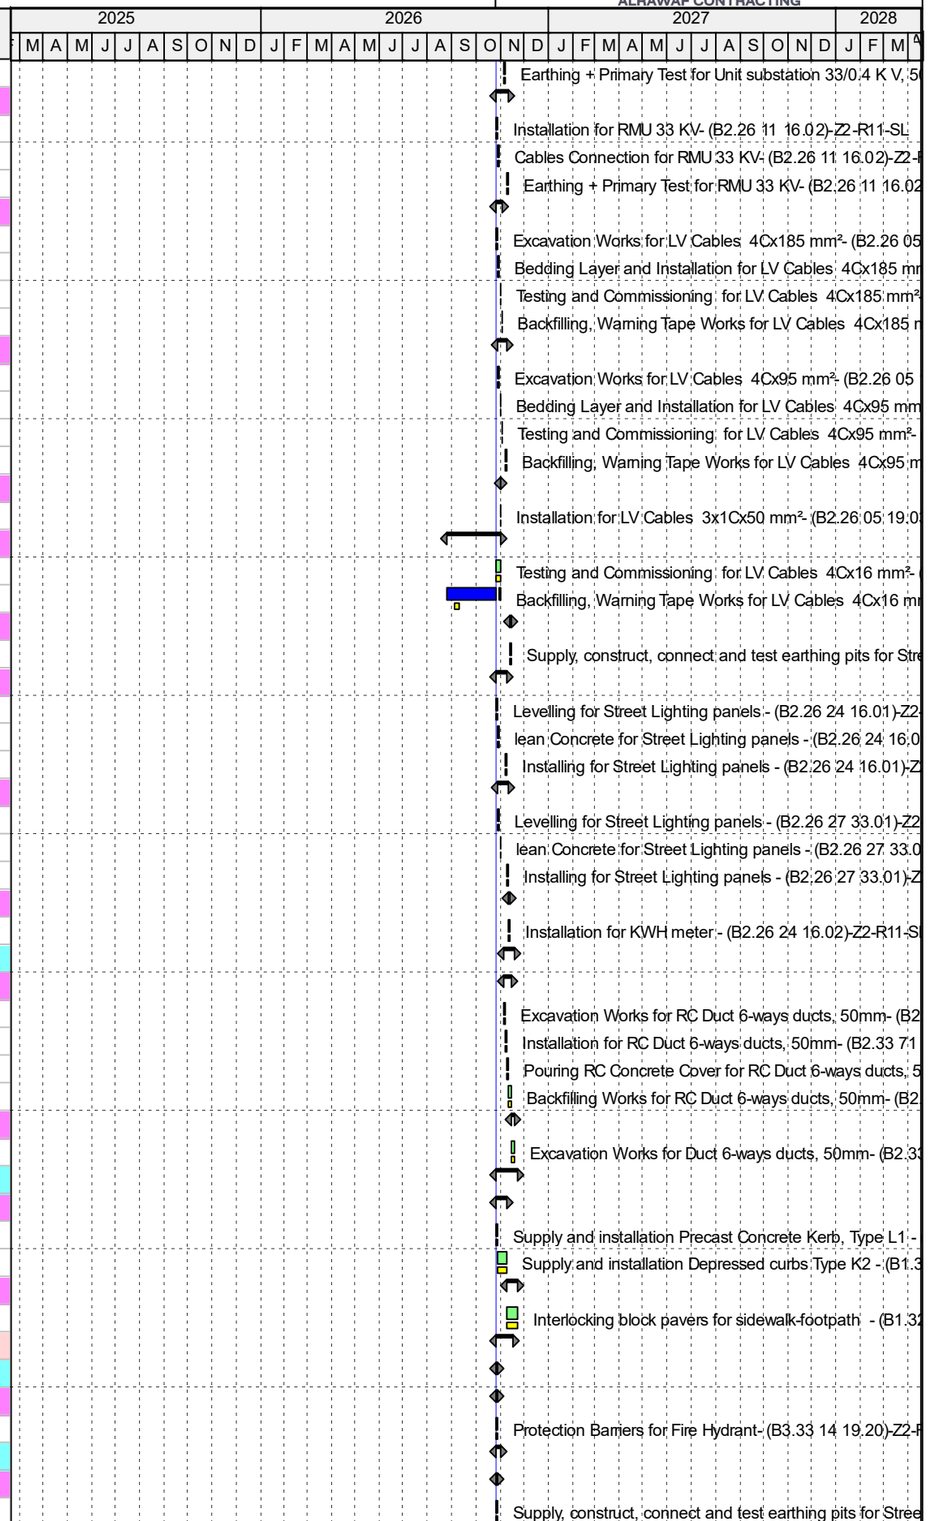


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R12-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	5d	27-Oct-26	01-Nov-26	418d	3,586	0	3,586
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	27-Oct-26	01-Nov-26	418d	3,586	0	3,586
	JDH3-02-009-R12-Telecommunications Network - TEL	9d	08-Nov-26	17-Nov-26	402d	113,131	0	113,131
	JDH3-02-009-R12-(TEL)-Reinforced Concrete Duct 6-ways ducts	8d	08-Nov-26	16-Nov-26	403d	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2d	08-Nov-26	09-Nov-26	402d	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2d	10-Nov-26	11-Nov-26	403d	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2d	12-Nov-26	14-Nov-26	403d	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2d	15-Nov-26	16-Nov-26	403d	191	0	191
	JDH3-02-009-R12-(TEL)-Unreinforced Concrete Duct 6-ways duc	7d	10-Nov-26	17-Nov-26	402d	111,224	0	111,224
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3d	10-Nov-26	12-Nov-26	402d	18,537	0	18,537
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	2d	14-Nov-26	15-Nov-26	402d	67,970	0	67,970
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	2d	16-Nov-26	17-Nov-26	402d	24,716	0	24,716
	JDH3-02-009-R12-Road Works - RD	19d	27-Oct-26	17-Nov-26	383d	490,916	0	490,916
	JDH3-02-009-R12-(RD)-Bituminous concrete wearing course 50	5d	05-Nov-26	10-Nov-26	383d	285,326	0	285,326
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	05-Nov-26	10-Nov-26	383d	285,326	0	285,326
	JDH3-02-009-R12-(RD)-Precast Concrete Curb	5d	27-Oct-26	01-Nov-26	383d	63,766	0	63,766
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	27-Oct-26	28-Oct-26	383d	9,920	0	9,920
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3d	29-Oct-26	01-Nov-26	383d	53,846	0	53,846
	JDH3-02-009-R12-(RD)-Precast Interlocking Block Pavers	3d	02-Nov-26	04-Nov-26	383d	122,836	0	122,836
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	3d	02-Nov-26	04-Nov-26	383d	122,836	0	122,836
	JDH3-02-009-R12-(RD)-Pavement Marking	6d	11-Nov-26	17-Nov-26	383d	6,136	0	6,136
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	11-Nov-26	12-Nov-26	383d	4,338	0	4,338
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	14-Nov-26	15-Nov-26	383d	364	0	364
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	16-Nov-26	17-Nov-26	383d	1,435	0	1,435
	JDH3-02-009-R12-(RD)-Traffic Signage	4d	11-Nov-26	15-Nov-26	383d	12,852	0	12,852
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2d	11-Nov-26	12-Nov-26	383d	3,270	0	3,270
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2d	14-Nov-26	15-Nov-26	383d	9,582	0	9,582
R131		125d	04-Aug-26 A	30-Dec-26	367d	730,438	246,580	733,176
	JDH3-02-009-R131-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R131-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R131-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R131-Electrical Network - EL	20d	27-Oct-26	18-Nov-26	391d	265,111	0	265,111
	JDH3-02-009-R131-(EL)-MV cable trench size 1.5m wide and 80	20d	27-Oct-26	18-Nov-26	391d	11,379	0	11,379
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	27-Oct-26	02-Nov-26	384d	6,828	0	6,828
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6d	12-Nov-26	18-Nov-26	391d	4,552	0	4,552
	JDH3-02-009-R131-(EL)-MV cables AL/XLPE/LLDPE Unarmored	8d	03-Nov-26	11-Nov-26	391d	253,732	0	253,732
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	6d	03-Nov-26	09-Nov-26	391d	239,230	0	239,230
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	10-Nov-26	11-Nov-26	391d	14,502	0	14,502
	JDH3-02-009-R131-Street Lighting Network -SL	41d	04-Aug-26 A	02-Dec-26	391d	197,560	138,292	197,560
	JDH3-02-009-R131-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLP	10d	17-Sep-26 A	18-Nov-26	391d	65,230	45,661	65,230
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	19-Sep-26 A	18-Nov-26	391d	57,555	40,289	57,555
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	17-Sep-26 A	18-Nov-26	391d	7,674	5,372	7,674
	JDH3-02-009-R131-(SL)-Lighting Pole with single arm 12 m heig	22d	04-Aug-26 A	18-Nov-26	394d	114,061	79,843	114,061
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	4d	04-Aug-26 A	18-Nov-26	394d	12,006	8,404	12,006
	Installation of RC foundation for Lighting Pole single arm- (B2.2(	5d	05-Aug-26 A	18-Nov-26	394d	12,006	8,404	12,006
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	4d	06-Aug-26 A	18-Nov-26	394d	12,006	8,404	12,006
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	9d	08-Aug-26 A	18-Nov-26	394d	78,042	54,629	78,042
	JDH3-02-009-R131-(SL)-Street Lighting(LED) Luminaire comple	10d	08-Aug-26 A	02-Dec-26	391d	18,270	12,789	18,270
	Installation for Lighting(LED) Luminaire 114 WATT- (B2.26.56.1	3d	08-Aug-26 A	16-Nov-26	406d	14,616	10,231	14,616
	Cable Connection for Lighting(LED) Luminaire 114 WATT- (B2.	3d	08-Aug-26 A	02-Dec-26	391d	3,654	2,558	3,654
	JDH3-02-009-R131-Telecommunications Network - TEL	77d	04-Aug-26 A	04-Nov-26	415d	95,189	56,403	95,189
	JDH3-02-009-R131-(TEL)-Ducts	8d	27-Oct-26	04-Nov-26	415d	19,984	0	19,984
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2d	27-Oct-26	28-Oct-26	415d	2,998	0	2,998

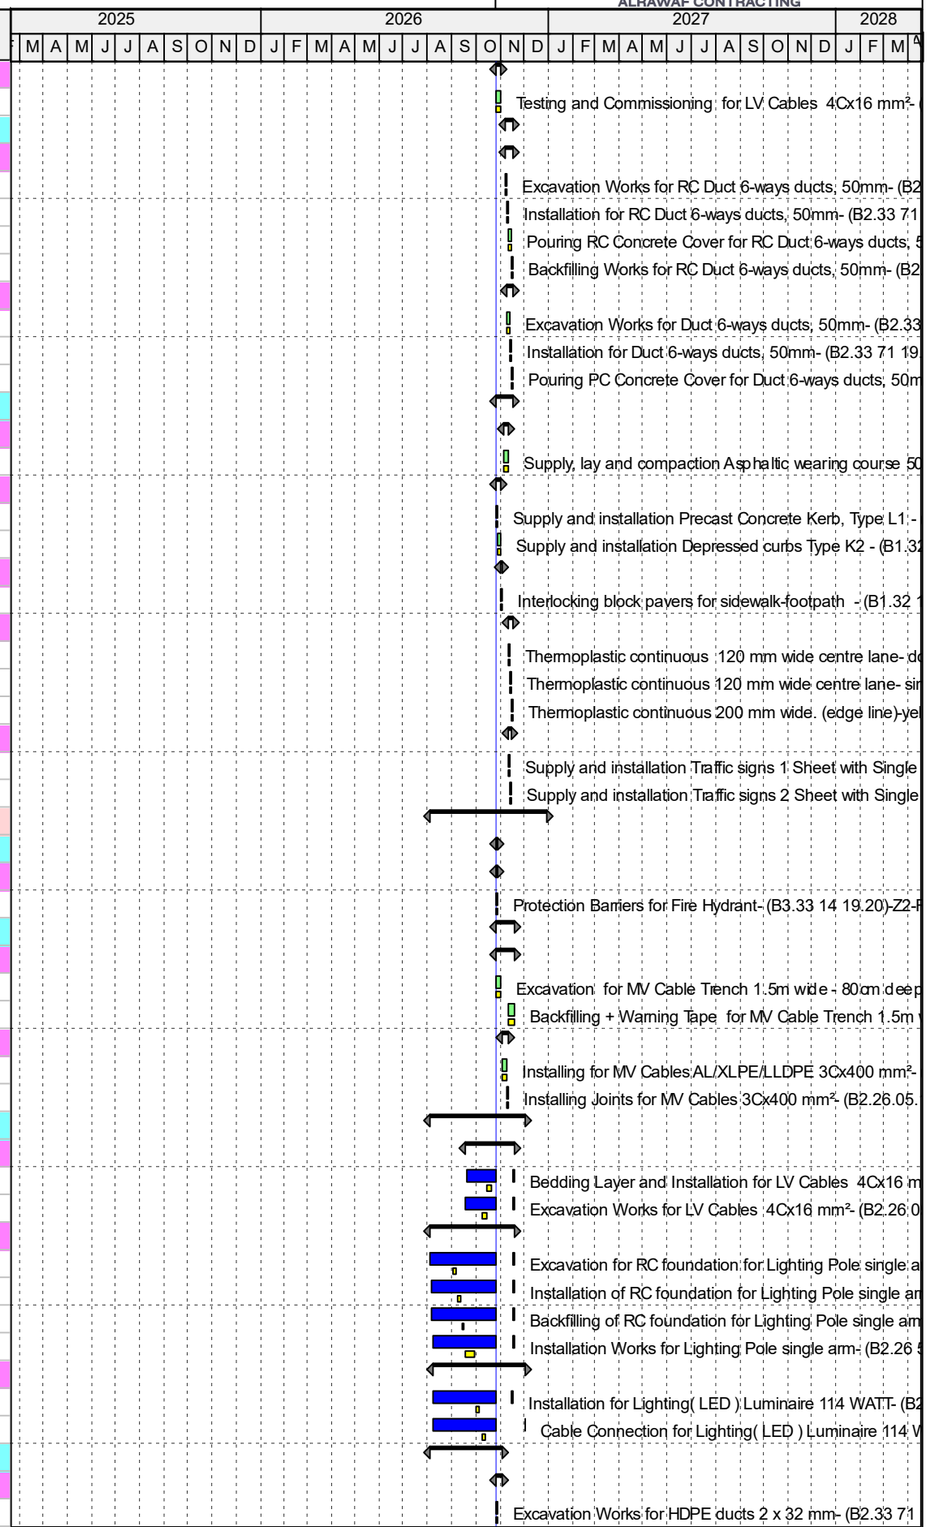


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	4d	29-Oct-26	02-Nov-26	415d	14,988	0	14,988
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2d	03-Nov-26	04-Nov-26	415d	1,998	0	1,998
	JDH3-02-009-R131-(TEL)-Manhole Type 1	8d	04-Aug-26 A	04-Nov-26	415d	41,021	30,765	41,021
	Backfilling Works for MH Type 1 Dim 2000*1000*1000 mm- (B2.	2d	06-Aug-26 A	04-Nov-26	415d	4,102	3,077	4,102
	Excavation and Bedding Works for MH Type 1 Dim 2000*1000*	2d	04-Aug-26 A	28-Oct-26	421d	6,153	4,615	6,153
	Installation for MH Type 1 Dim 2000*1000*1000 mm- (B2.33.71	2d	05-Aug-26 A	28-Oct-26	421d	30,765	23,074	30,765
	JDH3-02-009-R131-(TEL)-Manhole Type 2	8d	04-Aug-26 A	04-Nov-26	415d	34,184	25,638	34,184
	Installation for MH Type 2 Dim 2000*1000*1000 mm- (B2.33.71	2d	05-Aug-26 A	28-Oct-26	421d	25,638	19,228	25,638
	Backfilling Works for MH Type 2 Dim 2000*1000*1000 mm- (B2.	2d	06-Aug-26 A	04-Nov-26	415d	3,418	2,564	3,418
	Excavation and Bedding Works for MH Type 2 Dim 2000*1000*	2d	04-Aug-26 A	28-Oct-26	421d	5,128	3,846	5,128
	JDH3-02-009-R131-Road Works - RD	103d	01-Sep-26 A	30-Dec-26	351d	167,693	51,885	170,431
	JDH3-02-009-R131-(RD)-Precast Concrete Curb	70d	01-Sep-26 A	22-Nov-26	308d	167,693	51,885	167,693
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5d	29-Oct-26	04-Nov-26	308d	37,285	0	37,285
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	11d	09-Nov-26	22-Nov-26	308d	69,521	0	69,521
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	04-Nov-26	09-Nov-26	308d	3,238	0	3,238
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8d	01-Sep-26 A	29-Oct-26	308d	57,650	51,885	57,650
	JDH3-02-009-R131-(RD)-Pavement Marking	6d	23-Dec-26	30-Dec-26	351d	0	0	2,738
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2d	23-Dec-26	26-Dec-26	351d	0	0	275
	Thermoplastic continuous 100 mm wide (parking separator line)	2d	26-Dec-26	28-Dec-26	351d	0	0	681
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	28-Dec-26	30-Dec-26	351d	0	0	1,782
R132		205d	02-Jun-26 A	28-Feb-27	317d	328,379	178,126	356,423
	JDH3-02-009-R132-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R132-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R132-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R132-Electrical Network - EL	71d	02-Jun-26 A	24-Nov-26	317d	184,680	58,894	190,191
	JDH3-02-009-R132-(EL)-MV cable trench size 1.5m wide and 80	71d	02-Jun-26 A	24-Nov-26	317d	3,674	4,593	9,185
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6d	02-Jun-26 A	24-Nov-26	317d	0	2,756	5,511
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3d	18-Aug-26 A	24-Nov-26	317d	3,674	1,837	3,674
	JDH3-02-009-R132-(EL)-MV cables AL/XLPE/LLDPE Unarmored	7d	13-Aug-26 A	24-Nov-26	317d	181,006	54,302	181,006
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	13-Aug-26 A	24-Nov-26	317d	172,305	51,691	172,305
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	15-Aug-26 A	24-Nov-26	317d	8,701	2,610	8,701
	JDH3-02-009-R132-Street Lighting Network -SL	41d	16-Sep-26 A	08-Dec-26	384d	75,616	59,194	75,616
	JDH3-02-009-R132-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLP	19d	16-Sep-26 A	08-Dec-26	382d	59,656	53,848	59,656
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4d	23-Sep-26 A	08-Dec-26	382d	6,280	3,140	6,280
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	4d	17-Sep-26 A	28-Nov-26	387d	47,097	44,742	47,097
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	16-Sep-26 A	28-Nov-26	387d	6,280	5,966	6,280
	JDH3-02-009-R132-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	410d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R132-	2d	27-Oct-26	28-Oct-26	415d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2d	29-Oct-26	31-Oct-26	415d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R132-	2d	07-Nov-26	08-Nov-26	410d	7,232	0	7,232
	JDH3-02-009-R132-(SL)-Lighting Pole with single arm 12 m heig	6d	22-Sep-26 A	02-Nov-26	415d	5,628	5,347	5,628
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6d	22-Sep-26 A	02-Nov-26	415d	5,628	5,347	5,628
	JDH3-02-009-R132-Road Works - RD	130d	25-Aug-26 A	25-Feb-27	317d	63,197	60,038	67,346
	JDH3-02-009-R132-(RD)-Precast Concrete Curb	9d	25-Aug-26 A	23-Nov-26	317d	63,197	60,038	63,197
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9d	25-Aug-26 A	23-Nov-26	317d	63,197	60,038	63,197
	JDH3-02-009-R132-(RD)-Pavement Marking	6d	17-Feb-27	25-Feb-27	317d	0	0	4,148
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z2-R132-RL	2d	17-Feb-27	20-Feb-27	317d	0	0	3,004
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2d	20-Feb-27	23-Feb-27	317d	0	0	858
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.(	2d	23-Feb-27	25-Feb-27	317d	0	0	286
	JDH3-02-009-R132-Landscape Works - LS	2d	25-Feb-27	28-Feb-27	317d	0	0	18,385
	JDH3-02-009-R132-(LS)-HDPE for Secondary Network	2d	25-Feb-27	28-Feb-27	317d	0	0	18,385
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	2d	25-Feb-27	28-Feb-27	317d	0	0	18,385
R14		187d	25-Aug-26 A	05-Apr-27	289d	4,466,642	1,038,156	4,974,168

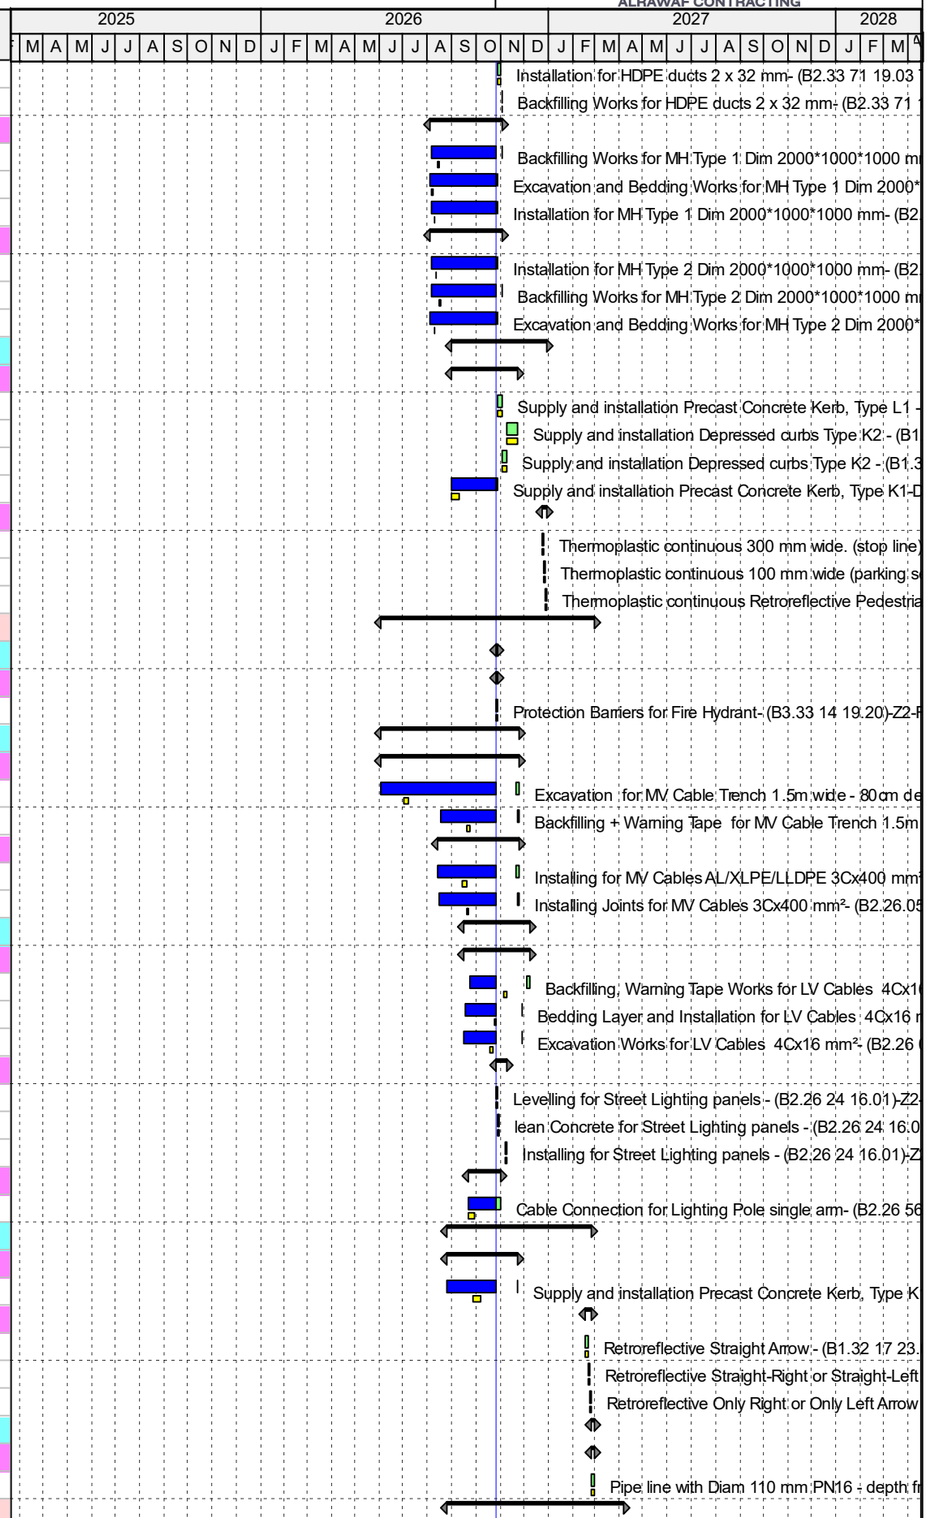


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R14-Catch Basins (Storm Network) - ST	10d	27-Oct-26	07-Nov-26	413d	39,262	0	39,262
	JDH3-02-009-R14-(ST)-Single Catch Basin Works	10d	27-Oct-26	07-Nov-26	413d	16,848	0	16,848
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5d	27-Oct-26	01-Nov-26	413d	11,232	0	11,232
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z2-R14-ST	5d	02-Nov-26	07-Nov-26	413d	5,616	0	5,616
	JDH3-02-009-R14-(ST)-Double Catch Basin Works	4d	27-Oct-26	31-Oct-26	414d	22,414	0	22,414
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	414d	14,942	0	14,942
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z2-R14-S	2d	29-Oct-26	31-Oct-26	414d	7,471	0	7,471
	JDH3-02-009-R14-TSE Network - TSE	8d	27-Oct-26	04-Nov-26	300d	91,453	0	91,453
	JDH3-02-009-R14-(TSE)-Butterfly Valve-300 mm on pipe dia (315	4d	29-Oct-26	02-Nov-26	300d	48,390	0	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2d	29-Oct-26	31-Oct-26	300d	43,551	0	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	01-Nov-26	02-Nov-26	300d	4,839	0	4,839
	JDH3-02-009-R14-(TSE)-Valve Chamber on 315 mm dia pipeline	8d	27-Oct-26	04-Nov-26	300d	43,064	0	43,064
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2d	27-Oct-26	28-Oct-26	300d	6,460	0	6,460
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	29-Oct-26	31-Oct-26	300d	4,306	0	4,306
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	01-Nov-26	02-Nov-26	300d	23,685	0	23,685
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	03-Nov-26	04-Nov-26	300d	8,613	0	8,613
	JDH3-02-009-R14-Potable Water Network - WT	57d	01-Sep-26 A	07-Nov-26	413d	228,708	32,436	228,708
	JDH3-02-009-R14-(WT)-Butterfly Valve-400 mm on pipe dia (400)	8d	16-Sep-26 A	28-Oct-26	399d	78,222	25,813	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2d	16-Sep-26 A	28-Oct-26	400d	70,400	23,232	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2d	24-Sep-26 A	28-Oct-26	399d	7,822	2,581	7,822
	JDH3-02-009-R14-(WT)-Valve Chamber on 400 mm dia pipeline	51d	01-Sep-26 A	31-Oct-26	399d	43,007	6,623	43,007
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	29-Oct-26	31-Oct-26	399d	8,601	0	8,601
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	16-Sep-26 A	28-Oct-26	399d	23,654	3,075	23,654
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	03-Sep-26 A	28-Oct-26	400d	4,301	1,419	4,301
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	01-Sep-26 A	28-Oct-26	400d	6,451	2,129	6,451
	JDH3-02-009-R14-(WT)-Fire Hydrant	10d	27-Oct-26	07-Nov-26	413d	107,479	0	107,479
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	27-Oct-26	28-Oct-26	413d	10,748	0	10,748
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2d	29-Oct-26	31-Oct-26	413d	21,496	0	21,496
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2d	01-Nov-26	02-Nov-26	413d	32,244	0	32,244
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2d	03-Nov-26	04-Nov-26	413d	37,618	0	37,618
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-W	2d	05-Nov-26	07-Nov-26	413d	5,374	0	5,374
	JDH3-02-009-R14-Street Lighting Network -SL	8d	27-Oct-26	04-Nov-26	415d	2,161	0	2,161
	JDH3-02-009-R14-(SL)-Road Crossing Ducts 2 way PVC 2 × 100	8d	27-Oct-26	04-Nov-26	415d	2,161	0	2,161
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	2d	27-Oct-26	28-Oct-26	318d	432	0	432
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z2-R	2d	29-Oct-26	31-Oct-26	326d	1,297	0	1,297
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	2d	01-Nov-26	02-Nov-26	326d	324	0	324
	Testing and Backfilling Works for PVC Pipes 2×100mm- (B2.33	2d	03-Nov-26	04-Nov-26	415d	108	0	108
	JDH3-02-009-R14-Road Works - RD	175d	25-Aug-26 A	22-Mar-27	301d	4,105,058	1,005,720	4,139,250
	JDH3-02-009-R14-(RD)-Aggregate Base Course	2d	25-Aug-26 A	27-Oct-26	289d	307,847	246,278	307,847
	Supply, lay and compaction Aggregate base course compacted	2d	25-Aug-26 A	27-Oct-26	289d	307,847	246,278	307,847
	JDH3-02-009-R14-(RD)-Bituminous base course 200 mm Two La	46d	09-Sep-26 A	03-Nov-26	351d	3,797,211	759,442	3,797,211
	Supply, lay and Asphaltic base course including tack Coat (RC2)	5d	28-Oct-26	03-Nov-26	351d	1,898,605	0	1,898,605
	Supply, lay and Asphaltic base course including Prime Coat (MC	2d	09-Sep-26 A	28-Oct-26	289d	1,898,605	759,442	1,898,605
	JDH3-02-009-R14-(RD)-Pavement Marking	10d	03-Mar-27	17-Mar-27	301d	0	0	28,526
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	03-Mar-27	04-Mar-27	301d	0	0	171
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	4d	06-Mar-27	13-Mar-27	301d	0	0	21,403
	Thermoplastic continuous Painted rumble strips marking (300m	2d	14-Mar-27	15-Mar-27	301d	0	0	3,158
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	16-Mar-27	17-Mar-27	301d	0	0	3,794
	JDH3-02-009-R14-(RD)-Traffic Signage	4d	18-Mar-27	22-Mar-27	301d	0	0	5,666
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2d	18-Mar-27	20-Mar-27	301d	0	0	3,270
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2d	21-Mar-27	22-Mar-27	301d	0	0	2,396
	JDH3-02-009-R14-Landscape Works - LS	24d	06-Mar-27	05-Apr-27	283d	0	0	473,334
	JDH3-02-009-R14-(LS)-Ground Cover and Shrubs	8d	14-Mar-27	22-Mar-27	283d	0	0	395,915

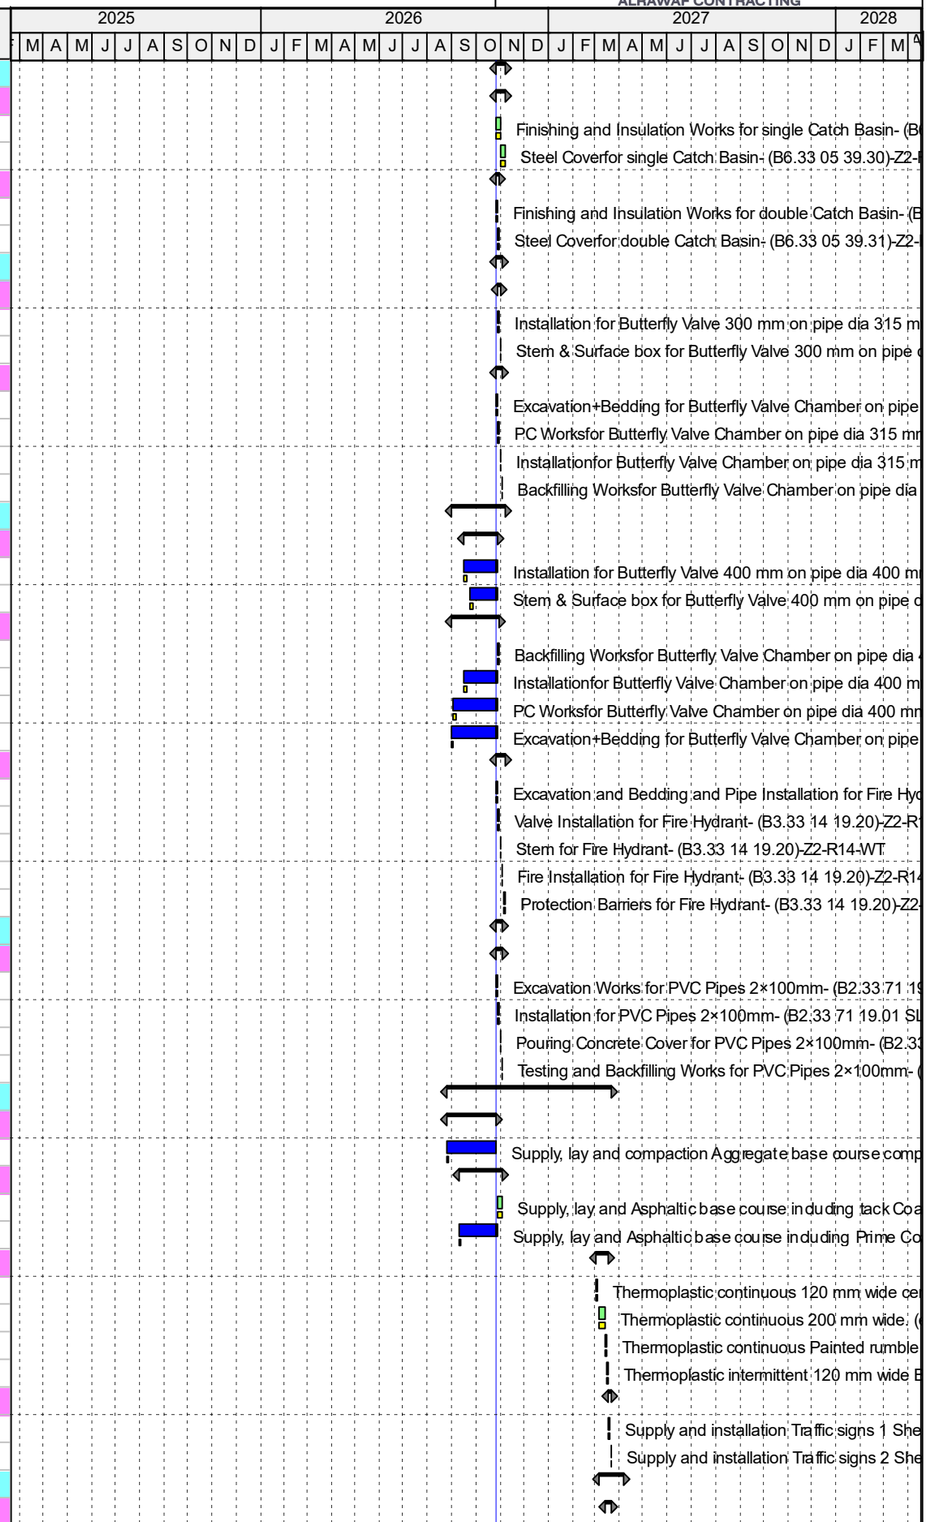


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Ref S1, Bougainvillea glabra pink - (B7.32 92 00.01)-Z2-R14-LS	8d	14-Mar-27	22-Mar-27	283d	0	0	112,831
	Ref S2, Dodonae viscosa - (B7.32 92 00.02)-Z2-R14-LS	8d	14-Mar-27	22-Mar-27	283d	0	0	120,838
	Ref S3, Leucophyllum frutescens - (B7.32 92 00.03)-Z2-R14-LS	6d	14-Mar-27	20-Mar-27	283d	0	0	73,671
	Ref G1, Ruellia ciliosa - (B7.32 92 00.04)-Z2-R14-LS	8d	14-Mar-27	22-Mar-27	283d	0	0	88,575
	JDH3-02-009-R14-(LS)-Trees	4d	06-Mar-27	13-Mar-27	283d	0	0	22,653
	Ref. COR SEB (Cordia Sebestena) - (B7.32 93 00.05)-Z2-R14-L	4d	06-Mar-27	13-Mar-27	283d	0	0	22,653
	JDH3-02-009-R14-(LS)-Design, Delive, install, wiring, control, pr	20d	14-Mar-27	05-Apr-27	283d	0	0	54,766
	Installation of 1" quick coupler valve - (B7.33.14.19.03)-Z2-R14	3d	21-Mar-27	23-Mar-27	283d	0	0	3,152
	LDPE plain pipes - (B7.32.80.00.01)-Z2-R14-LS	6d	14-Mar-27	20-Mar-27	283d	0	0	2,568
	Online pressure compensating emitters - (B7.32.80.00.02)-Z2-R	8d	28-Mar-27	05-Apr-27	283d	0	0	2,628
	Low density polyethylene tubing - (B7.32.80.00.03)-Z2-R14-LS	8d	14-Mar-27	22-Mar-27	283d	0	0	44,615
	Decoder cables 12 AWG between valves and controllers - (B7.3	6d	21-Mar-27	27-Mar-27	283d	0	0	1,803
Z1		168d	14-Jul-26 A	18-Feb-27	325d	2,172,889	1,278,816	4,729,762
R01		71d	25-Aug-26 A	16-Nov-26	405d	265,226	98,131	524,289
JDH3-02-009-R01-Storm Network - ST		8d	27-Oct-26	04-Nov-26	409d	3,913	0	3,913
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2d	27-Oct-26	28-Oct-26	409d	1,402	0	1,402
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2d	27-Oct-26	28-Oct-26	409d	1,402	0	1,402
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2d	29-Oct-26	31-Oct-26	409d	485	0	485
	Steel Coverfor MH 1200 mm - depth from 3.01 to 3.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	409d	485	0	485
JDH3-02-009-R01-(ST)-MH Works (1500) mm diameter depth fro		2d	01-Nov-26	02-Nov-26	409d	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	409d	1,003	0	1,003
JDH3-02-009-R01-(ST)-MH Works (1500) mm diameter depth fro		2d	27-Oct-26	28-Oct-26	413d	625	0	625
	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2d	27-Oct-26	28-Oct-26	413d	625	0	625
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2d	03-Nov-26	04-Nov-26	409d	397	0	397
	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2d	03-Nov-26	04-Nov-26	409d	397	0	397
JDH3-02-009-R01-TSE Network - TSE		50d	01-Sep-26 A	31-Oct-26	418d	21,532	6,316	21,532
JDH3-02-009-R01-(TSE)-Valve Chamber on 315 mm dia pipeline		50d	01-Sep-26 A	31-Oct-26	418d	21,532	6,316	21,532
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	28-Oct-26	31-Oct-26	418d	5,742	0	5,742
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	01-Sep-26 A	28-Oct-26	418d	15,790	6,316	15,790
JDH3-02-009-R01-Potable Water Network - WT		57d	01-Sep-26 A	07-Nov-26	413d	215,011	26,493	215,011
JDH3-02-009-R01-(WT)-Wash-Out Valve-150 mm on pipe dia (63		4d	27-Oct-26	31-Oct-26	343d	39,083	0	39,083
	Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E	2d	27-Oct-26	28-Oct-26	343d	35,175	0	35,175
	Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6:	2d	29-Oct-26	31-Oct-26	343d	3,908	0	3,908
JDH3-02-009-R01-(WT)-Valve Chamber on 630 mm dia pipeline		48d	03-Sep-26 A	31-Oct-26	416d	27,539	8,078	27,539
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2d	28-Oct-26	31-Oct-26	416d	7,344	0	7,344
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2d	03-Sep-26 A	28-Oct-26	343d	20,195	8,078	20,195
JDH3-02-009-R01-(WT)-Wash-Out Chamber on 630 mm dia pipe		8d	27-Oct-26	04-Nov-26	413d	54,422	0	54,422
	Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m	2d	27-Oct-26	28-Oct-26	413d	8,163	0	8,163
	PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fr	2d	29-Oct-26	31-Oct-26	413d	5,442	0	5,442
	Installationfor Wash-Out Chamber on pipe dia 630 mm - depth	2d	01-Nov-26	02-Nov-26	413d	29,932	0	29,932
	Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm - c	2d	03-Nov-26	04-Nov-26	413d	10,884	0	10,884
JDH3-02-009-R01-(WT)-Air Valve Chamber on 630 mm dia pipeli		2d	05-Nov-26	07-Nov-26	413d	1,428	0	1,428
	Backfilling Worksfor Air Valve Chamber on pipe dia 630 mm - de	2d	05-Nov-26	07-Nov-26	413d	1,428	0	1,428
JDH3-02-009-R01-(WT)-Fire Hydrant		2d	27-Oct-26	28-Oct-26	419d	2,443	0	2,443
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R01-W	2d	27-Oct-26	28-Oct-26	419d	2,443	0	2,443
JDH3-02-009-R01-(WT)-Valve Chamber on 315 mm dia pipeline		50d	01-Sep-26 A	31-Oct-26	418d	10,752	3,154	10,752
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	28-Oct-26	31-Oct-26	418d	2,867	0	2,867
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	01-Sep-26 A	28-Oct-26	418d	7,885	3,154	7,885
JDH3-02-009-R01-(WT)-Valve Chamber on 800 mm dia pipeline		52d	01-Sep-26 A	02-Nov-26	418d	47,994	14,078	47,994
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	31-Oct-26	02-Nov-26	418d	12,798	0	12,798
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	01-Sep-26 A	28-Oct-26	420d	35,195	14,078	35,195
JDH3-02-009-R01-(WT)-Butterfly Valve-400 mm on pipe dia (400)		2d	28-Oct-26	31-Oct-26	412d	23,467	0	23,467
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2d	28-Oct-26	31-Oct-26	412d	23,467	0	23,467

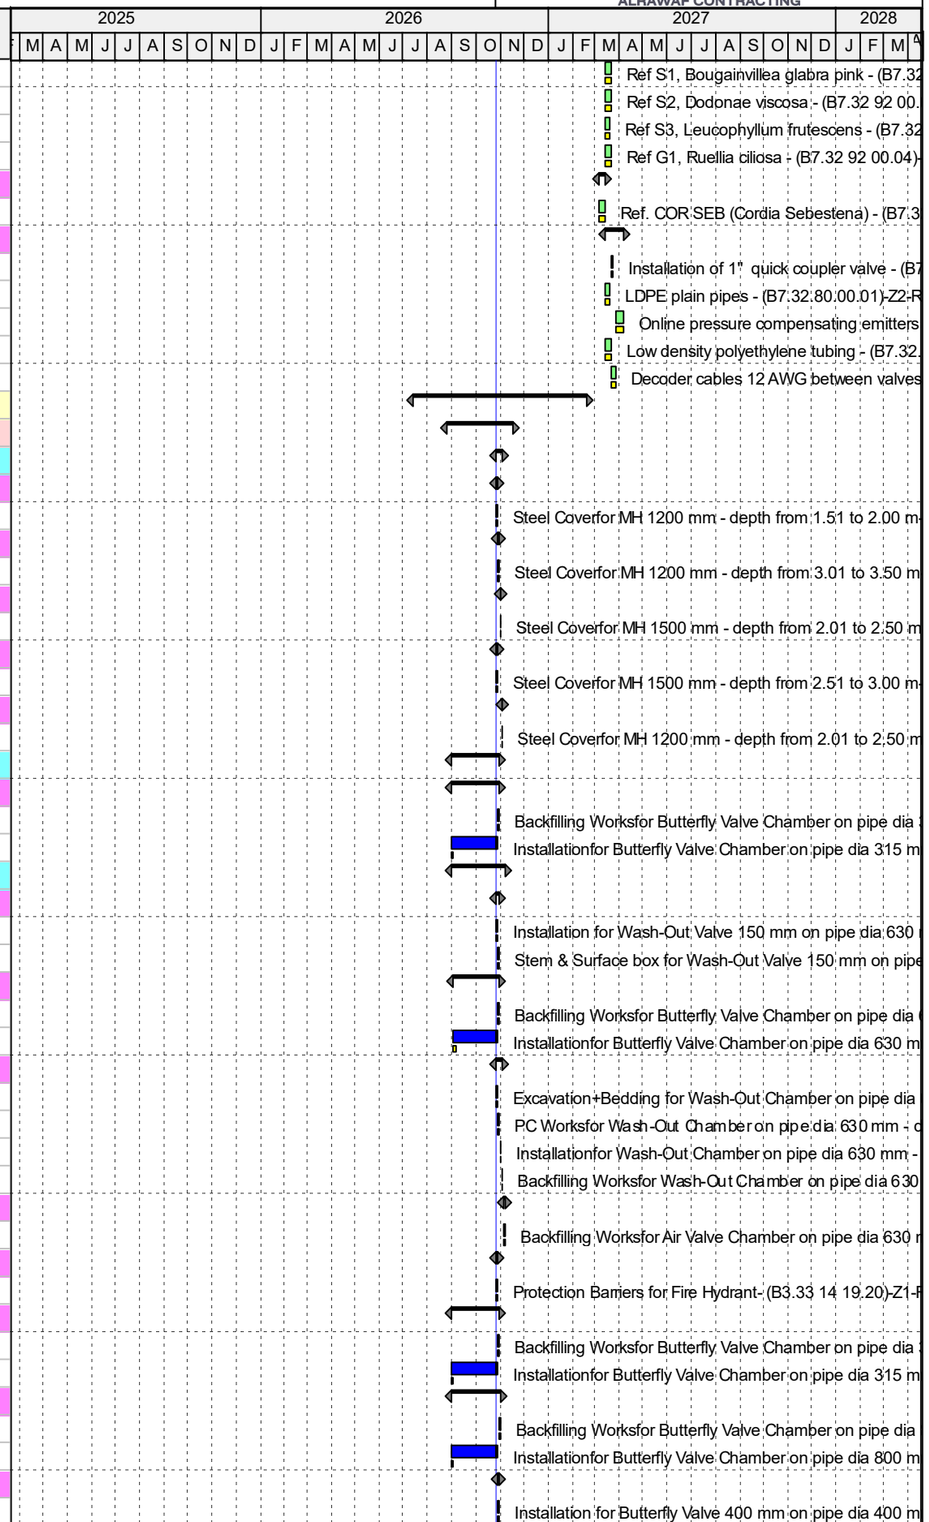


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R01-(WT)-Valve Chamber on 400 mm dia pipeline	2d	01-Sep-26 A	28-Oct-26	412d	7,885	1,183	7,885
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Sep-26 A	28-Oct-26	412d	7,885	1,183	7,885
	JDH3-02-009-R01-Street Lighting Network -SL	65d	25-Aug-26 A	10-Nov-26	411d	17,934	59,169	88,943
	JDH3-02-009-R01-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8d	27-Oct-26	05-Nov-26	411d	0	0	4,702
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	27-Oct-26	29-Oct-26	411d	0	0	470
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	29-Oct-26	01-Nov-26	411d	0	0	3,526
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	01-Nov-26	03-Nov-26	411d	0	0	235
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	03-Nov-26	05-Nov-26	411d	0	0	470
	JDH3-02-009-R01-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	65d	25-Aug-26 A	10-Nov-26	411d	0	51,947	64,330
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	27-Oct-26	01-Nov-26	415d	0	0	3,217
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4d	05-Nov-26	10-Nov-26	411d	0	0	6,433
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4d	29-Aug-26 A	27-Oct-26	415d	0	45,835	48,248
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	25-Aug-26 A	27-Oct-26	411d	0	6,111	6,433
	JDH3-02-009-R01-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2d	15-Sep-26 A	27-Oct-26	423d	7,603	7,222	7,603
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z1-R	2d	15-Sep-26 A	27-Oct-26	423d	7,603	7,222	7,603
	JDH3-02-009-R01-(SL)-Earthing System for Distribution panels,S	2d	27-Oct-26	28-Oct-26	419d	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	27-Oct-26	28-Oct-26	419d	0	0	1,126
	JDH3-02-009-R01-(SL)-Earthing System for Streetlighting feede	2d	29-Oct-26	31-Oct-26	419d	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2d	29-Oct-26	31-Oct-26	419d	0	0	852
	JDH3-02-009-R01-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	412d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R01-S	2d	27-Oct-26	28-Oct-26	417d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2d	29-Oct-26	31-Oct-26	417d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R01-S	2d	07-Nov-26	08-Nov-26	412d	7,232	0	7,232
	JDH3-02-009-R01-Telecommunications Network - TEL	8d	17-Sep-26 A	27-Oct-26	343d	6,837	6,153	6,837
	JDH3-02-009-R01-(TEL)-Manhole Type 2	8d	17-Sep-26 A	27-Oct-26	343d	6,837	6,153	6,837
	Backfilling Works for MH Type 2 Dim 2000*1000*1000 mm- (B2.	2d	26-Sep-26 A	27-Oct-26	343d	684	615	684
	Installation for MH Type 2 Dim 2000*1000*1000 mm- (B2.33.71	2d	20-Sep-26 A	27-Oct-26	343d	5,128	4,615	5,128
	Excavation and Bedding Works for MH Type 2 Dim 2000*1000*	2d	17-Sep-26 A	27-Oct-26	343d	1,026	923	1,026
	JDH3-02-009-R01-Road Works - RD	18d	27-Oct-26	16-Nov-26	359d	0	0	188,054
	JDH3-02-009-R01-(RD)-Precast Concrete Curb	18d	27-Oct-26	16-Nov-26	359d	0	0	188,054
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	12d	27-Oct-26	09-Nov-26	359d	0	0	174,752
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	10-Nov-26	11-Nov-26	359d	0	0	9,457
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	12-Nov-26	16-Nov-26	359d	0	0	3,845
R02		86d	25-Jul-26 A	06-Dec-26	389d	576,193	135,045	1,052,273
	JDH3-02-009-R02-Potable Water Network - WT	12d	27-Oct-26	09-Nov-26	411d	116,265	0	116,265
	JDH3-02-009-R02-(WT)-Air Valve-50 mm on pipe dia (225) mm	4d	03-Nov-26	07-Nov-26	411d	6,490	0	6,490
	Installation for Air Valve 50 mm on pipe dia 225 mm- (B3.33 14	2d	03-Nov-26	04-Nov-26	411d	5,841	0	5,841
	Stem & Surface box for Air Valve 50 mm on pipe dia 225 mm- (I	2d	05-Nov-26	07-Nov-26	411d	649	0	649
	JDH3-02-009-R02-(WT)-Air Valve Chamber on 225 mm dia pipeli	8d	27-Oct-26	04-Nov-26	415d	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 225 mm	2d	27-Oct-26	28-Oct-26	411d	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 225 mm - depth fro	2d	29-Oct-26	31-Oct-26	411d	714	0	714
	Installationfor Air Valve Chamber on pipe dia 225 mm - depth fr	2d	01-Nov-26	02-Nov-26	411d	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 225 mm - de	2d	03-Nov-26	04-Nov-26	415d	1,428	0	1,428
	JDH3-02-009-R02-(WT)-Fire Hydrant	2d	08-Nov-26	09-Nov-26	411d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R02-W	2d	08-Nov-26	09-Nov-26	411d	4,885	0	4,885
	JDH3-02-009-R02-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4d	27-Oct-26	31-Oct-26	417d	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	27-Oct-26	28-Oct-26	417d	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 800	2d	29-Oct-26	31-Oct-26	417d	6,575	0	6,575
	JDH3-02-009-R02-(WT)-Valve Chamber on 800 mm dia pipeline	8d	27-Oct-26	04-Nov-26	415d	31,996	0	31,996
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2d	27-Oct-26	28-Oct-26	415d	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	29-Oct-26	31-Oct-26	415d	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	01-Nov-26	02-Nov-26	415d	17,598	0	17,598
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	03-Nov-26	04-Nov-26	415d	6,399	0	6,399

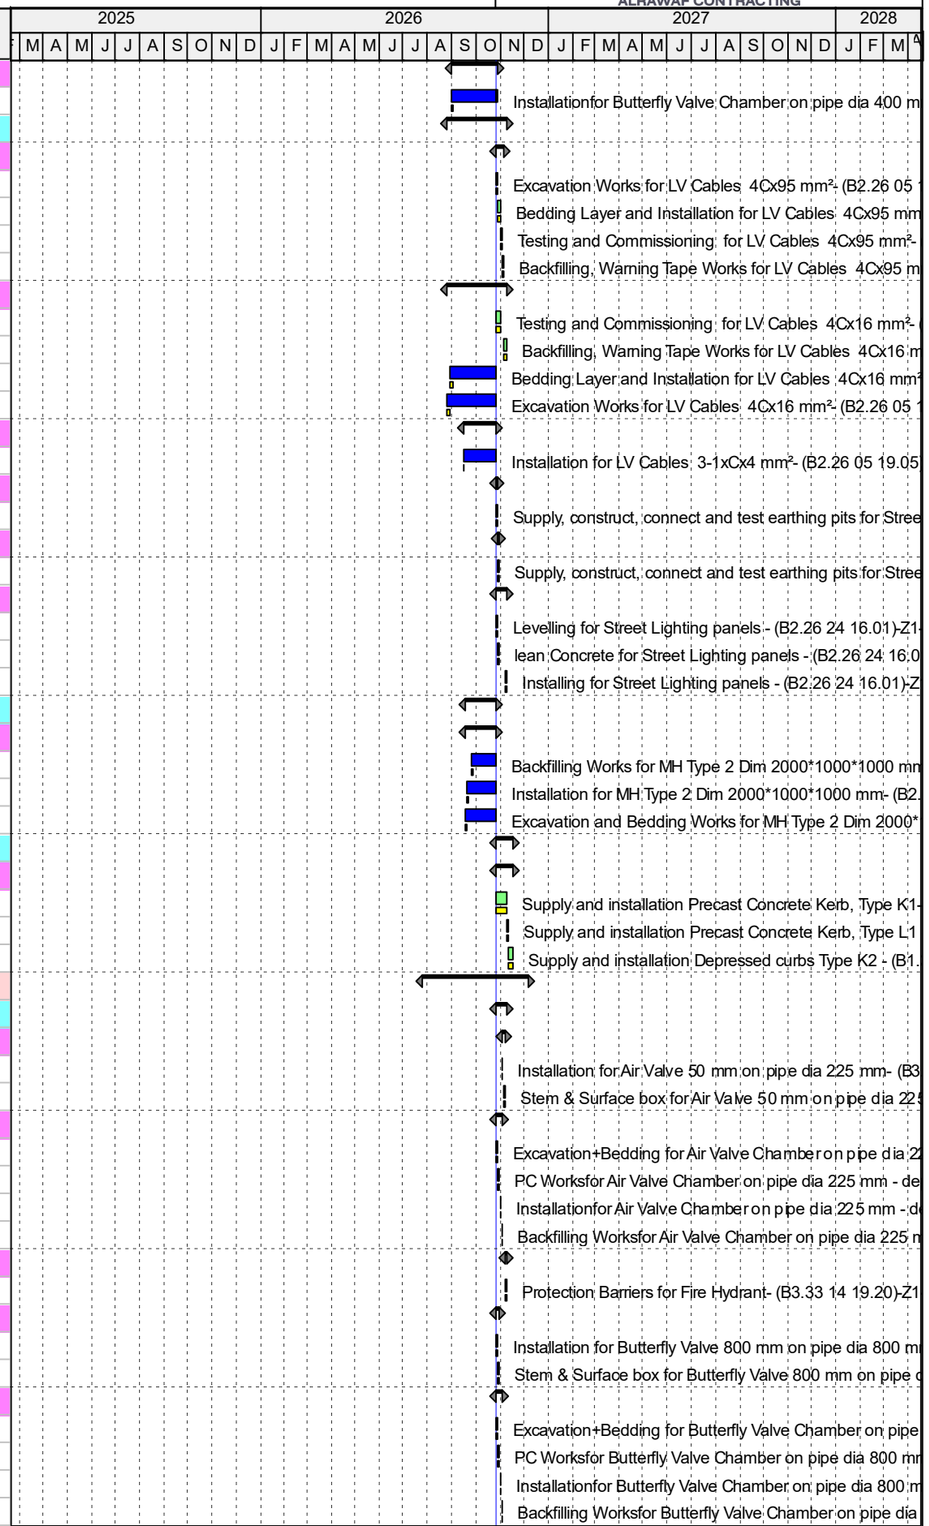


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R02-Electrical Network - EL	58d	22-Aug-26 A	02-Nov-26	367d	80,227	9,766	80,227
	JDH3-02-009-R02-(EL)-RMU 33 KV	6d	27-Oct-26	02-Nov-26	367d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R02-EL	2d	27-Oct-26	28-Oct-26	367d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R02-El	2d	29-Oct-26	31-Oct-26	367d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2d	01-Nov-26	02-Nov-26	367d	4,925	0	4,925
	JDH3-02-009-R02-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	4d	22-Aug-26 A	27-Oct-26	371d	11,281	9,766	11,281
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	23-Aug-26 A	27-Oct-26	371d	2,580	1,935	2,580
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	22-Aug-26 A	27-Oct-26	371d	8,701	7,831	8,701
	JDH3-02-009-R02-Street Lighting Network -SL	69d	25-Jul-26 A	18-Nov-26	381d	217,424	65,462	217,424
	JDH3-02-009-R02-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8d	27-Oct-26	04-Nov-26	385d	37,974	0	37,974
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	03-Nov-26	04-Nov-26	367d	3,797	0	3,797
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.:	2d	27-Oct-26	28-Oct-26	387d	28,480	0	28,480
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	29-Oct-26	31-Oct-26	387d	1,899	0	1,899
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	01-Nov-26	02-Nov-26	387d	3,797	0	3,797
	JDH3-02-009-R02-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	12d	05-Nov-26	18-Nov-26	367d	72,262	0	72,262
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6d	05-Nov-26	11-Nov-26	367d	8,501	0	8,501
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	6d	12-Nov-26	18-Nov-26	367d	63,761	0	63,761
	JDH3-02-009-R02-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2d	28-Oct-26	31-Oct-26	394d	4,134	0	4,134
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z1-R	2d	28-Oct-26	31-Oct-26	394d	4,134	0	4,134
	JDH3-02-009-R02-(SL)-Lighting Pole with single arm 12 m heigh	57d	25-Jul-26 A	04-Nov-26	392d	76,166	53,044	76,166
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6d	28-Oct-26	04-Nov-26	392d	5,440	0	5,440
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	6d	25-Jul-26 A	28-Oct-26	392d	70,725	53,044	70,725
	JDH3-02-009-R02-(SL)-Street Lighting(LED) Luminaire complet	6d	25-Jul-26 A	31-Oct-26	398d	16,557	12,418	16,557
	Installation for Lighting(LED) Luminaire 114 WATT- (B2.26.56.1	3d	25-Jul-26 A	31-Oct-26	394d	13,246	9,934	13,246
	Cable Connection for Lighting(LED) Luminaire 114 WATT- (B2.	3d	25-Jul-26 A	31-Oct-26	398d	3,311	2,484	3,311
	JDH3-02-009-R02-(SL)- Street Lighting Panels	11d	27-Oct-26	08-Nov-26	390d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R02-S	2d	27-Oct-26	28-Oct-26	395d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2d	31-Oct-26	02-Nov-26	394d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R02-S	2d	07-Nov-26	08-Nov-26	390d	7,232	0	7,232
	JDH3-02-009-R02-Road Works - RD	82d	01-Sep-26 A	06-Dec-26	385d	162,277	59,817	638,358
	JDH3-02-009-R02-(RD)-Bituminous concrete wearing course 50	5d	28-Nov-26	03-Dec-26	369d	0	0	345,894
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	28-Nov-26	03-Dec-26	369d	0	0	345,894
	JDH3-02-009-R02-(RD)-Precast Concrete Curb	61d	01-Sep-26 A	11-Nov-26	369d	142,002	59,817	142,002
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	28-Oct-26	31-Oct-26	369d	6,679	0	6,679
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10d	31-Oct-26	11-Nov-26	369d	64,950	0	64,950
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10d	01-Sep-26 A	28-Oct-26	369d	70,373	59,817	70,373
	JDH3-02-009-R02-(RD)-Precast Interlocking Block Pavers	14d	11-Nov-26	28-Nov-26	369d	20,275	0	141,927
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	14d	11-Nov-26	28-Nov-26	369d	20,275	0	141,927
	JDH3-02-009-R02-(RD)-Pavement Marking	2d	03-Dec-26	06-Dec-26	369d	0	0	5,264
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	03-Dec-26	06-Dec-26	369d	0	0	5,264
	JDH3-02-009-R02-(RD)-Traffic Signage	2d	03-Dec-26	06-Dec-26	385d	0	0	3,270
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2d	03-Dec-26	06-Dec-26	385d	0	0	3,270
R03		134d	02-Sep-26 A	18-Feb-27	325d	498,898	232,021	640,254
	JDH3-02-009-R03-Potable Water Network - WT	14d	27-Oct-26	11-Nov-26	409d	131,172	0	131,172
	JDH3-02-009-R03-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R03-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R03-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4d	03-Nov-26	07-Nov-26	409d	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	03-Nov-26	04-Nov-26	409d	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2d	05-Nov-26	07-Nov-26	409d	6,575	0	6,575
	JDH3-02-009-R03-(WT)-Wash-Out Valve-100 mm on pipe dia (22	6d	05-Nov-26	11-Nov-26	409d	7,673	0	7,673
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2d	05-Nov-26	07-Nov-26	411d	6,906	0	6,906
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	10-Nov-26	11-Nov-26	409d	767	0	767
	JDH3-02-009-R03-(WT)-Valve Chamber on 800 mm dia pipeline	8d	27-Oct-26	04-Nov-26	411d	31,996	0	31,996

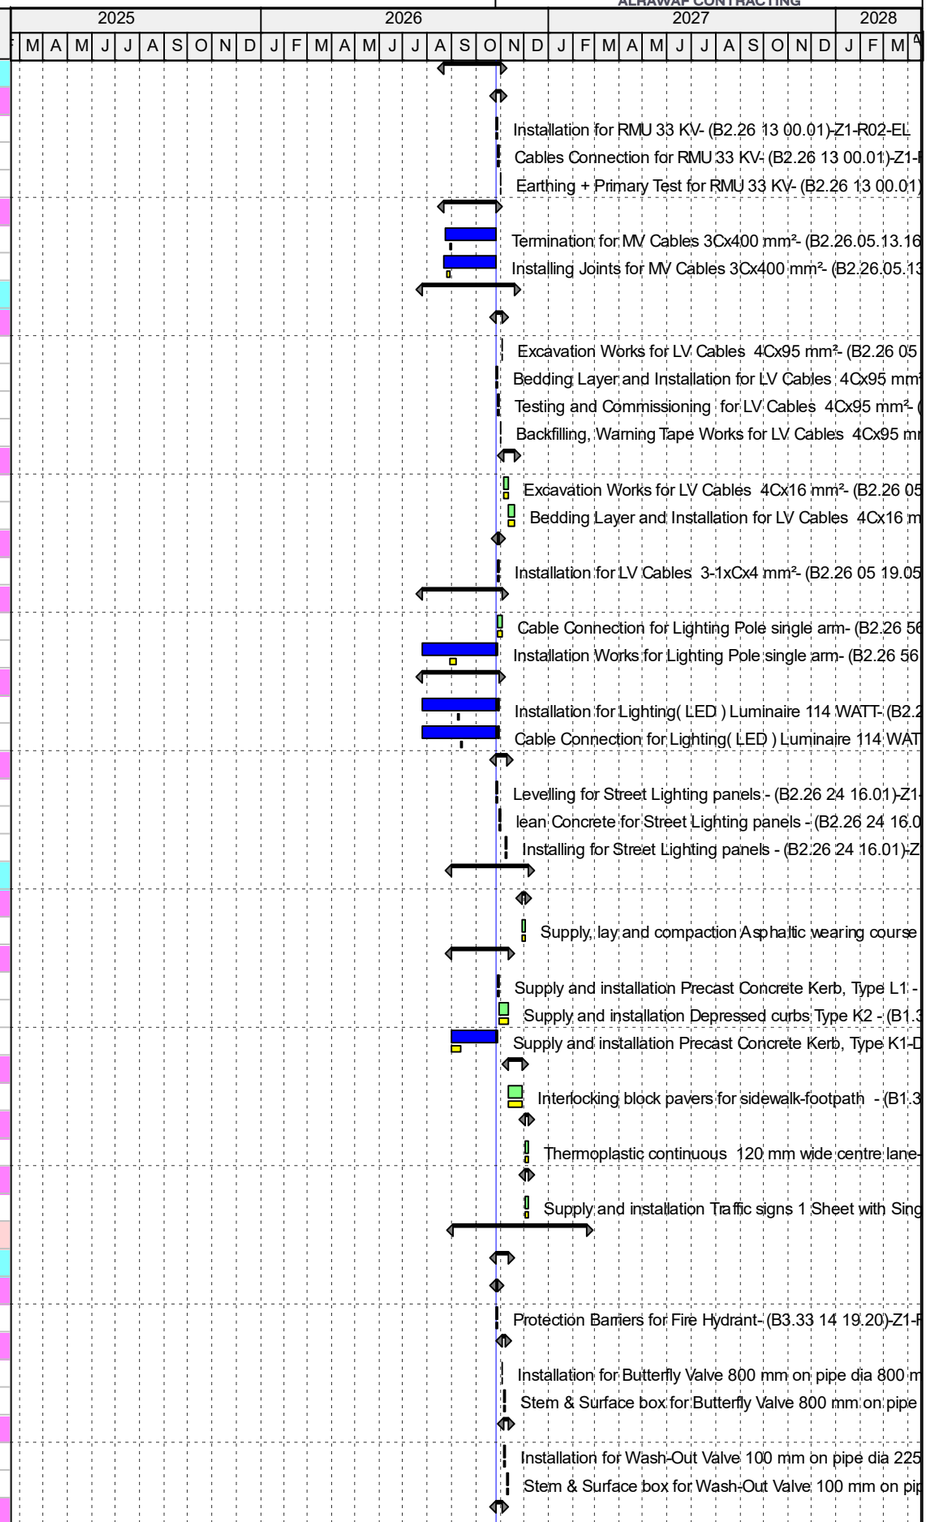


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2d	27-Oct-26	28-Oct-26	409d	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	29-Oct-26	31-Oct-26	409d	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	01-Nov-26	02-Nov-26	409d	17,598	0	17,598
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	03-Nov-26	04-Nov-26	411d	6,399	0	6,399
	JDH3-02-009-R03-(WT)-Wash-Out Chamber on 225 mm dia pipe	10d	29-Oct-26	09-Nov-26	409d	20,864	0	20,864
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2d	29-Oct-26	31-Oct-26	411d	3,130	0	3,130
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2d	01-Nov-26	02-Nov-26	411d	2,086	0	2,086
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	03-Nov-26	04-Nov-26	411d	11,475	0	11,475
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - c	2d	08-Nov-26	09-Nov-26	409d	4,173	0	4,173
	JDH3-02-009-R03-Electrical Network - EL	48d	15-Sep-26 A	10-Nov-26	298d	275,701	173,789	275,701
	JDH3-02-009-R03-(EL)-MV cable trench size 1.5m wide and 80c	6d	29-Oct-26	05-Nov-26	298d	3,992	0	3,992
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6d	29-Oct-26	05-Nov-26	298d	3,992	0	3,992
	JDH3-02-009-R03-(EL)-RMU 33 KV	13d	27-Oct-26	10-Nov-26	298d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R03-EL	2d	27-Oct-26	28-Oct-26	304d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R03-El	2d	29-Oct-26	31-Oct-26	304d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2d	08-Nov-26	10-Nov-26	298d	4,925	0	4,925
	JDH3-02-009-R03-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	46d	15-Sep-26 A	08-Nov-26	298d	202,763	173,789	202,763
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	27-Oct-26	29-Oct-26	298d	8,701	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	05-Nov-26	08-Nov-26	298d	5,160	0	5,160
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	15-Sep-26 A	27-Oct-26	298d	188,901	173,789	188,901
	JDH3-02-009-R03-Street Lighting Network -SL	20d	27-Oct-26	18-Nov-26	324d	23,518	0	23,518
	JDH3-02-009-R03-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	2d	27-Oct-26	28-Oct-26	333d	3,401	0	3,401
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2d	27-Oct-26	28-Oct-26	333d	3,401	0	3,401
	JDH3-02-009-R03-(SL)-RMU 33 KV	2d	27-Oct-26	28-Oct-26	337d	4,202	0	4,202
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z1-R03-SL	2d	27-Oct-26	28-Oct-26	337d	4,202	0	4,202
	JDH3-02-009-R03-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL/	2d	10-Nov-26	12-Nov-26	298d	121	0	121
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2d	10-Nov-26	12-Nov-26	298d	121	0	121
	JDH3-02-009-R03-(SL)- LV Cables - Copper, 3x1Cx50mm²,Cu/XL	2d	29-Oct-26	31-Oct-26	335d	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z1-F	2d	29-Oct-26	31-Oct-26	335d	1,520	0	1,520
	JDH3-02-009-R03-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	5d	12-Nov-26	18-Nov-26	298d	7,730	0	7,730
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	12-Nov-26	18-Nov-26	298d	7,730	0	7,730
	JDH3-02-009-R03-(SL)- Street Lighting Panels	2d	27-Oct-26	28-Oct-26	337d	1,033	0	1,033
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R03-S	2d	27-Oct-26	28-Oct-26	337d	1,033	0	1,033
	JDH3-02-009-R03-(SL)- LV Distribution Panel Main: 100A, MCCE	4d	29-Oct-26	02-Nov-26	337d	5,511	0	5,511
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z1-R03-S	2d	29-Oct-26	31-Oct-26	337d	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z1-F	2d	01-Nov-26	02-Nov-26	337d	3,674	0	3,674
	JDH3-02-009-R03-Road Works - RD	63d	02-Sep-26 A	18-Feb-27	298d	68,508	58,232	209,864
	JDH3-02-009-R03-(RD)-Precast Concrete Curb	10d	02-Sep-26 A	19-Jan-27	298d	68,508	58,232	68,508
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10d	02-Sep-26 A	19-Jan-27	298d	68,508	58,232	68,508
	JDH3-02-009-R03-(RD)-Precast Interlocking Block Pavers	14d	02-Feb-27	18-Feb-27	298d	0	0	141,356
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	14d	02-Feb-27	18-Feb-27	298d	0	0	141,356
R04		74d	01-Sep-26 A	26-Nov-26	396d	276,448	309,160	1,283,869
	JDH3-02-009-R04-Potable Water Network - WT	57d	01-Sep-26 A	07-Nov-26	413d	239,434	9,462	239,434
	JDH3-02-009-R04-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4d	03-Nov-26	07-Nov-26	413d	131,509	0	131,509
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	03-Nov-26	04-Nov-26	413d	118,358	0	118,358
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2d	05-Nov-26	07-Nov-26	413d	13,151	0	13,151
	JDH3-02-009-R04-(WT)-Butterfly Valve-300 mm on pipe dia (315)	2d	27-Oct-26	28-Oct-26	419d	4,839	0	4,839
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	27-Oct-26	28-Oct-26	419d	4,839	0	4,839
	JDH3-02-009-R04-(WT)-Valve Chamber on 315 mm dia pipeline	51d	01-Sep-26 A	31-Oct-26	419d	32,255	9,462	32,255
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	29-Oct-26	31-Oct-26	419d	8,601	0	8,601
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	01-Sep-26 A	28-Oct-26	422d	23,654	9,462	23,654
	JDH3-02-009-R04-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	419d	6,840	0	6,840
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R04-W	2d	27-Oct-26	28-Oct-26	419d	6,840	0	6,840

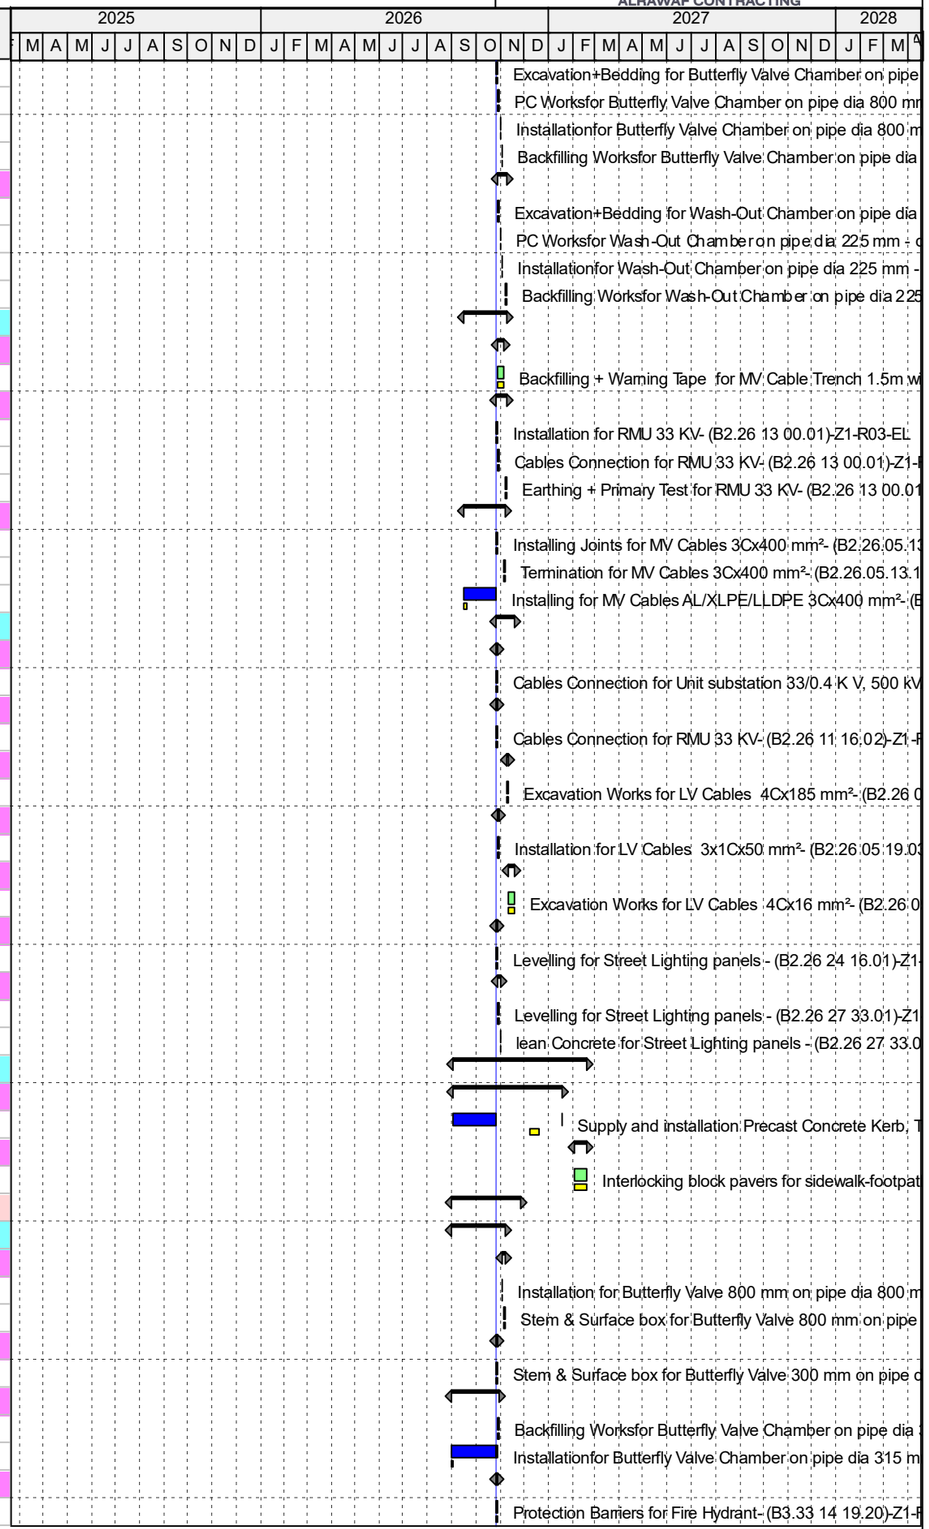


Actual Level of Effort · Primary Baseline · Actual Work · Remaining Work · Critical Remaining Work · Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R04-(WT)-Valve Chamber on 800 mm dia pipeline	8d	27-Oct-26	04-Nov-26	415d	63,992	0	63,992
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2d	27-Oct-26	28-Oct-26	413d	9,599	0	9,599
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	29-Oct-26	31-Oct-26	413d	6,399	0	6,399
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	01-Nov-26	02-Nov-26	413d	35,195	0	35,195
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	03-Nov-26	04-Nov-26	415d	12,798	0	12,798
	JDH3-02-009-R04-TSE Network - TSE	8d	27-Oct-26	04-Nov-26	415d	37,013	0	37,013
	JDH3-02-009-R04-(TSE)-Wash-Out Valve-100 mm on pipe dia (3	4d	27-Oct-26	31-Oct-26	419d	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2d	27-Oct-26	28-Oct-26	419d	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2d	29-Oct-26	31-Oct-26	419d	1,613	0	1,613
	JDH3-02-009-R04-(TSE)-Wash-Out Chamber on 315 mm dia pipe	8d	27-Oct-26	04-Nov-26	415d	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2d	27-Oct-26	28-Oct-26	415d	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2d	29-Oct-26	31-Oct-26	415d	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2d	01-Nov-26	02-Nov-26	415d	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2d	03-Nov-26	04-Nov-26	415d	4,177	0	4,177
	JDH3-02-009-R04-Electrical Network - EL	57d	08-Sep-26 A	14-Nov-26	328d	0	299,699	752,147
	JDH3-02-009-R04-(EL)-MV cable trench size 1.5m wide and 80c	26d	08-Sep-26 A	09-Nov-26	328d	0	358	918
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	2d	23-Sep-26 A	09-Nov-26	328d	0	110	367
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	2d	08-Sep-26 A	28-Oct-26	337d	0	248	551
	JDH3-02-009-R04-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	47d	16-Sep-26 A	11-Nov-26	328d	0	299,341	682,284
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	07-Nov-26	09-Nov-26	328d	0	0	14,502
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	09-Nov-26	11-Nov-26	328d	0	0	2,580
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	16d	16-Sep-26 A	07-Nov-26	328d	0	299,341	665,202
	JDH3-02-009-R04-(EL)-RMU 33 KV	16d	27-Oct-26	14-Nov-26	328d	0	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R04-EL	2d	27-Oct-26	28-Oct-26	338d	0	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R04-EL	2d	09-Nov-26	11-Nov-26	328d	0	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2d	11-Nov-26	14-Nov-26	328d	0	0	4,925
	JDH3-02-009-R04-Street Lighting Network -SL	8d	14-Nov-26	23-Nov-26	346d	0	0	73,307
	JDH3-02-009-R04-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	4d	14-Nov-26	18-Nov-26	350d	0	0	63,941
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	14-Nov-26	16-Nov-26	328d	0	0	7,522
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	16-Nov-26	18-Nov-26	350d	0	0	56,418
	JDH3-02-009-R04-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	6d	16-Nov-26	23-Nov-26	328d	0	0	9,366
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6d	16-Nov-26	23-Nov-26	328d	0	0	9,366
	JDH3-02-009-R04-Road Works - RD	27d	27-Oct-26	26-Nov-26	350d	0	0	181,967
	JDH3-02-009-R04-(RD)-Precast Concrete Curb	27d	27-Oct-26	26-Nov-26	350d	0	0	181,967
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10d	27-Oct-26	07-Nov-26	350d	0	0	71,130
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	4d	08-Nov-26	11-Nov-26	350d	0	0	27,910
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	13d	12-Nov-26	26-Nov-26	350d	0	0	82,926
	R05	58d	15-Sep-26 A	22-Nov-26	401d	35,329	206,906	490,261
	JDH3-02-009-R05-Potable Water Network - WT	8d	27-Oct-26	04-Nov-26	415d	33,422	0	33,422
	JDH3-02-009-R05-(WT)-Wash-Out Valve-100 mm on pipe dia (22	4d	27-Oct-26	31-Oct-26	350d	7,673	0	7,673
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2d	27-Oct-26	28-Oct-26	350d	6,906	0	6,906
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	29-Oct-26	31-Oct-26	350d	767	0	767
	JDH3-02-009-R05-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	343d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R05-W	2d	27-Oct-26	28-Oct-26	343d	4,885	0	4,885
	JDH3-02-009-R05-(WT)-Wash-Out Chamber on 225 mm dia pipe	8d	27-Oct-26	04-Nov-26	415d	20,864	0	20,864
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2d	27-Oct-26	28-Oct-26	415d	3,130	0	3,130
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2d	29-Oct-26	31-Oct-26	415d	2,086	0	2,086
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	01-Nov-26	02-Nov-26	415d	11,475	0	11,475
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - c	2d	03-Nov-26	04-Nov-26	415d	4,173	0	4,173
	JDH3-02-009-R05-Electrical Network - EL	47d	19-Sep-26 A	12-Nov-26	350d	0	179,456	273,029
	JDH3-02-009-R05-(EL)-MV cable trench size 1.5m wide and 80c	6d	01-Nov-26	08-Nov-26	350d	0	0	3,901
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6d	01-Nov-26	08-Nov-26	350d	0	0	3,901
	JDH3-02-009-R05-(EL)-RMU 33 KV	15d	27-Oct-26	12-Nov-26	350d	0	0	68,946

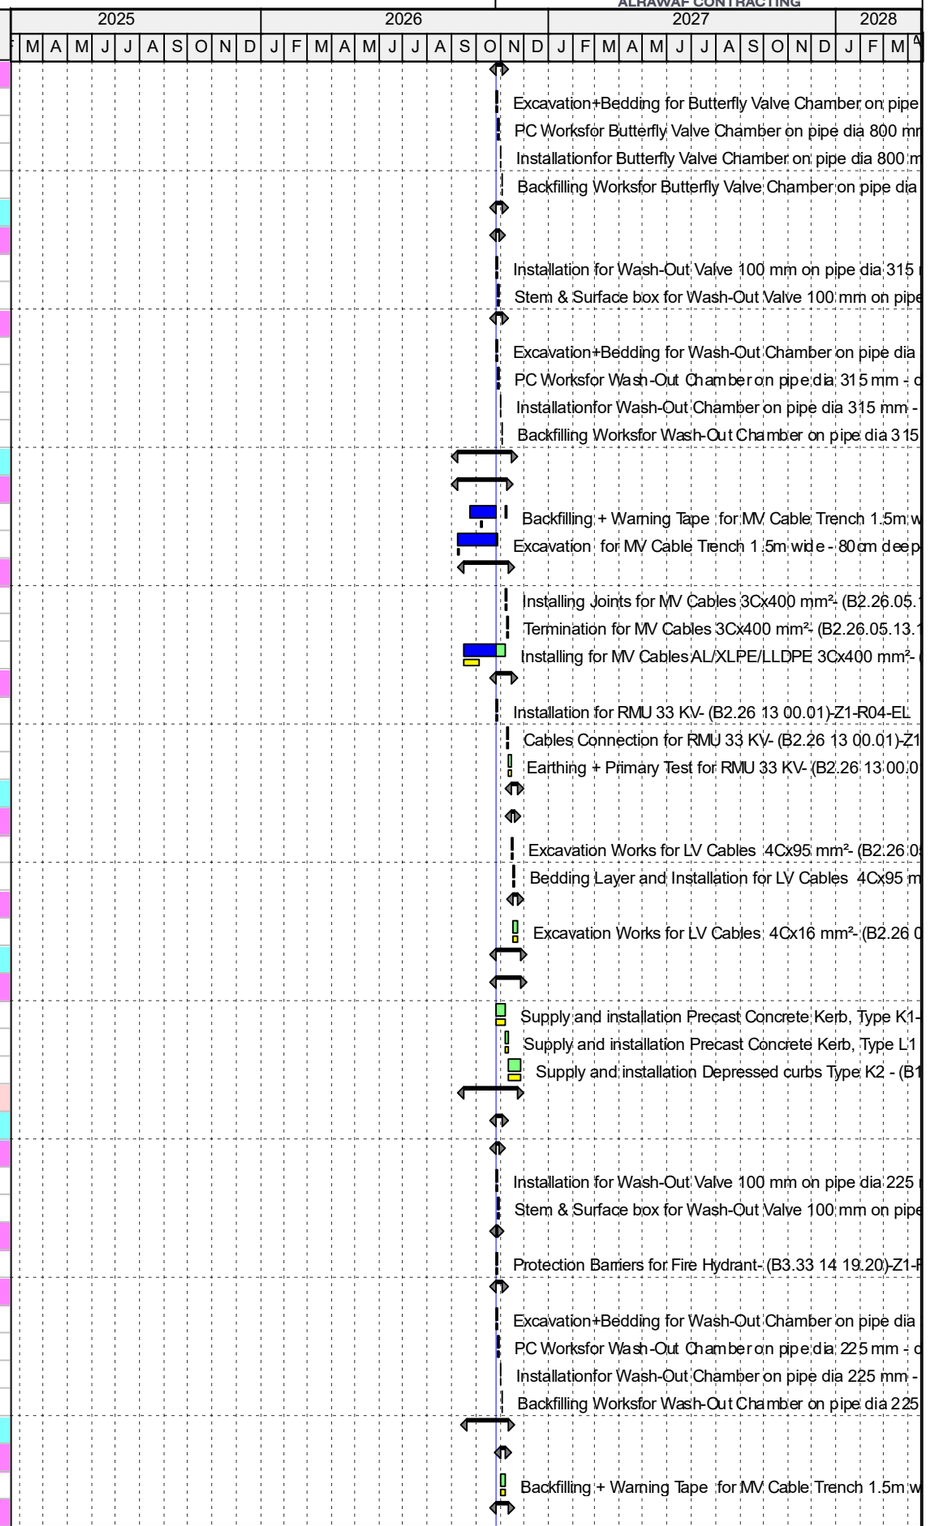

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R05-EL	2d	27-Oct-26	28-Oct-26	358d	0	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R05-EL	2d	29-Oct-26	31-Oct-26	358d	0	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2d	10-Nov-26	12-Nov-26	350d	0	0	4,925
	JDH3-02-009-R05-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	45d	19-Sep-26 A	10-Nov-26	350d	0	179,456	200,183
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	29-Oct-26	01-Nov-26	350d	0	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	08-Nov-26	10-Nov-26	350d	0	0	2,580
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5d	19-Sep-26 A	29-Oct-26	350d	0	179,456	188,901
	JDH3-02-009-R05-Street Lighting Network -SL	8d	12-Nov-26	22-Nov-26	361d	0	0	41,901
	JDH3-02-009-R05-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	4d	12-Nov-26	17-Nov-26	365d	0	0	33,200
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	12-Nov-26	15-Nov-26	350d	0	0	3,906
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	15-Nov-26	17-Nov-26	365d	0	0	29,294
	JDH3-02-009-R05-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	6d	15-Nov-26	22-Nov-26	350d	0	0	8,701
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6d	15-Nov-26	22-Nov-26	350d	0	0	8,701
	JDH3-02-009-R05-Telecommunications Network - TEL	8d	27-Oct-26	04-Nov-26	415d	1,907	0	1,907
	JDH3-02-009-R05-(TEL)-Reinforced Concrete Duct 6-ways ducts	8d	27-Oct-26	04-Nov-26	415d	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2d	27-Oct-26	28-Oct-26	401d	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2d	29-Oct-26	31-Oct-26	415d	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2d	01-Nov-26	02-Nov-26	415d	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2d	03-Nov-26	04-Nov-26	415d	191	0	191
	JDH3-02-009-R05-Road Works - RD	53d	15-Sep-26 A	16-Nov-26	364d	0	27,450	140,003
	JDH3-02-009-R05-(RD)-Precast Concrete Curb	53d	15-Sep-26 A	16-Nov-26	364d	0	27,450	140,003
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	03-Nov-26	04-Nov-26	364d	0	0	6,371
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10d	05-Nov-26	16-Nov-26	364d	0	0	65,006
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10d	15-Sep-26 A	02-Nov-26	364d	0	27,450	68,626
R06		87d	14-Jul-26 A	17-Nov-26	405d	520,796	297,553	738,816
	JDH3-02-009-R06-Catch Basins (Storm Network) - ST	5d	27-Oct-26	01-Nov-26	412d	23,966	0	23,966
	JDH3-02-009-R06-(ST)-Single Catch Basin Works	5d	27-Oct-26	01-Nov-26	412d	10,684	0	10,684
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5d	27-Oct-26	01-Nov-26	412d	10,684	0	10,684
	JDH3-02-009-R06-(ST)-Double Catch Basin Works	2d	27-Oct-26	28-Oct-26	415d	13,282	0	13,282
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	415d	13,282	0	13,282
	JDH3-02-009-R06-TSE Network - TSE	52d	01-Sep-26 A	01-Nov-26	418d	95,630	54,675	95,630
	JDH3-02-009-R06-(TSE)-Butterfly Valve-300 mm on pipe dia (315	9d	15-Sep-26 A	28-Oct-26	421d	48,390	31,937	48,390
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	22-Sep-26 A	28-Oct-26	421d	4,839	3,194	4,839
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2d	15-Sep-26 A	27-Oct-26	422d	43,551	28,743	43,551
	JDH3-02-009-R06-(TSE)-Valve Chamber on 315 mm dia pipeline	50d	01-Sep-26 A	29-Oct-26	418d	43,064	22,738	43,064
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	27-Oct-26	29-Oct-26	418d	8,613	0	8,613
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	15-Sep-26 A	27-Oct-26	418d	23,685	15,632	23,685
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2d	01-Sep-26 A	27-Oct-26	418d	6,460	4,263	6,460
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	03-Sep-26 A	27-Oct-26	418d	4,306	2,842	4,306
	JDH3-02-009-R06-(TSE)-Wash-Out Chamber on 315 mm dia pipe	2d	29-Oct-26	01-Nov-26	418d	4,177	0	4,177
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2d	29-Oct-26	01-Nov-26	418d	4,177	0	4,177
	JDH3-02-009-R06-Potable Water Network - WT	49d	03-Sep-26 A	31-Oct-26	419d	226,043	102,547	226,043
	JDH3-02-009-R06-(WT)-Butterfly Valve-600 mm on pipe dia (630)	38d	15-Sep-26 A	29-Oct-26	420d	147,949	87,882	147,949
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 630	2d	27-Oct-26	29-Oct-26	420d	14,795	0	14,795
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2d	15-Sep-26 A	27-Oct-26	420d	133,154	87,882	133,154
	JDH3-02-009-R06-(WT)-Valve Chamber on 630 mm dia pipeline	48d	03-Sep-26 A	31-Oct-26	420d	46,816	11,511	46,816
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2d	28-Oct-26	31-Oct-26	420d	11,015	0	11,015
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2d	17-Sep-26 A	28-Oct-26	420d	30,293	7,876	30,293
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2d	03-Sep-26 A	27-Oct-26	420d	5,508	3,635	5,508
	JDH3-02-009-R06-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R06-W	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R06-(WT)-Butterfly Valve-300 mm on pipe dia (315)	4d	27-Oct-26	31-Oct-26	413d	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2d	27-Oct-26	28-Oct-26	413d	14,517	0	14,517

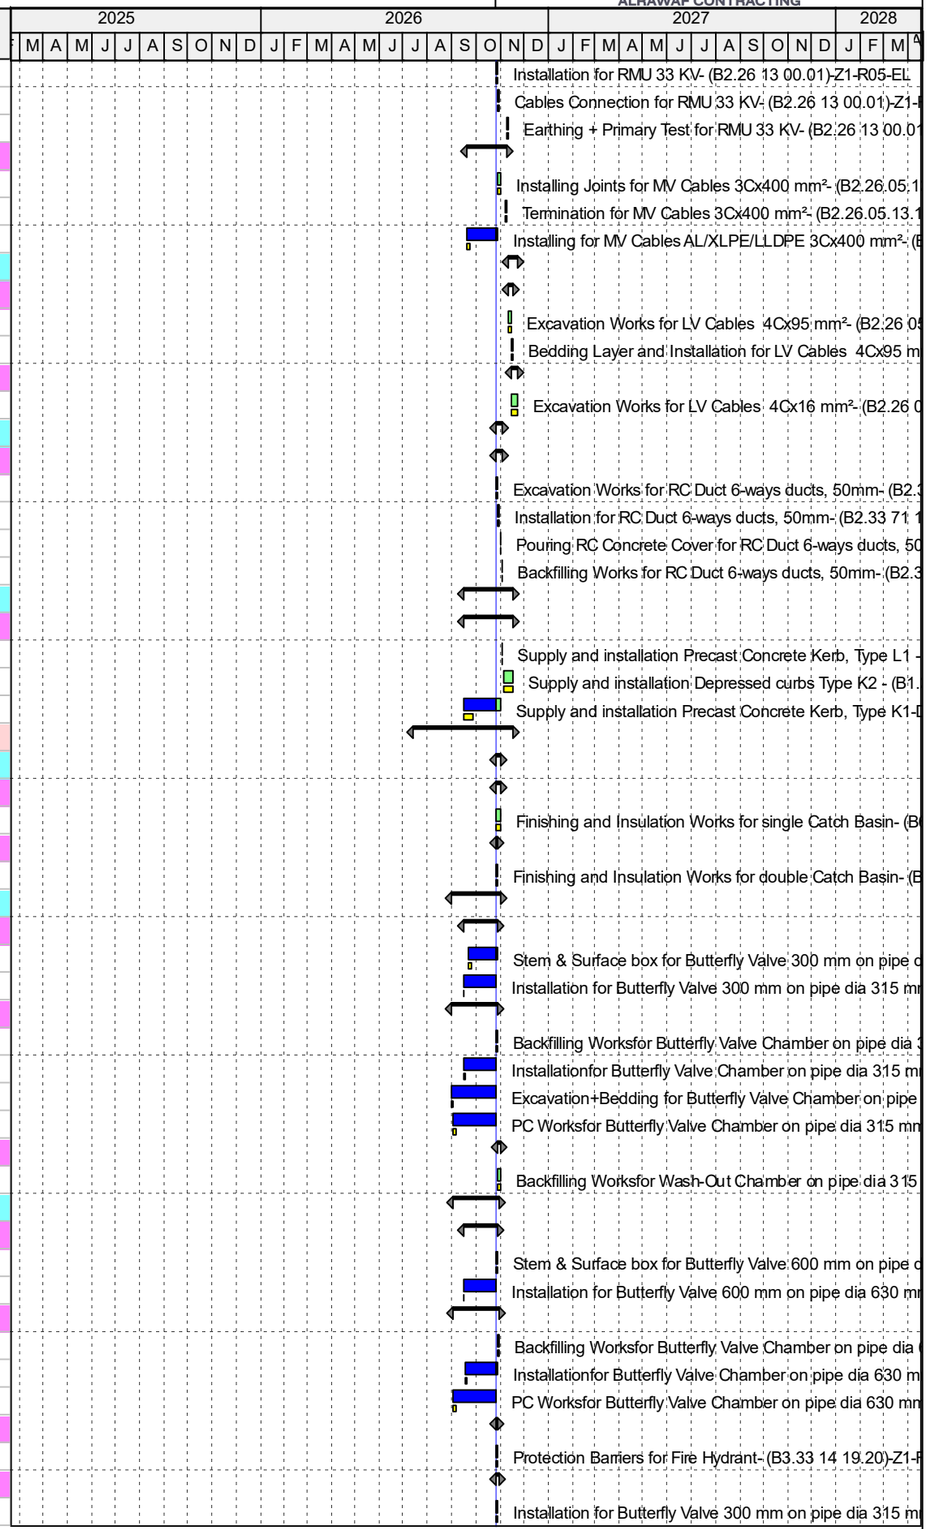


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	29-Oct-26	31-Oct-26	413d	1,613	0	1,613
	JDH3-02-009-R06-(WT)-Valve Chamber on 315 mm dia pipeline	44d	08-Sep-26 A	31-Oct-26	420d	10,752	3,154	10,752
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	28-Oct-26	31-Oct-26	420d	2,867	0	2,867
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	08-Sep-26 A	28-Oct-26	420d	7,885	3,154	7,885
	JDH3-02-009-R06-Street Lighting Network -SL	85d	14-Jul-26 A	14-Nov-26	398d	171,297	140,331	171,297
	JDH3-02-009-R06-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8d	27-Oct-26	04-Nov-26	398d	3,978	0	3,978
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2d	27-Oct-26	28-Oct-26	398d	398	0	398
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2d	29-Oct-26	31-Oct-26	398d	2,984	0	2,984
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2d	01-Nov-26	02-Nov-26	398d	199	0	199
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2d	03-Nov-26	04-Nov-26	398d	398	0	398
	JDH3-02-009-R06-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	57d	03-Sep-26 A	09-Nov-26	398d	48,619	39,260	48,619
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	29-Oct-26	02-Nov-26	400d	2,431	0	2,431
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4d	05-Nov-26	09-Nov-26	398d	4,862	0	4,862
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4d	05-Sep-26 A	28-Oct-26	400d	36,465	34,641	36,465
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	03-Sep-26 A	28-Oct-26	400d	4,862	4,619	4,862
	JDH3-02-009-R06-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2d	17-Sep-26 A	29-Oct-26	406d	6,462	6,139	6,462
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z1-R	2d	17-Sep-26 A	29-Oct-26	406d	6,462	6,139	6,462
	JDH3-02-009-R06-(SL)-Lighting Pole with double arms 16 m hei	31d	14-Jul-26 A	29-Oct-26	408d	79,730	75,744	79,730
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	3d	18-Jul-26 A	29-Oct-26	406d	51,825	49,233	51,825
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3d	05-Sep-26 A	29-Oct-26	408d	3,987	3,787	3,987
	Excavation for RC foundation for Lighting Pole double arms- (B2	2d	14-Jul-26 A	28-Oct-26	404d	7,973	7,574	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2d	15-Jul-26 A	28-Oct-26	406d	7,973	7,574	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2.2	2d	16-Jul-26 A	28-Oct-26	406d	7,973	7,574	7,973
	JDH3-02-009-R06-(SL)-Street Lighting(LED) Luminaire complet	18d	19-Jul-26 A	11-Nov-26	398d	20,198	19,188	20,198
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.'	3d	19-Jul-26 A	29-Oct-26	406d	16,159	15,351	16,159
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3d	28-Jul-26 A	11-Nov-26	398d	4,040	3,838	4,040
	JDH3-02-009-R06-(SL)-Earthing System for Distribution panels,S	2d	12-Nov-26	14-Nov-26	398d	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2d	12-Nov-26	14-Nov-26	398d	1,126	0	1,126
	JDH3-02-009-R06-(SL)-Earthing System for Streetlighting feede	2d	10-Nov-26	11-Nov-26	398d	852	0	852
	Supply, construct, connect and test earthing pits for Street Light	2d	10-Nov-26	11-Nov-26	398d	852	0	852
	JDH3-02-009-R06-(SL)- Street Lighting Panels	9d	29-Oct-26	08-Nov-26	401d	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R06-S	2d	29-Oct-26	31-Oct-26	404d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2d	01-Nov-26	02-Nov-26	404d	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R06-S	2d	07-Nov-26	08-Nov-26	401d	7,232	0	7,232
	JDH3-02-009-R06-Telecommunications Network - TEL	2d	15-Nov-26	16-Nov-26	398d	3,859	0	3,859
	JDH3-02-009-R06-(TEL)-Ducts	2d	15-Nov-26	16-Nov-26	398d	3,859	0	3,859
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2d	15-Nov-26	16-Nov-26	398d	3,859	0	3,859
	JDH3-02-009-R06-Road Works - RD	17d	28-Oct-26	17-Nov-26	371d	0	0	218,020
	JDH3-02-009-R06-(RD)-Precast Concrete Curb	17d	28-Oct-26	17-Nov-26	371d	0	0	218,020
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	12d	28-Oct-26	11-Nov-26	371d	0	0	178,517
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5d	11-Nov-26	17-Nov-26	371d	0	0	39,503
Z4		153d	18-Aug-26 A	13-Feb-27	329d	2,072,373	156,922	3,075,683
R21		98d	18-Aug-26 A	10-Dec-26	384d	829,535	56,723	1,140,519
	JDH3-02-009-R21-Sewage Network - SW	68d	18-Aug-26 A	05-Nov-26	414d	17,420	5,563	17,420
	JDH3-02-009-R21-(SW)-MH Works depth from 1.51 to 2.5 Diam	62d	18-Aug-26 A	29-Oct-26	418d	1,334	424	1,334
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	2d	28-Oct-26	29-Oct-26	418d	485	0	485
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	18-Aug-26 A	27-Oct-26	408d	849	424	849
	JDH3-02-009-R21-(SW)-MH Works depth from 2.51 to 3.5 Diam	62d	20-Aug-26 A	01-Nov-26	418d	2,912	946	2,912
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3	2d	31-Oct-26	01-Nov-26	418d	1,019	0	1,019
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	20-Aug-26 A	27-Oct-26	408d	1,893	946	1,893
	JDH3-02-009-R21-(SW)-MH Works depth from 3.51 to 4.5 Diam	58d	23-Aug-26 A	29-Oct-26	408d	1,834	584	1,834
	Steel Coverfor MH 1200 mm - depth from 3.51 to 4.5 m- (B5.33	2d	28-Oct-26	29-Oct-26	408d	667	0	667
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	23-Aug-26 A	27-Oct-26	408d	1,167	584	1,167

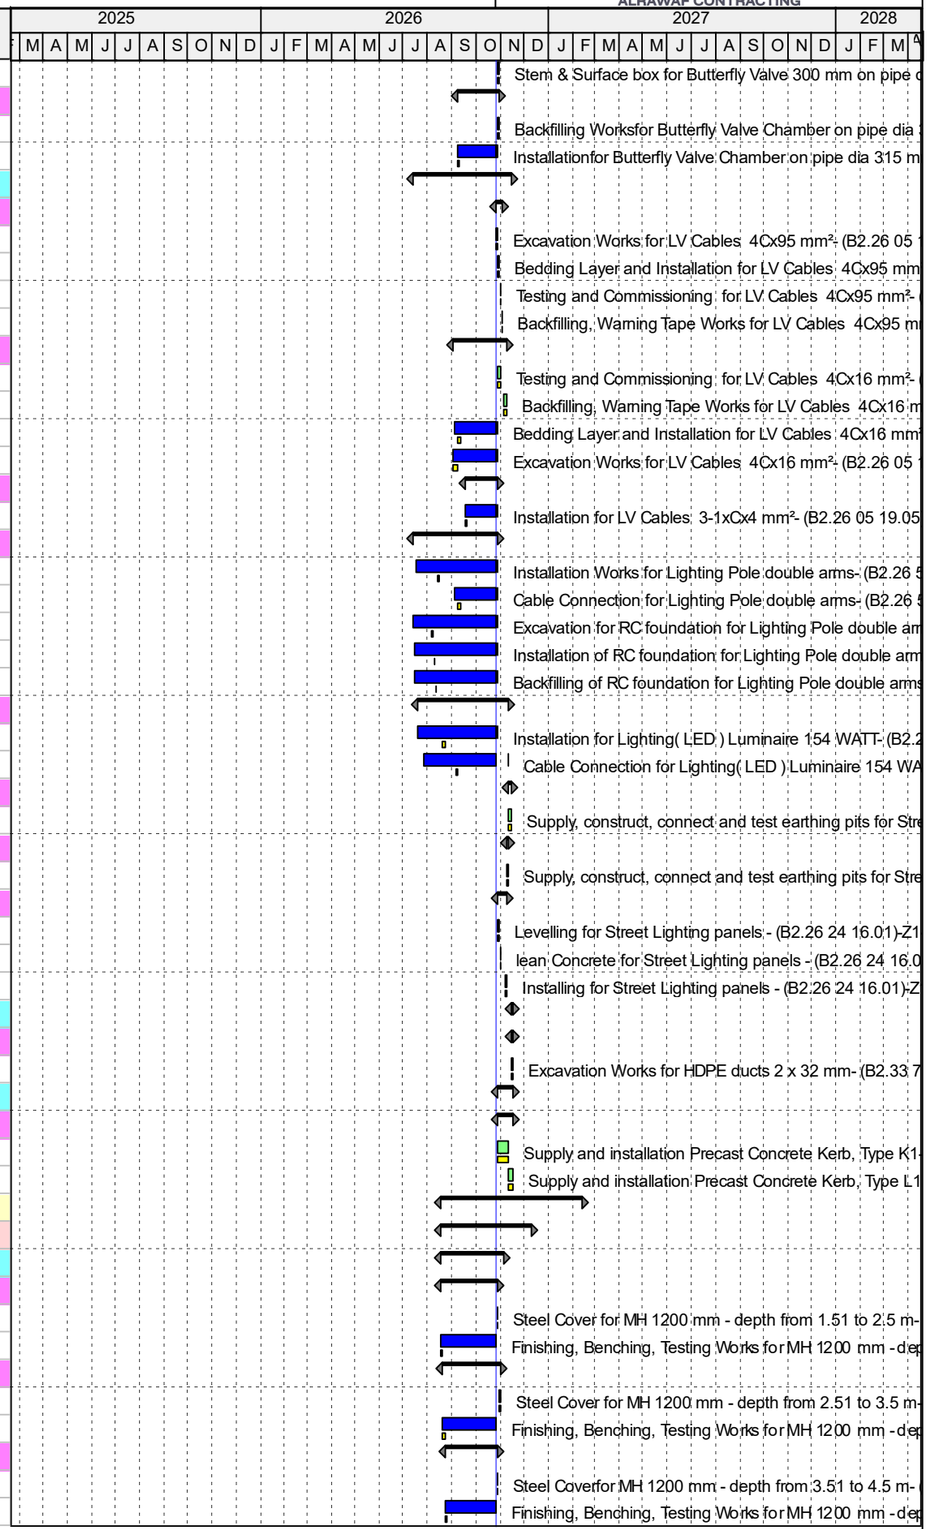


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R21-(SW)-MH Works depth from 3.51 to 4.5 Diam	58d	23-Aug-26 A	01-Nov-26	408d	2,154	685	2,154
	Steel Cover for MH 1200 mm - depth from 3.51 to 4.5 m- (B5.3	2d	31-Oct-26	01-Nov-26	408d	783	0	783
	Finishing, Benching Works for MH 1200 mm - depth from 3.51 t	2d	23-Aug-26 A	27-Oct-26	410d	1,371	685	1,371
	JDH3-02-009-R21-(SW)-MH Works depth from 4.51 to 5.5 Diam	54d	23-Aug-26 A	29-Oct-26	420d	2,013	641	2,013
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	2d	28-Oct-26	29-Oct-26	420d	732	0	732
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	23-Aug-26 A	27-Oct-26	412d	1,281	641	1,281
	JDH3-02-009-R21-(SW)-MH Works depth from 4.51 to 5.5 Diam	52d	23-Aug-26 A	29-Oct-26	420d	2,343	746	2,343
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	2d	28-Oct-26	29-Oct-26	420d	852	0	852
	Finishing, Benching Works for MH 1200 mm - depth from 4.51 t	2d	23-Aug-26 A	27-Oct-26	412d	1,491	746	1,491
	JDH3-02-009-R21-(SW)-MH Works depth from 5.51 to 6.5 Diam	54d	23-Aug-26 A	03-Nov-26	408d	2,250	716	2,250
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	2d	02-Nov-26	03-Nov-26	408d	818	0	818
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	23-Aug-26 A	27-Oct-26	412d	1,432	716	1,432
	JDH3-02-009-R21-(SW)-MH Works depth from 5.51 to 6.5 Diam	54d	23-Aug-26 A	05-Nov-26	408d	2,580	821	2,580
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	2d	04-Nov-26	05-Nov-26	408d	938	0	938
	Finishing, Benching Works for MH 1200 mm - depth from 5.51 t	2d	23-Aug-26 A	27-Oct-26	414d	1,642	821	1,642
	JDH3-02-009-R21-Storm Network - ST	6d	27-Oct-26	02-Nov-26	417d	11,086	0	11,086
	JDH3-02-009-R21-(ST)-MH Works (1200) mm diameter depth fro	4d	27-Oct-26	31-Oct-26	419d	2,104	0	2,104
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	419d	1,402	0	1,402
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2d	29-Oct-26	31-Oct-26	419d	701	0	701
	JDH3-02-009-R21-(ST)-MH Works (2000) mm diameter depth fro	4d	27-Oct-26	31-Oct-26	415d	6,228	0	6,228
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	27-Oct-26	28-Oct-26	415d	4,101	0	4,101
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	415d	2,127	0	2,127
	JDH3-02-009-R21-(ST)-MH Works (1500) mm diameter depth fro	4d	29-Oct-26	02-Nov-26	415d	2,754	0	2,754
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	29-Oct-26	31-Oct-26	415d	1,836	0	1,836
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2d	01-Nov-26	02-Nov-26	415d	918	0	918
	JDH3-02-009-R21-TSE Network - TSE	8d	27-Oct-26	04-Nov-26	370d	35,502	0	35,502
	JDH3-02-009-R152-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4d	27-Oct-26	31-Oct-26	372d	14,564	0	14,564
	Installation for Wash-Out Valve 100 mm on pipe dia 110 mm- (E	2d	27-Oct-26	28-Oct-26	372d	13,108	0	13,108
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 1	2d	29-Oct-26	31-Oct-26	372d	1,456	0	1,456
	JDH3-02-009-R152-(TSE)-Wash-Out Chamber on 110 mm dia pip	8d	27-Oct-26	04-Nov-26	370d	20,938	0	20,938
	Excavation+Bedding for Wash-Out Chamber on pipe dia 110 m	2d	27-Oct-26	28-Oct-26	370d	3,141	0	3,141
	PC Worksfor Wash-Out Chamber on pipe dia 110 mm - depth fr	2d	29-Oct-26	31-Oct-26	370d	2,094	0	2,094
	Installationfor Wash-Out Chamber on pipe dia 110 mm - depth	2d	01-Nov-26	02-Nov-26	370d	11,516	0	11,516
	Backfilling Worksfor Wash-Out Chamber on pipe dia 110 mm - c	2d	03-Nov-26	04-Nov-26	370d	4,188	0	4,188
	JDH3-02-009-R21-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R21-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R21-W	2d	27-Oct-26	28-Oct-26	421d	4,397	0	4,397
	JDH3-02-009-R21-Electrical Network - EL	66d	18-Aug-26 A	04-Nov-26	387d	196,180	38,170	196,180
	JDH3-02-009-R21-(EL)-MV cable trench size 1.5m wide and 80c	10d	18-Aug-26 A	31-Oct-26	389d	7,859	2,358	7,859
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	5d	18-Aug-26 A	31-Oct-26	387d	4,715	1,415	4,715
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5d	23-Aug-26 A	31-Oct-26	389d	3,143	943	3,143
	JDH3-02-009-R21-(EL)-RMU 33 KV	6d	28-Oct-26	04-Nov-26	387d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R21-EL	2d	28-Oct-26	31-Oct-26	387d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R21-EL	2d	31-Oct-26	02-Nov-26	387d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2d	02-Nov-26	04-Nov-26	387d	4,925	0	4,925
	JDH3-02-009-R21-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7d	19-Aug-26 A	31-Oct-26	389d	119,376	35,813	119,376
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	3d	19-Aug-26 A	31-Oct-26	387d	105,515	31,654	105,515
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	20-Aug-26 A	31-Oct-26	389d	8,701	2,610	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	22-Aug-26 A	31-Oct-26	389d	5,160	1,548	5,160
	JDH3-02-009-R21-Street Lighting Network -SL	21d	27-Oct-26	21-Nov-26	397d	310,515	0	310,515
	JDH3-02-009-R21-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	4d	27-Oct-26	31-Oct-26	403d	44,211	0	44,211
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2d	27-Oct-26	28-Oct-26	403d	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2d	29-Oct-26	31-Oct-26	403d	3,401	0	3,401

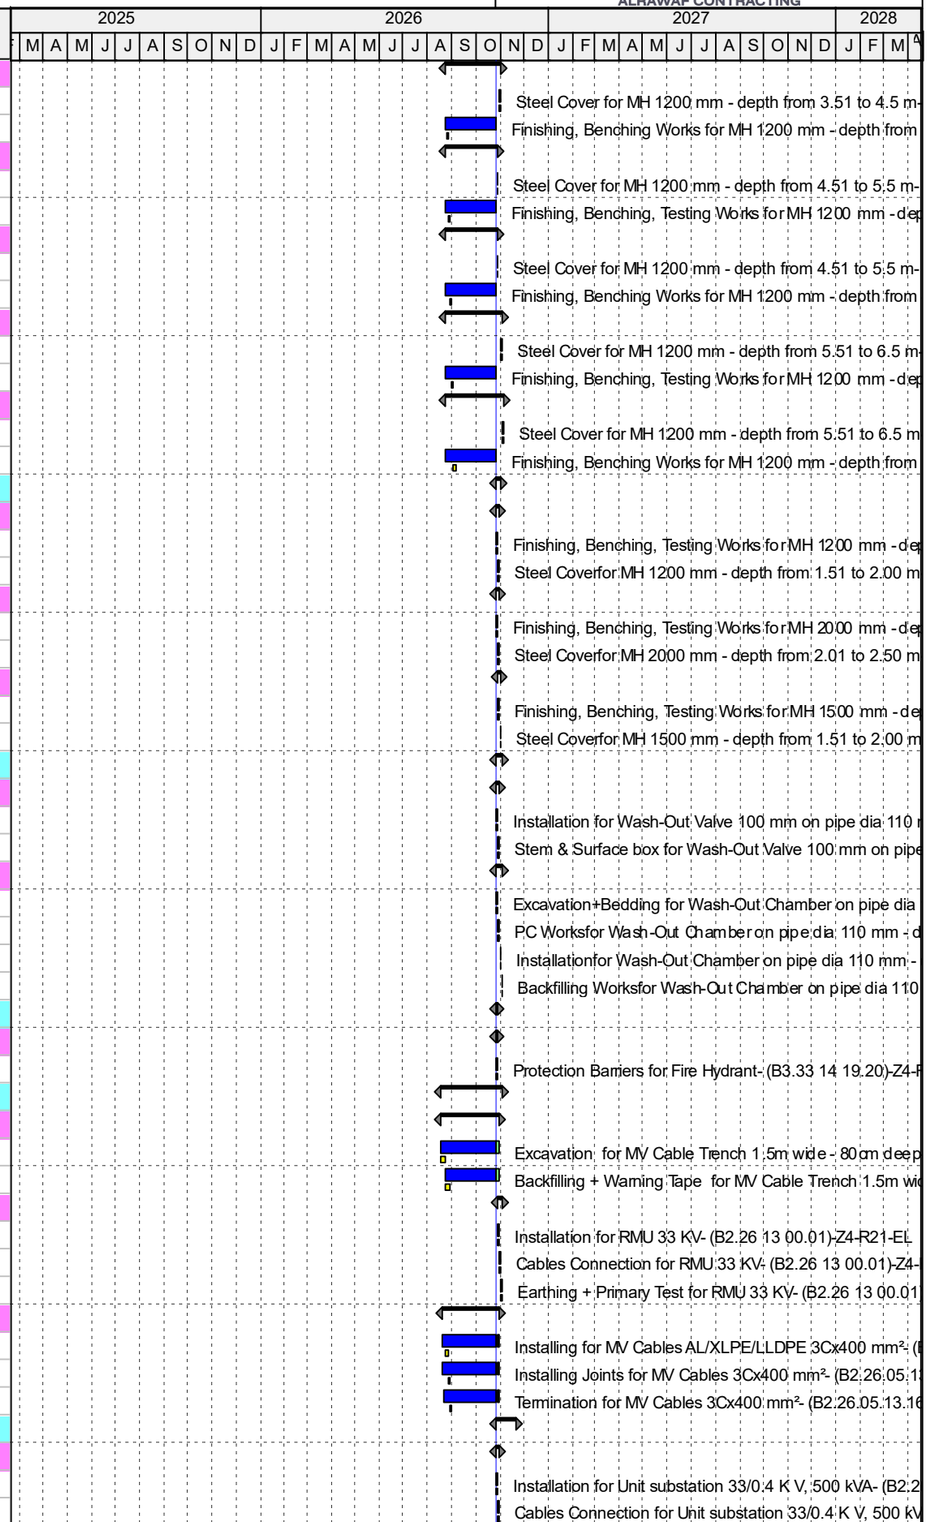


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 4Cx95mm², Cu/XLPE	9d	09-Nov-26	19-Nov-26	398d	101,716	0	101,716
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	3d	09-Nov-26	12-Nov-26	388d	11,302	0	11,302
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	3d	12-Nov-26	16-Nov-26	398d	84,763	0	84,763
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	3d	16-Nov-26	19-Nov-26	398d	5,651	0	5,651
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 3x1Cx50mm², Cu/XL	2d	01-Nov-26	02-Nov-26	403d	1,431	0	1,431
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z4-F	2d	01-Nov-26	02-Nov-26	403d	1,431	0	1,431
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 4Cx16mm², Cu/XLPE	6d	12-Nov-26	19-Nov-26	388d	35,321	0	35,321
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	3d	12-Nov-26	16-Nov-26	388d	4,155	0	4,155
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	3d	16-Nov-26	19-Nov-26	388d	31,166	0	31,166
	JDH3-02-009-R21-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2d	16-Nov-26	18-Nov-26	387d	2,423	0	2,423
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z4-R	2d	16-Nov-26	18-Nov-26	387d	2,423	0	2,423
	JDH3-02-009-R21-(SL)-Lighting Pole with single arm 12 m heigh	14d	04-Nov-26	21-Nov-26	393d	63,784	0	63,784
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	2d	04-Nov-26	07-Nov-26	387d	6,378	0	6,378
	Installation of RC foundation for Lighting Pole single arm- (B2.2	2d	07-Nov-26	09-Nov-26	387d	6,378	0	6,378
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	2d	09-Nov-26	11-Nov-26	387d	6,378	0	6,378
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	4d	11-Nov-26	16-Nov-26	387d	41,460	0	41,460
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	4d	16-Nov-26	21-Nov-26	393d	3,189	0	3,189
	JDH3-02-009-R21-(SL)- LV Distribution Panel Main: 100A, MCCB	2d	27-Oct-26	28-Oct-26	406d	1,837	0	1,837
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z4-R21-S	2d	27-Oct-26	28-Oct-26	406d	1,837	0	1,837
	JDH3-02-009-R21-(SL)- LV Cables - Aluminium, 4Cx185mm², ALU	4d	07-Nov-26	11-Nov-26	401d	970	0	970
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2d	07-Nov-26	09-Nov-26	388d	114	0	114
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2d	09-Nov-26	11-Nov-26	401d	855	0	855
	JDH3-02-009-R21-(SL)-RMU 33 KV	8d	27-Oct-26	04-Nov-26	403d	58,823	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z4-R21-SL	2d	27-Oct-26	28-Oct-26	405d	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z4-R21-SL	2d	29-Oct-26	31-Oct-26	405d	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z4-R2	2d	03-Nov-26	04-Nov-26	403d	4,202	0	4,202
	JDH3-02-009-R21-Telecommunications Network - TEL	8d	27-Oct-26	04-Nov-26	415d	129,372	0	129,372
	JDH3-02-009-R21-(TEL)-Ducts	8d	27-Oct-26	04-Nov-26	415d	19,984	0	19,984
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2d	27-Oct-26	28-Oct-26	356d	2,998	0	2,998
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	4d	29-Oct-26	02-Nov-26	415d	14,988	0	14,988
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2d	03-Nov-26	04-Nov-26	415d	1,998	0	1,998
	JDH3-02-009-R21-(TEL)-Manhole Type 1	6d	29-Oct-26	04-Nov-26	411d	54,694	0	54,694
	Excavation and Bedding Works for MH Type 1 Dim 2000*1000*	2d	29-Oct-26	31-Oct-26	411d	8,204	0	8,204
	Installation for MH Type 1 Dim 2000*1000*1000 mm- (B2.33.71	2d	01-Nov-26	02-Nov-26	411d	41,021	0	41,021
	Backfilling Works for MH Type 1 Dim 2000*1000*1000 mm- (B2.	2d	03-Nov-26	04-Nov-26	411d	5,469	0	5,469
	JDH3-02-009-R21-(TEL)-Manhole Type 2	6d	29-Oct-26	04-Nov-26	356d	54,694	0	54,694
	Excavation and Bedding Works for MH Type 2 Dim 2000*1000*	2d	29-Oct-26	31-Oct-26	356d	8,204	0	8,204
	Installation for MH Type 2 Dim 2000*1000*1000 mm- (B2.33.71	2d	01-Nov-26	02-Nov-26	356d	41,021	0	41,021
	Backfilling Works for MH Type 2 Dim 2000*1000*1000 mm- (B2.	2d	03-Nov-26	04-Nov-26	356d	5,469	0	5,469
	JDH3-02-009-R21-Road Works - RD	60d	26-Sep-26 A	10-Dec-26	384d	125,062	12,990	436,046
	JDH3-02-009-R21-(RD)-Bituminous concrete wearing course 50	5d	06-Dec-26	10-Dec-26	356d	0	0	307,786
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	06-Dec-26	10-Dec-26	356d	0	0	307,786
	JDH3-02-009-R21-(RD)-Precast Concrete Curb	40d	26-Sep-26 A	17-Nov-26	356d	125,062	12,990	125,062
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	05-Nov-26	07-Nov-26	356d	15,872	0	15,872
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9d	08-Nov-26	17-Nov-26	356d	57,229	0	57,229
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	7d	26-Sep-26 A	04-Nov-26	356d	51,960	12,990	51,960
	JDH3-02-009-R21-(RD)-Pavement Marking	4d	06-Dec-26	09-Dec-26	385d	0	0	3,197
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	06-Dec-26	09-Dec-26	385d	0	0	3,197
R22		153d	18-Aug-26 A	13-Feb-27	329d	293,744	2,899	506,624
	JDH3-02-009-R22-Sewage Network - SW	72d	18-Aug-26 A	10-Nov-26	408d	8,759	2,899	8,759
	JDH3-02-009-R22-(SW)-MH Works depth from 1.51 to 2.5 Diam	70d	18-Aug-26 A	08-Nov-26	408d	1,334	424	1,334
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.33	2d	07-Nov-26	08-Nov-26	408d	485	0	485
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	18-Aug-26 A	27-Oct-26	416d	849	424	849

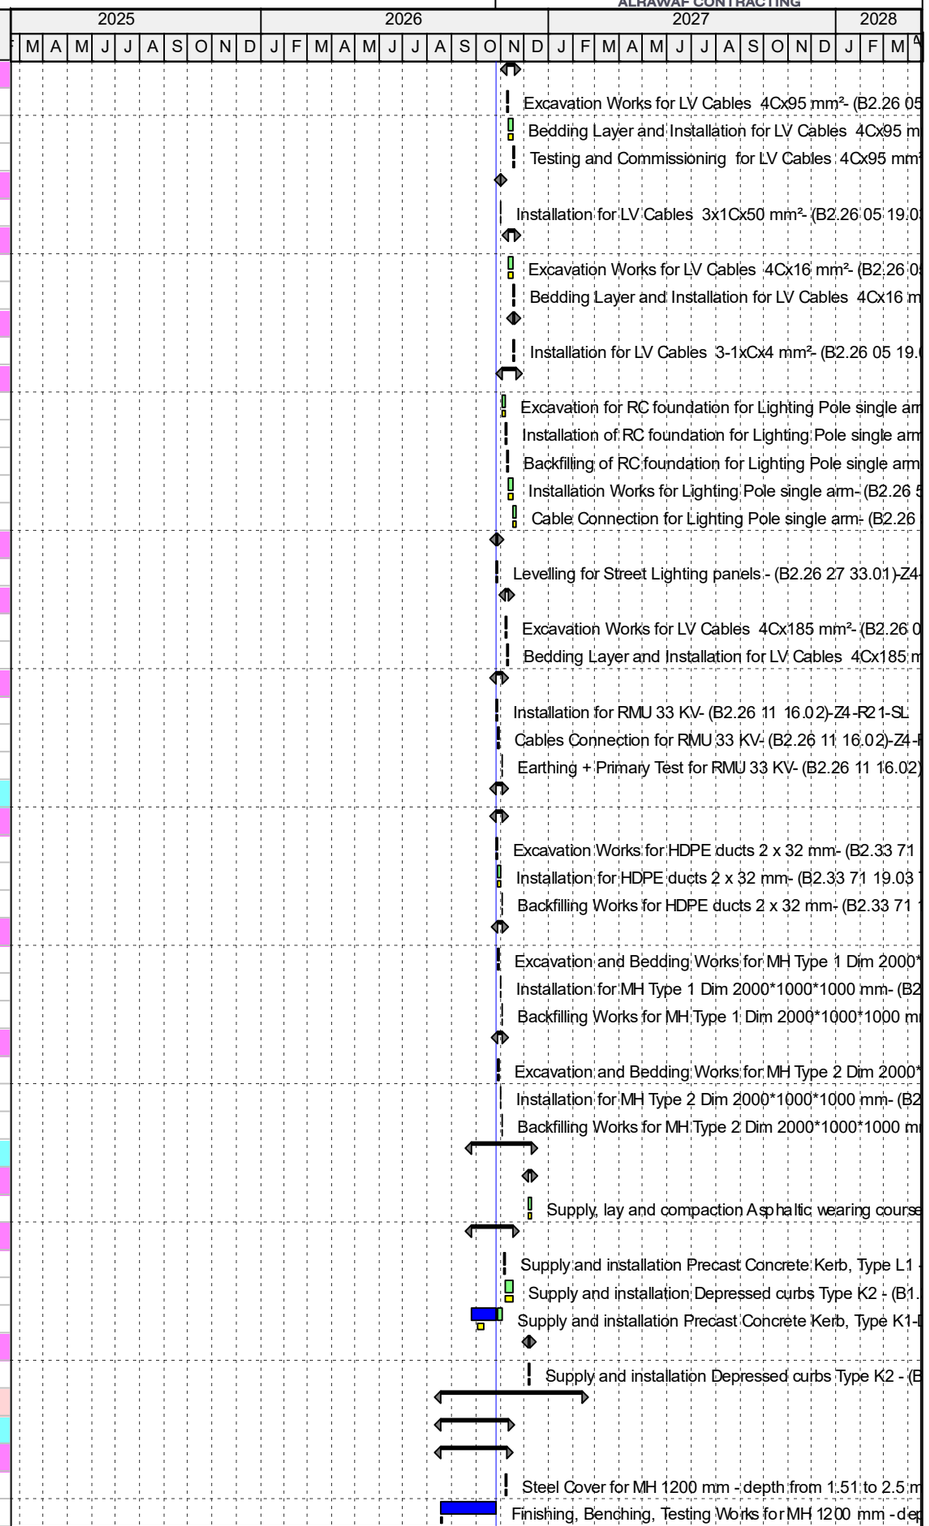


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R22-(SW)-MH Works depth from 2.51 to 3.5 Diam	70d	20-Aug-26 A	10-Nov-26	408d	7,425	2,475	7,425
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3	2d	09-Nov-26	10-Nov-26	408d	2,475	0	2,475
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	20-Aug-26 A	27-Oct-26	418d	4,950	2,475	4,950
	JDH3-02-009-R22-Storm Network - ST	8d	27-Oct-26	04-Nov-26	415d	6,206	0	6,206
	JDH3-02-009-R22-(ST)-MH Works (1200) mm diameter depth fro	4d	27-Oct-26	31-Oct-26	419d	1,091	0	1,091
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	419d	701	0	701
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2d	29-Oct-26	31-Oct-26	419d	390	0	390
	JDH3-02-009-R22-(ST)-MH Works (2000) mm diameter depth fro	4d	27-Oct-26	31-Oct-26	415d	2,127	0	2,127
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	27-Oct-26	28-Oct-26	415d	1,367	0	1,367
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2d	29-Oct-26	31-Oct-26	415d	760	0	760
	JDH3-02-009-R22-(ST)-MH Works (1500) mm diameter depth fro	4d	29-Oct-26	02-Nov-26	415d	1,428	0	1,428
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	29-Oct-26	31-Oct-26	415d	918	0	918
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2d	01-Nov-26	02-Nov-26	415d	510	0	510
	JDH3-02-009-R22-(ST)-MH Works (1500) mm diameter depth fro	4d	01-Nov-26	04-Nov-26	415d	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	01-Nov-26	02-Nov-26	415d	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	03-Nov-26	04-Nov-26	415d	557	0	557
	JDH3-02-009-R22-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	2,931	0	2,931
	JDH3-02-009-R22-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	2,931	0	2,931
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R22-W	2d	27-Oct-26	28-Oct-26	421d	2,931	0	2,931
	JDH3-02-009-R22-Electrical Network - EL	12d	27-Oct-26	09-Nov-26	324d	205,764	0	205,764
	JDH3-02-009-R22-(EL)-MV cable trench size 1.5m wide and 80c	11d	27-Oct-26	08-Nov-26	325d	5,449	0	5,449
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	3d	27-Oct-26	29-Oct-26	324d	3,270	0	3,270
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3d	05-Nov-26	08-Nov-26	325d	2,180	0	2,180
	JDH3-02-009-R22-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7d	31-Oct-26	07-Nov-26	324d	131,369	0	131,369
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	3d	31-Oct-26	02-Nov-26	324d	120,087	0	120,087
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	03-Nov-26	04-Nov-26	324d	8,701	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	05-Nov-26	07-Nov-26	324d	2,580	0	2,580
	JDH3-02-009-R22-(EL)-RMU 33 KV	12d	27-Oct-26	09-Nov-26	324d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R22-EL	2d	27-Oct-26	28-Oct-26	330d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R22-EL	2d	29-Oct-26	31-Oct-26	330d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2d	08-Nov-26	09-Nov-26	324d	4,925	0	4,925
	JDH3-02-009-R22-Street Lighting Network -SL	10d	10-Nov-26	21-Nov-26	333d	70,085	0	70,085
	JDH3-02-009-R22-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	10d	10-Nov-26	21-Nov-26	333d	59,580	0	59,580
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	10-Nov-26	15-Nov-26	324d	7,009	0	7,009
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	16-Nov-26	21-Nov-26	333d	52,570	0	52,570
	JDH3-02-009-R22-(SL)-Lighting Pole with single arm 12 m heigh	3d	16-Nov-26	18-Nov-26	324d	10,506	0	10,506
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3d	16-Nov-26	18-Nov-26	324d	10,506	0	10,506
	JDH3-02-009-R22-Road Works - RD	17d	25-Jan-27	13-Feb-27	324d	0	0	212,880
	JDH3-02-009-R22-(RD)-Bituminous concrete wearing course 50	3d	25-Jan-27	27-Jan-27	324d	0	0	194,813
	Supply, lay and compaction Asphaltic wearing course 50 mm in	3d	25-Jan-27	27-Jan-27	324d	0	0	194,813
	JDH3-02-009-R22-(RD)-Pavement Marking	14d	28-Jan-27	13-Feb-27	324d	0	0	8,485
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	28-Jan-27	30-Jan-27	324d	0	0	2,995
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	31-Jan-27	01-Feb-27	324d	0	0	356
	Thermoplastic continuous 100 mm wide (parking separator line)	2d	02-Feb-27	03-Feb-27	324d	0	0	846
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	04-Feb-27	06-Feb-27	324d	0	0	1,901
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2d	07-Feb-27	08-Feb-27	324d	0	0	1,013
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	09-Feb-27	10-Feb-27	324d	0	0	802
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z4-R22-RD	2d	11-Feb-27	13-Feb-27	324d	0	0	572
	JDH3-02-009-R22-(RD)-Traffic Signage	2d	28-Jan-27	30-Jan-27	336d	0	0	9,582
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2d	28-Jan-27	30-Jan-27	336d	0	0	9,582
R231		95d	18-Aug-26 A	07-Dec-26	387d	835,590	97,300	1,315,036
	JDH3-02-009-R231-Sewage Network - SW	74d	18-Aug-26 A	12-Nov-26	408d	12,077	4,001	12,077
	JDH3-02-009-R231-(SW)-MH Works depth from 0 to 1.50 Diam 1	62d	18-Aug-26 A	29-Oct-26	418d	3,201	1,067	3,201

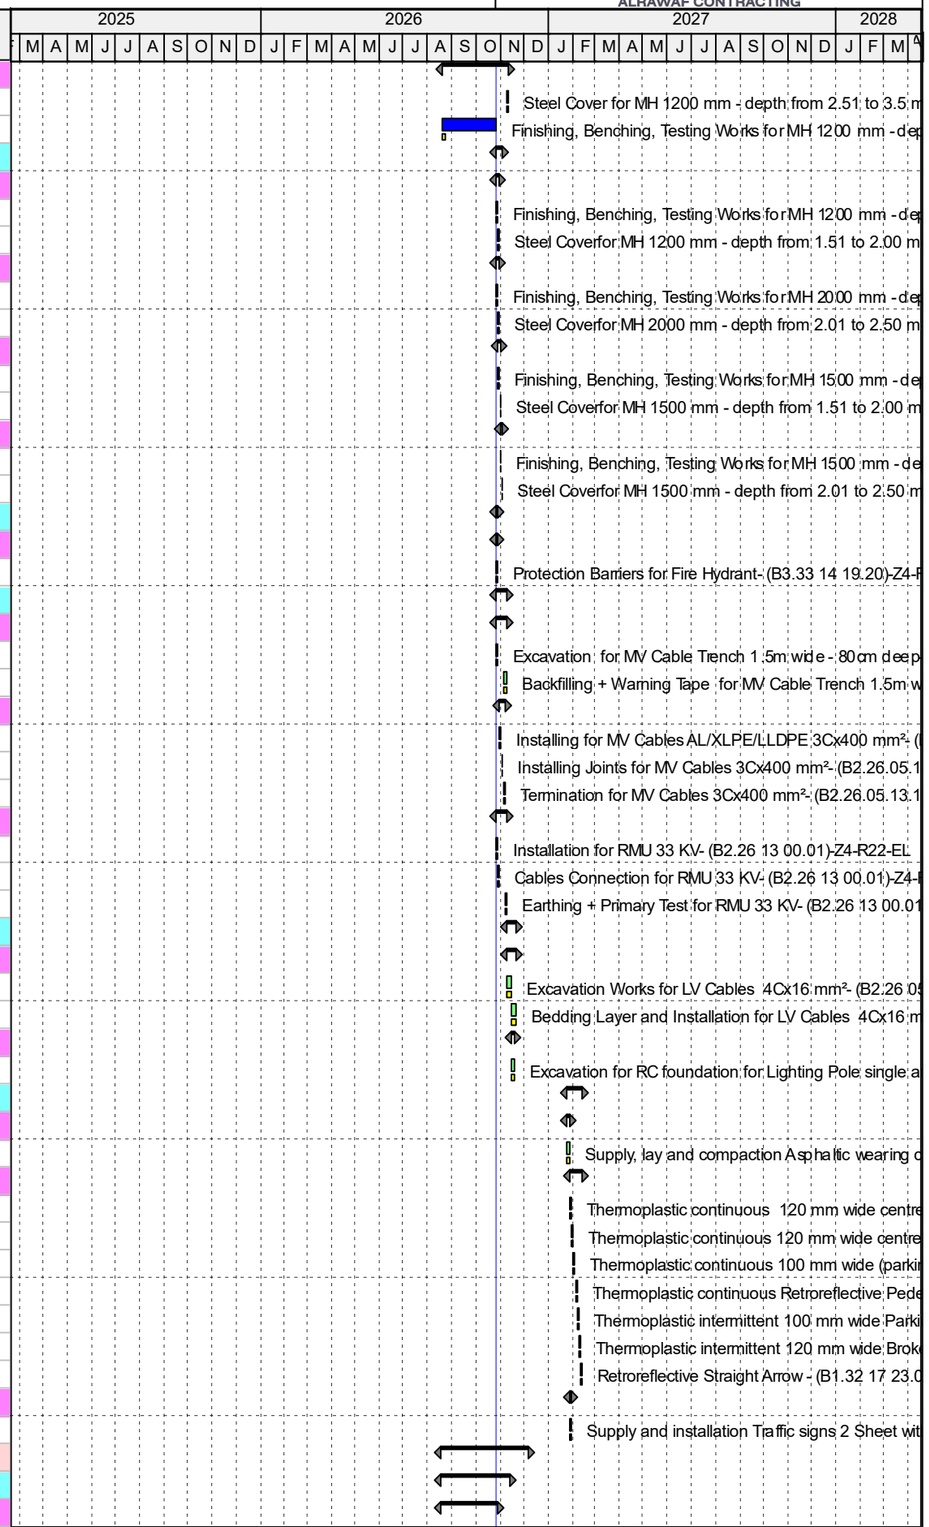

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Steel Cover for MH 1200 mm - depth from 0 to 1.5 m- (B5.33 05	2d	28-Oct-26	29-Oct-26	418d	1,067	0	1,067
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	18-Aug-26 A	27-Oct-26	418d	2,134	1,067	2,134
	JDH3-02-009-R231-(SW)-MH Works depth from 1.51 to 2.5 Diam	62d	20-Aug-26 A	01-Nov-26	418d	7,274	2,425	7,274
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.33	2d	31-Oct-26	01-Nov-26	418d	2,425	0	2,425
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	20-Aug-26 A	27-Oct-26	420d	4,850	2,425	4,850
	JDH3-02-009-R231-(SW)-MH Works depth from 2.51 to 3.5 Diam	70d	23-Aug-26 A	12-Nov-26	408d	1,601	510	1,601
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.33	2d	11-Nov-26	12-Nov-26	408d	582	0	582
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	23-Aug-26 A	27-Oct-26	420d	1,019	510	1,019
	JDH3-02-009-R231-Storm Network - ST	10d	27-Oct-26	07-Nov-26	413d	10,457	0	10,457
	JDH3-02-009-R231-(ST)-MH Works (1500) mm diameter depth fr	6d	27-Oct-26	02-Nov-26	413d	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	415d	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	01-Nov-26	02-Nov-26	413d	557	0	557
	JDH3-02-009-R231-(ST)-MH Works (2000) mm diameter depth fr	6d	29-Oct-26	04-Nov-26	413d	2,127	0	2,127
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	29-Oct-26	31-Oct-26	415d	1,367	0	1,367
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2d	03-Nov-26	04-Nov-26	413d	760	0	760
	JDH3-02-009-R231-(ST)-MH Works (2000) mm diameter depth fr	6d	01-Nov-26	07-Nov-26	413d	6,770	0	6,770
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	01-Nov-26	02-Nov-26	415d	4,459	0	4,459
	Steel Coverfor MH 2000 mm - depth from 2.51 to 3.00 m- (B6.3	2d	05-Nov-26	07-Nov-26	413d	2,312	0	2,312
	JDH3-02-009-R231-TSE Network - TSE	6d	27-Oct-26	02-Nov-26	417d	35,502	0	35,502
	JDH3-02-009-R231-(TSE)-Wash-Out Chamber on 110 mm dia pip	6d	27-Oct-26	02-Nov-26	417d	20,938	0	20,938
	Excavation+Bedding for Wash-Out Chamber on pipe dia 110 m	2d	27-Oct-26	28-Oct-26	417d	3,141	0	3,141
	PC Worksfor Wash-Out Chamber on pipe dia 110 mm - depth fr	2d	29-Oct-26	31-Oct-26	417d	2,094	0	2,094
	Installationfor Wash-Out Chamber on pipe dia 110 mm - depth	2d	01-Nov-26	02-Nov-26	417d	11,516	0	11,516
	Backfilling Worksfor Wash-Out Chamber on pipe dia 110 mm - c	2d	01-Nov-26	02-Nov-26	374d	4,188	0	4,188
	JDH3-02-009-R231-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4d	27-Oct-26	31-Oct-26	374d	14,564	0	14,564
	Installation for Wash-Out Valve 100 mm on pipe dia 110 mm- (E	2d	27-Oct-26	28-Oct-26	374d	13,108	0	13,108
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 1	2d	29-Oct-26	31-Oct-26	374d	1,456	0	1,456
	JDH3-02-009-R231-Potable Water Network - WT	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R231-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R231-W	2d	27-Oct-26	28-Oct-26	421d	4,885	0	4,885
	JDH3-02-009-R231-Electrical Network - EL	64d	18-Aug-26 A	08-Nov-26	373d	442,139	93,298	442,139
	JDH3-02-009-R231-(EL)-MV cable trench size 1.5m wide and 80	15d	18-Aug-26 A	03-Nov-26	373d	301	75	301
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	2d	18-Aug-26 A	02-Nov-26	374d	181	45	181
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	2d	23-Aug-26 A	03-Nov-26	373d	120	30	120
	JDH3-02-009-R231-(EL)-MV cables AL/XLPE/LLDPE Unarmored	13d	19-Aug-26 A	03-Nov-26	375d	372,892	93,223	372,892
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.0	9d	19-Aug-26 A	03-Nov-26	373d	361,611	90,403	361,611
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	20-Aug-26 A	03-Nov-26	373d	8,701	2,175	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	22-Aug-26 A	03-Nov-26	375d	2,580	645	2,580
	JDH3-02-009-R231-(EL)-RMU 33 KV	11d	27-Oct-26	08-Nov-26	373d	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R231-EL	2d	27-Oct-26	28-Oct-26	378d	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R231-E	2d	03-Nov-26	05-Nov-26	373d	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2d	05-Nov-26	08-Nov-26	373d	4,925	0	4,925
	JDH3-02-009-R231-Street Lighting Network -SL	10d	08-Nov-26	19-Nov-26	384d	77,768	0	77,768
	JDH3-02-009-R231-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	10d	08-Nov-26	19-Nov-26	377d	64,163	0	64,163
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	08-Nov-26	14-Nov-26	373d	7,549	0	7,549
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	14-Nov-26	19-Nov-26	377d	56,614	0	56,614
	JDH3-02-009-R231-(SL)- Street Lighting Panels	4d	14-Nov-26	18-Nov-26	385d	3,099	0	3,099
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z4-R231-	2d	14-Nov-26	16-Nov-26	385d	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z4-F	2d	16-Nov-26	18-Nov-26	385d	2,066	0	2,066
	JDH3-02-009-R231-(SL)-Lighting Pole with single arm 12 m heig	3d	14-Nov-26	17-Nov-26	373d	10,506	0	10,506
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3d	14-Nov-26	17-Nov-26	373d	10,506	0	10,506
	JDH3-02-009-R231-Road Works - RD	36d	27-Oct-26	07-Dec-26	383d	252,762	0	732,208
	JDH3-02-009-R231-(RD)-Bituminous concrete wearing course 5(	5d	17-Nov-26	22-Nov-26	376d	0	0	346,546

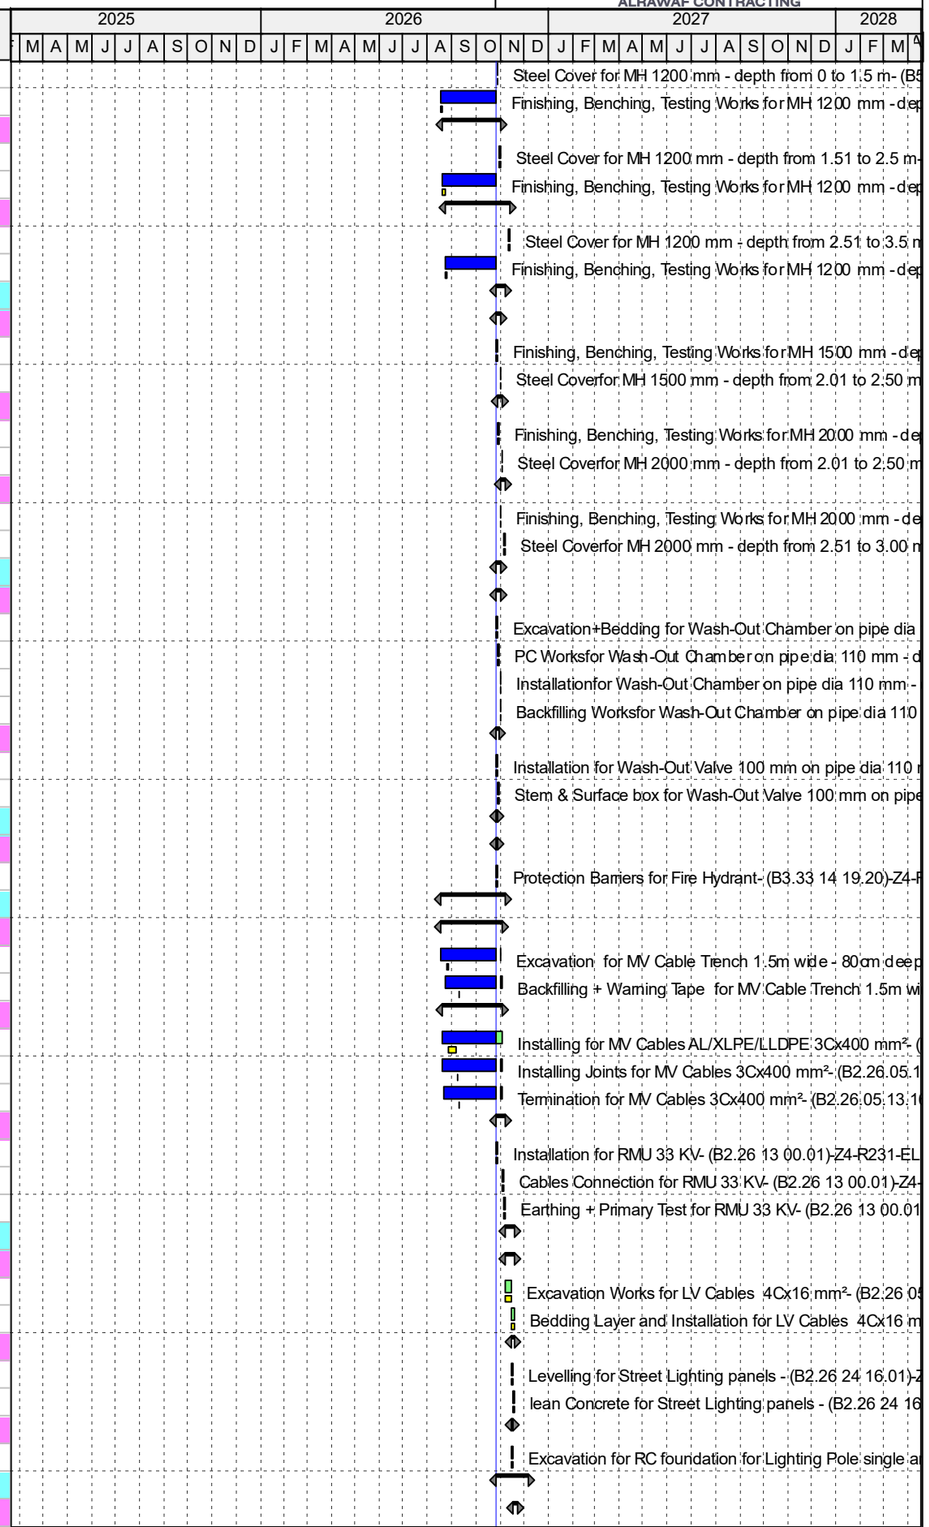


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	17-Nov-26	22-Nov-26	376d	0	0	346,546
	JDH3-02-009-R231-(RD)-Precast Concrete Curb	19d	27-Oct-26	17-Nov-26	376d	118,301	0	142,495
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8d	27-Oct-26	04-Nov-26	376d	53,533	0	53,533
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3d	05-Nov-26	08-Nov-26	376d	24,444	0	24,444
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8d	09-Nov-26	17-Nov-26	376d	40,323	0	64,518
	JDH3-02-009-R231-(RD)-Precast Interlocking Block Pavers	7d	09-Nov-26	16-Nov-26	376d	134,461	0	188,245
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	7d	09-Nov-26	16-Nov-26	376d	134,461	0	188,245
	JDH3-02-009-R231-(RD)-Pavement Marking	12d	23-Nov-26	06-Dec-26	376d	0	0	10,357
	Thermoplastic continuous 120 mm wide centre lane- double lin	2d	23-Nov-26	24-Nov-26	376d	0	0	4,325
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	25-Nov-26	26-Nov-26	376d	0	0	960
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	28-Nov-26	29-Nov-26	376d	0	0	2,793
	Thermoplastic continuous 100 mm wide (parking separator line)	2d	30-Nov-26	01-Dec-26	376d	0	0	1,200
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2d	02-Dec-26	03-Dec-26	376d	0	0	951
	Thermoplastic continuous Chevron hatching - white (round abou	2d	05-Dec-26	06-Dec-26	376d	0	0	128
	JDH3-02-009-R231-(RD)-Traffic Signage	13d	23-Nov-26	07-Dec-26	383d	0	0	44,564
	Supply and installation Traffic signs 1 Sheet with Single post - (E	9d	23-Nov-26	02-Dec-26	383d	0	0	27,796
	Supply and installation Traffic signs 2 Sheet with Single post - (E	4d	03-Dec-26	07-Dec-26	383d	0	0	16,769
R232		21d	27-Oct-26	19-Nov-26	402d	113,504	0	113,504
JDH3-02-009-R232-Storm Network - ST		4d	27-Oct-26	31-Oct-26	419d	8,703	0	8,703
JDH3-02-009-R232-(ST)-MH Works (1500) mm diameter depth fr		4d	27-Oct-26	31-Oct-26	419d	5,508	0	5,508
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	27-Oct-26	28-Oct-26	419d	3,672	0	3,672
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2d	29-Oct-26	31-Oct-26	419d	1,836	0	1,836
JDH3-02-009-R232-(ST)-MH Works (1200) mm diameter depth fr		4d	27-Oct-26	31-Oct-26	413d	3,194	0	3,194
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	27-Oct-26	28-Oct-26	413d	2,104	0	2,104
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2d	29-Oct-26	31-Oct-26	413d	1,091	0	1,091
JDH3-02-009-R232-Potable Water Network - WT		2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
JDH3-02-009-R232-(WT)-Fire Hydrant		2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R232-V	2d	27-Oct-26	28-Oct-26	421d	5,374	0	5,374
JDH3-02-009-R232-Street Lighting Network -SL		21d	27-Oct-26	19-Nov-26	402d	99,427	0	99,427
JDH3-02-009-R232-(SL)-Lighting Pole with single arm 12 m heig		21d	27-Oct-26	19-Nov-26	340d	86,296	0	86,296
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3d	27-Oct-26	29-Oct-26	340d	8,630	0	8,630
	Installation of RC foundation for Lighting Pole single arm- (B2.2	3d	31-Oct-26	02-Nov-26	340d	8,630	0	8,630
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	3d	03-Nov-26	05-Nov-26	340d	8,630	0	8,630
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	6d	07-Nov-26	12-Nov-26	340d	56,092	0	56,092
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6d	14-Nov-26	19-Nov-26	340d	4,315	0	4,315
JDH3-02-009-R232-(SL)-Street Lighting(LED) Luminaire comple		4d	14-Nov-26	17-Nov-26	404d	13,131	0	13,131
	Installation for Lighting(LED) Luminaire 114 WATT- (B2.26.56.1	2d	14-Nov-26	15-Nov-26	404d	10,505	0	10,505
	Cable Connection for Lighting(LED) Luminaire 114 WATT- (B2.	2d	16-Nov-26	17-Nov-26	404d	2,626	0	2,626
R45		98d	07-Jul-26 A	17-Nov-26	404d	74,608	607,073	1,810,102
R450		19d	27-Oct-26	17-Nov-26	0d	0	0	403,253
JDH3-02-009-R450-Road Works - RD		19d	27-Oct-26	17-Nov-26	0d	0	0	403,253
JDH3-02-009-R450-(RD)-Bituminous base course 200 mm Two l		4d	01-Nov-26	04-Nov-26	0d	0	0	223,035
	Supply, lay and Asphaltic base course including tack Coat (RC2)	2d	03-Nov-26	04-Nov-26	0d	0	0	111,517
	Supply, lay and Asphaltic base course including Prime Coat (MC	2d	01-Nov-26	02-Nov-26	0d	0	0	111,517
JDH3-02-009-R450-(RD)-Subgrade		2d	27-Oct-26	28-Oct-26	0d	0	0	27,243
	Supply, lay and compaction subgrade compacted thickness 300	2d	27-Oct-26	28-Oct-26	0d	0	0	27,243
JDH3-02-009-R450-(RD)-Bituminous concrete wearing course 5		2d	16-Nov-26	17-Nov-26	0d	0	0	54,713
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2d	16-Nov-26	17-Nov-26	0d	0	0	54,713
JDH3-02-009-R450-(RD)-Precast Concrete Curb		5d	05-Nov-26	10-Nov-26	0d	0	0	27,935
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	2d	05-Nov-26	07-Nov-26	0d	0	0	6,376
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3d	08-Nov-26	10-Nov-26	0d	0	0	21,559
JDH3-02-009-R450-(RD)-Precast Interlocking Block Pavers		4d	11-Nov-26	15-Nov-26	0d	0	0	37,971
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	4d	11-Nov-26	15-Nov-26	0d	0	0	37,971

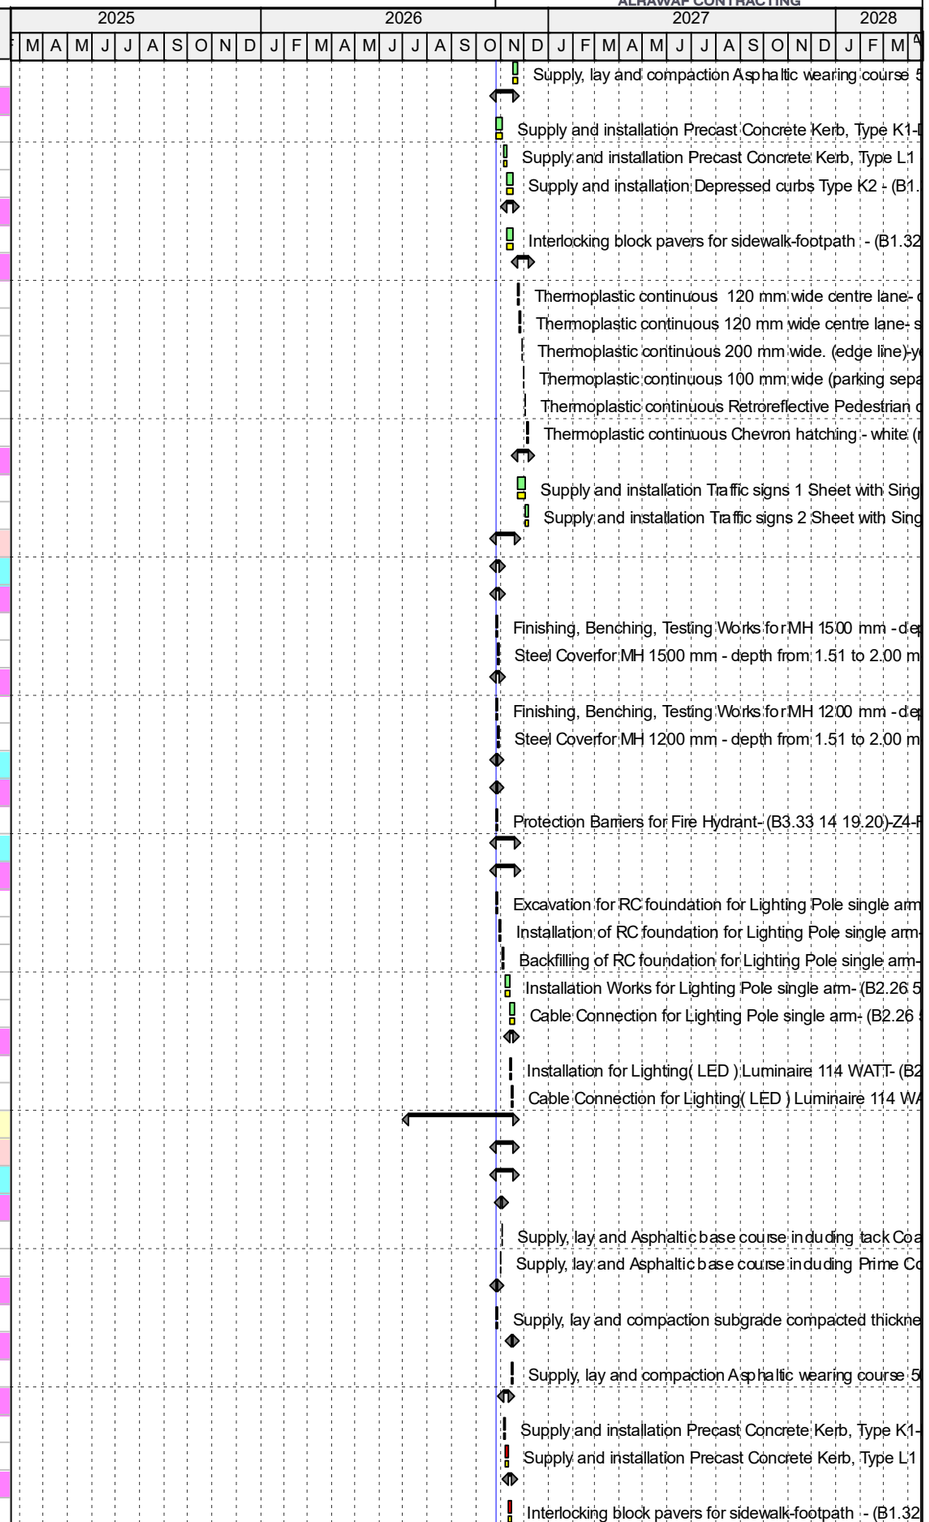

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R450-(RD)-Aggregate Base Course	2d	29-Oct-26	31-Oct-26	0d	0	0	32,356
	Supply, lay and compaction Aggregate base course compacted	2d	29-Oct-26	31-Oct-26	0d	0	0	32,356
R451		59d	08-Sep-26 A	17-Nov-26	399d	0	124,795	578,594
	JDH3-02-009-R451-Road Works - RD	59d	08-Sep-26 A	17-Nov-26	397d	0	124,795	568,364
	JDH3-02-009-R451-(RD)-Bituminous base course 200 mm Two l	4d	12-Sep-26 A	28-Oct-26	384d	0	96,688	297,502
	Supply, lay and Asphaltic base course including Prime Coat (MC	2d	12-Sep-26 A	28-Oct-26	369d	0	44,625	148,751
	Supply, lay and Asphaltic base course including tack Coat (RC2)	2d	13-Sep-26 A	28-Oct-26	384d	0	52,063	148,751
	JDH3-02-009-R451-(RD)-Subgrade	2d	08-Sep-26 A	28-Oct-26	369d	0	12,829	36,655
	Supply, lay and compaction subgrade compacted thickness 30(	2d	08-Sep-26 A	28-Oct-26	369d	0	12,829	36,655
	JDH3-02-009-R451-(RD)-Bituminous concrete wearing course 5	2d	15-Nov-26	17-Nov-26	369d	0	0	72,981
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2d	15-Nov-26	17-Nov-26	369d	0	0	72,981
	JDH3-02-009-R451-(RD)-Precast Concrete Curb	9d	28-Oct-26	08-Nov-26	405d	0	0	63,065
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	5d	28-Oct-26	03-Nov-26	369d	0	0	35,191
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	03-Nov-26	08-Nov-26	369d	0	0	21,323
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	03-Nov-26	08-Nov-26	405d	0	0	6,550
	JDH3-02-009-R451-(RD)-Precast Interlocking Block Pavers	6d	08-Nov-26	15-Nov-26	369d	0	0	54,510
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	6d	08-Nov-26	15-Nov-26	369d	0	0	54,510
	JDH3-02-009-R451-(RD)-Aggregate Base Course	2d	10-Sep-26 A	28-Oct-26	369d	0	15,278	43,651
	Supply, lay and compaction Aggregate base course compacted	2d	10-Sep-26 A	28-Oct-26	369d	0	15,278	43,651
	JDH3-02-009-R451-Landscape Works - LS	2d	08-Nov-26	10-Nov-26	405d	0	0	10,230
	JDH3-02-009-R451-(LS)-Miscellaneous Landscaping Items	2d	08-Nov-26	10-Nov-26	405d	0	0	10,230
	Sand hill in the roundabout with with natural height made from (	2d	08-Nov-26	10-Nov-26	405d	0	0	10,230
R452		17d	27-Oct-26	15-Nov-26	400d	0	0	146,987
	JDH3-02-009-R452-Road Works - RD	17d	27-Oct-26	15-Nov-26	400d	0	0	146,987
	JDH3-02-009-R452-(RD)-Bituminous concrete wearing course 5	2d	27-Oct-26	28-Oct-26	387d	0	0	46,611
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2d	27-Oct-26	28-Oct-26	387d	0	0	46,611
	JDH3-02-009-R452-(RD)-Precast Concrete Curb	13d	27-Oct-26	10-Nov-26	400d	0	0	61,428
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	4d	27-Oct-26	31-Oct-26	400d	0	0	22,842
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	5d	05-Nov-26	10-Nov-26	400d	0	0	30,737
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	01-Nov-26	04-Nov-26	400d	0	0	7,850
	JDH3-02-009-R452-(RD)-Precast Interlocking Block Pavers	4d	11-Nov-26	15-Nov-26	400d	0	0	34,731
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	4d	11-Nov-26	15-Nov-26	400d	0	0	34,731
	JDH3-02-009-R452-(RD)-Pavement Marking	4d	29-Oct-26	02-Nov-26	387d	0	0	4,217
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	29-Oct-26	31-Oct-26	387d	0	0	2,782
	Thermoplastic intermittent 200 mm wide Broken edge line - (B1.	2d	01-Nov-26	02-Nov-26	387d	0	0	1,434
R453		95d	07-Jul-26 A	14-Nov-26	309d	0	482,278	606,661
	JDH3-02-009-R453-Road Works - RD	16d	27-Oct-26	14-Nov-26	309d	0	0	70,797
	JDH3-02-009-R453-(RD)-Bituminous concrete wearing course 5	2d	05-Nov-26	07-Nov-26	309d	0	0	21,057
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2d	05-Nov-26	07-Nov-26	309d	0	0	21,057
	JDH3-02-009-R453-(RD)-Precast Concrete Curb	6d	27-Oct-26	02-Nov-26	309d	0	0	31,098
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	2d	27-Oct-26	28-Oct-26	309d	0	0	11,044
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	29-Oct-26	02-Nov-26	309d	0	0	20,054
	JDH3-02-009-R453-(RD)-Precast Interlocking Block Pavers	2d	03-Nov-26	04-Nov-26	309d	0	0	16,255
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	2d	03-Nov-26	04-Nov-26	309d	0	0	16,255
	JDH3-02-009-R453-(RD)-Pavement Marking	6d	08-Nov-26	14-Nov-26	309d	0	0	2,387
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	08-Nov-26	09-Nov-26	309d	0	0	1,305
	Thermoplastic intermittent 200 mm wide Broken edge line - (B1.	2d	10-Nov-26	11-Nov-26	309d	0	0	652
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-EX-R453-R(	2d	12-Nov-26	14-Nov-26	309d	0	0	429
	JDH3-02-009-R453-Electrical Network - EL	19d	07-Jul-26 A	14-Nov-26	309d	0	482,278	535,865
	JDH3-02-009-R453-(EL)-MV cable trench size 2.0m wide and 80	10d	07-Jul-26 A	14-Nov-26	309d	0	8,131	9,035
	Backfilling + Warning Tape for MV Cable Trench 2.0m wide - 80	5d	09-Jul-26 A	14-Nov-26	309d	0	3,252	3,614
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5d	07-Jul-26 A	14-Nov-26	309d	0	4,879	5,421
	JDH3-02-009-R453-(EL)-MV cables AL/XLPE/LLDPE Unarmored	9d	11-Jul-26 A	14-Nov-26	309d	0	474,147	526,830

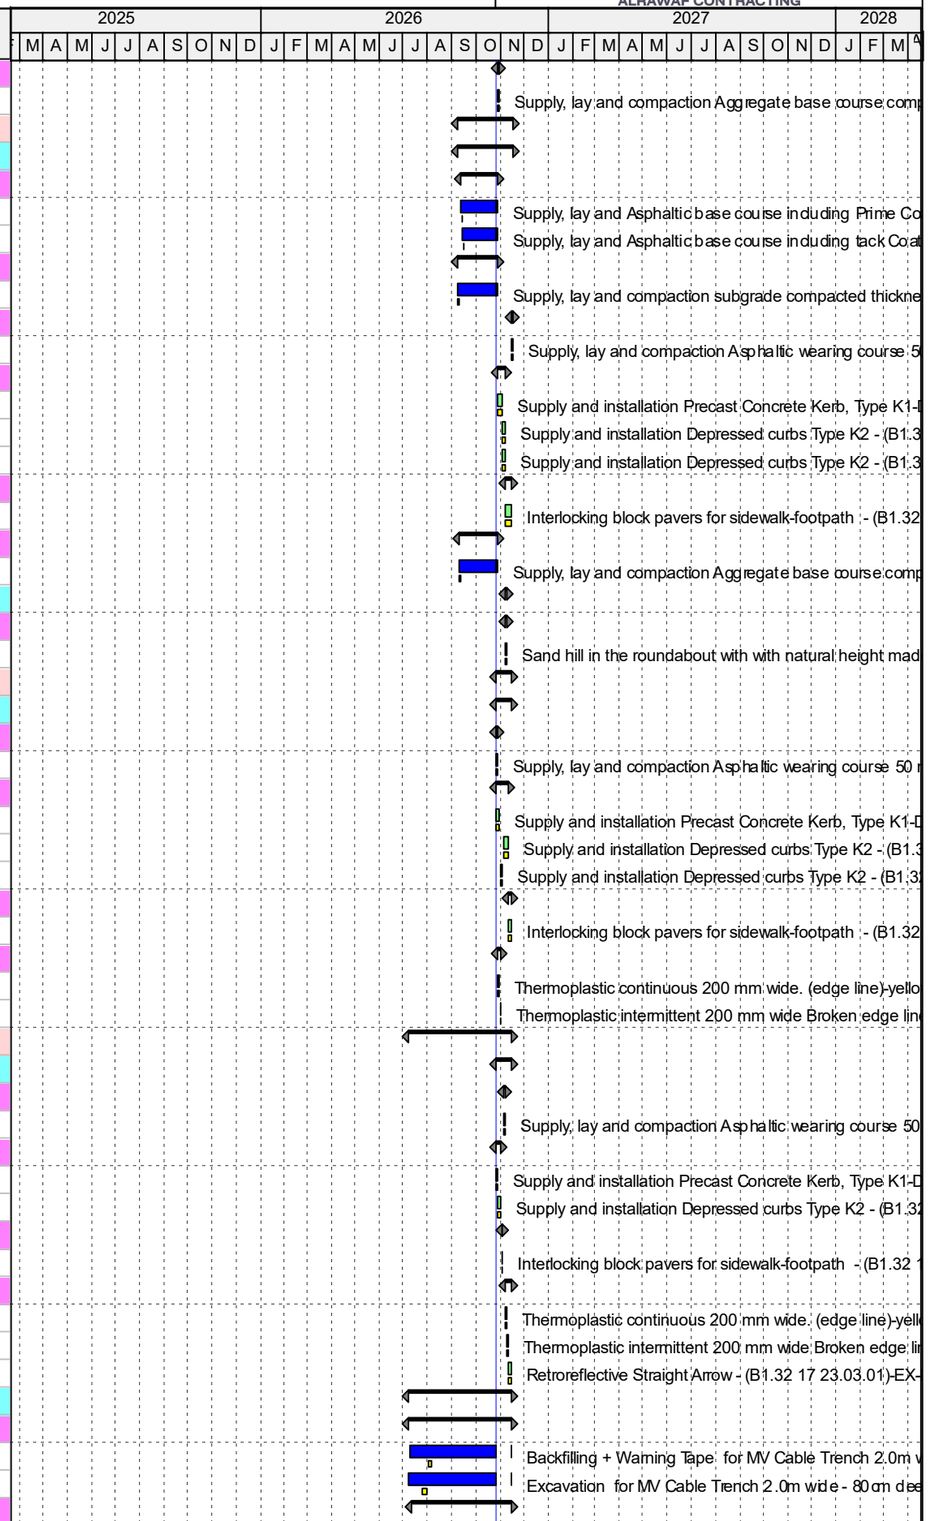


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	7d	11-Jul-26 A	14-Nov-26	309d	0	466,316	518,129
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	12-Jul-26 A	14-Nov-26	309d	0	7,831	8,701
R454		12d	27-Oct-26	09-Nov-26	411d	74,608	0	74,608
JDH3-02-009-R454-Potable Water Network - WT		12d	27-Oct-26	09-Nov-26	411d	74,608	0	74,608
JDH3-02-009-R454-(WT)-Valve Chamber on 400 mm dia pipeline		12d	27-Oct-26	09-Nov-26	411d	14,336	0	14,336
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	27-Oct-26	28-Oct-26	411d	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	29-Oct-26	31-Oct-26	411d	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Nov-26	02-Nov-26	411d	7,885	0	7,885
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	08-Nov-26	09-Nov-26	411d	2,867	0	2,867
JDH3-02-009-R454-(WT)-Fire Hydrant		6d	27-Oct-26	02-Nov-26	413d	34,198	0	34,198
	Stem for Fire Hydrant- (B3.33 14 19.20)-EX-R454-WT	2d	27-Oct-26	28-Oct-26	413d	14,656	0	14,656
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-EX-R454-WT	2d	29-Oct-26	31-Oct-26	413d	17,099	0	17,099
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-EX-R454-\	2d	01-Nov-26	02-Nov-26	413d	2,443	0	2,443
JDH3-02-009-R454-(WT)-Butterfly Valve-400 mm on pipe dia (40		4d	03-Nov-26	07-Nov-26	411d	26,074	0	26,074
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2d	03-Nov-26	04-Nov-26	411d	23,467	0	23,467
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2d	05-Nov-26	07-Nov-26	411d	2,607	0	2,607
R10		159d	07-Jul-26 A	26-Jan-27	344d	6,493,706	3,762,966	8,985,310
R103		128d	28-Jul-26 A	26-Jan-27	344d	919,780	645,712	2,279,441
JDH3-02-009-R103-Storm Network - ST		7d	27-Oct-26	03-Nov-26	408d	11,377	0	11,377
JDH3-02-009-R103-(ST)-MH Works (1200) mm diameter depth fr		3d	27-Oct-26	29-Oct-26	408d	9,817	0	9,817
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	3d	27-Oct-26	29-Oct-26	408d	9,817	0	9,817
JDH3-02-009-R103-(ST)-MH Works (1500) mm diameter depth fr		4d	31-Oct-26	03-Nov-26	408d	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	31-Oct-26	01-Nov-26	408d	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	02-Nov-26	03-Nov-26	408d	557	0	557
JDH3-02-009-R103-Catch Basins (Storm Network) - ST		37d	17-Sep-26 A	31-Oct-26	419d	36,772	6,129	36,772
JDH3-02-009-R103-(ST)-Single Catch Basin Works		35d	19-Sep-26 A	31-Oct-26	419d	16,848	2,808	16,848
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4d	27-Oct-26	31-Oct-26	419d	11,232	0	11,232
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z3-R103-S	4d	19-Sep-26 A	31-Oct-26	419d	5,616	2,808	5,616
JDH3-02-009-R103-(ST)-Double Catch Basin Works		35d	17-Sep-26 A	28-Oct-26	421d	19,923	3,321	19,923
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	421d	13,282	0	13,282
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z3-R103-S	2d	17-Sep-26 A	28-Oct-26	421d	6,641	3,321	6,641
JDH3-02-009-R103-TSE Network - TSE		10d	27-Oct-26	07-Nov-26	413d	135,563	0	135,563
JDH3-02-009-R103-(TSE)-Butterfly Valve-300 mm on pipe dia (31		8d	27-Oct-26	04-Nov-26	415d	48,390	0	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2d	27-Oct-26	28-Oct-26	419d	43,551	0	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	03-Nov-26	04-Nov-26	415d	4,839	0	4,839
JDH3-02-009-R103-(TSE)-Wash-Out Valve-100 mm on pipe dia (3		4d	27-Oct-26	31-Oct-26	168d	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2d	27-Oct-26	28-Oct-26	168d	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2d	29-Oct-26	31-Oct-26	168d	1,613	0	1,613
JDH3-02-009-R103-(TSE)-Air Valve-50 mm on pipe dia (315) mm		4d	29-Oct-26	02-Nov-26	168d	6,338	0	6,338
	Installation for Air Valve 50 mm on pipe dia 315 mm- (B4.33 14	2d	29-Oct-26	31-Oct-26	168d	5,704	0	5,704
	Stem & Surface box for Air Valve 50 mm on pipe dia 315 mm- (I	2d	01-Nov-26	02-Nov-26	168d	634	0	634
JDH3-02-009-R103-(TSE)-Valve Chamber on 315 mm dia pipelin		6d	27-Oct-26	02-Nov-26	415d	36,604	0	36,604
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	27-Oct-26	28-Oct-26	415d	4,306	0	4,306
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	29-Oct-26	31-Oct-26	415d	23,685	0	23,685
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	01-Nov-26	02-Nov-26	415d	8,613	0	8,613
JDH3-02-009-R103-(TSE)-Wash-Out Chamber on 315 mm dia pi		8d	27-Oct-26	04-Nov-26	168d	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2d	27-Oct-26	28-Oct-26	168d	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2d	29-Oct-26	31-Oct-26	168d	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2d	01-Nov-26	02-Nov-26	168d	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - (	2d	03-Nov-26	04-Nov-26	168d	4,177	0	4,177
JDH3-02-009-R103-(TSE)-Air Valve Chamber on 315 mm dia pip		8d	29-Oct-26	07-Nov-26	413d	7,218	0	7,218
	Excavation+Bedding for Air Valve Chamber on pipe dia 315 mm	2d	29-Oct-26	31-Oct-26	415d	1,083	0	1,083
	PC Worksfor Air Valve Chamber on pipe dia 315 mm - depth fro	2d	01-Nov-26	02-Nov-26	415d	722	0	722

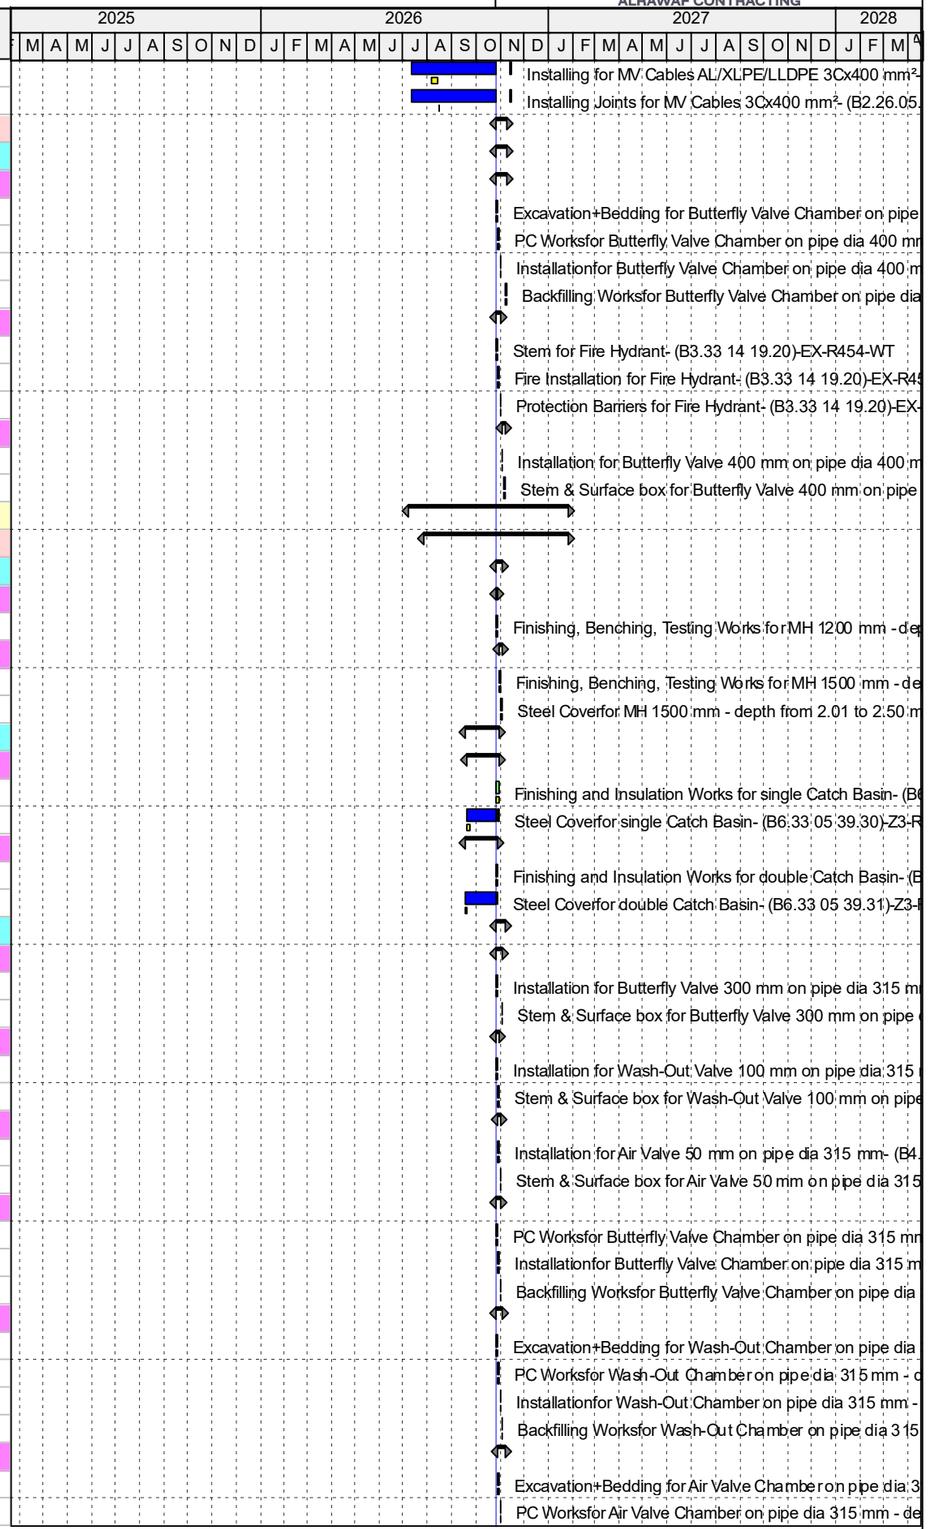


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installationfor Air Valve Chamber on pipe dia 315 mm - depth fr	2d	03-Nov-26	04-Nov-26	415d	3,970	0	3,970
	Backfilling Worksfor Air Valve Chamber on pipe dia 315 mm - de	2d	05-Nov-26	07-Nov-26	168d	1,444	0	1,444
	JDH3-02-009-R103-Potable Water Network - WT	37d	22-Sep-26 A	04-Nov-26	415d	179,197	23,408	179,197
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	6d	22-Sep-26 A	02-Nov-26	417d	20,256	6,077	20,256
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	6d	22-Sep-26 A	02-Nov-26	417d	20,256	6,077	20,256
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	4d	23-Sep-26 A	02-Nov-26	417d	52,791	15,837	52,791
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	4d	23-Sep-26 A	02-Nov-26	417d	52,791	15,837	52,791
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	4d	24-Sep-26 A	02-Nov-26	417d	4,981	1,494	4,981
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	4d	24-Sep-26 A	02-Nov-26	417d	4,981	1,494	4,981
	JDH3-02-009-R103-(WT)-Butterfly Valve-800 mm on pipe dia (80	4d	29-Oct-26	02-Nov-26	415d	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	29-Oct-26	31-Oct-26	415d	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2d	01-Nov-26	02-Nov-26	415d	6,575	0	6,575
	JDH3-02-009-R103-(WT)-Valve Chamber on 800 mm dia pipeline	8d	27-Oct-26	04-Nov-26	415d	31,996	0	31,996
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 8(	2d	27-Oct-26	28-Oct-26	415d	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	29-Oct-26	31-Oct-26	415d	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	01-Nov-26	02-Nov-26	415d	17,598	0	17,598
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	03-Nov-26	04-Nov-26	415d	6,399	0	6,399
	JDH3-02-009-R103-(WT)-Fire Hydrant	2d	27-Oct-26	28-Oct-26	176d	3,420	0	3,420
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R103-V	2d	27-Oct-26	28-Oct-26	176d	3,420	0	3,420
	JDH3-02-009-R103-Electrical Network - EL	15d	08-Nov-26	24-Nov-26	394d	454,467	0	454,467
	JDH3-02-009-R103-(EL)-MV cable trench size 2.0m wide and 80	10d	08-Nov-26	18-Nov-26	168d	8,795	0	8,795
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5d	08-Nov-26	12-Nov-26	168d	5,277	0	5,277
	Backfilling + Warning Tape for MV Cable Trench 2.0m wide - 80	5d	14-Nov-26	18-Nov-26	168d	3,518	0	3,518
	JDH3-02-009-R103-(EL)-MV cables AL/XLPE/LLDPE Unarmored	10d	14-Nov-26	24-Nov-26	394d	445,672	0	445,672
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	10d	14-Nov-26	24-Nov-26	394d	445,672	0	445,672
	JDH3-02-009-R103-Street Lighting Network -SL	49d	28-Jul-26 A	02-Dec-26	178d	102,404	92,164	102,404
	JDH3-02-009-R103-(SL)- LV Cables - Single Core Copper, 3-1x C	2d	17-Sep-26 A	18-Nov-26	184d	6,462	5,816	6,462
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2d	17-Sep-26 A	18-Nov-26	184d	6,462	5,816	6,462
	JDH3-02-009-R103-(SL)-Lighting Pole with double arms 16 m he	25d	28-Jul-26 A	18-Nov-26	184d	75,744	68,169	75,744
	Excavation for RC foundation for Lighting Pole double arms- (B2	2d	28-Jul-26 A	18-Nov-26	168d	7,973	7,176	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2d	29-Jul-26 A	18-Nov-26	182d	7,973	7,176	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2.:	2d	30-Jul-26 A	18-Nov-26	184d	7,973	7,176	7,973
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	3d	02-Sep-26 A	18-Nov-26	184d	51,825	46,642	51,825
	JDH3-02-009-R103-(SL)-Street Lighting(LED) Luminaire comple	13d	16-Sep-26 A	02-Dec-26	178d	20,198	18,179	20,198
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3d	17-Sep-26 A	02-Dec-26	178d	4,040	3,636	4,040
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.1	3d	16-Sep-26 A	18-Nov-26	184d	16,159	14,543	16,159
	JDH3-02-009-R103-Road Works - RD	53d	27-Aug-26 A	26-Jan-27	168d	0	524,012	1,341,344
	JDH3-02-009-R103-(RD)-Bituminous base course 150 mm Two l	7d	27-Aug-26 A	26-Jan-27	168d	0	524,012	748,588
	Supply, lay and Asphaltic base course including tack Coat (RC2)	7d	27-Aug-26 A	26-Jan-27	168d	0	524,012	748,588
	JDH3-02-009-R103-(RD)-Precast Concrete Curb	14d	05-Jan-27	20-Jan-27	168d	0	0	339,016
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	12d	05-Jan-27	18-Jan-27	168d	0	0	188,508
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2d	05-Jan-27	06-Jan-27	168d	0	0	55,364
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	12d	07-Jan-27	20-Jan-27	168d	0	0	95,145
	JDH3-02-009-R103-(RD)-Precast Interlocking Block Pavers	17d	07-Jan-27	26-Jan-27	168d	0	0	253,740
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	17d	07-Jan-27	26-Jan-27	168d	0	0	253,740
	JDH3-02-009-R103-Landscape Works - LS	13d	31-Dec-26	14-Jan-27	141d	0	0	18,318
	JDH3-02-009-R103-(LS)-HDPE for Secondary Network	13d	31-Dec-26	14-Jan-27	141d	0	0	18,318
	Pipe line with Diam 90 mm PN10 - depth from 0 to 1.5 m- (B7.3	2d	31-Dec-26	02-Jan-27	110d	0	0	2,364
	Pipe linefor Diam 75 mm PN10 - depth from 0 to 1.5 m- (B7.33.	4d	03-Jan-27	06-Jan-27	141d	0	0	4,940
	Pipe linefor Diam 63 mm PN10 - depth from 0 to 1.5 m- (B7.33.	7d	07-Jan-27	14-Jan-27	141d	0	0	11,014
R104		109d	18-Aug-26 A	16-Jan-27	354d	1,988,149	1,474,904	2,780,983
	JDH3-02-009-R104-Storm Network - ST	15d	27-Oct-26	12-Nov-26	408d	27,156	0	27,156
	JDH3-02-009-R104-(ST)-MH Works (1200) mm diameter depth fr	11d	27-Oct-26	08-Nov-26	408d	17,919	0	17,919

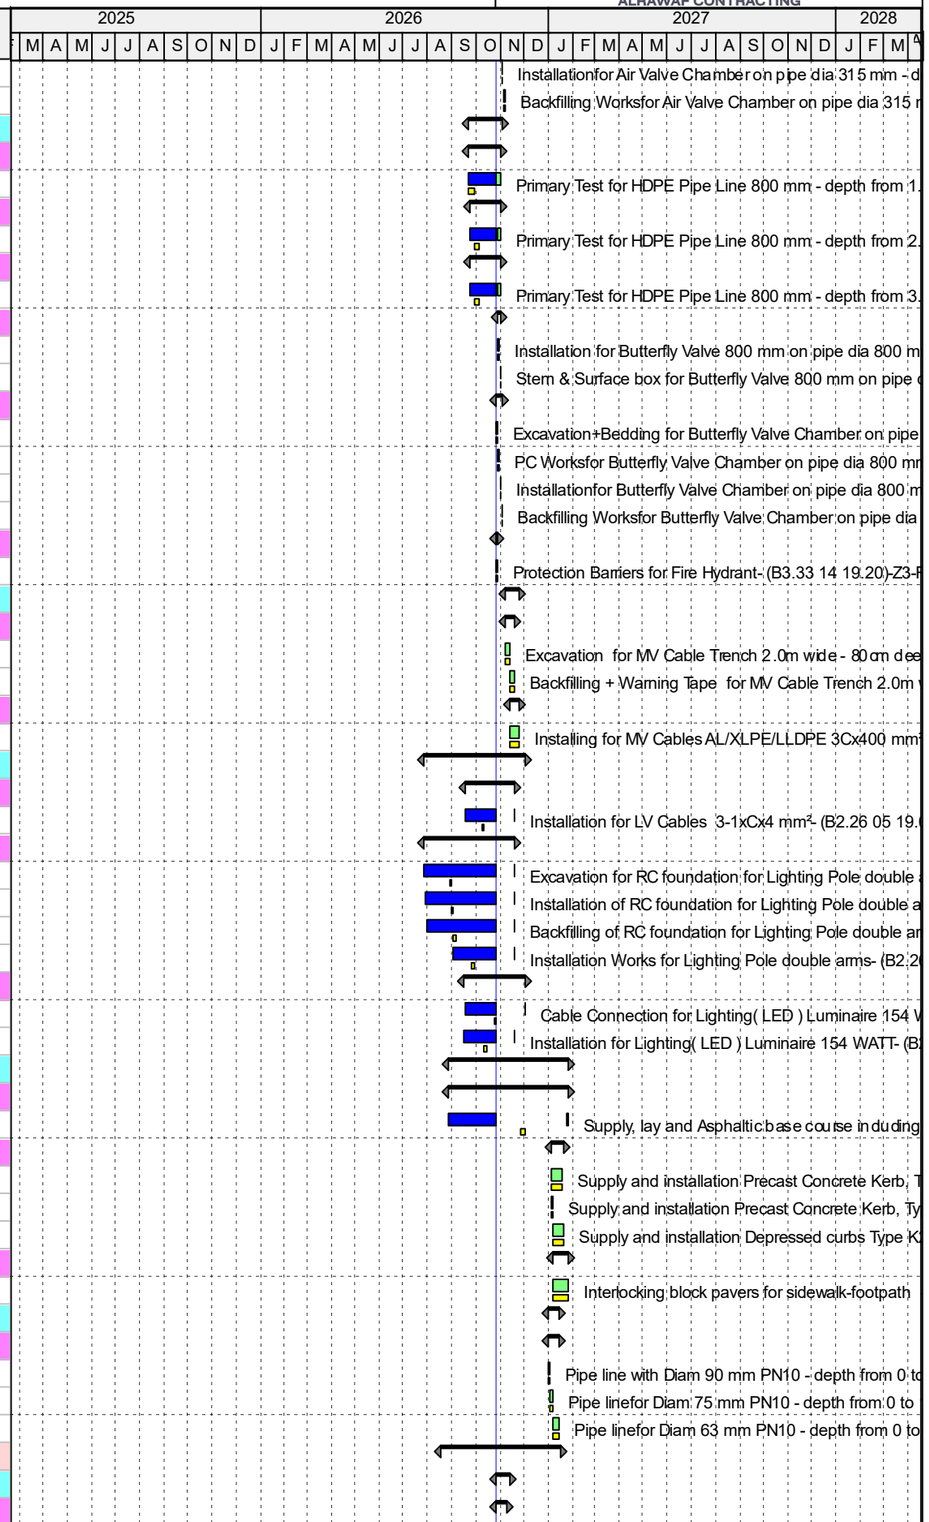


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4d	27-Oct-26	31-Oct-26	411d	11,920	0	11,920
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	4d	04-Nov-26	08-Nov-26	408d	5,999	0	5,999
	JDH3-02-009-R104-(ST)-MH Works (2000) mm diameter depth fr	9d	01-Nov-26	10-Nov-26	408d	6,228	0	6,228
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2d	01-Nov-26	02-Nov-26	413d	4,101	0	4,101
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2d	09-Nov-26	10-Nov-26	408d	2,127	0	2,127
	JDH3-02-009-R104-(ST)-MH Works (1500) mm diameter depth fr	9d	03-Nov-26	12-Nov-26	408d	3,009	0	3,009
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	03-Nov-26	04-Nov-26	413d	2,006	0	2,006
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2d	11-Nov-26	12-Nov-26	408d	1,003	0	1,003
	JDH3-02-009-R104-Catch Basins (Storm Network) - ST	69d	18-Aug-26 A	07-Nov-26	413d	243,657	193,401	243,657
	JDH3-02-009-R104-(ST)-For Catch Basins (GRP) Pipes-300 mm	67d	18-Aug-26 A	04-Nov-26	413d	213,040	187,901	213,040
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	7d	27-Oct-26	04-Nov-26	413d	21,304	0	21,304
	Backfilling and warning tape Works for CB GRP Pipe Line 300 r	8d	08-Sep-26 A	04-Nov-26	413d	21,304	20,878	21,304
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 to	5d	22-Aug-26 A	27-Oct-26	414d	10,652	10,439	10,652
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	8d	23-Aug-26 A	27-Oct-26	413d	117,172	114,828	117,172
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	5d	18-Aug-26 A	27-Oct-26	414d	42,608	41,756	42,608
	JDH3-02-009-R104-(ST)-For Catch Basins (GRP) Pipes-400 mm	35d	18-Aug-26 A	07-Nov-26	413d	6,236	5,500	6,236
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	2d	04-Nov-26	07-Nov-26	413d	624	0	624
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 to	2d	22-Aug-26 A	04-Nov-26	413d	312	306	312
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	2d	18-Aug-26 A	04-Nov-26	413d	1,247	1,222	1,247
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 n	2d	23-Aug-26 A	04-Nov-26	413d	3,430	3,361	3,430
	Backfilling and warning tape Works for CB GRP Pipe Line 400 r	2d	08-Sep-26 A	07-Nov-26	413d	624	611	624
	JDH3-02-009-R104-(ST)-Single Catch Basin Works	8d	27-Oct-26	04-Nov-26	415d	10,684	0	10,684
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4d	27-Oct-26	31-Oct-26	415d	7,123	0	7,123
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z4-R104-S	4d	01-Nov-26	04-Nov-26	415d	3,561	0	3,561
	JDH3-02-009-R104-(ST)-Double Catch Basin Works	4d	27-Oct-26	31-Oct-26	169d	13,697	0	13,697
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	169d	9,131	0	9,131
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z4-R104-S	2d	29-Oct-26	31-Oct-26	169d	4,566	0	4,566
	JDH3-02-009-R104-TSE Network - TSE	44d	15-Sep-26 A	05-Nov-26	414d	111,217	2,153	111,217
	JDH3-02-009-R104-(TSE)-Butterfly Valve-300 mm on pipe dia (31	4d	27-Oct-26	31-Oct-26	419d	32,260	0	32,260
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2d	27-Oct-26	28-Oct-26	419d	29,034	0	29,034
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	29-Oct-26	31-Oct-26	419d	3,226	0	3,226
	JDH3-02-009-R104-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4d	27-Oct-26	31-Oct-26	343d	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2d	27-Oct-26	28-Oct-26	343d	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2d	29-Oct-26	31-Oct-26	343d	1,613	0	1,613
	JDH3-02-009-R104-(TSE)-Valve Chamber on 315 mm dia pipelin	42d	15-Sep-26 A	03-Nov-26	414d	28,709	2,153	28,709
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	28-Oct-26	29-Oct-26	414d	2,871	0	2,871
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	31-Oct-26	01-Nov-26	414d	15,790	0	15,790
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2d	02-Nov-26	03-Nov-26	414d	5,742	0	5,742
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2d	15-Sep-26 A	27-Oct-26	414d	4,306	2,153	4,306
	JDH3-02-009-R104-(TSE)-Wash-Out Chamber on 315 mm dia pi	8d	27-Oct-26	04-Nov-26	341d	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2d	27-Oct-26	28-Oct-26	341d	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2d	29-Oct-26	31-Oct-26	341d	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2d	01-Nov-26	02-Nov-26	341d	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2d	03-Nov-26	04-Nov-26	341d	4,177	0	4,177
	JDH3-02-009-R104-(TSE)-Air Valve-50 mm on pipe dia (110) mm	4d	29-Oct-26	02-Nov-26	417d	6,016	0	6,016
	Installation for Air Valve 50 mm on pipe dia 110 mm- (B4.33 14	2d	29-Oct-26	31-Oct-26	417d	5,415	0	5,415
	Stem & Surface box for Air Valve 50 mm on pipe dia 110 mm- (I	2d	01-Nov-26	02-Nov-26	417d	602	0	602
	JDH3-02-009-R104-(TSE)-Air Valve Chamber on 110 mm dia pip	9d	27-Oct-26	05-Nov-26	414d	7,218	0	7,218
	Excavation+Bedding for Air Valve Chamber on pipe dia 110 mm	2d	27-Oct-26	28-Oct-26	415d	1,083	0	1,083
	PC Worksfor Air Valve Chamber on pipe dia 110 mm - depth fro	2d	29-Oct-26	31-Oct-26	415d	722	0	722
	Installationfor Air Valve Chamber on pipe dia 110 mm - depth fr	2d	01-Nov-26	02-Nov-26	415d	3,970	0	3,970
	Backfilling Worksfor Air Valve Chamber on pipe dia 110 mm - de	2d	04-Nov-26	05-Nov-26	414d	1,444	0	1,444
	JDH3-02-009-R104-Potable Water Network - WT	47d	22-Sep-26 A	16-Nov-26	405d	256,469	2,129	256,469

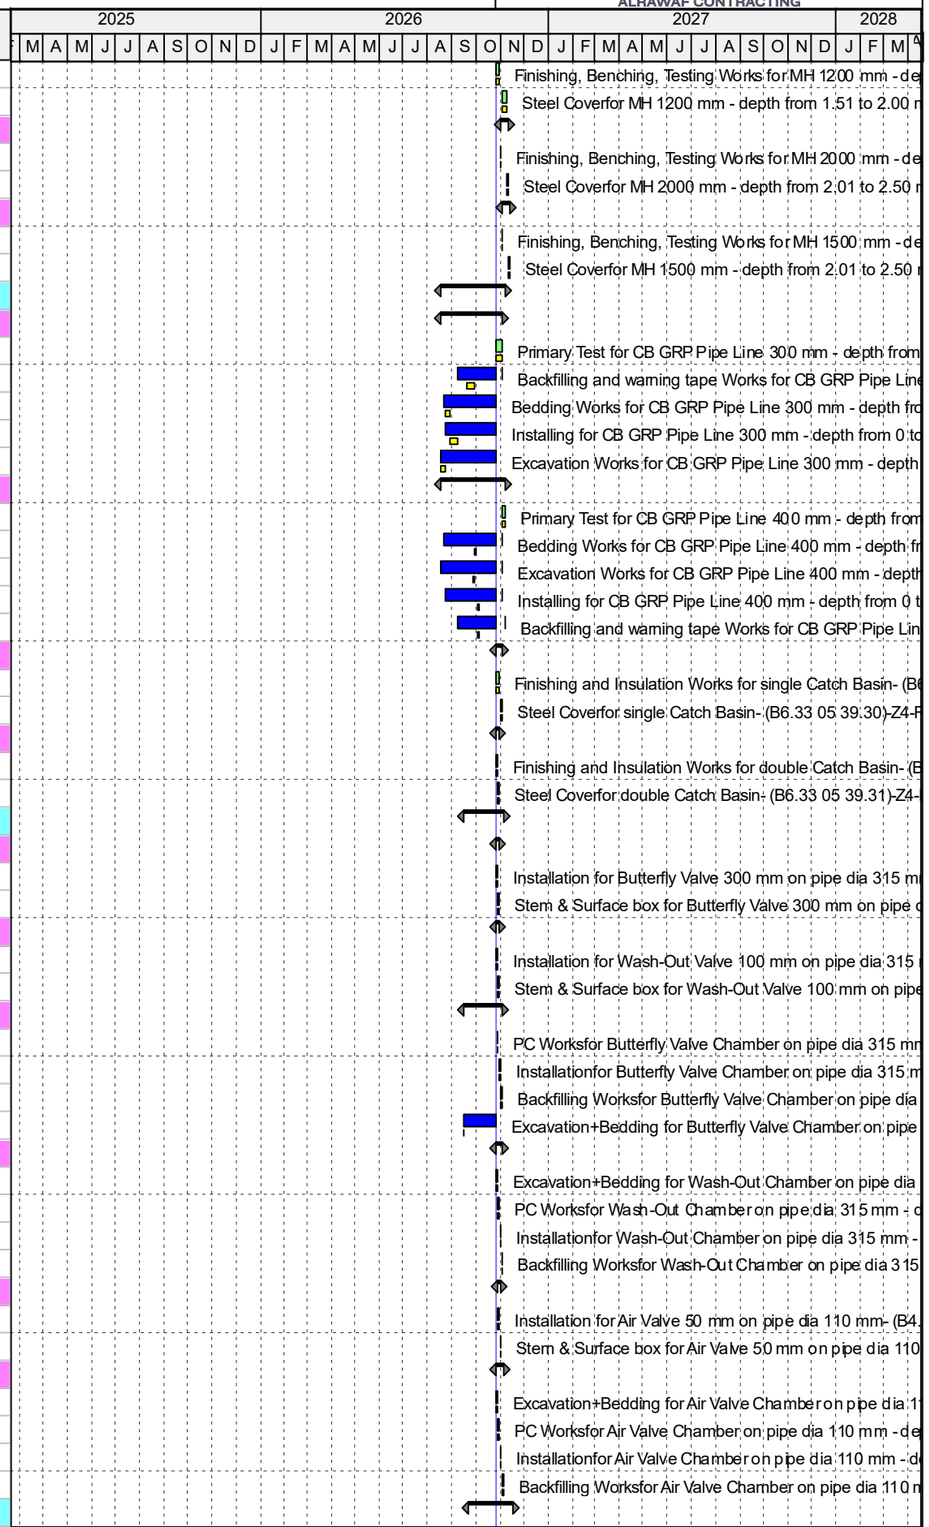


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R104-(WT)-Butterfly Valve-400 mm on pipe dia (40(	4d	27-Oct-26	31-Oct-26	415d	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2d	27-Oct-26	28-Oct-26	415d	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2d	29-Oct-26	31-Oct-26	415d	7,822	0	7,822
	JDH3-02-009-R104-(WT)-Valve Chamber on 400 mm dia pipeline	45d	22-Sep-26 A	14-Nov-26	405d	43,007	2,129	43,007
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	29-Oct-26	31-Oct-26	405d	4,301	0	4,301
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Nov-26	02-Nov-26	405d	23,654	0	23,654
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	12-Nov-26	14-Nov-26	405d	8,601	0	8,601
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	22-Sep-26 A	28-Oct-26	405d	6,451	2,129	6,451
	JDH3-02-009-R104-(WT)-Fire Hydrant	12d	29-Oct-26	11-Nov-26	405d	78,167	0	78,167
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	29-Oct-26	31-Oct-26	407d	7,817	0	7,817
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-W	2d	03-Nov-26	04-Nov-26	405d	15,633	0	15,633
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-WT	2d	05-Nov-26	07-Nov-26	405d	23,450	0	23,450
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-WT	2d	08-Nov-26	09-Nov-26	405d	27,358	0	27,358
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-V	2d	10-Nov-26	11-Nov-26	405d	3,908	0	3,908
	JDH3-02-009-R104-(WT)-Wash-Out Valve-100 mm on pipe dia (2	4d	29-Oct-26	02-Nov-26	417d	15,346	0	15,346
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2d	29-Oct-26	31-Oct-26	417d	13,811	0	13,811
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2d	01-Nov-26	02-Nov-26	417d	1,535	0	1,535
	JDH3-02-009-R104-(WT)-Wash-Out Chamber on 225 mm dia pip	18d	27-Oct-26	16-Nov-26	405d	41,727	0	41,727
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2d	27-Oct-26	28-Oct-26	415d	6,259	0	6,259
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2d	29-Oct-26	31-Oct-26	415d	4,173	0	4,173
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2d	01-Nov-26	02-Nov-26	415d	22,950	0	22,950
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - (	2d	15-Nov-26	16-Nov-26	405d	8,345	0	8,345
	JDH3-02-009-R104-Electrical Network - EL	4d	05-Nov-26	09-Nov-26	341d	77,785	0	77,785
	JDH3-02-009-R104-(EL)-MV cables AL/XLPE/LLDPE Unarmored	4d	05-Nov-26	09-Nov-26	341d	77,785	0	77,785
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	2d	05-Nov-26	07-Nov-26	341d	69,084	0	69,084
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2d	08-Nov-26	09-Nov-26	341d	8,701	0	8,701
	JDH3-02-009-R104-Street Lighting Network -SL	17d	17-Oct-26 A	18-Nov-26	345d	165,980	4,432	165,980
	JDH3-02-009-R104-(SL)- LV Cables - Copper, 4Cx95 mm²,Cu/XLP	6d	10-Nov-26	16-Nov-26	345d	129,726	0	129,726
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	3d	10-Nov-26	12-Nov-26	341d	15,262	0	15,262
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.:	3d	14-Nov-26	16-Nov-26	345d	114,464	0	114,464
	JDH3-02-009-R104-(SL)-Lighting Pole with double arms 16 m he	16d	17-Oct-26 A	17-Nov-26	346d	29,547	4,432	29,547
	Excavation for RC foundation for Lighting Pole double arms- (B:	2d	17-Oct-26 A	12-Nov-26	346d	9,849	4,432	9,849
	Installation of RC foundation for Lighting Pole double arms- (B2	2d	14-Nov-26	15-Nov-26	346d	9,849	0	9,849
	Backfilling of RC foundation for Lighting Pole double arms- (B2.:	2d	16-Nov-26	17-Nov-26	346d	9,849	0	9,849
	JDH3-02-009-R104-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	5d	14-Nov-26	18-Nov-26	341d	6,707	0	6,707
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	14-Nov-26	18-Nov-26	341d	6,707	0	6,707
	JDH3-02-009-R104-Road Works - RD	91d	08-Sep-26 A	16-Jan-27	318d	1,105,886	1,272,789	1,898,720
	JDH3-02-009-R104-(RD)-Aggregate Base Course	2d	08-Sep-26 A	27-Oct-26	349d	313,052	281,747	313,052
	Supply, lay and compaction Aggregate base course compacted	2d	08-Sep-26 A	27-Oct-26	349d	313,052	281,747	313,052
	JDH3-02-009-R104-(RD)-Bituminous base course 150 mm Two L	89d	10-Sep-26 A	16-Jan-27	318d	792,834	991,042	1,585,668
	Supply, lay and Asphaltic base course induding tack Coat (RC2)	7d	24-Sep-26 A	16-Jan-27	318d	0	317,134	792,834
	Supply, lay and Asphaltic base course induding Prime Coat (MC	2d	10-Sep-26 A	28-Oct-26	349d	792,834	673,909	792,834
R101		100d	07-Jul-26 A	19-Nov-26	403d	2,598,234	1,584,408	2,721,133
	JDH3-02-009-R101-TSE Network - TSE	99d	07-Jul-26 A	18-Nov-26	404d	344,679	63,009	344,679
	JDH3-02-009-R101-(TSE)-HDPE Pipes-400 mm diameter depth f	2d	27-Oct-26	28-Oct-26	421d	42,219	0	42,219
	Primary Test for HDPE Pipe Line 400 mm - depth from 1.51 to 2	2d	27-Oct-26	28-Oct-26	421d	42,219	0	42,219
	JDH3-02-009-R101-(TSE)-HDPE Pipes-400 mm diameter depth f	83d	07-Jul-26 A	31-Oct-26	420d	9,426	2,545	9,426
	Primary Test for HDPE Pipe Line 400 mm - depth from 2.51 to 3	2d	28-Oct-26	31-Oct-26	420d	943	0	943
	Bedding Works for HDPE Pipe Line 400 mm - depth from 2.51 t	2d	09-Jul-26 A	28-Oct-26	420d	471	141	471
	Installing for HDPE Pipe Line 400 mm - depth from 2.51 to 3.5 (	2d	11-Jul-26 A	28-Oct-26	420d	5,184	1,555	5,184
	Backfilling and warning tape Works for HDPE Pipe Line 400 mm	2d	25-Jul-26 A	31-Oct-26	420d	943	283	943
	Excavation Works for HDPE Pipe Line 400 mm - depth from 2.5	2d	07-Jul-26 A	28-Oct-26	420d	1,885	566	1,885
	JDH3-02-009-R101-(TSE)-Butterfly Valve-400 mm on pipe dia (31	44d	15-Sep-26 A	07-Nov-26	404d	130,370	46,933	130,370

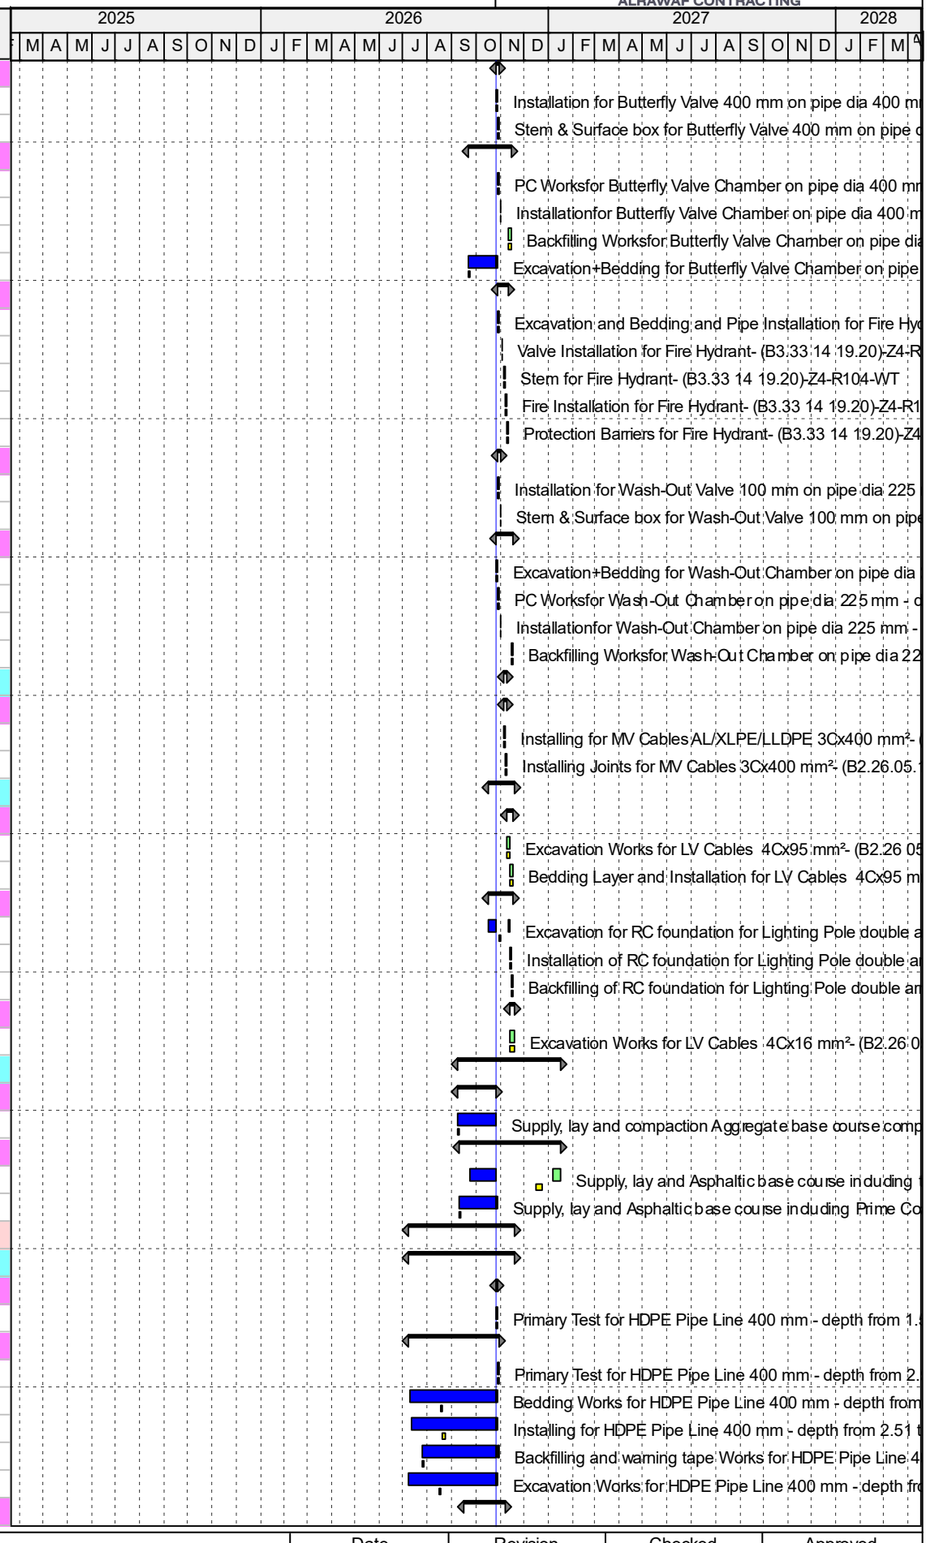

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2d	04-Nov-26	07-Nov-26	404d	13,037	0	13,037
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2d	15-Sep-26 A	28-Oct-26	410d	117,333	46,933	117,333
	JDH3-02-009-R101-(TSE)-Wash-Out Valve-100 mm on pipe dia (	10d	28-Oct-26	09-Nov-26	404d	33,818	0	33,818
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2d	28-Oct-26	31-Oct-26	410d	30,436	0	30,436
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 4	2d	07-Nov-26	09-Nov-26	404d	3,382	0	3,382
	JDH3-02-009-R101-(TSE)-Air Valve-65 mm on pipe dia (400) mm	10d	31-Oct-26	11-Nov-26	404d	7,790	0	7,790
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33 14	2d	31-Oct-26	02-Nov-26	410d	7,011	0	7,011
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (	2d	09-Nov-26	11-Nov-26	404d	779	0	779
	JDH3-02-009-R101-(TSE)-Valve Chamber on 400 mm dia pipelin	68d	25-Aug-26 A	14-Nov-26	404d	71,973	13,531	71,973
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	11-Nov-26	14-Nov-26	404d	14,395	0	14,395
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	16-Sep-26 A	28-Oct-26	415d	39,585	6,334	39,585
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	01-Sep-26 A	28-Oct-26	416d	7,197	2,879	7,197
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	25-Aug-26 A	28-Oct-26	404d	10,796	4,318	10,796
	JDH3-02-009-R101-(TSE)-Wash-Out Chamber on 400 mm dia pi	16d	28-Oct-26	16-Nov-26	404d	41,949	0	41,949
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2d	28-Oct-26	31-Oct-26	404d	6,292	0	6,292
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2d	31-Oct-26	02-Nov-26	404d	4,195	0	4,195
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2d	02-Nov-26	04-Nov-26	404d	23,072	0	23,072
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm -	2d	14-Nov-26	16-Nov-26	404d	8,390	0	8,390
	JDH3-02-009-R101-(TSE)-Air Valve Chamber on 400 mm dia pip	16d	31-Oct-26	18-Nov-26	404d	7,134	0	7,134
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2d	31-Oct-26	02-Nov-26	412d	1,070	0	1,070
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2d	02-Nov-26	04-Nov-26	412d	713	0	713
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2d	04-Nov-26	07-Nov-26	412d	3,924	0	3,924
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2d	16-Nov-26	18-Nov-26	404d	1,427	0	1,427
	JDH3-02-009-R101-Potable Water Network - WT	44d	22-Sep-26 A	16-Nov-26	405d	652,517	39,280	652,517
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	4d	27-Oct-26	31-Oct-26	419d	27,753	0	27,753
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	4d	27-Oct-26	31-Oct-26	419d	27,753	0	27,753
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	3d	27-Oct-26	29-Oct-26	420d	36,144	0	36,144
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	3d	27-Oct-26	29-Oct-26	420d	36,144	0	36,144
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	3d	27-Oct-26	29-Oct-26	408d	59,286	0	59,286
	Primary Test for HDPE Pipe Line 800 mm - depth from 4.51 to 5	3d	27-Oct-26	29-Oct-26	408d	59,286	0	59,286
	JDH3-02-009-R101-(WT)-Butterfly Valve-400 mm on pipe dia (40	4d	27-Oct-26	31-Oct-26	405d	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2d	27-Oct-26	28-Oct-26	405d	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2d	29-Oct-26	31-Oct-26	405d	7,822	0	7,822
	JDH3-02-009-R101-(WT)-Butterfly Valve-800 mm on pipe dia (80	4d	29-Oct-26	02-Nov-26	405d	197,263	0	197,263
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	29-Oct-26	31-Oct-26	405d	177,537	0	177,537
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 800	2d	01-Nov-26	02-Nov-26	405d	19,726	0	19,726
	JDH3-02-009-R101-(WT)-Wash-Out Valve-200 mm on pipe dia (8	2d	03-Nov-26	04-Nov-26	405d	2,736	0	2,736
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 8	2d	03-Nov-26	04-Nov-26	405d	2,736	0	2,736
	JDH3-02-009-R101-(WT)-Air Valve-110 mm on pipe dia (800) mm	10d	27-Oct-26	07-Nov-26	405d	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 1	2d	27-Oct-26	28-Oct-26	411d	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2d	05-Nov-26	07-Nov-26	405d	2,501	0	2,501
	JDH3-02-009-R101-(WT)-Valve Chamber on 400 mm dia pipeline	38d	27-Sep-26 A	09-Nov-26	405d	43,007	3,226	43,007
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	31-Oct-26	01-Nov-26	408d	4,301	0	4,301
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	02-Nov-26	03-Nov-26	408d	23,654	0	23,654
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	08-Nov-26	09-Nov-26	405d	8,601	0	8,601
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	27-Sep-26 A	29-Oct-26	408d	6,451	3,226	6,451
	JDH3-02-009-R101-(WT)-Valve Chamber on 800 mm dia pipeline	13d	28-Oct-26	11-Nov-26	405d	81,589	0	81,589
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	28-Oct-26	29-Oct-26	412d	9,599	0	9,599
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	31-Oct-26	01-Nov-26	412d	52,793	0	52,793
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2d	10-Nov-26	11-Nov-26	405d	19,197	0	19,197
	JDH3-02-009-R101-(WT)-Wash-Out Chamber on 800 mm dia pip	2d	12-Nov-26	14-Nov-26	405d	6,427	0	6,427
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm -	2d	12-Nov-26	14-Nov-26	405d	6,427	0	6,427
	JDH3-02-009-R101-(WT)-Air Valve Chamber on 800 mm dia pipe	17d	28-Oct-26	16-Nov-26	405d	7,139	0	7,139

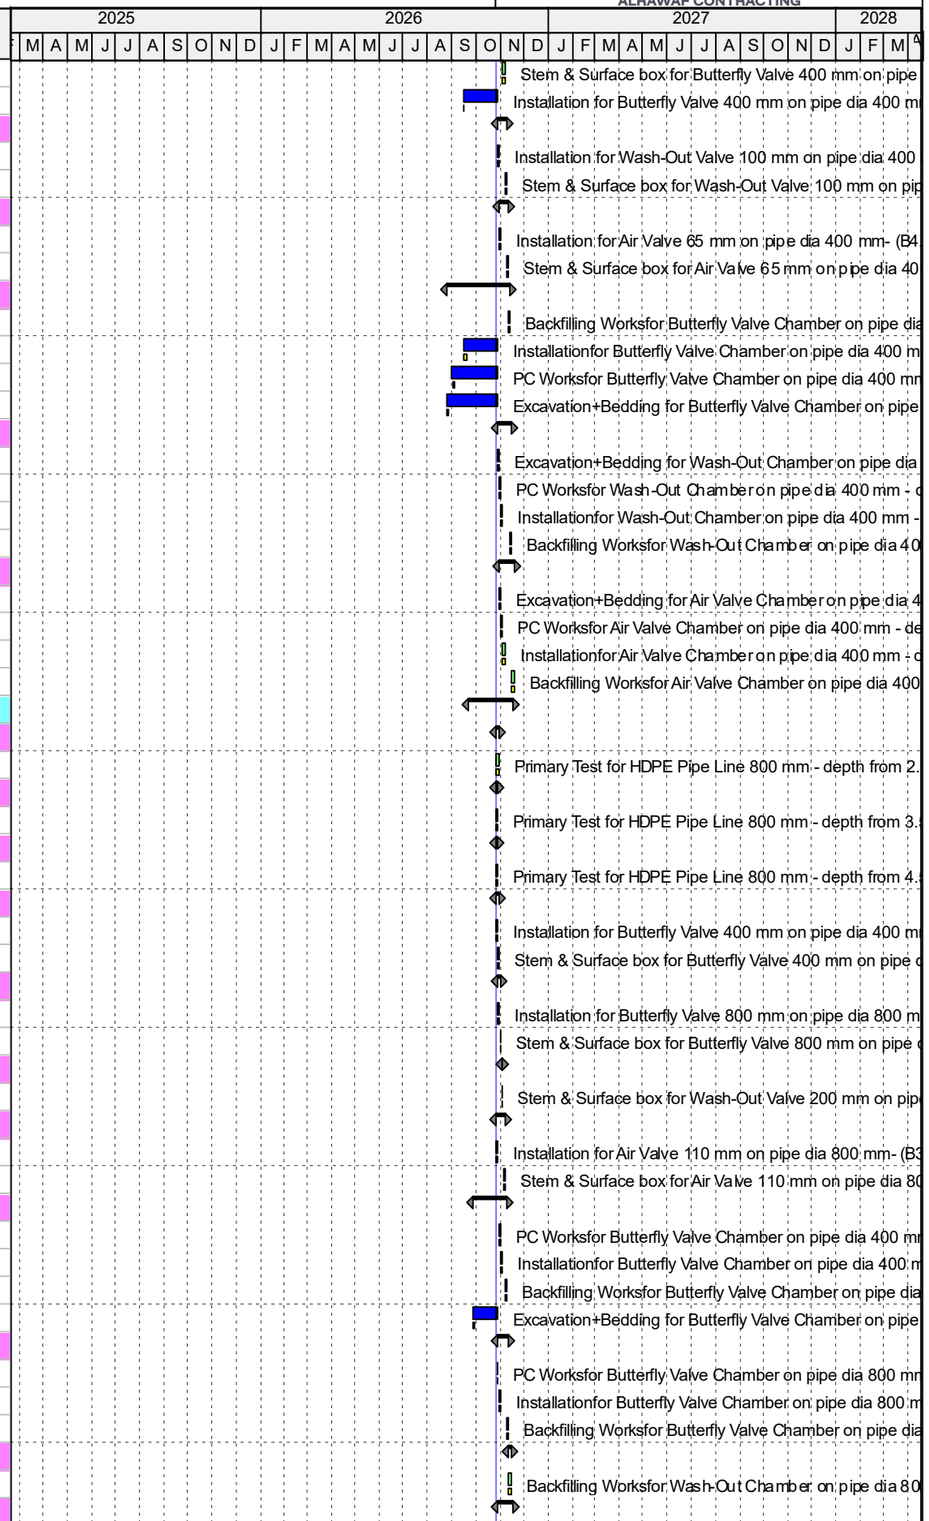


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2d	28-Oct-26	29-Oct-26	410d	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2d	31-Oct-26	01-Nov-26	414d	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2d	02-Nov-26	03-Nov-26	414d	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2d	15-Nov-26	16-Nov-26	405d	1,428	0	1,428
	JDH3-02-009-R101-(WT)-Fire Hydrant	23d	22-Sep-26 A	01-Nov-26	410d	87,937	36,054	87,937
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-W	2d	31-Oct-26	01-Nov-26	410d	4,397	0	4,397
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-WT	2d	27-Sep-26 A	29-Oct-26	410d	30,778	12,311	30,778
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-WT	2d	26-Sep-26 A	29-Oct-26	410d	26,381	10,552	26,381
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	22-Sep-26 A	29-Oct-26	410d	8,794	4,397	8,794
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-W	2d	24-Sep-26 A	29-Oct-26	410d	17,587	8,794	17,587
	JDH3-02-009-R101-Electrical Network - EL	26d	11-Aug-26 A	27-Oct-26	318d	1,507,917	1,432,521	1,507,917
	JDH3-02-009-R101-(EL)-MV cable trench size 3.0m wide and 80	8d	15-Aug-26 A	27-Oct-26	318d	7,566	7,188	7,566
	Backfilling + Warning Tape for MV Cable Trench 3.0m wide - 80	8d	15-Aug-26 A	27-Oct-26	318d	7,566	7,188	7,566
	JDH3-02-009-R101-(EL)-MV cables AL/XLPE/LLDPE Unarmored	16d	11-Aug-26 A	27-Oct-26	318d	1,500,351	1,425,333	1,500,351
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	14d	11-Aug-26 A	27-Oct-26	318d	1,431,061	1,359,508	1,431,061
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2d	13-Aug-26 A	27-Oct-26	318d	66,710	63,374	66,710
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2d	22-Aug-26 A	27-Oct-26	318d	2,580	2,451	2,580
	JDH3-02-009-R101-Street Lighting Network -SL	47d	22-Sep-26 A	19-Nov-26	318d	75,506	49,598	198,404
	JDH3-02-009-R101-(SL)-Lighting Unit Substation 33/0.4 KV, 500	10d	27-Oct-26	08-Nov-26	318d	42,511	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2d	27-Oct-26	29-Oct-26	322d	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2d	29-Oct-26	01-Nov-26	322d	1,700	0	3,401
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2d	05-Nov-26	08-Nov-26	318d	0	0	3,401
	JDH3-02-009-R101-(SL)- LV Cables - Copper, 3 x1 Cx 50 mm², Cu/X	2d	01-Nov-26	03-Nov-26	322d	0	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z1-F	2d	01-Nov-26	03-Nov-26	322d	0	0	1,520
	JDH3-02-009-R101-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP	43d	26-Sep-26 A	15-Nov-26	318d	4,797	46,210	63,958
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4d	01-Nov-26	05-Nov-26	322d	0	0	3,198
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4d	10-Nov-26	15-Nov-26	318d	0	0	6,396
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4d	27-Sep-26 A	01-Nov-26	322d	0	40,773	47,969
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	26-Sep-26 A	01-Nov-26	322d	4,797	5,436	6,396
	JDH3-02-009-R101-(SL)-Lighting Pole with double arms 16 m he	3d	22-Sep-26 A	10-Nov-26	318d	0	3,389	3,987
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3d	22-Sep-26 A	10-Nov-26	318d	0	3,389	3,987
	JDH3-02-009-R101-(SL)-Earthing System for Streetlighting feed	2d	15-Nov-26	17-Nov-26	318d	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2d	15-Nov-26	17-Nov-26	318d	0	0	852
	JDH3-02-009-R101-(SL)- LV Distribution Panel Main: 100A, MCC	6d	27-Oct-26	03-Nov-26	330d	1,837	0	18,369
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z1-R101-	2d	27-Oct-26	29-Oct-26	330d	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z1-F	2d	29-Oct-26	01-Nov-26	330d	0	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z1-R101-	2d	01-Nov-26	03-Nov-26	330d	0	0	12,858
	JDH3-02-009-R101-(SL)-KWH meter mounting frame	2d	17-Nov-26	19-Nov-26	318d	0	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z1-R101-SL	2d	17-Nov-26	19-Nov-26	318d	0	0	2,072
	JDH3-02-009-R101-(SL)- LV Cables - Aluminium, 4Cx185mm², AL	8d	27-Oct-26	05-Nov-26	318d	1,151	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2d	27-Oct-26	29-Oct-26	318d	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2d	29-Oct-26	01-Nov-26	318d	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2(	2d	01-Nov-26	03-Nov-26	318d	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2d	03-Nov-26	05-Nov-26	318d	61	0	121
	JDH3-02-009-R101-(SL)-RMU 33 KV	12d	27-Oct-26	10-Nov-26	318d	25,210	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z1-R101-SL	2d	27-Oct-26	29-Oct-26	324d	25,210	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z1-R101-S	2d	29-Oct-26	01-Nov-26	324d	0	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z1-R1	2d	08-Nov-26	10-Nov-26	318d	0	0	4,202
	JDH3-02-009-R101-Catch Basins (Storm Network) - ST	5d	27-Oct-26	01-Nov-26	389d	17,616	0	17,616
	JDH3-02-009-R101-(ST)-Single Catch Basin Works	5d	27-Oct-26	01-Nov-26	389d	9,315	0	9,315
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5d	27-Oct-26	01-Nov-26	389d	9,315	0	9,315
	JDH3-02-009-R101-(ST)-Double Catch Basin Works	2d	27-Oct-26	28-Oct-26	392d	8,301	0	8,301
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	392d	8,301	0	8,301

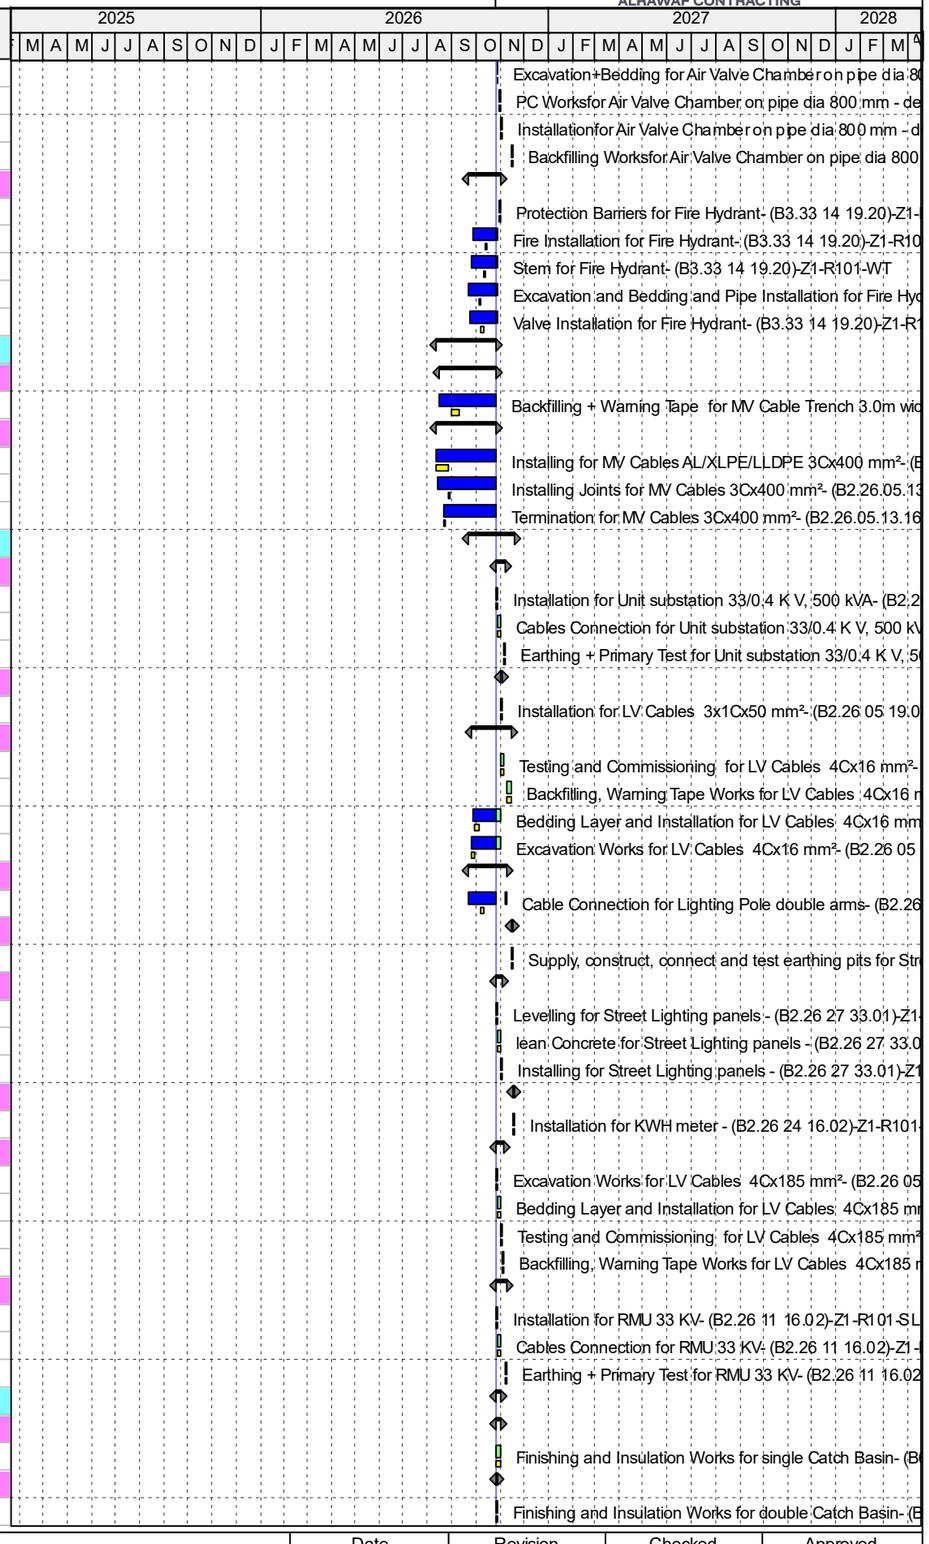

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
R102		45d	01-Sep-26 A	26-Nov-26	397d	746,024	54,783	746,024
JDH3-02-009-R102-Catch Basins (Storm Network) - ST		5d	27-Oct-26	01-Nov-26	384d	21,758	0	21,758
JDH3-02-009-R102-(ST)-Single Catch Basin Works		5d	27-Oct-26	01-Nov-26	384d	10,136	0	10,136
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5d	27-Oct-26	01-Nov-26	384d	10,136	0	10,136
JDH3-02-009-R102-(ST)-Double Catch Basin Works		2d	27-Oct-26	28-Oct-26	387d	11,622	0	11,622
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2d	27-Oct-26	28-Oct-26	387d	11,622	0	11,622
JDH3-02-009-R102-TSE Network - TSE		10d	27-Oct-26	07-Nov-26	413d	226,152	0	226,152
JDH3-02-009-R102-(TSE)-Butterfly Valve-400 mm on pipe dia (31		4d	29-Oct-26	02-Nov-26	415d	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2d	29-Oct-26	31-Oct-26	415d	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2d	01-Nov-26	02-Nov-26	415d	7,822	0	7,822
JDH3-02-009-R102-(TSE)-Wash-Out Valve-100 mm on pipe dia (3		4d	27-Oct-26	31-Oct-26	419d	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2d	27-Oct-26	28-Oct-26	419d	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2d	29-Oct-26	31-Oct-26	419d	1,613	0	1,613
JDH3-02-009-R102-(TSE)-Wash-Out Chamber on 315 mm dia pi		8d	27-Oct-26	04-Nov-26	415d	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2d	27-Oct-26	28-Oct-26	415d	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2d	29-Oct-26	31-Oct-26	415d	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2d	01-Nov-26	02-Nov-26	415d	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - (	2d	03-Nov-26	04-Nov-26	415d	4,177	0	4,177
JDH3-02-009-R102-(TSE)-Wash-Out Valve-100 mm on pipe dia (4		4d	27-Oct-26	31-Oct-26	415d	16,909	0	16,909
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2d	27-Oct-26	28-Oct-26	415d	15,218	0	15,218
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 4(	2d	29-Oct-26	31-Oct-26	415d	1,691	0	1,691
JDH3-02-009-R102-(TSE)-Air Valve-65 mm on pipe dia (400) mm		4d	29-Oct-26	02-Nov-26	415d	15,581	0	15,581
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33 14	2d	29-Oct-26	31-Oct-26	415d	14,023	0	14,023
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (I	2d	01-Nov-26	02-Nov-26	415d	1,558	0	1,558
JDH3-02-009-R102-(TSE)-Valve Chamber on 400 mm dia pipelin		8d	27-Oct-26	04-Nov-26	415d	43,184	0	43,184
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 4(	2d	27-Oct-26	28-Oct-26	415d	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	29-Oct-26	31-Oct-26	415d	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Nov-26	02-Nov-26	415d	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	03-Nov-26	04-Nov-26	415d	8,637	0	8,637
JDH3-02-009-R102-(TSE)-Wash-Out Chamber on 400 mm dia pi		8d	27-Oct-26	04-Nov-26	415d	20,974	0	20,974
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2d	27-Oct-26	28-Oct-26	372d	3,146	0	3,146
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2d	29-Oct-26	31-Oct-26	415d	2,097	0	2,097
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2d	01-Nov-26	02-Nov-26	415d	11,536	0	11,536
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm - (	2d	03-Nov-26	04-Nov-26	415d	4,195	0	4,195
JDH3-02-009-R102-(TSE)-Air Valve Chamber on 400 mm dia pip		8d	29-Oct-26	07-Nov-26	406d	14,269	0	14,269
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2d	29-Oct-26	31-Oct-26	372d	2,140	0	2,140
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2d	01-Nov-26	02-Nov-26	406d	1,427	0	1,427
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2d	03-Nov-26	04-Nov-26	406d	7,848	0	7,848
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2d	05-Nov-26	07-Nov-26	406d	2,854	0	2,854
JDH3-02-009-R102-Potable Water Network - WT		24d	27-Oct-26	23-Nov-26	399d	371,159	0	371,159
JDH3-02-009-R102-(WT)-Wash-Out Valve-200 mm on pipe dia (8		4d	29-Oct-26	02-Nov-26	415d	27,358	0	27,358
	Installation for Wash-Out Valve 200 mm on pipe dia 800 mm- (E	2d	29-Oct-26	31-Oct-26	415d	24,622	0	24,622
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 8(	2d	01-Nov-26	02-Nov-26	415d	2,736	0	2,736
JDH3-02-009-R102-(WT)-Wash-Out Chamber on 800 mm dia pip		8d	27-Oct-26	04-Nov-26	413d	32,136	0	32,136
	Excavation+Bedding for Wash-Out Chamber on pipe dia 800 m	2d	27-Oct-26	28-Oct-26	413d	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 800 mm - depth fr	2d	29-Oct-26	31-Oct-26	413d	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 800 mm - depth	2d	01-Nov-26	02-Nov-26	413d	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm - (	2d	03-Nov-26	04-Nov-26	413d	6,427	0	6,427
JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr		2d	27-Oct-26	28-Oct-26	352d	1,257	0	1,257
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	2d	27-Oct-26	28-Oct-26	352d	1,257	0	1,257
JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr		9d	14-Nov-26	23-Nov-26	399d	3,141	0	3,141
	Primary Test for HDPE Pipe Line 800 mm - depth from 4.51 to 5	9d	14-Nov-26	23-Nov-26	399d	3,141	0	3,141
JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr		9d	03-Nov-26	12-Nov-26	399d	23,070	0	23,070



Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	9d	03-Nov-26	12-Nov-26	399d	23,070	0	23,070
	JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr	2d	01-Nov-26	02-Nov-26	399d	71,275	0	71,275
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	2d	01-Nov-26	02-Nov-26	399d	71,275	0	71,275
	JDH3-02-009-R102-(WT)-Butterfly Valve-300 mm on pipe dia (315	14d	01-Nov-26	16-Nov-26	352d	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2d	01-Nov-26	02-Nov-26	362d	14,517	0	14,517
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2d	15-Nov-26	16-Nov-26	352d	1,613	0	1,613
	JDH3-02-009-R102-(WT)-Butterfly Valve-800 mm on pipe dia (80	2d	03-Nov-26	04-Nov-26	362d	59,179	0	59,179
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	03-Nov-26	04-Nov-26	362d	59,179	0	59,179
	JDH3-02-009-R102-(WT)-Air Valve-110 mm on pipe dia (800) mm	4d	01-Nov-26	04-Nov-26	415d	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 14	2d	01-Nov-26	02-Nov-26	415d	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2d	03-Nov-26	04-Nov-26	415d	2,501	0	2,501
	JDH3-02-009-R102-(WT)-Valve Chamber on 315 mm dia pipeline	6d	29-Oct-26	04-Nov-26	364d	11,469	0	11,469
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2d	29-Oct-26	31-Oct-26	352d	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	01-Nov-26	02-Nov-26	364d	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	03-Nov-26	04-Nov-26	364d	7,885	0	7,885
	JDH3-02-009-R102-(WT)-Valve Chamber on 800 mm dia pipeline	6d	01-Nov-26	07-Nov-26	364d	25,597	0	25,597
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2d	01-Nov-26	02-Nov-26	352d	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	03-Nov-26	04-Nov-26	364d	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	05-Nov-26	07-Nov-26	364d	17,598	0	17,598
	JDH3-02-009-R102-(WT)-Air Valve Chamber on 800 mm dia pipe	8d	29-Oct-26	07-Nov-26	413d	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2d	29-Oct-26	31-Oct-26	413d	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2d	01-Nov-26	02-Nov-26	413d	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2d	03-Nov-26	04-Nov-26	413d	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2d	05-Nov-26	07-Nov-26	413d	1,428	0	1,428
	JDH3-02-009-R102-(WT)-Fire Hydrant	10d	03-Nov-26	14-Nov-26	352d	68,396	0	68,396
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2d	03-Nov-26	04-Nov-26	352d	6,840	0	6,840
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-W	2d	05-Nov-26	07-Nov-26	352d	13,679	0	13,679
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-WT	2d	08-Nov-26	09-Nov-26	352d	20,519	0	20,519
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-WT	2d	10-Nov-26	11-Nov-26	352d	23,939	0	23,939
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-W	2d	12-Nov-26	14-Nov-26	352d	3,420	0	3,420
	JDH3-02-009-R102-Electrical Network - EL	7d	22-Sep-26 A	23-Nov-26	392d	7,400	5,920	7,400
	JDH3-02-009-R102-(EL)-MV cable trench size 3.0m wide and 80	2d	22-Sep-26 A	23-Nov-26	392d	1,084	867	1,084
	Excavation for MV Cable Trench 3.0m wide - 80cm deep- (B2.3	2d	22-Sep-26 A	23-Nov-26	392d	1,084	867	1,084
	JDH3-02-009-R102-(EL)-MV cable trench size 2.0m wide and 80	5d	23-Sep-26 A	23-Nov-26	352d	6,316	5,052	6,316
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5d	23-Sep-26 A	23-Nov-26	352d	6,316	5,052	6,316
	JDH3-02-009-R102-Street Lighting Network -SL	14d	01-Sep-26 A	26-Nov-26	363d	57,487	48,864	57,487
	JDH3-02-009-R102-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	8d	01-Sep-26 A	19-Nov-26	354d	46,423	39,460	46,423
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4d	01-Sep-26 A	19-Nov-26	353d	5,462	4,642	5,462
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4d	03-Sep-26 A	19-Nov-26	354d	40,962	34,817	40,962
	JDH3-02-009-R102-(SL)-Lighting Pole with double arms 16 m he	3d	03-Sep-26 A	26-Nov-26	353d	4,221	3,588	4,221
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3d	03-Sep-26 A	26-Nov-26	353d	4,221	3,588	4,221
	JDH3-02-009-R102-(SL)- LV Cables - Single Core Copper, 3-1x C	2d	17-Sep-26 A	19-Nov-26	369d	6,842	5,816	6,842
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z2-R	2d	17-Sep-26 A	19-Nov-26	369d	6,842	5,816	6,842
	JDH3-02-009-R102-Telecommunications Network - TEL	18d	27-Oct-26	16-Nov-26	403d	62,069	0	62,069
	JDH3-02-009-R102-(TEL)-Reinforced Concrete Duct 6-ways duct	8d	27-Oct-26	04-Nov-26	403d	3,766	0	3,766
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2d	27-Oct-26	28-Oct-26	403d	565	0	565
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2d	29-Oct-26	31-Oct-26	403d	1,695	0	1,695
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2d	01-Nov-26	02-Nov-26	403d	1,130	0	1,130
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2d	03-Nov-26	04-Nov-26	403d	377	0	377
	JDH3-02-009-R102-(TEL)-Unreinforced Concrete Duct 6-ways du	10d	05-Nov-26	16-Nov-26	403d	58,303	0	58,303
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	2d	05-Nov-26	07-Nov-26	403d	9,717	0	9,717
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	4d	08-Nov-26	11-Nov-26	403d	35,629	0	35,629
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	4d	12-Nov-26	16-Nov-26	403d	12,956	0	12,956

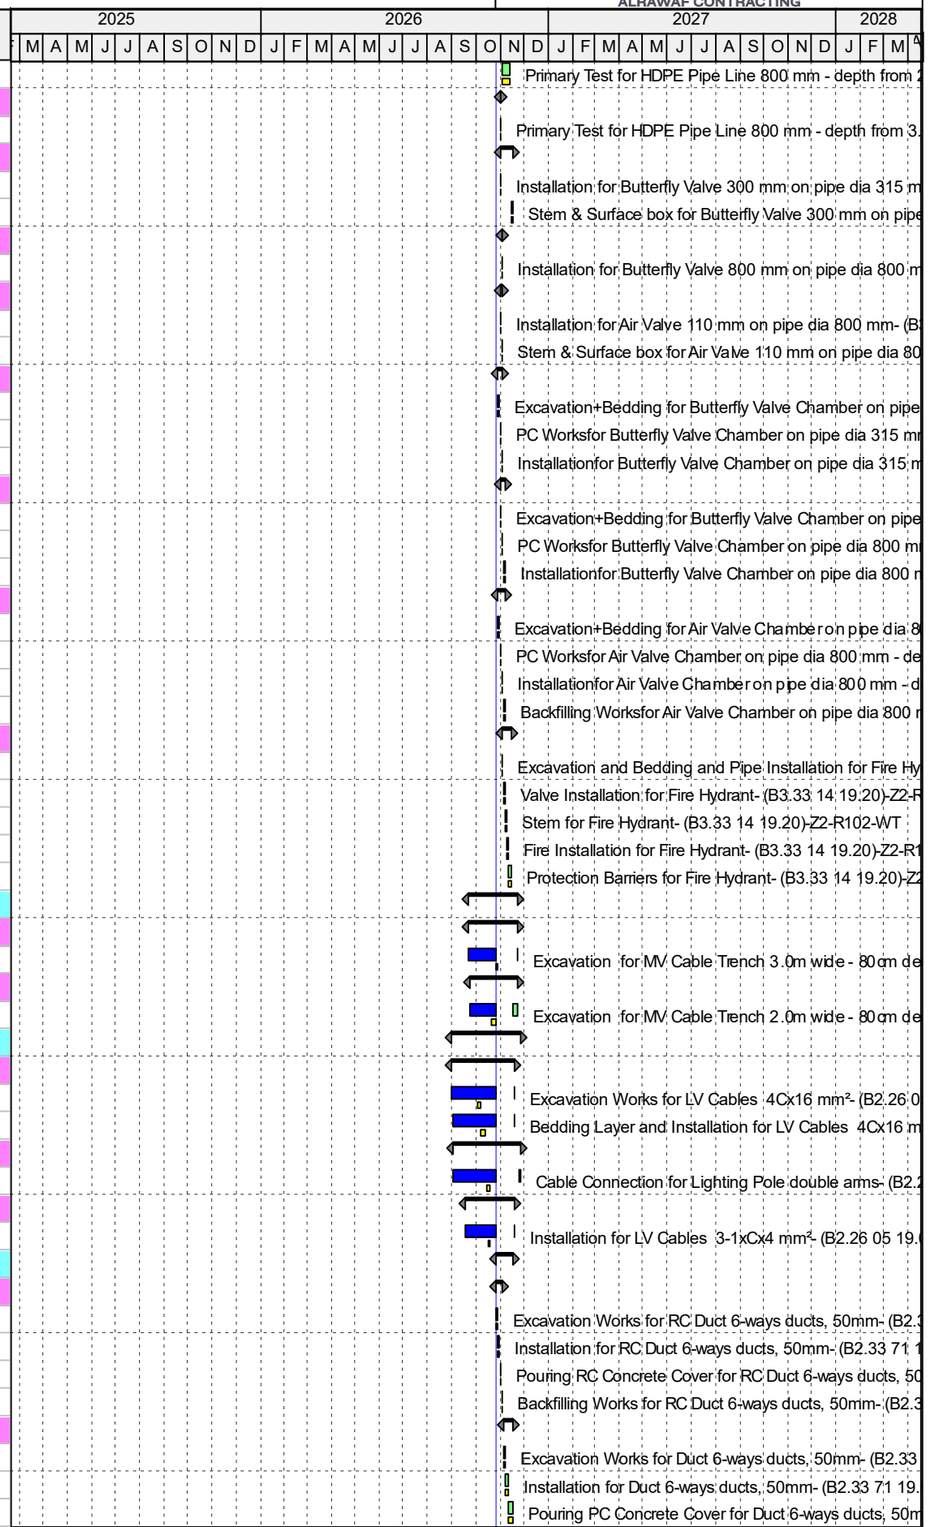


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
R100		78d	01-Sep-26 A	01-Dec-26	392d	241,519	3,158	457,729
JDH3-02-009-R100-TSE Network - TSE		50d	01-Sep-26 A	31-Oct-26	404d	10,766	3,158	10,766
JDH3-02-009-R100-(TSE)-Valve Chamber on 315 mm dia pipelin		50d	01-Sep-26 A	31-Oct-26	404d	10,766	3,158	10,766
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 mı	2d	28-Oct-26	31-Oct-26	404d	2,871	0	2,871
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	01-Sep-26 A	28-Oct-26	404d	7,895	3,158	7,895
JDH3-02-009-R100-Potable Water Network - WT		2d	27-Oct-26	28-Oct-26	421d	1,466	0	1,466
JDH3-02-009-R100-(WT)-Fire Hydrant		2d	27-Oct-26	28-Oct-26	421d	1,466	0	1,466
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R100-V	2d	27-Oct-26	28-Oct-26	421d	1,466	0	1,466
JDH3-02-009-R100-Street Lighting Network -SL		19d	27-Oct-26	18-Nov-26	404d	229,287	0	229,287
JDH3-02-009-R100-(SL)- LV Cables - Copper, 4 Cx 95 mm², Cu/XLP		16d	31-Oct-26	18-Nov-26	404d	207,771	0	207,771
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	4d	31-Oct-26	04-Nov-26	404d	20,777	0	20,777
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	4d	04-Nov-26	09-Nov-26	404d	155,828	0	155,828
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	4d	09-Nov-26	14-Nov-26	404d	10,389	0	10,389
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	4d	14-Nov-26	18-Nov-26	404d	20,777	0	20,777
JDH3-02-009-R100-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP		14d	27-Oct-26	11-Nov-26	392d	15,736	0	15,736
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	7d	27-Oct-26	03-Nov-26	392d	5,245	0	5,245
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	7d	04-Nov-26	11-Nov-26	392d	10,491	0	10,491
JDH3-02-009-R100-(SL)-Earthing System for Distribution panels		2d	15-Nov-26	16-Nov-26	392d	4,502	0	4,502
	Supply, construct, connect and test earthing pits for Street Light	2d	15-Nov-26	16-Nov-26	392d	4,502	0	4,502
JDH3-02-009-R100-(SL)-Earthing System for Streetlighting feed		2d	12-Nov-26	14-Nov-26	392d	1,278	0	1,278
	Supply, construct, connect and test earthing pits for Street Light	2d	12-Nov-26	14-Nov-26	392d	1,278	0	1,278
JDH3-02-009-R100-Road Works - RD		31d	27-Oct-26	01-Dec-26	392d	0	0	216,210
JDH3-02-009-R100-(RD)-Bituminous concrete wearing course 5(		2d	27-Oct-26	28-Oct-26	407d	0	0	125,069
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	2d	27-Oct-26	28-Oct-26	407d	0	0	125,069
JDH3-02-009-R100-(RD)-Precast Concrete Curb		3d	25-Nov-26	28-Nov-26	392d	0	0	26,534
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3d	25-Nov-26	28-Nov-26	392d	0	0	26,534
JDH3-02-009-R100-(RD)-Precast Interlocking Block Pavers		3d	29-Nov-26	01-Dec-26	392d	0	0	51,566
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	3d	29-Nov-26	01-Dec-26	392d	0	0	51,566
JDH3-02-009-R100-(RD)-Pavement Marking		10d	29-Oct-26	09-Nov-26	407d	0	0	9,010
	Thermoplastic continuous 120 mm wide centre lane- single line	2d	29-Oct-26	31-Oct-26	407d	0	0	32
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2d	01-Nov-26	02-Nov-26	407d	0	0	7,461
	Thermoplastic continuous Chevron hatching - white (round abou	2d	03-Nov-26	04-Nov-26	407d	0	0	162
	Thermoplastic continuous Painted rumble strips marking (300m	2d	05-Nov-26	07-Nov-26	407d	0	0	702
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2d	08-Nov-26	09-Nov-26	407d	0	0	654
JDH3-02-009-R100-(RD)-Traffic Signage		4d	10-Nov-26	14-Nov-26	407d	0	0	4,031
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2d	10-Nov-26	11-Nov-26	407d	0	0	1,635
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2d	12-Nov-26	14-Nov-26	407d	0	0	2,396
Roundabout - Road 450 - RA		20d	27-Oct-26	18-Nov-26	350d	0	0	989,960
RA5		20d	27-Oct-26	18-Nov-26	309d	0	0	714,089
JDH3-02-009-RA5-Earthworks - EW		8d	27-Oct-26	04-Nov-26	320d	0	0	141,956
	Excavation Works for Roundabout - (B1.31 22 00.01)-Z1-RA5-R	4d	27-Oct-26	31-Oct-26	289d	0	0	57,908
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	4d	01-Nov-26	04-Nov-26	320d	0	0	84,048
JDH3-02-009-RA5-Road Works - RD		16d	01-Nov-26	18-Nov-26	309d	0	0	572,134
JDH3-02-009-RA5-(RD)-Subgrade		8d	01-Nov-26	09-Nov-26	306d	0	0	133,981
	Supply, lay and compaction subgrade compacted thickness 30(	8d	01-Nov-26	09-Nov-26	306d	0	0	133,981
JDH3-02-009-RA5-(RD)-Bituminous concrete wearing course 50		4d	14-Nov-26	18-Nov-26	309d	0	0	281,253
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	4d	14-Nov-26	18-Nov-26	309d	0	0	281,253
JDH3-02-009-RA5-(RD)-Aggregate Base Course		6d	10-Nov-26	16-Nov-26	306d	0	0	156,900
	Supply, lay and compaction Aggregate base course compacted	6d	10-Nov-26	16-Nov-26	306d	0	0	156,900
RA6		15d	01-Nov-26	17-Nov-26	350d	0	0	275,870
JDH3-02-009-RA6-Earthworks - EW		10d	01-Nov-26	11-Nov-26	355d	0	0	151,926
	Excavation Works for Roundabout - (B1.31 22 00.01)-Z2-RA6-R	8d	01-Nov-26	09-Nov-26	289d	0	0	114,317
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	2d	10-Nov-26	11-Nov-26	355d	0	0	37,609

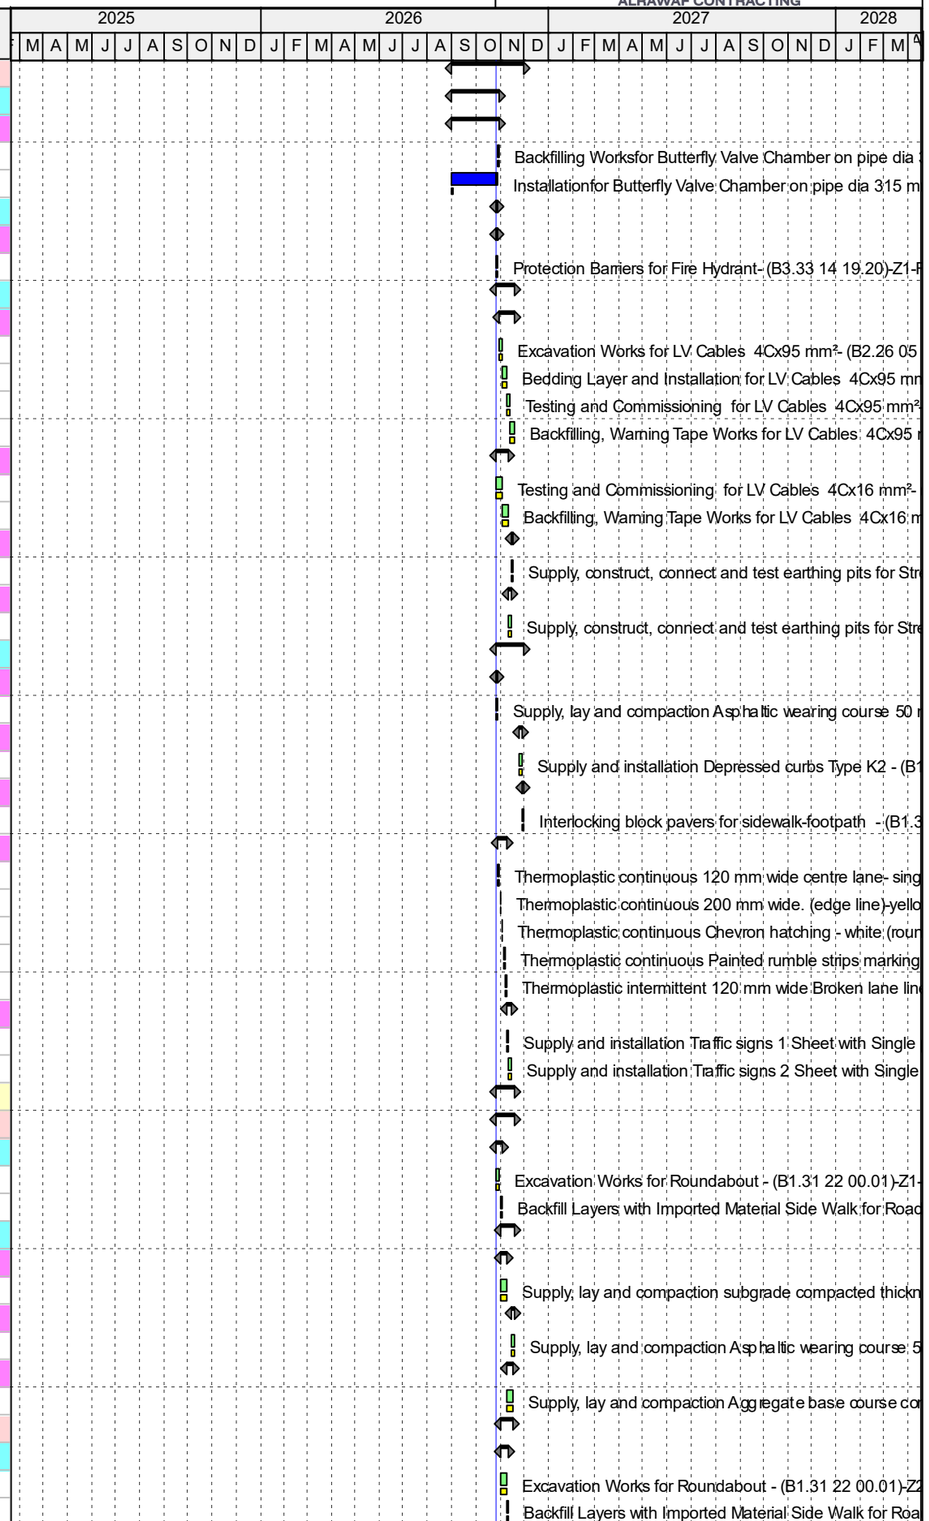

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-RA6-Road Works - RD	7d	10-Nov-26	17-Nov-26	289d	0	0	123,944
	JDH3-02-009-RA6-(RD)-Subgrade	7d	10-Nov-26	17-Nov-26	289d	0	0	123,944
	Supply, lay and compaction subgrade compacted thickness 300	7d	10-Nov-26	17-Nov-26	289d	0	0	123,944
	External Roads - EX	53d	15-Sep-26 A	16-Nov-26	405d	3,392,261	31,856	3,392,261
	R241 - Access Road PW Storage Tanks	18d	27-Oct-26	16-Nov-26	405d	555,912	0	555,912
	JDH3-02-009-R241-Potable Water Network - WT	18d	27-Oct-26	16-Nov-26	405d	555,912	0	555,912
	JDH3-02-009-R241-(WT)-HDPE Pipes-800 mm diameter depth fr	12d	27-Oct-26	09-Nov-26	411d	71,871	0	71,871
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	12d	27-Oct-26	09-Nov-26	411d	71,871	0	71,871
	JDH3-02-009-R241-(WT)-HDPE Pipes-800 mm diameter depth fr	12d	27-Oct-26	09-Nov-26	411d	1,394	0	1,394
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	12d	27-Oct-26	09-Nov-26	411d	1,394	0	1,394
	JDH3-02-009-R241-(WT)-Valve Chamber on 800 mm dia pipeline	8d	01-Nov-26	09-Nov-26	411d	127,983	0	127,983
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2d	01-Nov-26	02-Nov-26	405d	19,197	0	19,197
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2d	03-Nov-26	04-Nov-26	411d	12,798	0	12,798
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2d	05-Nov-26	07-Nov-26	411d	70,391	0	70,391
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 mi	2d	08-Nov-26	09-Nov-26	411d	25,597	0	25,597
	JDH3-02-009-R241-(WT)-Butterfly Valve-800 mm on pipe dia (80	4d	29-Oct-26	02-Nov-26	415d	263,018	0	263,018
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2d	29-Oct-26	31-Oct-26	415d	236,716	0	236,716
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2d	01-Nov-26	02-Nov-26	415d	26,302	0	26,302
	JDH3-02-009-R241-(WT)-Air Valve Chamber on 800 mm dia pipe	8d	03-Nov-26	11-Nov-26	409d	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2d	03-Nov-26	04-Nov-26	405d	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2d	05-Nov-26	07-Nov-26	409d	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2d	08-Nov-26	09-Nov-26	409d	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2d	10-Nov-26	11-Nov-26	409d	1,428	0	1,428
	JDH3-02-009-R241-(WT)-Air Valve-110 mm on pipe dia (800) mm	4d	27-Oct-26	31-Oct-26	417d	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 14	2d	27-Oct-26	28-Oct-26	417d	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2d	29-Oct-26	31-Oct-26	417d	2,501	0	2,501
	JDH3-02-009-R241-(WT)-Wash-Out Valve-200 mm on pipe dia (8	4d	12-Nov-26	16-Nov-26	405d	27,358	0	27,358
	Installation for Wash-Out Valve 200 mm on pipe dia 800 mm- (E	2d	12-Nov-26	14-Nov-26	405d	24,622	0	24,622
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 8(	2d	15-Nov-26	16-Nov-26	405d	2,736	0	2,736
	JDH3-02-009-R241-(WT)-Wash-Out Chamber on 800 mm dia pip	8d	05-Nov-26	14-Nov-26	407d	32,136	0	32,136
	Excavation+Bedding for Wash-Out Chamber on pipe dia 800 m	2d	05-Nov-26	07-Nov-26	405d	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 800 mm - depth fr	2d	08-Nov-26	09-Nov-26	405d	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 800 mm - depth	2d	10-Nov-26	11-Nov-26	405d	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm - c	2d	12-Nov-26	14-Nov-26	407d	6,427	0	6,427
	R242 - Access Road PW Storage Tanks	14d	27-Oct-26	11-Nov-26	409d	1,130,081	0	1,130,081
JDI	Surveying Works for Road - R242-EX	0d	27-Oct-26	27-Oct-26	423d	0	0	0
	JDH3-02-009-R242-Potable Water Network - WT	14d	27-Oct-26	11-Nov-26	409d	1,130,081	0	1,130,081
	JDH3-02-009-R242-(WT)-HDPE Pipes-1000 mm diameter depth f	8d	27-Oct-26	04-Nov-26	415d	65,924	0	65,924
	Primary Test for HDPE Pipe Line 1000 mm - depth from 1.51 to	8d	27-Oct-26	04-Nov-26	415d	65,924	0	65,924
	JDH3-02-009-R242-(WT)-HDPE Pipes-1000 mm diameter depth f	8d	27-Oct-26	04-Nov-26	415d	141,987	0	141,987
	Primary Test for HDPE Pipe Line 1000 mm - depth from 1.51 to	8d	27-Oct-26	04-Nov-26	415d	141,987	0	141,987
	JDH3-02-009-R242-(WT)-Wash-Out Valve-200 mm on pipe dia (1	4d	01-Nov-26	04-Nov-26	411d	39,083	0	39,083
	Installation for Wash-Out Valve 200 mm on pipe dia 1000 mm-	2d	01-Nov-26	02-Nov-26	411d	35,175	0	35,175
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 1(	2d	03-Nov-26	04-Nov-26	411d	3,908	0	3,908
	JDH3-02-009-R242-(WT)-Valve Chamber on 1000 mm dia pipelir	10d	27-Oct-26	07-Nov-26	411d	191,975	0	191,975
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 10	2d	27-Oct-26	28-Oct-26	405d	28,796	0	28,796
	PC Worksfor Butterfly Valve Chamber on pipe dia 1000 mm - de	2d	29-Oct-26	31-Oct-26	413d	19,197	0	19,197
	Installationfor Butterfly Valve Chamber on pipe dia 1000 mm - d	2d	01-Nov-26	02-Nov-26	413d	105,586	0	105,586
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 1000 m	2d	05-Nov-26	07-Nov-26	411d	38,395	0	38,395
	JDH3-02-009-R242-(WT)-Butterfly Valve-1000 mm on pipe dia (1(	4d	29-Oct-26	02-Nov-26	411d	493,159	0	493,159
	Installation for Butterfly Valve 1000 mm on pipe dia 1000 mm- (	2d	29-Oct-26	31-Oct-26	411d	443,843	0	443,843
	Stem & Surface box for Butterfly Valve 1000 mm on pipe dia 10	2d	01-Nov-26	02-Nov-26	411d	49,316	0	49,316
	JDH3-02-009-R242-(WT)-Wash-Out Chamber on 1000 mm dia pi	10d	29-Oct-26	09-Nov-26	411d	32,136	0	32,136

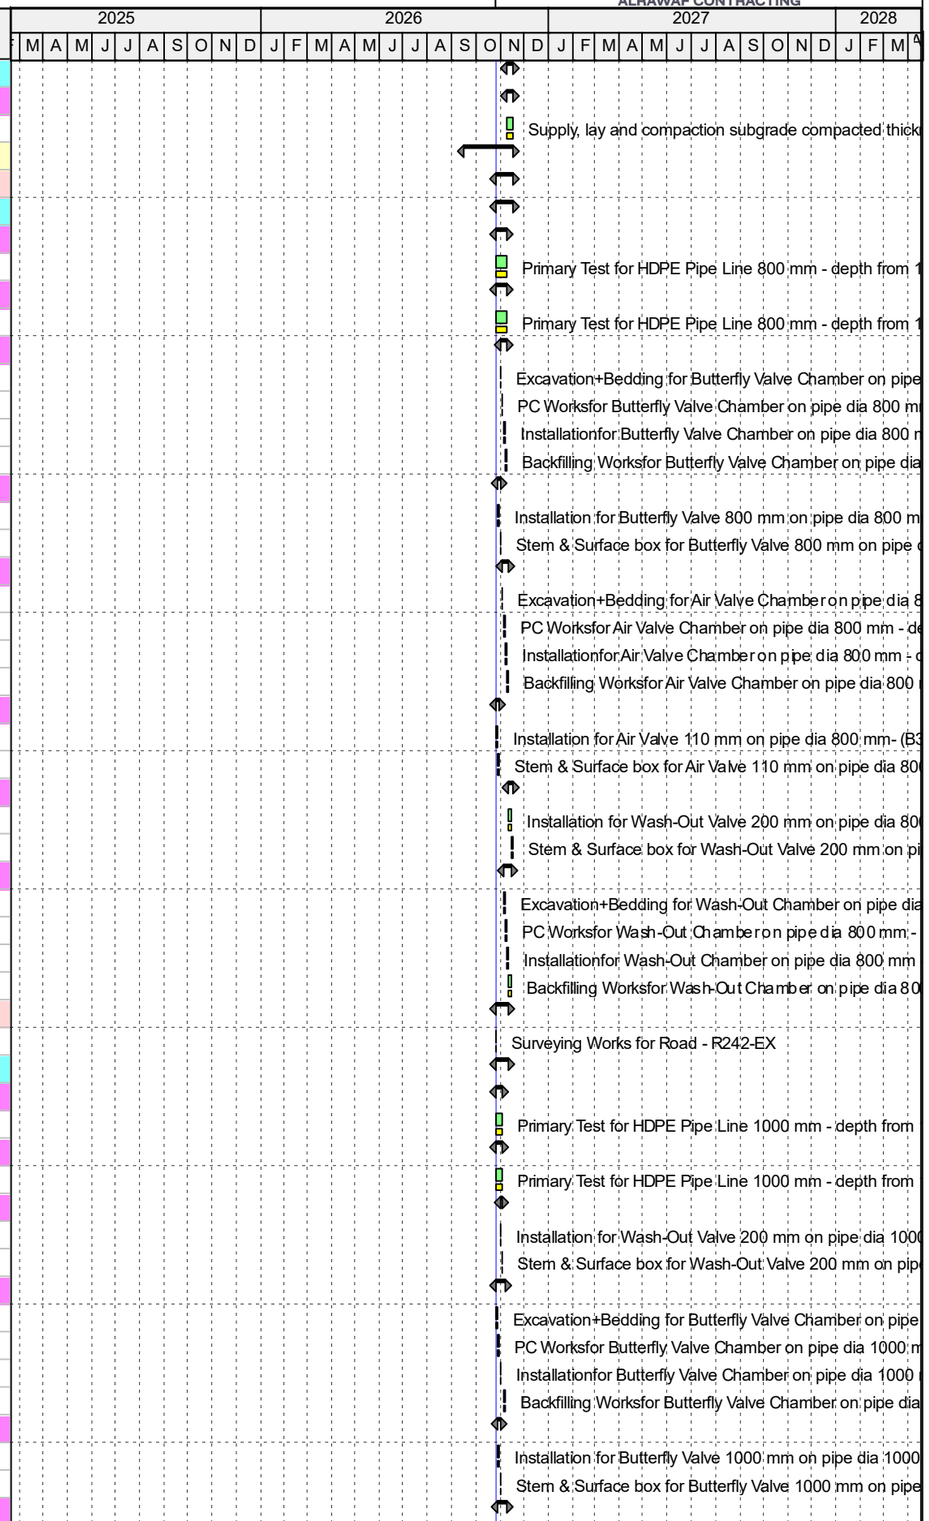

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Wash-Out Chamber on pipe dia 1000 r	2d	29-Oct-26	31-Oct-26	409d	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 1000 mm - depth	2d	01-Nov-26	02-Nov-26	413d	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 1000 mm - deptl	2d	03-Nov-26	04-Nov-26	413d	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 1000 mm -	2d	08-Nov-26	09-Nov-26	411d	6,427	0	6,427
	JDH3-02-009-R242-(WT)-Valve Chamber on 315 mm dia pipeline	8d	01-Nov-26	09-Nov-26	411d	14,336	0	14,336
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2d	01-Nov-26	02-Nov-26	409d	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2d	03-Nov-26	04-Nov-26	409d	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2d	05-Nov-26	07-Nov-26	409d	7,885	0	7,885
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 mi	2d	08-Nov-26	09-Nov-26	411d	2,867	0	2,867
	JDH3-02-009-R242-(WT)-Butterfly Valve-300 mm on pipe dia (31	4d	08-Nov-26	11-Nov-26	409d	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2d	08-Nov-26	09-Nov-26	409d	14,517	0	14,517
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 31	2d	10-Nov-26	11-Nov-26	409d	1,613	0	1,613
	JDH3-02-009-R242-(WT)-Butterfly Valve-600 mm on pipe dia (63	4d	27-Oct-26	31-Oct-26	415d	98,633	0	98,633
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2d	27-Oct-26	28-Oct-26	411d	88,769	0	88,769
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 63(	2d	29-Oct-26	31-Oct-26	415d	9,863	0	9,863
	JDH3-02-009-R242-(WT)-Valve Chamber on 630 mm dia pipeline	8d	29-Oct-26	07-Nov-26	411d	36,718	0	36,718
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2d	29-Oct-26	31-Oct-26	405d	5,508	0	5,508
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2d	01-Nov-26	02-Nov-26	411d	3,672	0	3,672
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2d	03-Nov-26	04-Nov-26	411d	20,195	0	20,195
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 mi	2d	05-Nov-26	07-Nov-26	411d	7,344	0	7,344
R251 - Access Road TSE Storage Tanks		39d	22-Sep-26 A	09-Nov-26	411d	227,022	13,498	227,022
JDH3-02-009-R251-TSE Network - TSE		39d	22-Sep-26 A	09-Nov-26	411d	227,022	13,498	227,022
JDH3-02-009-R251-(TSE)-Air Valve Chamber on 400 mm dia pip		39d	22-Sep-26 A	09-Nov-26	411d	14,269	5,708	14,269
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2d	08-Nov-26	09-Nov-26	411d	2,854	0	2,854
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2d	22-Sep-26 A	28-Oct-26	419d	2,140	1,070	2,140
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2d	23-Sep-26 A	28-Oct-26	419d	1,427	713	1,427
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2d	24-Sep-26 A	02-Nov-26	415d	7,848	3,924	7,848
	JDH3-02-009-R251-(TSE)-Wash-Out Chamber on 400 mm dia pi	10d	27-Oct-26	07-Nov-26	411d	41,949	0	41,949
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2d	27-Oct-26	28-Oct-26	413d	6,292	0	6,292
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2d	29-Oct-26	31-Oct-26	413d	4,195	0	4,195
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2d	01-Nov-26	02-Nov-26	413d	23,072	0	23,072
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm - c	2d	05-Nov-26	07-Nov-26	411d	8,390	0	8,390
	JDH3-02-009-R251-(TSE)-Air Valve-65 mm on pipe dia (400) mm	4d	26-Sep-26 A	09-Nov-26	411d	15,581	7,790	15,581
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (	2d	27-Sep-26 A	09-Nov-26	411d	1,558	779	1,558
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33 14	2d	26-Sep-26 A	07-Nov-26	413d	14,023	7,011	14,023
	JDH3-02-009-R251-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4d	05-Nov-26	09-Nov-26	411d	33,818	0	33,818
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2d	05-Nov-26	07-Nov-26	411d	30,436	0	30,436
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 4(	2d	08-Nov-26	09-Nov-26	411d	3,382	0	3,382
	JDH3-02-009-R251-(TSE)-Butterfly Valve-400 mm on pipe dia (31	4d	03-Nov-26	07-Nov-26	413d	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2d	03-Nov-26	04-Nov-26	413d	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2d	05-Nov-26	07-Nov-26	413d	7,822	0	7,822
	JDH3-02-009-R251-(TSE)-Valve Chamber on 400 mm dia pipelin	8d	27-Oct-26	04-Nov-26	415d	43,184	0	43,184
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 4(	2d	27-Oct-26	28-Oct-26	415d	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	29-Oct-26	31-Oct-26	415d	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Nov-26	02-Nov-26	415d	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 mi	2d	03-Nov-26	04-Nov-26	415d	8,637	0	8,637
R252 - Access Road TSE Storage Tanks		18d	27-Oct-26	16-Nov-26	405d	1,302,210	0	1,302,210
JDH3-02-009-R252-TSE Network - TSE		18d	27-Oct-26	16-Nov-26	405d	1,302,210	0	1,302,210
JDH3-02-009-R252-(TSE)-Butterfly Valve-600 mm on pipe dia (63		4d	08-Nov-26	11-Nov-26	405d	542,479	0	542,479
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B4	2d	08-Nov-26	09-Nov-26	405d	488,231	0	488,231
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 63(	2d	10-Nov-26	11-Nov-26	405d	54,248	0	54,248
	JDH3-02-009-R252-(TSE)-Wash-Out Valve-150 mm on pipe dia (	4d	10-Nov-26	14-Nov-26	405d	195,417	0	195,417
	Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E	2d	10-Nov-26	11-Nov-26	405d	175,875	0	175,875

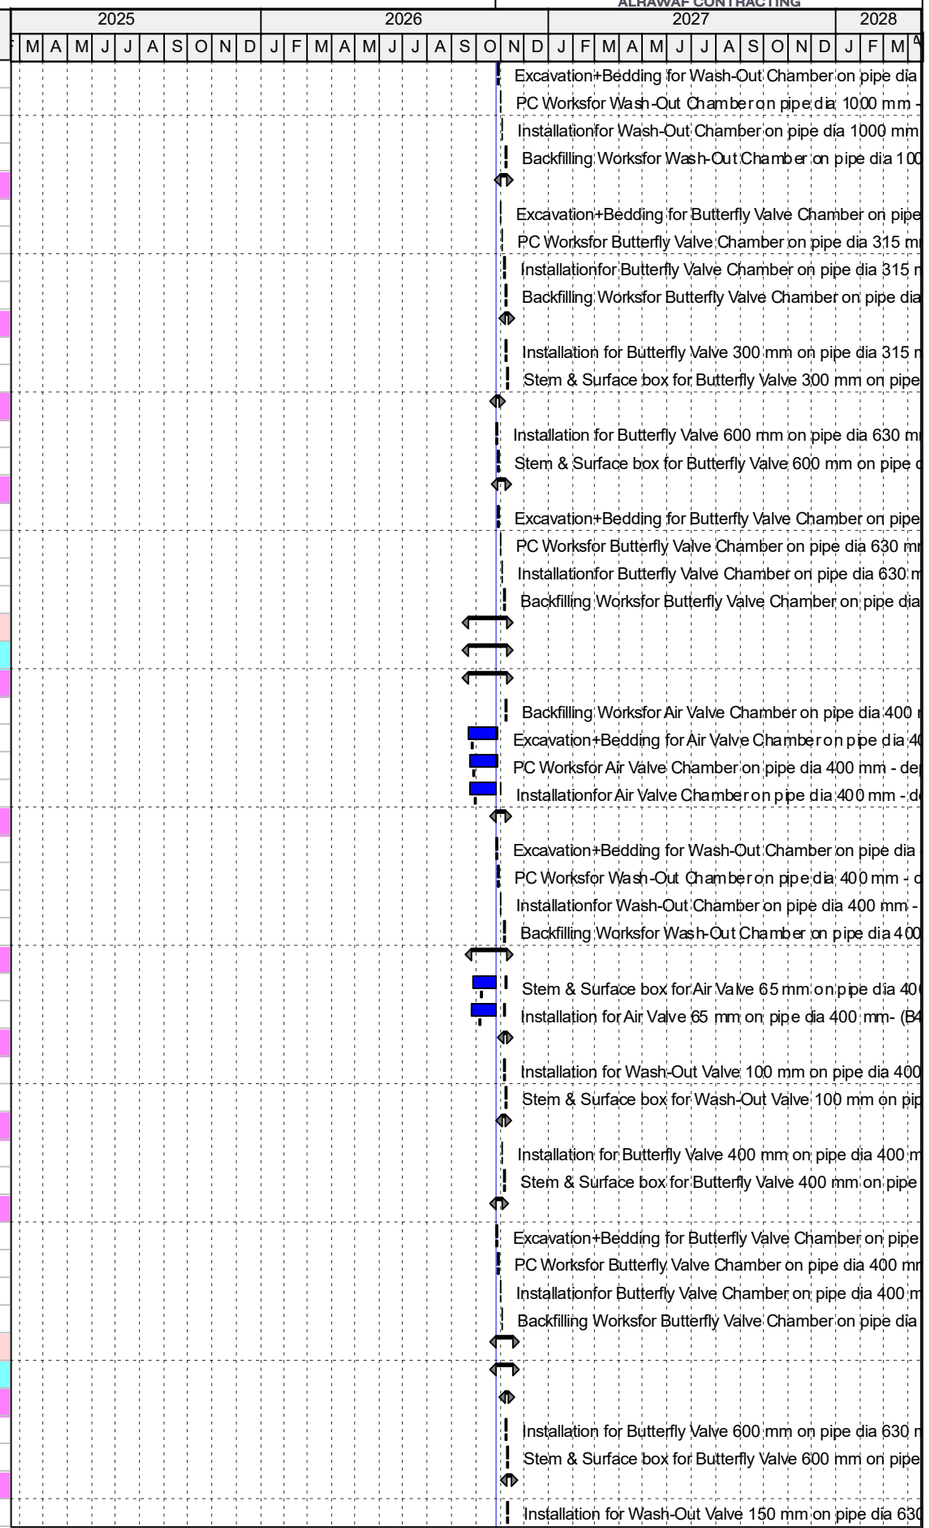


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6:	2d	12-Nov-26	14-Nov-26	405d	19,542	0	19,542
	JDH3-02-009-R252-(TSE)-Air Valve-65 mm on pipe dia (630) mm	4d	12-Nov-26	16-Nov-26	405d	187,600	0	187,600
	Installation for Air Valve 65 mm on pipe dia 630 mm- (B4.33 14	2d	12-Nov-26	14-Nov-26	405d	168,840	0	168,840
	Stem & Surface box for Air Valve 65 mm on pipe dia 630 mm-(	2d	15-Nov-26	16-Nov-26	405d	18,760	0	18,760
	JDH3-02-009-R252-(TSE)-Valve Chamber on 630 mm dia pipelin	8d	27-Oct-26	04-Nov-26	411d	202,721	0	202,721
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2d	27-Oct-26	28-Oct-26	405d	30,408	0	30,408
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2d	29-Oct-26	31-Oct-26	405d	20,272	0	20,272
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2d	01-Nov-26	02-Nov-26	405d	111,497	0	111,497
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2d	03-Nov-26	04-Nov-26	411d	40,544	0	40,544
	JDH3-02-009-R252-(TSE)-Wash-Out Chamber on 630 mm dia pi	8d	29-Oct-26	07-Nov-26	411d	137,902	0	137,902
	Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m	2d	29-Oct-26	31-Oct-26	405d	20,685	0	20,685
	PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fr	2d	01-Nov-26	02-Nov-26	405d	13,790	0	13,790
	Installationfor Wash-Out Chamber on pipe dia 630 mm - depth	2d	03-Nov-26	04-Nov-26	405d	75,846	0	75,846
	Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm -	2d	05-Nov-26	07-Nov-26	411d	27,580	0	27,580
	JDH3-02-009-R252-(TSE)-Air Valve Chamber on 630 mm dia pip	8d	01-Nov-26	09-Nov-26	411d	36,091	0	36,091
	Excavation+Bedding for Air Valve Chamber on pipe dia 630 mm	2d	01-Nov-26	02-Nov-26	405d	5,414	0	5,414
	PC Worksfor Air Valve Chamber on pipe dia 630 mm - depth fro	2d	03-Nov-26	04-Nov-26	405d	3,609	0	3,609
	Installationfor Air Valve Chamber on pipe dia 630 mm - depth fr	2d	05-Nov-26	07-Nov-26	405d	19,850	0	19,850
	Backfilling Worksfor Air Valve Chamber on pipe dia 630 mm - de	2d	08-Nov-26	09-Nov-26	411d	7,218	0	7,218
	R253 - Access Road TSE Storage Tanks	10d	27-Oct-26	07-Nov-26	411d	121,405	0	121,405
	JDH3-02-009-R253-TSE Network - TSE	10d	27-Oct-26	07-Nov-26	411d	121,405	0	121,405
	JDH3-02-009-R253-(TSE)-Valve Chamber on 400 mm dia pipelin	8d	27-Oct-26	04-Nov-26	411d	43,184	0	43,184
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2d	27-Oct-26	28-Oct-26	411d	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2d	29-Oct-26	31-Oct-26	411d	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2d	01-Nov-26	02-Nov-26	411d	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2d	03-Nov-26	04-Nov-26	411d	8,637	0	8,637
	JDH3-02-009-R253-(TSE)-Butterfly Valve-400 mm on pipe dia (31	4d	03-Nov-26	07-Nov-26	411d	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2d	03-Nov-26	04-Nov-26	411d	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2d	05-Nov-26	07-Nov-26	411d	7,822	0	7,822
	R26	42d	15-Sep-26 A	03-Nov-26	416d	55,631	18,358	55,631
	JDH3-02-009-R26-Sewage Network - SW	42d	15-Sep-26 A	03-Nov-26	416d	55,631	18,358	55,631
	JDH3-02-009-R26-(SW)-MH Works depth from 4.5 to 5.5 Diam 1	40d	15-Sep-26 A	01-Nov-26	419d	29,913	9,971	29,913
	Steel Cover for MH 1500 mm - depth from 4.51 to 5.5 m- (B5.3	3d	28-Oct-26	01-Nov-26	419d	9,971	0	9,971
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	3d	15-Sep-26 A	28-Oct-26	419d	19,942	9,971	19,942
	JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Dim 1	38d	15-Sep-26 A	29-Oct-26	416d	4,710	1,475	4,710
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	2d	28-Oct-26	29-Oct-26	416d	1,761	0	1,761
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2d	15-Sep-26 A	27-Oct-26	416d	2,949	1,475	2,949
	JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Diam	36d	20-Sep-26 A	01-Nov-26	416d	16,531	5,510	16,531
	Steel Cover for MH 1500 mm - depth from 5.51 to 6.5 m- (B5.3	2d	31-Oct-26	01-Nov-26	416d	5,510	0	5,510
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2d	20-Sep-26 A	29-Oct-26	416d	11,021	5,510	11,021
	JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Diam 2	42d	15-Sep-26 A	03-Nov-26	416d	4,477	1,402	4,477
	Steel Cover for MH 2000 mm - depth from 5.51 to 6.5 m- (B5.3	2d	02-Nov-26	03-Nov-26	416d	1,674	0	1,674
	Finishing, Benching Works for MH 2000 mm - depth from 5.51 t	2d	15-Sep-26 A	27-Oct-26	420d	2,803	1,402	2,803
	JDH3-02-009-Close Out	344d	21-Jul-26 A	02-Oct-27	128d	0	3,004,331	5,888,883
	JDH3-02-009-Engineering - EN	130d	27-Oct-26	31-Mar-27	281d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB	130d	27-Oct-26	31-Mar-27	275d	0	0	0
JDI	Prepare and Submit Drawing for Ponds - AS	7d	24-Mar-27	31-Mar-27	263d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z01	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z01-AS-S'	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z01-A	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z02	17d	27-Oct-26	15-Nov-26	383d	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z02-AS-S'	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z02-A	7d	27-Oct-26	03-Nov-26	393d	0	0	0

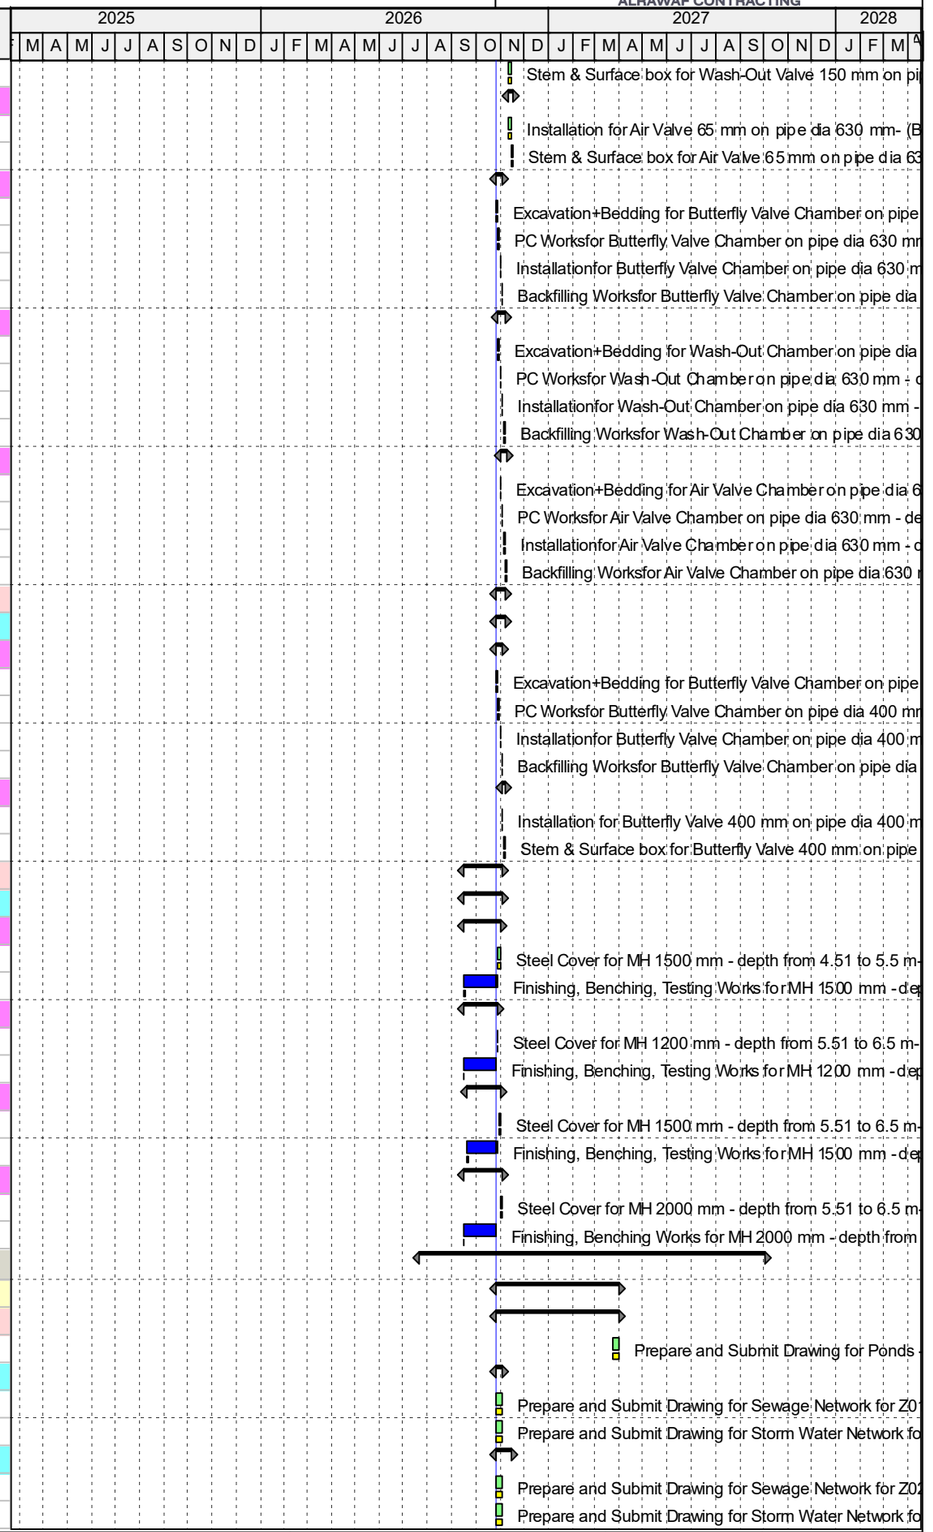

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Prepare and Submit Drawing for TSE Network for Z02-AS-TSE-S	7d	08-Nov-26	15-Nov-26	383d	0	0	0
	Prepare and Submit Drawing for Telecommunication Network fo	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z03	17d	27-Oct-26	15-Nov-26	383d	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z03-AS-S'	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z03-A	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	Prepare and Submit Drawing for TSE Network for Z03-AS-TSE-S	7d	08-Nov-26	15-Nov-26	383d	0	0	0
	Prepare and Submit Drawing for Telecommunication Network fo	7d	27-Oct-26	03-Nov-26	393d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z04	9d	27-Oct-26	05-Nov-26	396d	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z04-AS-S'	5d	27-Oct-26	01-Nov-26	400d	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z04-A	5d	27-Oct-26	01-Nov-26	400d	0	0	0
	Prepare and Submit Drawing for TSE Network for Z04-AS-TSE-S	5d	28-Oct-26	03-Nov-26	398d	0	0	0
	Prepare and Submit Drawing for Potable Water Network for Z04	5d	28-Oct-26	03-Nov-26	398d	0	0	0
	Prepare and Submit Drawing for Electrical Network for Z04-AS-E	5d	01-Nov-26	05-Nov-26	396d	0	0	0
	Prepare and Submit Drawing for Street Lighting Network for Z04	5d	01-Nov-26	05-Nov-26	396d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-EX	5d	27-Oct-26	01-Nov-26	400d	0	0	0
	Prepare and Submit Drawing for Electrical Network for EX-AS-EI	5d	27-Oct-26	01-Nov-26	400d	0	0	0
	Prepare and Submit Drawing for Landscape and Irrigation for E.	5d	27-Oct-26	01-Nov-26	400d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP	19d	02-Nov-26	26-Nov-26	318d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z01	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for Sewage Network for Z01-AS-SW-APP	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for Storm Water Network for Z01-AS-ST-AI	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z02	17d	04-Nov-26	26-Nov-26	318d	0	0	0
	Review and Approval for Sewage Network for Z02-AS-SW-APP	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for Storm Water Network for Z02-AS-ST-AI	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for TSE Network for Z02-AS-TSE-APP	9d	16-Nov-26	26-Nov-26	318d	0	0	0
	Review and Approval for Telecommunication Network for Z02-AS	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z03	17d	04-Nov-26	26-Nov-26	318d	0	0	0
	Review and Approval for Sewage Network for Z03-AS-SW-APP	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for Storm Water Network for Z03-AS-ST-AI	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	Review and Approval for TSE Network for Z03-AS-TSE-APP	9d	16-Nov-26	26-Nov-26	318d	0	0	0
	Review and Approval for Telecommunication Network for Z03-AS	9d	04-Nov-26	16-Nov-26	326d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z04	9d	02-Nov-26	12-Nov-26	328d	0	0	0
	Review and Approval for Sewage Network for Z04-AS-SW-APP	5d	02-Nov-26	08-Nov-26	332d	0	0	0
	Review and Approval for Storm Water Network for Z04-AS-ST-AI	5d	02-Nov-26	08-Nov-26	332d	0	0	0
	Review and Approval for TSE Network for Z04-AS-TSE-APP	5d	03-Nov-26	10-Nov-26	330d	0	0	0
	Review and Approval for Potable Water Network for Z04-AS-WT	5d	03-Nov-26	10-Nov-26	330d	0	0	0
	Review and Approval for Electrical Network for Z04-AS-EL-APP	5d	08-Nov-26	12-Nov-26	328d	0	0	0
	Review and Approval for Street Lighting Network for Z04-AS-SL-	5d	08-Nov-26	12-Nov-26	328d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-EX	5d	02-Nov-26	08-Nov-26	332d	0	0	0
	Review and Approval for Electrical Network for EX-AS-EL-APP	5d	02-Nov-26	08-Nov-26	332d	0	0	0
	Review and Approval for Landscape and Irrigation for EX-AS-LS	5d	02-Nov-26	08-Nov-26	332d	0	0	0
	JDH3-02-009-Final Testing and Commissioning - FT	344d	21-Jul-26 A	02-Oct-27	117d	0	3,004,331	5,888,883
	JDH3-02-009-Final Testing and Commissioning - FT-Z01	12d	21-Jul-26 A	07-Sep-27	110d	0	661,973	1,103,288
JDI	Final Testing and Commissioning for Potable Water - FT-Z01-W	5d	21-Jul-26 A	07-Sep-27	110d	0	430,073	716,788
JDI	Final Testing and Commissioning for TSE Network - FT-Z01-TSE	7d	21-Jul-26 A	07-Sep-27	110d	0	231,900	386,501
	JDH3-02-009-Final Testing and Commissioning - FT-Z02	305d	21-Jul-26 A	07-Sep-27	110d	0	661,973	1,103,288
JDI	Final Testing and Commissioning for Potable Water - FT-Z02-W	10d	21-Jul-26 A	07-Sep-27	110d	0	430,073	716,788
JDI	Final Testing and Commissioning for TSE (IRRIGATION) Networ	10d	21-Jul-26 A	07-Nov-26	363d	0	231,900	386,501
	JDH3-02-009-Final Testing and Commissioning - FT-Z03	305d	21-Jul-26 A	07-Sep-27	110d	0	551,644	1,103,288
JDI	Final Testing and Commissioning for Potable Water - FT-Z03-W	10d	21-Jul-26 A	07-Sep-27	110d	0	358,394	716,788
JDI	Final Testing and Commissioning for TSE (IRRIGATION) Networ	20d	21-Jul-26 A	07-Nov-26	363d	0	193,250	386,501
	JDH3-02-009-Final Testing and Commissioning - FT-Z04	87d	21-Jul-26 A	31-Oct-26	396d	0	661,973	1,722,782
JDI	Final Testing and Commissioning for Electrical Network - FT-Z04-	4d	27-Oct-26	31-Oct-26	396d	0	0	360,628




Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Final Testing and Commissioning for Street Lighting Network - F	4d	27-Oct-26	31-Oct-26	396d	0	0	258,865
JDH	Final Testing and Commissioning for Potable Water - FT-Z04-WT	4d	21-Jul-26 A	28-Oct-26	398d	0	430,073	716,788
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	4d	21-Jul-26 A	28-Oct-26	398d	0	231,900	386,501
JDH3-02-009-Final Testing and Commissioning - FT-EX		11d	21-Jul-26 A	02-Oct-27	117d	0	466,768	856,236
JDH	Final Testing and Commissioning for Sewage Network - FT-EX-S	5d	11-Aug-26 A	02-Oct-27	117d	0	234,867	469,735
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	4d	21-Jul-26 A	02-Oct-27	117d	0	231,900	386,501
JDH3-02-009-New Scope - R.BOQ. NO03		128d	14-Jul-26 A	25-Dec-26	372d	0	3,158,163	15,744,193
JDH3-02-009-Infrastructure Networks Zone 5		128d	14-Jul-26 A	25-Dec-26	372d	0	1,984,925	7,265,440
JDH3-02-009-Milestone		0d	27-Oct-26	27-Oct-26	354d	0	0	0
Network Milestones		0d	27-Oct-26	27-Oct-26	354d	0	0	0
JDH	Start of Potable Water Network - WT - .SMI-WT	0d	27-Oct-26		215d	0	0	0
JDH	Start of TSE Network - TSE - .SMI-TSE	0d	27-Oct-26		244d	0	0	0
JDH	Start of Road Works - RD - .SMI-RD	0d	27-Oct-26		354d	0	0	0
JDH3-02-009-Engineering - EN		15d	27-Oct-26	12-Nov-26	286d	0	0	0
JDH3-02-009-Shop Drawings - SD		15d	27-Oct-26	12-Nov-26	286d	0	0	0
JDH3-02-009-Shop Drawing Submittals - SUB		5d	27-Oct-26	01-Nov-26	286d	0	0	0
JDH3-02-009-Shop Drawing Submittals - SUB-Z05		5d	27-Oct-26	01-Nov-26	286d	0	0	0
Prepare and Submit Drawing for Street Lighting Network for Z05		5d	27-Oct-26	01-Nov-26	88d	0	0	0
Prepare and Submit Drawing for Electrical Network for Z05-SD-E		5d	27-Oct-26	01-Nov-26	144d	0	0	0
Prepare and Submit Drawing for Telecommunication Network fo		5d	27-Oct-26	01-Nov-26	286d	0	0	0
JDH3-02-009-Shop Drawing Approvals - APP		10d	02-Nov-26	12-Nov-26	286d	0	0	0
JDH3-02-009-Shop Drawing Approvals - APP-Z05		10d	02-Nov-26	12-Nov-26	286d	0	0	0
Review and Approval for Street Lighting Network for Z05-SD-SL-		10d	02-Nov-26	12-Nov-26	88d	0	0	0
Review and Approval for Electrical Network for Z05-SD-EL-APP		10d	02-Nov-26	12-Nov-26	144d	0	0	0
Review and Approval for Telecommunication Network for Z05-SI		10d	02-Nov-26	12-Nov-26	286d	0	0	0
JDH3-02-009-Procurement -PR		128d	14-Jul-26 A	25-Dec-26	372d	0	1,491,219	1,669,629
Long Lead Items		51d	27-Oct-26	25-Dec-26	191d	0	0	0
JDH3-02-009-Material Purchase Order - PO		10d	14-Nov-26	24-Nov-26	190d	0	0	0
JDH3-Material Purchase Order - PO-Electrical Network - EL		10d	14-Nov-26	24-Nov-26	144d	0	0	0
Material Purchase Order for MV Cables - PR-EL-PO		10d	14-Nov-26	24-Nov-26	144d	0	0	0
JDH3-Material Purchase Order - PO-Street Lighting Network -SI		10d	14-Nov-26	24-Nov-26	190d	0	0	0
Material Purchase Order for Cables&Conductors - PR-SL-PO		10d	14-Nov-26	24-Nov-26	190d	0	0	0
JDH3-02-009-Material Manufacturing- FAB		60d	27-Oct-26	25-Dec-26	232d	0	0	0
JDH3-Material Purchase Order - PO-Potable Water Network - W		60d	27-Oct-26	25-Dec-26	195d	0	0	0
Material Fabrication for Valves - PR-WT-FAB		60d	27-Oct-26	25-Dec-26	195d	0	0	0
JDH3-Material Purchase Order - PO-TSE Network - TSE		60d	27-Oct-26	25-Dec-26	232d	0	0	0
Material Fabrication for Valves - PR-TSE-FAB		60d	27-Oct-26	25-Dec-26	232d	0	0	0
Short Lead items		97d	14-Jul-26 A	18-Nov-26	403d	0	1,491,219	1,669,629
JDH3-02-009-Material Purchase Order - PO		5d	14-Nov-26	18-Nov-26	286d	0	0	0
JDH3-Material Purchase Order - PO-Electrical Network - EL		5d	14-Nov-26	18-Nov-26	144d	0	0	0
Material Purchase Order for Ducts - PR-EL-PO		5d	14-Nov-26	18-Nov-26	144d	0	0	0
JDH3-Material Purchase Order - PO-Street Lighting Network -SI		5d	14-Nov-26	18-Nov-26	88d	0	0	0
Material Purchase Order for Lighting Columns - PR-SL-PO		5d	14-Nov-26	18-Nov-26	88d	0	0	0
JDH3-Material Purchase Order - PO-Telecommunications Netw		5d	14-Nov-26	18-Nov-26	286d	0	0	0
Material Purchase Order for Duct Manhole - PR-TC-PO		5d	14-Nov-26	18-Nov-26	286d	0	0	0
JDH3-02-009-Material Delivery and staging on Site - DOS		83d	14-Jul-26 A	18-Nov-26	487d	0	1,491,219	1,669,629
JDH3-02-009-Material Delivery and staging on Site - DOS-Z03		83d	14-Jul-26 A	18-Nov-26	487d	0	1,491,219	1,669,629
JDH3-02-009-Material Delivery and staging on Site - DOS-Se		73d	28-Jul-26 A	01-Nov-26	505d	0	655,124	715,983
delivery and staging for GRP pipes - PR-SS-Z05-DOS		45d	28-Jul-26 A	01-Nov-26	505d	0	315,032	357,991
delivery and staging for Metal Works (Stairs - Covers) - PR-SS-Z		60d	06-Aug-26 A	29-Oct-26	507d	0	340,092	357,991
JDH3-02-009-Material Delivery and staging on Site - DOS-Stc		60d	14-Jul-26 A	29-Oct-26	507d	0	825,478	882,864
delivery and staging for GRP pipes - PR-ST-Z05-DOS		30d	14-Jul-26 A	29-Oct-26	508d	0	406,117	441,432

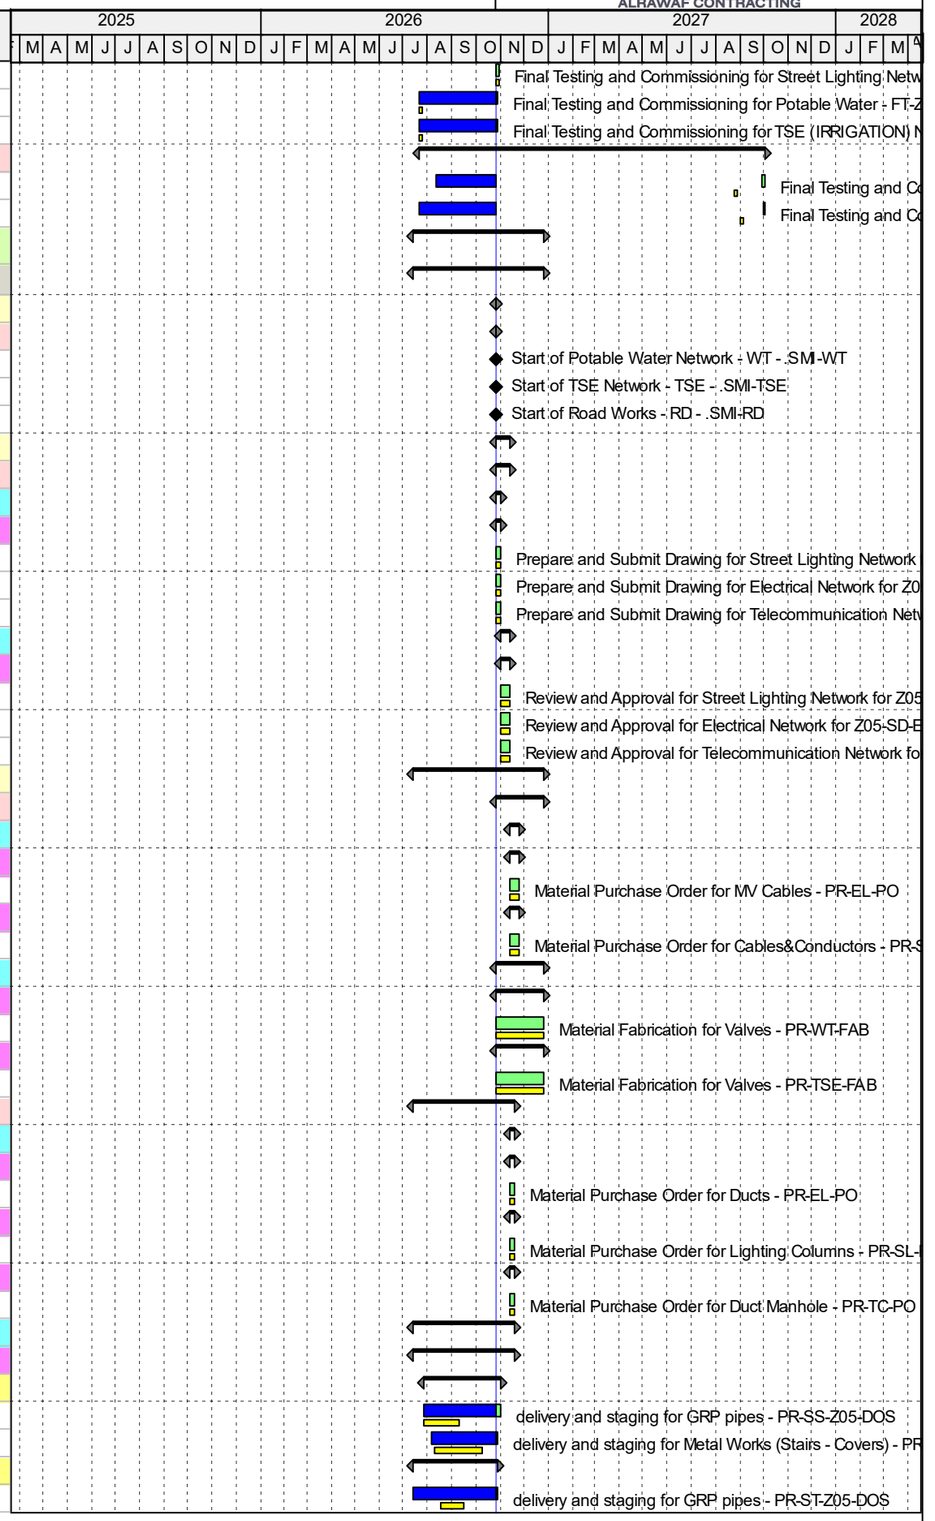


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	delivery and staging for Metal Works (Stairs - Covers) - PR-ST-Z(	60d	06-Aug-26 A	29-Oct-26	204d	0	419,360	441,432
	JDH3-02-009-Material Delivery and staging on Site - DOS-Tel	10d	17-Sep-26 A	18-Nov-26	345d	0	10,617	70,782
	delivery and staging for Duct Manhole - PR-TC-Z05-DOS	10d	17-Sep-26 A	18-Nov-26	345d	0	10,617	70,782
JDH3-02-009-Execution		81d	18-Aug-26 A	21-Nov-26	401d	0	493,706	5,595,812
Earthworks - EW		49d	22-Sep-26 A	18-Nov-26	332d	0	176,326	1,782,430
JDH3-02-009-R01-Road Works - RW		49d	22-Sep-26 A	18-Nov-26	332d	0	176,326	1,782,430
Z05		49d	22-Sep-26 A	18-Nov-26	332d	0	176,326	1,782,430
	JDH3-02-009-Road Works - RWZ3-R6605	37d	22-Sep-26 A	04-Nov-26	344d	0	105,673	314,206
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	4d	01-Nov-26	04-Nov-26	344d	0	0	55,741
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R6605-RW	4d	22-Sep-26 A	31-Oct-26	344d	0	72,892	182,230
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	28-Sep-26 A	31-Oct-26	344d	0	32,781	76,235
	JDH3-02-009-Road Works - RWZ3-R4019	7d	27-Oct-26	03-Nov-26	143d	0	0	207,529
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	27-Oct-26	31-Oct-26	143d	0	0	96,901
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	3d	01-Nov-26	03-Nov-26	143d	0	0	110,628
	JDH3-02-009-Road Works - RWZ3-R4017	12d	27-Oct-26	09-Nov-26	333d	0	0	205,202
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	27-Oct-26	31-Oct-26	195d	0	0	84,343
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4d	05-Nov-26	09-Nov-26	142d	0	0	90,569
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R4017-RW	4d	27-Oct-26	31-Oct-26	341d	0	0	30,290
	JDH3-02-009-Road Works - RWZ3-R40151	8d	15-Oct-26 A	14-Nov-26	142d	0	18,477	290,368
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R401511-RW	4d	27-Oct-26	31-Oct-26	150d	0	0	70,224
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	01-Nov-26	04-Nov-26	150d	0	0	111,456
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	3d	15-Oct-26 A	14-Nov-26	142d	0	18,477	108,688
	JDH3-02-009-Road Works - RWZ3-R40152	20d	27-Oct-26	18-Nov-26	153d	0	0	290,368
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R401512-RW	4d	27-Oct-26	31-Oct-26	142d	0	0	70,224
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	01-Nov-26	04-Nov-26	161d	0	0	111,456
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4d	15-Nov-26	18-Nov-26	153d	0	0	108,688
	JDH3-02-009-Road Works - RWZ3-R4016	12d	01-Nov-26	14-Nov-26	142d	0	0	183,389
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R4016-RW	4d	01-Nov-26	04-Nov-26	142d	0	0	44,730
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4d	10-Nov-26	14-Nov-26	142d	0	0	89,863
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	05-Nov-26	09-Nov-26	142d	0	0	48,796
	JDH3-02-009-Road Works - RWZ3-R4018	8d	22-Sep-26 A	31-Oct-26	143d	0	52,176	291,367
	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	4d	22-Sep-26 A	31-Oct-26	143d	0	25,553	170,356
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4d	27-Sep-26 A	31-Oct-26	143d	0	26,622	121,010
Z05		81d	18-Aug-26 A	21-Nov-26	401d	0	317,380	3,813,382
R40151		30d	22-Sep-26 A	18-Nov-26	403d	0	199,399	1,201,242
JDH3-02-009-R40151-Sewage Network - SW		30d	22-Sep-26 A	18-Nov-26	369d	0	199,399	763,072
	JDH3-02-009-R40151-(SW)-GRP Pipes-600 mm diameter dep	30d	22-Sep-26 A	18-Nov-26	365d	0	199,399	717,835
	Primary Test for (SW)-GRP Pipes-600 mm diameter depth from	4d	15-Nov-26	18-Nov-26	365d	0	0	79,759
	Bedding Works for (SW)-GRP Pipes-600 mm diameter depth fro	4d	23-Sep-26 A	14-Nov-26	365d	0	5,982	39,880
	Installing for (SW)-GRP Pipes-600 mm diameter depth from 4.5	4d	24-Sep-26 A	14-Nov-26	365d	0	65,802	438,677
	Excavation Works for (SW)-GRP Pipes-600 mm diameter depth	4d	22-Sep-26 A	14-Nov-26	353d	0	127,615	159,519
	JDH3-02-009-R40151-(SW)-GRP Pipes-150 mm diameter dep	4d	15-Nov-26	18-Nov-26	353d	0	0	14,775
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4d	15-Nov-26	18-Nov-26	353d	0	0	14,775
	JDH3-02-009-R40151-(SW)-MH Works depth from 1.51 to 2.5	16d	27-Oct-26	14-Nov-26	373d	0	0	30,462
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4d	27-Oct-26	31-Oct-26	373d	0	0	10,154
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	373d	0	0	14,215
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4d	05-Nov-26	09-Nov-26	373d	0	0	4,062
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	4d	10-Nov-26	14-Nov-26	373d	0	0	2,031
	JDH3-02-009-R40151-Storm Network - ST	20d	27-Oct-26	18-Nov-26	403d	0	0	126,220
	JDH3-02-009-R40151-(ST)-GRP Pipes-400 mm diameter dept	20d	27-Oct-26	18-Nov-26	399d	0	0	31,802
	Excavation Works for GRP Pipe Line 400 mm - depth from 1.51	4d	27-Oct-26	31-Oct-26	399d	0	0	6,360
	Bedding Works for GRP Pipe Line 400 mm - depth from 1.51 to	4d	01-Nov-26	04-Nov-26	399d	0	0	1,590
	Installing for GRP Pipe Line 400 mm - depth from 1.51 to 2.00	4d	05-Nov-26	09-Nov-26	399d	0	0	17,491

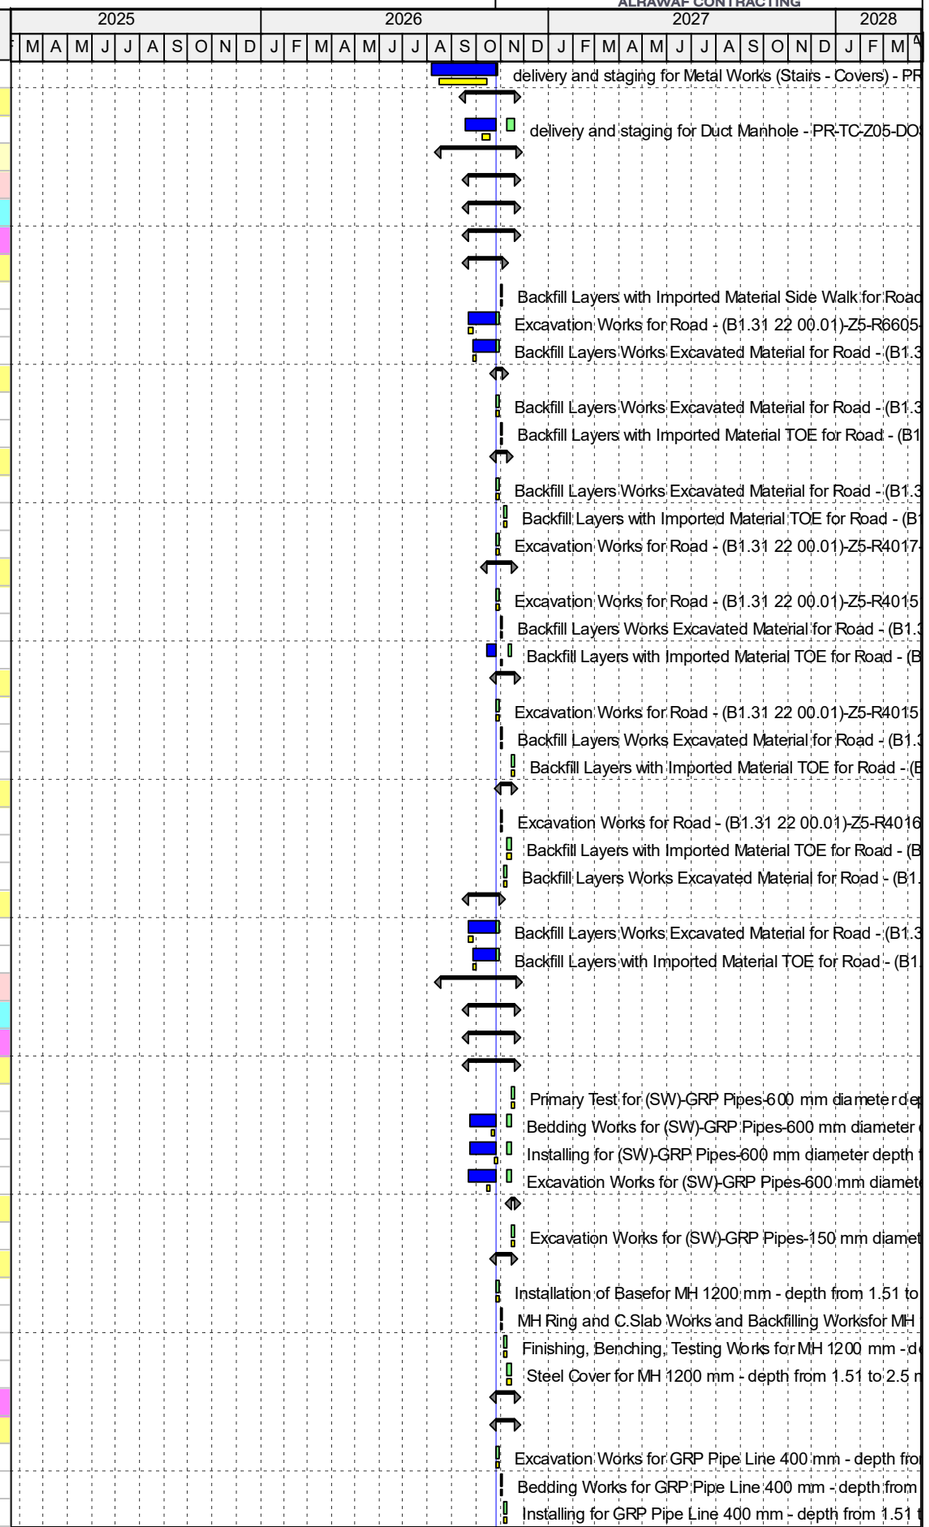


Actual Level of Effort · Remaining Work
Primary Baseline · Critical Remaining Work
Actual Work · Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for GRP Pipe Line 400 mm - depth from 1.51 to 2.(	4d	10-Nov-26	14-Nov-26	399d	0	0	3,180
	Backfilling and warning tape Works for GRP Pipe Line 400 mm	4d	15-Nov-26	18-Nov-26	399d	0	0	3,180
	JDH3-02-009-R40151-(ST)-GRP Pipes-700 mm diameter dept	16d	01-Nov-26	18-Nov-26	399d	0	0	75,636
	Excavation Works for (ST)-GRP Pipes-700 mm diameter depth	4d	01-Nov-26	04-Nov-26	399d	0	0	16,808
	Bedding Works for (ST)-GRP Pipes-700 mm diameter depth fro	4d	05-Nov-26	09-Nov-26	399d	0	0	4,202
	Installing for (ST)-GRP Pipes-700 mm diameter depth from 2.01	4d	10-Nov-26	14-Nov-26	399d	0	0	46,222
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4d	15-Nov-26	18-Nov-26	399d	0	0	8,404
	JDH3-02-009-R40151-(ST)-GRP Pipes-900 mm diameter dept	4d	27-Oct-26	31-Oct-26	419d	0	0	18,782
	Primary Test for (ST)-GRP Pipes-900 mm diameter depth from 2	4d	27-Oct-26	31-Oct-26	419d	0	0	18,782
	JDH3-02-009-R40151-Potable Water Network - WT	20d	27-Oct-26	18-Nov-26	329d	0	0	157,340
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	20d	27-Oct-26	18-Nov-26	329d	0	0	976
	Excavation Works for (WT)-HDPE Pipes-225 mm diameter depth	4d	27-Oct-26	31-Oct-26	329d	0	0	195
	Bedding Works for (WT)-HDPE Pipes-225 mm diameter depth fi	4d	01-Nov-26	04-Nov-26	329d	0	0	49
	Installing for (WT)-HDPE Pipes-225 mm diameter depth from 3.5	4d	05-Nov-26	09-Nov-26	329d	0	0	537
	Primary Test for (WT)-HDPE Pipes-225 mm diameter depth from	4d	10-Nov-26	14-Nov-26	329d	0	0	98
	Backfilling and warning tape Works for (WT)-HDPE Pipes-225 m	4d	15-Nov-26	18-Nov-26	329d	0	0	98
	JDH3-02-009-R40151-(WT)-Fire Hydrant	4d	01-Nov-26	04-Nov-26	329d	0	0	9,771
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	4d	01-Nov-26	04-Nov-26	329d	0	0	9,771
	JDH3-02-009-R40151-(WT)-Air Valve Chamber on 225 mm dia	11d	01-Nov-26	12-Nov-26	220d	0	0	5,711
	Excavation+Bedding for Air Valve Chamber on pipe dia 225 mm	3d	01-Nov-26	03-Nov-26	220d	0	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 225 mm - depth fro	4d	04-Nov-26	08-Nov-26	220d	0	0	714
	Installationfor Air Valve Chamber on pipe dia 225 mm - depth fr	4d	09-Nov-26	12-Nov-26	220d	0	0	3,926
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	4d	15-Nov-26	18-Nov-26	313d	0	0	5,031
	Excavation Works for HDPE Pipe Line 225 mm - depth from 2.5	4d	15-Nov-26	18-Nov-26	313d	0	0	5,031
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	20d	27-Oct-26	18-Nov-26	215d	0	0	135,850
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	4d	27-Oct-26	31-Oct-26	215d	0	0	27,170
	Bedding Works for HDPE Pipe Line 225 mm - depth from 1.51 t	4d	01-Nov-26	04-Nov-26	215d	0	0	6,793
	Installing for HDPE Pipe Line 225 mm - depth from 1.51 to 2.5	4d	05-Nov-26	09-Nov-26	215d	0	0	74,718
	Primary Test for HDPE Pipe Line 225 mm - depth from 1.51 to 2	4d	10-Nov-26	14-Nov-26	215d	0	0	13,585
	Backfilling and warning tape Works for HDPE Pipe Line 225 mm	4d	15-Nov-26	18-Nov-26	215d	0	0	13,585
	JDH3-02-009-R40151-Road Works - RD	20d	27-Oct-26	18-Nov-26	326d	0	0	154,611
	JDH3-02-009-R40151-(RD)-Subgrade	4d	15-Nov-26	18-Nov-26	142d	0	0	152,984
	Supply, lay and compaction subgrade compacted thickness 300	4d	15-Nov-26	18-Nov-26	142d	0	0	152,984
	JDH3-02-009-R40151-(RD)-Precast Concrete Curb	4d	27-Oct-26	31-Oct-26	342d	0	0	1,627
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	27-Oct-26	31-Oct-26	342d	0	0	1,627
	R40152	20d	27-Oct-26	18-Nov-26	369d	0	0	435,562
	JDH3-02-009-R40152-Sewage Network - SW	20d	27-Oct-26	18-Nov-26	369d	0	0	276,927
	JDH3-02-009-R40152-(SW)-GRP Pipes-600 mm diameter dep	8d	27-Oct-26	04-Nov-26	377d	0	0	4,967
	Primary Test for (SW)-GRP Pipes-600 mm diameter depth from	4d	27-Oct-26	31-Oct-26	377d	0	0	2,484
	Backfilling and warning tape Works for (SW)-GRP Pipes-600 mm	4d	01-Nov-26	04-Nov-26	377d	0	0	2,484
	JDH3-02-009-R40152-(SW)-GRP Pipes-150 mm diameter dep	20d	27-Oct-26	18-Nov-26	369d	0	0	33,015
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4d	27-Oct-26	31-Oct-26	369d	0	0	6,603
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4d	01-Nov-26	04-Nov-26	369d	0	0	1,651
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0 to	4d	05-Nov-26	09-Nov-26	369d	0	0	18,158
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4d	10-Nov-26	14-Nov-26	369d	0	0	3,301
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mm	4d	15-Nov-26	18-Nov-26	369d	0	0	3,301
	JDH3-02-009-R40152-(SW)-MH Works depth from 1.51 to 2.5	13d	27-Oct-26	10-Nov-26	376d	0	0	109,662
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	3d	27-Oct-26	29-Oct-26	376d	0	0	36,554
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	31-Oct-26	03-Nov-26	376d	0	0	51,175
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	3d	04-Nov-26	07-Nov-26	376d	0	0	14,622
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.33	3d	08-Nov-26	10-Nov-26	376d	0	0	7,311
	JDH3-02-009-R40152-(SW)-MH Works depth from 4.51 to 5.5	16d	27-Oct-26	14-Nov-26	369d	0	0	36,788
	Installation of Basefor MH 1200 mm - depth from 4.51 to 5.5 m	4d	27-Oct-26	31-Oct-26	369d	0	0	12,263

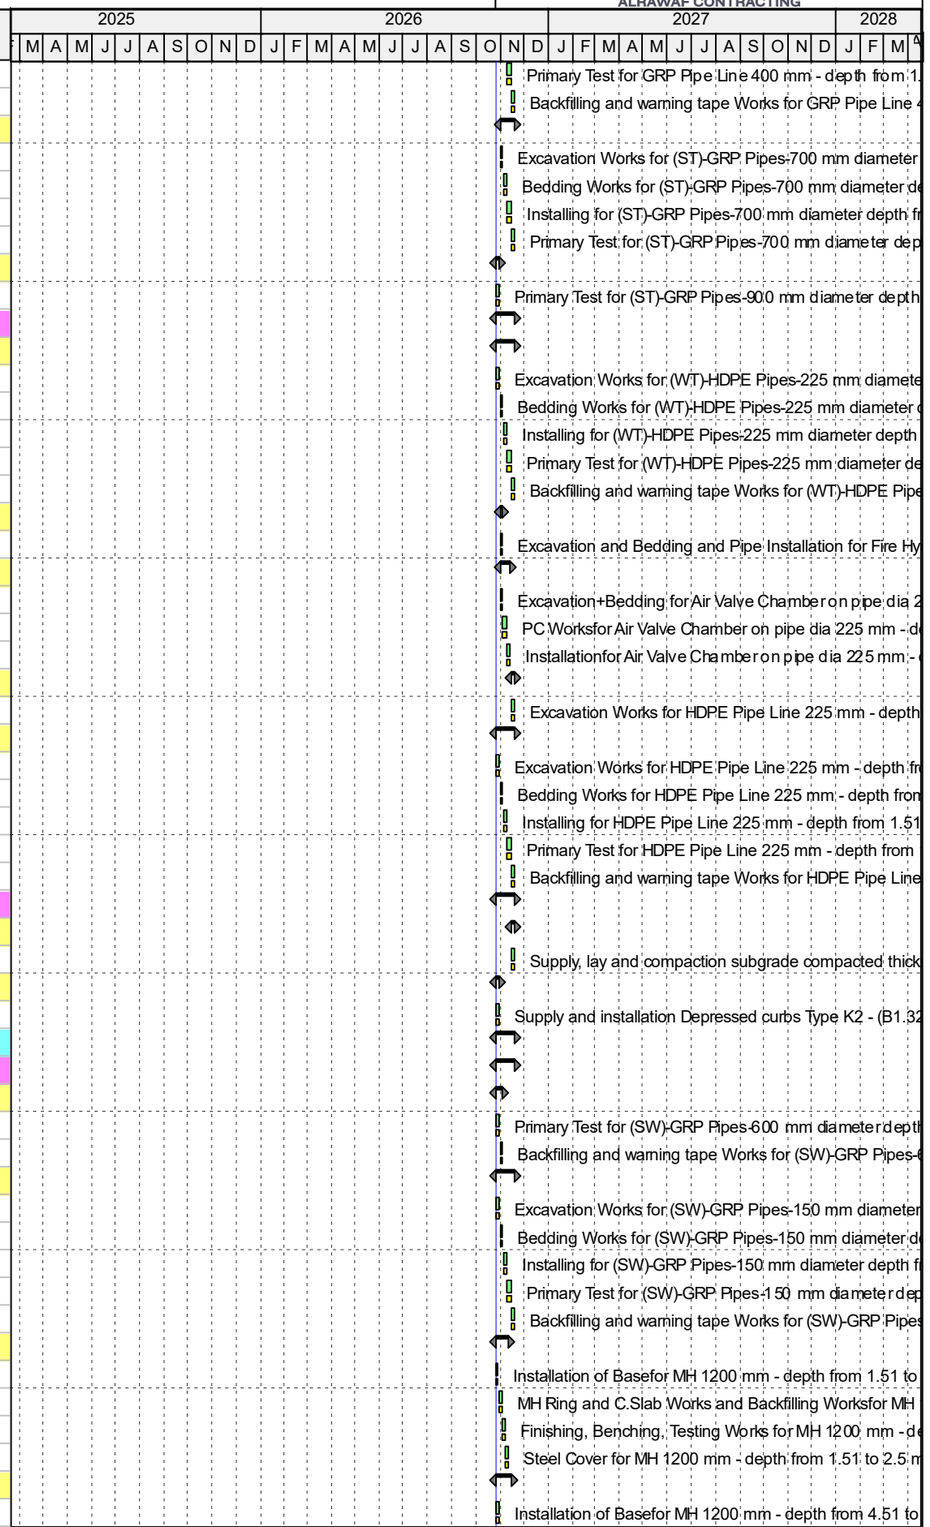


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	369d	0	0	17,168
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4d	05-Nov-26	09-Nov-26	369d	0	0	4,905
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	4d	10-Nov-26	14-Nov-26	369d	0	0	2,453
	JDH3-02-009-R40152-(SW)-MH Works depth from 5.51 to 6.5	20d	27-Oct-26	18-Nov-26	369d	0	0	92,495
	Installation of Basefor MH 1200 mm - depth from 5.51 to 6.5 m	4d	27-Oct-26	31-Oct-26	373d	0	0	30,832
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	373d	0	0	43,164
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4d	10-Nov-26	14-Nov-26	369d	0	0	12,333
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	4d	15-Nov-26	18-Nov-26	369d	0	0	6,166
	JDH3-02-009-R40152-Storm Network - ST	20d	27-Oct-26	18-Nov-26	365d	0	0	158,635
	JDH3-02-009-R40152-(ST)-GRP Pipes-1100 mm diameter dep	20d	27-Oct-26	18-Nov-26	365d	0	0	75,256
	Excavation Works for GRP Pipe Line 1100 mm - depth from 2.0	4d	27-Oct-26	31-Oct-26	365d	0	0	15,051
	Bedding Works for GRP Pipe Line 1100 mm - depth from 2.01 t	4d	01-Nov-26	04-Nov-26	365d	0	0	3,763
	Installing for GRP Pipe Line 1100 mm - depth from 2.01 to 2.50	4d	05-Nov-26	09-Nov-26	365d	0	0	41,391
	Primary Test for GRP Pipe Line 1100 mm - depth from 2.01 to 2	4d	10-Nov-26	14-Nov-26	365d	0	0	7,526
	Backfilling and warning tape Works for GRP Pipe Line 1100 mm	4d	15-Nov-26	18-Nov-26	365d	0	0	7,526
	JDH3-02-009-R40152-(ST)-GRP Pipes-1100 mm diameter dep	16d	01-Nov-26	18-Nov-26	365d	0	0	83,379
	Excavation Works for GRP Pipe Line 1100 mm - depth from 2.5	4d	01-Nov-26	04-Nov-26	365d	0	0	18,529
	Bedding Works for GRP Pipe Line 1100 mm - depth from 2.51 t	4d	05-Nov-26	09-Nov-26	365d	0	0	4,632
	Installing for GRP Pipe Line 1100 mm - depth from 2.51 to 3.00	4d	10-Nov-26	14-Nov-26	365d	0	0	50,954
	Primary Test for GRP Pipe Line 1100 mm - depth from 2.51 to 3	4d	15-Nov-26	18-Nov-26	365d	0	0	9,264
	R4016	61d	08-Sep-26 A	18-Nov-26	403d	0	16,683	419,680
	JDH3-02-009-R4016-Sewage Network - SW	49d	22-Sep-26 A	18-Nov-26	369d	0	12,595	185,524
	JDH3-02-009-R4016-(SW)-GRP Pipes-150 mm diameter deptl	20d	27-Oct-26	18-Nov-26	349d	0	0	45,076
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4d	27-Oct-26	31-Oct-26	349d	0	0	9,015
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4d	01-Nov-26	04-Nov-26	349d	0	0	2,254
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4d	05-Nov-26	09-Nov-26	349d	0	0	24,792
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4d	10-Nov-26	14-Nov-26	349d	0	0	4,508
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mm	4d	15-Nov-26	18-Nov-26	349d	0	0	4,508
	JDH3-02-009-R4016-(SW)-GRP Pipes-250 mm diameter deptl	4d	27-Oct-26	31-Oct-26	365d	0	0	4,110
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4d	27-Oct-26	31-Oct-26	365d	0	0	4,110
	JDH3-02-009-R4016-(SW)-GRP Pipes-250 mm diameter deptl	4d	27-Oct-26	31-Oct-26	369d	0	0	3,364
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4d	27-Oct-26	31-Oct-26	369d	0	0	3,364
	JDH3-02-009-R4016-(SW)-GRP Pipes-300 mm diameter deptl	4d	27-Oct-26	31-Oct-26	373d	0	0	5,635
	Primary Test for (SW)-GRP Pipes-300 mm diameter depth from	4d	27-Oct-26	31-Oct-26	373d	0	0	5,635
	JDH3-02-009-R4016-(SW)-MH Works depth from 1.51 to 2.5 I	37d	22-Sep-26 A	04-Nov-26	369d	0	7,108	68,234
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	369d	0	0	39,803
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4d	22-Sep-26 A	31-Oct-26	369d	0	7,108	28,431
	JDH3-02-009-R4016-(SW)-MH Works depth from 2.51 to 3.5 I	37d	22-Sep-26 A	04-Nov-26	373d	0	5,487	52,675
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	373d	0	0	30,727
	Installation of Basefor MH 1200 mm - depth from 2.51 to 3.5 m	4d	22-Sep-26 A	31-Oct-26	373d	0	5,487	21,948
	JDH3-02-009-R4016-(SW)-GRP Pipes-200 mm diameter deptl	8d	27-Oct-26	04-Nov-26	377d	0	0	3,386
	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	4d	27-Oct-26	31-Oct-26	377d	0	0	1,693
	Backfilling and warning tape Works for GRP Pipe Line 200 mm	4d	01-Nov-26	04-Nov-26	377d	0	0	1,693
	JDH3-02-009-R4016-(SW)-GRP Pipes-150 mm diameter deptl	12d	27-Oct-26	09-Nov-26	377d	0	0	3,044
	Primary Test for GRP Pipe Line 150 mm - depth from 2.51 to 3.	4d	27-Oct-26	31-Oct-26	381d	0	0	1,522
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4d	05-Nov-26	09-Nov-26	377d	0	0	1,522
	JDH3-02-009-R4016-Storm Network - ST	59d	08-Sep-26 A	16-Nov-26	405d	0	4,089	78,161
	JDH3-02-009-R4016-(ST)-GRP Pipes-700 mm diameter depth	12d	27-Oct-26	09-Nov-26	411d	0	0	24,807
	Installing for (ST)-GRP Pipes-700 mm diameter depth from 2.0	4d	27-Oct-26	31-Oct-26	411d	0	0	18,192
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4d	01-Nov-26	04-Nov-26	411d	0	0	3,308
	Backfilling and warning tape Works for (ST)-GRP Pipes-700 mm	4d	05-Nov-26	09-Nov-26	411d	0	0	3,308
	JDH3-02-009-R4016-(ST)-GRP Pipes-800 mm diameter depth	4d	27-Oct-26	31-Oct-26	419d	0	0	3,674
	Primary Test for GRP Pipe Line 800 mm - depth from 1.51 to 2.	4d	27-Oct-26	31-Oct-26	419d	0	0	3,674

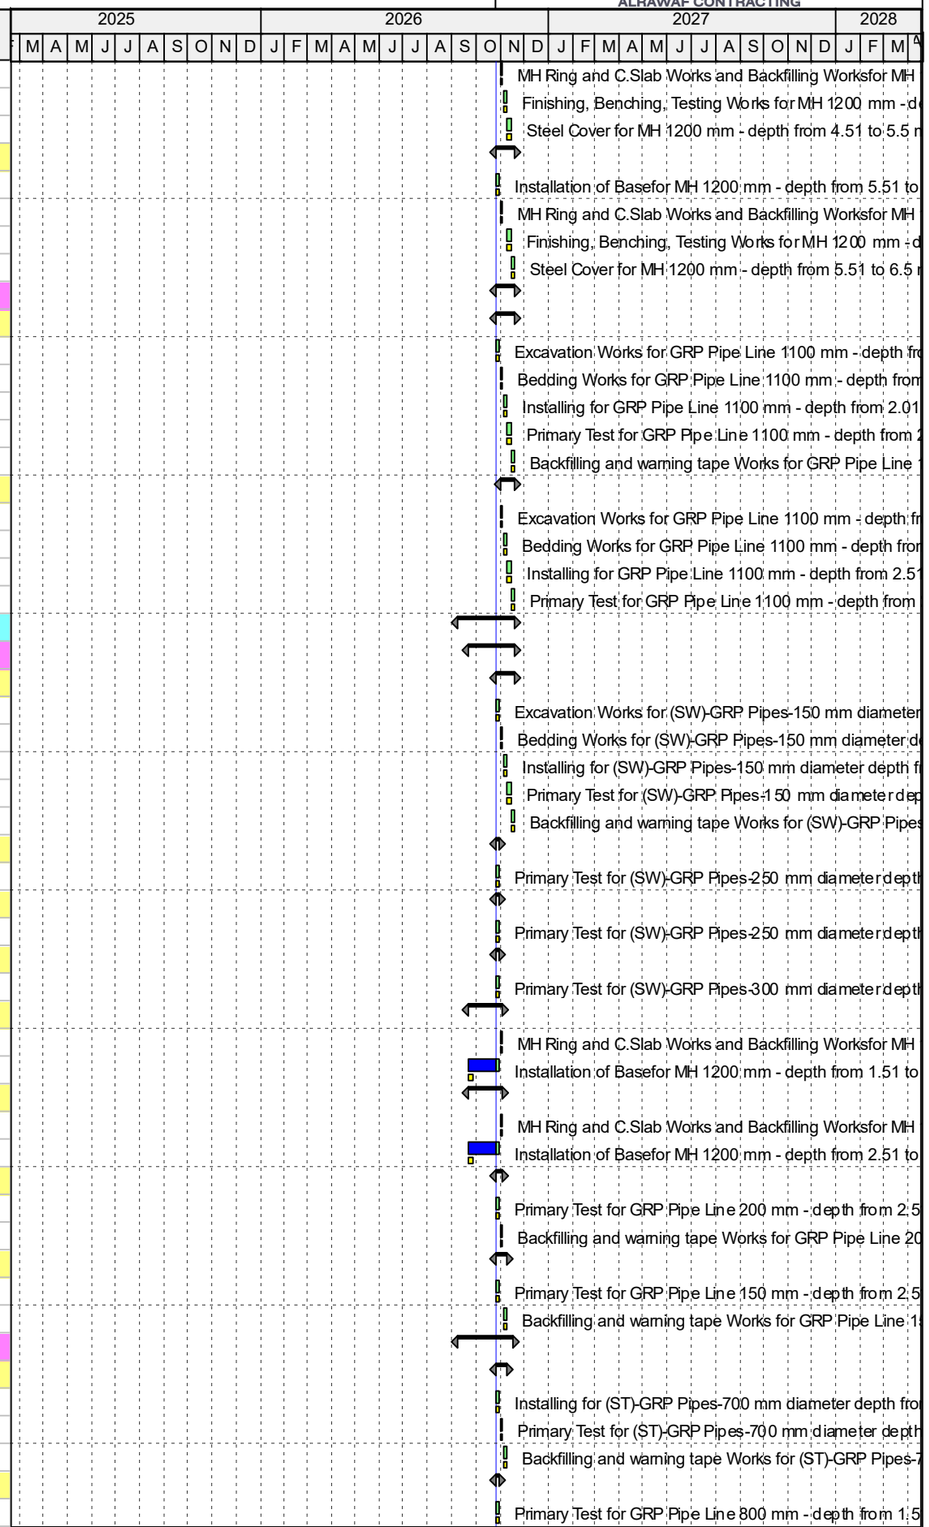


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R4016-(ST)-GRP Pipes-600 mm diameter depth	59d	08-Sep-26 A	16-Nov-26	405d	0	4,089	34,073
	Bedding Works for GRP Pipe Line 600 mm - depth from 1.51 tc	4d	28-Oct-26	02-Nov-26	405d	0	0	1,704
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4d	02-Nov-26	07-Nov-26	405d	0	0	18,740
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.	4d	07-Nov-26	11-Nov-26	405d	0	0	3,407
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	4d	11-Nov-26	16-Nov-26	405d	0	0	3,407
	Excavation Works for GRP Pipe Line 600 mm - depth from 1.51	4d	08-Sep-26 A	28-Oct-26	405d	0	4,089	6,815
	JDH3-02-009-R4016-(ST)-GRP Pipes-800 mm diameter depth	3d	27-Oct-26	29-Oct-26	420d	0	0	15,607
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.	3d	27-Oct-26	29-Oct-26	420d	0	0	15,607
	JDH3-02-009-R4016-Potable Water Network - WT	20d	27-Oct-26	18-Nov-26	231d	0	0	29,512
	JDH3-02-009-R4016-(WT)-HDPE Pipes-160 mm diameter dep	8d	10-Nov-26	18-Nov-26	187d	0	0	13,461
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	4d	10-Nov-26	14-Nov-26	187d	0	0	10,769
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4d	15-Nov-26	18-Nov-26	187d	0	0	2,692
	JDH3-02-009-R4016-(WT)-HDPE Pipes-160 mm diameter dep	4d	15-Nov-26	18-Nov-26	187d	0	0	574
	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	4d	15-Nov-26	18-Nov-26	187d	0	0	574
	JDH3-02-009-R4016-(WT)-Plot Connection	4d	27-Oct-26	31-Oct-26	247d	0	0	15,477
	HDPE road crossing with dia 110 mm (Including end cap, isolati	4d	27-Oct-26	31-Oct-26	247d	0	0	15,477
	JDH3-02-009-R4016-Road Works - RD	4d	15-Nov-26	18-Nov-26	142d	0	0	126,483
	JDH3-02-009-R4016-(RD)-Subgrade	4d	15-Nov-26	18-Nov-26	142d	0	0	126,483
	Supply, lay and compaction subgrade compacted thickness 300	4d	15-Nov-26	18-Nov-26	142d	0	0	126,483
R4017		57d	15-Sep-26 A	21-Nov-26	401d	0	59,893	454,182
	JDH3-02-009-R4017-Sewage Network - SW	57d	15-Sep-26 A	21-Nov-26	367d	0	59,893	193,617
	JDH3-02-009-R4017-(SW)-GRP Pipes-150 mm diameter deptl	45d	15-Sep-26 A	07-Nov-26	363d	0	38,773	51,017
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4d	28-Oct-26	02-Nov-26	363d	0	0	5,102
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4d	02-Nov-26	07-Nov-26	363d	0	0	5,102
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4d	15-Sep-26 A	28-Oct-26	363d	0	9,693	10,203
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4d	21-Sep-26 A	28-Oct-26	363d	0	26,656	28,059
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4d	20-Sep-26 A	28-Oct-26	363d	0	2,423	2,551
	JDH3-02-009-R4017-(SW)-GRP Pipes-250 mm diameter deptl	14d	27-Oct-26	11-Nov-26	363d	0	0	12,084
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4d	27-Oct-26	31-Oct-26	369d	0	0	6,042
	Backfilling and warning tape Works for (SW)-GRP Pipes-250 mr	4d	07-Nov-26	11-Nov-26	363d	0	0	6,042
	JDH3-02-009-R4017-(SW)-GRP Pipes-300 mm diameter deptl	18d	27-Oct-26	16-Nov-26	363d	0	0	3,177
	Primary Test for (SW)-GRP Pipes-300 mm diameter depth from	4d	27-Oct-26	31-Oct-26	373d	0	0	1,588
	Backfilling and warning tape Works for (SW)-GRP Pipes-300 mr	4d	11-Nov-26	16-Nov-26	363d	0	0	1,588
	JDH3-02-009-R4017-(SW)-GRP Pipes-150 mm diameter deptl	22d	27-Oct-26	21-Nov-26	363d	0	0	5,679
	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	4d	27-Oct-26	31-Oct-26	377d	0	0	2,840
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4d	16-Nov-26	21-Nov-26	363d	0	0	2,840
	JDH3-02-009-R4017-(SW)-MH Works depth from 2.51 to 3.5 I	4d	27-Oct-26	31-Oct-26	377d	0	0	20,485
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	27-Oct-26	31-Oct-26	377d	0	0	20,485
	JDH3-02-009-R4017-(SW)-MH Works depth from 1.51 to 2.5 I	51d	15-Sep-26 A	14-Nov-26	373d	0	21,120	97,477
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	31-Oct-26	04-Nov-26	373d	0	0	45,489
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4d	04-Nov-26	09-Nov-26	373d	0	0	12,997
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	4d	09-Nov-26	14-Nov-26	373d	0	0	6,498
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4d	15-Sep-26 A	31-Oct-26	373d	0	21,120	32,492
	JDH3-02-009-R4017-(SW)-GRP Pipes-200 mm diameter deptl	4d	27-Oct-26	31-Oct-26	381d	0	0	3,699
	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	4d	27-Oct-26	31-Oct-26	381d	0	0	3,699
JDH3-02-009-R4017-Storm Network - ST		8d	27-Oct-26	04-Nov-26	415d	0	0	53,107
	JDH3-02-009-R4017-(ST)-GRP Pipes-800 mm diameter depth	4d	27-Oct-26	31-Oct-26	419d	0	0	11,000
	Primary Test for GRP Pipe Line 800 mm - depth from 1.51 to 2.	4d	27-Oct-26	31-Oct-26	419d	0	0	11,000
	JDH3-02-009-R4017-(ST)-GRP Pipes-600 mm diameter depth	8d	27-Oct-26	04-Nov-26	381d	0	0	25,603
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4d	27-Oct-26	31-Oct-26	381d	0	0	18,965
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.	2d	01-Nov-26	02-Nov-26	381d	0	0	3,319
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	2d	03-Nov-26	04-Nov-26	381d	0	0	3,319
	JDH3-02-009-R4017-(ST)-GRP Pipes-700 mm diameter depth	8d	27-Oct-26	04-Nov-26	142d	0	0	12,494

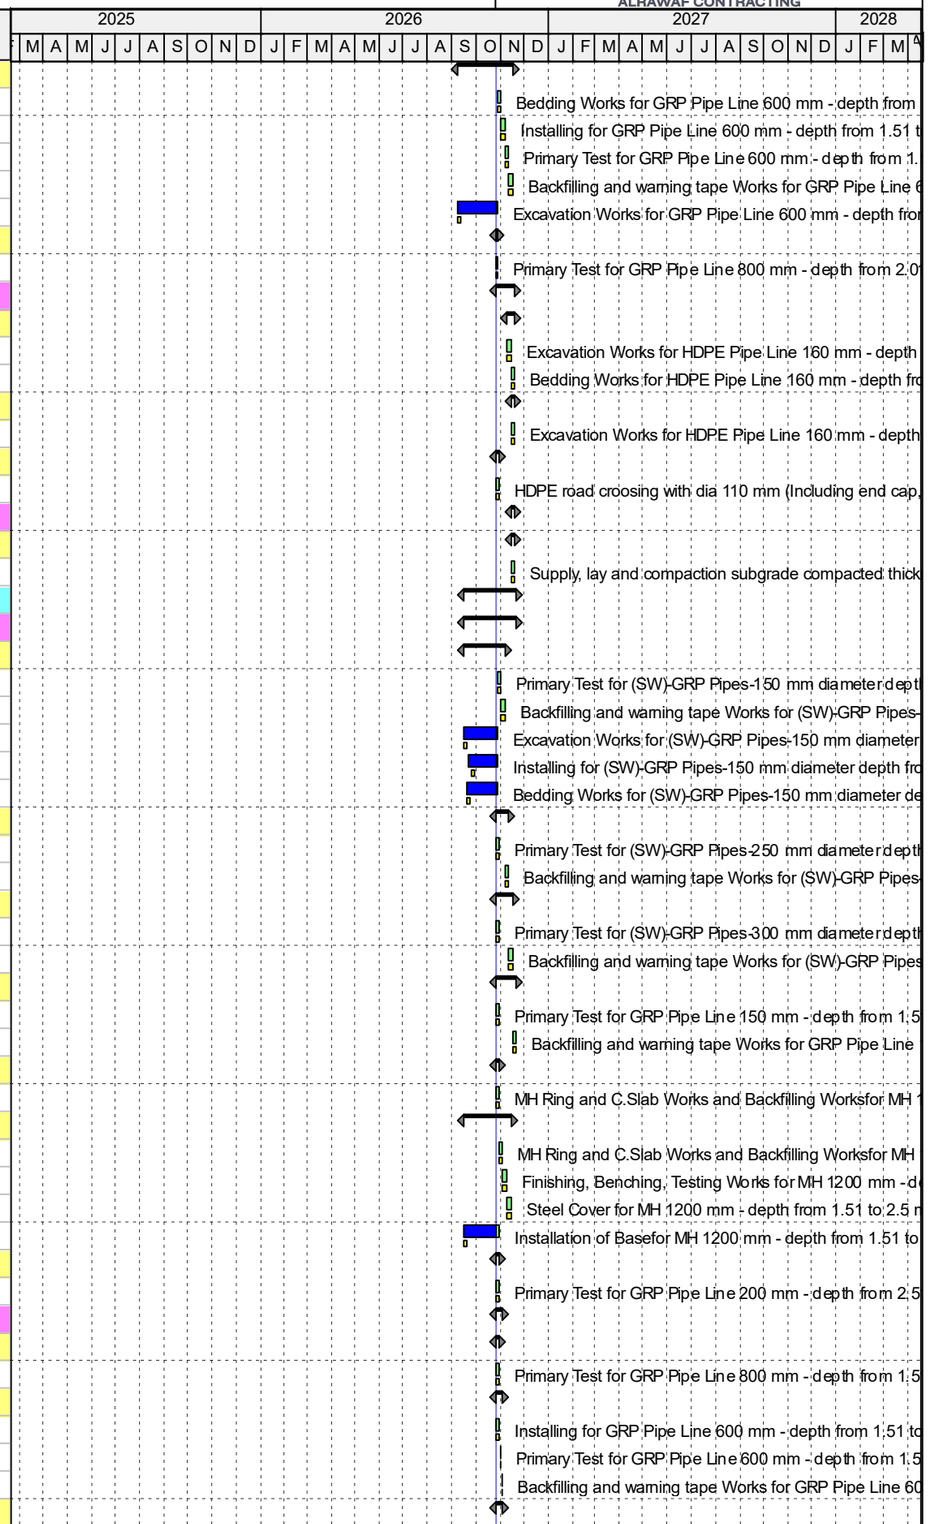

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for GRP Pipe Line 700 mm - depth from 1.51 to 2.(	4d	27-Oct-26	31-Oct-26	142d	0	0	6,247
	Backfilling and warning tape Works for GRP Pipe Line 700 mm	4d	01-Nov-26	04-Nov-26	142d	0	0	6,247
	JDH3-02-009-R4017-(ST)-GRP Pipes-800 mm diameter depth	3d	27-Oct-26	29-Oct-26	420d	0	0	4,011
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.:	3d	27-Oct-26	29-Oct-26	420d	0	0	4,011
	JDH3-02-009-R4017-Catch Basins (Storm Network) - ST	4d	15-Nov-26	18-Nov-26	142d	0	0	18,865
	JDH3-02-009-R4017-(ST)-For Catch Basins (GRP) Pipes-300	4d	15-Nov-26	18-Nov-26	142d	0	0	18,865
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4d	15-Nov-26	18-Nov-26	142d	0	0	18,865
	JDH3-02-009-R4017-TSE Network - TSE	4d	15-Nov-26	18-Nov-26	161d	0	0	8,270
	JDH3-02-009-R4017-(TSE)-HDPE Pipes-110 mm diameter dep	4d	15-Nov-26	18-Nov-26	161d	0	0	8,270
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t(	4d	15-Nov-26	18-Nov-26	161d	0	0	8,270
	JDH3-02-009-R4017-Potable Water Network - WT	16d	27-Oct-26	14-Nov-26	258d	0	0	52,572
	JDH3-02-009-R4017-(WT)-HDPE Pipes-160 mm diameter dep	12d	01-Nov-26	14-Nov-26	195d	0	0	38,815
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t(	4d	01-Nov-26	04-Nov-26	195d	0	0	9,704
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4d	05-Nov-26	09-Nov-26	195d	0	0	2,426
	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m-(	4d	10-Nov-26	14-Nov-26	195d	0	0	26,685
	JDH3-02-009-R4017-(WT)-Plot Connection	4d	27-Oct-26	31-Oct-26	270d	0	0	13,757
	HDPE road crossing with dia 110 mm (Including end cap, isolati	4d	27-Oct-26	31-Oct-26	270d	0	0	13,757
	JDH3-02-009-R4017-Telecommunications Network - TEL	3d	15-Nov-26	17-Nov-26	150d	0	0	286
	JDH3-02-009-R4017-(TEL)-Reinforced Concrete Duct 6-ways	3d	15-Nov-26	17-Nov-26	150d	0	0	286
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	3d	15-Nov-26	17-Nov-26	150d	0	0	286
	JDH3-02-009-R4017-Road Works - RD	4d	10-Nov-26	14-Nov-26	142d	0	0	127,464
	JDH3-02-009-R4017-(RD)-Subgrade	4d	10-Nov-26	14-Nov-26	142d	0	0	127,464
	Supply, lay and compaction subgrade compacted thickness 30(	4d	10-Nov-26	14-Nov-26	142d	0	0	127,464
	R4018	61d	08-Sep-26 A	18-Nov-26	403d	0	8,184	700,005
	JDH3-02-009-R4018-Sewage Network - SW	61d	08-Sep-26 A	18-Nov-26	366d	0	8,184	122,321
	JDH3-02-009-R4018-(SW)-GRP Pipes-150 mm diameter deptl	20d	27-Oct-26	18-Nov-26	366d	0	0	58,961
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4d	27-Oct-26	31-Oct-26	366d	0	0	11,792
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4d	01-Nov-26	04-Nov-26	366d	0	0	2,948
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4d	05-Nov-26	09-Nov-26	366d	0	0	32,429
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4d	10-Nov-26	14-Nov-26	366d	0	0	5,896
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4d	15-Nov-26	18-Nov-26	366d	0	0	5,896
	JDH3-02-009-R4018-(SW)-MH Works depth from 1.51 to 2.5 I	47d	08-Sep-26 A	03-Nov-26	377d	0	8,184	63,360
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	29-Oct-26	03-Nov-26	377d	0	0	36,960
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	3d	08-Sep-26 A	29-Oct-26	377d	0	8,184	26,400
	JDH3-02-009-R4018-Storm Network - ST	16d	27-Oct-26	14-Nov-26	407d	0	0	66,084
	JDH3-02-009-R4018-(ST)-GRP Pipes-400 mm diameter depth	8d	27-Oct-26	04-Nov-26	381d	0	0	1,704
	Primary Test for (ST)-GRP Pipes-400 mm diameter depth from 1	4d	27-Oct-26	31-Oct-26	381d	0	0	852
	Backfilling and warning tape Works for (ST)-GRP Pipes-400 mm	4d	01-Nov-26	04-Nov-26	381d	0	0	852
	JDH3-02-009-R4018-(ST)-GRP Pipes-700 mm diameter depth	8d	27-Oct-26	04-Nov-26	381d	0	0	6,597
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4d	27-Oct-26	31-Oct-26	381d	0	0	3,299
	Backfilling and warning tape Works for (ST)-GRP Pipes-700 mm	4d	01-Nov-26	04-Nov-26	381d	0	0	3,299
	JDH3-02-009-R4018-(ST)-GRP Pipes-600 mm diameter depth	12d	27-Oct-26	09-Nov-26	407d	0	0	40,426
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4d	27-Oct-26	31-Oct-26	407d	0	0	29,646
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.(	4d	01-Nov-26	04-Nov-26	407d	0	0	5,390
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	4d	05-Nov-26	09-Nov-26	407d	0	0	5,390
	JDH3-02-009-R4018-(ST)-GRP Pipes-700 mm diameter depth	16d	27-Oct-26	14-Nov-26	407d	0	0	6,234
	Primary Test for GRP Pipe Line 700 mm - depth from 1.51 to 2.(	4d	27-Oct-26	31-Oct-26	415d	0	0	3,117
	Backfilling and warning tape Works for GRP Pipe Line 700 mm	4d	10-Nov-26	14-Nov-26	407d	0	0	3,117
	JDH3-02-009-R4018-(ST)-GRP Pipes-800 mm diameter depth	3d	27-Oct-26	29-Oct-26	420d	0	0	7,817
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.:	3d	27-Oct-26	29-Oct-26	420d	0	0	7,817
	JDH3-02-009-R4018-(ST)-GRP Pipes-500 mm diameter depth	8d	27-Oct-26	04-Nov-26	381d	0	0	3,305
	Primary Test for GRP Pipe Line 500 mm - depth from 1.51 to 2.(	4d	27-Oct-26	31-Oct-26	381d	0	0	1,653
	Backfilling and warning tape Works for GRP Pipe Line 500 mm	4d	01-Nov-26	04-Nov-26	381d	0	0	1,653

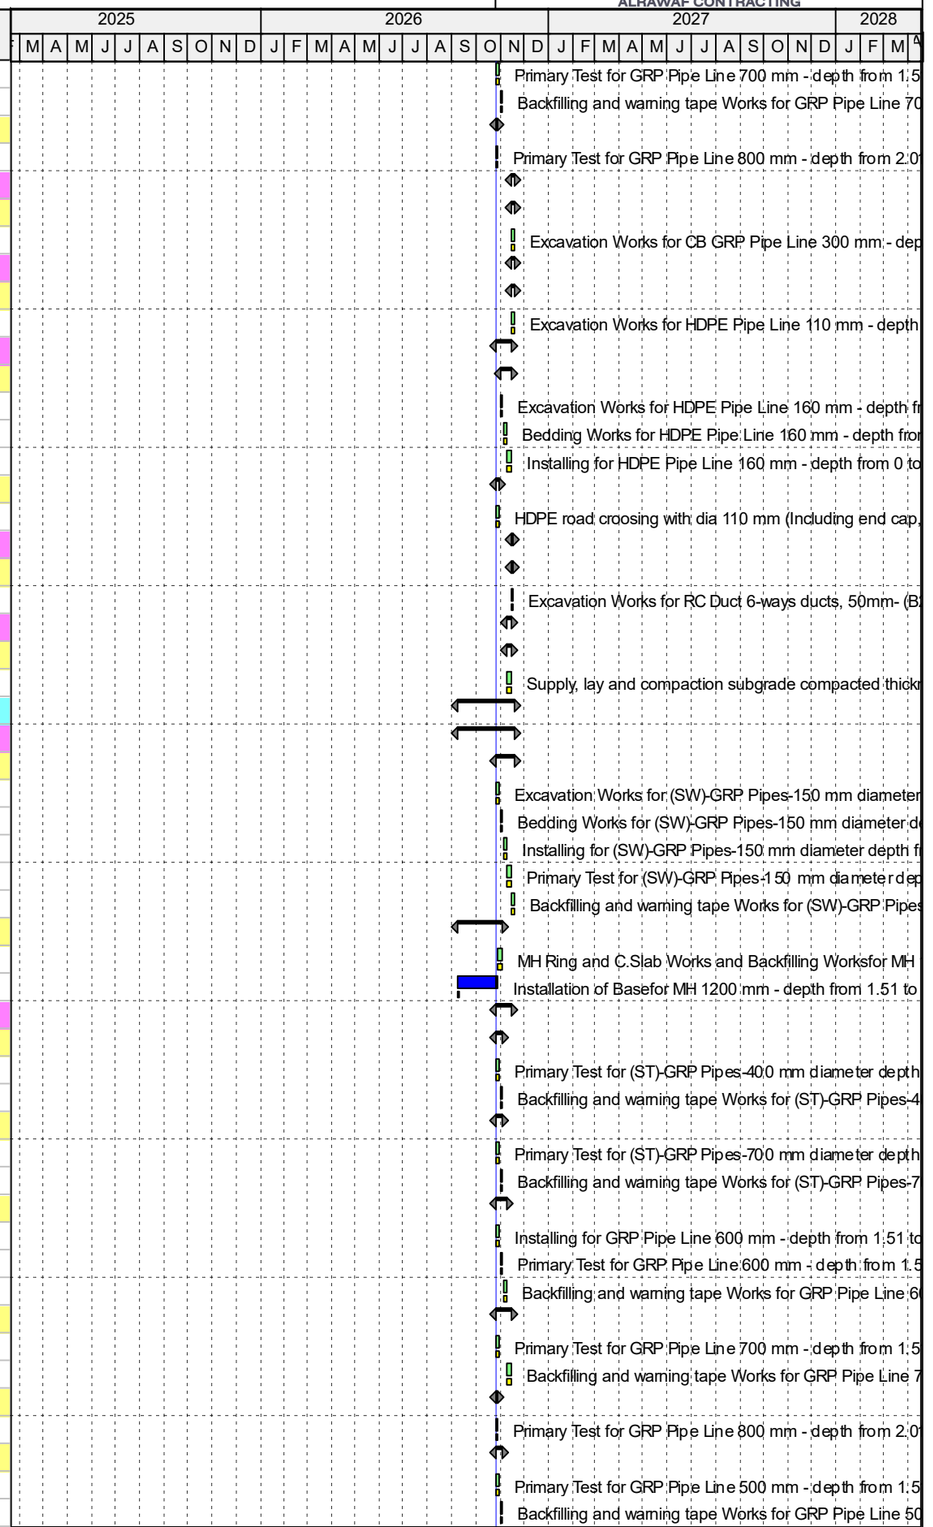


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R4018-Catch Basins (Storm Network) - ST	16d	01-Nov-26	18-Nov-26	153d	0	0	230,113
	JDH3-02-009-R4018-(ST)-For Catch Basins (GRP) Pipes-300	16d	01-Nov-26	18-Nov-26	145d	0	0	129,156
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4d	01-Nov-26	04-Nov-26	143d	0	0	28,701
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 t	4d	05-Nov-26	09-Nov-26	145d	0	0	7,175
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	4d	10-Nov-26	14-Nov-26	145d	0	0	78,928
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	4d	15-Nov-26	18-Nov-26	145d	0	0	14,351
	JDH3-02-009-R4018-(ST)-For Catch Basins (GRP) Pipes-400	14d	01-Nov-26	16-Nov-26	143d	0	0	1,509
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3d	01-Nov-26	03-Nov-26	143d	0	0	335
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 t	3d	04-Nov-26	07-Nov-26	143d	0	0	84
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 n	4d	08-Nov-26	11-Nov-26	143d	0	0	922
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	4d	12-Nov-26	16-Nov-26	143d	0	0	168
	JDH3-02-009-R4018-(ST)-Single Catch Basin Works	16d	01-Nov-26	18-Nov-26	149d	0	0	44,244
	Excavation Works for single Catch Basin- (B6.33 05 39.30)-Z3-F	4d	01-Nov-26	04-Nov-26	149d	0	0	11,643
	PC Blinding and Installationfor single Catch Basin- (B6.33 05 39	4d	05-Nov-26	09-Nov-26	149d	0	0	11,643
	Rings & C.Slab & Final Backfillfor single Catch Basin- (B6.33 05	4d	10-Nov-26	14-Nov-26	149d	0	0	16,301
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4d	15-Nov-26	18-Nov-26	149d	0	0	4,657
	JDH3-02-009-R4018-(ST)-Double Catch Basin Works	16d	01-Nov-26	18-Nov-26	153d	0	0	55,204
	Excavation Works for double Catch Basin- (B6.33 05 39.31)-Z3-	4d	01-Nov-26	04-Nov-26	153d	0	0	14,527
	PC Blinding and Installationfor double Catch Basin- (B6.33 05 3	4d	05-Nov-26	09-Nov-26	153d	0	0	14,527
	Rings & C.Slab & Final Backfillfor double Catch Basin- (B6.33 05	4d	10-Nov-26	14-Nov-26	153d	0	0	20,338
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	4d	15-Nov-26	18-Nov-26	153d	0	0	5,811
	JDH3-02-009-R4018-TSE Network - TSE	12d	27-Oct-26	09-Nov-26	244d	0	0	45,019
	JDH3-02-009-R4018-(TSE)-HDPE Pipes-110 mm diameter dep	12d	27-Oct-26	09-Nov-26	244d	0	0	45,019
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	4d	27-Oct-26	31-Oct-26	244d	0	0	11,255
	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4d	01-Nov-26	04-Nov-26	244d	0	0	2,814
	Installing for HDPE Pipe Line 110 mm - depth from 0 to 1.5 m- (	4d	05-Nov-26	09-Nov-26	244d	0	0	30,951
	JDH3-02-009-R4018-Potable Water Network - WT	20d	27-Oct-26	18-Nov-26	329d	0	0	62,052
	JDH3-02-009-R4018-(WT)-HDPE Pipes-225 mm diameter dep	12d	27-Oct-26	09-Nov-26	232d	0	0	1,368
	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 t	4d	27-Oct-26	31-Oct-26	228d	0	0	342
	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	4d	01-Nov-26	04-Nov-26	232d	0	0	86
	Installing for HDPE Pipe Line 225 mm - depth from 0 to 1.5 m- (	4d	05-Nov-26	09-Nov-26	232d	0	0	941
	JDH3-02-009-R4018-(WT)-Gate Valve-200 mm on pipe dia (22	8d	10-Nov-26	18-Nov-26	232d	0	0	2,660
	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B3.33	4d	10-Nov-26	14-Nov-26	232d	0	0	2,394
	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 m	4d	15-Nov-26	18-Nov-26	232d	0	0	266
	JDH3-02-009-R4018-(WT)-Fire Hydrant	4d	05-Nov-26	09-Nov-26	228d	0	0	9,771
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	4d	05-Nov-26	09-Nov-26	228d	0	0	9,771
	JDH3-02-009-R4018-(WT)-Plot Connection	3d	27-Oct-26	29-Oct-26	261d	0	0	6,879
	HDPE road crossing with dia 110 mm (Including end cap, isolati	3d	27-Oct-26	29-Oct-26	261d	0	0	6,879
	JDH3-02-009-R4018-(WT)-HDPE Pipes-225 mm diameter dep	16d	01-Nov-26	18-Nov-26	329d	0	0	41,375
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	4d	01-Nov-26	04-Nov-26	228d	0	0	9,194
	Bedding Works for HDPE Pipe Line 225 mm - depth from 1.51 t	4d	05-Nov-26	09-Nov-26	236d	0	0	2,299
	Installing for HDPE Pipe Line 225 mm - depth from 1.51 to 2.5 r	4d	10-Nov-26	14-Nov-26	236d	0	0	25,285
	Primary Test for HDPE Pipe Line 225 mm - depth from 1.51 to 2	4d	15-Nov-26	18-Nov-26	329d	0	0	4,597
	JDH3-02-009-R4018-Electrical Network - EL	12d	01-Nov-26	14-Nov-26	259d	0	0	2,054
	JDH3-02-009-R4018-(EL)-MV cables duct banks 2-way	12d	01-Nov-26	14-Nov-26	259d	0	0	2,054
	Excavation for MV cables duct banks 2-way- (B2.33 71 19.07)-Z	3d	01-Nov-26	03-Nov-26	257d	0	0	205
	Installing upvc pipe for MV cables duct banks 2-way- (B2.33 71	3d	04-Nov-26	07-Nov-26	259d	0	0	205
	Pouring Concrete Cover for MV cables duct banks 2-way- (B2.33	3d	08-Nov-26	10-Nov-26	259d	0	0	1,335
	Backfilling Works for MV cables duct banks 2-way- (B2.33 71 19	3d	11-Nov-26	14-Nov-26	259d	0	0	308
	JDH3-02-009-R4018-Street Lighting Network -SL	12d	04-Nov-26	17-Nov-26	287d	0	0	2,053
	JDH3-02-009-R4018-(SL)-Road Crossing Ducts 2 way PVC 2	12d	04-Nov-26	17-Nov-26	287d	0	0	2,053
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	4d	04-Nov-26	08-Nov-26	287d	0	0	432
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z3-R	4d	09-Nov-26	12-Nov-26	287d	0	0	1,297

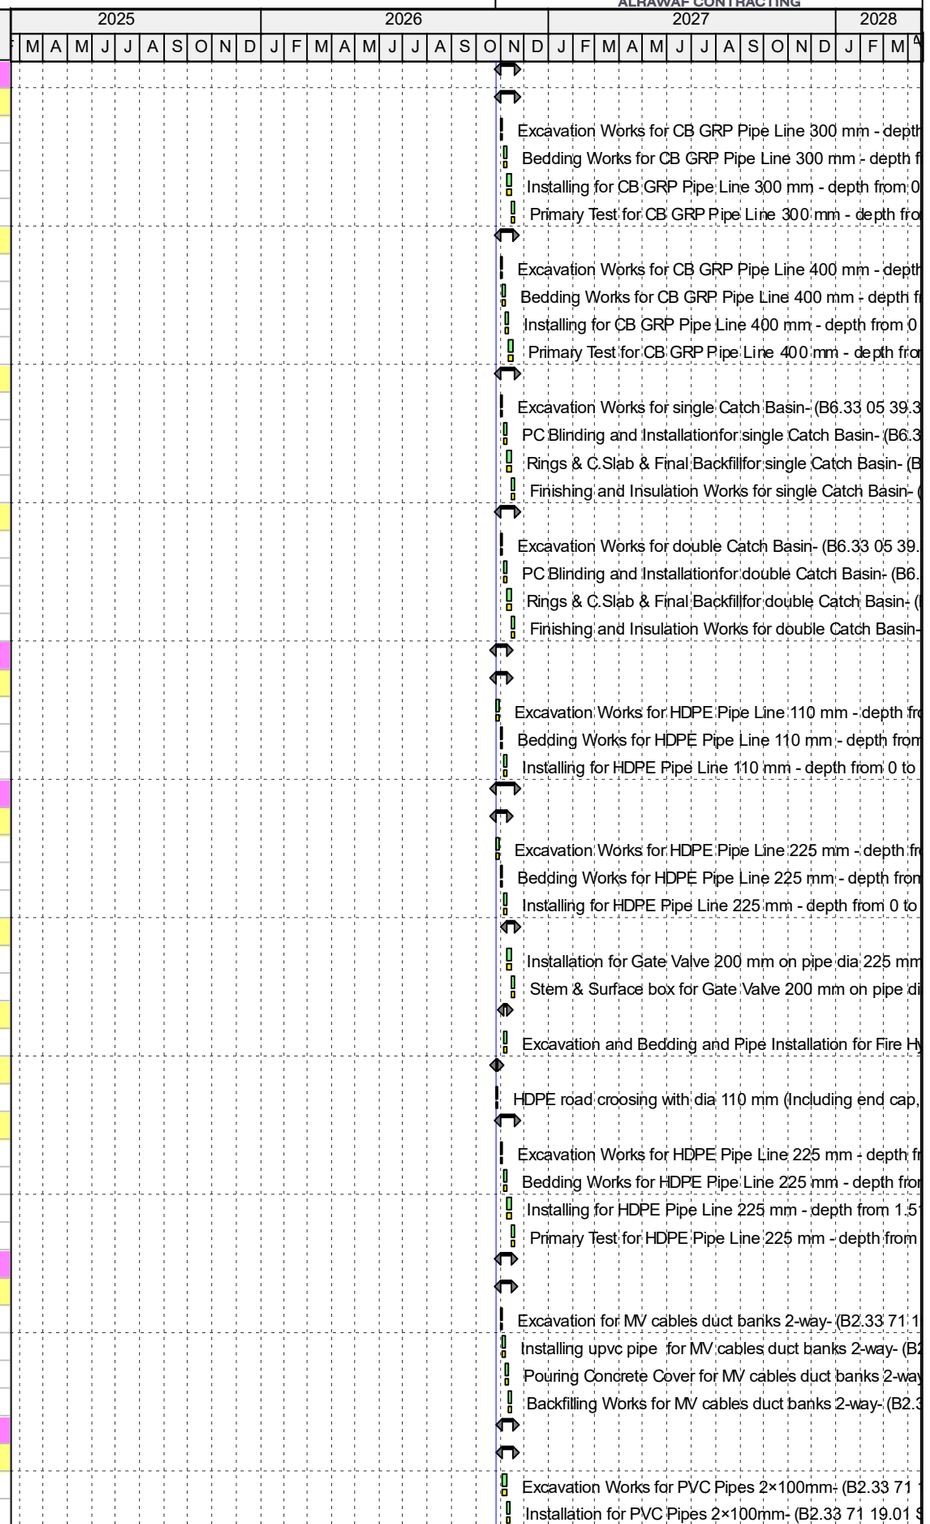


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	4d	14-Nov-26	17-Nov-26	287d	0	0	324
	JDH3-02-009-R4018-Road Works - RD	4d	27-Oct-26	31-Oct-26	143d	0	0	170,309
	JDH3-02-009-R4018-(RD)-Subgrade	4d	27-Oct-26	31-Oct-26	143d	0	0	170,309
	Supply, lay and compaction subgrade compacted thickness 300	4d	27-Oct-26	31-Oct-26	143d	0	0	170,309
	R4019	79d	18-Aug-26 A	18-Nov-26	369d	0	33,221	497,206
	JDH3-02-009-R4019-Sewage Network - SW	20d	27-Oct-26	18-Nov-26	365d	0	0	120,010
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter depth	20d	27-Oct-26	18-Nov-26	357d	0	0	29,707
	Excavation Works for GRP Pipe Line 150 mm - depth from 1.51	4d	27-Oct-26	31-Oct-26	357d	0	0	5,941
	Bedding Works for GRP Pipe Line 150 mm - depth from 1.51 to	4d	01-Nov-26	04-Nov-26	357d	0	0	1,485
	Installing for GRP Pipe Line 150 mm - depth from 1.51 to 2.5 m	4d	05-Nov-26	09-Nov-26	357d	0	0	16,339
	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	4d	10-Nov-26	14-Nov-26	357d	0	0	2,971
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4d	15-Nov-26	18-Nov-26	357d	0	0	2,971
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter depth	16d	01-Nov-26	18-Nov-26	357d	0	0	27,061
	Excavation Works for GRP Pipe Line 150 mm - depth from 0 to	4d	01-Nov-26	04-Nov-26	357d	0	0	6,013
	Bedding Works for GRP Pipe Line 150 mm - depth from 0 to 1.	4d	05-Nov-26	09-Nov-26	357d	0	0	1,503
	Installing for GRP Pipe Line 150 mm - depth from 0 to 1.5 m- (E	4d	10-Nov-26	14-Nov-26	357d	0	0	16,537
	Primary Test for GRP Pipe Line 150 mm - depth from 0 to 1.5 m	4d	15-Nov-26	18-Nov-26	357d	0	0	3,007
	JDH3-02-009-R4019-(SW)-MH Works depth from 1.51 to 2.5 D	8d	27-Oct-26	04-Nov-26	369d	0	0	43,865
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4d	27-Oct-26	31-Oct-26	369d	0	0	18,277
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4d	01-Nov-26	04-Nov-26	369d	0	0	25,588
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter depth	16d	27-Oct-26	14-Nov-26	369d	0	0	19,377
	Excavation Works for GRP Pipe Line 150 mm - depth from 2.51	4d	27-Oct-26	31-Oct-26	369d	0	0	4,306
	Bedding Works for GRP Pipe Line 150 mm - depth from 2.51 to	4d	01-Nov-26	04-Nov-26	369d	0	0	1,077
	Installing for GRP Pipe Line 150 mm - depth from 2.51 to 3.5 m	4d	05-Nov-26	09-Nov-26	369d	0	0	11,842
	Primary Test for GRP Pipe Line 150 mm - depth from 2.51 to 3.	4d	10-Nov-26	14-Nov-26	369d	0	0	2,153
	JDH3-02-009-R4019-Storm Network - ST	72d	18-Aug-26 A	11-Nov-26	376d	0	33,221	67,633
	JDH3-02-009-R4019-(ST)-GRP Pipes-400 mm diameter depth	68d	18-Aug-26 A	07-Nov-26	376d	0	33,221	62,919
	Primary Test for (ST)-GRP Pipes-400 mm diameter depth from 1	4d	28-Oct-26	02-Nov-26	376d	0	0	6,292
	Backfilling and warning tape Works for (ST)-GRP Pipes-400 mm	4d	02-Nov-26	07-Nov-26	376d	0	0	6,292
	Installing for (ST)-GRP Pipes-400 mm diameter depth from 1.51	4d	23-Aug-26 A	28-Oct-26	376d	0	22,839	34,605
	Excavation Works for (ST)-GRP Pipes-400 mm diameter depth f	4d	18-Aug-26 A	28-Oct-26	376d	0	8,305	12,584
	Bedding Works for (ST)-GRP Pipes-400 mm diameter depth fro	4d	20-Aug-26 A	28-Oct-26	376d	0	2,076	3,146
	JDH3-02-009-R4019-(ST)-GRP Pipes-500 mm diameter depth	13d	27-Oct-26	11-Nov-26	376d	0	0	4,715
	Primary Test for GRP Pipe Line 500 mm - depth from 1.51 to 2.	4d	27-Oct-26	31-Oct-26	381d	0	0	2,357
	Backfilling and warning tape Works for GRP Pipe Line 500 mm	4d	07-Nov-26	11-Nov-26	376d	0	0	2,357
	JDH3-02-009-R4019-Catch Basins (Storm Network) - ST	8d	09-Nov-26	17-Nov-26	150d	0	0	22,900
	JDH3-02-009-R4019-(ST)-For Catch Basins (GRP) Pipes-300 I	8d	09-Nov-26	17-Nov-26	150d	0	0	21,535
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4d	09-Nov-26	12-Nov-26	143d	0	0	17,228
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 to	4d	14-Nov-26	17-Nov-26	150d	0	0	4,307
	JDH3-02-009-R4019-(ST)-For Catch Basins (GRP) Pipes-400 I	3d	14-Nov-26	16-Nov-26	143d	0	0	1,365
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3d	14-Nov-26	16-Nov-26	143d	0	0	1,365
	JDH3-02-009-R4019-TSE Network - TSE	8d	09-Nov-26	17-Nov-26	346d	0	0	11,957
	JDH3-02-009-R4019-(TSE)-HDPE Pipes-110 mm diameter dep	8d	09-Nov-26	17-Nov-26	346d	0	0	9,664
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 to	4d	09-Nov-26	12-Nov-26	346d	0	0	7,731
	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4d	14-Nov-26	17-Nov-26	346d	0	0	1,933
	JDH3-02-009-R4019-(TSE)-HDPE Pipes-110 mm diameter dep	4d	14-Nov-26	17-Nov-26	346d	0	0	2,293
	Excavation Works for HDPE Pipe Line 110 mm - depth from 1.5	4d	14-Nov-26	17-Nov-26	346d	0	0	2,293
	JDH3-02-009-R4019-Potable Water Network - WT	20d	27-Oct-26	18-Nov-26	333d	0	0	116,343
	JDH3-02-009-R4019-(WT)-HDPE Pipes-160 mm diameter dep	12d	01-Nov-26	14-Nov-26	305d	0	0	70,153
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 to	4d	01-Nov-26	04-Nov-26	305d	0	0	17,538
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4d	05-Nov-26	09-Nov-26	305d	0	0	4,385
	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m-	4d	10-Nov-26	14-Nov-26	305d	0	0	48,230
	JDH3-02-009-R4019-(WT)-HDPE Pipes-160 mm diameter dep	12d	05-Nov-26	18-Nov-26	305d	0	0	41,030

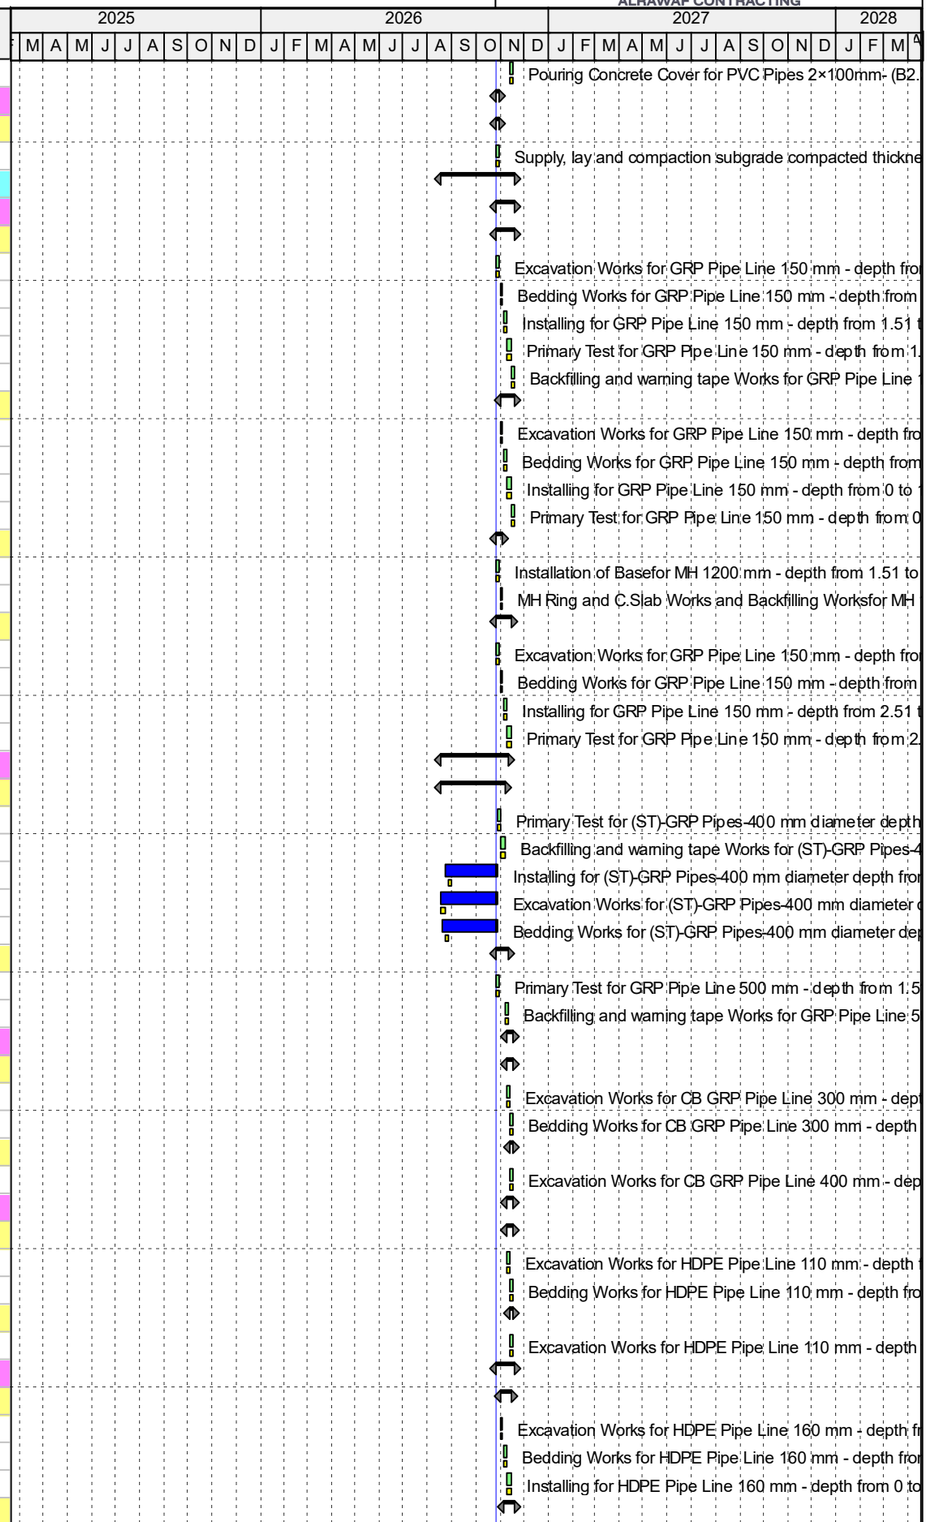


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	4d	05-Nov-26	09-Nov-26	305d	0	0	10,258
	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51 t	4d	10-Nov-26	14-Nov-26	305d	0	0	2,564
	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5 r	4d	15-Nov-26	18-Nov-26	305d	0	0	28,208
	JDH3-02-009-R4019-(WT)-Plot Connection	3d	27-Oct-26	29-Oct-26	350d	0	0	5,159
	HDPE road crossing with dia 110 mm (Including end cap, isolati	3d	27-Oct-26	29-Oct-26	350d	0	0	5,159
	JDH3-02-009-R4019-Electrical Network - EL	4d	09-Nov-26	12-Nov-26	274d	0	0	2,650
	JDH3-02-009-R4019-(EL)-MV cable trench size 1.5m wide an	4d	09-Nov-26	12-Nov-26	274d	0	0	2,650
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	4d	09-Nov-26	12-Nov-26	274d	0	0	2,650
	JDH3-02-009-R4019-Road Works - RD	4d	04-Nov-26	08-Nov-26	143d	0	0	155,714
	JDH3-02-009-R4019-(RD)-Subgrade	4d	04-Nov-26	08-Nov-26	143d	0	0	155,714
	Supply, lay and compaction subgrade compacted thickness 300	4d	04-Nov-26	08-Nov-26	143d	0	0	155,714
	R6605	20d	27-Oct-26	18-Nov-26	344d	0	0	105,505
	JDH3-02-009-R6605-Catch Basins (Storm Network) - ST	20d	27-Oct-26	18-Nov-26	344d	0	0	64,098
	JDH3-02-009-R6605-(ST)-For Catch Basins (GRP) Pipes-300 r	20d	27-Oct-26	18-Nov-26	344d	0	0	38,428
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4d	27-Oct-26	31-Oct-26	329d	0	0	7,686
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 t	4d	01-Nov-26	04-Nov-26	344d	0	0	1,921
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	4d	05-Nov-26	09-Nov-26	344d	0	0	21,135
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	4d	10-Nov-26	14-Nov-26	344d	0	0	3,843
	Backfilling and warning tape Works for CB GRP Pipe Line 300 n	4d	15-Nov-26	18-Nov-26	344d	0	0	3,843
	JDH3-02-009-R6605-(ST)-For Catch Basins (GRP) Pipes-400 r	14d	01-Nov-26	16-Nov-26	342d	0	0	561
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3d	01-Nov-26	03-Nov-26	329d	0	0	125
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 t	3d	04-Nov-26	07-Nov-26	342d	0	0	31
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 n	4d	08-Nov-26	11-Nov-26	342d	0	0	343
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	4d	12-Nov-26	16-Nov-26	342d	0	0	62
	JDH3-02-009-R6605-(ST)-Single Catch Basin Works	12d	04-Nov-26	17-Nov-26	337d	0	0	20,958
	Excavation Works for single Catch Basin- (B6.33 05 39.30)-Z3-F	4d	04-Nov-26	08-Nov-26	329d	0	0	6,164
	PC Blinding and Installationfor single Catch Basin- (B6.33 05 39	4d	09-Nov-26	12-Nov-26	337d	0	0	6,164
	Rings & C.Slab & Final Backfillfor single Catch Basin- (B6.33 05	4d	14-Nov-26	17-Nov-26	337d	0	0	8,630
	JDH3-02-009-R6605-(ST)-Double Catch Basin Works	8d	09-Nov-26	17-Nov-26	329d	0	0	4,151
	Excavation Works for double Catch Basin- (B6.33 05 39.31)-Z3-	4d	09-Nov-26	12-Nov-26	329d	0	0	2,075
	PC Blinding and Installationfor double Catch Basin- (B6.33 05 3	4d	14-Nov-26	17-Nov-26	329d	0	0	2,075
	JDH3-02-009-R6605-Road Works - RD	12d	05-Nov-26	18-Nov-26	344d	0	0	41,408
	JDH3-02-009-R6605-(RD)-Precast Concrete Curb	12d	05-Nov-26	18-Nov-26	344d	0	0	41,408
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	4d	05-Nov-26	09-Nov-26	344d	0	0	31,361
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	4d	10-Nov-26	14-Nov-26	344d	0	0	9,748
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4d	15-Nov-26	18-Nov-26	344d	0	0	298
	CMZ Linking Road	90d	11-Aug-26 A	24-Nov-26	398d	0	1,173,238	6,496,893
	JDH3-02-009-Execution	90d	11-Aug-26 A	24-Nov-26	398d	0	1,173,238	6,496,893
	JDH3-02-009-Road Works - CMZ Linking Road	52d	03-Sep-26 A	03-Nov-26	416d	0	301,368	505,344
JDI	Riprap with thickness 300mm for Logistic Area- (B6.31 22 00.02	7d	27-Oct-26	03-Nov-26	416d	0	0	3,064
JDI	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	3d	03-Sep-26 A	28-Oct-26	260d	0	301,368	502,281
	JDH3-02-009-CMZ-Catch Basins (Storm Network) - ST	10d	27-Oct-26	07-Nov-26	376d	0	0	432,421
	JDH3-02-009-R151-(ST)-For Catch Basins (GRP) Pipes-300 mm dia	10d	27-Oct-26	07-Nov-26	376d	0	0	432,421
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	2d	27-Oct-26	28-Oct-26	376d	0	0	86,484
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 t	2d	29-Oct-26	31-Oct-26	376d	0	0	21,621
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	2d	01-Nov-26	02-Nov-26	376d	0	0	237,832
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	2d	03-Nov-26	04-Nov-26	376d	0	0	43,242
	Backfilling and warning tape Works for CB GRP Pipe Line 300 n	2d	05-Nov-26	07-Nov-26	376d	0	0	43,242
	JDH3-02-009-CMZ-TSE Network - TSE	10d	08-Nov-26	18-Nov-26	403d	0	0	296,010
	JDH3-02-009-R07-(TSE)-Gate Valve-200 mm on pipe dia (225) mm	4d	08-Nov-26	11-Nov-26	407d	0	0	5,319
	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B4.33	2d	08-Nov-26	09-Nov-26	407d	0	0	4,787
	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 m	2d	10-Nov-26	11-Nov-26	407d	0	0	532
	JDH3-02-009-R151-(TSE)-Gate Valve-150 mm on pipe dia (160) mm	4d	08-Nov-26	11-Nov-26	407d	0	0	1,766

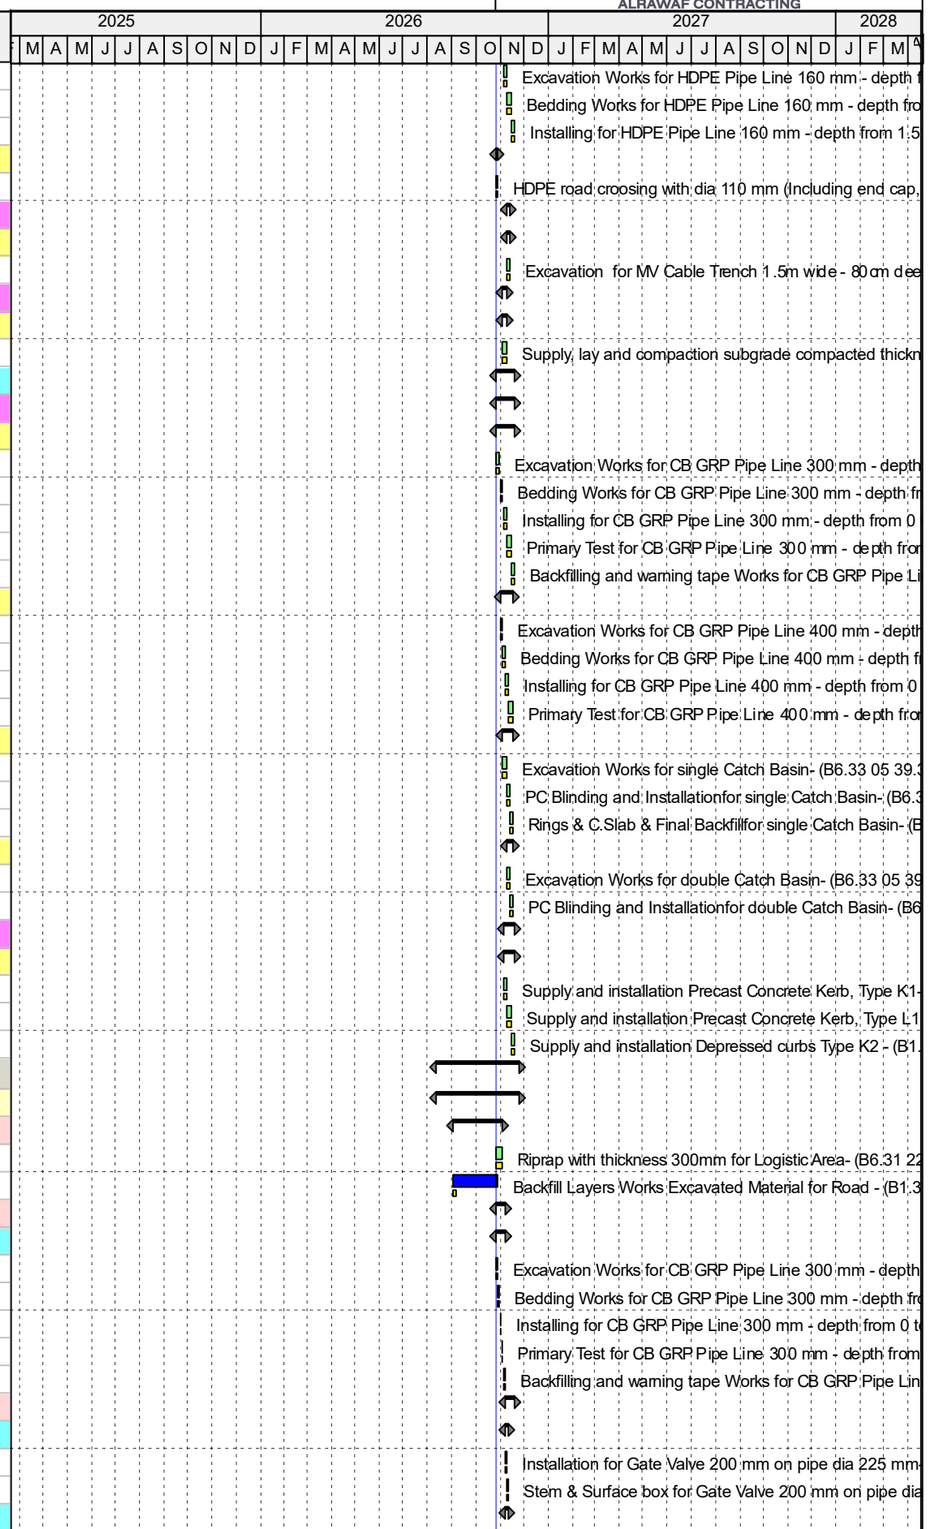


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B4.33	2d	08-Nov-26	09-Nov-26	407d	0	0	1,589
	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 m	2d	10-Nov-26	11-Nov-26	407d	0	0	177
JDH3-02-009-R151-(TSE)-Gate Valve-100 mm on pipe dia (110) mm		6d	08-Nov-26	14-Nov-26	407d	0	0	20,293
	Installation for Gate Valve 100 mm on pipe dia 110 mm- (B4.33	2d	08-Nov-26	09-Nov-26	409d	0	0	18,264
	Stem & Surface box for Gate Valve 100 mm on pipe dia 110 m	2d	12-Nov-26	14-Nov-26	407d	0	0	2,029
JDH3-02-009-CMZ-Potable Water Network - WT		10d	08-Nov-26	18-Nov-26	381d	0	0	268,632
JDH3-02-009-R16-(WT)-HDPE Pipes-160 mm diameter depth fro		8d	08-Nov-26	16-Nov-26	377d	0	0	20,065
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	3d	08-Nov-26	10-Nov-26	376d	0	0	16,052
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	5d	11-Nov-26	16-Nov-26	377d	0	0	4,013
JDH3-02-009-R151-(WT)-HDPE Pipes-225 mm diameter depth fr		7d	11-Nov-26	18-Nov-26	381d	0	0	822
	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 t	3d	11-Nov-26	14-Nov-26	376d	0	0	658
	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	4d	15-Nov-26	18-Nov-26	381d	0	0	164
JDH3-02-009-R151-(WT)-HDPE Pipes-225 mm diameter depth fr		3d	15-Nov-26	17-Nov-26	376d	0	0	247,745
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	3d	15-Nov-26	17-Nov-26	376d	0	0	247,745
JDH3-02-009-CMZ-Street Lighting Network -SL		22d	27-Oct-26	21-Nov-26	391d	0	0	219,171
JDH3-02-009-R151-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE/S		20d	27-Oct-26	18-Nov-26	393d	0	0	99,495
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5d	27-Oct-26	01-Nov-26	391d	0	0	9,950
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5d	02-Nov-26	07-Nov-26	393d	0	0	74,622
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5d	08-Nov-26	12-Nov-26	393d	0	0	4,975
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5d	14-Nov-26	18-Nov-26	393d	0	0	9,950
JDH3-02-009-R151-(SL)-Road Crossing Ducts 2 way PVC 2 × 100 n		8d	27-Oct-26	04-Nov-26	366d	0	0	7,879
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	2d	27-Oct-26	28-Oct-26	366d	0	0	1,576
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z3-R	2d	29-Oct-26	31-Oct-26	366d	0	0	4,728
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	2d	01-Nov-26	02-Nov-26	366d	0	0	1,182
	Testing and Backfilling Works for PVC Pipes 2×100mm- (B2.33	2d	03-Nov-26	04-Nov-26	366d	0	0	394
JDH3-02-009-R151-(SL)-Lighting Pole with single arm 12 m height		17d	02-Nov-26	21-Nov-26	391d	0	0	111,796
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3d	02-Nov-26	04-Nov-26	391d	0	0	11,768
	Installation of RC foundation for Lighting Pole single arm- (B2.2	4d	05-Nov-26	09-Nov-26	391d	0	0	11,768
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	3d	10-Nov-26	12-Nov-26	391d	0	0	11,768
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	7d	14-Nov-26	21-Nov-26	391d	0	0	76,492
JDH3-02-009-CMZ-Road Works - RD		56d	10-Sep-26 A	24-Nov-26	270d	0	539,121	3,496,526
JDH3-02-009-R151-(RD)-Aggregate Base Course		3d	10-Sep-26 A	27-Oct-26	260d	0	308,013	334,797
	Supply, lay and compaction Aggregate base course compacted	3d	10-Sep-26 A	27-Oct-26	260d	0	308,013	334,797
JDH3-02-009-R151-(RD)-Bituminous base course 150 mm Two Lay		27d	15-Oct-26 A	14-Nov-26	256d	0	231,107	1,491,016
	Supply, lay and Asphaltic base course induding tack Coat (RC2)	11d	02-Nov-26	14-Nov-26	256d	0	0	745,508
	Supply, lay and Asphaltic base course including Prime Coat (MC	5d	15-Oct-26 A	01-Nov-26	256d	0	231,107	745,508
JDH3-02-009-R151-(RD)-Bituminous concrete wearing course 50 m		5d	02-Nov-26	07-Nov-26	285d	0	0	379,592
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5d	02-Nov-26	07-Nov-26	285d	0	0	379,592
JDH3-02-009-R151-(RD)-Precast Concrete Curb		9d	15-Nov-26	24-Nov-26	256d	0	0	1,291,121
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9d	15-Nov-26	24-Nov-26	256d	0	0	1,291,121
Concrete & Guard rail		84d	11-Aug-26 A	17-Nov-26	404d	0	332,749	1,547,421
Concrete Works		19d	27-Oct-26	17-Nov-26	404d	0	0	881,923
	50 mm thickness lean concrete under the foundation and grade	2d	27-Oct-26	28-Oct-26	404d	0	0	2,825
	Concrete floor slab on grade Including Mastic sealant as per dra	17d	29-Oct-26	17-Nov-26	404d	0	0	879,099
Guard Rail		9d	11-Aug-26 A	28-Oct-26	421d	0	332,749	665,498
	Guard Rail For Roads Station 05 - Left side - Vertical Column	4d	11-Aug-26 A	28-Oct-26	421d	0	83,187	166,374
	Guard Rail For Roads Station 05 - Left side - Horizontal Guard	4d	12-Aug-26 A	28-Oct-26	421d	0	83,187	166,374
	Guard Rail For Roads Station 05 - Right side - Vertical Column	4d	12-Aug-26 A	28-Oct-26	421d	0	83,187	166,374
	Guard Rail For Roads Station 05 - Right side - Horizontal Guard	4d	13-Aug-26 A	28-Oct-26	421d	0	83,187	166,374
Pond 5		28d	27-Oct-26	28-Nov-26	383d	0	0	1,981,860
JDH3-02-009-ST1-Stage (1) - Pond 5		11d	27-Oct-26	08-Nov-26	394d	0	0	693,413
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5d	27-Oct-26	01-Nov-26	371d	0	0	595,034
JDH3(	Chain Link Fence for Pond 5- (B6.31 22 00.09)-PS-PN5-ST1	6d	02-Nov-26	08-Nov-26	394d	0	0	98,378

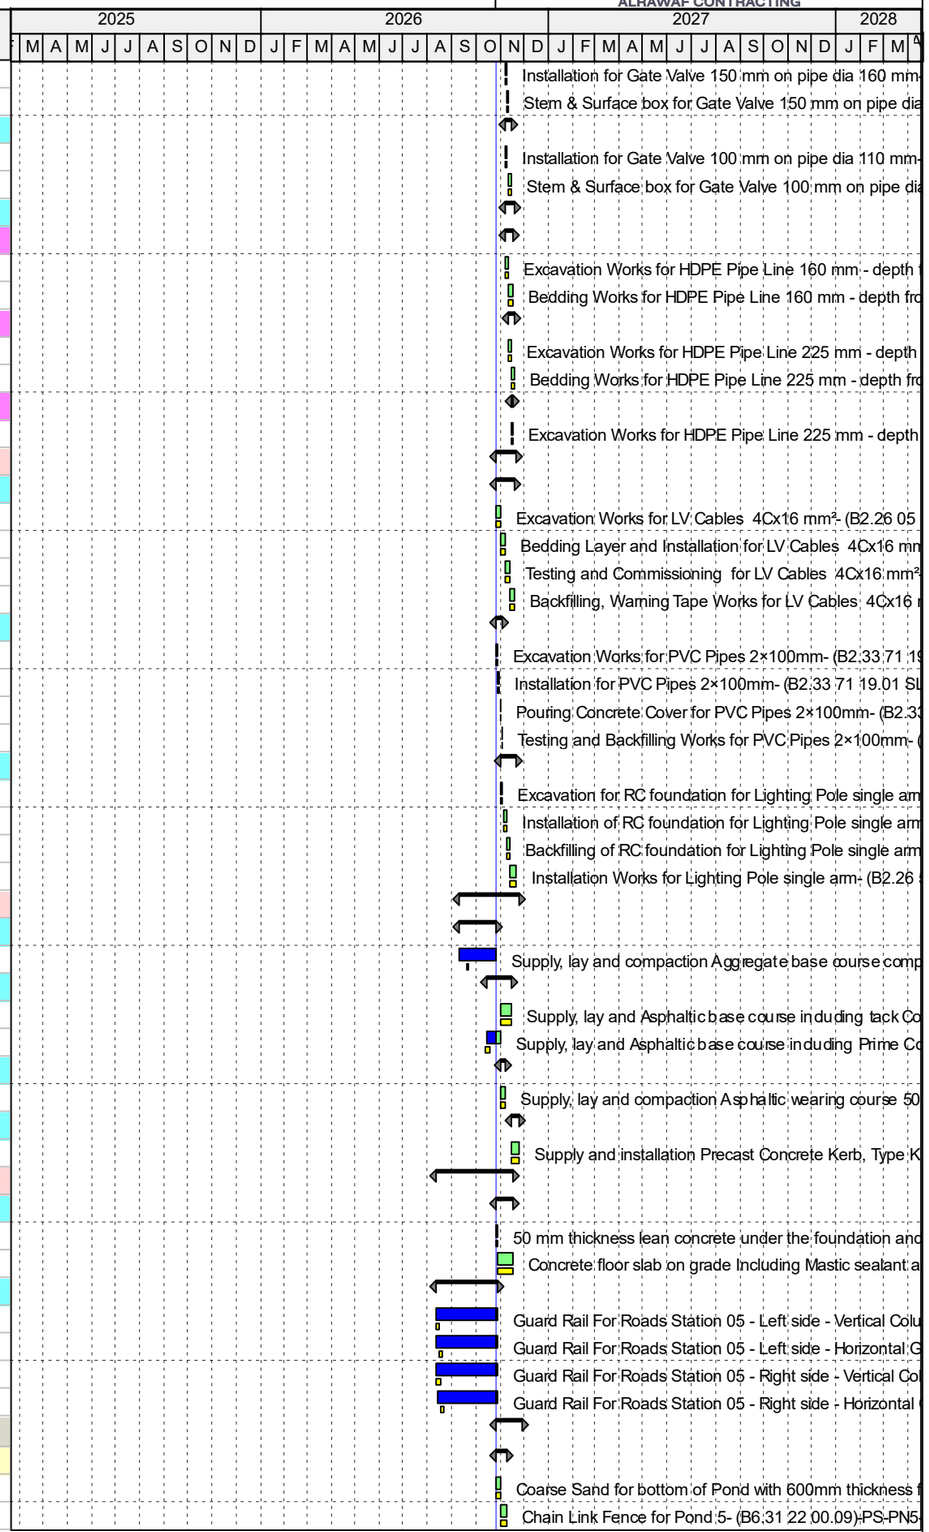


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-ST2-Stage (2) - Pond 5	12d	02-Nov-26	15-Nov-26	394d	0	0	693,413
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5d	02-Nov-26	07-Nov-26	371d	0	0	595,034
JDH3(	Chain Link Fence for Pond 5- (B6.31 22 00.09)-PS-PN5-ST2	6d	09-Nov-26	15-Nov-26	394d	0	0	98,378
	JDH3-02-009-ST3-Stage (3) - Pond 5	18d	08-Nov-26	28-Nov-26	371d	0	0	595,034
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	18d	08-Nov-26	28-Nov-26	371d	0	0	595,034
JDH3-02-009-Linking Road between CMZ and Jeddah-Jazan R		114d	04-Aug-26 A	10-Feb-27	331d	781,836	211,829	781,836
Linking Road Milestones		0d	10-Feb-27	10-Feb-27	331d	0	0	0
JDH3CCM	Finish of CMZ Road	0d		10-Feb-27	331d	0	0	0
Construction		26d	27-Oct-26	25-Nov-26	397d	358,179	0	358,179
JDH3-02-009-CZ-Street Lighting Network -SL		26d	27-Oct-26	25-Nov-26	397d	358,179	0	358,179
JDH3-02-009-CZ-(SL)-Lighting Pole with double arms 16 m height		16d	08-Nov-26	25-Nov-26	362d	106,138	0	106,138
JDI	Earthing + Primary Test for Lighting Pole double arms- (B2.26 5	16d	08-Nov-26	25-Nov-26	362d	106,138	0	106,138
JDH3-02-009-CZ-(SL)-Lighting Pole with single arm 12 m height		10d	27-Oct-26	07-Nov-26	362d	149,775	0	149,775
JDI	Installation of RC foundation for Lighting Pole single arm- (B2.2	2d	27-Oct-26	28-Oct-26	362d	37,444	0	37,444
JDI	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	2d	29-Oct-26	31-Oct-26	362d	28,083	0	28,083
JDI	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	3d	01-Nov-26	03-Nov-26	362d	65,526	0	65,526
JDI	Earthing + Primary Test for Lighting Pole single arm- (B2.26 56	3d	04-Nov-26	07-Nov-26	362d	18,722	0	18,722
JDH3-02-009-CZ-(SL)-Road Crossing Ducts 2 way PVC 2 × 150 mm		20d	27-Oct-26	18-Nov-26	343d	15,355	0	15,355
JDI	Excavation Works for PVC Pipes 2×150mm- (B2.33 71 19.01)-L	20d	27-Oct-26	18-Nov-26	343d	15,355	0	15,355
JDH3-02-009-CZ-(SL)- LV Cables - Copper, 4xC 50 mm² XLPE /PVC/S		12d	27-Oct-26	09-Nov-26	411d	9,255	0	9,255
JDI	Excavation Works for LV Cables 4Cx50 mm²- (B2.26 05 19.02)	2d	27-Oct-26	28-Oct-26	411d	2,776	0	2,776
JDI	Bedding Layer and Installation for LV Cables 4Cx50 mm²- (B2.2	2d	29-Oct-26	31-Oct-26	415d	2,776	0	2,776
JDI	Testing and Commissioning for LV Cables 4Cx50 mm²- (B2.26	2d	01-Nov-26	02-Nov-26	415d	2,776	0	2,776
JDI	Backfilling, Warning Tape Works for LV Cables 4Cx50 mm²- (B2	2d	08-Nov-26	09-Nov-26	411d	925	0	925
JDH3-02-009-CZ-(SL)- LV Cables - Single Core Copper, 1xC 25mm² X		8d	29-Oct-26	07-Nov-26	411d	1,376	0	1,376
JDI	Excavation Works for LV Cables 1Cx25 mm²- (B2.26 05 19.05)	2d	29-Oct-26	31-Oct-26	411d	413	0	413
JDI	Bedding Layer and Installation for LV Cables 1Cx25 mm²- (B2.2	2d	01-Nov-26	02-Nov-26	411d	413	0	413
JDI	Testing and Commissioning for LV Cables 1Cx25 mm²- (B2.26	2d	03-Nov-26	04-Nov-26	411d	413	0	413
JDI	Backfilling, Warning Tape Works for LV Cables 1Cx25 mm²- (B2	2d	05-Nov-26	07-Nov-26	411d	138	0	138
JDH3-02-009-CZ-(SL)-Street Lighting (LED) Luminaire complete with c		19d	27-Oct-26	17-Nov-26	369d	76,281	0	76,281
JDI	Earthing & Primary Test for Lighting(LED) Luminaire - (B2.26.5	19d	27-Oct-26	17-Nov-26	369d	76,281	0	76,281
Close Out		10d	04-Aug-26 A	22-Dec-26	362d	423,657	211,829	423,657
Final Testing and Commissioning - FT-Jeddah Jazan- CZ		10d	04-Aug-26 A	22-Dec-26	362d	423,657	211,829	423,657
JDH3F	Testing Street Lighting Work - FT-CZ	10d	04-Aug-26 A	22-Dec-26	362d	423,657	211,829	423,657
JDH3-02-009-Lift Station 01		178d	21-Jul-26 A	12-Apr-27	283d	0	900,406	1,857,890
Engineering		18d	27-Oct-26	16-Nov-26	327d	0	0	0
JDH3-02-009-Method of Statement for Lift Stations		18d	27-Oct-26	16-Nov-26	327d	0	0	0
JDH3-02-009-Pumps		18d	27-Oct-26	16-Nov-26	323d	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7d	27-Oct-26	03-Nov-26	324d	0	0	0
JDI	Review & approval MS for Pumps- MS	9d	04-Nov-26	16-Nov-26	268d	0	0	0
JDH3-02-009-Duct Works		18d	27-Oct-26	16-Nov-26	238d	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7d	27-Oct-26	03-Nov-26	238d	0	0	0
JDI	Review & approval MS for Duct Works- MS	9d	04-Nov-26	16-Nov-26	197d	0	0	0
JDH3-02-009-Drainage System		18d	27-Oct-26	16-Nov-26	294d	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7d	27-Oct-26	03-Nov-26	295d	0	0	0
JDI	Review & approval MS for Drainage System- MS	9d	04-Nov-26	16-Nov-26	244d	0	0	0
JDH3-02-009-Data Communication		18d	27-Oct-26	16-Nov-26	282d	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7d	27-Oct-26	03-Nov-26	283d	0	0	0
JDI	Review & approval MS for Data Communication- MS	9d	04-Nov-26	16-Nov-26	234d	0	0	0
JDH3-02-009-Programing Logical Control System		18d	27-Oct-26	16-Nov-26	327d	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7d	27-Oct-26	03-Nov-26	327d	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9d	04-Nov-26	16-Nov-26	271d	0	0	0

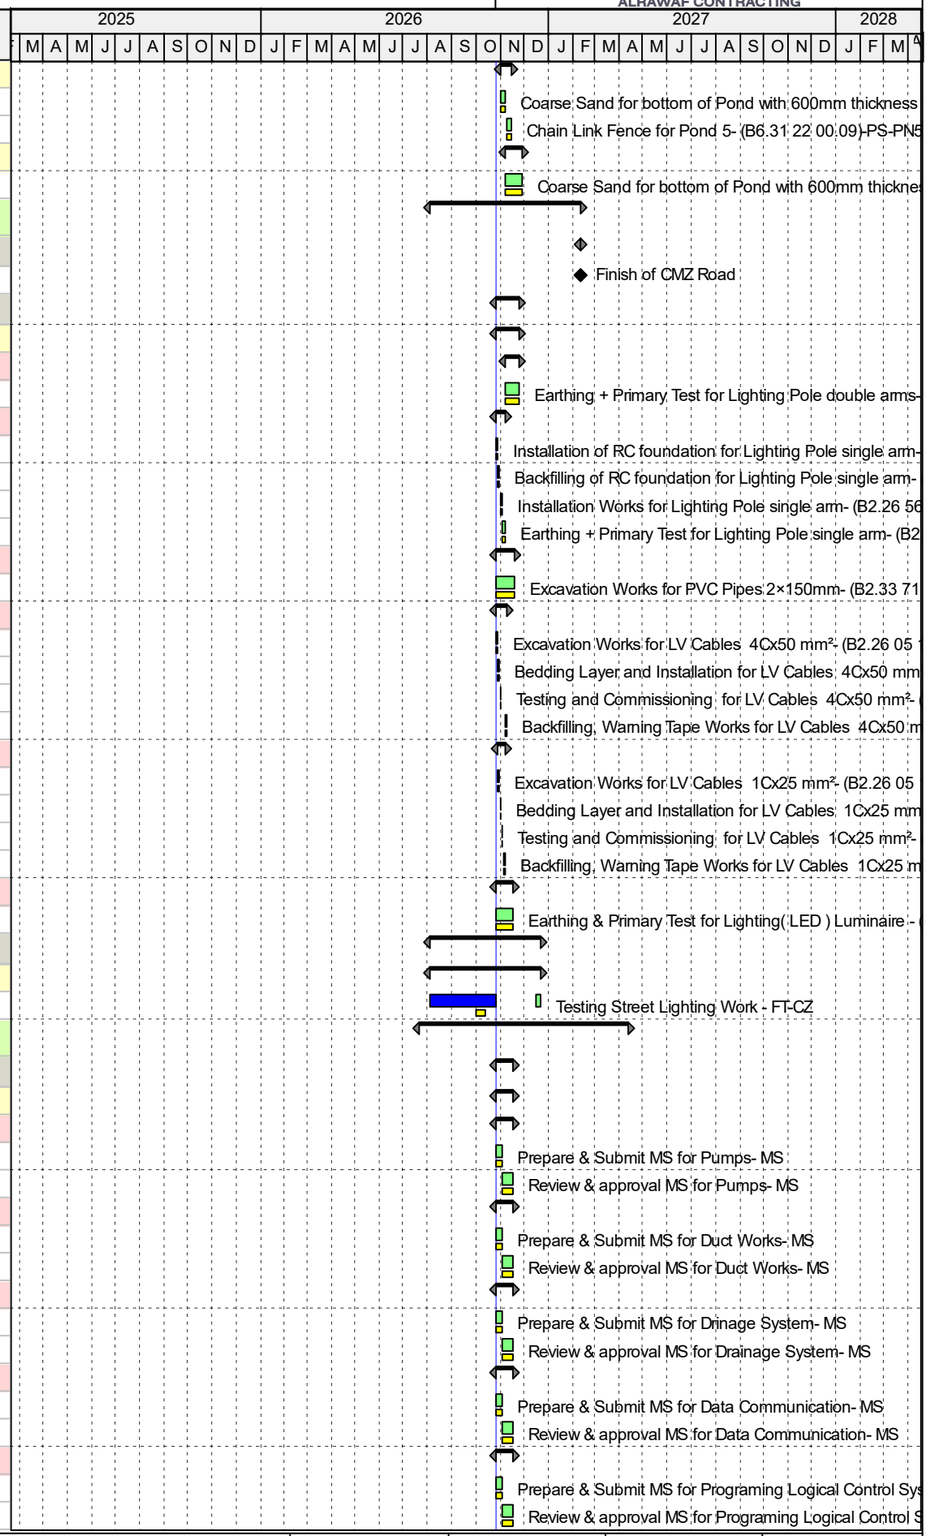


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Procurement	140d	04-Aug-26 A	12-Apr-27	283d	0	116,640	324,001
	Long Lead Items	140d	27-Oct-26	12-Apr-27	283d	0	0	64,800
	Purchase Order - PO - Lift Station	21d	27-Oct-26	19-Nov-26	347d	0	0	0
	JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR	21d	27-Oct-26	19-Nov-26	347d	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	21d	27-Oct-26	19-Nov-26	347d	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	21d	27-Oct-26	19-Nov-26	347d	0	0	0
	JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC	21d	27-Oct-26	19-Nov-26	325d	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	21d	27-Oct-26	19-Nov-26	325d	0	0	0
	Material Purchase Order for Data Communication System - LL-T	21d	27-Oct-26	19-Nov-26	325d	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	21d	27-Oct-26	19-Nov-26	301d	0	0	0
	Fabrication - FAB - Lift Station	168d	27-Oct-26	12-Apr-27	342d	0	0	0
	JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC	168d	27-Oct-26	12-Apr-27	342d	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	168d	27-Oct-26	12-Apr-27	288d	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	353d	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	168d	27-Oct-26	12-Apr-27	288d	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	323d	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	140d	27-Oct-26	15-Mar-27	297d	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	398d	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	84d	27-Oct-26	18-Jan-27	346d	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	84d	27-Oct-26	18-Jan-27	361d	0	0	0
	JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL	140d	27-Oct-26	15-Mar-27	370d	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	84d	27-Oct-26	18-Jan-27	380d	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	112d	27-Oct-26	15-Feb-27	362d	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	140d	27-Oct-26	15-Mar-27	370d	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL	84d	27-Oct-26	18-Jan-27	360d	0	0	0
	Delivery and staging on Site - DOS- Lift Station	10d	27-Oct-26	05-Nov-26	486d	0	0	64,800
	JDH3-02-009-LOL-DOS-LFT-AR-Architechture -AR	10d	27-Oct-26	05-Nov-26	486d	0	0	64,800
	Delivery for Steel Gates - LL-AR-DOS	10d	27-Oct-26	05-Nov-26	486d	0	0	64,800
	Short Lead Items	68d	04-Aug-26 A	17-Nov-26	404d	0	116,640	259,201
	Purchase Order - PO - Lift Station	10d	27-Oct-26	07-Nov-26	413d	0	0	0
	JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR	10d	27-Oct-26	07-Nov-26	403d	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	10d	27-Oct-26	07-Nov-26	346d	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	10d	27-Oct-26	07-Nov-26	236d	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	10d	27-Oct-26	07-Nov-26	403d	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	10d	27-Oct-26	07-Nov-26	232d	0	0	0
	Material Purchase Order for Interlocking concrete paving - SH-A	10d	27-Oct-26	07-Nov-26	236d	0	0	0
	JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC	10d	27-Oct-26	07-Nov-26	385d	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	10d	27-Oct-26	07-Nov-26	254d	0	0	0
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	10d	27-Oct-26	07-Nov-26	385d	0	0	0
	Material Purchase Order for Exhaust Fans - SH-MC-PO	10d	27-Oct-26	07-Nov-26	385d	0	0	0
	JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL	10d	27-Oct-26	07-Nov-26	413d	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	10d	27-Oct-26	07-Nov-26	413d	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	10d	27-Oct-26	07-Nov-26	413d	0	0	0
	Delivery and staging on Site - DOS- Lift Station	67d	04-Aug-26 A	17-Nov-26	486d	0	116,640	259,201
	JDH3-02-009-SHL-DOS-LFT-AR-Architechture -AR	10d	08-Nov-26	17-Nov-26	486d	0	0	64,800
	Delivery for Traffic signs - SH-AR-DOS	10d	08-Nov-26	17-Nov-26	486d	0	0	64,800
	JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC	10d	04-Aug-26 A	07-Nov-26	459d	0	116,640	194,401
	Delivery for Wall mounted Split Units - SH-MC-DOS	10d	04-Aug-26 A	07-Nov-26	459d	0	32,400	64,800
	Delivery for Exhaust Fans - SH-MC-DOS	10d	04-Aug-26 A	07-Nov-26	459d	0	32,400	64,800
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	10d	04-Aug-26 A	29-Oct-26	382d	0	51,840	64,800
	Construction	71d	21-Jul-26 A	16-Nov-26	387d	0	783,766	1,533,889
	FORCE MAIN	71d	21-Jul-26 A	03-Nov-26	399d	0	774,397	1,061,371

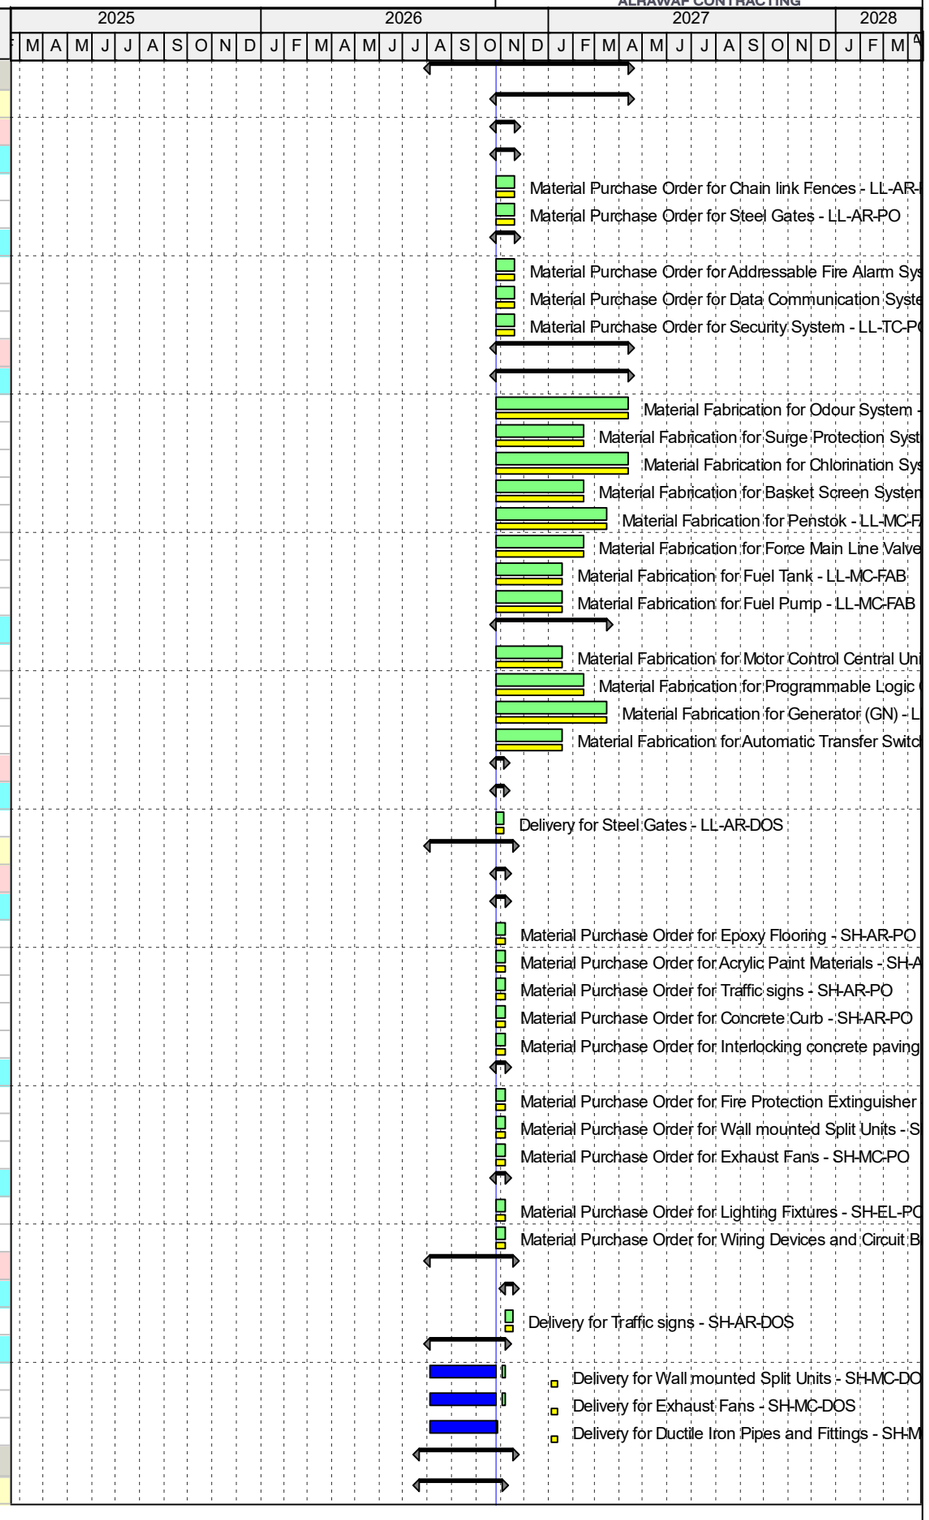


Actual Level of Effort
Actual Work
Remaining Work
Primary Baseline
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-BQ4-Pipes and Valves	71d	21-Jul-26 A	03-Nov-26	399d	0	774,397	1,061,371
	JDH3-02-009-BQ4-HDPE Pipes-450 mm diameter depth from 2.5 to	71d	21-Jul-26 A	27-Oct-26	376d	0	774,397	790,201
	Installing for HDPE Pipe Line 450 mm - depth from 2.5 to 3.5 m	17d	23-Jul-26 A	27-Oct-26	376d	0	425,918	434,611
	Excavation Works for HDPE Pipe Line 450 mm - depth from 2.5	9d	21-Jul-26 A	27-Oct-26	376d	0	154,879	158,040
	Soil Replacement and Bedding Works for HDPE Pipe Line 450	11d	22-Jul-26 A	27-Oct-26	376d	0	38,720	39,510
	Primary Test for HDPE Pipe Line 450 mm - depth from 2.5 to 3.	17d	28-Jul-26 A	27-Oct-26	376d	0	77,440	79,020
	Backfilling and warning tape Works for HDPE Pipe Line 450 mm	17d	25-Jul-26 A	27-Oct-26	376d	0	77,440	79,020
	JDH3-02-009-BQ4-Butterfly Valve-400 mm	6d	27-Oct-26	03-Nov-26	399d	0	0	271,170
	Installation for Butterfly Valve 400 mm on pipe dia 450 mm- (J8	3d	27-Oct-26	31-Oct-26	399d	0	0	244,053
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 450	3d	31-Oct-26	03-Nov-26	399d	0	0	27,117
	SEWERAGE PUMP STATION	24d	18-Oct-26 A	12-Nov-26	384d	0	9,369	467,613
	JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber	16d	18-Oct-26 A	02-Nov-26	315d	0	9,369	29,981
	JDH3-02-009-BQ4-Valve chamber	16d	18-Oct-26 A	02-Nov-26	315d	0	9,369	29,981
	Steel Fixing for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2d	18-Oct-26 A	28-Oct-26	315d	0	9,369	18,738
	RC Casting for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2d	29-Oct-26	31-Oct-26	315d	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2d	01-Nov-26	02-Nov-26	315d	0	0	3,748
	JDH3-02-009-BQ4-Sewerage Pumps & MCC	14d	27-Oct-26	11-Nov-26	313d	0	0	396,985
	JDH3-02-009-BQ4-Plinth for Odour Control System	8d	27-Oct-26	04-Nov-26	313d	0	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS1-BQ4-D03	2d	27-Oct-26	28-Oct-26	313d	0	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS1-BQ4-D03	2d	29-Oct-26	31-Oct-26	313d	0	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS1-BQ4-D03	2d	01-Nov-26	02-Nov-26	313d	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS1-BQ4-D03	2d	03-Nov-26	04-Nov-26	313d	0	0	2,710
	JDH3-02-009-BQ4-Valves and Fittings for Submersible Pumps	6d	05-Nov-26	11-Nov-26	313d	0	0	369,885
	Gate valves for Pump station - (J899.1)-LFTS1-BQ4-D15	3d	05-Nov-26	08-Nov-26	313d	0	0	199,169
	Non return valves for Pump station - (J899.2)-LFTS1-BQ4-D15	3d	09-Nov-26	11-Nov-26	313d	0	0	170,716
	JDH3-02-009-BQ4-Pump Lifting System	14d	27-Oct-26	12-Nov-26	384d	0	0	40,647
	JDH3-02-009-BQ4-Surge protection system	14d	27-Oct-26	12-Nov-26	384d	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS1-BQ4-D15	14d	27-Oct-26	12-Nov-26	384d	0	0	40,647
	MOTOR CONTROL CENTRE BUILDING	18d	27-Oct-26	16-Nov-26	313d	0	0	4,905
	JDH3-02-009-BQ4-Sub Structure	18d	27-Oct-26	16-Nov-26	313d	0	0	4,905
	JDH3-02-009-BQ4-Foundation	18d	27-Oct-26	16-Nov-26	313d	0	0	4,905
	Steel Fixing Foundation - (F623)-LFTS1-BQ4-D03	2d	27-Oct-26	28-Oct-26	325d	0	0	3,066
	RC Casting Foundation - (F623)-LFTS1-BQ4-D03	2d	12-Nov-26	14-Nov-26	313d	0	0	1,226
	Deshuttering Foundation - (F623)-LFTS1-BQ4-D03	2d	15-Nov-26	16-Nov-26	313d	0	0	613
	Close Out	24d	27-Oct-26	24-Nov-26	399d	0	0	0
	As Built Drawing Submittals - SUB-Lift Station - LFTS	23d	27-Oct-26	22-Nov-26	389d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	01-Nov-26	08-Nov-26	401d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST	19d	01-Nov-26	22-Nov-26	389d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for Trench Shopdrawingsfor SUB-/	7d	15-Nov-26	22-Nov-26	389d	0	0	0
JDI	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -Foundation Shop D	7d	15-Nov-26	22-Nov-26	389d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Infra - IN	13d	27-Oct-26	11-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Force Main Master Layout (forc	7d	27-Oct-26	04-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsIsolation Val	7d	03-Nov-26	11-Nov-26	399d	0	0	0
	As Built Drawing Approvals - APP-Lift Station - LFTS	14d	04-Nov-26	24-Nov-26	331d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9d	09-Nov-26	19-Nov-26	333d	0	0	0

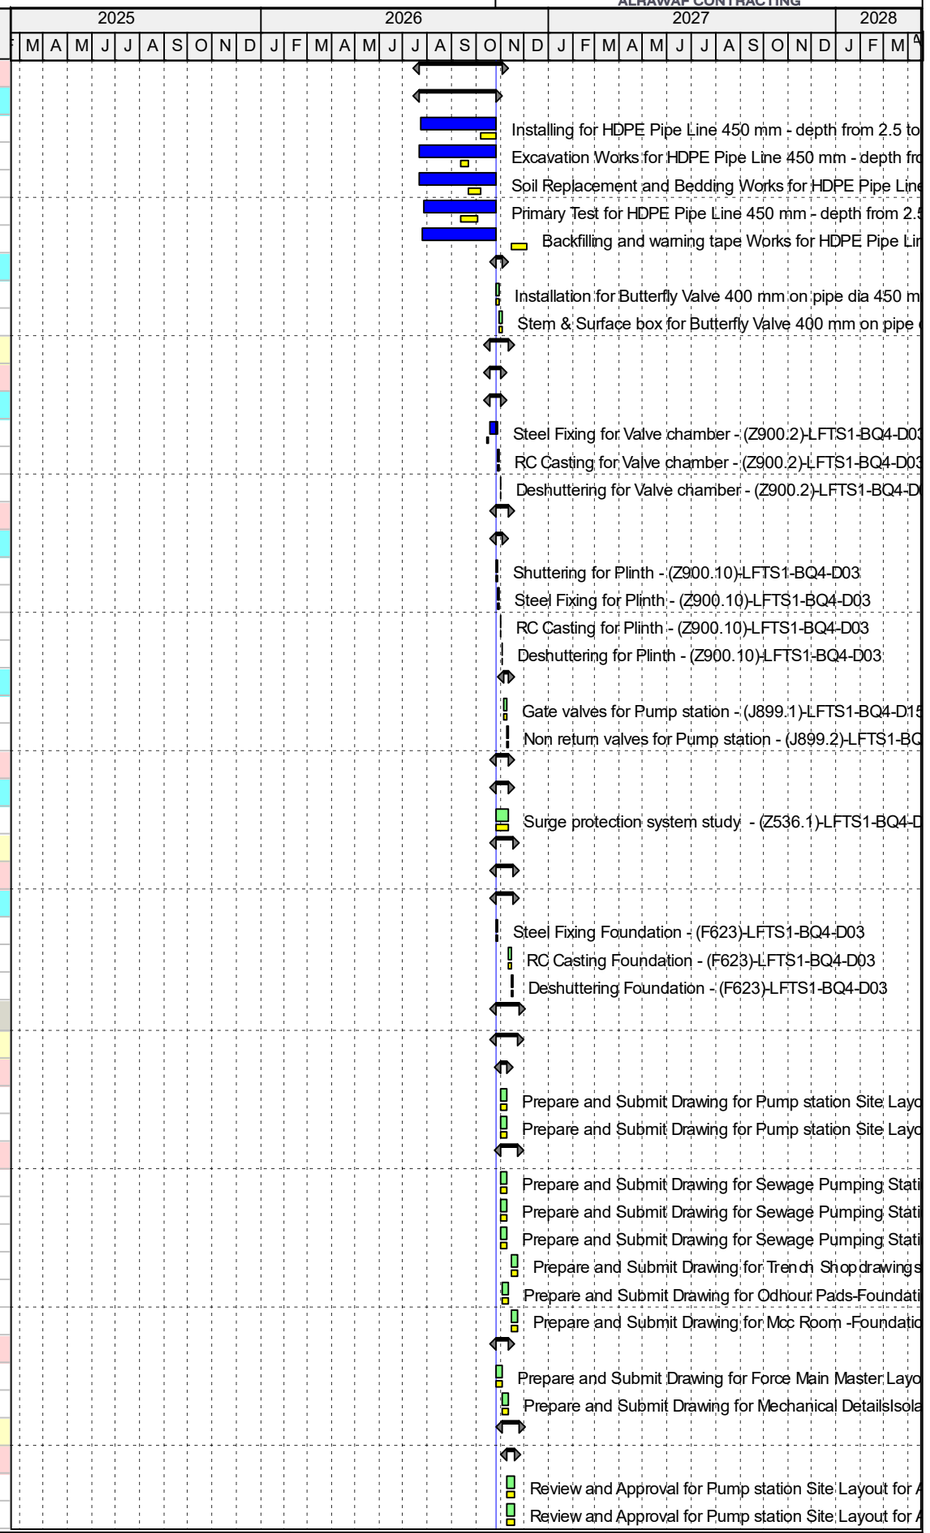


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST	11d	09-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Foun	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Walls	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for Odhour Pads-Foundation Shop Drawin	9d	11-Nov-26	23-Nov-26	331d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Infra - IN	14d	04-Nov-26	24-Nov-26	331d	0	0	0
JDI	Review and Approval for Force Main Master Layout (force Main-	9d	04-Nov-26	17-Nov-26	336d	0	0	0
JDI	Review and Approval for Mechanical DetailsIsolation Valve Char	9d	11-Nov-26	24-Nov-26	331d	0	0	0
JDH3-02-009-Lift Station 02		223d	14-Jul-26 A	12-Apr-27	283d	0	229,990	641,649
Procurement		140d	04-Aug-26 A	12-Apr-27	283d	0	119,790	352,322
Long Lead Items		140d	27-Oct-26	12-Apr-27	283d	0	0	0
Purchase Order - PO - Lift Station		10d	27-Oct-26	07-Nov-26	271d	0	0	0
JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR		10d	27-Oct-26	07-Nov-26	271d	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	10d	27-Oct-26	07-Nov-26	264d	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	10d	27-Oct-26	07-Nov-26	271d	0	0	0
JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC		10d	27-Oct-26	07-Nov-26	269d	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	10d	27-Oct-26	07-Nov-26	269d	0	0	0
	Material Purchase Order for Data Communication System - LL-T	10d	27-Oct-26	07-Nov-26	269d	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	10d	27-Oct-26	07-Nov-26	246d	0	0	0
Fabrication - FAB - Lift Station		168d	27-Oct-26	12-Apr-27	342d	0	0	0
JDH3-02-009-LOL-MAN-LFT-AR-Architechture -AR		70d	08-Nov-26	16-Jan-27	326d	0	0	0
	Material Fabrication for Chain link Fences - LL-AR-FAB	70d	08-Nov-26	16-Jan-27	317d	0	0	0
	Material Fabrication for Steel Gates - LL-AR-FAB	70d	08-Nov-26	16-Jan-27	326d	0	0	0
JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC		168d	27-Oct-26	12-Apr-27	342d	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	168d	27-Oct-26	12-Apr-27	191d	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	257d	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	168d	27-Oct-26	12-Apr-27	191d	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	226d	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	140d	27-Oct-26	15-Mar-27	205d	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	112d	27-Oct-26	15-Feb-27	398d	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	84d	27-Oct-26	18-Jan-27	298d	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	84d	27-Oct-26	18-Jan-27	310d	0	0	0
JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL		140d	27-Oct-26	15-Mar-27	370d	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	84d	27-Oct-26	18-Jan-27	306d	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	112d	27-Oct-26	15-Feb-27	287d	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	140d	27-Oct-26	15-Mar-27	370d	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL-	84d	27-Oct-26	18-Jan-27	309d	0	0	0
JDH3-02-009-LOL-MAN-LFT-TC-Telecommunications Network - TC		112d	08-Nov-26	27-Feb-27	296d	0	0	0
	Material Fabrication for Addressable Fire Alarm System - LL-TC-	84d	08-Nov-26	30-Jan-27	324d	0	0	0
	Material Fabrication for Data Communication System - LL-TC-FA	84d	08-Nov-26	30-Jan-27	324d	0	0	0
	Material Fabrication for Security System - LL-TC-FAB	112d	08-Nov-26	27-Feb-27	296d	0	0	0
Short Lead Items		44d	04-Aug-26 A	20-Jan-27	349d	0	119,790	352,322
Purchase Order - PO - Lift Station		14d	27-Oct-26	11-Nov-26	409d	0	0	0
JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR		14d	27-Oct-26	11-Nov-26	397d	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	14d	27-Oct-26	11-Nov-26	397d	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	14d	27-Oct-26	11-Nov-26	155d	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	14d	27-Oct-26	11-Nov-26	166d	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	14d	27-Oct-26	11-Nov-26	178d	0	0	0
	Material Purchase Order for Interlocking concrete paving - SH-A	14d	27-Oct-26	11-Nov-26	190d	0	0	0
JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC		14d	27-Oct-26	11-Nov-26	214d	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	14d	27-Oct-26	11-Nov-26	202d	0	0	0
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	14d	27-Oct-26	11-Nov-26	214d	0	0	0

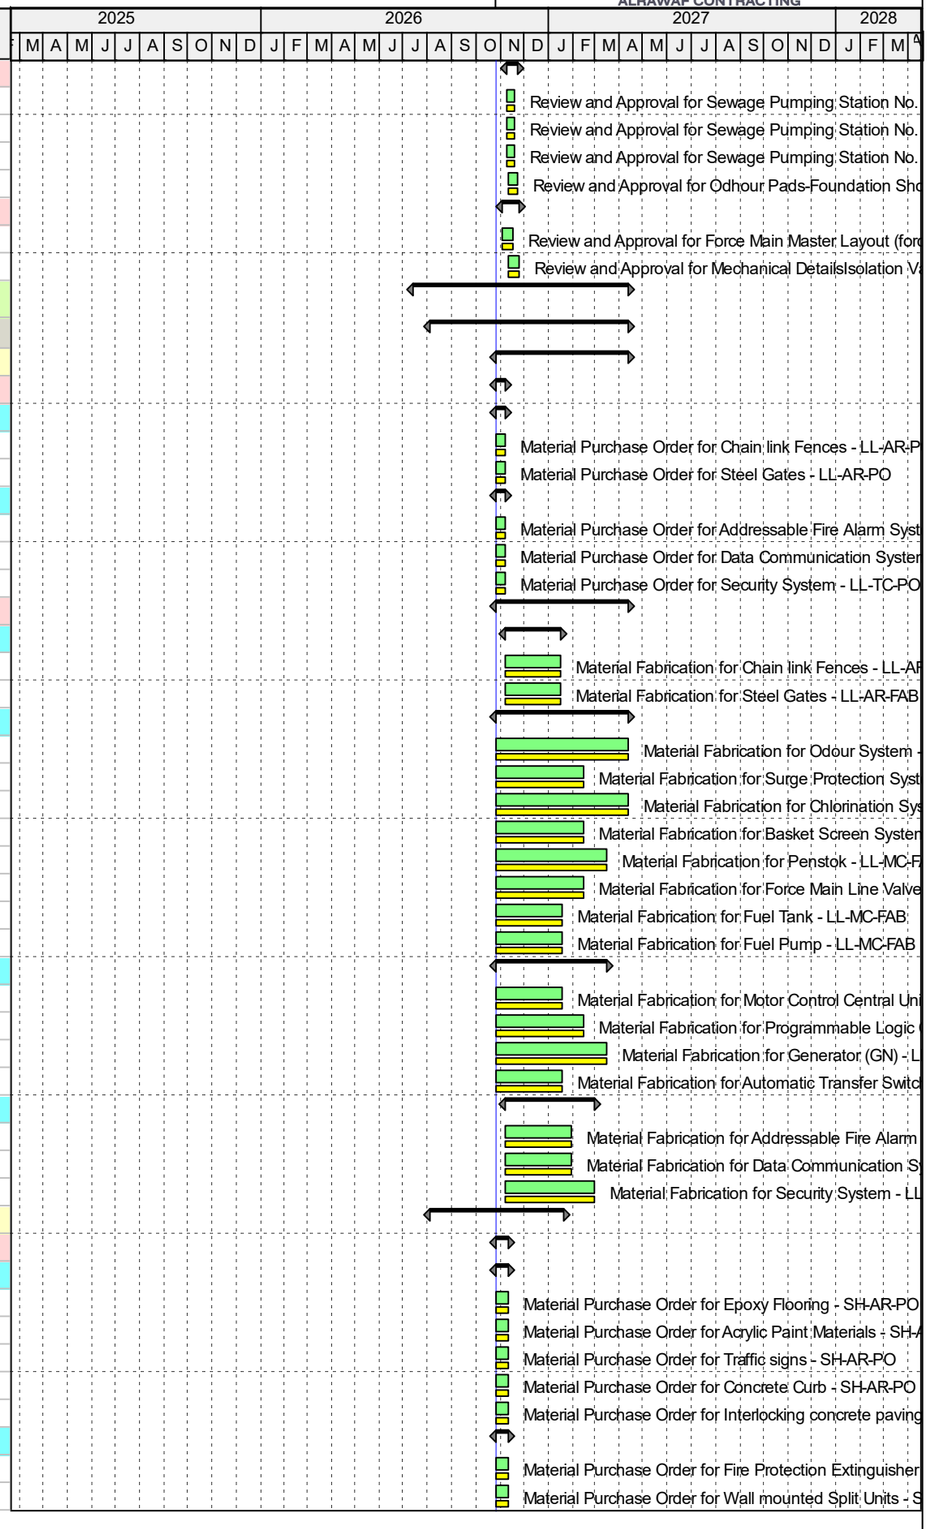


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Material Purchase Order for Exhaust Fans - SH-MC-PO	14d	27-Oct-26	11-Nov-26	214d	0	0	0
	JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Delivery and staging on Site - DOS- Lift Station	51d	04-Aug-26 A	20-Jan-27	424d	0	119,790	352,322
	JDH3-02-009-SHL-DOS-LFT-AR-Architechture -AR	14d	12-Nov-26	25-Nov-26	189d	0	0	70,464
	Delivery for Acrylic Paint Materials - SH-AR-DOS	14d	12-Nov-26	25-Nov-26	189d	0	0	70,464
	JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC	42d	04-Aug-26 A	20-Jan-27	189d	0	119,790	211,393
	Delivery for Wall mounted Split Units - SH-MC-DOS	14d	04-Aug-26 A	20-Jan-27	189d	0	35,232	70,464
	Delivery for Exhaust Fans - SH-MC-DOS	14d	04-Aug-26 A	20-Jan-27	189d	0	35,232	70,464
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	14d	04-Aug-26 A	20-Jan-27	189d	0	49,325	70,464
	JDH3-02-009-SHL-DOS-LFT-EL-Electrical Network - EL	14d	27-Oct-26	09-Nov-26	496d	0	0	70,464
	Delivery for Panel Boards - SH-EL-DOS	14d	27-Oct-26	09-Nov-26	496d	0	0	70,464
Construction		96d	14-Jul-26 A	10-Nov-26	410d	0	110,200	289,327
FORCE MAIN		13d	14-Jul-26 A	31-Oct-26	405d	0	110,200	157,429
JDH3-02-009-BQ4-Pipes and Valves		13d	14-Jul-26 A	31-Oct-26	405d	0	110,200	157,429
JDH3-02-009-BQ4-HDPE Pipes-450 mm diameter depth from 1.5 to		13d	14-Jul-26 A	31-Oct-26	405d	0	110,200	157,429
	Primary Test for HDPE Pipe Line 450 mm - depth from 1.5 to 2.	13d	14-Jul-26 A	31-Oct-26	405d	0	110,200	157,429
SEWERAGE PUMP STATION		13d	27-Oct-26	10-Nov-26	408d	0	0	105,224
JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber		8d	27-Oct-26	04-Nov-26	220d	0	0	37,476
JDH3-02-009-BQ4-Valve chamber		8d	27-Oct-26	04-Nov-26	220d	0	0	37,476
	Shuttering for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2d	27-Oct-26	28-Oct-26	220d	0	0	7,495
	Steel Fixing for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2d	29-Oct-26	31-Oct-26	220d	0	0	18,738
	RC Casting for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2d	01-Nov-26	02-Nov-26	220d	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2d	03-Nov-26	04-Nov-26	220d	0	0	3,748
JDH3-02-009-BQ4-Sewerage Pumps & MCC		13d	27-Oct-26	10-Nov-26	215d	0	0	27,101
JDH3-02-009-BQ4-Plinth for Odour Control System		13d	27-Oct-26	10-Nov-26	215d	0	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS2-BQ4-D03	3d	27-Oct-26	29-Oct-26	215d	0	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS2-BQ4-D03	6d	31-Oct-26	05-Nov-26	215d	0	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS2-BQ4-D03	2d	07-Nov-26	08-Nov-26	215d	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS2-BQ4-D03	2d	09-Nov-26	10-Nov-26	215d	0	0	2,710
JDH3-02-009-BQ4-Pump Lifting System		2d	27-Oct-26	28-Oct-26	419d	0	0	40,647
JDH3-02-009-BQ4-Surge protection system		2d	27-Oct-26	28-Oct-26	419d	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS2-BQ4-D15	2d	27-Oct-26	28-Oct-26	419d	0	0	40,647
MOTOR CONTROL CENTRE BUILDING		4d	27-Oct-26	31-Oct-26	244d	0	0	4,292
JDH3-02-009-BQ4-Sub Structure		4d	27-Oct-26	31-Oct-26	244d	0	0	4,292
JDH3-02-009-BQ4-Foundation		4d	27-Oct-26	31-Oct-26	244d	0	0	4,292
	Shuttering Foundation - (F623)-LFTS2-BQ4-D03	2d	27-Oct-26	28-Oct-26	244d	0	0	1,226
	Steel Fixing Foundation - (F623)-LFTS2-BQ4-D03	2d	29-Oct-26	31-Oct-26	244d	0	0	3,066
Site Works		2d	29-Oct-26	31-Oct-26	419d	0	0	22,383
JDH3-02-009-BQ4-Site Works		2d	29-Oct-26	31-Oct-26	419d	0	0	22,383
JDH3-02-009-BQ4-Earth work		2d	29-Oct-26	31-Oct-26	419d	0	0	22,383
	Excavation Works - (20301-1)-LFTS2-BQ4-D02	2d	29-Oct-26	31-Oct-26	419d	0	0	22,383
Close Out		18d	03-Nov-26	23-Nov-26	399d	0	0	0
As Built Drawing Submittals - SUB-Lift Station - LFTS		12d	03-Nov-26	16-Nov-26	394d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR		7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		12d	03-Nov-26	16-Nov-26	394d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7d	03-Nov-26	10-Nov-26	399d	0	0	0

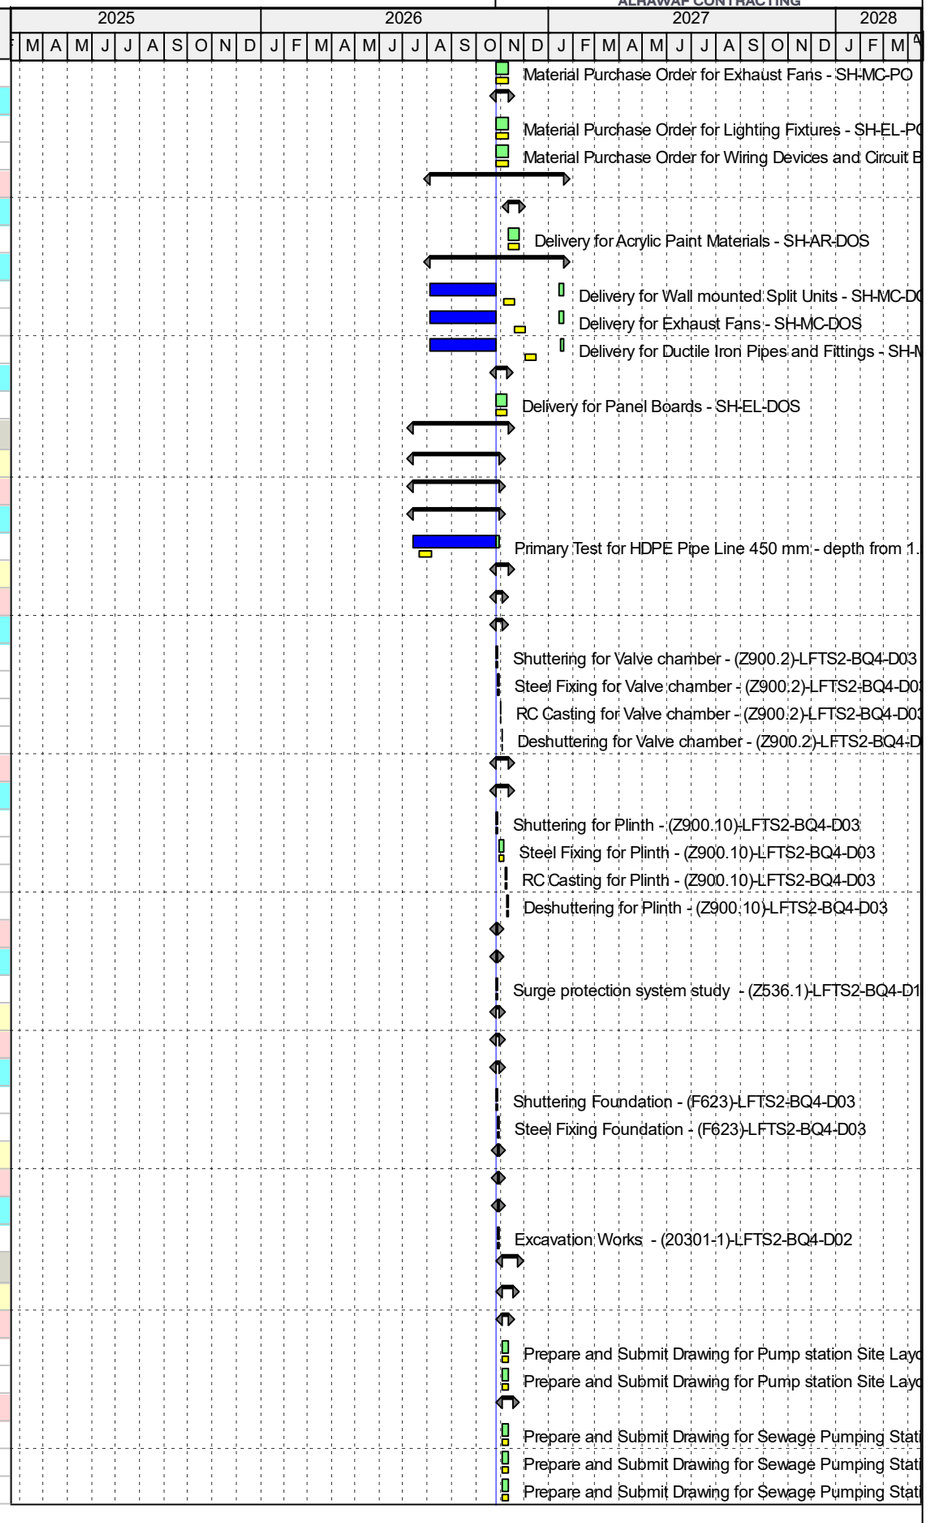

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7d	09-Nov-26	16-Nov-26	394d	0	0	0
	As Built Drawing Approvals - APP-Lift Station -LFTS	9d	11-Nov-26	23-Nov-26	331d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH	Review and Approval for Pump station Site Layout for APP-AS-I	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH	Review and Approval for Pump station Site Layout for APP-AS-I	9d	11-Nov-26	23-Nov-26	331d	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH	Review and Approval for Sewage Pumping Station No. 2 -Found	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH	Review and Approval for Sewage Pumping Station No. 2 -Walls	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH3-02-009-Lift Station 03		63d	04-Aug-26 A	19-Feb-27	324d	18,970	72,569	483,998
Procurement		63d	04-Aug-26 A	19-Feb-27	324d	0	70,570	249,072
Long Lead Items		51d	27-Oct-26	25-Dec-26	372d	0	0	41,512
Purchase Order - PO - Lift Station		14d	27-Oct-26	11-Nov-26	325d	0	0	0
JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR		14d	27-Oct-26	11-Nov-26	315d	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	14d	27-Oct-26	11-Nov-26	307d	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	14d	27-Oct-26	11-Nov-26	315d	0	0	0
JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC		14d	27-Oct-26	11-Nov-26	325d	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	14d	27-Oct-26	11-Nov-26	301d	0	0	0
	Material Purchase Order for Data Communication System - LL-T	14d	27-Oct-26	11-Nov-26	313d	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	14d	27-Oct-26	11-Nov-26	325d	0	0	0
Fabrication - FAB - Lift Station		60d	27-Oct-26	25-Dec-26	450d	0	0	0
JDH3-02-009-LOL-MAN-LFT-AR-Architechture -AR		14d	12-Nov-26	25-Nov-26	378d	0	0	0
	Material Fabrication for Chain link Fences - LL-AR-FAB	14d	12-Nov-26	25-Nov-26	369d	0	0	0
	Material Fabrication for Steel Gates - LL-AR-FAB	14d	12-Nov-26	25-Nov-26	378d	0	0	0
JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC		60d	27-Oct-26	25-Dec-26	450d	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	60d	27-Oct-26	25-Dec-26	332d	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	60d	27-Oct-26	25-Dec-26	327d	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	60d	27-Oct-26	25-Dec-26	341d	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	14d	27-Oct-26	09-Nov-26	401d	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	14d	27-Oct-26	09-Nov-26	415d	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	60d	27-Oct-26	25-Dec-26	450d	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	60d	27-Oct-26	25-Dec-26	297d	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	14d	27-Oct-26	09-Nov-26	357d	0	0	0
JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL		14d	27-Oct-26	09-Nov-26	496d	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	14d	27-Oct-26	09-Nov-26	371d	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	14d	27-Oct-26	09-Nov-26	385d	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	14d	27-Oct-26	09-Nov-26	496d	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL-	14d	27-Oct-26	09-Nov-26	364d	0	0	0
JDH3-02-009-LOL-MAN-LFT-TC-Telecommunications Network - TC		14d	12-Nov-26	25-Nov-26	390d	0	0	0
	Material Fabrication for Addressable Fire Alarm System - LL-TC-	14d	12-Nov-26	25-Nov-26	362d	0	0	0
	Material Fabrication for Data Communication System - LL-TC-FA	14d	12-Nov-26	25-Nov-26	376d	0	0	0
	Material Fabrication for Security System - LL-TC-FAB	14d	12-Nov-26	25-Nov-26	390d	0	0	0
Delivery and staging on Site - DOS- Lift Station		14d	10-Nov-26	23-Nov-26	364d	0	0	41,512
JDH3-02-009-LOL-DOS-LFT-EL-Electrical Network - EL		14d	10-Nov-26	23-Nov-26	364d	0	0	41,512
	Delivery for Automatic Transfer Switch (ATS) - LL-EL-DOS	14d	10-Nov-26	23-Nov-26	364d	0	0	41,512
Short Lead Items		63d	04-Aug-26 A	19-Feb-27	324d	0	70,570	207,560
Purchase Order - PO - Lift Station		14d	27-Oct-26	11-Nov-26	409d	0	0	0
JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR		14d	27-Oct-26	11-Nov-26	373d	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	14d	27-Oct-26	11-Nov-26	325d	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	14d	27-Oct-26	11-Nov-26	337d	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	14d	27-Oct-26	11-Nov-26	349d	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	14d	27-Oct-26	11-Nov-26	361d	0	0	0

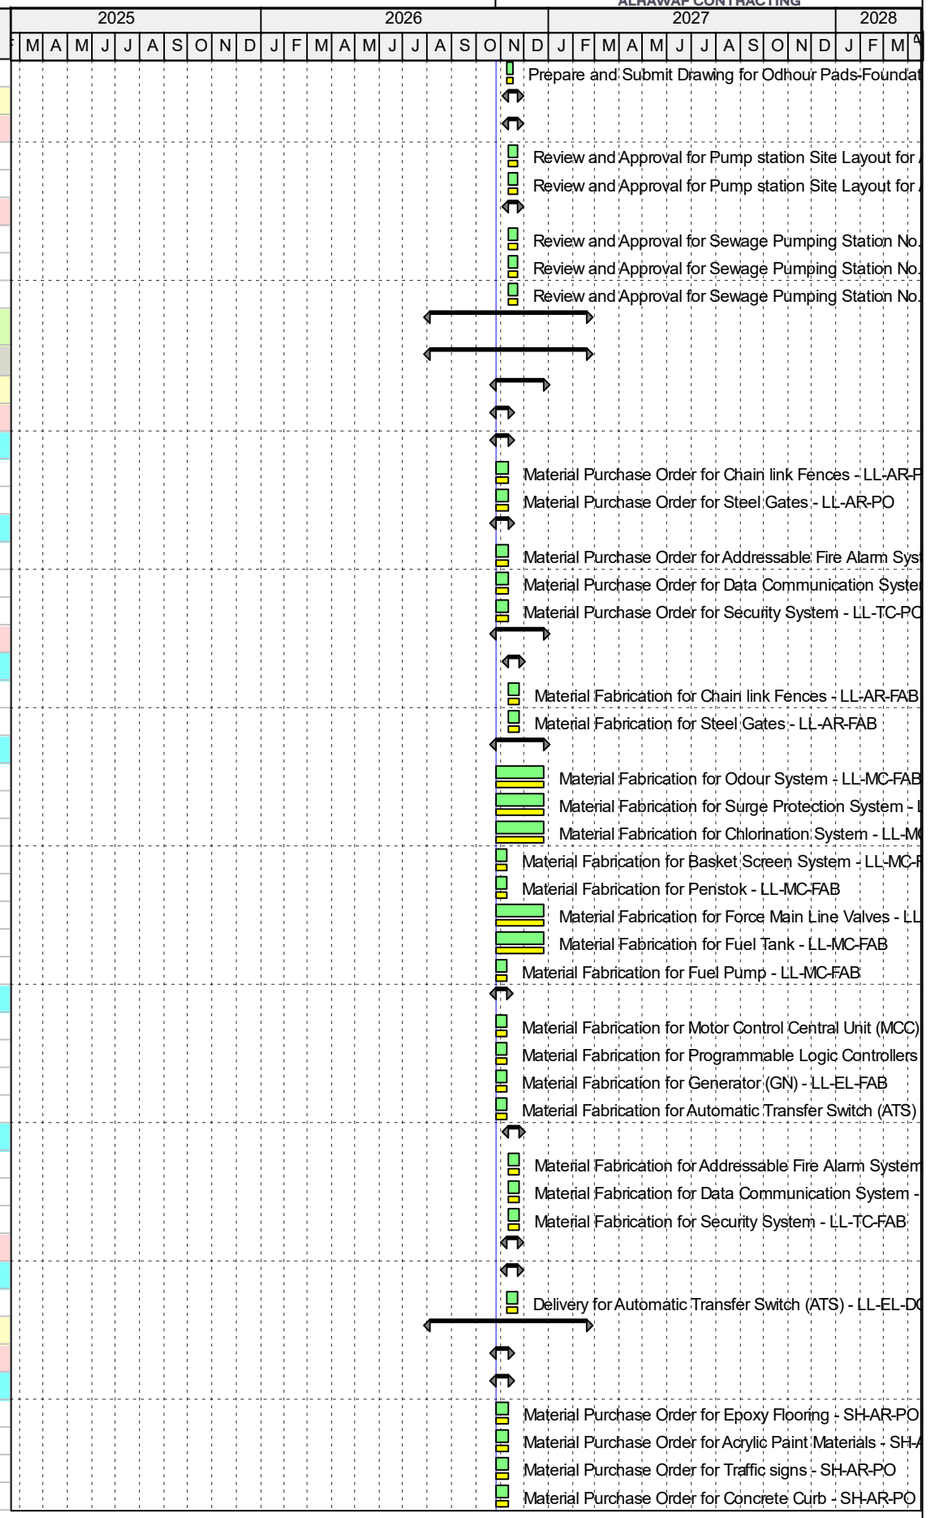

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Material Purchase Order for Interlocking concrete paving - SH-A	14d	27-Oct-26	11-Nov-26	373d	0	0	0
	JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC	14d	27-Oct-26	11-Nov-26	371d	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	14d	27-Oct-26	11-Nov-26	359d	0	0	0
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	14d	27-Oct-26	11-Nov-26	371d	0	0	0
	Material Purchase Order for Exhaust Fans - SH-MC-PO	14d	27-Oct-26	11-Nov-26	371d	0	0	0
	JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	14d	27-Oct-26	11-Nov-26	409d	0	0	0
	Delivery and staging on Site - DOS- Lift Station	74d	04-Aug-26 A	19-Feb-27	394d	0	70,570	207,560
	JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC	74d	04-Aug-26 A	19-Feb-27	344d	0	70,570	166,048
	Delivery for Pump Lifting Mechanism - SH-MC-DOS	14d	27-Oct-26	09-Nov-26	429d	0	0	41,512
	Delivery for Wall mounted Split Units - SH-MC-DOS	14d	04-Aug-26 A	19-Feb-27	344d	0	20,756	41,512
	Delivery for Exhaust Fans - SH-MC-DOS	14d	04-Aug-26 A	19-Feb-27	344d	0	20,756	41,512
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	14d	04-Aug-26 A	19-Feb-27	344d	0	29,058	41,512
	JDH3-02-009-SHL-DOS-LFT-EL-Electrical Network - EL	14d	27-Oct-26	09-Nov-26	496d	0	0	41,512
	Delivery for Panel Boards - SH-EL-DOS	14d	27-Oct-26	09-Nov-26	496d	0	0	41,512
Construction		31d	27-Sep-26 A	01-Dec-26	363d	18,970	1,998	234,926
Site Work and Service Road		2d	16-Nov-26	17-Nov-26	375d	0	0	5,063
JDH3-02-009-BQ4-Roads Work		2d	16-Nov-26	17-Nov-26	375d	0	0	5,063
JDH3-02-009-BQ4-Roads		2d	16-Nov-26	17-Nov-26	375d	0	0	5,063
	300mm thick Subgrade - (R116)-LFTS3-BQ4-D02	2d	16-Nov-26	17-Nov-26	375d	0	0	5,063
SEWERAGE PUMP STATION		21d	27-Oct-26	19-Nov-26	370d	18,970	0	126,766
JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber		8d	27-Oct-26	04-Nov-26	377d	0	0	37,476
JDH3-02-009-BQ4-Valve chamber		8d	27-Oct-26	04-Nov-26	377d	0	0	37,476
	Shuttering for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2d	27-Oct-26	28-Oct-26	367d	0	0	7,495
	Steel Fixing for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2d	29-Oct-26	31-Oct-26	367d	0	0	18,738
	RC Casting for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2d	01-Nov-26	02-Nov-26	377d	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2d	03-Nov-26	04-Nov-26	377d	0	0	3,748
JDH3-02-009-BQ4-Sewerage Pumps & MCC		13d	27-Oct-26	10-Nov-26	370d	18,970	0	27,101
JDH3-02-009-BQ4-Plinth for Odour Control System		13d	27-Oct-26	10-Nov-26	370d	18,970	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS3-BQ4-D03	3d	27-Oct-26	29-Oct-26	370d	5,420	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS3-BQ4-D03	6d	31-Oct-26	05-Nov-26	370d	13,550	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS3-BQ4-D03	2d	07-Nov-26	08-Nov-26	370d	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS3-BQ4-D03	2d	09-Nov-26	10-Nov-26	370d	0	0	2,710
JDH3-02-009-BQ4-Pump Lifting System		21d	27-Oct-26	19-Nov-26	370d	0	0	62,189
JDH3-02-009-BQ4-Surge protection system		2d	27-Oct-26	28-Oct-26	389d	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS3-BQ4-D15	2d	27-Oct-26	28-Oct-26	389d	0	0	40,647
JDH3-02-009-BQ4-Underground Ducts and Raceways for Electrica		4d	16-Nov-26	19-Nov-26	277d	0	0	21,543
	Electrical Hand Hole 600 x 600 mm - (K151.1)-LFTS3-BQ4-D16	4d	16-Nov-26	19-Nov-26	277d	0	0	21,543
MOTOR CONTROL CENTRE BUILDING		30d	27-Sep-26 A	01-Dec-26	271d	0	1,998	101,002
JDH3-02-009-BQ4-Super Structure		10d	27-Sep-26 A	08-Nov-26	268d	0	1,998	19,985
JDH3-02-009-BQ4-Roof Slab		10d	27-Sep-26 A	08-Nov-26	268d	0	1,998	19,985
	Steel Fixing Roof Slab - (F622)-LFTS3-BQ4-D03	5d	29-Oct-26	03-Nov-26	268d	0	0	9,992
	RC Casting Roof Slab - (F622)-LFTS3-BQ4-D03	2d	04-Nov-26	05-Nov-26	268d	0	0	3,997
	Deshuttering Roof Slab - (F622)-LFTS3-BQ4-D03	2d	07-Nov-26	08-Nov-26	268d	0	0	1,998
	Shuttering Roof Slab - (F622)-LFTS3-BQ4-D03	2d	27-Sep-26 A	28-Oct-26	268d	0	1,998	3,997
JDH3-02-009-BQ4-Finishes		4d	09-Nov-26	12-Nov-26	268d	0	0	17,623
JDH3-02-009-BQ4-Masonary		2d	11-Nov-26	12-Nov-26	268d	0	0	5,971
	Masonary Block work (CMU walls) Insulated Block Work - (F644)	2d	11-Nov-26	12-Nov-26	268d	0	0	5,971
JDH3-02-009-BQ4-Thermal & Moisture Protection		2d	09-Nov-26	10-Nov-26	268d	0	0	11,652
	Install Roof Isulation - (W149)-LFTS3-BQ4-D07	2d	09-Nov-26	10-Nov-26	268d	0	0	11,652
JDH3-02-009-BQ4-Electrical Works		16d	14-Nov-26	01-Dec-26	271d	0	0	63,395
JDH3-02-009-BQ4-LV Cables - 4Cx 185mm2 Cu/XLPE//PVC		5d	14-Nov-26	18-Nov-26	277d	0	0	32,417

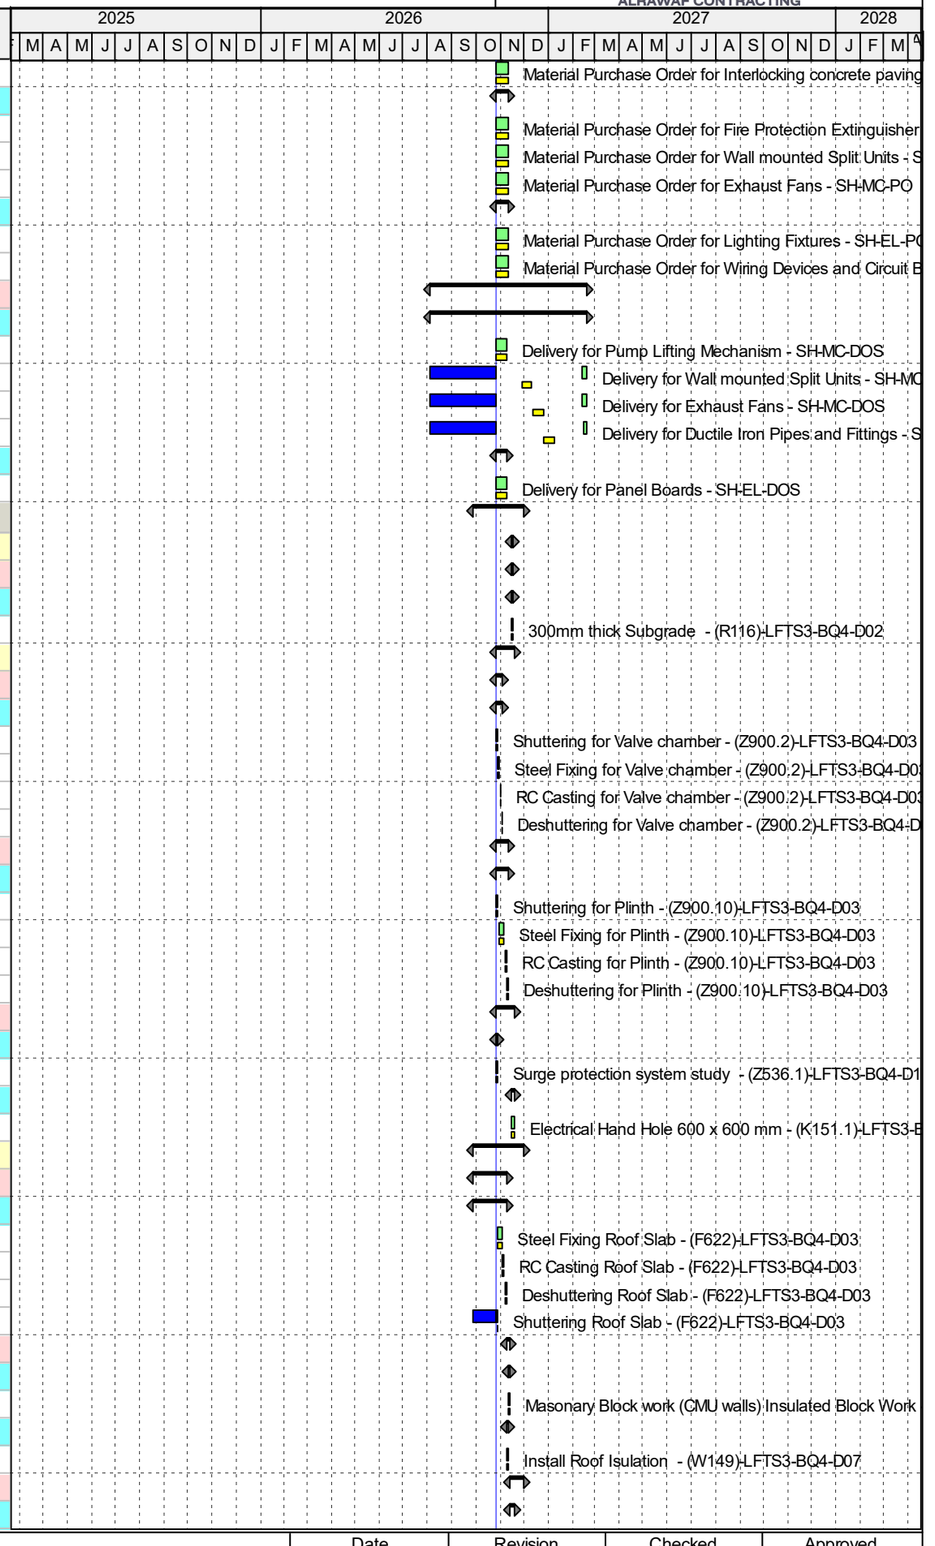


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	5d	14-Nov-26	18-Nov-26	277d	0	0	32,417
	JDH3-02-009-BQ4-LV Cables - 4Cx 95mm2 Cu/XLPE//PVC	16d	14-Nov-26	01-Dec-26	269d	0	0	12,607
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx9	16d	14-Nov-26	01-Dec-26	269d	0	0	12,607
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 Cu/XLPE/SWA/PVC	10d	14-Nov-26	24-Nov-26	277d	0	0	400
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	10d	14-Nov-26	24-Nov-26	277d	0	0	400
	JDH3-02-009-BQ4-LV Cables - 4Cx 150mm2 + 1Cx25mm2	9d	14-Nov-26	23-Nov-26	268d	0	0	11,162
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	9d	14-Nov-26	23-Nov-26	268d	0	0	11,162
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	2d	14-Nov-26	15-Nov-26	285d	0	0	400
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	2d	14-Nov-26	15-Nov-26	285d	0	0	400
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	4d	14-Nov-26	17-Nov-26	280d	0	0	800
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	4d	14-Nov-26	17-Nov-26	280d	0	0	800
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	4d	14-Nov-26	17-Nov-26	280d	0	0	800
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	4d	14-Nov-26	17-Nov-26	280d	0	0	800
	JDH3-02-009-BQ4-LV Cables - 4Cx 6mm2 + 1Cx6mm2 Cu/XLPE/P	4d	14-Nov-26	17-Nov-26	281d	0	0	490
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx6	4d	14-Nov-26	17-Nov-26	281d	0	0	490
	JDH3-02-009-BQ4-LV Cables - 3Cx 6mm2 Cu/XLPE/PVC FROM MC	4d	14-Nov-26	17-Nov-26	280d	0	0	525
	Electrical Conduits and Pull Box Installation for LV Cables 3Cx6	4d	14-Nov-26	17-Nov-26	280d	0	0	525
	JDH3-02-009-BQ4-LV Cables - 3Cx 4mm2 Cu/XLPE/PVC to the AC.	4d	14-Nov-26	17-Nov-26	281d	0	0	360
	Electrical Conduits and Pull Box Installation for LV Cables 3Cx4	4d	14-Nov-26	17-Nov-26	281d	0	0	360
	JDH3-02-009-BQ4-LED Interior Lighting	2d	14-Nov-26	15-Nov-26	285d	0	0	380
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	14-Nov-26	15-Nov-26	285d	0	0	380
	JDH3-02-009-BQ4-Addressable Fire-Alarm System	2d	14-Nov-26	15-Nov-26	285d	0	0	3,052
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (Z900.	2d	14-Nov-26	15-Nov-26	285d	0	0	3,052
Site Works		8d	09-Nov-26	17-Nov-26	306d	0	0	2,094
JDH3-02-009-BQ4-Electrical Works		8d	09-Nov-26	17-Nov-26	306d	0	0	2,094
JDH3-02-009-BQ4-(LV)-Ducts Bank (1 x 50 mm UPVC)		2d	09-Nov-26	10-Nov-26	277d	0	0	163
	Duct Bank Installationfor UPVC Duct Bank 1x50 mm - - (K591)-L	2d	09-Nov-26	10-Nov-26	277d	0	0	163
JDH3-02-009-BQ4-(LV)-Ducts Bank (2 x 50 mm UPVC)		2d	11-Nov-26	12-Nov-26	277d	0	0	231
	Duct Bank Installationfor UPVC Duct Bank 2x50 mm - - (K592)-L	2d	11-Nov-26	12-Nov-26	277d	0	0	231
JDH3-02-009-BQ4-(LV)-Ducts Bank (8 x 50 mm UPVC)		2d	14-Nov-26	15-Nov-26	277d	0	0	887
	Duct Bank Installationfor UPVC Duct Bank 8x50 mm - - (K593)-L	2d	14-Nov-26	15-Nov-26	277d	0	0	887
JDH3-02-009-BQ4-Earthing		2d	16-Nov-26	17-Nov-26	306d	0	0	813
	Supply, construct, connect and test earthing pitsfor Earthing Sys	2d	16-Nov-26	17-Nov-26	306d	0	0	813
Close Out		26d	27-Oct-26	25-Nov-26	397d	0	0	0
As Built Drawing Submittals - SUB-Lift Station - LFTS		22d	27-Oct-26	21-Nov-26	390d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR		16d	03-Nov-26	21-Nov-26	390d	0	0	0
JDI	Prepare and Submit Drawing for Flooring Roof Floor Plan for SU	7d	07-Nov-26	14-Nov-26	396d	0	0	0
JDI	Prepare and Submit Drawing for Over All Plan Ceiling for SUB-A	7d	07-Nov-26	14-Nov-26	396d	0	0	0
JDI	Prepare and Submit Drawing for Walls Ground Floor plan for SU	7d	14-Nov-26	21-Nov-26	390d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Motor Control CenterBuilding fo	7d	07-Nov-26	14-Nov-26	396d	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Motor Control CenterBuilding fo	7d	07-Nov-26	14-Nov-26	396d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		18d	27-Oct-26	16-Nov-26	394d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. :	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. :	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. :	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Trench Shopdrawingsfor SUB-/	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7d	09-Nov-26	16-Nov-26	394d	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -Foundation Shop D	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -ColumnsShop Drav	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -RoofShop Drawing	7d	07-Nov-26	14-Nov-26	396d	0	0	0
JDI	Prepare and Submit Drawing for Air Release Valve Chamber Str	7d	05-Nov-26	12-Nov-26	397d	0	0	0

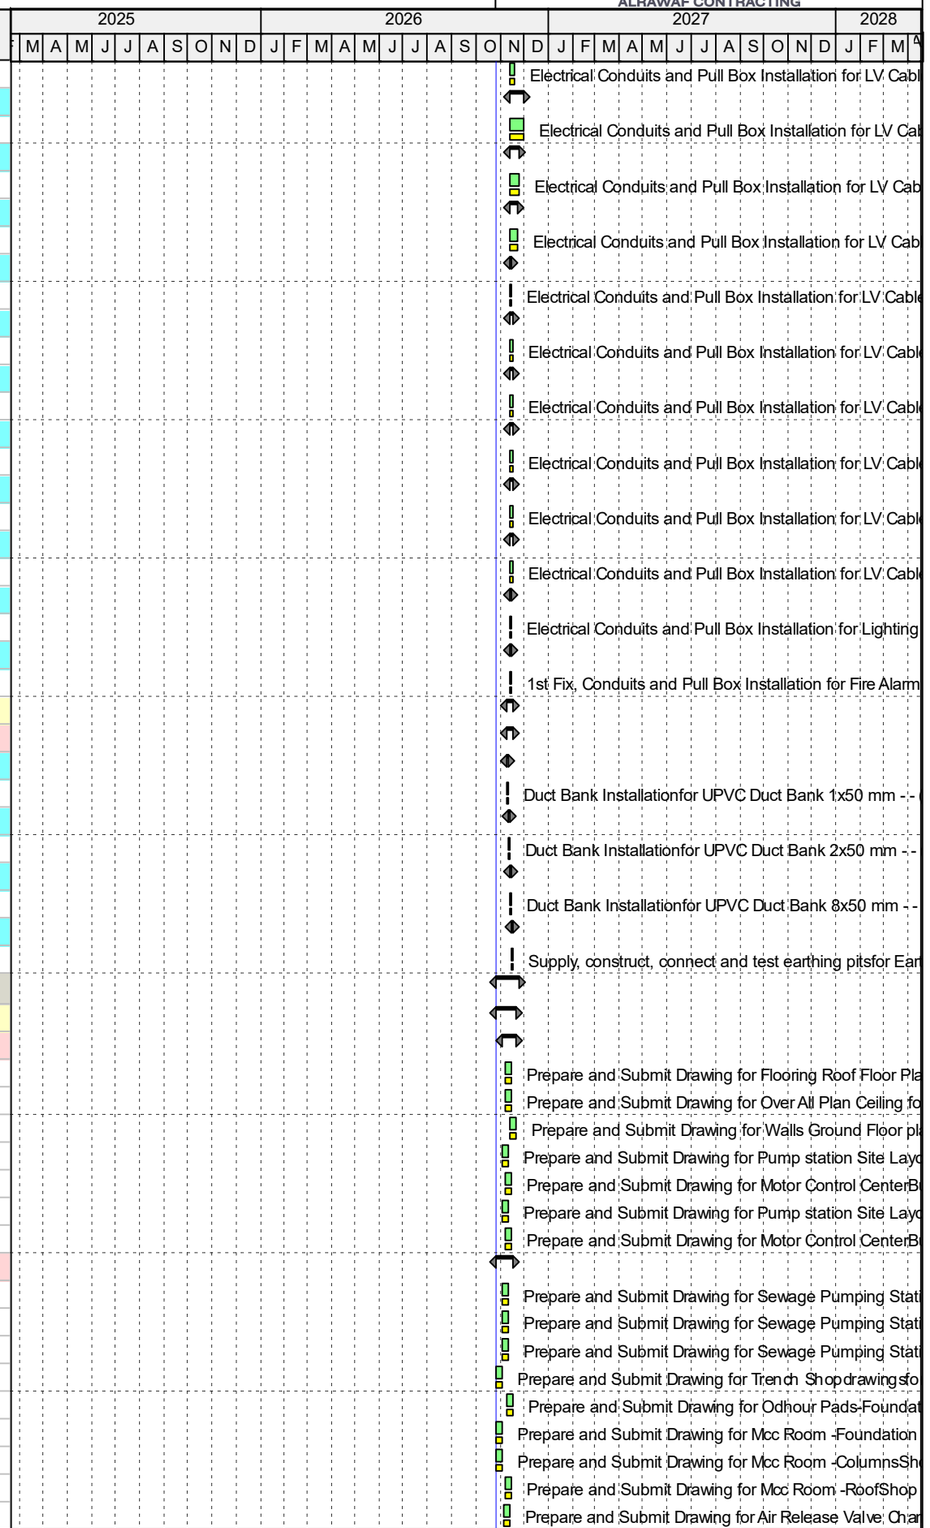


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Prepare and Submit Drawing for Wash-out Valve Chamber Stru	7d	05-Nov-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for Single Valve Chamber Structur	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Infra - IN		7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Force Main Master Layout (forc	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsIsolation Val	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsAir Chambe	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsWashout Ch	7d	27-Oct-26	03-Nov-26	405d	0	0	0
As Built Drawing Approvals - APP-Lift Station - LFTS		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR		11d	11-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Flooring Roof Floor Plan for APP-AS-LI	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Over All Plan Ceiling for APP-AS-LFTS:	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Motor Control CenterBuilding for APP-A	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Motor Control CenterBuilding for APP-A	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Foun	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Walls	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Trench Shopdrawingsfor APP-AS-LFTS	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mcc Room -Foundation Shop Drawing	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mcc Room -ColumnsShop Drawing for	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mcc Room -RoofShop Drawing for APF	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Air Release Valve Chamber Structure T	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Wash-out Valve Chamber Structure Typ	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Single Valve Chamber Structure Typica	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Infra - IN		9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Force Main Master Layout (force Main-A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mechanical DetailsIsolation Valve Char	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mechanical DetailsAir Chambers for AF	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Mechanical DetailsWashout Chambers	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDH3-02-009-Mosque		113d	28-Jul-26 A	18-Jan-27	351d	278,276	149,356	794,848
Engineering		60d	01-Sep-26 A	17-Nov-26	404d	26,382	3,693	26,382
JDH3-02-009-Prequalification and Material Submittals - SUB-MQ		48d	08-Sep-26 A	03-Nov-26	416d	0	0	0
Architectural		7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . doors &	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . eboxy m	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . paint an	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . CEMENT	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . PORCEL	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . anti slip r	7d	27-Oct-26	03-Nov-26	319d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . wall pape	7d	27-Oct-26	03-Nov-26	272d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . speciel it	7d	27-Oct-26	03-Nov-26	295d	0	0	0
Steel Material		7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . STAINLE	7d	27-Oct-26	03-Nov-26	416d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . Steel La	7d	27-Oct-26	03-Nov-26	416d	0	0	0
Mechanical		7d	08-Sep-26 A	03-Nov-26	134d	0	0	0
JDI	Submission of P.Q issuance for supplier and material . PLUMBII	7d	08-Sep-26 A	03-Nov-26	134d	0	0	0
Landscape		7d	08-Sep-26 A	31-Oct-26	279d	0	0	0
JDI	Submission of P.Q issuance for roads,pavements,trees-PR-MQ-	7d	08-Sep-26 A	31-Oct-26	279d	0	0	0
JDH3-02-009-Prequalification and Material Approvals - APP-MQ		49d	01-Sep-26 A	17-Nov-26	264d	26,382	3,693	26,382
Architectural		10d	04-Nov-26	17-Nov-26	264d	15,829	0	15,829

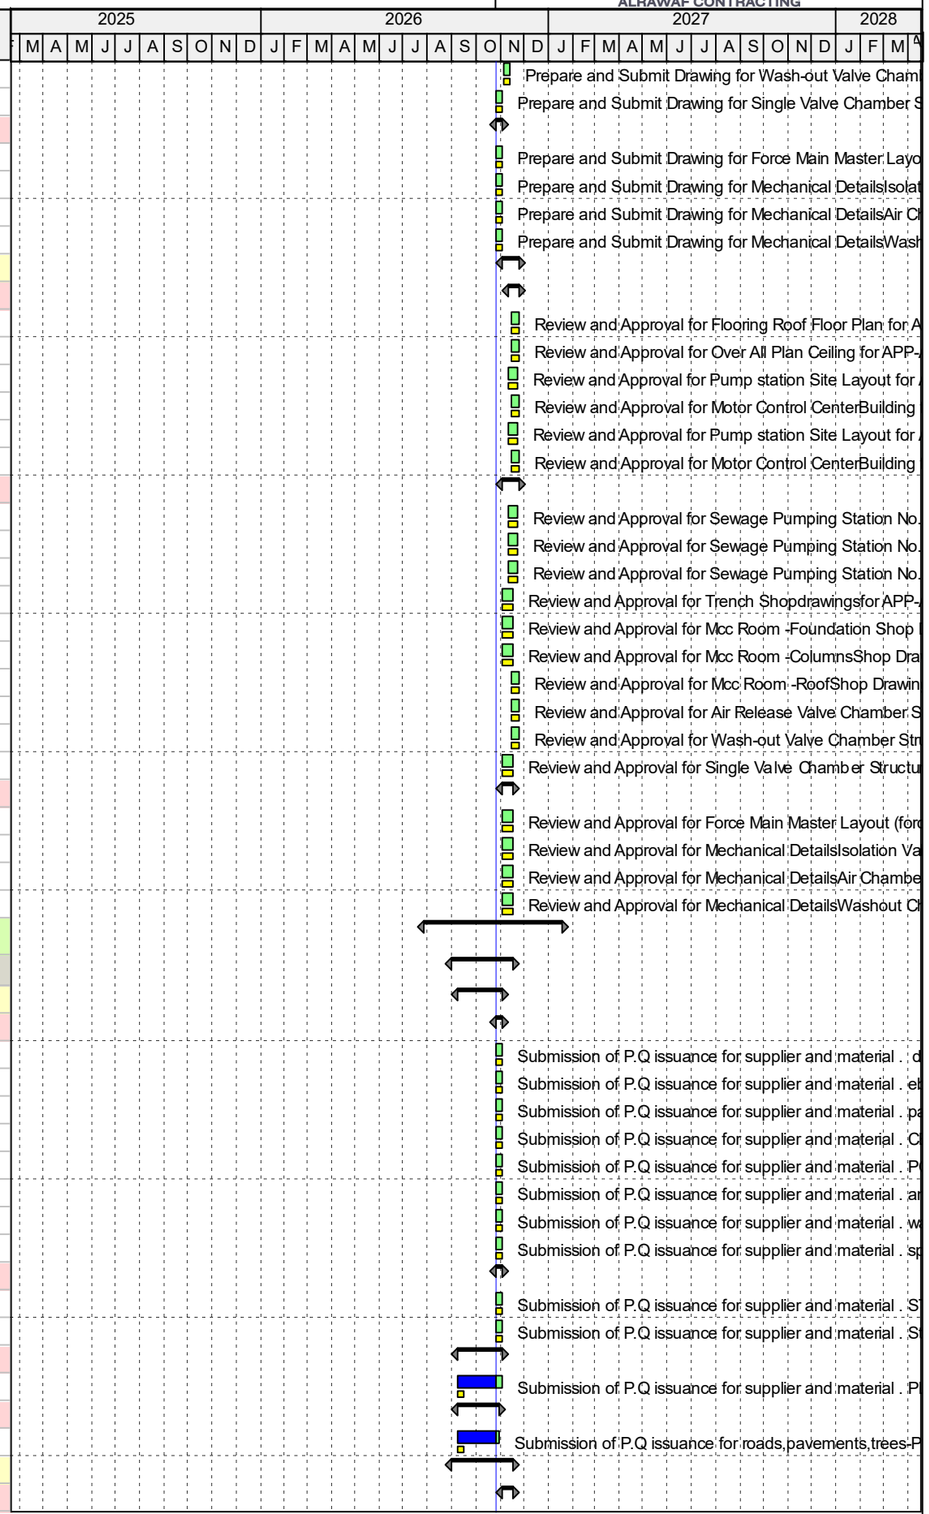

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Approval of Material Submittal for anti slip matt-PR-MQ-AR-App-	10d	04-Nov-26	17-Nov-26	264d	5,276	0	5,276
JDI	Approval of Material Submittal for wall paper-PR-MQ-AR-App-13	10d	04-Nov-26	17-Nov-26	225d	5,276	0	5,276
JDI	Approval of Material Submittal for speciel items for bathrooms ,	10d	04-Nov-26	17-Nov-26	244d	5,276	0	5,276
Mechanical		10d	01-Sep-26 A	05-Nov-26	109d	5,276	1,055	5,276
JDI	Approval of Material Submittal for PLUMBING Material-PR-MQ-M	10d	01-Sep-26 A	05-Nov-26	109d	5,276	1,055	5,276
Landscape		10d	01-Sep-26 A	02-Nov-26	229d	5,276	2,638	5,276
JDI	Approval of Material Submittal for roads,pavements,trees-PR-M	10d	01-Sep-26 A	02-Nov-26	229d	5,276	2,638	5,276
Procurement		38d	08-Sep-26 A	30-Nov-26	329d	25,229	2,523	50,458
Short Lead Items		38d	08-Sep-26 A	30-Nov-26	329d	25,229	2,523	50,458
Purchase Order - PO-Mosque		30d	27-Oct-26	30-Nov-26	329d	0	0	0
Architectural		21d	27-Oct-26	19-Nov-26	338d	0	0	0
	P.O Issue For Material . CARPET FLOOR ADHERED-PQ-MQ-A	21d	27-Oct-26	19-Nov-26	338d	0	0	0
	P.O Issue For Material for doors & windows materials-PQ-MQ-A	21d	27-Oct-26	19-Nov-26	299d	0	0	0
	P.O Issue For Material for eboxy materials-PQ-MQ-AR-PO-1520	21d	27-Oct-26	19-Nov-26	334d	0	0	0
	P.O Issue For Material for gypsom materials-PQ-MQ-AR-PO-153	21d	27-Oct-26	19-Nov-26	330d	0	0	0
	P.O Issue For Material for paint and ecrylic materials-PQ-MQ-AF	21d	27-Oct-26	19-Nov-26	332d	0	0	0
	P.O Issue For Material for CEMENT TILES 300x300 MM-PQ-MC	21d	27-Oct-26	19-Nov-26	155d	0	0	0
	P.O Issue For Material for PORCELAIN TILE 600X600MM-PQ-M	21d	27-Oct-26	19-Nov-26	155d	0	0	0
	P.O Issue For Material for Marbles-PQ-MQ-AR-PO-1640	21d	27-Oct-26	19-Nov-26	171d	0	0	0
Steel Material		21d	27-Oct-26	19-Nov-26	297d	0	0	0
	P.O Issue For Material . STAINLESS STEEL RAILING WITH WO	21d	27-Oct-26	19-Nov-26	294d	0	0	0
	P.O Issue For Material . Steel Ladder-PQ-MQ-SM-PO-1200	21d	27-Oct-26	19-Nov-26	297d	0	0	0
Electrical		21d	27-Oct-26	19-Nov-26	327d	0	0	0
	P.O Issue For Material . Telecommunication-PQ-MQ-EL-PO-133	21d	27-Oct-26	19-Nov-26	327d	0	0	0
	P.O Issue For Material . DISTRIBUTION BOARDS-PQ-MQ-EL-P	21d	27-Oct-26	19-Nov-26	170d	0	0	0
	P.O Issue For Material . FIRE ALARM SYSTEM-PQ-MQ-EL-PO-	21d	27-Oct-26	19-Nov-26	118d	0	0	0
	P.O Issue For Material . SOUND SYSTEM-PQ-MQ-EL-PO-1360	21d	27-Oct-26	19-Nov-26	120d	0	0	0
Mechanical		30d	27-Oct-26	30-Nov-26	132d	0	0	0
	P.O Issue For Material . PLUMBING Material-PQ-MQ-MC-PO-13	21d	07-Nov-26	30-Nov-26	132d	0	0	0
	P.O Issue For Material . HVAC-PQ-MQ-MC-PO-1390	21d	27-Oct-26	19-Nov-26	119d	0	0	0
Landscape		21d	03-Nov-26	26-Nov-26	277d	0	0	0
	P.O Issue For Material for roads,pavements,trees-PQ-MQ-LC-PC	21d	03-Nov-26	26-Nov-26	277d	0	0	0
Delivery and staging on Site - DOS-Mosque		30d	08-Sep-26 A	30-Nov-26	218d	25,229	2,523	50,458
Electrical		21d	27-Oct-26	16-Nov-26	232d	0	0	25,229
	INS&delivery and staging Material . change to wires & caples-P	21d	27-Oct-26	16-Nov-26	232d	0	0	25,229
Mechanical		21d	08-Sep-26 A	30-Nov-26	159d	25,229	2,523	25,229
	INS&delivery and staging Material . PLUMBING Material-PQ-MC	21d	08-Sep-26 A	30-Nov-26	159d	25,229	2,523	25,229
Construction		107d	28-Jul-26 A	18-Jan-27	351d	226,665	143,140	718,008
Mosque Main Building		98d	01-Sep-26 A	18-Jan-27	351d	144,213	33,434	180,307
SuperStructure for Building		4d	27-Oct-26	31-Oct-26	419d	4,295	0	4,295
Slab For Main Building		4d	27-Oct-26	31-Oct-26	419d	4,295	0	4,295
	Pouring for RC Steps And Ramps - (B3.1.3.4.3)-MQ-MB-SI-D03	1d	27-Oct-26	27-Oct-26	419d	3,754	0	3,754
	De Shuttering for RC Steps And Ramps - (B3.1.3.4.3)-MQ-MB-S	3d	28-Oct-26	31-Oct-26	419d	541	0	541
Finishing of Mosque Building		98d	01-Sep-26 A	18-Jan-27	118d	139,918	30,462	142,353
Masonary Work - MSW		31d	01-Sep-26 A	01-Nov-26	151d	47,259	26,849	47,259
	Installation for External Insulated CMU (Parpet) - 200mm - (B3.1	4d	27-Oct-26	01-Nov-26	151d	13,697	0	13,697
	Installation for Internal Insulated CMU - 100mm - (B3.1.4.2.1)-M	4d	03-Sep-26 A	01-Nov-26	151d	987	789	987
	Installation for External Insulated CMU - 200mm - (B3.1.4.1.1)-M	4d	01-Sep-26 A	27-Oct-26	151d	16,189	12,951	16,189
	Installation for External Insulated CMU - 300mm - (B3.1.4.1.3)-M	4d	02-Sep-26 A	01-Nov-26	151d	10,718	8,574	10,718
	Installation for Internal Insulated CMU - 200mm - (B3.1.4.2.2)-M	4d	01-Sep-26 A	01-Nov-26	151d	5,668	4,535	5,668
Thermal & Moisture Protection - INS		14d	01-Nov-26	17-Nov-26	164d	56,537	0	56,537
	Provide and Apply 4mm Thick Membrane To Roof - (B3.1.7.4.1	3d	01-Nov-26	04-Nov-26	164d	21,108	0	21,108

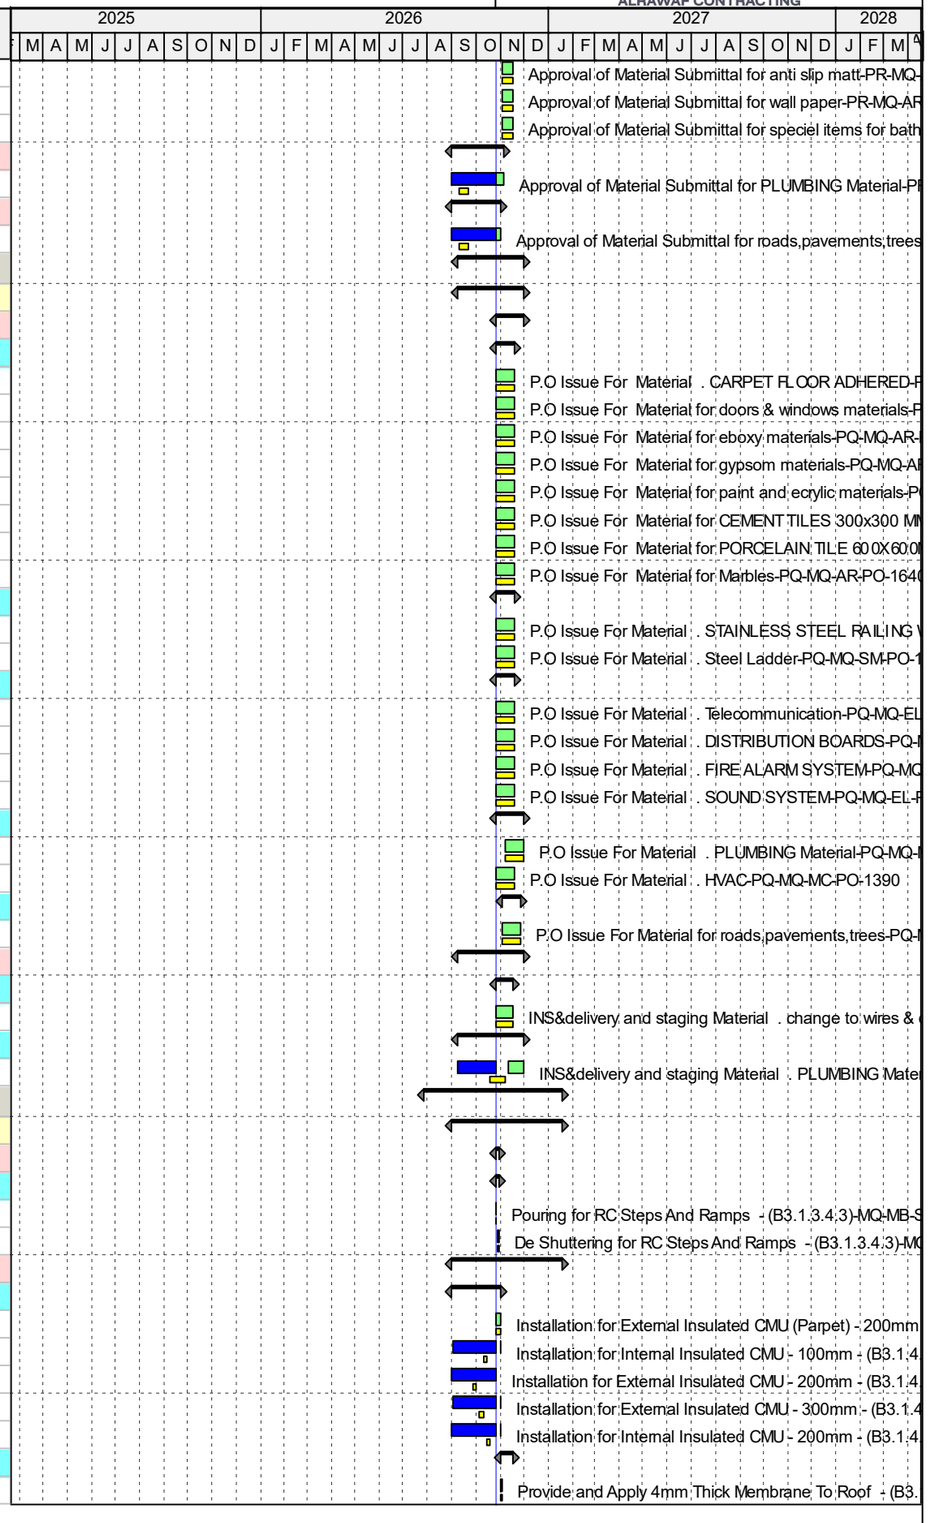


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Provide and Apply 50 Mm Thk Rigid Insulation To Roof - (B3.1.	3d	04-Nov-26	08-Nov-26	164d	14,734	0	14,734
	Provide and Apply 150 Micron Polyethylene Sheet To Roof - (B:	3d	08-Nov-26	11-Nov-26	164d	2,742	0	2,742
	Supplying and Fixing 3 Mm Thk Extruded Aluminum Flashing To	2d	11-Nov-26	14-Nov-26	164d	5,486	0	5,486
	Supplying and Apply Lightweight Concrete Screed To Roof - (B:	3d	14-Nov-26	17-Nov-26	164d	12,468	0	12,468
	Floor Finishes - FLR	12d	05-Jan-27	18-Jan-27	118d	0	0	2,435
	Installation of ceramic tiles To Living/Kitchen, women entrance,	8d	05-Jan-27	13-Jan-27	118d	0	0	2,374
	Installation of ceramic tiles To Steps (Threads & Risers) - (B3.1	4d	14-Jan-27	18-Jan-27	118d	0	0	61
	Walls Finishes - Wal	10d	16-Sep-26 A	16-Dec-26	118d	36,122	3,612	36,122
	Plastering to internal walls and columns - (B3.1.9.2.4)-MQ-MB-W	10d	16-Sep-26 A	16-Dec-26	118d	36,122	3,612	36,122
	Electrical Works of Mosque Building	10d	15-Sep-26 A	10-Dec-26	328d	0	2,972	33,659
	Grounding System - ER	9d	15-Sep-26 A	10-Dec-26	327d	0	2,972	13,518
	Installation of grounding system Ground rod with inspection pit	2d	27-Oct-26	28-Oct-26	357d	0	0	1,528
	Installation of grounding system Ground rod without inspection	2d	29-Oct-26	31-Oct-26	360d	0	0	2,081
	Installation of grounding system PVC insulated copper wire 70 r	2d	17-Sep-26 A	10-Dec-26	327d	0	619	2,064
	Installation of grounding system Bare copper ground wire 120 n	3d	15-Sep-26 A	10-Dec-26	327d	0	2,353	7,844
	Lightning system - LIG	10d	27-Oct-26	07-Nov-26	357d	0	0	20,141
	Installation of lightning protection system Bare tape copper con	5d	29-Oct-26	03-Nov-26	357d	0	0	12,756
	Installation of lightning protection system Air teminal rod 60 cm l	3d	04-Nov-26	07-Nov-26	357d	0	0	2,845
	Installation of lightning protection system Bare copper down cor	3d	27-Oct-26	29-Oct-26	364d	0	0	4,540
	Mosque Wash Room	52d	15-Sep-26 A	15-Nov-26	400d	12,837	1,043	24,491
	Finishing of Mosque Wash Room	17d	27-Oct-26	15-Nov-26	186d	1,403	0	13,056
	Masonary Work - MSW	2d	27-Oct-26	28-Oct-26	154d	1,403	0	1,403
	Installation for External Insulated CMU (Parpet) - 200 mm - (B3.:	2d	27-Oct-26	28-Oct-26	154d	1,403	0	1,403
	Thermal & Moisture Protection - INS	17d	27-Oct-26	15-Nov-26	181d	0	0	7,589
	Installation of 4mm thick membrane to Toilet - (B3.2.7.4.1.1)-MQ	4d	29-Oct-26	02-Nov-26	192d	0	0	2,294
	Installation of 4mm thick membrane to roof - (B3.2.7.4.1.2)-MQ	4d	27-Oct-26	31-Oct-26	180d	0	0	2,399
	Installation of 50 mm thk rigid insulation to Roof - (B3.2.7.4.2.1	4d	01-Nov-26	04-Nov-26	180d	0	0	1,597
	Installation of 150 micron polyethylene sheet to roof - (B3.2.7.4	4d	05-Nov-26	09-Nov-26	180d	0	0	286
	Installation of 3 mm thk extruded aluminum flashing to roof - (E	5d	10-Nov-26	15-Nov-26	180d	0	0	1,012
	Floor Finishes - FLR	2d	03-Nov-26	04-Nov-26	195d	0	0	4,065
	Installation of Anti -slip Rubber Hollow Mat - (B3.2.9.1.4)-MQ-WI	2d	03-Nov-26	04-Nov-26	195d	0	0	4,065
	Electrical Works of Wash Room	41d	15-Sep-26 A	02-Nov-26	411d	11,434	1,043	11,434
	Grounding System - GR	39d	15-Sep-26 A	31-Oct-26	413d	4,119	1,043	4,119
	Installation of grounding system Ground rod with inspection pit	2d	27-Oct-26	28-Oct-26	379d	382	0	382
	Installation of grounding system Ground rod without inspection	2d	29-Oct-26	31-Oct-26	379d	260	0	260
	Installation of grounding system PVC insulated copper wire 70 r	4d	15-Sep-26 A	29-Oct-26	414d	413	124	413
	Installation of grounding system Bare copper ground wire 120 n	4d	15-Sep-26 A	29-Oct-26	414d	3,064	919	3,064
	Lightning system - LIG	4d	27-Oct-26	31-Oct-26	413d	3,686	0	3,686
	Installation of lightning protection system Bare tape copper con	2d	27-Oct-26	28-Oct-26	379d	2,658	0	2,658
	Installation of lightning protection system Air teminal rod 60 cm l	2d	29-Oct-26	31-Oct-26	379d	203	0	203
	Installation of lightning protection system Bare copper down cor	2d	27-Oct-26	28-Oct-26	415d	825	0	825
	Low Voltage - LV	4d	29-Oct-26	02-Nov-26	182d	3,629	0	3,629
	Installation of Conduits and wiring outlets - (B5.2.16.4)-MQ-WR	4d	29-Oct-26	02-Nov-26	182d	3,629	0	3,629
	Mechanical Works For (Mosque Bldg+ Wash Area)	35d	13-Aug-26 A	29-Dec-26	149d	69,614	27,559	80,182
	Water Supply System - PW	6d	01-Nov-26	08-Nov-26	151d	18,722	0	18,722
JDI	Installation of for cold and hot water supply pipes 90 mm - (B4.1	6d	01-Nov-26	08-Nov-26	151d	18,722	0	18,722
	Sewer And Drainage System - SW	35d	13-Aug-26 A	29-Dec-26	149d	48,453	27,559	59,021
JDI	Installation of Galvanized iron vent - (B4.15.3.5)-MQ-MEP-SW-I	4d	01-Nov-26	05-Nov-26	153d	3,902	0	3,902
JDI	Installation of UPVC Pipes for Drainage 6" ? - (B4.15.3.1)-MQ-M	6d	13-Aug-26 A	30-Nov-26	132d	44,551	22,275	44,551
JDI	Installation of Roof Drain - (B4.15.3.4)-MQ-MEP-SW-D15-2nd F	4d	09-Sep-26 A	29-Dec-26	149d	0	5,284	10,568
	HVAC System - AC	4d	01-Nov-26	05-Nov-26	153d	2,439	0	2,439
JDI	Installation of Ducted Split Air Conditioning (For women prayer a	4d	01-Nov-26	05-Nov-26	153d	2,439	0	2,439
	Manarit	23d	27-Oct-26	22-Nov-26	362d	0	0	62,027

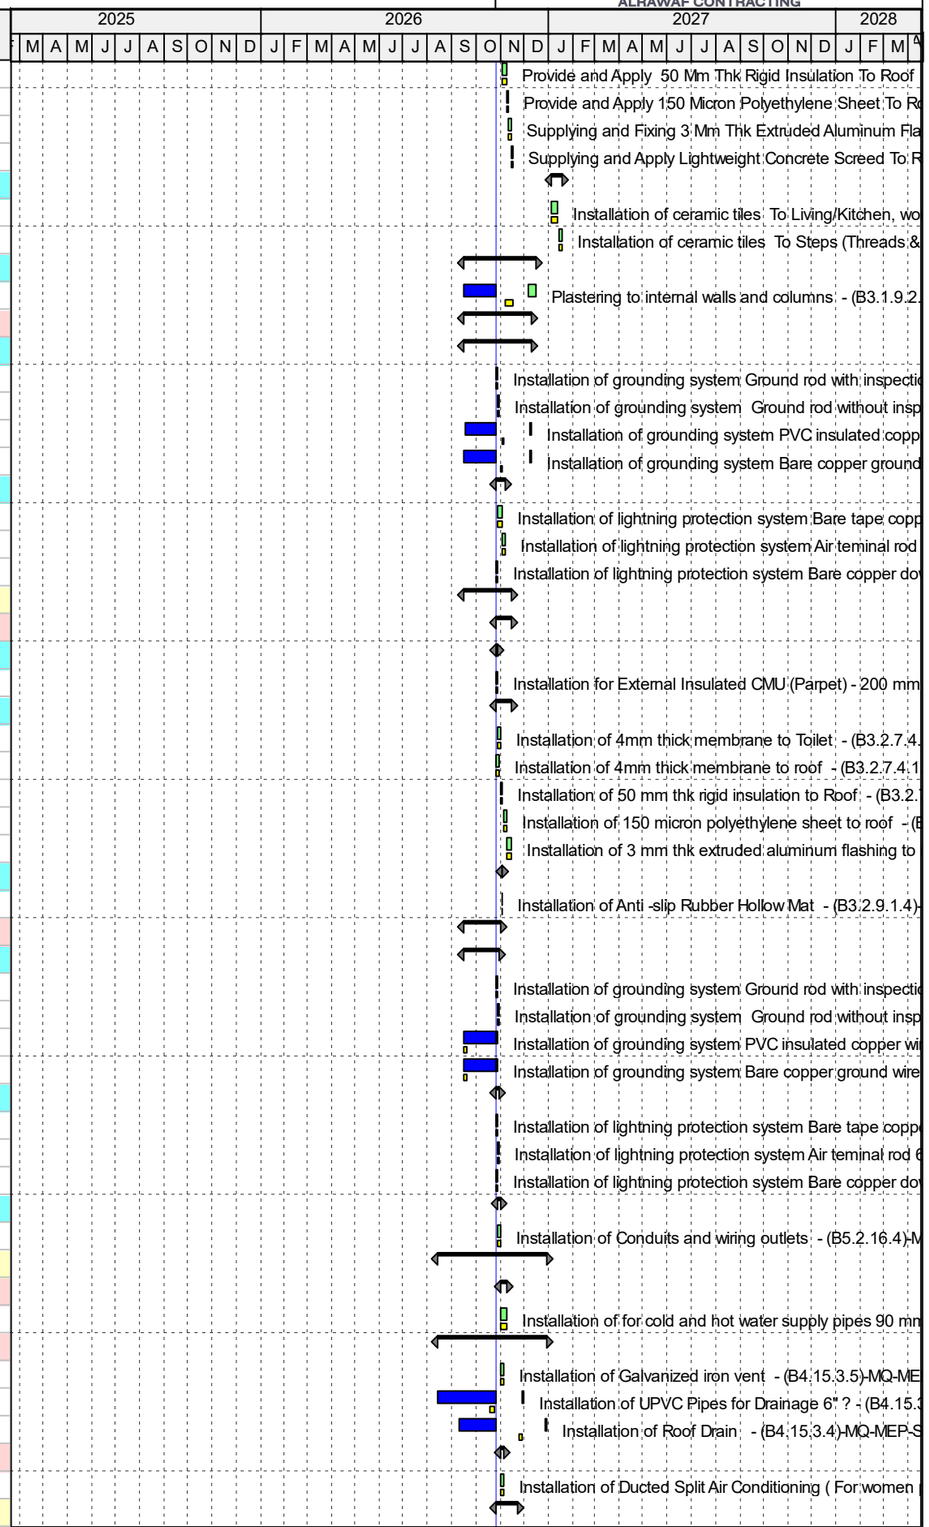


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Finishing For Minarat	23d	27-Oct-26	22-Nov-26	358d	0	0	58,231
	Masonary Work For Minaret	2d	27-Oct-26	28-Oct-26	358d	0	0	15,039
	Installation of Insulated CMU (EXTERNAL) 200mm thk - (B3.3.	2d	27-Oct-26	28-Oct-26	358d	0	0	15,039
	Floor Finishes For Minaret	2d	03-Nov-26	04-Nov-26	358d	0	0	204
	Installation of 600*600 mm granite tiles - (B3.3.9.1.1)-MQ-MNI	2d	03-Nov-26	04-Nov-26	358d	0	0	204
	Wall Finishes For Minaret	15d	05-Nov-26	22-Nov-26	358d	0	0	18,600
	Installation of Marble chips (Exposed Aggregate) at External wal	15d	05-Nov-26	22-Nov-26	358d	0	0	18,600
	Metal Work -MTW	2d	01-Nov-26	02-Nov-26	358d	0	0	24,388
	External Cement Plaster For Walls - (B3.3.5.1)-MQ-MNR-MTW-I	2d	01-Nov-26	02-Nov-26	358d	0	0	24,388
	Electrical Works of Minaret	8d	27-Oct-26	04-Nov-26	377d	0	0	3,796
	GROUNDING SYSTEM For Minaret	6d	27-Oct-26	02-Nov-26	372d	0	0	995
	Installation of Bare Copper Ground Wire 120 mm2 - (B5.3.16.1	4d	29-Oct-26	02-Nov-26	358d	0	0	613
	Installation of Ground Rod With Inspection Pit - (B5.3.16.1.2)-M	2d	27-Oct-26	28-Oct-26	376d	0	0	382
	LIGHTNING SYSTEM For Minaret	6d	29-Oct-26	04-Nov-26	377d	0	0	2,151
	Installation of Bare Tape Copper Conductor 3*25 mm - (B5.3.1(	3d	29-Oct-26	01-Nov-26	376d	0	0	1,329
	Installation of Air Teminal Rod 60 Cm Hieght - (B5.3.16.2.2)-MC	2d	29-Oct-26	31-Oct-26	377d	0	0	203
	Installation of Bare Copper Down Conductor 70 mm2 - (B5.3.1(	2d	03-Nov-26	04-Nov-26	377d	0	0	619
	LIGHTING FIXTURES For Minaret	2d	29-Oct-26	31-Oct-26	358d	0	0	650
	Installation of Light outlet including wiring ,conduit ,light switch -	2d	29-Oct-26	31-Oct-26	358d	0	0	650
	Service Building	19d	27-Oct-26	17-Nov-26	366d	0	0	28,564
	Sub Structure	15d	27-Oct-26	12-Nov-26	366d	0	0	21,548
	Foundation For pump Room	15d	27-Oct-26	12-Nov-26	366d	0	0	21,548
	shuttering for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	2d	27-Oct-26	28-Oct-26	366d	0	0	92
	pouring for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	1d	01-Nov-26	01-Nov-26	366d	0	0	709
	De shuttering for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	2d	02-Nov-26	03-Nov-26	366d	0	0	92
	Shuttering of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2d	04-Nov-26	05-Nov-26	366d	0	0	2,064
	Steel Fixing of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2d	07-Nov-26	08-Nov-26	366d	0	0	10,336
	RC Casting of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2d	09-Nov-26	10-Nov-26	366d	0	0	7,224
	Deshuttering of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2d	11-Nov-26	12-Nov-26	366d	0	0	1,032
	Finishing Service Building	15d	29-Oct-26	15-Nov-26	366d	0	0	2,951
	Insulation For Service Building	15d	29-Oct-26	15-Nov-26	366d	0	0	2,951
	Installation of two coats of bitumen waterproofing paint - (B6.7.	2d	14-Nov-26	15-Nov-26	366d	0	0	975
	Installation of two coats of Epoxy for inner surfaces(Slab on gra	2d	14-Nov-26	15-Nov-26	366d	0	0	1,626
	Installation of 250 micron thick polythelene sheet under blinding	2d	29-Oct-26	31-Oct-26	366d	0	0	175
	Applying of anti termite under all concrete in touch with earth fo	2d	29-Oct-26	31-Oct-26	366d	0	0	175
	Mechanical Work Service Building	2d	16-Nov-26	17-Nov-26	366d	0	0	4,065
	Water Storage Tank - GRP	2d	16-Nov-26	17-Nov-26	366d	0	0	4,065
	Supply and install water storage tanks - (B6.15.1.1)-MQ-SB-GR	2d	16-Nov-26	17-Nov-26	366d	0	0	4,065
	External Works	66d	28-Jul-26 A	17-Nov-26	314d	0	81,103	342,437
	Water Supply System	5d	12-Nov-26	17-Nov-26	314d	0	0	13,208
JDI	Installation of water supply piping system 110 mm - (B2.1.3.1)-M	5d	12-Nov-26	17-Nov-26	314d	0	0	13,208
	Sewer and Drainage	11d	27-Oct-26	08-Nov-26	314d	0	0	149,368
JDI	Installation of Sewer piping system 150 mm - (B2.1.4.1.1)-MQ-E	4d	27-Oct-26	31-Oct-26	314d	0	0	29,512
JDI	Installation of Inspection chambe - (B2.1.4.2)-MQ-EW-SW-D15-	2d	01-Nov-26	02-Nov-26	314d	0	0	36,582
JDI	installation of manhole - (B2.1.4.3)-MQ-EW-SW-D15-2nd Fix	3d	03-Nov-26	05-Nov-26	314d	0	0	22,304
JDI	Connecting the proposed sewerage network to the exisiting sew	2d	07-Nov-26	08-Nov-26	314d	0	0	60,970
	Storm Water Drainage	55d	28-Jul-26 A	11-Nov-26	314d	0	81,103	179,861
JDI	Installation of catch basins - (B2.1.5.3)-MQ-EW-SN-D15-2nd Fi	3d	09-Nov-26	11-Nov-26	314d	0	0	78,482
JDI	Installation of manhole - (B2.1.5.4)-MQ-EW-SN-D15-2nd Fix	3d	28-Jul-26 A	27-Oct-26	324d	0	81,103	101,379
	JDH3-02-009-TSE Pump Station	324d	25-Jul-26 A	15-Sep-27	153d	458,002	1,263,276	2,453,785
	Engineering	18d	27-Oct-26	16-Nov-26	405d	0	0	0
	JDH3-02-009-Prequalification and Material Submittals -SUB-PW Station Station -	10d	27-Oct-26	07-Nov-26	413d	0	0	0

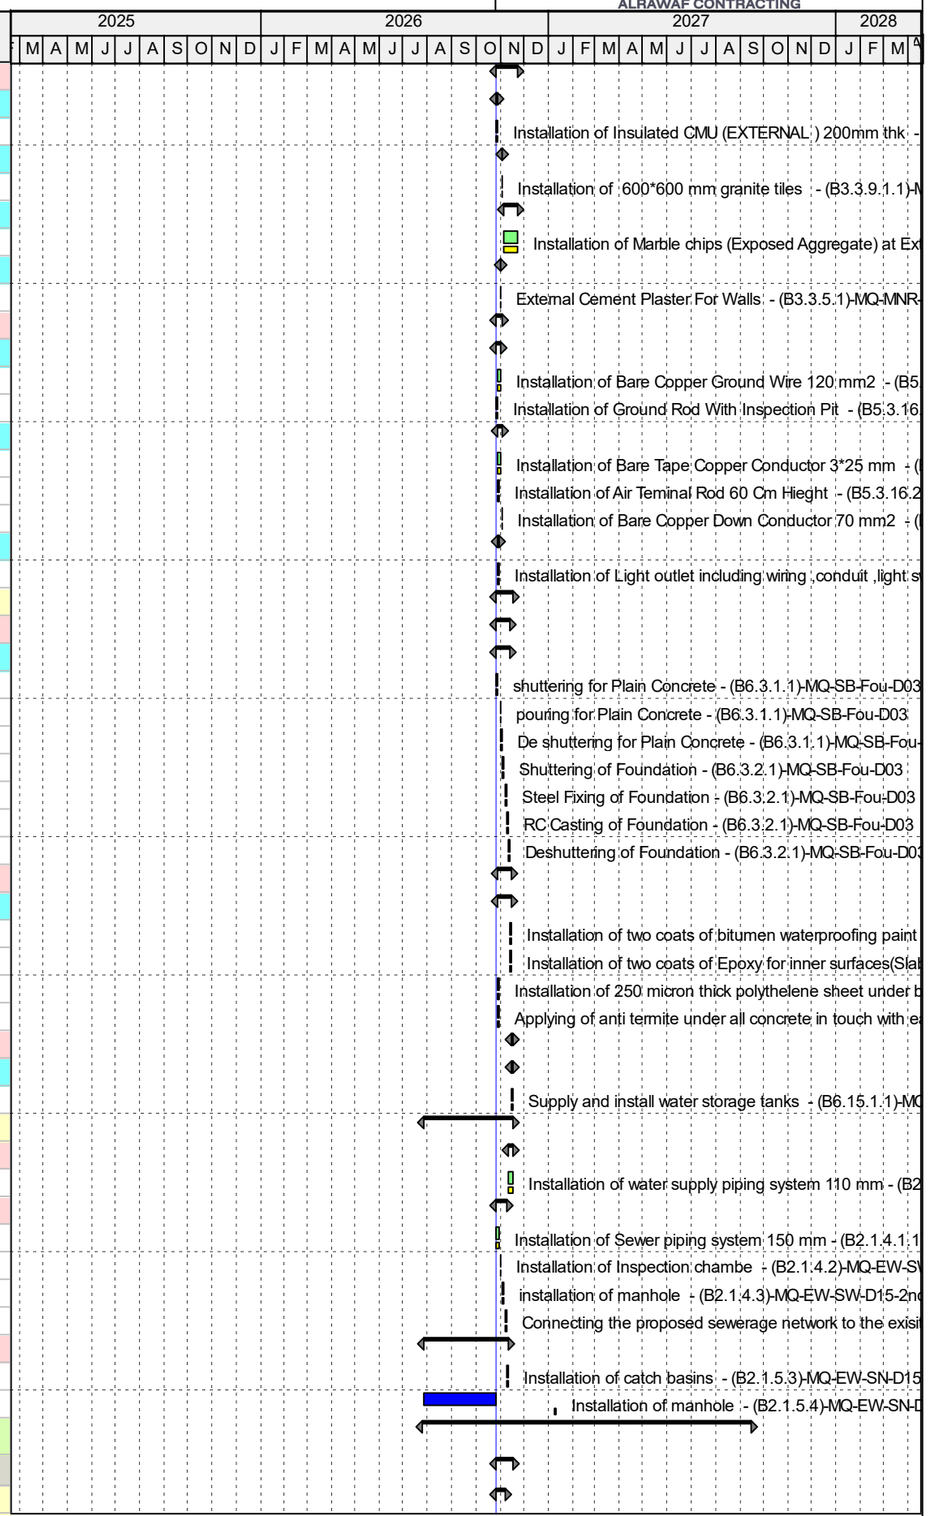


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-Prequalifications and Material prepare and Submit - SU	10d	27-Oct-26	07-Nov-26	413d	0	0	0
JDI	Prepare Material Submittal for Acrylic Paint Materials - EN-AR-SU	10d	27-Oct-26	07-Nov-26	413d	0	0	0
	JDH3-02-009-Method of Statement for TSE Pump Station	18d	27-Oct-26	16-Nov-26	370d	0	0	0
	JDH3-02-009-Pumps	18d	27-Oct-26	16-Nov-26	315d	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7d	27-Oct-26	03-Nov-26	315d	0	0	0
JDI	Review & approval MS for Pumps- MS	9d	04-Nov-26	16-Nov-26	261d	0	0	0
	JDH3-02-009-Duct Works	18d	27-Oct-26	16-Nov-26	276d	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7d	27-Oct-26	03-Nov-26	277d	0	0	0
JDI	Review & approval MS for Duct Works- MS	9d	04-Nov-26	16-Nov-26	229d	0	0	0
	JDH3-02-009-Drainage System	18d	27-Oct-26	16-Nov-26	247d	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7d	27-Oct-26	03-Nov-26	248d	0	0	0
JDI	Review & approval MS for Drainage System- MS	9d	04-Nov-26	16-Nov-26	205d	0	0	0
	JDH3-02-009-Water Supply System	18d	27-Oct-26	16-Nov-26	273d	0	0	0
JDI	Prepare & Submit MS for Water Supply System- MS	7d	27-Oct-26	03-Nov-26	273d	0	0	0
JDI	Review & approval MS for Water Supply System- MS	9d	04-Nov-26	16-Nov-26	226d	0	0	0
	JDH3-02-009-Chlorination System	18d	27-Oct-26	16-Nov-26	330d	0	0	0
JDI	Prepare & Submit MS for Chlorination System- MS	7d	27-Oct-26	03-Nov-26	331d	0	0	0
JDI	Review & approval MS for Chlorination System- MS	9d	04-Nov-26	16-Nov-26	274d	0	0	0
	JDH3-02-009-Over head Crane	18d	27-Oct-26	16-Nov-26	196d	0	0	0
JDI	Prepare & Submit MS for Over head Crane- MS	7d	27-Oct-26	03-Nov-26	196d	0	0	0
JDI	Review & approval MS for Over head Crane- MS	9d	04-Nov-26	16-Nov-26	162d	0	0	0
	JDH3-02-009-GLS Tank	18d	27-Oct-26	16-Nov-26	352d	0	0	0
JDI	Prepare & Submit MS for GLS Tank- MS	7d	27-Oct-26	03-Nov-26	352d	0	0	0
JDI	Review & approval MS for GLS Tank- MS	9d	04-Nov-26	16-Nov-26	292d	0	0	0
	JDH3-02-009-Access Control	18d	27-Oct-26	16-Nov-26	167d	0	0	0
JDI	Prepare & Submit MS for Access Control- MS	7d	27-Oct-26	03-Nov-26	167d	0	0	0
JDI	Review & approval MS for Access Control- MS	9d	04-Nov-26	16-Nov-26	138d	0	0	0
	JDH3-02-009-Data Communication	18d	27-Oct-26	16-Nov-26	166d	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7d	27-Oct-26	03-Nov-26	166d	0	0	0
JDI	Review & approval MS for Data Communication- MS	9d	04-Nov-26	16-Nov-26	137d	0	0	0
	JDH3-02-009-Security System	18d	27-Oct-26	16-Nov-26	168d	0	0	0
JDI	Prepare & Submit MS for Security System- MS	7d	27-Oct-26	03-Nov-26	169d	0	0	0
JDI	Review & approval MS for Security System- MS	9d	04-Nov-26	16-Nov-26	139d	0	0	0
	JDH3-02-009-Programing Logical Control System	18d	27-Oct-26	16-Nov-26	370d	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7d	27-Oct-26	03-Nov-26	370d	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9d	04-Nov-26	16-Nov-26	307d	0	0	0
Procurement		137d	04-Aug-26 A	05-Feb-27	336d	458,002	171,751	801,503
Long Lead Items		87d	27-Oct-26	05-Feb-27	285d	458,002	0	458,002
	Purchase Order - PO - TSE Pump Station	10d	27-Oct-26	07-Nov-26	285d	0	0	0
	JDH3-02-009-Long Lead Items - LOL-Material Purchase Order - PO	10d	27-Oct-26	07-Nov-26	285d	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - PR	10d	27-Oct-26	07-Nov-26	79d	0	0	0
	Material Purchase Order for Access Control System - PR-TC-PO	10d	27-Oct-26	07-Nov-26	88d	0	0	0
	Material Purchase Order for Data Communication System - PR-	10d	27-Oct-26	07-Nov-26	95d	0	0	0
	Material Purchase Order for Security System - PR-TC-PO	10d	27-Oct-26	07-Nov-26	285d	0	0	0
	Fabrication - FAB - TSE Pump Station	90d	08-Nov-26	05-Feb-27	343d	0	0	0
	JDH3-02-009-Long Lead Items - LOL-Manufacturing and Custom Cl	90d	08-Nov-26	05-Feb-27	343d	0	0	0
	Material Fabrication for Addressable Fire Alarm System - PR-TC-	90d	08-Nov-26	05-Feb-27	92d	0	0	0
	Material Fabrication for Access Control System - PR-TC-FAB	90d	08-Nov-26	05-Feb-27	102d	0	0	0
	Material Fabrication for Data Communication System - PR-TC-FA	90d	08-Nov-26	05-Feb-27	112d	0	0	0
	Material Fabrication for Security System - PR-TC-FAB	90d	08-Nov-26	05-Feb-27	343d	0	0	0
	Delivery and staging on Site - DOS -TSE Pump Station	10d	27-Oct-26	05-Nov-26	403d	458,002	0	458,002
	JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging	10d	27-Oct-26	05-Nov-26	249d	229,001	0	229,001
	delivery and staging for Surge Protection System - PR-MC-DOS	10d	27-Oct-26	05-Nov-26	249d	114,500	0	114,500

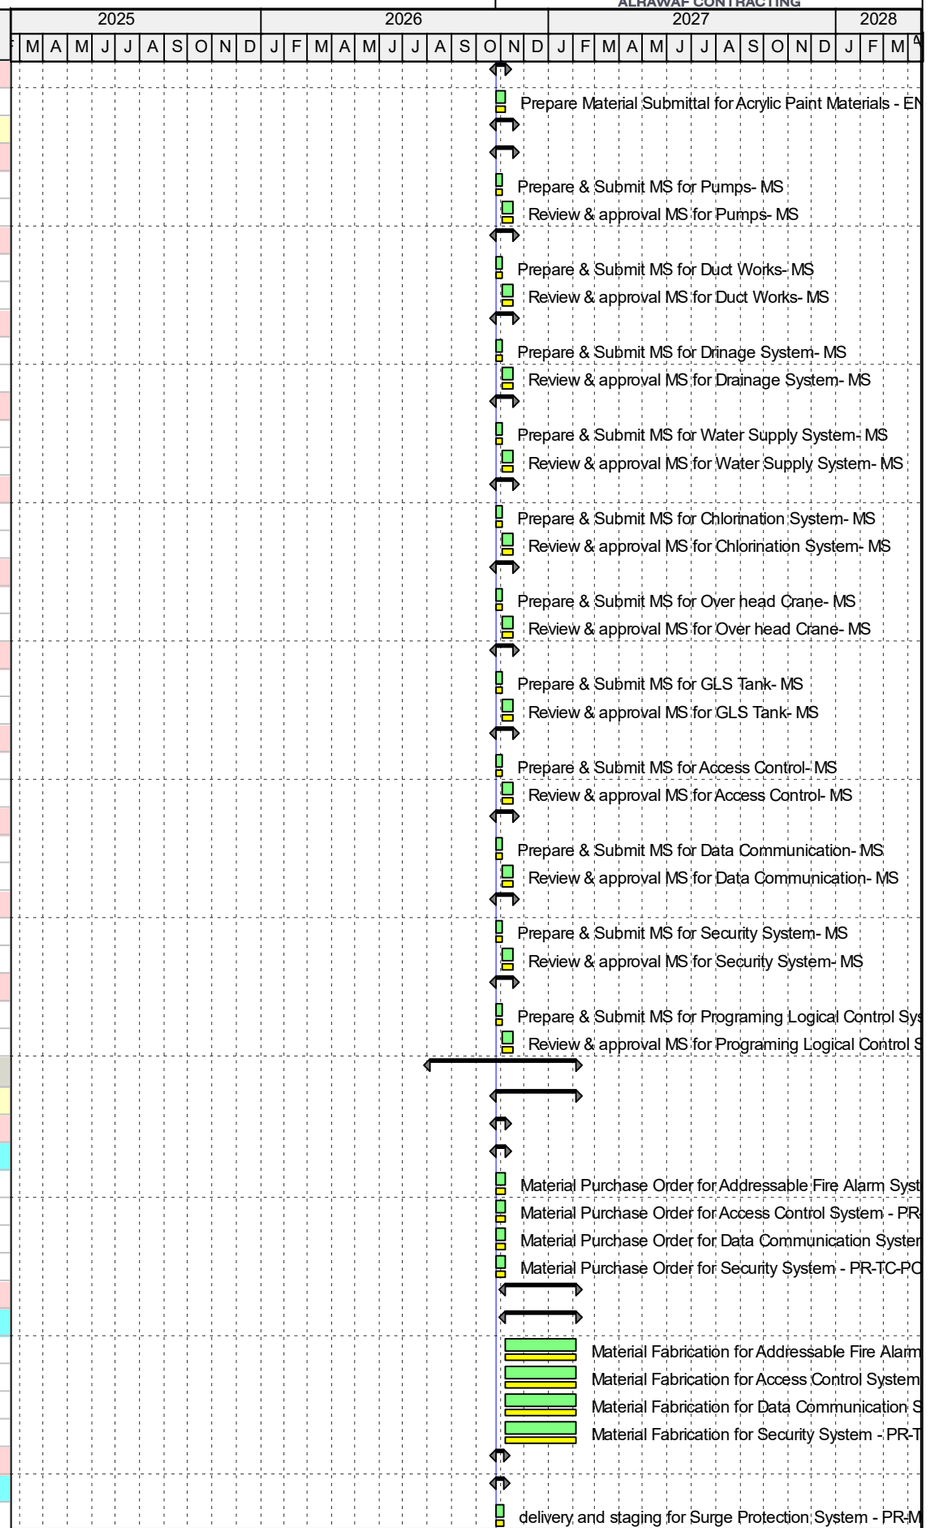


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	delivery and staging for Overhead Crane - PR-MC-DOS	10d	27-Oct-26	05-Nov-26	249d	114,500	0	114,500
	JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging	10d	27-Oct-26	05-Nov-26	403d	229,001	0	229,001
	delivery and staging for Transformer (TR) - PR-EL-DOS	10d	27-Oct-26	05-Nov-26	380d	114,500	0	114,500
	delivery and staging for Main Distribution Boards (MDB) - PR-EL-	10d	27-Oct-26	05-Nov-26	403d	114,500	0	114,500
Short Lead Items		71d	04-Aug-26 A	19-Nov-26	402d	0	171,751	343,501
Purchase Order - PO - TSE Pump Station		21d	27-Oct-26	19-Nov-26	402d	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(		21d	27-Oct-26	19-Nov-26	296d	0	0	0
	Material Purchase Order for Epoxy Flooring - PR-AR-PO	21d	27-Oct-26	19-Nov-26	296d	0	0	0
	Material Purchase Order for Acrylic Paint Materials - PR-AR-PO	21d	27-Oct-26	19-Nov-26	247d	0	0	0
	Material Purchase Order for Chain link Fences - PR-AR-PO	21d	27-Oct-26	19-Nov-26	68d	0	0	0
	Material Purchase Order for Steel Gates - PR-AR-PO	21d	27-Oct-26	19-Nov-26	97d	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(		21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Fuel Oil System - PR-MC-PO	21d	27-Oct-26	19-Nov-26	193d	0	0	0
	Material Purchase Order for GRP Tank - PR-MC-PO	21d	27-Oct-26	19-Nov-26	258d	0	0	0
	Material Purchase Order for Fire Protection System - PR-MC-PO	21d	27-Oct-26	19-Nov-26	354d	0	0	0
	Material Purchase Order for Wall mounted Split Units - PR-MC-P	21d	27-Oct-26	19-Nov-26	347d	0	0	0
	Material Purchase Order for Exhaust Fans - PR-MC-PO	21d	27-Oct-26	19-Nov-26	366d	0	0	0
	Material Purchase Order for Galvanized Iron Sheets for Duct Wo	21d	27-Oct-26	19-Nov-26	193d	0	0	0
	Material Purchase Order for Air Outlets - PR-MC-PO	21d	27-Oct-26	19-Nov-26	269d	0	0	0
	Material Purchase Order for GLS Tank - PR-MC-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(		21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Low Voltage Cables - PR-EL-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Panel Boards - PR-EL-PO	21d	27-Oct-26	19-Nov-26	354d	0	0	0
	Material Purchase Order for Earthing Sytem - PR-EL-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Lighting Fixtures - PR-EL-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for KWH Meter - PR-EL-PO	21d	27-Oct-26	19-Nov-26	354d	0	0	0
Delivery and staging on Site - DOS - TSE Pump Station		14d	04-Aug-26 A	19-Nov-26	438d	0	171,751	343,501
JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging		14d	04-Aug-26 A	19-Nov-26	438d	0	171,751	343,501
	delivery and staging for Wall mounted Split Units - PR-MC-DOS	14d	04-Aug-26 A	19-Nov-26	416d	0	57,250	114,500
	delivery and staging for Exhaust Fans - PR-MC-DOS	14d	04-Aug-26 A	19-Nov-26	438d	0	57,250	114,500
	delivery and staging for Galvanized Iron Sheets for Duct Works	14d	04-Aug-26 A	19-Nov-26	235d	0	57,250	114,500
Construction		324d	25-Jul-26 A	15-Sep-27	118d	0	1,091,526	1,652,282
JDH3-02-009 -SITE WORK		12d	15-Sep-26 A	15-Sep-27	52d	0	77,551	110,787
JDH3-02-009-B15-Mechanical Works-phase 1		12d	15-Sep-26 A	15-Sep-27	52d	0	77,551	110,787
JDH3-02-009-B15-Site Interconnecting Pipes 200mm		12d	15-Sep-26 A	15-Sep-27	52d	0	20,463	29,233
	Soil Replacement and Bedding for Ductile Iron Pipe 200 mm -	2d	16-Sep-26 A	15-Sep-27	52d	0	1,279	1,827
	Pipe.Installation for Ductile Iron Pipe 200 mm - Depth from 2.5	8d	17-Sep-26 A	15-Sep-27	52d	0	14,068	20,098
	Excavation Works for Ductile Iron Pipe 200 mm - Depth from 2.	2d	15-Sep-26 A	15-Sep-27	33d	0	5,116	7,308
JDH3-02-009-B15-Site Interconnecting Pipes 400 mm		8d	15-Sep-26 A	15-Sep-27	41d	0	57,087	81,553
	Excavation Works for Ductile Iron Pipe 400 mm - Depth from 2.5	2d	15-Sep-26 A	15-Sep-27	33d	0	14,272	20,388
	Soil Replacement and Bedding Works for Ductile Iron Pipe 400	2d	16-Sep-26 A	15-Sep-27	41d	0	3,568	5,097
	Pipe.Installation for Ductile Iron Pipe 400 mm - Depth from 2.51	4d	17-Sep-26 A	15-Sep-27	41d	0	39,248	56,068
JDH3-02-009 -PUMP STATION		164d	28-Jul-26 A	11-May-27	0d	0	94,475	197,230
JDH3-02-009-B16-Site Works		2d	28-Jul-26 A	11-May-27	0d	0	10,107	14,439
JDH3-02-009-B16-Earth work		2d	28-Jul-26 A	11-May-27	0d	0	10,107	14,439
	Backfill Layers Works Excavated Material - (B16. 2.2)-TSEP-B1	2d	28-Jul-26 A	11-May-27	0d	0	10,107	14,439
JDH3-02-009-B16-Sub Structure		124d	15-Sep-26 A	31-Mar-27	0d	0	56,995	98,566
JDH3-02-009-B16-Grade Beams		10d	27-Oct-26	07-Nov-26	120d	0	0	17,144
	Shuttering Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2d	27-Oct-26	28-Oct-26	120d	0	0	3,429
	Steel Fixing Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	4d	29-Oct-26	02-Nov-26	120d	0	0	8,572
	RC Casting Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2d	03-Nov-26	04-Nov-26	120d	0	0	3,429
	Deshuttering Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2d	05-Nov-26	07-Nov-26	120d	0	0	1,714

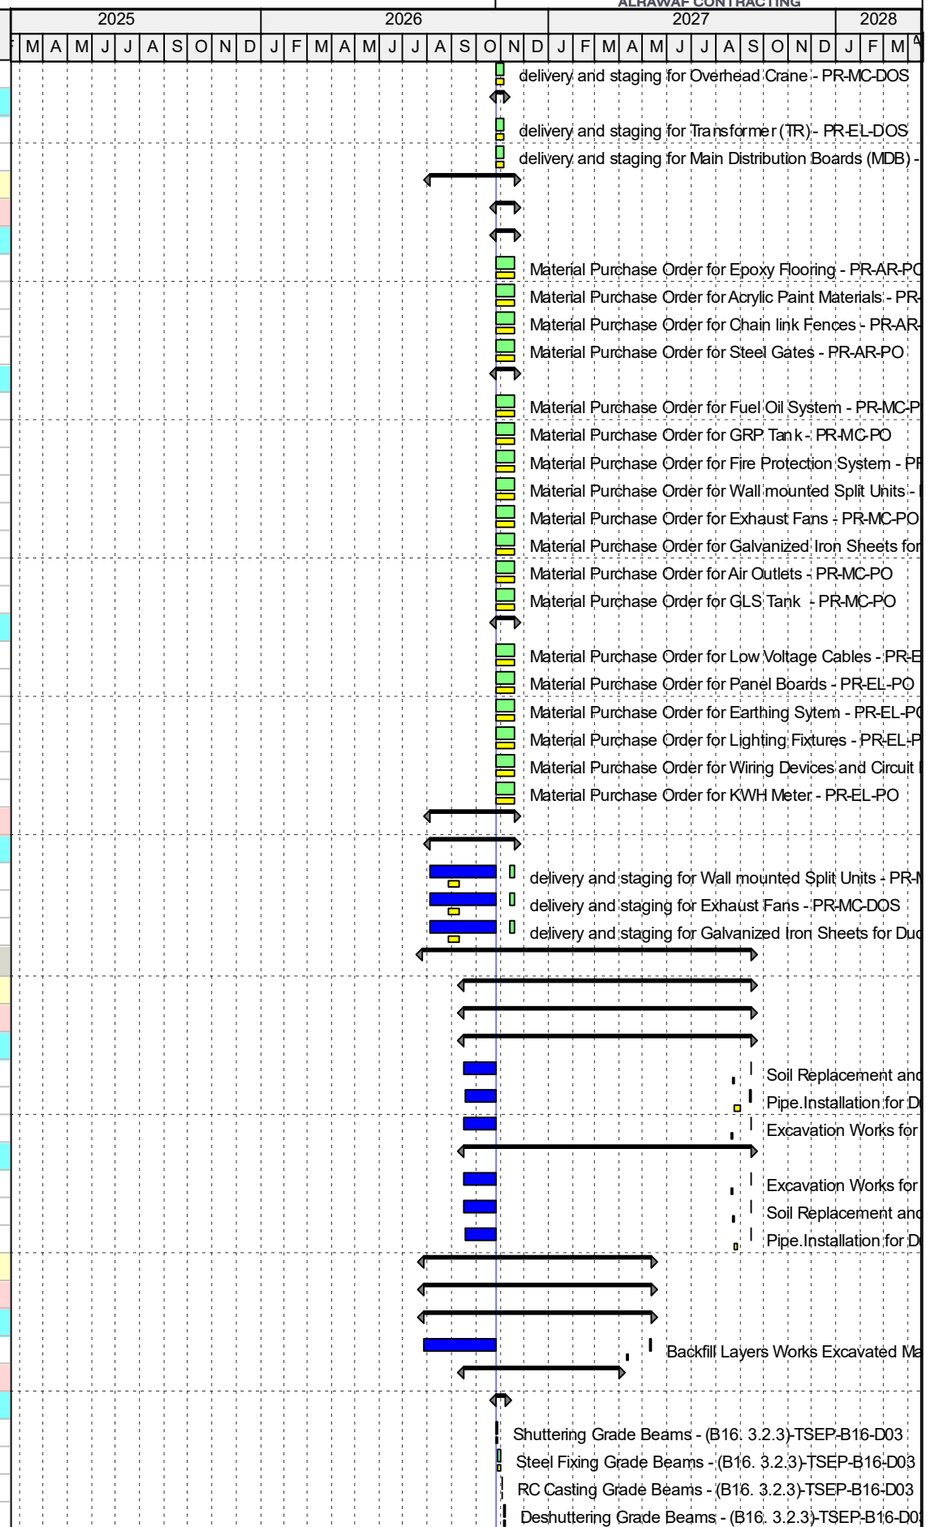


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-B16-Concrete trench (Walls and Slabs)	124d	15-Sep-26 A	31-Mar-27	0d	0	56,995	81,421
	Deshuttering Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2d	19-Sep-26 A	31-Mar-27	0d	0	5,699	8,142
	Steel Fixing Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	4d	16-Sep-26 A	07-Nov-26	120d	0	28,497	40,711
	Shuttering Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2d	15-Sep-26 A	07-Nov-26	120d	0	11,399	16,284
	RC Casting Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2d	17-Sep-26 A	31-Mar-27	0d	0	11,399	16,284
	JDH3-02-009-B16-Super Structure	14d	15-Sep-26 A	12-Apr-27	0d	0	27,373	84,225
	JDH3-02-009-B16-Columns	14d	15-Sep-26 A	12-Apr-27	0d	0	27,373	84,225
	Shuttering Columns - (B16. 3.2.2)-TSEP-B16-D03	2d	15-Sep-26 A	07-Apr-27	0d	0	2,527	16,845
	Steel Fixing Columns - (B16. 3.2.2)-TSEP-B16-D03	4d	16-Sep-26 A	07-Apr-27	0d	0	21,056	42,112
	RC Casting Columns - (B16. 3.2.2)-TSEP-B16-D03	2d	17-Sep-26 A	12-Apr-27	0d	0	2,527	16,845
	Deshuttering Columns - (B16. 3.2.2)-TSEP-B16-D03	2d	19-Sep-26 A	12-Apr-27	0d	0	1,263	8,422
	JDH3-02-009 -GUARD HOUSE	19d	27-Oct-26	17-Nov-26	353d	0	0	15,970
	JDH3-02-009-B17-Sub Structure	18d	27-Oct-26	16-Nov-26	324d	0	0	7,929
	JDH3-02-009-B17-Plain Concrete	4d	27-Oct-26	31-Oct-26	241d	0	0	325
	Shuttering Plain Concrete - (B17. 3.1.1)-TSEP-B17-D03	2d	27-Oct-26	28-Oct-26	241d	0	0	65
	PC Casting Plain Concrete - (B17. 3.1.1)-TSEP-B17-D03	2d	29-Oct-26	31-Oct-26	241d	0	0	260
	JDH3-02-009-B17-Foundation	8d	01-Nov-26	09-Nov-26	241d	0	0	1,560
	Shuttering Foundation - (B17. 3.2.1)-TSEP-B17-D03	2d	01-Nov-26	02-Nov-26	241d	0	0	312
	Steel Fixing Foundation - (B17. 3.2.1)-TSEP-B17-D03	2d	03-Nov-26	04-Nov-26	241d	0	0	780
	RC Casting Foundation - (B17. 3.2.1)-TSEP-B17-D03	2d	05-Nov-26	07-Nov-26	241d	0	0	312
	Deshuttering Foundation - (B17. 3.2.1)-TSEP-B17-D03	2d	08-Nov-26	09-Nov-26	241d	0	0	156
	JDH3-02-009-B17-Columns neck	6d	10-Nov-26	16-Nov-26	241d	0	0	2,832
	Shuttering Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2d	10-Nov-26	11-Nov-26	241d	0	0	629
	Steel Fixing Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2d	12-Nov-26	14-Nov-26	241d	0	0	1,573
	RC Casting Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2d	15-Nov-26	16-Nov-26	241d	0	0	629
	JDH3-02-009-B17-Grade Beams	6d	10-Nov-26	16-Nov-26	241d	0	0	1,379
	Shuttering Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2d	10-Nov-26	11-Nov-26	241d	0	0	306
	Steel Fixing Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2d	12-Nov-26	14-Nov-26	241d	0	0	766
	RC Casting Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2d	15-Nov-26	16-Nov-26	241d	0	0	306
	JDH3-02-009-B17-Slab on Grade	8d	29-Oct-26	07-Nov-26	332d	0	0	1,832
	Shuttering Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2d	29-Oct-26	31-Oct-26	332d	0	0	366
	Steel Fixing Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2d	01-Nov-26	02-Nov-26	332d	0	0	916
	RC Casting Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2d	03-Nov-26	04-Nov-26	332d	0	0	366
	Deshuttering Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2d	05-Nov-26	07-Nov-26	332d	0	0	183
	JDH3-02-009-B17-Electrical Works for Potable Water Pump Station	5d	12-Nov-26	17-Nov-26	351d	0	0	1,706
	JDH3-02-009-B17-LED Interior Lighting	2d	12-Nov-26	14-Nov-26	336d	0	0	303
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	12-Nov-26	14-Nov-26	336d	0	0	303
	JDH3-02-009-B17-Addressable Fire-Alarm System	4d	12-Nov-26	16-Nov-26	336d	0	0	349
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B17.	4d	12-Nov-26	16-Nov-26	336d	0	0	349
	JDH3-02-009-B17-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+	5d	12-Nov-26	17-Nov-26	335d	0	0	908
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	5d	12-Nov-26	17-Nov-26	335d	0	0	908
	JDH3-02-009-B17-Data Communications	2d	12-Nov-26	14-Nov-26	354d	0	0	146
	1st Fix, Conduits and Pull Box Installation for Data Communicat	2d	12-Nov-26	14-Nov-26	354d	0	0	146
	JDH3-02-009-B17-Finishes	18d	27-Oct-26	16-Nov-26	354d	0	0	3,999
	JDH3-02-009-B17-Thermal & Moisture Protection	18d	27-Oct-26	16-Nov-26	354d	0	0	1,379
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	2d	27-Oct-26	28-Oct-26	332d	0	0	96
	Applying Foam concrete screed Insulation Foam concrete - (B1	2d	12-Nov-26	14-Nov-26	354d	0	0	536
	Applying PVC Waterproofing Membrane PVC Membrane - (B17	2d	15-Nov-26	16-Nov-26	354d	0	0	747
	JDH3-02-009-B17-Masonary	4d	08-Nov-26	11-Nov-26	332d	0	0	2,620
	Masonary Block work ACC Block - (B17. 4.1.1)-TSEP-B17-D04	2d	08-Nov-26	09-Nov-26	332d	0	0	2,251
	Masonary Block work Block Work - (B17. 4.1.2)-TSEP-B17-D04	2d	10-Nov-26	11-Nov-26	332d	0	0	369
	JDH3-02-009-B17-Mechanical Works-phase 1	4d	12-Nov-26	16-Nov-26	332d	0	0	2,336
	JDH3-02-009-B17-PPR For Cold Water Supply Piping System	4d	12-Nov-26	16-Nov-26	332d	0	0	2,336

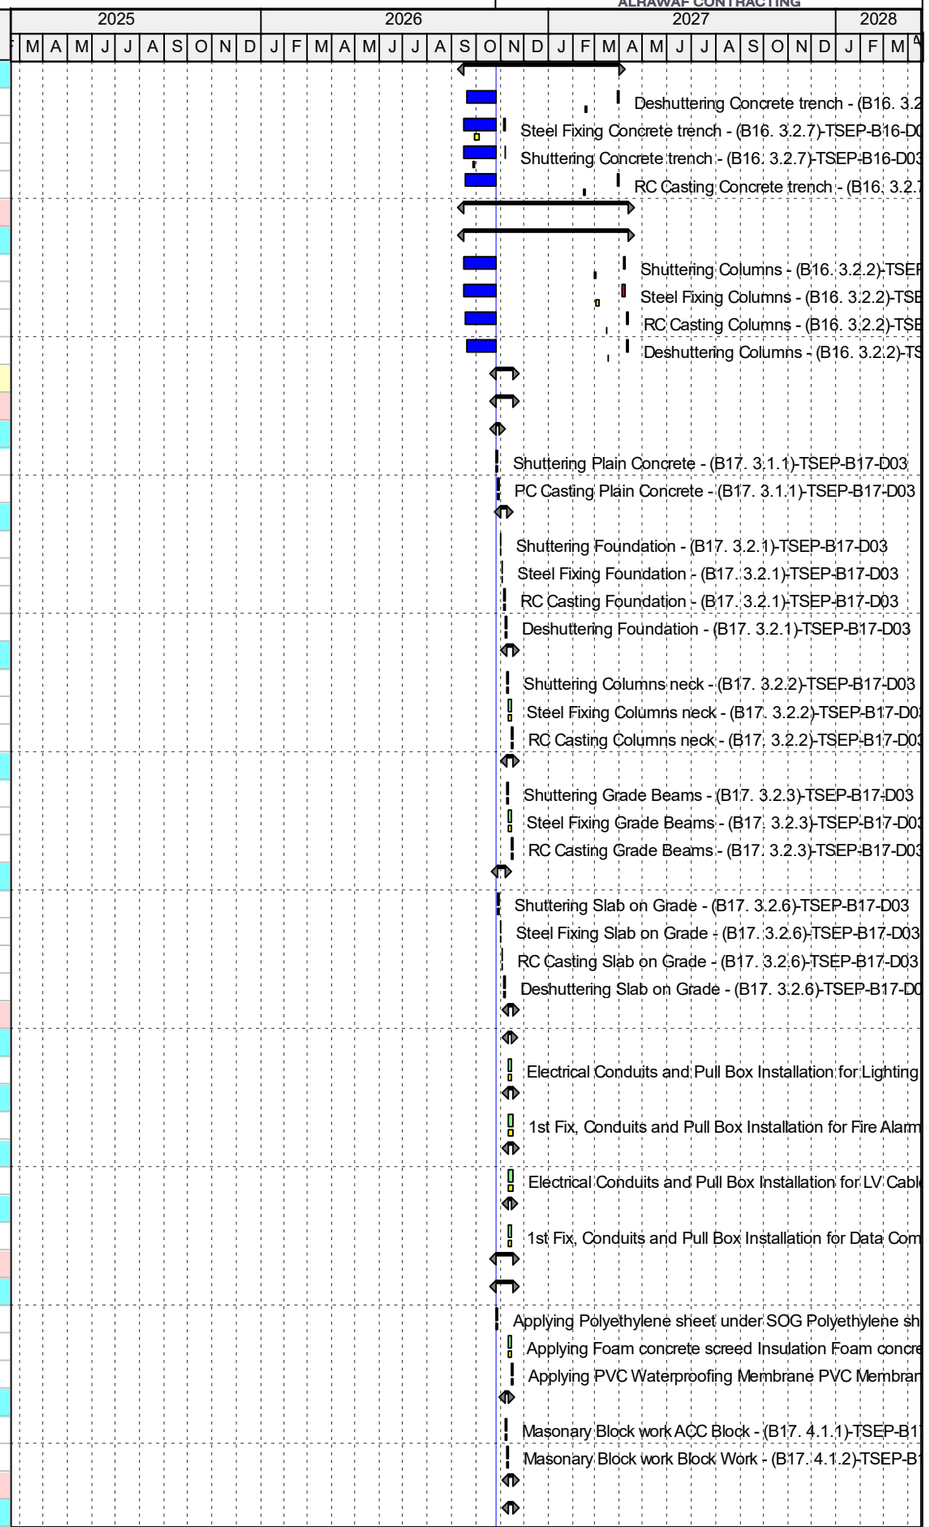


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	PPR Pipes Installation 32 mm - (B17. 15.3.1.1)-TSEP-B17-D15	2d	12-Nov-26	14-Nov-26	332d	0	0	1,005
	PPR Pipes Installation 25 mm - (B17. 15.3.1.2)-TSEP-B17-D15	2d	15-Nov-26	16-Nov-26	332d	0	0	1,331
	JDH3-02-009 -ADMIN BUILDING	41d	28-Jul-26 A	18-Nov-26	250d	0	1,605	49,706
	JDH3-02-009-B18-Site Works	2d	28-Jul-26 A	18-Nov-26	215d	0	1,605	1,783
	JDH3-02-009-B18-Earth work	2d	28-Jul-26 A	18-Nov-26	215d	0	1,605	1,783
	Backfill Layers Works Excavated Material - (B18. 2.2)-TSEP-B1	2d	28-Jul-26 A	18-Nov-26	215d	0	1,605	1,783
	JDH3-02-009-B18-Super Structure	20d	27-Oct-26	18-Nov-26	215d	0	0	25,143
	JDH3-02-009-B18-Roof Beam	6d	27-Oct-26	02-Nov-26	229d	0	0	1,455
	Steel Fixing Roof Beam - (B18. 3.2.6)-TSEP-B18-D03	2d	27-Oct-26	28-Oct-26	229d	0	0	909
	RC Casting Roof Beam - (B18. 3.2.6)-TSEP-B18-D03	2d	29-Oct-26	31-Oct-26	229d	0	0	364
	Deshuttering Roof Beam - (B18. 3.2.6)-TSEP-B18-D03	2d	01-Nov-26	02-Nov-26	229d	0	0	182
	JDH3-02-009-B18-Roof Slab	20d	27-Oct-26	18-Nov-26	215d	0	0	23,688
	Shuttering Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2d	27-Oct-26	28-Oct-26	215d	0	0	4,738
	Steel Fixing Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2d	29-Oct-26	31-Oct-26	215d	0	0	11,844
	RC Casting Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2d	01-Nov-26	02-Nov-26	215d	0	0	4,738
	Deshuttering Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	14d	03-Nov-26	18-Nov-26	215d	0	0	2,369
	JDH3-02-009-B18-Finishes	2d	27-Oct-26	28-Oct-26	249d	0	0	2,259
	JDH3-02-009-B18-Thermal & Moisture Protection	2d	27-Oct-26	28-Oct-26	249d	0	0	2,259
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2d	27-Oct-26	28-Oct-26	249d	0	0	2,259
	JDH3-02-009-B18-Electrical Works for Potable Water Pump Station	4d	27-Oct-26	31-Oct-26	266d	0	0	20,522
	JDH3-02-009-B18-Grounding and Bonding	4d	27-Oct-26	31-Oct-26	266d	0	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	266d	0	0	20,522
	JDH3-02-009 -TSE STO RAGE TANK	47d	25-Jul-26 A	07-Dec-26	352d	0	916,989	1,248,666
	JDH3-02-009-B19-Mechanical Works-phase 1	47d	25-Jul-26 A	07-Dec-26	352d	0	916,989	1,248,666
	JDH3-02-009-B19-Storage Tank	47d	25-Jul-26 A	07-Dec-26	352d	0	916,989	1,248,666
	Laying and Welding of First Ring for Base of shell - (B19. 15.1)	16d	25-Jul-26 A	16-Nov-26	352d	0	299,159	598,319
	Roof Aluminum Cover Installation - (B19. 15.1)-TSEP-B19-D15	13d	29-Jul-26 A	07-Dec-26	352d	0	247,132	260,139
	Roof Steel Structure Installation - (B19. 15.1)-TSEP-B19-D15	10d	28-Jul-26 A	07-Dec-26	352d	0	370,698	390,208
	JDH3-02-009 -CHLORINATION BUILDING	49d	02-Aug-26 A	18-Nov-26	319d	0	906	29,923
	JDH3-02-009-B20-Site Works	2d	02-Aug-26 A	18-Nov-26	278d	0	906	1,007
	JDH3-02-009-B20-Earth work	2d	02-Aug-26 A	18-Nov-26	278d	0	906	1,007
	Backfill Layers Works Excavated Material - (B20. 2.2)-TSEP-B2	2d	02-Aug-26 A	18-Nov-26	278d	0	906	1,007
	JDH3-02-009-B20-Super Structure	20d	27-Oct-26	18-Nov-26	278d	0	0	20,958
	JDH3-02-009-B20-Roof Beam	8d	27-Oct-26	04-Nov-26	290d	0	0	2,214
	Shuttering Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2d	27-Oct-26	28-Oct-26	290d	0	0	443
	Steel Fixing Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2d	29-Oct-26	31-Oct-26	290d	0	0	1,107
	RC Casting Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2d	01-Nov-26	02-Nov-26	290d	0	0	443
	Deshuttering Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2d	03-Nov-26	04-Nov-26	290d	0	0	221
	JDH3-02-009-B20-Roof Slab	20d	27-Oct-26	18-Nov-26	278d	0	0	18,745
	Shuttering Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2d	27-Oct-26	28-Oct-26	278d	0	0	3,749
	Steel Fixing Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2d	29-Oct-26	31-Oct-26	278d	0	0	9,372
	RC Casting Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2d	01-Nov-26	02-Nov-26	278d	0	0	3,749
	Deshuttering Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	14d	03-Nov-26	18-Nov-26	278d	0	0	1,874
	JDH3-02-009-B20-Finishes	2d	27-Oct-26	28-Oct-26	296d	0	0	1,429
	JDH3-02-009-B20-Thermal & Moisture Protection	2d	27-Oct-26	28-Oct-26	296d	0	0	1,429
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2d	27-Oct-26	28-Oct-26	296d	0	0	1,429
	JDH3-02-009-B20-Electrical Works for Potable Water Pump Station	4d	27-Oct-26	31-Oct-26	335d	0	0	6,529
	JDH3-02-009-B20-Grounding and Bonding	4d	27-Oct-26	31-Oct-26	335d	0	0	6,529
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	335d	0	0	6,529
	Close Out	26d	27-Oct-26	25-Nov-26	397d	0	0	0
	As Built Drawing Submittals - SUB-TSE Pump Station - TSEP	15d	27-Oct-26	12-Nov-26	397d	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST	15d	27-Oct-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for Irrigation Pump Building - Four	7d	27-Oct-26	03-Nov-26	405d	0	0	0

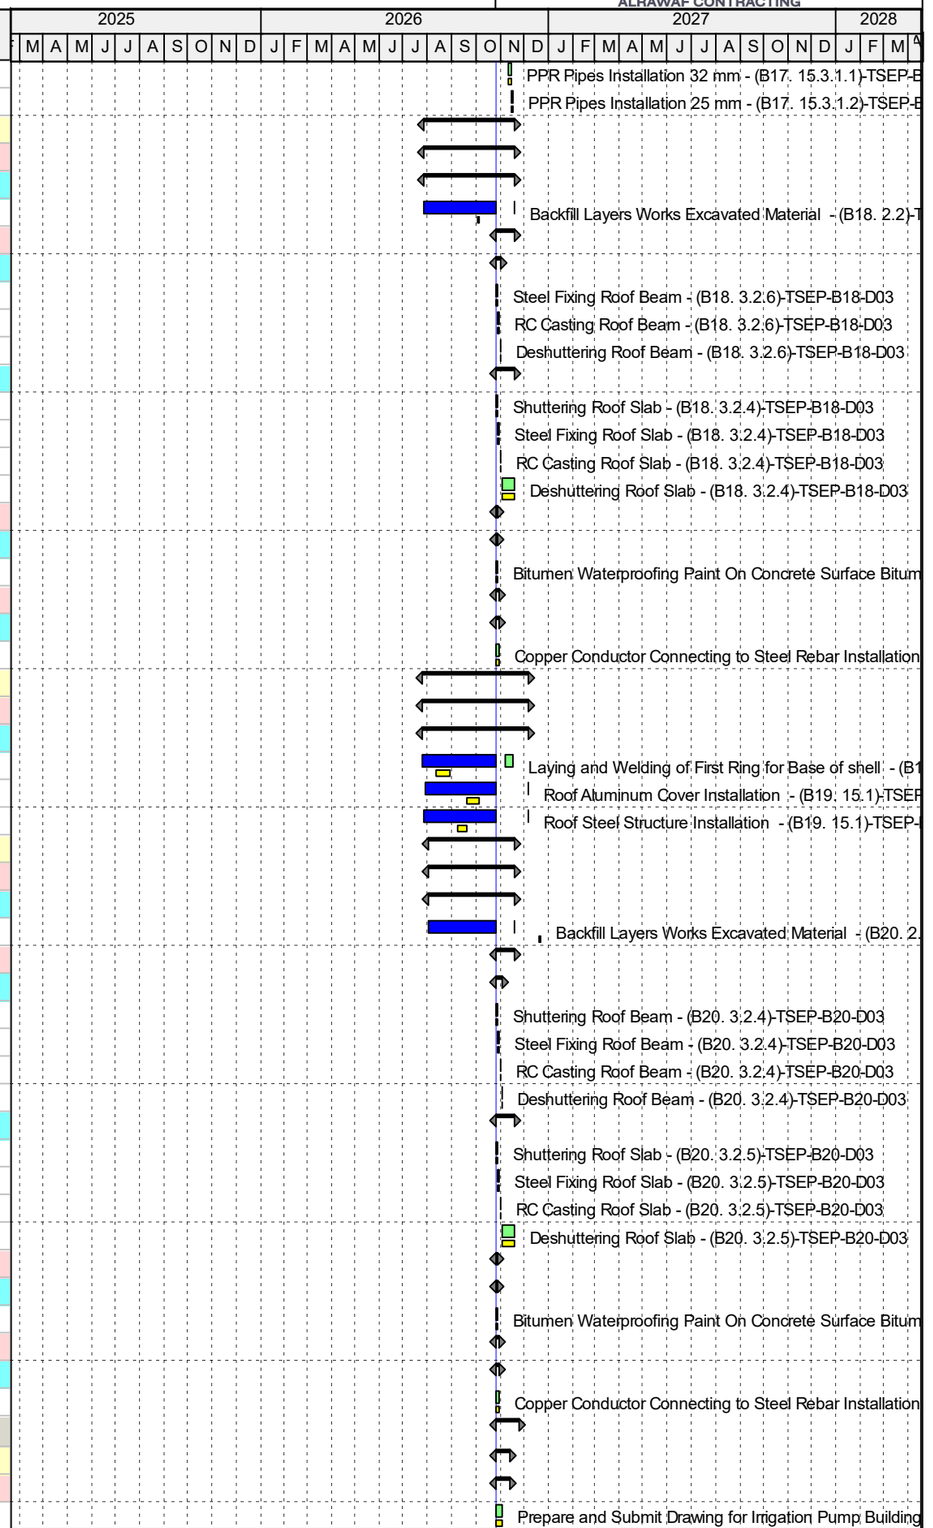

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Prepare and Submit Drawing for Irrigation Pump Building - Grou	7d	05-Nov-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for GLS Tank - Shopdrawings Plar	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Founc	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Colum	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Grade	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof S	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof B	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for SEC Building - Foundation for	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for SEC Building - Grade Beam fo	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Foundat	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Columns	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Grade B	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof for	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof Be	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Plans & Sectior	7d	05-Nov-26	12-Nov-26	397d	0	0	0
As Built Drawing Approvals - APP-TSE Pump Station - TSEP		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Irrigation Pump Building - Foundation f	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Irrigation Pump Building - Ground Bear	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for GLS Tank - Shopdrawings Plan & Sect	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Foundation Sl	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Columns & Ax	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Grade Beam	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Roof Shop Dr	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Administration Building - Roof Beam Sl	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for SEC Building - Foundation for APP-AS	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for SEC Building - Grade Beam for APP-A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Foundation for A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Columns & Axis	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Grade Beam for	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Roof for APP-AS	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Chlorination Building - Roof Beam for A	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDI	Review and Approval for Guard House - Plans & Sections for AF	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDH3-02-009-PW Pump Station		358d	16-Jun-26 A	13-Nov-27	104d	1,265,780	2,823,058	10,030,259
Engineering		18d	27-Oct-26	16-Nov-26	405d	0	0	0
JDH3-02-009-Prequalification and Material Submittals -SUB-PW Station Station -		11d	27-Oct-26	08-Nov-26	412d	0	0	0
JDH3-02-009-Prequalifications and Material prepare and Submit - SU		11d	27-Oct-26	08-Nov-26	412d	0	0	0
JDI	Prepare Material Submittal for Acrylic Paint Materials - EN-AR-SU	11d	27-Oct-26	08-Nov-26	412d	0	0	0
JDH3-02-009-Method of Statement for PW Pump Stations		18d	27-Oct-26	16-Nov-26	384d	0	0	0
JDH3-02-009-Pumps		18d	27-Oct-26	16-Nov-26	344d	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7d	27-Oct-26	03-Nov-26	344d	0	0	0
JDI	Review & approval MS for Pumps- MS	9d	04-Nov-26	16-Nov-26	285d	0	0	0
JDH3-02-009-Duct Works		18d	27-Oct-26	16-Nov-26	365d	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7d	27-Oct-26	03-Nov-26	366d	0	0	0
JDI	Review & approval MS for Duct Works- MS	9d	04-Nov-26	16-Nov-26	303d	0	0	0
JDH3-02-009-Drainage System		18d	27-Oct-26	16-Nov-26	247d	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7d	27-Oct-26	03-Nov-26	248d	0	0	0
JDI	Review & approval MS for Drainage System- MS	9d	04-Nov-26	16-Nov-26	205d	0	0	0
JDH3-02-009-Water Supply System		18d	27-Oct-26	16-Nov-26	336d	0	0	0
JDI	Prepare & Submit MS for Water Supply System- MS	7d	27-Oct-26	03-Nov-26	337d	0	0	0
JDI	Review & approval MS for Water Supply System- MS	9d	04-Nov-26	16-Nov-26	279d	0	0	0
JDH3-02-009-Chlorination System		18d	27-Oct-26	16-Nov-26	360d	0	0	0

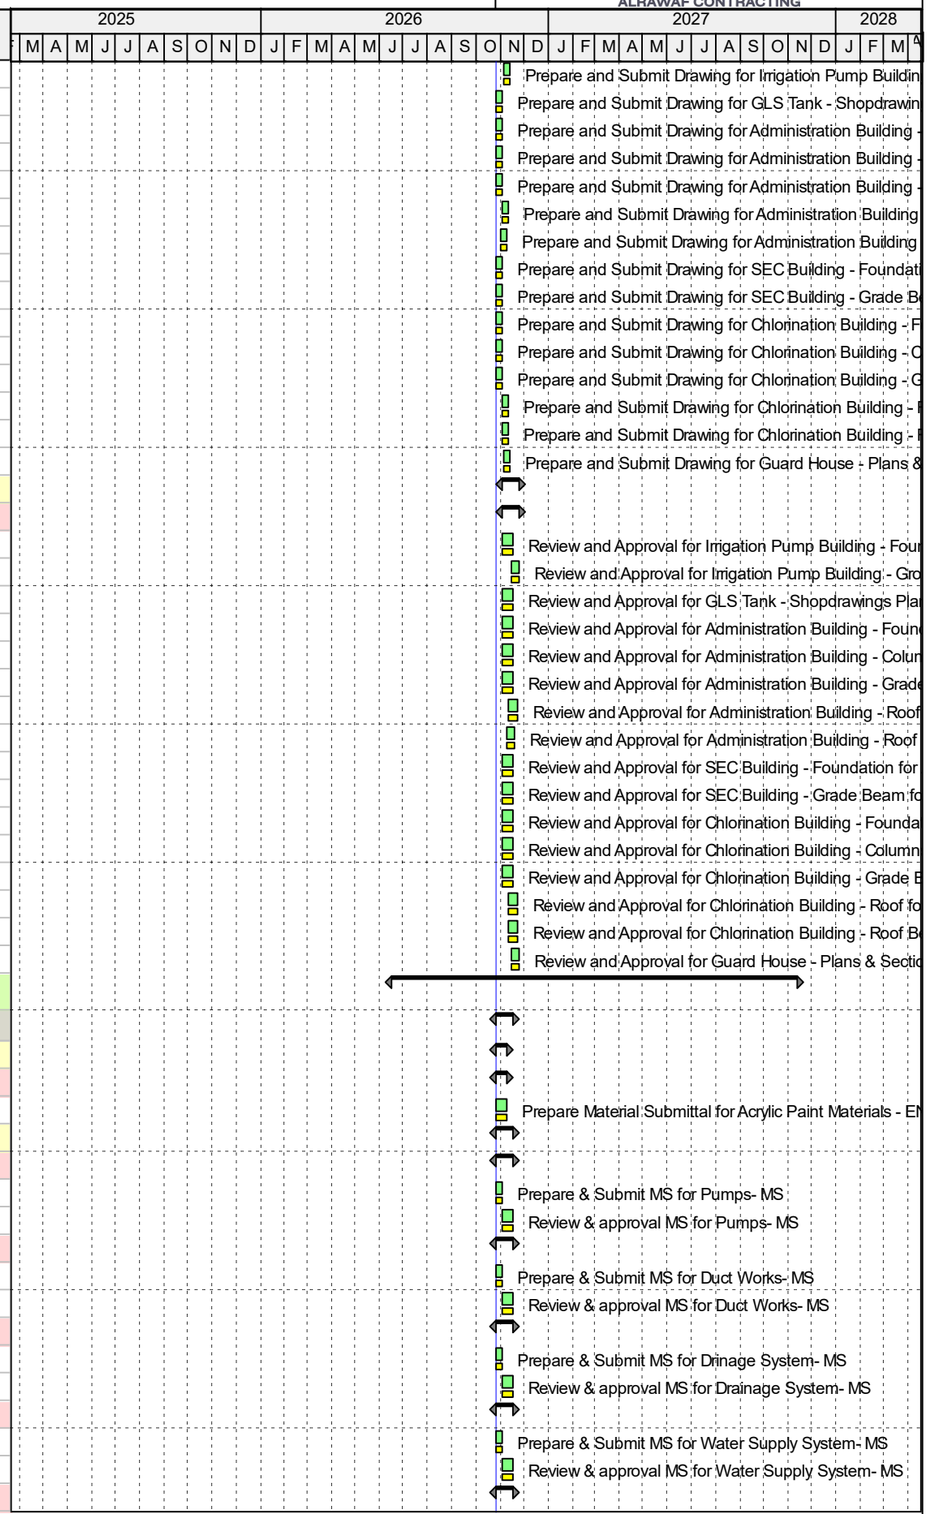


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Prepare & Submit MS for Chlorination System- MS	7d	27-Oct-26	03-Nov-26	361d	0	0	0
JDI	Review & approval MS for Chlorination System- MS	9d	04-Nov-26	16-Nov-26	299d	0	0	0
JDH3-02-009-Over head Crane		18d	27-Oct-26	16-Nov-26	145d	0	0	0
JDI	Prepare & Submit MS for Over head Crane- MS	7d	27-Oct-26	03-Nov-26	145d	0	0	0
JDI	Review & approval MS for Over head Crane- MS	9d	04-Nov-26	16-Nov-26	120d	0	0	0
JDH3-02-009-Access Control		18d	27-Oct-26	16-Nov-26	253d	0	0	0
JDI	Prepare & Submit MS for Access Control- MS	7d	27-Oct-26	03-Nov-26	254d	0	0	0
JDI	Review & approval MS for Access Control- MS	9d	04-Nov-26	16-Nov-26	210d	0	0	0
JDH3-02-009-Data Communication		18d	27-Oct-26	16-Nov-26	205d	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7d	27-Oct-26	03-Nov-26	206d	0	0	0
JDI	Review & approval MS for Data Communication- MS	9d	04-Nov-26	16-Nov-26	170d	0	0	0
JDH3-02-009-Security System		18d	27-Oct-26	16-Nov-26	384d	0	0	0
JDI	Prepare & Submit MS for Security System- MS	7d	27-Oct-26	03-Nov-26	385d	0	0	0
JDI	Review & approval MS for Security System- MS	9d	04-Nov-26	16-Nov-26	319d	0	0	0
JDH3-02-009-Programing Logical Control System		18d	27-Oct-26	16-Nov-26	310d	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7d	27-Oct-26	03-Nov-26	310d	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9d	04-Nov-26	16-Nov-26	257d	0	0	0
Procurement		146d	04-Aug-26 A	15-Feb-27	327d	0	492,877	2,957,261
Long Lead Items		112d	27-Oct-26	15-Feb-27	386d	0	0	985,754
Fabrication - FAB - PW Pump Station		112d	27-Oct-26	15-Feb-27	352d	0	0	0
JDH3-02-009-Long Lead Items - LOL-Manufacturing and Custom Cl		112d	27-Oct-26	15-Feb-27	352d	0	0	0
	Material Fabrication for Addressable Fire Alarm System - PR-TC-	84d	27-Oct-26	18-Jan-27	19d	0	0	0
	Material Fabrication for Access Control System - PR-TC-FAB	84d	27-Oct-26	18-Jan-27	44d	0	0	0
	Material Fabrication for Data Communication System - PR-TC-FA	84d	27-Oct-26	18-Jan-27	365d	0	0	0
	Material Fabrication for Security System - PR-TC-FAB	112d	27-Oct-26	15-Feb-27	352d	0	0	0
Delivery and staging on Site - DOS - PW Pump Station		21d	27-Oct-26	16-Nov-26	477d	0	0	985,754
JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging		21d	27-Oct-26	16-Nov-26	153d	0	0	328,585
	delivery and staging for Surge Protection System - PR-MC-DOS	21d	27-Oct-26	16-Nov-26	153d	0	0	328,585
JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging		10d	27-Oct-26	05-Nov-26	488d	0	0	657,169
	delivery and staging for Transformer (TR) - PR-EL-DOS	10d	27-Oct-26	05-Nov-26	488d	0	0	328,585
	delivery and staging for Main Distribution Boards (MDB) - PR-EL-	10d	27-Oct-26	05-Nov-26	327d	0	0	328,585
Short Lead Items		71d	04-Aug-26 A	29-Nov-26	394d	0	492,877	1,971,507
Purchase Order - PO - PW Pump Station		21d	27-Oct-26	19-Nov-26	402d	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(		21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Epoxy Flooring - PR-AR-PO	21d	27-Oct-26	19-Nov-26	364d	0	0	0
	Material Purchase Order for Acrylic Paint Materials - PR-AR-PO	21d	27-Oct-26	19-Nov-26	385d	0	0	0
	Material Purchase Order for Chain link Fences - PR-AR-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Steel Gates - PR-AR-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(		21d	27-Oct-26	19-Nov-26	402d	0	0	0
	Material Purchase Order for Fuel Oil System - PR-MC-PO	21d	27-Oct-26	19-Nov-26	271d	0	0	0
	Material Purchase Order for Fire Protection System - PR-MC-PO	21d	27-Oct-26	19-Nov-26	238d	0	0	0
	Material Purchase Order for Wall mounted Split Units - PR-MC-P	21d	27-Oct-26	19-Nov-26	247d	0	0	0
	Material Purchase Order for Exhaust Fans - PR-MC-PO	21d	27-Oct-26	19-Nov-26	247d	0	0	0
	Material Purchase Order for Galvanized Iron Sheets for Duct Wo	21d	27-Oct-26	19-Nov-26	247d	0	0	0
	Material Purchase Order for Air Outlets - PR-MC-PO	21d	27-Oct-26	19-Nov-26	402d	0	0	0
Delivery and staging on Site - DOS - PW Pump Station		70d	04-Aug-26 A	29-Nov-26	450d	0	492,877	1,971,507
JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging		70d	04-Aug-26 A	29-Nov-26	288d	0	492,877	1,314,338
	delivery and staging for GRP Tank - PR-MC-DOS	10d	27-Oct-26	05-Nov-26	312d	0	0	328,585
	delivery and staging for Wall mounted Split Units - PR-MC-DOS	10d	04-Aug-26 A	29-Nov-26	288d	0	164,292	328,585
	delivery and staging for Exhaust Fans - PR-MC-DOS	10d	04-Aug-26 A	29-Nov-26	288d	0	164,292	328,585
	delivery and staging for Galvanized Iron Sheets for Duct Works	10d	04-Aug-26 A	29-Nov-26	288d	0	164,292	328,585
JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging		10d	27-Oct-26	05-Nov-26	474d	0	0	657,169
	delivery and staging for Panel Boards - PR-EL-DOS	10d	27-Oct-26	05-Nov-26	327d	0	0	328,585

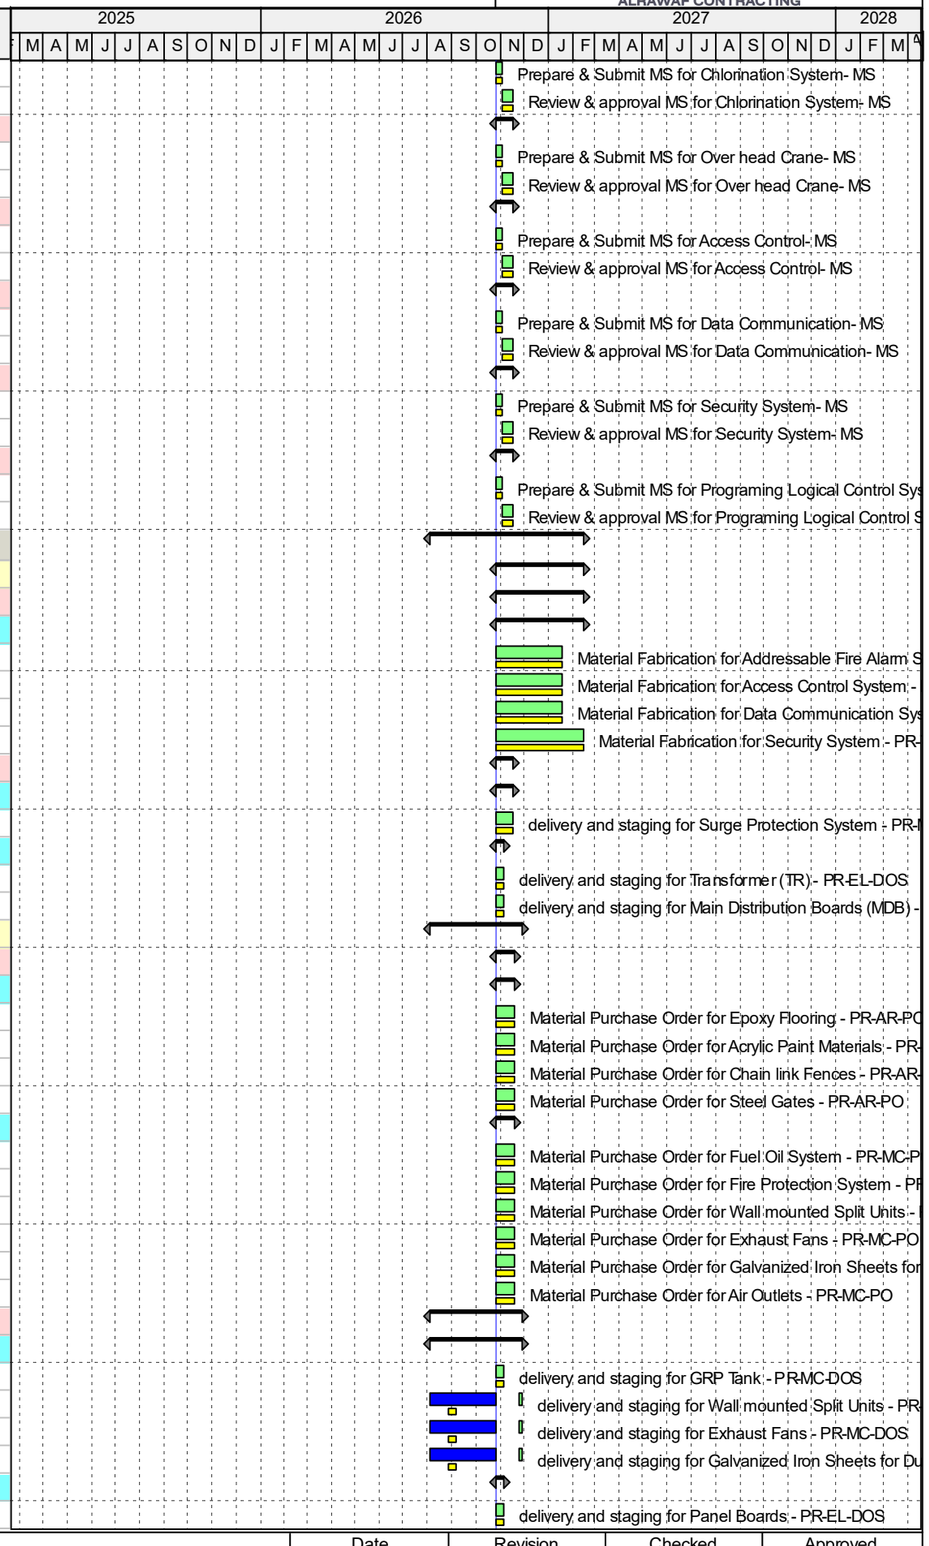


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	delivery and staging for KWH Meter - PR-EL-DOS	10d	27-Oct-26	05-Nov-26	474d	0	0	328,585
Construction		358d	16-Jun-26 A	13-Nov-27	104d	1,265,780	2,330,182	7,072,999
JDH3-02-009-B8-SITE WORK		358d	24-Jun-26 A	13-Nov-27	86d	0	600,511	3,096,849
JDH3-02-009-B8-Site Works		23d	27-Oct-26	22-Nov-26	333d	0	0	855,764
JDH3-02-009-B8-Roads		7d	27-Oct-26	03-Nov-26	137d	0	0	763,520
	Bituminrus base course, Including Prime Coat (MC1) - (B8 2.2.1	4d	27-Oct-26	31-Oct-26	137d	0	0	436,444
	Bituminrus concrete wearing course, Including Tack coat (RC2).	3d	01-Nov-26	03-Nov-26	137d	0	0	327,076
JDH3-02-009-B8-Pavement Markings		16d	04-Nov-26	22-Nov-26	333d	0	0	26,527
	120mm wide centre lane- double line (solid) - M4 - (B8 2.2.3)-P'	5d	04-Nov-26	09-Nov-26	333d	0	0	2,390
	200mm wide. (edge line)-yellow - M1 - (B8 2.2.4)-PWPS-B8-D0	11d	10-Nov-26	22-Nov-26	333d	0	0	24,137
JDH3-02-009-B8-Traffic Signage		12d	04-Nov-26	17-Nov-26	137d	0	0	65,717
	Traffic signs, ground mounted, 1 Sheet Alumenium, (breakawa	12d	04-Nov-26	17-Nov-26	137d	0	0	65,717
JDH3-02-009-B8-Mechanical Works-phase 1		358d	24-Jun-26 A	13-Nov-27	86d	0	600,511	2,241,084
JDH3-02-009-B8-Site Interconnecting Pipes 400 mm		8d	03-Nov-26	11-Nov-26	361d	0	0	1,155,666
	Excavation Works for Ductile Iron Pipe 400 mm - Depth from 2.5	2d	03-Nov-26	04-Nov-26	350d	0	0	231,036
	Soil Replacement and Bedding Works for Ductile Iron Pipe 400	2d	05-Nov-26	07-Nov-26	350d	0	0	57,759
	Pipe.Installationfor Ductile Iron Pipe 400 mm - Depth from 2.51	4d	08-Nov-26	11-Nov-26	350d	0	0	635,348
	Fitting.Installationfor Ductile Iron Pipe 400 mm - Depth from 2.5	4d	08-Nov-26	11-Nov-26	361d	0	0	231,523
JDH3-02-009-B8-Site Interconnecting Pipes 500 mm		344d	24-Jun-26 A	13-Nov-27	86d	0	146,058	243,430
	Pipe.Installationfor Ductile Iron Pipe 500 mm - Depth from 2.51	6d	27-Jun-26 A	06-Feb-27	287d	0	114,760	191,266
	Soil Replacement and Bedding Works for Ductile Iron Pipe 500	2d	24-Jun-26 A	27-Oct-26	366d	0	10,433	17,388
	Backfilling and warning tape Works for Ductile Iron Pipe 500 mn	4d	22-Jul-26 A	13-Nov-27	86d	0	20,865	34,776
JDH3-02-009-B8-Site Interconnecting Pipes 600 mm		2d	27-Oct-26	28-Oct-26	365d	0	0	175
	Soil Replacement and Bedding Works for Ductile Iron Pipe 600	2d	27-Oct-26	28-Oct-26	365d	0	0	175
JDH3-02-009-B8-Site Interconnecting Pipes 800 mm		218d	08-Jul-26 A	27-Feb-27	286d	0	108,234	216,468
	Soil Replacement and Bedding Works for Ductile Iron Pipe 800	2d	09-Jul-26 A	27-Oct-26	363d	0	7,731	15,462
	Backfilling and warning tape Works for Ductile Iron Pipe 800 mn	2d	22-Jul-26 A	27-Feb-27	286d	0	15,462	30,924
	Pipe.Installationfor Ductile Iron Pipe 800 mm - Depth from 2.51	4d	08-Jul-26 A	27-Jan-27	284d	0	85,041	170,082
JDH3-02-009-B8-Site Interconnecting Pipes 1000 mm		322d	11-Aug-26 A	13-Nov-27	84d	0	346,219	494,598
	Pipe.Installationfor Ductile Iron Pipe 1000 mm - Depth from 2.5	4d	13-Aug-26 A	09-Feb-27	289d	0	272,029	388,613
	Soil Replacement and Bedding Works for Ductile Iron Pipe 100(	2d	11-Aug-26 A	27-Oct-26	380d	0	24,730	35,328
	Backfilling and warning tape Works for Ductile Iron Pipe 1000 m	2d	13-Aug-26 A	13-Nov-27	84d	0	49,460	70,657
JDH3-02-009-B8-Connection of main inlet pipe 800 mm with exterr		6d	27-Oct-26	02-Nov-26	350d	0	0	32,586
	Excavation Works for Flow Meter Chamber - - (B8 15.3.1)-PWP	2d	27-Oct-26	28-Oct-26	350d	0	0	7,241
	PC Casting for Flow Meter Chamber - - (B8 15.3.1)-PWPS-B8-D	2d	29-Oct-26	31-Oct-26	350d	0	0	7,241
	Base RC Casting Flow Meter Chamber - (B8 15.3.1)-PWPS-B8-I	2d	01-Nov-26	02-Nov-26	350d	0	0	18,103
JDH3-02-009-B8-Connection of main inlet pipe 1000 mm with exter		6d	27-Oct-26	02-Nov-26	399d	0	0	45,727
	Excavation Works for Flow Meter Chamber - - (B8 15.3.2)-PWP	2d	27-Oct-26	28-Oct-26	399d	0	0	10,162
	PC Casting for Flow Meter Chamber - - (B8 15.3.2)-PWPS-B8-D	2d	29-Oct-26	31-Oct-26	399d	0	0	10,162
	Base RC Casting Flow Meter Chamber - (B8 15.3.2)-PWPS-B8-I	2d	01-Nov-26	02-Nov-26	399d	0	0	25,404
JDH3-02-009-B8-Connection of main overflow pipe 500 mm with ex		4d	27-Oct-26	31-Oct-26	363d	0	0	12,194
	Excavation Works for Ductile Iron Pipe 1200 mm - Depth from 2	2d	27-Oct-26	28-Oct-26	363d	0	0	8,129
	Soil Replacement and Bedding Works for Ductile Iron Pipe 120(	2d	29-Oct-26	31-Oct-26	363d	0	0	4,065
JDH3-02-009-B8-Connection with existing CMZ site and feeding PS		6d	27-Oct-26	02-Nov-26	350d	0	0	3,658
	Excavation Works for Flow Meter Chamber - - (B8 15.3.4)-PWP	2d	27-Oct-26	28-Oct-26	350d	0	0	813
	PC Casting for Flow Meter Chamber - - (B8 15.3.4)-PWPS-B8-D	2d	29-Oct-26	31-Oct-26	350d	0	0	813
	Base RC Casting Flow Meter Chamber - (B8 15.3.4)-PWPS-B8-I	2d	01-Nov-26	02-Nov-26	350d	0	0	2,032
JDH3-02-009-B8-Fuel Tank		4d	27-Oct-26	31-Oct-26	309d	0	0	36,582
	Excavation Works for FRP Fuel Tank - Depth from 1.51 to 2.50-	2d	27-Oct-26	28-Oct-26	309d	0	0	12,194
	Concrete Base Castingfor FRP Fuel Tank - Depth from 1.51 to 2	2d	29-Oct-26	31-Oct-26	309d	0	0	24,388
JDH3-02-009-B9-PUMP STATION		35d	26-Sep-26 A	17-Nov-26	404d	137,878	6,572	177,962
JDH3-02-009-B9-Sub Structure		9d	27-Oct-26	05-Nov-26	210d	33,790	0	33,790
JDH3-02-009-B9-Slab on Grade		9d	27-Oct-26	05-Nov-26	210d	33,790	0	33,790

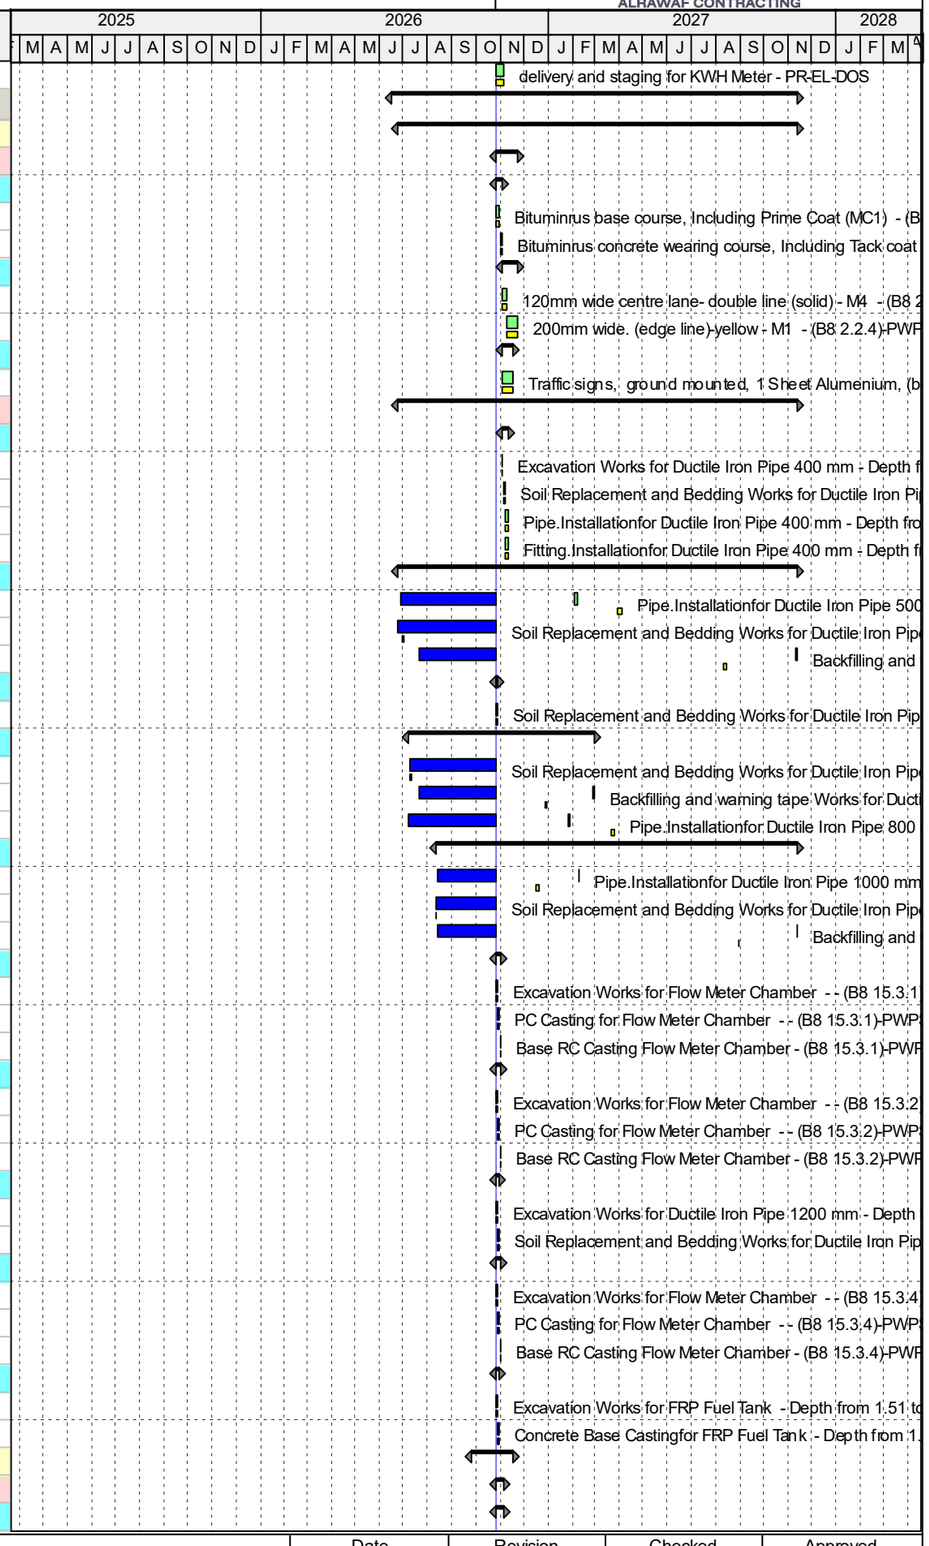


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Shuttering Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2d	27-Oct-26	28-Oct-26	210d	6,758	0	6,758
	Steel Fixing Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	3d	29-Oct-26	01-Nov-26	210d	16,895	0	16,895
	RC Casting Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2d	02-Nov-26	03-Nov-26	210d	6,758	0	6,758
	Deshuttering Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2d	04-Nov-26	05-Nov-26	210d	3,379	0	3,379
JDH3-02-009-B9-Super Structure		35d	26-Sep-26 A	17-Nov-26	218d	29,497	6,572	29,497
JDH3-02-009-B9-Roof Beam		4d	26-Sep-26 A	17-Nov-26	210d	16,290	4,654	16,290
	Steel Fixing Roof Beam - (B9. 3.2.4)-PWPS-B9-D03	2d	27-Sep-26 A	17-Nov-26	210d	11,636	2,327	11,636
	Shuttering Roof Beam - (B9. 3.2.4)-PWPS-B9-D03	2d	26-Sep-26 A	17-Nov-26	210d	4,654	2,327	4,654
JDH3-02-009-B9-Roof Slab		22d	26-Sep-26 A	02-Nov-26	110d	9,590	1,918	9,590
	RC Casting Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2d	29-Oct-26	31-Oct-26	110d	1,918	0	1,918
	Deshuttering Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2d	01-Nov-26	02-Nov-26	110d	959	0	959
	Steel Fixing Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2d	27-Sep-26 A	28-Oct-26	110d	4,795	959	4,795
	Shuttering Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2d	26-Sep-26 A	28-Oct-26	110d	1,918	959	1,918
JDH3-02-009-B9-pump pads		2d	16-Nov-26	17-Nov-26	218d	3,617	0	3,617
	Shuttering Pump Pads - (B9. 3.2.9)-PWPS-B9-D03	2d	16-Nov-26	17-Nov-26	218d	3,617	0	3,617
JDH3-02-009-B9-Finishes		19d	27-Oct-26	17-Nov-26	404d	46,860	0	49,285
JDH3-02-009-B9-Masonary		13d	03-Nov-26	17-Nov-26	115d	34,746	0	34,746
	Masonary Block work Insulated Block Work - (B9. 4.1.1)-PWPS-I	11d	03-Nov-26	15-Nov-26	110d	33,109	0	33,109
	Masonary Block work Block Work - (B9. 4.1.2)-PWPS-B9-D04	2d	16-Nov-26	17-Nov-26	115d	1,637	0	1,637
JDH3-02-009-B9-Thermal & Moisture Protection		11d	27-Oct-26	08-Nov-26	412d	12,114	0	14,538
	Applying Bitumen waterproofing Paint Insulation Bitumen water	7d	27-Oct-26	03-Nov-26	412d	12,114	0	12,114
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	4d	04-Nov-26	08-Nov-26	412d	0	0	2,424
JDH3-02-009-B9-Mechanical Works-phase 1		19d	27-Oct-26	17-Nov-26	370d	2,845	0	40,504
JDH3-02-009-B9-Soakage Pits (For AC Condensated Water)		10d	07-Nov-26	17-Nov-26	210d	2,845	0	2,845
	Soakage Pits Installation 600*600 mm - (B9. 15.8.3.1)-PWPS-E	10d	07-Nov-26	17-Nov-26	210d	2,845	0	2,845
JDH3-02-009-B9-Manhole Works depth 1.50 Diam 600 mm		16d	31-Oct-26	17-Nov-26	370d	0	0	25,912
	Excavation and PC Blinding Works for Manhole 600 mm - - (B9.	3d	31-Oct-26	02-Nov-26	376d	0	0	4,573
	Installation of Basefor Manhole 600 mm - - (B9. 15.8.5.1)-PWP	4d	10-Nov-26	14-Nov-26	370d	0	0	15,243
	MH Ring and C.Slab Works and Backfilling Worksfor Manhole 6(	3d	15-Nov-26	17-Nov-26	370d	0	0	6,097
JDH3-02-009-B9-Manhole Works depth 2.00 Diam 600 mm		12d	27-Oct-26	09-Nov-26	370d	0	0	11,747
	Excavation and PC Blinding Works for Manhole 600 mm - - (B9.	3d	27-Oct-26	29-Oct-26	370d	0	0	2,073
	Installation of Basefor Manhole 600 mm - - (B9. 15.8.5.2)-PWP	5d	31-Oct-26	04-Nov-26	370d	0	0	6,910
	MH Ring and C.Slab Works and Backfilling Worksfor Manhole 6(	4d	05-Nov-26	09-Nov-26	370d	0	0	2,764
JDH3-02-009-B9-Electrical Works for Potable Water Pump Station		19d	27-Oct-26	17-Nov-26	343d	24,885	0	24,885
JDH3-02-009-B9-LED Interior Lighting		2d	16-Nov-26	17-Nov-26	112d	4,363	0	4,363
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	16-Nov-26	17-Nov-26	112d	4,363	0	4,363
JDH3-02-009-B9-Grounding and Bonding		4d	27-Oct-26	31-Oct-26	358d	20,522	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	358d	20,522	0	20,522
JDH3-02-009-B10-GUARD HOUSE		22d	27-Oct-26	21-Nov-26	401d	6,054	0	14,950
JDH3-02-009-B10-Sub Structure		8d	29-Oct-26	07-Nov-26	201d	1,852	0	1,852
JDH3-02-009-B10-Slab on Grade		8d	29-Oct-26	07-Nov-26	201d	1,852	0	1,852
	Shuttering Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2d	29-Oct-26	31-Oct-26	201d	370	0	370
	Steel Fixing Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2d	01-Nov-26	02-Nov-26	201d	926	0	926
	RC Casting Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2d	03-Nov-26	04-Nov-26	201d	370	0	370
	Deshuttering Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2d	05-Nov-26	07-Nov-26	201d	185	0	185
JDH3-02-009-B10-Finishes		16d	27-Oct-26	14-Nov-26	407d	2,716	0	3,728
JDH3-02-009-B10-Masonary		4d	08-Nov-26	11-Nov-26	201d	2,616	0	2,616
	Masonary Block work ACC Block - (B10. 4.1.1)-PWPS-B10-D04	2d	08-Nov-26	09-Nov-26	201d	2,263	0	2,263
	Masonary Block work Block Work - (B10. 4.1.2)-PWPS-B10-D04	2d	10-Nov-26	11-Nov-26	201d	353	0	353
JDH3-02-009-B10-Thermal & Moisture Protection		16d	27-Oct-26	14-Nov-26	407d	101	0	1,112
	Applying Bitumen waterproofing Paint Insulation Bitumen water	2d	27-Oct-26	28-Oct-26	421d	0	0	501
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	2d	27-Oct-26	28-Oct-26	201d	101	0	101
	Applying Foam concrete screed Insulation Foam concrete - (B1	2d	12-Nov-26	14-Nov-26	210d	0	0	511

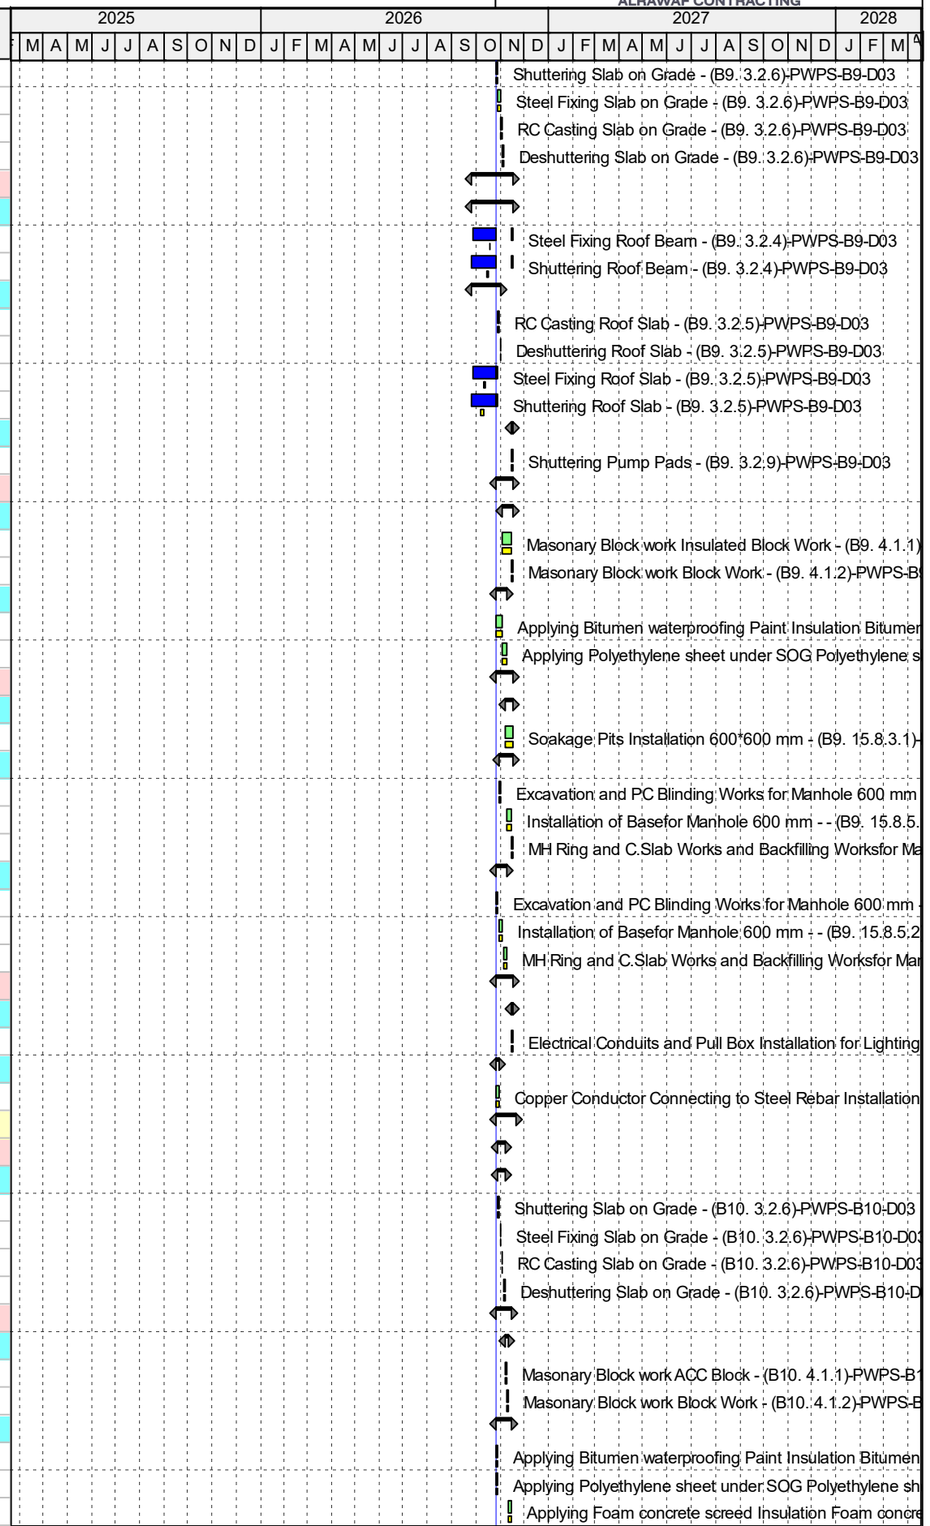


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-B10-Mechanical Works-phase 1	4d	12-Nov-26	16-Nov-26	208d	0	0	2,336
	JDH3-02-009-B10-PPR For Cold Water Supply Piping System	4d	12-Nov-26	16-Nov-26	208d	0	0	2,336
	PPR Pipes Installation 32 mm - (B10. 15.3.1.1)-PWPS-B10-D15	2d	12-Nov-26	14-Nov-26	208d	0	0	1,005
	PPR Pipes Installation 25 mm - (B10. 15.3.1.2)-PWPS-B10-D15	2d	15-Nov-26	16-Nov-26	208d	0	0	1,331
	JDH3-02-009-B10-Electrical Works for Potable Water Pump Station	22d	27-Oct-26	21-Nov-26	219d	1,486	0	7,035
	JDH3-02-009-B10-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+	8d	12-Nov-26	21-Nov-26	201d	1,486	0	1,486
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	8d	12-Nov-26	21-Nov-26	201d	1,486	0	1,486
	JDH3-02-009-B10-LED Interior Lighting	2d	12-Nov-26	14-Nov-26	210d	0	0	303
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	12-Nov-26	14-Nov-26	210d	0	0	303
	JDH3-02-009-B10-Grounding and Bonding	4d	27-Oct-26	31-Oct-26	237d	0	0	4,897
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	237d	0	0	4,897
	JDH3-02-009-B10-Addressable Fire-Alarm System	4d	12-Nov-26	16-Nov-26	210d	0	0	349
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B10.	4d	12-Nov-26	16-Nov-26	210d	0	0	349
	JDH3-02-009-B11-ADMIN BUILDING	75d	13-Aug-26 A	18-Nov-26	403d	0	1,564	106,377
	JDH3-02-009-B11-Sub Structure	8d	29-Oct-26	07-Nov-26	413d	0	0	13,752
	JDH3-02-009-B11-Slab on Grade	8d	29-Oct-26	07-Nov-26	413d	0	0	13,752
	Shuttering Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2d	29-Oct-26	31-Oct-26	397d	0	0	2,750
	Steel Fixing Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2d	01-Nov-26	02-Nov-26	397d	0	0	6,876
	RC Casting Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2d	03-Nov-26	04-Nov-26	397d	0	0	2,750
	Deshuttering Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2d	05-Nov-26	07-Nov-26	413d	0	0	1,375
	JDH3-02-009-B11-Super Structure	5d	14-Nov-26	18-Nov-26	258d	0	0	2,629
	JDH3-02-009-B11-Entrance and Ramps	5d	14-Nov-26	18-Nov-26	258d	0	0	2,629
	Shuttering Landing & Steel Ladder Pad - (B11. 3.2.7)-PWPS-B1	2d	14-Nov-26	15-Nov-26	258d	0	0	751
	Steel Fixing Landing & Steel Ladder Pad - (B11. 3.2.7)-PWPS-E	3d	16-Nov-26	18-Nov-26	258d	0	0	1,878
	JDH3-02-009-B11-Finishes	19d	27-Oct-26	17-Nov-26	380d	0	0	59,041
	JDH3-02-009-B11-Masonary	6d	27-Oct-26	02-Nov-26	257d	0	0	13,121
	Masonary Block work Insulated Masonary Unit - (B11. 4.1.1)-PW	2d	27-Oct-26	28-Oct-26	255d	0	0	5,918
	Masonary Block work Block Work - (B11. 4.1.2)-PWPS-B11-D04	2d	29-Oct-26	31-Oct-26	257d	0	0	1,919
	Masonary Block work Block Work - (B11. 4.1.3)-PWPS-B11-D04	4d	29-Oct-26	02-Nov-26	255d	0	0	3,333
	Precast Concrete Scupper Scrupper - (B11. 4.2)-PWPS-B11-D0	2d	01-Nov-26	02-Nov-26	257d	0	0	1,951
	JDH3-02-009-B11-Metals	2d	16-Nov-26	17-Nov-26	259d	0	0	17,654
	Steel Ladder Installation Aluminum Canopy Shade - (B11. 5.2)-I	2d	16-Nov-26	17-Nov-26	259d	0	0	17,654
	JDH3-02-009-B11-Thermal & Moisture Protection	8d	27-Oct-26	04-Nov-26	391d	0	0	4,939
	Polyethylene Sheet Under SOG Polyethylene sheet - (B11. 7.1)	2d	27-Oct-26	28-Oct-26	397d	0	0	520
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2d	27-Oct-26	28-Oct-26	259d	0	0	2,238
	Liquid Applied Waterproofing Membrane For Toilets Liquid Wate	2d	03-Nov-26	04-Nov-26	255d	0	0	2,181
	JDH3-02-009-B11-Architecture Finishes	6d	09-Nov-26	15-Nov-26	259d	0	0	23,326
	Internal Cement Plaster For Walls 15 mm - (B11. 9.2.1)-PWPS-I	2d	09-Nov-26	10-Nov-26	255d	0	0	6,903
	External Cement Plaster For Walls Cement Plaster - (B11. 9.3.1	2d	11-Nov-26	12-Nov-26	255d	0	0	9,040
	External Acrylic Paint For Walls - (B11. 9.3.2)-PWPS-B11-D09	2d	14-Nov-26	15-Nov-26	255d	0	0	5,056
	Plaster On Internal Ceiling Cement Plaster - (B11. 9.4.3)-PWPS	2d	11-Nov-26	12-Nov-26	259d	0	0	604
	Acrylic Paint Applied On Plaster Acrylic Paint - (B11. 9.4.4)-PWF	2d	14-Nov-26	15-Nov-26	259d	0	0	1,724
	JDH3-02-009-B11-Electrical Works for Potable Water Pump Station	66d	13-Aug-26 A	16-Nov-26	405d	0	1,564	30,955
	JDH3-02-009-B11-LV Cables - Copper, 4Cx10mm2 CU/XLPE/SWA/I	3d	05-Nov-26	08-Nov-26	255d	0	0	495
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	3d	05-Nov-26	08-Nov-26	255d	0	0	495
	JDH3-02-009-B11-LED Interior Lighting	2d	05-Nov-26	07-Nov-26	256d	0	0	2,116
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	05-Nov-26	07-Nov-26	256d	0	0	2,116
	JDH3-02-009-B11-Grounding and Bonding	4d	27-Oct-26	31-Oct-26	419d	0	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	419d	0	0	20,522
	JDH3-02-009-B11-Data Communications	4d	13-Aug-26 A	04-Nov-26	258d	0	289	1,445
	1st Fix, Conduits and Pull Box Installation for Data Communicat	4d	13-Aug-26 A	04-Nov-26	258d	0	289	1,445
	JDH3-02-009-B11-Addressable Fire-Alarm System	4d	13-Aug-26 A	16-Nov-26	254d	0	622	3,111
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B11.	4d	13-Aug-26 A	16-Nov-26	254d	0	622	3,111

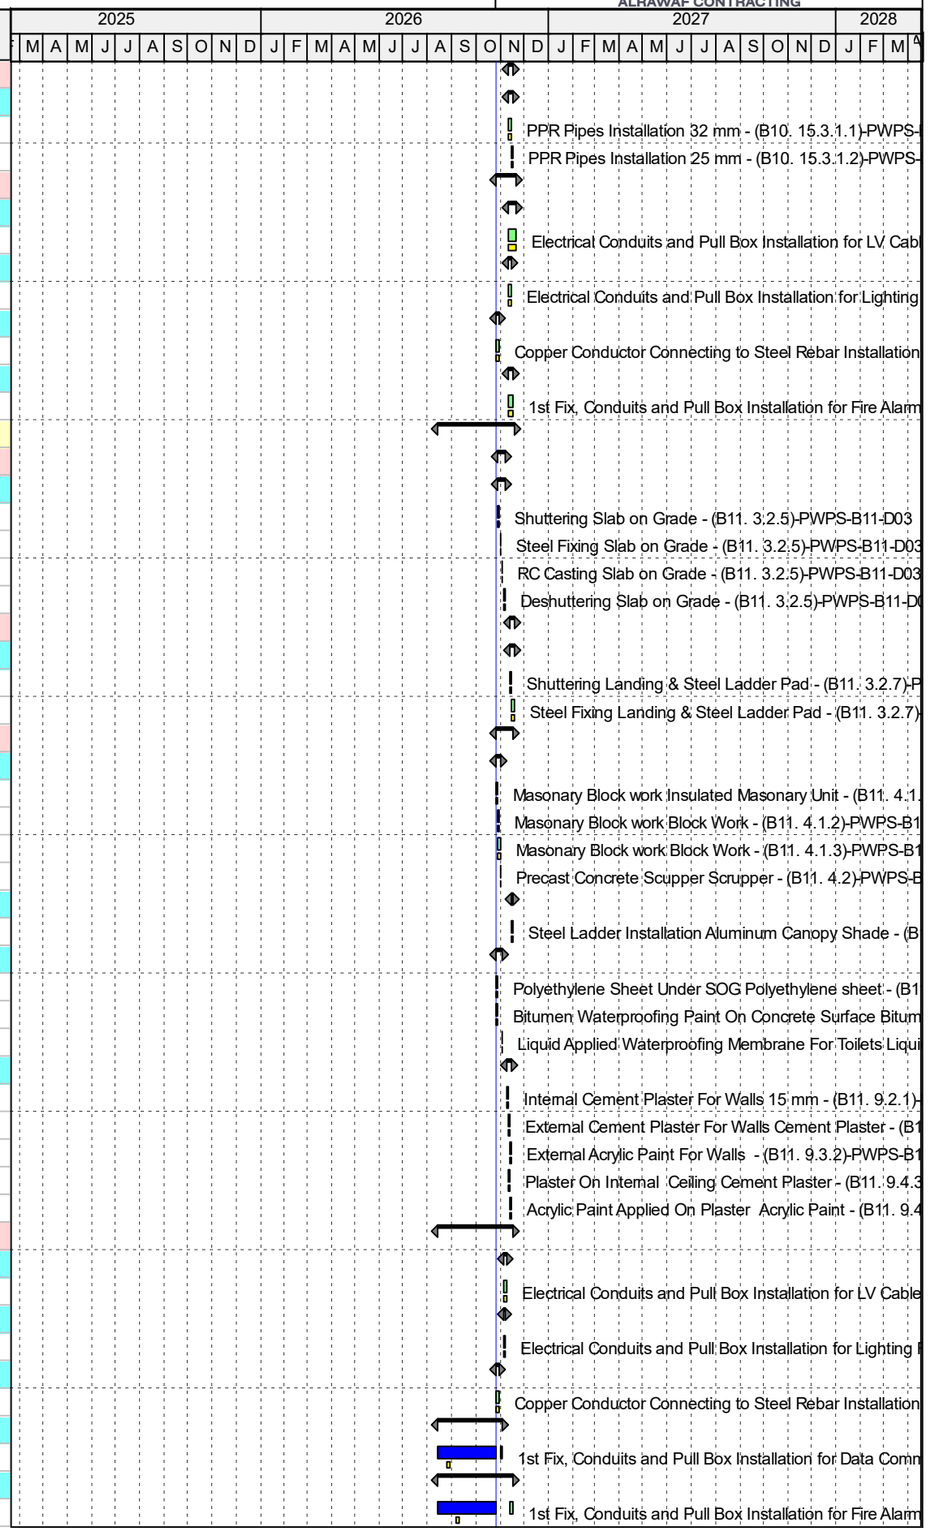


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-B11-Access control system	4d	13-Aug-26 A	16-Nov-26	254d	0	412	2,060
	1st Fix, Conduits and Pull Box Installation for Access control - (B	4d	13-Aug-26 A	16-Nov-26	254d	0	412	2,060
	JDH3-02-009-B11-CCTV system	2d	13-Aug-26 A	02-Nov-26	260d	0	241	1,207
	1st Fix, Conduits and Pull Box Installation for CCTV Camera - (E	2d	13-Aug-26 A	02-Nov-26	260d	0	241	1,207
	JDH3-02-009-B12-POTABLE WATER TANK	151d	16-Jun-26 A	15-Dec-26	240d	1,121,848	1,719,354	3,560,648
	JDH3-02-009-B12-Mechanical Works-phase 1	151d	16-Jun-26 A	15-Dec-26	240d	1,121,848	1,719,354	3,560,648
	JDH3-02-009-B12-Storage Tank 2	151d	16-Jun-26 A	15-Dec-26	240d	1,121,848	1,719,354	3,560,648
	Laying and Welding of second Ring - (B12. 15.1.2)-PWPS-B12	17d	05-Nov-26	25-Nov-26	240d	0	0	1,219,400
	Laying and Welding of First Ring for Base of shell - (B12. 15.1.:	17d	16-Jun-26 A	05-Nov-26	240d	1,121,848	560,924	1,121,848
	Roof Aluminum Cover Installation - (B12. 15.1.2)-PWPS-B12-D	17d	21-Jul-26 A	15-Dec-26	240d	0	463,372	487,760
	Roof Steel Structure Installation - (B12. 15.1.2)-PWPS-B12-D1!	17d	24-Jun-26 A	15-Dec-26	240d	0	695,058	731,640
	JDH3-02-009-B13-CHLORINATION BUILDING	76d	15-Aug-26 A	16-Nov-26	405d	0	2,180	116,214
	JDH3-02-009-B13-Super Structure	13d	02-Nov-26	16-Nov-26	359d	0	0	6,968
	JDH3-02-009-B13-Entrance and Ramps	4d	12-Nov-26	16-Nov-26	359d	0	0	1,397
	Shuttering Landing & Steel Ladder Pad - (B13. 3.2.7)-PWPS-B	2d	12-Nov-26	14-Nov-26	359d	0	0	399
	Steel Fixing Landing & Steel Ladder Pad - (B13. 3.2.7)-PWPS-E	2d	15-Nov-26	16-Nov-26	359d	0	0	998
	JDH3-02-009-B13-Mechanical Equipment Pads	9d	02-Nov-26	11-Nov-26	359d	0	0	5,571
	Shuttering Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2d	02-Nov-26	03-Nov-26	359d	0	0	1,114
	Steel Fixing Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	3d	04-Nov-26	07-Nov-26	359d	0	0	2,786
	RC Casting Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2d	08-Nov-26	09-Nov-26	359d	0	0	1,114
	Deshuttering Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2d	10-Nov-26	11-Nov-26	359d	0	0	557
	JDH3-02-009-B13-Finishes	18d	27-Oct-26	16-Nov-26	405d	0	0	76,235
	JDH3-02-009-B13-Masonary	3d	27-Oct-26	29-Oct-26	332d	0	0	8,929
	Masonary Block work Insulated Masonary Unit - (B13. 4.1.1)-PW	3d	27-Oct-26	29-Oct-26	332d	0	0	8,929
	JDH3-02-009-B13-Metals	2d	08-Nov-26	09-Nov-26	332d	0	0	31,777
	Steel Ladder Installation Steel Ladder - (B13. 5.1.1)-PWPS-B13	2d	08-Nov-26	09-Nov-26	332d	0	0	31,777
	JDH3-02-009-B13-Thermal & Moisture Protection	13d	27-Oct-26	10-Nov-26	410d	0	0	13,489
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2d	27-Oct-26	28-Oct-26	421d	0	0	1,487
	Polyethylene Sheet Under SOG Polyethylene sheet - (B13. 7.2)	2d	27-Oct-26	28-Oct-26	369d	0	0	369
	Concrete Screed Foam - (B13. 7.3.1)-PWPS-B13-D07	2d	31-Oct-26	01-Nov-26	333d	0	0	2,169
	Waterproofing Membrane PVC - (B13. 7.3.2)-PWPS-B13-D07	2d	02-Nov-26	03-Nov-26	333d	0	0	3,023
	Installation Of Rigid Insulation Extruded Polystyrene - (B13. 7.3.	2d	07-Nov-26	08-Nov-26	340d	0	0	5,981
	Geotextile Sheet Geotextile Sheet - (B13. 7.3.4)-PWPS-B13-D0	2d	09-Nov-26	10-Nov-26	340d	0	0	460
	JDH3-02-009-B13-Architecture Finishes	15d	31-Oct-26	16-Nov-26	332d	0	0	22,040
	Internal Cement Plaster For Walls 25 mm - (B13. 9.2.1)-PWPS-I	2d	08-Nov-26	09-Nov-26	332d	0	0	2,876
	External Cement Plaster For Walls Cement Plaster - (B13. 9.2.2	2d	31-Oct-26	01-Nov-26	332d	0	0	9,556
	External Acrylic Paint For Walls - (B13. 9.2.3)-PWPS-B13-D09	5d	02-Nov-26	07-Nov-26	332d	0	0	4,212
	Alkyd Enamel Paint For Internal Walls - (B13. 9.2.4)-PWPS-B1	2d	15-Nov-26	16-Nov-26	332d	0	0	2,064
	Plaster On Internal Ceiling Cement Plaster - (B13. 9.3.1)-PWPS	2d	10-Nov-26	11-Nov-26	332d	0	0	2,128
	Acrylic Paint Applied for Internal Ceiling Acrylic Paint - (B13. 9.3.	2d	12-Nov-26	14-Nov-26	332d	0	0	1,203
	JDH3-02-009-B13-Mechanical Works-phase 1	31d	19-Sep-26 A	16-Nov-26	357d	0	1,016	15,551
	JDH3-02-009-B13-HVAC System	4d	08-Nov-26	11-Nov-26	332d	0	0	4,065
	Sand Trap Louvers Installation - (B13. 15.3.2)-PWPS-B13-D15	4d	08-Nov-26	11-Nov-26	332d	0	0	4,065
	JDH3-02-009-B13-Water Supply System	4d	29-Oct-26	02-Nov-26	369d	0	0	2,626
	Cold Water Pipes Installation PPR 32 mm - (B13. 15.4.1.1)-PWI	2d	29-Oct-26	31-Oct-26	369d	0	0	1,331
	Cold Water Pipes Installation PPR 25 mm - (B13. 15.4.1.2)-PWI	2d	01-Nov-26	02-Nov-26	369d	0	0	1,295
	JDH3-02-009-B13-Sewer And Drainage System	26d	19-Sep-26 A	16-Nov-26	357d	0	1,016	8,861
	Roof Drain Installation - (B13. 15.5.1)-PWPS-B13-D15	2d	04-Nov-26	05-Nov-26	333d	0	0	6,829
	Drainage Pipe Installation UPVC 75 mm - (B13. 15.5.3.1)-PWPS	2d	19-Sep-26 A	16-Nov-26	357d	0	1,016	2,032
	JDH3-02-009-B13-Electrical Works for Potable Water Pump Station	73d	15-Aug-26 A	12-Nov-26	408d	0	1,164	17,459
	JDH3-02-009-B13-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+	7d	31-Oct-26	07-Nov-26	332d	0	0	1,238
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	3d	31-Oct-26	02-Nov-26	332d	0	0	495
	Cable Tray Installation for LV Cables 4Cx10 mm²- (B13. 16.1.1)	4d	03-Nov-26	07-Nov-26	332d	0	0	743

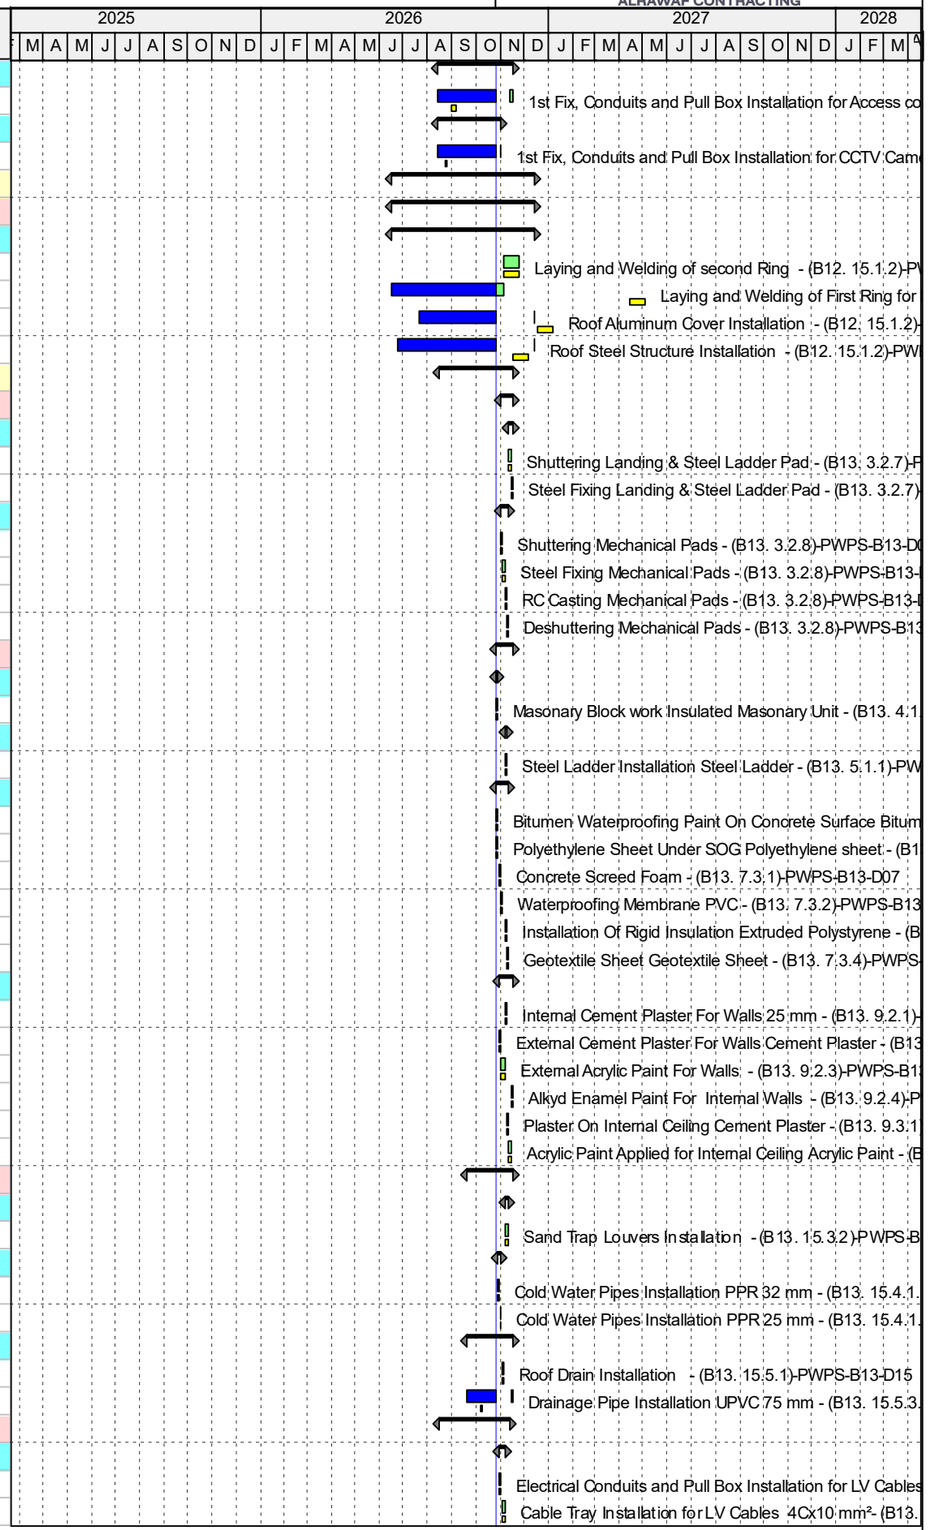


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-B13-LED Interior Lighting	2d	31-Oct-26	01-Nov-26	337d	0	0	606
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2d	31-Oct-26	01-Nov-26	337d	0	0	606
	JDH3-02-009-B13-Grounding and Bonding	15d	27-Oct-26	12-Nov-26	408d	0	0	9,794
	Copper Conductor Connecting to Steel Rebar Installation for Co	4d	27-Oct-26	31-Oct-26	419d	0	0	6,529
	Earth pits Installation for Copper Rods - (B13. 16.5.1)-PWPS-B1	4d	02-Nov-26	05-Nov-26	344d	0	0	1,632
	Earth Bars Installation for Copper Rods - (B13. 16.5.1)-PWPS-B	6d	07-Nov-26	12-Nov-26	344d	0	0	1,632
	JDH3-02-009-B13-Addressable Fire-Alarm System	4d	15-Aug-26 A	31-Oct-26	339d	0	65	324
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B13.	4d	15-Aug-26 A	31-Oct-26	339d	0	65	324
	JDH3-02-009-B13-Data Communications	2d	15-Aug-26 A	29-Oct-26	337d	0	15	73
	1st Fix, Conduits and Pull Box Installation for Data Communicat	2d	15-Aug-26 A	29-Oct-26	337d	0	15	73
	JDH3-02-009-B13-Access control system	4d	15-Aug-26 A	01-Nov-26	337d	0	967	4,837
	1st Fix, Conduits and Pull Box Installation for Access control - (B	4d	15-Aug-26 A	01-Nov-26	337d	0	967	4,837
	JDH3-02-009-B13-CCTV system	2d	15-Aug-26 A	29-Oct-26	339d	0	117	585
	1st Fix, Conduits and Pull Box Installation for CCTV Camera - (E	2d	15-Aug-26 A	29-Oct-26	339d	0	117	585
Close Out		26d	27-Oct-26	25-Nov-26	397d	0	0	0
As Built Drawing Submittals - SUB-PW Pump Station - PWPS		15d	27-Oct-26	12-Nov-26	397d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		15d	27-Oct-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Columns	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Foundatic	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Slab On (	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Ground B	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Roof for S	7d	01-Nov-26	08-Nov-26	401d	0	0	0
JDI	Prepare and Submit Drawing for GLS1 Tank - Shopdrawings Pla	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for GLS2 Tank - Shopdrawings Pla	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Founc	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Colum	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Slab (	7d	05-Nov-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Grade	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof S	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof E	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Foundat	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Columns	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Grade B	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof for	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof Be	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Foundation & C	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Plans & Sectior	7d	05-Nov-26	12-Nov-26	397d	0	0	0
JDI	Prepare and Submit Drawing for Valve Chamber - Raft for SUB-,	7d	03-Nov-26	10-Nov-26	399d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Mechanical - MC		7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDI	Prepare and Submit Drawing for Water Tank 1 Piping System fo	7d	27-Oct-26	03-Nov-26	405d	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Roads - RD		7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Overall Road Layout Plan for S	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Road Layout Plan - Sheet 01 (	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Roads Profiles for SUB-AS-PW	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Roads Finish Grading Overall F	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Typical Road Details for SUB-A	7d	04-Nov-26	11-Nov-26	398d	0	0	0
JDI	Prepare and Submit Drawing for Swept Path Analysis for SUB-A	7d	04-Nov-26	11-Nov-26	398d	0	0	0
As Built Drawing Approvals - APP-PW Pump Station - PWPS		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		16d	04-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for PW Pump Building - Columns for APP-	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for PW Pump Building - Foundation for AF	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for PW Pump Building - Slab On Grade fo	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for PW Pump Building - Ground Beam for	9d	04-Nov-26	16-Nov-26	336d	0	0	0

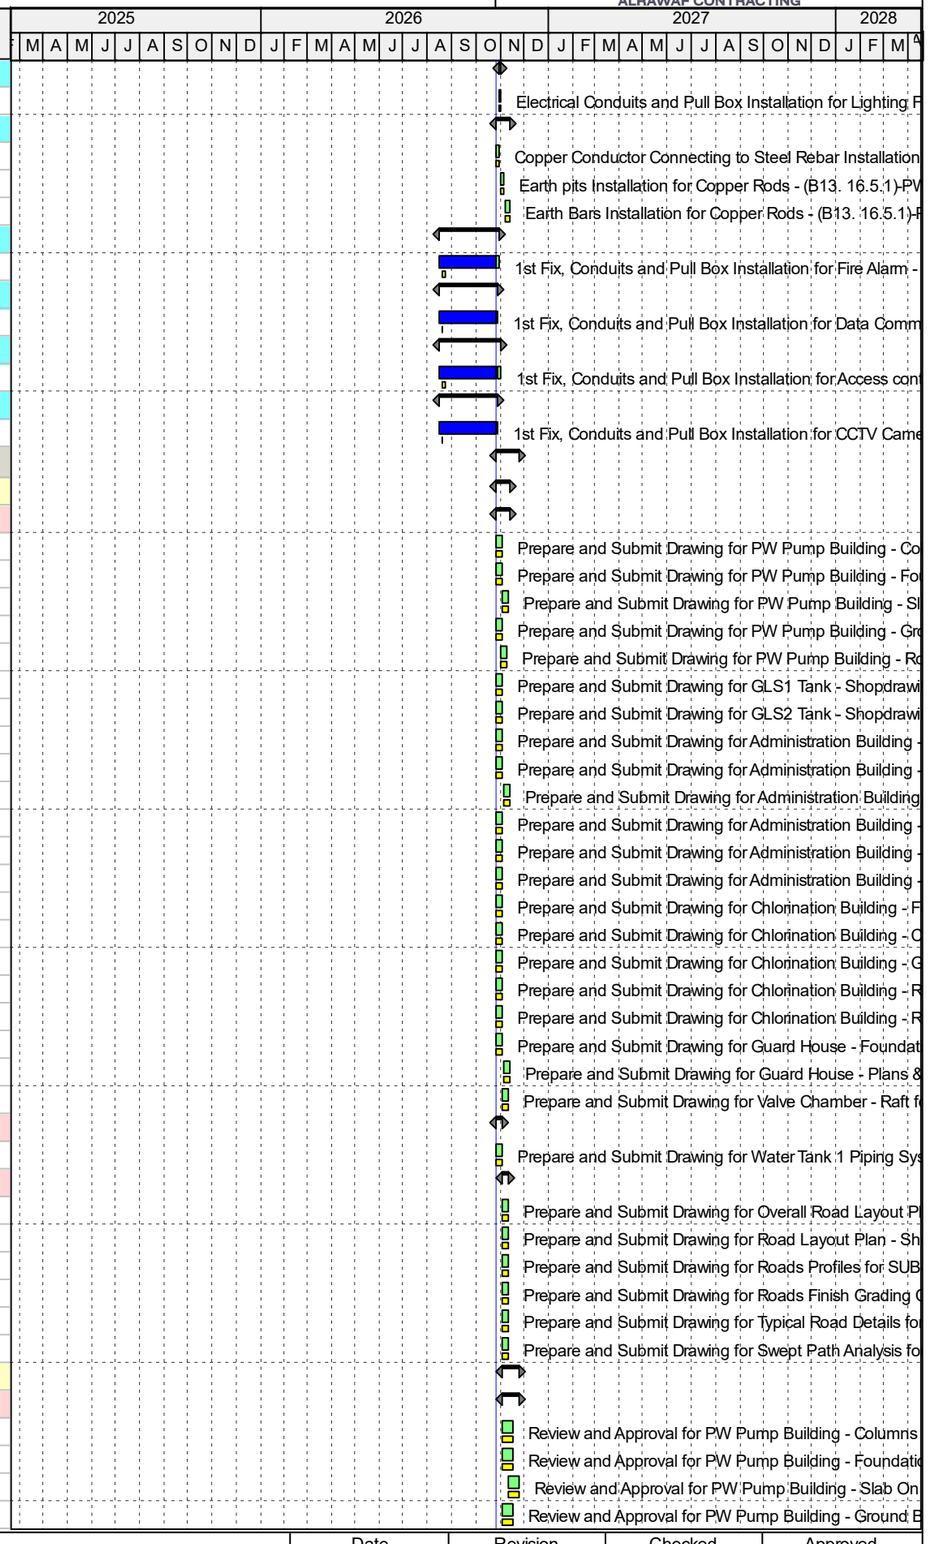

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
26-Oct-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Review and Approval for PW Pump Building - Roof for APP-AS-I	9d	09-Nov-26	19-Nov-26	333d	0	0	0
JDI	Review and Approval for GLS1 Tank - Shopdrawings Plan & Sec	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for GLS2 Tank - Shopdrawings Plan & Sec	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Foundation Sl	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Columns & Ax	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Slab On Grad	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Administration Building - Grade Beam	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Roof Shop Dr	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Administration Building - Roof Beam Sl	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Foundation for A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Columns & Axis	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Grade Beam for	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Roof for APP-AS	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Chlorination Building - Roof Beam for A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Guard House - Foundation & Columns	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Guard House - Plans & Sections for AF	9d	15-Nov-26	25-Nov-26	329d	0	0	0
JDI	Review and Approval for Valve Chamber - Raft for APP-AS-PWF	9d	11-Nov-26	23-Nov-26	331d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Mechanical - MC		9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDI	Review and Approval for Water Tank 1 Piping System for APP-A	9d	04-Nov-26	16-Nov-26	336d	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Roads - RD		9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Overall Road Layout Plan for APP-AS-I	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Road Layout Plan - Sheet 01 Of 01 for	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Roads Profiles for APP-AS-PWPS-RD	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Roads Finish Grading Overall Plan for A	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Typical Road Details for APP-AS-PWPS	9d	12-Nov-26	24-Nov-26	330d	0	0	0
JDI	Review and Approval for Swept Path Analysis for APP-AS-PWPS	9d	12-Nov-26	24-Nov-26	330d	0	0	0

