
Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Development of the Technology City in Dammam-RECOVERY SCHEDU		282	22-Jul-26 A	13-Jun-27	23-Jun-26	24-Feb-27	14.12%	59,233,415	58,492,973
Key Milestones		54	05-Apr-27	13-Jun-27	03-Jan-27	24-Feb-27	0%	0	0
Contractual Milestones		54	05-Apr-27	13-Jun-27	03-Jan-27	24-Feb-27	0%	0	0
MS-CF-SD	Completion of Construction Works for Storm Drainage Network	0		05-Apr-27		03-Jan-27	0%	0	0
MS-CF-IR	Completion of Construction Works for Irrigation Network	0		19-Apr-27		03-Jan-27	0%	0	0
MS-CF-SW	Completion of Construction Works for Sewage Network	0		27-Apr-27		13-Jan-27	0%	0	0
MS-CF-MV	Completion of Construction Works for Medium Voltage Network	0		27-Apr-27		11-Jan-27	0%	0	0
MS-CF-TSE	Completion of Construction Works for Treated Sewage Effluent Network	0		03-May-27		17-Jan-27	0%	0	0
MS-CF-TE	Completion of Construction Works for Telecom Network	0		06-May-27		20-Jan-27	0%	0	0
MS-CF-SL	Completion of Construction Works for Street Lighting Network	0		13-May-27		27-Jan-27	0%	0	0
MS-CF-PW	Completion of Construction Works for Potable Water Network	0		20-May-27		28-Jan-27	0%	0	0
MS-CF-RD	Completion of Construction Works for Road Works	0		06-Jun-27		16-Feb-27	0%	0	0
MS-CF-PF	Project Completion Date	0		13-Jun-27		24-Feb-27	0%	0	0
Engineering Works		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Material Submittals and Approvals		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Short Lead Time Items		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Superstructure Works		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Storage Tank (TSE)		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Submission of Material		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
ENG-MT-TSE-CV-S	Material Submittal for Civil Works for Storage Tank (TSE)	7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0%	0	0
Procurement Cycle		224	22-Jul-26 A	21-Apr-27	23-Jun-26	28-Jan-27	0%	0	0
Short Lead Time Items		215	22-Jul-26 A	11-Apr-27	23-Jun-26	28-Jan-27	0%	0	0
Infrastructure Networks		215	22-Jul-26 A	11-Apr-27	23-Jun-26	28-Jan-27	0%	0	0
Road Works		11	02-Aug-26 A	20-Oct-26	02-Nov-26	05-Dec-26	0%	0	0
Material Delivery & Site Inspection		11	02-Aug-26 A	20-Oct-26	02-Nov-26	05-Dec-26	0%	0	0
Pre-Bituminous Construction		11	02-Aug-26 A	20-Oct-26	02-Nov-26	12-Nov-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	20-Oct-26	02-Nov-26	02-Nov-26	30%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0%	0	0
Bituminous Construction		0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection for Prime Coat of Road Works	0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0%	0	0
PRO-R25-RD-DL-17(	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road Works	0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0%	0	0
Pavement Works		0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Curbstones for Landscaping	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0%	0	0
Traffic Signs Boards and Roads Marking		0	20-Oct-26	20-Oct-26	08-Nov-26	25-Nov-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	20-Oct-26	20-Oct-26	08-Nov-26	08-Nov-26	0%	0	0
PRO-R25-RD-DL-1	Material Delivery & Site Inspection of Road Markings For Road Works	0	20-Oct-26	20-Oct-26	25-Nov-26	25-Nov-26	0%	0	0
Softscape and Planting Works		105	20-Oct-26	22-Feb-27	11-Jul-26	10-Nov-26	0%	0	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	11-Jul-26	19-Jul-26	0%	0	0
Main Line Pipes		6	20-Oct-26	26-Oct-26	11-Jul-26	19-Jul-26	0%	0	0
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	20-Oct-26	26-Oct-26	12-Jul-26	19-Jul-26	0%	0	0
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	20-Oct-26	26-Oct-26	11-Jul-26	18-Jul-26	0%	0	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	18-Jul-26	17-Oct-26	0%	0	0
Main Line Pipes		90	27-Oct-26	24-Jan-27	18-Jul-26	17-Oct-26	0%	0	0
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	27-Oct-26	24-Jan-27	19-Jul-26	17-Oct-26	0%	0	0
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	90	27-Oct-26	24-Jan-27	18-Jul-26	16-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		6	25-Jan-27	31-Jan-27	17-Oct-26	24-Oct-26	0%	0	0
Main Line Pipes		6	25-Jan-27	31-Jan-27	17-Oct-26	24-Oct-26	0%	0	0
PRO-IR-1DL-140	1ST Material Delivery for Softscape and Planting Works	6	25-Jan-27	31-Jan-27	17-Oct-26	24-Oct-26	0%	0	0

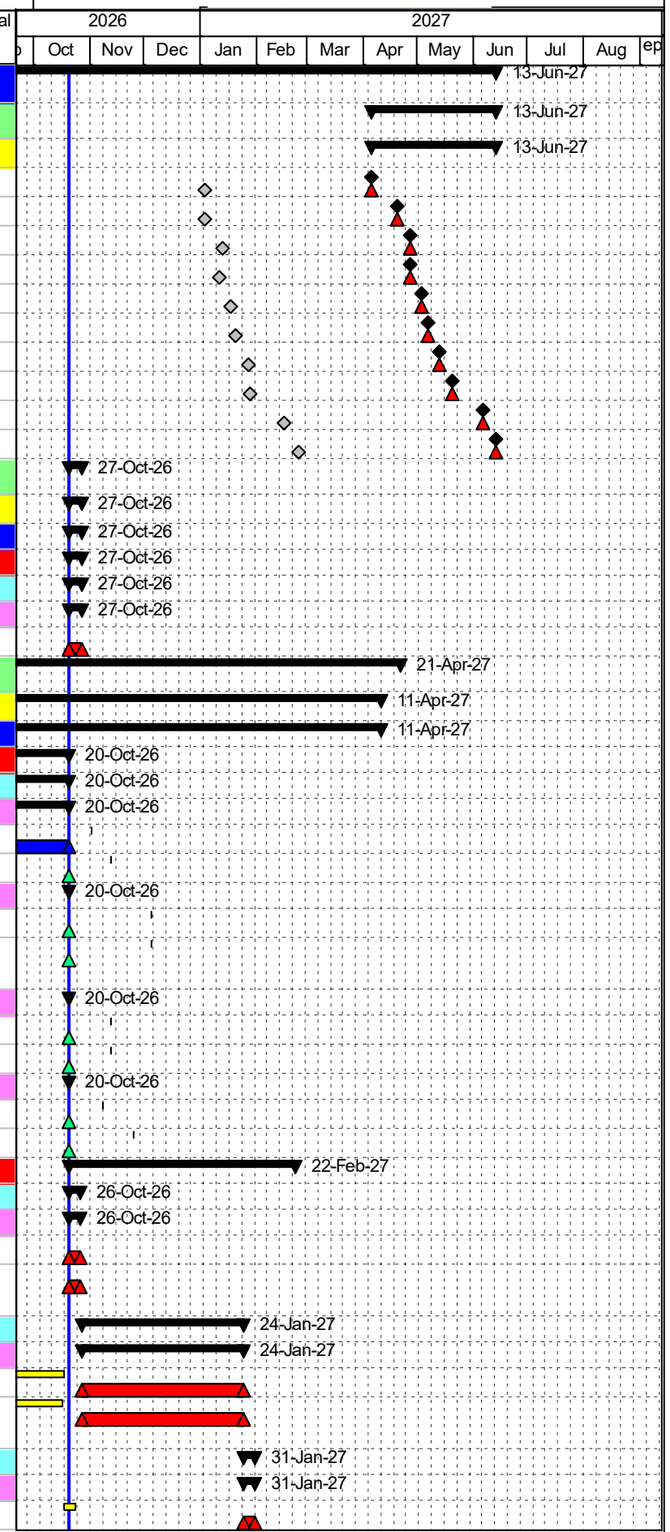


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-IR-1DL-150	1ST Material Delivery for Site Furnishings (Seating Bench,Stone Boulders and Gravel)	6	25-Jan-27	31-Jan-27	17-Oct-26	22-Oct-26	0%	0	0
Material Delivery & Site Inspection		16	01-Feb-27	22-Feb-27	24-Oct-26	10-Nov-26	0%	0	0
Main Line Pipes		16	01-Feb-27	22-Feb-27	24-Oct-26	10-Nov-26	0%	0	0
PRO-R25-IR-DL-14	Material Delivery & Site Inspection of Softscape and Planting Works	12	01-Feb-27	16-Feb-27	24-Oct-26	07-Nov-26	0%	0	0
PRO-R25-IR-DL-150	Material Delivery & Site Inspection of Site Furnishings (Seating Bench,Stone Boulders and Gravel)	16	01-Feb-27	22-Feb-27	24-Oct-26	10-Nov-26	0%	0	0
Sewage Network		145	13-Sep-26 A	11-Apr-27	15-Jul-26	28-Dec-26	0%	0	0
Manufacturing of Material		130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0%	0	0
Testing and Finishes		130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0%	0	0
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0%	0	0
1st Material Delivery & Site Inspection		6	27-Feb-27	07-Mar-27	22-Nov-26	28-Nov-26	0%	0	0
Testing and Finishes		6	27-Feb-27	07-Mar-27	22-Nov-26	28-Nov-26	0%	0	0
PRO-SW-1DL-120	1ST Material Delivery for Manholes Covers of Sewage Network	6	27-Feb-27	07-Mar-27	22-Nov-26	28-Nov-26	0%	0	0
Material Delivery & Site Inspection		145	13-Sep-26 A	11-Apr-27	09-Aug-26	28-Dec-26	0%	0	0
Main Line Sections		0	13-Sep-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0%	0	0
PRO-R25-SW-DL-1	Material Delivery & Site Inspection of Manholes for Sewage Network	0	13-Sep-26 A	20-Oct-26	09-Aug-26	09-Aug-26	30%	0	0
Testing and Finishes		26	08-Mar-27	11-Apr-27	29-Nov-26	28-Dec-26	0%	0	0
PRO-R25-SW-DL-1	Material Delivery & Site Inspection of Manholes Covers for Sewage Network	26	08-Mar-27	11-Apr-27	29-Nov-26	28-Dec-26	0%	0	0
Storm Drainage Network		203	02-Aug-26 A	31-Mar-27	15-Jul-26	10-Dec-26	0%	0	0
Manufacturing of Material		100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0%	0	0
Testing and Finishes		100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0%	0	0
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0%	0	0
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		98	13-Sep-26 A	03-Feb-27	20-Jul-26	29-Oct-26	0%	0	0
Catch Basin Sections		6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	0%	0	0
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	40%	0	0
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	40%	0	0
Testing and Finishes		6	28-Jan-27	03-Feb-27	24-Oct-26	29-Oct-26	0%	0	0
PRO-SD-1DL-140	1ST Material Delivery for Manholes Covers of Storm Drainage Network	6	28-Jan-27	03-Feb-27	24-Oct-26	29-Oct-26	0%	0	0
PRO-SD-1DL-150	1ST Material Delivery for Catch Basin Covers of Storm Drainage Network	6	28-Jan-27	03-Feb-27	24-Oct-26	29-Oct-26	0%	0	0
Material Delivery & Site Inspection		203	02-Aug-26 A	31-Mar-27	27-Jul-26	10-Dec-26	0%	0	0
Main Line Sections		0	02-Aug-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0%	0	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	20-Oct-26	09-Aug-26	09-Aug-26	40%	0	0
Catch Basin Sections		0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	0%	0	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Networl	0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	40%	0	0
PRO-R25-SD-DL-11(	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	40%	0	0
Testing and Finishes		39	04-Feb-27	31-Mar-27	31-Oct-26	10-Dec-26	0%	0	0
PRO-R25-SD-DL-15(	Material Delivery & Site Inspection of Catch Basin Covers for Storm Drainage Network	20	04-Feb-27	06-Mar-27	31-Oct-26	22-Nov-26	0%	0	0
PRO-R25-SD-DL-14(	Material Delivery & Site Inspection of Manholes Covers for Storm Drainage Network	26	23-Feb-27	31-Mar-27	11-Nov-26	10-Dec-26	0%	0	0
Potable Water Network		153	30-Jul-26 A	05-Apr-27	07-Jul-26	13-Dec-26	0%	0	0
Issuance of Purchase Orders		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0%	0	0
Main Line Sections		6	20-Oct-26	26-Oct-26	08-Jul-26	14-Jul-26	0%	0	0
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	20-Oct-26	26-Oct-26	08-Jul-26	14-Jul-26	0%	0	0
Fire Hydrant		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0%	0	0
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0%	0	0
Testing and Finishes		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0%	0	0
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0%	0	0
Manufacturing of Material		115	27-Oct-26	18-Feb-27	15-Jul-26	06-Nov-26	0%	0	0
Main Line Sections		90	27-Oct-26	24-Jan-27	15-Jul-26	12-Oct-26	0%	0	0

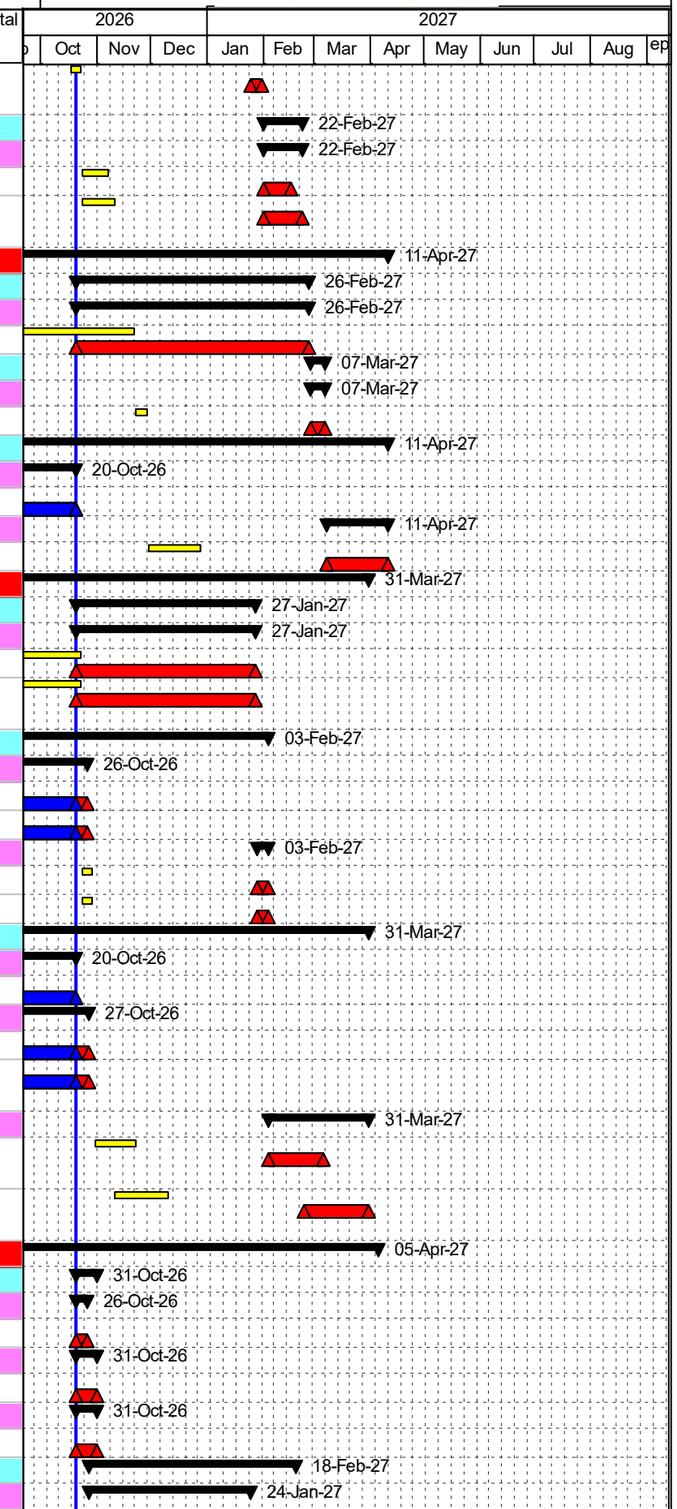


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	27-Oct-26	24-Jan-27	15-Jul-26	12-Oct-26	0%	0	0
Fire Hydrant		60	01-Nov-26	30-Dec-26	20-Jul-26	17-Sep-26	0%	0	0
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	01-Nov-26	30-Dec-26	20-Jul-26	17-Sep-26	0%	0	0
Testing and Finishes		110	01-Nov-26	18-Feb-27	20-Jul-26	06-Nov-26	0%	0	0
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	01-Nov-26	18-Feb-27	20-Jul-26	06-Nov-26	0%	0	0
1st Material Delivery & Site Inspection		107	30-Jul-26 A	28-Feb-27	07-Jul-26	12-Nov-26	0%	0	0
Main Line Sections		87	30-Jul-26 A	31-Jan-27	07-Jul-26	19-Oct-26	0%	0	0
PRO-PW-1DL-100_R	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	30-Jul-26 A	10-Jan-27	07-Jul-26	28-Sep-26	90%	0	0
PRO-PW-1DL-110	1ST Material Delivery for Valves of Potable Water Network	6	25-Jan-27	31-Jan-27	13-Oct-26	19-Oct-26	0%	0	0
Fire Hydrant		6	31-Dec-26	06-Jan-27	19-Sep-26	26-Sep-26	0%	0	0
PRO-PW-1DL-120	1ST Material Delivery for Fire Hydrants of Potable Water Network	6	31-Dec-26	06-Jan-27	19-Sep-26	26-Sep-26	0%	0	0
Testing and Finishes		6	20-Feb-27	28-Feb-27	07-Nov-26	12-Nov-26	0%	0	0
PRO-PW-1DL-130	1ST Material Delivery for Finishes of Potable Water Network	6	20-Feb-27	28-Feb-27	07-Nov-26	12-Nov-26	0%	0	0
Material Delivery & Site Inspection		153	02-Aug-26 A	05-Apr-27	27-Sep-26	13-Dec-26	0%	0	0
Main Line Sections		107	02-Aug-26 A	01-Feb-27	29-Sep-26	20-Oct-26	0%	0	0
PRO-R25-PW-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Remaining)	0	02-Aug-26 A	10-Jan-27	29-Sep-26	29-Sep-26	90%	0	0
PRO-R25-PW-DL-1	Material Delivery & Site Inspection of Valves for Potable Water Network	0	01-Feb-27	01-Feb-27	20-Oct-26	20-Oct-26	0%	0	0
Fire Hydrant		0	07-Jan-27	07-Jan-27	27-Sep-26	27-Sep-26	0%	0	0
PRO-R25-PW-DL-1	Material Delivery & Site Inspection of Fire Hydrants for Potable Water Network	0	07-Jan-27	07-Jan-27	27-Sep-26	27-Sep-26	0%	0	0
Testing and Finishes		26	28-Feb-27	05-Apr-27	14-Nov-26	13-Dec-26	0%	0	0
PRO-R25-PW-DL-1	Material Delivery & Site Inspection for Finishes of Potable Water Network	26	28-Feb-27	05-Apr-27	14-Nov-26	13-Dec-26	0%	0	0
Irrigation Network		170	22-Jul-26 A	08-Feb-27	15-Jul-26	27-Oct-26	0%	0	0
Issuance of Purchase Orders		6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0%	0	0
Main Line Pipes		6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0%	0	0
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0%	0	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0%	0	0
Main Line Pipes		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0%	0	0
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		170	22-Jul-26 A	07-Feb-27	05-Oct-26	26-Oct-26	0%	0	0
Main Line Pipes		170	22-Jul-26 A	07-Feb-27	05-Oct-26	26-Oct-26	0%	0	0
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	22-Jul-26 A	25-Oct-26	05-Oct-26	11-Oct-26	30%	0	0
PRO-IR-1DL-110	1ST Material Delivery for Valves of Irrigation Network	6	01-Feb-27	07-Feb-27	20-Oct-26	26-Oct-26	0%	0	0
Material Delivery & Site Inspection		90	26-Oct-26	08-Feb-27	11-Oct-26	27-Oct-26	0%	0	0
Main Line Pipes		90	26-Oct-26	08-Feb-27	11-Oct-26	27-Oct-26	0%	0	0
PRO-R25-IR-DL-10	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	26-Oct-26	26-Oct-26	11-Oct-26	11-Oct-26	0%	0	0
PRO-R25-IR-DL-11	Material Delivery & Site Inspection of Valves for Irrigation Network	0	08-Feb-27	08-Feb-27	27-Oct-26	27-Oct-26	0%	0	0
Treated Sewage Effluent (Tse)		98	02-Aug-26 A	01-Feb-27	27-Jun-26	10-Oct-26	0%	0	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0%	0	0
Main Line Pipes		6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0%	0	0
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0%	0	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0%	0	0
Main Line Pipes		90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0%	0	0
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		6	25-Jan-27	31-Jan-27	03-Oct-26	08-Oct-26	0%	0	0
Main Line Pipes		6	25-Jan-27	31-Jan-27	03-Oct-26	08-Oct-26	0%	0	0
PRO-TSE-1DL-130	1ST Material Delivery for Valves of Treated Sewage Effluent (Tse)	6	25-Jan-27	31-Jan-27	03-Oct-26	08-Oct-26	0%	0	0
Material Delivery & Site Inspection		98	02-Aug-26 A	01-Feb-27	10-Oct-26	10-Oct-26	0%	0	0
Main Line Pipes		98	02-Aug-26 A	01-Feb-27	10-Oct-26	10-Oct-26	0%	0	0
PRO-R25-TSE-DL-12	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (Tse)(Remaining)	0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	50%	0	0
PRO-R25-TSE-DL-	Material Delivery & Site Inspection of Valves for Treated Sewage Effluent (Tse)	0	01-Feb-27	01-Feb-27	10-Oct-26	10-Oct-26	0%	0	0
Medium Voltage Network		129	20-Oct-26	29-Mar-27	23-Jun-26	05-Dec-26	0%	0	0

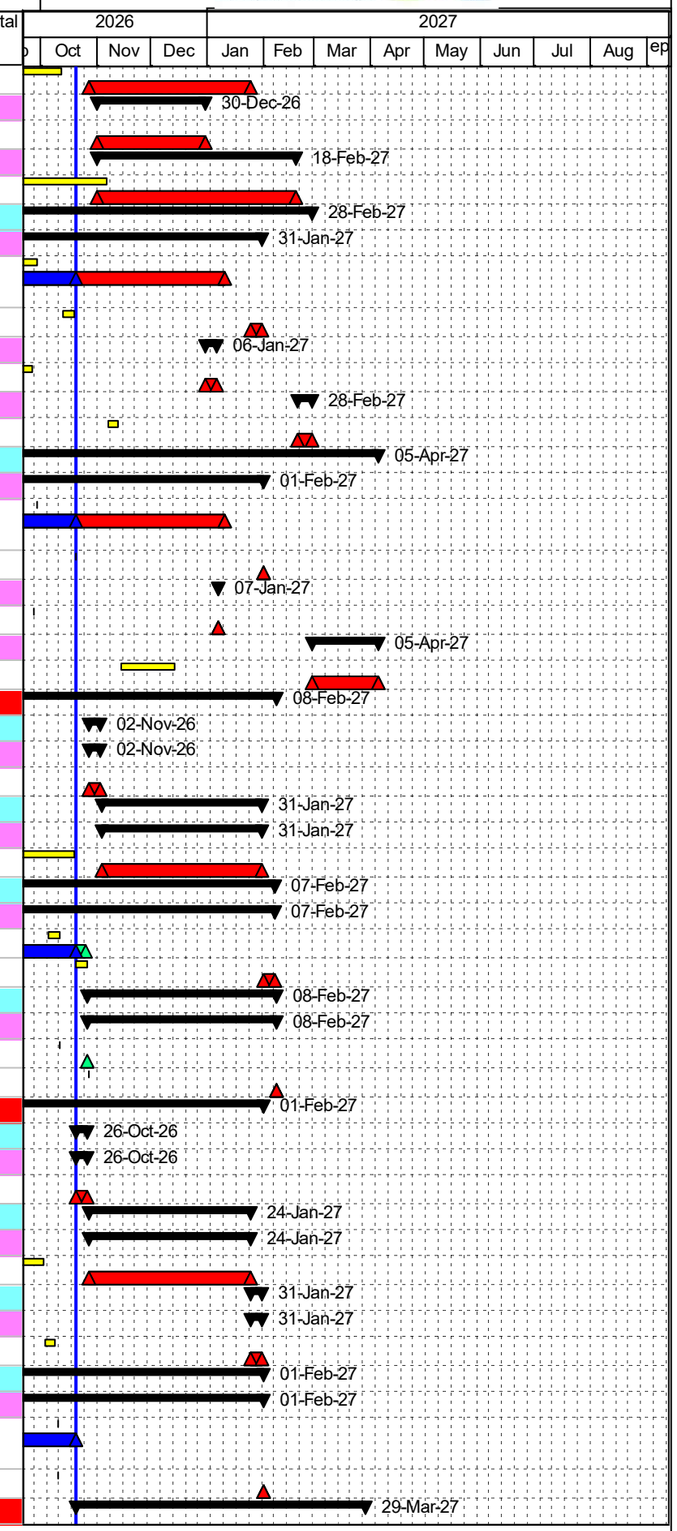


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Issuance of Purchase Orders		12	20-Oct-26	02-Nov-26	23-Jun-26	21-Jul-26	0%	0	0
Cabling Works		12	20-Oct-26	02-Nov-26	23-Jun-26	06-Jul-26	0%	0	0
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	20-Oct-26	02-Nov-26	23-Jun-26	06-Jul-26	0%	0	0
Termination and Testing Works		12	20-Oct-26	02-Nov-26	08-Jul-26	21-Jul-26	0%	0	0
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Network	12	20-Oct-26	02-Nov-26	08-Jul-26	21-Jul-26	0%	0	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	07-Jul-26	19-Oct-26	0%	0	0
Cabling Works		60	03-Nov-26	01-Jan-27	07-Jul-26	04-Sep-26	0%	0	0
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	03-Nov-26	01-Jan-27	07-Jul-26	04-Sep-26	0%	0	0
Termination and Testing Works		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0%	0	0
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		40	02-Jan-27	20-Feb-27	05-Sep-26	04-Nov-26	0%	0	0
Cabling Works		12	02-Jan-27	14-Jan-27	05-Sep-26	17-Sep-26	0%	0	0
PRO-MV-1DL-100	1ST Material Delivery for Medium Voltage Cables of Medium Voltage Network	12	02-Jan-27	14-Jan-27	05-Sep-26	17-Sep-26	0%	0	0
Termination and Testing Works		14	01-Feb-27	20-Feb-27	20-Oct-26	04-Nov-26	0%	0	0
PRO-MV-1DL-120	1ST Material Delivery for Termination and Joints Kits of Medium Voltage Network	14	01-Feb-27	20-Feb-27	20-Oct-26	04-Nov-26	0%	0	0
Material Delivery & Site Inspection		54	16-Jan-27	29-Mar-27	19-Sep-26	05-Dec-26	0%	0	0
Cabling Works		0	16-Jan-27	16-Jan-27	19-Sep-26	19-Sep-26	0%	0	0
PRO-MV-DL-100	Material Delivery & Site Inspection of Medium Voltage Cables for Medium Voltage Network	0	16-Jan-27	16-Jan-27	19-Sep-26	19-Sep-26	0%	0	0
Termination and Testing Works		26	20-Feb-27	29-Mar-27	05-Nov-26	05-Dec-26	0%	0	0
PRO-MV-DL-110	Material Delivery & Site Inspection of Termination and Joints Kits for Medium Voltage Network	26	20-Feb-27	29-Mar-27	05-Nov-26	05-Dec-26	0%	0	0
Low Voltage and Street Lighting Network		41	20-Oct-26	06-Dec-26	28-Sep-26	28-Jan-27	0%	0	0
1st Material Delivery & Site Inspection		15	20-Oct-26	05-Nov-26	28-Sep-26	29-Dec-26	0%	0	0
Cabling Works		6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0%	0	0
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0%	0	0
Lighting Poles Works		6	20-Oct-26	26-Oct-26	28-Sep-26	19-Dec-26	0%	0	0
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0%	0	0
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0%	0	0
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	20-Oct-26	26-Oct-26	13-Dec-26	19-Dec-26	0%	0	0
Distribution Panel Board		6	20-Oct-26	26-Oct-26	24-Oct-26	29-Oct-26	0%	0	0
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	20-Oct-26	26-Oct-26	24-Oct-26	29-Oct-26	0%	0	0
Termination and Testing Works		15	20-Oct-26	05-Nov-26	03-Nov-26	29-Dec-26	0%	0	0
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	20-Oct-26	05-Nov-26	13-Dec-26	29-Dec-26	0%	0	0
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	20-Oct-26	05-Nov-26	03-Nov-26	21-Nov-26	0%	0	0
Earthing System Works		6	20-Oct-26	26-Oct-26	03-Dec-26	09-Dec-26	0%	0	0
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	20-Oct-26	26-Oct-26	03-Dec-26	09-Dec-26	0%	0	0
Material Delivery & Site Inspection		35	27-Oct-26	06-Dec-26	05-Oct-26	28-Jan-27	0%	0	0
Cabling Works		0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0%	0	0
PRO-R25-SL-DL-100	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0%	0	0
Lighting Poles Works		18	27-Oct-26	16-Nov-26	05-Oct-26	20-Dec-26	0%	0	0
PRO-R25-SL-DL-110	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting Network	18	27-Oct-26	16-Nov-26	05-Oct-26	25-Oct-26	0%	0	0
PRO-R25-SL-DL-1[illegible]	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0%	0	0
PRO-R25-SL-DL-140	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	27-Oct-26	27-Oct-26	20-Dec-26	20-Dec-26	0%	0	0
Distribution Panel Board		0	27-Oct-26	27-Oct-26	31-Oct-26	31-Oct-26	0%	0	0
PRO-R25-SL-DL-160	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting Network	0	27-Oct-26	27-Oct-26	31-Oct-26	31-Oct-26	0%	0	0
Termination and Testing Works		26	07-Nov-26	06-Dec-26	21-Nov-26	28-Jan-27	0%	0	0

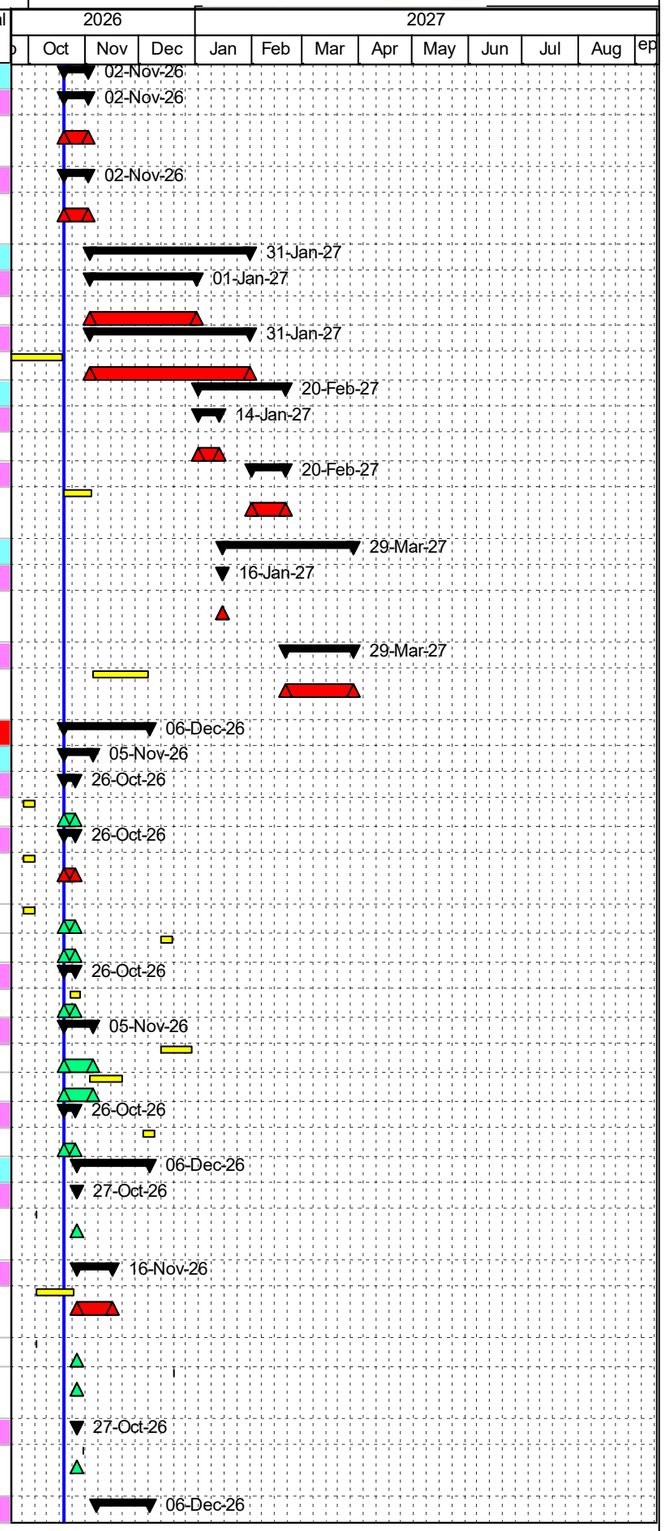


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
PRO-R25-SL-DL-1:	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	07-Nov-26	06-Dec-26	30-Dec-26	28-Jan-27	0%	0	0
PRO-R25-SL-DL-1:	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	07-Nov-26	06-Dec-26	21-Nov-26	21-Dec-26	0%	0	0
Earthing System Works		0	27-Oct-26	27-Oct-26	10-Dec-26	10-Dec-26	0%	0	0
PRO-R25-SL-DL-150	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	27-Oct-26	27-Oct-26	10-Dec-26	10-Dec-26	0%	0	0
Telecom Network		93	20-Oct-26	06-Feb-27	07-Jul-26	24-Oct-26	0%	0	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
Ducts Works		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
Manholes Works		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
CCTV System Wroks		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0%	0	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0%	0	0
Ducts Works		60	27-Oct-26	25-Dec-26	14-Jul-26	11-Sep-26	0%	0	0
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	27-Oct-26	25-Dec-26	14-Jul-26	11-Sep-26	0%	0	0
Manholes Works		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0%	0	0
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0%	0	0
CCTV System Wroks		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0%	0	0
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		36	26-Dec-26	04-Feb-27	12-Sep-26	22-Oct-26	0%	0	0
Ducts Works		6	26-Dec-26	31-Dec-26	12-Sep-26	17-Sep-26	0%	0	0
PRO-TE-1DL-100	1ST Material Delivery for Ducts of Telecom Network	6	26-Dec-26	31-Dec-26	12-Sep-26	17-Sep-26	0%	0	0
Manholes Works		6	25-Jan-27	31-Jan-27	12-Oct-26	18-Oct-26	0%	0	0
PRO-TE-1DL-110	1ST Material Delivery for Manholes of Telecom Network	6	25-Jan-27	31-Jan-27	12-Oct-26	18-Oct-26	0%	0	0
CCTV System Wroks		10	25-Jan-27	04-Feb-27	12-Oct-26	22-Oct-26	0%	0	0
PRO-CTV-1DL-100	1ST Material Delivery for Civil and Finishes Works of CCTV Complete System	10	25-Jan-27	04-Feb-27	12-Oct-26	22-Oct-26	0%	0	0
Material Delivery & Site Inspection		30	02-Jan-27	06-Feb-27	19-Sep-26	24-Oct-26	0%	0	0
Ducts Works		0	02-Jan-27	02-Jan-27	19-Sep-26	19-Sep-26	0%	0	0
PRO-R25-TE-DL-1(	Material Delivery & Site Inspection for Ducts of Telecom Network	0	02-Jan-27	02-Jan-27	19-Sep-26	19-Sep-26	0%	0	0
Manholes Works		0	01-Feb-27	01-Feb-27	19-Oct-26	19-Oct-26	0%	0	0
PRO-R25-TE-DL-1'	Material Delivery & Site Inspection of Manholes for Telecom Network	0	01-Feb-27	01-Feb-27	19-Oct-26	19-Oct-26	0%	0	0
CCTV System Wroks		0	06-Feb-27	06-Feb-27	24-Oct-26	24-Oct-26	0%	0	0
PRO-R25-CTV-DL-1(	Material Delivery & Site Inspection of for Civil and Finishes Works of CCTV Complete System	0	06-Feb-27	06-Feb-27	24-Oct-26	24-Oct-26	0%	0	0
Superstructure Works		151	02-Aug-26 A	18-Jan-27	23-Jun-26	11-Oct-26	0%	0	0
Issuance of Purchase Orders		18	20-Oct-26	09-Nov-26	23-Jun-26	13-Jul-26	0%	0	0
Storage Tank (TSE)		11	28-Oct-26	09-Nov-26	01-Jul-26	13-Jul-26	0%	0	0
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	28-Oct-26	09-Nov-26	01-Jul-26	13-Jul-26	0%	0	0
Gaurd Room		11	20-Oct-26	01-Nov-26	23-Jun-26	05-Jul-26	0%	0	0
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	20-Oct-26	01-Nov-26	23-Jun-26	05-Jul-26	0%	0	0
Manufacturing of Material		90	20-Oct-26	17-Jan-27	05-Jul-26	11-Oct-26	0%	0	0
Storage Tank (TSE)		40	10-Nov-26	19-Dec-26	14-Jul-26	22-Aug-26	0%	0	0
PRO-TSE-CV-MF-40	Manufacturing of Civil Works for Civil Works for Storage Tank (TSE)	40	10-Nov-26	19-Dec-26	14-Jul-26	22-Aug-26	0%	0	0
Gaurd Room		40	01-Nov-26	11-Dec-26	05-Jul-26	14-Aug-26	0%	0	0
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	01-Nov-26	11-Dec-26	05-Jul-26	14-Aug-26	0%	0	0
Softscape and Planting Works		90	20-Oct-26	17-Jan-27	13-Jul-26	11-Oct-26	0%	0	0
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	20-Oct-26	17-Jan-27	13-Jul-26	11-Oct-26	0%	0	0
1st Material Delivery & Site Inspection		12	12-Dec-26	24-Dec-26	15-Aug-26	27-Aug-26	0%	0	0
Storage Tank (TSE)		1	20-Dec-26	20-Dec-26	23-Aug-26	23-Aug-26	0%	0	0
PRO-TSE-CV-1DL-5	1ST Material Delivery for Civil Works for Civil Works for Storage Tank (TSE)	1	20-Dec-26	20-Dec-26	23-Aug-26	23-Aug-26	0%	0	0
Gaurd Room		12	12-Dec-26	24-Dec-26	15-Aug-26	27-Aug-26	0%	0	0
PRO-GR-CV-1DL-60	1ST Material Delivery for Civil Works for Civil Works for Gaurd Room	12	12-Dec-26	24-Dec-26	15-Aug-26	27-Aug-26	0%	0	0

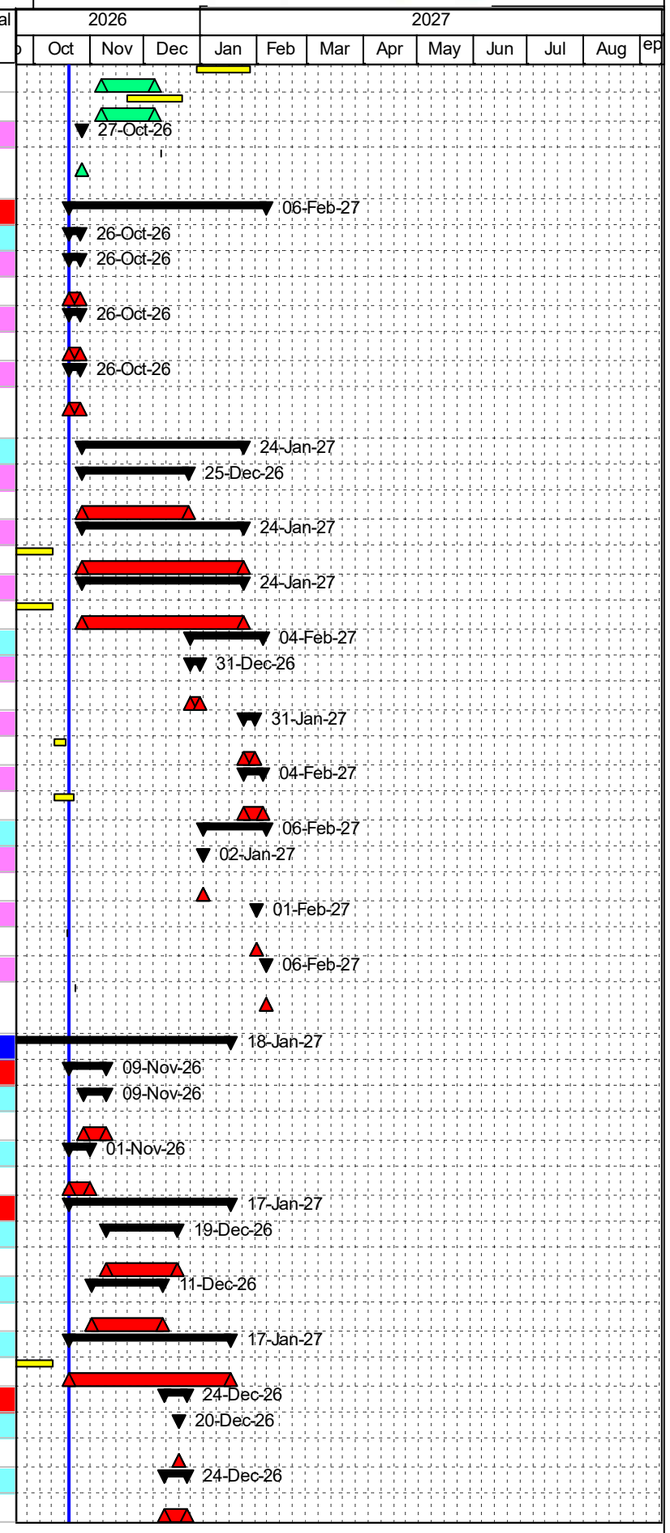


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Material Delivery & Site Inspection		151	02-Aug-26 A	18-Jan-27	25-Jul-26	11-Oct-26	0%	0	0
Lift Station		0	17-Sep-26 A	20-Oct-26	03-Aug-26	03-Aug-26	0%	0	0
PRO-LS-CV-DL-50	Material Delivery & Site Inspection for Civil Works for Lift Stations	0	17-Sep-26 A	20-Oct-26	03-Aug-26	03-Aug-26	70%	0	0
Storage Tank (TSE)		0	20-Dec-26	20-Dec-26	23-Aug-26	23-Aug-26	0%	0	0
PRO-TSE-CV-DL-60	Material Delivery & Site Inspection for Civil Works for Storage Tank (TSE)	0	20-Dec-26	20-Dec-26	23-Aug-26	23-Aug-26	0%	0	0
Gaurd Room		0	26-Dec-26	26-Dec-26	29-Aug-26	29-Aug-26	0%	0	0
PRO-GR-CV-DL-70	Material Delivery & Site Inspection for Civil Works for Gaurd Room	0	26-Dec-26	26-Dec-26	29-Aug-26	29-Aug-26	0%	0	0
Fence		0	02-Aug-26 A	20-Oct-26	25-Jul-26	25-Jul-26	0%	0	0
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	20-Oct-26	25-Jul-26	25-Jul-26	80%	0	0
Softscape and Planting Works		0	18-Jan-27	18-Jan-27	11-Oct-26	11-Oct-26	0%	0	0
PRO-FE-CV-DL-90	Material Delivery & Site Inspection for Softscape and Planting Works	0	18-Jan-27	18-Jan-27	11-Oct-26	11-Oct-26	0%	0	0
Long Lead Time Items		149	26-Aug-26 A	21-Apr-27	23-Jun-26	23-Dec-26	0%	0	0
Infrastructure Networks		112	20-Oct-26	04-Mar-27	23-Jun-26	31-Oct-26	0%	0	0
CCTV System Wroks of Telecom Network		112	20-Oct-26	04-Mar-27	23-Jun-26	31-Oct-26	0%	0	0
Issuance of Purchase Orders		20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0%	0	0
PRO-CTV-LL-PO-10	Issuance of Purchase Order for Low Current Works of CCTV Complete System with All Accessories	20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0%	0	0
Manufacturing of Material		90	12-Nov-26	09-Feb-27	16-Jul-26	13-Oct-26	0%	0	0
PRO-CTV-LL-MF-10	Manufacturing of Low Current Works for CCTV Complete System with All Accessories	90	12-Nov-26	09-Feb-27	16-Jul-26	13-Oct-26	0%	0	0
Material Shipping/Custom Clearance/Delivery		15	10-Feb-27	04-Mar-27	13-Oct-26	31-Oct-26	0%	0	0
PRO-CTV-LL-SH/DL-1	Material Delivery for Low Current Works of CCTV Complete System with All Accessories	15	10-Feb-27	04-Mar-27	13-Oct-26	31-Oct-26	0%	0	0
Material Site Inspection		0	04-Mar-27	04-Mar-27	31-Oct-26	31-Oct-26	0%	0	0
PRO-CTV-LL-MSI-10	Material Site Inspection for Low Current Works of CCTV Complete System with All Accessories	0	04-Mar-27	04-Mar-27	31-Oct-26	31-Oct-26	0%	0	0
Superstructure Works		149	26-Aug-26 A	21-Apr-27	04-Jul-26	23-Dec-26	0%	0	0
Pump Stations		84	26-Aug-26 A	14-Mar-27	07-Aug-26	20-Dec-26	0%	0	0
Manufacturing of Material		60	26-Aug-26 A	18-Dec-26	07-Aug-26	05-Oct-26	0%	0	0
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	26-Aug-26 A	18-Dec-26	07-Aug-26	05-Oct-26	35%	0	0
Material Shipping/Custom Clearance/Delivery		30	19-Dec-26	21-Jan-27	06-Oct-26	09-Nov-26	0%	0	0
PRO-SPS-LL-SH/DL	Material Delivery for Electromechanical Works for Pump Stations	30	19-Dec-26	21-Jan-27	06-Oct-26	09-Nov-26	0%	0	0
Material Site Inspection		35	23-Jan-27	14-Mar-27	10-Nov-26	20-Dec-26	0%	0	0
PRO-SPS-LL-MSI-1(	Material Site Inspection for Electromechanical Works for Pump Stations	35	23-Jan-27	14-Mar-27	10-Nov-26	20-Dec-26	0%	0	0
Lift Stations		119	20-Oct-26	17-Mar-27	07-Aug-26	23-Dec-26	0%	0	0
Manufacturing of Material		60	20-Oct-26	18-Dec-26	07-Aug-26	05-Oct-26	0%	0	0
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	20-Oct-26	18-Dec-26	07-Aug-26	05-Oct-26	0%	0	0
Material Shipping/Custom Clearance/Delivery		30	19-Dec-26	21-Jan-27	06-Oct-26	09-Nov-26	0%	0	0
PRO-LS-LL-SH/DL-2	Material Delivery for Electromechanical Works for Lift Stations	30	19-Dec-26	21-Jan-27	06-Oct-26	09-Nov-26	0%	0	0
Material Site Inspection		38	23-Jan-27	17-Mar-27	10-Nov-26	23-Dec-26	0%	0	0
PRO-LS-LL-MSI-20	Material Site Inspection for Electromechanical Works for Lift Stations	38	23-Jan-27	17-Mar-27	10-Nov-26	23-Dec-26	0%	0	0
Storage Tank (TSE)		149	20-Oct-26	21-Apr-27	04-Jul-26	23-Dec-26	0%	0	0
Issuance of Purchase Orders		30	20-Oct-26	23-Nov-26	04-Jul-26	06-Aug-26	0%	0	0
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	20-Oct-26	23-Nov-26	04-Jul-26	06-Aug-26	0%	0	0
Manufacturing of Material		60	24-Nov-26	22-Jan-27	07-Aug-26	05-Oct-26	0%	0	0
PRO-TSE-LL-MF-30	Manufacturing of Electromechanical Works for Storage Tank (TSE)	60	24-Nov-26	22-Jan-27	07-Aug-26	05-Oct-26	0%	0	0
Material Shipping/Custom Clearance/Delivery		30	23-Jan-27	03-Mar-27	06-Oct-26	09-Nov-26	0%	0	0
PRO-TSE-LL-SH/DL	Material Delivery for Electromechanical Works for Storage Tank (TSE)	30	23-Jan-27	03-Mar-27	06-Oct-26	09-Nov-26	0%	0	0
Material Site Inspection		38	04-Mar-27	21-Apr-27	10-Nov-26	23-Dec-26	0%	0	0
PRO-TSE-LL-MSI-3(	Material Site Inspection for Electromechanical Works for Storage Tank (TSE)	38	04-Mar-27	21-Apr-27	10-Nov-26	23-Dec-26	0%	0	0
Construction Works		276	02-Aug-26 A	06-Jun-27	04-Jul-26	23-Feb-27	14.12%	59,233,415	58,492,973
Infrastructure Networks		276	02-Aug-26 A	06-Jun-27	04-Jul-26	16-Feb-27	12.22%	26,355,596	26,355,596
Earthworks		26	02-Aug-26 A	07-Nov-26	04-Jul-26	02-Aug-26	83.1%	3,797,029	3,797,029

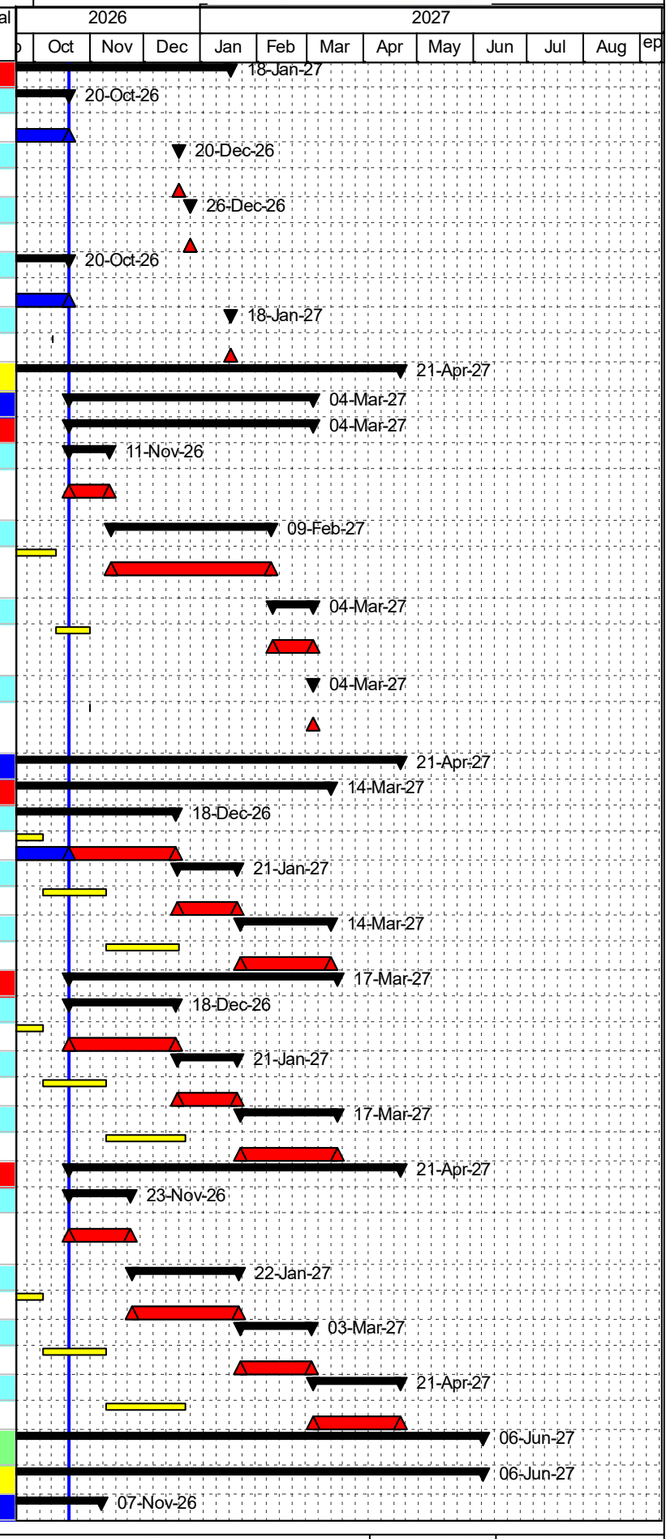

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
Earthworks		26	02-Aug-26 A	07-Nov-26	04-Jul-26	02-Aug-26	83.1%	3,797,029	3,797,029
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	31-Oct-26	04-Jul-26	14-Jul-26	84%	522,497	522,497
CO-EW-110_R	Embankments Works Upto Design Level for Earthworks(Remaining)	16	02-Aug-26 A	07-Nov-26	15-Jul-26	02-Aug-26	84%	2,419,920	2,419,920
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	31-Oct-26	04-Jul-26	14-Jul-26	80%	275,827	275,827
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	02-Nov-26	04-Jul-26	16-Jul-26	80%	578,784	578,784
Storm Drainage Network		168	02-Aug-26 A	26-Jan-27	15-Jul-26	01-Nov-26	1.3%	4,958,378	4,958,378
FROM MH-25:MH-12		137	02-Aug-26 A	21-Dec-26	15-Jul-26	30-Sep-26	2.37%	2,725,883	2,725,883
Main Line Sections		18	02-Aug-26 A	08-Nov-26	15-Jul-26	04-Aug-26	3.28%	1,787,973	1,787,973
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	31-Oct-26	15-Jul-26	18-Jul-26	4%	496,659	496,659
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	02-Nov-26	19-Jul-26	23-Jul-26	3%	893,986	893,986
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	08-Nov-26	25-Jul-26	04-Aug-26	3%	397,327	397,327
Manholes		18	17-Oct-26 A	28-Nov-26	09-Aug-26	06-Sep-26	2.4%	247,670	247,670
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	17-Oct-26 A	07-Nov-26	09-Aug-26	16-Aug-26	12%	49,534	49,534
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network	7	08-Nov-26	15-Nov-26	17-Aug-26	24-Aug-26	0%	82,557	82,557
CO-SD-MH-200	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	4	16-Nov-26	19-Nov-26	25-Aug-26	29-Aug-26	0%	49,534	49,534
CO-SD-MH-220	Backfilling Works for Manholes of Storm Drainage Network	7	21-Nov-26	28-Nov-26	30-Aug-26	06-Sep-26	0%	66,045	66,045
Catch Basin Sections		38	08-Nov-26	21-Dec-26	17-Aug-26	30-Sep-26	0%	690,240	690,240
CO-SD-CB-140	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	10	08-Nov-26	18-Nov-26	17-Aug-26	27-Aug-26	0%	129,420	129,420
CO-SD-CB-150	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network	10	29-Nov-26	09-Dec-26	07-Sep-26	17-Sep-26	0%	388,260	388,260
CO-SD-CB-170	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network	10	10-Dec-26	21-Dec-26	19-Sep-26	30-Sep-26	0%	172,560	172,560
FROM MH-12:MH-01		69	08-Nov-26	26-Jan-27	03-Aug-26	01-Nov-26	0%	2,232,495	2,232,495
Main Line Sections		48	08-Nov-26	02-Jan-27	03-Aug-26	28-Sep-26	0%	1,462,887	1,462,887
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	0%	406,357	406,357
CO-SD-ML-150	Pipes Laying Works for Main Lines of Storm Drainage Network	14	24-Nov-26	09-Dec-26	19-Aug-26	03-Sep-26	0%	731,443	731,443
CO-SD-ML-160	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	20	10-Dec-26	02-Jan-27	05-Sep-26	28-Sep-26	0%	325,086	325,086
Manholes		32	10-Dec-26	16-Jan-27	05-Sep-26	12-Oct-26	0%	197,929	197,929
CO-SD-MH-230	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	9	10-Dec-26	20-Dec-26	05-Sep-26	14-Sep-26	0%	39,586	39,586
CO-SD-MH-240	Install RC Footing Works for Manholes of Storm Drainage Network	7	21-Dec-26	28-Dec-26	15-Sep-26	22-Sep-26	0%	65,976	65,976
CO-SD-MH-250	Install RC Wall Rings & Slab Works for Manholes of Storm Drainage Network	7	29-Dec-26	05-Jan-27	24-Sep-26	01-Oct-26	0%	39,586	39,586
CO-SD-MH-260	Backfilling Works for Manholes of Storm Drainage Network	9	06-Jan-27	16-Jan-27	03-Oct-26	12-Oct-26	0%	52,781	52,781
Catch Basin Sections		31	22-Dec-26	26-Jan-27	01-Oct-26	01-Nov-26	0%	571,680	571,680
CO-SD-CB-180	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	9	22-Dec-26	31-Dec-26	01-Oct-26	11-Oct-26	0%	107,190	107,190
CO-SD-CB-190	Installation and Pipes Laying Connection Works for Catch Basins of Storm Drainage Network	9	02-Jan-27	11-Jan-27	12-Oct-26	21-Oct-26	0%	321,570	321,570
CO-SD-CB-200	Trench Backfilling and Compaction Works for Catch Basins of Storm Drainage Network	9	17-Jan-27	26-Jan-27	22-Oct-26	01-Nov-26	0%	142,920	142,920
Sewage Network		61	08-Nov-26	17-Jan-27	03-Aug-26	13-Oct-26	0%	651,749	651,749
FROM MH-18:MH-10		53	08-Nov-26	07-Jan-27	03-Aug-26	04-Oct-26	0%	258,641	258,641
Main Line Sections		44	08-Nov-26	28-Dec-26	03-Aug-26	22-Sep-26	0%	223,587	223,587
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	08-Nov-26	21-Nov-26	03-Aug-26	16-Aug-26	0%	62,108	62,108
CO-SW-ML-120	Pipes Laying Works for Main Lines of Sewage Network	12	22-Nov-26	05-Dec-26	17-Aug-26	30-Aug-26	0%	111,794	111,794
CO-SW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Sewage Network	20	06-Dec-26	28-Dec-26	31-Aug-26	22-Sep-26	0%	49,686	49,686
Manholes		29	06-Dec-26	07-Jan-27	31-Aug-26	04-Oct-26	0%	35,054	35,054
CO-SW-MH-160	Excavation Works for Main Line Manholes of Sewage Network	7	06-Dec-26	13-Dec-26	31-Aug-26	07-Sep-26	0%	6,573	6,573

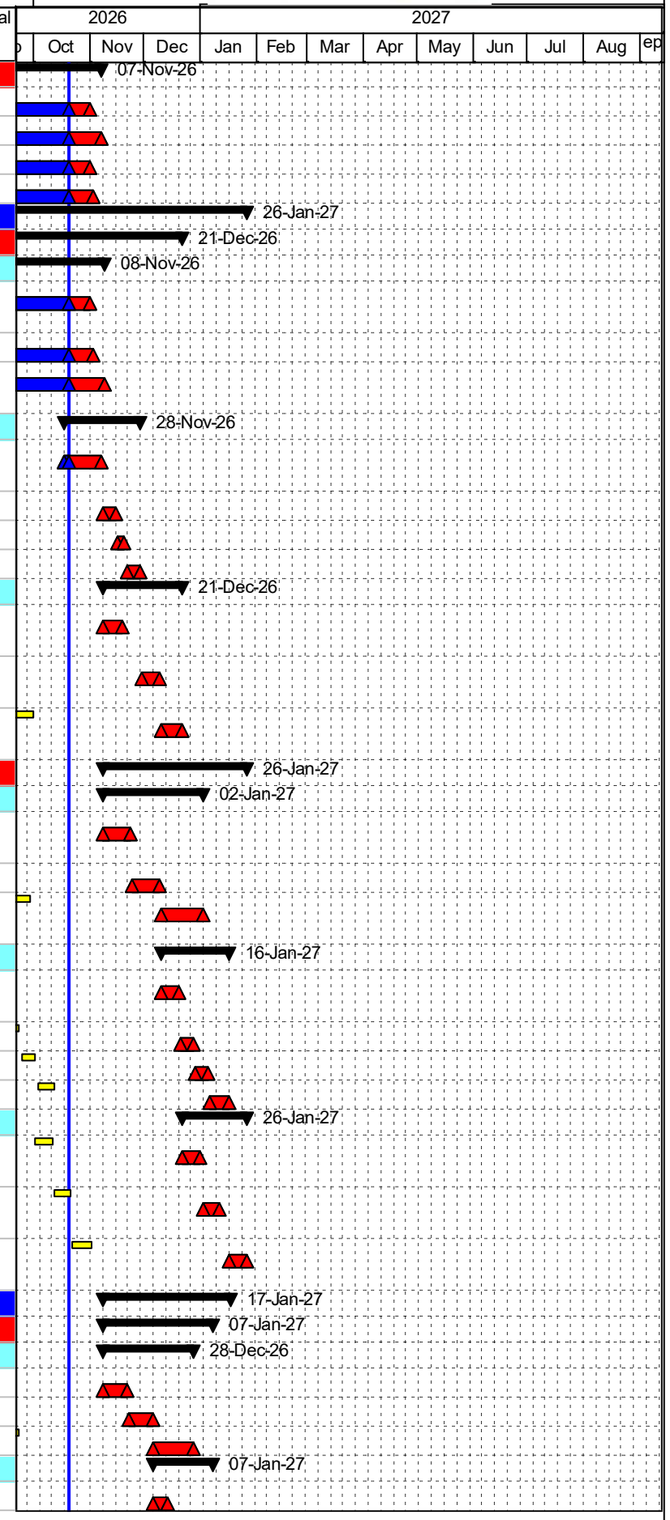


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SW-MH-170	Installation RC Footing Works for Main Line Manholes of Sewage Network	7	14-Dec-26	21-Dec-26	08-Sep-26	15-Sep-26	0%	8,763	8,763
CO-SW-MH-180	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network	7	22-Dec-26	29-Dec-26	16-Sep-26	24-Sep-26	0%	8,763	8,763
CO-SW-MH-190	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network	4	30-Dec-26	03-Jan-27	26-Sep-26	29-Sep-26	0%	2,191	2,191
CO-SW-MH-200	Backfilling Works for Main Line Manholes of Sewage Network	4	04-Jan-27	07-Jan-27	30-Sep-26	04-Oct-26	0%	8,763	8,763
FROM MH-10:MH-01		49	22-Nov-26	17-Jan-27	17-Aug-26	13-Oct-26	0%	393,108	393,108
Main Line Sections		25	22-Nov-26	20-Dec-26	17-Aug-26	14-Sep-26	0%	335,381	335,381
CO-SW-ML-140	Trench Excavation and Bedding Works for Main Lines of Sewage Network	6	22-Nov-26	28-Nov-26	17-Aug-26	23-Aug-26	0%	93,161	93,161
CO-SW-ML-150	Pipes Laying Works for Main Lines of Sewage Network	7	29-Nov-26	06-Dec-26	24-Aug-26	31-Aug-26	0%	167,691	167,691
CO-SW-ML-160	Trench Backfilling and Compaction Works for Main Lines of Sewage Network	12	07-Dec-26	20-Dec-26	01-Sep-26	14-Sep-26	0%	74,529	74,529
Manholes		30	14-Dec-26	17-Jan-27	08-Sep-26	13-Oct-26	0%	57,727	57,727
CO-SW-MH-210	Excavation Works for Main Line Manholes of Sewage Network	8	14-Dec-26	22-Dec-26	08-Sep-26	16-Sep-26	0%	10,824	10,824
CO-SW-MH-220	Installation RC Footing Works for Main Line Manholes of Sewage Network	7	23-Dec-26	30-Dec-26	17-Sep-26	26-Sep-26	0%	14,432	14,432
CO-SW-MH-230	Install Grp Liner Wall Works for Main Line Manholes of Sewage Network	7	31-Dec-26	07-Jan-27	27-Sep-26	04-Oct-26	0%	14,432	14,432
CO-SW-MH-240	Pouring Grp Liner Wall Works for Main Line Manholes of Sewage Network	4	09-Jan-27	12-Jan-27	05-Oct-26	08-Oct-26	0%	3,608	3,608
CO-SW-MH-250	Backfilling Works for Main Line Manholes of Sewage Network	4	13-Jan-27	17-Jan-27	10-Oct-26	13-Oct-26	0%	14,432	14,432
Potable Water Network		61	18-Jan-27	08-Apr-27	14-Oct-26	23-Dec-26	0%	956,108	956,108
Main Line Sections		24	18-Jan-27	16-Feb-27	14-Oct-26	10-Nov-26	0%	522,248	522,248
CO-PW-ML-100	Trench Excavation and Bedding Works for Main Lines of Potable Water Network	8	18-Jan-27	26-Jan-27	14-Oct-26	22-Oct-26	0%	145,069	145,069
CO-PW-ML-110	Pipes Laying and accessories for Main Lines of Potable Water Network	8	27-Jan-27	04-Feb-27	24-Oct-26	01-Nov-26	0%	261,124	261,124
CO-PW-ML-130	Trench Backfilling and Compaction Works for Main Lines of Potable Water Network	8	06-Feb-27	16-Feb-27	02-Nov-26	10-Nov-26	0%	116,055	116,055
Valve Chamber		16	17-Feb-27	15-Mar-27	11-Nov-26	29-Nov-26	0%	259,440	259,440
CO-PW-VC-170	Excavation Works for Main Line Valves and Valve Chambers of Potable Water Network	2	17-Feb-27	20-Feb-27	11-Nov-26	12-Nov-26	0%	15,000	15,000
CO-PW-VC180	Installation Works for Valve Chambers of Potable Water Network	4	20-Feb-27	25-Feb-27	14-Nov-26	17-Nov-26	0%	27,000	27,000
CO-PW-VC-190	Installation Works for Valves of Potable Water Network	7	25-Feb-27	08-Mar-27	18-Nov-26	25-Nov-26	0%	205,440	205,440
CO-PW-VC-220	Backfilling Works for Main Line Valves and Valve Chambers of Potable Water Network	3	13-Mar-27	15-Mar-27	26-Nov-26	29-Nov-26	0%	12,000	12,000
Fire Hydrant		21	16-Mar-27	08-Apr-27	30-Nov-26	23-Dec-26	0%	174,420	174,420
CO-PW-FH-140	Excavation Works for Fire Hydrants of Potable Water Network	7	16-Mar-27	23-Mar-27	30-Nov-26	07-Dec-26	0%	48,450	48,450
CO-PW-FH-150	Installation Works for Fire Hydrant of Potable Water Network	7	24-Mar-27	31-Mar-27	08-Dec-26	15-Dec-26	0%	87,210	87,210
CO-PW-FH-160	Trench Backfilling and Compaction Works for Fire Hydrants of Potable Water Network	7	01-Apr-27	08-Apr-27	16-Dec-26	23-Dec-26	0%	38,760	38,760
Irrigation Network		50	27-Jan-27	05-Apr-27	24-Oct-26	20-Dec-26	0%	760,970	760,970
Main Line Pipes		50	27-Jan-27	05-Apr-27	24-Oct-26	20-Dec-26	0%	760,970	760,970
CO-IR-ML-100	Trench Excavation and Bedding Works for Main Lines of Irrigation Network	10	27-Jan-27	07-Feb-27	24-Oct-26	03-Nov-26	0%	48,300	48,300
CO-IR-ML-110	Pipes Laying Works for Main Lines of Irrigation Network	10	08-Feb-27	22-Feb-27	04-Nov-26	15-Nov-26	0%	86,940	86,940
CO-IR-ML-120	Installation Works for Main Line Valves of Irrigation Network	9	22-Feb-27	08-Mar-27	15-Nov-26	25-Nov-26	0%	572,640	572,640
CO-IR-ML-130	Trench Backfilling and Compaction Works for Main Lines of Irrigation Network	9	16-Mar-27	25-Mar-27	30-Nov-26	09-Dec-26	0%	38,640	38,640
CO-IR-ML-140	Installation Works for Bulbblers And Sprinklers of Irrigation Network	9	27-Mar-27	05-Apr-27	10-Dec-26	20-Dec-26	0%	14,450	14,450
Treated Sewage Effluent (Tse)		50	27-Jan-27	05-Apr-27	24-Oct-26	20-Dec-26	0%	530,262	530,262
Main Line Pipes		50	27-Jan-27	05-Apr-27	24-Oct-26	20-Dec-26	0%	530,262	530,262
CO-TSE-ML-150	Trench Excavation and Bedding Works for Main Lines of Treated Sewage Effluent (Tse)	9	27-Jan-27	06-Feb-27	24-Oct-26	02-Nov-26	0%	76,734	76,734
CO-TSE-ML-160	Pipes Laying Works for Main Lines of Treated Sewage Effluent (Tse)	9	08-Feb-27	21-Feb-27	04-Nov-26	14-Nov-26	0%	138,121	138,121
CO-TSE-ML-170	Installation Works for Main Line Valves of Treated Sewage Effluent (Tse)	8	22-Feb-27	06-Mar-27	15-Nov-26	24-Nov-26	0%	127,320	127,320
CO-TSE-ML-180	Trench Backfilling and Compaction Works for Treated Sewage Effluent (Tse)	9	16-Mar-27	25-Mar-27	30-Nov-26	09-Dec-26	0%	61,387	61,387
CO-TSE-ML-190	Installation Works for Valve and Washout Chambers of Treated Sewage Effluent (Tse)	9	27-Mar-27	05-Apr-27	10-Dec-26	20-Dec-26	0%	126,700	126,700
Medium Voltage Network		43	06-Feb-27	06-Apr-27	02-Nov-26	21-Dec-26	0%	639,985	639,985
Cabling Works		43	06-Feb-27	06-Apr-27	02-Nov-26	21-Dec-26	0%	639,985	639,985
CO-MV-ML-250	Trench Excavation and Bedding Works for Medium Voltage Network	11	06-Feb-27	21-Feb-27	02-Nov-26	14-Nov-26	0%	41,649	41,649

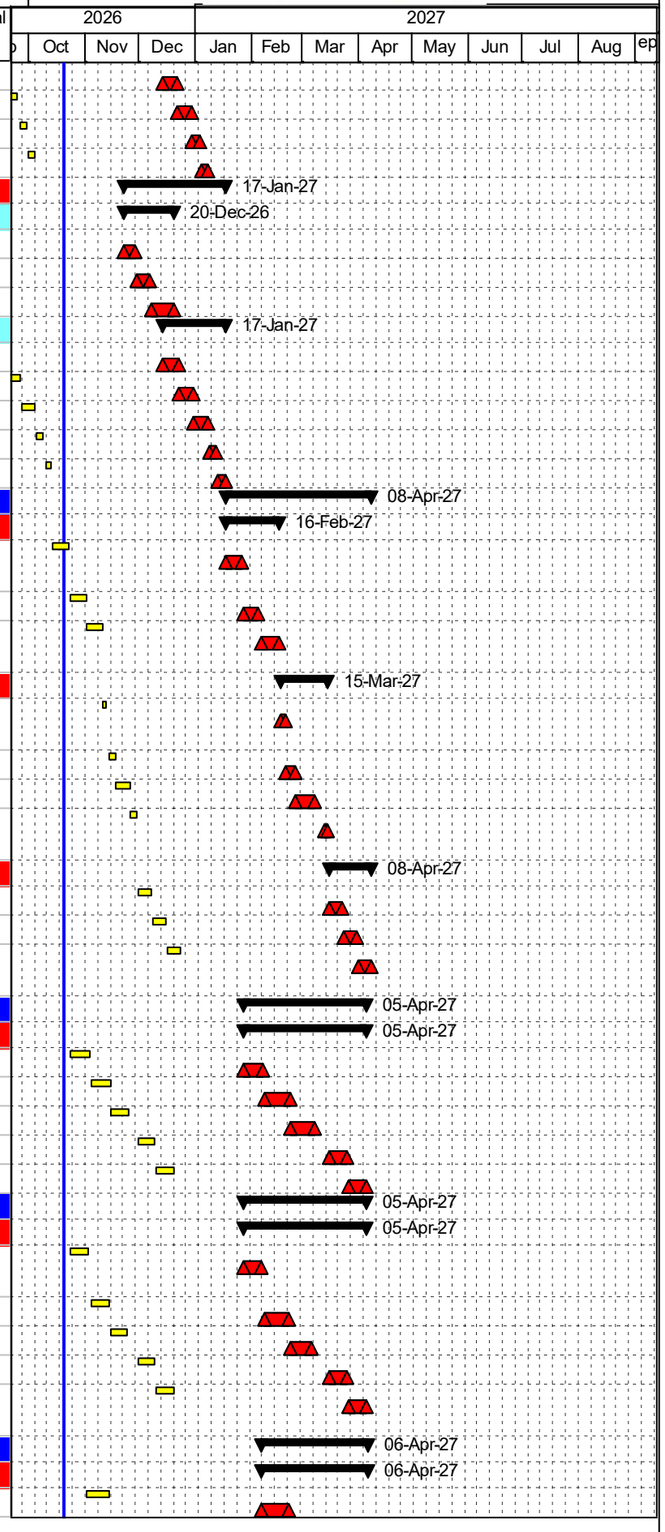

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-MV-ML-260	Cable Laying Works for Medium Voltage Network	16	22-Feb-27	18-Mar-27	15-Nov-26	02-Dec-26	0%	465,372	465,372
CO-MV-ML-270	Trench Backfilling and Compaction Works for Medium Voltage Network	16	20-Mar-27	06-Apr-27	03-Dec-26	21-Dec-26	0%	132,964	132,964
Street Lighting Network		67	06-Feb-27	04-May-27	02-Nov-26	18-Jan-27	0%	824,677	824,677
Lighting Poles Works		35	06-Feb-27	28-Mar-27	02-Nov-26	12-Dec-26	0%	239,640	239,640
CO-SL-LP-300	Foundation Excavation Works for Lighting Poles of Street Lighting Network	8	06-Feb-27	16-Feb-27	02-Nov-26	10-Nov-26	0%	29,955	29,955
CO-SL-LP-310	Installation Works for Lighting Poles Foundation of Street Lighting Network	8	17-Feb-27	01-Mar-27	11-Nov-26	19-Nov-26	0%	59,910	59,910
CO-SL-LP-320	Installation Works for Lighting Poles of Street Lighting Network	9	01-Mar-27	16-Mar-27	21-Nov-26	30-Nov-26	0%	119,820	119,820
CO-SL-LP-210	Backfilling Works for Lighting Poles of Street Lighting Network	10	17-Mar-27	28-Mar-27	01-Dec-26	12-Dec-26	0%	29,955	29,955
Cabling Works		25	17-Feb-27	25-Mar-27	11-Nov-26	09-Dec-26	0%	554,960	554,960
CO-SL-CL-250	Trench Excavation and Bedding Works for Street Lighting Network	7	17-Feb-27	27-Feb-27	11-Nov-26	18-Nov-26	0%	76,890	76,890
CO-SL-CL-260	Cable Laying Works for Street Lighting Network	7	28-Feb-27	13-Mar-27	19-Nov-26	26-Nov-26	0%	382,456	382,456
CO-SL-CL-270	Trench Backfilling and Compaction Works for Street Lighting Network	8	17-Mar-27	25-Mar-27	01-Dec-26	09-Dec-26	0%	95,614	95,614
Distrubution Panel Boards		24	07-Apr-27	04-May-27	22-Dec-26	18-Jan-27	0%	30,077	30,077
CO-SL-DB-250	Foundation Excavation Works For Panel Boards of Street Lighting Network	6	07-Apr-27	13-Apr-27	22-Dec-26	28-Dec-26	0%	4,792	4,792
CO-SL-DB-260	Installation Works for Panel Board Concrete Foundations of Street Lighting Network	6	14-Apr-27	20-Apr-27	29-Dec-26	04-Jan-27	0%	4,792	4,792
CO-SL-DB-270	Installation Works for Lighting Panel Boards of Street Lighting Network	6	21-Apr-27	27-Apr-27	05-Jan-27	11-Jan-27	0%	9,584	9,584
CO-SL-DB-220	A wall of concrete blocks to install the KWH meter of Street Lighting Network	6	28-Apr-27	04-May-27	12-Jan-27	18-Jan-27	0%	10,908	10,908
Telecom Network		42	22-Feb-27	18-Apr-27	15-Nov-26	02-Jan-27	0%	4,775,135	4,775,135
Ducts Works		26	22-Feb-27	30-Mar-27	15-Nov-26	14-Dec-26	0%	1,277,742	1,277,742
CO-TE-DW-100	Trench Excavation and Bedding Works for Ducts of Telecom Network	4	22-Feb-27	27-Feb-27	15-Nov-26	18-Nov-26	0%	274,682	274,682
CO-TE-DW-110	Pipes Laying Works for Ducts of Telecom Network	4	28-Feb-27	06-Mar-27	19-Nov-26	23-Nov-26	0%	604,299	604,299
CO-TE-DW-130	Trench Backfilling and Compaction Works for Ducts of Telecom Network	8	06-Mar-27	18-Mar-27	24-Nov-26	02-Dec-26	0%	219,745	219,745
CO-TE-DW-120	Pouring Road Crossing Concrete Encasement	10	20-Mar-27	30-Mar-27	03-Dec-26	14-Dec-26	0%	179,016	179,016
Manholes Works		19	06-Mar-27	31-Mar-27	24-Nov-26	15-Dec-26	0%	266,796	266,796
CO-TE-MH-140	Excavation Works for Manholes of Telecom Network	5	06-Mar-27	15-Mar-27	24-Nov-26	29-Nov-26	0%	66,699	66,699
CO-TE-MH-150	Installation Works for Manholes of Telecom Network	7	16-Mar-27	23-Mar-27	30-Nov-26	07-Dec-26	0%	146,738	146,738
CO-TE-MH-160	Backfilling Works for Manholes of Telecom Network	7	24-Mar-27	31-Mar-27	08-Dec-26	15-Dec-26	0%	53,359	53,359
CCTV System Wroks		15	01-Apr-27	18-Apr-27	16-Dec-26	02-Jan-27	0%	3,230,597	3,230,597
CO-TE-CTV-100	Digging and Pulling Trenches PVC ducts , Backfilling, Excavations, of Power Cable	5	01-Apr-27	06-Apr-27	16-Dec-26	21-Dec-26	0%	44,838	44,838
CO-TE-CTV-110	Installation of Network Cable Cat.6A from Network switch to CCTV Camera and ACS Device	5	07-Apr-27	12-Apr-27	22-Dec-26	27-Dec-26	0%	3,142,189	3,142,189
CO-TE-CTV-130	Installation of Access Control System	5	13-Apr-27	18-Apr-27	28-Dec-26	02-Jan-27	0%	43,570	43,570
Road Works		51	22-Mar-27	25-May-27	06-Dec-26	02-Feb-27	0%	294,864	294,864
ST+1000:ST+1531		28	22-Mar-27	22-Apr-27	06-Dec-26	06-Jan-27	0%	127,702	127,702
Pre-Bituminous Construction		28	22-Mar-27	22-Apr-27	06-Dec-26	06-Jan-27	0%	127,702	127,702
CO-RD-PB-140	Subgrade Layer for Road Works	14	22-Mar-27	06-Apr-27	06-Dec-26	21-Dec-26	0%	75,313	75,313
CO-RD-PB-150	Aggregate Base Course Layer for Road Works	14	06-Apr-27	22-Apr-27	21-Dec-26	06-Jan-27	0%	52,389	52,389
ST+500:ST+1000		25	07-Apr-27	05-May-27	22-Dec-26	19-Jan-27	0%	78,702	78,702
Pre-Bituminous Construction		25	07-Apr-27	05-May-27	22-Dec-26	19-Jan-27	0%	78,702	78,702
CO-RD-PB-120	Subgrade Layer for Road Works	11	07-Apr-27	19-Apr-27	22-Dec-26	03-Jan-27	0%	26,313	26,313
CO-RD-PB-130	Aggregate Base Course Layer for Road Works	11	22-Apr-27	05-May-27	06-Jan-27	19-Jan-27	0%	52,389	52,389
ST+01:ST+500		26	19-Apr-27	25-May-27	03-Jan-27	02-Feb-27	0%	88,461	88,461
Pre-Bituminous Construction		26	19-Apr-27	25-May-27	03-Jan-27	02-Feb-27	0%	88,461	88,461
CO-RD-PB-100	Subgrade Layer for Road Works	12	19-Apr-27	03-May-27	03-Jan-27	17-Jan-27	0%	43,556	43,556
CO-RD-PB-110	Aggregate Base Course Layer for Road Works	12	05-May-27	25-May-27	19-Jan-27	02-Feb-27	0%	44,905	44,905
Finishes for Infrastructure Networks		106	18-Jan-27	06-Jun-27	14-Oct-26	16-Feb-27	0%	8,166,438	8,166,438
Storm Drainage Network		56	27-Jan-27	12-Apr-27	02-Nov-26	05-Jan-27	0%	825,220	825,220
Testing and Finishes		56	27-Jan-27	12-Apr-27	02-Nov-26	05-Jan-27	0%	825,220	825,220
CO-SD-ML-TF-100	Testing Work for Pipes of Storm Drainage Network	10	27-Jan-27	07-Feb-27	02-Nov-26	12-Nov-26	0%	361,207	361,207
CO-SD-CB-TF-130	Catch Basin Internal Finishes (Benching) for Storm Drainage Network	10	08-Feb-27	22-Feb-27	14-Nov-26	24-Nov-26	0%	78,870	78,870
CO-SD-CB-TF-160	Testing Works for Catch Basins of Storm Drainage Network	10	23-Feb-27	13-Mar-27	25-Nov-26	06-Dec-26	0%	157,740	157,740

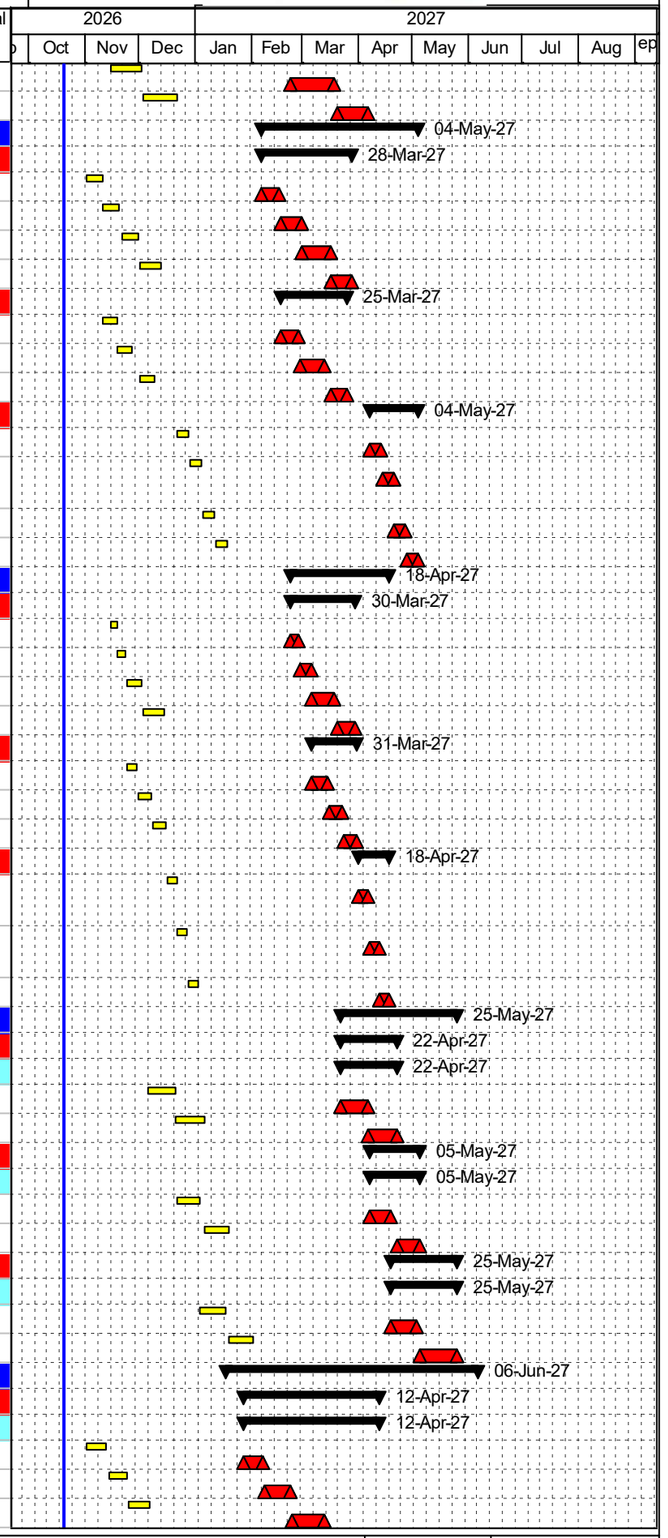

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SD-CB-TF-110	Install Catch Basin Cover Works for External Finishes of Storm Drainage Network	10	14-Mar-27	24-Mar-27	07-Dec-26	17-Dec-26	0%	78,870	78,870
CO-SD-MH-TF-120	Main Manhole Internal Finishes (Benching) for Storm Drainage Network	10	25-Mar-27	05-Apr-27	19-Dec-26	29-Dec-26	0%	89,120	89,120
CO-SD-MH-TF-210	Testing Works for Manholes of Storm Drainage Network	6	06-Apr-27	12-Apr-27	30-Dec-26	05-Jan-27	0%	59,413	59,413
Sewage Network		76	18-Jan-27	27-Apr-27	14-Oct-26	13-Jan-27	0%	85,303	85,303
Testing and Finishes		76	18-Jan-27	27-Apr-27	14-Oct-26	13-Jan-27	0%	85,303	85,303
CO-SW-TF-100	Final Testing For Main Line of Sewage Network	9	18-Jan-27	27-Jan-27	14-Oct-26	24-Oct-26	0%	62,108	62,108
CO-SW-TF-130	Main Manhole Internal Finishes (Benching + Insulation) of Sewage Network	21	28-Jan-27	25-Feb-27	25-Oct-26	17-Nov-26	0%	5,799	5,799
CO-SW-TF-110	Install Manhole Cover Works for External Finishes of Sewage Network	10	11-Apr-27	22-Apr-27	29-Dec-26	09-Jan-27	0%	5,799	5,799
CO-SW-TF-210	Testing Works for Main Line Manholes of Sewage Network	4	22-Apr-27	27-Apr-27	10-Jan-27	13-Jan-27	0%	11,598	11,598
Potable Water Network		31	10-Apr-27	20-May-27	24-Dec-26	28-Jan-27	0%	83,408	83,408
Testing and Finishes		31	10-Apr-27	20-May-27	24-Dec-26	28-Jan-27	0%	83,408	83,408
CO-PW-TF-110	Testing Work for Main Line of Potable Water Network	11	10-Apr-27	21-Apr-27	24-Dec-26	05-Jan-27	0%	58,028	58,028
CO-PW-TF-120	Fire Hydrant Finishies (S.Box + Safety + Marker Post) of Potable Water Network	10	21-Apr-27	03-May-27	05-Jan-27	17-Jan-27	0%	19,380	19,380
CO-PW-TF-100	Final Finishes works and Covers for Valves and Valve Chambers of Potable Water Network	10	03-May-27	20-May-27	17-Jan-27	28-Jan-27	0%	6,000	6,000
Irrigation Network		12	06-Apr-27	19-Apr-27	21-Dec-26	03-Jan-27	0%	19,320	19,320
Testing and Finishes		12	06-Apr-27	19-Apr-27	21-Dec-26	03-Jan-27	0%	19,320	19,320
CO-IR-TF-160	Final Testing (pressure tests) of Irrigation Network	12	06-Apr-27	19-Apr-27	21-Dec-26	03-Jan-27	0%	19,320	19,320
Treated Sewage Effluent (Tse)		12	20-Apr-27	03-May-27	04-Jan-27	17-Jan-27	0%	30,694	30,694
Testing and Finishes		12	20-Apr-27	03-May-27	04-Jan-27	17-Jan-27	0%	30,694	30,694
CO-TSE-TF-170	Final Testing (pressure tests) of Treated Sewage Effluent (Tse)	12	20-Apr-27	03-May-27	04-Jan-27	17-Jan-27	0%	30,694	30,694
Medium Voltage Network		18	07-Apr-27	27-Apr-27	22-Dec-26	11-Jan-27	0%	66,482	66,482
Termination and Testing Works		18	07-Apr-27	27-Apr-27	22-Dec-26	11-Jan-27	0%	66,482	66,482
CO-MV-TF-220	Termination Works of Medium Voltage Network	18	07-Apr-27	27-Apr-27	22-Dec-26	11-Jan-27	0%	66,482	66,482
Street Lighting Network		14	28-Apr-27	13-May-27	12-Jan-27	03-Feb-27	0%	143,686	143,686
Termination and Testing Works		14	28-Apr-27	13-May-27	12-Jan-27	03-Feb-27	0%	130,636	130,636
CO-SL-LP-330	Installation Works for Lighting Fixtures With Drop Wire of Street Lighting Network	7	28-Apr-27	05-May-27	12-Jan-27	19-Jan-27	0%	65,934	65,934
CO-SL-TF-220	Termination Works For Lighting Poles Cables of Street Lighting Network	7	06-May-27	13-May-27	20-Jan-27	27-Jan-27	0%	29,955	29,955
CO-SL-TF-230	Termination Works For Panel Board Cables of Street Lighting Network	7	06-May-27	13-May-27	20-Jan-27	27-Jan-27	0%	2,396	2,396
CO-SL-TF-200	Testing Works for Lighting Poles of Street Lighting Network	5	06-May-27	11-May-27	30-Jan-27	03-Feb-27	0%	29,955	29,955
CO-SL-TF-380	Testing Works For Panel Board Cables of Street Lighting Network	2	06-May-27	08-May-27	20-Jan-27	21-Jan-27	0%	2,396	2,396
Earthing System Works		7	28-Apr-27	05-May-27	12-Jan-27	19-Jan-27	0%	13,050	13,050
CO-SL-ES-220	Install Earthing System Works for Lighting Poles of Street Lighting Network	7	28-Apr-27	05-May-27	12-Jan-27	19-Jan-27	0%	9,135	9,135
CO-SL-ES-230	Install Earthing System Works for Lighting Panel Boards of Street Lighting Network	7	28-Apr-27	05-May-27	12-Jan-27	19-Jan-27	0%	3,915	3,915
Telecom Network		16	19-Apr-27	06-May-27	03-Jan-27	20-Jan-27	0%	82,794	82,794
Testing and Finishes		16	19-Apr-27	06-May-27	03-Jan-27	20-Jan-27	0%	82,794	82,794
CO-TE-CTV-TF-110	Smart Card Printer	4	19-Apr-27	22-Apr-27	03-Jan-27	06-Jan-27	0%	9,324	9,324
CO-TE-CTV-TF-120	Card Issue Work Station	4	24-Apr-27	27-Apr-27	07-Jan-27	11-Jan-27	0%	14,918	14,918
CO-TE-CTV-TF-130	Photographic Camera with stand	4	28-Apr-27	02-May-27	12-Jan-27	16-Jan-27	0%	11,189	11,189
CO-TE-CTV-TF-140	Interface modules with CCTV, Fire and other systems	4	03-May-27	06-May-27	17-Jan-27	20-Jan-27	0%	47,363	47,363
Road Works		47	06-Apr-27	06-Jun-27	21-Dec-26	16-Feb-27	0%	6,829,532	6,829,532
ST+1000:ST+1531		42	06-Apr-27	31-May-27	21-Dec-26	08-Feb-27	0%	2,390,336	2,390,336
Bituminous Construction		14	22-Apr-27	09-May-27	06-Jan-27	23-Jan-27	0%	212,667	212,667
CO-RD-B-150	Application of Prime Coat Layer for Road Works	7	22-Apr-27	01-May-27	06-Jan-27	14-Jan-27	0%	105,815	105,815
CO-RD-B-160	Bituminous Base Courses Layers for Road Works-	7	01-May-27	09-May-27	14-Jan-27	23-Jan-27	0%	106,852	106,852
Pavement Works		23	06-Apr-27	03-May-27	21-Dec-26	17-Jan-27	0%	2,104,946	2,104,946
CO-RD-PV-160	Fixing of Curbstone for Sidewalks Pavement	12	06-Apr-27	20-Apr-27	21-Dec-26	04-Jan-27	0%	258,754	258,754
CO-RD-PV-170	Fixing of Interlock Tiles for Sidewalks Pavement	11	20-Apr-27	03-May-27	04-Jan-27	17-Jan-27	0%	1,846,193	1,846,193
Traffic Signs Boards and Roads Marking		14	09-May-27	31-May-27	23-Jan-27	08-Feb-27	0%	72,723	72,723

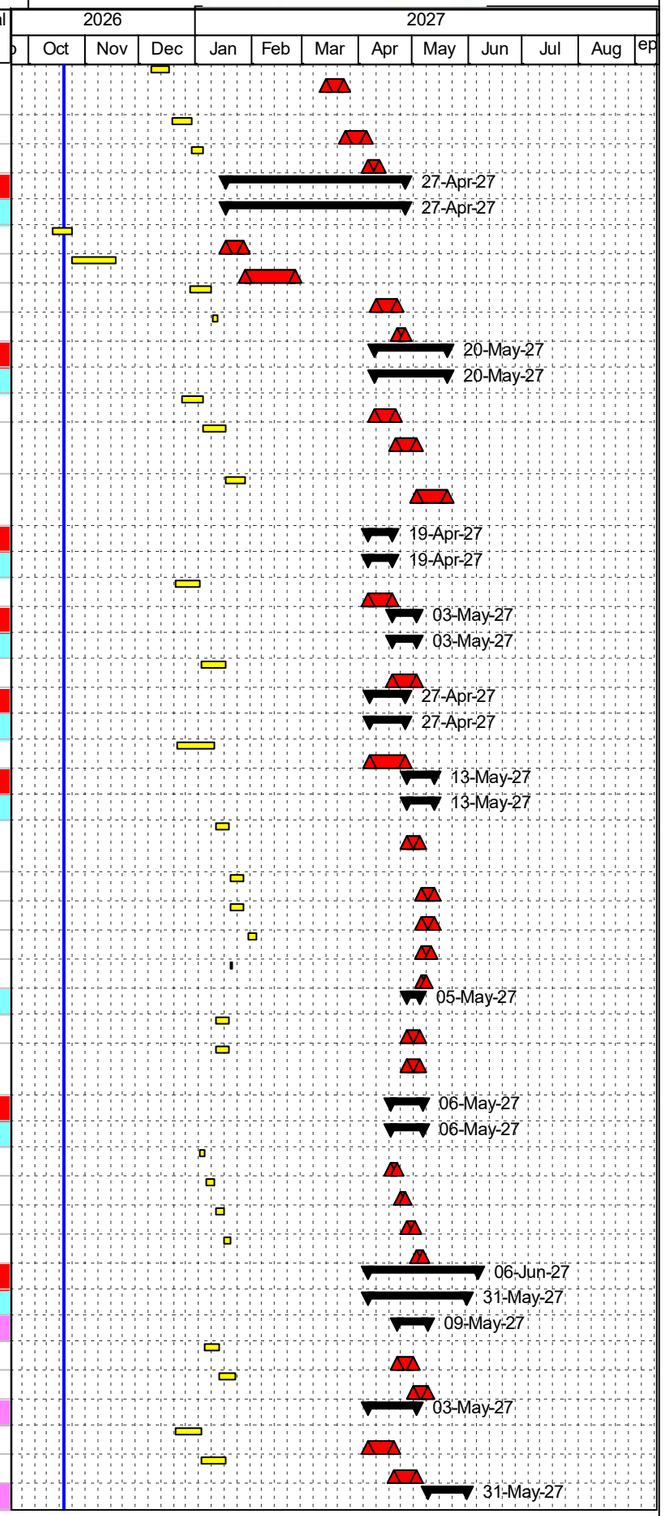

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-RD-F-RM-180	Application of Road Marking Works For Road Works	7	09-May-27	23-May-27	23-Jan-27	31-Jan-27	0%	35,427	35,427
CO-RD-F-TS-120	Installation Works of Traffic Signs Boards For Road Works	7	23-May-27	31-May-27	31-Jan-27	08-Feb-27	0%	37,296	37,296
ST+500:ST+1000		34	20-Apr-27	05-Jun-27	04-Jan-27	14-Feb-27	0%	2,390,336	2,390,336
Bituminous Construction		8	09-May-27	24-May-27	23-Jan-27	01-Feb-27	0%	212,667	212,667
CO-RD-B-130	Application of Prime Coat Layer for Road Works	4	09-May-27	13-May-27	23-Jan-27	27-Jan-27	0%	105,815	105,815
CO-RD-B-140	Bituminous Base Courses Layers for Road Works-	4	13-May-27	24-May-27	27-Jan-27	01-Feb-27	0%	106,852	106,852
Pavement Works		22	20-Apr-27	22-May-27	04-Jan-27	30-Jan-27	0%	2,104,946	2,104,946
CO-RD-PV-140	Fixing of Curbstone for Sidewalks Pavement	11	20-Apr-27	03-May-27	04-Jan-27	17-Jan-27	0%	258,754	258,754
CO-RD-PV-150	Fixing of Interlock Tiles for Sidewalks Pavement	11	03-May-27	22-May-27	17-Jan-27	30-Jan-27	0%	1,846,193	1,846,193
Traffic Signs Boards and Roads Marking		9	25-May-27	05-Jun-27	02-Feb-27	14-Feb-27	0%	72,723	72,723
CO-RD-F-RM-170	Application of Road Marking Works For Road Works	5	25-May-27	31-May-27	02-Feb-27	08-Feb-27	0%	35,427	35,427
CO-RD-F-TS-110	Installation Works of Traffic Signs Boards For Road Works	4	31-May-27	05-Jun-27	08-Feb-27	14-Feb-27	0%	37,296	37,296
ST+01:ST+500		24	03-May-27	06-Jun-27	17-Jan-27	16-Feb-27	0%	2,048,860	2,048,860
Bituminous Construction		9	25-May-27	05-Jun-27	02-Feb-27	14-Feb-27	0%	182,286	182,286
CO-RD-B-110	Application of Prime Coat Layer for Road Works	5	25-May-27	31-May-27	02-Feb-27	08-Feb-27	0%	90,698	90,698
CO-RD-B-120	Bituminous Base Courses Layers for Road Works-	4	31-May-27	05-Jun-27	08-Feb-27	14-Feb-27	0%	91,588	91,588
Pavement Works		22	03-May-27	03-Jun-27	17-Jan-27	14-Feb-27	0%	1,804,240	1,804,240
CO-RD-PV-120	Fixing of Curbstone for Sidewalks Pavement	11	03-May-27	22-May-27	17-Jan-27	30-Jan-27	0%	221,789	221,789
CO-RD-PV-130	Fixing of Interlock Tiles for Sidewalks Pavement	11	22-May-27	03-Jun-27	30-Jan-27	14-Feb-27	0%	1,582,451	1,582,451
Traffic Signs Boards and Roads Marking		1	05-Jun-27	06-Jun-27	15-Feb-27	16-Feb-27	0%	62,334	62,334
CO-RD-F-RM-160	Application of Road Marking Works For Road Works	1	05-Jun-27	06-Jun-27	15-Feb-27	16-Feb-27	0%	30,366	30,366
CO-RD-F-TS-100	Installation Works of Traffic Signs Boards For Road Works	1	05-Jun-27	06-Jun-27	15-Feb-27	16-Feb-27	0%	31,968	31,968
Superstructure Work		242	02-Aug-26 A	03-Jun-27	11-Aug-26	23-Feb-27	15.65%	32,877,819	32,137,377
Utility Buildings		167	23-Sep-26 A	12-May-27	24-Aug-26	28-Jan-27	1.11%	12,869,852	12,869,852
Pump Station		167	20-Oct-26	12-May-27	30-Nov-26	28-Jan-27	0%	3,104,581	3,104,581
Civil work		2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	0%	72,069	72,069
Super structure		2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	0%	72,069	72,069
CO-UB-PS-250	curing and deshuttering formwork for pump roof	2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	0%	72,069	72,069
Architectural work		35	22-Oct-26	01-Dec-26	02-Dec-26	12-Jan-27	0%	870,438	870,438
CO-UB-PS-260	Executing Masonry Works for Pump station building	5	22-Oct-26	27-Oct-26	02-Dec-26	08-Dec-26	0%	183,776	183,776
CO-UB-PS-270	Executing Plastering Works for Pump station building	5	28-Oct-26	02-Nov-26	08-Dec-26	14-Dec-26	0%	229,720	229,720
CO-UB-PS-280	Executing Painting Works for Pump station building	5	03-Nov-26	08-Nov-26	14-Dec-26	20-Dec-26	0%	227,221	227,221
CO-UB-PS-320	Doors and windows Fixing &Stair Tiles	7	24-Nov-26	01-Dec-26	04-Jan-27	12-Jan-27	0%	229,720	229,720
Electrical work		145	09-Nov-26	06-May-27	20-Dec-26	23-Jan-27	0%	540,519	540,519
CO-UB-PS-290	Lighting system for pump house	5	09-Nov-26	14-Nov-26	20-Dec-26	26-Dec-26	0%	135,130	135,130
CO-UB-PS-300	Wiring connection for pump house	5	15-Nov-26	19-Nov-26	26-Dec-26	31-Dec-26	0%	54,052	54,052
CO-UB-PS-310	Sockets and switches for pump house	3	21-Nov-26	23-Nov-26	31-Dec-26	04-Jan-27	0%	81,078	81,078
CO-UB-PS-330	Installation for Distribution boards for pump house	8	24-Nov-26	02-Dec-26	04-Jan-27	13-Jan-27	0%	135,130	135,130
CO-UB-PS-370	Executing Earthing and bonding for the entire system	8	28-Apr-27	06-May-27	13-Jan-27	23-Jan-27	0%	135,130	135,130
Mechanical work		137	24-Nov-26	12-May-27	04-Jan-27	28-Jan-27	0%	1,621,556	1,621,556
CO-UB-PS-340	Executing HVAC System for Pump station building	14	24-Nov-26	09-Dec-26	04-Jan-27	20-Jan-27	0%	162,156	162,156
CO-UB-PS-350	Executing Fire Alarm System for Pump station building	5	24-Nov-26	29-Nov-26	04-Jan-27	10-Jan-27	0%	324,311	324,311
CO-UB-PS-360	Executing Fire fighting institution works(piping and wire installation) for Pump station building	5	30-Nov-26	05-Dec-26	10-Jan-27	16-Jan-27	0%	405,389	405,389
CO-UB-PS-380	Executing Fire fighting finishing works for Pump station building	5	06-Dec-26	10-Dec-26	16-Jan-27	21-Jan-27	0%	162,156	162,156
CO-UB-PS-390	Installation of pumps	5	08-May-27	12-May-27	23-Jan-27	28-Jan-27	0%	567,545	567,545
Lift Station		68	23-Sep-26 A	17-Jan-27	15-Oct-26	21-Jan-27	5.65%	2,530,828	2,530,828
Civil work		51	23-Sep-26 A	23-Nov-26	15-Oct-26	28-Nov-26	25.76%	554,932	554,932
Super structure		51	23-Sep-26 A	23-Nov-26	15-Oct-26	28-Nov-26	25.76%	554,932	554,932
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	27-Oct-26	15-Oct-26	22-Oct-26	70%	84,081	84,081
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	29-Oct-26	24-Oct-26	02-Nov-26	70%	84,081	84,081
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	29-Oct-26	03-Nov-26	03-Nov-26	50%	50,448	50,448

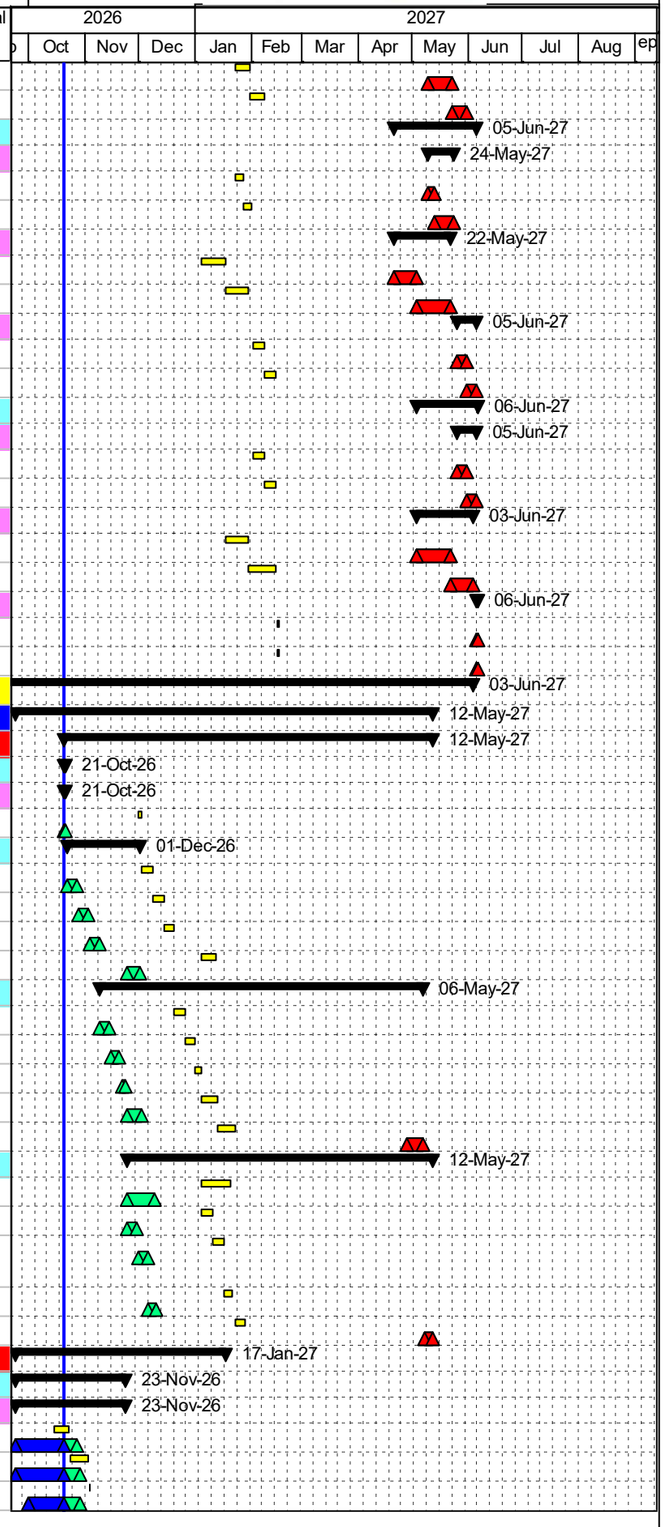

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	2	31-Oct-26	01-Nov-26	04-Nov-26	05-Nov-26	0%	8,408	8,408
CO-UB-LS-330	Waterproofing for Walls columns	4	02-Nov-26	05-Nov-26	07-Nov-26	10-Nov-26	0%	84,081	84,081
CO-UB-LS-340	Formwork for pump roof	5	07-Nov-26	11-Nov-26	11-Nov-26	16-Nov-26	0%	84,081	84,081
CO-UB-LS-350	Steel fixing for pump roof	6	12-Nov-26	18-Nov-26	17-Nov-26	23-Nov-26	0%	84,081	84,081
CO-UB-LS-360	pouring for pump roof	1	19-Nov-26	19-Nov-26	24-Nov-26	24-Nov-26	0%	67,265	67,265
CO-UB-LS-370	curing and deshuttering formwork for pump roof	3	21-Nov-26	23-Nov-26	25-Nov-26	28-Nov-26	0%	8,408	8,408
Architectural work		15	24-Nov-26	10-Dec-26	29-Nov-26	15-Dec-26	0%	714,686	714,686
CO-UB-LS-380	Executing Masonry Works for Pump station building	7	24-Nov-26	01-Dec-26	29-Nov-26	06-Dec-26	0%	357,343	357,343
CO-UB-LS-390	Executing Plastering Works for Pump station building	8	02-Dec-26	10-Dec-26	07-Dec-26	15-Dec-26	0%	357,343	357,343
Electrical work		32	12-Dec-26	17-Jan-27	16-Dec-26	21-Jan-27	0%	420,403	420,403
CO-UB-LS-400	Lighting system for pump house	8	12-Dec-26	20-Dec-26	16-Dec-26	24-Dec-26	0%	147,141	147,141
CO-UB-LS-420	Wiring connection for pump house	6	21-Dec-26	27-Dec-26	26-Dec-26	31-Dec-26	0%	84,081	84,081
CO-UB-LS-440	Sockets and switches for pump house	6	28-Dec-26	03-Jan-27	02-Jan-27	07-Jan-27	0%	42,040	42,040
CO-UB-LS-460	Installation for Distribution boards for pump house	6	04-Jan-27	10-Jan-27	09-Jan-27	14-Jan-27	0%	105,101	105,101
CO-UB-LS-480	Executing Earthing and bonding for the entire system	6	11-Jan-27	17-Jan-27	16-Jan-27	21-Jan-27	0%	42,040	42,040
Mechanical work		30	12-Dec-26	14-Jan-27	16-Dec-26	19-Jan-27	0%	840,807	840,807
CO-UB-LS-410	Internal pipe installation	8	12-Dec-26	20-Dec-26	16-Dec-26	24-Dec-26	0%	210,202	210,202
CO-UB-LS-430	Guide rails & lifting chains installation	7	21-Dec-26	28-Dec-26	26-Dec-26	02-Jan-27	0%	168,161	168,161
CO-UB-LS-450	ExeValve installation	7	29-Dec-26	05-Jan-27	03-Jan-27	10-Jan-27	0%	210,202	210,202
CO-UB-LS-470	Installation of pumps	8	06-Jan-27	14-Jan-27	11-Jan-27	19-Jan-27	0%	252,242	252,242
Potable Water Tank		66	21-Dec-26	17-Mar-27	24-Aug-26	09-Nov-26	0%	615,094	615,094
Eearth Work		12	21-Dec-26	03-Jan-27	24-Aug-26	06-Sep-26	0%	7,354	7,354
CO-UB-PWT-100	Excavation work for tank foundation tank formation level	7	21-Dec-26	28-Dec-26	24-Aug-26	31-Aug-26	0%	0	0
CO-UB-PWT-110	Soil replacement Up to tank formation level	5	29-Dec-26	03-Jan-27	01-Sep-26	06-Sep-26	0%	7,354	7,354
Structural Work		15	04-Jan-27	20-Jan-27	07-Sep-26	24-Sep-26	0%	118,429	118,429
CO-UB-PWT-120	Plain Concrete works	3	04-Jan-27	06-Jan-27	07-Sep-26	09-Sep-26	0%	24,787	24,787
CO-UB-PWT-130	Form work for Tank Foundation	5	07-Jan-27	12-Jan-27	10-Sep-26	15-Sep-26	0%	41,312	41,312
CO-UB-PWT-140	Steel Reinforcement work for Tank Foundation	6	13-Jan-27	19-Jan-27	16-Sep-26	22-Sep-26	0%	38,558	38,558
CO-UB-PWT-150	Casting concrete for Tank Foundation	1	20-Jan-27	20-Jan-27	24-Sep-26	24-Sep-26	0%	13,771	13,771
Tank Shell Erection&Roof Installation		22	21-Jan-27	18-Feb-27	26-Sep-26	20-Oct-26	0%	330,498	330,498
CO-UB-PWT-160	Bottom ring installation	6	21-Jan-27	27-Jan-27	26-Sep-26	01-Oct-26	0%	82,625	82,625
CO-UB-PWT-170	shell erection	8	28-Jan-27	06-Feb-27	03-Oct-26	11-Oct-26	0%	110,166	110,166
CO-UB-PWT-180	Aluminum dome / steel roof installation	8	07-Feb-27	18-Feb-27	12-Oct-26	20-Oct-26	0%	137,708	137,708
Mechanical Work&Accessories		17	18-Feb-27	17-Mar-27	21-Oct-26	09-Nov-26	0%	158,814	158,814
CO-UB-PWT-190	Inlet / outlet piping connections	6	18-Feb-27	27-Feb-27	21-Oct-26	27-Oct-26	0%	81,697	81,697
CO-UB-PWT-200	installation Valves	6	28-Feb-27	08-Mar-27	28-Oct-26	03-Nov-26	0%	55,083	55,083
CO-UB-PWT-210	Ladders, platforms & handrails	5	13-Mar-27	17-Mar-27	04-Nov-26	09-Nov-26	0%	22,033	22,033
IrrigationTank		119	14-Oct-26 A	21-Dec-26	10-Nov-26	11-Jan-27	0%	615,094	615,094
Eearth Work		119	14-Oct-26 A	01-Nov-26	10-Nov-26	22-Nov-26	0%	7,354	7,354
CO-UB-IRT-140	Excavation work for tank foundation tank formation level	6	14-Oct-26 A	26-Oct-26	10-Nov-26	16-Nov-26	30%	0	0
CO-UB-IRT-150	Soil replacement Up to tank formation level	5	27-Oct-26	01-Nov-26	17-Nov-26	22-Nov-26	0%	7,354	7,354
Structural Work		15	02-Nov-26	18-Nov-26	23-Nov-26	09-Dec-26	0%	118,429	118,429
CO-UB-IRT-160	Plain Concrete works	3	02-Nov-26	04-Nov-26	23-Nov-26	25-Nov-26	0%	24,787	24,787
CO-UB-IRT-170	Form work for Tank Foundation	6	05-Nov-26	11-Nov-26	26-Nov-26	02-Dec-26	0%	41,312	41,312
CO-UB-IRT-180	Steel Reinforcement work for Tank Foundation	5	12-Nov-26	17-Nov-26	03-Dec-26	08-Dec-26	0%	38,558	38,558
CO-UB-IRT-190	Casting concrete for Tank Foundation	1	18-Nov-26	18-Nov-26	09-Dec-26	09-Dec-26	0%	13,771	13,771
Tank Shell Erection&Roof Installation		18	19-Nov-26	09-Dec-26	10-Dec-26	30-Dec-26	0%	330,498	330,498
CO-UB-IRT-200	Bottom ring installation	6	19-Nov-26	25-Nov-26	10-Dec-26	16-Dec-26	0%	82,625	82,625
CO-UB-IRT-210	shell erection	6	26-Nov-26	02-Dec-26	17-Dec-26	23-Dec-26	0%	110,166	110,166
CO-UB-IRT-220	Aluminum dome / steel roof installation	6	03-Dec-26	09-Dec-26	24-Dec-26	30-Dec-26	0%	137,708	137,708
Mechanical Work&Accessories		10	10-Dec-26	21-Dec-26	31-Dec-26	11-Jan-27	0%	158,814	158,814

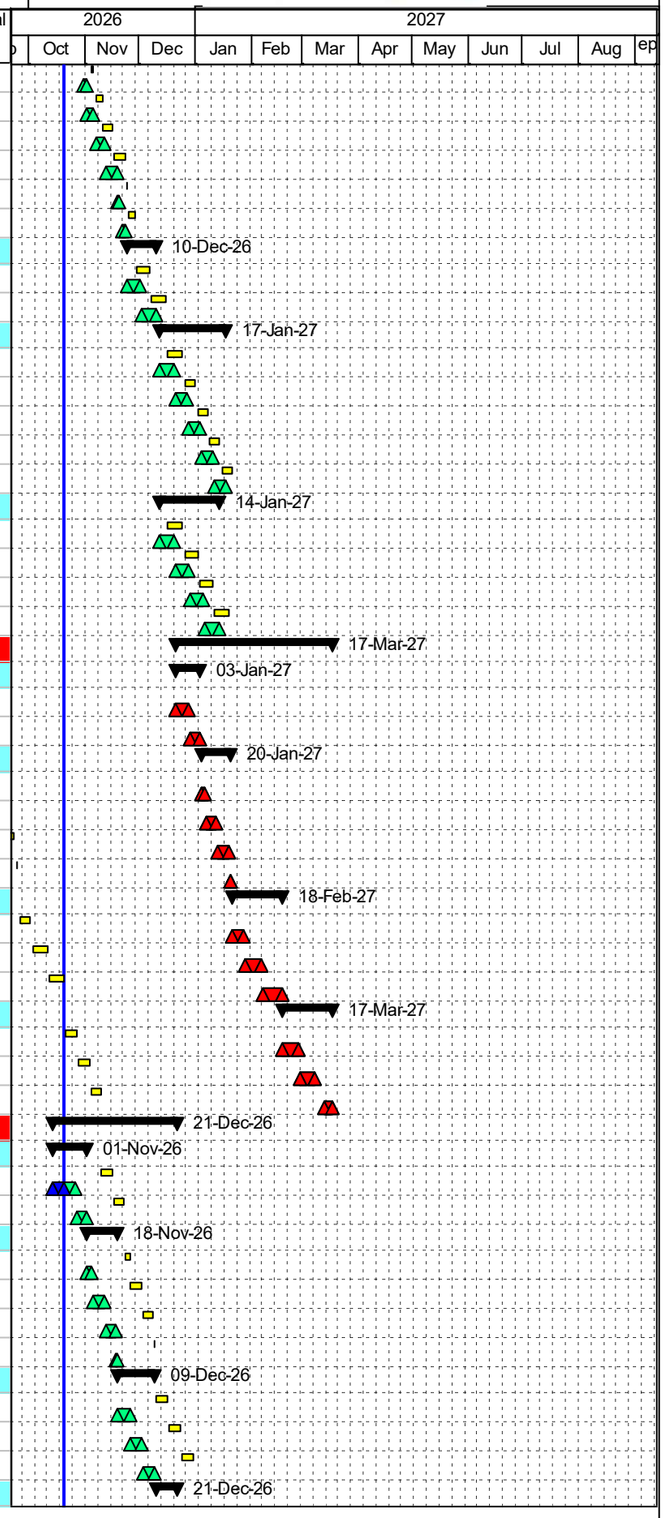


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-UB-IRT-230	Inlet / outlet piping connections	4	10-Dec-26	14-Dec-26	31-Dec-26	04-Jan-27	0%	81,697	81,697
CO-UB-IRT-240	installation Valves	4	15-Dec-26	19-Dec-26	05-Jan-27	09-Jan-27	0%	55,083	55,083
CO-UB-IRT-250	Ladders, platforms & handrails	2	20-Dec-26	21-Dec-26	10-Jan-27	11-Jan-27	0%	22,033	22,033
Control Room		82	20-Oct-26	23-Jan-27	19-Oct-26	21-Jan-27	0%	2,078,714	2,078,714
Civil Work		16	20-Oct-26	07-Nov-26	19-Oct-26	05-Nov-26	0%	397,101	397,101
CO-UB-CR-130	Pouring R.C Columns For Control Room	8	20-Oct-26	28-Oct-26	19-Oct-26	27-Oct-26	0%	144,859	144,859
CO-UB-CR-140	Pouring Beams and Slab For Control Room	8	29-Oct-26	07-Nov-26	28-Oct-26	05-Nov-26	0%	252,242	252,242
Finishing Work		66	08-Nov-26	23-Jan-27	07-Nov-26	21-Jan-27	0%	1,681,613	1,681,613
Architictural work		40	08-Nov-26	23-Dec-26	07-Nov-26	22-Dec-26	0%	480,461	480,461
CO-UB-CR-150	Brick Work For Control Room	9	08-Nov-26	17-Nov-26	07-Nov-26	16-Nov-26	0%	96,092	96,092
CO-UB-CR-160	Thermal & Moisture Protection Work for Control Room	7	18-Nov-26	25-Nov-26	17-Nov-26	24-Nov-26	0%	96,092	96,092
CO-UB-CR-200	Install For Curtian Wall and Windows and Doors	8	26-Nov-26	05-Dec-26	25-Nov-26	03-Dec-26	0%	96,092	96,092
CO-UB-CR-240	External Finshing Work (Walls and Floor)	8	06-Dec-26	14-Dec-26	05-Dec-26	13-Dec-26	0%	96,092	96,092
CO-UB-CR-250	Internal Finshing Work (Walls,Floor and Ceiling)	8	15-Dec-26	23-Dec-26	14-Dec-26	22-Dec-26	0%	96,092	96,092
Mechanical Work		41	18-Nov-26	04-Jan-27	17-Nov-26	03-Jan-27	0%	480,461	480,461
HVAC System		41	18-Nov-26	04-Jan-27	17-Nov-26	03-Jan-27	0%	288,277	288,277
CO-UB-CR-170	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports, vanes, dampers)	4	18-Nov-26	22-Nov-26	17-Nov-26	21-Nov-26	0%	96,092	96,092
CO-UB-CR-260	Install of Mini split actual capacity 2 Ton and Ducted split actual capacity 4 Ton	7	24-Dec-26	31-Dec-26	23-Dec-26	30-Dec-26	0%	96,092	96,092
CO-UB-CR-310	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	3	02-Jan-27	04-Jan-27	31-Dec-26	03-Jan-27	0%	96,092	96,092
Fire Fitting System		30	23-Nov-26	27-Dec-26	22-Nov-26	26-Dec-26	0%	192,184	192,184
CO-UB-CR-180	Installation & Testing of 2 hours Fire rated system for closing the openings between rooms with help of Rock wool	4	23-Nov-26	26-Nov-26	22-Nov-26	25-Nov-26	0%	96,092	96,092
CO-UB-CR-270	Install Fire Extinguishers	3	24-Dec-26	27-Dec-26	23-Dec-26	26-Dec-26	0%	96,092	96,092
Electrical Work		44	28-Nov-26	17-Jan-27	26-Nov-26	16-Jan-27	0%	480,461	480,461
LV Power		15	24-Dec-26	10-Jan-27	23-Dec-26	09-Jan-27	0%	131,035	131,035
CO-UB-CR-190	Install of Distribution board For Control Room	5	24-Dec-26	29-Dec-26	23-Dec-26	28-Dec-26	0%	43,678	43,678
CO-UB-CR-220	Install of Earting Cable for Control Room	5	30-Dec-26	04-Jan-27	29-Dec-26	03-Jan-27	0%	43,678	43,678
CO-UB-CR-280	Install of Socket outlet and LED Lighting	5	05-Jan-27	10-Jan-27	04-Jan-27	09-Jan-27	0%	43,678	43,678
Fire Detection And Alarm System		44	28-Nov-26	17-Jan-27	26-Nov-26	16-Jan-27	0%	349,426	349,426
CO-UB-CR-210	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	5	28-Nov-26	02-Dec-26	26-Nov-26	01-Dec-26	0%	43,678	43,678
CO-UB-CR-230	Install of Transmission Communication cable - Fiber Optics 12Core	5	03-Dec-26	08-Dec-26	02-Dec-26	07-Dec-26	0%	43,678	43,678
CO-UB-CR-290	Install of power supply system for fire alarm control panel	5	24-Dec-26	29-Dec-26	23-Dec-26	28-Dec-26	0%	43,678	43,678
CO-UB-CR-300	Install of Fire Alarm Control panel	6	30-Dec-26	05-Jan-27	29-Dec-26	04-Jan-27	0%	43,678	43,678
CO-UB-CR-320	Installation of the addressable manual call point with operation safety glass breaking	3	06-Jan-27	09-Jan-27	05-Jan-27	07-Jan-27	0%	43,678	43,678
CO-UB-CR-330	Install of the photoelectric heat & smoke detector	3	10-Jan-27	12-Jan-27	09-Jan-27	11-Jan-27	0%	43,678	43,678
CO-UB-CR-340	Install of Sounder With Beacon	3	10-Jan-27	12-Jan-27	09-Jan-27	11-Jan-27	0%	43,678	43,678
CO-UB-CR-350	Install of Addressable Control module	4	13-Jan-27	17-Jan-27	12-Jan-27	16-Jan-27	0%	43,678	43,678
Furnitures work		5	18-Jan-27	23-Jan-27	17-Jan-27	21-Jan-27	0%	240,230	240,230
CO-UB-CR-360	Office Chairs,Tables and Stand	5	18-Jan-27	23-Jan-27	17-Jan-27	21-Jan-27	0%	240,230	240,230
Softscape and Planting Works		39	17-Feb-27	11-Apr-27	07-Nov-26	22-Dec-26	0%	3,925,540	3,925,540
Planting Beds Preparation		21	17-Feb-27	21-Mar-27	07-Nov-26	01-Dec-26	0%	1,011,244	1,011,244
CO-LS-PL-100	Excavation of planting beds	7	17-Feb-27	27-Feb-27	07-Nov-26	15-Nov-26	0%	144,463	144,463
CO-LS-PL-110	Supply & placement of suitable topsoil	7	28-Feb-27	13-Mar-27	15-Nov-26	23-Nov-26	0%	433,390	433,390
CO-LS-PL-120	Soil improvement (fertilizer, compost, additives)	7	14-Mar-27	21-Mar-27	23-Nov-26	01-Dec-26	0%	433,390	433,390
Supports & Protection		6	22-Mar-27	28-Mar-27	01-Dec-26	08-Dec-26	0%	1,011,244	1,011,244
CO-LS-PL-130	installation of plant supports / stakes	3	22-Mar-27	24-Mar-27	01-Dec-26	05-Dec-26	0%	433,390	433,390
CO-LS-PL-140	Ties and protection materials	3	25-Mar-27	28-Mar-27	05-Dec-26	08-Dec-26	0%	577,854	577,854
Plant Supply		3	29-Mar-27	31-Mar-27	08-Dec-26	12-Dec-26	0%	866,781	866,781
CO-LS-PL-150	installation of trees	3	29-Mar-27	31-Mar-27	08-Dec-26	12-Dec-26	0%	866,781	866,781
Site Furnishings		9	01-Apr-27	11-Apr-27	12-Dec-26	22-Dec-26	0%	1,036,272	1,036,272

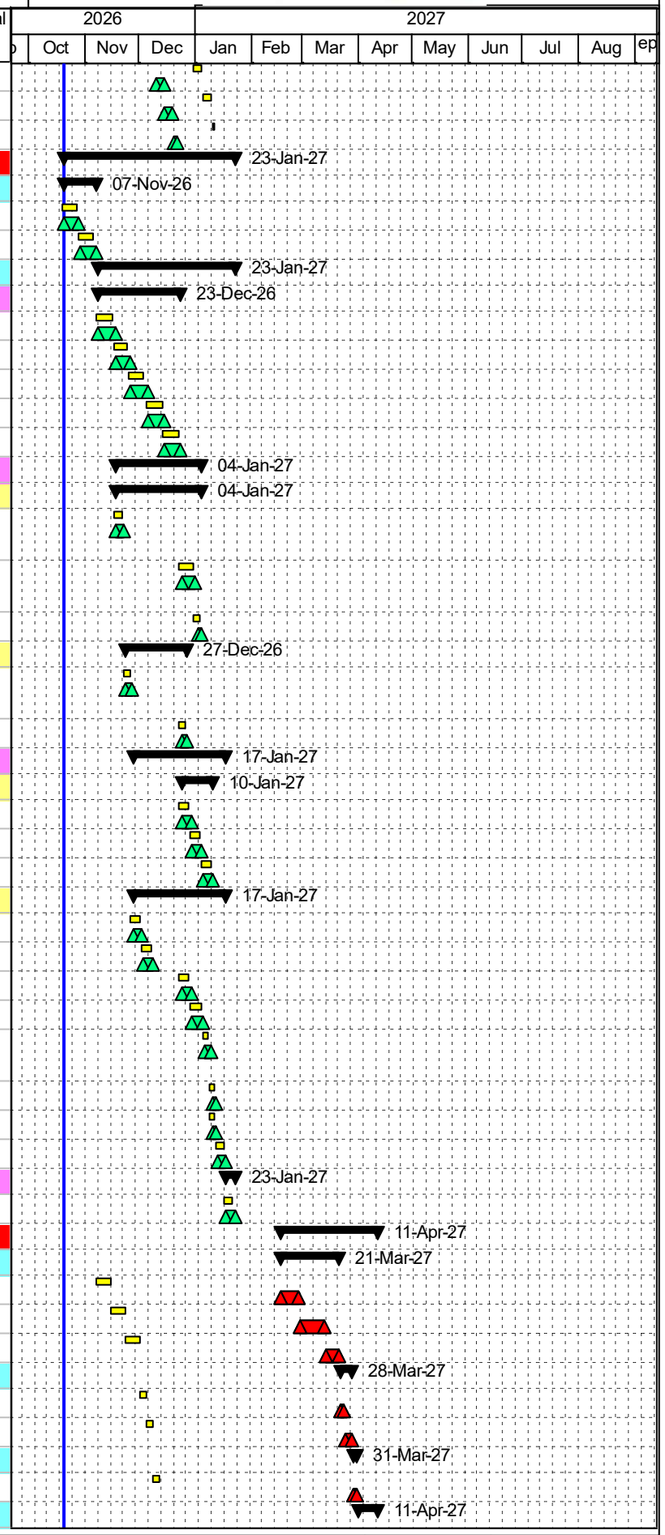


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-LS-PL-160	installation of Seating benches	3	01-Apr-27	04-Apr-27	12-Dec-26	15-Dec-26	0%	345,424	345,424
CO-LS-PL-170	tone boulders placement & fixing Works	3	05-Apr-27	07-Apr-27	15-Dec-26	19-Dec-26	0%	345,424	345,424
CO-LS-PL-180	Gravel Works	3	08-Apr-27	11-Apr-27	19-Dec-26	22-Dec-26	0%	345,424	345,424
Fence and Gaurd Room		242	02-Aug-26 A	03-Jun-27	11-Aug-26	23-Feb-27	25%	20,007,967	19,267,524
Gaurd Room Work		124	26-Dec-26	03-Jun-27	29-Aug-26	20-Jan-27	0%	2,138,081	2,138,081
Civil Work		41	26-Dec-26	11-Feb-27	29-Aug-26	15-Oct-26	0%	198,090	198,090
A1000	Excavation Work For Gaurd Room Foundation	7	26-Dec-26	02-Jan-27	29-Aug-26	05-Sep-26	0%	0	0
A1010	Pouring for Plain Concrete	4	03-Jan-27	06-Jan-27	06-Sep-26	09-Sep-26	0%	42,000	42,000
A1020	Pouring R.C Footing For Gaurd Room	11	07-Jan-27	19-Jan-27	10-Sep-26	22-Sep-26	0%	60,600	60,600
A1030	Pouring R.C Columns For Gaurd Room	10	20-Jan-27	31-Jan-27	24-Sep-26	05-Oct-26	0%	12,600	12,600
A1040	Pouring Beams and Slab For Gaurd Room	9	01-Feb-27	11-Feb-27	06-Oct-26	15-Oct-26	0%	82,890	82,890
Finishing Work		83	13-Feb-27	03-Jun-27	17-Oct-26	20-Jan-27	0%	1,939,991	1,939,991
Architictural work		46	13-Feb-27	15-Apr-27	17-Oct-26	08-Dec-26	0%	287,137	287,137
A1050	Brick Work For Gaurd Room	9	13-Feb-27	25-Feb-27	17-Oct-26	26-Oct-26	0%	32,904	32,904
A1060	Thermal & Moisture Protection Work for Gaurd Room	7	25-Feb-27	08-Mar-27	27-Oct-26	03-Nov-26	0%	40,920	40,920
A1070	Install For Curtian Wall and Windows and Doors	8	20-Mar-27	28-Mar-27	11-Nov-26	19-Nov-26	0%	170,473	170,473
A1080	External Finshing Work (Walls and Floor)	8	29-Mar-27	06-Apr-27	21-Nov-26	29-Nov-26	0%	11,172	11,172
A1090	Internal Finshing Work (Walls,Floor and Ceiling)	8	07-Apr-27	15-Apr-27	30-Nov-26	08-Dec-26	0%	31,668	31,668
Mechanical Work		47	25-Feb-27	27-Apr-27	27-Oct-26	20-Dec-26	0%	190,986	190,986
Sanitary Drainage & Plumbing System		13	25-Feb-27	18-Mar-27	27-Oct-26	10-Nov-26	0%	33,408	33,408
A1110	Install Sanitary Piping System (UPVC)	4	25-Feb-27	03-Mar-27	27-Oct-26	31-Oct-26	0%	22,224	22,224
A1120	Install Base mounted flush tank water Western water closet system	6	04-Mar-27	15-Mar-27	01-Nov-26	07-Nov-26	0%	7,680	7,680
A1130	Install 1 meter length 10mm diameter Flexible Hose and Gate Valves and Slow Closing Valve	3	16-Mar-27	18-Mar-27	08-Nov-26	10-Nov-26	0%	3,504	3,504
Water Supply System		39	25-Feb-27	18-Apr-27	27-Oct-26	10-Dec-26	0%	69,498	69,498
A1240	Install GRP water tanks capacity of each 1000 liter	3	25-Feb-27	02-Mar-27	27-Oct-26	29-Oct-26	0%	25,200	25,200
A1140	Install for Cold Water Pipe complete with joints, angles, reducer etc.	5	02-Mar-27	13-Mar-27	31-Oct-26	04-Nov-26	0%	4,044	4,044
A1150	Install for Hot Water Pipe complete with joints, angles, reducer etc.	4	14-Mar-27	17-Mar-27	05-Nov-26	09-Nov-26	0%	714	714
A1160	Install for Isolation Valve,Spray Head,Roof Drain,Floor Drain,Gully teap,Vend on Roof to exhaust air	3	18-Mar-27	21-Mar-27	10-Nov-26	12-Nov-26	0%	16,140	16,140
A1170	Install of Inspection chamber, size 800x900x1000	2	22-Mar-27	23-Mar-27	14-Nov-26	15-Nov-26	0%	10,800	10,800
A1180	Install OF Electric Water Heater set with connection and Water meter complete with accessories	2	17-Apr-27	18-Apr-27	09-Dec-26	10-Dec-26	0%	12,600	12,600
HVAC System		43	04-Mar-27	27-Apr-27	01-Nov-26	20-Dec-26	0%	29,280	29,280
A1200	Install of Refrigerant Piping (fabricated metal ducts with flanges complete with supports, vanes, dampers)	4	04-Mar-27	13-Mar-27	01-Nov-26	04-Nov-26	0%	7,560	7,560
A1190	Install of Mini split actual capacity 2 Ton and Ducted split actual capacity 4 Ton	7	17-Apr-27	24-Apr-27	09-Dec-26	16-Dec-26	0%	18,600	18,600
A1210	Install of Air Grills 150mm x150mm and Air Diffuser 600mm x 600mm	3	25-Apr-27	27-Apr-27	17-Dec-26	20-Dec-26	0%	3,120	3,120
Fire Fitting System		35	14-Mar-27	22-Apr-27	05-Nov-26	15-Dec-26	0%	58,800	58,800
A1220	Installation & Testing of 2 hours Fire rated system for closing the openings between rooms with help of Rock wool	6	14-Mar-27	20-Mar-27	05-Nov-26	11-Nov-26	0%	30,000	30,000
A1230	Install Fire Extinguishers	6	17-Apr-27	22-Apr-27	09-Dec-26	15-Dec-26	0%	28,800	28,800
Electrical Work		61	14-Mar-27	29-May-27	05-Nov-26	14-Jan-27	0%	1,440,268	1,440,268
LV Power		34	14-Mar-27	21-Apr-27	05-Nov-26	14-Dec-26	0%	67,800	67,800
A1250	Install of Distribution board For Gaurd Room	5	14-Mar-27	18-Mar-27	05-Nov-26	10-Nov-26	0%	11,904	11,904
A1270	Install of Earting Cable for Gaurd Room	5	20-Mar-27	24-Mar-27	11-Nov-26	16-Nov-26	0%	7,920	7,920
A1260	Install of Socket outlet and LED Lighting	5	17-Apr-27	21-Apr-27	09-Dec-26	14-Dec-26	0%	47,976	47,976
Fire Detection And Alarm System		44	21-Mar-27	10-May-27	12-Nov-26	02-Jan-27	0%	232,960	232,960
A1340	Install of 2C x 1.5 Sqm FR Rated Armored - Cable For Loop Wiring	5	21-Mar-27	25-Mar-27	12-Nov-26	17-Nov-26	0%	27,000	27,000
A1350	Install of Transmission Communication cable - Fiber Optics 12Core	5	27-Mar-27	31-Mar-27	18-Nov-26	23-Nov-26	0%	129,735	129,735
A1360	Install of power supply system for fire alarm control panel	5	17-Apr-27	21-Apr-27	09-Dec-26	14-Dec-26	0%	4,617	4,617
A1280	Install of Fire Alarm Control panel	6	22-Apr-27	28-Apr-27	15-Dec-26	21-Dec-26	0%	40,620	40,620

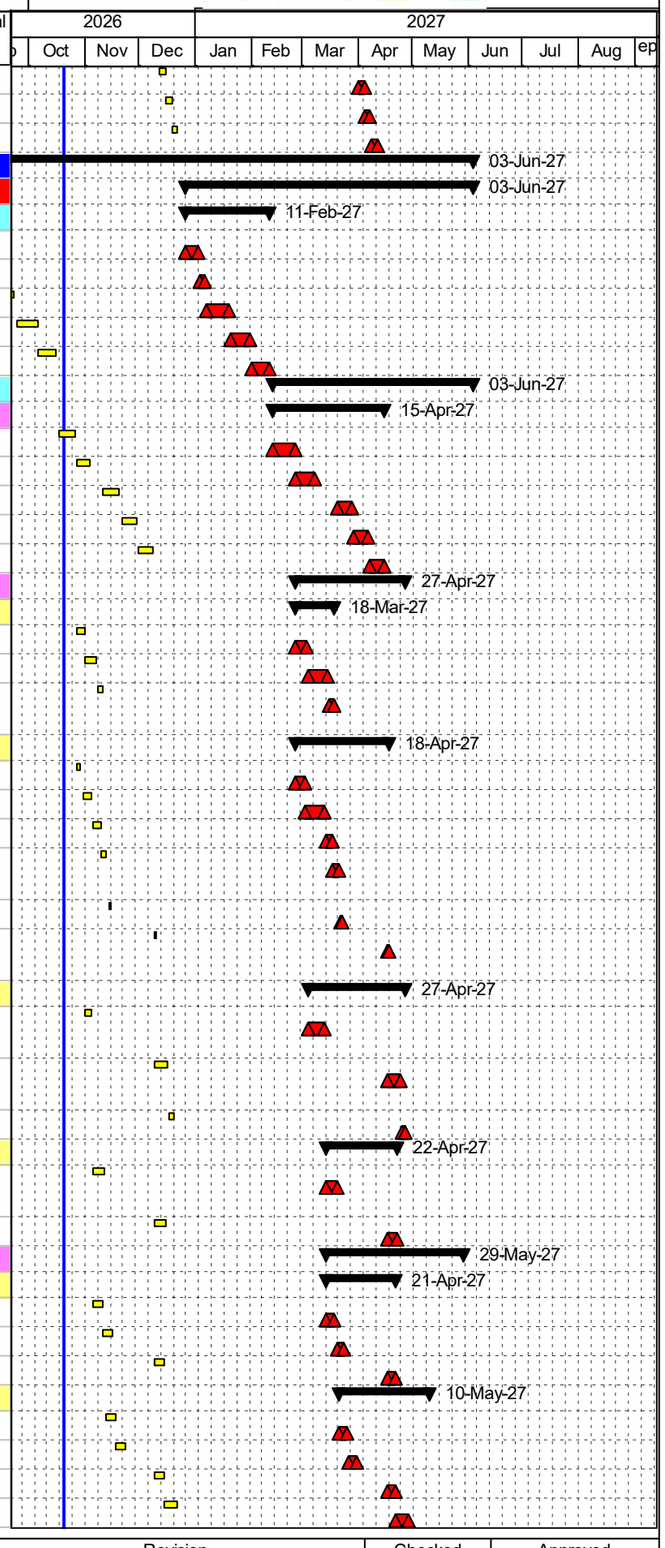


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
A1290	Installation of the addressable manual call point with operation safety glass breaking	3	29-Apr-27	02-May-27	22-Dec-26	24-Dec-26	0%	4,182	4,182
A1300	Install of the photoelectric heat & smoke detector	3	03-May-27	05-May-27	26-Dec-26	28-Dec-26	0%	14,760	14,760
A1310	Install of Sounder With Beacon	3	03-May-27	05-May-27	26-Dec-26	28-Dec-26	0%	4,920	4,920
A1320	Install of Addressable Control module	4	06-May-27	10-May-27	29-Dec-26	02-Jan-27	0%	7,126	7,126
Security System		30	19-Apr-27	29-May-27	12-Dec-26	14-Jan-27	0%	1,139,508	1,139,508
A1580	Install 8 Port Industrial PoE Switch 10/100BaseT (0 deg to +70 deg. Celsius)	5	19-Apr-27	24-Apr-27	12-Dec-26	16-Dec-26	0%	337,590	337,590
A1590	Optical Fiber,48 Core Splice Closure	3	25-Apr-27	27-Apr-27	17-Dec-26	20-Dec-26	0%	277,542	277,542
A1650	Pole/Bollard mounted IP(PoE) and 12U rack dimension	4	25-Apr-27	28-Apr-27	17-Dec-26	21-Dec-26	0%	114,735	114,735
A1600	Boom Barrier at Security Guard Room	5	29-Apr-27	04-May-27	22-Dec-26	27-Dec-26	0%	239,100	239,100
A1610	Pedestrian turnstile at Security Guard Room	5	05-May-27	10-May-27	28-Dec-26	02-Jan-27	0%	149,918	149,918
A1620	Access Control Unit and Access Card Reader	4	11-May-27	20-May-27	03-Jan-27	06-Jan-27	0%	14,268	14,268
A1630	Magnetic Lock and Break Glass and Exit Push button	4	22-May-27	25-May-27	07-Jan-27	11-Jan-27	0%	4,485	4,485
A1640	Door Sensor and Biometrics Reader	3	26-May-27	29-May-27	12-Jan-27	14-Jan-27	0%	1,870	1,870
Furnitures work		5	30-May-27	03-Jun-27	16-Jan-27	20-Jan-27	0%	21,600	21,600
A1100	Office Chairs,Tables and Stand	5	30-May-27	03-Jun-27	16-Jan-27	20-Jan-27	0%	21,600	21,600
Fence Work		224	02-Aug-26 A	09-May-27	11-Aug-26	23-Feb-27	27.99%	17,869,886	17,129,443
Northern Fence N01:N03		82	20-Oct-26	23-Jan-27	29-Aug-26	17-Jan-27	0%	2,415,262	2,415,262
Finishing Work		82	20-Oct-26	23-Jan-27	29-Aug-26	17-Jan-27	0%	2,415,262	2,415,262
Electrical Work		82	20-Oct-26	23-Jan-27	29-Aug-26	09-Dec-26	0%	165,946	165,946
CO-SU-FE-N-EL-1	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	20-Oct-26	28-Oct-26	29-Aug-26	06-Sep-26	0%	17,844	17,844
CO-SU-FE-N-EL-1	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	20-Oct-26	28-Oct-26	29-Aug-26	06-Sep-26	0%	8,182	8,182
CO-SU-FE-N-EL-1	Fixing of Control cable,CAT6A cable	9	29-Oct-26	08-Nov-26	07-Sep-26	16-Sep-26	0%	4,241	4,241
CO-SU-FE-N-EL-1	Install 800mm x 800mm x 800mm height concrete handhole	9	29-Oct-26	08-Nov-26	07-Sep-26	16-Sep-26	0%	4,436	4,436
CO-SU-FE-N-EL-14(	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	8	29-Oct-26	07-Nov-26	07-Sep-26	15-Sep-26	0%	5,767	5,767
CO-SU-FE-N-EL-1	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	8	09-Nov-26	17-Nov-26	17-Sep-26	27-Sep-26	0%	2,609	2,609
CO-SU-FE-N-EL-16(	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	8	18-Nov-26	26-Nov-26	28-Sep-26	06-Oct-26	0%	15,946	15,946
CO-SU-FE-N-EL-1	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	8	18-Nov-26	26-Nov-26	28-Sep-26	06-Oct-26	0%	0	0
CO-SU-FE-N-EL-1	Install of direct buried armored cable 4C-16mm2 ,10mm2	9	28-Nov-26	07-Dec-26	07-Oct-26	17-Oct-26	0%	11,145	11,145
CO-SU-FE-N-EL-1	Install 16mm2,10mm2 CU/PVC wire	9	28-Nov-26	07-Dec-26	07-Oct-26	17-Oct-26	0%	1,995	1,995
CO-SU-FE-N-EL-20(	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	8	28-Nov-26	06-Dec-26	07-Oct-26	15-Oct-26	0%	25,964	25,964
CO-SU-FE-N-EL-2	Junction Box for lighting fixture	8	08-Dec-26	16-Dec-26	18-Oct-26	26-Oct-26	0%	1,521	1,521
CO-SU-FE-N-EL-2	IR Intrusion Detection System Quad Beams	8	05-Jan-27	13-Jan-27	22-Nov-26	30-Nov-26	0%	57,469	57,469
CO-SU-FE-N-EL-2	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	9	05-Jan-27	14-Jan-27	22-Nov-26	01-Dec-26	0%	8,457	8,457
CO-SU-FE-N-EL-2	Install, fixings, testing and commissioning 80W LED	7	16-Jan-27	23-Jan-27	02-Dec-26	09-Dec-26	0%	371	371
Architictural work		37	08-Dec-26	19-Jan-27	18-Oct-26	17-Jan-27	0%	2,249,316	2,249,316
CO-SU-FE-N-AR-1	External plastering to walls and columns	7	08-Dec-26	15-Dec-26	18-Oct-26	25-Oct-26	0%	0	0
CO-SU-FE-N-AR-1	Install 50mm thick random cut stone cladding	7	16-Dec-26	23-Dec-26	26-Oct-26	02-Nov-26	0%	2,046,910	2,046,910
CO-SU-FE-N-AR-1	Install 2 coats of weatherproof paint at walls	6	24-Dec-26	30-Dec-26	03-Nov-26	09-Nov-26	0%	64,012	64,012
CO-SU-FE-N-AR-1	Install Stone coping 500mm,525mm	4	31-Dec-26	04-Jan-27	10-Nov-26	14-Nov-26	0%	74,030	74,030
CO-SU-FE-N-AR-1	Install MODON Signage	7	12-Jan-27	19-Jan-27	09-Jan-27	17-Jan-27	0%	64,364	64,364
Western Fence P1 (W01:W06)		124	17-Sep-26 A	23-Mar-27	12-Sep-26	26-Jan-27	38.91%	2,208,449	1,468,007
Civil Work		28	17-Sep-26 A	25-Oct-26	12-Sep-26	01-Nov-26	80%	757,244	192,922
CO-SU-FE-WP1-CI	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	24-Oct-26	12-Sep-26	01-Oct-26	80%	675,382	168,845
CO-SU-FE-WP1-CI	Pouring Beams For Northern Fence	17	05-Oct-26 A	25-Oct-26	12-Oct-26	01-Nov-26	80%	81,862	24,077
Finishing Work		116	29-Sep-26 A	23-Mar-27	01-Oct-26	26-Jan-27	17.48%	1,451,205	1,275,084
Electrical Work		116	29-Oct-26	23-Mar-27	12-Oct-26	20-Jan-27	0%	331,892	331,892
CO-SU-FE-WP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	14	29-Oct-26	14-Nov-26	12-Oct-26	28-Oct-26	0%	35,687	35,687
CO-SU-FE-WP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	14	29-Oct-26	14-Nov-26	12-Oct-26	28-Oct-26	0%	16,364	16,364

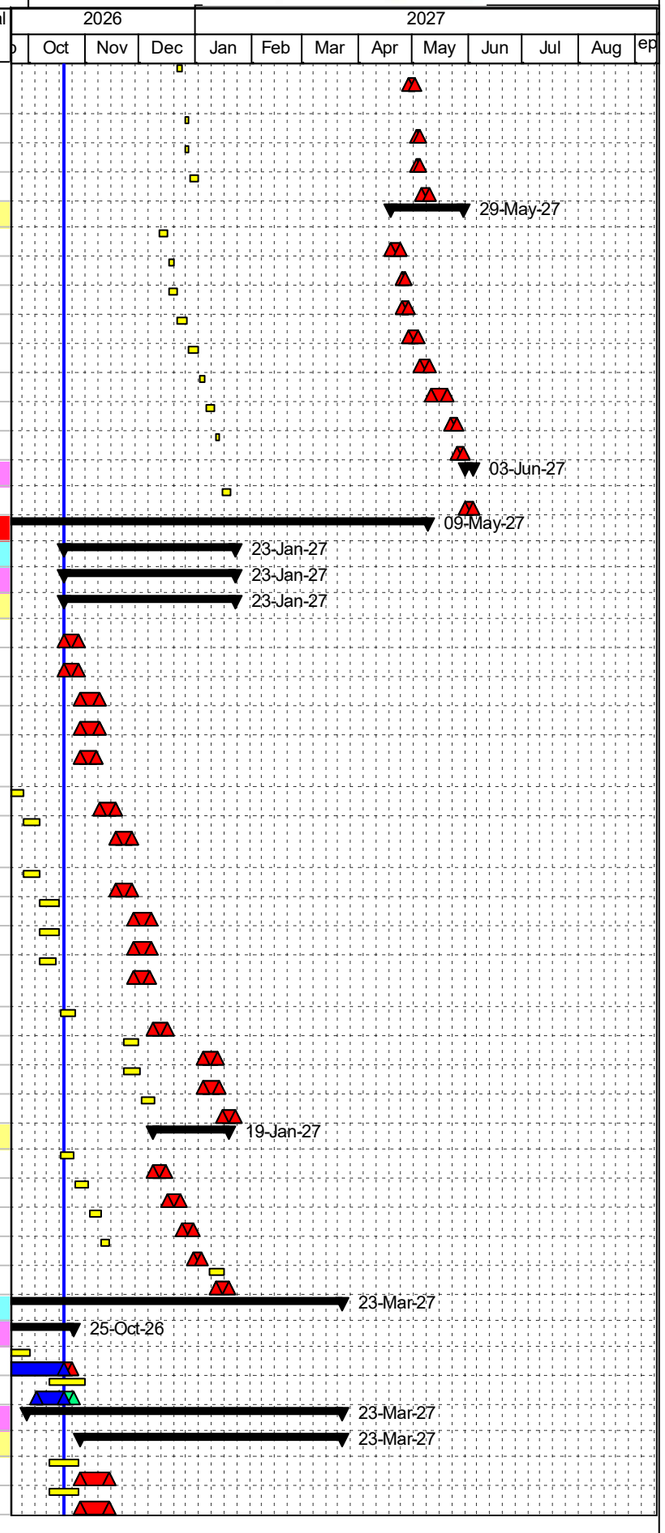

Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SU-FE-WP1-E	Fixing of Control cable,CAT6A cable	14	15-Nov-26	30-Nov-26	28-Oct-26	14-Nov-26	0%	8,482	8,482
CO-SU-FE-WP1-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	14	15-Nov-26	30-Nov-26	28-Oct-26	14-Nov-26	0%	11,535	11,535
CO-SU-FE-WP1-E	Install 800mm x 800mm x 800mm height concrete handhole	14	17-Dec-26	02-Jan-27	28-Oct-26	14-Nov-26	0%	8,871	8,871
CO-SU-FE-WP1-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	11	05-Jan-27	17-Jan-27	15-Nov-26	26-Nov-26	0%	5,218	5,218
CO-SU-FE-WP1-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	9	18-Jan-27	27-Jan-27	28-Nov-26	07-Dec-26	0%	31,892	31,892
CO-SU-FE-WP1-E	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	9	18-Jan-27	27-Jan-27	28-Nov-26	07-Dec-26	0%	0	0
CO-SU-FE-WP1-E	Install of direct buried armored cable 4C-16mm2 ,10mm2	8	28-Jan-27	06-Feb-27	08-Dec-26	16-Dec-26	0%	22,291	22,291
CO-SU-FE-WP1-E	Install 16mm2,10mm2 CU/PVC wire	8	28-Jan-27	06-Feb-27	08-Dec-26	16-Dec-26	0%	3,991	3,991
CO-SU-FE-WP1-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	9	28-Jan-27	07-Feb-27	08-Dec-26	17-Dec-26	0%	51,927	51,927
CO-SU-FE-WP1-E	Junction Box for lighting fixture	11	07-Feb-27	22-Feb-27	17-Dec-26	29-Dec-26	0%	3,041	3,041
CO-SU-FE-WP1-E	IR Intrusion Detection System Quad Beams	4	15-Mar-27	18-Mar-27	12-Jan-27	16-Jan-27	0%	114,938	114,938
CO-SU-FE-WP1-E	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	4	15-Mar-27	18-Mar-27	12-Jan-27	16-Jan-27	0%	16,913	16,913
CO-SU-FE-WP1-E	Install, fixings, testing and commissioning 80W LED	4	20-Mar-27	23-Mar-27	17-Jan-27	20-Jan-27	0%	741	741
Architictural work		103	29-Sep-26 A	23-Mar-27	01-Oct-26	26-Jan-27	22.66%	1,119,313	943,192
CO-SU-FE-WP1-A	Install Brick Work For Northern Fence	9	29-Sep-26 A	24-Oct-26	01-Oct-26	12-Oct-26	80%	317,018	140,897
CO-SU-FE-WP1-A	External plastering to walls and columns	6	08-Feb-27	16-Feb-27	19-Dec-26	24-Dec-26	0%	0	0
CO-SU-FE-WP1-A	Install 50mm thick random cut stone cladding	5	17-Feb-27	24-Feb-27	26-Dec-26	30-Dec-26	0%	397,485	397,485
CO-SU-FE-WP1-A	Install 2 coats of weatherproof paint at walls	6	24-Feb-27	06-Mar-27	31-Dec-26	06-Jan-27	0%	128,024	128,024
CO-SU-FE-WP1-A	Install Stone coping 500mm,525mm	4	06-Mar-27	14-Mar-27	07-Jan-27	11-Jan-27	0%	148,059	148,059
CO-SU-FE-WP1-A	Install MODON Signage	8	15-Mar-27	23-Mar-27	17-Jan-27	26-Jan-27	0%	128,727	128,727
Western Fence P2 (W07:W12)		135	19-Sep-26 A	04-Apr-27	07-Oct-26	04-Feb-27	24.86%	3,108,242	3,108,242
Civil Work		36	19-Sep-26 A	29-Oct-26	07-Oct-26	09-Nov-26	80%	649,037	649,037
CO-SU-FE-WP2-CI	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	29-Oct-26	07-Oct-26	18-Oct-26	80%	567,175	567,175
CO-SU-FE-WP2-CI	Pouring Beams For Northern Fence	7	11-Oct-26 A	29-Oct-26	01-Nov-26	09-Nov-26	80%	81,862	81,862
Finishing Work		125	29-Sep-26 A	04-Apr-27	18-Oct-26	04-Feb-27	10.31%	2,459,205	2,459,205
Electrical Work		125	31-Oct-26	04-Apr-27	27-Oct-26	01-Feb-27	0%	331,892	331,892
CO-SU-FE-WP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	31-Oct-26	03-Nov-26	27-Oct-26	01-Nov-26	0%	35,687	35,687
CO-SU-FE-WP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	31-Oct-26	05-Nov-26	27-Oct-26	03-Nov-26	0%	16,364	16,364
CO-SU-FE-WP2-E	Fixing of Control cable,CAT6A cable	7	07-Nov-26	14-Nov-26	03-Nov-26	11-Nov-26	0%	8,482	8,482
CO-SU-FE-WP2-E	Install 800mm x 800mm x 800mm height concrete handhole	7	07-Nov-26	14-Nov-26	03-Nov-26	10-Nov-26	0%	8,871	8,871
CO-SU-FE-WP2-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	6	07-Nov-26	12-Nov-26	03-Nov-26	10-Nov-26	0%	11,535	11,535
CO-SU-FE-WP2-E	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	15-Nov-26	21-Nov-26	11-Nov-26	18-Nov-26	0%	5,218	5,218
CO-SU-FE-WP2-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	22-Nov-26	25-Nov-26	18-Nov-26	23-Nov-26	0%	31,892	31,892
CO-SU-FE-WP2-E	Install of direct buried armored cable 4C-16mm2 ,10mm2	8	26-Nov-26	05-Dec-26	23-Nov-26	01-Dec-26	0%	22,291	22,291
CO-SU-FE-WP2-E	Install 16mm2,10mm2 CU/PVC wire	8	26-Nov-26	05-Dec-26	23-Nov-26	01-Dec-26	0%	3,991	3,991
CO-SU-FE-WP2-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	8	26-Nov-26	05-Dec-26	23-Nov-26	02-Dec-26	0%	51,927	51,927
CO-SU-FE-WP2-E	Junction Box for lighting fixture	3	05-Dec-26	08-Dec-26	01-Dec-26	05-Dec-26	0%	3,041	3,041
CO-SU-FE-WP2-E	IR Intrusion Detection System Quad Beams	7	20-Mar-27	27-Mar-27	17-Jan-27	24-Jan-27	0%	114,938	114,938
CO-SU-FE-WP2-E	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	7	20-Mar-27	27-Mar-27	17-Jan-27	24-Jan-27	0%	16,913	16,913
CO-SU-FE-WP2-E	Install, fixings, testing and commissioning 80W LED	7	28-Mar-27	04-Apr-27	25-Jan-27	01-Feb-27	0%	741	741
Architictural work		119	29-Sep-26 A	01-Apr-27	18-Oct-26	04-Feb-27	11.92%	2,127,313	2,127,313
CO-SU-FE-WP2-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	29-Oct-26	18-Oct-26	27-Oct-26	80%	317,018	317,018
CO-SU-FE-WP2-A	External plastering to walls and columns	8	06-Dec-26	14-Dec-26	02-Dec-26	12-Dec-26	0%	0	0
CO-SU-FE-WP2-A	Install 50mm thick random cut stone cladding	8	15-Dec-26	23-Dec-26	12-Dec-26	21-Dec-26	0%	1,405,485	1,405,485
CO-SU-FE-WP2-A	Install 2 coats of weatherproof paint at walls	8	24-Dec-26	02-Jan-27	21-Dec-26	30-Dec-26	0%	128,024	128,024
CO-SU-FE-WP2-A	Install Stone coping 500mm,525mm	8	03-Jan-27	11-Jan-27	30-Dec-26	09-Jan-27	0%	148,059	148,059

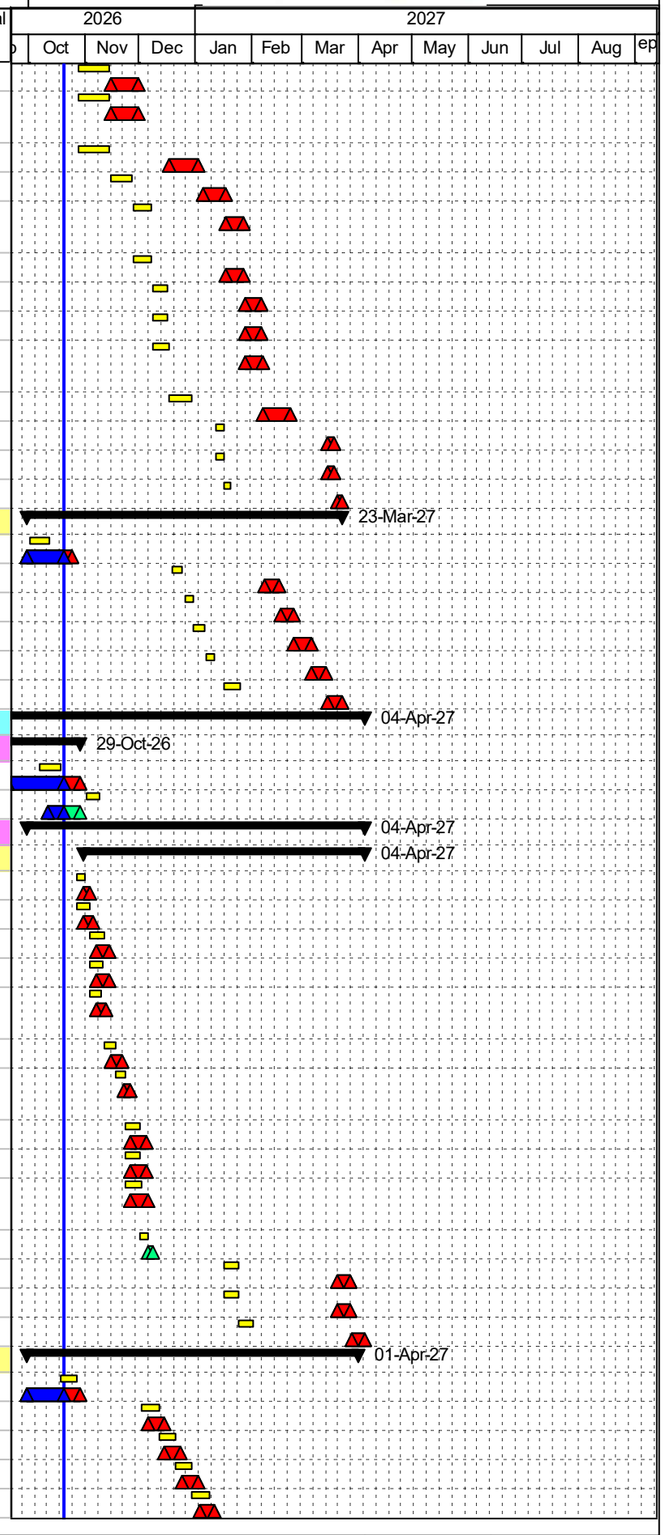


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work


Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SU-FE-WP2-A	Install MODON Signage	8	24-Mar-27	01-Apr-27	26-Jan-27	04-Feb-27	0%	128,727	128,727
Southern Fence S01:S05		202	02-Aug-26 A	12-Apr-27	11-Aug-26	15-Feb-27	32.71%	3,635,456	3,635,456
Civil Work		76	02-Aug-26 A	03-Nov-26	11-Aug-26	14-Sep-26	58.06%	1,866,175	1,866,175
CO-SU-FE-S-CI-26	Pouring for Plain Concrete Northern Fence	3	02-Aug-26 A	22-Oct-26	11-Aug-26	13-Aug-26	95%	89,091	89,091
CO-SU-FE-S-CI-27	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	28-Oct-26	15-Aug-26	23-Aug-26	85%	990,000	990,000
CO-SU-FE-S-CI-28	Pouring R.C Columns For Northern Fence	10	05-Oct-26 A	31-Oct-26	24-Aug-26	03-Sep-26	20%	718,865	718,865
CO-SU-FE-S-CI-29	Pouring Beams For Northern Fence	9	08-Oct-26 A	03-Nov-26	05-Sep-26	14-Sep-26	20%	68,218	68,218
Finishing Work		141	29-Sep-26 A	12-Apr-27	05-Sep-26	15-Feb-27	5.97%	1,769,282	1,769,282
Electrical Work		137	25-Oct-26	12-Apr-27	05-Sep-26	10-Feb-27	0%	276,577	276,577
CO-SU-FE-S-EL-5	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	25-Oct-26	10-Nov-26	05-Sep-26	21-Sep-26	0%	29,739	29,739
CO-SU-FE-S-EL-6	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	25-Oct-26	10-Nov-26	05-Sep-26	21-Sep-26	0%	13,636	13,636
CO-SU-FE-S-EL-6	Fixing of Control cable,CAT6A cable	15	11-Nov-26	28-Nov-26	22-Sep-26	10-Oct-26	0%	7,068	7,068
CO-SU-FE-S-EL-6	Install 800mm x 800mm x 800mm height concrete handhole	15	11-Nov-26	28-Nov-26	22-Sep-26	10-Oct-26	0%	7,393	7,393
CO-SU-FE-S-EL-63	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	15	11-Nov-26	28-Nov-26	22-Sep-26	10-Oct-26	0%	9,612	9,612
CO-SU-FE-S-EL-5	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	29-Nov-26	05-Dec-26	11-Oct-26	17-Oct-26	0%	4,348	4,348
CO-SU-FE-S-EL-64	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	01-Dec-26	05-Dec-26	13-Oct-26	17-Oct-26	0%	26,577	26,577
CO-SU-FE-S-EL-6	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	4	01-Dec-26	05-Dec-26	13-Oct-26	17-Oct-26	0%	0	0
CO-SU-FE-S-EL-6	Install of direct buried armored cable 4C-16mm2 ,10mm2	10	01-Dec-26	12-Dec-26	13-Oct-26	24-Oct-26	0%	18,576	18,576
CO-SU-FE-S-EL-6	Install 16mm2,10mm2 CU/PVC wire	6	06-Dec-26	12-Dec-26	18-Oct-26	24-Oct-26	0%	3,326	3,326
CO-SU-FE-S-EL-69	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	7	06-Dec-26	13-Dec-26	18-Oct-26	25-Oct-26	0%	43,273	43,273
CO-SU-FE-S-EL-5	Junction Box for lighting fixture	7	13-Dec-26	20-Dec-26	05-Dec-26	13-Dec-26	0%	2,535	2,535
CO-SU-FE-S-EL-5	IR Intrusion Detection System Quad Beams	7	07-Mar-27	18-Mar-27	09-Jan-27	16-Jan-27	0%	95,782	95,782
CO-SU-FE-S-EL-6	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	7	28-Mar-27	04-Apr-27	25-Jan-27	01-Feb-27	0%	14,095	14,095
CO-SU-FE-S-EL-5	Install, fixings, testing and commissioning 80W LED	7	05-Apr-27	12-Apr-27	02-Feb-27	10-Feb-27	0%	618	618
Architictural work		140	29-Sep-26 A	11-Apr-27	05-Sep-26	15-Feb-27	7.08%	1,492,705	1,492,705
CO-SU-FE-S-AR-2	Install Brick Work For Northern Fence	6	29-Sep-26 A	31-Oct-26	05-Sep-26	10-Sep-26	40%	264,182	264,182
CO-SU-FE-S-AR-2	External plastering to walls and columns	6	14-Dec-26	20-Dec-26	26-Oct-26	01-Nov-26	0%	0	0
CO-SU-FE-S-AR-3	Install 50mm thick random cut stone cladding	6	21-Dec-26	27-Dec-26	02-Nov-26	08-Nov-26	0%	891,181	891,181
CO-SU-FE-S-AR-3	Install 2 coats of weatherproof paint at walls	8	23-Feb-27	07-Mar-27	30-Dec-26	07-Jan-27	0%	106,686	106,686
CO-SU-FE-S-AR-3	Install Stone coping 500mm,525mm	10	07-Mar-27	22-Mar-27	09-Jan-27	19-Jan-27	0%	123,383	123,383
CO-SU-FE-S-AR-3	Install MODON Signage	8	03-Apr-27	11-Apr-27	04-Feb-27	15-Feb-27	0%	107,273	107,273
Eastern Fence P1 (E01:E06)		191	02-Aug-26 A	17-Apr-27	29-Aug-26	20-Feb-27	38.65%	3,514,791	3,514,791
Civil Work		68	02-Aug-26 A	05-Nov-26	29-Aug-26	26-Oct-26	64.97%	1,895,585	1,895,585
CO-SU-FE-EP1-CI-	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	28-Oct-26	29-Aug-26	06-Sep-26	95%	106,909	106,909
CO-SU-FE-EP1-CI-	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	02-Nov-26	07-Sep-26	20-Sep-26	85%	1,188,000	1,188,000
CO-SU-FE-EP1-CI-	Pouring R.C Columns For Northern Fence	15	06-Oct-26 A	05-Nov-26	21-Sep-26	08-Oct-26	20%	518,815	518,815
CO-SU-FE-EP1-CI-	Pouring Beams For Northern Fence	7	08-Oct-26 A	05-Nov-26	19-Oct-26	26-Oct-26	20%	81,862	81,862
Finishing Work		136	29-Sep-26 A	17-Apr-27	10-Oct-26	20-Feb-27	7.83%	1,619,205	1,619,205
Electrical Work		130	07-Nov-26	17-Apr-27	19-Oct-26	16-Feb-27	0%	331,892	331,892
CO-SU-FE-EP1-EI	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	19-Oct-26	22-Oct-26	0%	35,687	35,687
CO-SU-FE-EP1-EI	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	19-Oct-26	22-Oct-26	0%	16,364	16,364
CO-SU-FE-EP1-EI	Fixing of Control cable,CAT6A cable	4	11-Nov-26	15-Nov-26	24-Oct-26	27-Oct-26	0%	8,482	8,482
CO-SU-FE-EP1-EI	Install 800mm x 800mm x 800mm height concrete handhole	4	11-Nov-26	15-Nov-26	24-Oct-26	27-Oct-26	0%	8,871	8,871
CO-SU-FE-EP1-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	4	11-Nov-26	15-Nov-26	24-Oct-26	27-Oct-26	0%	11,535	11,535
CO-SU-FE-EP1-EI	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	6	16-Nov-26	22-Nov-26	28-Oct-26	03-Nov-26	0%	5,218	5,218
CO-SU-FE-EP1-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	23-Nov-26	26-Nov-26	04-Nov-26	08-Nov-26	0%	31,892	31,892
CO-SU-FE-EP1-EI	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	4	23-Nov-26	26-Nov-26	04-Nov-26	08-Nov-26	0%	0	0

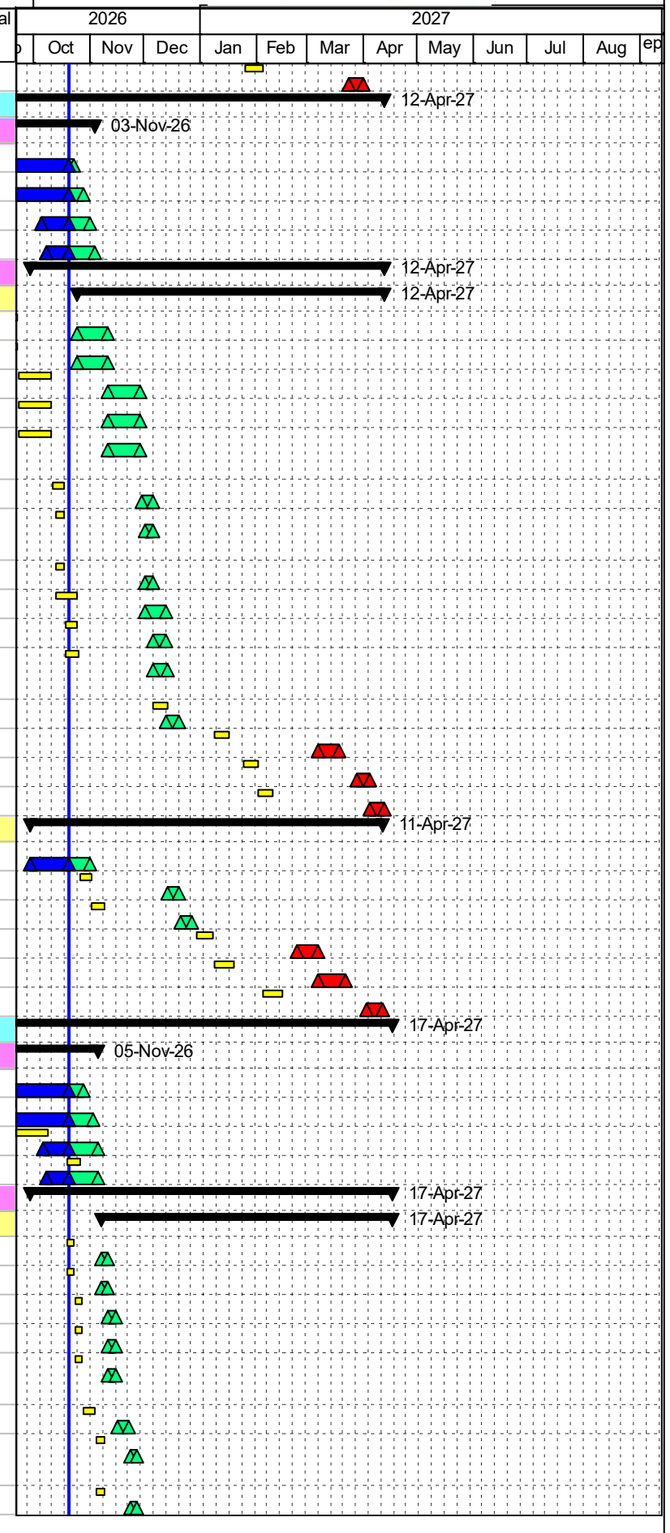

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
CO-SU-FE-EP1-EI	Install of direct buried armored cable 4C-16mm2 ,10mm2	4	28-Nov-26	01-Dec-26	09-Nov-26	12-Nov-26	0%	22,291	22,291
CO-SU-FE-EP1-EI	Install 16mm2,10mm2 CU/PVC wire	4	28-Nov-26	01-Dec-26	09-Nov-26	12-Nov-26	0%	3,991	3,991
CO-SU-FE-EP1-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	4	28-Nov-26	01-Dec-26	09-Nov-26	12-Nov-26	0%	51,927	51,927
CO-SU-FE-EP1-EI	Junction Box for lighting fixture	3	21-Dec-26	23-Dec-26	13-Dec-26	16-Dec-26	0%	3,041	3,041
CO-SU-FE-EP1-EI	IR Intrusion Detection System Quad Beams	4	20-Mar-27	23-Mar-27	17-Jan-27	20-Jan-27	0%	114,938	114,938
CO-SU-FE-EP1-EI	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	4	20-Mar-27	23-Mar-27	17-Jan-27	20-Jan-27	0%	16,913	16,913
CO-SU-FE-EP1-EI	Install, fixings, testing and commissioning 80W LED	4	13-Apr-27	17-Apr-27	10-Feb-27	16-Feb-27	0%	741	741
Architictural work		134	29-Sep-26 A	14-Apr-27	10-Oct-26	20-Feb-27	9.85%	1,287,313	1,287,313
CO-SU-FE-EP1-AI	Install Brick Work For Northern Fence	8	29-Sep-26 A	05-Nov-26	10-Oct-26	18-Oct-26	40%	317,018	317,018
CO-SU-FE-EP1-AI	External plastering to walls and columns	8	02-Dec-26	10-Dec-26	14-Nov-26	22-Nov-26	0%	0	0
CO-SU-FE-EP1-AI	Install 50mm thick random cut stone cladding	10	12-Dec-26	22-Dec-26	23-Nov-26	03-Dec-26	0%	565,485	565,485
CO-SU-FE-EP1-AI	Install 2 coats of weatherproof paint at walls	10	23-Dec-26	03-Jan-27	05-Dec-26	15-Dec-26	0%	128,024	128,024
CO-SU-FE-EP1-AI	Install Stone coping 500mm,525mm	10	04-Jan-27	14-Jan-27	16-Dec-26	27-Dec-26	0%	148,059	148,059
CO-SU-FE-EP1-AI	Install MODON Signage	3	12-Apr-27	14-Apr-27	15-Feb-27	20-Feb-27	0%	128,727	128,727
Eastern Fence P2 (E07:E13)		177	02-Aug-26 A	09-May-27	06-Oct-26	23-Feb-27	27.53%	2,987,685	2,987,685
Civil Work		61	02-Aug-26 A	11-Nov-26	06-Oct-26	02-Dec-26	57.05%	1,182,556	1,182,556
CO-SU-FE-EP2-CI-	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	07-Nov-26	06-Oct-26	19-Oct-26	95%	124,727	124,727
CO-SU-FE-EP2-CI-	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	07-Nov-26	20-Oct-26	02-Nov-26	85%	486,000	486,000
CO-SU-FE-EP2-CI-	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	07-Nov-26	03-Nov-26	14-Nov-26	30%	476,324	476,324
CO-SU-FE-EP2-CI-	Pouring Beams For Northern Fence	10	01-Oct-26 A	11-Nov-26	22-Nov-26	02-Dec-26	0.2%	95,505	95,505
Finishing Work		147	29-Sep-26 A	09-May-27	15-Nov-26	23-Feb-27	8.2%	1,805,129	1,805,129
Electrical Work		147	08-Nov-26	09-May-27	22-Nov-26	21-Feb-27	0%	387,208	387,208
CO-SU-FE-EP2-EI	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	08-Nov-26	11-Nov-26	22-Nov-26	25-Nov-26	0%	41,635	41,635
CO-SU-FE-EP2-EI	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	08-Nov-26	11-Nov-26	22-Nov-26	25-Nov-26	0%	19,091	19,091
CO-SU-FE-EP2-EI	Install 800mm x 800mm x 800mm height concrete handhole	3	12-Nov-26	15-Nov-26	26-Nov-26	29-Nov-26	0%	10,350	10,350
CO-SU-FE-EP2-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedded to wall	3	12-Nov-26	15-Nov-26	26-Nov-26	29-Nov-26	0%	13,457	13,457
CO-SU-FE-EP2-EI	Fixing of Control cable,CAT6A cable	3	24-Dec-26	27-Dec-26	16-Dec-26	20-Dec-26	0%	9,895	9,895
CO-SU-FE-EP2-EI	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	3	28-Dec-26	30-Dec-26	20-Dec-26	23-Dec-26	0%	6,087	6,087
CO-SU-FE-EP2-EL-	Field Equipment Cabinet enclosed outdoor complete with precast concrete footing,	4	31-Dec-26	04-Jan-27	23-Dec-26	28-Dec-26	0%	37,208	37,208
CO-SU-FE-EP2-EI	Fence Lightining 400V, 3PH, 60Hz lighting control panel (LCP-02)	4	31-Dec-26	04-Jan-27	23-Dec-26	28-Dec-26	0%	0	0
CO-SU-FE-EP2-EI	Install of direct buried armored cable 4C-16mm2 ,10mm2	3	05-Jan-27	07-Jan-27	28-Dec-26	31-Dec-26	0%	26,006	26,006
CO-SU-FE-EP2-EI	Install 16mm2,10mm2 CU/PVC wire	3	05-Jan-27	07-Jan-27	28-Dec-26	31-Dec-26	0%	4,656	4,656
CO-SU-FE-EP2-EL-	FEC-CCTV (4C-16mm2 CU/XLPE/PVC direct buried armored cable,16mm2 CU/PVC wire	6	05-Jan-27	11-Jan-27	28-Dec-26	04-Jan-27	0%	60,582	60,582
CO-SU-FE-EP2-EI	Junction Box for lighting fixture	3	09-Jan-27	11-Jan-27	31-Dec-26	04-Jan-27	0%	3,548	3,548
CO-SU-FE-EP2-EI	IR Intrusion Detection System Quad Beams	3	02-May-27	05-May-27	26-Jan-27	30-Jan-27	0%	134,095	134,095
CO-SU-FE-EP2-EI	Install of 38W, 230V, 1PH, 60Hz fence, led linear uplight lighting, IP66	3	02-May-27	05-May-27	26-Jan-27	30-Jan-27	0%	19,732	19,732
CO-SU-FE-EP2-EI	Install, fixings, testing and commissioning 80W LED	3	05-May-27	09-May-27	17-Feb-27	21-Feb-27	0%	865	865
Architictural work		120	29-Sep-26 A	04-May-27	15-Nov-26	23-Feb-27	10.43%	1,417,922	1,417,922
CO-SU-FE-EP2-AI	Install Brick Work For Northern Fence	6	29-Sep-26 A	07-Nov-26	15-Nov-26	21-Nov-26	40%	369,855	369,855
CO-SU-FE-EP2-AI	External plastering to walls and columns	5	12-Jan-27	17-Jan-27	04-Jan-27	10-Jan-27	0%	0	0
CO-SU-FE-EP2-AI	Install 50mm thick random cut stone cladding	5	18-Jan-27	23-Jan-27	10-Jan-27	16-Jan-27	0%	575,788	575,788
CO-SU-FE-EP2-AI	Install 2 coats of weatherproof paint at walls	5	24-Jan-27	28-Jan-27	16-Jan-27	21-Jan-27	0%	149,361	149,361
CO-SU-FE-EP2-AI	Install Stone coping 500mm,525mm	4	27-Apr-27	02-May-27	21-Jan-27	26-Jan-27	0%	172,736	172,736
CO-SU-FE-EP2-AI	Install MODON Signage	2	02-May-27	04-May-27	20-Feb-27	23-Feb-27	0%	150,182	150,182
Testing and Comissioning		186	20-Oct-26	09-Jun-27	04-Jan-27	21-Feb-27	0%	0	0
Infrastructure Networks		45	13-Apr-27	09-Jun-27	06-Jan-27	21-Feb-27	0%	0	0
Irrigation Network		5	20-May-27	26-May-27	28-Jan-27	03-Feb-27	0%	0	0

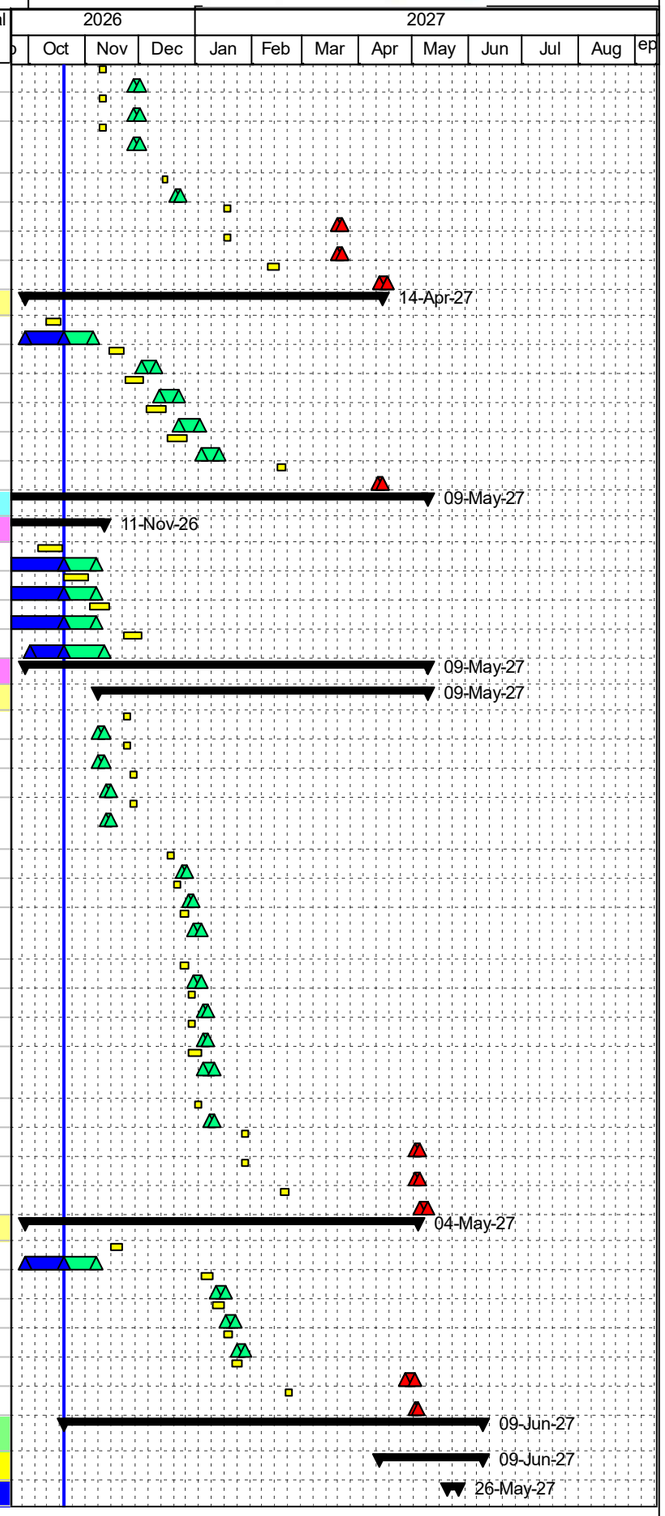


Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
Remaining work

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Performance % Complete	Budgeted Total Cost	Remaining Total Cost
T/C-IR	Testing and Commissioning of Irrigation Network	5	20-May-27	26-May-27	28-Jan-27	03-Feb-27	0%	0	0
TSE Network		15	03-May-27	26-May-27	17-Jan-27	03-Feb-27	0%	0	0
T/C-TSE-10	Testing and Commissioning of TSE Network	15	03-May-27	26-May-27	17-Jan-27	03-Feb-27	0%	0	0
Potable Water Network		6	20-May-27	27-May-27	28-Jan-27	04-Feb-27	0%	0	0
T/C-PW	Testing and Commissioning of Potable Water Network	6	20-May-27	27-May-27	28-Jan-27	04-Feb-27	0%	0	0
Sewage Network		3	27-Apr-27	01-May-27	17-Jan-27	19-Jan-27	0%	0	0
T/C-SW	Testing and Commissioning of Sewage Network	3	27-Apr-27	01-May-27	17-Jan-27	19-Jan-27	0%	0	0
Storm Drainage Network		9	13-Apr-27	22-Apr-27	06-Jan-27	16-Jan-27	0%	0	0
T/C-SD	Testing and Commissioning of Storm Drainage Network	9	13-Apr-27	22-Apr-27	06-Jan-27	16-Jan-27	0%	0	0
Street Lighting Network		6	26-May-27	02-Jun-27	04-Feb-27	11-Feb-27	0%	0	0
T/C-SL	Testing and Commissioning of Street Lighting Network	6	26-May-27	02-Jun-27	04-Feb-27	11-Feb-27	0%	0	0
Telecom Network		3	08-May-27	10-May-27	21-Jan-27	24-Jan-27	0%	0	0
T/C-TE	Testing and Commissioning of Telecom Network	3	08-May-27	10-May-27	21-Jan-27	24-Jan-27	0%	0	0
Medium Voltage Network		14	08-May-27	29-May-27	21-Jan-27	06-Feb-27	0%	0	0
T/C-MV	Testing and Commissioning of Medium Voltage Network	14	08-May-27	29-May-27	21-Jan-27	06-Feb-27	0%	0	0
Road Works		4	05-Jun-27	09-Jun-27	15-Feb-27	21-Feb-27	0%	0	0
T/C-RD	Testing and Commissioning of Road Works	4	05-Jun-27	09-Jun-27	15-Feb-27	21-Feb-27	0%	0	0
Utility Buildings		181	20-Oct-26	05-Jun-27	04-Jan-27	03-Feb-27	0%	0	0
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	20-Oct-26	20-Oct-26	04-Jan-27	04-Jan-27	0%	0	0
T/C-SPS	Testing and Commissioning of Sewage Pump Stations& soft scape and planting work	0	26-May-27	26-May-27	03-Feb-27	03-Feb-27	0%	0	0
T/C-CTV	Testing and Commissioning of Guard Room and Fence	0	05-Jun-27	05-Jun-27	23-Jan-27	23-Jan-27	0%	0	0
Handing over and close out		189	20-Oct-26	13-Jun-27	04-Jan-27	24-Feb-27	0%	0	0
As-Built		189	20-Oct-26	13-Jun-27	04-Jan-27	24-Feb-27	0%	0	0
HO-130	Submission As-Built Drawing For Pond	14	20-Oct-26	04-Nov-26	04-Jan-27	19-Jan-27	0%	0	0
HO-100	Submission As-Built Drawing For Sewage Network	14	01-May-27	23-May-27	20-Jan-27	04-Feb-27	0%	0	0
HO-160	Submission As-Built Drawing For Telecom Network	12	11-May-27	30-May-27	25-Jan-27	07-Feb-27	0%	0	0
HO-180	Submission As-Built Drawing For Irrigation Network	12	26-May-27	09-Jun-27	03-Feb-27	21-Feb-27	0%	0	0
HO-210	Submission As-Built Drawing For Pump station	1	26-May-27	27-May-27	03-Feb-27	04-Feb-27	0%	0	0
HO-190	As-Built Drawing For Potable Water Network	12	27-May-27	10-Jun-27	04-Feb-27	22-Feb-27	0%	0	0
HO-170	Submission As-Built Drawing For Medium Voltage Network	12	30-May-27	12-Jun-27	07-Feb-27	24-Feb-27	0%	0	0
HO-150	Submission As-Built Drawing For Street Lighting Network	7	02-Jun-27	10-Jun-27	13-Feb-27	22-Feb-27	0%	0	0
HO-140	Submission As-Built Drawing For Roads Network	3	09-Jun-27	13-Jun-27	21-Feb-27	24-Feb-27	0%	0	0
De-Mobilization Works		5	05-Jun-27	10-Jun-27	15-Feb-27	22-Feb-27	0%	0	0
HO-230	Remove Temporary Car Shades	5	05-Jun-27	10-Jun-27	15-Feb-27	22-Feb-27	0%	0	0
Handing Over		3	09-Jun-27	13-Jun-27	21-Feb-27	24-Feb-27	0%	0	0
HO-250	Review B.O.Q Qty. to ensure compliance with the actual status	3	09-Jun-27	13-Jun-27	21-Feb-27	24-Feb-27	0%	0	0

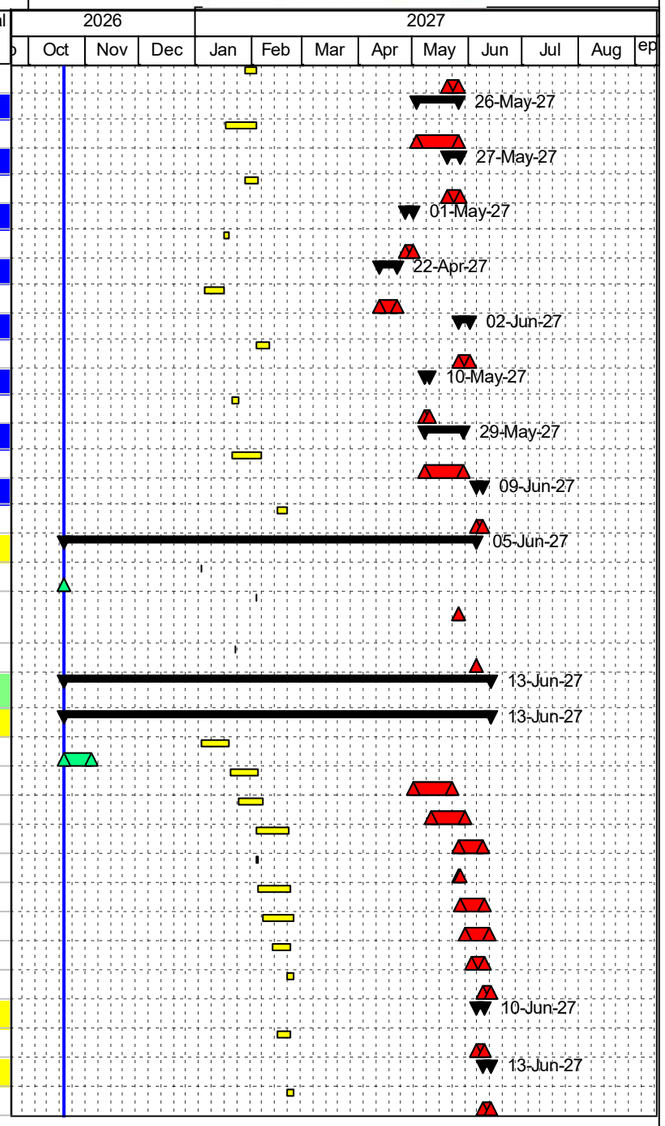

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		
