Infrastructure Development for Industrial City 1 in Jeddah

تطوير البنية التحتية بالمدينة الصناعية الأولى بجدة (1كم2)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al Enjaz Company for Trading and Contracting	EGIS	Eng. Abdallah Aljulayfi	19-Nov-2025	18-Nov-2027

Scope: road works, storm, sewer, potable water and TSE networks, electrical works, fence and gates, a bridge and landscaping. Contract value 86.8M SAR, 24 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 75.2% against a plan of 49.1%, the project is 26.1% ahead (SPI 1.53). This week it gained 1.77% against 1.10% planned, more than twice last week's 0.77%. Yet the schedule now forecasts completion 198 days after the contract date, another week later than last week.

PHYSICAL % COMPLETE

75.2% / 49.1% plan

▲ SPI 1.53 +26.1%

PROGRESS THIS WEEK

+1.77 % / +1.10% plan

▲ 0.67% above the weekly plan

CONTRACT TIME ELAPSED

47.9% · day 349 of 729

▼ Forecast finish 03-Jun-2028

INVOICED TO DATE (GROSS)

56.5% · 49.1M SAR

8 invoices, last period ends 29-Oct-2026

Well ahead on progress, but the forecast finish is six months late.

Both the weekly report and the P6 update forecast completion on 03-Jun-2028, 198 days after the contract completion date of 18-Nov-2027, with −169 days of total float (−163 last week). Every open milestone slipped another 7 days this week, the third weekly slip in a row. Roads and medium voltage, the WBS that is behind plan (73.5% against 100%, unchanged for three weeks), depends on the MV network, which is waiting for the MODON–SEC agreement; MV cable, ring main units and lighting substations have not been ordered.

Site photos this week

Six photos from the Weekly Photos sheet of the 03-Nov-2026 weekly report, camera-stamped 29 Oct to 2 Nov 2026 where the stamp is visible. Asphalt wearing course, telecom ducts, irrigation pipes, curbs and signboard foundations are in progress. Select a photo to view it larger, then use the arrows to move between photos.




Telecom pipes, local road L01

Ducts laid along the trench. Stamped 02-Nov-2026, 06:49.



Asphalt wearing course

Tipper trucks feeding the paver. No date stamp.

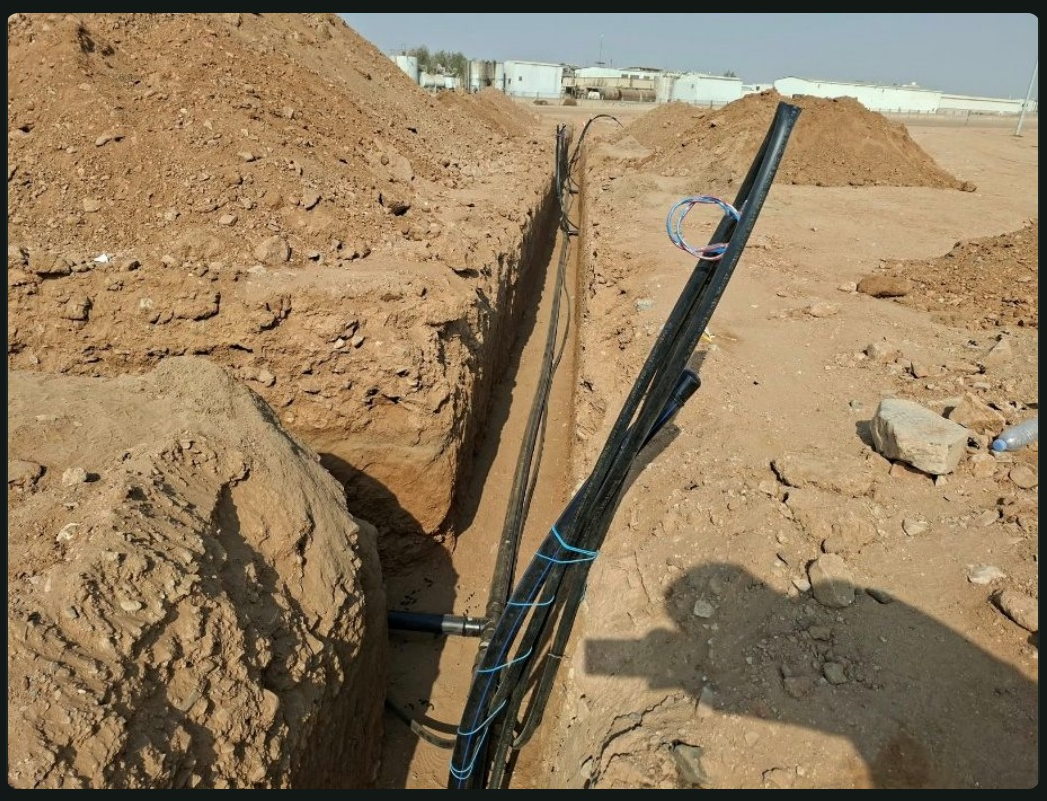

Irrigation pipes

Irrigation pipes laid in the trench for landscaping. No date stamp.




Asphalt wearing course works

Paver and crew on the wearing course. Stamped 02-Nov-2026, 07:45.



Curbstone works

Curb machine and crew along the road edge. Stamped 29-Oct-2026, 07:25.

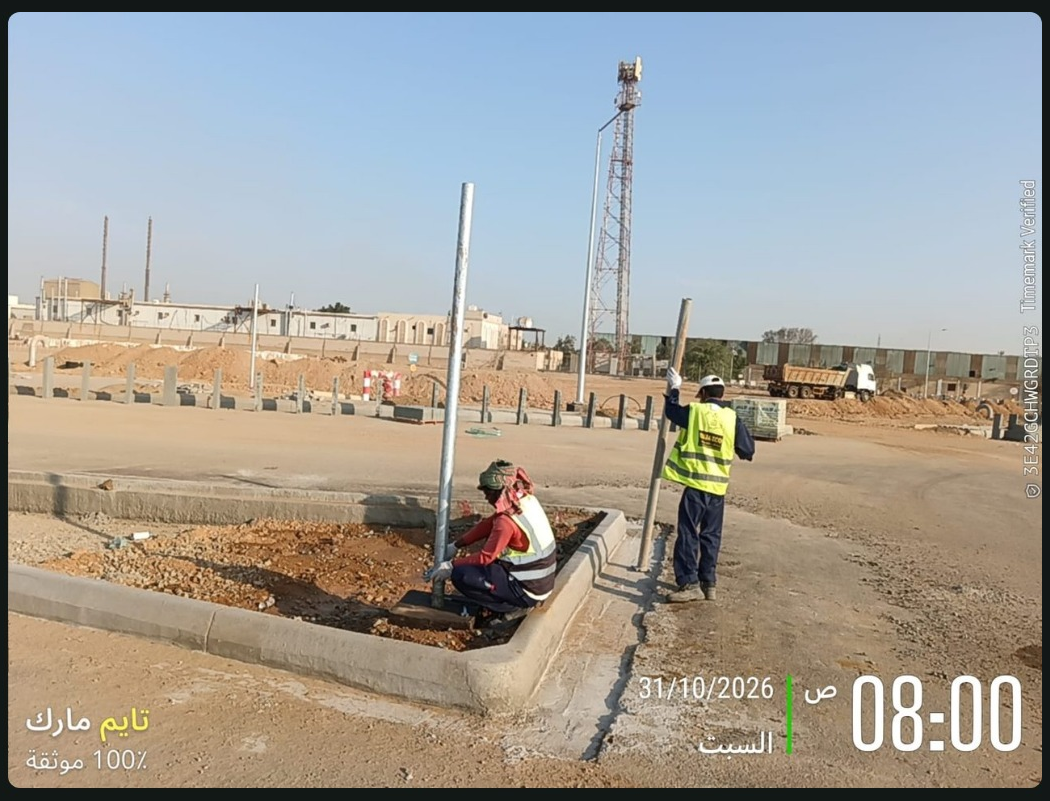


Signboard foundations

Sign post set in its foundation. Stamped 31-Oct-2026, 08:00.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet. The revised plan in the sheet is identical to the baseline, so only the baseline is drawn.

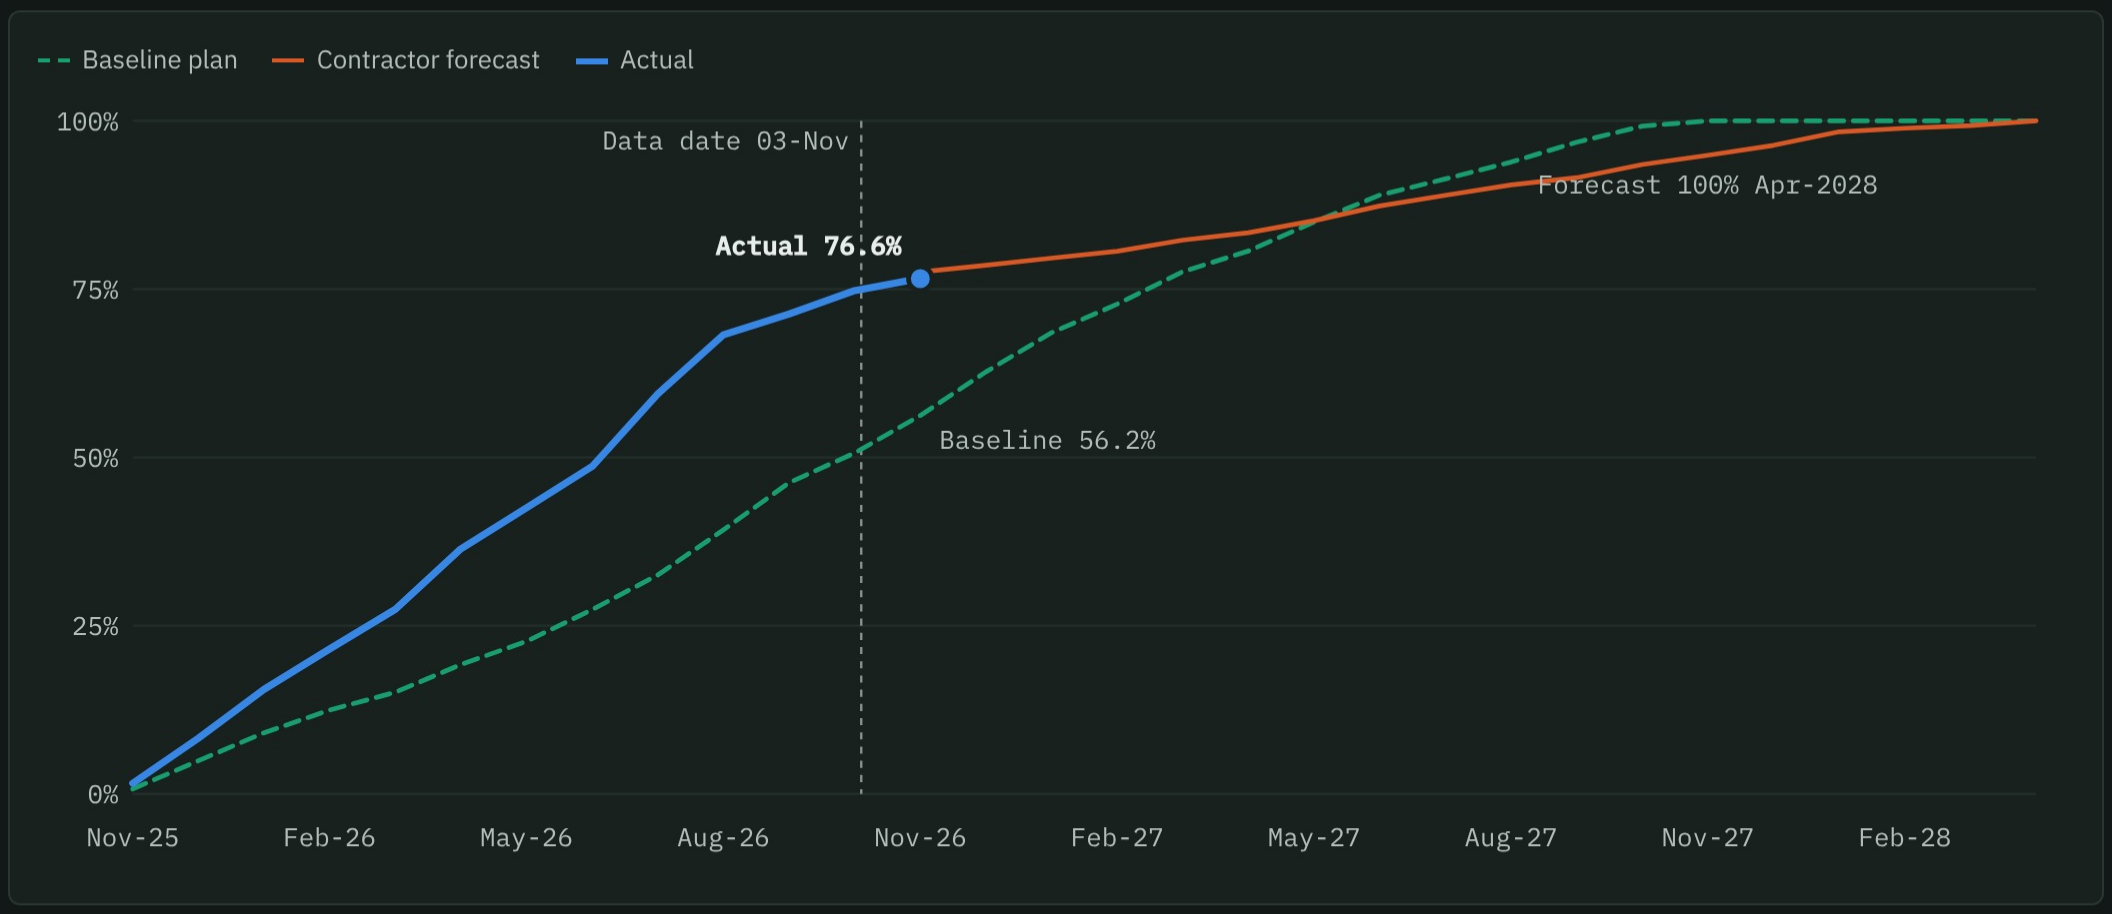

WEEK	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
20-Oct-2026	46.99	72.61	+25.63	–	1.55
27-Oct-2026	47.99	73.38	+25.40	+0.77	1.53
03-Nov-2026	**49.08**	**75.16**	**+26.07**	**+1.77**	**1.53**

Rows for 27 Oct and 3 Nov come from the weekly reports of those dates; the first row is the "last week" column of the 27-Oct report, whose gain is not stated there. The chart's latest actual (76.6%) comes from the P6 export and is higher than the 75.2% on the report dashboard; see Data notes.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Construction sub-phases are listed under Construction.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilization	2.8%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.7%	100.0%	98.8%	−1.2%	0.99	▼ Slightly behind
Procurement	11.5%	43.5%	78.9%	+35.4%	1.81	▲ Ahead
Construction	76.3%	47.9%	74.9%	+26.9%	1.56	▲ Ahead
· Site demolition	1.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Roads & medium voltage	14.0%	100.0%	73.5%	−26.5%	0.73	▼ Behind
· Deep infrastructure network	7.6%	100.0%	95.9%	−4.1%	0.96	▼ Slightly behind
· Shallow infrastructure network	27.8%	28.1%	80.5%	+52.4%	2.87	▲ Ahead
· Bridge	2.0%	57.7%	87.1%	+29.4%	1.51	▲ Ahead
· Outside boundary area (tie-in lines)	2.8%	55.4%	99.7%	+44.3%	1.80	▲ Ahead
· Roads finishing	9.2%	0.0%	78.7%	+78.7%	–	▲ Ahead
· Fence and gate	6.1%	57.1%	58.2%	+1.1%	1.02	▲ On track
· Roundabout & landscape	5.8%	0.0%	15.1%	+15.1%	–	▲ Ahead
Testing & commissioning	2.8%	0.0%	53.1%	+53.1%	–	▲ Ahead
Project close-out	1.9%	0.0%	0.0%	0.0%	–	● Not yet due
Total	100%	**49.1%**	**75.2%**	**+26.1%**	**1.53**	▲ Ahead

The schedule statistics for the P6 update (data date 03-Nov-2026) list 1,905 activities: 1,339 completed, 187 in progress and 379 not started. Of the 187 active activities, 71 are ahead and 116 behind. Critical-path activities fell from 448 to 432, while failed starts rose from 105 to 116. Landscape work started this week, ahead of its planned start.

Scope of work: quantities

Total, finished and remaining quantity for the major BOQ items, from the Major Quantities sheet of the 03-Nov-2026 weekly report. "This week" is the change from the 27-Oct-2026 report. The report gives no zone split and no backfilled quantity.

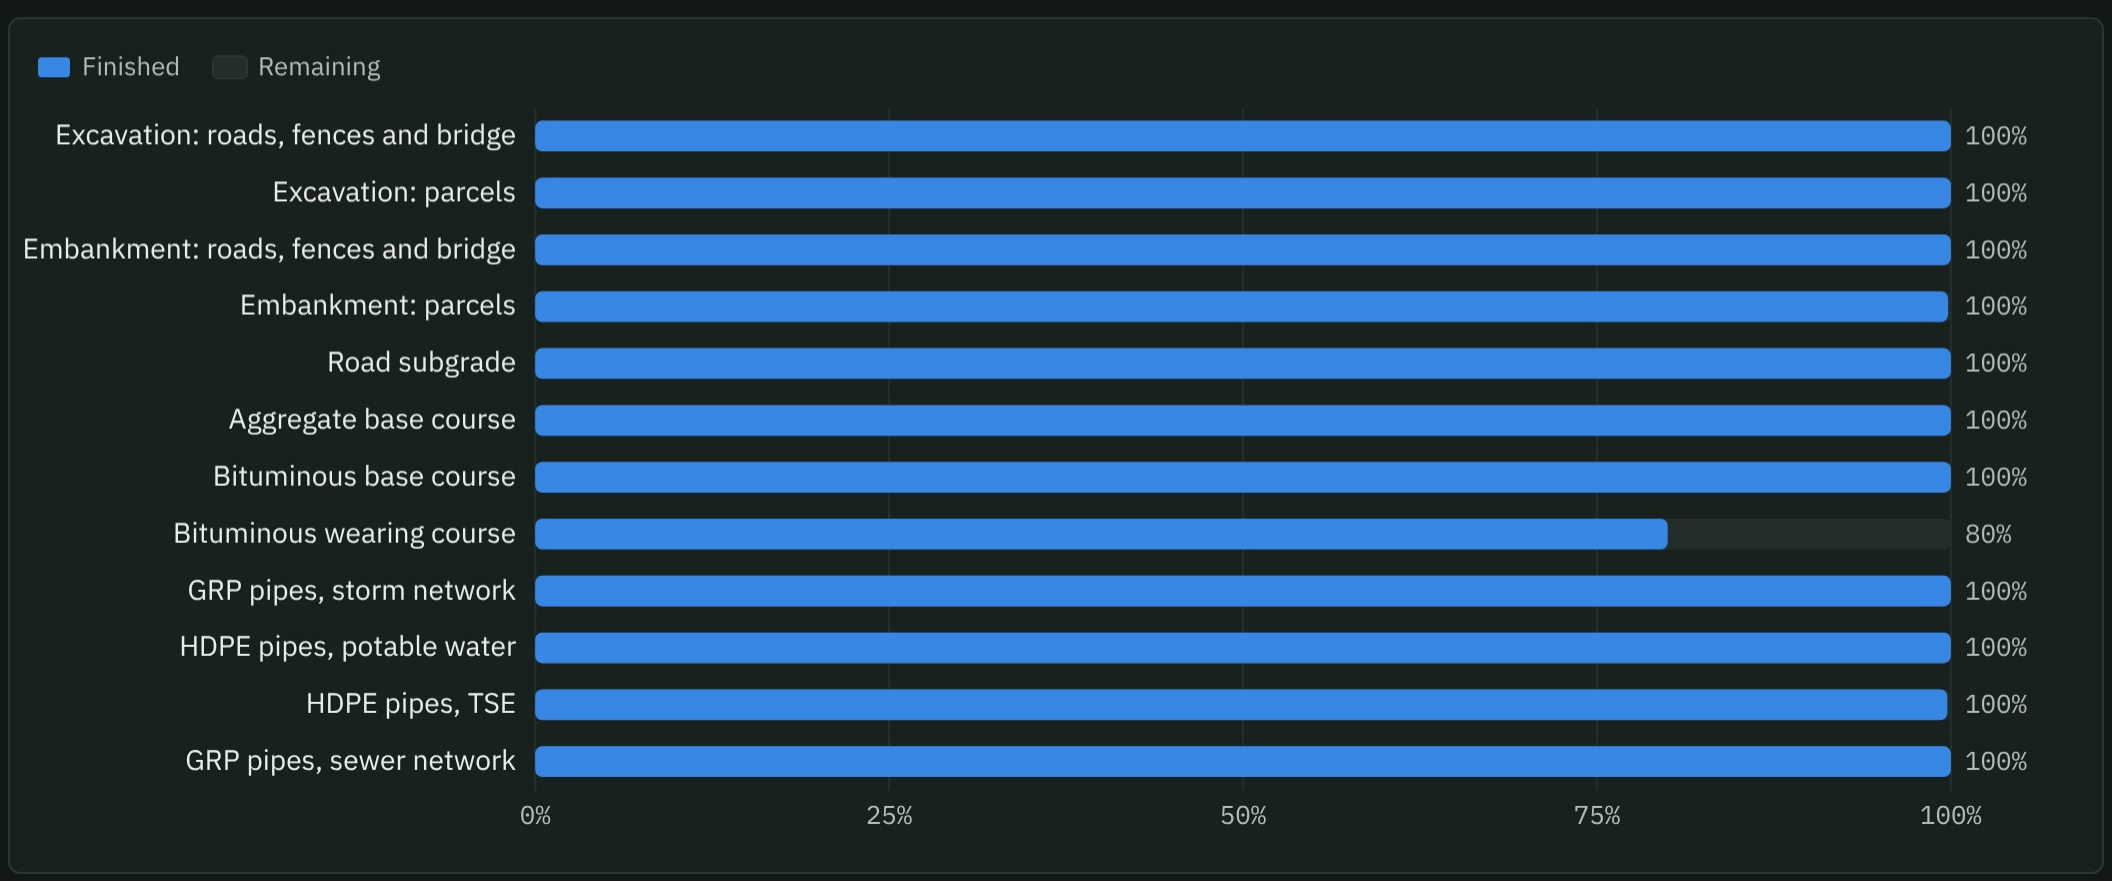

SCOPE ITEM	ZONE	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	BACKFILLED
Excavation: roads, fences and bridge	All	m³	116,177	116,177	0	0	100.0%	–
Excavation: parcels	All	m³	123,555	123,555	0	0	100.0%	–
Embankment: roads, fences and bridge	All	m³	80,920	80,920	0	0	100.0%	–
Embankment: parcels	All	m³	94,645	94,456	0	189.3	99.8%	–
Road subgrade	All	m³	34,694	34,694	0	0	100.0%	–
Aggregate base course	All	m³	23,129	23,129	0	0	100.0%	–
Bituminous base course	All	m³	8,290	8,290	0	0	100.0%	–
Bituminous wearing course	All	m³	5,920	4,736	+710.4	1,184	80.0%	–
GRP pipes, storm network	All	LM	5,650	5,650	0	0	100.0%	–
HDPE pipes, potable water	All	LM	12,075	12,075	0	0.3	100.0%	–
HDPE pipes, TSE	All	LM	8,722	8,700	0	22	99.7%	–
GRP pipes, sewer network	All	LM	6,244	6,244	0	0	100.0%	–

Asphalt wearing course is the only item that moved

710.4 m³ was laid this week, bringing it to 4,736 of 5,920 m³ (80.0%). All other earthworks, base course and pipe items are unchanged and complete or within 0.3% of their totals.

Milestones

Baseline dates and forecasts from the Milestones sheet of the weekly report, and forecasts and total float from the P6 export in the same workbook.


MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	19-Nov-2025	19-Nov-2025	19-Nov-2025 (actual)	–	✓ Done
Baseline time schedule	18-Dec-2025	18-Dec-2025	18-Dec-2025 (actual)	–	✓ Done
Finish mobilization	18-Dec-2025	04-Mar-2026	04-Mar-2026 (actual)	–	✓ Done late
Shop drawings, method statements and materials approved	19-Jan-2026	21-Nov-2026	21-Nov-2026	−67	▼ Late
All purchase orders issued	19-Jan-2026	15-Nov-2026	15-Nov-2026	−61	▼ Late
Roads & medium voltage complete	17-Sep-2026	01-Feb-2027	03-Jul-2027	−104	▼ Late
Deep infrastructure network complete	18-Nov-2026	03-Jul-2027	01-Feb-2027	42	? Conflicts with P6
Shallow infrastructure network complete	18-Mar-2027	17-Oct-2027	17-Oct-2027	−46	▼ Late
Completion of all works	18-Nov-2027	03-Jun-2028	03-Jun-2028	−169	▼ Late

The two sources swap the dates of two milestones.

The weekly report forecasts roads and medium voltage on 01-Feb-2027 and the deep network on 03-Jul-2027; the P6 export gives the same two dates the other way round. All other forecasts agree. Every open forecast moved 7 days later than in the 27-Oct report, so the approvals and purchase-order milestones (14-Nov and 08-Nov last week) are now due on 21-Nov and 15-Nov-2026.

Procurement of key materials

Share of the revised BOQ quantity delivered to site. Source: Material Monitoring sheet, weekly report 03-Nov-2026.

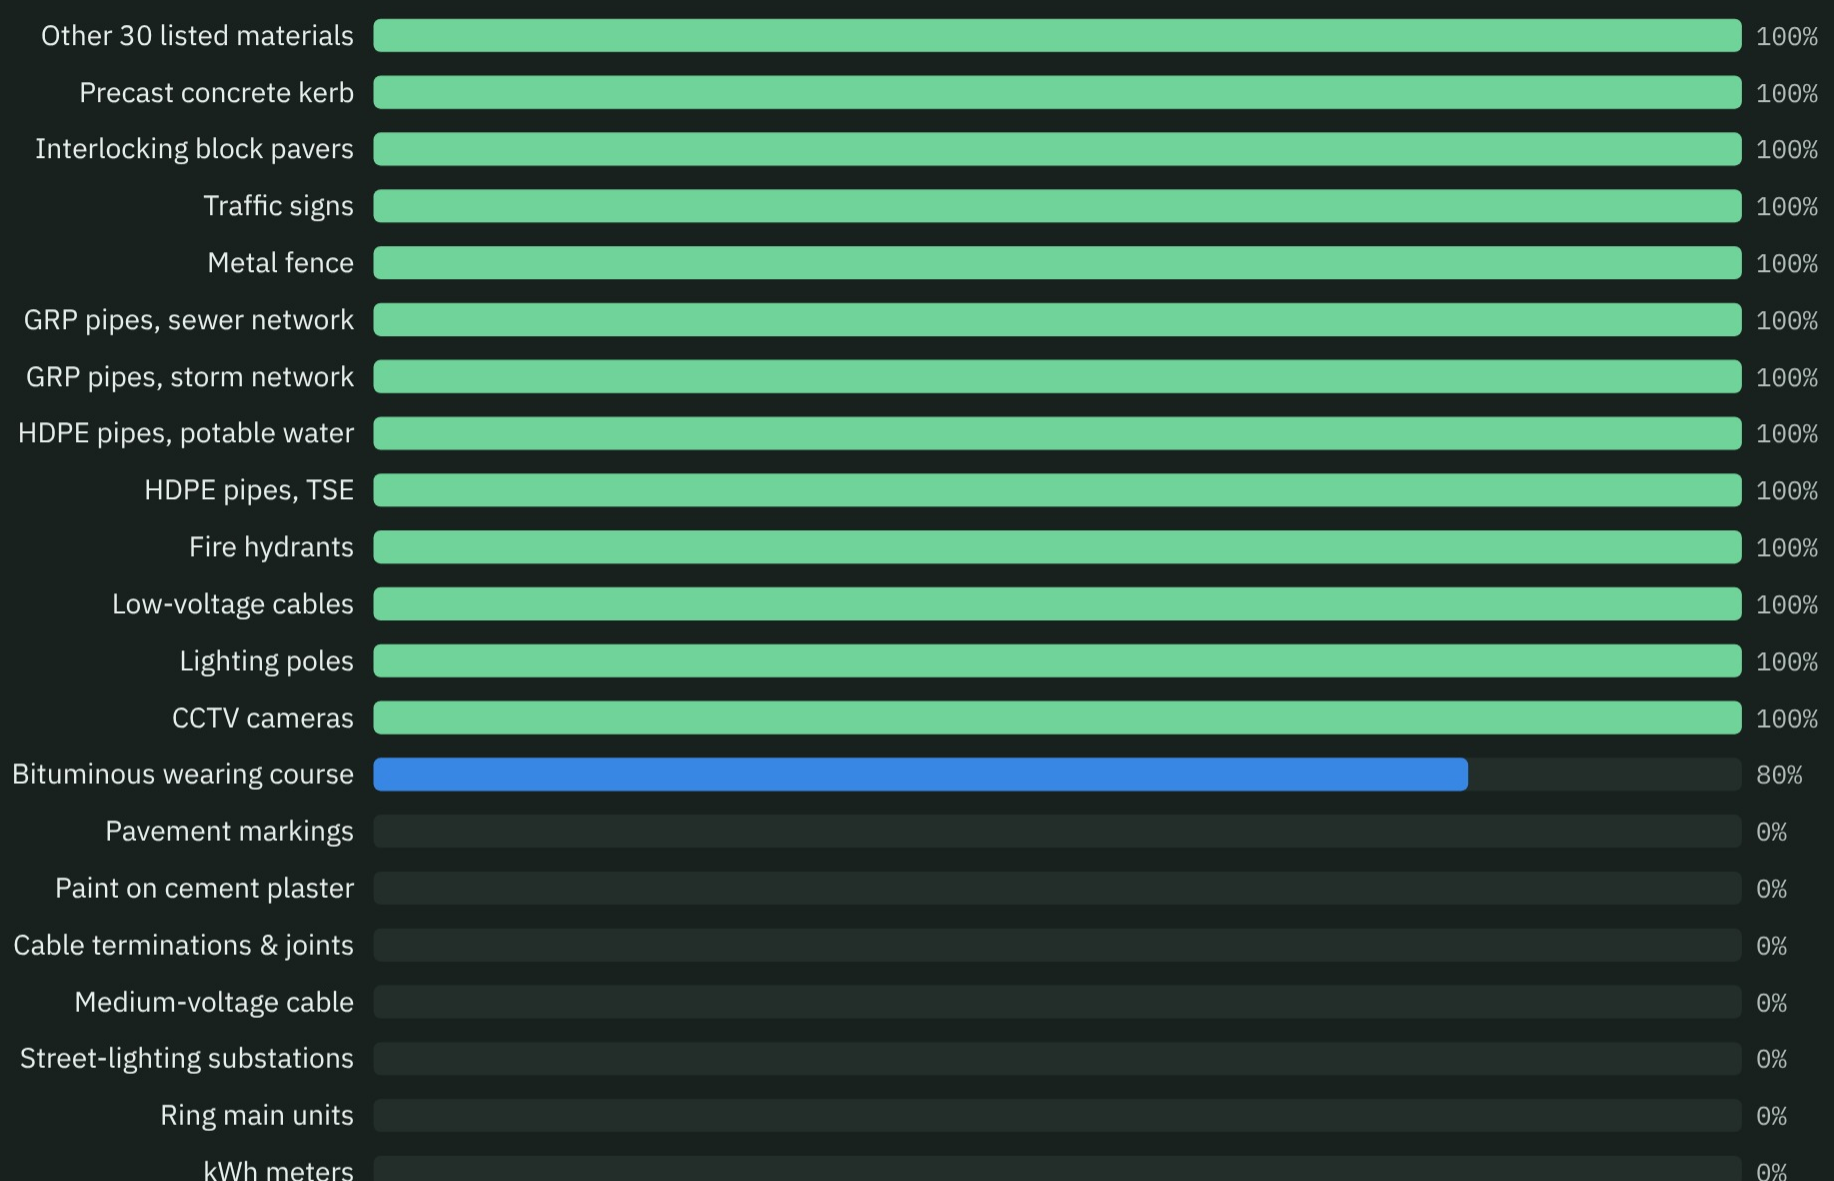

Medium-voltage materials: nothing ordered


MV cable (14,500 m), ring main units (4), street-lighting substations (4), kWh meters (4) and cable terminations (64) are not delivered. The Procurement Log shows the MV cable and substation orders on hold until the MODON–SEC electricity agreement is completed, with delivery now expected 30-Nov-2026.

Road finishing items

Asphalt wearing course 4,736 of 5,920 m³ delivered (80%, up from 68%). Pavement markings (3,780 m²) and paint on cement plaster (4,062 m²) not yet delivered. Overall, 108 of 113 purchase orders are issued and 105 of 113 materials are on site.

Manpower

Monthly manual (direct) head count on site, planned vs actual. Source: Manpower sheet.

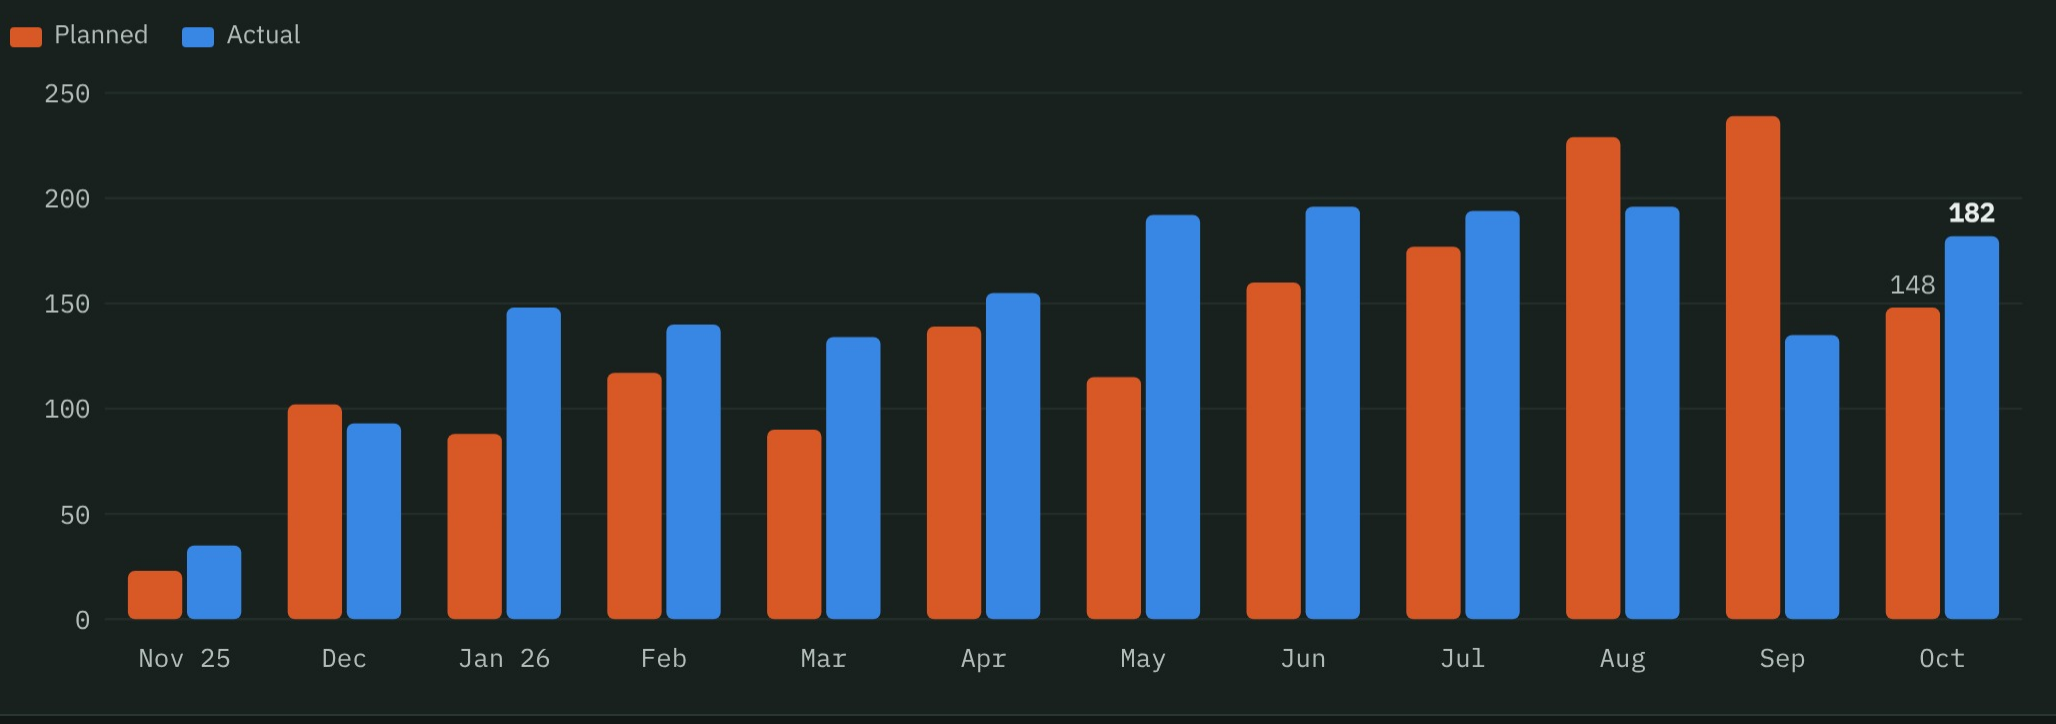

October manual head count is 182 against 148 planned (+23%); November is not yet reported. Non-manual staff are 48 against 22 planned. Equipment on site is 75 against 60 planned. The plan rises to 187 manual workers in November.

Cost and invoicing

Contract value

Original contract value	86,782,345
Revised contract value	86,782,345
Estimate at completion	86,782,345
Change orders	0

All values in SAR. No change orders are registered (CCO sheet).

Invoices

Invoices submitted	8
Gross value	49,066,274
Approved by PM (7, incl. VAT)	51,579,627
Paid (7, incl. VAT)	51,579,627
Retention / deductions	0 / 36,000
Advance payment	0

Gross invoicing is 56.5% of the contract value against 75.2% physical progress. Invoice 7 was paid on 25-Oct-2026. Invoice 8 (period to 29-Oct-2026, 4,882,589 incl. VAT after a 36,000 deduction) was approved by the consultant on 31-Oct-2026 and awaits PM approval.

Health, safety and quality

Safety Score 0.73

Safe man-hours (cumulative)	483,442
Man-hours this week	3,072
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks (cumulative)	65 / 92

MODON HSE inspection 03-Nov-2026: 7 topics good, 13 need improvement and 3 failed (site waste management, HSE communications and meetings, project leadership site tours).

Quality Score 0.86

Field inspection requests issued / closed	5,549 / 5,481
FIRs with the consultant	47
Material inspections issued / closed	105 / 105
NCRs issued / closed	17 / 16
Site instructions issued / closed	21 / 21
Shop drawings pending	3

Consultant quality score 0.86 this week; average 0.83 across all audits.

Open issues and risks

ISSUE	OWNER	DETAIL
MODON–SEC agreement for medium voltage	Owner	Open since 15-Dec-2025, target closure 30-Dec-2025. MODON is following up with SEC for the electricity source; the contractor is waiting for a reply to letter 2818 of 13-Jan-2026.
MV materials on hold	Owner / Contractor	Orders for MV cable, ring main units and street-lighting substations wait for the agreement. The ring main unit order is marked "PO in delay"; it was required on site by 20-Oct-2026 and is still not ordered.
Completion forecast	Contractor	The schedule forecasts completion on 03-Jun-2028 with –169 days of float, 198 days after the contract date, although physical progress is 26.1% ahead of plan. The forecast has moved 7 days later in each of the last three reports.

The other two issues in the log are closed: tie-in permits from SEC, STC and NWC (closed 10-Feb-2026) and supplier prequalification for post-tensioning, bearings and expansion joints.

Data notes

Built from the 03-Nov-2026 weekly upload (W06), with the 27-Oct-2026 upload (W05) for this week's changes.

- Week number: the report states week 49.86 (whole weeks since site handover: 49); the file reference is WPR-050.
- Physical progress differs between sheets: the dashboard shows 75.2% (537,033 of 714,561 man-hours), while the P6 export and the Physical-Chart Data sheet show 76.6% (547,132 man-hours).

- The weekly summary file (works executed this week) and the Look Ahead and Conclusion sheets label cost-based progress as "actual"; this report uses physical % complete (man-hours) only. The weekly summary file also gives project code JDH3-03-011, contract value 86,742,345 and an expected finish of 30-Nov-2026, as does the Look Ahead sheet; the dashboard and P6 forecast 03-Jun-2028.
- MODON PM: Eng. Abdallah Aljulayfi in the General Information sheet; م. رضا المنشاوي in the Look Ahead sheet and the weekly summary file.
- Milestones: P6 and the weekly report still swap the roads/MV and deep-network forecast dates, and the dashboard's "Original (Baseline)" column shows latest-plan dates.
- Manpower: the summary panel is now labelled November but still shows October's figures (148 planned, 182 actual), while the November plan is 187. HSE reports 3,072 man-hours for the week, a third of the 9,216 reported in each of the two previous weeks.
- Material Monitoring: the revised quantity of lighting poles and luminaires changed from 404 to 443 (all delivered), and the installed quantity of the 6,115 m low-voltage cable line went from 230 m back to 6,115 m.
- The Procurement Log content is unchanged for the third week running.
- Invoice 8 carries a 36,000 deduction, also shown as penalties on the dashboard; the reason is not stated.
- HDPE pipes: the Major Quantities sheet does not name the network; potable water and TSE are inferred from quantities, and installed quantities differ from the Material Monitoring sheet.
- Equipment cumulative actual stays at 564 from July although monthly counts continue. Several dashboard cells show #REF! errors.

Compiled 04-Nov-2026 from the weekly report for the week ending 03-Nov-2026 (W06), with the 27-Oct-2026 report (W05) for this week's changes.
