
Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
Dammam 3rd Industrial City Gates and Fence - B1		75	06-May-26	05-Aug-26	89.5%	100%
Key Milestones		75	06-May-26	05-Aug-26	0%	0%
General Milestones		0	06-May-26	06-May-26	0%	0%
DAM3-05-012-1080	Project Start	0	06-May-26		100%	100%
Contractual Milestones		58	25-May-26	05-Aug-26	0%	0%
DAM3-05-012-4880	Preliminary Submittals	0		25-May-26	100%	100%
DAM3-05-012-4870	Mobilization	0		31-May-26	100%	100%
DAM3-05-012-4890	Shop Drawings	0		22-Jun-26	100%	100%
DAM3-05-012-4900	Material Submittal & Approval	0		18-Jul-26	100%	100%
DAM3-05-012-4910	Fabrication & Delivery	0		04-Aug-26	100%	100%
DAM3-05-012-4860	Project Finish	0		05-Aug-26	100%	100%
DAM3-05-012-4920	Construction	0		05-Aug-26	100%	100%
Mobilization		18	06-May-26	31-May-26	0%	0%
Site Survey		4	06-May-26	10-May-26	0%	0%
DAM3-05-012-1020	Site Survey	2	06-May-26	07-May-26	100%	100%
DAM3-05-012-1090	Survey Report	2	09-May-26	10-May-26	100%	100%
Site Layout Plan		3	11-May-26	13-May-26	0%	0%
DAM3-05-012-1100	Site Office Layout Drawing Proposal Submittal	1	11-May-26	11-May-26	100%	100%
DAM3-05-012-1110	Site Office Layout Drawing Review & Approval	2	12-May-26	13-May-26	100%	100%
Construct Site Access Roads		4	14-May-26	19-May-26	0%	0%
DAM3-05-012-1120	Site Preparation	1	14-May-26	14-May-26	100%	100%
DAM3-05-012-1150	Grading & Leveling	2	16-May-26	17-May-26	100%	100%
DAM3-05-012-1160	Temporary Access Road	2	17-May-26	19-May-26	100%	100%
Construct Site Office Fence		7	18-May-26	31-May-26	0%	0%
DAM3-05-012-1190	Excavation for Fence Foundation	4	18-May-26	23-May-26	100%	100%
DAM3-05-012-1220	Installation of Fence Posts	4	19-May-26	24-May-26	100%	100%
DAM3-05-012-1460	Installation of Fence Mesh	3	23-May-26	31-May-26	100%	100%
Construct Site Offices		4	18-May-26	21-May-26	0%	0%
DAM3-05-012-1170	Installation of Site Offices	3	18-May-26	20-May-26	100%	100%
DAM3-05-012-1200	MEP Works	2	18-May-26	20-May-26	100%	100%
DAM3-05-012-1210	Installation of Furniture	2	19-May-26	21-May-26	100%	100%
Mobilization of Manpower		6	14-May-26	20-May-26	0%	0%
DAM3-05-012-1130	Mobilization of Manpower	6	14-May-26	20-May-26	100%	100%
Mobilization of Equipment		6	14-May-26	20-May-26	0%	0%
DAM3-05-012-1140	Mobilization of Tools & Equipment	6	14-May-26	20-May-26	100%	100%
Preliminary Submittals		17	06-May-26	25-May-26	0%	0%
DAM3-05-012-1000	Insurances	17	06-May-26	25-May-26	100%	100%
DAM3-05-012-1010	Performance Bonds	17	06-May-26	25-May-26	100%	100%
DAM3-05-012-1030	Contract Schedule (Baseline Program)	13	06-May-26	20-May-26	100%	100%
DAM3-05-012-1040	HSE Plan	12	06-May-26	19-May-26	100%	100%
DAM3-05-012-1050	Quality Control Plan	10	06-May-26	17-May-26	100%	100%
DAM3-05-012-1060	Project Organization Chart	12	06-May-26	19-May-26	100%	100%
DAM3-05-012-1070	Submission of Staff CVs	10	06-May-26	17-May-26	100%	100%
Engineering		49	18-May-26	18-Jul-26	100%	100%
Shop Drawings		27	18-May-26	22-Jun-26	0%	0%
Prepare & Submit		15	18-May-26	08-Jun-26	0%	0%




© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-118	Fence Type 1 - Shopdrawings - (Prepare & Submit)	11	18-May-26	03-Jun-26	100%	100%
DAM3-05-012-134	Fence Type 2 - Shopdrawings - (Prepare & Submit)	9	21-May-26	04-Jun-26	100%	100%
DAM3-05-012-162	Guard Room - Shopdrawings - (Prepare & Submit)	9	25-May-26	08-Jun-26	100%	100%
Review & Approve		17	03-Jun-26	22-Jun-26	0%	0%
DAM3-05-012-219	Fence Type 1 - Shopdrawings - (Prepare & Submit)	12	03-Jun-26	17-Jun-26	100%	100%
DAM3-05-012-266	Fence Type 2 - Shopdrawings - (Prepare & Submit)	12	06-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-310	Guard Room - Shopdrawings - (Prepare & Submit)	12	09-Jun-26	22-Jun-26	100%	100%
Material Submittal		47	20-May-26	18-Jul-26	100%	100%
Material Prepare & Submit		41	20-May-26	11-Jul-26	0%	0%
Civil & Arch		40	21-May-26	11-Jul-26	0%	0%
DAM3-05-012-1	Backfilling for guard rooms under G Beams (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	interlocking paving blocks (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	Concrete Masonry Unit (CMU) for walls (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	overflow galvanized steel roof scupper with gray color with angular secondary	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	aluminum framed double glazed windows (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	Riyadh stone cladding (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	PANEL SIGNAGE (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	Aluminum Door (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	structural steel members for gate frame (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	structural steel members and plates for main gates (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	plant trees, plants, and ground covers including fixations, sweet soil (Material	4	24-May-26	02-Jun-26	100%	100%
DAM3-05-012-1	precast concrete curbstone (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	stone gravel (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	PANTRY CABINET (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	COUNTER DESK (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	Roller blind (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	structural steel members and plates for pedestrian gates (Material Prepare &	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	Backfilling for Roads (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	interlocking pedstrian paving blocks (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	folding & sliding mounter combination ladder for building maintenance purpose	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	heavy steel cover with frame including all necessary fixings (Material Prepare &	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	hollow metal door (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	granite saddles and thresholds (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	ceramic wall tiles (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	acrylic paint on internal walls (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	two coats of acrylic paint (suitable for exterior use) on external (Material Prepare	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	aluminum cladding (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	gypsum board suspended ceiling (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	Waste Receptacle(Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	structural steel members and steel hollow sections for wall fence (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	galvanized steel chain link gate (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	gully traps with heavy duty cover (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	chamber with heavy duty cover (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-2	ceramic floor tiles (Material Prepare & Submit)	5	01-Jun-26	06-Jun-26	100%	100%
DAM3-05-012-2	matt stainless steel flag pole (Material Prepare & Submit) (Material Prepare &	5	02-Jun-26	07-Jun-26	100%	100%
DAM3-05-012-2	galvanized steel chain link ,steel tube framing and posts, turn buckle, tension	5	02-Jun-26	07-Jun-26	100%	100%
DAM3-05-012-3	granite flooring (Material Prepare & Submit)	5	09-Jun-26	14-Jun-26	100%	100%
DAM3-05-012-3	Workstation chair (Material Prepare & Submit)	5	06-Jul-26	11-Jul-26	100%	100%
DAM3-05-012-3	Workstation table (Material Prepare & Submit)	5	06-Jul-26	11-Jul-26	100%	100%
Mechanical		9	20-May-26	03-Jun-26	0%	0%

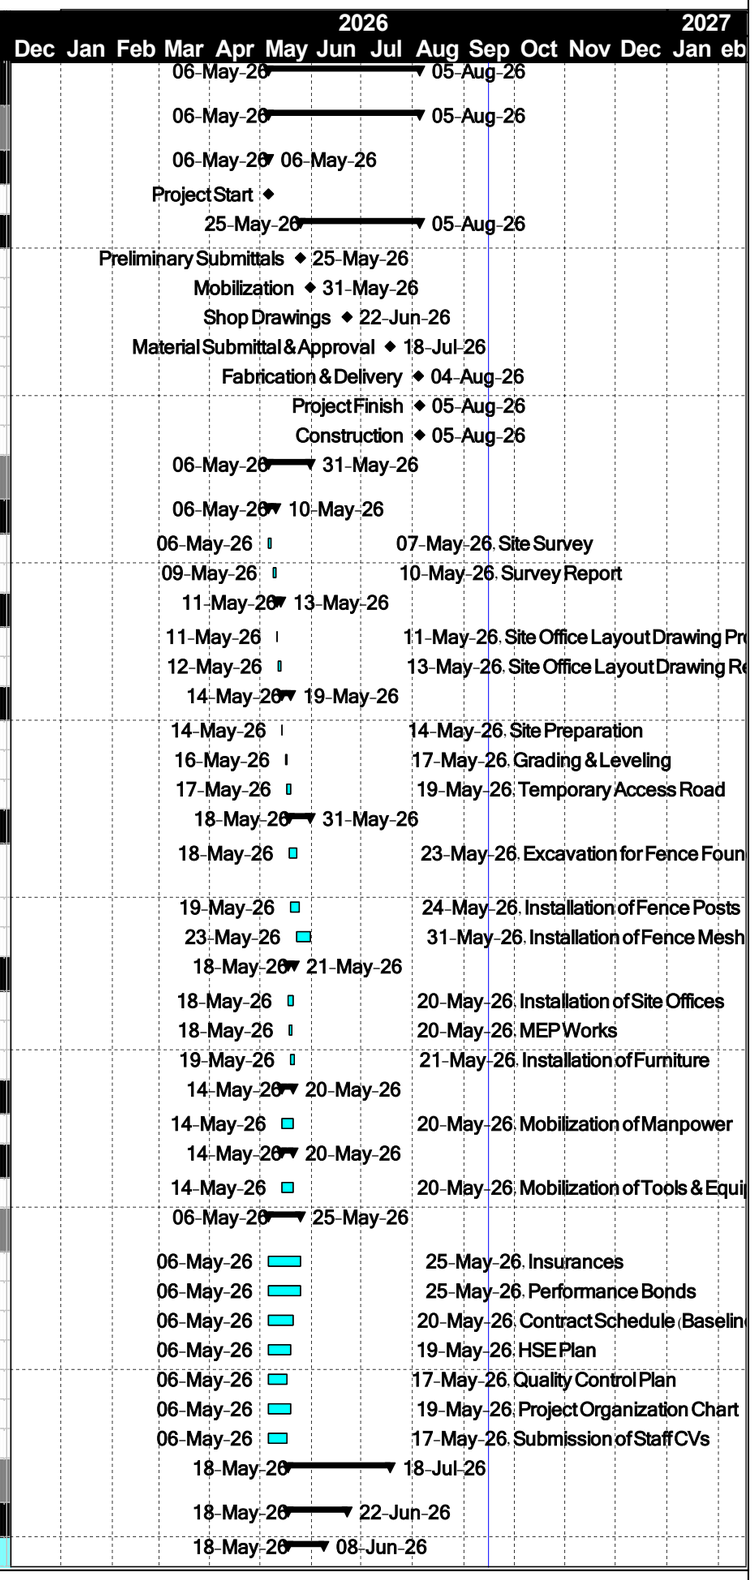


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-1	Fire extinguishers as per drawings, specifications (Material Prepare & Submit)	5	20-May-26	25-May-26	100%	100%
DAM3-05-012-1	HEATING, VENTILATION AND AIR CONDITIONING - (Material Prepare &	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	Bulbblers and Spreyers of IRRIGATION SYSTEM (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	TOILET ACCESSROIES (Material Prepare & Submit)	4	24-May-26	02-Jun-26	100%	100%
DAM3-05-012-1	Exhaust fans - (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	IRRIGATION SYSTEM (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	PLUMBING FIXTURES (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	WATER SUPPLY SYSTEM (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
Electrical		11	21-May-26	07-Jun-26	0%	0%
DAM3-05-012-1	Central (Headend) System Components - (Material Prepare & Submit)	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	Analog addressable fire alarm control panel with battery (Material Prepare &	4	21-May-26	31-May-26	100%	100%
DAM3-05-012-1	LIGHTING FIXTURES (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	COMPUTERS AND RELATED PERIPHERALS (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	CCTV storage system, as specified (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	ELECTRICAL GATE BARRIER (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	LIGHTNING PROTECTION (Material Prepare & Submit)	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	Intelligent Ionization / Photoelectric smoke and heat detector with base	4	23-May-26	01-Jun-26	100%	100%
DAM3-05-012-1	power source with built-in photocell sensor for automatic electrical connection	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	UNDERGROUND DISTRIBUTION SYSTEM -(Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	GROUNDING - (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	card reader IN/OUT (Material Prepare & Submit)	4	25-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	switches and Receptacle outlets complete with device boxes (Material Prepare	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	12-Port CAT6A UTP fully loaded patch panel (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	(Material Prepare & Submit)Port, SMF, Fiber Optic Patch Panels	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	VIDEO SURVEILLANCE (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	VSS System, as specified (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	CCTV cameras (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	20A, ATS (Automatic transfer switch) for UPS (Material Prepare & Submit)	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-1	fire alarm system including wires, conduit and other materials - (Material	4	31-May-26	03-Jun-26	100%	100%
DAM3-05-012-2	3mm steel CNC laser cut panels (Material Prepare & Submit)	5	01-Jun-26	06-Jun-26	100%	100%
DAM3-05-012-2	Access control panel - (Material Prepare & Submit)	5	01-Jun-26	06-Jun-26	100%	100%
DAM3-05-012-2	LIGHTING AND POWER TYPE PANELBOARDS (Material Prepare & Submit)	5	02-Jun-26	07-Jun-26	100%	100%
Material Review & Approve		42	31-May-26	18-Jul-26	100%	100%
Civil & Arch		42	31-May-26	18-Jul-26	100%	100%
DAM3-05-012-1	Backfilling for guard rooms under G Beams (Material Review & Approve)	2	31-May-26	02-Jun-26	100%	100%
DAM3-05-012-1	interlocking paving blocks (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	Concrete Masonry Unit (CMU) for walls (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	overflow galvanized steel roof scupper with gray color with angular secondary	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	aluminum framed double glazed windows (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	Riyadh stone cladding (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	PANEL SIGNAGE (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-2	Aluminum Door (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	structural steel members for gate frame (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	installation of structural steel members and plates for main gates (Material	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	plant trees, plants, and ground covers including fixations, sweet soil (Material	6	02-Jun-26	09-Jun-26	100%	100%
DAM3-05-012-2	precast concrete curbstone (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	19 to 38mm locally available stone gravel (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	PANTRY CABINET (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	COUNTER DESK (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	Roller blind (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	installation of structural steel members and plates for pedestrian gates (Material	6	03-Jun-26	10-Jun-26	100%	100%

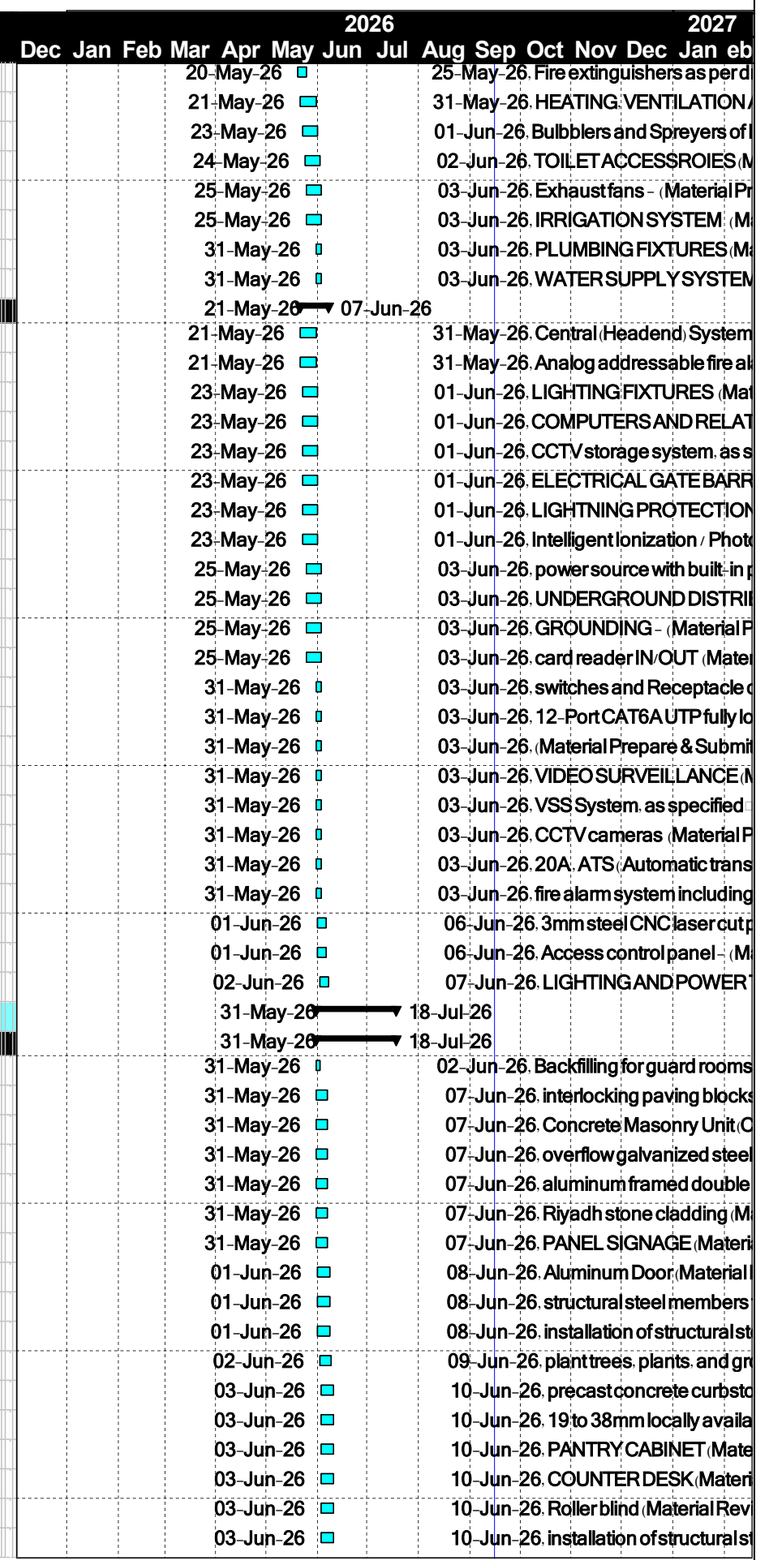


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-2	Backfilling for Roads (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	interlocking pedstrian paving blocks (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	folding & sliding mounter combination ladder for building maintenance purpose	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	hollow metal door (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	granite saddles and thresholds (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	ceramic wall tiles (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	two coats of acrylic paint on internal walls (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	two coats of acrylic paint (suitable for exterior use) on external (Material Review &	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	aluminum cladding (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	gypsum board suspended ceiling (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	Waste Receptacle(Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	structural steel members and steel hollow sections for wall fence (Material	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	fix galvanized steel chain link gate (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	gully traps with heavy duty cover (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	chamber with heavy duty cover (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	ceramic floor tiles (Material Review & Approve)	6	07-Jun-26	13-Jun-26	100%	100%
DAM3-05-012-2	3mm steel CNC laser cut panels (Material Review & Approve)	6	07-Jun-26	13-Jun-26	100%	100%
DAM3-05-012-2	matt stainless steel flag pole (Material Review & Approve) (Material Review &	6	08-Jun-26	14-Jun-26	100%	100%
DAM3-05-012-2	galvanized steel chain link ,steel tube framing and posts, turn buckle, tension	6	08-Jun-26	14-Jun-26	100%	100%
DAM3-05-012-3	granite flooring (Material Review & Approve)	6	15-Jun-26	21-Jun-26	100%	100%
DAM3-05-012-3	Workstation chair (Material Review & Approve)	6	12-Jul-26	18-Jul-26	100%	100%
DAM3-05-012-3	Workstation table (Material Review & Approve)	6	12-Jul-26	18-Jul-26	100%	100%
Mechanical		10	31-May-26	10-Jun-26	100%	100%
DAM3-05-012-1	installation of Fire extinguishers as per drawings, specifications (Material	5	31-May-26	04-Jun-26	100%	100%
DAM3-05-012-2	Bulbblers and Spreyers of IRRIGATION SYSTEM (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	TOILET ACCESSROIES (Material Review & Approve)	6	02-Jun-26	09-Jun-26	100%	100%
DAM3-05-012-2	GROUNDING - (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	IRRIGATION SYSTEM (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	heavy steel cover with frame including all necessary fixings(Material Review &	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	PLUMBING FIXTURES (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	WATER SUPPLY SYSTEM (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
Electrical		13	31-May-26	14-Jun-26	100%	100%
DAM3-05-012-1	HEATING, VENTILATION AND AIR CONDITIONING - (Material Review &	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	Central (Headend) System Components - (Material Review & Approve)	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-1	Analog addressable fire alarm control panel with battery (Material Review &	6	31-May-26	07-Jun-26	100%	100%
DAM3-05-012-2	LIGHTING FIXTURES (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	COMPUTERS AND RELATED PERIPHERALS (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	CCTV storage system, as specified(Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	ELECTRICAL GATE BARRIER (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	LIGHTNING PROTECTION (Material Review & Approve)	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	Intelligent Ionization / Photoelectric smoke and heat detector with base	6	01-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-2	Exhaust fans - (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	power source with built-in photocell sensor for automatic electrical connection	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	UNDERGROUND DISTRIBUTION SYSTEM -(Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	card reader IN/OUT (Material Review & Approve)	6	03-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	switches and Receptacle outlets complete with device boxes (Material Review	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	12-Port CAT6A UTP fully loaded patch panel (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	(Material Review & Approve)Port, SMF, Fiber Optic Patch Panels	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	VIDEO SURVEILLANCE (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	VSS System, as specified (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	CCTV cameras (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%

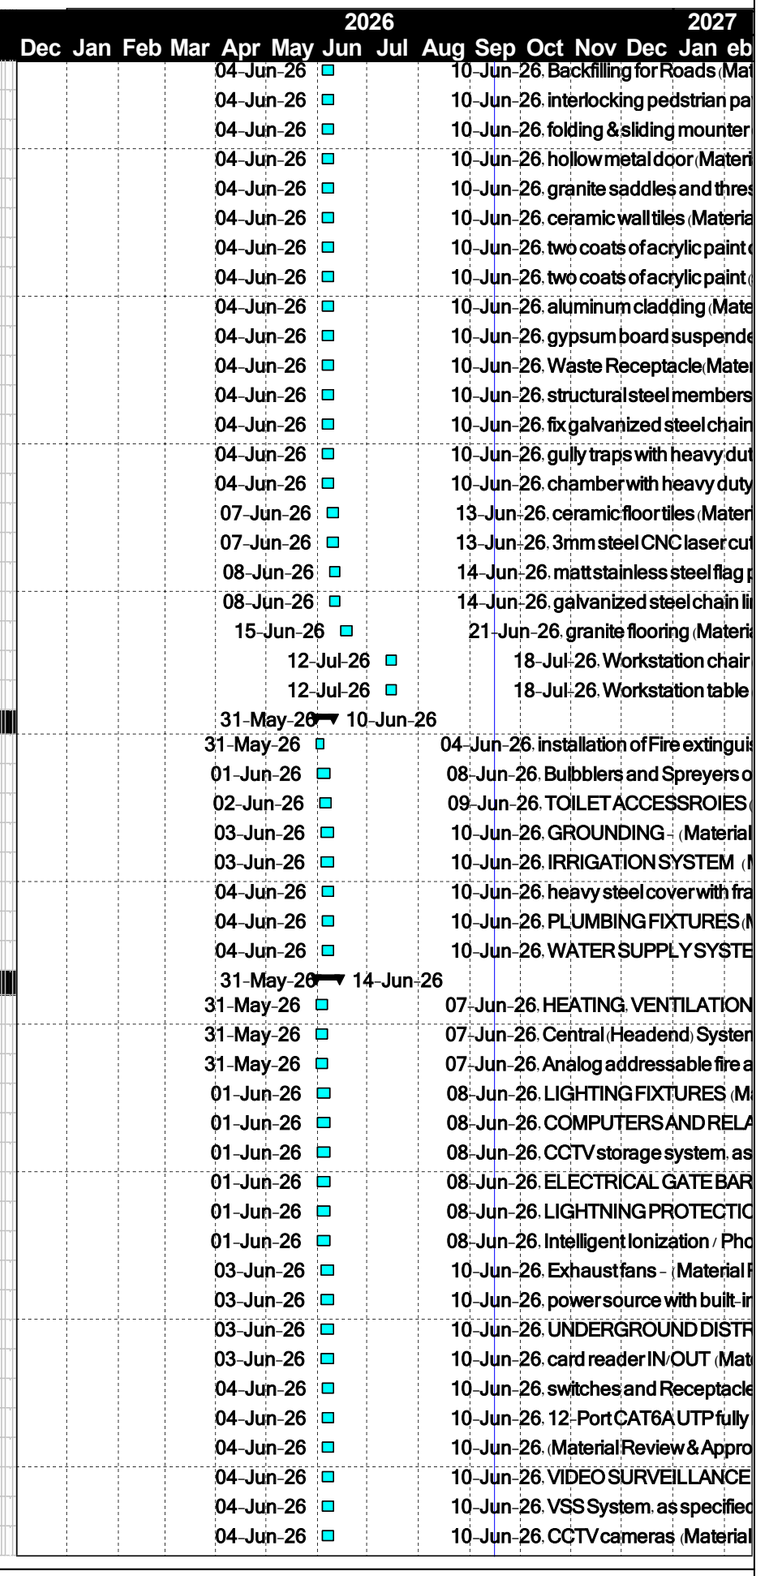


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-2	20A. ATS (Automatic transfer switch) for UPS (Material Review & Approve)	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	fire alarm system including wires, conduit and other materials - (Material Review	6	04-Jun-26	10-Jun-26	100%	100%
DAM3-05-012-2	Access control panel - (Material Review & Approve)	6	07-Jun-26	13-Jun-26	100%	100%
DAM3-05-012-2	LIGHTING AND POWER TYPE PANELBOARDS (Material Review & Approve)	6	08-Jun-26	14-Jun-26	100%	100%
Procurement		55	02-Jun-26	04-Aug-26	100%	100%
Fabrication & Delivery		55	02-Jun-26	04-Aug-26	100%	100%
Civil & Arch		55	02-Jun-26	04-Aug-26	100%	100%
DAM3-05-012-216	Backfilling for guard rooms under G.Beams (Fabrication & Delivery)	2	02-Jun-26	04-Jun-26	100%	100%
DAM3-05-012-283	interlocking paving blocks (Fabrication & Delivery)	5	07-Jun-26	13-Jun-26	100%	100%
DAM3-05-012-284	Concrete Masonry Unit (CMU) for walls (Fabrication & Delivery)	4	07-Jun-26	11-Jun-26	100%	100%
DAM3-05-012-285	overflow galvanized steel roof scupper with gray color with angular secondary	15	07-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-286	aluminum framed double glazed windows (Fabrication & Delivery)	13	07-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-287	Riyadh stone cladding (Fabrication & Delivery)	12	07-Jun-26	21-Jun-26	100%	100%
DAM3-05-012-288	PANEL SIGNAGE (Fabrication & Delivery)	12	07-Jun-26	21-Jun-26	100%	100%
DAM3-05-012-297	Aluminum Door (Fabrication & Delivery)	15	08-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-298	structural steel members for gate frame (Fabrication & Delivery)	15	08-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-299	installation of structural steel members and plates for main gates (Fabrication &	12	08-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-309	TOILET ACCESSROIES (Fabrication & Delivery)	14	09-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-313	precast concrete curbstone (Fabrication & Delivery)	5	10-Jun-26	16-Jun-26	100%	100%
DAM3-05-012-314	19 to 38mm locally available stone gravel (Fabrication & Delivery)	5	10-Jun-26	16-Jun-26	100%	100%
DAM3-05-012-315	PANTRY CABINET (Fabrication & Delivery)	14	10-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-316	COUNTER DESK (Fabrication & Delivery)	12	10-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-317	Roller blind (Fabrication & Delivery)	10	10-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-318	installation of structural steel members and plates for pedestrian gates	14	10-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-325	Backfilling for Roads (Fabrication & Delivery)	4	11-Jun-26	15-Jun-26	100%	100%
DAM3-05-012-326	interlocking pedstrian paving blocks (Fabrication & Delivery)	5	11-Jun-26	16-Jun-26	100%	100%
DAM3-05-012-327	folding & sliding mounter combination ladder for building maintenance purpose	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-328	heavy steel cover with frame including all necessary fixings (Fabrication &	12	11-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-329	hollow metal door (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-330	granite saddles and thresholds (Fabrication & Delivery)	12	11-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-331	ceramic wall tiles (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-332	two coats of acrylic paint on internal walls (Fabrication & Delivery)	10	11-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-333	two coats of acrylic paint (suitable for exterior use) on external (Fabrication &	5	11-Jun-26	16-Jun-26	100%	100%
DAM3-05-012-334	aluminum cladding (Fabrication & Delivery)	13	11-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-335	gypsum board suspended ceiling (Fabrication & Delivery)	4	11-Jun-26	15-Jun-26	100%	100%
DAM3-05-012-337	structural steel members and steel hollow sections for wall fence (Fabrication &	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-338	fix galvanized steel chain link gate (Fabrication & Delivery)	10	11-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-339	gully traps with heavy duty cover (Fabrication & Delivery)	14	11-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-340	chamber with heavy duty cover (Fabrication & Delivery)	12	11-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-341	PLUMBING FIXTURES (Fabrication & Delivery)	10	11-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-351	ceramic floor tiles (Fabrication & Delivery)	10	14-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-352	3mm steel CNC laser cut panels (Fabrication & Delivery)	12	14-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-356	matt stainless steel flag pole (Fabrication & Delivery) (Fabrication & Delivery)	10	15-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-357	galvanized steel chain link ,steel tube framing and posts, turn buckle, tension	15	15-Jun-26	01-Jul-26	100%	100%
DAM3-05-012-408	Workstation chair (Fabrication & Delivery)	15	19-Jul-26	04-Aug-26	100%	100%
DAM3-05-012-409	Workstation table (Fabrication & Delivery)	15	19-Jul-26	04-Aug-26	100%	100%
DAM3-05-012-412	granite flooring (Fabrication & Delivery)	10	22-Jul-26	02-Aug-26	100%	100%
Mechanical		20	06-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-262	installation of Fire extinguishers as per drawings, specifications (Fabrication &	12	06-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-289	HEATING, VENTILATION AND AIR CONDITIONING - (Fabrication & Delivery)	12	07-Jun-26	21-Jun-26	100%	100%

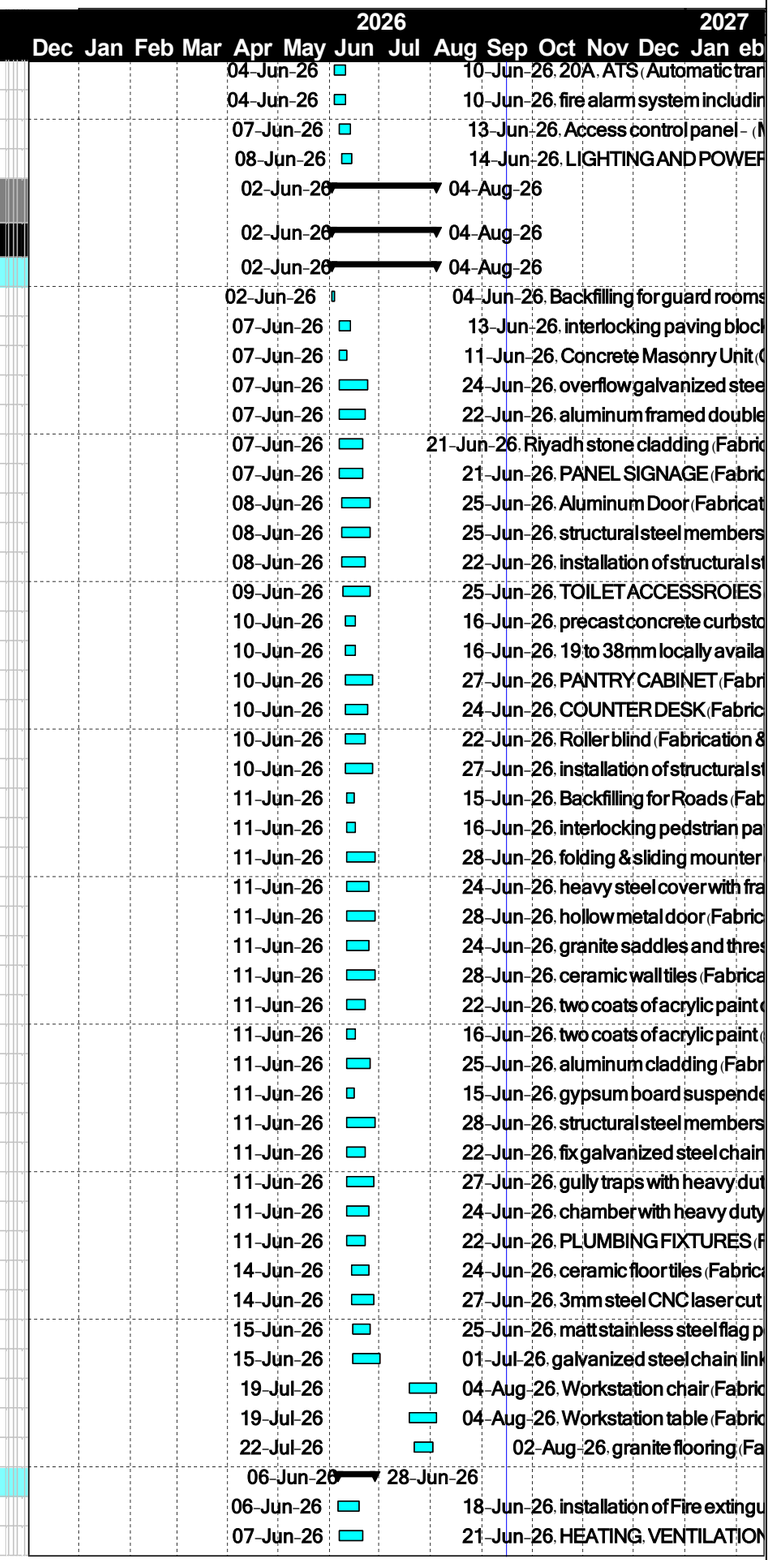


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-30(	Bulbblers and Spreyers of IRRIGATION SYSTEM (Fabrication & Delivery)	12	08-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-302	COMPUTERS AND RELATED PERIPHERALS (Fabrication & Delivery)	12	08-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-306	Intelligent Ionization / Photoelectric smoke and heat detector with base	14	08-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-308	plant trees, plants, and ground covers including fixations, sweet soil (Fabrication	12	09-Jun-26	23-Jun-26	100%	100%
DAM3-05-012-31(	Exhaust fans - (Fabrication & Delivery)	14	10-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-324	IRRIGATION SYSTEM (Fabrication & Delivery)	15	10-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-336	Waste Receptacle(Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-350	WATER SUPPLY SYSTEM (Fabrication & Delivery)	12	11-Jun-26	24-Jun-26	100%	100%
Electrical		21	07-Jun-26	30-Jun-26	100%	100%
DAM3-05-012-290	Central (Headend) System Components (Fabrication & Delivery)	12	07-Jun-26	21-Jun-26	100%	100%
DAM3-05-012-291	Analog addressable fire alarm control panel with battery (Fabrication & Delivery)	12	07-Jun-26	21-Jun-26	100%	100%
DAM3-05-012-301	LIGHTING FIXTURES (Fabrication & Delivery)	10	08-Jun-26	20-Jun-26	100%	100%
DAM3-05-012-303	CCTV storage system, as specified (Fabrication & Delivery)	14	08-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-304	ELECTRICAL GATE BARRIER (Fabrication & Delivery)	12	08-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-305	LIGHTNING PROTECTION (Fabrication & Delivery)	14	08-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-320	power source with built-in photocell sensor for automatic electrical connection	10	10-Jun-26	22-Jun-26	100%	100%
DAM3-05-012-321	UNDERGROUND DISTRIBUTION SYSTEM -(Fabrication & Delivery)	12	10-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-322	GROUNDING - (Fabrication & Delivery)	8	10-Jun-26	20-Jun-26	100%	100%
DAM3-05-012-323	card reader IN/OUT (Fabrication & Delivery)	15	10-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-342	switches and Receptacle outlets complete with device boxes (Fabrication &	12	11-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-343	12-Port CAT6A UTP fully loaded patch panel (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-344	(Fabrication & Delivery)Port, SMF, Fiber Optic Patch Panels	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-345	VIDEO SURVEILLANCE (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-346	VSS System, as specified (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-347	CCTV cameras (Fabrication & Delivery)	14	11-Jun-26	27-Jun-26	100%	100%
DAM3-05-012-348	20A, ATS (Automatic transfer switch) for UPS (Fabrication & Delivery)	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-349	fire alarm system including wires, conduit and other materials - (Fabrication &	15	11-Jun-26	28-Jun-26	100%	100%
DAM3-05-012-353	Access control panel - (Fabrication & Delivery)	15	14-Jun-26	30-Jun-26	100%	100%
DAM3-05-012-358	LIGHTING AND POWER TYPE PANELBOARDS (Fabrication & Delivery)	14	15-Jun-26	30-Jun-26	100%	100%
Construction		62	21-May-26	05-Aug-26	98.4%	100%
SITE WORKS		61	21-May-26	05-Aug-26	98.09%	100%
Guard Rooms & Gates		17	21-May-26	15-Jun-26	100%	100%
DAM3-05-012-135	Excavation for guard rooms	8	21-May-26	03-Jun-26	100%	100%
DAM3-05-012-260	Replacment Under Foundation	2	04-Jun-26	07-Jun-26	100%	100%
DAM3-05-012-354	Backfilling Under G.Beam	2	13-Jun-26	15-Jun-26	100%	100%
DAM3-05-012-355	Backfilling Under S.O.G	2	13-Jun-26	15-Jun-26	100%	100%
Guard Rooms & Gates (CONCRETE Works)		48	04-Jun-26	30-Jul-26	100%	100%
DAM3-05-012-261	50 mm thickness lean concrete under the foundation.	3	04-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-295	Isolated Footings & Column Neck	5	07-Jun-26	13-Jun-26	100%	100%
DAM3-05-012-360	50 mm thickness lean concrete under grade beams.	3	15-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-361	Grade beams	5	18-Jun-26	24-Jun-26	100%	100%
DAM3-05-012-364	Columns	4	24-Jun-26	29-Jun-26	100%	100%
DAM3-05-012-366	Raft and R.C. walls	5	27-Jun-26	02-Jul-26	100%	100%
DAM3-05-012-369	Roof Slab	8	29-Jun-26	08-Jul-26	100%	100%
DAM3-05-012-370	Beams	8	29-Jun-26	08-Jul-26	100%	100%
DAM3-05-012-386	Provide and cast concrete floor slab on grade	5	08-Jul-26	14-Jul-26	100%	100%
DAM3-05-012-387	Concrete Pad	3	08-Jul-26	12-Jul-26	100%	100%
DAM3-05-012-388	Tanks Raft	5	08-Jul-26	14-Jul-26	100%	100%
DAM3-05-012-393	Tanks Walls	5	14-Jul-26	20-Jul-26	100%	100%

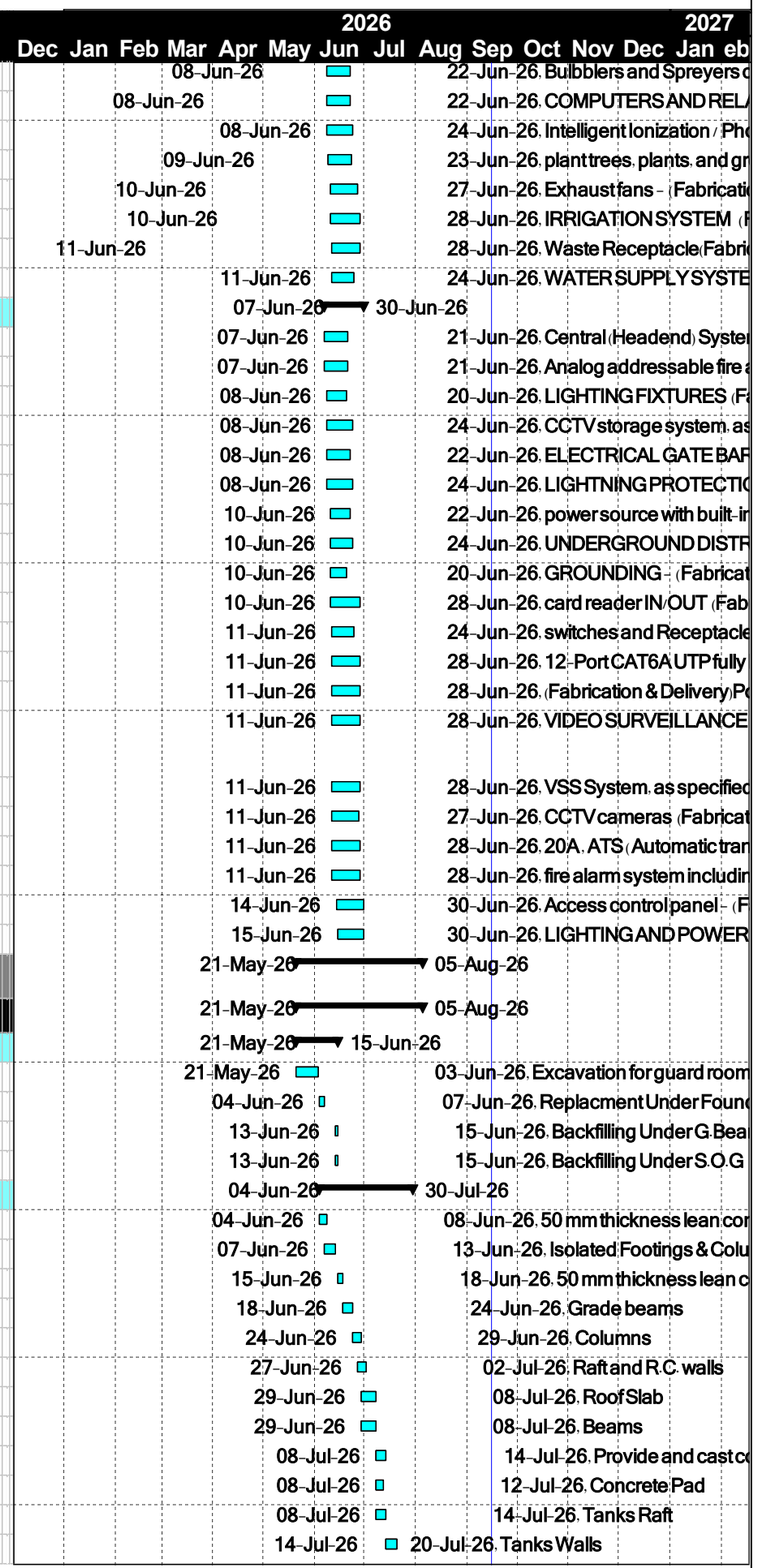


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-414	Tanks Slab	4	26-Jul-26	30-Jul-26	100%	100%
Fence Type 1		22	23-May-26	22-Jun-26	100%	100%
DAM3-05-012-147	Excavation	6	23-May-26	03-Jun-26	100%	100%
DAM3-05-012-233	Replacment Under Foundation	3	04-Jun-26	08-Jun-26	100%	100%
DAM3-05-012-362	Backfilling Under G.Beam	2	20-Jun-26	22-Jun-26	100%	100%
Fence Type 1 (CONCRETE Works)		23	08-Jun-26	05-Jul-26	100%	100%
DAM3-05-012-296	50 mm thickness lean concrete under the foundation.	3	08-Jun-26	11-Jun-26	100%	100%
DAM3-05-012-312	Isolated Footings & Column Neck	8	10-Jun-26	20-Jun-26	100%	100%
DAM3-05-012-363	50 mm thickness lean concrete under grade beams.	3	22-Jun-26	25-Jun-26	100%	100%
DAM3-05-012-365	Grade beams	8	25-Jun-26	05-Jul-26	100%	100%
Fence Type 2		20	03-Jun-26	27-Jun-26	95%	100%
DAM3-05-012-232	Excavation for Fence Type 2	20	03-Jun-26	27-Jun-26	95%	100%
Roads		49	09-Jun-26	05-Aug-26	96%	100%
DAM3-05-012-311	Demolition of the existing asphalt layers to reach the foundation level of	2	09-Jun-26	11-Jun-26	100%	100%
DAM3-05-012-367	Excavation for Roads	10	25-Jul-26	05-Aug-26	100%	100%
DAM3-05-012-371	Backfilling for Roads	8	27-Jul-26	05-Aug-26	95%	100%
DAM3-05-012-377	install 19 to 38mm locally available stone gravel	4	30-Jul-26	04-Aug-26	100%	100%
DAM3-05-012-381	plant trees, plants, and ground covers including fixations, sweet soil	3	01-Aug-26	04-Aug-26	77.01%	100%
DAM3-05-012-382	install matt stainless steel flag pole	3	01-Aug-26	04-Aug-26	100%	100%
DAM3-05-012-374	install interlocking paving blocks	2	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-380	install interlocking pedstrian paving blocks	2	03-Aug-26	05-Aug-26	95%	100%
DAM3-05-012-376	install precast concrete curbstone	2	03-Aug-26	05-Aug-26	96.98%	100%
MASONRY UNIT		3	02-Jul-26	06-Jul-26	100%	100%
DAM3-05-012-3730	install Concrete Masonry Unit (CMU) for walls	3	02-Jul-26	06-Jul-26	100%	100%
THERMAL & MOISTURE PROTECTION		14	14-Jul-26	30-Jul-26	100%	100%
THERMAL & MOISTURE PROTECTION - Foundation		4	14-Jul-26	19-Jul-26	100%	100%
DAM3-05-012-391	apply 2 coats of bitumen waterproofing paint on concrete surface in contact with	2	14-Jul-26	16-Jul-26	100%	100%
DAM3-05-012-392	install of waterproofing membrane 4mm including protection board for RC	2	14-Jul-26	16-Jul-26	100%	100%
DAM3-05-012-395	lay epoxy 2 coating for inner surfaces for RC walls, RC footings	2	16-Jul-26	19-Jul-26	100%	100%
THERMAL & MOISTURE PROTECTION - Tanks		11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-407	lay epoxy 2 coating for inner surfaces for bottom of the roof	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-411	install water stop for tanks according to the drawings and specification	5	20-Jul-26	26-Jul-26	100%	100%
ROOFING SYSTEM		11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-3970	install liquid applied waterproofing coating single-component pitch modified	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-3980	install 4mm thick APP modified bituminous membrane - single layer	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-3990	install 75mm thick rigid insulation (extruded polystyrene)	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4000	cast in place foam concrete screed, 50mm thick minimum laid to fall and cross	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4010	install 300 micron polyethylene sheet	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4020	install 50mm thick loose gravel toppings	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4030	install high density polyisocynurate cover board	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4040	install UV resistant geotextile sheet	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4050	fixing 3mm thick extruded aluminum flashing 40mm with sealant and all other	11	18-Jul-26	30-Jul-26	100%	100%
DAM3-05-012-4060	install Terrazzo tiles	11	18-Jul-26	30-Jul-26	100%	100%
FINISHES		27	06-Jul-26	05-Aug-26	98.36%	100%
DAM3-05-012-3840	install concrete plastering	4	06-Jul-26	11-Jul-26	100%	100%
DAM3-05-012-4170	install granite saddles and thresholds	3	30-Jul-26	02-Aug-26	100%	100%
DAM3-05-012-4190	install 3mm steel CNC laser cut panels	3	30-Jul-26	02-Aug-26	100%	100%
DAM3-05-012-4200	gypsum board suspended ceiling	4	30-Jul-26	03-Aug-26	100%	100%
DAM3-05-012-3830	install ceramic floor tiles	3	30-Jul-26	03-Aug-26	100%	100%
DAM3-05-012-4180	install Riyadh stone cladding	3	30-Jul-26	03-Aug-26	100%	100%

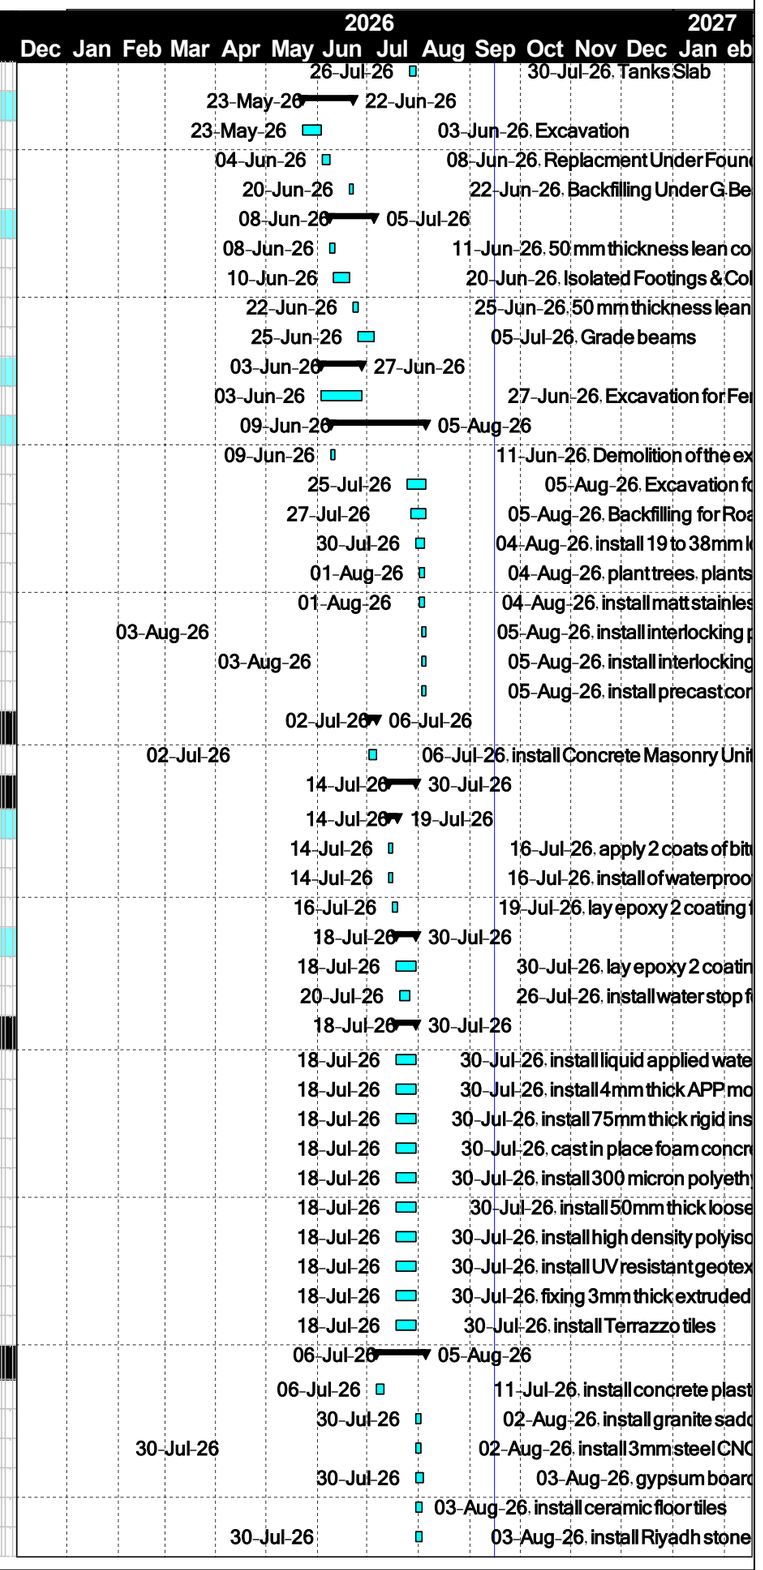

© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-4210	install aluminum cladding	2	01-Aug-26	02-Aug-26	100%	100%
DAM3-05-012-4280	install granite flooring	2	03-Aug-26	04-Aug-26	85%	100%
DAM3-05-012-4290	install ceramic wall tiles	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4480	install two coats of acrylic paint on internal walls	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4490	install two coats of acrylic paint (suitable for exterior use) on external	2	04-Aug-26	05-Aug-26	96.98%	100%
SPECIAL CONSTRUCTION- STRUCTURAL STEEL (Fence Type 2)		**30**	**02-Jul-26**	**05-Aug-26**	**98.33%**	**100%**
DAM3-05-012-3720	fix galvanized steel chain link fence wall including steel tube framing and posts.	30	02-Jul-26	05-Aug-26	95%	100%
DAM3-05-012-3750	install structural steel members for gate frame	25	05-Jul-26	02-Aug-26	100%	100%
DAM3-05-012-3850	installation of structural steel members and plates for main gates	26	07-Jul-26	05-Aug-26	100%	100%
DAM3-05-012-3940	installation of structural steel members and plates for pedestrian gates	18	16-Jul-26	05-Aug-26	100%	100%
DAM3-05-012-3960	Install structural steel members and steel hollow sections for wall fence	17	18-Jul-26	05-Aug-26	100%	100%
DAM3-05-012-4130	fix galvanized steel chain link gate	11	25-Jul-26	05-Aug-26	95%	100%
MECHANICAL WORKS		**52**	**07-Jun-26**	**05-Aug-26**	**100%**	**100%**
MECHANICAL WORKS - 1st Fix		**10**	**07-Jun-26**	**18-Jun-26**	**100%**	**100%**
DAM3-05-012-267	WATER SUPPLY SYSTEM - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-268	SEWER AND DRAINAGE SYSTEM - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-269	IRRIGATION SYSTEM - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-272	HEATING, VENTILATION AND AIR CONDITIONING - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-273	Exhaust fans - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
MECHANICAL WORKS - Final Fix		**3**	**03-Aug-26**	**05-Aug-26**	**100%**	**100%**
DAM3-05-012-430	installation of Fire extinguishers as per drawings, specifications	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-452	gully traps with heavy duty cover	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-431	chamber with heavy duty cover	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-432	INSTALL PLUMBING FIXTURES	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-433	HEATING, VENTILATION AND AIR CONDITIONING - Final Fix	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-434	Exhaust fans - Final Fix	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-453	Bulbblers and Spreyers of IRRIGATION SYSTEM	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-465	WATER SUPPLY SYSTEM - Final Fix	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-439	IRRIGATION SYSTEM - Final Fix	3	03-Aug-26	05-Aug-26	100%	100%
ELECTRICAL WORKS		**52**	**07-Jun-26**	**05-Aug-26**	**99.09%**	**100%**
ELECTRICAL WORKS - 1st Fix		**10**	**07-Jun-26**	**18-Jun-26**	**100%**	**100%**
DAM3-05-012-270	LIGHTING AND POWER TYPE PANELBOARDS - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-271	UPS 3KVA (installed inside the rack) - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-274	power source with built-in photocell sensor for automatic electrical connection	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-275	UNDERGROUND DISTRIBUTION SYSTEM - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-276	LIGHTING FIXTURES - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-277	installation of Wiring devices includes switches and Receptacle outlets	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-278	GROUNDING - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-279	card reader IN/OUT - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-280	CCTV cameras - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-281	Access control panel - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
DAM3-05-012-282	fire alarm system including wires, conduit and other materials - 1st Fix	10	07-Jun-26	18-Jun-26	100%	100%
ELECTRICAL WORKS - Final Fix		**3**	**03-Aug-26**	**05-Aug-26**	**98.64%**	**100%**
DAM3-05-012-477	UNDERGROUND DISTRIBUTION SYSTEM - Final Fix	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-455	LIGHTING FIXTURES - Final Fix	3	03-Aug-26	05-Aug-26	90%	100%
DAM3-05-012-478	installation of Wiring devices includes switches and Receptacle outlets	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-454	power source with built-in photocell sensor for automatic electrical connection	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-435	GROUNDING - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-456	card reader IN/OUT - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-479	Access control panel - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%

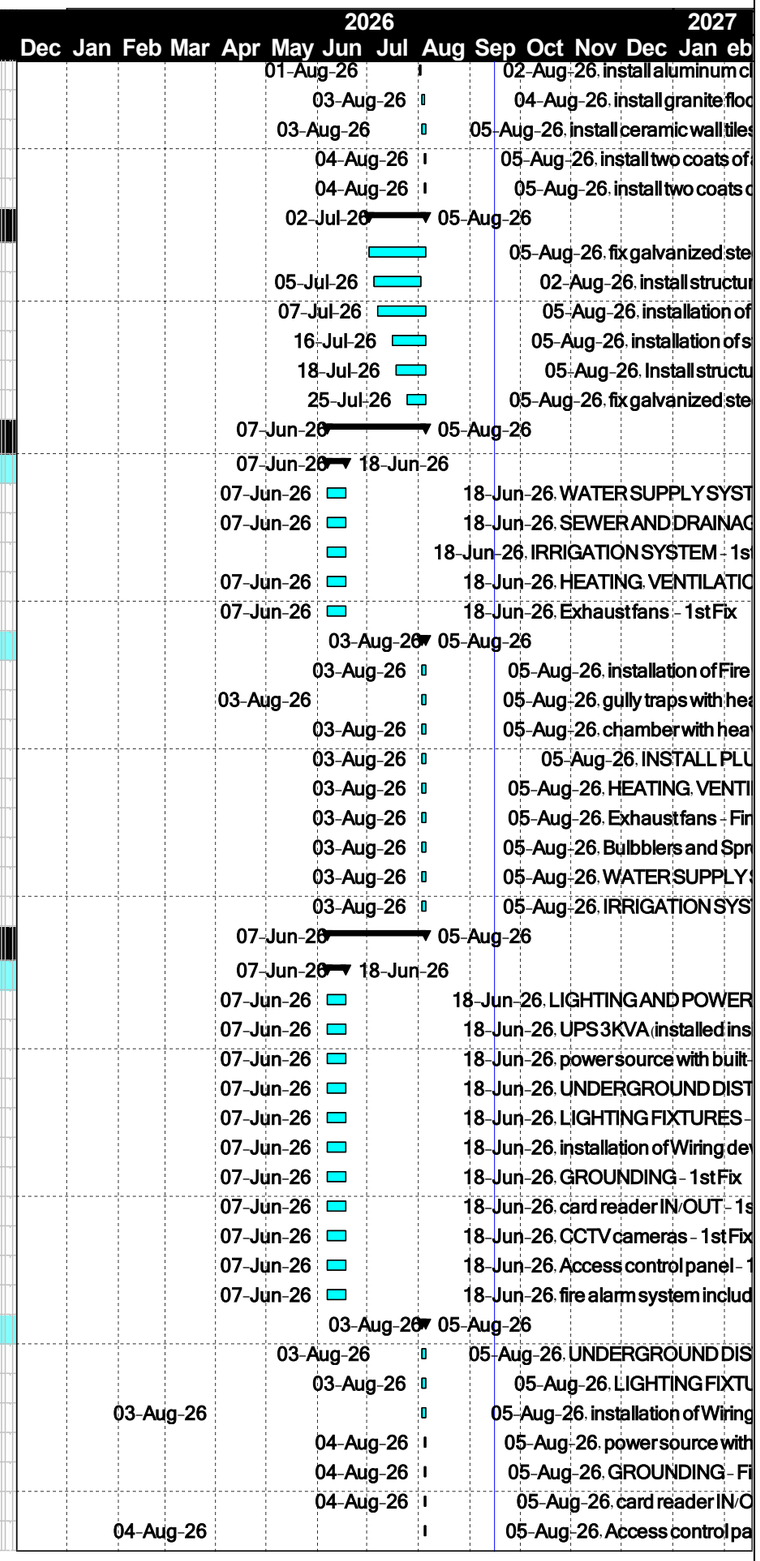


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities


© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-457	12-Port CAT6A UTP fully loaded patch panel	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-436	12-Port SMF Fiber Optic Patch Panels	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-458	COMPUTERS AND RELATED PERIPHERALS	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-437	VIDEO SURVEILLANCE	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-459	Central (Headend) System Components	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-460	VSS System, as specified	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-438	CCTV storage system, as specified	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-461	CCTV cameras - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-480	20A, ATS (Automatic transfer switch) for UPS	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-462	ELECTRICAL GATE BARRIER	2	04-Aug-26	05-Aug-26	95%	100%
DAM3-05-012-481	LIGHTNING PROTECTION	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-463	fire alarm system including wires, conduit and other materials - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-464	Analog addressable fire alarm control panel with battery	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-482	Intelligent Ionization / Photoelectric smoke and heat detector with base	2	04-Aug-26	05-Aug-26	85%	100%
DAM3-05-012-466	LIGHTING AND POWER TYPE PANELBOARDS - Final Fix	2	04-Aug-26	05-Aug-26	100%	100%
METALS		2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4440	folding & sliding mounter combination ladder for building maintenance purpose	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4450	install of overflow galvanized steel roof scupper with gray color with angular	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4460	install heavy steel cover with frame including all necessary fixings	2	04-Aug-26	05-Aug-26	100%	100%
WOODS AND PLASTICS		3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4260	COUNTER DESK	3	03-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4470	PANTRY CABINET	2	04-Aug-26	05-Aug-26	100%	100%
DOORS & WINDOWS		7	29-Jul-26	05-Aug-26	100%	100%
DAM3-05-012-4150	install hollow metal door	4	29-Jul-26	02-Aug-26	100%	100%
DAM3-05-012-4160	Install aluminum framed double glazed windows	3	29-Jul-26	01-Aug-26	100%	100%
DAM3-05-012-4270	Install Aluminum Door	3	03-Aug-26	05-Aug-26	100%	100%
SPECIALTIES		2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4500	TOILET ACCESSROIES	2	04-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4510	PANEL SIGNAGE	2	04-Aug-26	05-Aug-26	100%	100%
FURNISHINGS		1	05-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4730	Workstation chair	1	05-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4740	Workstation table	1	05-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4750	Roller blind	1	05-Aug-26	05-Aug-26	100%	100%
DAM3-05-012-4760	Waste Receptacle	1	05-Aug-26	05-Aug-26	100%	100%
Testing & Commissioning		4	02-Aug-26	05-Aug-26	41.5%	100%
DAM3-05-012-4400	Testing & Commissioning - Electrical Systems	2	02-Aug-26	03-Aug-26	43%	100%
DAM3-05-012-4720	Testing & Commissioning - Mechanical Systems	2	04-Aug-26	05-Aug-26	40%	100%
Handing Over		6	30-Jul-26	05-Aug-26	0%	100%
Engineering		6	30-Jul-26	05-Aug-26	0%	100%
As-Built Drawings		5	30-Jul-26	05-Aug-26	0%	100%
DAM3-05-012-422	Prepare & Submit	3	30-Jul-26	03-Aug-26	0%	100%
DAM3-05-012-423	Review & Approve	4	01-Aug-26	05-Aug-26	0%	100%
Operational Spares		4	02-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-424	Prepare & Submit	2	02-Aug-26	03-Aug-26	0%	100%
DAM3-05-012-443	Acceptance	3	03-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-469	Inspection	2	04-Aug-26	05-Aug-26	0%	100%
Warranties and Guarantees		4	02-Aug-26	05-Aug-26	0%	100%

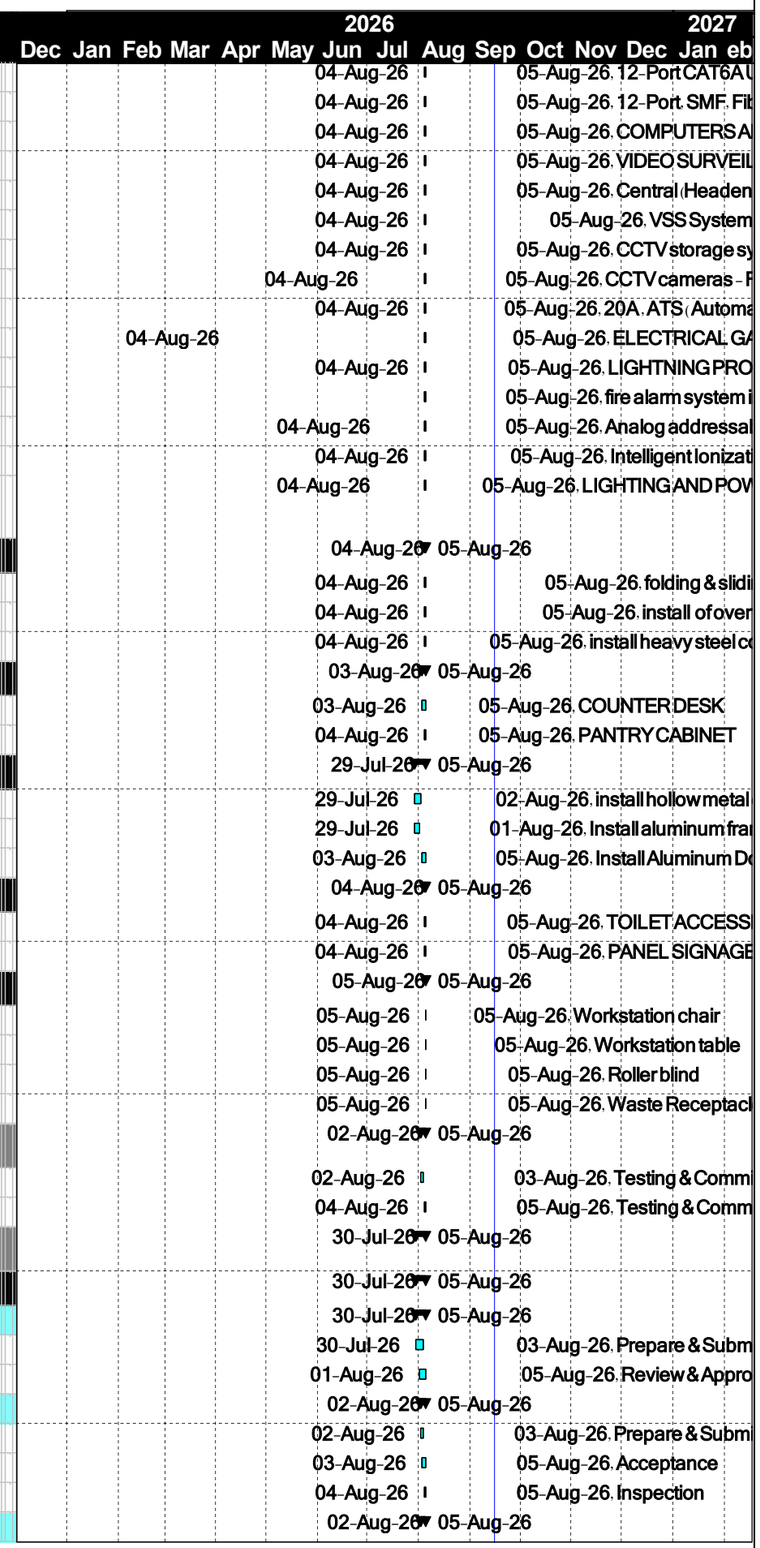

© Oracle Corporation

Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
DAM3-05-012-425	Review & Approve	2	02-Aug-26	03-Aug-26	0%	100%
DAM3-05-012-470	Prepare & Submit	2	04-Aug-26	05-Aug-26	0%	100%
Training and Manuals		4	02-Aug-26	05-Aug-26	0%	100%
Training		4	02-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-441	Prepare & Submit	2	02-Aug-26	03-Aug-26	0%	100%
DAM3-05-012-483	Review & Approve	2	04-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-484	Fabrication & Delivery	2	04-Aug-26	05-Aug-26	0%	100%
Manuals		4	02-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-442	Prepare & Submit	2	02-Aug-26	03-Aug-26	0%	100%
DAM3-05-012-471	Review & Approve	2	04-Aug-26	05-Aug-26	0%	100%
Demobilization		2	04-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-4670	Demobilize	2	04-Aug-26	05-Aug-26	0%	100%
Snaglist Rectification		2	04-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-4680	Snaglist Rectification	2	04-Aug-26	05-Aug-26	0%	100%
DAM3-05-012-4850	Initial Handing Over	1	05-Aug-26	05-Aug-26	0%	100%

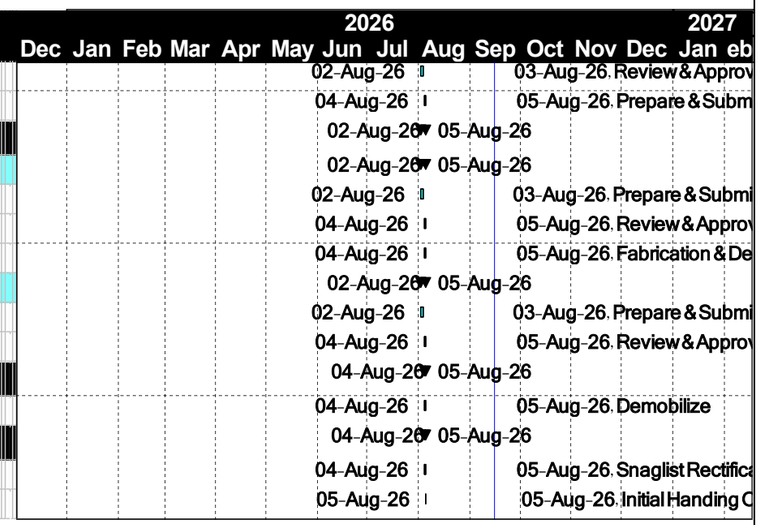

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
