MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oa		257	48.22%	35.97%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	14,463,874.66	10,791,062.05	29,997,851.67	-96
KEY MILESTONES		257	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	0.00	0.00	0.00	-96
GENERAL MILESTONES		257	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-MS-1010	Project Commencement Date	0	100%	100%	03-Mar-26		03-Mar-26 A		0.00	0.00	0.00	0
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		28-Apr-27	0.00	0.00	0.00	-96
CONTRACTUAL MILESTONE		222	0%	0%	28-Mar-26	02-Jan-27	02-Apr-26 A	15-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-MS-1050	Completion of Mobilization	0	100%	100%		02-Apr-26		02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MS-1060	Baseline Programme Approval	0	100%	100%		04-Apr-26		04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		26-Dec-26		15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-MS-1100	Completion of Engineering	0	100%	0%		28-Mar-26		06-Oct-26	0.00	0.00	0.00	-160
MLTX-02-005-MS-1120	Completion of Levelling Works	0	100%	100%		04-Jun-26		02-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-MS-1130	Completion of Toilet Building	0	100%	0%		26-Sep-26		23-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		02-Jan-27		25-Mar-27	0.00	0.00	0.00	-67
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		19-Nov-26		28-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		04-Nov-26		09-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		22-Dec-26		01-Nov-26	0.00	0.00	0.00	44
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		29-Dec-26		13-Apr-27	0.00	0.00	0.00	-86
ARAR		246	32.16%	32.45%	03-Mar-26	02-Jan-27	04-Mar-26 A	15-Apr-27	3,251,318.73	3,280,871.77	10,110,715.45	-85
MOBILIZATION		23	0%	0%	03-Mar-26	01-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
TOPOGRAPHIC SURVEY		4	0%	0%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1320	Site Survey Works	4	100%	100%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
SITE FACILITIES & OFFICES		19	0%	0%	03-Mar-26	28-Mar-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-MB-1340	Site Layout Plan	3	100%	100%	03-Mar-26	05-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-1350	Clear & Grub for Offices & Access Road	3	100%	100%	07-Mar-26	09-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-1360	Construct Site Access Roads	3	100%	100%	07-Mar-26	09-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	-3
MLTX-02-005-MB-1370	Construct Temporary Fence	5	100%	100%	10-Mar-26	15-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-4
MLTX-02-005-MB-1380	Construct Site Offices & Storage	10	100%	100%	10-Mar-26	24-Mar-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-7
MLTX-02-005-MB-1390	Install Project Signs	8	100%	100%	10-Mar-26	18-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	-3
MLTX-02-005-MB-1400	Install Site Facilities	4	100%	100%	16-Mar-26	19-Mar-26	16-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	-4
MLTX-02-005-MB-1410	Electrical Works & Connections	6	100%	100%	16-Mar-26	25-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	-4
MLTX-02-005-MB-1420	Construct Parking Sheds	6	100%	100%	16-Mar-26	25-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	-4
MLTX-02-005-MB-1430	Equipment Mobalization	5	100%	100%	19-Mar-26	28-Mar-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-MB-1440	Manpower Mobalization	3	100%	100%	24-Mar-26	26-Mar-26	24-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-6
PRELIMINARY SUBMITTALS		20	0%	0%	07-Mar-26	01-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
PREPARATIONS & SUBMITTAL BY CONTRACTORS		10	0%	0%	07-Mar-26	17-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-154	Preparation and Submittal of Detailed Work Order	10	100%	100%	07-Mar-26	17-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-155	Preparation and Submittal of Project Execution Plan	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-156	Submission of Contractor Project Quality Plan	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-157	Submission of Construction Safety & Environmental	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-158	Preparation and Submittal of Organization Chart	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-159	Preparation and Submittal of Communication Plan	8	100%	100%	07-Mar-26	15-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-2
APPROVALS BY EMPLOYERS		12	0%	0%	16-Mar-26	01-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-168	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	18-Mar-26	01-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-169	Approval of Project Execution Plan	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-170	Approval of Contractor Project Quality Plan	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-171	Approval of Construction Safety & Environmental	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-172	Approval of Organization Chart	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
MLTX-02-005-MB-173	Approval of Communication Plan	10	100%	100%	16-Mar-26	30-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-2
ENGINEERING		202	0%	0%	07-Mar-26	25-Oct-26	07-Mar-26 A	23-Feb-27	0.00	0.00	0.00	-103
SHOP DRAWINGS		201	0%	0%	08-Mar-26	25-Oct-26	07-Mar-26 A	23-Feb-27	0.00	0.00	0.00	-103
SHOP DRAWINGS SUBMISSION		141	0%	0%	08-Mar-26	29-Jun-26	07-Mar-26 A	14-Dec-26	0.00	0.00	0.00	-143
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		46	0%	0%	08-Mar-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN-1	Shop DWG Submittal for Layout Plan	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-1	Shop DWG Submittal for Setting Out	16	100%	100%	08-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN-1	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-1	Shop DWG Submittal for Standards Details	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		92	0%	0%	08-Mar-26	29-Jun-26	07-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-27
ARCHITECTURE WORKS		46	0%	0%	08-Mar-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40

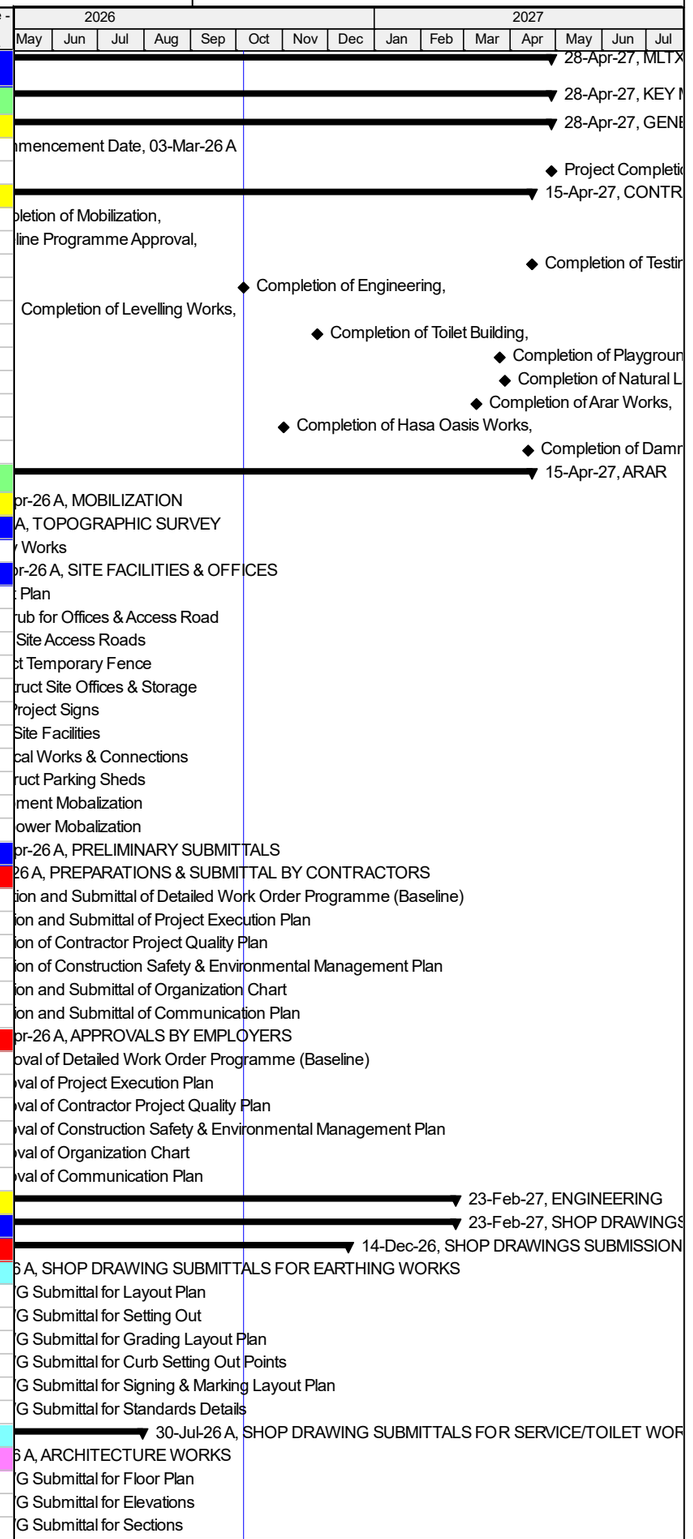

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Shop DWG Submittal for Ceiling Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Finishes Plan	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Toilet Details	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	16-Apr-26	03-May-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	40
STRUCTURE WORKS		21	0%	0%	04-May-26	31-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Shop DWG Submittal for Foundation Plan	15	100%	100%	04-May-26	20-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	50
MLTX-02-005-EM	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	04-May-26	31-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	56
MLTX-02-005-EM	Shop DWG Submittal for Sections/Details	21	100%	100%	04-May-26	31-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	56
MECHANCAL WORKS		30	0%	0%	04-May-26	10-Jun-26	07-Mar-26 A	07-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for HVAC Equipment Schedule	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Drainage Layout	30	100%	100%	04-May-26	10-Jun-26	07-Mar-26 A	07-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Drainage Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EM	Shop DWG Submittal for Dut Routing Layout	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	29
MLTX-02-005-EM	Shop DWG Submittal for Diffusers Layout	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EM	Shop DWG Submittal for Fire Fighting Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Water Supply Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Water Supply Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
ELECTRICAL WORKS		64	0%	0%	04-May-26	29-Jun-26	12-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	30	100%	100%	23-May-26	29-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	81
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	09-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Shop DWG Submittal for Lighting Installation Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Cable Tray Installation Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EM	Shop DWG Submittal for Manhole & Ductbank Details	30	100%	100%	04-May-26	10-Jun-26	12-Mar-26 A	07-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Submittal for Grounding Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection System Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	30	100%	100%	04-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	30	100%	100%	04-May-26	10-Jun-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for Grounding Layout	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	30	100%	100%	04-May-26	10-Jun-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Riser Diagram	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	65
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		141	0%	0%	08-Mar-26	19-May-26	08-Mar-26 A	14-Dec-26	0.00	0.00	0.00	-175
ARCHITECTURE WORKS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EM	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Furniture & Marking	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Shop DWG Submittal for Sections	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Interlock Pattern Plan	30	100%	100%	08-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	30	100%	100%	08-Mar-26	14-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Shop DWG Submittal for Dome Internal Layout	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
STRUCTURE WORKS		45	0%	0%	15-Apr-26	19-May-26	14-Mar-26 A	14-Jul-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EM	Shop DWG Submittal for Air Dome System	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	07-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Foundation of Air Dome	30	100%	100%	15-Apr-26	19-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EM	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	30	100%	100%	15-Apr-26	19-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-45
AIR DOME SYSTEM		30	0%	0%	15-Apr-26	19-May-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for Air Dome Structural Layout	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	07-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Membrane Panel Layout	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for Cable Tension Layout	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for Airlock Door Details	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for Emergency Exit Details	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-4
SPORTS EQUIPMENT		30	0%	0%	15-Apr-26	19-May-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EM	Shop DWG Submittal for Football Turf Installation	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EM	Shop DWG Submittal for Basketball Court Marking	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EM	Shop DWG Submittal for Padel Court Structure	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-5
MECHANCAL WORKS		30	0%	0%	15-Apr-26	19-May-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	14

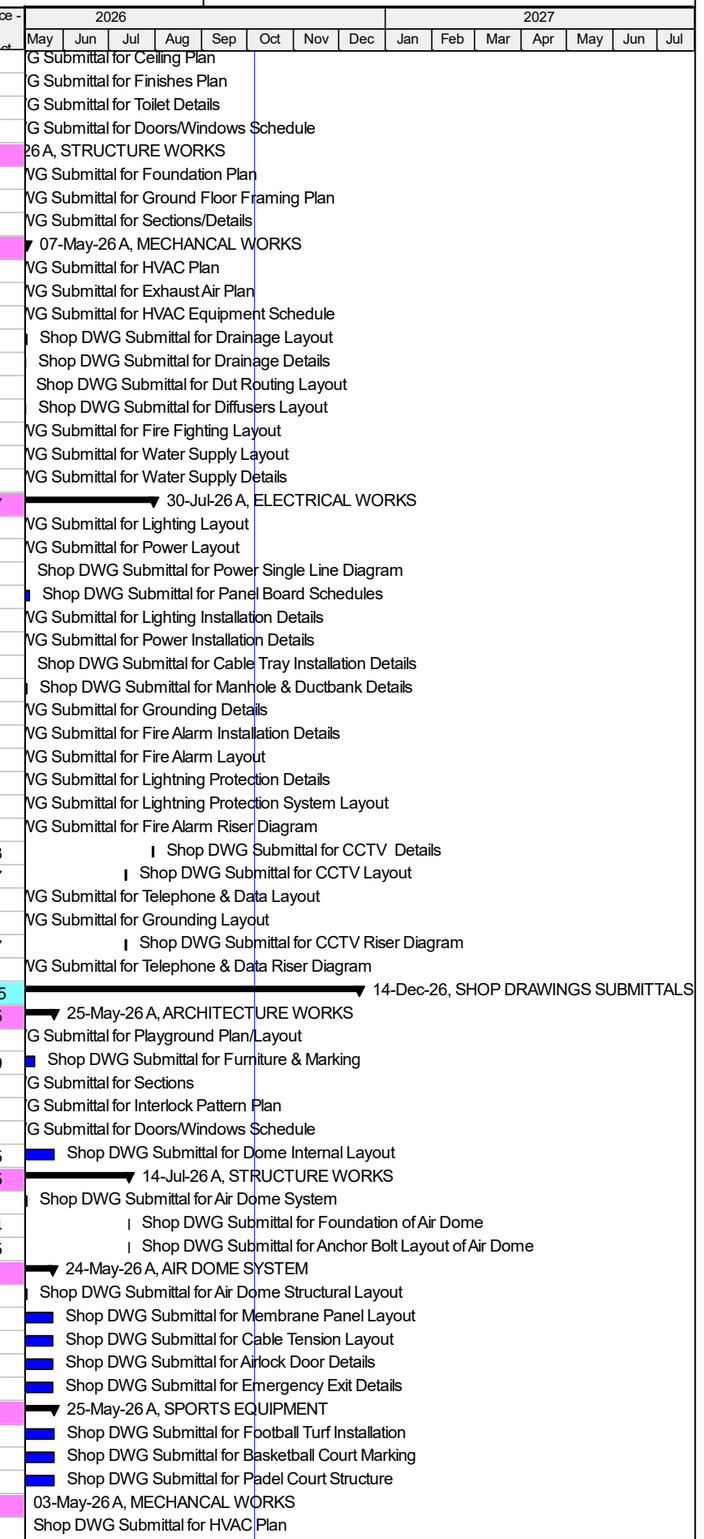


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	03-May-26 A	0.00	0.00	0.00	14
ELECTRICAL WORKS		125	0%	0%	15-Apr-26	19-May-26	14-Mar-26 A	14-Dec-26	0.00	0.00	0.00	-175
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	30	100%	100%	15-Apr-26	19-May-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	30	100%	100%	15-Apr-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	30	100%	100%	15-Apr-26	19-May-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	30	100%	100%	15-Apr-26	19-May-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	30	100%	0%	15-Apr-26	19-May-26	10-Nov-26	14-Dec-26	0.00	0.00	0.00	-175
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	30	100%	100%	15-Apr-26	19-May-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	30	100%	100%	15-Apr-26	19-May-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	30	100%	100%	15-Apr-26	19-May-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-77
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		46	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	13-Jul-26 A	0.00	0.00	0.00	-74
ARCHITECTURE WORKS		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EN	Shop DWG Submittal for Landscape Layout	21	100%	100%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Shop DWG Submittal for Hardscape Plan	21	100%	100%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Shop DWG Submittal for Planting Plan	15	100%	100%	29-Mar-26	14-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EN	Shop DWG Submittal for Landscape Details	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MECHANCAL WORKS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Details	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Layout	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	-40
ELECTRICAL WORKS		30	0%	0%	08-Mar-26	14-Apr-26	12-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	-74
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	08-Mar-26	14-Apr-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	-74
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	08-Mar-26	14-Apr-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	-74
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	08-Mar-26	14-Apr-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-73
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	08-Mar-26	14-Apr-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-73
SHOP DRAWINGS APPROVALS		191	0%	0%	29-Mar-26	25-Oct-26	14-Mar-26 A	23-Feb-27	0.00	0.00	0.00	-103
SHOP DRAWING APPROVAL FOR EARTHING WORKS		47	0%	0%	29-Mar-26	21-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN-2	Shop DWG Approval for Layout Plan	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-2	Shop DWG Approval for Setting Out	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-2	Shop DWG Approval for Grading Layout Plan	16	100%	100%	04-May-26	21-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	46
MLTX-02-005-EN-2	Shop DWG Approval for Curb Setting Out Points	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-2	Shop DWG Approval for Signing & Marking Layout Plan	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-2	Shop DWG Approval for Standards Details	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		107	0%	0%	29-Mar-26	03-Aug-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	3
ARCHITECTURE WORKS		75	0%	0%	29-Mar-26	27-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	74
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	29-Mar-26	02-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	29-Mar-26	02-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	29
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	20-May-26	27-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	74
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	04-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
STRUCTURE WORKS		27	0%	0%	21-May-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN	Shop DWG Approval for Foundation Plan	4	100%	100%	21-May-26	25-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	44
MLTX-02-005-EN	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	01-Jun-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MLTX-02-005-EN	Shop DWG Approval for Sections/Details	21	100%	100%	01-Jun-26	24-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	67
MECHANCAL WORKS		30	0%	0%	11-Jun-26	15-Jul-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	54
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for HVAC Equipment Schedule	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for Drainage Layout	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	09-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Drainage Details	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	09-May-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Duct Routing Layout	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	54
MLTX-02-005-EN	Shop DWG Approval for Diffusers Layout	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	10-May-26 A	0.00	0.00	0.00	54
MLTX-02-005-EN	Shop DWG Approval for Fire Fighting Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for Water Supply Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for Water Supply Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
ELECTRICAL WORKS		106	0%	0%	11-Jun-26	03-Aug-26	18-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	30	100%	100%	30-Jun-26	03-Aug-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	101
MLTX-02-005-EN	Shop DWG Approval for Power Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	58
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	30	100%	100%	11-Jun-26	15-Jul-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-1

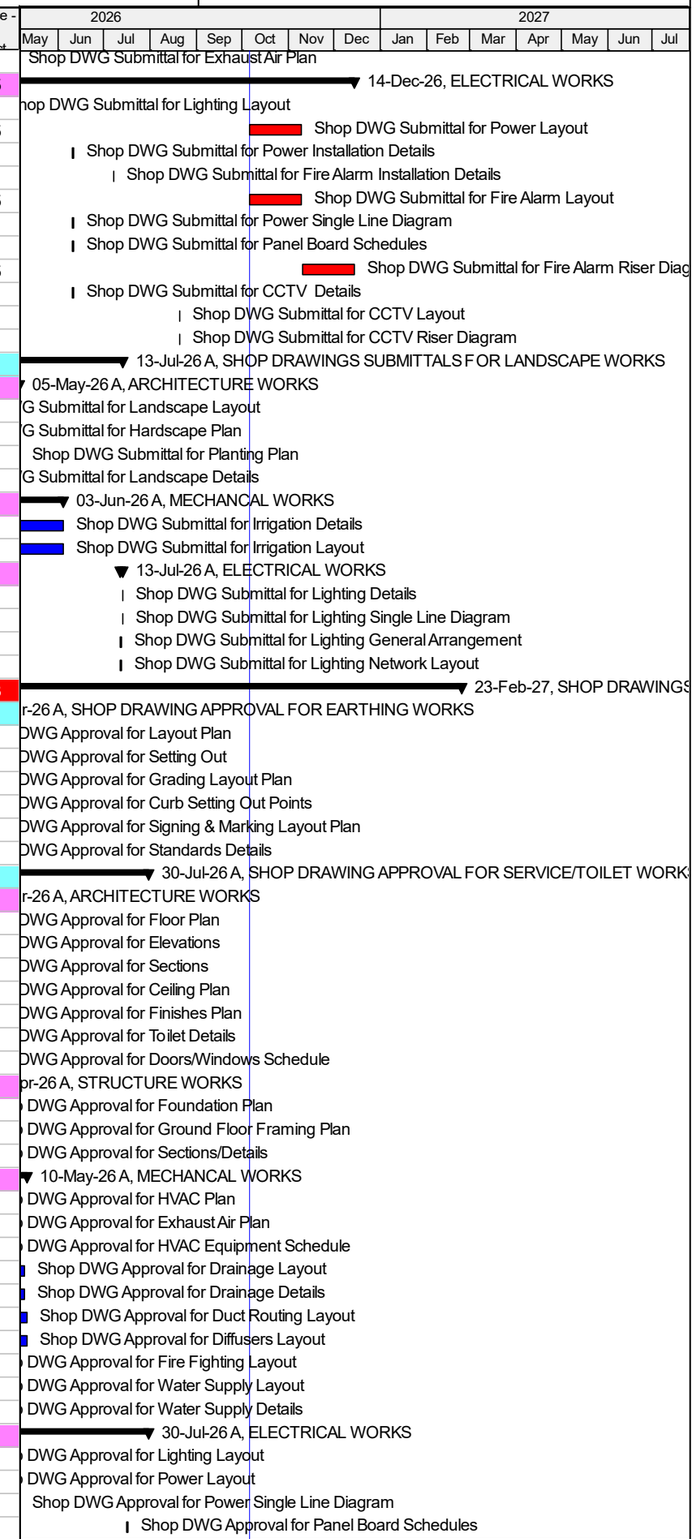

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Shop DWG Approval for Lighting Installation Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Cable Tray Installation Details	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	58
MLTX-02-005-EM	Shop DWG Approval for Manhole & Ductbank Details	30	100%	100%	11-Jun-26	15-Jul-26	18-Mar-26 A	05-May-26 A	0.00	0.00	0.00	58
MLTX-02-005-EM	Shop DWG Approval for Grounding Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Fire Alarm Installation Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Fire Alarm Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Lightning Protection Details	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Lightning Protection System Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Fire Alarm Riser Diagram	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for CCTV Details	30	100%	100%	11-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EM	Shop DWG Approval for CCTV Layout	30	100%	100%	11-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EM	Shop DWG Approval for Telephone & Data Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for Grounding Layout	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
MLTX-02-005-EM	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	11-Jun-26	15-Jul-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EM	Shop DWG Approval for Telephone & Data Riser Diagram	30	100%	100%	11-Jun-26	15-Jul-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	85
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		186	0%	0%	29-Mar-26	25-Oct-26	14-Mar-26 A	23-Feb-27	0.00	0.00	0.00	-103
ARCHITECTURE WORKS		96	0%	0%	29-Mar-26	09-Jun-26	14-Mar-26 A	09-Nov-26	0.00	0.00	0.00	-130
MLTX-02-005-EM	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Shop DWG Approval for Furniture & Marking	30	100%	100%	29-Mar-26	02-May-26	14-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Approval for Sections	15	100%	100%	29-Mar-26	14-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Shop DWG Approval for Interlock Pattern Plan	30	100%	100%	15-Apr-26	19-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	15-Apr-26	19-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Shop DWG Approval for Dome Internal Layout	30	100%	0%	03-May-26	09-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-130
STRUCTURE WORKS		45	0%	0%	20-May-26	27-Jun-26	19-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EM	Shop DWG Approval for Air Dome System	30	100%	100%	20-May-26	27-Jun-26	19-Mar-26 A	09-May-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Shop DWG Approval for Foundation of Air Dome	30	100%	100%	20-May-26	27-Jun-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EM	Shop DWG Approval for Foundation of Air Dome	30	100%	100%	20-May-26	27-Jun-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EM	Shop DWG Approval for Anchor Bolt Layout of Air Dome	30	100%	100%	20-May-26	27-Jun-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-17
AIR DOME SYSTEM		111	0%	0%	20-May-26	27-Jun-26	19-Mar-26 A	18-Jan-27	0.00	0.00	0.00	-175
MLTX-02-005-EM	Shop DWG Approval for Air Dome Structural Layout	30	100%	100%	20-May-26	27-Jun-26	19-Mar-26 A	09-May-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Shop DWG Approval for Membrane Panel Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Cable Tension Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Airlock Door Details	30	100%	0%	20-May-26	27-Jun-26	10-Nov-26	14-Dec-26	0.00	0.00	0.00	-145
MLTX-02-005-EM	Shop DWG Approval for Emergency Exit Details	30	100%	0%	20-May-26	27-Jun-26	15-Dec-26	18-Jan-27	0.00	0.00	0.00	-175
SPORTS EQUIPMENT		173	0%	0%	20-May-26	27-Jun-26	20-Jul-26 A	23-Feb-27	0.00	0.00	0.00	-205
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	30	100%	0%	20-May-26	27-Jun-26	19-Jan-27	23-Feb-27	0.00	0.00	0.00	-205
MLTX-02-005-EM	Shop DWG Approval for Basketball Court Marking	30	100%	100%	20-May-26	27-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-51
MLTX-02-005-EM	Shop DWG Approval for Padel Court Structure	30	100%	100%	20-May-26	27-Jun-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	-20
MECHANCAL WORKS		60	0%	0%	20-May-26	01-Aug-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	73
MLTX-02-005-EM	Shop DWG Approval for HVAC Plan	30	100%	100%	20-May-26	27-Jun-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	43
MLTX-02-005-EM	Shop DWG Approval for Exhaust Air Plan	30	100%	100%	28-Jun-26	01-Aug-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	73
ELECTRICAL WORKS		169	0%	0%	20-May-26	25-Oct-26	13-Jun-26 A	03-Feb-27	0.00	0.00	0.00	-87
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	15	100%	0%	20-May-26	09-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Power Layout	30	100%	0%	02-Aug-26	05-Sep-26	15-Dec-26	18-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	14	100%	0%	06-Sep-26	21-Sep-26	19-Jan-27	03-Feb-27	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Power Single Line Diagram	30	100%	100%	20-May-26	27-Jun-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EM	Shop DWG Approval for Panel Board Schedules	20	100%	100%	20-May-26	15-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	2
MLTX-02-005-EM	Shop DWG Approval for CCTV Details	25	44%	100%	22-Sep-26	21-Oct-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	48
MLTX-02-005-EM	Shop DWG Approval for CCTV Layout	3	0%	100%	22-Oct-26	25-Oct-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	20-May-26	27-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-51
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		41	0%	0%	29-Mar-26	01-Aug-26	15-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	13
ARCHITECTURE WORKS		36	0%	0%	29-Mar-26	09-May-26	15-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Approval for Landscape Layout	21	100%	100%	15-Apr-26	09-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EM	Shop DWG Approval for Hardscape Plan	21	100%	100%	05-Apr-26	28-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EM	Shop DWG Approval for Planting Plan	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EM	Shop DWG Approval for Landscape Details	21	100%	100%	29-Mar-26	21-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	20
MECHANCAL WORKS		30	0%	0%	15-Apr-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Shop DWG Approval for Irrigation Details	30	100%	100%	15-Apr-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Shop DWG Approval for Irrigation Layout	30	100%	100%	15-Apr-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
ELECTRICAL WORKS		30	0%	0%	15-Apr-26	01-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Shop DWG Approval for Lighting Details	30	100%	100%	15-Apr-26	19-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EM	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	28-Jun-26	01-Aug-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	15-Apr-26	19-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-47

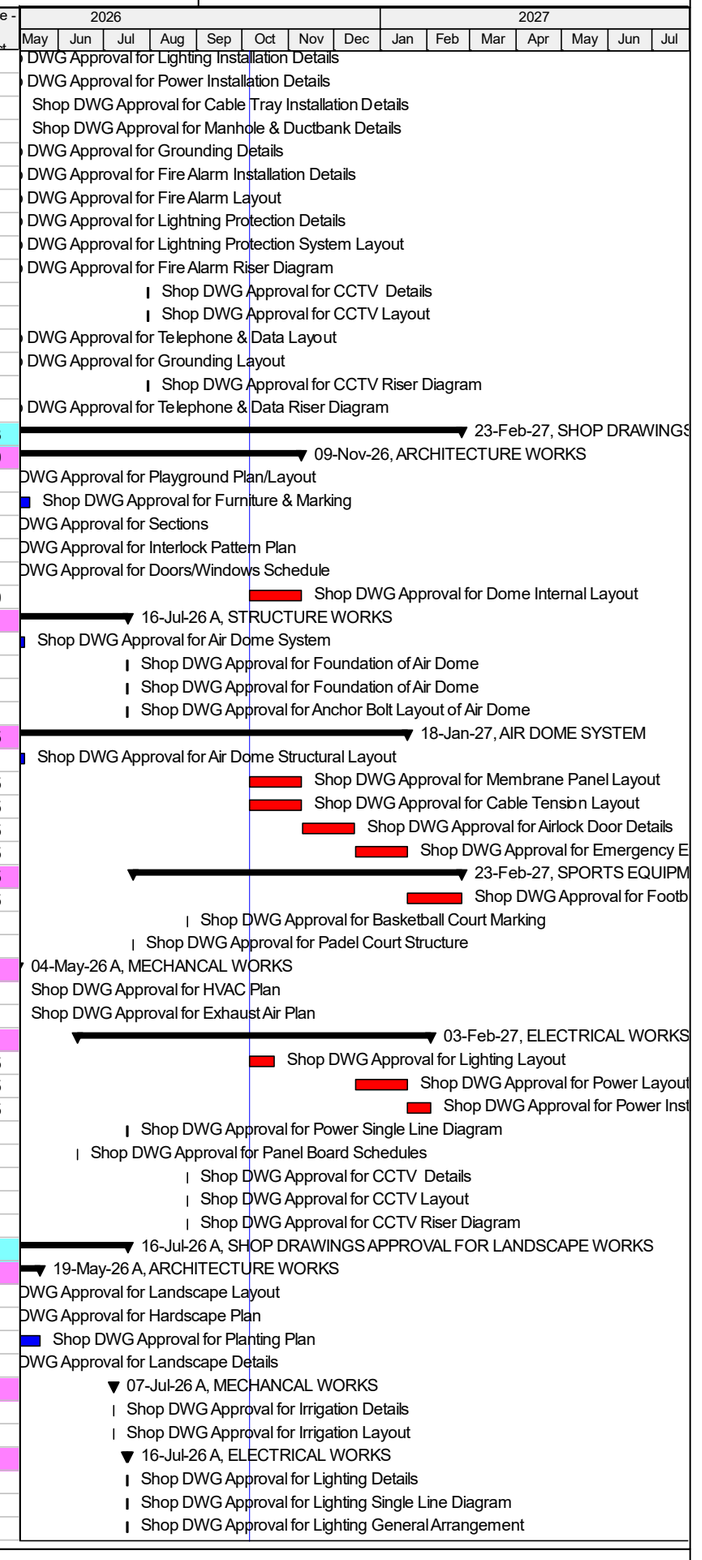

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	15-Apr-26	19-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-47
METHOD STATEMENTS		97	0%	0%	07-Mar-26	20-Jul-26	07-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-46
METHOD STATEMENT SUBMITTAL		80	0%	0%	07-Mar-26	14-Jun-26	07-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	8
CIVIL WORKS		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Concrete	30	100%	100%	07-Mar-26	13-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	21	100%	100%	07-Mar-26	02-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	14
ARCHITECTURE WORKS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Plastering	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Tilling	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	17-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Parking	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Soft	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Fence	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Metal	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Partitions	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Gypsum	30	100%	100%	07-Mar-26	13-Apr-26	07-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-40
MECHANICAL WORKS		45	0%	0%	28-Mar-26	18-May-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	28-Mar-26	30-Apr-26	12-Mar-26 A	02-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Water	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	02-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Fire	30	100%	100%	04-Apr-26	07-May-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for HVAC	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-12
ELECTRICAL WORKS		50	0%	0%	14-Apr-26	14-Jun-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for CCTV	30	100%	100%	07-May-26	14-Jun-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Lighting	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Panel	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Electrical	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN-4	Preparation & Submission of Method Statement for Lighting	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
METHOD STATEMENT APPROVAL		82	0%	0%	28-Mar-26	20-Jul-26	12-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-46
CIVIL WORKS		45	0%	0%	28-Mar-26	18-May-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-4	Approval of Method Statement for Earthwork	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN-4	Approval of Method Statement for Concrete Works	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-4	Approval of Method Statement for Waterproofing	21	100%	100%	04-Apr-26	27-Apr-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-3
ARCHITECTURE WORKS		80	0%	0%	28-Mar-26	18-May-26	12-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN-4	Approval of Method Statement for Plastering Works	30	100%	100%	28-Mar-26	30-Apr-26	12-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN-4	Approval of Method Statement for Masonary Works	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN-4	Approval of Method Statement for Tilling Works	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN-4	Approval of Method Statement for Seats/Benches Works	30	100%	100%	14-Apr-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN-4	Approval of Method Statement for Doors/Windows Works	30	100%	100%	14-Apr-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN-4	Approval of Method Statement for Interlock/Curbstone Works	30	100%	100%	14-Apr-26	18-May-26	12-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN-4	Approval of Method Statement for Parking Works	30	100%	100%	14-Apr-26	18-May-26	20-May-26 A	20-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN-4	Approval of Method Statement for Soft Scape Works	30	100%	100%	14-Apr-26	18-May-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	-50
MLTX-02-005-EN-4	Approval of Method Statement for Fence Works	20	100%	100%	14-Apr-26	06-May-26	19-Jul-26 A	19-Jul-26 A	0.00	0.00	0.00	-60
MLTX-02-005-EN-4	Approval of Method Statement for Air Dome Works	30	100%	100%	14-Apr-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EN-4	Approval of Method Statement for Partitions Works	30	100%	100%	14-Apr-26	18-May-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN-4	Approval of Method Statement for Gypsum Board Works	30	100%	100%	14-Apr-26	18-May-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-78
MECHANICAL WORKS		63	0%	0%	14-Apr-26	25-Jun-26	14-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	-53
MLTX-02-005-EN-4	Approval of Method Statement for Sewage/Drainage System	30	100%	100%	02-May-26	08-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN-4	Approval of Method Statement for Water Supply System	30	100%	100%	19-May-26	25-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Approval of Method Statement for Fire Fighting System	30	100%	100%	09-May-26	15-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-62
MLTX-02-005-EN-4	Approval of Method Statement for Irrigation System	15	100%	100%	14-Apr-26	30-Apr-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN-4	Approval of Method Statement for HVAC System	30	100%	100%	19-May-26	25-Jun-26	14-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-23
ELECTRICAL WORKS		80	0%	0%	19-May-26	20-Jul-26	06-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN-4	Approval of Method Statement for Electrical Conduits/Pulling	30	100%	100%	19-May-26	25-Jun-26	06-Jun-26 A	06-Jun-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN-4	Approval of Method Statement for Lighting Poles Installation	30	100%	100%	19-May-26	25-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Approval of Method Statement for Telecommunication & Data	30	100%	100%	19-May-26	25-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Approval of Method Statement for CCTV System	30	100%	100%	15-Jun-26	19-Jul-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	30

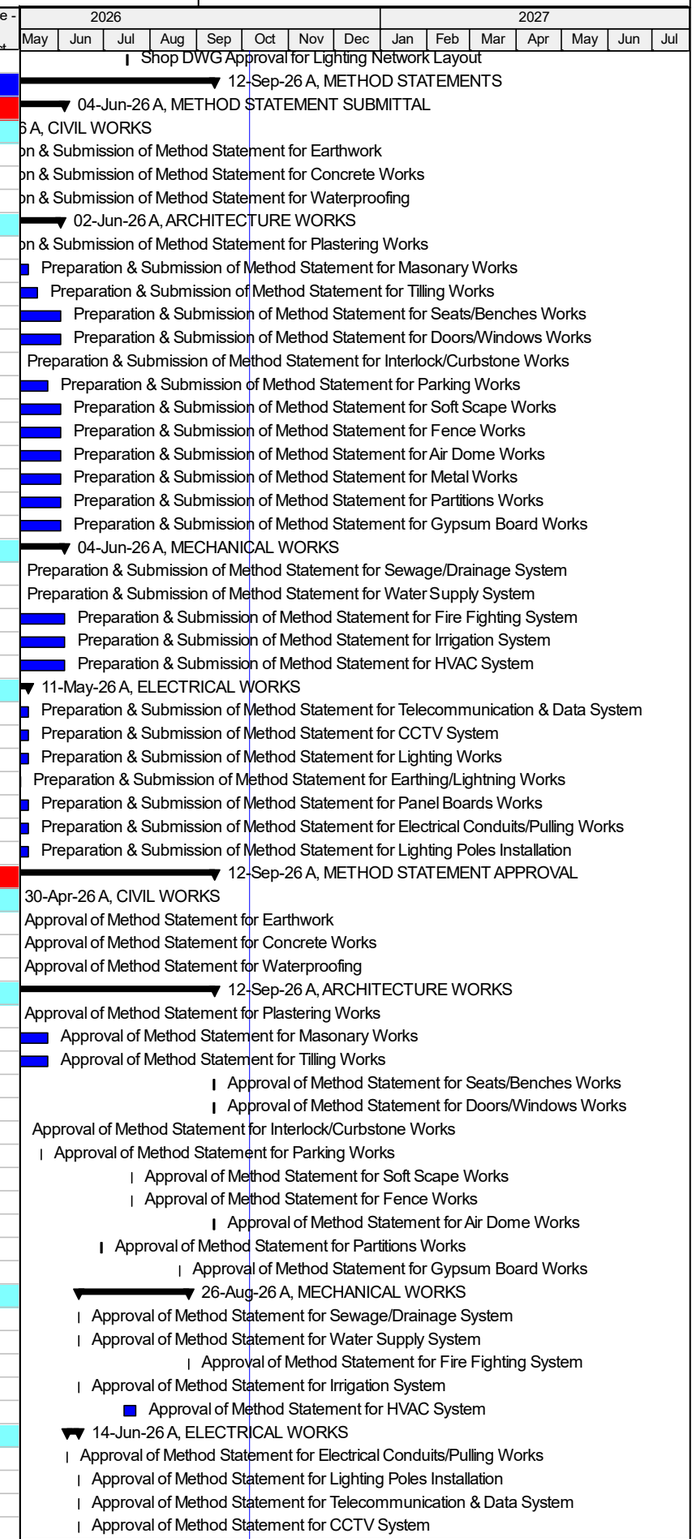

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-4	Approval of Method Statement for Lighting Works	30	100%	100%	10-Jun-26	14-Jul-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN-4	Approval of Method Statement for Earthing/Lightning Works	30	100%	100%	19-May-26	25-Jun-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-4	Approval of Method Statement for Panel Boards Works	30	100%	100%	16-Jun-26	20-Jul-26	14-Jun-26 A	14-Jun-26 A	0.00	0.00	0.00	31
PRE-QUALIFICATION & MATERIAL		105	0%	0%	07-Mar-26	13-Jul-26	07-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-52
PRE-QUALIFICATION		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
TOILET/SERVICE WORKS		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
STEEL REINFORCEMENT		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
READY MIX CONCRETE		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
CONCRETE BLOCKS		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
WATER PROOFING		45	0%	0%	07-Mar-26	30-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	30	100%	100%	28-Mar-26	30-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	33
FLOOR/WALL TILES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	5
SUSPENDED CEILING		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
DOORS/WINDOWS		30	0%	0%	07-Mar-26	13-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	07-Mar-26	26-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	18
FURNITURES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	5
SANITARY FIXTURES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	05-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	3
WATER SUPPLY PIPES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
SEWAGE/DRAINAGE PIPES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	23-Mar-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	13
PACKAGE AC UNITS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
AIR DIFUSSERS/GRILLS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
GALVANIZED DUCTS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
LIGHTING FIXTURES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
SWITCHES/SOCKETS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
EARTHING SYSTEM		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Pre-Qualification Submittal for Earthing System	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Approval for Earthing System	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
DISTRIBUTION PANNELS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Panels	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-5
PLAYGROUND WORKS		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29

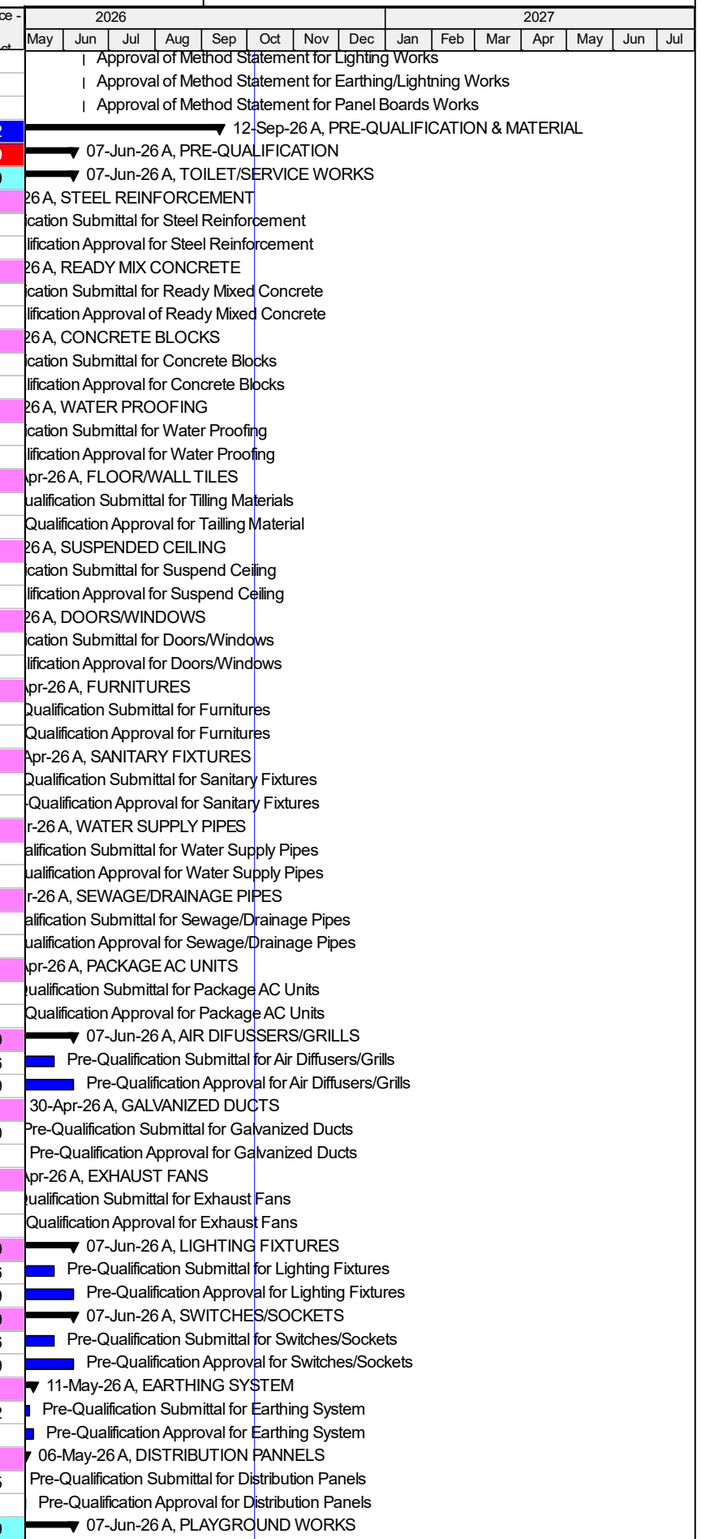


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PVC MEMBRANE		36	0%	0%	07-Mar-26	20-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EI	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-50
MLTX-02-005-EI	Pre-Qualification Approval for PVC Membrane	21	100%	100%	28-Mar-26	20-Apr-26	10-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-26
STEEL TENSION CABLES		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EI	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
EMERGENCY DOORS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EI	Pre-Qualification Approval for Emergency Doors	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
PRESSURE UNITS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Submittal for Pressure Units	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EI	Pre-Qualification Approval for Pressure Units	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
AIR LOCK DOORS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Submittal for Lock Doors	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EI	Pre-Qualification Approval for Lock Doors	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-35
ARTIFICIAL TURF		45	0%	0%	07-Mar-26	30-Apr-26	07-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
MLTX-02-005-EI	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EI	Pre-Qualification Approval for Artificial TURF	30	100%	100%	28-Mar-26	30-Apr-26	10-Mar-26 A	09-Apr-26 A	0.00	0.00	0.00	18
RUBBER GRANULES		36	0%	0%	07-Mar-26	20-Apr-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EI	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Rubber Granules	21	100%	100%	28-Mar-26	20-Apr-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-17
PADEL GLASS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EI	Pre-Qualification Submittal for Padel Glass	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Padel Glass	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-23
PADEL WIRE MESH/STEEL SETS		30	0%	0%	07-Mar-26	13-Apr-26	07-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EI	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-23
AGGREGATE BASE COURSE		36	0%	0%	07-Mar-26	20-Apr-26	07-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EI	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	07-Mar-26	26-Mar-26	07-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EI	Pre-Qualification Approval for Aggregate Base Course	21	100%	100%	28-Mar-26	20-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-5
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	4
MLTX-02-005-EI	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EI	Pre-Qualification Approval for the Site	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	4
INTERLOCKING PAVING		30	0%	0%	28-Mar-26	30-Apr-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
MLTX-02-005-EI	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	22
MLTX-02-005-EI	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	14-Apr-26	30-Apr-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
MARKING PAINT		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EI	Pre-Qualification Submittal for Marking Paint	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EI	Pre-Qualification Approval for Marking Paint	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
PACKAGE AC UNITS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Pre-Qualification Submittal for Package AC Units	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EI	Pre-Qualification Approval for Package AC Units	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
AIR DIFUSSERS/GRILLS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EI	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EI	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
GALVANIZED DUCTS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EI	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EI	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
EXHAUST FANS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
MLTX-02-005-EI	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	10
MLTX-02-005-EI	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	08-Apr-26 A	0.00	0.00	0.00	19
DISTRIBUTION BOARDS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EI	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EI	Pre-Qualification Approval for Distribution Boards	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
POWER CABLES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EI	Pre-Qualification Submittal for Power Cables	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Pre-Qualification Approval for Power Cables	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
LIGHT FIXTURES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EI	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EI	Pre-Qualification Approval for Light Fixtures	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
CCTV MATERIALS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EI	Pre-Qualification Submittal for CCTV	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EI	Pre-Qualification Approval for CCTV	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
POWER OUTLETS/SWITCHES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29

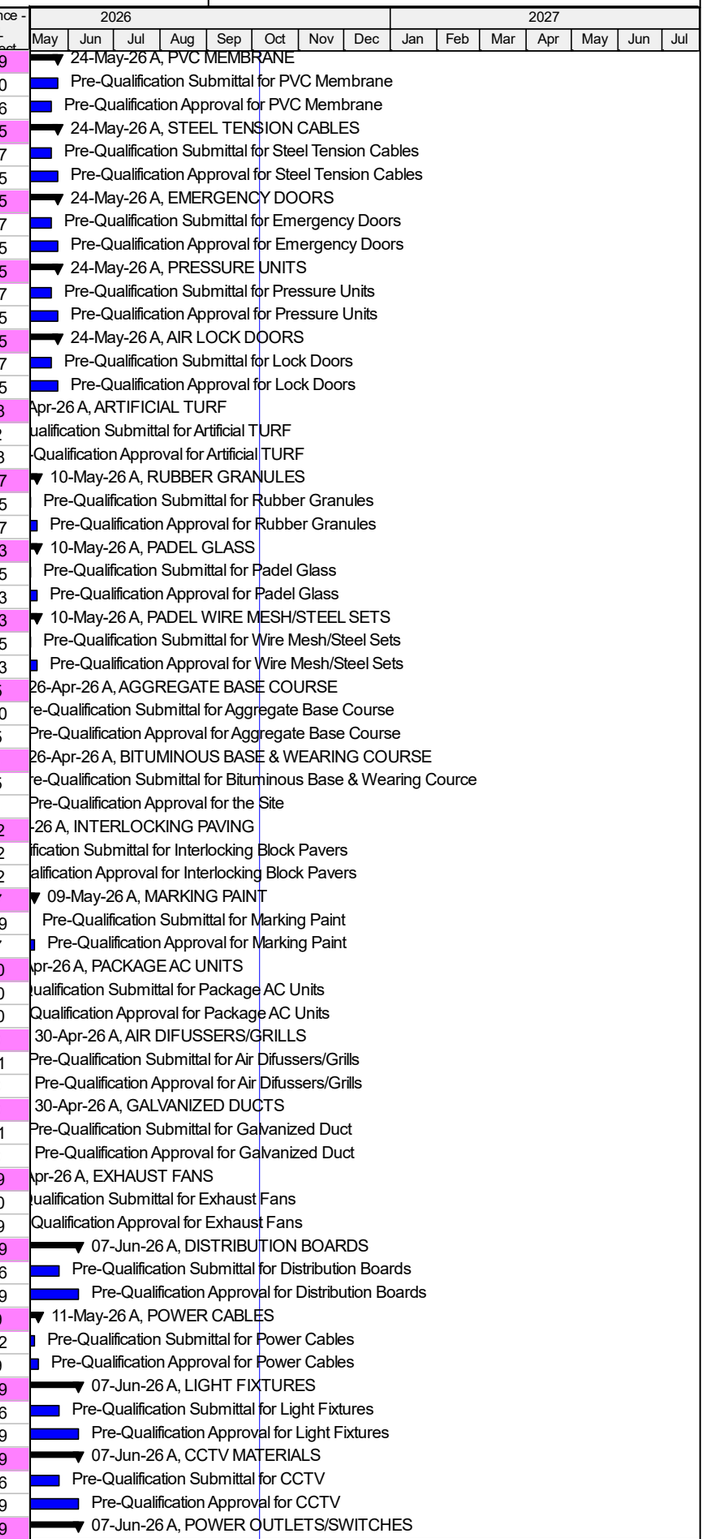

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-29
LANDSCAPE WORKS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
INTERLOCKING PAVING		30	0%	0%	28-Mar-26	30-Apr-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	14-Apr-26	30-Apr-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
CURBSTONE		30	0%	0%	28-Mar-26	30-Apr-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	28-Mar-26	13-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	14-Apr-26	30-Apr-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	32
PAVEMENT MARKING		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
TRAFFIC SIGNS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-7
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
AGRICULTURE SOIL		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
TRACK SURFACE		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
GRASS/TREES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-4
CABLES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-9
LIGHT POLES		30	0%	0%	28-Mar-26	30-Apr-26	10-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	28-Mar-26	13-Apr-26	10-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	14-Apr-26	30-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	0
MATERIAL SUBMITTAL & APPROVAL		94	0%	0%	14-Apr-26	13-Jul-26	18-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-52
TOILET/SERVICE WORKS		64	0%	0%	14-Apr-26	08-Jun-26	18-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
STEEL REINFORCEMENT		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
READY MIX CONCRETE		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
CONCRETE BLOCKS		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Material Approval for Concrete Blocks	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
FLOOR/WALL TILES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	17-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Material Submittal for Tilling Materials	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN	Material Approval for Tilling Material	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	17-May-26 A	0.00	0.00	0.00	1
SUSPENDED CEILING		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Material Submittal for Suspend Ceiling	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	15-Apr-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Material Approval for Suspend Ceiling	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	19-Apr-26 A	0.00	0.00	0.00	25
DOORS/WINDOWS		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Material Submittal for Doors/Windows	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Material Approval for Doors/Windows	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	31
FURNITURES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Material Submittal for Furnitures	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Material Approval for Furnitures	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	35
SANITARY FIXTURES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Material Submittal for Sanitary Fixtures	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	13-Apr-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Material Approval for Sanitary Fixtures	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
WATER SUPPLY PIPES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Material Submittal for Water Supply Pipes	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Material Approval for Water Supply Pipes	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
SEWAGE/DRAINAGE PIPES		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	23

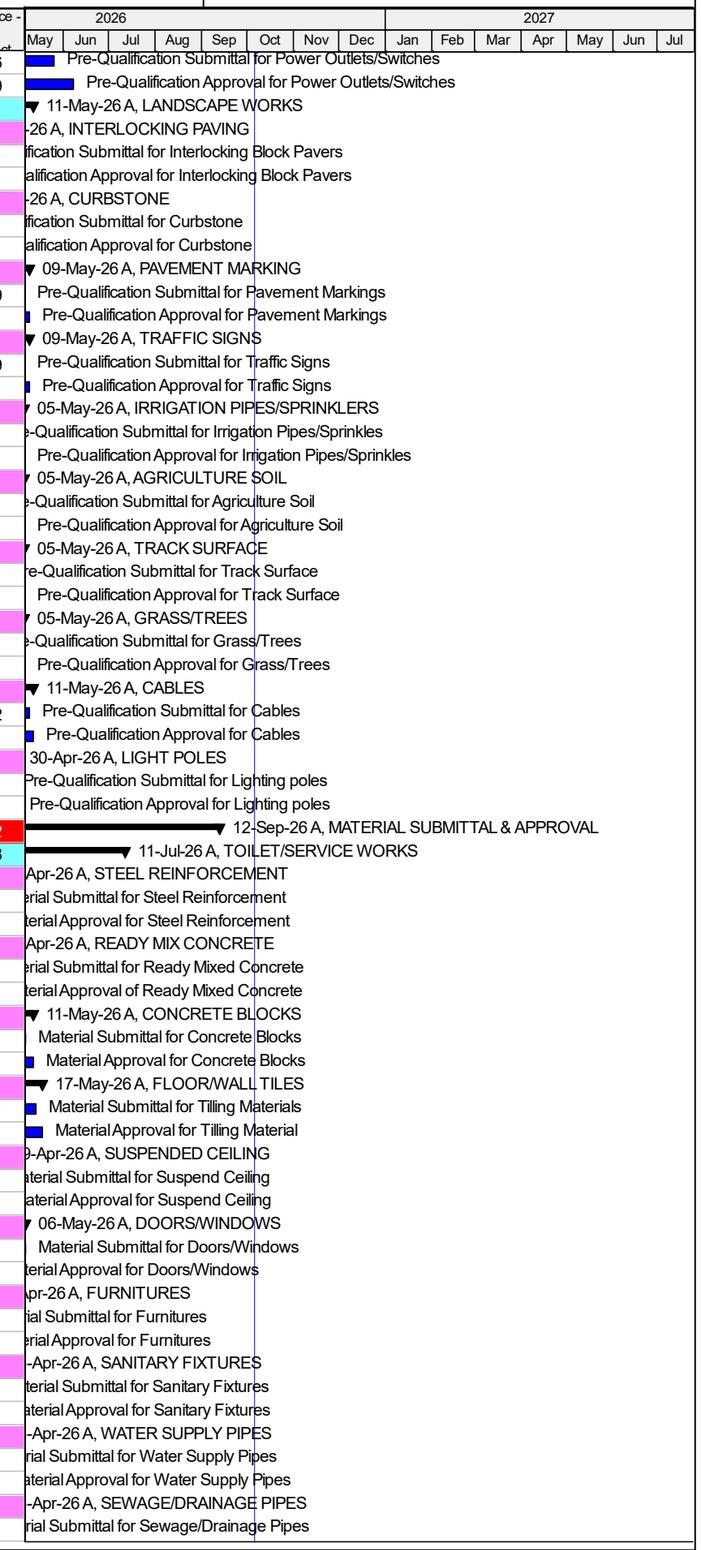


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Sewage/Drainage Pipes	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	16-Apr-26 A	0.00	0.00	0.00	27
PACKAGE AC UNITS		30	0%	0%	02-May-26	08-Jun-26	21-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	02-May-26	18-May-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	19-May-26	08-Jun-26	02-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	-21
AIR DIFUSSERS/GRILLS		30	0%	0%	02-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Material Submittal for Air Diffusers/Grills	15	100%	100%	02-May-26	18-May-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EM	Material Approval for Air Diffusers/Grills	15	100%	100%	19-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
GALVANIZED DUCTS		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Galvanized Ducts	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Material Approval for Galvanized Ducts	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
EXHAUST FANS		30	0%	0%	02-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	02-May-26	18-May-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	19-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
LIGHTING FIXTURES		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Lighting Fixtures	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Lighting Fixtures	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
SWITCHES/SOCKETS		30	0%	0%	02-May-26	08-Jun-26	25-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EM	Material Submittal for Switches/Sockets	15	100%	100%	02-May-26	18-May-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EM	Material Approval for Switches/Sockets	15	100%	100%	19-May-26	08-Jun-26	27-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-16
EARTHING SYSTEM		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Earthing System	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Earthing System	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
DISTRIBUTION PANNELS		43	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Submittal for Distribution Panels	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EM	Material Approval for Distribution Panels	15	100%	100%	19-May-26	08-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
PLAYGROUND WORKS		94	0%	0%	14-Apr-26	13-Jul-26	18-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-52
PVC MEMBRANE		42	0%	0%	21-Apr-26	11-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-65
MLTX-02-005-EM	Material Submittal for PVC Membrane	21	100%	100%	21-Apr-26	14-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-86
MLTX-02-005-EM	Material Approval for PVC Membrane	21	100%	100%	16-May-26	11-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-65
STEEL TENSION CABLES		30	0%	0%	14-Apr-26	18-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-83
MLTX-02-005-EM	Material Submittal for Steel Tension Cables	15	100%	100%	14-Apr-26	30-Apr-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Material Approval for Steel Tension Cables	15	100%	100%	02-May-26	18-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-83
EMERGENCY DOORS		28	0%	0%	14-Apr-26	18-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Submittal for Emergency Doors	15	100%	100%	14-Apr-26	30-Apr-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Material Approval for Emergency Doors	15	100%	100%	02-May-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
PRESSURE UNITS		30	0%	0%	14-Apr-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Submittal for Pressure Units	15	100%	100%	14-Apr-26	30-Apr-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-112
MLTX-02-005-EM	Material Approval for Pressure Units	15	100%	100%	02-May-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
AIR LOCK DOORS		28	0%	0%	14-Apr-26	18-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Submittal for Lock Doors	15	100%	100%	14-Apr-26	30-Apr-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Material Approval for Lock Doors	15	100%	100%	02-May-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
ARTIFICIAL TURF		60	0%	0%	02-May-26	13-Jul-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	44
MLTX-02-005-EM	Material Submittal for Artificial TURF	30	100%	100%	02-May-26	08-Jun-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EM	Material Approval for Artificial TURF	30	100%	100%	09-Jun-26	13-Jul-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	44
RUBBER GRANULES		42	0%	0%	21-Apr-26	11-Jun-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Submittal for Rubber Granules	21	100%	100%	21-Apr-26	14-May-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	0
MLTX-02-005-EM	Material Approval for Rubber Granules	21	100%	100%	16-May-26	11-Jun-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	17
PADEL GLASS		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-1
PADEL WIRE MESH/STEEL SETS		30	0%	0%	14-Apr-26	18-May-26	18-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	14-Apr-26	30-Apr-26	18-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	02-May-26	18-May-26	25-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-1
AGGREGATE BASE COURSE		42	0%	0%	21-Apr-26	11-Jun-26	18-Mar-26 A	03-May-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	21	100%	100%	21-Apr-26	14-May-26	18-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Approval for Aggregate Base Course	21	100%	100%	16-May-26	11-Jun-26	25-Mar-26 A	03-May-26 A	0.00	0.00	0.00	31
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	04-May-26 A	0.00	0.00	0.00	27
INTERLOCKING PAVING		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MARKING PAINT		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	4

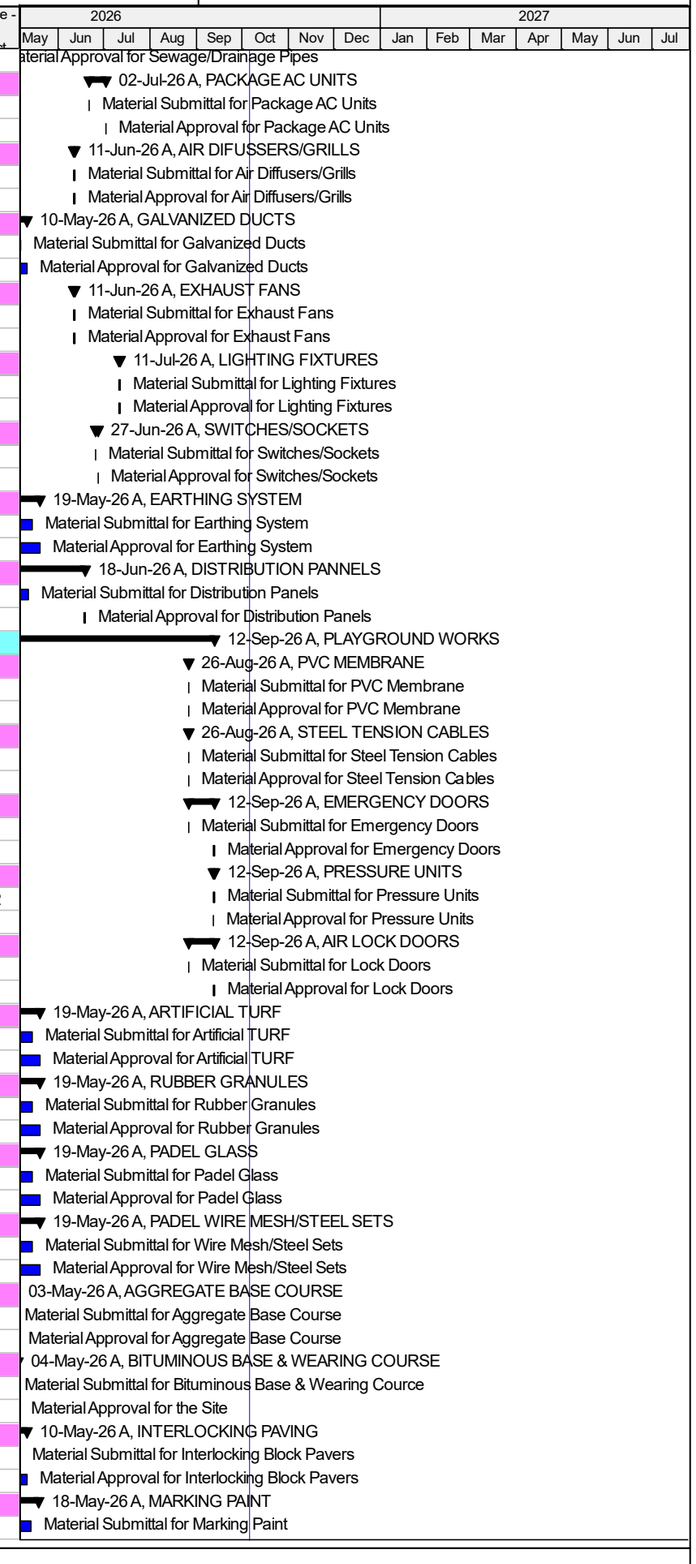

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
PACKAGE AC UNITS		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
AIR DIFUSSERS/GRILLS		30	0%	0%	02-May-26	08-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	02-May-26	18-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	19-May-26	08-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-82
GALVANIZED DUCTS		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
EXHAUST FANS		30	0%	0%	02-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	02-May-26	18-May-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	19-May-26	08-Jun-26	11-Jun-26 A	11-Jun-26 A	0.00	0.00	0.00	-3
DISTRIBUTION BOARDS		30	0%	0%	02-May-26	08-Jun-26	15-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	02-May-26	18-May-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	19-May-26	08-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
POWER CABLES		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
LIGHT FIXTURES		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
CCTV MATERIALS		28	0%	0%	02-May-26	08-Jun-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	02-May-26	18-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-83
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	19-May-26	08-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-82
POWER OUTLETS/SWITCHES		30	0%	0%	02-May-26	08-Jun-26	25-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	02-May-26	18-May-26	25-Jun-26 A	25-Jun-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	19-May-26	08-Jun-26	27-Jun-26 A	27-Jun-26 A	0.00	0.00	0.00	-16
LANDSCAPE WORKS		64	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
INTERLOCKING PAVING		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	22
CURBSTONE		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	21
PAVEMENT MARKING		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
TRAFFIC SIGNS		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	18-May-26 A	0.00	0.00	0.00	15
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	02-May-26	08-Jun-26	16-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	02-May-26	18-May-26	16-Jun-26 A	16-Jun-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EM	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	19-May-26	08-Jun-26	18-Jun-26 A	18-Jun-26 A	0.00	0.00	0.00	-9
AGRICULTURE SOIL		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	21-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Submittal for Agriculture Soil	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Agriculture Soil	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	21-May-26 A	0.00	0.00	0.00	12
TRACK SURFACE		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Track Surface	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Track Surface	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
GRASS/TREES		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	21-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Submittal for Grass/Trees	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Grass/Trees	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	21-May-26 A	0.00	0.00	0.00	12
CABLES		30	0%	0%	02-May-26	08-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Cables	15	100%	100%	02-May-26	18-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EM	Material Approval for Cables	15	100%	100%	19-May-26	08-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	14
LIGHT POLES		30	0%	0%	02-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EM	Material Submittal for Lighting poles	15	100%	100%	02-May-26	18-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Approval for Lighting poles	15	100%	100%	19-May-26	08-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-28
PROCUREMENT		189	0%	0%	19-May-26	22-Nov-26	02-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-77
SHORT LEAD ITEM		189	0%	0%	19-May-26	19-Oct-26	02-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-106
TOILET/SERVICE WORKS		100	0%	0%	19-May-26	09-Aug-26	02-Apr-26 A	08-Nov-26	0.00	0.00	0.00	-77
STEEL REINFORCEMENT		54	0%	0%	19-May-26	02-Jun-26	02-Apr-26 A	24-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-PR-7	PO for Steel Reinforcement	5	100%	100%	19-May-26	24-May-26	02-Apr-26 A	10-May-26 A	0.00	0.00	0.00	12

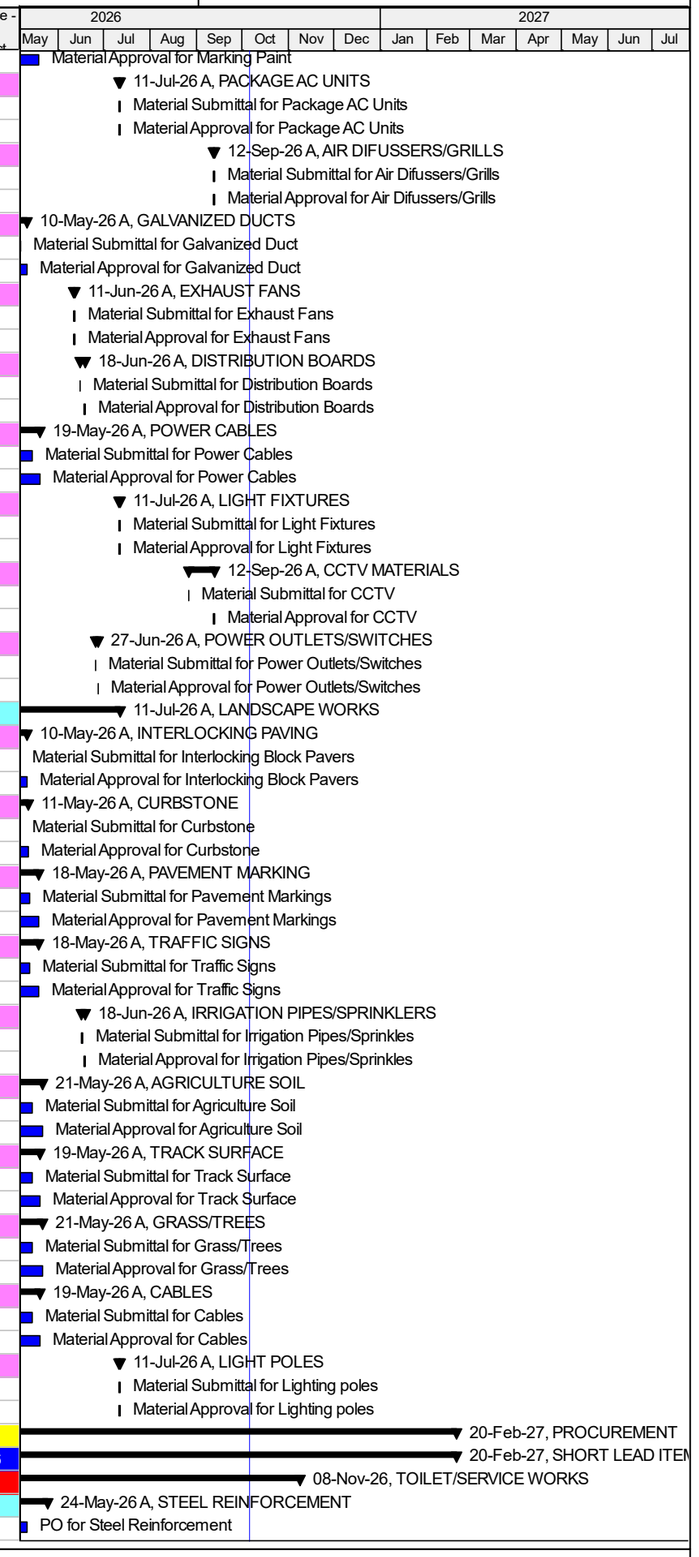

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-7	Material Delivery of Steel Reinforcement	5	100%	100%	25-May-26	02-Jun-26	24-May-26 A	24-May-26 A	0.00	0.00	0.00	5
CONCRETE BLOCKS		59	0%	0%	25-May-26	11-Jun-26	08-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-22
MLTX-02-005-PR-7	PO for Concrete Blocks	5	100%	100%	25-May-26	02-Jun-26	08-Apr-26 A	10-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-PR-7	Material Delivery of Concrete Blocks	8	100%	100%	03-Jun-26	11-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-22
FLOOR/WALL TILES		18	0%	0%	03-Jun-26	23-Jun-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	PO for Tilling Materials	5	100%	100%	03-Jun-26	08-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-61
MLTX-02-005-PR-8	Material Delivery of Tailling Material	13	100%	100%	09-Jun-26	23-Jun-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-50
SUSPENDED CEILING		21	0%	0%	20-Jul-26	09-Aug-26	26-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	PO for Suspend Ceiling	5	100%	100%	20-Jul-26	25-Jul-26	26-Jul-26 A	26-Jul-26 A	0.00	0.00	0.00	-1
MLTX-02-005-PR-8	Material Delivery of Suspend Ceiling	13	100%	100%	26-Jul-26	09-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-10
DOORS/WINDOWS		20	0%	0%	09-Jun-26	01-Jul-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-69
MLTX-02-005-PR-8	PO for Doors/Windows	5	100%	100%	09-Jun-26	14-Jun-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-PR-8	Material Delivery for Doors/Windows	15	100%	100%	15-Jun-26	01-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-69
WATER SUPPLY PIPES		39	0%	0%	15-Jun-26	28-Jun-26	28-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-PR-8	PO for Water Supply Pipes	5	100%	100%	15-Jun-26	20-Jun-26	28-Apr-26 A	03-May-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-8	Material Delivery for Water Supply Pipes	7	100%	100%	21-Jun-26	28-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
SEWAGE/DRAINAGE PIPES		27	0%	0%	15-Jun-26	28-Jun-26	26-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-PR-8	PO for Sewage/Drainage Pipes	5	100%	100%	15-Jun-26	20-Jun-26	26-Apr-26 A	10-May-26 A	0.00	0.00	0.00	32
MLTX-02-005-PR-8	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	21-Jun-26	28-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-8
SANITARY FIXTURES		31	0%	0%	21-Jun-26	11-Jul-26	28-Jul-26 A	20-Aug-26 A	0.00	0.00	0.00	-35
MLTX-02-005-PR-8	PO for Sanitary Fixtures	5	100%	100%	21-Jun-26	25-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-28
MLTX-02-005-PR-8	Material Delivery for Sanitary Fixtures	13	100%	100%	27-Jun-26	11-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-35
PACKAGE AC UNITS		20	0%	0%	27-Jun-26	19-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-8	PO for Package AC Units	5	100%	100%	27-Jun-26	01-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-5
MLTX-02-005-PR-8	Material Delivery for Package AC Units	15	100%	100%	02-Jul-26	19-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	10
AIR DIFUSSERS/GRILLS		20	0%	0%	27-Jun-26	19-Jul-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-005-PR-8	PO for Air Diffusers/Grills	5	100%	100%	27-Jun-26	01-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-41
MLTX-02-005-PR-8	Material Delivery for Air Diffusers/Grills	15	100%	100%	02-Jul-26	19-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-28
GALVANIZED DUCTS		20	0%	0%	27-Jun-26	19-Jul-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-28
MLTX-02-005-PR-8	PO for Galvanized Ducts	5	100%	100%	27-Jun-26	01-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-41
MLTX-02-005-PR-8	Material Delivery for Galvanized Ducts	15	100%	100%	02-Jul-26	19-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-28
EXHAUST FANS		15	0%	0%	27-Jun-26	13-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-33
MLTX-02-005-PR-8	PO for Exhaust Fans	5	100%	100%	27-Jun-26	01-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-43
MLTX-02-005-PR-8	Material Delivery for Exhaust Fans	10	100%	100%	02-Jul-26	13-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-33
LIGHTING FIXTURES		36	0%	0%	02-Jul-26	19-Jul-26	07-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8	PO for Lighting Fixtures	5	100%	100%	02-Jul-26	07-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-005-PR-8	Material Delivery for Lighting Fixtures	10	100%	0%	08-Jul-26	19-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-76
SWITCHES/SOCKETS		12	0%	0%	08-Jul-26	21-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8	PO for Switches/Sockets	5	100%	0%	08-Jul-26	13-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8	Material Delivery for Switches/Sockets	7	100%	0%	14-Jul-26	21-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
EARTHING SYSTEM		22	0%	0%	09-Jun-26	09-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-2
MLTX-02-005-PR-8	PO for Earthing System	5	100%	100%	09-Jun-26	14-Jun-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-PR-8	Material Delivery for Earthing System	15	100%	100%	23-Jun-26	09-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-2
DISTRIBUTION PANNELS		20	0%	0%	09-Jun-26	01-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-8	PO for Distribution Panels	5	100%	0%	09-Jun-26	14-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-8	Material Delivery for Distribution Panels	15	100%	0%	15-Jun-26	01-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
FURNITURES		29	0%	0%	02-Jul-26	04-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	PO for Furnitures	9	100%	0%	02-Jul-26	12-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	Material Delivery for Furnitures	20	100%	0%	13-Jul-26	04-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
PLAYGROUND WORKS		149	0%	0%	19-May-26	12-Sep-26	02-Apr-26 A	02-Dec-26	0.00	0.00	0.00	-69
PVC MEMBRANE		25	0%	0%	13-Jun-26	18-Jul-26	02-Apr-26 A	29-Oct-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-8	PO for PVC Membrane	10	100%	100%	13-Jun-26	23-Jun-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-8	Material Delivery for PVC Membrane	21	100%	0%	24-Jun-26	18-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-88
ARTIFICIAL TURF		12	0%	0%	14-Jul-26	02-Aug-26	02-Apr-26 A	12-Nov-26	0.00	0.00	0.00	-87
MLTX-02-005-PR-8	PO for Artificial TURF	5	100%	100%	14-Jul-26	19-Jul-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	49
MLTX-02-005-PR-8	Material Delivery for Artificial TURF	12	100%	0%	20-Jul-26	02-Aug-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-87
RUBBER GRANULES		16	0%	0%	13-Jun-26	01-Jul-26	02-Apr-26 A	19-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-8	PO for Rubber Granules	5	100%	100%	13-Jun-26	17-Jun-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	22
MLTX-02-005-PR-8	Material Delivery for Rubber Granules	12	100%	0%	18-Jun-26	01-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-93
PADEL GLASS		40	0%	0%	19-May-26	17-Jun-26	02-Apr-26 A	26-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-8	PO for Padel Glass	5	100%	100%	19-May-26	24-May-26	02-Apr-26 A	19-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-8	Material Delivery for Padel Glass	18	100%	0%	25-May-26	17-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-111
PADEL WIRE MESH/STEEL SETS		32	0%	0%	25-May-26	20-Jun-26	08-Apr-26 A	22-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-8	PO for Wire Mesh/Steel Sets	5	100%	100%	25-May-26	02-Jun-26	08-Apr-26 A	19-May-26 A	0.00	0.00	0.00	9

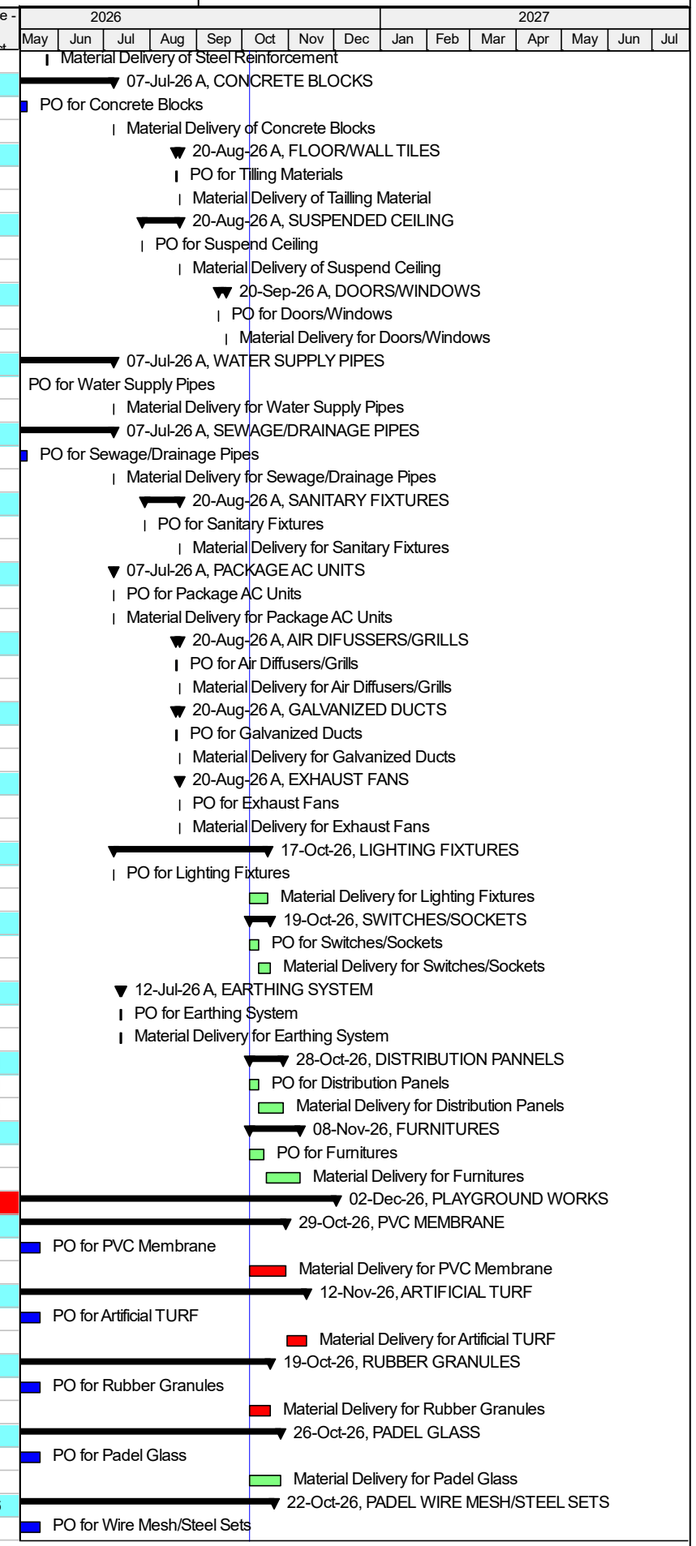

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-8	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	03-Jun-26	20-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-106
AGGREGATE BASE COURSE		12	0%	0%	13-Jun-26	25-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-8	PO for Aggregate Base Course	5	100%	100%	13-Jun-26	17-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-17
MLTX-02-005-PR-8	Material Delivery for Aggregate Base Course	7	100%	100%	18-Jun-26	25-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-10
BITUMINOUS BASE & WEARING COURSE		14	0%	0%	09-Jun-26	22-Jun-26	02-Apr-26 A	13-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	PO for Bituminous Base & Wearing Course	5	100%	100%	09-Jun-26	14-Jun-26	02-Apr-26 A	14-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-PR-8	Material Delivery for the Site	7	100%	0%	15-Jun-26	22-Jun-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-96
INTERLOCKING PAVING		13	0%	0%	14-Jul-26	27-Jul-26	15-Sep-26 A	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-8	PO for Interlocking Block Pavers	5	100%	100%	14-Jul-26	19-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-50
MLTX-02-005-PR-8	Material Delivery for Interlocking Block Pavers	7	100%	0%	20-Jul-26	27-Jul-26	14-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
MARKING PAINT		12	0%	0%	15-Jun-26	28-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	PO for Marking Paint	5	100%	0%	15-Jun-26	20-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	Material Delivery for Marking Paint	7	100%	0%	21-Jun-26	28-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
PACKAGE AC UNITS		20	0%	0%	03-Aug-26	25-Aug-26	04-Jul-26 A	10-Jul-26 A	0.00	0.00	0.00	40
MLTX-02-005-PR-8	PO for Package AC Units	5	100%	100%	03-Aug-26	08-Aug-26	04-Jul-26 A	04-Jul-26 A	0.00	0.00	0.00	30
MLTX-02-005-PR-8	Material Delivery for Package AC Units	15	100%	100%	09-Aug-26	25-Aug-26	10-Jul-26 A	10-Jul-26 A	0.00	0.00	0.00	40
AIR DIFUSSERS/GRILLS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	PO for Air Difussers/Grills	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	Material Delivery for Air Difussers/Grills	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
GALVANIZED DUCTS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	PO for Galvanized Duct	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	Material Delivery for Galvanized Duct	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
EXHAUST FANS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	PO for Exhaust Fans	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8	Material Delivery for Exhaust Fans	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
DISTRIBUTION BOARDS		20	0%	0%	02-Jul-26	25-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	PO for Distribution Boards	5	100%	0%	02-Jul-26	07-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	Material Delivery for Distribution Boards	15	100%	0%	08-Jul-26	25-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
POWER CABLES		15	0%	0%	08-Jul-26	25-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	PO for Power Cables	5	100%	0%	08-Jul-26	13-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-8	Material Delivery for Power Cables	10	100%	0%	14-Jul-26	25-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-96
LIGHT FIXTURES		51	0%	0%	14-Jul-26	30-Jul-26	07-Jul-26 A	15-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-PR-8	PO for Light Fixtures	5	100%	100%	14-Jul-26	19-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-8	Material Delivery for Light Fixtures	10	100%	0%	20-Jul-26	30-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-91
CCTV MATERIALS		50	0%	0%	20-Jul-26	12-Sep-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-8	PO for CCTV	5	100%	0%	20-Jul-26	25-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-8	Material Delivery for CCTV	15	100%	0%	26-Aug-26	12-Sep-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-69
POWER OUTLETS/SWITCHES		78	0%	0%	26-Jul-26	18-Aug-26	07-Jul-26 A	22-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-8	PO for Power Outlets/Switches	6	100%	100%	26-Jul-26	01-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	21
MLTX-02-005-PR-8	Material Delivery for Power Outlets/Switches	15	100%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
LANDSCAPE WORKS		124	0%	0%	02-Aug-26	19-Oct-26	16-May-26 A	20-Feb-27	0.00	0.00	0.00	-106
INTERLOCKING PAVING		23	0%	0%	02-Aug-26	20-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-5
MLTX-02-005-PR-8	PO for Interlocking Block Pavers	5	100%	100%	02-Aug-26	06-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-17
MLTX-02-005-PR-8	Material Delivery for Interlocking Block Pavers	12	100%	100%	08-Aug-26	20-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-5
CURBSTONE		17	0%	0%	02-Aug-26	20-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	20
MLTX-02-005-PR-8	PO for Curbstone	5	100%	100%	02-Aug-26	06-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	8
MLTX-02-005-PR-8	Material Delivery for Curbstone	12	100%	100%	08-Aug-26	20-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	20
PAVEMENT MARKING		15	0%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-8	PO for Pavement Markings	5	100%	0%	02-Aug-26	06-Aug-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-8	Material Delivery for Pavement Markings	10	100%	0%	08-Aug-26	18-Aug-26	12-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
TRAFFIC SIGNS		14	0%	0%	03-Oct-26	18-Oct-26	12-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-8	PO for Traffic Signs	5	60%	0%	03-Oct-26	07-Oct-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-8	Material Delivery for Traffic Signs	9	0%	0%	08-Oct-26	18-Oct-26	18-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
IRRIGATION PIPES/SPRINKLERS		13	0%	0%	08-Aug-26	22-Aug-26	10-Jun-26 A	02-Jul-26 A	0.00	0.00	0.00	43
MLTX-02-005-PR-8	PO for Irrigation Pipes/Sprinkles	5	100%	100%	08-Aug-26	12-Aug-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	54
MLTX-02-005-PR-8	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	100%	13-Aug-26	22-Aug-26	02-Jul-26 A	02-Jul-26 A	0.00	0.00	0.00	43
AGRICULTURE SOIL		17	0%	0%	20-Sep-26	10-Oct-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-8	PO for Agriculture Soil	5	100%	0%	20-Sep-26	26-Sep-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-8	Material Delivery for Agriculture Soil	12	66.67%	0%	27-Sep-26	10-Oct-26	03-Feb-27	16-Feb-27	0.00	0.00	0.00	-111
TRACK SURFACE		32	0%	0%	02-Sep-26	19-Sep-26	16-May-26 A	27-Jan-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-8	PO for Track Surface	5	100%	100%	02-Sep-26	07-Sep-26	16-May-26 A	19-May-26 A	0.00	0.00	0.00	92
MLTX-02-005-PR-8	Material Delivery for Track Surface	10	100%	0%	08-Sep-26	19-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-111
GRASS/TREES		32	0%	0%	27-Sep-26	19-Oct-26	17-May-26 A	20-Feb-27	0.00	0.00	0.00	-106
MLTX-02-005-PR-8	PO for Grass/Trees	5	100%	100%	27-Sep-26	01-Oct-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	111

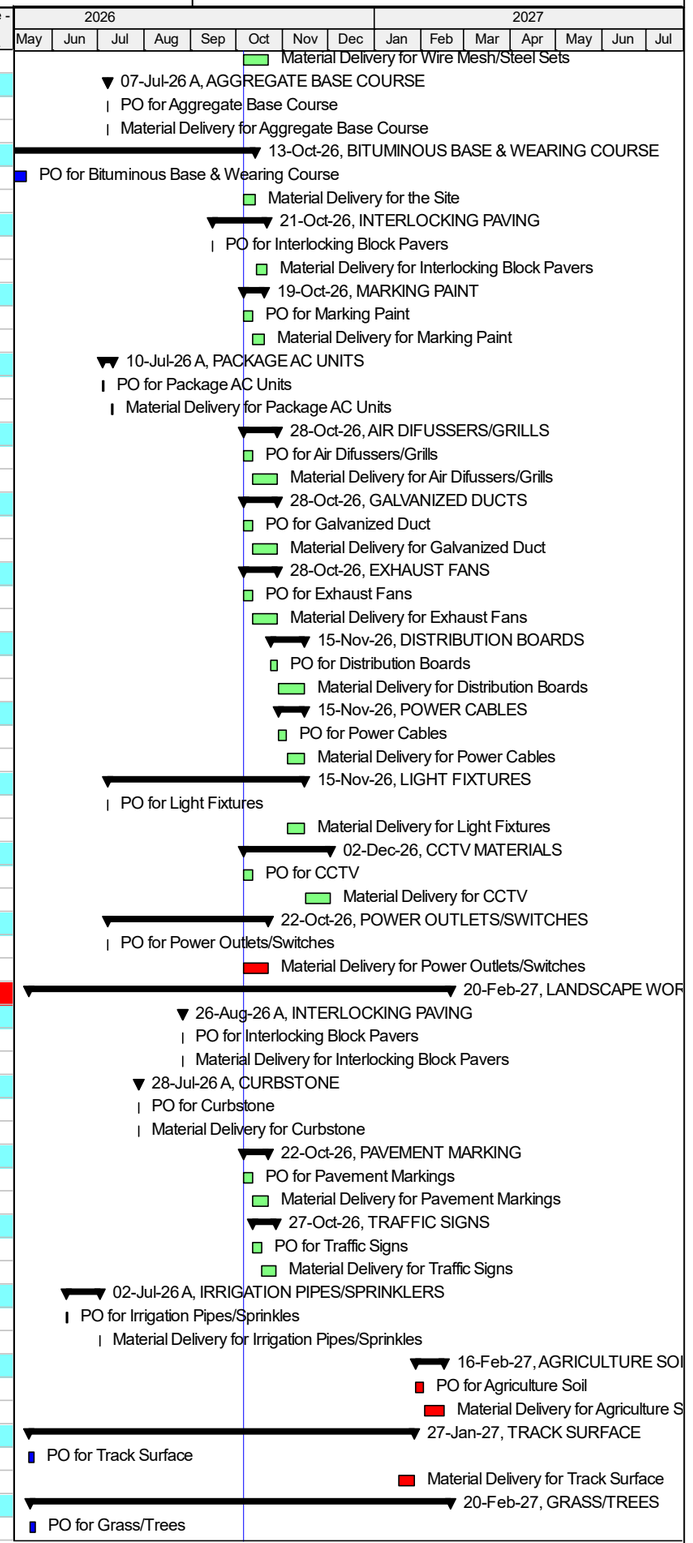

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-S	Material Delivery for Grass/Trees	15	20%	0%	03-Oct-26	19-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-106
CABLES		20	0%	0%	08-Aug-26	30-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-14
MLTX-02-005-PR-S	PO for Cables	5	100%	100%	08-Aug-26	12-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-S	Material Delivery for Cables	15	100%	100%	13-Aug-26	30-Aug-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-14
LONG LEAD ITEM		109	0%	0%	19-May-26	22-Nov-26	07-Jul-26 A	16-Jan-27	0.00	0.00	0.00	-47
PLAYGROUND WORKS		88	0%	0%	19-May-26	01-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-116
STEEL TENSION CABLES		65	0%	0%	19-May-26	09-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-S	PO for Steel Tension Cables	8	100%	0%	19-May-26	31-May-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Fabrication for Steel Tension Cables	20	100%	0%	01-Jun-26	23-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Delivery for Steel Tension Cables	30	100%	0%	28-Jun-26	01-Aug-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-S	Staging time	7	100%	0%	02-Aug-26	09-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-113
EMERGENCY DOORS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	PO for Emergency Doors	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Fabrication for Emergency Doors	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Delivery for Emergency Doors	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116
PRESSURE UNITS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	PO for Pressure Units	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Fabrication for Pressure Units	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Delivery for Pressure Units	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116
AIR LOCK DOORS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	PO for Lock Doors	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Fabrication for Lock Doors	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Material Delivery for Lock Doors	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-S	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116
LANDSCAPE WORKS		109	0%	0%	13-Aug-26	22-Nov-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	53
LIGHT POLES		109	0%	0%	13-Aug-26	22-Nov-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	53
MLTX-02-005-PR-S	PO for Lighting poles	10	100%	100%	13-Aug-26	24-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	41
MLTX-02-005-PR-S	Material Fabrication for Lighting poles	30	63.33%	100%	13-Sep-26	18-Oct-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	44
MLTX-02-005-PR-S	Material Delivery for Lighting poles	25	0%	100%	19-Oct-26	16-Nov-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	48
MLTX-02-005-PR-S	Staging time	5	0%	100%	17-Nov-26	22-Nov-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	53
CONSTRUCTION PHASE		238	32.16%	32.45%	15-Apr-26	02-Jan-27	04-Apr-26 A	30-Mar-27	3,251,318.73	3,280,871.77	10,110,715.45	-71
SITE WORKS		238	23.03%	30.14%	15-Apr-26	02-Jan-27	04-Apr-26 A	30-Mar-27	2,051,955.04	2,686,155.21	8,911,351.76	-71
EARTH WORKS		81	100%	100%	15-Apr-26	11-Jun-26	04-Apr-26 A	05-Aug-26 A	1,017,621.97	1,017,621.97	1,017,621.97	-46
MLTX-02-005-CN-993	Excavation (in all types of soil) including Compaction	12	100%	100%	02-May-26	14-May-26	06-Apr-26 A	12-Apr-26 A	180,460.75	180,460.75	180,460.75	29
MLTX-02-005-CN-994	Excavation (in all types of soil) including Compaction	14	100%	100%	15-Apr-26	30-Apr-26	04-Apr-26 A	02-Aug-26 A	266,892.26	266,892.26	266,892.26	-76
MLTX-02-005-CN-995	Excavation (in all types of soil) including Compaction	7	100%	100%	16-May-26	23-May-26	28-Jun-26 A	05-Aug-26 A	243,701.49	243,701.49	243,701.49	-60
MLTX-02-005-CN-996	Backfilling on Layers (Selected Soil) including Compaction	21	100%	100%	16-May-26	11-Jun-26	13-Apr-26 A	30-Apr-26 A	117,028.93	117,028.93	117,028.93	34
MLTX-02-005-CN-997	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	02-May-26	24-May-26	06-Apr-26 A	08-Apr-26 A	60,984.78	60,984.78	60,984.78	39
MLTX-02-005-CN-998	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	24-May-26	04-Jun-26	21-Apr-26 A	05-Aug-26 A	148,553.76	148,553.76	148,553.76	-52
LANDSCAPE WORKS		207	13.2%	20.81%	13-Jun-26	02-Jan-27	17-May-26 A	30-Mar-27	1,034,333.07	1,630,512.58	7,835,236.46	-71
PLAYGROUND AREA		200	36.55%	50.77%	13-Jun-26	02-Jan-27	19-May-26 A	22-Mar-27	520,731.38	723,206.72	1,424,564.96	-64
FOOTBALL PLAYGROUND		188	35%	35%	13-Jun-26	01-Dec-26	19-May-26 A	16-Mar-27	110,897.50	110,897.50	316,849.99	-86
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	20	100%	100%	13-Jun-26	05-Jul-26	19-May-26 A	01-Jun-26 A	79,212.50	79,212.50	79,212.50	29
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	21	100%	100%	06-Jul-26	29-Jul-26	01-Jun-26 A	22-Jun-26 A	15,842.50	15,842.50	15,842.50	33
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	21	0%	0%	21-Oct-26	14-Nov-26	14-Nov-26	07-Dec-26	0.00	0.00	158,424.99	-20
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	31,685.00	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	10	0%	0%	15-Nov-26	25-Nov-26	25-Jan-27	04-Feb-27	0.00	0.00	15,842.50	-61
MLTX-02-005-CI	Aggregate base course layer (Football Playground)	21	100%	100%	30-Jul-26	23-Aug-26	02-Aug-26 A	06-Aug-26 A	15,842.50	15,842.50	15,842.50	14
PADEL PLAYGROUND		195	45%	70%	06-Jul-26	01-Dec-26	19-May-26 A	16-Mar-27	105,292.80	163,788.80	233,984.00	-86
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	21	100%	100%	06-Jul-26	29-Jul-26	19-May-26 A	01-Jun-26 A	81,894.40	81,894.40	81,894.40	50
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	21	100%	100%	30-Jul-26	23-Aug-26	01-Jun-26 A	14-Jun-26 A	11,699.20	11,699.20	11,699.20	61
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	0%	100%	21-Oct-26	14-Nov-26	29-Aug-26 A	31-Aug-26 A	0.00	58,496.00	58,496.00	64
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	58,496.00	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	10	0%	0%	15-Nov-26	25-Nov-26	24-Feb-27	07-Mar-27	0.00	0.00	11,699.20	-86
MLTX-02-005-CI	Aggregate base course layer (Padel Playground)	21	100%	100%	24-Aug-26	16-Sep-26	15-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	70
BASKETBALL PLAYGROUND		179	37.98%	70%	30-Jul-26	07-Dec-26	19-May-26 A	22-Mar-27	122,756.74	226,230.90	323,187.00	-86
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	20	100%	100%	30-Jul-26	22-Aug-26	19-May-26 A	01-Jun-26 A	95,055.00	95,055.00	95,055.00	70
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	21	100%	100%	23-Aug-26	15-Sep-26	01-Jun-26 A	14-Jun-26 A	16,159.35	16,159.35	16,159.35	81
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	0%	100%	13-Oct-26	05-Nov-26	19-Aug-26 A	31-Aug-26 A	0.00	98,857.20	98,857.20	57
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	80,796.75	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	10	0%	0%	26-Nov-26	07-Dec-26	08-Mar-27	22-Mar-27	0.00	0.00	16,159.35	-86
MLTX-02-005-CI	Aggregate base course layer (Basketball Playground)	21	71.43%	100%	17-Sep-26	12-Oct-26	15-Jun-26 A	28-Jun-26 A	11,542.39	16,159.35	16,159.35	91

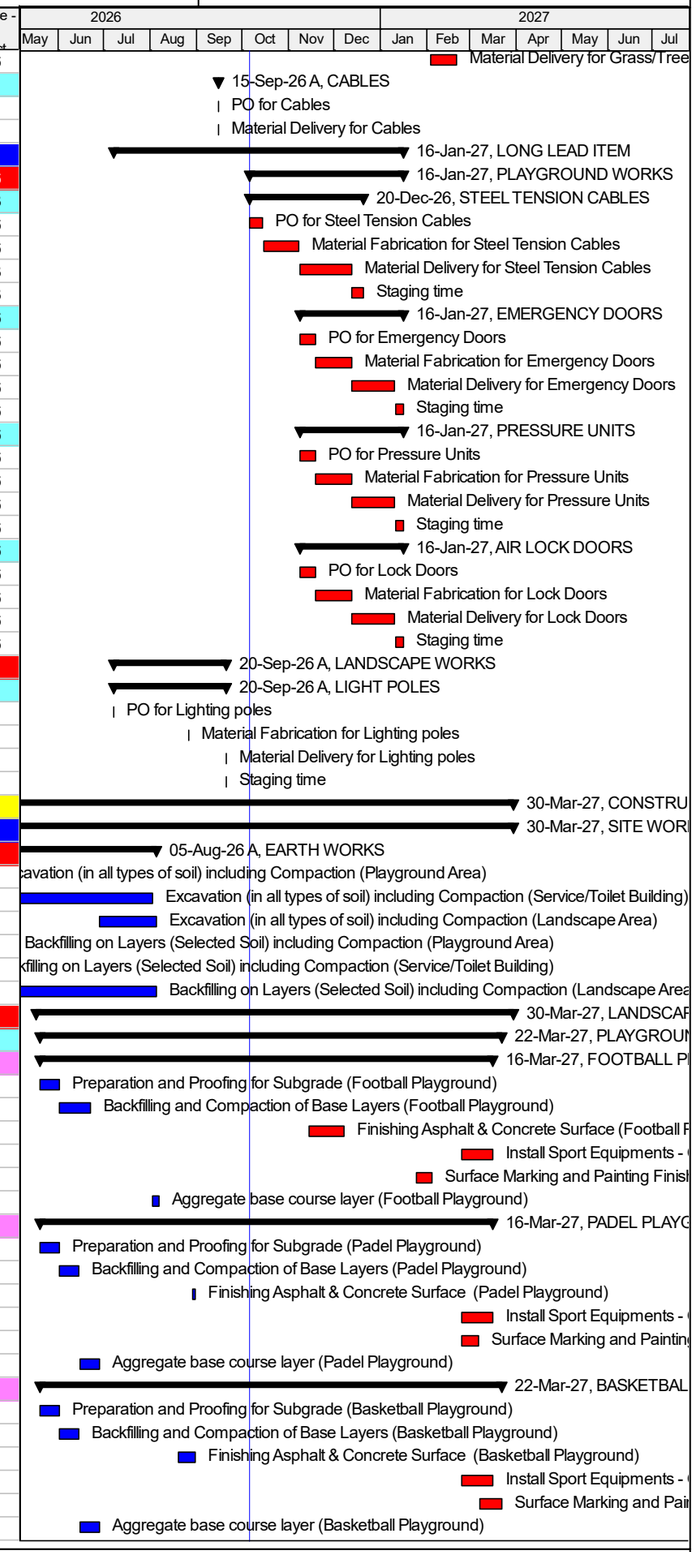

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PADEL FENCE		168	0%	21.52%	08-Dec-26	19-Dec-26	08-Aug-26 A	17-Oct-26	0.00	40,505.18	188,238.96	54
MLTX-02-005-CI	Excavation for Fence	8	0%	100%	08-Dec-26	16-Dec-26	08-Aug-26 A	08-Aug-26 A	0.00	23,931.36	23,931.36	111
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	0%	100%	08-Dec-26	15-Dec-26	15-Aug-26 A	19-Aug-26 A	0.00	16,573.82	16,573.82	100
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	7	0%	0%	08-Dec-26	15-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	4,143.45	54
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	33,147.63	54
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	16,573.82	54
MLTX-02-005-CI	Install of Fence Gates	2	0%	0%	08-Dec-26	09-Dec-26	06-Oct-26	07-Oct-26	0.00	0.00	93,868.88	54
CURBSTOEN/INTERLOCK		65	50.17%	50.17%	15-Sep-26	02-Jan-27	15-Aug-26 A	15-Nov-26	181,784.34	181,784.34	362,305.01	41
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	10-Dec-26	02-Jan-27	24-Oct-26	15-Nov-26	0.00	0.00	180,520.67	41
MLTX-02-005-CI	Concrete Works Under Curbstone	7	100%	100%	15-Sep-26	22-Sep-26	15-Aug-26 A	15-Aug-26 A	54,535.30	54,535.30	54,535.30	33
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	24-Sep-26	28-Sep-26	19-Aug-26 A	05-Sep-26 A	127,249.04	127,249.04	127,249.04	19
AIR DOME		175	7.58%	11.91%	24-Aug-26	09-Dec-26	17-May-26 A	30-Mar-27	370,238.11	581,544.30	4,881,359.87	-91
CIVIL WORKS		112	18.83%	29.58%	24-Aug-26	01-Nov-26	17-May-26 A	03-Nov-26	370,238.11	581,544.30	1,966,294.68	-2
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	6	100%	100%	24-Aug-26	30-Aug-26	17-May-26 A	31-May-26 A	127,762.34	127,762.34	127,762.34	78
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	13	100%	100%	31-Aug-26	14-Sep-26	29-Jul-26 A	21-Sep-26 A	168,176.84	168,176.84	168,176.84	-6
MLTX-02-005-CI	Cable System Installation (Air Dome)	5	100%	100%	15-Sep-26	20-Sep-26	21-Sep-26 A	21-Sep-26 A	41,790.29	41,790.29	41,790.29	-1
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	17-Oct-26	0.00	0.00	936,278.81	13
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	24-Oct-26	03-Nov-26	0.00	0.00	448,471.57	-2
MLTX-02-005-CI	Perimeter Clamping System Installation	15	13.33%	100%	04-Oct-26	20-Oct-26	21-Sep-26 A	28-Sep-26 A	32,508.64	243,814.83	243,814.83	19
MECHANICAL WORKS		76	0%	0%	02-Nov-26	16-Nov-26	04-Nov-26	31-Jan-27	0.00	0.00	1,233,296.81	-65
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	02-Nov-26	12-Nov-26	04-Nov-26	15-Nov-26	0.00	0.00	728,766.30	-2
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	02-Nov-26	16-Nov-26	17-Jan-27	31-Jan-27	0.00	0.00	336,353.67	-65
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	7	0%	0%	02-Nov-26	09-Nov-26	17-Jan-27	24-Jan-27	0.00	0.00	168,176.84	-65
ELECTRICAL WORKS		20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	1,513,591.54	-65
MLTX-02-005-CI	Light Fixture Works (Air Dome)	6	0%	0%	17-Nov-26	23-Nov-26	01-Feb-27	07-Feb-27	0.00	0.00	224,235.78	-65
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	10	0%	0%	17-Nov-26	28-Nov-26	01-Feb-27	11-Feb-27	0.00	0.00	168,176.84	-65
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	168,176.84	-65
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	504,530.51	-65
MLTX-02-005-CI	Control System Installation (Air Dome)	13	0%	0%	17-Nov-26	01-Dec-26	04-Feb-27	18-Feb-27	0.00	0.00	448,471.57	-68
FINISHES WORKS		49	0%	0%	14-Nov-26	09-Dec-26	28-Jan-27	30-Mar-27	0.00	0.00	168,176.84	-91
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	3	0%	0%	14-Nov-26	16-Nov-26	28-Jan-27	31-Jan-27	0.00	0.00	112,117.89	-65
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	7	0%	0%	02-Dec-26	09-Dec-26	23-Mar-27	30-Mar-27	0.00	0.00	56,058.95	-91
IRRIGATION NETWORK		87	51.62%	80.44%	29-Sep-26	22-Oct-26	18-Aug-26 A	24-Feb-27	78,683.91	122,596.50	152,414.87	-106
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	4	100%	100%	29-Sep-26	03-Oct-26	18-Aug-26 A	02-Sep-26 A	53,620.00	53,620.00	53,620.00	25
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	4	50%	100%	04-Oct-26	07-Oct-26	03-Sep-26 A	10-Sep-26 A	25,063.92	50,127.83	50,127.83	22
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	4	0%	80%	08-Oct-26	12-Oct-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	2
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	20-Oct-26	22-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	25,106.20	-106
NATURAL GROUND		81	0%	0%	13-Oct-26	22-Oct-26	22-Nov-26	24-Feb-27	0.00	0.00	191,740.00	-106
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	20-Oct-26	22-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	126,740.00	-106
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	13-Oct-26	19-Oct-26	22-Nov-26	28-Nov-26	0.00	0.00	65,000.00	-34
PLANTING		24	0%	0%	24-Oct-26	19-Nov-26	25-Feb-27	28-Mar-27	0.00	0.00	347,251.46	-106
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	10	0%	0%	24-Oct-26	03-Nov-26	25-Feb-27	08-Mar-27	0.00	0.00	104,175.44	-106
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	17-Nov-26	19-Nov-26	25-Mar-27	28-Mar-27	0.00	0.00	141,732.50	-106
MLTX-02-005-CN-1	Placement and Fixation of Trees	11	0%	0%	04-Nov-26	16-Nov-26	09-Mar-27	24-Mar-27	0.00	0.00	101,343.52	-106
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	165,435.26	367,633.90	51
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	84,399.35	187,554.12	51
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	81,035.90	180,079.78	51
GENERAL/FURNITURE		29	13.75%	8.02%	29-Sep-26	02-Jan-27	03-Oct-26 A	05-Nov-26	64,679.66	37,729.80	470,271.40	49
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	05-Dec-26	09-Dec-26	06-Oct-26	11-Oct-26	0.00	0.00	93,594.00	51
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	26-Dec-26	02-Jan-27	29-Oct-26	05-Nov-26	0.00	0.00	9,749.30	49
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	05-Dec-26	12-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	17,274.79	51
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	40,307.84	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	32,757.76	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	12,869.04	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	21-Dec-26	02-Jan-27	24-Oct-26	04-Nov-26	0.00	0.00	12,186.67	50
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	7	85.71%	50%	29-Sep-26	06-Oct-26	03-Oct-26 A	13-Oct-26	64,679.66	37,729.80	75,459.60	-6
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	0%	10-Dec-26	24-Dec-26	14-Oct-26	28-Oct-26	0.00	0.00	176,072.40	49
PARKING		155	0%	65%	10-Dec-26	16-Dec-26	16-May-26 A	08-Oct-26	0.00	38,020.67	58,493.33	59
MLTX-02-005-CN-106	Interlock Installation (8 Cm) for Parking Area (Including	3	0%	50%	14-Dec-26	16-Dec-26	03-Oct-26 A	08-Oct-26	0.00	20,472.67	40,945.33	59
MLTX-02-005-CN-107	Site Preparation & Compaction Under Interlock for Parking	3	0%	100%	10-Dec-26	13-Dec-26	16-May-26 A	22-Jul-26 A	0.00	17,548.00	17,548.00	123
TOILET/SERVICE BUILDING		129	100%	49.59%	06-Jun-26	26-Sep-26	21-May-26 A	07-Dec-26	1,199,363.69	594,716.57	1,199,363.69	-62
STRUCTURE WORKS		98	100%	100%	06-Jun-26	27-Jul-26	21-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-5
CONCRETE WORKS		86	100%	100%	25-Jun-26	27-Jul-26	20-Jun-26 A	12-Jul-26 A	134,099.30	134,099.30	134,099.30	13
SUB-STRUCTURE		86	100%	100%	25-Jun-26	05-Jul-26	20-Jun-26 A	25-Jun-26 A	53,666.80	53,666.80	53,666.80	8

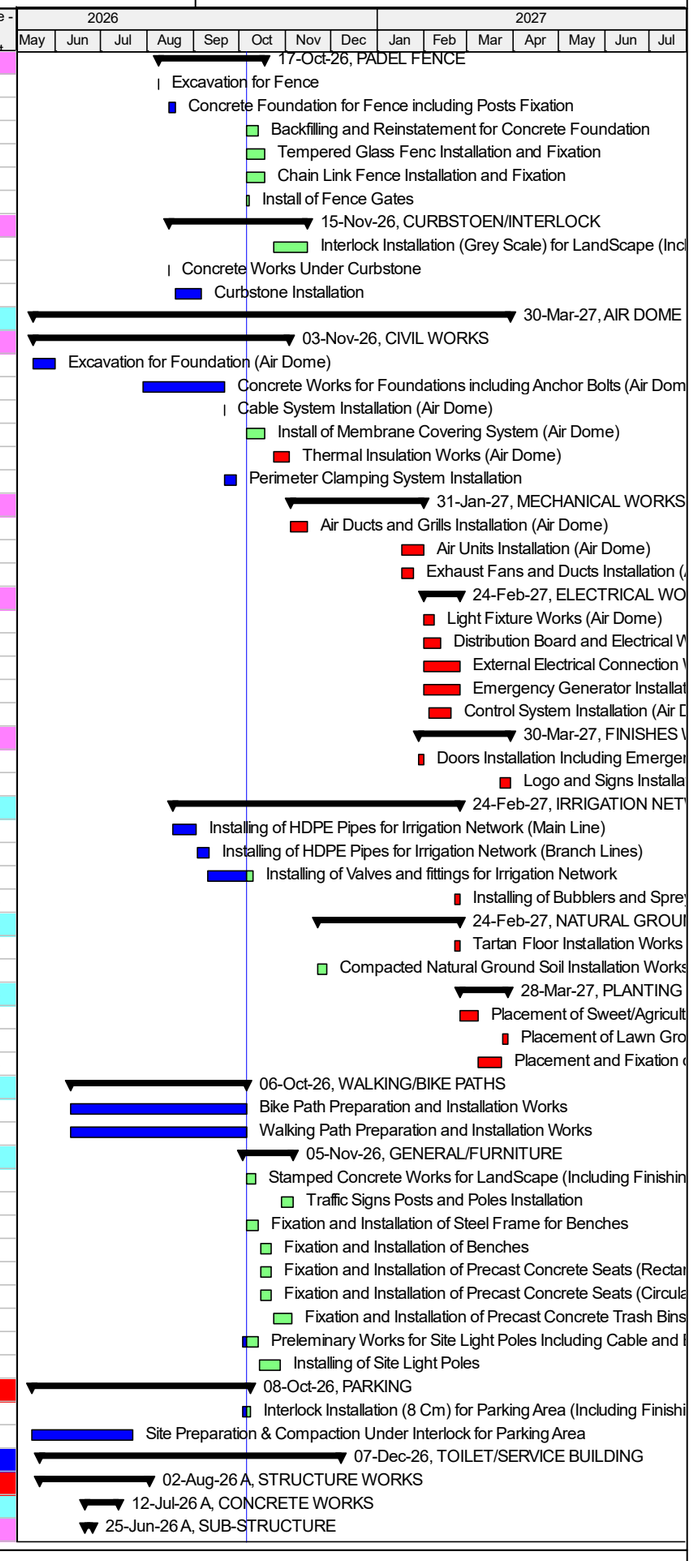

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Plain Concrete Under Footing	4	100%	100%	25-Jun-26	29-Jun-26	20-Jun-26 A	21-Jun-26 A	17,106.85	17,106.85	17,106.85	7
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	30-Jun-26	05-Jul-26	22-Jun-26 A	25-Jun-26 A	36,559.95	36,559.95	36,559.95	8
SUPER-STRUCTURE		10	100%	100%	12-Jul-26	27-Jul-26	07-Jul-26 A	12-Jul-26 A	80,432.50	80,432.50	80,432.50	13
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	12-Jul-26	19-Jul-26	07-Jul-26 A	08-Jul-26 A	48,259.50	48,259.50	48,259.50	9
MLTX-02-005-CI	AAC Panels Works for Slabs	3	100%	100%	20-Jul-26	22-Jul-26	09-Jul-26 A	11-Jul-26 A	16,086.50	16,086.50	16,086.50	10
MLTX-02-005-CI	Parpet Works and Lintels	4	100%	100%	23-Jul-26	27-Jul-26	11-Jul-26 A	12-Jul-26 A	16,086.50	16,086.50	16,086.50	13
UNDER GROUND SEPTIC TANK		32	100%	100%	07-Jun-26	13-Jul-26	31-May-26 A	24-Jun-26 A	49,852.54	49,852.54	49,852.54	16
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	07-Jun-26	09-Jun-26	31-May-26 A	01-Jun-26 A	17,106.85	17,106.85	17,106.85	7
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	8	100%	100%	10-Jun-26	18-Jun-26	10-Jun-26 A	13-Jun-26 A	7,604.46	7,604.46	7,604.46	5
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	11	100%	100%	20-Jun-26	01-Jul-26	07-Jun-26 A	11-Jun-26 A	16,366.86	16,366.86	16,366.86	17
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	10	100%	100%	02-Jul-26	13-Jul-26	20-Jun-26 A	24-Jun-26 A	8,774.37	8,774.37	8,774.37	16
THERMAL & MOISTER PROTECTION		74	100%	100%	06-Jun-26	22-Jul-26	21-May-26 A	02-Aug-26 A	10,236.80	10,236.80	10,236.80	-9
ANTI TERMIT CONTROL		13	100%	100%	06-Jun-26	20-Jun-26	21-May-26 A	25-May-26 A	4,387.50	4,387.50	4,387.50	19
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	06-Jun-26	06-Jun-26	24-May-26 A	25-May-26 A	1,755.00	1,755.00	1,755.00	7
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	20-Jun-26	20-Jun-26	21-May-26 A	21-May-26 A	2,632.50	2,632.50	2,632.50	23
POLYETHYLENE SHEET		62	100%	100%	06-Jun-26	20-Jun-26	25-May-26 A	21-Jun-26 A	2,193.30	2,193.30	2,193.30	-1
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	06-Jun-26	06-Jun-26	25-May-26 A	31-May-26 A	877.32	877.32	877.32	5
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	20-Jun-26	20-Jun-26	21-Jun-26 A	21-Jun-26 A	1,315.98	1,315.98	1,315.98	-1
EPOXY		8	100%	100%	14-Jul-26	22-Jul-26	12-Jul-26 A	02-Aug-26 A	3,656.00	3,656.00	3,656.00	-9
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	14-Jul-26	16-Jul-26	12-Jul-26 A	12-Jul-26 A	1,096.80	1,096.80	1,096.80	4
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	18-Jul-26	22-Jul-26	25-Jul-26 A	02-Aug-26 A	2,559.20	2,559.20	2,559.20	-9
MASONARY WORK		5	100%	100%	06-Jul-26	11-Jul-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
MLTX-02-005-CN-11C	CMU Masonary Works Including all Accessories	5	100%	100%	06-Jul-26	11-Jul-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
THERMAL & MOISTER PROTECTION		15	100%	57.12%	28-Jul-26	20-Aug-26	26-Sep-26 A	14-Oct-26	34,698.32	19,820.29	34,698.32	-46
MLTX-02-005-CN-11C	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	28-Jul-26	29-Jul-26	26-Sep-26 A	26-Sep-26 A	2,105.86	2,105.86	2,105.86	-49
MLTX-02-005-CN-11C	Preparing Surface and Preliminary Works for Roofing and	5	100%	100%	06-Aug-26	11-Aug-26	30-Sep-26 A	30-Sep-26 A	11,071.52	11,071.52	11,071.52	-42
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Toilets	6	100%	0%	30-Jul-26	05-Aug-26	06-Oct-26	12-Oct-26	4,913.66	0.00	4,913.66	-57
MLTX-02-005-CN-11C	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	40%	12-Aug-26	20-Aug-26	03-Oct-26 A	14-Oct-26	16,607.28	6,642.91	16,607.28	-46
MECHANICAL WORK		63	100%	44.49%	06-Aug-26	21-Sep-26	18-Jul-26 A	19-Nov-26	264,673.10	117,742.89	264,673.10	-50
HVAC SYSTEM		58	100%	47.55%	20-Aug-26	20-Sep-26	19-Jul-26 A	18-Nov-26	27,883.37	13,259.41	27,883.37	-50
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	20-Aug-26	23-Aug-26	19-Jul-26 A	22-Jul-26 A	9,359.69	9,359.69	9,359.69	27
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	24-Aug-26	30-Aug-26	12-Sep-26 A	12-Sep-26 A	3,899.72	3,899.72	3,899.72	-11
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	14,623.96	0.00	14,623.96	-50
WATER SUPPLY SYSTEM		56	100%	59.85%	09-Aug-26	13-Sep-26	28-Jul-26 A	11-Nov-26	154,916.69	92,716.08	154,916.69	-50
MLTX-02-005-CN-1	Installing of Valves and Fittings	2	100%	100%	12-Aug-26	13-Aug-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	-19
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	80%	15-Aug-26	17-Aug-26	29-Sep-26 A	08-Oct-26	25,998.40	20,798.72	25,998.40	-44
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	09-Aug-26	11-Aug-26	28-Jul-26 A	02-Aug-26 A	6,921.94	6,921.94	6,921.94	8
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	100%	0%	02-Sep-26	09-Sep-26	15-Oct-26	22-Oct-26	48,746.52	0.00	48,746.52	-36
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	90%	24-Aug-26	01-Sep-26	28-Sep-26 A	14-Oct-26	64,995.36	58,495.82	64,995.36	-36
MLTX-02-005-CN-1	Installing of Water Heater	4	100%	0%	09-Sep-26	13-Sep-26	08-Nov-26	11-Nov-26	1,754.87	0.00	1,754.87	-50
SEWER/DRAINAGE SYSTEM		52	100%	14.72%	06-Aug-26	13-Sep-26	18-Jul-26 A	11-Nov-26	79,923.17	11,767.40	79,923.17	-50
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	15-Aug-26	18-Aug-26	12-Oct-26	15-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	06-Aug-26	08-Aug-26	18-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	14
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	24-Aug-26	25-Aug-26	22-Oct-26	24-Oct-26	10,358.68	0.00	10,358.68	-50
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	09-Aug-26	13-Aug-26	06-Oct-26	11-Oct-26	12,186.63	0.00	12,186.63	-49
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	08-Nov-26	11-Nov-26	31,392.79	0.00	31,392.79	-50
FIRE PROTECTION		2	100%	0%	20-Sep-26	21-Sep-26	18-Nov-26	19-Nov-26	1,949.87	0.00	1,949.87	-50
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	20-Sep-26	21-Sep-26	18-Nov-26	19-Nov-26	1,949.87	0.00	1,949.87	-50
ELECTRICAL WORKS		119	100%	53.29%	28-Jul-26	26-Sep-26	19-Jul-26 A	07-Dec-26	386,998.59	206,217.32	386,998.59	-62
ROUGH-IN WORKS		82	100%	100%	28-Jul-26	05-Aug-26	19-Jul-26 A	09-Aug-26 A	206,217.32	206,217.32	206,217.32	-2
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	09-Aug-26 A	32,172.69	32,172.69	32,172.69	-8
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	20-Jul-26 A	68,245.12	68,245.12	68,245.12	8
MLTX-02-005-CN-1	Preleminary Works for Cable Works	2	100%	100%	04-Aug-26	05-Aug-26	19-Jul-26 A	22-Jul-26 A	12,488.92	12,488.92	12,488.92	12
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	20-Jul-26 A	15,990.55	15,990.55	15,990.55	8
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	09-Aug-26 A	21,935.93	21,935.93	21,935.93	-8
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	09-Aug-26 A	24,470.75	24,470.75	24,470.75	-8
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	2	100%	100%	28-Jul-26	29-Jul-26	19-Jul-26 A	09-Aug-26 A	30,913.36	30,913.36	30,913.36	-8
FIXTURE WORKS		19	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	07-Dec-26	180,781.27	0.00	180,781.27	-62
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	100%	0%	17-Sep-26	22-Sep-26	16-Nov-26	21-Nov-26	102,367.69	0.00	102,367.69	-50
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	6,239.59	0.00	6,239.59	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	7,085.10	0.00	7,085.10	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	6,824.51	0.00	6,824.51	-50
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	100%	0%	21-Sep-26	26-Sep-26	19-Nov-26	23-Nov-26	34,317.53	0.00	34,317.53	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	14,259.43	0.00	14,259.43	-50

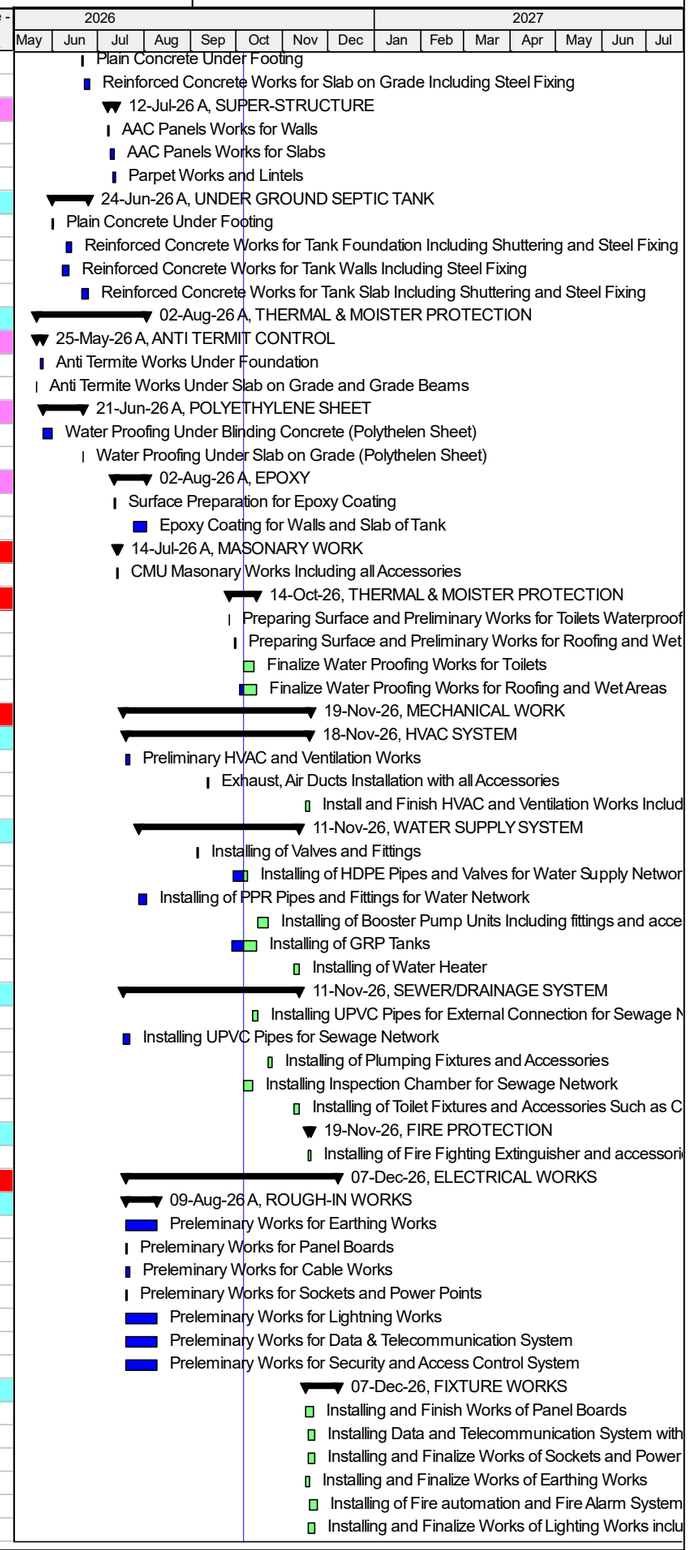


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	100%	0%	17-Sep-26	24-Sep-26	16-Nov-26	22-Nov-26	2,437.33	0.00	2,437.33	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	17-Sep-26	21-Sep-26	03-Dec-26	07-Dec-26	7,250.09	0.00	7,250.09	-65
DOORS/WINDOWS		42	100%	0%	28-Jul-26	26-Sep-26	06-Oct-26	23-Nov-26	68,245.12	0.00	68,245.12	-50
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	28-Jul-26	29-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-59
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	0%	28-Jul-26	30-Jul-26	06-Oct-26	08-Oct-26	7,799.44	0.00	7,799.44	-59
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	7	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	23-Nov-26	1,949.86	0.00	1,949.86	-50
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	23-Nov-26	5,849.58	0.00	5,849.58	-50
METAL WORKS		16	100%	28.57%	23-Jul-26	01-Sep-26	16-Sep-26 A	21-Oct-26	13,649.02	3,899.72	13,649.02	-42
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	4	100%	0%	24-Aug-26	27-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-46
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	23-Jul-26	27-Jul-26	06-Oct-26	10-Oct-26	3,899.72	0.00	3,899.72	-63
MLTX-02-005-CN-111	Installation of Galvanized Steel Roof Scupper	4	100%	100%	29-Aug-26	01-Sep-26	16-Sep-26 A	16-Sep-26 A	3,899.72	3,899.72	3,899.72	-13
FINISHING WORKS		77	100%	24.42%	06-Aug-26	20-Sep-26	10-Aug-26 A	18-Nov-26	166,130.97	40,563.60	166,130.97	-50
FLOOR FINISHES		34	100%	0%	12-Aug-26	20-Sep-26	11-Oct-26	18-Nov-26	17,159.03	0.00	17,159.03	-50
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	12-Aug-26	13-Aug-26	11-Oct-26	12-Oct-26	11,894.39	0.00	11,894.39	-50
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	15-Aug-26	18-Aug-26	13-Oct-26	17-Oct-26	2,924.82	0.00	2,924.82	-50
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	1,169.94	0.00	1,169.94	-50
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	19-Aug-26	23-Aug-26	18-Oct-26	21-Oct-26	1,169.88	0.00	1,169.88	-50
WALL FINISHES		76	100%	30.27%	06-Aug-26	19-Sep-26	10-Aug-26 A	17-Nov-26	134,001.04	40,563.60	134,001.04	-50
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	26-Aug-26	31-Aug-26	18-Oct-26	22-Oct-26	2,275.00	0.00	2,275.00	-44
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	100%	0%	09-Sep-26	16-Sep-26	08-Nov-26	15-Nov-26	13,649.02	0.00	13,649.02	-50
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	22-Aug-26	23-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-46
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	5	100%	100%	06-Aug-26	11-Aug-26	10-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	-7
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	4	100%	100%	06-Aug-26	10-Aug-26	15-Aug-26 A	29-Aug-26 A	6,551.63	6,551.63	6,551.63	-15
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	0%	18-Aug-26	25-Aug-26	10-Oct-26	17-Oct-26	35,825.58	0.00	35,825.58	-44
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	5	100%	100%	15-Aug-26	19-Aug-26	20-Sep-26 A	26-Sep-26 A	15,696.35	15,696.35	15,696.35	-31
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	01-Sep-26	08-Sep-26	31-Oct-26	07-Nov-26	31,197.60	0.00	31,197.60	-50
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	0%	17-Sep-26	19-Sep-26	16-Nov-26	17-Nov-26	2,340.00	0.00	2,340.00	-50
CELLING FINISHES		10	100%	0%	12-Aug-26	03-Sep-26	06-Oct-26	17-Oct-26	14,970.90	0.00	14,970.90	-36
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	0%	12-Aug-26	15-Aug-26	06-Oct-26	08-Oct-26	5,771.52	0.00	5,771.52	-46
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	0%	01-Sep-26	03-Sep-26	14-Oct-26	17-Oct-26	3,427.86	0.00	3,427.86	-36
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	24-Aug-26	31-Aug-26	06-Oct-26	13-Oct-26	5,771.52	0.00	5,771.52	-36
SPECIALTIES WORK		24	100%	0%	26-Aug-26	22-Sep-26	25-Oct-26	21-Nov-26	58,495.83	0.00	58,495.83	-50
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	100%	0%	09-Sep-26	12-Sep-26	08-Nov-26	10-Nov-26	24,373.26	0.00	24,373.26	-50
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	26-Aug-26	31-Aug-26	25-Oct-26	29-Oct-26	14,623.96	0.00	14,623.96	-50
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	100%	0%	20-Sep-26	22-Sep-26	18-Nov-26	21-Nov-26	19,498.61	0.00	19,498.61	-50
TESTING & COMMISSIONING		40	0%	0%	24-Oct-26	26-Dec-26	25-Feb-27	15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	31-Mar-27	15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	10	0%	0%	24-Oct-26	03-Nov-26	25-Feb-27	08-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	11	0%	0%	24-Oct-26	04-Nov-26	25-Feb-27	09-Mar-27	0.00	0.00	0.00	-106
HASA OASIS		238	55.28%	38.98%	03-Mar-26	02-Jan-27	04-Mar-26 A	06-Apr-27	5,518,703.57	3,890,949.37	9,982,829.07	-77
MOBILIZATION		24	0%	0%	03-Mar-26	02-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
TOPOGRAPHIC SURVEY		5	0%	0%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-1860	Site Survey Works	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
SITE FACILITIES & OFFICES		23	0%	0%	03-Mar-26	01-Apr-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1740	Manpower Mobalization	5	100%	100%	28-Mar-26	01-Apr-26	29-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1750	Equipment Mobalization	7	100%	100%	25-Mar-26	01-Apr-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1770	Site Layout Plan	4	100%	100%	03-Mar-26	07-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1780	Clear & Grub for Offices & Access Road	3	100%	100%	08-Mar-26	10-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1790	Construct Site Access Roads	4	100%	100%	08-Mar-26	11-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1800	Construct Temporary Fence	7	100%	100%	11-Mar-26	18-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1810	Construct Site Offices & Storage	14	100%	100%	12-Mar-26	31-Mar-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1820	Install Project Signs	8	100%	100%	12-Mar-26	24-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1830	Install Site Facilities	4	100%	100%	19-Mar-26	26-Mar-26	24-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1840	Electrical Works & Connections	6	100%	100%	19-Mar-26	29-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-1850	Construct Parking Sheds	6	100%	100%	19-Mar-26	29-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	-1
PRELIMINARY SUBMITTALS		20	0%	0%	08-Mar-26	02-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
PREPARATIONS & SUBMITTAL BY CONTRACTORS		10	0%	0%	08-Mar-26	18-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-176	Preparation and Submittal of Detailed Work Order	10	100%	100%	08-Mar-26	18-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-187	Preparation and Submittal of Project Execution Plan	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-188	Submission of Contractor Project Quality Plan	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-189	Submission of Construction Safety & Environmental	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-190	Preparation and Submittal of Organization Chart	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-191	Preparation and Submittal of Communication Plan	8	100%	100%	08-Mar-26	16-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	-1
APPROVALS BY EMPLOYERS		12	0%	0%	17-Mar-26	02-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1

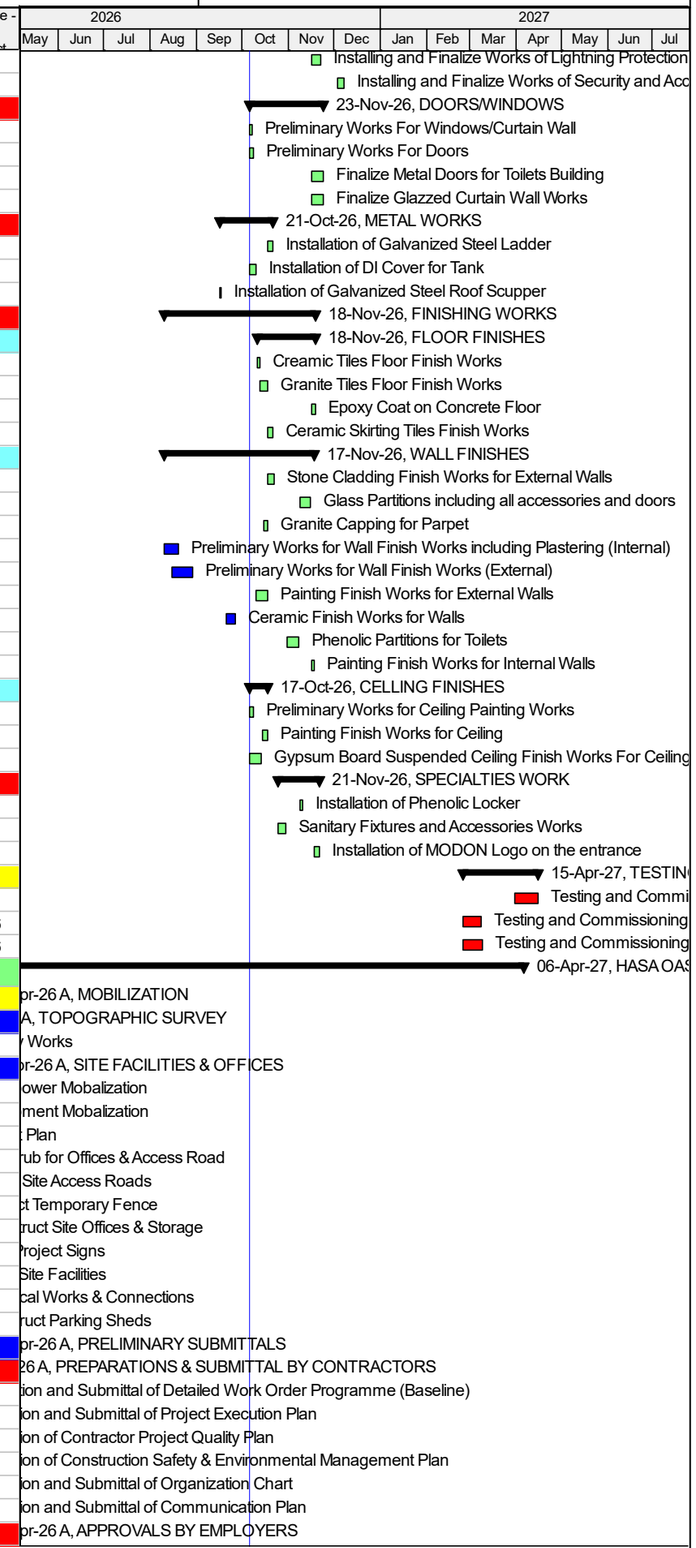

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-MB-192	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	19-Mar-26	02-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-193	Approval of Project Execution Plan	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-194	Approval of Contractor Project Quality Plan	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-195	Approval of Construction Safety & Environmental	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-196	Approval of Organization Chart	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
MLTX-02-005-MB-197	Approval of Communication Plan	10	100%	100%	17-Mar-26	31-Mar-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	-1
ENGINEERING		123	0%	0%	08-Mar-26	20-Sep-26	08-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS		122	0%	0%	09-Mar-26	20-Sep-26	09-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS SUBMISSION		110	0%	0%	09-Mar-26	06-Sep-26	09-Mar-26 A	09-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		15	0%	0%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Setting Out	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-7	Shop DWG Submittal for Standards Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		42	0%	0%	09-Mar-26	22-Apr-26	09-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-82
ARCHITECTURE WORKS		15	0%	0%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Ceiling Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Finishes Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Toilet Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
STRUCTURE WORKS		21	0%	0%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Foundation Plan	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Sections/Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MECHANCAL WORKS		27	0%	0%	30-Mar-26	22-Apr-26	15-Mar-26 A	07-Jul-26 A	0.00	0.00	0.00	-62
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for HVAC Equipment Schedule	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Fire Fighting Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN	Shop DWG Submittal for Drainage Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-32
MLTX-02-005-EN	Shop DWG Submittal for Drainage Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-32
MLTX-02-005-EN	Shop DWG Submittal for Dut Routing Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Diffusers Layout	21	100%	100%	30-Mar-26	22-Apr-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-62
ELECTRICAL WORKS		27	0%	0%	30-Mar-26	22-Apr-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	21	100%	100%	30-Mar-26	22-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	15	100%	100%	30-Mar-26	15-Apr-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Shop DWG Submittal for Lighting Installation Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Cable Tray Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Manhole & Ductbank Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Grounding Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Lightning Protection Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	15	100%	100%	30-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Grounding Layout	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Lightning Protection System Layout	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Telephone & Data Layout	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Shop DWG Submittal for Telephone & Data Riser Diagram	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		110	0%	0%	09-Mar-26	06-Sep-26	09-Mar-26 A	09-Nov-26	0.00	0.00	0.00	-54
ARCHITECTURE WORKS		41	0%	0%	09-Mar-26	05-Apr-26	09-Mar-26 A	13-Jul-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10

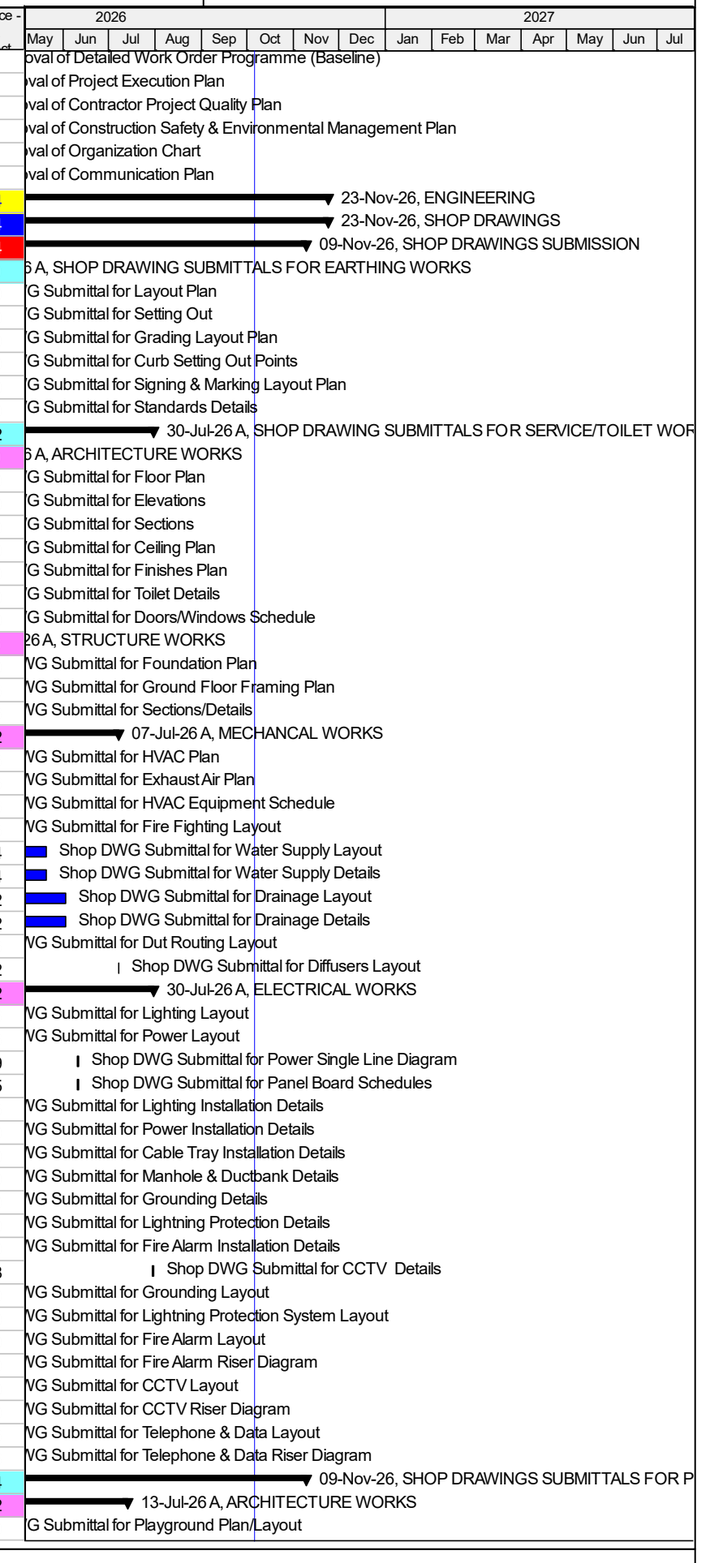

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Submittal for Furniture & Marking	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	28-Apr-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Interlock Pattern Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	21	100%	100%	09-Mar-26	05-Apr-26	13-Jul-26 A	13-Jul-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN	Shop DWG Submittal for Dome Internal Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-39
STRUCTURE WORKS		35	0%	0%	06-Apr-26	29-Apr-26	15-Mar-26 A	14-Jul-26 A	0.00	0.00	0.00	-62
MLTX-02-005-EN	Shop DWG Submittal for Air Dome System	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Shop DWG Submittal for Foundation of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-62
MLTX-02-005-EN	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-62
AIR DOME SYSTEM		21	0%	0%	06-Apr-26	29-Apr-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for Air Dome Structural Layout	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Shop DWG Submittal for Membrane Panel Layout	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for Cable Tension Layout	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for Airlock Door Details	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for Emergency Exit Details	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-22
SPORTS EQUIPMENT		21	0%	0%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Shop DWG Submittal for Football Turf Installation	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Shop DWG Submittal for Basketball Court Marking	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Shop DWG Submittal for Padel Court Structure	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MECHANCAL WORKS		21	0%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
ELECTRICAL WORKS		65	0%	0%	03-Aug-26	06-Sep-26	20-Aug-26 A	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for CCTV Details	21	100%	100%	03-Aug-26	26-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Submittal for CCTV Layout	21	100%	100%	03-Aug-26	26-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Shop DWG Submittal for CCTV Riser Diagram	21	100%	100%	03-Aug-26	26-Aug-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	5
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		57	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
ARCHITECTURE WORKS		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Landscape Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Hardscape Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN	Shop DWG Submittal for Planting Plan	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Shop DWG Submittal for Landscape Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MECHANCAL WORKS		30	0%	0%	09-Mar-26	15-Apr-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	-67
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Details	30	100%	100%	09-Mar-26	15-Apr-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	-67
MLTX-02-005-EN	Shop DWG Submittal for Irrigation Layout	30	100%	100%	09-Mar-26	15-Apr-26	06-Jul-26 A	06-Jul-26 A	0.00	0.00	0.00	-67
ELECTRICAL WORKS		30	0%	0%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	09-Mar-26	15-Apr-26	29-Jul-26 A	29-Jul-26 A	0.00	0.00	0.00	-87
SHOP DRAWINGS APPROVALS		107	0%	0%	30-Mar-26	20-Sep-26	15-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWING APPROVAL FOR EARTHING WORKS		90	0%	0%	16-Apr-26	02-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	105
MLTX-02-005-EN-1	Shop DWG Approval for Layout Plan	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN-1	Shop DWG Approval for Setting Out	15	100%	100%	04-May-26	20-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN-1	Shop DWG Approval for Grading Layout Plan	15	100%	100%	21-May-26	10-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	60
MLTX-02-005-EN-1	Shop DWG Approval for Curb Setting Out Points	15	100%	100%	11-Jun-26	28-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	75
MLTX-02-005-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	15	100%	100%	29-Jun-26	15-Jul-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	90
MLTX-02-005-EN-1	Shop DWG Approval for Standards Details	15	100%	100%	16-Jul-26	02-Aug-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	105
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		63	0%	0%	30-Mar-26	06-Jun-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-47
ARCHITECTURE WORKS		56	0%	0%	30-Mar-26	06-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	22-Apr-26	30-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30

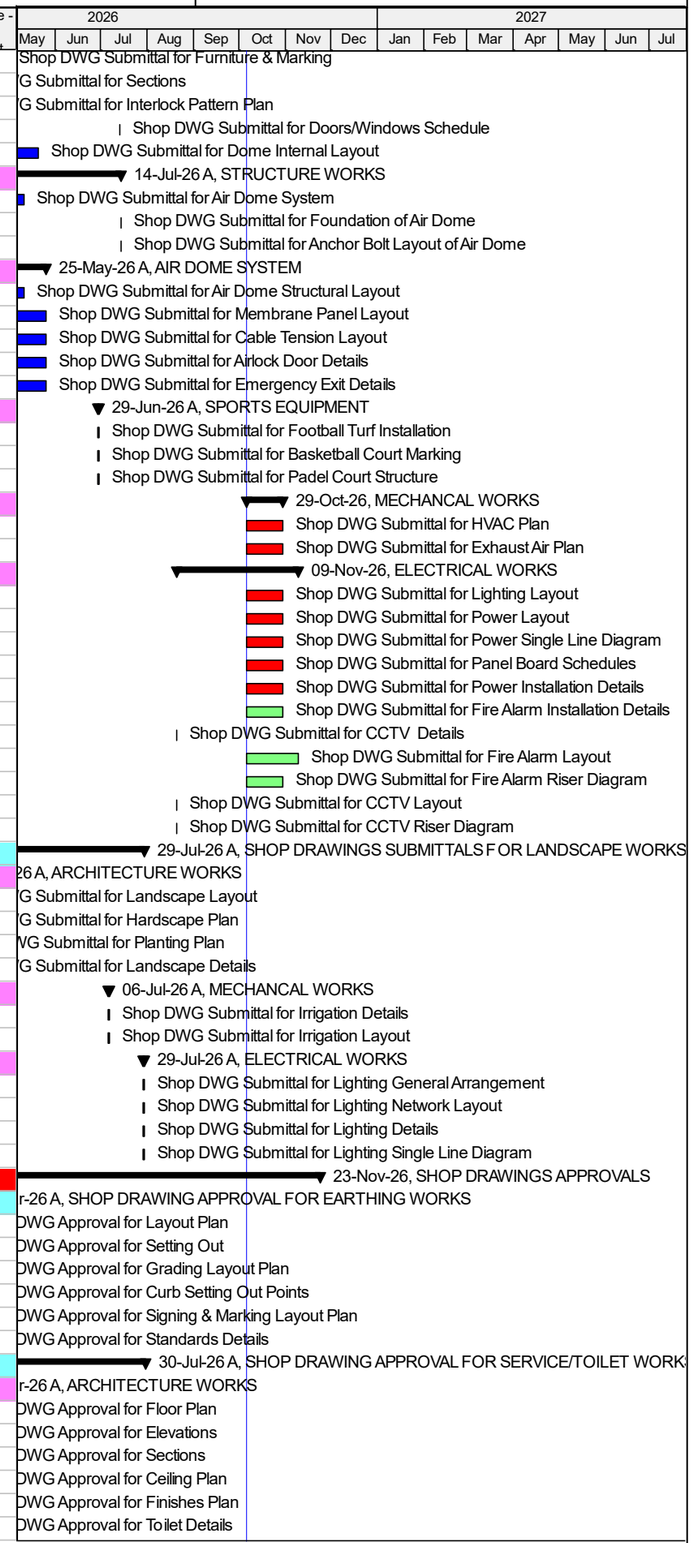

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	29-Apr-26	06-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	56
STRUCTURE WORKS		27	0%	0%	16-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Foundation Plan	15	100%	100%	16-Apr-26	03-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	25
MLTX-02-005-EI	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Sections/Details	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MECHANCAL WORKS		36	0%	0%	23-Apr-26	17-May-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	21	100%	100%	23-Apr-26	17-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for HVAC Equipment Schedule	21	100%	100%	23-Apr-26	17-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
MLTX-02-005-EI	Shop DWG Approval for Fire Fighting Layout	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Water Supply Layout	21	100%	100%	23-Apr-26	17-May-26	03-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EI	Shop DWG Approval for Water Supply Details	21	100%	100%	23-Apr-26	17-May-26	03-Jun-26 A	03-Jun-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EI	Shop DWG Approval for Drainage Layout	21	100%	100%	23-Apr-26	17-May-26	30-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EI	Shop DWG Approval for Drainage Details	21	100%	100%	23-Apr-26	17-May-26	30-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EI	Shop DWG Approval for Duct Routing Layout	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Diffusers Layout	21	100%	100%	23-Apr-26	17-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
ELECTRICAL WORKS		51	0%	0%	16-Apr-26	20-May-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for Lighting Layout	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Power Layout	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Power Single Line Diagram	21	100%	100%	23-Apr-26	17-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
MLTX-02-005-EI	Shop DWG Approval for Panel Board Schedules	30	100%	100%	16-Apr-26	20-May-26	22-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-51
MLTX-02-005-EI	Shop DWG Approval for Lighting Installation Details	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Power Installation Details	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Cable Tray Installation Details	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for Manhole & Ductbank Details	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for Grounding Details	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection Details	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Installation Details	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for CCTV Details	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for Grounding Layout	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Lightning Protection System Layout	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Layout	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for Fire Alarm Riser Diagram	30	100%	100%	16-Apr-26	20-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	40
MLTX-02-005-EI	Shop DWG Approval for CCTV Layout	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Layout	21	100%	100%	23-Apr-26	17-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	37
MLTX-02-005-EI	Shop DWG Approval for Telephone & Data Riser Diagram	21	100%	100%	23-Apr-26	17-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-61
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		107	0%	0%	30-Mar-26	20-Sep-26	15-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-54
ARCHITECTURE WORKS		36	0%	0%	30-Mar-26	10-May-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-12
MLTX-02-005-EI	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EI	Shop DWG Approval for Furniture & Marking	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EI	Shop DWG Approval for Sections	20	100%	100%	30-Mar-26	21-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EI	Shop DWG Approval for Interlock Pattern Plan	30	100%	100%	06-Apr-26	10-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	36
MLTX-02-005-EI	Shop DWG Approval for Doors/Windows Schedule	20	100%	100%	06-Apr-26	28-Apr-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Shop DWG Approval for Dome Internal Layout	30	100%	100%	06-Apr-26	10-May-26	15-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-12
STRUCTURE WORKS		35	0%	0%	30-Apr-26	24-May-26	24-Mar-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EI	Shop DWG Approval for Air Dome System	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EI	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EI	Shop DWG Approval for Anchor Bolt Layout of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
AIR DOME SYSTEM		21	0%	0%	30-Apr-26	24-May-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Air Dome Structural Layout	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EI	Shop DWG Approval for Membrane Panel Layout	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Cable Tension Layout	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Airlock Door Details	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EI	Shop DWG Approval for Emergency Exit Details	21	100%	100%	30-Apr-26	24-May-26	24-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-1
SPORTS EQUIPMENT		74	0%	0%	30-Apr-26	07-Jun-26	20-Jul-26 A	29-Oct-26	0.00	0.00	0.00	-123
MLTX-02-005-EI	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EI	Shop DWG Approval for Basketball Court Marking	30	100%	100%	30-Apr-26	07-Jun-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-68
MLTX-02-005-EI	Shop DWG Approval for Padel Court Structure	30	100%	100%	30-Apr-26	07-Jun-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	-37
MECHANCAL WORKS		21	0%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EI	Shop DWG Approval for HVAC Plan	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EI	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
ELECTRICAL WORKS		72	0%	0%	27-Aug-26	20-Sep-26	25-Aug-26 A	23-Nov-26	0.00	0.00	0.00	-54

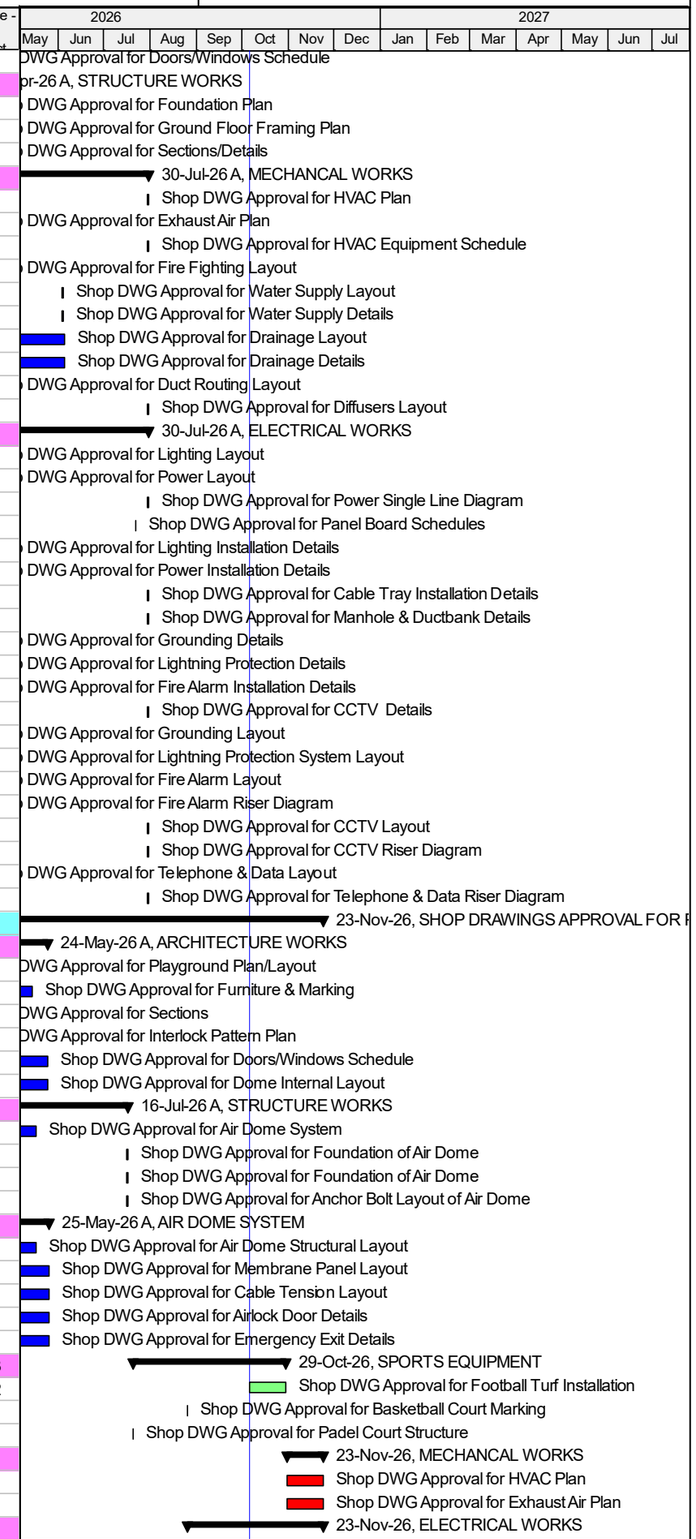


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Approval for Power Layout	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	21	100%	100%	27-Aug-26	20-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	21	100%	100%	27-Aug-26	20-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	21	100%	100%	27-Aug-26	20-Sep-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	22
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		72	0%	0%	30-Mar-26	20-May-26	15-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
ARCHITECTURE WORKS		30	0%	0%	30-Mar-26	03-May-26	15-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Landscape Layout	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Hardscape Plan	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Planting Plan	15	100%	100%	16-Apr-26	03-May-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Landscape Details	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MECHANCAL WORKS		30	0%	0%	16-Apr-26	20-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Shop DWG Approval for Irrigation Details	30	100%	100%	16-Apr-26	20-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN	Shop DWG Approval for Irrigation Layout	30	100%	100%	16-Apr-26	20-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-39
ELECTRICAL WORKS		30	0%	0%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Details	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
METHOD STATEMENTS		94	0%	0%	08-Mar-26	27-Jun-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-66
METHOD STATEMENT SUBMITTAL		60	0%	0%	08-Mar-26	19-May-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-11
CIVIL WORKS		21	0%	0%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Concrete	21	100%	100%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	15
ARCHITECTURE WORKS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Plastering	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	9
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-32
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Tilling	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	17-May-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Parking	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Soft	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-48
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Fence	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	08-Mar-26	14-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Metal	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-48
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Partitions	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-48
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Gypsum	21	100%	100%	08-Mar-26	04-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-48
MECHANICAL WORKS		27	0%	0%	29-Mar-26	28-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	29-Mar-26	21-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Water	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Fire	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	29-Mar-26	14-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-41
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for HVAC	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-29
ELECTRICAL WORKS		39	0%	0%	05-Apr-26	19-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Electrical	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-7	Preparation & Submission of Method Statement for Lighting	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for CCTV	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Lighting	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EN-8	Preparation & Submission of Method Statement for Panel	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-11
METHOD STATEMENT APPROVAL		79	0%	0%	29-Mar-26	27-Jun-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-66
CIVIL WORKS		36	0%	0%	29-Mar-26	09-May-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-1	Approval of Method Statement for Earthwork	15	100%	100%	29-Mar-26	14-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN-1	Approval of Method Statement for Concrete Works	30	100%	100%	05-Apr-26	09-May-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN-1	Approval of Method Statement for Waterproofing	21	100%	100%	05-Apr-26	28-Apr-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-2
ARCHITECTURE WORKS		79	0%	0%	29-Mar-26	19-May-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EN-1	Approval of Method Statement for Plastering Works	30	100%	100%	29-Mar-26	02-May-26	14-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN-1	Approval of Method Statement for Masonary Works	30	100%	100%	05-Apr-26	09-May-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-11

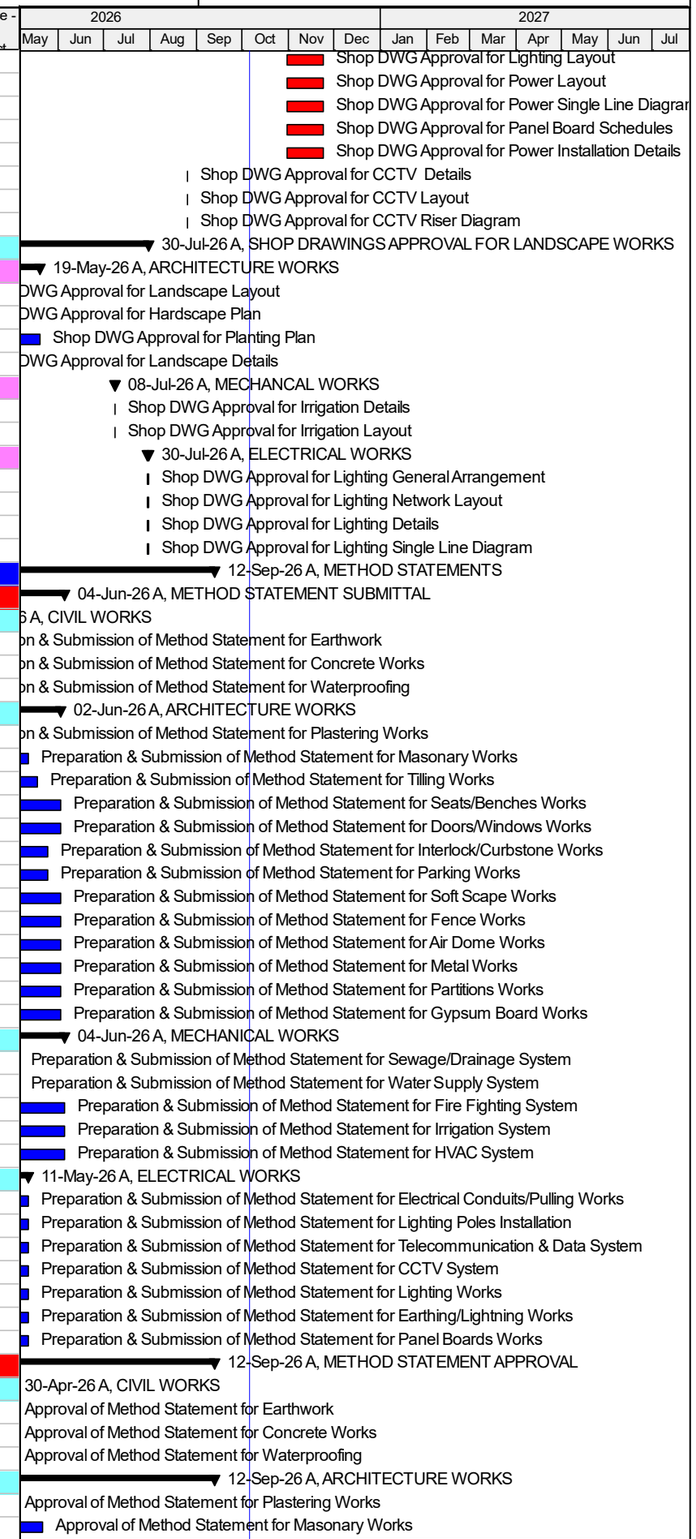


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-1	Approval of Method Statement for Tilling Works	30	100%	100%	15-Apr-26	19-May-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN-1	Approval of Method Statement for Seats/Benches Works	30	100%	100%	15-Apr-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EN-1	Approval of Method Statement for Doors/Windows Works	30	100%	100%	15-Apr-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EN-1	Approval of Method Statement for Interlock/Curbstone Works	30	100%	100%	05-Apr-26	09-May-26	15-Aug-26 A	15-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EN-1	Approval of Method Statement for Parking Works	30	100%	100%	15-Apr-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EN-1	Approval of Method Statement for Soft Scape Works	30	100%	100%	05-Apr-26	09-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-105
MLTX-02-005-EN-1	Approval of Method Statement for Fence Works	30	100%	100%	15-Apr-26	19-May-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-68
MLTX-02-005-EN-1	Approval of Method Statement for Air Dome Works	30	100%	100%	15-Apr-26	19-May-26	11-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-52
MLTX-02-005-EN-1	Approval of Method Statement for Partitions Works	30	100%	100%	05-Apr-26	09-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-105
MLTX-02-005-EN-1	Approval of Method Statement for Gypsum Board Works	30	100%	100%	05-Apr-26	09-May-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-86
MECHANICAL WORKS		50	0%	0%	15-Apr-26	23-May-26	02-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	-79
MLTX-02-005-EN-1	Approval of Method Statement for Sewage/Drainage System	21	100%	100%	22-Apr-26	16-May-26	09-Jun-26 A	09-Jun-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EN-1	Approval of Method Statement for Water Supply System	21	100%	100%	29-Apr-26	23-May-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EN-1	Approval of Method Statement for Fire Fighting System	21	100%	100%	29-Apr-26	23-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-79
MLTX-02-005-EN-1	Approval of Method Statement for Irrigation System	15	100%	100%	15-Apr-26	02-May-26	28-Jun-26 A	28-Jun-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EN-1	Approval of Method Statement for HVAC System	21	100%	100%	29-Apr-26	23-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-78
ELECTRICAL WORKS		58	0%	0%	29-Apr-26	27-Jun-26	12-Jul-26 A	26-Aug-26 A	0.00	0.00	0.00	-52
MLTX-02-005-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	21	100%	100%	29-Apr-26	23-May-26	12-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Poles Installation	21	100%	100%	29-Apr-26	23-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-79
MLTX-02-005-EN-1	Approval of Method Statement for Telecommunication & Data	30	100%	100%	20-May-26	27-Jun-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Approval of Method Statement for CCTV System	30	100%	100%	20-May-26	27-Jun-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Works	21	100%	100%	29-Apr-26	23-May-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-65
MLTX-02-005-EN-1	Approval of Method Statement for Earthing/Lightning Works	21	100%	100%	29-Apr-26	23-May-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-65
MLTX-02-005-EN-1	Approval of Method Statement for Panel Boards Works	21	100%	100%	29-Apr-26	23-May-26	12-Jul-26 A	22-Jul-26 A	0.00	0.00	0.00	-49
PRE-QUALIFICATION & MATERIAL		94	0%	0%	08-Mar-26	13-Jun-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-78
PRE-QUALIFICATION		45	0%	0%	08-Mar-26	02-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
TOILET/SERVICE WORKS		45	0%	0%	08-Mar-26	02-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
STEEL REINFORCEMENT		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
READY MIX CONCRETE		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
CONCRETE BLOCKS		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
WATER PROOFING		36	0%	0%	08-Mar-26	21-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	25
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	21	100%	100%	29-Mar-26	21-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	25
FLOOR/WALL TILES		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
SUSPENDED CEILING		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
DOORS/WINDOWS		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
FURNITURES		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
SANITARY FIXTURES		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
WATER SUPPLY PIPES		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
SEWAGE/DRAINAGE PIPES		30	0%	0%	08-Mar-26	14-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	08-Mar-26	28-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	11
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	19
PACKAGE AC UNITS		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
AIR DIFUSSERS/GRILLS		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3

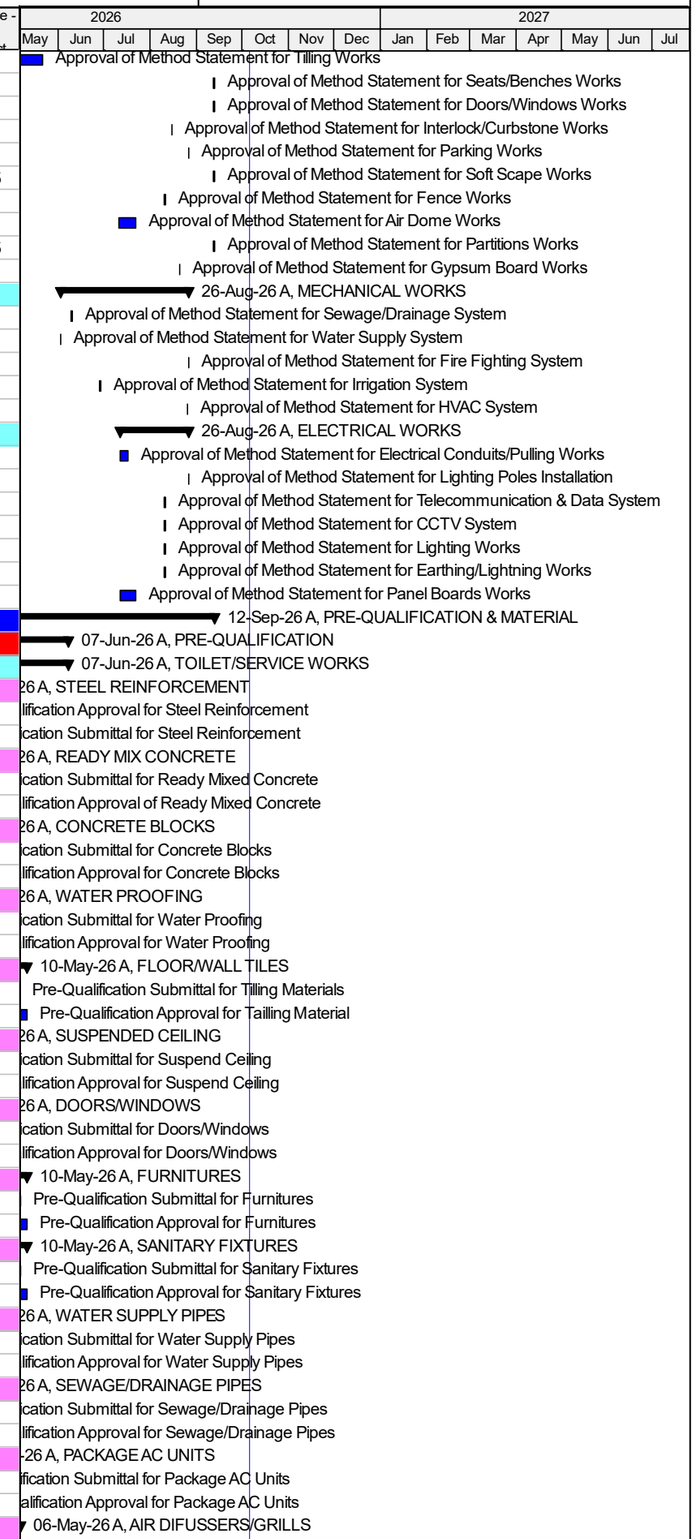

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EI	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EI	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
GALVANIZED DUCTS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-EI	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EI	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
EXHAUST FANS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EI	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
LIGHTING FIXTURES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EI	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
SWITCHES/SOCKETS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EI	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
EARTHING SYSTEM		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EI	Pre-Qualification Submittal for Earthing System	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EI	Pre-Qualification Approval for Earthing System	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
DISTRIBUTION PANNELS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EI	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Distribution Panels	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
PLAYGROUND WORKS		45	0%	0%	08-Mar-26	02-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
PVC MEMBRANE		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EI	Pre-Qualification Approval for PVC Membrane	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
STEEL TENSION CABLES		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EI	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
EMERGENCY DOORS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EI	Pre-Qualification Approval for Emergency Doors	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
PRESSURE UNITS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Submittal for Pressure Units	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EI	Pre-Qualification Approval for Pressure Units	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
AIR LOCK DOORS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Submittal for Lock Doors	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EI	Pre-Qualification Approval for Lock Doors	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-34
ARTIFICIAL TURF		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Approval for Artificial TURF	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
RUBBER GRANULES		36	0%	0%	08-Mar-26	21-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EI	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Approval for Rubber Granules	21	100%	100%	29-Mar-26	21-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-16
PADEL GLASS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Pre-Qualification Submittal for Padel Glass	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Approval for Padel Glass	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
PADEL WIRE MESH/STEEL SETS		30	0%	0%	08-Mar-26	14-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EI	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EI	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
AGGREGATE BASE COURSE		36	0%	0%	08-Mar-26	21-Apr-26	08-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EI	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	08-Mar-26	28-Mar-26	08-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-25
MLTX-02-005-EI	Pre-Qualification Approval for Aggregate Base Course	21	100%	100%	29-Mar-26	21-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-8
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-EI	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EI	Pre-Qualification Approval for the Site	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
INTERLOCKING PAVING		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	15
MLTX-02-005-EI	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	11-Apr-26 A	0.00	0.00	0.00	3
MLTX-02-005-EI	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	15
MARKING PAINT		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EI	Pre-Qualification Submittal for Marking Paint	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EI	Pre-Qualification Approval for Marking Paint	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
PACKAGE AC UNITS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EI	Pre-Qualification Submittal for Package AC Units	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EI	Pre-Qualification Approval for Package AC Units	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
AIR DIFUSSERS/GRILLS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28

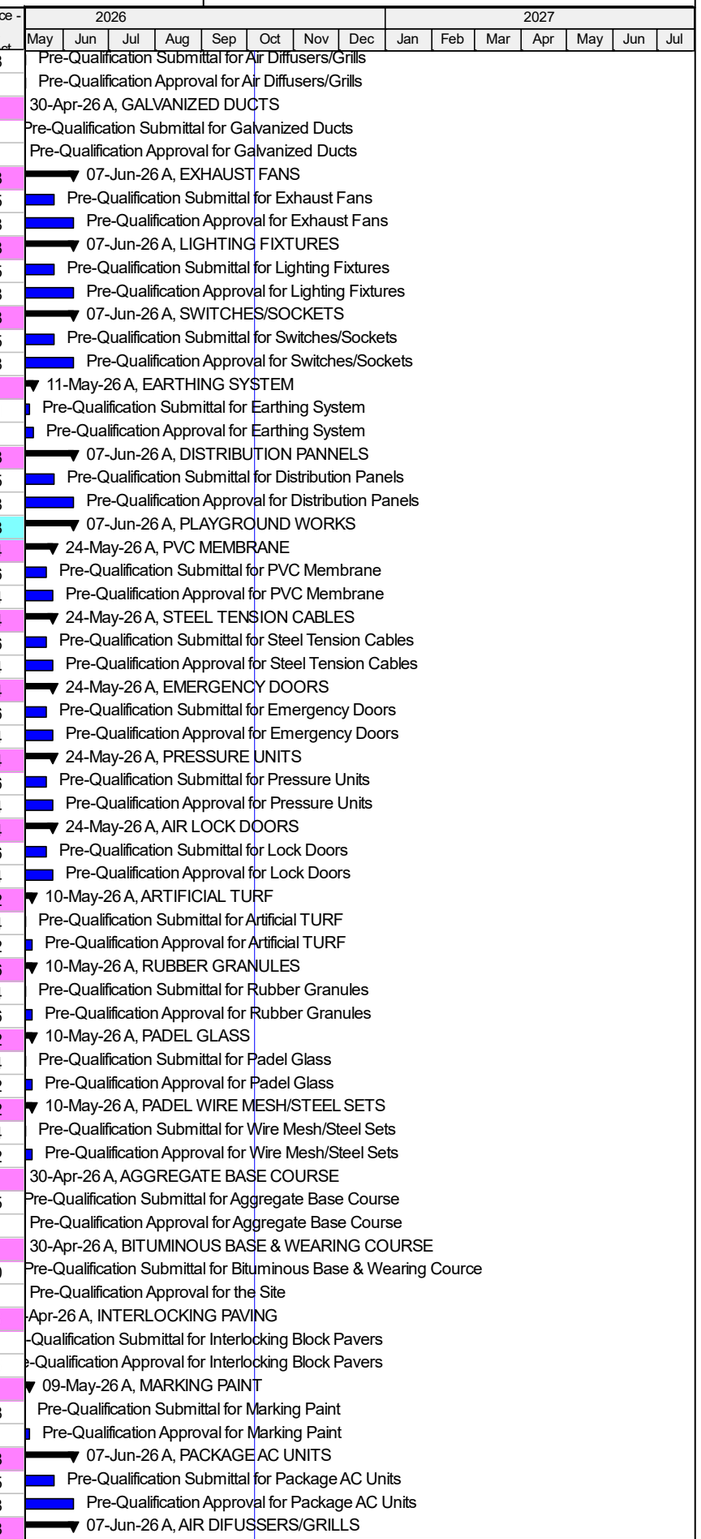

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
GALVANIZED DUCTS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	6
EXHAUST FANS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
DISTRIBUTION BOARDS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Boards	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
POWER CABLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Submittal for Power Cables	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Approval for Power Cables	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
LIGHT FIXTURES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for Light Fixtures	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
CCTV MATERIALS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN	Pre-Qualification Submittal for CCTV	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for CCTV	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
POWER OUTLETS/SWITCHES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-35
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-28
LANDSCAPE WORKS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	18-May-26 A	0.00	0.00	0.00	-14
INTERLOCKING PAVING		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
CURBSTONE		30	0%	0%	29-Mar-26	02-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	29-Mar-26	14-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	23
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	15-Apr-26	02-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	33
PAVEMENT MARKING		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
TRAFFIC SIGNS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-18
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-6
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-7
AGRICULTURE SOIL		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	07-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
TRACK SURFACE		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-10
GRASS/TREES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	18-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-25
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	18-May-26 A	0.00	0.00	0.00	-14
CABLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-8
LIGHT POLES		30	0%	0%	29-Mar-26	02-May-26	11-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	29-Mar-26	14-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	15-Apr-26	02-May-26	15-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-2
MATERIAL SUBMITTAL		84	0%	0%	15-Apr-26	13-Jun-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-78
TOILET/SERVICE WORKS		65	0%	0%	15-Apr-26	09-Jun-26	19-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
STEEL REINFORCEMENT		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
READY MIX CONCRETE		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
CONCRETE BLOCKS		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31



© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Concrete Blocks	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
FLOOR/WALL TILES		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
MLTX-02-005-EM	Material Submittal for Tilling Materials	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Material Approval for Tilling Material	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
SUSPENDED CEILING		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Material Submittal for Suspend Ceiling	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Approval for Suspend Ceiling	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
DOORS/WINDOWS		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Material Submittal for Doors/Windows	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Approval for Doors/Windows	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
FURNITURES		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
MLTX-02-005-EM	Material Submittal for Furnitures	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Furnitures	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
SANITARY FIXTURES		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
MLTX-02-005-EM	Material Submittal for Sanitary Fixtures	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Sanitary Fixtures	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	2
WATER SUPPLY PIPES		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Material Submittal for Water Supply Pipes	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Approval for Water Supply Pipes	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
SEWAGE/DRAINAGE PIPES		30	0%	0%	15-Apr-26	19-May-26	08-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EM	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	15-Apr-26	02-May-26	08-Jun-26 A	08-Jun-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EM	Material Approval for Sewage/Drainage Pipes	15	100%	100%	03-May-26	19-May-26	15-Jun-26 A	15-Jun-26 A	0.00	0.00	0.00	-20
PACKAGE AC UNITS		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
AIR DIFUSSERS/GRILLS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EM	Material Submittal for Air Diffusers/Grills	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Air Diffusers/Grills	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
GALVANIZED DUCTS		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Submittal for Galvanized Ducts	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Approval for Galvanized Ducts	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	31
EXHAUST FANS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
LIGHTING FIXTURES		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EM	Material Submittal for Lighting Fixtures	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Material Approval for Lighting Fixtures	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
SWITCHES/SOCKETS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EM	Material Submittal for Switches/Sockets	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Switches/Sockets	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
EARTHING SYSTEM		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Earthing System	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for Earthing System	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
DISTRIBUTION PANNELS		30	0%	0%	03-May-26	09-Jun-26	27-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EM	Material Submittal for Distribution Panels	15	100%	100%	03-May-26	19-May-26	27-Jul-26 A	27-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Distribution Panels	15	100%	100%	20-May-26	09-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-44
PLAYGROUND WORKS		84	0%	0%	15-Apr-26	13-Jun-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-78
PVC MEMBRANE		30	0%	0%	15-Apr-26	19-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
MLTX-02-005-EM	Material Submittal for PVC Membrane	15	100%	100%	15-Apr-26	02-May-26	24-Mar-26 A	26-Mar-26 A	0.00	0.00	0.00	31
MLTX-02-005-EM	Material Approval for PVC Membrane	15	100%	100%	03-May-26	19-May-26	28-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	39
STEEL TENSION CABLES		30	0%	0%	15-Apr-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Submittal for Steel Tension Cables	15	100%	100%	15-Apr-26	02-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Approval for Steel Tension Cables	15	100%	100%	03-May-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
EMERGENCY DOORS		28	0%	0%	15-Apr-26	19-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Submittal for Emergency Doors	15	100%	100%	15-Apr-26	02-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Approval for Emergency Doors	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
PRESSURE UNITS		30	0%	0%	15-Apr-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Submittal for Pressure Units	15	100%	100%	15-Apr-26	02-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-111
MLTX-02-005-EM	Material Approval for Pressure Units	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
AIR LOCK DOORS		28	0%	0%	15-Apr-26	19-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Submittal for Lock Doors	15	100%	100%	15-Apr-26	02-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-97
MLTX-02-005-EM	Material Approval for Lock Doors	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
ARTIFICIAL TURF		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
MLTX-02-005-EM	Material Submittal for Artificial TURF	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-11

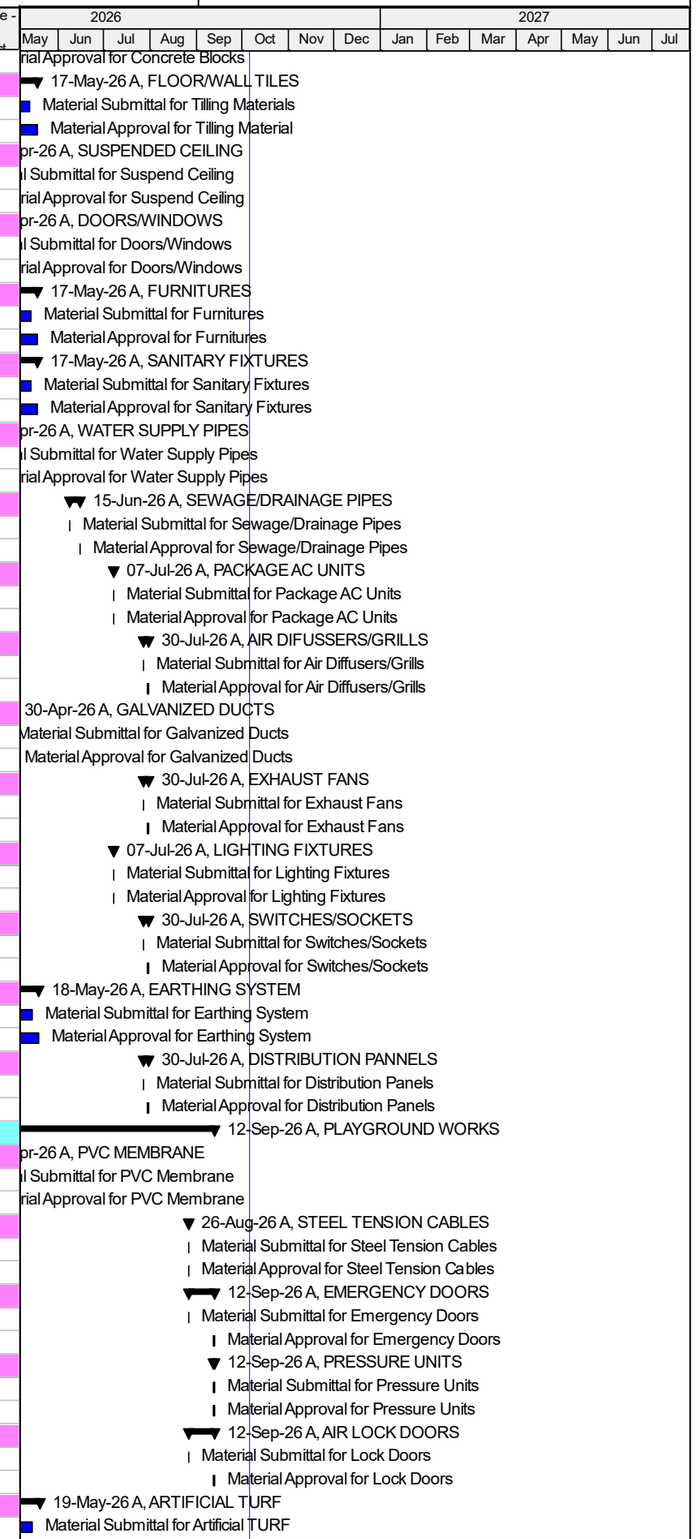

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Material Approval for Artificial TURF	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
RUBBER GRANULES		42	0%	0%	22-Apr-26	13-Jun-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	18
MLTX-02-005-EM	Material Submittal for Rubber Granules	21	100%	100%	22-Apr-26	16-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Approval for Rubber Granules	21	100%	100%	17-May-26	13-Jun-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	18
PADEL GLASS		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
PADEL WIRE MESH/STEEL SETS		30	0%	0%	15-Apr-26	19-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	15-Apr-26	02-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-11
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	03-May-26	19-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	0
AGGREGATE BASE COURSE		42	0%	0%	22-Apr-26	13-Jun-26	19-Mar-26 A	07-May-26 A	0.00	0.00	0.00	28
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	21	100%	100%	22-Apr-26	16-May-26	19-Mar-26 A	04-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Material Approval for Aggregate Base Course	21	100%	100%	17-May-26	13-Jun-26	26-Mar-26 A	07-May-26 A	0.00	0.00	0.00	28
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	04-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
INTERLOCKING PAVING		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	04-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	07-May-26 A	0.00	0.00	0.00	25
MARKING PAINT		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
PACKAGE AC UNITS		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
AIR DIFUSSERS/GRILLS		30	0%	0%	03-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
GALVANIZED DUCTS		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	05-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	23
EXHAUST FANS		30	0%	0%	03-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
DISTRIBUTION BOARDS		30	0%	0%	03-May-26	09-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-67
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	03-May-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	20-May-26	09-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-67
POWER CABLES		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
LIGHT FIXTURES		30	0%	0%	03-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	03-May-26	19-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-39
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	20-May-26	09-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-24
CCTV MATERIALS		28	0%	0%	03-May-26	09-Jun-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	03-May-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
POWER OUTLETS/SWITCHES		30	0%	0%	03-May-26	09-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-67
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	03-May-26	19-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-82
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	20-May-26	09-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-67
LANDSCAPE WORKS		84	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
INTERLOCKING PAVING		30	0%	0%	03-May-26	09-Jun-26	25-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	03-May-26	19-May-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	20-May-26	09-Jun-26	29-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
CURBSTONE		30	0%	0%	03-May-26	09-Jun-26	25-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	03-May-26	19-May-26	25-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	20-May-26	09-Jun-26	29-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	54
PAVEMENT MARKING		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
TRAFFIC SIGNS		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	16
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	03-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96

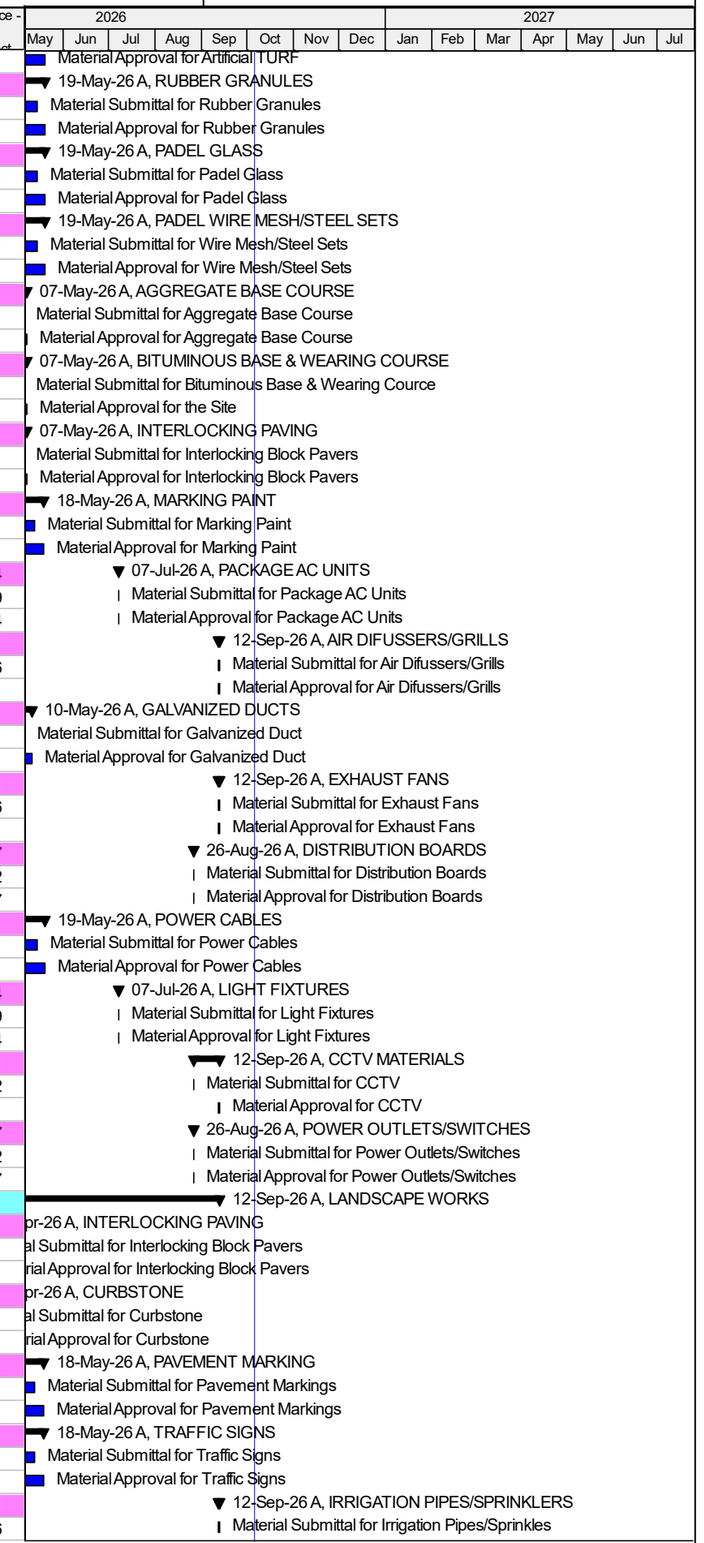


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
AGRICULTURE SOIL		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Material Submittal for Agriculture Soil	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Material Approval for Agriculture Soil	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	13
TRACK SURFACE		30	0%	0%	03-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EN	Material Submittal for Track Surface	15	100%	100%	03-May-26	19-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EN	Material Approval for Track Surface	15	100%	100%	20-May-26	09-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-81
GRASS/TREES		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Material Submittal for Grass/Trees	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Material Approval for Grass/Trees	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	13
CABLES		30	0%	0%	03-May-26	09-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Material Submittal for Cables	15	100%	100%	03-May-26	19-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EN	Material Approval for Cables	15	100%	100%	20-May-26	09-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	15
LIGHT POLES		30	0%	0%	03-May-26	09-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Material Submittal for Lighting poles	15	100%	100%	03-May-26	19-May-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EN	Material Approval for Lighting poles	15	100%	100%	20-May-26	09-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-27
PROCUREMENT		184	0%	0%	20-May-26	04-Nov-26	04-Apr-26 A	14-Feb-27	0.00	0.00	0.00	-87
SHORT LEAD ITEM		184	0%	0%	20-May-26	20-Oct-26	04-Apr-26 A	14-Feb-27	0.00	0.00	0.00	-100
TOILET/SERVICE WORKS		100	0%	0%	20-May-26	10-Aug-26	04-Apr-26 A	08-Nov-26	0.00	0.00	0.00	-76
STEEL REINFORCEMENT		55	0%	0%	20-May-26	03-Jun-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	Material Delivery of Steel Reinforcement	5	100%	100%	30-May-26	03-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-9	PO for Steel Reinforcement	5	100%	100%	20-May-26	25-May-26	04-Apr-26 A	18-May-26 A	0.00	0.00	0.00	6
CONCRETE BLOCKS		60	0%	0%	30-May-26	13-Jun-26	09-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-21
MLTX-02-005-PR-1	PO for Concrete Blocks	5	100%	100%	30-May-26	03-Jun-26	09-Apr-26 A	18-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery of Concrete Blocks	8	100%	100%	04-Jun-26	13-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-21
FLOOR/WALL TILES		18	0%	0%	04-Jun-26	24-Jun-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-49
MLTX-02-005-PR-1	PO for Tilling Materials	5	100%	100%	04-Jun-26	09-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-60
MLTX-02-005-PR-1	Material Delivery of Tailling Material	13	100%	100%	10-Jun-26	24-Jun-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-49
SUSPENDED CEILING		27	0%	0%	21-Jul-26	10-Aug-26	28-Jul-26 A	18-Aug-26 A	0.00	0.00	0.00	-7
MLTX-02-005-PR-1	PO for Suspend Ceiling	5	100%	100%	21-Jul-26	26-Jul-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-2
MLTX-02-005-PR-1	Material Delivery of Suspend Ceiling	13	100%	100%	27-Jul-26	10-Aug-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-7
DOORS/WINDOWS		20	0%	0%	10-Jun-26	02-Jul-26	15-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-68
MLTX-02-005-PR-1	PO for Doors/Windows	5	100%	100%	10-Jun-26	15-Jun-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Doors/Windows	15	100%	100%	16-Jun-26	02-Jul-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	-68
WATER SUPPLY PIPES		19	0%	0%	16-Jun-26	29-Jun-26	07-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-8
MLTX-02-005-PR-1	PO for Water Supply Pipes	5	100%	100%	16-Jun-26	21-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-005-PR-1	Material Delivery for Water Supply Pipes	7	100%	100%	22-Jun-26	29-Jun-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-8
SEWAGE/DRAINAGE PIPES		12	0%	0%	16-Jun-26	29-Jun-26	13-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	8
MLTX-02-005-PR-1	PO for Sewage/Drainage Pipes	5	100%	100%	16-Jun-26	21-Jun-26	20-Jun-26 A	20-Jun-26 A	0.00	0.00	0.00	1
MLTX-02-005-PR-1	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	22-Jun-26	29-Jun-26	13-Jun-26 A	13-Jun-26 A	0.00	0.00	0.00	14
SANITARY FIXTURES		18	0%	0%	22-Jun-26	12-Jul-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-14
MLTX-02-005-PR-1	PO for Sanitary Fixtures	5	100%	100%	22-Jun-26	27-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	Material Delivery for Sanitary Fixtures	13	100%	100%	28-Jun-26	12-Jul-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-14
PACKAGE AC UNITS		20	0%	0%	28-Jun-26	20-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	28-Jun-26	02-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	04-Jul-26	20-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	11
AIR DIFUSSERS/GRILLS		20	0%	0%	28-Jun-26	20-Jul-26	18-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	PO for Air Diffusers/Grills	5	100%	100%	28-Jun-26	02-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-005-PR-1	Material Delivery for Air Diffusers/Grills	15	100%	100%	04-Jul-26	20-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-27
GALVANIZED DUCTS		20	0%	0%	28-Jun-26	20-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-27
MLTX-02-005-PR-1	PO for Galvanized Ducts	5	100%	100%	28-Jun-26	02-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-42
MLTX-02-005-PR-1	Material Delivery for Galvanized Ducts	15	100%	100%	04-Jul-26	20-Jul-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-27
EXHAUST FANS		15	0%	0%	28-Jun-26	14-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-30
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	100%	28-Jun-26	02-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-40
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	10	100%	100%	04-Jul-26	14-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-30
LIGHTING FIXTURES		31	0%	0%	04-Jul-26	20-Jul-26	07-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	PO for Lighting Fixtures	5	100%	100%	04-Jul-26	08-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	09-Jul-26	20-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-75
SWITCHES/SOCKETS		12	0%	0%	09-Jul-26	22-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	09-Jul-26	14-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	15-Jul-26	22-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
EARTHING SYSTEM		27	0%	0%	10-Jun-26	11-Jul-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	PO for Earthing System	5	100%	100%	10-Jun-26	15-Jun-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-48
MLTX-02-005-PR-1	Material Delivery for Earthing System	15	100%	100%	24-Jun-26	11-Jul-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-26

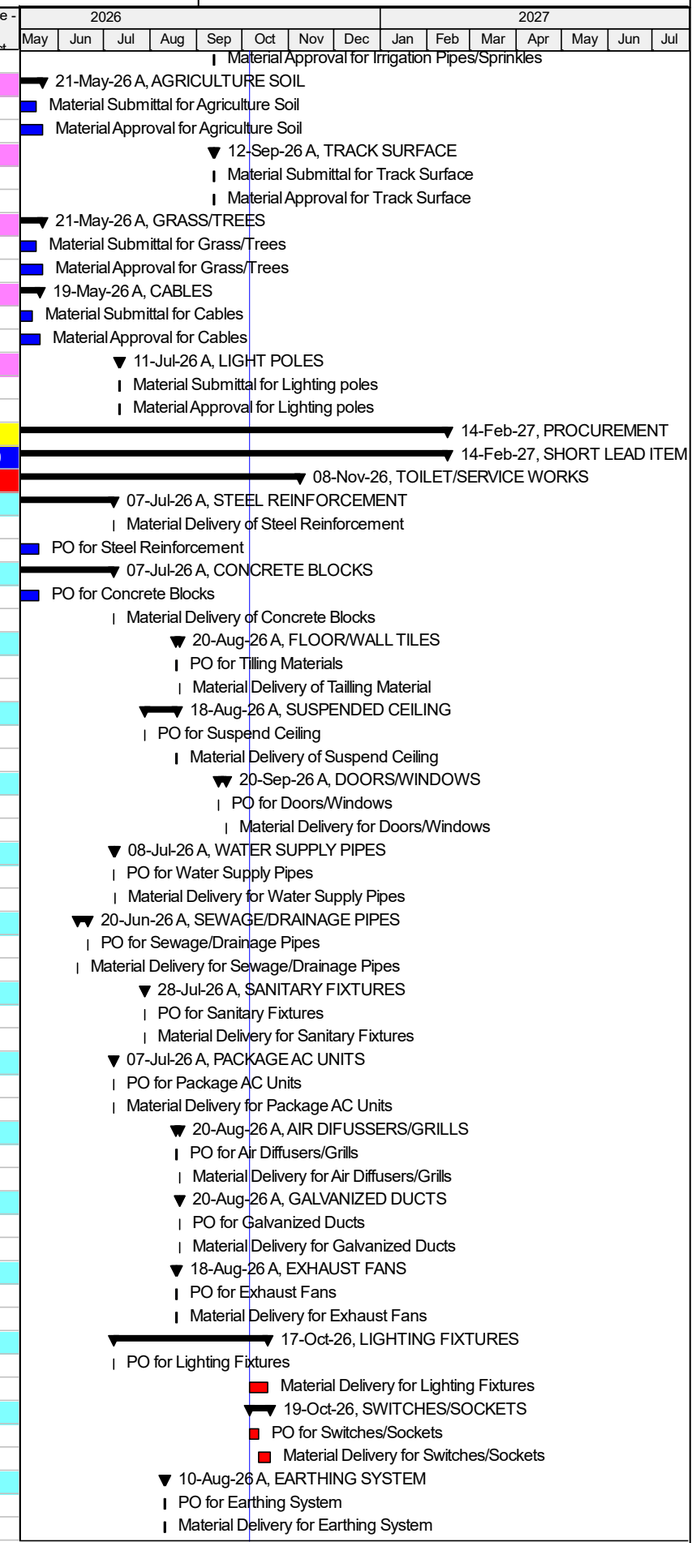

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION PANNELS		20	0%	0%	10-Jun-26	02-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	10-Jun-26	15-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	16-Jun-26	02-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
FURNITURES		29	0%	0%	04-Jul-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	04-Jul-26	13-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	14-Jul-26	05-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
PLAYGROUND WORKS		121	0%	0%	20-May-26	19-Aug-26	04-Apr-26 A	02-Dec-26	0.00	0.00	0.00	-89
PVC MEMBRANE		25	0%	0%	20-May-26	01-Jun-26	04-Apr-26 A	10-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	PO for PVC Membrane	4	100%	100%	20-May-26	24-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	4	100%	0%	25-May-26	01-Jun-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-111
ARTIFICIAL TURF		33	0%	0%	20-May-26	11-Jun-26	04-Apr-26 A	19-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Artificial TURF	5	100%	100%	20-May-26	25-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	30-May-26	11-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-110
RUBBER GRANULES		15	0%	0%	14-Jun-26	02-Jul-26	04-Apr-26 A	19-Oct-26	0.00	0.00	0.00	-92
MLTX-02-005-PR-1	PO for Rubber Granules	5	100%	100%	14-Jun-26	18-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	23
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	20-Jun-26	02-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-92
PADEL GLASS		39	0%	0%	20-May-26	18-Jun-26	04-Apr-26 A	26-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Padel Glass	5	100%	100%	20-May-26	25-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	30-May-26	18-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-110
PADEL WIRE MESH/STEEL SETS		31	0%	0%	30-May-26	21-Jun-26	09-Apr-26 A	22-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	PO for Wire Mesh/Steel Sets	5	100%	100%	30-May-26	03-Jun-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	04-Jun-26	21-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-105
AGGREGATE BASE COURSE		73	0%	0%	14-Jun-26	27-Jun-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
MLTX-02-005-PR-9	PO for Aggregate Base Course	5	100%	100%	14-Jun-26	18-Jun-26	04-Apr-26 A	14-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-PR-9	Material Delivery for Aggregate Base Course	7	100%	100%	20-Jun-26	27-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-9
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	10-Jun-26	23-Jun-26	15-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	-77
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	5	100%	100%	10-Jun-26	15-Jun-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for the Site	7	100%	100%	16-Jun-26	23-Jun-26	21-Sep-26 A	21-Sep-26 A	0.00	0.00	0.00	-77
INTERLOCKING PAVING		12	0%	0%	15-Jul-26	28-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-42
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	100%	15-Jul-26	20-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-49
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	7	100%	100%	21-Jul-26	28-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-42
MARKING PAINT		12	0%	0%	16-Jun-26	29-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	16-Jun-26	21-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	22-Jun-26	29-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
PACKAGE AC UNITS		20	0%	0%	04-Jul-26	26-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	16
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	04-Jul-26	08-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	1
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	09-Jul-26	26-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	16
AIR DIFUSSERS/GRILLS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
GALVANIZED DUCTS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
EXHAUST FANS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
DISTRIBUTION BOARDS		20	0%	0%	04-Jul-26	26-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	04-Jul-26	08-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	09-Jul-26	26-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
POWER CABLES		15	0%	0%	09-Jul-26	26-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	09-Jul-26	14-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	15-Jul-26	26-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-95
LIGHT FIXTURES		46	0%	0%	15-Jul-26	01-Aug-26	07-Jul-26 A	15-Nov-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-1	PO for Light Fixtures	5	100%	100%	15-Jul-26	20-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	21-Jul-26	01-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-90
CCTV MATERIALS		50	0%	0%	21-Jul-26	12-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	21-Jul-26	26-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	27-Jul-26	12-Aug-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-95
POWER OUTLETS/SWITCHES		21	0%	0%	27-Jul-26	19-Aug-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	27-Jul-26	02-Aug-26	20-Oct-26	26-Oct-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	03-Aug-26	19-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
LANDSCAPE WORKS		115	0%	0%	03-Aug-26	20-Oct-26	16-May-26 A	14-Feb-27	0.00	0.00	0.00	-100
INTERLOCKING PAVING		21	0%	0%	03-Aug-26	22-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	100%	03-Aug-26	08-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-16

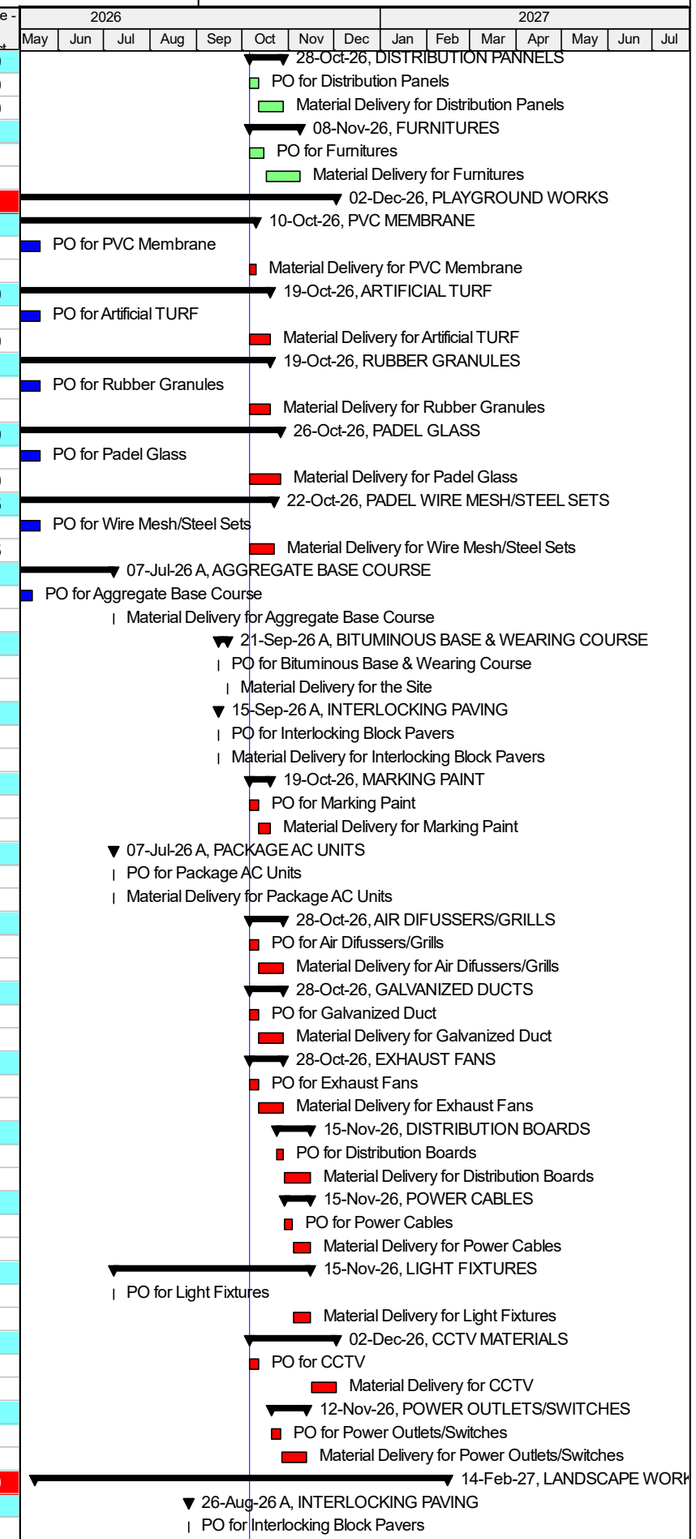

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	12	100%	100%	09-Aug-26	22-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-4
CURBSTONE		17	0%	0%	03-Aug-26	22-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	21
MLTX-02-005-PR-1	PO for Curbstone	5	100%	100%	03-Aug-26	08-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	9
MLTX-02-005-PR-1	Material Delivery for Curbstone	12	100%	100%	09-Aug-26	22-Aug-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	21
PAVEMENT MARKING		15	0%	0%	03-Aug-26	19-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	03-Aug-26	08-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	09-Aug-26	19-Aug-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-72
TRAFFIC SIGNS		14	0%	0%	04-Oct-26	19-Oct-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	PO for Traffic Signs	5	40%	0%	04-Oct-26	08-Oct-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	10-Oct-26	19-Oct-26	08-Nov-26	17-Nov-26	0.00	0.00	0.00	-25
IRRIGATION PIPES/SPRINKLERS		16	0%	0%	09-Aug-26	23-Aug-26	17-Jun-26 A	21-Jul-26 A	0.00	0.00	0.00	28
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	100%	09-Aug-26	13-Aug-26	17-Jun-26 A	17-Jun-26 A	0.00	0.00	0.00	49
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	100%	15-Aug-26	23-Aug-26	21-Jul-26 A	21-Jul-26 A	0.00	0.00	0.00	28
AGRICULTURE SOIL		12	0%	0%	21-Sep-26	11-Oct-26	01-Oct-26 A	03-Oct-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-1	PO for Agriculture Soil	5	100%	100%	21-Sep-26	27-Sep-26	01-Oct-26 A	01-Oct-26 A	0.00	0.00	0.00	-4
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	12	58.33%	100%	28-Sep-26	11-Oct-26	03-Oct-26 A	03-Oct-26 A	0.00	0.00	0.00	7
TRACK SURFACE		31	0%	0%	03-Sep-26	20-Sep-26	16-May-26 A	27-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	PO for Track Surface	5	100%	100%	03-Sep-26	08-Sep-26	16-May-26 A	19-May-26 A	0.00	0.00	0.00	93
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	09-Sep-26	20-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-110
GRASS/TREES		26	0%	0%	28-Sep-26	20-Oct-26	17-May-26 A	14-Feb-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Grass/Trees	5	100%	100%	28-Sep-26	03-Oct-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	112
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	13.33%	0%	04-Oct-26	20-Oct-26	28-Jan-27	14-Feb-27	0.00	0.00	0.00	-100
CABLES		20	0%	0%	09-Aug-26	31-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	4
MLTX-02-005-PR-1	PO for Cables	5	100%	100%	09-Aug-26	13-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-11
MLTX-02-005-PR-1	Material Delivery for Cables	15	100%	100%	15-Aug-26	31-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	4
LONG LEAD ITEM		99	0%	0%	20-May-26	04-Nov-26	07-Jul-26 A	16-Jan-27	0.00	0.00	0.00	-62
PLAYGROUND WORKS		88	0%	0%	20-May-26	02-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-115
STEEL TENSION CABLES		65	0%	0%	20-May-26	06-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	20-May-26	01-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	25-Jun-26	29-Jul-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	02-Jun-26	24-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	7	100%	0%	30-Jul-26	06-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-115
EMERGENCY DOORS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
PRESSURE UNITS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
AIR LOCK DOORS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
LANDSCAPE WORKS		76	0%	0%	15-Aug-26	04-Nov-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	38
LIGHT POLES		76	0%	0%	15-Aug-26	04-Nov-26	07-Jul-26 A	20-Sep-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-1	Staging time	5	0%	100%	31-Oct-26	04-Nov-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	38
MLTX-02-005-PR-9	PO for Lighting poles	10	100%	100%	15-Aug-26	25-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	42
MLTX-02-005-PR-9	Material Fabrication for Lighting poles	30	100%	100%	26-Aug-26	30-Sep-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	29
MLTX-02-005-PR-9	Material Delivery for Lighting poles	25	16%	100%	01-Oct-26	29-Oct-26	20-Sep-26 A	20-Sep-26 A	0.00	0.00	0.00	33
CONSTRUCTION PHASE		224	55.28%	38.98%	29-Mar-26	28-Dec-26	04-Apr-26 A	21-Mar-27	5,518,703.57	3,890,949.37	9,982,829.07	-67
SITE WORKS		224	49.31%	35.71%	29-Mar-26	28-Dec-26	04-Apr-26 A	21-Mar-27	4,330,752.96	3,136,990.68	8,783,465.12	-67
EARTH WORKS		73	100%	100%	29-Mar-26	02-Jun-26	04-Apr-26 A	08-Aug-26 A	979,460.76	979,460.76	979,460.76	-56
MLTX-02-005-CN-118	Excavation (in all types of soil) including Compaction	21	100%	100%	29-Mar-26	21-Apr-26	06-Apr-26 A	12-Apr-26 A	182,051.70	182,051.70	182,051.70	9
MLTX-02-005-CN-118	Excavation (in all types of soil) including Compaction	20	100%	100%	15-Apr-26	07-May-26	04-Apr-26 A	02-Aug-26 A	350,569.47	350,569.47	350,569.47	-70
MLTX-02-005-CN-119	Excavation (in all types of soil) including Compaction	12	100%	100%	04-May-26	17-May-26	06-Apr-26 A	05-Aug-26 A	139,891.20	139,891.20	139,891.20	-66
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	22-Apr-26	14-May-26	13-Apr-26 A	03-May-26 A	125,667.86	125,667.86	125,667.86	11
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	19	100%	100%	09-May-26	02-Jun-26	06-Apr-26 A	08-Apr-26 A	76,629.23	76,629.23	76,629.23	44
MLTX-02-005-CN-119	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	18-May-26	30-May-26	21-Apr-26 A	08-Aug-26 A	104,651.30	104,651.30	104,651.30	-59
LANDSCAPE WORKS		222	43.27%	27.1%	16-May-26	28-Dec-26	16-May-26 A	21-Mar-27	3,351,292.21	2,099,036.60	7,745,511.03	-67
PLAYGROUND AREA		218	61.37%	74.16%	16-May-26	28-Dec-26	18-May-26 A	16-Mar-27	819,147.49	989,944.11	1,334,839.53	-63

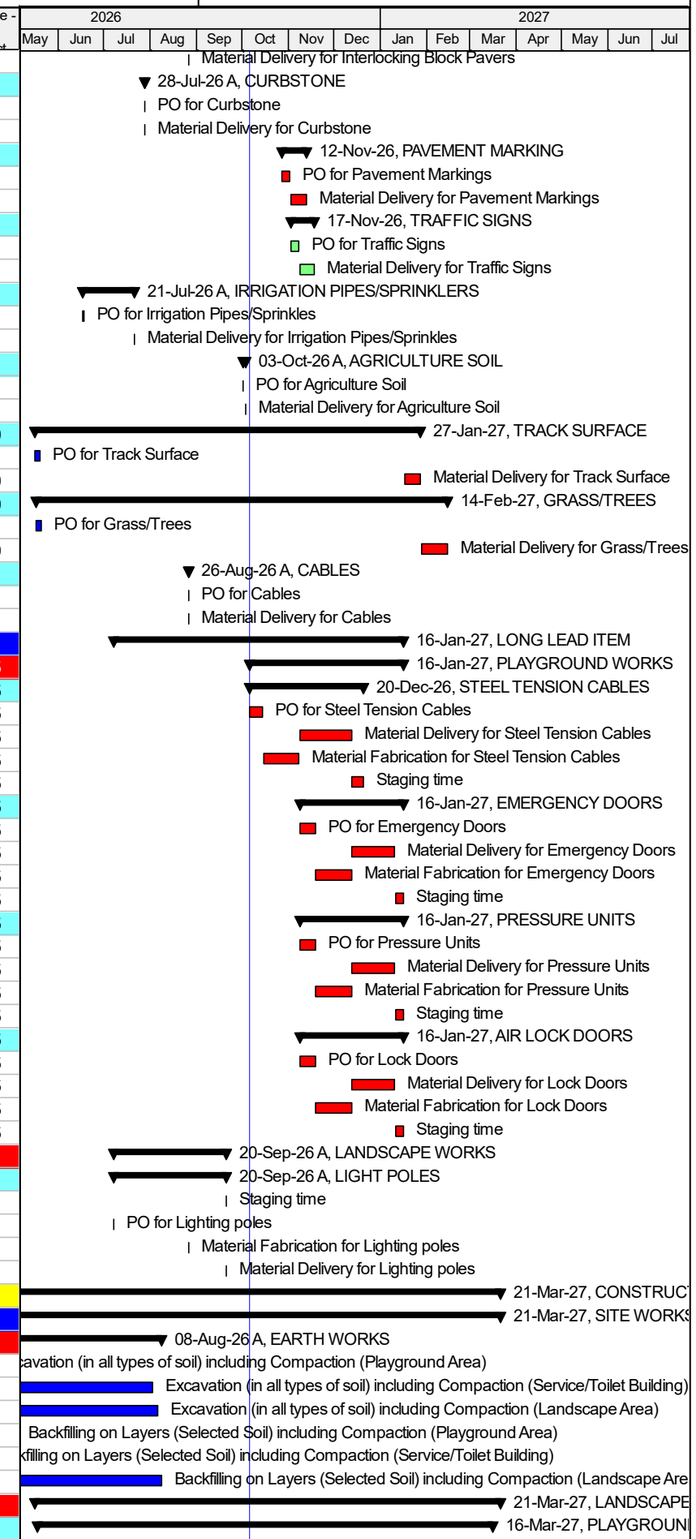

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FOOTBALL PLAYGROUND		174	67.69%	85%	16-May-26	24-Oct-26	18-May-26 A	05-Dec-26	214,466.49	269,322.49	316,849.99	-36
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	20	100%	100%	16-May-26	10-Jun-26	18-May-26 A	31-May-26 A	79,212.50	79,212.50	79,212.50	9
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	21	100%	100%	11-Jun-26	05-Jul-26	01-Jun-26 A	23-Jun-26 A	15,842.50	15,842.50	15,842.50	10
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	21	23.81%	100%	30-Sep-26	24-Oct-26	14-Sep-26 A	21-Sep-26 A	56,041.49	158,424.99	158,424.99	27
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	100%	0%	23-Jul-26	15-Aug-26	12-Nov-26	05-Dec-26	31,685.00	0.00	31,685.00	-95
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	20	100%	0%	30-Jun-26	22-Jul-26	20-Oct-26	11-Nov-26	15,842.50	0.00	15,842.50	-95
MLTX-02-005-CI	Aggregate basecourse layer (Football Playground)	21	100%	100%	06-Jul-26	29-Jul-26	24-Jun-26 A	27-Jun-26 A	15,842.50	15,842.50	15,842.50	28
PADEL PLAYGROUND		191	45%	70%	11-Jun-26	16-Dec-26	18-May-26 A	03-Jan-27	105,292.80	163,788.80	233,984.00	-15
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	20	100%	100%	11-Jun-26	04-Jul-26	18-May-26 A	31-May-26 A	81,894.40	81,894.40	81,894.40	29
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	21	100%	100%	06-Jul-26	29-Jul-26	01-Jun-26 A	23-Jun-26 A	11,699.20	11,699.20	11,699.20	31
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	0%	100%	25-Oct-26	17-Nov-26	30-Aug-26 A	30-Aug-26 A	0.00	58,496.00	58,496.00	67
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	18-Nov-26	05-Dec-26	06-Dec-26	22-Dec-26	0.00	0.00	58,496.00	-15
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	10	0%	0%	06-Dec-26	16-Dec-26	23-Dec-26	03-Jan-27	0.00	0.00	11,699.20	-15
MLTX-02-005-CI	Aggregate basecourse layer (Padel Playground)	21	100%	100%	30-Jul-26	23-Aug-26	23-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	48
BASKETBALL PLAYGROUND		167	65.83%	71.39%	05-Jul-26	14-Dec-26	18-May-26 A	16-Mar-27	223,045.41	241,875.35	338,831.45	-75
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	20	100%	100%	05-Jul-26	27-Jul-26	18-May-26 A	31-May-26 A	95,055.00	95,055.00	95,055.00	49
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	21	100%	100%	28-Jul-26	20-Aug-26	01-Jun-26 A	23-Jun-26 A	16,159.35	16,159.35	16,159.35	50
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	80.95%	100%	15-Sep-26	10-Oct-26	29-Aug-26 A	30-Aug-26 A	80,027.26	98,857.20	98,857.20	34
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	80,796.75	-86
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	06-Dec-26	14-Dec-26	24-Feb-27	04-Mar-27	0.00	0.00	16,159.35	-68
MLTX-02-005-CI	Aggregate basecourse layer (Basketball Playground)	21	100%	100%	22-Aug-26	14-Sep-26	23-Jun-26 A	28-Jun-26 A	31,803.80	31,803.80	31,803.80	67
PADEL FENCE		71	0%	30%	17-Dec-26	28-Dec-26	06-Aug-26 A	07-Nov-26	0.00	24,860.73	82,869.08	44
MLTX-02-005-CI	Excavation for Fence	8	0%	100%	17-Dec-26	26-Dec-26	06-Aug-26 A	06-Aug-26 A	0.00	8,286.91	8,286.91	120
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	0%	100%	17-Dec-26	24-Dec-26	15-Aug-26 A	19-Aug-26 A	0.00	16,573.82	16,573.82	108
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	17-Dec-26	23-Dec-26	06-Oct-26	12-Oct-26	0.00	0.00	4,143.45	62
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	33,147.63	44
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	16,573.82	44
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	17-Dec-26	22-Dec-26	27-Oct-26	01-Nov-26	0.00	0.00	4,143.45	44
CURBSTOEN/INTERLOCK		58	76.27%	80.07%	03-Sep-26	17-Oct-26	12-Aug-26 A	29-Oct-26	276,342.79	290,096.74	362,305.01	-11
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	52.38%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	180,520.67	-11
MLTX-02-005-CI	Concrete Works Under Curbstone	12	100%	100%	03-Sep-26	16-Sep-26	12-Aug-26 A	12-Aug-26 A	54,535.30	54,535.30	54,535.30	30
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	17-Sep-26	21-Sep-26	12-Aug-26 A	23-Aug-26 A	127,249.04	127,249.04	127,249.04	25
AIR DOME		144	49.52%	11.91%	27-Jul-26	09-Dec-26	16-May-26 A	21-Mar-27	2,417,363.79	581,544.30	4,881,359.87	-83
CIVIL WORKS		81	52.32%	29.58%	30-Jul-26	24-Oct-26	16-May-26 A	24-Nov-26	1,028,703.61	581,544.30	1,966,294.68	-27
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	15	100%	100%	30-Jul-26	16-Aug-26	16-May-26 A	01-Jun-26 A	127,762.34	127,762.34	127,762.34	65
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	15	100%	100%	17-Aug-26	02-Sep-26	22-Jul-26 A	21-Sep-26 A	168,176.84	168,176.84	168,176.84	-16
MLTX-02-005-CI	Cable System Installation (Air Dome)	2	100%	100%	03-Sep-26	05-Sep-26	21-Sep-26 A	21-Sep-26 A	41,790.29	41,790.29	41,790.29	-14
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	21	23.81%	0%	30-Sep-26	24-Oct-26	11-Oct-26	03-Nov-26	222,923.53	0.00	936,278.81	-9
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	50%	0%	30-Sep-26	11-Oct-26	14-Nov-26	24-Nov-26	224,235.79	0.00	448,471.57	-38
MLTX-02-005-CI	Perimeter Clamping System Installation	10	100%	100%	17-Sep-26	29-Sep-26	21-Sep-26 A	28-Sep-26 A	243,814.83	243,814.83	243,814.83	1
MECHANICAL WORKS		98	13.64%	0%	27-Jul-26	15-Nov-26	29-Oct-26	20-Feb-27	168,176.84	0.00	1,233,296.81	-83
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	20	0%	0%	12-Oct-26	03-Nov-26	17-Jan-27	08-Feb-27	0.00	0.00	728,766.30	-83
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	04-Nov-26	15-Nov-26	09-Feb-27	20-Feb-27	0.00	0.00	336,353.67	-83
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	20	100%	0%	27-Jul-26	18-Aug-26	29-Oct-26	21-Nov-26	168,176.84	0.00	168,176.84	-80
ELECTRICAL WORKS		58	80.63%	0%	03-Sep-26	15-Oct-26	03-Dec-26	08-Feb-27	1,220,483.34	0.00	1,513,591.54	-99
MLTX-02-005-CI	Light Fixture Works (Air Dome)	12	100%	0%	03-Sep-26	16-Sep-26	17-Jan-27	30-Jan-27	224,235.78	0.00	224,235.78	-115
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	14	85.71%	0%	21-Sep-26	07-Oct-26	17-Jan-27	01-Feb-27	144,151.58	0.00	168,176.84	-100
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	60%	0%	21-Sep-26	14-Oct-26	17-Jan-27	08-Feb-27	100,906.10	0.00	168,176.84	-100
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	60%	0%	21-Sep-26	14-Oct-26	17-Jan-27	08-Feb-27	302,718.31	0.00	504,530.51	-100
MLTX-02-005-CI	Control System Installation (Air Dome)	21	57.14%	0%	21-Sep-26	15-Oct-26	03-Dec-26	27-Dec-26	448,471.57	0.00	448,471.57	-62
FINISHES WORKS		68	0%	0%	17-Oct-26	09-Dec-26	28-Dec-26	21-Mar-27	0.00	0.00	168,176.84	-83
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	21	0%	0%	17-Oct-26	09-Nov-26	28-Dec-26	20-Jan-27	0.00	0.00	112,117.89	-62
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	21	0%	0%	16-Nov-26	09-Dec-26	21-Feb-27	21-Mar-27	0.00	0.00	56,058.95	-83
IRRIGATION NETWORK		79	25.8%	80.44%	22-Sep-26	17-Nov-26	18-Jul-26 A	17-Feb-27	39,321.33	122,596.50	152,414.87	-79
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	15	73.33%	100%	22-Sep-26	10-Oct-26	18-Jul-26 A	20-Jul-26 A	39,321.33	53,620.00	53,620.00	69
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	15	0%	100%	11-Oct-26	27-Oct-26	24-Aug-26 A	01-Sep-26 A	0.00	50,127.83	50,127.83	47
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	17-Oct-26	0.00	18,848.67	23,560.84	19
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	15-Nov-26	17-Nov-26	15-Feb-27	17-Feb-27	0.00	0.00	25,106.20	-79
NATURAL GROUND		76	0%	0%	09-Nov-26	17-Nov-26	22-Nov-26	17-Feb-27	0.00	0.00	191,740.00	-79
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	15-Nov-26	17-Nov-26	15-Feb-27	17-Feb-27	0.00	0.00	126,740.00	-79
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	09-Nov-26	14-Nov-26	22-Nov-26	26-Nov-26	0.00	0.00	65,000.00	-11
PLANTING		8	0%	21%	12-Oct-26	29-Oct-26	03-Oct-26 A	24-Feb-27	0.00	72,922.81	347,251.46	-100
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	5	0%	70%	12-Oct-26	17-Oct-26	03-Oct-26 A	11-Oct-26	0.00	72,922.81	104,175.44	5
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	27-Oct-26	29-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	141,732.50	-100

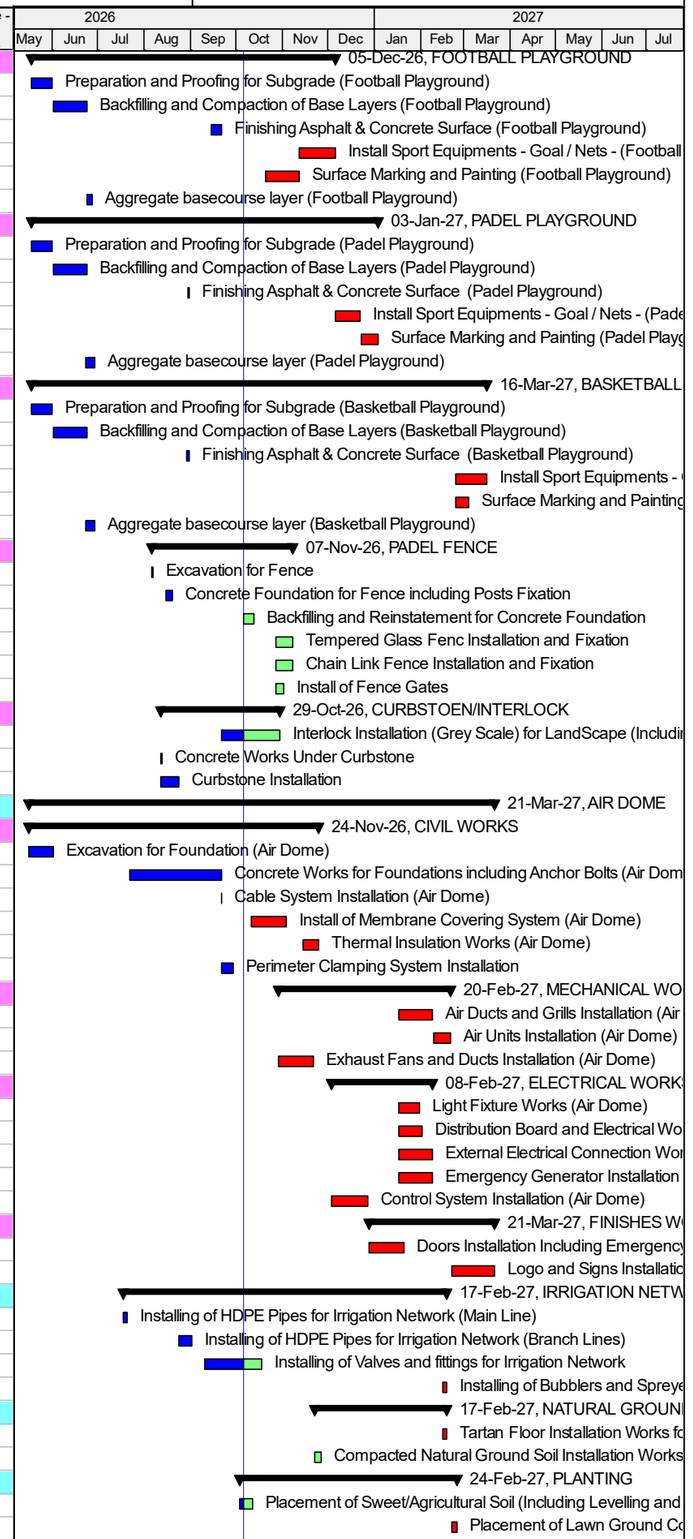

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	0%	0%	21-Oct-26	26-Oct-26	15-Feb-27	20-Feb-27	0.00	0.00	101,343.52	-100
WALKING/BIKE PATHS		8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	238,962.04	367,633.90	29
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	121,910.18	187,554.12	29
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	10-Jun-26 A	06-Oct-26	0.00	117,051.86	180,079.78	29
GENERAL/FURNITURE		163	16.05%	19.79%	22-Sep-26	10-Dec-26	03-Sep-26 A	25-Nov-26	75,459.60	93,066.84	470,271.40	13
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	29
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	02-Dec-26	09-Dec-26	18-Nov-26	25-Nov-26	0.00	0.00	9,749.30	12
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	29
MLTX-02-005-CN-1	Fixation and Installation of Benches	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	40,307.84	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	32,757.76	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	12,869.04	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	02-Dec-26	10-Dec-26	25-Oct-26	02-Nov-26	0.00	0.00	12,186.67	33
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	8	100%	100%	22-Sep-26	01-Oct-26	03-Sep-26 A	07-Sep-26 A	75,459.60	75,459.60	75,459.60	20
MLTX-02-005-CN-1	Installing of Site Light Poles	12	0%	10%	18-Nov-26	01-Dec-26	01-Oct-26 A	19-Oct-26	0.00	17,607.24	176,072.40	37
PARKING		148	0%	100%	18-Nov-26	01-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	63
MLTX-02-005-CN-119	Interlock Installation (8 Cm) for Parking Area (Including	7	0%	100%	24-Nov-26	01-Dec-26	10-Sep-26 A	19-Sep-26 A	0.00	40,945.33	40,945.33	63
MLTX-02-005-CN-119	Site Preparation & Compaction Under Interlock for Parking	5	0%	100%	18-Nov-26	23-Nov-26	14-May-26 A	30-Jun-26 A	0.00	17,548.00	17,548.00	124
TOILET/SERVICE BUILDING		117	99.05%	62.86%	03-Jun-26	21-Oct-26	24-May-26 A	21-Nov-26	1,187,950.61	753,958.69	1,199,363.95	-26
STRUCTURE WORKS		78	100%	100%	03-Jun-26	16-Jul-26	24-May-26 A	10-Aug-26 A	194,188.64	194,188.64	194,188.64	-21
CONCRETE WORKS		71	100%	100%	20-Jun-26	16-Jul-26	25-May-26 A	02-Jul-26 A	134,099.30	134,099.30	134,099.30	12
SUB-STRUCTURE		7	100%	100%	20-Jun-26	27-Jun-26	25-May-26 A	06-Jun-26 A	53,666.80	53,666.80	53,666.80	18
MLTX-02-005-CI	Plain Concrete Under Footing	2	100%	100%	20-Jun-26	21-Jun-26	25-May-26 A	31-May-26 A	17,106.85	17,106.85	17,106.85	18
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	22-Jun-26	27-Jun-26	03-Jun-26 A	06-Jun-26 A	36,559.95	36,559.95	36,559.95	18
SUPER-STRUCTURE		7	100%	100%	04-Jul-26	16-Jul-26	28-Jun-26 A	02-Jul-26 A	80,432.50	80,432.50	80,432.50	12
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	04-Jul-26	11-Jul-26	28-Jun-26 A	30-Jun-26 A	48,259.50	48,259.50	48,259.50	9
MLTX-02-005-CI	Parpet Works and Lintels	3	100%	100%	14-Jul-26	16-Jul-26	02-Jul-26 A	02-Jul-26 A	16,086.50	16,086.50	16,086.50	12
MLTX-02-005-CI	AAC Panels Works for Slabs	2	100%	100%	12-Jul-26	13-Jul-26	01-Jul-26 A	01-Jul-26 A	16,086.50	16,086.50	16,086.50	10
UNDER GROUND SEPTIC TANK		78	100%	100%	06-Jun-26	07-Jul-26	04-Jun-26 A	06-Jul-26 A	49,852.54	49,852.54	49,852.54	1
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	06-Jun-26	08-Jun-26	04-Jun-26 A	06-Jun-26 A	17,106.85	17,106.85	17,106.85	2
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	8	100%	100%	29-Jun-26	07-Jul-26	02-Jul-26 A	06-Jul-26 A	8,774.37	8,774.37	8,774.37	1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	7	100%	100%	09-Jun-26	16-Jun-26	18-Jun-26 A	20-Jun-26 A	7,604.46	7,604.46	7,604.46	-3
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	10	100%	100%	17-Jun-26	28-Jun-26	20-Jun-26 A	29-Jun-26 A	16,366.86	16,366.86	16,366.86	-1
THERMAL & MOISTER PROTECTION		61	100%	100%	03-Jun-26	16-Jul-26	24-May-26 A	10-Aug-26 A	10,236.80	10,236.80	10,236.80	-21
ANTI TERMIT CONTROL		13	100%	100%	03-Jun-26	17-Jun-26	24-May-26 A	03-Jun-26 A	4,387.50	4,387.50	4,387.50	12
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	03-Jun-26	03-Jun-26	31-May-26 A	03-Jun-26 A	1,755.00	1,755.00	1,755.00	0
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	17-Jun-26	17-Jun-26	24-May-26 A	25-May-26 A	2,632.50	2,632.50	2,632.50	17
POLYETHYLENE SHEET		13	100%	100%	04-Jun-26	18-Jun-26	25-May-26 A	04-Jun-26 A	2,193.30	2,193.30	2,193.30	12
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	04-Jun-26	04-Jun-26	01-Jun-26 A	04-Jun-26 A	877.32	877.32	877.32	0
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	18-Jun-26	18-Jun-26	25-May-26 A	31-May-26 A	1,315.98	1,315.98	1,315.98	16
EPOXY		6	100%	100%	08-Jul-26	16-Jul-26	11-Jul-26 A	10-Aug-26 A	3,656.00	3,656.00	3,656.00	-21
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	08-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	1,096.80	1,096.80	1,096.80	0
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	12-Jul-26	16-Jul-26	28-Jul-26 A	10-Aug-26 A	2,559.20	2,559.20	2,559.20	-21
MASONARY WORK		5	100%	100%	28-Jun-26	02-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-4
MLTX-02-005-CN-126	CMU Masonary Works Including all Accessories	5	100%	100%	28-Jun-26	02-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-4
THERMAL & MOISTER PROTECTION		22	100%	85.64%	18-Jul-26	10-Aug-26	10-Sep-26 A	14-Oct-26	34,698.32	29,716.14	34,698.32	-55
MLTX-02-005-CN-126	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	18-Jul-26	19-Jul-26	10-Sep-26 A	10-Sep-26 A	2,105.86	2,105.86	2,105.86	-46
MLTX-02-005-CN-126	Finalize Water Proofing Works for Toilets	5	100%	100%	20-Jul-26	25-Jul-26	12-Sep-26 A	12-Sep-26 A	4,913.66	4,913.66	4,913.66	-42
MLTX-02-005-CN-126	Preparing Surface and Preliminary Works for Roofing and	6	100%	100%	26-Jul-26	01-Aug-26	20-Sep-26 A	20-Sep-26 A	11,071.52	11,071.52	11,071.52	-43
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	70%	02-Aug-26	10-Aug-26	20-Sep-26 A	14-Oct-26	16,607.28	11,625.10	16,607.28	-55
MECHANICAL WORK		73	99.93%	72.58%	26-Jul-26	07-Oct-26	12-Jul-26 A	10-Nov-26	264,487.40	192,109.79	264,673.10	-29
HVAC SYSTEM		41	100%	47.55%	12-Aug-26	14-Sep-26	12-Jul-26 A	27-Oct-26	27,883.37	13,259.41	27,883.37	-36
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	12-Aug-26	15-Aug-26	12-Jul-26 A	12-Jul-26 A	9,359.69	9,359.69	9,359.69	29
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	4	100%	0%	10-Sep-26	14-Sep-26	24-Oct-26	27-Oct-26	14,623.96	0.00	14,623.96	-36
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	16-Aug-26	22-Aug-26	25-Aug-26 A	29-Aug-26 A	3,899.72	3,899.72	3,899.72	-6
WATER SUPPLY SYSTEM		73	100%	96.64%	28-Jul-26	29-Sep-26	21-Jul-26 A	13-Oct-26	154,916.69	149,717.01	154,916.69	-12
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	6	100%	100%	28-Jul-26	03-Aug-26	21-Jul-26 A	21-Jul-26 A	6,921.94	6,921.94	6,921.94	11
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	7	100%	80%	10-Aug-26	17-Aug-26	19-Sep-26 A	13-Oct-26	25,998.40	20,798.72	25,998.40	-48
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	20	100%	100%	06-Sep-26	29-Sep-26	04-Oct-26 A	04-Oct-26 A	48,746.52	48,746.52	48,746.52	-4
MLTX-02-005-CN-1	Installing of GRP Tanks	20	100%	100%	13-Aug-26	05-Sep-26	06-Sep-26 A	14-Sep-26 A	64,995.36	64,995.36	64,995.36	-8
MLTX-02-005-CN-1	Installing of Valves and Fittings	5	100%	100%	04-Aug-26	09-Aug-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	-23
MLTX-02-005-CN-1	Installing of Water Heater	20	100%	100%	05-Sep-26	28-Sep-26	29-Sep-26 A	29-Sep-26 A	1,754.87	1,754.87	1,754.87	-1
SEWER/DRAINAGE SYSTEM		46	100%	36.45%	26-Jul-26	29-Sep-26	21-Jul-26 A	10-Nov-26	79,923.17	29,133.37	79,923.17	-36
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	26-Jul-26	27-Jul-26	21-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	4
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	5	100%	50%	18-Aug-26	23-Aug-26	04-Oct-26 A	11-Oct-26	10,358.68	5,179.34	10,358.68	-41

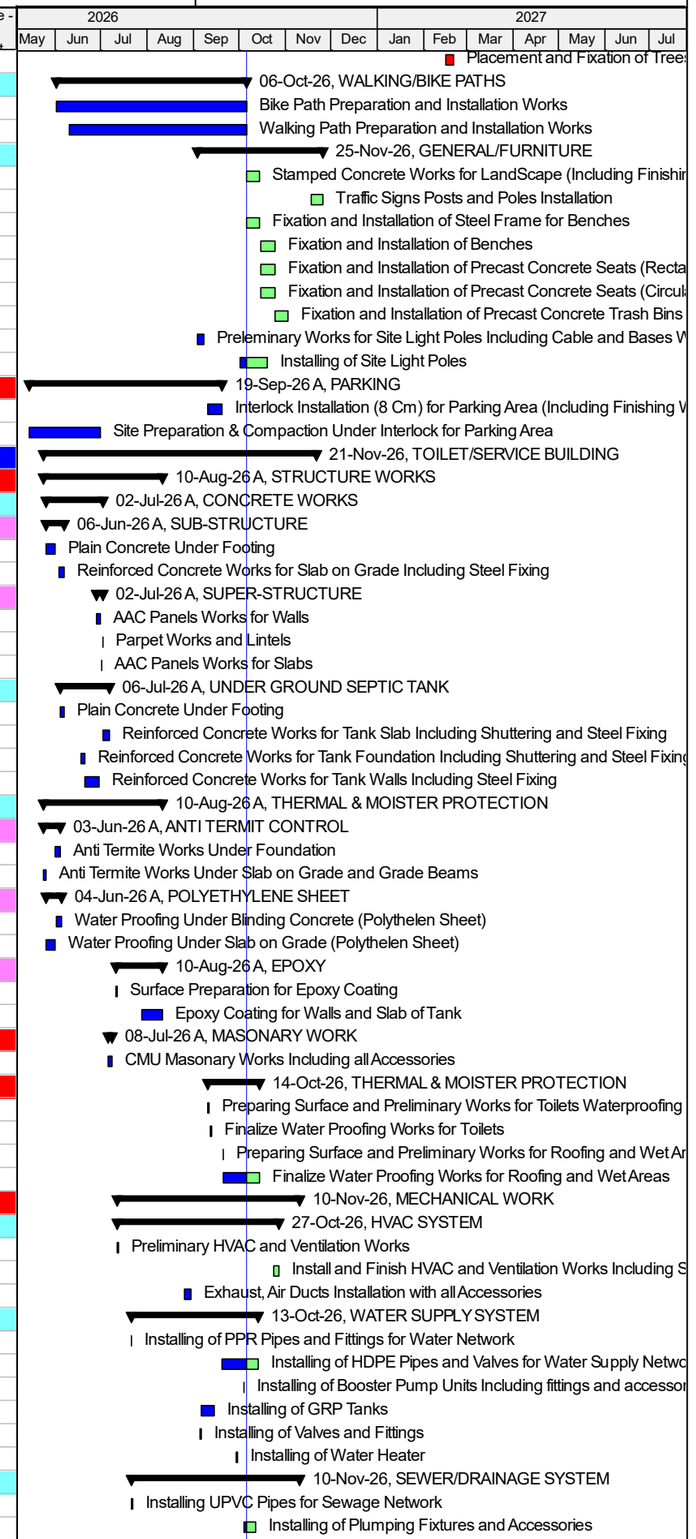

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	8	100%	0%	09-Aug-26	17-Aug-26	06-Oct-26	14-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	10	100%	100%	28-Jul-26	08-Aug-26	03-Oct-26 A	03-Oct-26 A	12,186.63	12,186.63	12,186.63	-47
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	21	100%	0%	05-Sep-26	29-Sep-26	18-Oct-26	10-Nov-26	31,392.79	0.00	31,392.79	-36
FIRE PROTECTION		21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
ELECTRICAL WORKS		89	97.1%	53.29%	18-Jul-26	21-Oct-26	14-Jul-26 A	21-Nov-26	375,771.21	206,217.58	386,998.85	-26
ROUGH-IN WORKS		46	100%	100%	18-Jul-26	19-Jul-26	14-Jul-26 A	17-Aug-26 A	206,217.58	206,217.58	206,217.58	-25
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	18-Jul-26	19-Jul-26	22-Jul-26 A	09-Aug-26 A	68,245.12	68,245.12	68,245.12	-18
MLTX-02-005-CN-1	Preleminary Works for Cable Works	2	100%	100%	18-Jul-26	19-Jul-26	22-Jul-26 A	09-Aug-26 A	12,488.95	12,488.95	12,488.95	-17
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	18-Jul-26	19-Jul-26	14-Jul-26 A	09-Aug-26 A	15,990.55	15,990.55	15,990.55	-18
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	18-Jul-26	19-Jul-26	09-Aug-26 A	17-Aug-26 A	21,935.93	21,935.93	21,935.93	-25
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	18-Jul-26	19-Jul-26	09-Aug-26 A	17-Aug-26 A	24,470.75	24,470.75	24,470.75	-25
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	2	100%	100%	18-Jul-26	19-Jul-26	09-Aug-26 A	17-Aug-26 A	30,913.59	30,913.59	30,913.59	-25
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	2	100%	100%	18-Jul-26	19-Jul-26	09-Aug-26 A	17-Aug-26 A	32,172.69	32,172.69	32,172.69	-25
FIXTURE WORKS		38	93.79%	0%	10-Sep-26	21-Oct-26	08-Oct-26	21-Nov-26	169,553.63	0.00	180,781.27	-26
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	20	85%	0%	15-Sep-26	08-Oct-26	28-Oct-26	19-Nov-26	29,169.90	0.00	34,317.53	-36
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	100%	0%	10-Sep-26	04-Oct-26	29-Oct-26	21-Nov-26	102,367.69	0.00	102,367.69	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	95%	0%	13-Sep-26	06-Oct-26	20-Oct-26	11-Nov-26	6,730.85	0.00	7,085.10	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	90.48%	0%	13-Sep-26	07-Oct-26	18-Oct-26	10-Nov-26	12,901.39	0.00	14,259.43	-29
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	30%	0%	29-Sep-26	21-Oct-26	08-Oct-26	31-Oct-26	1,871.88	0.00	6,239.59	-8
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	7,250.09	0.00	7,250.09	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	6,824.51	0.00	6,824.51	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	2,437.33	0.00	2,437.33	-36
DOORS/WINDOWS		39	100%	14.29%	18-Jul-26	10-Sep-26	28-Sep-26 A	24-Oct-26	68,245.12	9,749.30	68,245.12	-36
MLTX-02-005-CN-126	Preliminary Works For Doors	3	100%	100%	18-Jul-26	20-Jul-26	28-Sep-26 A	28-Sep-26 A	7,799.44	7,799.44	7,799.44	-59
MLTX-02-005-CN-126	Finalize Metal Doors for Toilets Building	1	100%	100%	10-Sep-26	10-Sep-26	29-Sep-26 A	29-Sep-26 A	1,949.86	1,949.86	1,949.86	-15
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	1	100%	0%	10-Sep-26	10-Sep-26	24-Oct-26	24-Oct-26	5,849.58	0.00	5,849.58	-36
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	2	100%	0%	18-Jul-26	19-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-68
METAL WORKS		15	100%	28.57%	18-Jul-26	22-Aug-26	06-Sep-26 A	26-Oct-26	13,649.02	3,899.72	13,649.02	-55
MLTX-02-005-CN-126	Installation of Galvanized Steel Ladder	4	100%	0%	13-Aug-26	17-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-55
MLTX-02-005-CN-125	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	22-Oct-26	26-Oct-26	3,899.72	0.00	3,899.72	-82
MLTX-02-005-CN-125	Installation of Galvanized Steel Roof Scupper	4	100%	100%	18-Aug-26	22-Aug-26	06-Sep-26 A	06-Sep-26 A	3,899.72	3,899.72	3,899.72	-13
FINISHING WORKS		69	100%	61.04%	26-Jul-26	13-Sep-26	17-Aug-26 A	26-Oct-26	166,130.97	101,406.23	166,130.97	-36
FLOOR FINISHES		18	100%	76.14%	04-Aug-26	13-Sep-26	15-Sep-26 A	26-Oct-26	17,159.03	13,064.27	17,159.03	-36
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	100%	04-Aug-26	05-Aug-26	15-Sep-26 A	16-Sep-26 A	11,894.39	11,894.39	11,894.39	-36
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	06-Aug-26	12-Aug-26	06-Oct-26	12-Oct-26	2,924.82	0.00	2,924.82	-51
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	10-Sep-26	13-Sep-26	24-Oct-26	26-Oct-26	1,169.94	0.00	1,169.94	-36
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	100%	13-Aug-26	17-Aug-26	04-Oct-26 A	04-Oct-26 A	1,169.88	1,169.88	1,169.88	-40
WALL FINISHES		69	100%	54.75%	26-Jul-26	12-Sep-26	17-Aug-26 A	22-Oct-26	134,001.04	73,371.06	134,001.04	-34
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	26-Jul-26	28-Jul-26	17-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	-19
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	6	100%	100%	26-Jul-26	01-Aug-26	19-Aug-26 A	31-Aug-26 A	6,551.63	6,551.63	6,551.63	-26
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	80%	18-Aug-26	20-Aug-26	27-Sep-26 A	08-Oct-26	35,825.58	28,660.46	35,825.58	-41
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	5	100%	100%	06-Aug-26	11-Aug-26	01-Sep-26 A	03-Sep-26 A	15,696.35	15,696.35	15,696.35	-20
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	27-Aug-26	03-Sep-26	10-Oct-26	17-Oct-26	31,197.60	0.00	31,197.60	-36
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	22-Aug-26	26-Aug-26	04-Oct-26 A	04-Oct-26 A	2,275.00	2,275.00	2,275.00	-32
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	100%	0%	05-Sep-26	09-Sep-26	18-Oct-26	22-Oct-26	13,649.02	0.00	13,649.02	-36
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	11-Aug-26	12-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-55
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	80%	10-Sep-26	12-Sep-26	29-Sep-26 A	07-Oct-26	2,340.00	1,872.00	2,340.00	-21
CELLING FINISHES		5	100%	100%	11-Aug-26	24-Aug-26	28-Sep-26 A	01-Oct-26 A	14,970.90	14,970.90	14,970.90	-32
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	100%	22-Aug-26	24-Aug-26	30-Sep-26 A	01-Oct-26 A	3,427.86	3,427.86	3,427.86	-32
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	5	100%	100%	16-Aug-26	20-Aug-26	28-Sep-26 A	29-Sep-26 A	5,771.52	5,771.52	5,771.52	-33
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	100%	11-Aug-26	13-Aug-26	28-Sep-26 A	29-Sep-26 A	5,771.52	5,771.52	5,771.52	-39
SPECIALTIES WORK		26	100%	7.5%	24-Aug-26	20-Sep-26	04-Oct-26 A	16-Nov-26	58,495.83	4,387.19	58,495.83	-48
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	30%	24-Aug-26	26-Aug-26	04-Oct-26 A	08-Oct-26	14,623.96	4,387.19	14,623.96	-36
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	7	100%	0%	13-Sep-26	20-Sep-26	09-Nov-26	16-Nov-26	19,498.61	0.00	19,498.61	-48
MLTX-02-005-CN-131	Installation of Phenolic Locker	2	100%	0%	05-Sep-26	06-Sep-26	18-Oct-26	19-Oct-26	24,373.26	0.00	24,373.26	-36
TESTING & COMMISSIONING		109	0%	0%	18-Nov-26	02-Jan-27	26-Nov-26	06-Apr-27	0.00	0.00	0.00	-77
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	22-Mar-27	06-Apr-27	0.00	0.00	0.00	-83
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	15	0%	0%	18-Nov-26	05-Dec-26	18-Feb-27	08-Mar-27	0.00	0.00	0.00	-79
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	20	0%	0%	10-Dec-26	02-Jan-27	26-Nov-26	19-Dec-26	0.00	0.00	0.00	12
DAMMAM		251	57.49%	36.54%	03-Mar-26	29-Dec-26	04-Mar-26 A	21-Apr-27	5,693,852.37	3,619,240.90	9,904,307.16	-93
MOBILIZATION		25	0%	0%	03-Mar-26	04-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
TOPOGRAPHIC SURVEY		5	0%	0%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2100	Site Survey Works	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0

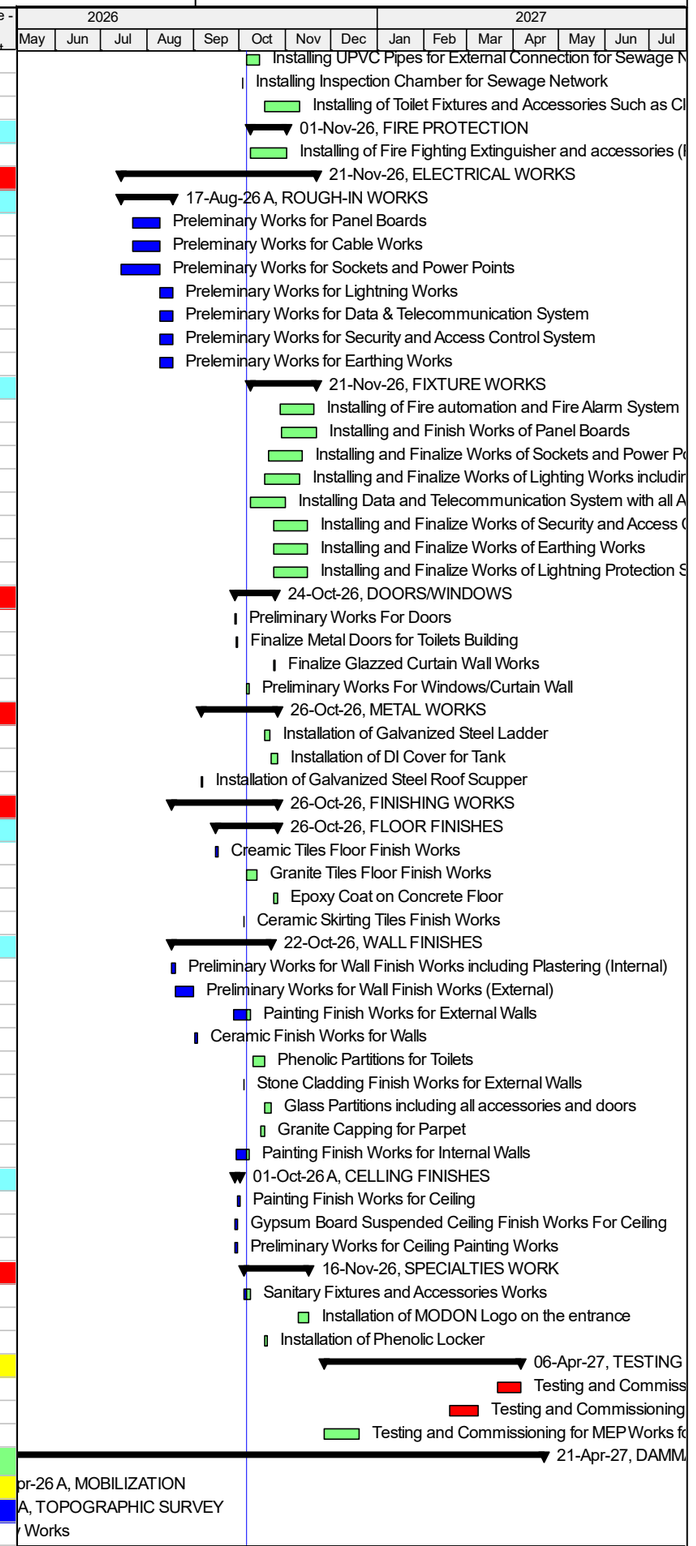

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SITE FACILITIES & OFFICES		24	0%	0%	03-Mar-26	02-Apr-26	04-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-1980	Manpower Mobalization	5	100%	100%	29-Mar-26	02-Apr-26	29-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-1990	Equipment Mobalization	7	100%	100%	26-Mar-26	02-Apr-26	26-Mar-26 A	02-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2010	Site Layout Plan	5	100%	100%	03-Mar-26	08-Mar-26	04-Mar-26 A	08-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2020	Clear & Grub for Offices & Access Road	3	100%	100%	09-Mar-26	11-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2030	Construct Site Access Roads	4	100%	100%	09-Mar-26	12-Mar-26	09-Mar-26 A	12-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2040	Construct Temporary Fence	7	100%	100%	12-Mar-26	19-Mar-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2050	Construct Site Offices & Storage	14	100%	100%	14-Mar-26	01-Apr-26	14-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2060	Install Project Signs	8	100%	100%	14-Mar-26	25-Mar-26	14-Mar-26 A	25-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2070	Install Site Facilities	4	100%	100%	24-Mar-26	28-Mar-26	24-Mar-26 A	28-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2080	Electrical Works & Connections	6	100%	100%	24-Mar-26	30-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-2090	Construct Parking Sheds	6	100%	100%	24-Mar-26	30-Mar-26	24-Mar-26 A	30-Mar-26 A	0.00	0.00	0.00	0
PRELIMINARY SUBMITTALS		20	0%	0%	09-Mar-26	04-Apr-26	09-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
PREPARATIONS & SUBMITTAL BY CONTRACTORS		10	0%	0%	09-Mar-26	19-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-200	Preparation and Submittal of Detailed Work Order	10	100%	100%	09-Mar-26	19-Mar-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-211	Preparation and Submittal of Project Execution Plan	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-212	Submission of Contractor Project Quality Plan	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-213	Submission of Construction Safety & Environmental	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-214	Preparation and Submittal of Organization Chart	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-215	Preparation and Submittal of Communication Plan	8	100%	100%	09-Mar-26	17-Mar-26	09-Mar-26 A	17-Mar-26 A	0.00	0.00	0.00	0
APPROVALS BY EMPLOYERS		12	0%	0%	18-Mar-26	04-Apr-26	18-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-216	Approval of Detailed Work Order Programme (Baseline)	10	100%	100%	24-Mar-26	04-Apr-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-217	Approval of Project Execution Plan	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-218	Approval of Contractor Project Quality Plan	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-219	Approval of Construction Safety & Environmental	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-220	Approval of Organization Chart	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
MLTX-02-005-MB-221	Approval of Communication Plan	10	100%	100%	18-Mar-26	01-Apr-26	18-Mar-26 A	01-Apr-26 A	0.00	0.00	0.00	0
ENGINEERING		185	0%	0%	09-Mar-26	07-Jul-26	08-Mar-26 A	04-Feb-27	0.00	0.00	0.00	-181
SHOP DRAWINGS		185	0%	0%	09-Mar-26	07-Jul-26	08-Mar-26 A	04-Feb-27	0.00	0.00	0.00	-181
SHOP DRAWINGS SUBMISSION		101	0%	0%	09-Mar-26	13-Jun-26	08-Mar-26 A	29-Oct-26	0.00	0.00	0.00	-118
SHOP DRAWING SUBMITTALS FOR EARTHING WORKS		40	0%	0%	09-Mar-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN-1	Shop DWG Submittal for Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Setting Out	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Grading Layout Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN-1	Shop DWG Submittal for Curb Setting Out Points	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Signing & Marking Layout Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Submittal for Standards Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
SHOP DRAWING SUBMITTALS FOR SERVICE/TOILET WORKS		61	0%	0%	09-Mar-26	13-Jun-26	09-Mar-26 A	08-Jul-26 A	0.00	0.00	0.00	-22
ARCHITECTURE WORKS		40	0%	0%	09-Mar-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Floor Plan	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Elevations	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN	Shop DWG Submittal for Sections	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Ceiling Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Finishes Plan	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Toilet Details	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
MLTX-02-005-EN	Shop DWG Submittal for Doors/Windows Schedule	15	100%	100%	11-Apr-26	27-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	35
STRUCTURE WORKS		21	0%	0%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Foundation Plan	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EN	Shop DWG Submittal for Ground Floor Framing Plan	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Sections/Details	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MECHANCAL WORKS		52	0%	0%	28-Apr-26	13-Jun-26	12-Mar-26 A	08-Jul-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	100%	17-May-26	13-Jun-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Shop DWG Submittal for HVAC Equipment Schedule	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Shop DWG Submittal for Fire Fighting Layout	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Layout	21	100%	100%	28-Apr-26	21-May-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Shop DWG Submittal for Water Supply Details	21	100%	100%	28-Apr-26	21-May-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Shop DWG Submittal for Drainage Layout	21	100%	100%	28-Apr-26	21-May-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Shop DWG Submittal for Drainage Details	21	100%	100%	28-Apr-26	21-May-26	12-Mar-26 A	31-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Shop DWG Submittal for Dut Routing Layout	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Shop DWG Submittal for Diffusers Layout	21	100%	100%	28-Apr-26	21-May-26	08-Jul-26 A	08-Jul-26 A	0.00	0.00	0.00	-38
ELECTRICAL WORKS		34	0%	0%	28-Apr-26	21-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN	Shop DWG Submittal for Lighting Layout	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51

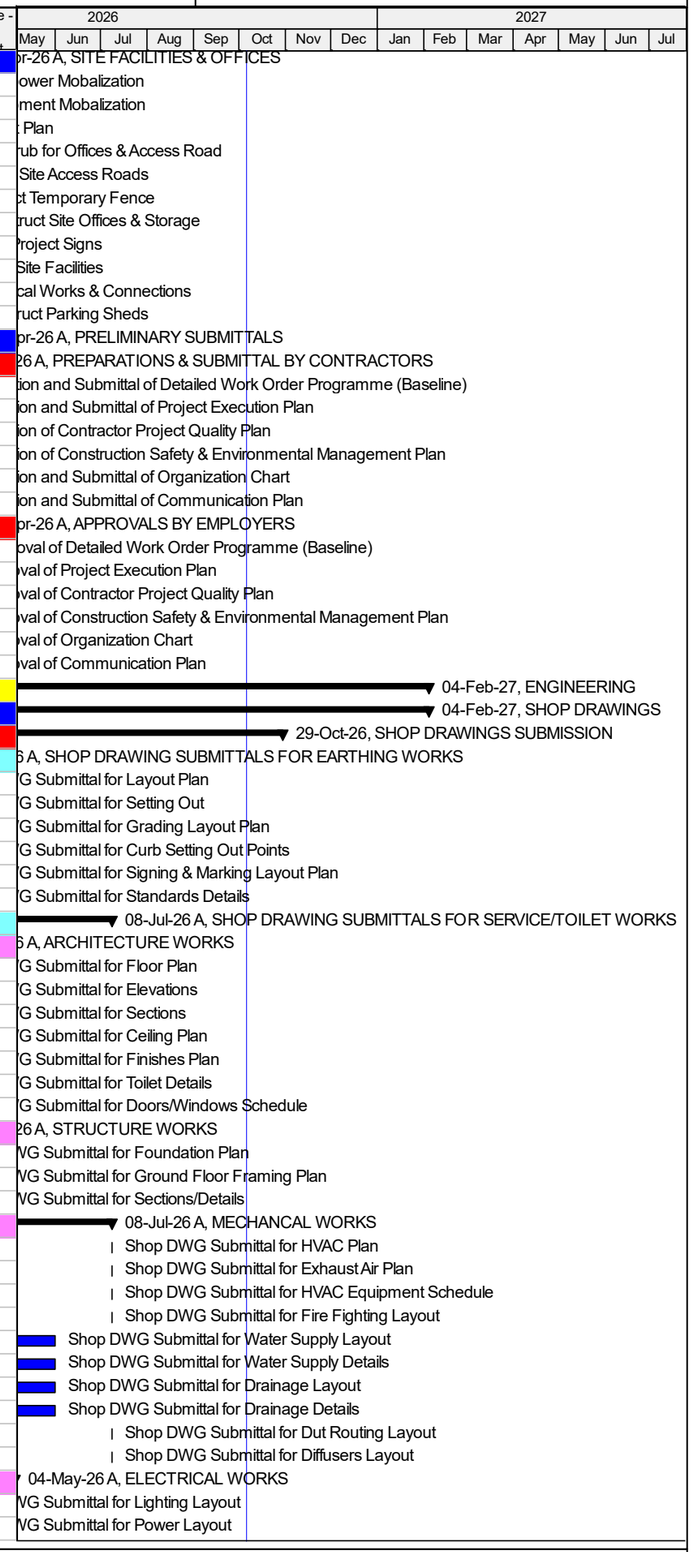

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	21	100%	100%	28-Apr-26	21-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	15
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Lighting Installation Details	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Cable Tray Installation Details	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Manhole & Ductbank Details	15	100%	100%	28-Apr-26	14-May-26	12-Mar-26 A	04-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Shop DWG Submittal for Grounding Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Grounding Layout	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Lightning Protection System Layout	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	45
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	15	100%	100%	28-Apr-26	14-May-26	15-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	49
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	15	100%	100%	28-Apr-26	14-May-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	35
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Layout	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
MLTX-02-005-EM	Shop DWG Submittal for Telephone & Data Riser Diagram	21	100%	100%	28-Apr-26	21-May-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	51
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		101	0%	0%	09-Mar-26	29-Apr-26	08-Mar-26 A	29-Oct-26	0.00	0.00	0.00	-153
ARCHITECTURE WORKS		21	0%	0%	09-Mar-26	05-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Playground Plan/Layout	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Furniture & Marking	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Sections	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EM	Shop DWG Submittal for Interlock Pattern Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Shop DWG Submittal for Doors/Windows Schedule	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Dome Internal Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
STRUCTURE WORKS		21	0%	0%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Air Dome System	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Submittal for Foundation of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EM	Shop DWG Submittal for Anchor Bolt Layout of Air Dome	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-26
AIR DOME SYSTEM		81	0%	0%	06-Apr-26	29-Apr-26	14-Mar-26 A	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Air Dome Structural Layout	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EM	Shop DWG Submittal for Membrane Panel Layout	21	100%	100%	06-Apr-26	29-Apr-26	21-Jun-26 A	21-Jun-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EM	Shop DWG Submittal for Cable Tension Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Airlock Door Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Emergency Exit Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
SPORTS EQUIPMENT		21	0%	0%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Football Turf Installation	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Basketball Court Marking	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Padel Court Structure	21	100%	100%	06-Apr-26	29-Apr-26	29-Jun-26 A	29-Jun-26 A	0.00	0.00	0.00	-49
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
ELECTRICAL WORKS		80	0%	0%	06-Apr-26	29-Apr-26	14-Mar-26 A	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	21	100%	100%	06-Apr-26	29-Apr-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	100%	06-Apr-26	29-Apr-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Shop DWG Submittal for CCTV Details	21	100%	100%	06-Apr-26	29-Apr-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EM	Shop DWG Submittal for CCTV Layout	21	100%	100%	06-Apr-26	29-Apr-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-98
MLTX-02-005-EM	Shop DWG Submittal for CCTV Riser Diagram	21	100%	100%	06-Apr-26	29-Apr-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-98
SHOP DRAWINGS SUBMITTALS FOR LANDSCAPE WORKS		57	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
ARCHITECTURE WORKS		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EM	Shop DWG Submittal for Landscape Layout	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Shop DWG Submittal for Hardscape Plan	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Shop DWG Submittal for Planting Plan	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EM	Shop DWG Submittal for Landscape Details	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MECHANCAL WORKS		21	0%	0%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Irrigation Details	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EM	Shop DWG Submittal for Irrigation Layout	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-49

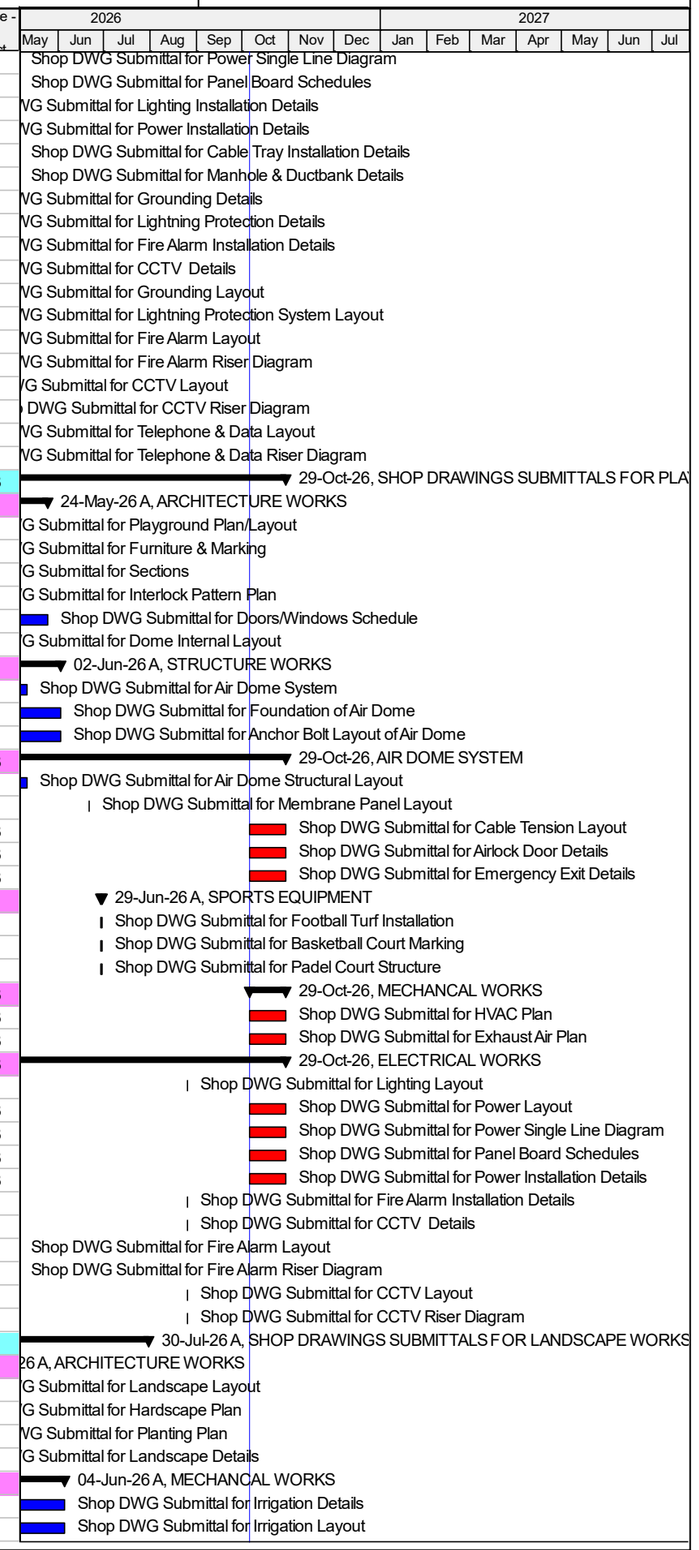

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
ELECTRICAL WORKS		30	0%	0%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Lighting General Arrangement	30	100%	100%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Lighting Network Layout	30	100%	100%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Lighting Details	30	100%	100%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
MLTX-02-005-EN	Shop DWG Submittal for Lighting Single Line Diagram	30	100%	100%	09-Mar-26	15-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-88
SHOP DRAWINGS APPROVALS		170	0%	0%	30-Mar-26	07-Jul-26	14-Mar-26 A	04-Feb-27	0.00	0.00	0.00	-181
SHOP DRAWING APPROVAL FOR EARTHING WORKS		41	0%	0%	30-Mar-26	16-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN-1	Shop DWG Approval for Layout Plan	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Shop DWG Approval for Setting Out	10	100%	100%	30-Mar-26	09-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Approval for Grading Layout Plan	16	100%	100%	28-Apr-26	16-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	41
MLTX-02-005-EN-1	Shop DWG Approval for Curb Setting Out Points	21	100%	100%	30-Mar-26	22-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	21
MLTX-02-005-EN-1	Shop DWG Approval for Signing & Marking Layout Plan	10	100%	100%	30-Mar-26	09-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Shop DWG Approval for Standards Details	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
SHOP DRAWING APPROVAL FOR SERVICE/TOILET WORKS		67	0%	0%	30-Mar-26	07-Jul-26	15-Mar-26 A	28-Jul-26 A	0.00	0.00	0.00	-18
ARCHITECTURE WORKS		55	0%	0%	30-Mar-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Floor Plan	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Elevations	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN	Shop DWG Approval for Sections	30	100%	100%	28-Apr-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Ceiling Plan	30	100%	100%	28-Apr-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Finishes Plan	30	100%	100%	28-Apr-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Toilet Details	30	100%	100%	28-Apr-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	30	100%	100%	28-Apr-26	04-Jun-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	55
STRUCTURE WORKS		27	0%	0%	16-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Foundation Plan	15	100%	100%	16-May-26	04-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	50
MLTX-02-005-EN	Shop DWG Approval for Ground Floor Framing Plan	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Sections/Details	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MECHANCAL WORKS		52	0%	0%	23-May-26	07-Jul-26	18-Mar-26 A	11-Jul-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	21	100%	100%	14-Jun-26	07-Jul-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Shop DWG Approval for HVAC Equipment Schedule	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Shop DWG Approval for Fire Fighting Layout	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Shop DWG Approval for Water Supply Layout	21	100%	100%	23-May-26	18-Jun-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Water Supply Details	21	100%	100%	23-May-26	18-Jun-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Drainage Layout	21	100%	100%	23-May-26	18-Jun-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Drainage Details	21	100%	100%	23-May-26	18-Jun-26	18-Mar-26 A	03-Jun-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Duct Routing Layout	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN	Shop DWG Approval for Diffusers Layout	21	100%	100%	23-May-26	18-Jun-26	11-Jul-26 A	11-Jul-26 A	0.00	0.00	0.00	-19
ELECTRICAL WORKS		40	0%	0%	16-May-26	22-Jun-26	18-Mar-26 A	28-Jul-26 A	0.00	0.00	0.00	-31
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Power Layout	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	21	100%	100%	23-May-26	18-Jun-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	21	100%	100%	16-May-26	11-Jun-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Lighting Installation Details	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Cable Tray Installation Details	21	100%	100%	16-May-26	11-Jun-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Manhole & Ductbank Details	21	100%	100%	16-May-26	11-Jun-26	18-Mar-26 A	07-May-26 A	0.00	0.00	0.00	27
MLTX-02-005-EN	Shop DWG Approval for Grounding Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Lightning Protection Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Installation Details	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	30	100%	100%	16-May-26	22-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-31
MLTX-02-005-EN	Shop DWG Approval for Grounding Layout	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Lightning Protection System Layout	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Layout	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for Fire Alarm Riser Diagram	21	100%	100%	16-May-26	11-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	56
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	30	100%	100%	16-May-26	22-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	30	100%	100%	16-May-26	22-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	65
MLTX-02-005-EN	Shop DWG Approval for Telephone & Data Layout	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
MLTX-02-005-EN	Shop DWG Approval for Telephone & Data Riser Diagram	21	100%	100%	23-May-26	18-Jun-26	24-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	62
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		170	0%	0%	30-Mar-26	24-May-26	14-Mar-26 A	04-Feb-27	0.00	0.00	0.00	-216
ARCHITECTURE WORKS		30	0%	0%	30-Mar-26	03-May-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Playground Plan/Layout	15	100%	100%	30-Mar-26	15-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Shop DWG Approval for Furniture & Marking	30	100%	100%	30-Mar-26	03-May-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-14
MLTX-02-005-EN	Shop DWG Approval for Sections	15	100%	100%	30-Mar-26	15-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-29
MLTX-02-005-EN	Shop DWG Approval for Interlock Pattern Plan	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-17

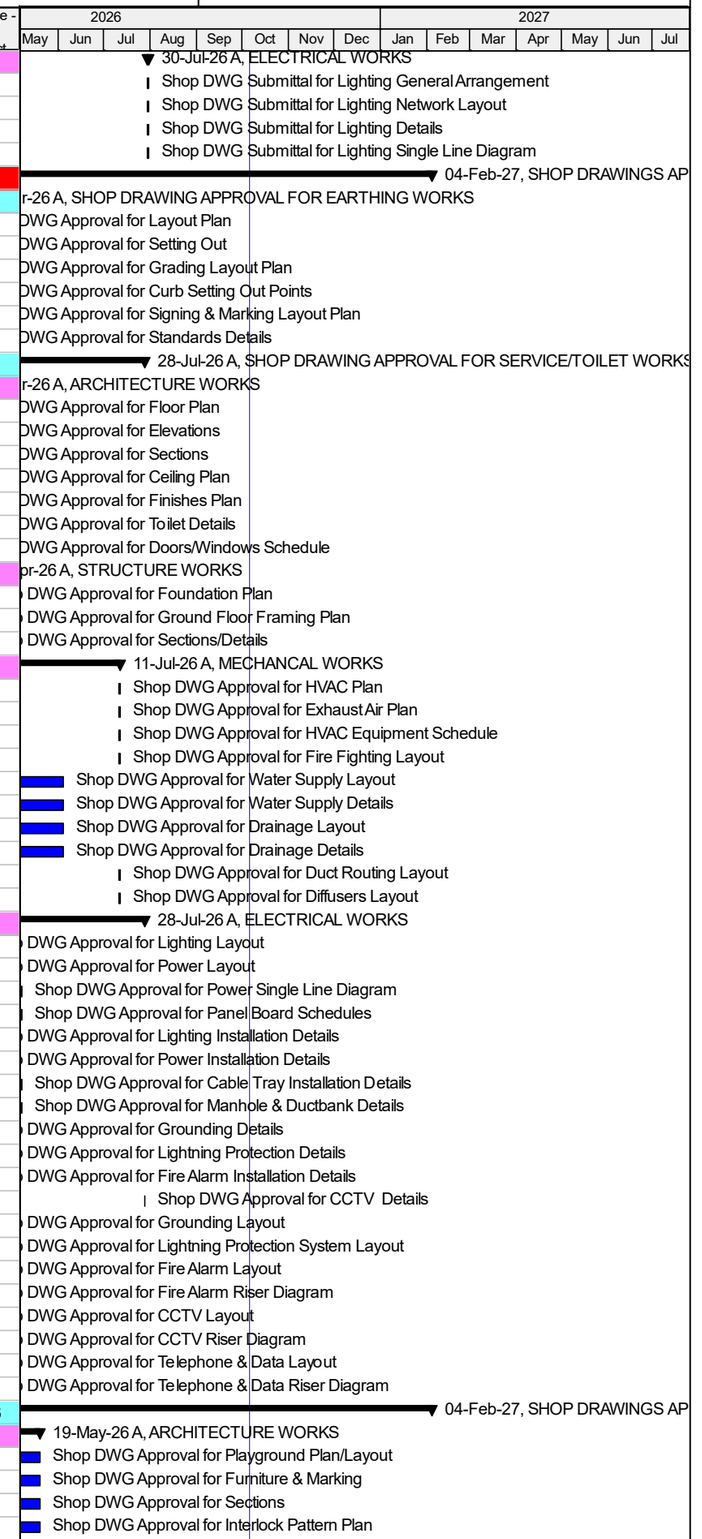


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Shop DWG Approval for Doors/Windows Schedule	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Shop DWG Approval for Dome Internal Layout	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	19-May-26 A	0.00	0.00	0.00	-17
STRUCTURE WORKS		21	0%	0%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Shop DWG Approval for Air Dome System	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Shop DWG Approval for Foundation of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Shop DWG Approval for Anchor Bolt Layout of Air Dome	21	100%	100%	30-Apr-26	24-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-43
AIR DOME SYSTEM		84	0%	0%	30-Apr-26	24-May-26	06-Oct-26	11-Jan-27	0.00	0.00	0.00	-195
MLTX-02-005-EN	Shop DWG Approval for Air Dome Structural Layout	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN	Shop DWG Approval for Membrane Panel Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Cable Tension Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Airlock Door Details	21	100%	0%	30-Apr-26	24-May-26	24-Nov-26	17-Dec-26	0.00	0.00	0.00	-174
MLTX-02-005-EN	Shop DWG Approval for Emergency Exit Details	21	100%	0%	30-Apr-26	24-May-26	19-Dec-26	11-Jan-27	0.00	0.00	0.00	-195
SPORTS EQUIPMENT		74	0%	0%	30-Apr-26	24-May-26	20-Jul-26 A	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN	Shop DWG Approval for Basketball Court Marking	21	100%	100%	30-Apr-26	24-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Approval for Padel Court Structure	21	100%	100%	30-Apr-26	24-May-26	20-Jul-26 A	20-Jul-26 A	0.00	0.00	0.00	-46
MECHANCAL WORKS		84	0%	0%	30-Apr-26	24-May-26	31-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	30-Apr-26	24-May-26	12-Jan-27	04-Feb-27	0.00	0.00	0.00	-216
ELECTRICAL WORKS		80	0%	0%	30-Apr-26	24-May-26	19-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Lighting Layout	21	100%	100%	30-Apr-26	24-May-26	19-Mar-26 A	18-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Shop DWG Approval for Power Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for CCTV Details	21	100%	100%	30-Apr-26	24-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Approval for CCTV Layout	21	100%	100%	30-Apr-26	24-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-77
MLTX-02-005-EN	Shop DWG Approval for CCTV Riser Diagram	21	100%	100%	30-Apr-26	24-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-77
SHOP DRAWINGS APPROVAL FOR LANDSCAPE WORKS		72	0%	0%	30-Mar-26	20-May-26	14-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
ARCHITECTURE WORKS		30	0%	0%	30-Mar-26	03-May-26	14-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Shop DWG Approval for Landscape Layout	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Hardscape Plan	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	13
MLTX-02-005-EN	Shop DWG Approval for Planting Plan	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Shop DWG Approval for Landscape Details	21	100%	100%	30-Mar-26	22-Apr-26	14-Mar-26 A	14-Apr-26 A	0.00	0.00	0.00	7
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
MLTX-02-005-EN	Shop DWG Approval for Irrigation Details	21	100%	100%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
MLTX-02-005-EN	Shop DWG Approval for Irrigation Layout	21	100%	100%	06-Apr-26	29-Apr-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-76
ELECTRICAL WORKS		30	0%	0%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting General Arrangement	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Network Layout	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Details	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
MLTX-02-005-EN	Shop DWG Approval for Lighting Single Line Diagram	30	100%	100%	16-Apr-26	20-May-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-58
METHOD STATEMENTS		87	0%	0%	09-Mar-26	28-Jun-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-65
METHOD STATEMENT SUBMITTAL		60	0%	0%	09-Mar-26	20-May-26	08-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-10
CIVIL WORKS		21	0%	0%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Concrete	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	16
ARCHITECTURE WORKS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Plastering	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	14-Mar-26 A	0.00	0.00	0.00	10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	17-May-26 A	0.00	0.00	0.00	-36
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Tilling	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Parking	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Soft	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Fence	30	100%	100%	09-Mar-26	15-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Air Dome	30	100%	100%	09-Mar-26	15-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Metal	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Partitions	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Gypsum	21	100%	100%	09-Mar-26	05-Apr-26	08-Mar-26 A	02-Jun-26 A	0.00	0.00	0.00	-47
MECHANICAL WORKS		27	0%	0%	30-Mar-26	29-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-28

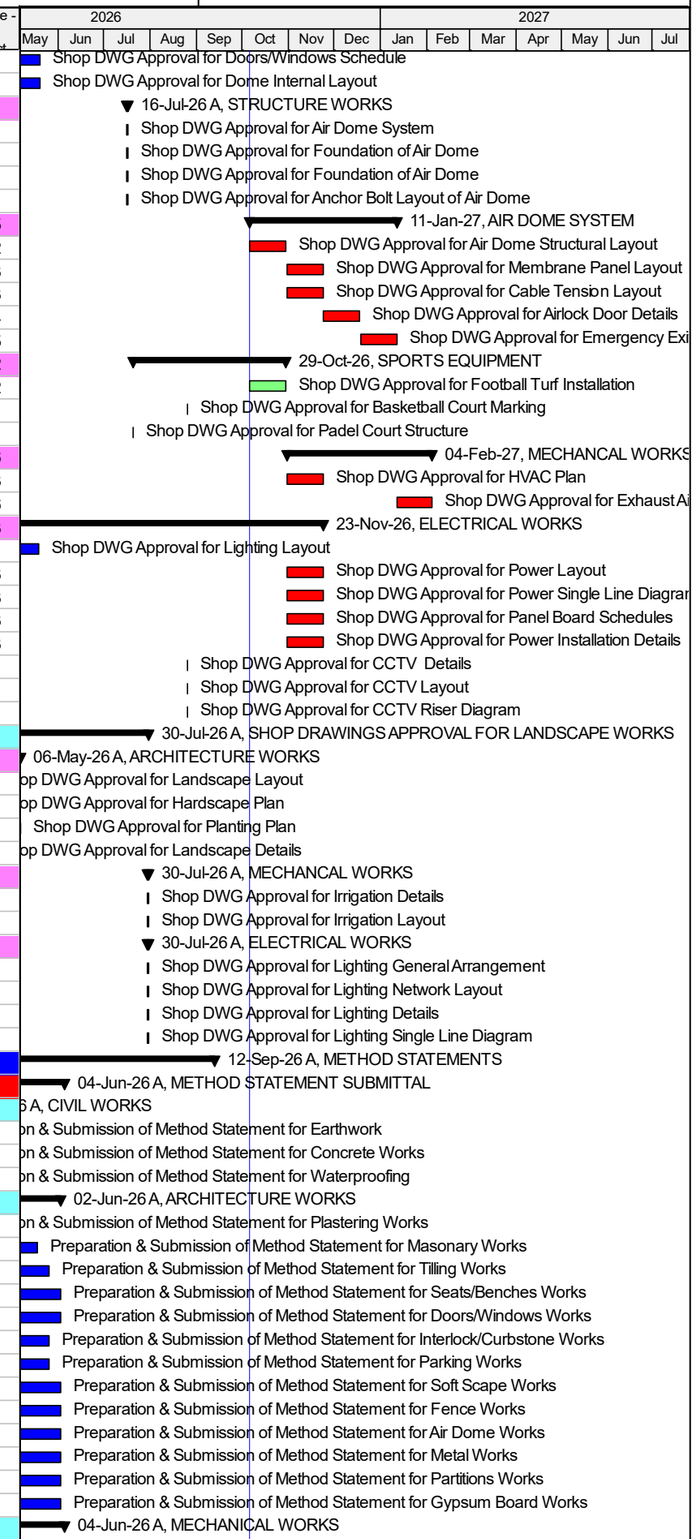


© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	30-Mar-26	22-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Water	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Fire	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-28
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Irrigation	15	100%	100%	30-Mar-26	15-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-40
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for HVAC	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	04-Jun-26 A	0.00	0.00	0.00	-28
ELECTRICAL WORKS		39	0%	0%	06-Apr-26	20-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Electrical	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Lighting	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	30	100%	100%	16-Apr-26	20-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for CCTV	30	100%	100%	16-Apr-26	20-May-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Lighting	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN-1	Preparation & Submission of Method Statement for Panel	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-10
METHOD STATEMENT APPROVAL		72	0%	0%	30-Mar-26	28-Jun-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-65
CIVIL WORKS		36	0%	0%	30-Mar-26	10-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	36
MLTX-02-005-EN-1	Approval of Method Statement for Earthwork	15	100%	100%	30-Mar-26	15-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	15
MLTX-02-005-EN-1	Approval of Method Statement for Concrete Works	30	100%	100%	06-Apr-26	10-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	36
MLTX-02-005-EN-1	Approval of Method Statement for Waterproofing	21	100%	100%	06-Apr-26	29-Apr-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	27
ARCHITECTURE WORKS		69	0%	0%	30-Mar-26	20-May-26	14-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EN-1	Approval of Method Statement for Plastering Works	30	100%	100%	30-Mar-26	03-May-26	15-Mar-26 A	29-Mar-26 A	0.00	0.00	0.00	30
MLTX-02-005-EN-1	Approval of Method Statement for Masonary Works	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN-1	Approval of Method Statement for Tilling Works	21	100%	100%	06-Apr-26	29-Apr-26	14-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-19
MLTX-02-005-EN-1	Approval of Method Statement for Seats/Benches Works	21	100%	100%	06-Apr-26	29-Apr-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-113
MLTX-02-005-EN-1	Approval of Method Statement for Doors/Windows Works	21	100%	100%	06-Apr-26	29-Apr-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-113
MLTX-02-005-EN-1	Approval of Method Statement for Interlock/Curbstone Works	21	100%	100%	06-Apr-26	29-Apr-26	10-Aug-26 A	10-Aug-26 A	0.00	0.00	0.00	-85
MLTX-02-005-EN-1	Approval of Method Statement for Parking Works	21	100%	100%	06-Apr-26	29-Apr-26	15-May-26 A	15-May-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN-1	Approval of Method Statement for Soft Scape Works	21	100%	100%	06-Apr-26	29-Apr-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-113
MLTX-02-005-EN-1	Approval of Method Statement for Fence Works	30	100%	100%	16-Apr-26	20-May-26	16-Jul-26 A	16-Jul-26 A	0.00	0.00	0.00	-46
MLTX-02-005-EN-1	Approval of Method Statement for Air Dome Works	30	100%	100%	16-Apr-26	20-May-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EN-1	Approval of Method Statement for Partitions Works	21	100%	100%	06-Apr-26	29-Apr-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-113
MLTX-02-005-EN-1	Approval of Method Statement for Gypsum Board Works	21	100%	100%	06-Apr-26	29-Apr-26	20-Aug-26 A	20-Aug-26 A	0.00	0.00	0.00	-94
MECHANICAL WORKS		54	0%	0%	16-Apr-26	24-May-26	24-Jun-26 A	26-Aug-26 A	0.00	0.00	0.00	-78
MLTX-02-005-EN-1	Approval of Method Statement for Sewage/Drainage System	21	100%	100%	23-Apr-26	17-May-26	24-Jun-26 A	24-Jun-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EN-1	Approval of Method Statement for Water Supply System	21	100%	100%	30-Apr-26	24-May-26	12-Jul-26 A	18-Jul-26 A	0.00	0.00	0.00	-44
MLTX-02-005-EN-1	Approval of Method Statement for Fire Fighting System	21	100%	100%	30-Apr-26	24-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-78
MLTX-02-005-EN-1	Approval of Method Statement for Irrigation System	15	100%	100%	16-Apr-26	03-May-26	25-Aug-26 A	25-Aug-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EN-1	Approval of Method Statement for HVAC System	21	100%	100%	30-Apr-26	24-May-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-71
ELECTRICAL WORKS		72	0%	0%	30-Apr-26	28-Jun-26	14-Jul-26 A	26-Aug-26 A	0.00	0.00	0.00	-51
MLTX-02-005-EN-1	Approval of Method Statement for Electrical Conduits/Pulling	21	100%	100%	30-Apr-26	24-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-41
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Poles Installation	21	100%	100%	30-Apr-26	24-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-78
MLTX-02-005-EN-1	Approval of Method Statement for Telecommunication & Data	30	100%	100%	21-May-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN-1	Approval of Method Statement for CCTV System	30	100%	100%	21-May-26	28-Jun-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-EN-1	Approval of Method Statement for Lighting Works	21	100%	100%	30-Apr-26	24-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-41
MLTX-02-005-EN-1	Approval of Method Statement for Earthing/Lightning Works	21	100%	100%	30-Apr-26	24-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-41
MLTX-02-005-EN-1	Approval of Method Statement for Panel Boards Works	21	100%	100%	30-Apr-26	24-May-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	-41
PRE-QUALIFICATION & MATERIAL		93	0%	0%	09-Mar-26	10-Jun-26	08-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
PRE-QUALIFICATION		45	0%	0%	09-Mar-26	03-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
TOILET/SERVICE WORKS		45	0%	0%	09-Mar-26	03-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
STEEL REINFORCEMENT		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Reinforcement	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Steel Reinforcement	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
READY MIX CONCRETE		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Ready Mixed Concrete	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval of Ready Mixed Concrete	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
CONCRETE BLOCKS		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Concrete Blocks	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Concrete Blocks	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
WATER PROOFING		36	0%	0%	09-Mar-26	22-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
MLTX-02-005-EN	Pre-Qualification Submittal for Water Proofing	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Water Proofing	21	100%	100%	30-Mar-26	22-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	26
FLOOR/WALL TILES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Submittal for Tilling Materials	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Tailling Material	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
SUSPENDED CEILING		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20

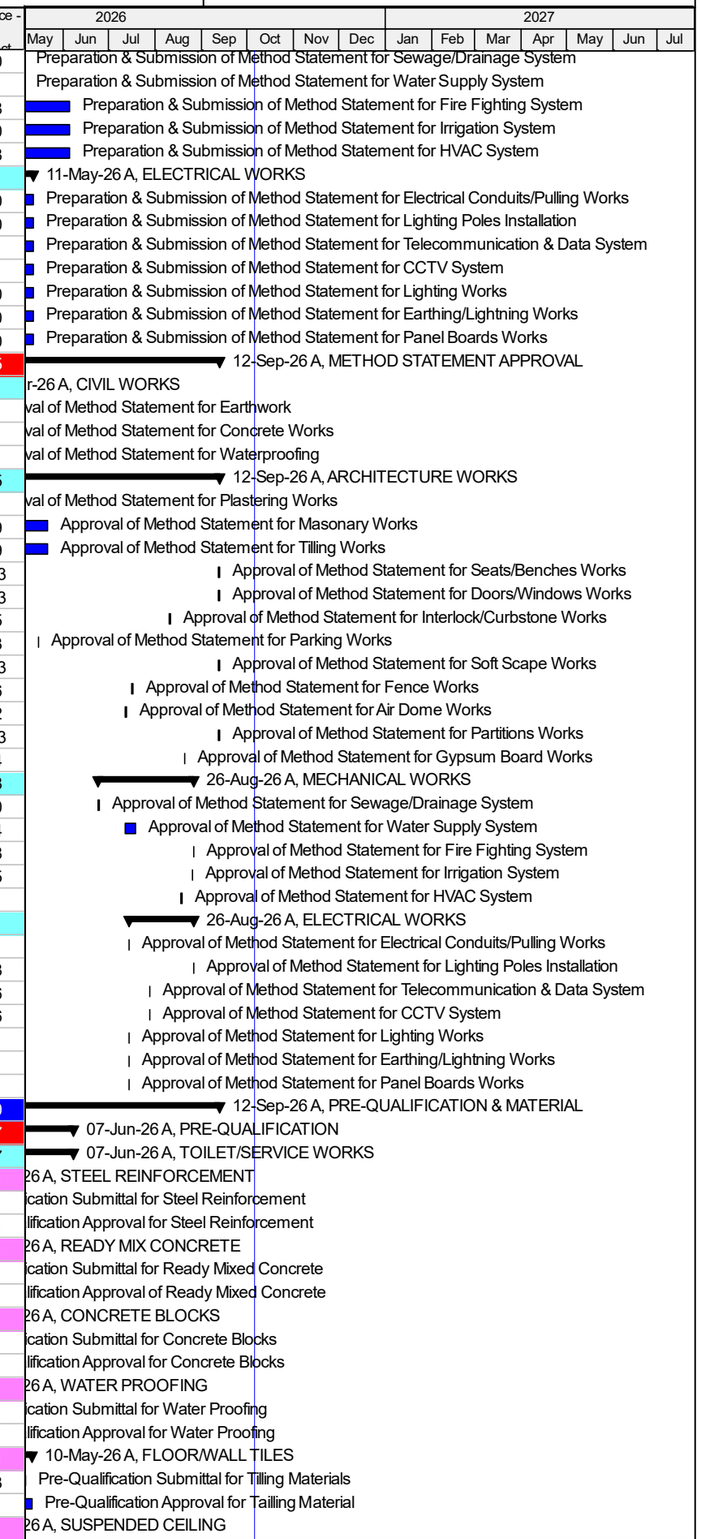

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Suspend Ceiling	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Suspend Ceiling	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
DOORS/WINDOWS		30	0%	0%	09-Mar-26	15-Apr-26	09-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
MLTX-02-005-EN	Pre-Qualification Submittal for Doors/Windows	15	100%	100%	09-Mar-26	29-Mar-26	09-Mar-26 A	11-Mar-26 A	0.00	0.00	0.00	12
MLTX-02-005-EN	Pre-Qualification Approval for Doors/Windows	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	19-Mar-26 A	0.00	0.00	0.00	20
FURNITURES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EN	Pre-Qualification Submittal for Furnitures	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	07-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Furnitures	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	12-May-26 A	0.00	0.00	0.00	-23
SANITARY FIXTURES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Submittal for Sanitary Fixtures	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Sanitary Fixtures	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
WATER SUPPLY PIPES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EN	Pre-Qualification Submittal for Water Supply Pipes	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Pre-Qualification Approval for Water Supply Pipes	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-42
SEWAGE/DRAINAGE PIPES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-42
MLTX-02-005-EN	Pre-Qualification Submittal for Sewage/Drainage Pipes	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-49
MLTX-02-005-EN	Pre-Qualification Approval for Sewage/Drainage Pipes	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-42
PACKAGE AC UNITS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
AIR DIFUSSERS/GRILLS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Air Diffusers/Grills	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Air Diffusers/Grills	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
GALVANIZED DUCTS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Ducts	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Ducts	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
EXHAUST FANS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
LIGHTING FIXTURES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting Fixtures	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Lighting Fixtures	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
SWITCHES/SOCKETS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Switches/Sockets	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Switches/Sockets	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
EARTHING SYSTEM		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Earthing System	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Earthing System	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
DISTRIBUTION PANNELS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Panels	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Panels	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
PLAYGROUND WORKS		45	0%	0%	09-Mar-26	03-May-26	08-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
PVC MEMBRANE		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for PVC Membrane	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for PVC Membrane	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
STEEL TENSION CABLES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Steel Tension Cables	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Steel Tension Cables	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
EMERGENCY DOORS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Emergency Doors	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Emergency Doors	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
PRESSURE UNITS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Pressure Units	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Pressure Units	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
AIR LOCK DOORS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Submittal for Lock Doors	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-45
MLTX-02-005-EN	Pre-Qualification Approval for Lock Doors	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	24-May-26 A	0.00	0.00	0.00	-33
ARTIFICIAL TURF		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
MLTX-02-005-EN	Pre-Qualification Submittal for Artificial TURF	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Artificial TURF	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-21
RUBBER GRANULES		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Rubber Granules	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Rubber Granules	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
PADEL GLASS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22

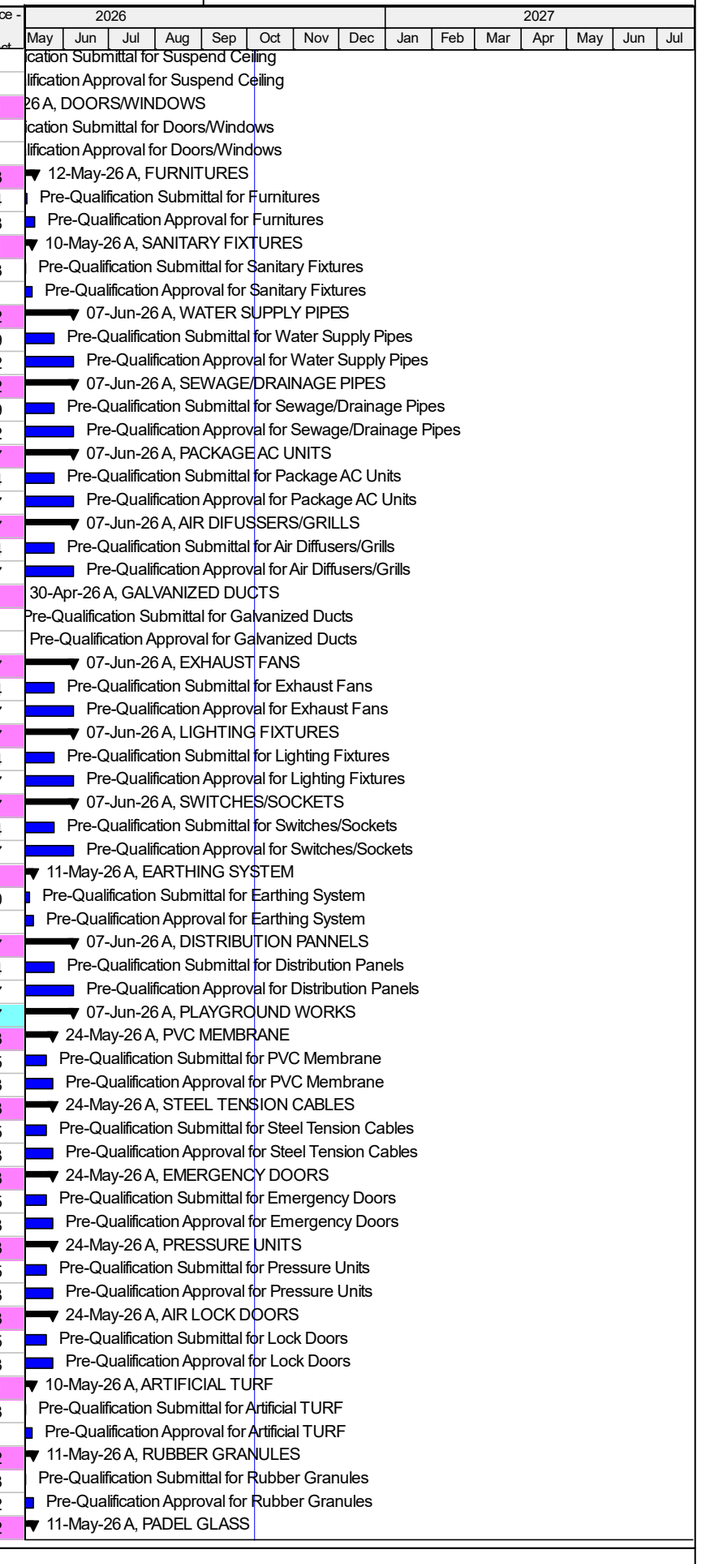

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Padel Glass	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Padel Glass	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
PADEL WIRE MESH/STEEL SETS		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
MLTX-02-005-EN	Pre-Qualification Submittal for Wire Mesh/Steel Sets	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-33
MLTX-02-005-EN	Pre-Qualification Approval for Wire Mesh/Steel Sets	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-22
AGGREGATE BASE COURSE		30	0%	0%	09-Mar-26	15-Apr-26	08-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Pre-Qualification Submittal for Aggregate Base Course	15	100%	100%	09-Mar-26	29-Mar-26	08-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-24
MLTX-02-005-EN	Pre-Qualification Approval for Aggregate Base Course	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-13
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
MLTX-02-005-EN	Pre-Qualification Submittal for Bituminous Base & Wearing	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	26-Apr-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Pre-Qualification Approval for the Site	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
INTERLOCKING PAVING		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-1
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	-13
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	04-May-26 A	0.00	0.00	0.00	-1
MARKING PAINT		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Submittal for Marking Paint	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Pre-Qualification Approval for Marking Paint	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
PACKAGE AC UNITS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Package AC Units	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Package AC Units	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
AIR DIFUSSERS/GRILLS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Air Difussers/Grills	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Air Difussers/Grills	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
GALVANIZED DUCTS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
MLTX-02-005-EN	Pre-Qualification Submittal for Galvanized Duct	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	-8
MLTX-02-005-EN	Pre-Qualification Approval for Galvanized Duct	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	2
EXHAUST FANS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Exhaust Fans	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Exhaust Fans	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
DISTRIBUTION BOARDS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Distribution Boards	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Distribution Boards	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
POWER CABLES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Power Cables	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Power Cables	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
LIGHT FIXTURES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Light Fixtures	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Light Fixtures	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
CCTV MATERIALS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for CCTV	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for CCTV	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
POWER OUTLETS/SWITCHES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Submittal for Power Outlets/Switches	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	25-May-26 A	0.00	0.00	0.00	-34
MLTX-02-005-EN	Pre-Qualification Approval for Power Outlets/Switches	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	07-Jun-26 A	0.00	0.00	0.00	-27
LANDSCAPE WORKS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
INTERLOCKING PAVING		30	0%	0%	30-Mar-26	03-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	34
MLTX-02-005-EN	Pre-Qualification Submittal for Interlocking Block Pavers	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Pre-Qualification Approval for Interlocking Block Pavers	15	100%	100%	16-Apr-26	03-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	34
CURBSTONE		30	0%	0%	30-Mar-26	03-May-26	12-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	34
MLTX-02-005-EN	Pre-Qualification Submittal for Curbstone	15	100%	100%	30-Mar-26	15-Apr-26	12-Mar-26 A	15-Mar-26 A	0.00	0.00	0.00	24
MLTX-02-005-EN	Pre-Qualification Approval for Curbstone	15	100%	100%	16-Apr-26	03-May-26	16-Mar-26 A	24-Mar-26 A	0.00	0.00	0.00	34
PAVEMENT MARKING		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Submittal for Pavement Markings	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Pre-Qualification Approval for Pavement Markings	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
TRAFFIC SIGNS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
MLTX-02-005-EN	Pre-Qualification Submittal for Traffic Signs	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-17
MLTX-02-005-EN	Pre-Qualification Approval for Traffic Signs	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-5
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Pre-Qualification Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EN	Pre-Qualification Approval for Irrigation Pipes/Sprinkles	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
AGRICULTURE SOIL		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Pre-Qualification Submittal for Agriculture Soil	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EN	Pre-Qualification Approval for Agriculture Soil	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
TRACK SURFACE		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16

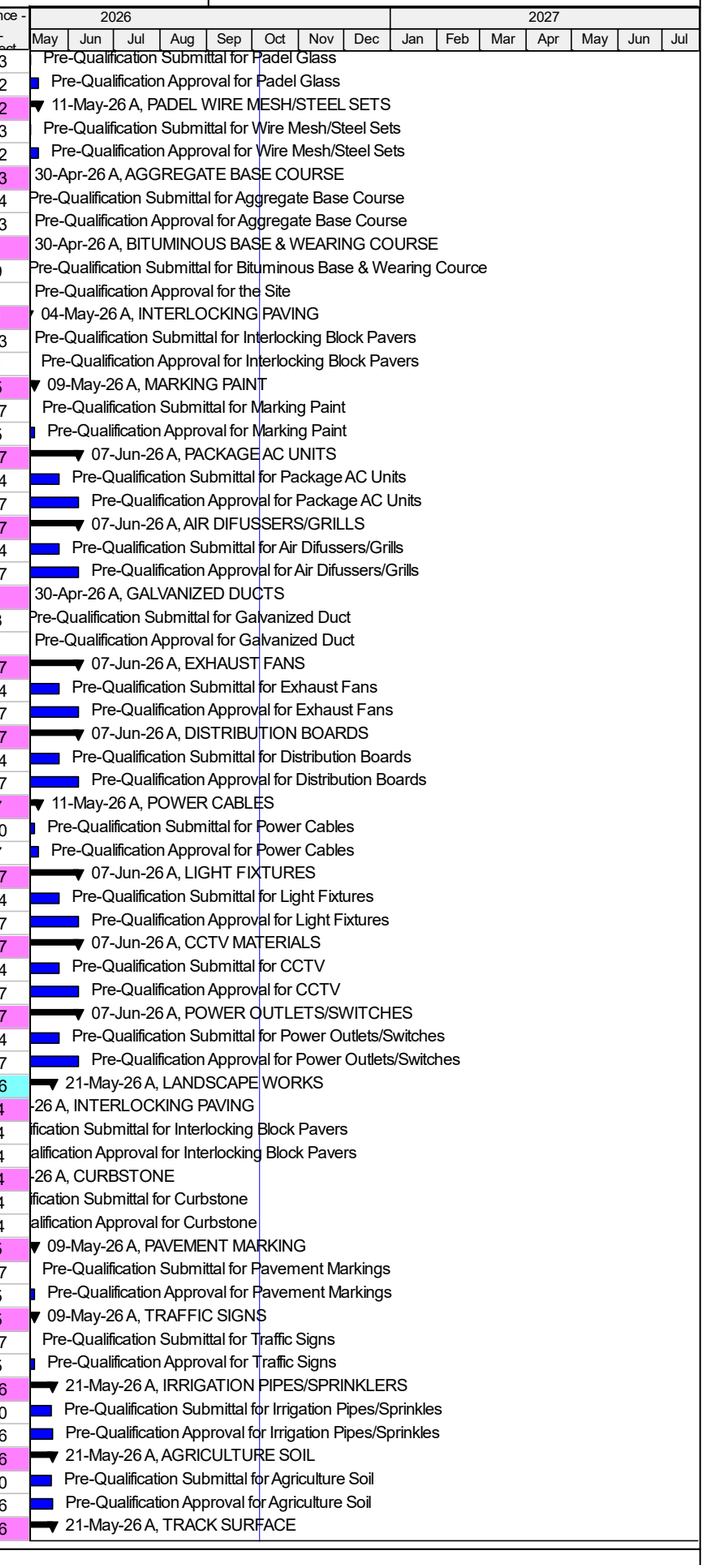

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-EN	Pre-Qualification Submittal for Track Surface	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EN	Pre-Qualification Approval for Track Surface	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
GRASS/TREES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
MLTX-02-005-EN	Pre-Qualification Submittal for Grass/Trees	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-30
MLTX-02-005-EN	Pre-Qualification Approval for Grass/Trees	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	21-May-26 A	0.00	0.00	0.00	-16
CABLES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
MLTX-02-005-EN	Pre-Qualification Submittal for Cables	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	09-May-26 A	0.00	0.00	0.00	-20
MLTX-02-005-EN	Pre-Qualification Approval for Cables	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	11-May-26 A	0.00	0.00	0.00	-7
LIGHT POLES		30	0%	0%	30-Mar-26	03-May-26	11-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-15
MLTX-02-005-EN	Pre-Qualification Submittal for Lighting poles	15	100%	100%	30-Mar-26	15-Apr-26	11-Mar-26 A	17-May-26 A	0.00	0.00	0.00	-27
MLTX-02-005-EN	Pre-Qualification Approval for Lighting poles	15	100%	100%	16-Apr-26	03-May-26	15-Mar-26 A	20-May-26 A	0.00	0.00	0.00	-15
MATERIAL SUBMITTAL		84	0%	0%	16-Apr-26	10-Jun-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
TOILET/SERVICE WORKS		66	0%	0%	16-Apr-26	10-Jun-26	19-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
STEEL REINFORCEMENT		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Material Submittal for Steel Reinforcement	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Material Approval for Steel Reinforcement	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
READY MIX CONCRETE		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
MLTX-02-005-EN	Material Submittal for Ready Mixed Concrete	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	07-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Material Approval of Ready Mixed Concrete	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	12-Apr-26 A	0.00	0.00	0.00	33
CONCRETE BLOCKS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Material Submittal for Concrete Blocks	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Material Approval for Concrete Blocks	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
FLOOR/WALL TILES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	17-May-26 A	0.00	0.00	0.00	3
MLTX-02-005-EN	Material Submittal for Tilling Materials	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	-9
MLTX-02-005-EN	Material Approval for Tilling Material	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	17-May-26 A	0.00	0.00	0.00	3
SUSPENDED CEILING		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	13-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-EN	Material Submittal for Suspend Ceiling	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	-6
MLTX-02-005-EN	Material Approval for Suspend Ceiling	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	13-May-26 A	0.00	0.00	0.00	6
DOORS/WINDOWS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EN	Material Submittal for Doors/Windows	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	07-May-26 A	0.00	0.00	0.00	-4
MLTX-02-005-EN	Material Approval for Doors/Windows	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
FURNITURES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0
MLTX-02-005-EN	Material Submittal for Furnitures	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Material Approval for Furnitures	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	20-May-26 A	0.00	0.00	0.00	0
SANITARY FIXTURES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EN	Material Submittal for Sanitary Fixtures	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EN	Material Approval for Sanitary Fixtures	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
WATER SUPPLY PIPES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Material Submittal for Water Supply Pipes	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Material Approval for Water Supply Pipes	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
SEWAGE/DRAINAGE PIPES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
MLTX-02-005-EN	Material Submittal for Sewage/Drainage Pipes	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	06-May-26 A	0.00	0.00	0.00	-3
MLTX-02-005-EN	Material Approval for Sewage/Drainage Pipes	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	11-May-26 A	0.00	0.00	0.00	8
PACKAGE AC UNITS		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EN	Material Submittal for Package AC Units	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Material Approval for Package AC Units	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
AIR DIFUSSERS/GRILLS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Material Submittal for Air Diffusers/Grills	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Air Diffusers/Grills	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
GALVANIZED DUCTS		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	32
MLTX-02-005-EN	Material Submittal for Galvanized Ducts	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	25-Apr-26 A	0.00	0.00	0.00	22
MLTX-02-005-EN	Material Approval for Galvanized Ducts	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	30-Apr-26 A	0.00	0.00	0.00	32
EXHAUST FANS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Material Submittal for Exhaust Fans	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Exhaust Fans	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
LIGHTING FIXTURES		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EN	Material Submittal for Lighting Fixtures	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EN	Material Approval for Lighting Fixtures	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
SWITCHES/SOCKETS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EN	Material Submittal for Switches/Sockets	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EN	Material Approval for Switches/Sockets	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
EARTHING SYSTEM		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EN	Material Submittal for Earthing System	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EN	Material Approval for Earthing System	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17

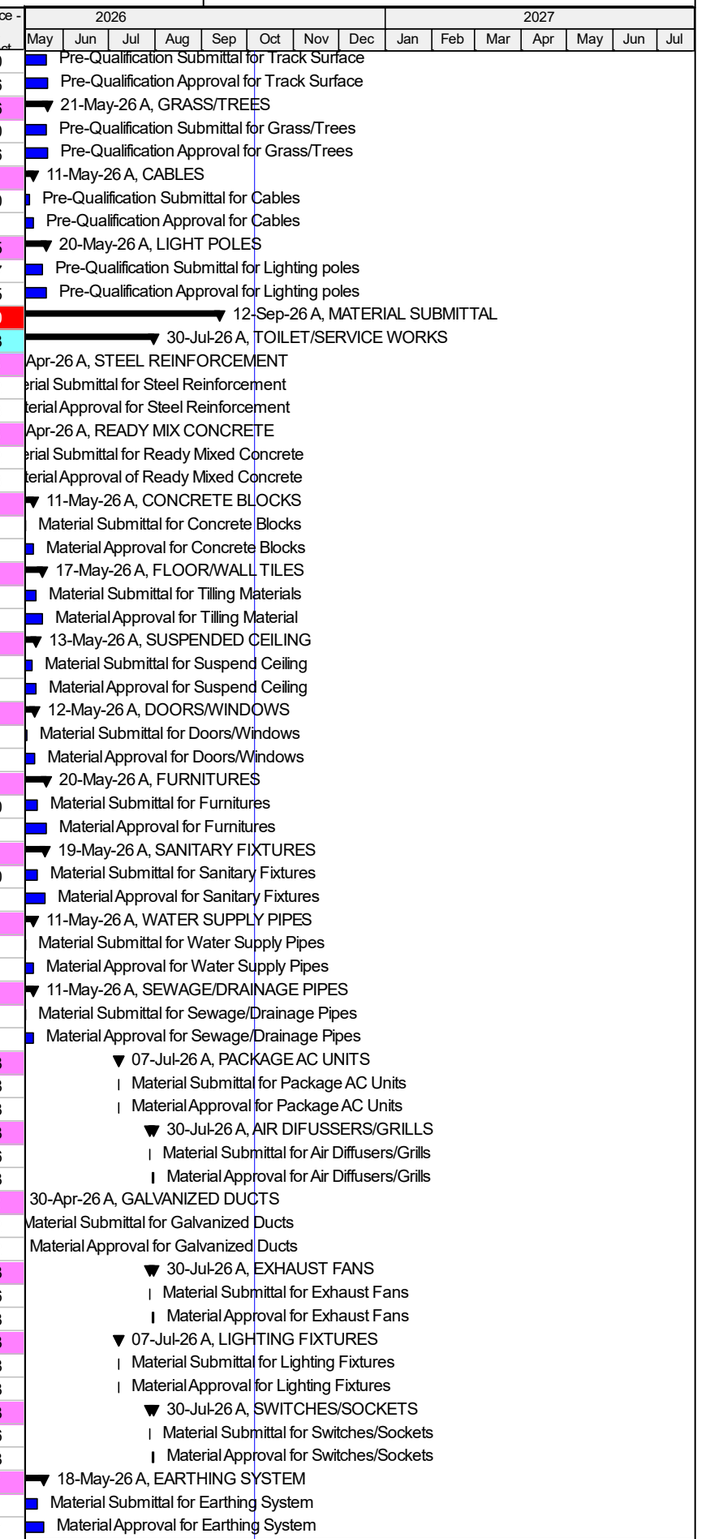

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)


Updateded schedule
D.D 05-10-2026

PROFAST شركة برو فاست المحدودة

egis

MODON مدن

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION PANNELS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Submittal for Distribution Panels	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Distribution Panels	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
PLAYGROUND WORKS		84	0%	0%	16-Apr-26	10-Jun-26	19-Mar-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
PVC MEMBRANE		30	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for PVC Membrane	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for PVC Membrane	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
STEEL TENSION CABLES		30	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Submittal for Steel Tension Cables	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Steel Tension Cables	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
EMERGENCY DOORS		28	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Submittal for Emergency Doors	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Emergency Doors	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
PRESSURE UNITS		30	0%	0%	16-Apr-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Submittal for Pressure Units	15	100%	100%	16-Apr-26	03-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-110
MLTX-02-005-EM	Material Approval for Pressure Units	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
AIR LOCK DOORS		28	0%	0%	16-Apr-26	20-May-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Submittal for Lock Doors	15	100%	100%	16-Apr-26	03-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-96
MLTX-02-005-EM	Material Approval for Lock Doors	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
ARTIFICIAL TURF		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Artificial TURF	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Artificial TURF	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
RUBBER GRANULES		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Rubber Granules	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Rubber Granules	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
PADEL GLASS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Padel Glass	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Padel Glass	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
PADEL WIRE MESH/STEEL SETS		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
MLTX-02-005-EM	Material Submittal for Wire Mesh/Steel Sets	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	14-May-26 A	0.00	0.00	0.00	-10
MLTX-02-005-EM	Material Approval for Wire Mesh/Steel Sets	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	19-May-26 A	0.00	0.00	0.00	1
AGGREGATE BASE COURSE		30	0%	0%	16-Apr-26	20-May-26	19-Mar-26 A	10-May-26 A	0.00	0.00	0.00	9
MLTX-02-005-EM	Material Submittal for Aggregate Base Course	15	100%	100%	16-Apr-26	03-May-26	19-Mar-26 A	05-May-26 A	0.00	0.00	0.00	-2
MLTX-02-005-EM	Material Approval for Aggregate Base Course	15	100%	100%	04-May-26	20-May-26	26-Mar-26 A	10-May-26 A	0.00	0.00	0.00	9
BITUMINOUS BASE & WEARING COURSE		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Material Submittal for Bituminous Base & Wearing Cource	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	05-May-26 A	0.00	0.00	0.00	13
MLTX-02-005-EM	Material Approval for the Site	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
INTERLOCKING PAVING		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
MARKING PAINT		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Submittal for Marking Paint	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Approval for Marking Paint	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
PACKAGE AC UNITS		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Submittal for Package AC Units	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Approval for Package AC Units	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
AIR DIFUSSERS/GRILLS		30	0%	0%	04-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-EM	Material Submittal for Air Difussers/Grills	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Approval for Air Difussers/Grills	15	100%	100%	21-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
GALVANIZED DUCTS		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
MLTX-02-005-EM	Material Submittal for Galvanized Duct	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	06-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-EM	Material Approval for Galvanized Duct	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	10-May-26 A	0.00	0.00	0.00	24
EXHAUST FANS		30	0%	0%	04-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-EM	Material Submittal for Exhaust Fans	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Approval for Exhaust Fans	15	100%	100%	21-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
DISTRIBUTION BOARDS		30	0%	0%	04-May-26	10-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-66
MLTX-02-005-EM	Material Submittal for Distribution Boards	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Approval for Distribution Boards	15	100%	100%	21-May-26	10-Jun-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-66
POWER CABLES		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Power Cables	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EM	Material Approval for Power Cables	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
LIGHT FIXTURES		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Submittal for Light Fixtures	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Approval for Light Fixtures	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23

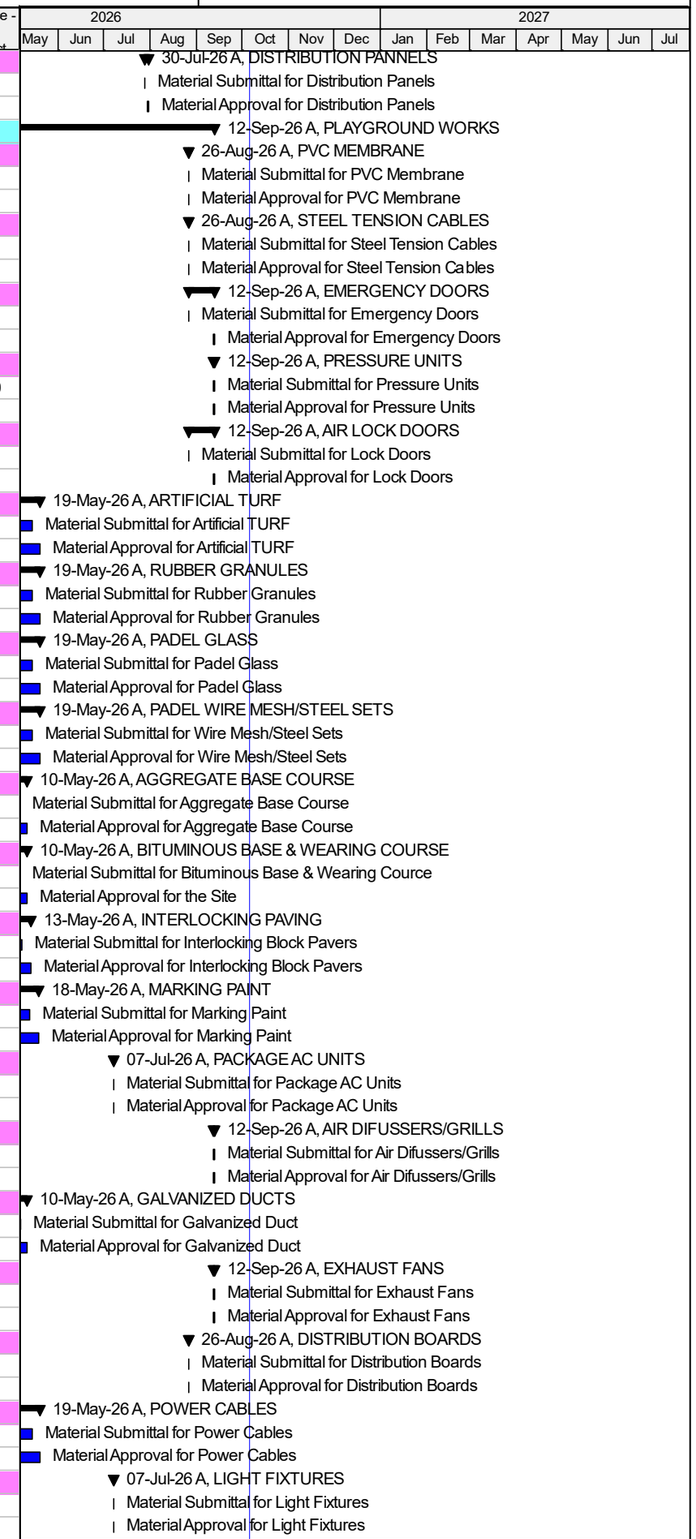

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CCTV MATERIALS		28	0%	0%	04-May-26	10-Jun-26	26-Aug-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-EM	Material Submittal for CCTV	15	100%	100%	04-May-26	20-May-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-81
MLTX-02-005-EM	Material Approval for CCTV	15	100%	100%	21-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
POWER OUTLETS/SWITCHES		30	0%	0%	04-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
MLTX-02-005-EM	Material Submittal for Power Outlets/Switches	15	100%	100%	04-May-26	20-May-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-95
MLTX-02-005-EM	Material Approval for Power Outlets/Switches	15	100%	100%	21-May-26	10-Jun-26	12-Sep-26 A	12-Sep-26 A	0.00	0.00	0.00	-80
LANDSCAPE WORKS		66	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
INTERLOCKING PAVING		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Submittal for Interlocking Block Pavers	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Interlocking Block Pavers	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
CURBSTONE		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
MLTX-02-005-EM	Material Submittal for Curbstone	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	07-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-EM	Material Approval for Curbstone	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	13-May-26 A	0.00	0.00	0.00	21
PAVEMENT MARKING		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Submittal for Pavement Markings	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Approval for Pavement Markings	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
TRAFFIC SIGNS		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
MLTX-02-005-EM	Material Submittal for Traffic Signs	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	12-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-EM	Material Approval for Traffic Signs	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	18-May-26 A	0.00	0.00	0.00	17
IRRIGATION PIPES/SPRINKLERS		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Submittal for Irrigation Pipes/Sprinkles	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Irrigation Pipes/Sprinkles	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
AGRICULTURE SOIL		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Agriculture Soil	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for Agriculture Soil	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	14
TRACK SURFACE		30	0%	0%	04-May-26	10-Jun-26	28-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
MLTX-02-005-EM	Material Submittal for Track Surface	15	100%	100%	04-May-26	20-May-26	28-Jul-26 A	28-Jul-26 A	0.00	0.00	0.00	-56
MLTX-02-005-EM	Material Approval for Track Surface	15	100%	100%	21-May-26	10-Jun-26	30-Jul-26 A	30-Jul-26 A	0.00	0.00	0.00	-43
GRASS/TREES		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	21-May-26 A	0.00	0.00	0.00	14
MLTX-02-005-EM	Material Submittal for Grass/Trees	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	16-May-26 A	0.00	0.00	0.00	4
MLTX-02-005-EM	Material Approval for Grass/Trees	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	21-May-26 A	0.00	0.00	0.00	14
CABLES		30	0%	0%	04-May-26	10-Jun-26	24-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
MLTX-02-005-EM	Material Submittal for Cables	15	100%	100%	04-May-26	20-May-26	24-Mar-26 A	14-May-26 A	0.00	0.00	0.00	5
MLTX-02-005-EM	Material Approval for Cables	15	100%	100%	21-May-26	10-Jun-26	28-Mar-26 A	19-May-26 A	0.00	0.00	0.00	16
LIGHT POLES		30	0%	0%	04-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
MLTX-02-005-EM	Material Submittal for Lighting poles	15	100%	100%	04-May-26	20-May-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-38
MLTX-02-005-EM	Material Approval for Lighting poles	15	100%	100%	21-May-26	10-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-23
PROCUREMENT		189	0%	0%	21-May-26	08-Nov-26	04-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-89
SHORT LEAD ITEM		189	0%	0%	21-May-26	21-Oct-26	04-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-104
TOILET/SERVICE WORKS		100	0%	0%	21-May-26	11-Aug-26	04-Apr-26 A	08-Nov-26	0.00	0.00	0.00	-75
STEEL REINFORCEMENT		10	0%	0%	21-May-26	04-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	PO for Steel Reinforcement	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	18-May-26 A	0.00	0.00	0.00	7
MLTX-02-005-PR-1	Material Delivery of Steel Reinforcement	5	100%	100%	31-May-26	04-Jun-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	11
CONCRETE BLOCKS		61	0%	0%	31-May-26	14-Jun-26	09-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-20
MLTX-02-005-PR-1	PO for Concrete Blocks	5	100%	100%	31-May-26	04-Jun-26	09-Apr-26 A	18-May-26 A	0.00	0.00	0.00	12
MLTX-02-005-PR-1	Material Delivery of Concrete Blocks	8	100%	100%	06-Jun-26	14-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-20
FLOOR/WALL TILES		18	0%	0%	06-Jun-26	25-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-46
MLTX-02-005-PR-1	PO for Tilling Materials	5	100%	100%	06-Jun-26	10-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-59
MLTX-02-005-PR-1	Material Delivery of Tailling Material	13	100%	100%	11-Jun-26	25-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-46
SUSPENDED CEILING		18	0%	0%	22-Jul-26	11-Aug-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-6
MLTX-02-005-PR-1	PO for Suspend Ceiling	5	100%	100%	22-Jul-26	27-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-19
MLTX-02-005-PR-1	Material Delivery of Suspend Ceiling	13	100%	100%	28-Jul-26	11-Aug-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-6
DOORS/WINDOWS		20	0%	0%	11-Jun-26	04-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-63
MLTX-02-005-PR-1	PO for Doors/Windows	5	100%	100%	11-Jun-26	16-Jun-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-78
MLTX-02-005-PR-1	Material Delivery for Doors/Windows	15	100%	100%	17-Jun-26	04-Jul-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-63
WATER SUPPLY PIPES		12	0%	0%	17-Jun-26	30-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-6
MLTX-02-005-PR-1	PO for Water Supply Pipes	5	100%	100%	17-Jun-26	22-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-13
MLTX-02-005-PR-1	Material Delivery for Water Supply Pipes	7	100%	100%	23-Jun-26	30-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-6
SEWAGE/DRAINAGE PIPES		12	0%	0%	17-Jun-26	30-Jun-26	02-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	17
MLTX-02-005-PR-1	PO for Sewage/Drainage Pipes	5	100%	100%	17-Jun-26	22-Jun-26	02-Jun-26 A	02-Jun-26 A	0.00	0.00	0.00	17
MLTX-02-005-PR-1	Material Delivery for Sewage/Drainage Pipes	7	100%	100%	23-Jun-26	30-Jun-26	10-Jun-26 A	10-Jun-26 A	0.00	0.00	0.00	17
SANITARY FIXTURES		18	0%	0%	23-Jun-26	13-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-31
MLTX-02-005-PR-1	PO for Sanitary Fixtures	5	100%	100%	23-Jun-26	28-Jun-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-44
MLTX-02-005-PR-1	Material Delivery for Sanitary Fixtures	13	100%	100%	29-Jun-26	13-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-31

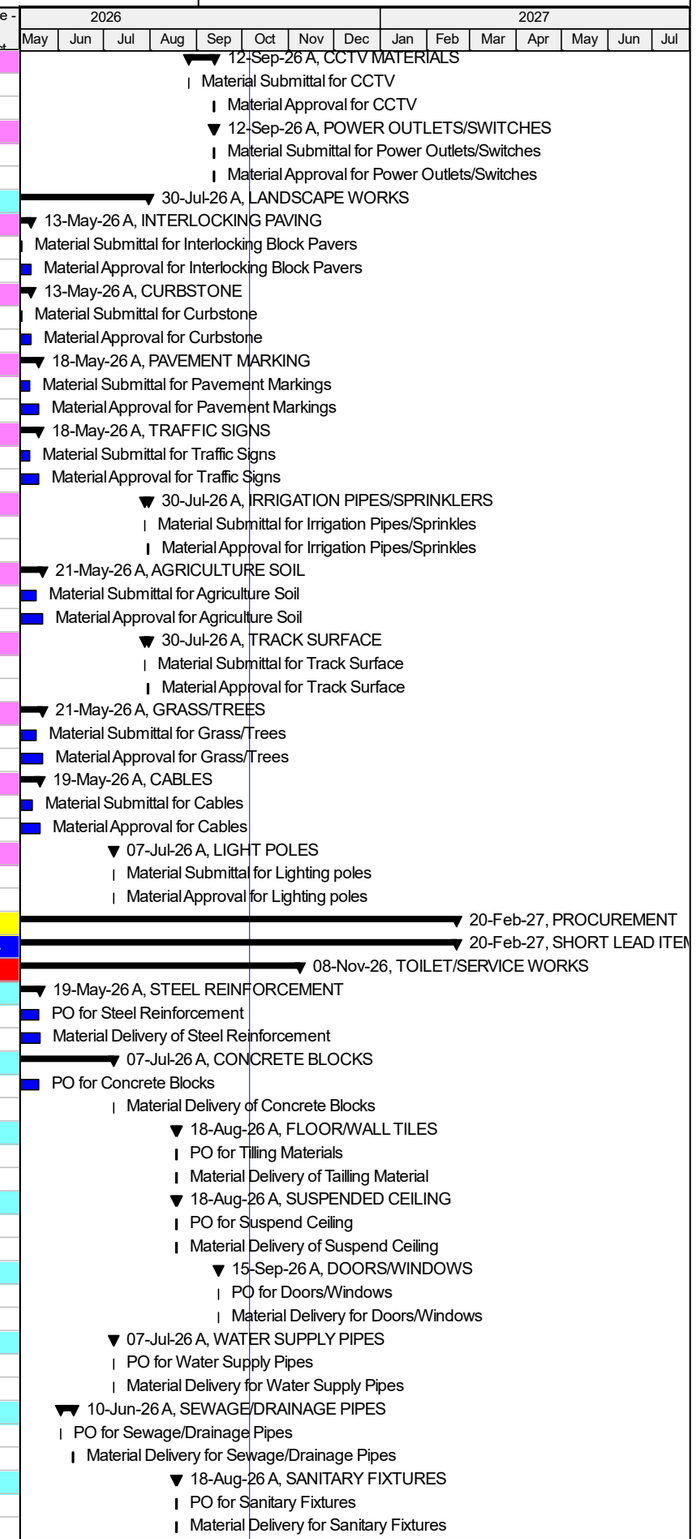

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
PACKAGE AC UNITS		20	0%	0%	29-Jun-26	21-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	12
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	29-Jun-26	04-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	05-Jul-26	21-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	12
AIR DIFUSSERS/GRILLS		20	0%	0%	29-Jun-26	21-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	PO for Air Diffusers/Grills	5	100%	100%	29-Jun-26	04-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Air Diffusers/Grills	15	100%	100%	05-Jul-26	21-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-24
GALVANIZED DUCTS		20	0%	0%	29-Jun-26	21-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	PO for Galvanized Ducts	5	100%	100%	29-Jun-26	04-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Galvanized Ducts	15	100%	100%	05-Jul-26	21-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-24
EXHAUST FANS		15	0%	0%	29-Jun-26	15-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-29
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	100%	29-Jun-26	04-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-39
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	10	100%	100%	05-Jul-26	15-Jul-26	18-Aug-26 A	18-Aug-26 A	0.00	0.00	0.00	-29
LIGHTING FIXTURES		31	0%	0%	05-Jul-26	21-Jul-26	07-Jul-26 A	17-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Lighting Fixtures	5	100%	100%	05-Jul-26	09-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	2
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
SWITCHES/SOCKETS		12	0%	0%	11-Jul-26	23-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	11-Jul-26	15-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	16-Jul-26	23-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
EARTHING SYSTEM		27	0%	0%	11-Jun-26	12-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0
MLTX-02-005-PR-1	PO for Earthing System	5	100%	100%	11-Jun-26	16-Jun-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	-22
MLTX-02-005-PR-1	Material Delivery for Earthing System	15	100%	100%	25-Jun-26	12-Jul-26	12-Jul-26 A	12-Jul-26 A	0.00	0.00	0.00	0
DISTRIBUTION PANNELS		20	0%	0%	11-Jun-26	04-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	17-Jun-26	04-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
FURNITURES		29	0%	0%	05-Jul-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	05-Jul-26	14-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	15-Jul-26	06-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
PLAYGROUND WORKS		121	0%	0%	21-May-26	29-Aug-26	04-Apr-26 A	02-Dec-26	0.00	0.00	0.00	-81
PVC MEMBRANE		41	0%	0%	21-May-26	29-Jun-26	04-Apr-26 A	29-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	PO for PVC Membrane	10	100%	100%	21-May-26	04-Jun-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	06-Jun-26	29-Jun-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-104
ARTIFICIAL TURF		22	0%	0%	30-Jun-26	19-Jul-26	04-Apr-26 A	12-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Artificial TURF	5	100%	100%	30-Jun-26	05-Jul-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	37
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	06-Jul-26	19-Jul-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-99
RUBBER GRANULES		32	0%	0%	21-May-26	13-Jun-26	04-Apr-26 A	19-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Rubber Granules	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-109
PADEL GLASS		38	0%	0%	21-May-26	20-Jun-26	04-Apr-26 A	26-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Padel Glass	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	19-May-26 A	0.00	0.00	0.00	6
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	31-May-26	20-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-109
PADEL WIRE MESH/STEEL SETS		30	0%	0%	31-May-26	22-Jun-26	09-Apr-26 A	22-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	PO for Wire Mesh/Steel Sets	5	100%	100%	31-May-26	04-Jun-26	09-Apr-26 A	19-May-26 A	0.00	0.00	0.00	11
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-104
AGGREGATE BASE COURSE		56	0%	0%	21-May-26	07-Jun-26	04-Apr-26 A	07-Jul-26 A	0.00	0.00	0.00	-26
MLTX-02-005-PR-1	PO for Aggregate Base Course	5	100%	100%	21-May-26	30-May-26	04-Apr-26 A	14-May-26 A	0.00	0.00	0.00	10
MLTX-02-005-PR-1	Material Delivery for Aggregate Base Course	7	100%	100%	31-May-26	07-Jun-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	-26
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	11-Jun-26	24-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for the Site	7	100%	0%	17-Jun-26	24-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
INTERLOCKING PAVING		12	0%	0%	16-Jul-26	29-Jul-26	26-Oct-26	08-Nov-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	0%	16-Jul-26	21-Jul-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	7	100%	0%	22-Jul-26	29-Jul-26	01-Nov-26	08-Nov-26	0.00	0.00	0.00	-86
MARKING PAINT		12	0%	0%	17-Jun-26	30-Jun-26	12-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	17-Jun-26	22-Jun-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	23-Jun-26	30-Jun-26	18-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
PACKAGE AC UNITS		20	0%	0%	20-Jul-26	11-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	30
MLTX-02-005-PR-1	PO for Package AC Units	5	100%	100%	20-Jul-26	25-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	15
MLTX-02-005-PR-1	Material Delivery for Package AC Units	15	100%	100%	26-Jul-26	11-Aug-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	30
AIR DIFUSSERS/GRILLS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79

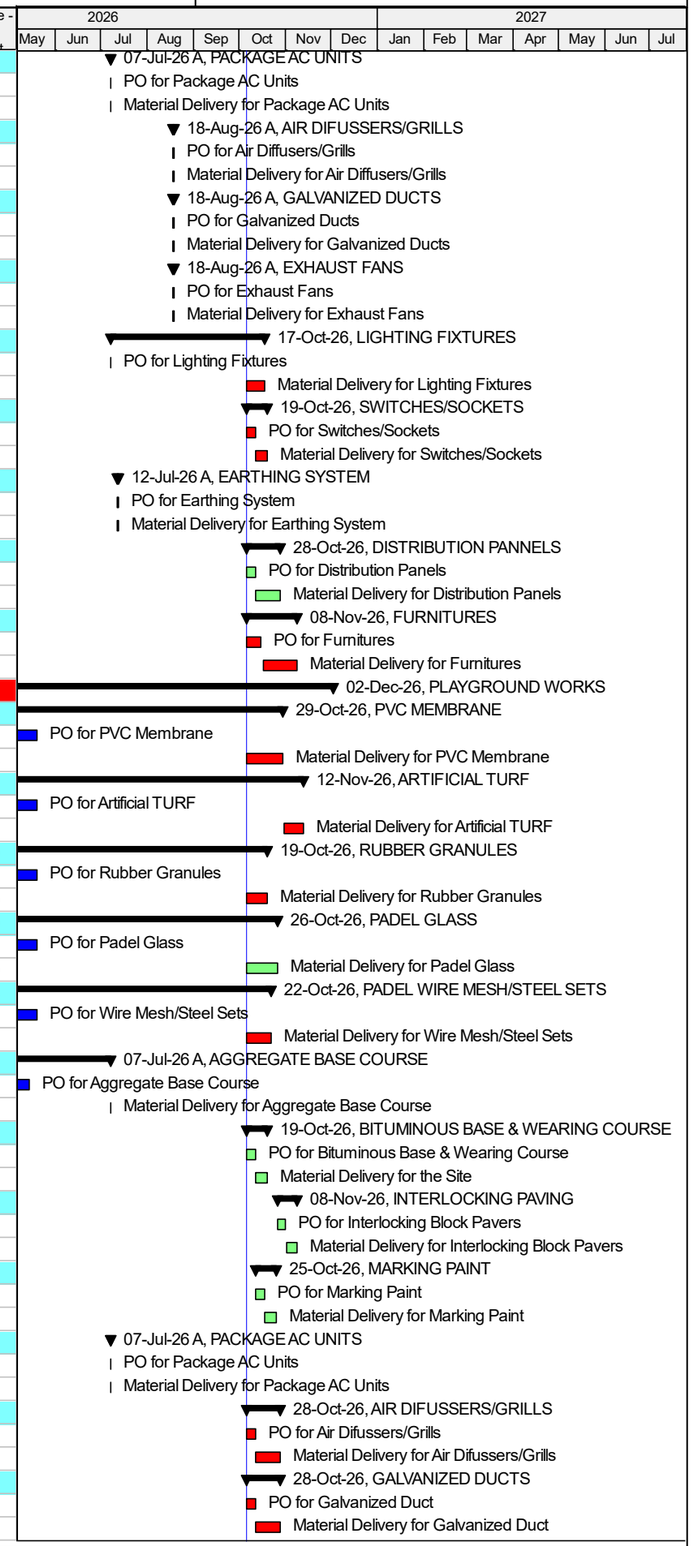

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
EXHAUST FANS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
DISTRIBUTION BOARDS		20	0%	0%	05-Jul-26	27-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	05-Jul-26	09-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	11-Jul-26	27-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
POWER CABLES		15	0%	0%	11-Jul-26	27-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	11-Jul-26	15-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	16-Jul-26	27-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-94
LIGHT FIXTURES		46	0%	0%	16-Jul-26	02-Aug-26	07-Jul-26 A	15-Nov-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	PO for Light Fixtures	5	100%	100%	16-Jul-26	21-Jul-26	07-Jul-26 A	07-Jul-26 A	0.00	0.00	0.00	12
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-89
CCTV MATERIALS		50	0%	0%	22-Jul-26	29-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	22-Jul-26	27-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	12-Aug-26	29-Aug-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-81
POWER OUTLETS/SWITCHES		21	0%	0%	28-Jul-26	20-Aug-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	28-Jul-26	03-Aug-26	20-Oct-26	26-Oct-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	04-Aug-26	20-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
LANDSCAPE WORKS		130	0%	0%	04-Aug-26	21-Oct-26	16-May-26 A	20-Feb-27	0.00	0.00	0.00	-104
INTERLOCKING PAVING		21	0%	0%	04-Aug-26	23-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-3
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	100%	04-Aug-26	09-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-15
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	12	100%	100%	10-Aug-26	23-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-3
CURBSTONE		21	0%	0%	04-Aug-26	23-Aug-26	14-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	26
MLTX-02-005-PR-1	PO for Curbstone	5	100%	100%	04-Aug-26	09-Aug-26	14-Jul-26 A	14-Jul-26 A	0.00	0.00	0.00	22
MLTX-02-005-PR-1	Material Delivery for Curbstone	12	100%	100%	10-Aug-26	23-Aug-26	23-Jul-26 A	23-Jul-26 A	0.00	0.00	0.00	26
PAVEMENT MARKING		15	0%	0%	04-Aug-26	20-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	04-Aug-26	09-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	10-Aug-26	20-Aug-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-71
TRAFFIC SIGNS		14	0%	0%	05-Oct-26	20-Oct-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	PO for Traffic Signs	5	20%	0%	05-Oct-26	10-Oct-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	11-Oct-26	20-Oct-26	08-Nov-26	17-Nov-26	0.00	0.00	0.00	-24
IRRIGATION PIPES/SPRINKLERS		14	0%	0%	10-Aug-26	24-Aug-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	0%	10-Aug-26	15-Aug-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	16-Aug-26	24-Aug-26	09-Nov-26	17-Nov-26	0.00	0.00	0.00	-72
AGRICULTURE SOIL		17	0%	0%	22-Sep-26	12-Oct-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Agriculture Soil	5	100%	0%	22-Sep-26	28-Sep-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	12	50%	0%	29-Sep-26	12-Oct-26	03-Feb-27	16-Feb-27	0.00	0.00	0.00	-109
TRACK SURFACE		30	0%	0%	05-Sep-26	21-Sep-26	16-May-26 A	27-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Track Surface	5	100%	100%	05-Sep-26	09-Sep-26	16-May-26 A	20-May-26 A	0.00	0.00	0.00	93
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	10-Sep-26	21-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-109
GRASS/TREES		30	0%	0%	29-Sep-26	21-Oct-26	17-May-26 A	20-Feb-27	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	PO for Grass/Trees	5	100%	100%	29-Sep-26	04-Oct-26	17-May-26 A	20-May-26 A	0.00	0.00	0.00	113
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	6.67%	0%	05-Oct-26	21-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-104
CABLES		33	0%	0%	10-Aug-26	01-Sep-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	-12
MLTX-02-005-PR-1	PO for Cables	5	100%	100%	10-Aug-26	15-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	-10
MLTX-02-005-PR-1	Material Delivery for Cables	15	100%	100%	16-Aug-26	01-Sep-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	-12
LONG LEAD ITEM		99	0%	0%	21-May-26	08-Nov-26	26-Aug-26 A	16-Jan-27	0.00	0.00	0.00	-59
PLAYGROUND WORKS		88	0%	0%	21-May-26	03-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-114
STEEL TENSION CABLES		65	0%	0%	21-May-26	08-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	27-Jun-26	30-Jul-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	03-Jun-26	25-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	7	100%	0%	01-Aug-26	08-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-114
EMERGENCY DOORS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
PRESSURE UNITS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
AIR LOCK DOORS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114

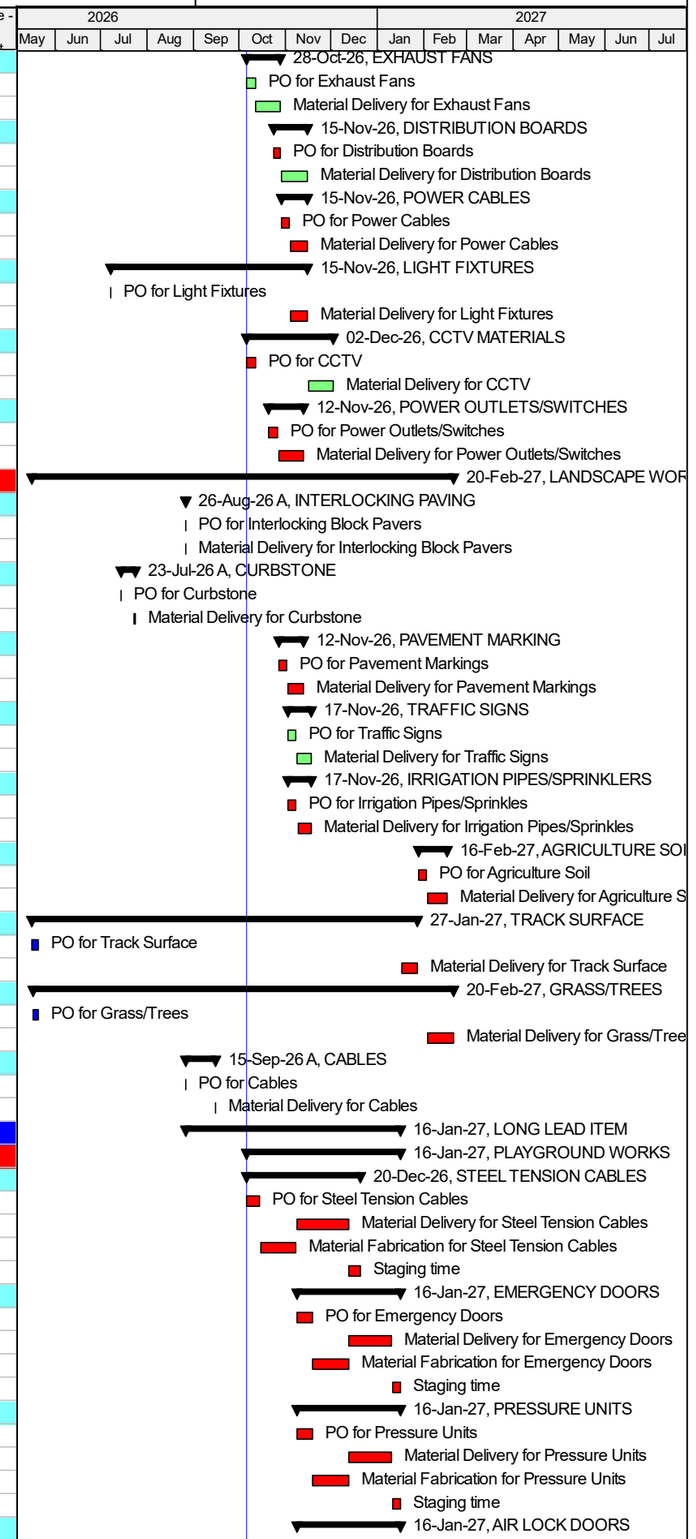

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
LANDSCAPE WORKS		89	0%	0%	16-Aug-26	08-Nov-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	45
LIGHT POLES		89	0%	0%	16-Aug-26	08-Nov-26	26-Aug-26 A	15-Sep-26 A	0.00	0.00	0.00	45
MLTX-02-005-PR-1	PO for Lighting poles	10	100%	100%	16-Aug-26	26-Aug-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	0
MLTX-02-005-PR-1	Material Fabrication for Lighting poles	30	100%	100%	30-Aug-26	04-Oct-26	26-Aug-26 A	26-Aug-26 A	0.00	0.00	0.00	32
MLTX-02-005-PR-1	Material Delivery for Lighting poles	25	4%	100%	05-Oct-26	02-Nov-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	40
MLTX-02-005-PR-1	Staging time	5	0%	100%	03-Nov-26	08-Nov-26	15-Sep-26 A	15-Sep-26 A	0.00	0.00	0.00	45
CONSTRUCTION PHASE		246	57.49%	36.54%	16-Apr-26	29-Dec-26	04-Apr-26 A	15-Apr-27	5,693,852.37	3,619,240.90	9,904,307.16	-88
SITE WORKS		246	51.91%	32.51%	16-Apr-26	29-Dec-26	04-Apr-26 A	15-Apr-27	4,518,861.71	2,829,873.24	8,704,943.25	-88
EARTH WORKS		66	100%	100%	16-Apr-26	31-May-26	04-Apr-26 A	13-Aug-26 A	947,872.24	947,872.24	947,872.24	-63
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	12	100%	100%	27-Apr-26	10-May-26	06-Apr-26 A	12-Apr-26 A	167,998.20	167,998.20	167,998.20	24
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	9	100%	100%	16-Apr-26	26-Apr-26	04-Apr-26 A	02-Aug-26 A	350,569.48	350,569.48	350,569.48	-81
MLTX-02-005-CN-133	Excavation (in all types of soil) including Compaction	7	100%	100%	11-May-26	18-May-26	06-Apr-26 A	05-Aug-26 A	132,864.45	132,864.45	132,864.45	-64
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	10	100%	100%	11-May-26	21-May-26	13-Apr-26 A	30-Apr-26 A	118,662.34	118,662.34	118,662.34	19
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	20	100%	100%	27-Apr-26	19-May-26	06-Apr-26 A	08-Apr-26 A	76,629.23	76,629.23	76,629.23	35
MLTX-02-005-CN-133	Backfilling on Layers (Selected Soil) including Compaction	8	100%	100%	19-May-26	31-May-26	21-Apr-26 A	13-Aug-26 A	101,148.54	101,148.54	101,148.54	-63
LANDSCAPE WORKS		229	46.39%	23.69%	23-May-26	29-Dec-26	19-May-26 A	15-Apr-27	3,570,989.48	1,823,507.67	7,698,577.68	-88
PLAYGROUND AREA		219	73.72%	53.64%	23-May-26	08-Dec-26	19-May-26 A	04-Apr-27	972,520.36	707,562.27	1,319,195.08	-96
FOOTBALL PLAYGROUND		211	88.81%	35%	23-May-26	11-Nov-26	19-May-26 A	25-Mar-27	281,392.97	110,897.50	316,849.99	-111
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Football Playground)	10	100%	100%	23-May-26	06-Jun-26	19-May-26 A	31-May-26 A	79,212.50	79,212.50	79,212.50	5
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Football	16	100%	100%	25-Jun-26	13-Jul-26	01-Jun-26 A	18-Jun-26 A	15,842.50	15,842.50	15,842.50	22
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	24-Aug-26	15-Sep-26	14-Nov-26	06-Dec-26	158,424.99	0.00	158,424.99	-69
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	31,685.00	-111
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	21	76.19%	0%	16-Sep-26	11-Oct-26	07-Dec-26	30-Dec-26	12,070.48	0.00	15,842.50	-69
MLTX-02-005-CI	Aggregate basecourse layer (Football Playground)	21	100%	100%	14-Jul-26	06-Aug-26	20-Jun-26 A	28-Jun-26 A	15,842.50	15,842.50	15,842.50	35
PADEL PLAYGROUND		190	70%	70%	07-Jun-26	11-Nov-26	19-May-26 A	25-Mar-27	163,788.80	163,788.80	233,984.00	-111
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Padel Playground)	7	100%	100%	07-Jun-26	14-Jun-26	19-May-26 A	31-May-26 A	81,894.40	81,894.40	81,894.40	12
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Padel	16	100%	100%	25-Jun-26	13-Jul-26	01-Jun-26 A	18-Jun-26 A	11,699.20	11,699.20	11,699.20	22
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Padel Playground)	21	100%	100%	01-Sep-26	26-Sep-26	24-Aug-26 A	25-Aug-26 A	58,496.00	58,496.00	58,496.00	26
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	58,496.00	-111
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	11,699.20	-111
MLTX-02-005-CI	Aggregate basecourse layer (Padel Playground)	21	100%	100%	08-Aug-26	31-Aug-26	20-Jun-26 A	28-Jun-26 A	11,699.20	11,699.20	11,699.20	56
BASKETBALL PLAYGROUND		177	51.06%	70%	15-Jun-26	21-Nov-26	19-May-26 A	04-Apr-27	165,033.59	226,230.90	323,187.00	-111
MLTX-02-005-CI	Preparation and Proofing for Subgrade (Basketball	10	100%	100%	15-Jun-26	25-Jun-26	19-May-26 A	31-May-26 A	95,055.00	95,055.00	95,055.00	22
MLTX-02-005-CI	Backfilling and Compaction of Base Layers (Basketball	11	100%	100%	01-Jul-26	13-Jul-26	01-Jun-26 A	18-Jun-26 A	16,159.35	16,159.35	16,159.35	22
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Basketball	21	38.1%	100%	27-Sep-26	20-Oct-26	20-Aug-26 A	25-Aug-26 A	37,659.89	98,857.20	98,857.20	47
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	8	0%	0%	12-Nov-26	21-Nov-26	27-Mar-27	04-Apr-27	0.00	0.00	80,796.75	-111
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	12-Nov-26	21-Nov-26	27-Mar-27	04-Apr-27	0.00	0.00	16,159.35	-111
MLTX-02-005-CI	Aggregate basecourse layer (Basketball Playground)	21	100%	100%	01-Sep-26	26-Sep-26	20-Jun-26 A	28-Jun-26 A	16,159.35	16,159.35	16,159.35	77
PADEL FENCE		153	0%	30%	22-Nov-26	08-Dec-26	08-Aug-26 A	12-Nov-26	0.00	24,860.73	82,869.08	22
MLTX-02-005-CI	Excavation for Fence	8	0%	100%	22-Nov-26	30-Nov-26	08-Aug-26 A	08-Aug-26 A	0.00	8,286.91	8,286.91	97
MLTX-02-005-CI	Concrete Foundation for Fence including Posts Fixation	7	0%	100%	22-Nov-26	29-Nov-26	15-Aug-26 A	23-Aug-26 A	0.00	16,573.82	16,573.82	83
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	22-Nov-26	28-Nov-26	27-Oct-26	02-Nov-26	0.00	0.00	4,143.45	22
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	33,147.63	22
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	16,573.82	22
MLTX-02-005-CI	Install of Fence Gates	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	4,143.45	22
CURBSTOEN/INTERLOCK		68	100%	50.17%	12-Aug-26	01-Oct-26	10-Aug-26 A	07-Dec-26	362,305.01	181,784.34	362,305.01	-57
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	100%	0%	07-Sep-26	01-Oct-26	14-Nov-26	07-Dec-26	180,520.67	0.00	180,520.67	-57
MLTX-02-005-CI	Concrete Works Under Curbstone	3	100%	100%	12-Aug-26	15-Aug-26	10-Aug-26 A	10-Aug-26 A	54,535.30	54,535.30	54,535.30	4
MLTX-02-005-CI	Curbstone Installation	4	100%	100%	02-Sep-26	06-Sep-26	11-Aug-26 A	13-Aug-26 A	127,249.04	127,249.04	127,249.04	20
AIR DOME		190	49.24%	11.91%	14-Jul-26	24-Nov-26	14-Jul-26 A	15-Apr-27	2,403,554.46	581,544.30	4,881,359.87	-118
CIVIL WORKS		113	100%	29.58%	14-Jul-26	04-Oct-26	14-Jul-26 A	02-Dec-26	1,966,294.68	581,544.30	1,966,294.68	-51
MLTX-02-005-CI	Excavation for Foundation (Air Dome)	10	100%	100%	14-Jul-26	25-Jul-26	14-Jul-26 A	02-Aug-26 A	127,762.34	127,762.34	127,762.34	-7
MLTX-02-005-CI	Concrete Works for Foundations including Anchor Bolts (Air	15	100%	100%	26-Jul-26	11-Aug-26	10-Aug-26 A	21-Sep-26 A	168,176.84	168,176.84	168,176.84	-35
MLTX-02-005-CI	Cable System Installation (Air Dome)	10	100%	100%	12-Aug-26	23-Aug-26	21-Sep-26 A	21-Sep-26 A	41,790.29	41,790.29	41,790.29	-25
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	15	100%	0%	16-Sep-26	04-Oct-26	16-Nov-26	02-Dec-26	936,278.81	0.00	936,278.81	-51
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	100%	0%	16-Sep-26	28-Sep-26	16-Nov-26	26-Nov-26	448,471.57	0.00	448,471.57	-51
MLTX-02-005-CI	Perimeter Clamping System Installation	10	100%	100%	05-Sep-26	15-Sep-26	21-Sep-26 A	28-Sep-26 A	243,814.83	243,814.83	243,814.83	-10
MECHANICAL WORKS		33	35.45%	0%	29-Sep-26	05-Nov-26	06-Feb-27	20-Mar-27	437,259.78	0.00	1,233,296.81	-111
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	60%	0%	29-Sep-26	10-Oct-26	06-Feb-27	16-Feb-27	437,259.78	0.00	728,766.30	-111
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	11-Oct-26	25-Oct-26	17-Feb-27	04-Mar-27	0.00	0.00	336,353.67	-111

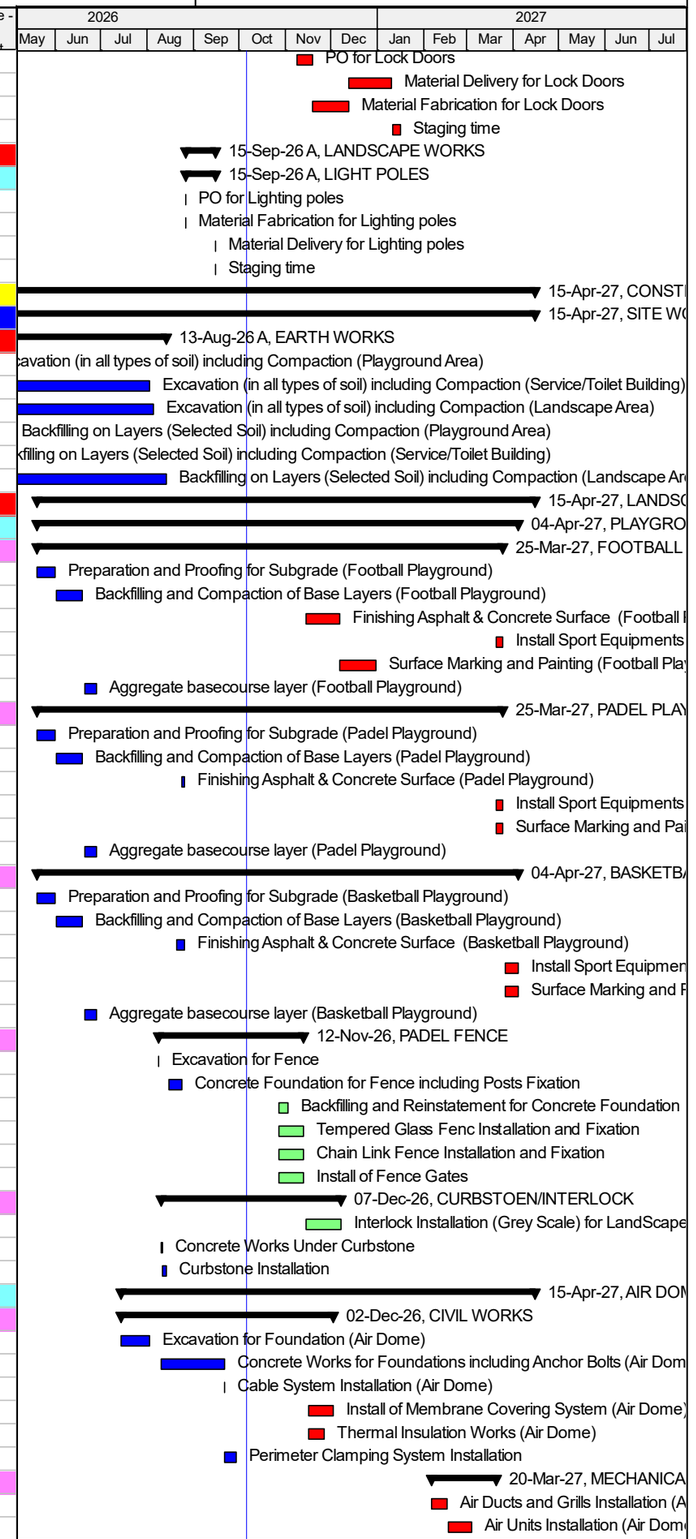

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	26-Oct-26	05-Nov-26	06-Mar-27	20-Mar-27	0.00	0.00	168,176.84	-111
ELECTRICAL WORKS		39	0%	0%	11-Oct-26	24-Nov-26	17-Feb-27	07-Apr-27	0.00	0.00	1,513,591.54	-111
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	11-Oct-26	21-Oct-26	17-Feb-27	01-Mar-27	0.00	0.00	224,235.78	-111
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	22-Oct-26	29-Oct-26	02-Mar-27	09-Mar-27	0.00	0.00	168,176.84	-111
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	31-Oct-26	05-Nov-26	14-Mar-27	20-Mar-27	0.00	0.00	168,176.84	-111
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	11	0%	0%	07-Nov-26	18-Nov-26	21-Mar-27	01-Apr-27	0.00	0.00	504,530.51	-111
MLTX-02-005-CI	Control System Installation (Air Dome)	5	0%	0%	19-Nov-26	24-Nov-26	03-Apr-27	07-Apr-27	0.00	0.00	448,471.57	-111
FINISHES WORKS		29	0%	0%	31-Oct-26	22-Nov-26	14-Mar-27	15-Apr-27	0.00	0.00	168,176.84	-120
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	10	0%	0%	31-Oct-26	10-Nov-26	14-Mar-27	24-Mar-27	0.00	0.00	112,117.89	-111
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	10	0%	0%	11-Nov-26	22-Nov-26	05-Apr-27	15-Apr-27	0.00	0.00	56,058.95	-120
IRRIGATION NETWORK		52	78.37%	80.44%	27-Sep-26	14-Oct-26	24-Aug-26 A	18-Feb-27	119,455.06	122,596.50	152,414.87	-109
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Main Line)	3	100%	100%	27-Sep-26	29-Sep-26	24-Aug-26 A	14-Sep-26 A	53,620.00	53,620.00	53,620.00	12
MLTX-02-005-CN-1	Installing of HDPE Pipes for Irrigation Network (Branch Lines)	3	100%	100%	30-Sep-26	03-Oct-26	19-Sep-26 A	29-Sep-26 A	50,127.83	50,127.83	50,127.83	3
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	3	66.67%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	08-Oct-26	15,707.23	18,848.67	23,560.84	-2
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	13-Oct-26	14-Oct-26	17-Feb-27	18-Feb-27	0.00	0.00	25,106.20	-109
NATURAL GROUND		30	0%	0%	07-Oct-26	10-Nov-26	10-Oct-26	12-Nov-26	0.00	0.00	191,740.00	-2
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	25-Oct-26	10-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	126,740.00	-2
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	0%	0%	07-Oct-26	24-Oct-26	10-Oct-26	26-Oct-26	0.00	0.00	65,000.00	-2
PLANTING		23	0%	0%	15-Oct-26	10-Nov-26	20-Feb-27	22-Mar-27	0.00	0.00	347,251.46	-109
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	0%	15-Oct-26	21-Oct-26	20-Feb-27	27-Feb-27	0.00	0.00	104,175.44	-109
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	03-Nov-26	10-Nov-26	15-Mar-27	22-Mar-27	0.00	0.00	141,732.50	-109
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	22-Oct-26	02-Nov-26	28-Feb-27	14-Mar-27	0.00	0.00	101,343.52	-109
WALKING/BIKE PATHS		10	0%	100%	11-Nov-26	22-Nov-26	19-Jul-26 A	16-Sep-26 A	0.00	336,345.00	336,345.00	56
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	10	0%	100%	11-Nov-26	22-Nov-26	19-Jul-26 A	16-Sep-26 A	0.00	171,909.67	171,909.67	56
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	10	0%	100%	11-Nov-26	22-Nov-26	19-Jul-26 A	16-Sep-26 A	0.00	164,435.33	164,435.33	56
GENERAL/FURNITURE		159	16.05%	16.05%	07-Sep-26	29-Dec-26	20-Sep-26 A	13-Apr-27	75,459.60	75,459.60	470,271.40	-86
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	41
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	9	0%	0%	20-Dec-26	29-Dec-26	04-Apr-27	13-Apr-27	0.00	0.00	9,749.30	-86
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	41
MLTX-02-005-CN-1	Fixation and Installation of Benches	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	40,307.84	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	32,757.76	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	12,869.04	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	20-Dec-26	28-Dec-26	27-Oct-26	04-Nov-26	0.00	0.00	12,186.67	46
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	13	100%	100%	07-Sep-26	21-Sep-26	20-Sep-26 A	30-Sep-26 A	75,459.60	75,459.60	75,459.60	-7
MLTX-02-005-CN-1	Installing of Site Light Poles	10	0%	0%	02-Dec-26	13-Dec-26	23-Mar-27	03-Apr-27	0.00	0.00	176,072.40	-91
PARKING		145	0%	100%	02-Dec-26	19-Dec-26	18-Jul-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	77
MLTX-02-005-CN-133	Interlock Installation (8 Cm) for Parking Area (Including	11	0%	100%	07-Dec-26	19-Dec-26	10-Sep-26 A	19-Sep-26 A	0.00	40,945.33	40,945.33	77
MLTX-02-005-CN-133	Site Preparation & Compaction Under Interlock for Parking	4	0%	100%	02-Dec-26	06-Dec-26	18-Jul-26 A	18-Jul-26 A	0.00	17,548.00	17,548.00	120
TOILET/SERVICE BUILDING		116	97.97%	65.82%	01-Jun-26	11-Oct-26	23-May-26 A	28-Nov-26	1,174,990.65	789,367.66	1,199,363.91	-41
STRUCTURE WORKS		97	100%	100%	01-Jun-26	21-Jul-26	23-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-10
CONCRETE WORKS		87	100%	100%	20-Jun-26	21-Jul-26	25-May-26 A	27-Jun-26 A	134,099.30	134,099.30	134,099.30	21
SUB-STRUCTURE		9	100%	100%	20-Jun-26	29-Jun-26	25-May-26 A	07-Jun-26 A	53,666.80	53,666.80	53,666.80	19
MLTX-02-005-CI	Plain Concrete Under Footing	4	100%	100%	20-Jun-26	23-Jun-26	25-May-26 A	31-May-26 A	17,106.85	17,106.85	17,106.85	20
MLTX-02-005-CI	Reinforced Concrete Works for Slab on Grade Including	5	100%	100%	24-Jun-26	29-Jun-26	03-Jun-26 A	07-Jun-26 A	36,559.95	36,559.95	36,559.95	19
SUPER-STRUCTURE		87	100%	100%	06-Jul-26	21-Jul-26	20-Jun-26 A	27-Jun-26 A	80,432.50	80,432.50	80,432.50	21
MLTX-02-005-CI	AAC Panels Works for Walls	7	100%	100%	06-Jul-26	13-Jul-26	20-Jun-26 A	20-Jun-26 A	48,259.50	48,259.50	48,259.50	20
MLTX-02-005-CI	Parpet Works and Lintels	3	100%	100%	19-Jul-26	21-Jul-26	25-Jun-26 A	27-Jun-26 A	16,086.50	16,086.50	16,086.50	21
MLTX-02-005-CI	AAC Panels Works for Slabs	4	100%	100%	14-Jul-26	18-Jul-26	21-Jun-26 A	24-Jun-26 A	16,086.50	16,086.50	16,086.50	20
UNDER GROUND SEPTIC TANK		78	100%	100%	02-Jun-26	07-Jul-26	01-Jun-26 A	06-Jul-26 A	49,852.54	49,852.54	49,852.54	1
MLTX-02-005-CN-1	Plain Concrete Under Footing	3	100%	100%	02-Jun-26	04-Jun-26	01-Jun-26 A	06-Jun-26 A	17,106.85	17,106.85	17,106.85	-1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Slab Including	10	100%	100%	27-Jun-26	07-Jul-26	06-Jul-26 A	06-Jul-26 A	8,774.37	8,774.37	8,774.37	1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Foundation Including	8	100%	100%	06-Jun-26	14-Jun-26	09-Jun-26 A	13-Jun-26 A	7,604.46	7,604.46	7,604.46	1
MLTX-02-005-CN-1	Reinforced Concrete Works for Tank Walls Including Steel	10	100%	100%	15-Jun-26	25-Jun-26	18-Jun-26 A	05-Jul-26 A	16,366.86	16,366.86	16,366.86	-8
THERMAL & MOISTER PROTECTION		62	100%	100%	01-Jun-26	16-Jul-26	23-May-26 A	02-Aug-26 A	10,236.80	10,236.80	10,236.80	-14
ANTI TERMIT CONTROL		13	100%	100%	01-Jun-26	15-Jun-26	23-May-26 A	03-Jun-26 A	4,387.50	4,387.50	4,387.50	10
MLTX-02-005-CI	Anti Termite Works Under Foundation	1	100%	100%	01-Jun-26	01-Jun-26	31-May-26 A	03-Jun-26 A	1,755.00	1,755.00	1,755.00	-2
MLTX-02-005-CI	Anti Termite Works Under Slab on Grade and Grade Beams	1	100%	100%	15-Jun-26	15-Jun-26	23-May-26 A	24-May-26 A	2,632.50	2,632.50	2,632.50	16
POLYETHYLENE SHEET		13	100%	100%	01-Jun-26	15-Jun-26	24-May-26 A	04-Jun-26 A	2,193.30	2,193.30	2,193.30	9
MLTX-02-005-CI	Water Proofing Under Blinding Concrete (Polythelen Sheet)	1	100%	100%	01-Jun-26	01-Jun-26	31-May-26 A	04-Jun-26 A	877.32	877.32	877.32	-3
MLTX-02-005-CI	Water Proofing Under Slab on Grade (Polythelen Sheet)	1	100%	100%	15-Jun-26	15-Jun-26	24-May-26 A	25-May-26 A	1,315.98	1,315.98	1,315.98	15
EPOXY		15	100%	100%	08-Jul-26	16-Jul-26	11-Jul-26 A	02-Aug-26 A	3,656.00	3,656.00	3,656.00	-14
MLTX-02-005-CI	Surface Preparation for Epoxy Coating	3	100%	100%	08-Jul-26	11-Jul-26	11-Jul-26 A	11-Jul-26 A	1,096.80	1,096.80	1,096.80	0
MLTX-02-005-CI	Epoxy Coating for Walls and Slab of Tank	5	100%	100%	12-Jul-26	16-Jul-26	02-Aug-26 A	02-Aug-26 A	2,559.20	2,559.20	2,559.20	-14
MASONARY WORK		5	100%	100%	30-Jun-26	05-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-3

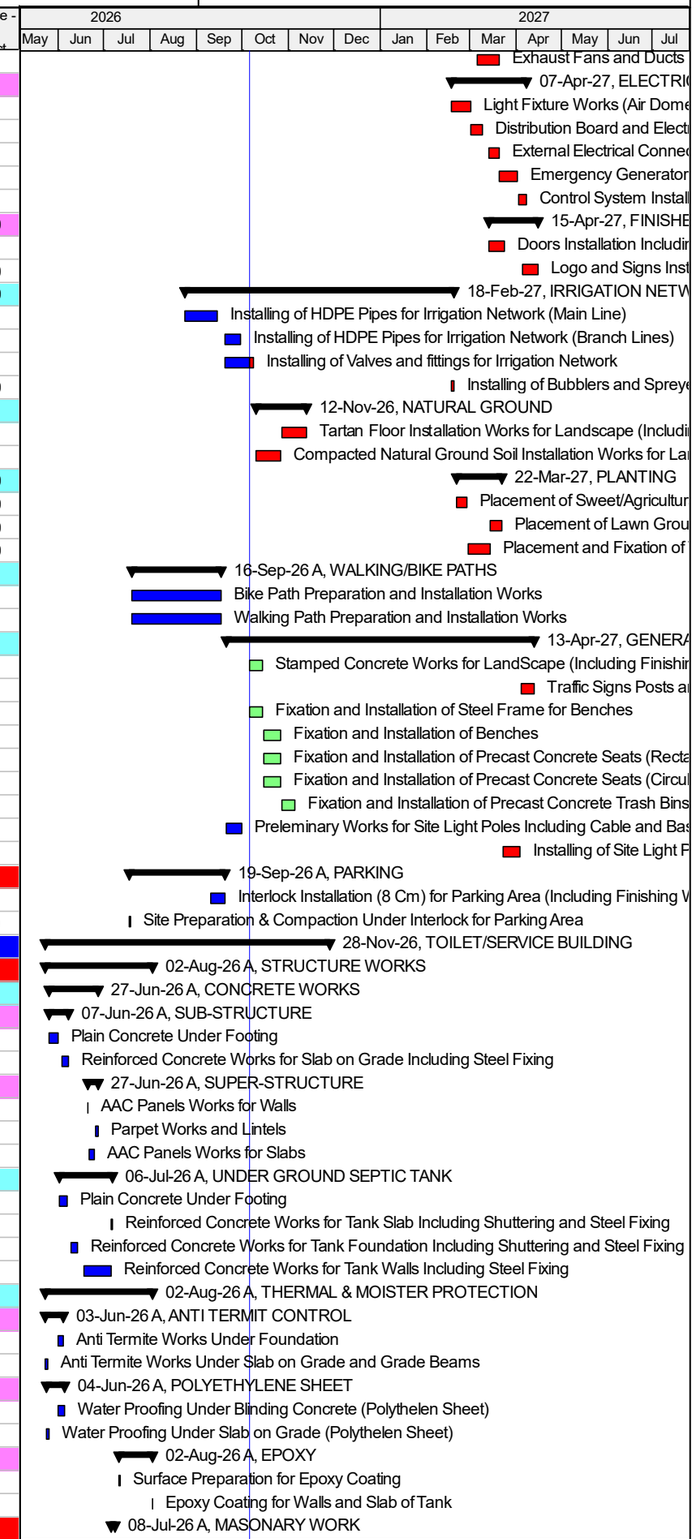

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-140	CMU Masonary Works Including all Accessories	5	100%	100%	30-Jun-26	05-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
THERMAL & MOISTER PROTECTION		23	100%	95.21%	22-Jul-26	15-Aug-26	25-Aug-26 A	14-Oct-26	34,698.32	33,037.59	34,698.32	-51
MLTX-02-005-CN-140	Preparing Surface and Preliminary Works for Toilets	2	100%	100%	22-Jul-26	23-Jul-26	25-Aug-26 A	25-Aug-26 A	2,105.86	2,105.86	2,105.86	-28
MLTX-02-005-CN-140	Finalize Water Proofing Works for Toilets	5	100%	100%	25-Jul-26	29-Jul-26	25-Aug-26 A	29-Aug-26 A	4,913.66	4,913.66	4,913.66	-26
MLTX-02-005-CN-140	Preparing Surface and Preliminary Works for Roofing and	6	100%	100%	30-Jul-26	05-Aug-26	05-Sep-26 A	05-Sep-26 A	11,071.52	11,071.52	11,071.52	-26
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	06-Aug-26	15-Aug-26	06-Sep-26 A	14-Oct-26	16,607.28	14,946.55	16,607.28	-51
MECHANICAL WORK		50	100%	83.48%	30-Jul-26	20-Sep-26	12-Jul-26 A	01-Nov-26	264,673.10	220,951.42	264,673.10	-35
HVAC SYSTEM		36	100%	100%	17-Aug-26	19-Sep-26	12-Jul-26 A	03-Oct-26 A	27,883.37	27,883.37	27,883.37	-11
MLTX-02-005-CN-1	Preliminary HVAC and Ventilation Works	3	100%	100%	17-Aug-26	19-Aug-26	12-Jul-26 A	12-Jul-26 A	9,359.69	9,359.69	9,359.69	33
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	100%	100%	16-Sep-26	19-Sep-26	03-Oct-26 A	03-Oct-26 A	14,623.96	14,623.96	14,623.96	-11
MLTX-02-005-CN-1	Exhaust, Air Ducts Installation with all Accessories	6	100%	100%	20-Aug-26	26-Aug-26	18-Aug-26 A	23-Aug-26 A	3,899.72	3,899.72	3,899.72	3
WATER SUPPLY SYSTEM		39	100%	96.64%	02-Aug-26	13-Sep-26	19-Jul-26 A	12-Oct-26	154,916.69	149,717.01	154,916.69	-24
MLTX-02-005-CN-1	Installing of PPR Pipes and Fittings for Water Network	3	100%	100%	02-Aug-26	04-Aug-26	19-Jul-26 A	22-Jul-26 A	6,921.94	6,921.94	6,921.94	11
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	12-Oct-26	25,998.40	20,798.72	25,998.40	-50
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	5	100%	100%	27-Aug-26	01-Sep-26	04-Oct-26 A	04-Oct-26 A	48,746.52	48,746.52	48,746.52	-27
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	100%	18-Aug-26	26-Aug-26	06-Sep-26 A	14-Sep-26 A	64,995.36	64,995.36	64,995.36	-16
MLTX-02-005-CN-1	Installing of Valves and Fittings	2	100%	100%	05-Aug-26	06-Aug-26	05-Sep-26 A	05-Sep-26 A	6,499.60	6,499.60	6,499.60	-25
MLTX-02-005-CN-1	Installing of Water Heater	4	100%	100%	09-Sep-26	13-Sep-26	15-Sep-26 A	15-Sep-26 A	1,754.87	1,754.87	1,754.87	-2
SEWER/DRAINAGE SYSTEM		38	100%	54.24%	30-Jul-26	13-Sep-26	20-Jul-26 A	01-Nov-26	79,923.17	43,351.04	79,923.17	-41
MLTX-02-005-CN-1	Installing UPVC Pipes for Sewage Network	2	100%	100%	30-Jul-26	01-Aug-26	20-Jul-26 A	22-Jul-26 A	11,767.40	11,767.40	11,767.40	8
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	4	100%	50%	17-Aug-26	20-Aug-26	04-Oct-26 A	10-Oct-26	10,358.68	5,179.34	10,358.68	-42
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	3	100%	100%	06-Aug-26	09-Aug-26	26-Sep-26 A	26-Sep-26 A	14,217.67	14,217.67	14,217.67	-40
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	4	100%	100%	02-Aug-26	05-Aug-26	26-Sep-26 A	26-Sep-26 A	12,186.63	12,186.63	12,186.63	-43
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	28-Oct-26	01-Nov-26	31,392.79	0.00	31,392.79	-41
FIRE PROTECTION		2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
ELECTRICAL WORKS		116	93.7%	53.29%	22-Jul-26	11-Oct-26	14-Jul-26 A	28-Nov-26	362,625.56	206,217.55	386,998.82	-41
ROUGH-IN WORKS		80	100%	100%	22-Jul-26	25-Jul-26	14-Jul-26 A	17-Aug-26 A	206,217.55	206,217.55	206,217.55	-19
MLTX-02-005-CN-1	Preleminary Works for Panel Boards	2	100%	100%	22-Jul-26	23-Jul-26	15-Jul-26 A	22-Jul-26 A	68,245.12	68,245.12	68,245.12	1
MLTX-02-005-CN-1	Preleminary Works for Cable Works	3	100%	100%	22-Jul-26	25-Jul-26	14-Jul-26 A	14-Jul-26 A	12,488.92	12,488.92	12,488.92	9
MLTX-02-005-CN-1	Preleminary Works for Sockets and Power Points	2	100%	100%	22-Jul-26	23-Jul-26	14-Jul-26 A	14-Jul-26 A	15,990.55	15,990.55	15,990.55	8
MLTX-02-005-CN-1	Preleminary Works for Lightning Works	2	100%	100%	22-Jul-26	23-Jul-26	28-Jul-26 A	17-Aug-26 A	21,935.93	21,935.93	21,935.93	-20
MLTX-02-005-CN-1	Preleminary Works for Data & Telecommunication System	2	100%	100%	22-Jul-26	23-Jul-26	28-Jul-26 A	17-Aug-26 A	24,470.75	24,470.75	24,470.75	-20
MLTX-02-005-CN-1	Preleminary Works for Security and Access Control System	3	100%	100%	22-Jul-26	25-Jul-26	28-Jul-26 A	17-Aug-26 A	30,913.59	30,913.59	30,913.59	-19
MLTX-02-005-CN-1	Preleminary Works for Earthing Works	3	100%	100%	22-Jul-26	25-Jul-26	28-Jul-26 A	17-Aug-26 A	32,172.69	32,172.69	32,172.69	-19
FIXTURE WORKS		46	86.52%	0%	16-Sep-26	11-Oct-26	06-Oct-26	28-Nov-26	156,408.01	0.00	180,781.27	-41
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	5	100%	0%	20-Sep-26	26-Sep-26	06-Oct-26	11-Oct-26	34,317.53	0.00	34,317.53	-13
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	76.19%	0%	16-Sep-26	11-Oct-26	04-Nov-26	28-Nov-26	77,994.43	0.00	102,367.69	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	3	100%	0%	19-Sep-26	21-Sep-26	20-Oct-26	22-Oct-26	7,085.10	0.00	7,085.10	-26
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	19-Sep-26	22-Sep-26	18-Oct-26	21-Oct-26	14,259.43	0.00	14,259.43	-24
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	19-Sep-26	22-Sep-26	06-Oct-26	10-Oct-26	6,239.59	0.00	6,239.59	-14
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,250.09	0.00	7,250.09	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	6,824.51	0.00	6,824.51	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	5	100%	0%	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	2,437.33	0.00	2,437.33	-41
DOORS/WINDOWS		29	100%	14.29%	22-Jul-26	20-Sep-26	17-Sep-26 A	08-Nov-26	68,245.12	9,749.30	68,245.12	-41
MLTX-02-005-CN-140	Preliminary Works For Doors	3	100%	100%	22-Jul-26	25-Jul-26	17-Sep-26 A	26-Sep-26 A	7,799.44	7,799.44	7,799.44	-53
MLTX-02-005-CN-141	Finalize Metal Doors for Toilets Building	3	100%	100%	16-Sep-26	19-Sep-26	29-Sep-26 A	29-Sep-26 A	1,949.86	1,949.86	1,949.86	-8
MLTX-02-005-CN-142	Finalize Glazzed Curtain Wall Works	4	100%	0%	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	5,849.58	0.00	5,849.58	-41
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	2	100%	0%	22-Jul-26	23-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-64
METAL WORKS		22	100%	28.57%	18-Jul-26	26-Aug-26	05-Sep-26 A	26-Oct-26	13,649.02	3,899.72	13,649.02	-51
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	4	100%	0%	18-Aug-26	22-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-51
MLTX-02-005-CN-142	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	22-Oct-26	26-Oct-26	3,899.72	0.00	3,899.72	-82
MLTX-02-005-CN-142	Installation of Galvanized Steel Roof Scupper	4	100%	100%	23-Aug-26	26-Aug-26	05-Sep-26 A	05-Sep-26 A	3,899.72	3,899.72	3,899.72	-8
FINISHING WORKS		70	100%	65.63%	30-Jul-26	17-Sep-26	17-Aug-26 A	05-Nov-26	166,130.96	109,039.34	166,130.96	-41
FLOOR FINISHES		33	100%	76.14%	05-Aug-26	17-Sep-26	01-Sep-26 A	05-Nov-26	17,159.03	13,064.27	17,159.03	-41
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	4	100%	100%	05-Aug-26	09-Aug-26	01-Sep-26 A	03-Sep-26 A	11,894.39	11,894.39	11,894.39	-22
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	10-Aug-26	13-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-48
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	2	100%	0%	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,169.94	0.00	1,169.94	-41
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	2	100%	100%	15-Aug-26	16-Aug-26	26-Sep-26 A	26-Sep-26 A	1,169.88	1,169.88	1,169.88	-34
WALL FINISHES		66	100%	60.45%	30-Jul-26	17-Sep-26	17-Aug-26 A	03-Nov-26	134,001.04	81,004.18	134,001.04	-39
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works including Plastering	3	100%	100%	30-Jul-26	02-Aug-26	17-Aug-26 A	19-Aug-26 A	18,315.62	18,315.62	18,315.62	-15
MLTX-02-005-CN-1	Preliminary Works for Wall Finish Works (External)	4	100%	100%	30-Jul-26	03-Aug-26	17-Aug-26 A	19-Aug-26 A	6,551.63	6,551.63	6,551.63	-14
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	100%	15-Aug-26	17-Aug-26	21-Sep-26 A	26-Sep-26 A	35,825.58	35,825.58	35,825.58	-33
MLTX-02-005-CN-1	Ceramic Finish Works for Walls	6	100%	100%	10-Aug-26	16-Aug-26	20-Aug-26 A	23-Aug-26 A	15,696.35	15,696.35	15,696.35	-6

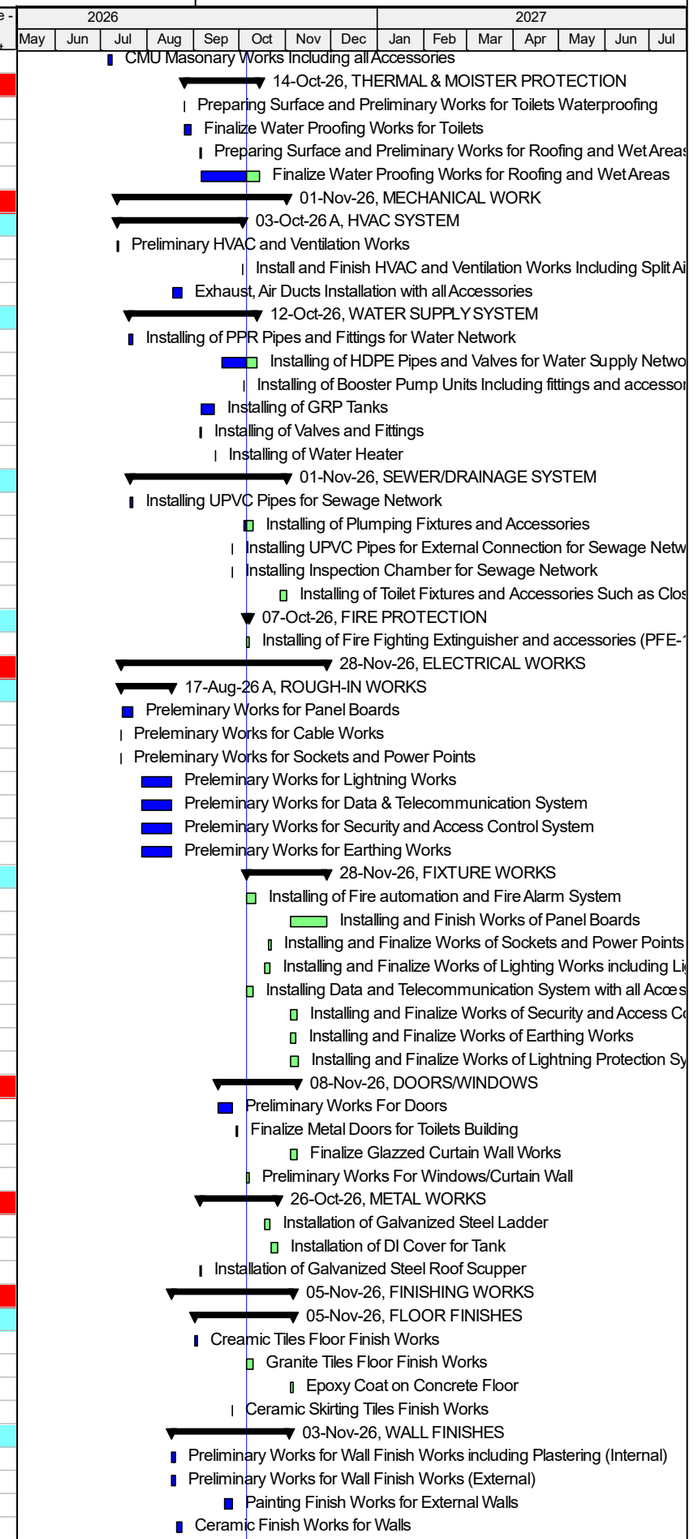

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Updateded schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	100%	0%	27-Aug-26	08-Sep-26	15-Oct-26	27-Oct-26	31,197.60	0.00	31,197.60	-41
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	100%	18-Aug-26	23-Aug-26	29-Sep-26 A	29-Sep-26 A	2,275.00	2,275.00	2,275.00	-31
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	100%	0%	09-Sep-26	15-Sep-26	28-Oct-26	03-Nov-26	13,649.02	0.00	13,649.02	-41
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	16-Aug-26	17-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-51
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	100%	16-Sep-26	17-Sep-26	19-Sep-26 A	26-Sep-26 A	2,340.00	2,340.00	2,340.00	-6
CELLING FINISHES		11	100%	100%	12-Aug-26	30-Aug-26	15-Sep-26 A	26-Sep-26 A	14,970.89	14,970.89	14,970.89	-22
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	100%	27-Aug-26	30-Aug-26	26-Sep-26 A	26-Sep-26 A	3,427.86	3,427.86	3,427.86	-22
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	6	100%	100%	20-Aug-26	26-Aug-26	16-Sep-26 A	16-Sep-26 A	5,771.52	5,771.52	5,771.52	-18
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	100%	12-Aug-26	15-Aug-26	15-Sep-26 A	15-Sep-26 A	5,771.51	5,771.51	5,771.51	-27
SPECIALTIES WORK		30	100%	0%	22-Aug-26	24-Sep-26	11-Oct-26	14-Nov-26	58,495.83	0.00	58,495.83	-43
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	0%	22-Aug-26	25-Aug-26	11-Oct-26	14-Oct-26	14,623.96	0.00	14,623.96	-42
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	5	100%	0%	19-Sep-26	24-Sep-26	09-Nov-26	14-Nov-26	19,498.61	0.00	19,498.61	-43
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	100%	0%	09-Sep-26	10-Sep-26	28-Oct-26	29-Oct-26	24,373.26	0.00	24,373.26	-41
TESTING & COMMISSIONING		49	0%	0%	15-Oct-26	29-Dec-26	20-Feb-27	21-Apr-27	0.00	0.00	0.00	-93
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	25-Nov-26	30-Nov-26	17-Apr-27	21-Apr-27	0.00	0.00	0.00	-118
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	6	0%	0%	15-Oct-26	21-Oct-26	20-Feb-27	27-Feb-27	0.00	0.00	0.00	-109
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	24-Dec-26	29-Dec-26	08-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
PROJECT CLOSEOUT & DEMOBILIZATION		18	0%	0%	24-Dec-26	02-Jan-27	08-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
As-Built DWGs		17	0%	0%	24-Dec-26	31-Dec-26	08-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
As-Built DWGs Submittals		14	0%	0%	24-Dec-26	28-Dec-26	08-Apr-27	24-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	27-Dec-26	28-Dec-26	22-Apr-27	24-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	24-Dec-26	26-Dec-26	08-Apr-27	10-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	2	0%	0%	24-Dec-26	26-Dec-26	08-Apr-27	10-Apr-27	0.00	0.00	0.00	-86
As-Built DWGs Approvals		15	0%	0%	27-Dec-26	31-Dec-26	11-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	29-Dec-26	31-Dec-26	25-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	27-Dec-26	29-Dec-26	11-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	27-Dec-26	29-Dec-26	11-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
Demobilization		4	0%	0%	30-Dec-26	02-Jan-27	25-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	30-Dec-26	30-Dec-26	25-Apr-27	25-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	30-Dec-26	30-Dec-26	25-Apr-27	25-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	26-Apr-27	26-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	28-Apr-27	28-Apr-27	0.00	0.00	0.00	-96

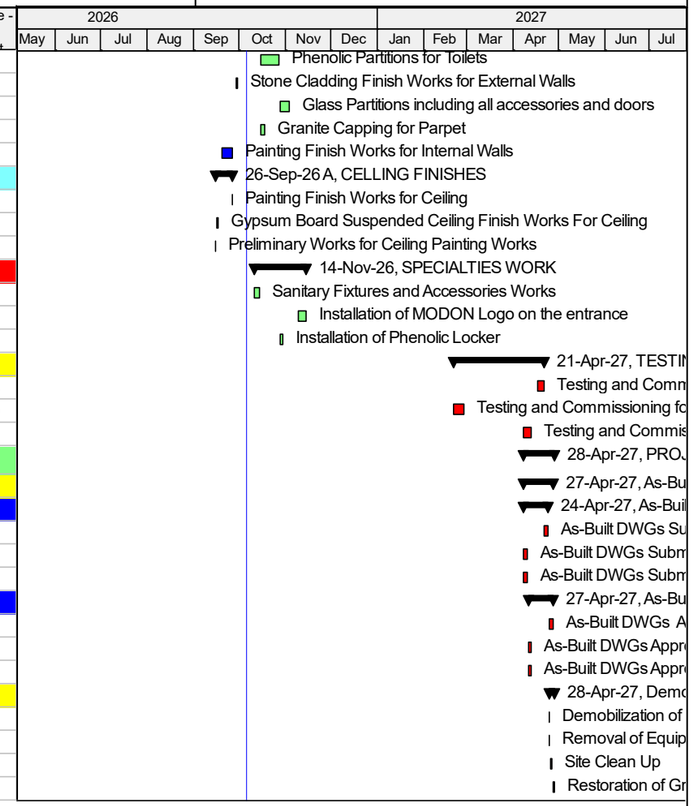

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
