
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oasis - Dammam) -R F		163	24.74%	17.95%	28-Mar-26	24-Dec-26	01-Jun-26 A	10-Nov-26	1,264,755.94	917,373.10	5,111,839.84	38
KEY MILESTONES		0	0%	0%	28-Mar-26	28-Mar-26	06-Oct-26	06-Oct-26	0.00	0.00	0.00	-160
CONTRACTUAL MILESTONE		0	0%	0%	28-Mar-26	28-Mar-26	06-Oct-26	06-Oct-26	0.00	0.00	0.00	-160
MLTX-02-005-MS-1100	Completion of Engineering	0	100%	0%		28-Mar-26		06-Oct-26	0.00	0.00	0.00	-160
ARAR		149	17.38%	14.28%	15-Apr-26	24-Dec-26	11-Jun-26 A	09-Nov-26	399,750.97	328,423.85	2,299,559.40	39
ENGINEERING		30	0%	0%	15-Apr-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
SHOP DRAWINGS		30	0%	0%	15-Apr-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
SHOP DRAWINGS SUBMISSION		30	0%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
ELECTRICAL WORKS		30	0%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EN-2580	Shop DWG Submittal for Power Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EN-2610	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
SHOP DRAWINGS APPROVALS		30	0%	0%	03-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		30	0%	0%	03-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
ARCHITECTURE WORKS		30	0%	0%	03-May-26	09-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-130
MLTX-02-005-EN-3480	Shop DWG Approval for Dome Internal Layout	30	100%	0%	03-May-26	09-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-130
AIR DOME SYSTEM		30	0%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EN-3560	Shop DWG Approval for Membrane Panel Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EN-3570	Shop DWG Approval for Cable Tension Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
ELECTRICAL WORKS		15	0%	0%	20-May-26	09-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-EN-3680	Shop DWG Approval for Lighting Layout	15	100%	0%	20-May-26	09-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-115
PROCUREMENT		29	0%	0%	19-May-26	18-Oct-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-18
SHORT LEAD ITEM		29	0%	0%	25-May-26	18-Oct-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-18
TOILET/SERVICE WORKS		29	0%	0%	09-Jun-26	04-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
LIGHTING FIXTURES		10	0%	0%	08-Jul-26	19-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8490	Material Delivery for Lighting Fixtures	10	100%	0%	08-Jul-26	19-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-76
SWITCHES/SOCKETS		12	0%	0%	08-Jul-26	21-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8510	PO for Switches/Sockets	5	100%	0%	08-Jul-26	13-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-8530	Material Delivery for Switches/Sockets	7	100%	0%	14-Jul-26	21-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
DISTRIBUTION PANNELS		20	0%	0%	09-Jun-26	01-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-8590	PO for Distribution Panels	5	100%	0%	09-Jun-26	14-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-8610	Material Delivery for Distribution Panels	15	100%	0%	15-Jun-26	01-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
FURNITURES		29	0%	0%	02-Jul-26	04-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8150	PO for Furnitures	9	100%	0%	02-Jul-26	12-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-8170	Material Delivery for Furnitures	20	100%	0%	13-Jul-26	04-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
PLAYGROUND WORKS		21	0%	0%	25-May-26	18-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-61
PVC MEMBRANE		21	0%	0%	24-Jun-26	18-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-8650	Material Delivery for PVC Membrane	21	100%	0%	24-Jun-26	18-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-88
RUBBER GRANULES		12	0%	0%	18-Jun-26	01-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-8890	Material Delivery for Rubber Granules	12	100%	0%	18-Jun-26	01-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-93
PADEL GLASS		18	0%	0%	25-May-26	17-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-8930	Material Delivery for Padel Glass	18	100%	0%	25-May-26	17-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-111
PADEL WIRE MESH/STEEL SETS		15	0%	0%	03-Jun-26	20-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-8970	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	03-Jun-26	20-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-106
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	15-Jun-26	22-Jun-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9030	Material Delivery for the Site	7	100%	0%	15-Jun-26	22-Jun-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-96
INTERLOCKING PAVING		7	0%	0%	20-Jul-26	27-Jul-26	14-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-9070	Material Delivery for Interlocking Block Pavers	7	100%	0%	20-Jul-26	27-Jul-26	14-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
MARKING PAINT		12	0%	0%	15-Jun-26	28-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9090	PO for Marking Paint	5	100%	0%	15-Jun-26	20-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9110	Material Delivery for Marking Paint	7	100%	0%	21-Jun-26	28-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
AIR DIFUSSERS/GRILLS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9170	PO for Air Difussers/Grills	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9190	Material Delivery for Air Difussers/Grills	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
GALVANIZED DUCTS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9210	PO for Galvanized Duct	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9230	Material Delivery for Galvanized Duct	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
EXHAUST FANS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9250	PO for Exhaust Fans	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9270	Material Delivery for Exhaust Fans	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
CCTV MATERIALS		5	0%	0%	20-Jul-26	25-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-9410	PO for CCTV	5	100%	0%	20-Jul-26	25-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-66
POWER OUTLETS/SWITCHES		15	0%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55

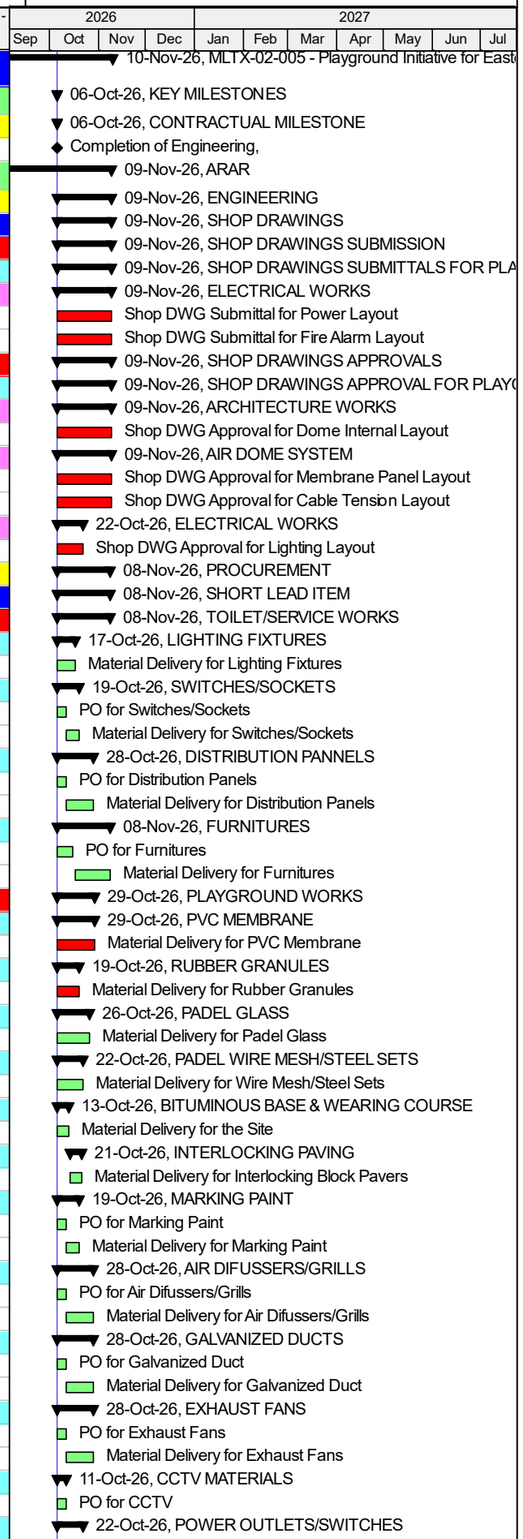

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9470	Material Delivery for Power Outlets/Switches	15	100%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
LANDSCAPE WORKS		19	0%	0%	02-Aug-26	18-Oct-26	06-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
PAVEMENT MARKING		15	0%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-9580	PO for Pavement Markings	5	100%	0%	02-Aug-26	06-Aug-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-9600	Material Delivery for Pavement Markings	10	100%	0%	08-Aug-26	18-Aug-26	12-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
TRAFFIC SIGNS		14	0%	0%	03-Oct-26	18-Oct-26	12-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-9620	PO for Traffic Signs	5	60%	0%	03-Oct-26	07-Oct-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-9640	Material Delivery for Traffic Signs	9	0%	0%	08-Oct-26	18-Oct-26	18-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
LONG LEAD ITEM		28	0%	0%	19-May-26	23-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
PLAYGROUND WORKS		28	0%	0%	19-May-26	23-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
STEEL TENSION CABLES		28	0%	0%	19-May-26	23-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8670	PO for Steel Tension Cables	8	100%	0%	19-May-26	31-May-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8680	Material Fabrication for Steel Tension Cables	20	100%	0%	01-Jun-26	23-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
CONSTRUCTION PHASE		149	17.38%	14.28%	23-Jul-26	24-Dec-26	11-Jun-26 A	28-Oct-26	399,750.97	328,423.85	2,299,559.40	49
SITE WORKS		147	3.29%	12.34%	29-Sep-26	24-Dec-26	11-Jun-26 A	28-Oct-26	64,679.66	242,486.39	1,964,488.09	49
LANDSCAPE WORKS		147	3.36%	11.54%	29-Sep-26	24-Dec-26	11-Jun-26 A	28-Oct-26	64,679.66	222,013.73	1,923,542.76	49
PLAYGROUND AREA		10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	147,733.78	54
PADEL FENCE		10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	147,733.78	54
MLTX-02-005-CN-1025	Backfilling and Reinstatement for Concrete Foundation	7	0%	0%	08-Dec-26	15-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	4,143.45	54
MLTX-02-005-CN-1026(	Tempered Glass Fenc Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	33,147.63	54
MLTX-02-005-CN-1027(	Chain Link Fence Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	16,573.82	54
MLTX-02-005-CN-1028(	Install of Fence Gates	2	0%	0%	08-Dec-26	09-Dec-26	06-Oct-26	07-Oct-26	0.00	0.00	93,868.88	54
AIR DOME		10	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	17-Oct-26	0.00	0.00	936,278.81	13
CIVIL WORKS		10	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	17-Oct-26	0.00	0.00	936,278.81	13
MLTX-02-005-CN-1036(	Install of Membrane Covering System (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	17-Oct-26	0.00	0.00	936,278.81	13
IRRIGATION NETWORK		4	0%	80%	08-Oct-26	12-Oct-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	2
MLTX-02-005-CN-11450	Installing of Valves and fittings for Irrigation Network	4	0%	80%	08-Oct-26	12-Oct-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	2
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	165,435.26	367,633.90	51
MLTX-02-005-CN-10510	Bike Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	84,399.35	187,554.12	51
MLTX-02-005-CN-10520	Walking Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	81,035.90	180,079.78	51
GENERAL/FURNITURE		22	14.43%	8.42%	29-Sep-26	24-Dec-26	03-Oct-26 A	28-Oct-26	64,679.66	37,729.80	448,335.43	49
MLTX-02-005-CN-10610	Stamped Concrete Works for LandScape (Including Finishing Works)	5	0%	0%	05-Dec-26	09-Dec-26	06-Oct-26	11-Oct-26	0.00	0.00	93,594.00	51
MLTX-02-005-CN-10630	Fixation and Installation of Steel Frame for Benches	7	0%	0%	05-Dec-26	12-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	17,274.79	51
MLTX-02-005-CN-10640	Fixation and Installation of Benches	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	40,307.84	50
MLTX-02-005-CN-10650	Fixation and Installation of Precast Concrete Seats (Rectangular)	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	32,757.76	50
MLTX-02-005-CN-10660	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	12,869.04	50
MLTX-02-005-CN-11710	Preleminary Works for Site Light Poles Including Cable and Bases Works	7	85.71%	50%	29-Sep-26	06-Oct-26	03-Oct-26 A	13-Oct-26	64,679.66	37,729.80	75,459.60	-6
MLTX-02-005-CN-11800	Installing of Site Light Poles	13	0%	0%	10-Dec-26	24-Dec-26	14-Oct-26	28-Oct-26	0.00	0.00	176,072.40	49
PARKING		3	0%	50%	14-Dec-26	16-Dec-26	03-Oct-26 A	08-Oct-26	0.00	20,472.67	40,945.33	59
MLTX-02-005-CN-10690	Interlock Installation (8 Cm) for Parking Area (Including Finishing Works)	3	0%	50%	14-Dec-26	16-Dec-26	03-Oct-26 A	08-Oct-26	0.00	20,472.67	40,945.33	59
TOILET/SERVICE BUILDING		27	100%	25.65%	23-Jul-26	09-Sep-26	28-Sep-26 A	22-Oct-26	335,071.31	85,937.46	335,071.31	-36
THERMAL & MOISTER PROTECTION		8	100%	30.87%	30-Jul-26	20-Aug-26	03-Oct-26 A	14-Oct-26	21,520.94	6,642.91	21,520.94	-46
MLTX-02-005-CN-11070	Finalize Water Proofing Works for Toilets	6	100%	0%	30-Jul-26	05-Aug-26	06-Oct-26	12-Oct-26	4,913.66	0.00	4,913.66	-57
MLTX-02-005-CN-11080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	40%	12-Aug-26	20-Aug-26	03-Oct-26 A	14-Oct-26	16,607.28	6,642.91	16,607.28	-46
MECHANICAL WORK		27	100%	47.73%	09-Aug-26	09-Sep-26	28-Sep-26 A	22-Oct-26	166,144.58	79,294.54	166,144.58	-36
WATER SUPPLY SYSTEM		27	100%	56.74%	15-Aug-26	09-Sep-26	28-Sep-26 A	22-Oct-26	139,740.28	79,294.54	139,740.28	-36
MLTX-02-005-CN-11530	Installing of HDPE Pipes and Valves for Water Supply Network	3	100%	80%	15-Aug-26	17-Aug-26	29-Sep-26 A	08-Oct-26	25,998.40	20,798.72	25,998.40	-44
MLTX-02-005-CN-11550	Installing of Booster Pump Units Including fittings and accessories	7	100%	0%	02-Sep-26	09-Sep-26	15-Oct-26	22-Oct-26	48,746.52	0.00	48,746.52	-36
MLTX-02-005-CN-11560	Installing of GRP Tanks	8	100%	90%	24-Aug-26	01-Sep-26	28-Sep-26 A	14-Oct-26	64,995.36	58,495.82	64,995.36	-36
SEWER/DRAINAGE SYSTEM		9	100%	0%	09-Aug-26	18-Aug-26	06-Oct-26	15-Oct-26	26,404.30	0.00	26,404.30	-49
MLTX-02-005-CN-11580	Installing UPVC Pipes for External Connection for Sewage Network	4	100%	0%	15-Aug-26	18-Aug-26	12-Oct-26	15-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-11850	Installing Inspection Chamber for Sewage Network	5	100%	0%	09-Aug-26	13-Aug-26	06-Oct-26	11-Oct-26	12,186.63	0.00	12,186.63	-49
DOORS/WINDOWS		3	100%	0%	28-Jul-26	30-Jul-26	06-Oct-26	08-Oct-26	60,445.68	0.00	60,445.68	-59
MLTX-02-005-CN-11100	Preliminary Works For Windows/Curtain Wall	2	100%	0%	28-Jul-26	29-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-59
MLTX-02-005-CN-11110	Preliminary Works For Doors	3	100%	0%	28-Jul-26	30-Jul-26	06-Oct-26	08-Oct-26	7,799.44	0.00	7,799.44	-59
METAL WORKS		14	100%	0%	23-Jul-26	27-Aug-26	06-Oct-26	21-Oct-26	9,749.30	0.00	9,749.30	-46
MLTX-02-005-CN-11150	Installation of Galvanized Steel Ladder	4	100%	0%	24-Aug-26	27-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-46
MLTX-02-005-CN-11160	Installation of DI Cover for Tank	4	100%	0%	23-Jul-26	27-Jul-26	06-Oct-26	10-Oct-26	3,899.72	0.00	3,899.72	-63
FINISHING WORKS		15	100%	0%	12-Aug-26	03-Sep-26	06-Oct-26	22-Oct-26	77,210.81	0.00	77,210.81	-41
FLOOR FINISHES		10	100%	0%	12-Aug-26	23-Aug-26	11-Oct-26	21-Oct-26	15,989.09	0.00	15,989.09	-50
MLTX-02-005-CN-11200	Creamic Tiles Floor Finish Works	2	100%	0%	12-Aug-26	13-Aug-26	11-Oct-26	12-Oct-26	11,894.39	0.00	11,894.39	-50
MLTX-02-005-CN-11210	Granite Tiles Floor Finish Works	4	100%	0%	15-Aug-26	18-Aug-26	13-Oct-26	17-Oct-26	2,924.82	0.00	2,924.82	-50
MLTX-02-005-CN-11230	Ceramic Skirting Tiles Finish Works	4	100%	0%	19-Aug-26	23-Aug-26	18-Oct-26	21-Oct-26	1,169.88	0.00	1,169.88	-50
WALL FINISHES		12	100%	0%	18-Aug-26	31-Aug-26	10-Oct-26	22-Oct-26	46,250.82	0.00	46,250.82	-44

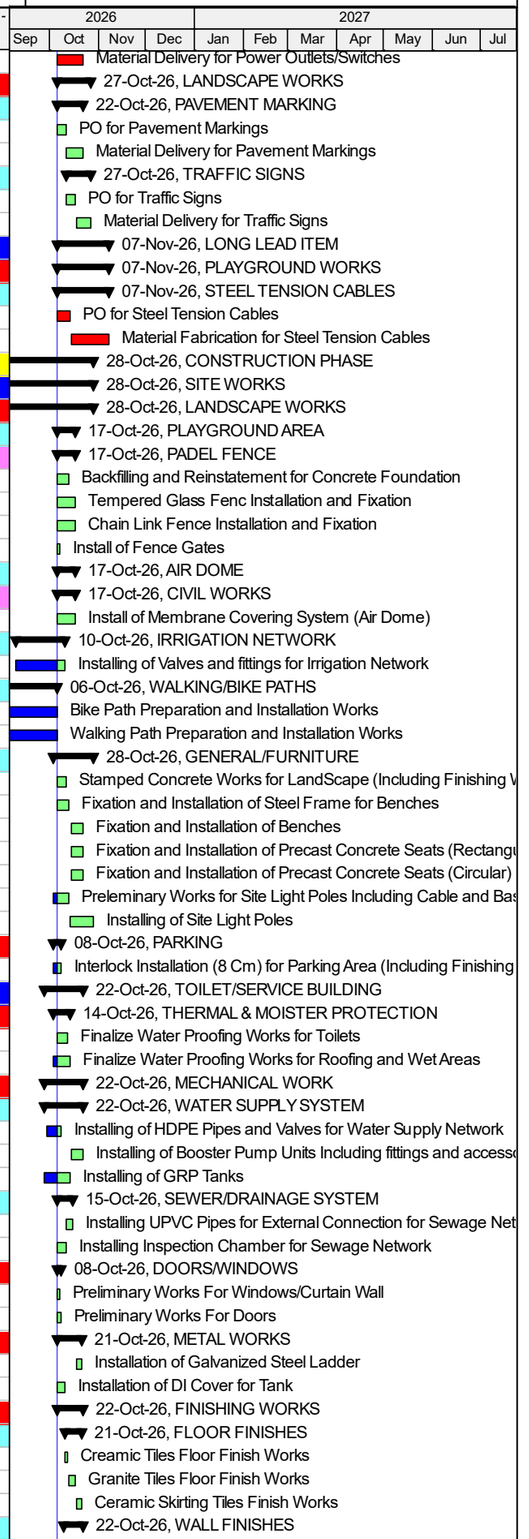

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-11250	Stone Cladding Finish Works for External Walls	5	100%	0%	26-Aug-26	31-Aug-26	18-Oct-26	22-Oct-26	2,275.00	0.00	2,275.00	-44
MLTX-02-005-CN-11270	Granite Capping for Parpet	2	100%	0%	22-Aug-26	23-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-46
MLTX-02-005-CN-11300	Painting Finish Works for External Walls	7	100%	0%	18-Aug-26	25-Aug-26	10-Oct-26	17-Oct-26	35,825.58	0.00	35,825.58	-44
CELLING FINISHES		10	100%	0%	12-Aug-26	03-Sep-26	06-Oct-26	17-Oct-26	14,970.90	0.00	14,970.90	-36
MLTX-02-005-CN-11340	Preliminary Works for Ceiling Painting Works	3	100%	0%	12-Aug-26	15-Aug-26	06-Oct-26	08-Oct-26	5,771.52	0.00	5,771.52	-46
MLTX-02-005-CN-11350	Painting Finish Works for Ceiling	3	100%	0%	01-Sep-26	03-Sep-26	14-Oct-26	17-Oct-26	3,427.86	0.00	3,427.86	-36
MLTX-02-005-CN-11360	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	24-Aug-26	31-Aug-26	06-Oct-26	13-Oct-26	5,771.52	0.00	5,771.52	-36
HASA OASIS		150	27.12%	22.99%	30-Apr-26	23-Dec-26	01-Jun-26 A	10-Nov-26	624,174.53	529,175.96	2,301,792.95	37
ENGINEERING		30	0%	0%	30-Apr-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS		30	0%	0%	30-Apr-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS SUBMISSION		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MECHANCAL WORKS		21	0%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8760	Shop DWG Submittal for HVAC Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8770	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
ELECTRICAL WORKS		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8650	Shop DWG Submittal for Lighting Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8660	Shop DWG Submittal for Power Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8670	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8680	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8690	Shop DWG Submittal for Power Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8700	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8720	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EN-8730	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
SHOP DRAWINGS APPROVALS		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN-1207(	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
PROCUREMENT		29	0%	0%	20-May-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
SHORT LEAD ITEM		29	0%	0%	25-May-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
TOILET/SERVICE WORKS		29	0%	0%	10-Jun-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
LIGHTING FIXTURES		10	0%	0%	09-Jul-26	20-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-10300	Material Delivery for Lighting Fixtures	10	100%	0%	09-Jul-26	20-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-75
SWITCHES/SOCKETS		12	0%	0%	09-Jul-26	22-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-10310	PO for Switches/Sockets	5	100%	0%	09-Jul-26	14-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-10320	Material Delivery for Switches/Sockets	7	100%	0%	15-Jul-26	22-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
DISTRIBUTION PANNELS		20	0%	0%	10-Jun-26	02-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-10130	PO for Distribution Panels	5	100%	0%	10-Jun-26	15-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-10140	Material Delivery for Distribution Panels	15	100%	0%	16-Jun-26	02-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
FURNITURES		29	0%	0%	04-Jul-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10330	PO for Furnitures	9	100%	0%	04-Jul-26	13-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10340	Material Delivery for Furnitures	20	100%	0%	14-Jul-26	05-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
PLAYGROUND WORKS		20	0%	0%	25-May-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
PVC MEMBRANE		4	0%	0%	25-May-26	01-Jun-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-10540	Material Delivery for PVC Membrane	4	100%	0%	25-May-26	01-Jun-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-111
ARTIFICIAL TURF		12	0%	0%	30-May-26	11-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-10780	Material Delivery for Artificial TURF	12	100%	0%	30-May-26	11-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-110
RUBBER GRANULES		12	0%	0%	20-Jun-26	02-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-92
MLTX-02-005-PR-10800	Material Delivery for Rubber Granules	12	100%	0%	20-Jun-26	02-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-92
PADEL GLASS		18	0%	0%	30-May-26	18-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-10820	Material Delivery for Padel Glass	18	100%	0%	30-May-26	18-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-110
PADEL WIRE MESH/STEEL SETS		15	0%	0%	04-Jun-26	21-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-10840	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	04-Jun-26	21-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-105
MARKING PAINT		12	0%	0%	16-Jun-26	29-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-10350	PO for Marking Paint	5	100%	0%	16-Jun-26	21-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-10360	Material Delivery for Marking Paint	7	100%	0%	22-Jun-26	29-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
AIR DIFUSSERS/GRILLS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10470	PO for Air Difussers/Grills	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10480	Material Delivery for Air Difussers/Grills	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
GALVANIZED DUCTS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10490	PO for Galvanized Duct	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10500	Material Delivery for Galvanized Duct	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
EXHAUST FANS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-10510	PO for Exhaust Fans	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80



Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-10520	Material Delivery for Exhaust Fans	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
CCTV MATERIALS		5	0%	0%	21-Jul-26	26-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-10690	PO for CCTV	5	100%	0%	21-Jul-26	26-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-65
LONG LEAD ITEM		28	0%	0%	20-May-26	24-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
PLAYGROUND WORKS		28	0%	0%	20-May-26	24-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
STEEL TENSION CABLES		28	0%	0%	20-May-26	24-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-10550	PO for Steel Tension Cables	8	100%	0%	20-May-26	01-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-10930	Material Fabrication for Steel Tension Cables	20	100%	0%	02-Jun-26	24-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
CONSTRUCTION PHASE		150	27.12%	22.99%	18-Jul-26	23-Dec-26	01-Jun-26 A	10-Nov-26	624,174.53	529,175.96	2,301,792.95	37
SITE WORKS		137	15.96%	22.96%	22-Sep-26	23-Dec-26	01-Jun-26 A	03-Nov-26	317,481.97	456,653.16	1,989,188.94	43
LANDSCAPE WORKS		137	15.96%	22.96%	22-Sep-26	23-Dec-26	01-Jun-26 A	03-Nov-26	317,481.97	456,653.16	1,989,188.94	43
PLAYGROUND AREA		43	51.21%	58.65%	22-Sep-26	23-Dec-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	184,664.12	47
PADEL FENCE		6	0%	0%	17-Dec-26	23-Dec-26	06-Oct-26	12-Oct-26	0.00	0.00	4,143.45	62
MLTX-02-005-CN-1224	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	17-Dec-26	23-Dec-26	06-Oct-26	12-Oct-26	0.00	0.00	4,143.45	62
CURBSTOEN/INTERLOCK		21	52.38%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	180,520.67	-11
MLTX-02-005-CN-1196(	Interlock Installation (Grey Scale) for LandScape (Including Finishing Works)	21	52.38%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	180,520.67	-11
AIR DOME		21	23.81%	0%	30-Sep-26	24-Oct-26	11-Oct-26	03-Nov-26	222,923.53	0.00	936,278.81	-9
CIVIL WORKS		21	23.81%	0%	30-Sep-26	24-Oct-26	11-Oct-26	03-Nov-26	222,923.53	0.00	936,278.81	-9
MLTX-02-005-CN-1231(	Install of Membrane Covering System (Air Dome)	21	23.81%	0%	30-Sep-26	24-Oct-26	11-Oct-26	03-Nov-26	222,923.53	0.00	936,278.81	-9
IRRIGATION NETWORK		10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	17-Oct-26	0.00	18,848.67	23,560.84	19
MLTX-02-005-CN-13210	Installing of Valves and fittings for Irrigation Network	10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	17-Oct-26	0.00	18,848.67	23,560.84	19
PLANTING		5	0%	70%	12-Oct-26	17-Oct-26	03-Oct-26 A	11-Oct-26	0.00	72,922.81	104,175.44	5
MLTX-02-005-CN-12050	Placement of Sweet/Agricultural Soil (Including Levelling and Grading)	5	0%	70%	12-Oct-26	17-Oct-26	03-Oct-26 A	11-Oct-26	0.00	72,922.81	104,175.44	5
WALKING/BIKE PATHS		8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	238,962.04	367,633.90	29
MLTX-02-005-CN-12000	Bike Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	121,910.18	187,554.12	29
MLTX-02-005-CN-12010	Walking Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	10-Jun-26 A	06-Oct-26	0.00	117,051.86	180,079.78	29
GENERAL/FURNITURE		137	0%	4.72%	09-Nov-26	01-Dec-26	01-Oct-26 A	24-Oct-26	0.00	17,607.24	372,875.83	33
MLTX-02-005-CN-11970	Stamped Concrete Works for LandScape (Including Finishing Works)	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	29
MLTX-02-005-CN-12440	Fixation and Installation of Steel Frame for Benches	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	29
MLTX-02-005-CN-12450	Fixation and Installation of Benches	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	40,307.84	29
MLTX-02-005-CN-12460	Fixation and Installation of Precast Concrete Seats (Rectangular)	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	32,757.76	29
MLTX-02-005-CN-12470	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	12,869.04	29
MLTX-02-005-CN-12930	Installing of Site Light Poles	12	0%	10%	18-Nov-26	01-Dec-26	01-Oct-26 A	19-Oct-26	0.00	17,607.24	176,072.40	37
TOILET/SERVICE BUILDING		48	98.11%	23.2%	18-Jul-26	21-Oct-26	19-Sep-26 A	10-Nov-26	306,692.55	72,522.81	312,604.01	-17
THERMAL & MOISTER PROTECTION		8	100%	70%	02-Aug-26	10-Aug-26	20-Sep-26 A	14-Oct-26	16,607.28	11,625.10	16,607.28	-55
MLTX-02-005-CN-12650	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	70%	02-Aug-26	10-Aug-26	20-Sep-26 A	14-Oct-26	16,607.28	11,625.10	16,607.28	-55
MECHANICAL WORK		44	99.78%	30.96%	09-Aug-26	07-Oct-26	19-Sep-26 A	10-Nov-26	83,731.71	25,978.06	83,917.41	-29
WATER SUPPLY SYSTEM		7	100%	80%	10-Aug-26	17-Aug-26	19-Sep-26 A	13-Oct-26	25,998.40	20,798.72	25,998.40	-48
MLTX-02-005-CN-12760	Installing of HDPE Pipes and Valves for Water Supply Network	7	100%	80%	10-Aug-26	17-Aug-26	19-Sep-26 A	13-Oct-26	25,998.40	20,798.72	25,998.40	-48
SEWER/DRAINAGE SYSTEM		31	100%	9.25%	09-Aug-26	29-Sep-26	04-Oct-26 A	10-Nov-26	55,969.14	5,179.34	55,969.14	-36
MLTX-02-005-CN-12800	Installing of Plumping Fixtures and Accessories	5	100%	50%	18-Aug-26	23-Aug-26	04-Oct-26 A	11-Oct-26	10,358.68	5,179.34	10,358.68	-41
MLTX-02-005-CN-13180	Installing UPVC Pipes for External Connection for Sewage Network	8	100%	0%	09-Aug-26	17-Aug-26	06-Oct-26	14-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-13270	Installing of Toilet Fixtures and Accessories Such as Closets and Basins	21	100%	0%	05-Sep-26	29-Sep-26	18-Oct-26	10-Nov-26	31,392.79	0.00	31,392.79	-36
FIRE PROTECTION		21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
MLTX-02-005-CN-12810	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
ELECTRICAL WORKS		29	72.07%	0%	13-Sep-26	21-Oct-26	08-Oct-26	10-Nov-26	14,773.27	0.00	20,499.02	-17
FIXTURE WORKS		29	72.07%	0%	13-Sep-26	21-Oct-26	08-Oct-26	10-Nov-26	14,773.27	0.00	20,499.02	-17
MLTX-02-005-CN-12890	Installing and Finalize Works of Lighting Works including Light Fixtures	21	90.48%	0%	13-Sep-26	07-Oct-26	18-Oct-26	10-Nov-26	12,901.39	0.00	14,259.43	-29
MLTX-02-005-CN-12910	Installing Data and Telecommunication System with all Accessories	20	30%	0%	29-Sep-26	21-Oct-26	08-Oct-26	31-Oct-26	1,871.88	0.00	6,239.59	-8
DOORS/WINDOWS		2	100%	0%	18-Jul-26	19-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-68
MLTX-02-005-CN-13120	Preliminary Works For Windows/Curtain Wall	2	100%	0%	18-Jul-26	19-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-68
METAL WORKS		4	100%	0%	13-Aug-26	17-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-55
MLTX-02-005-CN-12610	Installation of Galvanized Steel Ladder	4	100%	0%	13-Aug-26	17-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-55
FINISHING WORKS		35	100%	32.45%	06-Aug-26	12-Sep-26	27-Sep-26 A	22-Oct-26	94,087.26	30,532.46	94,087.26	-34
FLOOR FINISHES		6	100%	0%	06-Aug-26	12-Aug-26	06-Oct-26	12-Oct-26	2,924.82	0.00	2,924.82	-51
MLTX-02-005-CN-13050	Granite Tiles Floor Finish Works	6	100%	0%	06-Aug-26	12-Aug-26	06-Oct-26	12-Oct-26	2,924.82	0.00	2,924.82	-51
WALL FINISHES		34	100%	33.49%	11-Aug-26	12-Sep-26	27-Sep-26 A	22-Oct-26	91,162.44	30,532.46	91,162.44	-34
MLTX-02-005-CN-13010	Painting Finish Works for External Walls	3	100%	80%	18-Aug-26	20-Aug-26	27-Sep-26 A	08-Oct-26	35,825.58	28,660.46	35,825.58	-41
MLTX-02-005-CN-13030	Phenolic Partitions for Toilets	7	100%	0%	27-Aug-26	03-Sep-26	10-Oct-26	17-Oct-26	31,197.60	0.00	31,197.60	-36
MLTX-02-005-CN-13140	Glass Partitions including all accessories and doors	5	100%	0%	05-Sep-26	09-Sep-26	18-Oct-26	22-Oct-26	13,649.02	0.00	13,649.02	-36
MLTX-02-005-CN-13150	Granite Capping for Parpet	2	100%	0%	11-Aug-26	12-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-55
MLTX-02-005-CN-13240	Painting Finish Works for Internal Walls	2	100%	80%	10-Sep-26	12-Sep-26	29-Sep-26 A	07-Oct-26	2,340.00	1,872.00	2,340.00	-21
SPECIALTIES WORK		15	100%	11.25%	24-Aug-26	06-Sep-26	04-Oct-26 A	19-Oct-26	38,997.22	4,387.19	38,997.22	-36
MLTX-02-005-CN-12700	Sanitary Fixtures and Accessories Works	3	100%	30%	24-Aug-26	26-Aug-26	04-Oct-26 A	08-Oct-26	14,623.96	4,387.19	14,623.96	-36

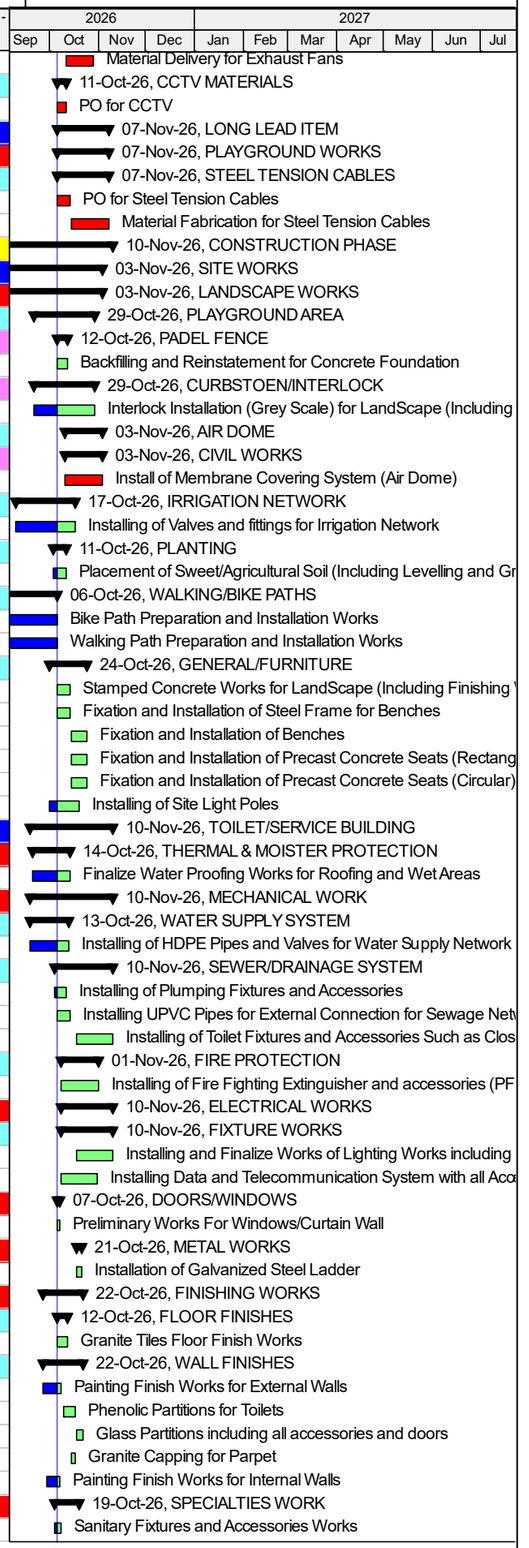

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-13160	Installation of Phenolic Locker	2	100%	0%	05-Sep-26	06-Sep-26	18-Oct-26	19-Oct-26	24,373.26	0.00	24,373.26	-36
DAMMAM		99	47.18%	11.71%	06-Apr-26	13-Dec-26	06-Sep-26 A	08-Nov-26	240,830.45	59,773.28	510,487.49	30
ENGINEERING		21	0%	0%	06-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SHOP DRAWINGS		21	0%	0%	06-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SHOP DRAWINGS SUBMISSION		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
AIR DOME SYSTEM		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1316(	Shop DWG Submittal for Cable Tension Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1317(	Shop DWG Submittal for Airlock Door Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1318(	Shop DWG Submittal for Emergency Exit Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1303(	Shop DWG Submittal for HVAC Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1304(	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
ELECTRICAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1293(	Shop DWG Submittal for Power Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1294(	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1295(	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN-1296(	Shop DWG Submittal for Power Installation Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
SHOP DRAWINGS APPROVALS		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
AIR DOME SYSTEM		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN-1627(	Shop DWG Approval for Air Dome Structural Layout	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN-1634(	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
PROCUREMENT		29	0%	0%	21-May-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
SHORT LEAD ITEM		29	0%	0%	31-May-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
TOILET/SERVICE WORKS		29	0%	0%	11-Jun-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
LIGHTING FIXTURES		10	0%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-11380	Material Delivery for Lighting Fixtures	10	100%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
SWITCHES/SOCKETS		12	0%	0%	11-Jul-26	23-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-11390	PO for Switches/Sockets	5	100%	0%	11-Jul-26	15-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-11400	Material Delivery for Switches/Sockets	7	100%	0%	16-Jul-26	23-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
DISTRIBUTION PANNELS		20	0%	0%	11-Jun-26	04-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11210	PO for Distribution Panels	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11220	Material Delivery for Distribution Panels	15	100%	0%	17-Jun-26	04-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
FURNITURES		29	0%	0%	05-Jul-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11410	PO for Furnitures	9	100%	0%	05-Jul-26	14-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11420	Material Delivery for Furnitures	20	100%	0%	15-Jul-26	06-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
PLAYGROUND WORKS		21	0%	0%	31-May-26	27-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-80
PVC MEMBRANE		21	0%	0%	06-Jun-26	29-Jun-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-11620	Material Delivery for PVC Membrane	21	100%	0%	06-Jun-26	29-Jun-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-104
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-11880	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-109
PADEL GLASS		18	0%	0%	31-May-26	20-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-11900	Material Delivery for Padel Glass	18	100%	0%	31-May-26	20-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-109
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-11920	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-104
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	11-Jun-26	24-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11080	PO for Bituminous Base & Wearing Course	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11090	Material Delivery for the Site	7	100%	0%	17-Jun-26	24-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
MARKING PAINT		12	0%	0%	17-Jun-26	30-Jun-26	12-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11430	PO for Marking Paint	5	100%	0%	17-Jun-26	22-Jun-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-11440	Material Delivery for Marking Paint	7	100%	0%	23-Jun-26	30-Jun-26	18-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
AIR DIFUSSERS/GRILLS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11550	PO for Air Difussers/Grills	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11560	Material Delivery for Air Difussers/Grills	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11570	PO for Galvanized Duct	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11580	Material Delivery for Galvanized Duct	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11590	PO for Exhaust Fans	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-11600	Material Delivery for Exhaust Fans	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
CCTV MATERIALS		5	0%	0%	22-Jul-26	27-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-11770	PO for CCTV	5	100%	0%	22-Jul-26	27-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-64

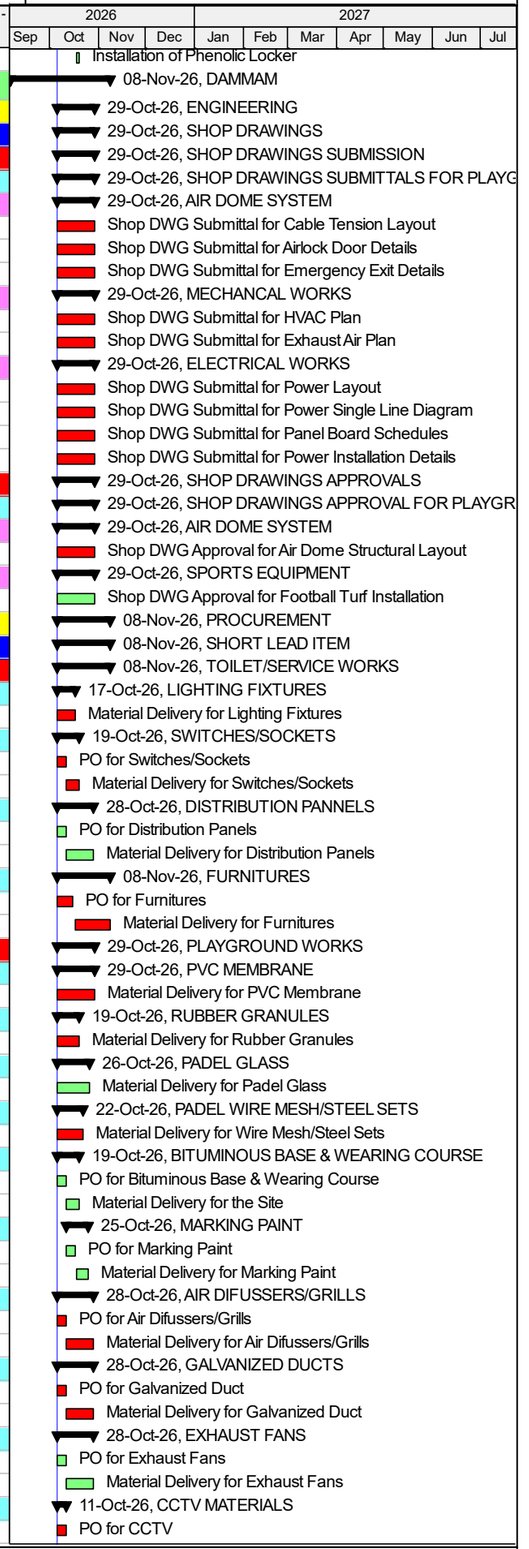

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: 2 weeks look ahead .

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

2 Weeks look ahead schedule
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
LONG LEAD ITEM		28	0%	0%	21-May-26	25-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
PLAYGROUND WORKS		28	0%	0%	21-May-26	25-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
STEEL TENSION CABLES		28	0%	0%	21-May-26	25-Jun-26	06-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-11630	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-12010	Material Fabrication for Steel Tension Cables	20	100%	0%	03-Jun-26	25-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
CONSTRUCTION PHASE		99	47.18%	11.71%	22-Jul-26	13-Dec-26	06-Sep-26 A	27-Oct-26	240,830.45	59,773.28	510,487.49	40
SITE WORKS		81	5.5%	6.61%	04-Oct-26	13-Dec-26	19-Sep-26 A	26-Oct-26	15,707.23	18,848.67	285,364.27	41
LANDSCAPE WORKS		81	5.5%	6.61%	04-Oct-26	13-Dec-26	19-Sep-26 A	26-Oct-26	15,707.23	18,848.67	285,364.27	41
IRRIGATION NETWORK		3	66.67%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	08-Oct-26	15,707.23	18,848.67	23,560.84	-2
MLTX-02-005-CN-14640	Installing of Valves and fittings for Irrigation Network	3	66.67%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	08-Oct-26	15,707.23	18,848.67	23,560.84	-2
NATURAL GROUND		15	0%	0%	07-Oct-26	24-Oct-26	10-Oct-26	26-Oct-26	0.00	0.00	65,000.00	-2
MLTX-02-005-CN-13420	Compacted Natural Ground Soil Installation Works for Landscape	15	0%	0%	07-Oct-26	24-Oct-26	10-Oct-26	26-Oct-26	0.00	0.00	65,000.00	-2
GENERAL/FURNITURE		18	0%	0%	23-Nov-26	13-Dec-26	06-Oct-26	26-Oct-26	0.00	0.00	196,803.43	41
MLTX-02-005-CN-13400	Stamped Concrete Works for LandScape (Including Finishing Works)	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	41
MLTX-02-005-CN-13870	Fixation and Installation of Steel Frame for Benches	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	41
MLTX-02-005-CN-13880	Fixation and Installation of Benches	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	40,307.84	41
MLTX-02-005-CN-13890	Fixation and Installation of Precast Concrete Seats (Rectangular)	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	32,757.76	41
MLTX-02-005-CN-13900	Fixation and Installation of Precast Concrete Seats (Circular)	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	12,869.04	41
TOILET/SERVICE BUILDING		37	100%	18.18%	22-Jul-26	26-Sep-26	06-Sep-26 A	27-Oct-26	225,123.22	40,924.61	225,123.22	-27
THERMAL & MOISTER PROTECTION		8	100%	90%	06-Aug-26	15-Aug-26	06-Sep-26 A	14-Oct-26	16,607.28	14,946.55	16,607.28	-51
MLTX-02-005-CN-14080	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	06-Aug-26	15-Aug-26	06-Sep-26 A	14-Oct-26	16,607.28	14,946.55	16,607.28	-51
MECHANICAL WORK		17	100%	67.82%	08-Aug-26	20-Sep-26	19-Sep-26 A	12-Oct-26	38,306.95	25,978.06	38,306.95	-18
WATER SUPPLY SYSTEM		6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	12-Oct-26	25,998.40	20,798.72	25,998.40	-50
MLTX-02-005-CN-14190	Installing of HDPE Pipes and Valves for Water Supply Network	6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	12-Oct-26	25,998.40	20,798.72	25,998.40	-50
SEWER/DRAINAGE SYSTEM		4	100%	50%	17-Aug-26	20-Aug-26	04-Oct-26 A	10-Oct-26	10,358.68	5,179.34	10,358.68	-42
MLTX-02-005-CN-14230	Installing of Plumping Fixtures and Accessories	4	100%	50%	17-Aug-26	20-Aug-26	04-Oct-26 A	10-Oct-26	10,358.68	5,179.34	10,358.68	-42
FIRE PROTECTION		2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
MLTX-02-005-CN-14240	Installing of Fire Fighting Extinguisher and accessories (PFE-1, PFE-2)	2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
ELECTRICAL WORKS		14	100%	0%	19-Sep-26	26-Sep-26	06-Oct-26	21-Oct-26	54,816.55	0.00	54,816.55	-22
FIXTURE WORKS		14	100%	0%	19-Sep-26	26-Sep-26	06-Oct-26	21-Oct-26	54,816.55	0.00	54,816.55	-22
MLTX-02-005-CN-14250	Installing of Fire automation and Fire Alarm System	5	100%	0%	20-Sep-26	26-Sep-26	06-Oct-26	11-Oct-26	34,317.53	0.00	34,317.53	-13
MLTX-02-005-CN-14320	Installing and Finalize Works of Lighting Works including Light Fixtures	4	100%	0%	19-Sep-26	22-Sep-26	18-Oct-26	21-Oct-26	14,259.43	0.00	14,259.43	-24
MLTX-02-005-CN-14340	Installing Data and Telecommunication System with all Accessories	4	100%	0%	19-Sep-26	22-Sep-26	06-Oct-26	10-Oct-26	6,239.59	0.00	6,239.59	-14
DOORS/WINDOWS		2	100%	0%	22-Jul-26	23-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-64
MLTX-02-005-CN-14550	Preliminary Works For Windows/Curtain Wall	2	100%	0%	22-Jul-26	23-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-64
METAL WORKS		4	100%	0%	18-Aug-26	22-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-51
MLTX-02-005-CN-14040	Installation of Galvanized Steel Ladder	4	100%	0%	18-Aug-26	22-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-51
FINISHING WORKS		19	100%	0%	10-Aug-26	08-Sep-26	06-Oct-26	27-Oct-26	42,272.66	0.00	42,272.66	-41
FLOOR FINISHES		4	100%	0%	10-Aug-26	13-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-48
MLTX-02-005-CN-14480	Granite Tiles Floor Finish Works	4	100%	0%	10-Aug-26	13-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-48
WALL FINISHES		11	100%	0%	16-Aug-26	08-Sep-26	15-Oct-26	27-Oct-26	39,347.84	0.00	39,347.84	-41
MLTX-02-005-CN-14460	Phenolic Partitions for Toilets	11	100%	0%	27-Aug-26	08-Sep-26	15-Oct-26	27-Oct-26	31,197.60	0.00	31,197.60	-41
MLTX-02-005-CN-14580	Granite Capping for Parpet	2	100%	0%	16-Aug-26	17-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-51
SPECIALTIES WORK		4	100%	0%	22-Aug-26	25-Aug-26	11-Oct-26	14-Oct-26	14,623.96	0.00	14,623.96	-42
MLTX-02-005-CN-14130	Sanitary Fixtures and Accessories Works	4	100%	0%	22-Aug-26	25-Aug-26	11-Oct-26	14-Oct-26	14,623.96	0.00	14,623.96	-42

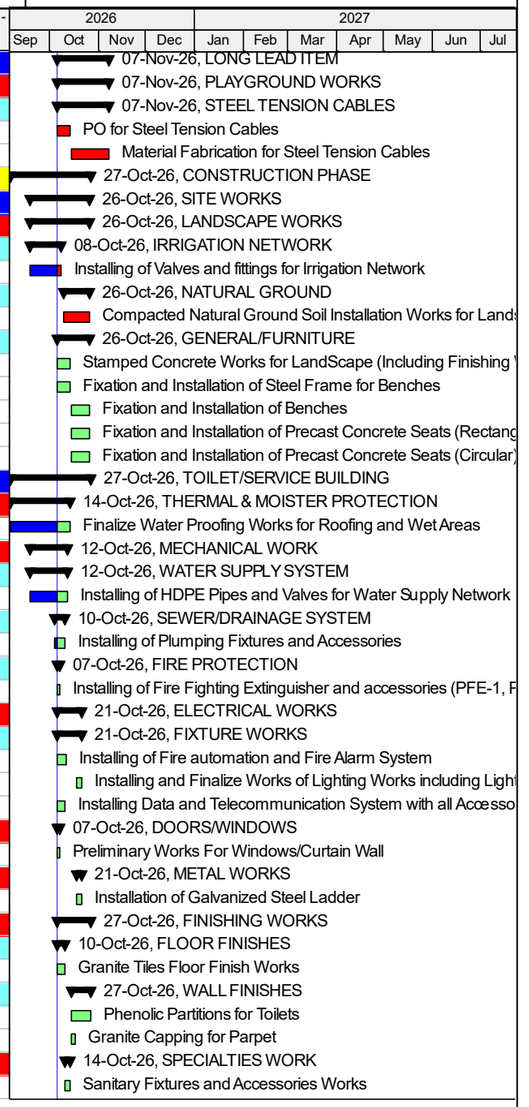

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: 2 weeks look ahead .

© Oracle Corporation
