
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005	Playground Initiative for Eastern Region (Arar - Hasa Oa	257	48.22%	35.97%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	14,463,874.66	10,791,062.05	29,997,851.67	-96
KEY MILESTONES		257	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	0.00	0.00	0.00	-96
GENERAL MILESTONES		257	0%	0%	03-Mar-26	02-Jan-27	03-Mar-26 A	28-Apr-27	0.00	0.00	0.00	-96
CONTRACTUAL MILESTONE		222	0%	0%	28-Mar-26	02-Jan-27	02-Apr-26 A	15-Apr-27	0.00	0.00	0.00	-85
ARAR		246	32.16%	32.45%	03-Mar-26	02-Jan-27	04-Mar-26 A	15-Apr-27	3,251,318.73	3,280,871.77	10,110,715.45	-85
MOBILIZATION		23	0%	0%	03-Mar-26	01-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-2
ENGINEERING		202	0%	0%	07-Mar-26	25-Oct-26	07-Mar-26 A	23-Feb-27	0.00	0.00	0.00	-103
PROCUREMENT		189	0%	0%	19-May-26	22-Nov-26	02-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-77
CONSTRUCTION PHASE		238	32.16%	32.45%	15-Apr-26	02-Jan-27	04-Apr-26 A	30-Mar-27	3,251,318.73	3,280,871.77	10,110,715.45	-71
SITE WORKS		238	23.03%	30.14%	15-Apr-26	02-Jan-27	04-Apr-26 A	30-Mar-27	2,051,955.04	2,686,155.21	8,911,351.76	-71
EARTH WORKS		81	100%	100%	15-Apr-26	11-Jun-26	04-Apr-26 A	05-Aug-26 A	1,017,621.97	1,017,621.97	1,017,621.97	-46
LANDSCAPE WORKS		207	13.2%	20.81%	13-Jun-26	02-Jan-27	17-May-26 A	30-Mar-27	1,034,333.07	1,630,512.58	7,835,236.46	-71
PLAYGROUND AREA		200	36.55%	50.77%	13-Jun-26	02-Jan-27	19-May-26 A	22-Mar-27	520,731.38	723,206.72	1,424,564.96	-64
FOOTBALL PLAYGROUND		188	35%	35%	13-Jun-26	01-Dec-26	19-May-26 A	16-Mar-27	110,897.50	110,897.50	316,849.99	-86
PADEL PLAYGROUND		195	45%	70%	06-Jul-26	01-Dec-26	19-May-26 A	16-Mar-27	105,292.80	163,788.80	233,984.00	-86
BASKETBALL PLAYGROUND		179	37.98%	70%	30-Jul-26	07-Dec-26	19-May-26 A	22-Mar-27	122,756.74	226,230.90	323,187.00	-86
PADEL FENCE		168	0%	21.52%	08-Dec-26	19-Dec-26	08-Aug-26 A	17-Oct-26	0.00	40,505.18	188,238.96	54
CURBSTOEN/INTERLOCK		65	50.17%	50.17%	15-Sep-26	02-Jan-27	15-Aug-26 A	15-Nov-26	181,784.34	181,784.34	362,305.01	41
AIR DOME		175	7.58%	11.91%	24-Aug-26	09-Dec-26	17-May-26 A	30-Mar-27	370,238.11	581,544.30	4,881,359.87	-91
CIVIL WORKS		112	18.83%	29.58%	24-Aug-26	01-Nov-26	17-May-26 A	03-Nov-26	370,238.11	581,544.30	1,966,294.68	-2
MECHANICAL WORKS		76	0%	0%	02-Nov-26	16-Nov-26	04-Nov-26	31-Jan-27	0.00	0.00	1,233,296.81	-65
ELECTRICAL WORKS		20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	1,513,591.54	-65
FINISHES WORKS		49	0%	0%	14-Nov-26	09-Dec-26	28-Jan-27	30-Mar-27	0.00	0.00	168,176.84	-91
IRRIGATION NETWORK		87	51.62%	80.44%	29-Sep-26	22-Oct-26	18-Aug-26 A	24-Feb-27	78,683.91	122,596.50	152,414.87	-106
NATURAL GROUND		81	0%	0%	13-Oct-26	22-Oct-26	22-Nov-26	24-Feb-27	0.00	0.00	191,740.00	-106
PLANTING		24	0%	0%	24-Oct-26	19-Nov-26	25-Feb-27	28-Mar-27	0.00	0.00	347,251.46	-106
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	165,435.26	367,633.90	51
GENERAL/FURNITURE		29	13.75%	8.02%	29-Sep-26	02-Jan-27	03-Oct-26 A	05-Nov-26	64,679.66	37,729.80	470,271.40	49
PARKING		155	0%	65%	10-Dec-26	16-Dec-26	16-May-26 A	08-Oct-26	0.00	38,020.67	58,493.33	59
TOILET/SERVICE BUILDING		129	100%	49.59%	06-Jun-26	26-Sep-26	21-May-26 A	07-Dec-26	1,199,363.69	594,716.57	1,199,363.69	-62
STRUCTURE WORKS		98	100%	100%	06-Jun-26	27-Jul-26	21-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-5
MASONARY WORK		5	100%	100%	06-Jul-26	11-Jul-26	13-Jul-26 A	14-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
THERMAL & MOISTER PROTECTION		15	100%	57.12%	28-Jul-26	20-Aug-26	26-Sep-26 A	14-Oct-26	34,698.32	19,820.29	34,698.32	-46
MECHANICAL WORK		63	100%	44.49%	06-Aug-26	21-Sep-26	18-Jul-26 A	19-Nov-26	264,673.10	117,742.89	264,673.10	-50
ELECTRICAL WORKS		119	100%	53.29%	28-Jul-26	26-Sep-26	19-Jul-26 A	07-Dec-26	386,998.59	206,217.32	386,998.59	-62
DOORS/WINDOWS		42	100%	0%	28-Jul-26	26-Sep-26	06-Oct-26	23-Nov-26	68,245.12	0.00	68,245.12	-50
METAL WORKS		16	100%	28.57%	23-Jul-26	01-Sep-26	16-Sep-26 A	21-Oct-26	13,649.02	3,899.72	13,649.02	-42
FINISHING WORKS		77	100%	24.42%	06-Aug-26	20-Sep-26	10-Aug-26 A	18-Nov-26	166,130.97	40,563.60	166,130.97	-50
SPECIALTIES WORK		24	100%	0%	26-Aug-26	22-Sep-26	25-Oct-26	21-Nov-26	58,495.83	0.00	58,495.83	-50
TESTING & COMMISSIONING		40	0%	0%	24-Oct-26	26-Dec-26	25-Feb-27	15-Apr-27	0.00	0.00	0.00	-91
HASA OASIS		238	55.28%	38.98%	03-Mar-26	02-Jan-27	04-Mar-26 A	06-Apr-27	5,518,703.57	3,890,949.37	9,982,829.07	-77
MOBILIZATION		24	0%	0%	03-Mar-26	02-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	-1
ENGINEERING		123	0%	0%	08-Mar-26	20-Sep-26	08-Mar-26 A	23-Nov-26	0.00	0.00	0.00	-54
PROCUREMENT		184	0%	0%	20-May-26	04-Nov-26	04-Apr-26 A	14-Feb-27	0.00	0.00	0.00	-87
CONSTRUCTION PHASE		224	55.28%	38.98%	29-Mar-26	28-Dec-26	04-Apr-26 A	21-Mar-27	5,518,703.57	3,890,949.37	9,982,829.07	-67
SITE WORKS		224	49.31%	35.71%	29-Mar-26	28-Dec-26	04-Apr-26 A	21-Mar-27	4,330,752.96	3,136,990.68	8,783,465.12	-67
EARTH WORKS		73	100%	100%	29-Mar-26	02-Jun-26	04-Apr-26 A	08-Aug-26 A	979,460.76	979,460.76	979,460.76	-56
LANDSCAPE WORKS		222	43.27%	27.1%	16-May-26	28-Dec-26	16-May-26 A	21-Mar-27	3,351,292.21	2,099,036.60	7,745,511.03	-67
PLAYGROUND AREA		218	61.37%	74.16%	16-May-26	28-Dec-26	18-May-26 A	16-Mar-27	819,147.49	989,944.11	1,334,839.53	-63
FOOTBALL PLAYGROUND		174	67.69%	85%	16-May-26	24-Oct-26	18-May-26 A	05-Dec-26	214,466.49	269,322.49	316,849.99	-36
PADEL PLAYGROUND		191	45%	70%	11-Jun-26	16-Dec-26	18-May-26 A	03-Jan-27	105,292.80	163,788.80	233,984.00	-15
BASKETBALL PLAYGROUND		167	65.83%	71.39%	05-Jul-26	14-Dec-26	18-May-26 A	16-Mar-27	223,045.41	241,875.35	338,831.45	-75
PADEL FENCE		71	0%	30%	17-Dec-26	28-Dec-26	06-Aug-26 A	07-Nov-26	0.00	24,860.73	82,869.08	44
CURBSTOEN/INTERLOCK		58	76.27%	80.07%	03-Sep-26	17-Oct-26	12-Aug-26 A	29-Oct-26	276,342.79	290,096.74	362,305.01	-11
AIR DOME		144	49.52%	11.91%	27-Jul-26	09-Dec-26	16-May-26 A	21-Mar-27	2,417,363.79	581,544.30	4,881,359.87	-83
CIVIL WORKS		81	52.32%	29.58%	30-Jul-26	24-Oct-26	16-May-26 A	24-Nov-26	1,028,703.61	581,544.30	1,966,294.68	-27
MECHANICAL WORKS		98	13.64%	0%	27-Jul-26	15-Nov-26	29-Oct-26	20-Feb-27	168,176.84	0.00	1,233,296.81	-83
ELECTRICAL WORKS		58	80.63%	0%	03-Sep-26	15-Oct-26	03-Dec-26	08-Feb-27	1,220,483.34	0.00	1,513,591.54	-99
FINISHES WORKS		68	0%	0%	17-Oct-26	09-Dec-26	28-Dec-26	21-Mar-27	0.00	0.00	168,176.84	-83
IRRIGATION NETWORK		79	25.8%	80.44%	22-Sep-26	17-Nov-26	18-Jul-26 A	17-Feb-27	39,321.33	122,596.50	152,414.87	-79
NATURAL GROUND		76	0%	0%	09-Nov-26	17-Nov-26	22-Nov-26	17-Feb-27	0.00	0.00	191,740.00	-79
PLANTING		8	0%	21%	12-Oct-26	29-Oct-26	03-Oct-26 A	24-Feb-27	0.00	72,922.81	347,251.46	-100
WALKING/BIKE PATHS		8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	238,962.04	367,633.90	29

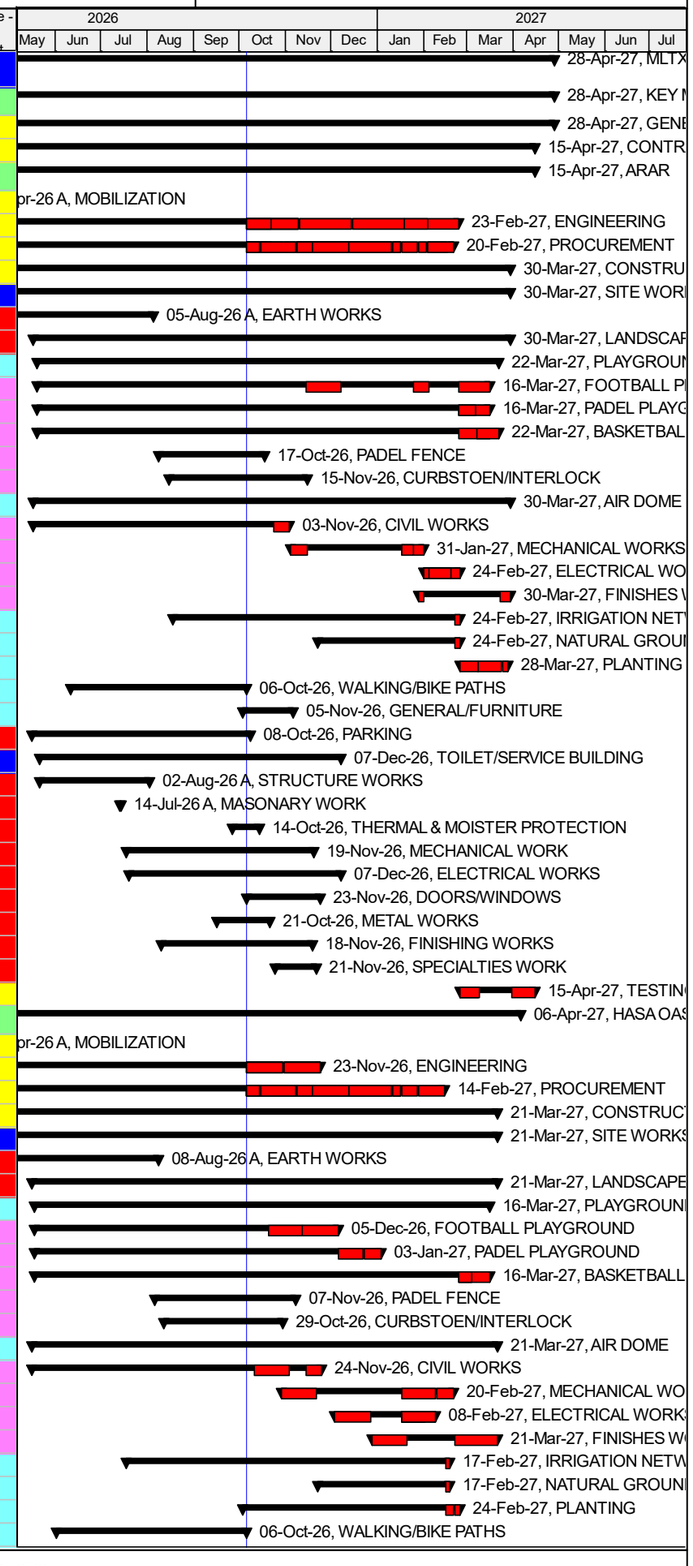

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: All Activities

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

WBS Summary
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
	GENERAL/FURNITURE	163	16.05%	19.79%	22-Sep-26	10-Dec-26	03-Sep-26 A	25-Nov-26	75,459.60	93,066.84	470,271.40	13
	PARKING	148	0%	100%	18-Nov-26	01-Dec-26	14-May-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	63
	TOILET/SERVICE BUILDING	117	99.05%	62.86%	03-Jun-26	21-Oct-26	24-May-26 A	21-Nov-26	1,187,950.61	753,958.69	1,199,363.95	-26
	STRUCTURE WORKS	78	100%	100%	03-Jun-26	16-Jul-26	24-May-26 A	10-Aug-26 A	194,188.64	194,188.64	194,188.64	-21
	MASONARY WORK	5	100%	100%	28-Jun-26	02-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-4
	THERMAL & MOISTER PROTECTION	22	100%	85.64%	18-Jul-26	10-Aug-26	10-Sep-26 A	14-Oct-26	34,698.32	29,716.14	34,698.32	-55
	MECHANICAL WORK	73	99.93%	72.58%	26-Jul-26	07-Oct-26	12-Jul-26 A	10-Nov-26	264,487.40	192,109.79	264,673.10	-29
	ELECTRICAL WORKS	89	97.1%	53.29%	18-Jul-26	21-Oct-26	14-Jul-26 A	21-Nov-26	375,771.21	206,217.58	386,998.85	-26
	DOORS/WINDOWS	39	100%	14.29%	18-Jul-26	10-Sep-26	28-Sep-26 A	24-Oct-26	68,245.12	9,749.30	68,245.12	-36
	METAL WORKS	15	100%	28.57%	18-Jul-26	22-Aug-26	06-Sep-26 A	26-Oct-26	13,649.02	3,899.72	13,649.02	-55
	FINISHING WORKS	69	100%	61.04%	26-Jul-26	13-Sep-26	17-Aug-26 A	26-Oct-26	166,130.97	101,406.23	166,130.97	-36
	SPECIALTIES WORK	26	100%	7.5%	24-Aug-26	20-Sep-26	04-Oct-26 A	16-Nov-26	58,495.83	4,387.19	58,495.83	-48
	TESTING & COMMISSIONING	109	0%	0%	18-Nov-26	02-Jan-27	26-Nov-26	06-Apr-27	0.00	0.00	0.00	-77
	DAMMAM	251	57.49%	36.54%	03-Mar-26	29-Dec-26	04-Mar-26 A	21-Apr-27	5,693,852.37	3,619,240.90	9,904,307.16	-93
	MOBILIZATION	25	0%	0%	03-Mar-26	04-Apr-26	04-Mar-26 A	04-Apr-26 A	0.00	0.00	0.00	0
	ENGINEERING	185	0%	0%	09-Mar-26	07-Jul-26	08-Mar-26 A	04-Feb-27	0.00	0.00	0.00	-181
	PROCUREMENT	189	0%	0%	21-May-26	08-Nov-26	04-Apr-26 A	20-Feb-27	0.00	0.00	0.00	-89
	CONSTRUCTION PHASE	246	57.49%	36.54%	16-Apr-26	29-Dec-26	04-Apr-26 A	15-Apr-27	5,693,852.37	3,619,240.90	9,904,307.16	-88
	SITE WORKS	246	51.91%	32.51%	16-Apr-26	29-Dec-26	04-Apr-26 A	15-Apr-27	4,518,861.71	2,829,873.24	8,704,943.25	-88
	EARTH WORKS	66	100%	100%	16-Apr-26	31-May-26	04-Apr-26 A	13-Aug-26 A	947,872.24	947,872.24	947,872.24	-63
	LANDSCAPE WORKS	229	46.39%	23.69%	23-May-26	29-Dec-26	19-May-26 A	15-Apr-27	3,570,989.48	1,823,507.67	7,698,577.68	-88
	PLAYGROUND AREA	219	73.72%	53.64%	23-May-26	08-Dec-26	19-May-26 A	04-Apr-27	972,520.36	707,562.27	1,319,195.08	-96
	FOOTBALL PLAYGROUND	211	88.81%	35%	23-May-26	11-Nov-26	19-May-26 A	25-Mar-27	281,392.97	110,897.50	316,849.99	-111
	PADEL PLAYGROUND	190	70%	70%	07-Jun-26	11-Nov-26	19-May-26 A	25-Mar-27	163,788.80	163,788.80	233,984.00	-111
	BASKETBALL PLAYGROUND	177	51.06%	70%	15-Jun-26	21-Nov-26	19-May-26 A	04-Apr-27	165,033.59	226,230.90	323,187.00	-111
	PADEL FENCE	153	0%	30%	22-Nov-26	08-Dec-26	08-Aug-26 A	12-Nov-26	0.00	24,860.73	82,869.08	22
	CURBSTOEN/INTERLOCK	68	100%	50.17%	12-Aug-26	01-Oct-26	10-Aug-26 A	07-Dec-26	362,305.01	181,784.34	362,305.01	-57
	AIR DOME	190	49.24%	11.91%	14-Jul-26	24-Nov-26	14-Jul-26 A	15-Apr-27	2,403,554.46	581,544.30	4,881,359.87	-118
	CIVIL WORKS	113	100%	29.58%	14-Jul-26	04-Oct-26	14-Jul-26 A	02-Dec-26	1,966,294.68	581,544.30	1,966,294.68	-51
	MECHANICAL WORKS	33	35.45%	0%	29-Sep-26	05-Nov-26	06-Feb-27	20-Mar-27	437,259.78	0.00	1,233,296.81	-111
	ELECTRICAL WORKS	39	0%	0%	11-Oct-26	24-Nov-26	17-Feb-27	07-Apr-27	0.00	0.00	1,513,591.54	-111
	FINISHES WORKS	29	0%	0%	31-Oct-26	22-Nov-26	14-Mar-27	15-Apr-27	0.00	0.00	168,176.84	-120
	IRRIGATION NETWORK	52	78.37%	80.44%	27-Sep-26	14-Oct-26	24-Aug-26 A	18-Feb-27	119,455.06	122,596.50	152,414.87	-109
	NATURAL GROUND	30	0%	0%	07-Oct-26	10-Nov-26	10-Oct-26	12-Nov-26	0.00	0.00	191,740.00	-2
	PLANTING	23	0%	0%	15-Oct-26	10-Nov-26	20-Feb-27	22-Mar-27	0.00	0.00	347,251.46	-109
	WALKING/BIKE PATHS	10	0%	100%	11-Nov-26	22-Nov-26	19-Jul-26 A	16-Sep-26 A	0.00	336,345.00	336,345.00	56
	GENERAL/FURNITURE	159	16.05%	16.05%	07-Sep-26	29-Dec-26	20-Sep-26 A	13-Apr-27	75,459.60	75,459.60	470,271.40	-86
	PARKING	145	0%	100%	02-Dec-26	19-Dec-26	18-Jul-26 A	19-Sep-26 A	0.00	58,493.33	58,493.33	77
	TOILET/SERVICE BUILDING	116	97.97%	65.82%	01-Jun-26	11-Oct-26	23-May-26 A	28-Nov-26	1,174,990.65	789,367.66	1,199,363.91	-41
	STRUCTURE WORKS	97	100%	100%	01-Jun-26	21-Jul-26	23-May-26 A	02-Aug-26 A	194,188.64	194,188.64	194,188.64	-10
	MASONARY WORK	5	100%	100%	30-Jun-26	05-Jul-26	06-Jul-26 A	08-Jul-26 A	12,284.10	12,284.10	12,284.10	-3
	THERMAL & MOISTER PROTECTION	23	100%	95.21%	22-Jul-26	15-Aug-26	25-Aug-26 A	14-Oct-26	34,698.32	33,037.59	34,698.32	-51
	MECHANICAL WORK	50	100%	83.48%	30-Jul-26	20-Sep-26	12-Jul-26 A	01-Nov-26	264,673.10	220,951.42	264,673.10	-35
	ELECTRICAL WORKS	116	93.7%	53.29%	22-Jul-26	11-Oct-26	14-Jul-26 A	28-Nov-26	362,625.56	206,217.55	386,998.82	-41
	DOORS/WINDOWS	29	100%	14.29%	22-Jul-26	20-Sep-26	17-Sep-26 A	08-Nov-26	68,245.12	9,749.30	68,245.12	-41
	METAL WORKS	22	100%	28.57%	18-Jul-26	26-Aug-26	05-Sep-26 A	26-Oct-26	13,649.02	3,899.72	13,649.02	-51
	FINISHING WORKS	70	100%	65.63%	30-Jul-26	17-Sep-26	17-Aug-26 A	05-Nov-26	166,130.96	109,039.34	166,130.96	-41
	SPECIALTIES WORK	30	100%	0%	22-Aug-26	24-Sep-26	11-Oct-26	14-Nov-26	58,495.83	0.00	58,495.83	-43
	TESTING & COMMISSIONING	49	0%	0%	15-Oct-26	29-Dec-26	20-Feb-27	21-Apr-27	0.00	0.00	0.00	-93
	PROJECT CLOSEOUT & DEMOBILIZATION	18	0%	0%	24-Dec-26	02-Jan-27	08-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
	As-Built DWGs	17	0%	0%	24-Dec-26	31-Dec-26	08-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
	Demobilization	4	0%	0%	30-Dec-26	02-Jan-27	25-Apr-27	28-Apr-27	0.00	0.00	0.00	-96

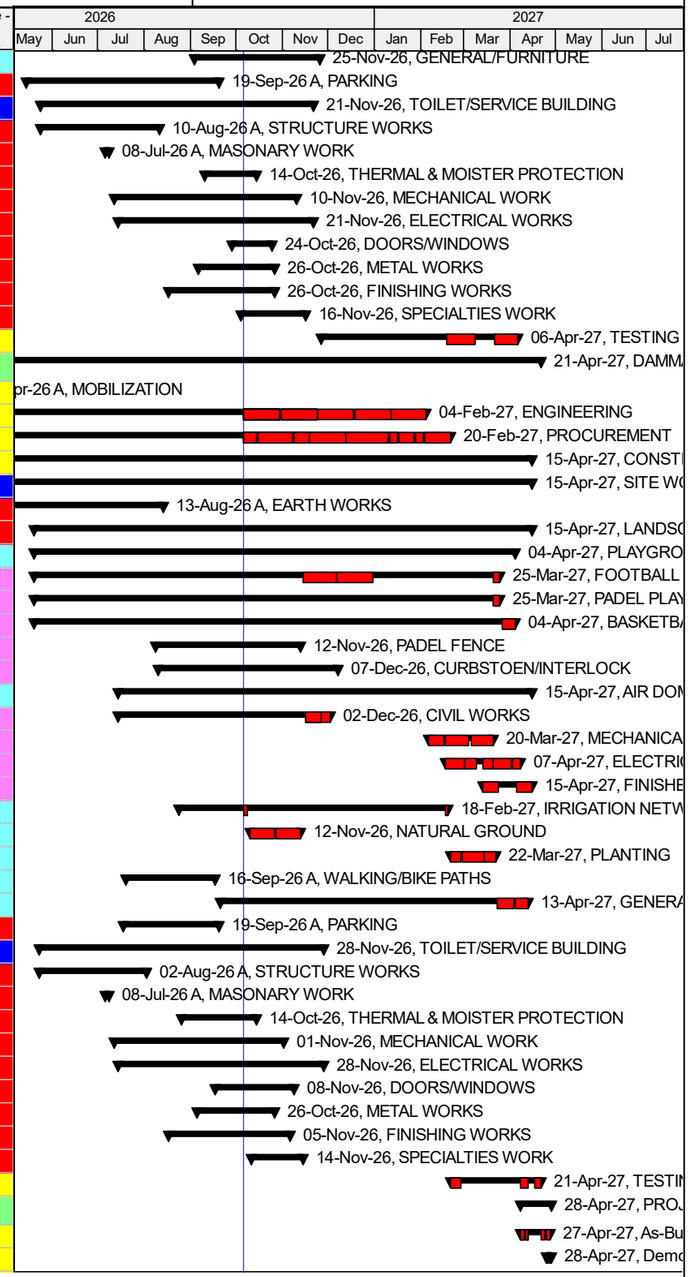

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation
