
MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005 - Playground Initiative for Eastern Region (Arar - Hasa Oa		190	29.09%	4.56%	28-Mar-26	02-Jan-27	01-Jun-26 A	28-Apr-27	5,854,965.52	917,373.10	20,124,162.72	-96
KEY MILESTONES		172	0%	0%	28-Mar-26	02-Jan-27	06-Oct-26	28-Apr-27	0.00	0.00	0.00	-96
GENERAL MILESTONES		0	0%	0%	02-Jan-27	02-Jan-27	28-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-MS-1030	Project Completion	0	0%	0%		02-Jan-27		28-Apr-27	0.00	0.00	0.00	-96
CONTRACTUAL MILESTONE		161	0%	0%	28-Mar-26	02-Jan-27	06-Oct-26	15-Apr-27	0.00	0.00	0.00	-85
MLTX-02-005-MS-1070	Completion of Testing & Commissioning	0	0%	0%		26-Dec-26		15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-MS-1100	Completion of Engineering	0	100%	0%		28-Mar-26		06-Oct-26	0.00	0.00	0.00	-160
MLTX-02-005-MS-1130	Completion of Toilet Building	0	100%	0%		26-Sep-26		23-Nov-26	0.00	0.00	0.00	-50
MLTX-02-005-MS-1140	Completion of Playground Area	0	0%	0%		02-Jan-27		25-Mar-27	0.00	0.00	0.00	-67
MLTX-02-005-MS-1150	Completion of Natural Landscape Works	0	0%	0%		19-Nov-26		28-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-MS-1160	Completion of Arar Works	0	0%	0%		04-Nov-26		09-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-MS-1170	Completion of Hasa Oasis Works	0	0%	0%		22-Dec-26		01-Nov-26	0.00	0.00	0.00	44
MLTX-02-005-MS-1180	Completion of Dammam Works	0	0%	0%		29-Dec-26		13-Apr-27	0.00	0.00	0.00	-86
ARAR		165	10.55%	4.59%	15-Apr-26	02-Jan-27	11-Jun-26 A	15-Apr-27	755,264.24	328,423.85	7,158,267.52	-85
ENGINEERING		120	0%	0%	15-Apr-26	21-Sep-26	06-Oct-26	23-Feb-27	0.00	0.00	0.00	-131
SHOP DRAWINGS		120	0%	0%	15-Apr-26	21-Sep-26	06-Oct-26	23-Feb-27	0.00	0.00	0.00	-131
SHOP DRAWINGS SUBMISSION		60	0%	0%	15-Apr-26	19-May-26	06-Oct-26	14-Dec-26	0.00	0.00	0.00	-175
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		60	0%	0%	15-Apr-26	19-May-26	06-Oct-26	14-Dec-26	0.00	0.00	0.00	-175
ELECTRICAL WORKS		60	0%	0%	15-Apr-26	19-May-26	06-Oct-26	14-Dec-26	0.00	0.00	0.00	-175
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	15-Apr-26	19-May-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-145
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	30	100%	0%	15-Apr-26	19-May-26	10-Nov-26	14-Dec-26	0.00	0.00	0.00	-175
SHOP DRAWINGS APPROVALS		120	0%	0%	03-May-26	21-Sep-26	06-Oct-26	23-Feb-27	0.00	0.00	0.00	-131
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		120	0%	0%	03-May-26	21-Sep-26	06-Oct-26	23-Feb-27	0.00	0.00	0.00	-131
ARCHITECTURE WORKS		30	0%	0%	03-May-26	09-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-130
MLTX-02-005-EM	Shop DWG Approval for Dome Internal Layout	30	100%	0%	03-May-26	09-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-130
AIR DOME SYSTEM		90	0%	0%	20-May-26	27-Jun-26	06-Oct-26	18-Jan-27	0.00	0.00	0.00	-175
MLTX-02-005-EM	Shop DWG Approval for Membrane Panel Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Cable Tension Layout	30	100%	0%	20-May-26	27-Jun-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Airlock Door Details	30	100%	0%	20-May-26	27-Jun-26	10-Nov-26	14-Dec-26	0.00	0.00	0.00	-145
MLTX-02-005-EM	Shop DWG Approval for Emergency Exit Details	30	100%	0%	20-May-26	27-Jun-26	15-Dec-26	18-Jan-27	0.00	0.00	0.00	-175
SPORTS EQUIPMENT		30	0%	0%	20-May-26	27-Jun-26	19-Jan-27	23-Feb-27	0.00	0.00	0.00	-205
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	30	100%	0%	20-May-26	27-Jun-26	19-Jan-27	23-Feb-27	0.00	0.00	0.00	-205
ELECTRICAL WORKS		104	0%	0%	20-May-26	21-Sep-26	06-Oct-26	03-Feb-27	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	15	100%	0%	20-May-26	09-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Power Layout	30	100%	0%	02-Aug-26	05-Sep-26	15-Dec-26	18-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	14	100%	0%	06-Sep-26	21-Sep-26	19-Jan-27	03-Feb-27	0.00	0.00	0.00	-115
PROCUREMENT		118	0%	0%	19-May-26	19-Oct-26	06-Oct-26	20-Feb-27	0.00	0.00	0.00	-106
SHORT LEAD ITEM		118	0%	0%	25-May-26	19-Oct-26	06-Oct-26	20-Feb-27	0.00	0.00	0.00	-106
TOILET/SERVICE WORKS		29	0%	0%	09-Jun-26	04-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
LIGHTING FIXTURES		10	0%	0%	08-Jul-26	19-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-E	Material Delivery for Lighting Fixtures	10	100%	0%	08-Jul-26	19-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-76
SWITCHES/SOCKETS		12	0%	0%	08-Jul-26	21-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-E	PO for Switches/Sockets	5	100%	0%	08-Jul-26	13-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-76
MLTX-02-005-PR-E	Material Delivery for Switches/Sockets	7	100%	0%	14-Jul-26	21-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-76
DISTRIBUTION PANNELS		20	0%	0%	09-Jun-26	01-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-E	PO for Distribution Panels	5	100%	0%	09-Jun-26	14-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-101
MLTX-02-005-PR-E	Material Delivery for Distribution Panels	15	100%	0%	15-Jun-26	01-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-101
FURNITURES		29	0%	0%	02-Jul-26	04-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-E	PO for Furnitures	9	100%	0%	02-Jul-26	12-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-E	Material Delivery for Furnitures	20	100%	0%	13-Jul-26	04-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-81
PLAYGROUND WORKS		50	0%	0%	25-May-26	12-Sep-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-69
PVC MEMBRANE		21	0%	0%	24-Jun-26	18-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-88
MLTX-02-005-PR-E	Material Delivery for PVC Membrane	21	100%	0%	24-Jun-26	18-Jul-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-88
ARTIFICIAL TURF		12	0%	0%	20-Jul-26	02-Aug-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-87
MLTX-02-005-PR-E	Material Delivery for Artificial TURF	12	100%	0%	20-Jul-26	02-Aug-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-87
RUBBER GRANULES		12	0%	0%	18-Jun-26	01-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-93
MLTX-02-005-PR-E	Material Delivery for Rubber Granules	12	100%	0%	18-Jun-26	01-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-93
PADEL GLASS		18	0%	0%	25-May-26	17-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-E	Material Delivery for Padel Glass	18	100%	0%	25-May-26	17-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-111
PADEL WIRE MESH/STEEL SETS		15	0%	0%	03-Jun-26	20-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-106
MLTX-02-005-PR-E	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	03-Jun-26	20-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-106
BITUMINOUS BASE & WEARING COURSE		7	0%	0%	15-Jun-26	22-Jun-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-96

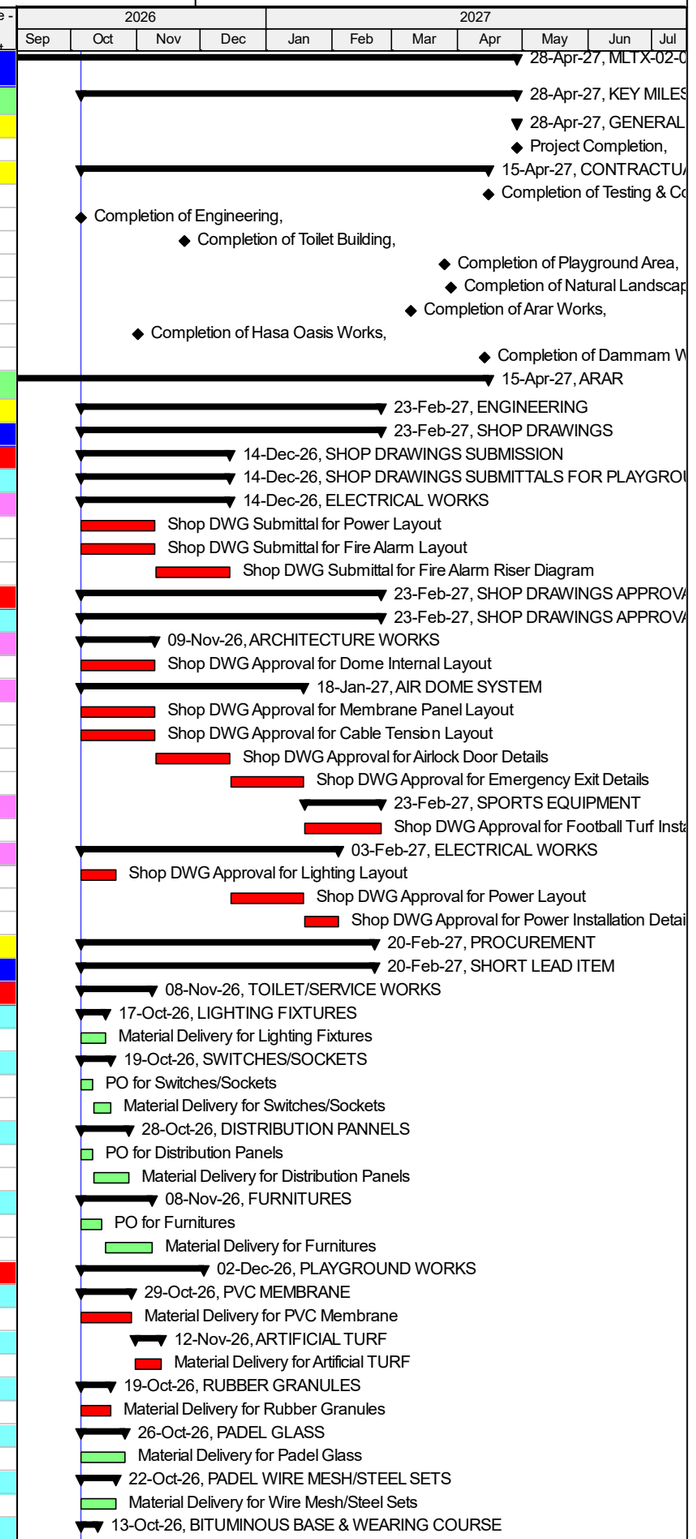

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-PR-9	Material Delivery for the Site	7	100%	0%	15-Jun-26	22-Jun-26	06-Oct-26	13-Oct-26	0.00	0.00	0.00	-96
INTERLOCKING PAVING		7	0%	0%	20-Jul-26	27-Jul-26	14-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
MLTX-02-005-PR-9	Material Delivery for Interlocking Block Pavers	7	100%	0%	20-Jul-26	27-Jul-26	14-Oct-26	21-Oct-26	0.00	0.00	0.00	-73
MARKING PAINT		12	0%	0%	15-Jun-26	28-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	PO for Marking Paint	5	100%	0%	15-Jun-26	20-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	Material Delivery for Marking Paint	7	100%	0%	21-Jun-26	28-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-96
AIR DIFUSSERS/GRILLS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	PO for Air Difussers/Grills	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	Material Delivery for Air Difussers/Grills	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
GALVANIZED DUCTS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	PO for Galvanized Duct	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	Material Delivery for Galvanized Duct	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
EXHAUST FANS		20	0%	0%	02-Jul-26	25-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	PO for Exhaust Fans	5	100%	0%	02-Jul-26	07-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-9	Material Delivery for Exhaust Fans	15	100%	0%	08-Jul-26	25-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-81
DISTRIBUTION BOARDS		20	0%	0%	02-Jul-26	25-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	PO for Distribution Boards	5	100%	0%	02-Jul-26	07-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	Material Delivery for Distribution Boards	15	100%	0%	08-Jul-26	25-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
POWER CABLES		15	0%	0%	08-Jul-26	25-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	PO for Power Cables	5	100%	0%	08-Jul-26	13-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-96
MLTX-02-005-PR-9	Material Delivery for Power Cables	10	100%	0%	14-Jul-26	25-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-96
LIGHT FIXTURES		10	0%	0%	20-Jul-26	30-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-91
MLTX-02-005-PR-9	Material Delivery for Light Fixtures	10	100%	0%	20-Jul-26	30-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-91
CCTV MATERIALS		50	0%	0%	20-Jul-26	12-Sep-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-69
MLTX-02-005-PR-9	PO for CCTV	5	100%	0%	20-Jul-26	25-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-66
MLTX-02-005-PR-9	Material Delivery for CCTV	15	100%	0%	26-Aug-26	12-Sep-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-69
POWER OUTLETS/SWITCHES		15	0%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-9	Material Delivery for Power Outlets/Switches	15	100%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
LANDSCAPE WORKS		118	0%	0%	02-Aug-26	19-Oct-26	06-Oct-26	20-Feb-27	0.00	0.00	0.00	-106
PAVEMENT MARKING		15	0%	0%	02-Aug-26	18-Aug-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-9	PO for Pavement Markings	5	100%	0%	02-Aug-26	06-Aug-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-55
MLTX-02-005-PR-9	Material Delivery for Pavement Markings	10	100%	0%	08-Aug-26	18-Aug-26	12-Oct-26	22-Oct-26	0.00	0.00	0.00	-55
TRAFFIC SIGNS		14	0%	0%	03-Oct-26	18-Oct-26	12-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-9	PO for Traffic Signs	5	60%	0%	03-Oct-26	07-Oct-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-8
MLTX-02-005-PR-9	Material Delivery for Traffic Signs	9	0%	0%	08-Oct-26	18-Oct-26	18-Oct-26	27-Oct-26	0.00	0.00	0.00	-8
AGRICULTURE SOIL		17	0%	0%	20-Sep-26	10-Oct-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-9	PO for Agriculture Soil	5	100%	0%	20-Sep-26	26-Sep-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-9	Material Delivery for Agriculture Soil	12	66.67%	0%	27-Sep-26	10-Oct-26	03-Feb-27	16-Feb-27	0.00	0.00	0.00	-111
TRACK SURFACE		10	0%	0%	08-Sep-26	19-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-111
MLTX-02-005-PR-9	Material Delivery for Track Surface	10	100%	0%	08-Sep-26	19-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-111
GRASS/TREES		15	0%	0%	03-Oct-26	19-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-106
MLTX-02-005-PR-9	Material Delivery for Grass/Trees	15	20%	0%	03-Oct-26	19-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-106
LONG LEAD ITEM		88	0%	0%	19-May-26	01-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-116
PLAYGROUND WORKS		88	0%	0%	19-May-26	01-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-116
STEEL TENSION CABLES		65	0%	0%	19-May-26	09-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-8	PO for Steel Tension Cables	8	100%	0%	19-May-26	31-May-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Fabrication for Steel Tension Cables	20	100%	0%	01-Jun-26	23-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Delivery for Steel Tension Cables	30	100%	0%	28-Jun-26	01-Aug-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-113
MLTX-02-005-PR-9	Staging time	7	100%	0%	02-Aug-26	09-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-113
EMERGENCY DOORS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	PO for Emergency Doors	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Fabrication for Emergency Doors	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Delivery for Emergency Doors	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116
PRESSURE UNITS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	PO for Pressure Units	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Fabrication for Pressure Units	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Delivery for Pressure Units	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116
AIR LOCK DOORS		60	0%	0%	24-Jun-26	01-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	PO for Lock Doors	10	100%	0%	24-Jun-26	05-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Fabrication for Lock Doors	20	100%	0%	06-Jul-26	28-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-116
MLTX-02-005-PR-8	Material Delivery for Lock Doors	25	100%	0%	29-Jul-26	26-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-116
MLTX-02-005-PR-9	Staging time	5	100%	0%	27-Aug-26	01-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-116

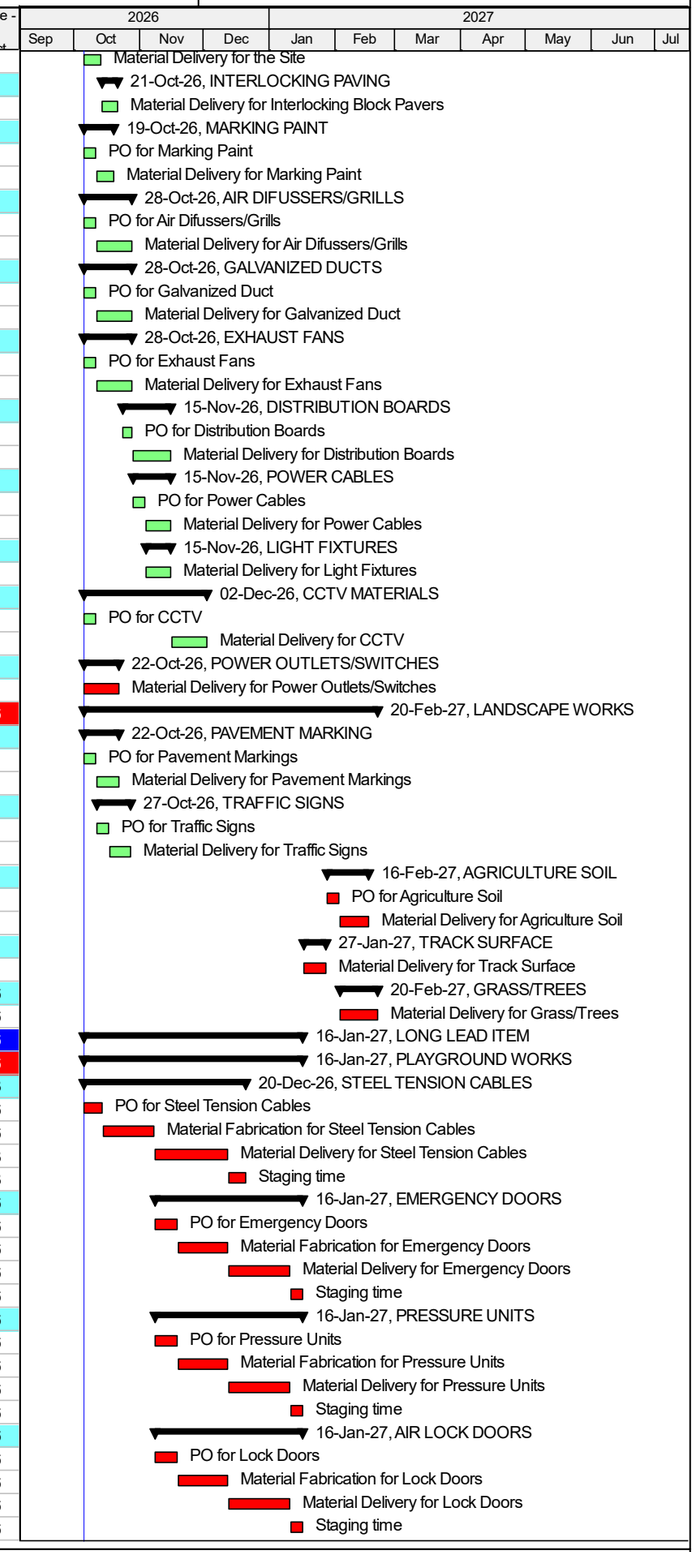

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
CONSTRUCTION PHASE		151	10.55%	4.59%	23-Jul-26	02-Jan-27	11-Jun-26 A	30-Mar-27	755,264.24	328,423.85	7,158,267.52	-71
SITE WORKS		149	1%	3.75%	29-Sep-26	02-Jan-27	11-Jun-26 A	30-Mar-27	64,679.66	242,486.39	6,467,682.94	-71
LANDSCAPE WORKS		149	1.01%	3.45%	29-Sep-26	02-Jan-27	11-Jun-26 A	30-Mar-27	64,679.66	222,013.73	6,426,737.61	-71
PLAYGROUND AREA		140	0%	0%	21-Oct-26	02-Jan-27	06-Oct-26	22-Mar-27	0.00	0.00	701,358.24	-64
FOOTBALL PLAYGROUND		102	0%	0%	21-Oct-26	01-Dec-26	14-Nov-26	16-Mar-27	0.00	0.00	205,952.49	-86
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	21	0%	0%	21-Oct-26	14-Nov-26	14-Nov-26	07-Dec-26	0.00	0.00	158,424.99	-20
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	31,685.00	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Football	10	0%	0%	15-Nov-26	25-Nov-26	25-Jan-27	04-Feb-27	0.00	0.00	15,842.50	-61
PADEL PLAYGROUND		15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	70,195.20	-86
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	58,496.00	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Padel	10	0%	0%	15-Nov-26	25-Nov-26	24-Feb-27	07-Mar-27	0.00	0.00	11,699.20	-86
BASKETBALL PLAYGROUND		20	0%	0%	15-Nov-26	07-Dec-26	24-Feb-27	22-Mar-27	0.00	0.00	96,956.10	-86
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	80,796.75	-86
MLTX-02-005-CI	Surface Marking and Painting Finishing Work (Basketball	10	0%	0%	26-Nov-26	07-Dec-26	08-Mar-27	22-Mar-27	0.00	0.00	16,159.35	-86
PADEL FENCE		10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	147,733.78	54
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	7	0%	0%	08-Dec-26	15-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	4,143.45	54
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	33,147.63	54
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	08-Dec-26	19-Dec-26	06-Oct-26	17-Oct-26	0.00	0.00	16,573.82	54
MLTX-02-005-CI	Install of Fence Gates	2	0%	0%	08-Dec-26	09-Dec-26	06-Oct-26	07-Oct-26	0.00	0.00	93,868.88	54
CURBSTOEN/INTERLOCK		20	0%	0%	10-Dec-26	02-Jan-27	24-Oct-26	15-Nov-26	0.00	0.00	180,520.67	41
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	20	0%	0%	10-Dec-26	02-Jan-27	24-Oct-26	15-Nov-26	0.00	0.00	180,520.67	41
AIR DOME		147	0%	0%	21-Oct-26	09-Dec-26	06-Oct-26	30-Mar-27	0.00	0.00	4,299,815.57	-91
CIVIL WORKS		25	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	03-Nov-26	0.00	0.00	1,384,750.38	-2
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	06-Oct-26	17-Oct-26	0.00	0.00	936,278.81	13
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	0%	0%	21-Oct-26	01-Nov-26	24-Oct-26	03-Nov-26	0.00	0.00	448,471.57	-2
MECHANICAL WORKS		76	0%	0%	02-Nov-26	16-Nov-26	04-Nov-26	31-Jan-27	0.00	0.00	1,233,296.81	-65
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	0%	0%	02-Nov-26	12-Nov-26	04-Nov-26	15-Nov-26	0.00	0.00	728,766.30	-2
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	02-Nov-26	16-Nov-26	17-Jan-27	31-Jan-27	0.00	0.00	336,353.67	-65
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	7	0%	0%	02-Nov-26	09-Nov-26	17-Jan-27	24-Jan-27	0.00	0.00	168,176.84	-65
ELECTRICAL WORKS		20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	1,513,591.54	-65
MLTX-02-005-CI	Light Fixture Works (Air Dome)	6	0%	0%	17-Nov-26	23-Nov-26	01-Feb-27	07-Feb-27	0.00	0.00	224,235.78	-65
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	10	0%	0%	17-Nov-26	28-Nov-26	01-Feb-27	11-Feb-27	0.00	0.00	168,176.84	-65
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	168,176.84	-65
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	0%	0%	17-Nov-26	09-Dec-26	01-Feb-27	24-Feb-27	0.00	0.00	504,530.51	-65
MLTX-02-005-CI	Control System Installation (Air Dome)	13	0%	0%	17-Nov-26	01-Dec-26	04-Feb-27	18-Feb-27	0.00	0.00	448,471.57	-68
FINISHES WORKS		49	0%	0%	14-Nov-26	09-Dec-26	28-Jan-27	30-Mar-27	0.00	0.00	168,176.84	-91
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	3	0%	0%	14-Nov-26	16-Nov-26	28-Jan-27	31-Jan-27	0.00	0.00	112,117.89	-65
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	7	0%	0%	02-Dec-26	09-Dec-26	23-Mar-27	30-Mar-27	0.00	0.00	56,058.95	-91
IRRIGATION NETWORK		51	0%	38.73%	08-Oct-26	22-Oct-26	10-Sep-26 A	24-Feb-27	0.00	18,848.67	48,667.04	-106
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	4	0%	80%	08-Oct-26	12-Oct-26	10-Sep-26 A	10-Oct-26	0.00	18,848.67	23,560.84	2
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	20-Oct-26	22-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	25,106.20	-106
NATURAL GROUND		81	0%	0%	13-Oct-26	22-Oct-26	22-Nov-26	24-Feb-27	0.00	0.00	191,740.00	-106
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	20-Oct-26	22-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	126,740.00	-106
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	6	0%	0%	13-Oct-26	19-Oct-26	22-Nov-26	28-Nov-26	0.00	0.00	65,000.00	-34
PLANTING		24	0%	0%	24-Oct-26	19-Nov-26	25-Feb-27	28-Mar-27	0.00	0.00	347,251.46	-106
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	10	0%	0%	24-Oct-26	03-Nov-26	25-Feb-27	08-Mar-27	0.00	0.00	104,175.44	-106
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	17-Nov-26	19-Nov-26	25-Mar-27	28-Mar-27	0.00	0.00	141,732.50	-106
MLTX-02-005-CN-1	Placement and Fixation of Trees	11	0%	0%	04-Nov-26	16-Nov-26	09-Mar-27	24-Mar-27	0.00	0.00	101,343.52	-106
WALKING/BIKE PATHS		12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	165,435.26	367,633.90	51
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	84,399.35	187,554.12	51
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	12	0%	45%	21-Nov-26	03-Dec-26	11-Jun-26 A	06-Oct-26	0.00	81,035.90	180,079.78	51
GENERAL/FURNITURE		29	13.75%	8.02%	29-Sep-26	02-Jan-27	03-Oct-26 A	05-Nov-26	64,679.66	37,729.80	470,271.40	49
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	5	0%	0%	05-Dec-26	09-Dec-26	06-Oct-26	11-Oct-26	0.00	0.00	93,594.00	51
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	26-Dec-26	02-Jan-27	29-Oct-26	05-Nov-26	0.00	0.00	9,749.30	49
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	7	0%	0%	05-Dec-26	12-Dec-26	06-Oct-26	13-Oct-26	0.00	0.00	17,274.79	51
MLTX-02-005-CN-1	Fixation and Installation of Benches	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	40,307.84	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	32,757.76	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	7	0%	0%	13-Dec-26	20-Dec-26	15-Oct-26	22-Oct-26	0.00	0.00	12,869.04	50
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	11	0%	0%	21-Dec-26	02-Jan-27	24-Oct-26	04-Nov-26	0.00	0.00	12,186.67	50
MLTX-02-005-CN-1	Preleminary Works for Site Light Poles Including Cable and	7	85.71%	50%	29-Sep-26	06-Oct-26	03-Oct-26 A	13-Oct-26	64,679.66	37,729.80	75,459.60	-6
MLTX-02-005-CN-1	Installing of Site Light Poles	13	0%	0%	10-Dec-26	24-Dec-26	14-Oct-26	28-Oct-26	0.00	0.00	176,072.40	49
PARKING		3	0%	50%	14-Dec-26	16-Dec-26	03-Oct-26 A	08-Oct-26	0.00	20,472.67	40,945.33	59
MLTX-02-005-CN-10	Interlock Installation (8 Cm) for Parking Area (Including	3	0%	50%	14-Dec-26	16-Dec-26	03-Oct-26 A	08-Oct-26	0.00	20,472.67	40,945.33	59
TOILET/SERVICE BUILDING		58	100%	12.44%	23-Jul-26	26-Sep-26	28-Sep-26 A	07-Dec-26	690,584.58	85,937.46	690,584.58	-62

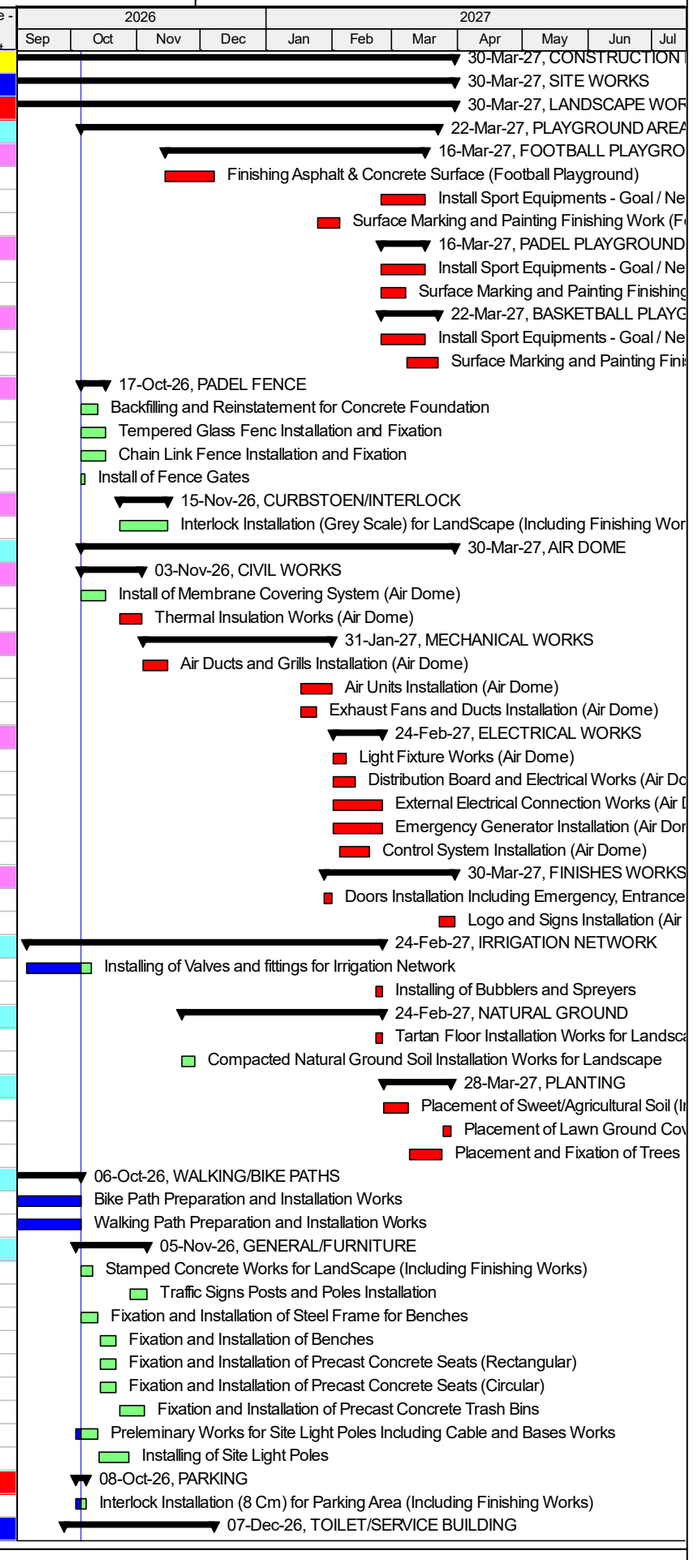

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
THERMAL & MOISTER PROTECTION		8	100%	30.87%	30-Jul-26	20-Aug-26	03-Oct-26 A	14-Oct-26	21,520.94	6,642.91	21,520.94	-46
MLTX-02-005-CN-110	Finalize Water Proofing Works for Toilets	6	100%	0%	30-Jul-26	05-Aug-26	06-Oct-26	12-Oct-26	4,913.66	0.00	4,913.66	-57
MLTX-02-005-CN-110	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	40%	12-Aug-26	20-Aug-26	03-Oct-26 A	14-Oct-26	16,607.28	6,642.91	16,607.28	-46
MECHANICAL WORK		43	100%	35.05%	09-Aug-26	21-Sep-26	28-Sep-26 A	19-Nov-26	226,224.75	79,294.54	226,224.75	-50
HVAC SYSTEM		3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	14,623.96	0.00	14,623.96	-50
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	14,623.96	0.00	14,623.96	-50
WATER SUPPLY SYSTEM		36	100%	56.04%	15-Aug-26	13-Sep-26	28-Sep-26 A	11-Nov-26	141,495.15	79,294.54	141,495.15	-50
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	3	100%	80%	15-Aug-26	17-Aug-26	29-Sep-26 A	08-Oct-26	25,998.40	20,798.72	25,998.40	-44
MLTX-02-005-CN-1	Installing of Booster Pump Units Including fittings and	7	100%	0%	02-Sep-26	09-Sep-26	15-Oct-26	22-Oct-26	48,746.52	0.00	48,746.52	-36
MLTX-02-005-CN-1	Installing of GRP Tanks	8	100%	90%	24-Aug-26	01-Sep-26	28-Sep-26 A	14-Oct-26	64,995.36	58,495.82	64,995.36	-36
MLTX-02-005-CN-1	Installing of Water Heater	4	100%	0%	09-Sep-26	13-Sep-26	08-Nov-26	11-Nov-26	1,754.87	0.00	1,754.87	-50
SEWER/DRAINAGE SYSTEM		32	100%	0%	09-Aug-26	13-Sep-26	06-Oct-26	11-Nov-26	68,155.77	0.00	68,155.77	-50
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	4	100%	0%	15-Aug-26	18-Aug-26	12-Oct-26	15-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	2	100%	0%	24-Aug-26	25-Aug-26	22-Oct-26	24-Oct-26	10,358.68	0.00	10,358.68	-50
MLTX-02-005-CN-1	Installing Inspection Chamber for Sewage Network	5	100%	0%	09-Aug-26	13-Aug-26	06-Oct-26	11-Oct-26	12,186.63	0.00	12,186.63	-49
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	08-Nov-26	11-Nov-26	31,392.79	0.00	31,392.79	-50
FIRE PROTECTION		2	100%	0%	20-Sep-26	21-Sep-26	18-Nov-26	19-Nov-26	1,949.87	0.00	1,949.87	-50
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	20-Sep-26	21-Sep-26	18-Nov-26	19-Nov-26	1,949.87	0.00	1,949.87	-50
ELECTRICAL WORKS		19	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	07-Dec-26	180,781.27	0.00	180,781.27	-62
FIXTURE WORKS		19	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	07-Dec-26	180,781.27	0.00	180,781.27	-62
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	5	100%	0%	17-Sep-26	22-Sep-26	16-Nov-26	21-Nov-26	102,367.69	0.00	102,367.69	-50
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	6,239.59	0.00	6,239.59	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	7,085.10	0.00	7,085.10	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	6,824.51	0.00	6,824.51	-50
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	4	100%	0%	21-Sep-26	26-Sep-26	19-Nov-26	23-Nov-26	34,317.53	0.00	34,317.53	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	20-Sep-26	24-Sep-26	18-Nov-26	22-Nov-26	14,259.43	0.00	14,259.43	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	6	100%	0%	17-Sep-26	24-Sep-26	16-Nov-26	22-Nov-26	2,437.33	0.00	2,437.33	-50
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	17-Sep-26	21-Sep-26	03-Dec-26	07-Dec-26	7,250.09	0.00	7,250.09	-65
DOORS/WINDOWS		42	100%	0%	28-Jul-26	26-Sep-26	06-Oct-26	23-Nov-26	68,245.12	0.00	68,245.12	-50
MLTX-02-005-CN-111	Preliminary Works For Windows/Curtain Wall	2	100%	0%	28-Jul-26	29-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-59
MLTX-02-005-CN-111	Preliminary Works For Doors	3	100%	0%	28-Jul-26	30-Jul-26	06-Oct-26	08-Oct-26	7,799.44	0.00	7,799.44	-59
MLTX-02-005-CN-111	Finalize Metal Doors for Toilets Building	7	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	23-Nov-26	1,949.86	0.00	1,949.86	-50
MLTX-02-005-CN-111	Finalize Glazzed Curtain Wall Works	7	100%	0%	17-Sep-26	26-Sep-26	16-Nov-26	23-Nov-26	5,849.58	0.00	5,849.58	-50
METAL WORKS		14	100%	0%	23-Jul-26	27-Aug-26	06-Oct-26	21-Oct-26	9,749.30	0.00	9,749.30	-46
MLTX-02-005-CN-111	Installation of Galvanized Steel Ladder	4	100%	0%	24-Aug-26	27-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-46
MLTX-02-005-CN-111	Installation of DI Cover for Tank	4	100%	0%	23-Jul-26	27-Jul-26	06-Oct-26	10-Oct-26	3,899.72	0.00	3,899.72	-63
FINISHING WORKS		38	100%	0%	12-Aug-26	20-Sep-26	06-Oct-26	18-Nov-26	125,567.37	0.00	125,567.37	-50
FLOOR FINISHES		34	100%	0%	12-Aug-26	20-Sep-26	11-Oct-26	18-Nov-26	17,159.03	0.00	17,159.03	-50
MLTX-02-005-CN-1	Creamic Tiles Floor Finish Works	2	100%	0%	12-Aug-26	13-Aug-26	11-Oct-26	12-Oct-26	11,894.39	0.00	11,894.39	-50
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	15-Aug-26	18-Aug-26	13-Oct-26	17-Oct-26	2,924.82	0.00	2,924.82	-50
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	17-Sep-26	20-Sep-26	16-Nov-26	18-Nov-26	1,169.94	0.00	1,169.94	-50
MLTX-02-005-CN-1	Ceramic Skirting Tiles Finish Works	4	100%	0%	19-Aug-26	23-Aug-26	18-Oct-26	21-Oct-26	1,169.88	0.00	1,169.88	-50
WALL FINISHES		34	100%	0%	18-Aug-26	19-Sep-26	10-Oct-26	17-Nov-26	93,437.44	0.00	93,437.44	-50
MLTX-02-005-CN-1	Stone Cladding Finish Works for External Walls	5	100%	0%	26-Aug-26	31-Aug-26	18-Oct-26	22-Oct-26	2,275.00	0.00	2,275.00	-44
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	7	100%	0%	09-Sep-26	16-Sep-26	08-Nov-26	15-Nov-26	13,649.02	0.00	13,649.02	-50
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	22-Aug-26	23-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-46
MLTX-02-005-CN-1	Painting Finish Works for External Walls	7	100%	0%	18-Aug-26	25-Aug-26	10-Oct-26	17-Oct-26	35,825.58	0.00	35,825.58	-44
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	01-Sep-26	08-Sep-26	31-Oct-26	07-Nov-26	31,197.60	0.00	31,197.60	-50
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	0%	17-Sep-26	19-Sep-26	16-Nov-26	17-Nov-26	2,340.00	0.00	2,340.00	-50
CELLING FINISHES		10	100%	0%	12-Aug-26	03-Sep-26	06-Oct-26	17-Oct-26	14,970.90	0.00	14,970.90	-36
MLTX-02-005-CN-1	Preliminary Works for Ceiling Painting Works	3	100%	0%	12-Aug-26	15-Aug-26	06-Oct-26	08-Oct-26	5,771.52	0.00	5,771.52	-46
MLTX-02-005-CN-1	Painting Finish Works for Ceiling	3	100%	0%	01-Sep-26	03-Sep-26	14-Oct-26	17-Oct-26	3,427.86	0.00	3,427.86	-36
MLTX-02-005-CN-1	Gypsum Board Suspended Ceiling Finish Works For Ceiling	7	100%	0%	24-Aug-26	31-Aug-26	06-Oct-26	13-Oct-26	5,771.52	0.00	5,771.52	-36
SPECIALTIES WORK		24	100%	0%	26-Aug-26	22-Sep-26	25-Oct-26	21-Nov-26	58,495.83	0.00	58,495.83	-50
MLTX-02-005-CN-113	Installation of Phenolic Locker	3	100%	0%	09-Sep-26	12-Sep-26	08-Nov-26	10-Nov-26	24,373.26	0.00	24,373.26	-50
MLTX-02-005-CN-113	Sanitary Fixtures and Accessories Works	5	100%	0%	26-Aug-26	31-Aug-26	25-Oct-26	29-Oct-26	14,623.96	0.00	14,623.96	-50
MLTX-02-005-CN-114	Installation of MODON Logo on the entrance	3	100%	0%	20-Sep-26	22-Sep-26	18-Nov-26	21-Nov-26	19,498.61	0.00	19,498.61	-50
TESTING & COMMISSIONING		40	0%	0%	24-Oct-26	26-Dec-26	25-Feb-27	15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-TC-11860	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	31-Mar-27	15-Apr-27	0.00	0.00	0.00	-91
MLTX-02-005-TC-11870	Testing and Commissioning for MEP Works for Toilet/Service	10	0%	0%	24-Oct-26	03-Nov-26	25-Feb-27	08-Mar-27	0.00	0.00	0.00	-106
MLTX-02-005-TC-11880	Testing and Commissioning for MEP Works for Landscape	11	0%	0%	24-Oct-26	04-Nov-26	25-Feb-27	09-Mar-27	0.00	0.00	0.00	-106
HASA OASIS		166	37.52%	7.99%	30-Apr-26	02-Jan-27	01-Jun-26 A	06-Apr-27	2,484,420.16	529,175.96	6,621,055.66	-77
ENGINEERING		42	0%	0%	30-Apr-26	20-Sep-26	06-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS		42	0%	0%	30-Apr-26	20-Sep-26	06-Oct-26	23-Nov-26	0.00	0.00	0.00	-54

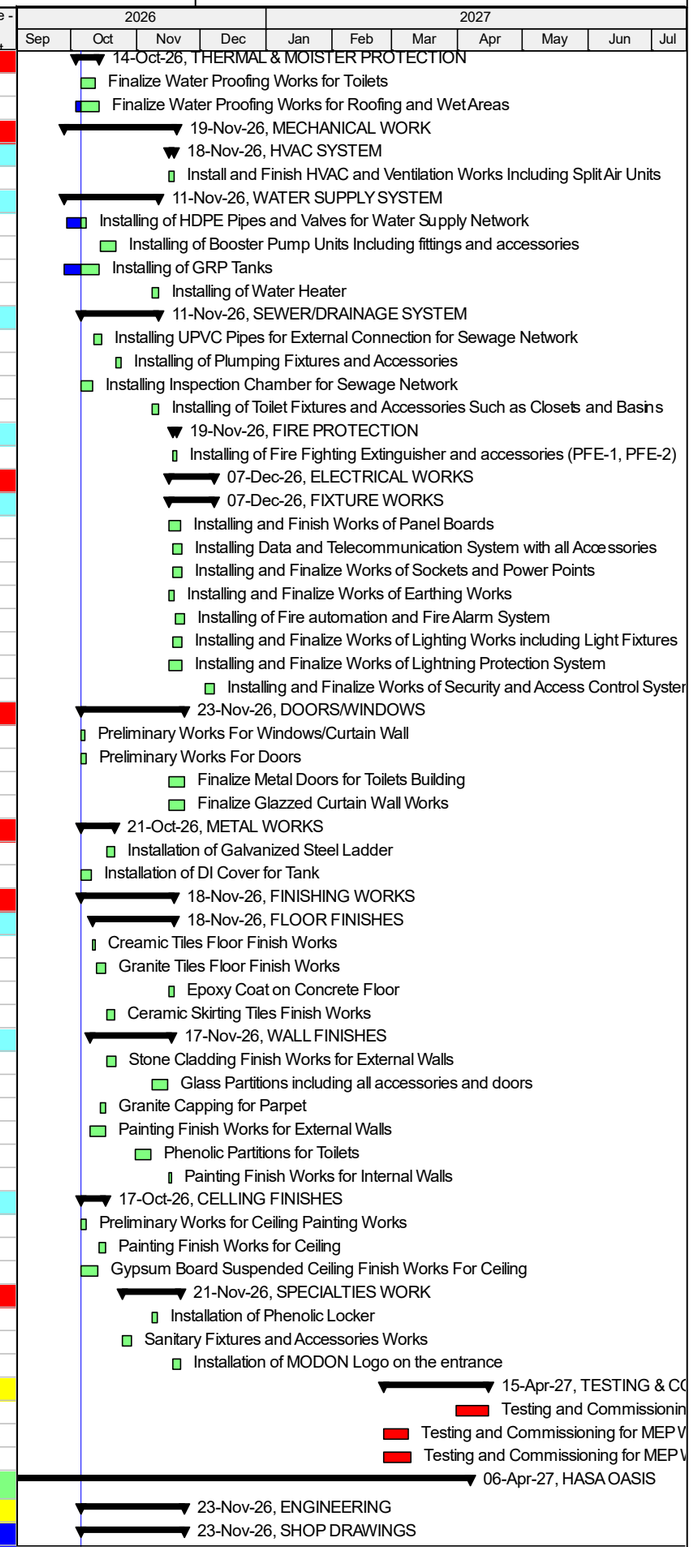

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
SHOP DRAWINGS SUBMISSION		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MECHANCAL WORKS		21	0%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for HVAC Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
ELECTRICAL WORKS		30	0%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Lighting Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Power Layout	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Power Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Installation Details	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Layout	30	100%	0%	03-Aug-26	06-Sep-26	06-Oct-26	09-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Submittal for Fire Alarm Riser Diagram	21	100%	0%	03-Aug-26	26-Aug-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-54
SHOP DRAWINGS APPROVALS		42	0%	0%	30-Apr-26	20-Sep-26	06-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		42	0%	0%	30-Apr-26	20-Sep-26	06-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EM	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MECHANCAL WORKS		21	0%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for HVAC Plan	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
ELECTRICAL WORKS		21	0%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Lighting Layout	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Power Layout	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Panel Board Schedules	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
MLTX-02-005-EM	Shop DWG Approval for Power Installation Details	21	100%	0%	27-Aug-26	20-Sep-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-54
PROCUREMENT		113	0%	0%	20-May-26	20-Oct-26	06-Oct-26	14-Feb-27	0.00	0.00	0.00	-100
SHORT LEAD ITEM		113	0%	0%	25-May-26	20-Oct-26	06-Oct-26	14-Feb-27	0.00	0.00	0.00	-100
TOILET/SERVICE WORKS		29	0%	0%	10-Jun-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
LIGHTING FIXTURES		10	0%	0%	09-Jul-26	20-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	09-Jul-26	20-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-75
SWITCHES/SOCKETS		12	0%	0%	09-Jul-26	22-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	09-Jul-26	14-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-75
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	15-Jul-26	22-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-75
DISTRIBUTION PANNELS		20	0%	0%	10-Jun-26	02-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	10-Jun-26	15-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	16-Jun-26	02-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-100
FURNITURES		29	0%	0%	04-Jul-26	05-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	04-Jul-26	13-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	14-Jul-26	05-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-80
PLAYGROUND WORKS		50	0%	0%	25-May-26	19-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-89
PVC MEMBRANE		4	0%	0%	25-May-26	01-Jun-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-111
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	4	100%	0%	25-May-26	01-Jun-26	06-Oct-26	10-Oct-26	0.00	0.00	0.00	-111
ARTIFICIAL TURF		12	0%	0%	30-May-26	11-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	30-May-26	11-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-110
RUBBER GRANULES		12	0%	0%	20-Jun-26	02-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-92
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	20-Jun-26	02-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-92
PADEL GLASS		18	0%	0%	30-May-26	18-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	30-May-26	18-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-110
PADEL WIRE MESH/STEEL SETS		15	0%	0%	04-Jun-26	21-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-105
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	04-Jun-26	21-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-105
MARKING PAINT		12	0%	0%	16-Jun-26	29-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	16-Jun-26	21-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	22-Jun-26	29-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-95
AIR DIFUSSERS/GRILLS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
GALVANIZED DUCTS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
EXHAUST FANS		20	0%	0%	04-Jul-26	26-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	04-Jul-26	08-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-80
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	09-Jul-26	26-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-80

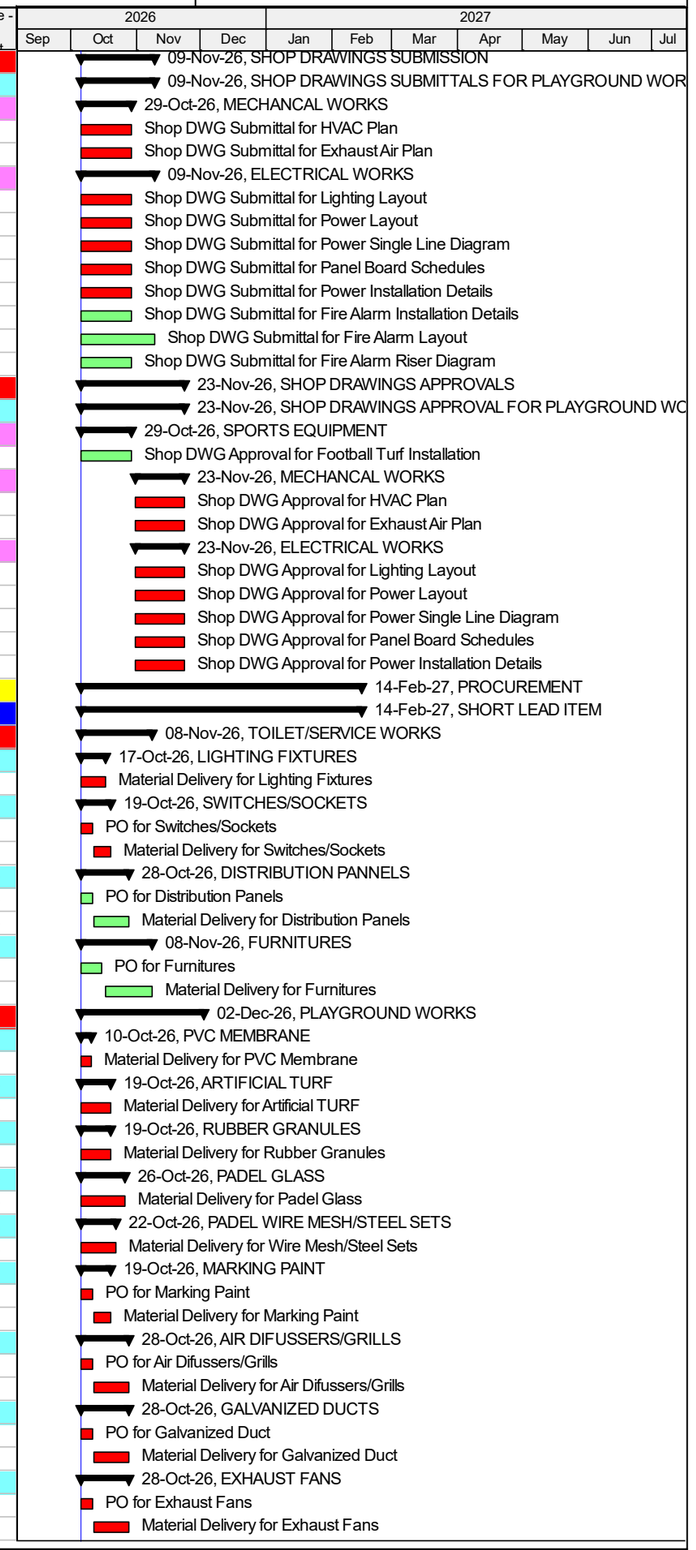

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
DISTRIBUTION BOARDS		20	0%	0%	04-Jul-26	26-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	04-Jul-26	08-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	09-Jul-26	26-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
POWER CABLES		15	0%	0%	09-Jul-26	26-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	09-Jul-26	14-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	15-Jul-26	26-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-95
LIGHT FIXTURES		10	0%	0%	21-Jul-26	01-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-90
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	21-Jul-26	01-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-90
CCTV MATERIALS		50	0%	0%	21-Jul-26	12-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-95
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	21-Jul-26	26-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-65
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	27-Jul-26	12-Aug-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-95
POWER OUTLETS/SWITCHES		21	0%	0%	27-Jul-26	19-Aug-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	27-Jul-26	02-Aug-26	20-Oct-26	26-Oct-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	03-Aug-26	19-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
LANDSCAPE WORKS		95	0%	0%	03-Aug-26	20-Oct-26	27-Oct-26	14-Feb-27	0.00	0.00	0.00	-100
PAVEMENT MARKING		15	0%	0%	03-Aug-26	19-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	03-Aug-26	08-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	09-Aug-26	19-Aug-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-72
TRAFFIC SIGNS		14	0%	0%	04-Oct-26	19-Oct-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	PO for Traffic Signs	5	40%	0%	04-Oct-26	08-Oct-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-25
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	10-Oct-26	19-Oct-26	08-Nov-26	17-Nov-26	0.00	0.00	0.00	-25
TRACK SURFACE		10	0%	0%	09-Sep-26	20-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-110
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	09-Sep-26	20-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-110
GRASS/TREES		15	0%	0%	04-Oct-26	20-Oct-26	28-Jan-27	14-Feb-27	0.00	0.00	0.00	-100
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	13.33%	0%	04-Oct-26	20-Oct-26	28-Jan-27	14-Feb-27	0.00	0.00	0.00	-100
LONG LEAD ITEM		88	0%	0%	20-May-26	02-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-115
PLAYGROUND WORKS		88	0%	0%	20-May-26	02-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-115
STEEL TENSION CABLES		65	0%	0%	20-May-26	06-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	20-May-26	01-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	25-Jun-26	29-Jul-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	02-Jun-26	24-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	7	100%	0%	30-Jul-26	06-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-115
EMERGENCY DOORS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
PRESSURE UNITS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
AIR LOCK DOORS		60	0%	0%	25-Jun-26	02-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	25-Jun-26	06-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	30-Jul-26	27-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	07-Jul-26	29-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-115
MLTX-02-005-PR-1	Staging time	5	100%	0%	29-Aug-26	02-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-115
CONSTRUCTION PHASE		152	37.52%	7.99%	30-Jun-26	28-Dec-26	01-Jun-26 A	21-Mar-27	2,484,420.16	529,175.96	6,621,055.66	-67
SITE WORKS		139	32.41%	7.48%	30-Jun-26	28-Dec-26	01-Jun-26 A	21-Mar-27	1,977,905.43	456,653.16	6,103,127.59	-67
LANDSCAPE WORKS		139	32.41%	7.48%	30-Jun-26	28-Dec-26	01-Jun-26 A	21-Mar-27	1,977,905.43	456,653.16	6,103,127.59	-67
PLAYGROUND AREA		135	31.35%	23.9%	30-Jun-26	28-Dec-26	21-Sep-26 A	16-Mar-27	142,085.95	108,312.40	453,207.82	-63
FOOTBALL PLAYGROUND		40	100%	0%	30-Jun-26	15-Aug-26	20-Oct-26	05-Dec-26	47,527.50	0.00	47,527.50	-95
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	20	100%	0%	23-Jul-26	15-Aug-26	12-Nov-26	05-Dec-26	31,685.00	0.00	31,685.00	-95
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	20	100%	0%	30-Jun-26	22-Jul-26	20-Oct-26	11-Nov-26	15,842.50	0.00	15,842.50	-95
PADEL PLAYGROUND		25	0%	0%	18-Nov-26	16-Dec-26	06-Dec-26	03-Jan-27	0.00	0.00	70,195.20	-15
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	15	0%	0%	18-Nov-26	05-Dec-26	06-Dec-26	22-Dec-26	0.00	0.00	58,496.00	-15
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	10	0%	0%	06-Dec-26	16-Dec-26	23-Dec-26	03-Jan-27	0.00	0.00	11,699.20	-15
BASKETBALL PLAYGROUND		15	0%	0%	15-Nov-26	14-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	96,956.10	-75
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	15	0%	0%	15-Nov-26	01-Dec-26	24-Feb-27	16-Mar-27	0.00	0.00	80,796.75	-86
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	06-Dec-26	14-Dec-26	24-Feb-27	04-Mar-27	0.00	0.00	16,159.35	-68
PADEL FENCE		28	0%	0%	17-Dec-26	28-Dec-26	06-Oct-26	07-Nov-26	0.00	0.00	58,008.35	44
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	17-Dec-26	23-Dec-26	06-Oct-26	12-Oct-26	0.00	0.00	4,143.45	62
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	33,147.63	44
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	10	0%	0%	17-Dec-26	28-Dec-26	27-Oct-26	07-Nov-26	0.00	0.00	16,573.82	44

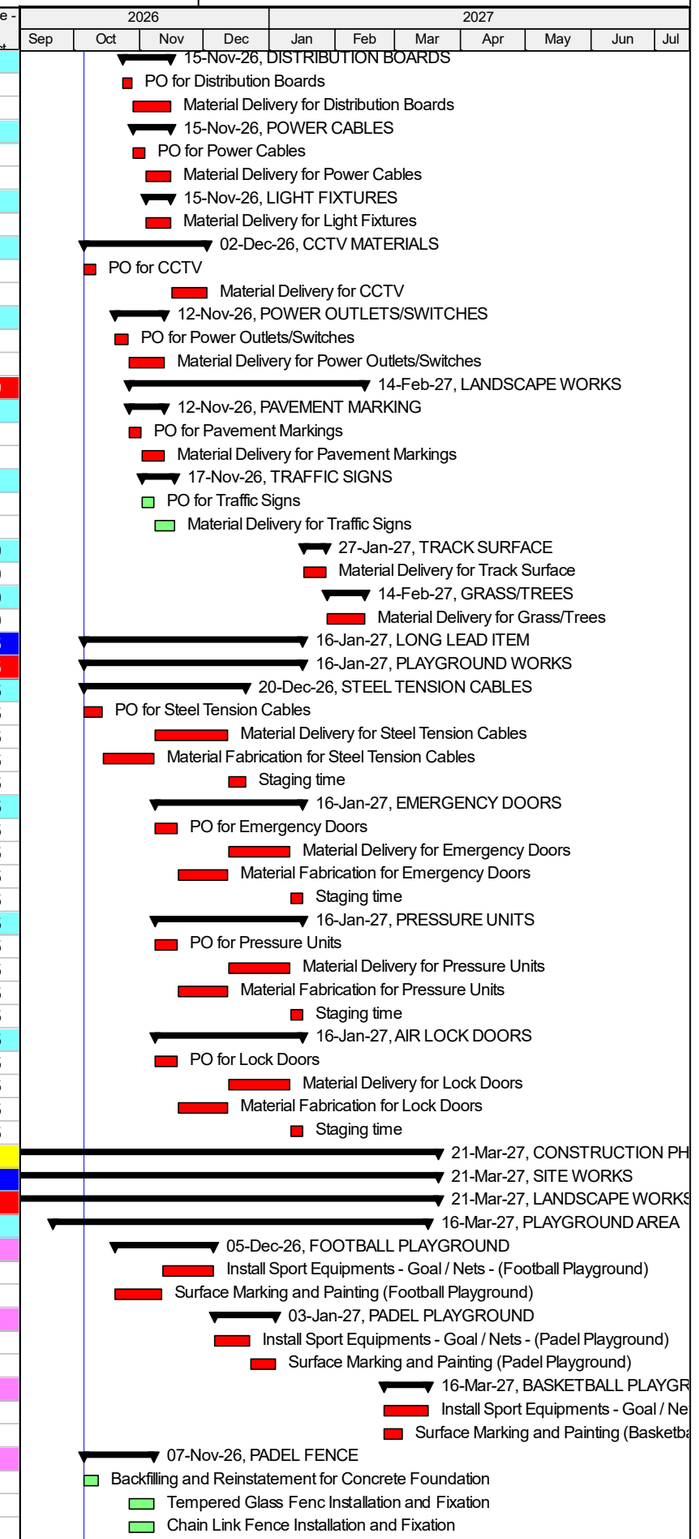

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CI	Install of Fence Gates	5	0%	0%	17-Dec-26	22-Dec-26	27-Oct-26	01-Nov-26	0.00	0.00	4,143.45	44
CURBSTOEN/INTERLOCK		21	52.38%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	180,520.67	-11
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	52.38%	60%	22-Sep-26	17-Oct-26	21-Sep-26 A	29-Oct-26	94,558.45	108,312.40	180,520.67	-11
AIR DOME		135	42.7%	0%	27-Jul-26	09-Dec-26	11-Oct-26	21-Mar-27	1,835,819.49	0.00	4,299,815.57	-83
CIVIL WORKS		39	32.29%	0%	30-Sep-26	24-Oct-26	11-Oct-26	24-Nov-26	447,159.31	0.00	1,384,750.38	-27
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	21	23.81%	0%	30-Sep-26	24-Oct-26	11-Oct-26	03-Nov-26	222,923.53	0.00	936,278.81	-9
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	50%	0%	30-Sep-26	11-Oct-26	14-Nov-26	24-Nov-26	224,235.79	0.00	448,471.57	-38
MECHANICAL WORKS		98	13.64%	0%	27-Jul-26	15-Nov-26	29-Oct-26	20-Feb-27	168,176.84	0.00	1,233,296.81	-83
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	20	0%	0%	12-Oct-26	03-Nov-26	17-Jan-27	08-Feb-27	0.00	0.00	728,766.30	-83
MLTX-02-005-CI	Air Units Installation (Air Dome)	10	0%	0%	04-Nov-26	15-Nov-26	09-Feb-27	20-Feb-27	0.00	0.00	336,353.67	-83
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	20	100%	0%	27-Jul-26	18-Aug-26	29-Oct-26	21-Nov-26	168,176.84	0.00	168,176.84	-80
ELECTRICAL WORKS		58	80.63%	0%	03-Sep-26	15-Oct-26	03-Dec-26	08-Feb-27	1,220,483.34	0.00	1,513,591.54	-99
MLTX-02-005-CI	Light Fixture Works (Air Dome)	12	100%	0%	03-Sep-26	16-Sep-26	17-Jan-27	30-Jan-27	224,235.78	0.00	224,235.78	-115
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	14	85.71%	0%	21-Sep-26	07-Oct-26	17-Jan-27	01-Feb-27	144,151.58	0.00	168,176.84	-100
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	20	60%	0%	21-Sep-26	14-Oct-26	17-Jan-27	08-Feb-27	100,906.10	0.00	168,176.84	-100
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	20	60%	0%	21-Sep-26	14-Oct-26	17-Jan-27	08-Feb-27	302,718.31	0.00	504,530.51	-100
MLTX-02-005-CI	Control System Installation (Air Dome)	21	57.14%	0%	21-Sep-26	15-Oct-26	03-Dec-26	27-Dec-26	448,471.57	0.00	448,471.57	-62
FINISHES WORKS		68	0%	0%	17-Oct-26	09-Dec-26	28-Dec-26	21-Mar-27	0.00	0.00	168,176.84	-83
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	21	0%	0%	17-Oct-26	09-Nov-26	28-Dec-26	20-Jan-27	0.00	0.00	112,117.89	-62
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	21	0%	0%	16-Nov-26	09-Dec-26	21-Feb-27	21-Mar-27	0.00	0.00	56,058.95	-83
IRRIGATION NETWORK		16	0%	38.73%	28-Oct-26	17-Nov-26	10-Sep-26 A	17-Feb-27	0.00	18,848.67	48,667.04	-79
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	10	0%	80%	28-Oct-26	08-Nov-26	10-Sep-26 A	17-Oct-26	0.00	18,848.67	23,560.84	19
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	3	0%	0%	15-Nov-26	17-Nov-26	15-Feb-27	17-Feb-27	0.00	0.00	25,106.20	-79
NATURAL GROUND		76	0%	0%	09-Nov-26	17-Nov-26	22-Nov-26	17-Feb-27	0.00	0.00	191,740.00	-79
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	3	0%	0%	15-Nov-26	17-Nov-26	15-Feb-27	17-Feb-27	0.00	0.00	126,740.00	-79
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	5	0%	0%	09-Nov-26	14-Nov-26	22-Nov-26	26-Nov-26	0.00	0.00	65,000.00	-11
PLANTING		8	0%	21%	12-Oct-26	29-Oct-26	03-Oct-26 A	24-Feb-27	0.00	72,922.81	347,251.46	-100
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	5	0%	70%	12-Oct-26	17-Oct-26	03-Oct-26 A	11-Oct-26	0.00	72,922.81	104,175.44	5
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	3	0%	0%	27-Oct-26	29-Oct-26	21-Feb-27	24-Feb-27	0.00	0.00	141,732.50	-100
MLTX-02-005-CN-1	Placement and Fixation of Trees	5	0%	0%	21-Oct-26	26-Oct-26	15-Feb-27	20-Feb-27	0.00	0.00	101,343.52	-100
WALKING/BIKE PATHS		8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	238,962.04	367,633.90	29
MLTX-02-005-CN-1	Bike Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	01-Jun-26 A	06-Oct-26	0.00	121,910.18	187,554.12	29
MLTX-02-005-CN-1	Walking Path Preparation and Installation Works	8	0%	65%	31-Oct-26	08-Nov-26	10-Jun-26 A	06-Oct-26	0.00	117,051.86	180,079.78	29
GENERAL/FURNITURE		137	0%	4.46%	09-Nov-26	10-Dec-26	01-Oct-26 A	25-Nov-26	0.00	17,607.24	394,811.80	13
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	29
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	7	0%	0%	02-Dec-26	09-Dec-26	18-Nov-26	25-Nov-26	0.00	0.00	9,749.30	12
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	09-Nov-26	17-Nov-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	29
MLTX-02-005-CN-1	Fixation and Installation of Benches	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	40,307.84	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	32,757.76	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	8	0%	0%	18-Nov-26	26-Nov-26	15-Oct-26	24-Oct-26	0.00	0.00	12,869.04	29
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	02-Dec-26	10-Dec-26	25-Oct-26	02-Nov-26	0.00	0.00	12,186.67	33
MLTX-02-005-CN-1	Installing of Site Light Poles	12	0%	10%	18-Nov-26	01-Dec-26	01-Oct-26 A	19-Oct-26	0.00	17,607.24	176,072.40	37
TOILET/SERVICE BUILDING		53	97.8%	14%	18-Jul-26	21-Oct-26	19-Sep-26 A	21-Nov-26	506,514.73	72,522.81	517,928.07	-26
THERMAL & MOISTER PROTECTION		8	100%	70%	02-Aug-26	10-Aug-26	20-Sep-26 A	14-Oct-26	16,607.28	11,625.10	16,607.28	-55
MLTX-02-005-CN-126	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	70%	02-Aug-26	10-Aug-26	20-Sep-26 A	14-Oct-26	16,607.28	11,625.10	16,607.28	-55
MECHANICAL WORK		44	99.81%	26.36%	09-Aug-26	07-Oct-26	19-Sep-26 A	10-Nov-26	98,355.67	25,978.06	98,541.37	-29
HVAC SYSTEM		4	100%	0%	10-Sep-26	14-Sep-26	24-Oct-26	27-Oct-26	14,623.96	0.00	14,623.96	-36
MLTX-02-005-CN-1	Install and Finish HVAC and Ventilation Works Including Split	4	100%	0%	10-Sep-26	14-Sep-26	24-Oct-26	27-Oct-26	14,623.96	0.00	14,623.96	-36
WATER SUPPLY SYSTEM		7	100%	80%	10-Aug-26	17-Aug-26	19-Sep-26 A	13-Oct-26	25,998.40	20,798.72	25,998.40	-48
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	7	100%	80%	10-Aug-26	17-Aug-26	19-Sep-26 A	13-Oct-26	25,998.40	20,798.72	25,998.40	-48
SEWER/DRAINAGE SYSTEM		31	100%	9.25%	09-Aug-26	29-Sep-26	04-Oct-26 A	10-Nov-26	55,969.14	5,179.34	55,969.14	-36
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	5	100%	50%	18-Aug-26	23-Aug-26	04-Oct-26 A	11-Oct-26	10,358.68	5,179.34	10,358.68	-41
MLTX-02-005-CN-1	Installing UPVC Pipes for External Connection for Sewage	8	100%	0%	09-Aug-26	17-Aug-26	06-Oct-26	14-Oct-26	14,217.67	0.00	14,217.67	-49
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	21	100%	0%	05-Sep-26	29-Sep-26	18-Oct-26	10-Nov-26	31,392.79	0.00	31,392.79	-36
FIRE PROTECTION		21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	21	90.48%	0%	13-Sep-26	07-Oct-26	08-Oct-26	01-Nov-26	1,764.17	0.00	1,949.87	-21
ELECTRICAL WORKS		38	93.79%	0%	10-Sep-26	21-Oct-26	08-Oct-26	21-Nov-26	169,553.63	0.00	180,781.27	-26
FIXTURE WORKS		38	93.79%	0%	10-Sep-26	21-Oct-26	08-Oct-26	21-Nov-26	169,553.63	0.00	180,781.27	-26
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	20	85%	0%	15-Sep-26	08-Oct-26	28-Oct-26	19-Nov-26	29,169.90	0.00	34,317.53	-36
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	20	100%	0%	10-Sep-26	04-Oct-26	29-Oct-26	21-Nov-26	102,367.69	0.00	102,367.69	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	20	95%	0%	13-Sep-26	06-Oct-26	20-Oct-26	11-Nov-26	6,730.85	0.00	7,085.10	-31
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	21	90.48%	0%	13-Sep-26	07-Oct-26	18-Oct-26	10-Nov-26	12,901.39	0.00	14,259.43	-29
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	20	30%	0%	29-Sep-26	21-Oct-26	08-Oct-26	31-Oct-26	1,871.88	0.00	6,239.59	-8
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	7,250.09	0.00	7,250.09	-36

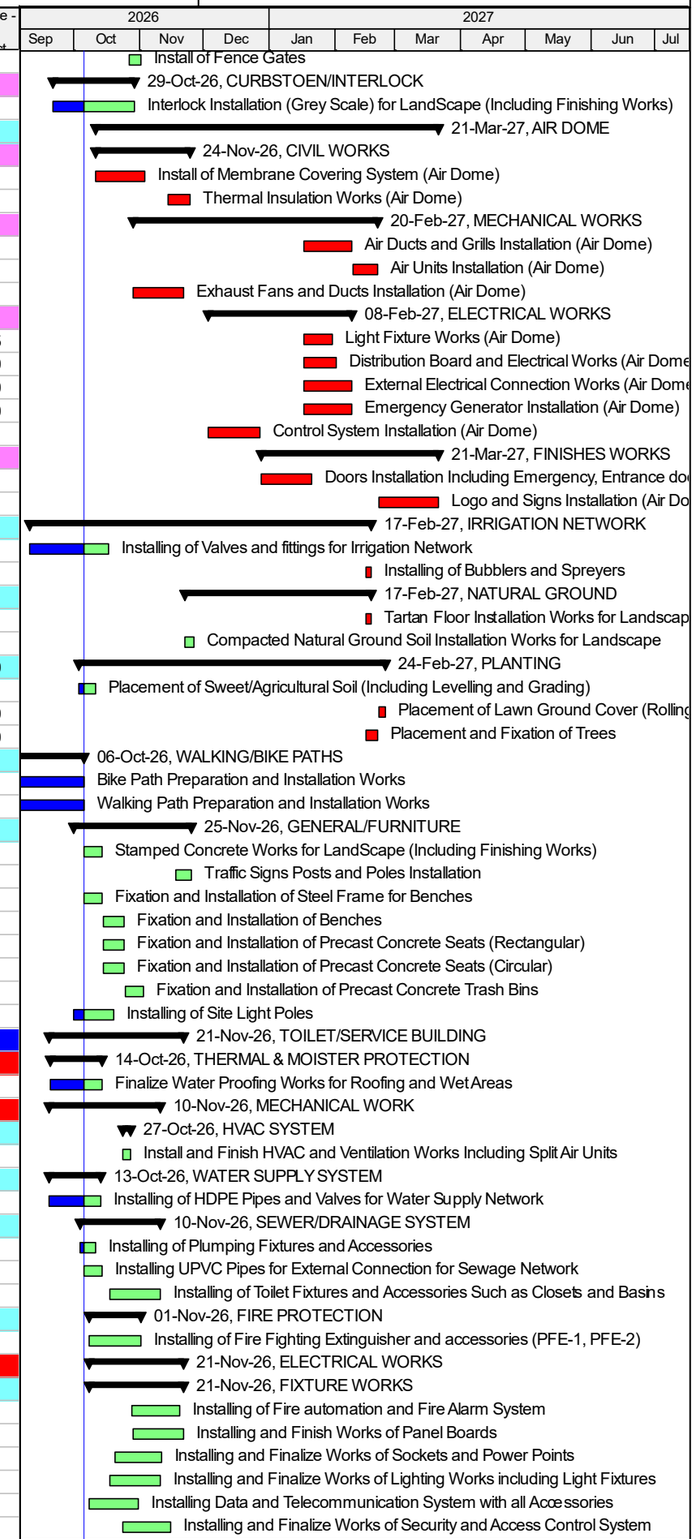

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	6,824.51	0.00	6,824.51	-36
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	20	100%	0%	10-Sep-26	04-Oct-26	24-Oct-26	15-Nov-26	2,437.33	0.00	2,437.33	-36
DOORS/WINDOWS		16	100%	0%	18-Jul-26	10-Sep-26	06-Oct-26	24-Oct-26	58,495.82	0.00	58,495.82	-36
MLTX-02-005-CN-130	Finalize Glazzed Curtain Wall Works	1	100%	0%	10-Sep-26	10-Sep-26	24-Oct-26	24-Oct-26	5,849.58	0.00	5,849.58	-36
MLTX-02-005-CN-131	Preliminary Works For Windows/Curtain Wall	2	100%	0%	18-Jul-26	19-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-68
METAL WORKS		8	100%	0%	18-Jul-26	17-Aug-26	18-Oct-26	26-Oct-26	9,749.30	0.00	9,749.30	-59
MLTX-02-005-CN-126	Installation of Galvanized Steel Ladder	4	100%	0%	13-Aug-26	17-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-55
MLTX-02-005-CN-125	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	22-Oct-26	26-Oct-26	3,899.72	0.00	3,899.72	-82
FINISHING WORKS		35	100%	32.05%	06-Aug-26	13-Sep-26	27-Sep-26 A	26-Oct-26	95,257.20	30,532.46	95,257.20	-36
FLOOR FINISHES		18	100%	0%	06-Aug-26	13-Sep-26	06-Oct-26	26-Oct-26	4,094.76	0.00	4,094.76	-36
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	6	100%	0%	06-Aug-26	12-Aug-26	06-Oct-26	12-Oct-26	2,924.82	0.00	2,924.82	-51
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	3	100%	0%	10-Sep-26	13-Sep-26	24-Oct-26	26-Oct-26	1,169.94	0.00	1,169.94	-36
WALL FINISHES		34	100%	33.49%	11-Aug-26	12-Sep-26	27-Sep-26 A	22-Oct-26	91,162.44	30,532.46	91,162.44	-34
MLTX-02-005-CN-1	Painting Finish Works for External Walls	3	100%	80%	18-Aug-26	20-Aug-26	27-Sep-26 A	08-Oct-26	35,825.58	28,660.46	35,825.58	-41
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	7	100%	0%	27-Aug-26	03-Sep-26	10-Oct-26	17-Oct-26	31,197.60	0.00	31,197.60	-36
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	5	100%	0%	05-Sep-26	09-Sep-26	18-Oct-26	22-Oct-26	13,649.02	0.00	13,649.02	-36
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	11-Aug-26	12-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-55
MLTX-02-005-CN-1	Painting Finish Works for Internal Walls	2	100%	80%	10-Sep-26	12-Sep-26	29-Sep-26 A	07-Oct-26	2,340.00	1,872.00	2,340.00	-21
SPECIALTIES WORK		26	100%	7.5%	24-Aug-26	20-Sep-26	04-Oct-26 A	16-Nov-26	58,495.83	4,387.19	58,495.83	-48
MLTX-02-005-CN-127	Sanitary Fixtures and Accessories Works	3	100%	30%	24-Aug-26	26-Aug-26	04-Oct-26 A	08-Oct-26	14,623.96	4,387.19	14,623.96	-36
MLTX-02-005-CN-127	Installation of MODON Logo on the entrance	7	100%	0%	13-Sep-26	20-Sep-26	09-Nov-26	16-Nov-26	19,498.61	0.00	19,498.61	-48
MLTX-02-005-CN-131	Installation of Phenolic Locker	2	100%	0%	05-Sep-26	06-Sep-26	18-Oct-26	19-Oct-26	24,373.26	0.00	24,373.26	-36
TESTING & COMMISSIONING		109	0%	0%	18-Nov-26	02-Jan-27	26-Nov-26	06-Apr-27	0.00	0.00	0.00	-77
MLTX-02-005-TC-11890	Testing and Commissioning for MEP Works for Playground	14	0%	0%	10-Dec-26	26-Dec-26	22-Mar-27	06-Apr-27	0.00	0.00	0.00	-83
MLTX-02-005-TC-11900	Testing and Commissioning for MEP Works for Toilet/Service	15	0%	0%	18-Nov-26	05-Dec-26	18-Feb-27	08-Mar-27	0.00	0.00	0.00	-79
MLTX-02-005-TC-11910	Testing and Commissioning for MEP Works for Landscape	20	0%	0%	10-Dec-26	02-Jan-27	26-Nov-26	19-Dec-26	0.00	0.00	0.00	12
DAMMAM		184	41.22%	0.94%	06-Apr-26	29-Dec-26	06-Sep-26 A	21-Apr-27	2,615,281.12	59,773.28	6,344,839.54	-93
ENGINEERING		105	0%	0%	06-Apr-26	24-May-26	06-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
SHOP DRAWINGS		105	0%	0%	06-Apr-26	24-May-26	06-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
SHOP DRAWINGS SUBMISSION		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
SHOP DRAWINGS SUBMITTALS FOR PLAYGROUND WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
AIR DOME SYSTEM		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Cable Tension Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Airlock Door Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Emergency Exit Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MECHANCAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for HVAC Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Exhaust Air Plan	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
ELECTRICAL WORKS		21	0%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Power Layout	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Power Single Line Diagram	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Panel Board Schedules	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Submittal for Power Installation Details	21	100%	0%	06-Apr-26	29-Apr-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-153
SHOP DRAWINGS APPROVALS		105	0%	0%	30-Apr-26	24-May-26	06-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
SHOP DRAWINGS APPROVAL FOR PLAYGROUND WORKS		105	0%	0%	30-Apr-26	24-May-26	06-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
AIR DOME SYSTEM		84	0%	0%	30-Apr-26	24-May-26	06-Oct-26	11-Jan-27	0.00	0.00	0.00	-195
MLTX-02-005-EN	Shop DWG Approval for Air Dome Structural Layout	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN	Shop DWG Approval for Membrane Panel Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Cable Tension Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Airlock Door Details	21	100%	0%	30-Apr-26	24-May-26	24-Nov-26	17-Dec-26	0.00	0.00	0.00	-174
MLTX-02-005-EN	Shop DWG Approval for Emergency Exit Details	21	100%	0%	30-Apr-26	24-May-26	19-Dec-26	11-Jan-27	0.00	0.00	0.00	-195
SPORTS EQUIPMENT		21	0%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MLTX-02-005-EN	Shop DWG Approval for Football Turf Installation	21	100%	0%	30-Apr-26	24-May-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-132
MECHANCAL WORKS		84	0%	0%	30-Apr-26	24-May-26	31-Oct-26	04-Feb-27	0.00	0.00	0.00	-216
MLTX-02-005-EN	Shop DWG Approval for HVAC Plan	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Exhaust Air Plan	21	100%	0%	30-Apr-26	24-May-26	12-Jan-27	04-Feb-27	0.00	0.00	0.00	-216
ELECTRICAL WORKS		21	0%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Power Layout	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Power Single Line Diagram	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Panel Board Schedules	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
MLTX-02-005-EN	Shop DWG Approval for Power Installation Details	21	100%	0%	30-Apr-26	24-May-26	31-Oct-26	23-Nov-26	0.00	0.00	0.00	-153
PROCUREMENT		118	0%	0%	21-May-26	21-Oct-26	06-Oct-26	20-Feb-27	0.00	0.00	0.00	-104
SHORT LEAD ITEM		118	0%	0%	31-May-26	21-Oct-26	06-Oct-26	20-Feb-27	0.00	0.00	0.00	-104
TOILET/SERVICE WORKS		29	0%	0%	11-Jun-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79

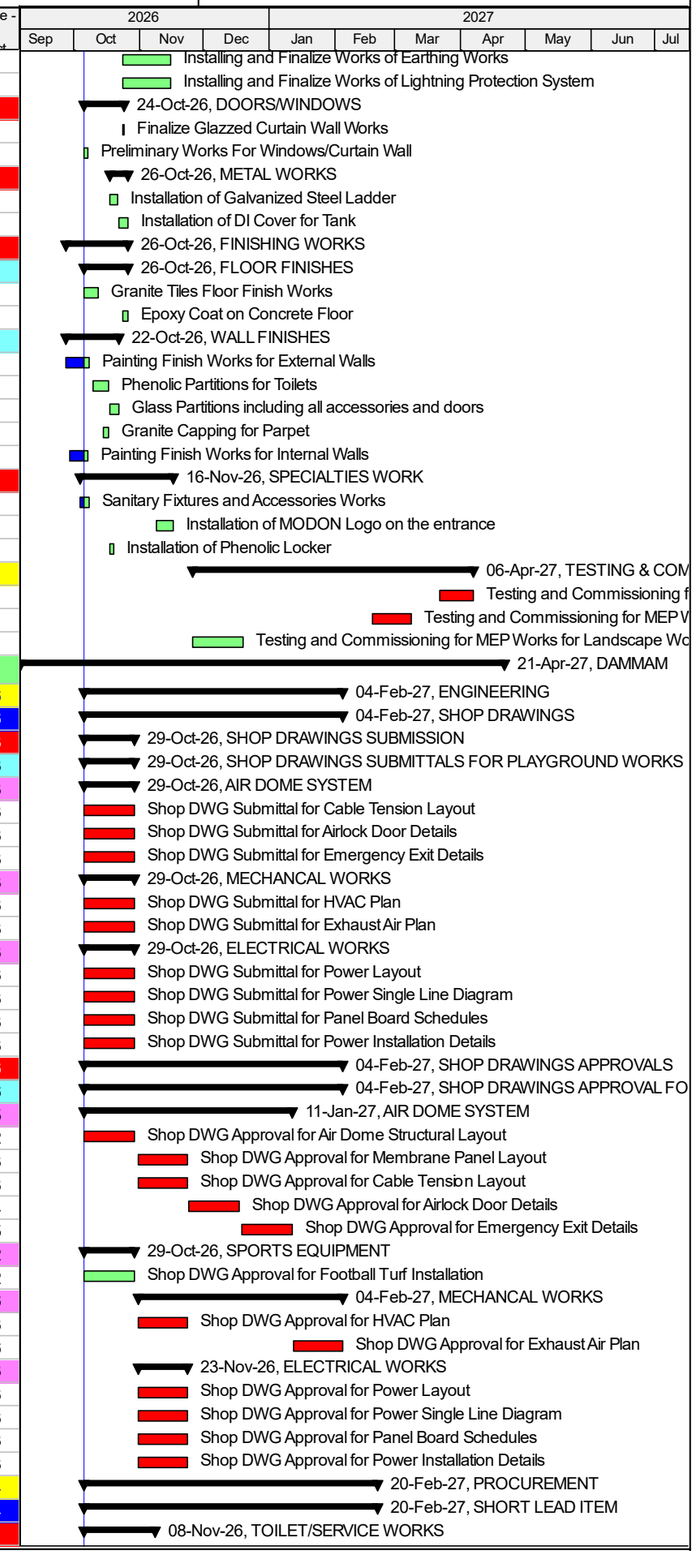

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
LIGHTING FIXTURES		10	0%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Lighting Fixtures	10	100%	0%	11-Jul-26	21-Jul-26	06-Oct-26	17-Oct-26	0.00	0.00	0.00	-74
SWITCHES/SOCKETS		12	0%	0%	11-Jul-26	23-Jul-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	PO for Switches/Sockets	5	100%	0%	11-Jul-26	15-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-74
MLTX-02-005-PR-1	Material Delivery for Switches/Sockets	7	100%	0%	16-Jul-26	23-Jul-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-74
DISTRIBUTION PANNELS		20	0%	0%	11-Jun-26	04-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Distribution Panels	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Distribution Panels	15	100%	0%	17-Jun-26	04-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-99
FURNITURES		29	0%	0%	05-Jul-26	06-Aug-26	06-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Furnitures	9	100%	0%	05-Jul-26	14-Jul-26	06-Oct-26	15-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Furnitures	20	100%	0%	15-Jul-26	06-Aug-26	17-Oct-26	08-Nov-26	0.00	0.00	0.00	-79
PLAYGROUND WORKS		50	0%	0%	31-May-26	29-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-81
PVC MEMBRANE		21	0%	0%	06-Jun-26	29-Jun-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for PVC Membrane	21	100%	0%	06-Jun-26	29-Jun-26	06-Oct-26	29-Oct-26	0.00	0.00	0.00	-104
ARTIFICIAL TURF		12	0%	0%	06-Jul-26	19-Jul-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Artificial TURF	12	100%	0%	06-Jul-26	19-Jul-26	31-Oct-26	12-Nov-26	0.00	0.00	0.00	-99
RUBBER GRANULES		12	0%	0%	31-May-26	13-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Rubber Granules	12	100%	0%	31-May-26	13-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-109
PADEL GLASS		18	0%	0%	31-May-26	20-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Padel Glass	18	100%	0%	31-May-26	20-Jun-26	06-Oct-26	26-Oct-26	0.00	0.00	0.00	-109
PADEL WIRE MESH/STEEL SETS		15	0%	0%	06-Jun-26	22-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Wire Mesh/Steel Sets	15	100%	0%	06-Jun-26	22-Jun-26	06-Oct-26	22-Oct-26	0.00	0.00	0.00	-104
BITUMINOUS BASE & WEARING COURSE		12	0%	0%	11-Jun-26	24-Jun-26	06-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Bituminous Base & Wearing Course	5	100%	0%	11-Jun-26	16-Jun-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for the Site	7	100%	0%	17-Jun-26	24-Jun-26	12-Oct-26	19-Oct-26	0.00	0.00	0.00	-99
INTERLOCKING PAVING		12	0%	0%	16-Jul-26	29-Jul-26	26-Oct-26	08-Nov-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	PO for Interlocking Block Pavers	5	100%	0%	16-Jul-26	21-Jul-26	26-Oct-26	31-Oct-26	0.00	0.00	0.00	-86
MLTX-02-005-PR-1	Material Delivery for Interlocking Block Pavers	7	100%	0%	22-Jul-26	29-Jul-26	01-Nov-26	08-Nov-26	0.00	0.00	0.00	-86
MARKING PAINT		12	0%	0%	17-Jun-26	30-Jun-26	12-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	PO for Marking Paint	5	100%	0%	17-Jun-26	22-Jun-26	12-Oct-26	17-Oct-26	0.00	0.00	0.00	-99
MLTX-02-005-PR-1	Material Delivery for Marking Paint	7	100%	0%	23-Jun-26	30-Jun-26	18-Oct-26	25-Oct-26	0.00	0.00	0.00	-99
AIR DIFUSSERS/GRILLS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Air Difussers/Grills	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Air Difussers/Grills	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
GALVANIZED DUCTS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Galvanized Duct	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Galvanized Duct	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
EXHAUST FANS		20	0%	0%	05-Jul-26	27-Jul-26	06-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	PO for Exhaust Fans	5	100%	0%	05-Jul-26	09-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-79
MLTX-02-005-PR-1	Material Delivery for Exhaust Fans	15	100%	0%	11-Jul-26	27-Jul-26	12-Oct-26	28-Oct-26	0.00	0.00	0.00	-79
DISTRIBUTION BOARDS		20	0%	0%	05-Jul-26	27-Jul-26	24-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Distribution Boards	5	100%	0%	05-Jul-26	09-Jul-26	24-Oct-26	28-Oct-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Distribution Boards	15	100%	0%	11-Jul-26	27-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
POWER CABLES		15	0%	0%	11-Jul-26	27-Jul-26	29-Oct-26	15-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	PO for Power Cables	5	100%	0%	11-Jul-26	15-Jul-26	29-Oct-26	03-Nov-26	0.00	0.00	0.00	-94
MLTX-02-005-PR-1	Material Delivery for Power Cables	10	100%	0%	16-Jul-26	27-Jul-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-94
LIGHT FIXTURES		10	0%	0%	22-Jul-26	02-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-89
MLTX-02-005-PR-1	Material Delivery for Light Fixtures	10	100%	0%	22-Jul-26	02-Aug-26	04-Nov-26	15-Nov-26	0.00	0.00	0.00	-89
CCTV MATERIALS		50	0%	0%	22-Jul-26	29-Aug-26	06-Oct-26	02-Dec-26	0.00	0.00	0.00	-81
MLTX-02-005-PR-1	PO for CCTV	5	100%	0%	22-Jul-26	27-Jul-26	06-Oct-26	11-Oct-26	0.00	0.00	0.00	-64
MLTX-02-005-PR-1	Material Delivery for CCTV	15	100%	0%	12-Aug-26	29-Aug-26	16-Nov-26	02-Dec-26	0.00	0.00	0.00	-81
POWER OUTLETS/SWITCHES		21	0%	0%	28-Jul-26	20-Aug-26	20-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	PO for Power Outlets/Switches	6	100%	0%	28-Jul-26	03-Aug-26	20-Oct-26	26-Oct-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Power Outlets/Switches	15	100%	0%	04-Aug-26	20-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
LANDSCAPE WORKS		100	0%	0%	04-Aug-26	21-Oct-26	27-Oct-26	20-Feb-27	0.00	0.00	0.00	-104
PAVEMENT MARKING		15	0%	0%	04-Aug-26	20-Aug-26	27-Oct-26	12-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	PO for Pavement Markings	5	100%	0%	04-Aug-26	09-Aug-26	27-Oct-26	01-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Pavement Markings	10	100%	0%	10-Aug-26	20-Aug-26	02-Nov-26	12-Nov-26	0.00	0.00	0.00	-71
TRAFFIC SIGNS		14	0%	0%	05-Oct-26	20-Oct-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	PO for Traffic Signs	5	20%	0%	05-Oct-26	10-Oct-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-24
MLTX-02-005-PR-1	Material Delivery for Traffic Signs	9	0%	0%	11-Oct-26	20-Oct-26	08-Nov-26	17-Nov-26	0.00	0.00	0.00	-24
IRRIGATION PIPES/SPRINKLERS		14	0%	0%	10-Aug-26	24-Aug-26	02-Nov-26	17-Nov-26	0.00	0.00	0.00	-72
MLTX-02-005-PR-1	PO for Irrigation Pipes/Sprinkles	5	100%	0%	10-Aug-26	15-Aug-26	02-Nov-26	07-Nov-26	0.00	0.00	0.00	-71
MLTX-02-005-PR-1	Material Delivery for Irrigation Pipes/Sprinkles	8	100%	0%	16-Aug-26	24-Aug-26	09-Nov-26	17-Nov-26	0.00	0.00	0.00	-72

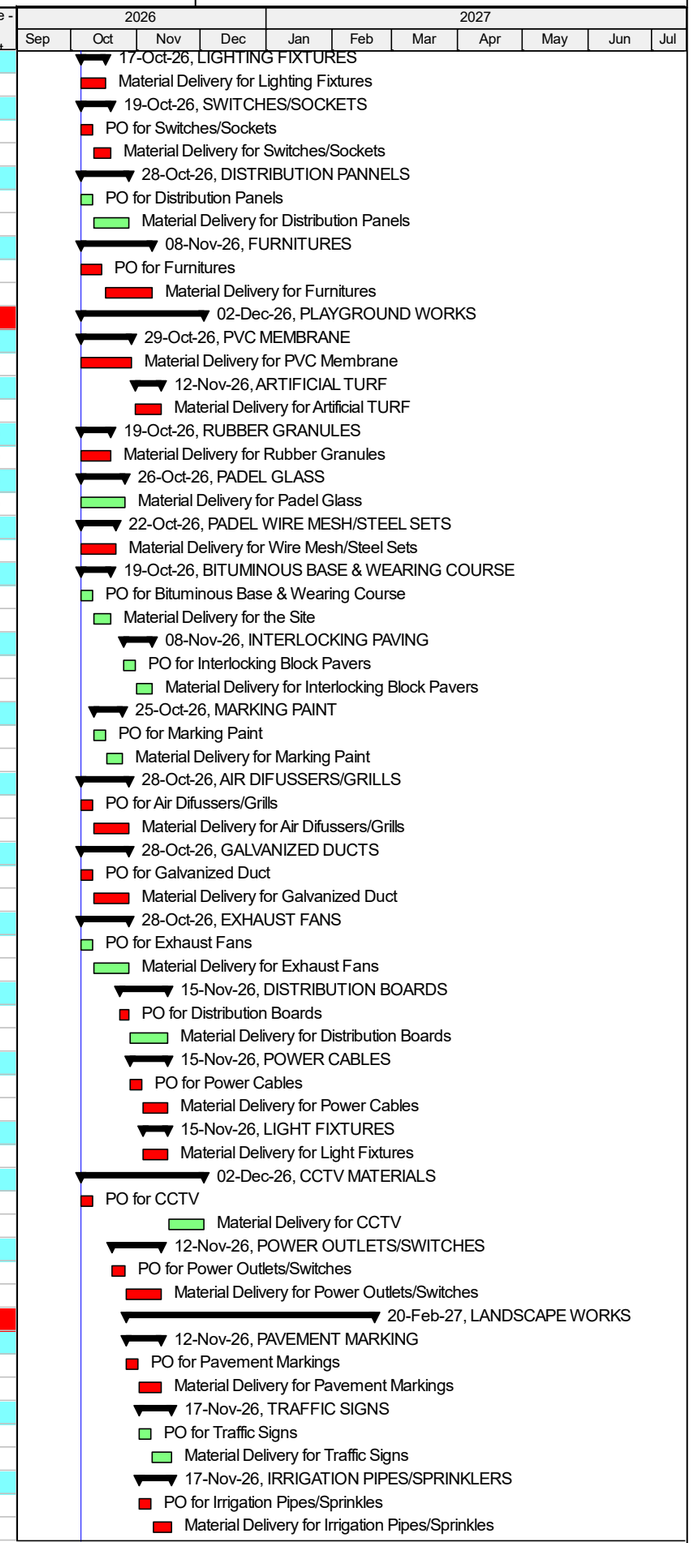

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
AGRICULTURE SOIL		17	0%	0%	22-Sep-26	12-Oct-26	28-Jan-27	16-Feb-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	PO for Agriculture Soil	5	100%	0%	22-Sep-26	28-Sep-26	28-Jan-27	02-Feb-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Agriculture Soil	12	50%	0%	29-Sep-26	12-Oct-26	03-Feb-27	16-Feb-27	0.00	0.00	0.00	-109
TRACK SURFACE		10	0%	0%	10-Sep-26	21-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-109
MLTX-02-005-PR-1	Material Delivery for Track Surface	10	100%	0%	10-Sep-26	21-Sep-26	17-Jan-27	27-Jan-27	0.00	0.00	0.00	-109
GRASS/TREES		15	0%	0%	05-Oct-26	21-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-104
MLTX-02-005-PR-1	Material Delivery for Grass/Trees	15	6.67%	0%	05-Oct-26	21-Oct-26	03-Feb-27	20-Feb-27	0.00	0.00	0.00	-104
LONG LEAD ITEM		88	0%	0%	21-May-26	03-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-114
PLAYGROUND WORKS		88	0%	0%	21-May-26	03-Sep-26	06-Oct-26	16-Jan-27	0.00	0.00	0.00	-114
STEEL TENSION CABLES		65	0%	0%	21-May-26	08-Aug-26	06-Oct-26	20-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Steel Tension Cables	8	100%	0%	21-May-26	02-Jun-26	06-Oct-26	14-Oct-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Steel Tension Cables	30	100%	0%	27-Jun-26	30-Jul-26	08-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Steel Tension Cables	20	100%	0%	03-Jun-26	25-Jun-26	15-Oct-26	07-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	7	100%	0%	01-Aug-26	08-Aug-26	13-Dec-26	20-Dec-26	0.00	0.00	0.00	-114
EMERGENCY DOORS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Emergency Doors	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Emergency Doors	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Emergency Doors	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
PRESSURE UNITS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Pressure Units	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Pressure Units	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Pressure Units	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
AIR LOCK DOORS		60	0%	0%	27-Jun-26	03-Sep-26	08-Nov-26	16-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	PO for Lock Doors	10	100%	0%	27-Jun-26	07-Jul-26	08-Nov-26	18-Nov-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Delivery for Lock Doors	25	100%	0%	01-Aug-26	29-Aug-26	13-Dec-26	10-Jan-27	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Material Fabrication for Lock Doors	20	100%	0%	08-Jul-26	30-Jul-26	19-Nov-26	12-Dec-26	0.00	0.00	0.00	-114
MLTX-02-005-PR-1	Staging time	5	100%	0%	30-Aug-26	03-Sep-26	11-Jan-27	16-Jan-27	0.00	0.00	0.00	-114
CONSTRUCTION PHASE		179	41.22%	0.94%	18-Jul-26	29-Dec-26	06-Sep-26 A	15-Apr-27	2,615,281.12	59,773.28	6,344,839.54	-88
SITE WORKS		161	37.14%	0.32%	24-Aug-26	29-Dec-26	19-Sep-26 A	15-Apr-27	2,188,733.52	18,848.67	5,893,918.68	-88
LANDSCAPE WORKS		161	37.14%	0.32%	24-Aug-26	29-Dec-26	19-Sep-26 A	15-Apr-27	2,188,733.52	18,848.67	5,893,918.68	-88
PLAYGROUND AREA		133	57.39%	0%	24-Aug-26	08-Dec-26	27-Oct-26	04-Apr-27	351,016.14	0.00	611,632.81	-96
FOOTBALL PLAYGROUND		110	82.78%	0%	24-Aug-26	11-Nov-26	14-Nov-26	25-Mar-27	170,495.47	0.00	205,952.49	-111
MLTX-02-005-CI	Finishing Asphalt & Concrete Surface (Football Playground)	20	100%	0%	24-Aug-26	15-Sep-26	14-Nov-26	06-Dec-26	158,424.99	0.00	158,424.99	-69
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Football Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	31,685.00	-111
MLTX-02-005-CI	Surface Marking and Painting (Football Playground)	21	76.19%	0%	16-Sep-26	11-Oct-26	07-Dec-26	30-Dec-26	12,070.48	0.00	15,842.50	-69
PADEL PLAYGROUND		5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	70,195.20	-111
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	58,496.00	-111
MLTX-02-005-CI	Surface Marking and Painting (Padel Playground)	5	0%	0%	07-Nov-26	11-Nov-26	21-Mar-27	25-Mar-27	0.00	0.00	11,699.20	-111
BASKETBALL PLAYGROUND		8	0%	0%	12-Nov-26	21-Nov-26	27-Mar-27	04-Apr-27	0.00	0.00	96,956.10	-111
MLTX-02-005-CI	Install Sport Equipments - Goal / Nets - (Basketball	8	0%	0%	12-Nov-26	21-Nov-26	27-Mar-27	04-Apr-27	0.00	0.00	80,796.75	-111
MLTX-02-005-CI	Surface Marking and Painting (Basketball Playground)	8	0%	0%	12-Nov-26	21-Nov-26	27-Mar-27	04-Apr-27	0.00	0.00	16,159.35	-111
PADEL FENCE		15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	58,008.35	22
MLTX-02-005-CI	Backfilling and Reinstatement for Concrete Foundation	6	0%	0%	22-Nov-26	28-Nov-26	27-Oct-26	02-Nov-26	0.00	0.00	4,143.45	22
MLTX-02-005-CI	Tempered Glass Fenc Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	33,147.63	22
MLTX-02-005-CI	Chain Link Fence Installation and Fixation	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	16,573.82	22
MLTX-02-005-CI	Install of Fence Gates	15	0%	0%	22-Nov-26	08-Dec-26	27-Oct-26	12-Nov-26	0.00	0.00	4,143.45	22
CURBSTOEN/INTERLOCK		21	100%	0%	07-Sep-26	01-Oct-26	14-Nov-26	07-Dec-26	180,520.67	0.00	180,520.67	-57
MLTX-02-005-CI	Interlock Installation (Grey Scale) for LandScape (Including	21	100%	0%	07-Sep-26	01-Oct-26	14-Nov-26	07-Dec-26	180,520.67	0.00	180,520.67	-57
AIR DOME		126	42.37%	0%	16-Sep-26	24-Nov-26	16-Nov-26	15-Apr-27	1,822,010.16	0.00	4,299,815.57	-118
CIVIL WORKS		15	100%	0%	16-Sep-26	04-Oct-26	16-Nov-26	02-Dec-26	1,384,750.38	0.00	1,384,750.38	-51
MLTX-02-005-CI	Install of Membrane Covering System (Air Dome)	15	100%	0%	16-Sep-26	04-Oct-26	16-Nov-26	02-Dec-26	936,278.81	0.00	936,278.81	-51
MLTX-02-005-CI	Thermal Insulation Works (Air Dome)	10	100%	0%	16-Sep-26	28-Sep-26	16-Nov-26	26-Nov-26	448,471.57	0.00	448,471.57	-51
MECHANICAL WORKS		33	35.45%	0%	29-Sep-26	05-Nov-26	06-Feb-27	20-Mar-27	437,259.78	0.00	1,233,296.81	-111
MLTX-02-005-CI	Air Ducts and Grills Installation (Air Dome)	10	60%	0%	29-Sep-26	10-Oct-26	06-Feb-27	16-Feb-27	437,259.78	0.00	728,766.30	-111
MLTX-02-005-CI	Air Units Installation (Air Dome)	13	0%	0%	11-Oct-26	25-Oct-26	17-Feb-27	04-Mar-27	0.00	0.00	336,353.67	-111
MLTX-02-005-CI	Exhaust Fans and Ducts Installation (Air Dome)	10	0%	0%	26-Oct-26	05-Nov-26	06-Mar-27	20-Mar-27	0.00	0.00	168,176.84	-111
ELECTRICAL WORKS		39	0%	0%	11-Oct-26	24-Nov-26	17-Feb-27	07-Apr-27	0.00	0.00	1,513,591.54	-111
MLTX-02-005-CI	Light Fixture Works (Air Dome)	10	0%	0%	11-Oct-26	21-Oct-26	17-Feb-27	01-Mar-27	0.00	0.00	224,235.78	-111
MLTX-02-005-CI	Distribution Board and Electrical Works (Air Dome)	7	0%	0%	22-Oct-26	29-Oct-26	02-Mar-27	09-Mar-27	0.00	0.00	168,176.84	-111
MLTX-02-005-CI	External Electrical Connection Works (Air Dome)	6	0%	0%	31-Oct-26	05-Nov-26	14-Mar-27	20-Mar-27	0.00	0.00	168,176.84	-111
MLTX-02-005-CI	Emergency Generator Installation (Air Dome)	11	0%	0%	07-Nov-26	18-Nov-26	21-Mar-27	01-Apr-27	0.00	0.00	504,530.51	-111
MLTX-02-005-CI	Control System Installation (Air Dome)	5	0%	0%	19-Nov-26	24-Nov-26	03-Apr-27	07-Apr-27	0.00	0.00	448,471.57	-111

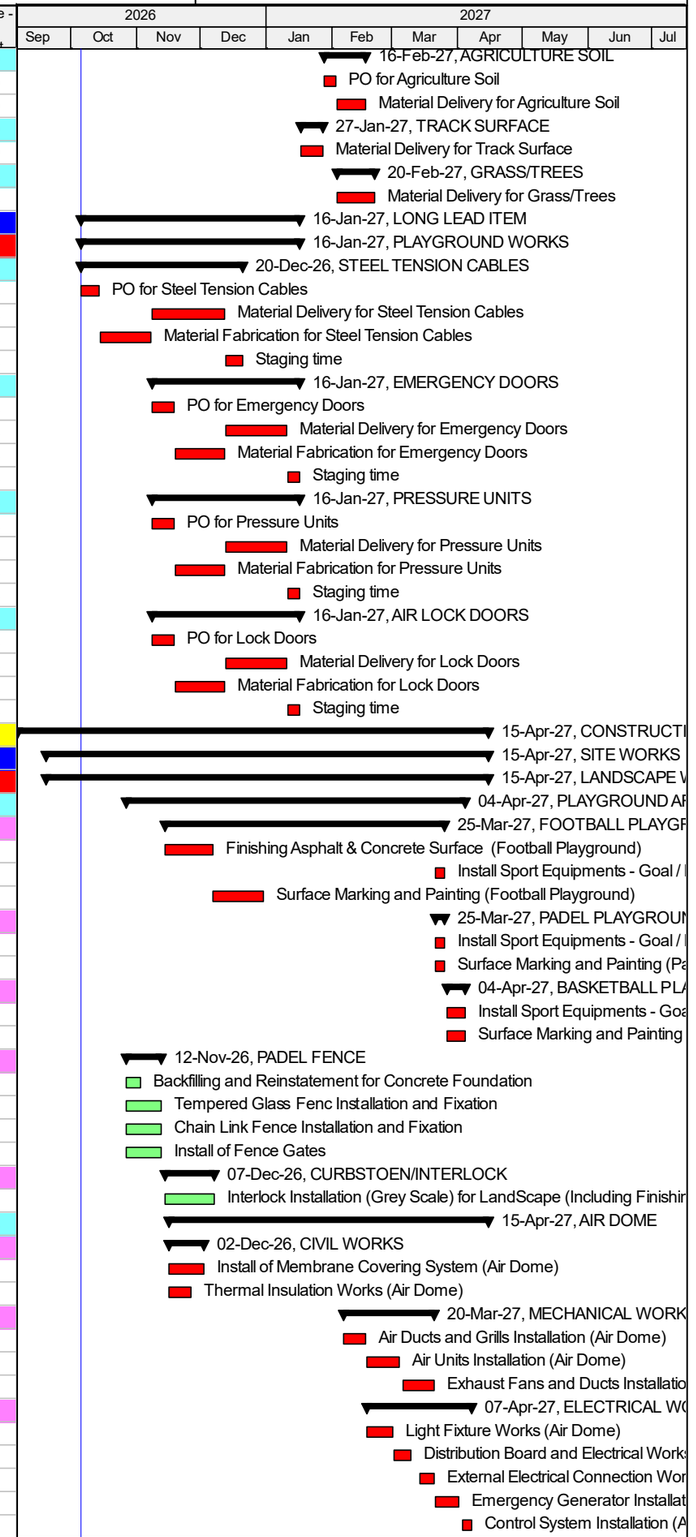

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
FINISHES WORKS		29	0%	0%	31-Oct-26	22-Nov-26	14-Mar-27	15-Apr-27	0.00	0.00	168,176.84	-120
MLTX-02-005-CI	Doors Installation Including Emergency, Entrance doors (Air	10	0%	0%	31-Oct-26	10-Nov-26	14-Mar-27	24-Mar-27	0.00	0.00	112,117.89	-111
MLTX-02-005-CI	Logo and Signs Installation (Air Dome)	10	0%	0%	11-Nov-26	22-Nov-26	05-Apr-27	15-Apr-27	0.00	0.00	56,058.95	-120
IRRIGATION NETWORK		39	32.27%	38.73%	04-Oct-26	14-Oct-26	19-Sep-26 A	18-Feb-27	15,707.23	18,848.67	48,667.04	-109
MLTX-02-005-CN-1	Installing of Valves and fittings for Irrigation Network	3	66.67%	80%	04-Oct-26	06-Oct-26	19-Sep-26 A	08-Oct-26	15,707.23	18,848.67	23,560.84	-2
MLTX-02-005-CN-1	Installing of Bubblers and Spreyers	2	0%	0%	13-Oct-26	14-Oct-26	17-Feb-27	18-Feb-27	0.00	0.00	25,106.20	-109
NATURAL GROUND		30	0%	0%	07-Oct-26	10-Nov-26	10-Oct-26	12-Nov-26	0.00	0.00	191,740.00	-2
MLTX-02-005-CN-1	Tartan Floor Installation Works for Landscape (Including	15	0%	0%	25-Oct-26	10-Nov-26	27-Oct-26	12-Nov-26	0.00	0.00	126,740.00	-2
MLTX-02-005-CN-1	Compacted Natural Ground Soil Installation Works for	15	0%	0%	07-Oct-26	24-Oct-26	10-Oct-26	26-Oct-26	0.00	0.00	65,000.00	-2
PLANTING		23	0%	0%	15-Oct-26	10-Nov-26	20-Feb-27	22-Mar-27	0.00	0.00	347,251.46	-109
MLTX-02-005-CN-1	Placement of Sweet/Agricultural Soil (Including Levelling and	6	0%	0%	15-Oct-26	21-Oct-26	20-Feb-27	27-Feb-27	0.00	0.00	104,175.44	-109
MLTX-02-005-CN-1	Placement of Lawn Ground Cover (Rolling and Compaction)	7	0%	0%	03-Nov-26	10-Nov-26	15-Mar-27	22-Mar-27	0.00	0.00	141,732.50	-109
MLTX-02-005-CN-1	Placement and Fixation of Trees	10	0%	0%	22-Oct-26	02-Nov-26	28-Feb-27	14-Mar-27	0.00	0.00	101,343.52	-109
GENERAL/FURNITURE		159	0%	0%	23-Nov-26	29-Dec-26	06-Oct-26	13-Apr-27	0.00	0.00	394,811.80	-86
MLTX-02-005-CN-1	Stamped Concrete Works for LandScape (Including	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	93,594.00	41
MLTX-02-005-CN-1	Traffic Signs Posts and Poles Installation	9	0%	0%	20-Dec-26	29-Dec-26	04-Apr-27	13-Apr-27	0.00	0.00	9,749.30	-86
MLTX-02-005-CN-1	Fixation and Installation of Steel Frame for Benches	8	0%	0%	23-Nov-26	01-Dec-26	06-Oct-26	14-Oct-26	0.00	0.00	17,274.79	41
MLTX-02-005-CN-1	Fixation and Installation of Benches	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	40,307.84	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	32,757.76	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Seats (Circular)	10	0%	0%	02-Dec-26	13-Dec-26	15-Oct-26	26-Oct-26	0.00	0.00	12,869.04	41
MLTX-02-005-CN-1	Fixation and Installation of Precast Concrete Trash Bins	8	0%	0%	20-Dec-26	28-Dec-26	27-Oct-26	04-Nov-26	0.00	0.00	12,186.67	46
MLTX-02-005-CN-1	Installing of Site Light Poles	10	0%	0%	02-Dec-26	13-Dec-26	23-Mar-27	03-Apr-27	0.00	0.00	176,072.40	-91
TOILET/SERVICE BUILDING		64	94.59%	9.08%	18-Jul-26	11-Oct-26	06-Sep-26 A	28-Nov-26	426,547.60	40,924.61	450,920.86	-41
THERMAL & MOISTER PROTECTION		8	100%	90%	06-Aug-26	15-Aug-26	06-Sep-26 A	14-Oct-26	16,607.28	14,946.55	16,607.28	-51
MLTX-02-005-CN-140	Finalize Water Proofing Works for Roofing and Wet Areas	8	100%	90%	06-Aug-26	15-Aug-26	06-Sep-26 A	14-Oct-26	16,607.28	14,946.55	16,607.28	-51
MECHANICAL WORK		36	100%	37.27%	08-Aug-26	20-Sep-26	19-Sep-26 A	01-Nov-26	69,699.74	25,978.06	69,699.74	-35
WATER SUPPLY SYSTEM		6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	12-Oct-26	25,998.40	20,798.72	25,998.40	-50
MLTX-02-005-CN-1	Installing of HDPE Pipes and Valves for Water Supply	6	100%	80%	08-Aug-26	13-Aug-26	19-Sep-26 A	12-Oct-26	25,998.40	20,798.72	25,998.40	-50
SEWER/DRAINAGE SYSTEM		23	100%	12.41%	17-Aug-26	13-Sep-26	04-Oct-26 A	01-Nov-26	41,751.47	5,179.34	41,751.47	-41
MLTX-02-005-CN-1	Installing of Plumping Fixtures and Accessories	4	100%	50%	17-Aug-26	20-Aug-26	04-Oct-26 A	10-Oct-26	10,358.68	5,179.34	10,358.68	-42
MLTX-02-005-CN-1	Installing of Toilet Fixtures and Accessories Such as Closets	4	100%	0%	09-Sep-26	13-Sep-26	28-Oct-26	01-Nov-26	31,392.79	0.00	31,392.79	-41
FIRE PROTECTION		2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
MLTX-02-005-CN-1	Installing of Fire Fighting Extinguisher and accessories	2	100%	0%	19-Sep-26	20-Sep-26	06-Oct-26	07-Oct-26	1,949.87	0.00	1,949.87	-14
ELECTRICAL WORKS		46	86.52%	0%	16-Sep-26	11-Oct-26	06-Oct-26	28-Nov-26	156,408.01	0.00	180,781.27	-41
FIXTURE WORKS		46	86.52%	0%	16-Sep-26	11-Oct-26	06-Oct-26	28-Nov-26	156,408.01	0.00	180,781.27	-41
MLTX-02-005-CN-1	Installing of Fire automation and Fire Alarm System	5	100%	0%	20-Sep-26	26-Sep-26	06-Oct-26	11-Oct-26	34,317.53	0.00	34,317.53	-13
MLTX-02-005-CN-1	Installing and Finish Works of Panel Boards	21	76.19%	0%	16-Sep-26	11-Oct-26	04-Nov-26	28-Nov-26	77,994.43	0.00	102,367.69	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Sockets and Power Points	3	100%	0%	19-Sep-26	21-Sep-26	20-Oct-26	22-Oct-26	7,085.10	0.00	7,085.10	-26
MLTX-02-005-CN-1	Installing and Finalize Works of Lighting Works including Light	4	100%	0%	19-Sep-26	22-Sep-26	18-Oct-26	21-Oct-26	14,259.43	0.00	14,259.43	-24
MLTX-02-005-CN-1	Installing Data and Telecommunication System with all	4	100%	0%	19-Sep-26	22-Sep-26	06-Oct-26	10-Oct-26	6,239.59	0.00	6,239.59	-14
MLTX-02-005-CN-1	Installing and Finalize Works of Security and Access Control	4	100%	0%	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	7,250.09	0.00	7,250.09	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Earthing Works	3	100%	0%	16-Sep-26	19-Sep-26	04-Nov-26	07-Nov-26	6,824.51	0.00	6,824.51	-41
MLTX-02-005-CN-1	Installing and Finalize Works of Lightning Protection System	5	100%	0%	16-Sep-26	21-Sep-26	04-Nov-26	09-Nov-26	2,437.33	0.00	2,437.33	-41
DOORS/WINDOWS		29	100%	0%	22-Jul-26	20-Sep-26	06-Oct-26	08-Nov-26	58,495.82	0.00	58,495.82	-41
MLTX-02-005-CN-144	Finalize Glazzed Curtain Wall Works	4	100%	0%	16-Sep-26	20-Sep-26	04-Nov-26	08-Nov-26	5,849.58	0.00	5,849.58	-41
MLTX-02-005-CN-145	Preliminary Works For Windows/Curtain Wall	2	100%	0%	22-Jul-26	23-Jul-26	06-Oct-26	07-Oct-26	52,646.24	0.00	52,646.24	-64
METAL WORKS		8	100%	0%	18-Jul-26	22-Aug-26	18-Oct-26	26-Oct-26	9,749.30	0.00	9,749.30	-55
MLTX-02-005-CN-140	Installation of Galvanized Steel Ladder	4	100%	0%	18-Aug-26	22-Aug-26	18-Oct-26	21-Oct-26	5,849.58	0.00	5,849.58	-51
MLTX-02-005-CN-144	Installation of DI Cover for Tank	4	100%	0%	18-Jul-26	21-Jul-26	22-Oct-26	26-Oct-26	3,899.72	0.00	3,899.72	-82
FINISHING WORKS		27	100%	0%	10-Aug-26	17-Sep-26	06-Oct-26	05-Nov-26	57,091.62	0.00	57,091.62	-41
FLOOR FINISHES		27	100%	0%	10-Aug-26	17-Sep-26	06-Oct-26	05-Nov-26	4,094.76	0.00	4,094.76	-41
MLTX-02-005-CN-1	Granite Tiles Floor Finish Works	4	100%	0%	10-Aug-26	13-Aug-26	06-Oct-26	10-Oct-26	2,924.82	0.00	2,924.82	-48
MLTX-02-005-CN-1	Epoxy Coat on Concrete Floor	2	100%	0%	16-Sep-26	17-Sep-26	04-Nov-26	05-Nov-26	1,169.94	0.00	1,169.94	-41
WALL FINISHES		17	100%	0%	16-Aug-26	15-Sep-26	15-Oct-26	03-Nov-26	52,996.86	0.00	52,996.86	-41
MLTX-02-005-CN-1	Phenolic Partitions for Toilets	11	100%	0%	27-Aug-26	08-Sep-26	15-Oct-26	27-Oct-26	31,197.60	0.00	31,197.60	-41
MLTX-02-005-CN-1	Glass Partitions including all accessories and doors	6	100%	0%	09-Sep-26	15-Sep-26	28-Oct-26	03-Nov-26	13,649.02	0.00	13,649.02	-41
MLTX-02-005-CN-1	Granite Capping for Parpet	2	100%	0%	16-Aug-26	17-Aug-26	15-Oct-26	17-Oct-26	8,150.24	0.00	8,150.24	-51
SPECIALTIES WORK		30	100%	0%	22-Aug-26	24-Sep-26	11-Oct-26	14-Nov-26	58,495.83	0.00	58,495.83	-43
MLTX-02-005-CN-141	Sanitary Fixtures and Accessories Works	4	100%	0%	22-Aug-26	25-Aug-26	11-Oct-26	14-Oct-26	14,623.96	0.00	14,623.96	-42
MLTX-02-005-CN-141	Installation of MODON Logo on the entrance	5	100%	0%	19-Sep-26	24-Sep-26	09-Nov-26	14-Nov-26	19,498.61	0.00	19,498.61	-43
MLTX-02-005-CN-145	Installation of Phenolic Locker	2	100%	0%	09-Sep-26	10-Sep-26	28-Oct-26	29-Oct-26	24,373.26	0.00	24,373.26	-41
TESTING & COMMISSIONING		49	0%	0%	15-Oct-26	29-Dec-26	20-Feb-27	21-Apr-27	0.00	0.00	0.00	-93
MLTX-02-005-TC-11920	Testing and Commissioning for MEP Works for Playground	5	0%	0%	25-Nov-26	30-Nov-26	17-Apr-27	21-Apr-27	0.00	0.00	0.00	-118
MLTX-02-005-TC-11930	Testing and Commissioning for MEP Works for Toilet/Service	6	0%	0%	15-Oct-26	21-Oct-26	20-Feb-27	27-Feb-27	0.00	0.00	0.00	-109

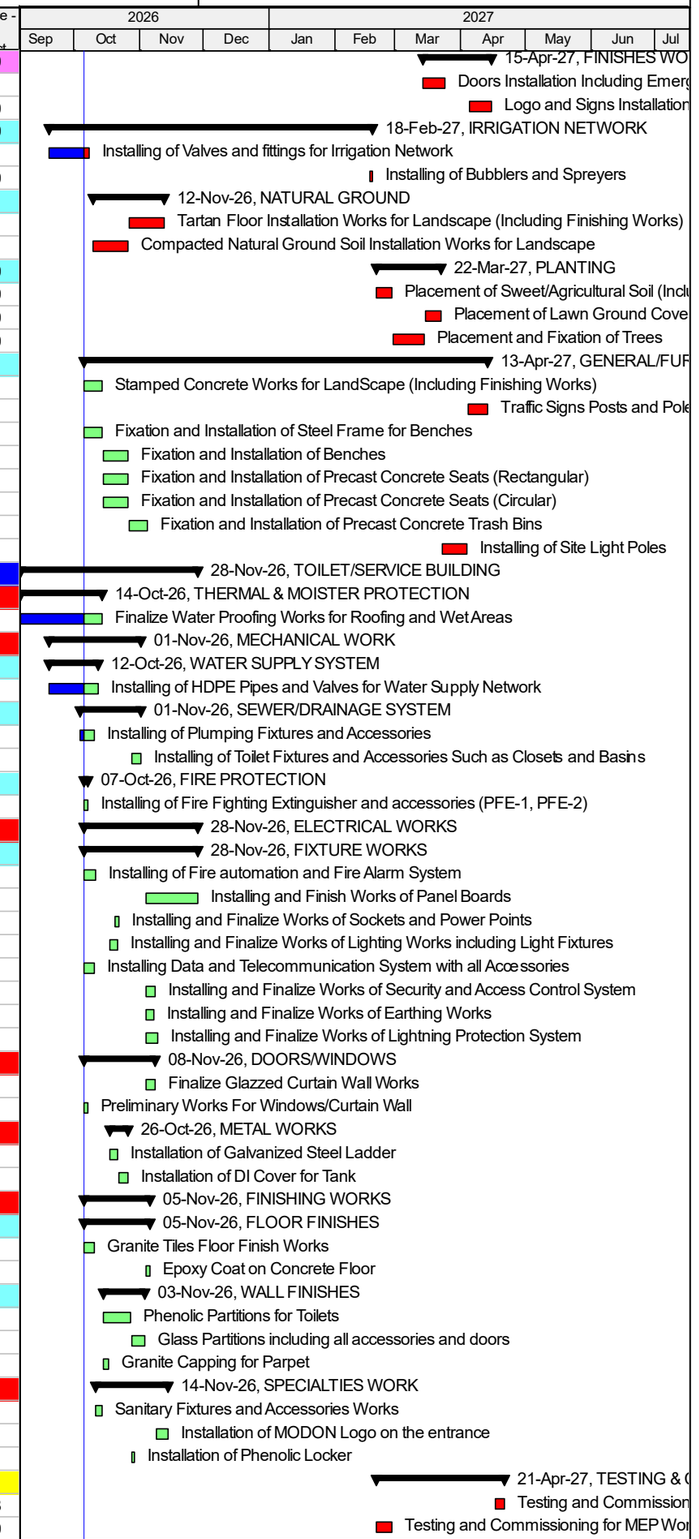

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary


TASK filter: Remaining works.

© Oracle Corporation

MLTX-02-005 - Playground Initiative for Eastern Region (Arar-Hasa osis -Dammam)

Remaining work
D.D 05-10-2026

Activity ID	Activity Name	Original Duration	Schedule % Complete	Performance % Complete	BL Project Start	BL Project Finish	Start	Finish	Planned Value Cost	Earned Value Cost	Budgeted Total Cost	Variance - BL Project
MLTX-02-005-TC-11940	Testing and Commissioning for MEP Works for Landscape	5	0%	0%	24-Dec-26	29-Dec-26	08-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
PROJECT CLOSEOUT & DEMOBILIZATION		18	0%	0%	24-Dec-26	02-Jan-27	08-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
As-Built DWGs		17	0%	0%	24-Dec-26	31-Dec-26	08-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
As-Built DWGs Submittals		14	0%	0%	24-Dec-26	28-Dec-26	08-Apr-27	24-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1200(	As-Built DWGs Submittal for Playground Area Works	2	0%	0%	27-Dec-26	28-Dec-26	22-Apr-27	24-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1201(	As-Built DWGs Submittal for Toilet/Service Building Works	2	0%	0%	24-Dec-26	26-Dec-26	08-Apr-27	10-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1202(	As-Built DWGs Submittal for Landscape Works	2	0%	0%	24-Dec-26	26-Dec-26	08-Apr-27	10-Apr-27	0.00	0.00	0.00	-86
As-Built DWGs Approvals		15	0%	0%	27-Dec-26	31-Dec-26	11-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1204(	As-Built DWGs Approval for Playground Area Works	3	0%	0%	29-Dec-26	31-Dec-26	25-Apr-27	27-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-1205(	As-Built DWGs Approval for Toilet/Service Building Works	3	0%	0%	27-Dec-26	29-Dec-26	11-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
MLTX-02-005-CO-1206(	As-Built DWGs Approval for Landscape Works	3	0%	0%	27-Dec-26	29-Dec-26	11-Apr-27	13-Apr-27	0.00	0.00	0.00	-86
Demobilization		4	0%	0%	30-Dec-26	02-Jan-27	25-Apr-27	28-Apr-27	0.00	0.00	0.00	-96
MLTX-02-005-CO-12080	Demobilization of Manpower	1	0%	0%	30-Dec-26	30-Dec-26	25-Apr-27	25-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12090	Removal of Equipment from Site	1	0%	0%	30-Dec-26	30-Dec-26	25-Apr-27	25-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12100	Site Clean Up	1	0%	0%	31-Dec-26	31-Dec-26	26-Apr-27	26-Apr-27	0.00	0.00	0.00	-95
MLTX-02-005-CO-12110	Restoration of Ground Surfaces	1	0%	0%	02-Jan-27	02-Jan-27	28-Apr-27	28-Apr-27	0.00	0.00	0.00	-96

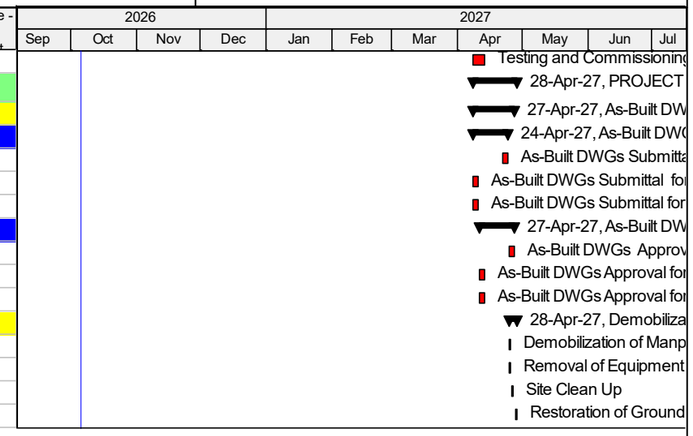

© Oracle Corporation
