PROGRESS PLAN

MODON مدن

egis

Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City

Current Date : 09/08/2026

6


الرواف للمقاولات
ALRAWAF CONTRACTING

Asphalt

scope of work.

Progress Legend

	Excavation (Orange)
	Embankment (Purple)
	Final Embankment (Red)
	Sub Grade (Yellow)
	Aggregate Base Course (Green)
	BWC (Black)

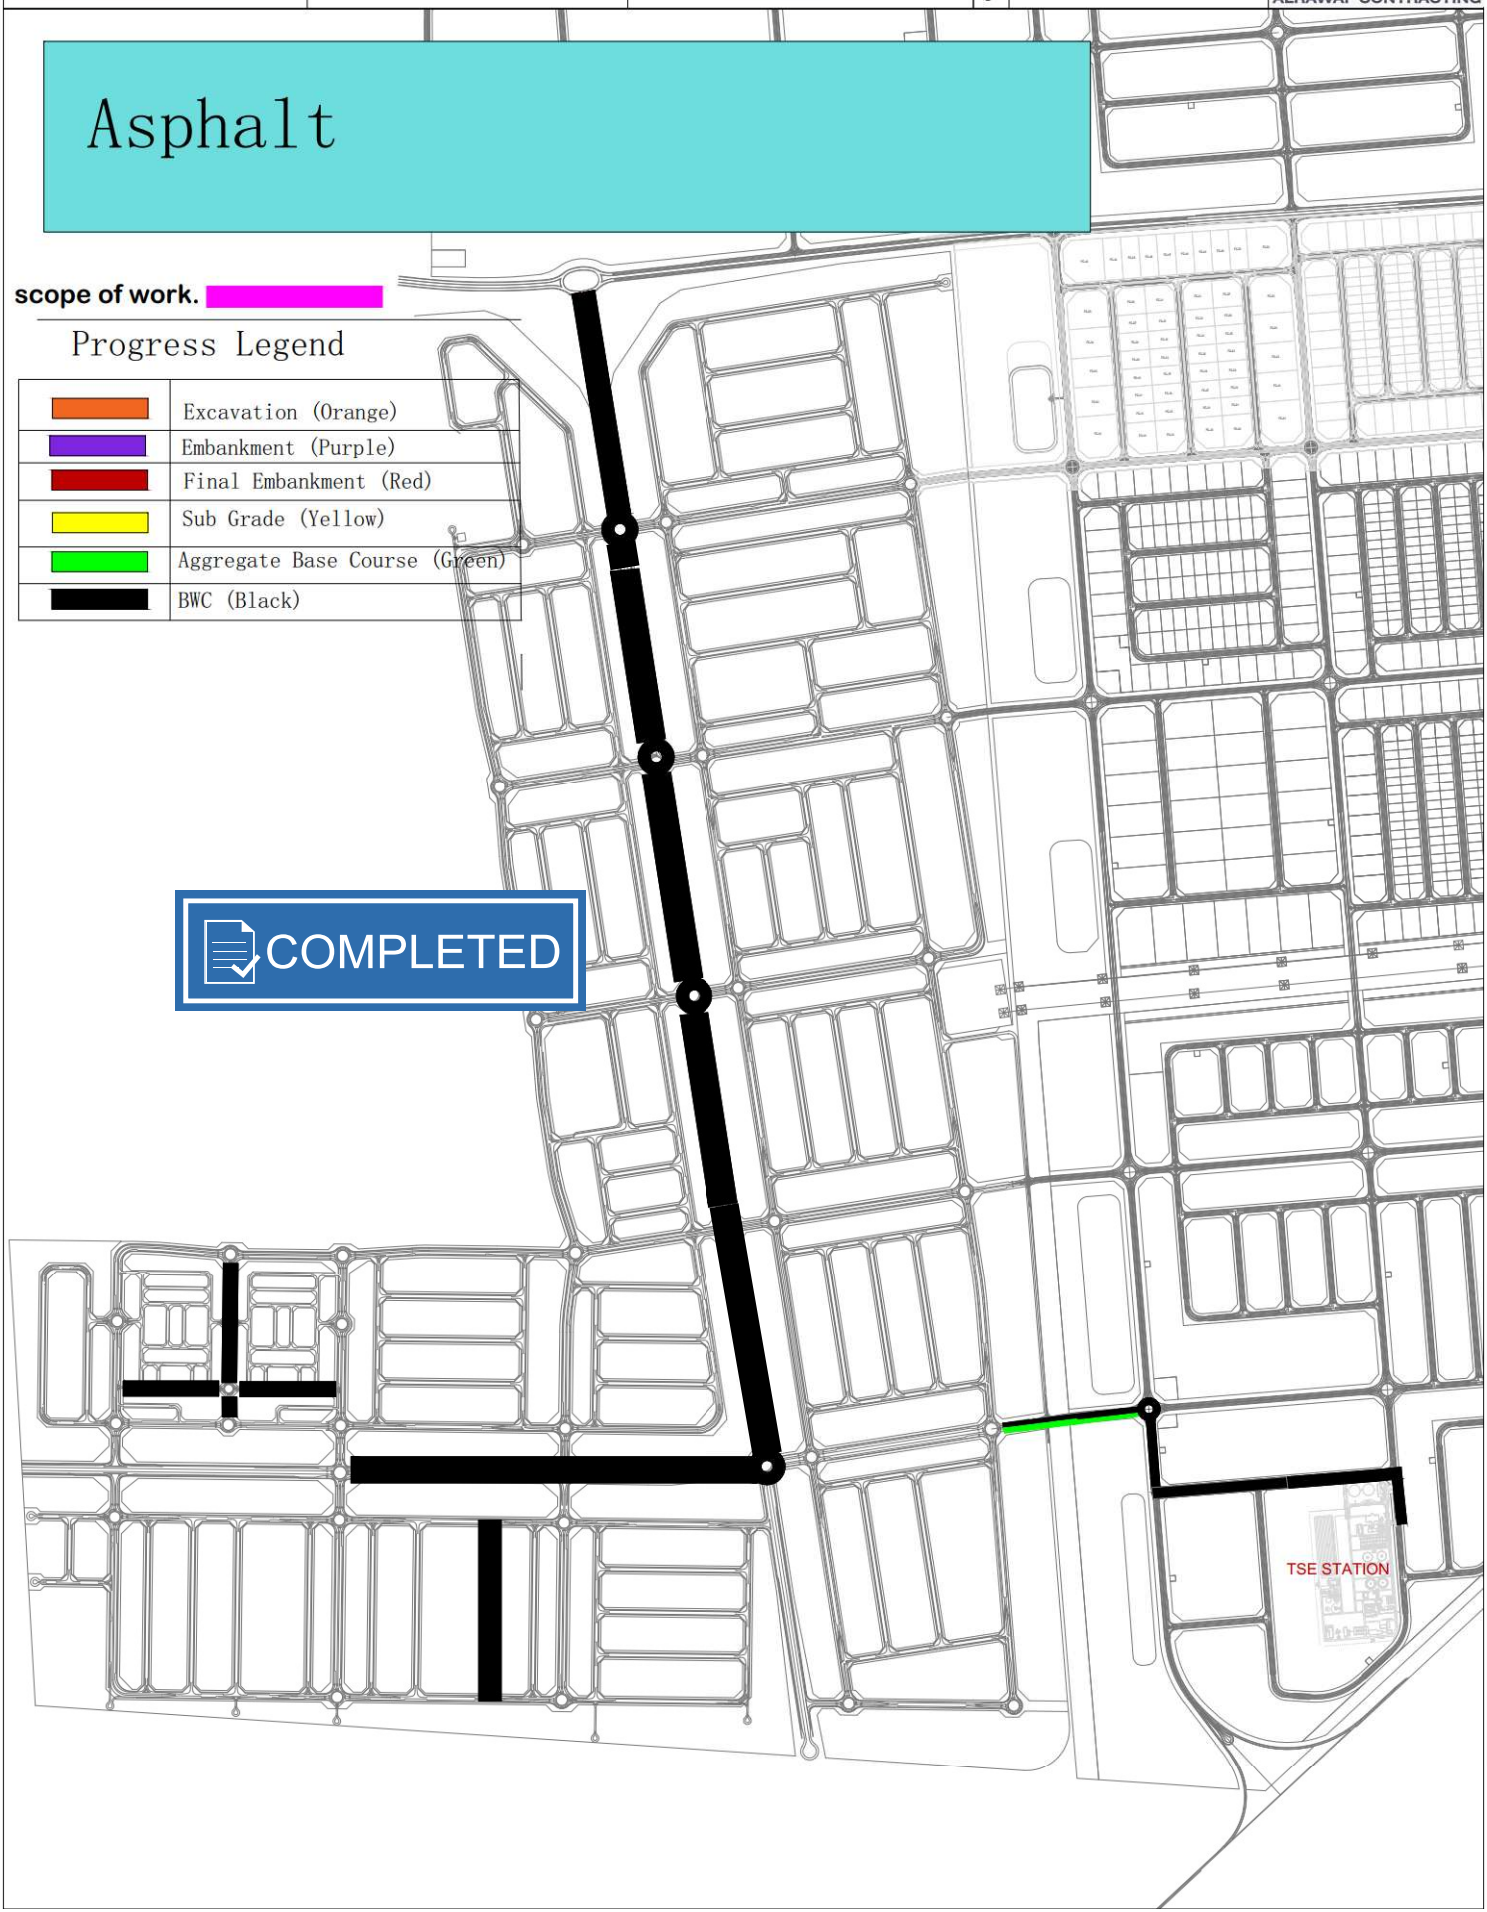

PROGRESS PLAN

MODON مدن — Saudi Authority for Industrial Cities and Technology Zones | egis | Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City | Current Date : 09/08/2026 | 10 | الرواف للمقاولات ALRAWAF CONTRACTING


Kerbstone

scope of work

Progress Legend

	Excavation (orange)
	lean concrete (red)
	Installation (blue)
	Backing (grey)

Kerbstone	
total	43,192
Excavated	42,841
installed	42,635
Remaining	557

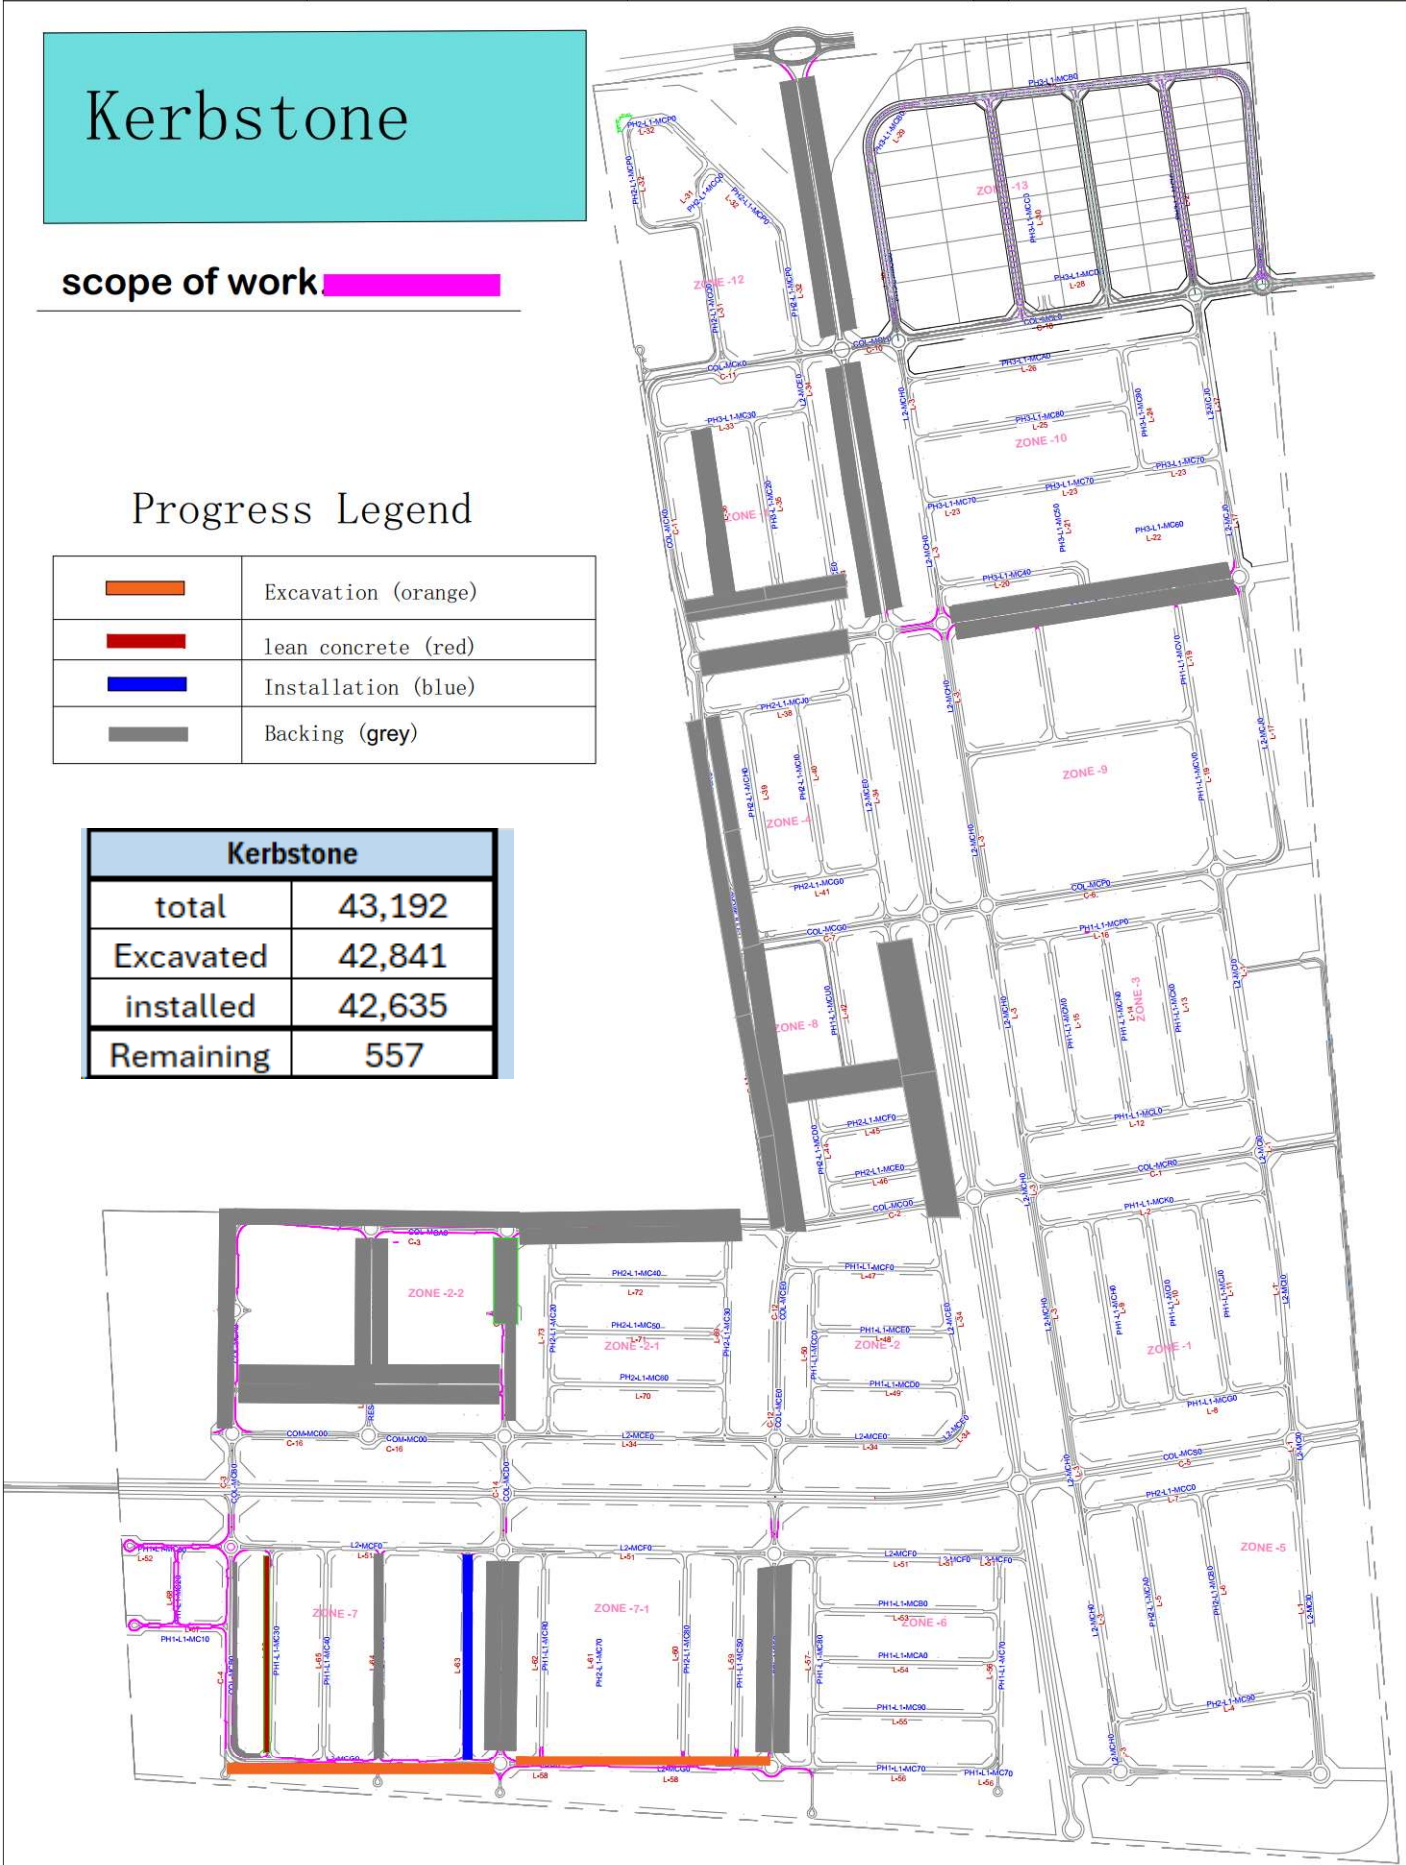


Interlock

Scope of work

Progress Legend

	Excavation (orange)
	Bedding (red)
	Subgrade (blue)
	Installation (grey)

COMPLETED

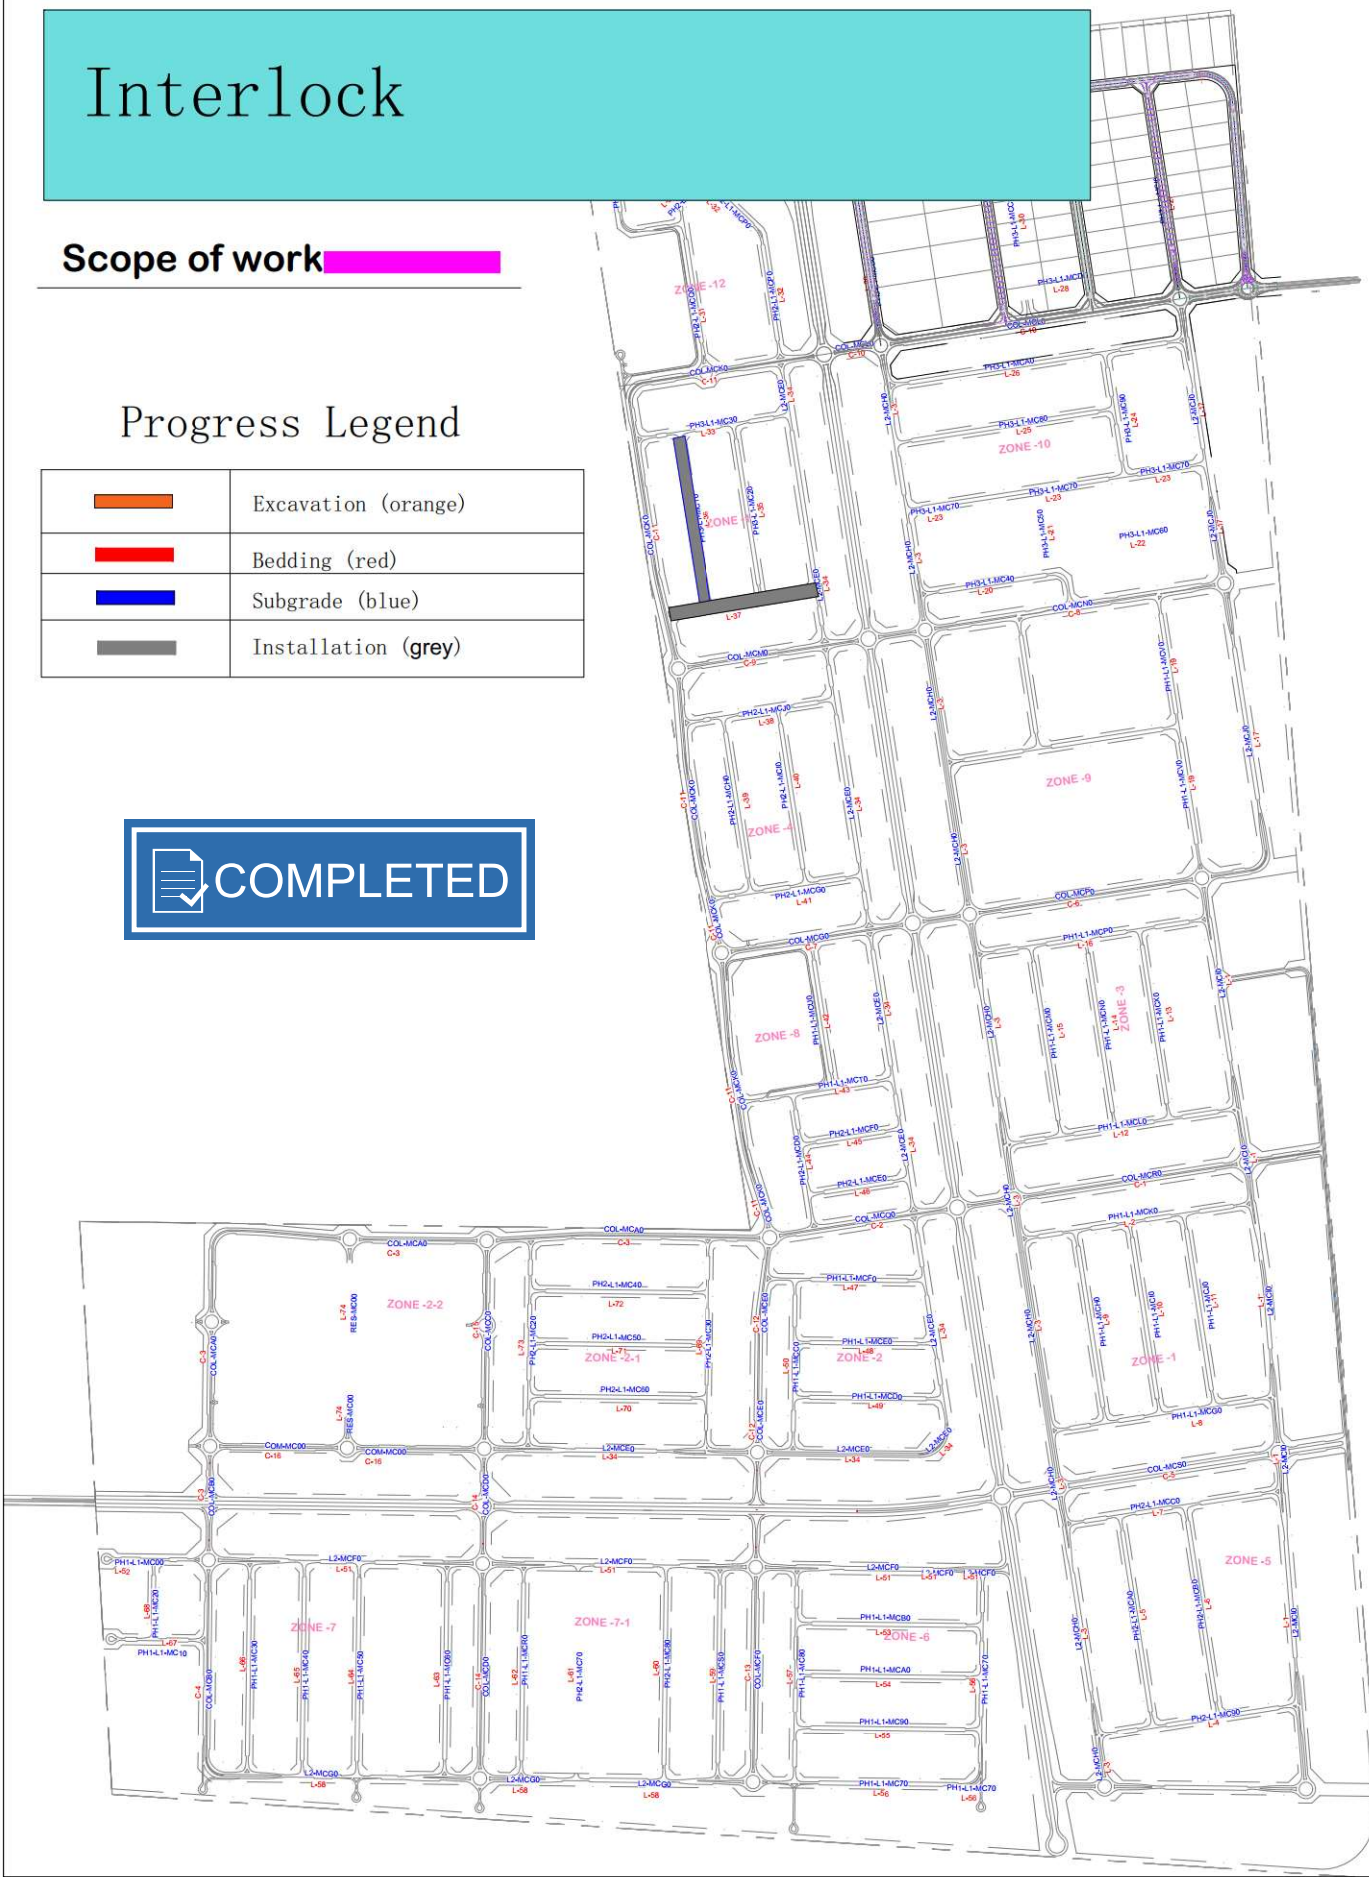


Storm network

scope of work.

Progress Legend

	Excavation (orange)
	Bedding (red)
	Pipe Installation (blue)
	Testing (Grey)
	Backfilling (black)
	Manhole (Green)

COMPLETED

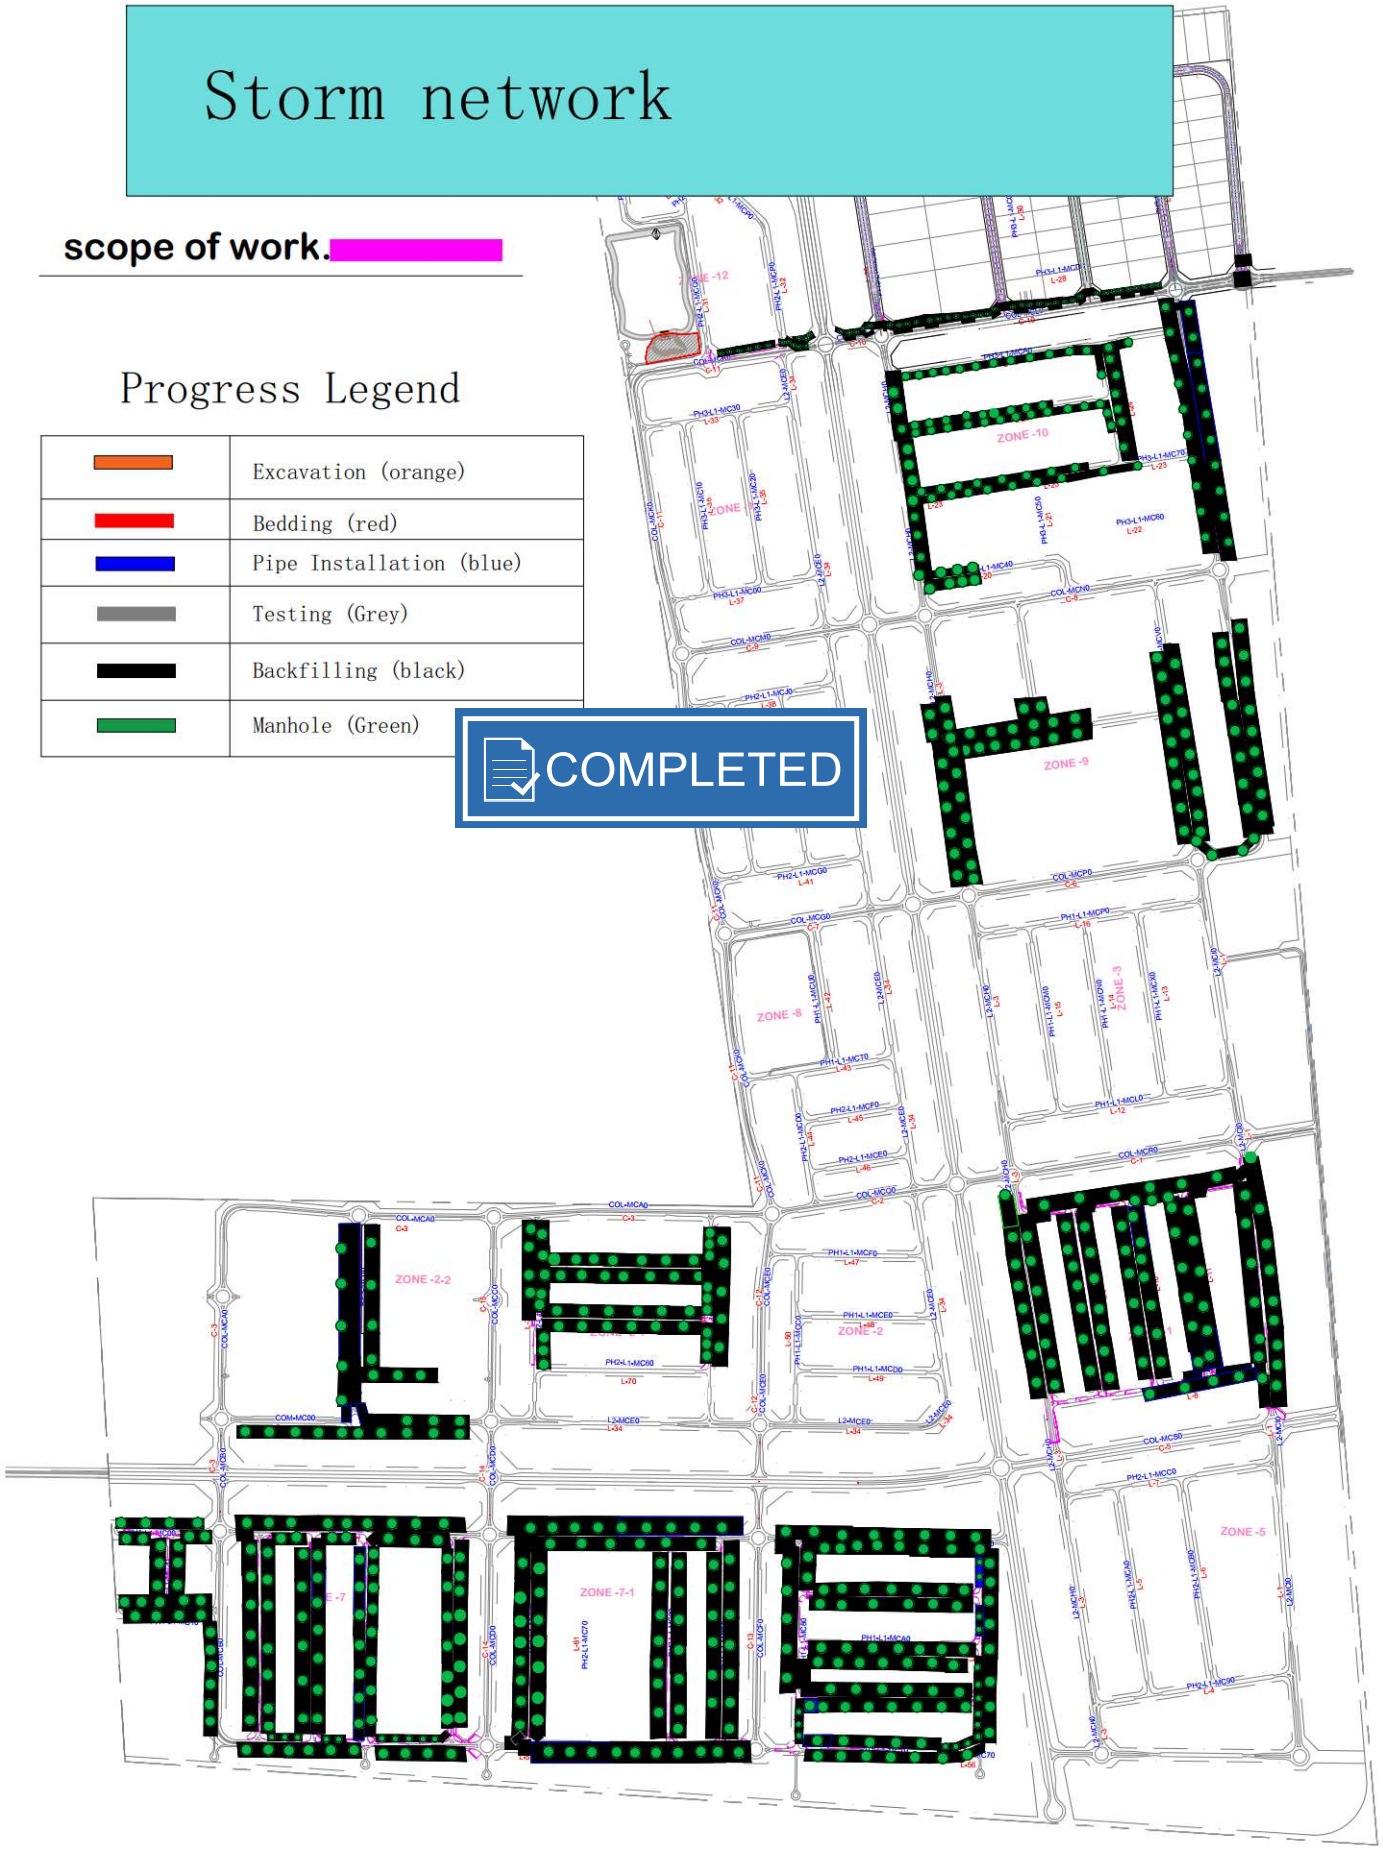

PROGRESS PLAN

MODON مدن

egis

Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City

Current Date : 09/08/2026

3-1

الرواف للمقاولات
ALRAWAF CONTRACTING

Storm CB network


scope of work.

Progress Legend

	Excavation (orange)
	Bedding (red)
	CH installation (Green)

Catch Basin Pipes	
total	39,257
Excavated	34,407
installed	33,185
Remaining	6,071

Catch Basin Precast	
total	1,888
Excavated	1,712
installed	1,651
Remaining	246

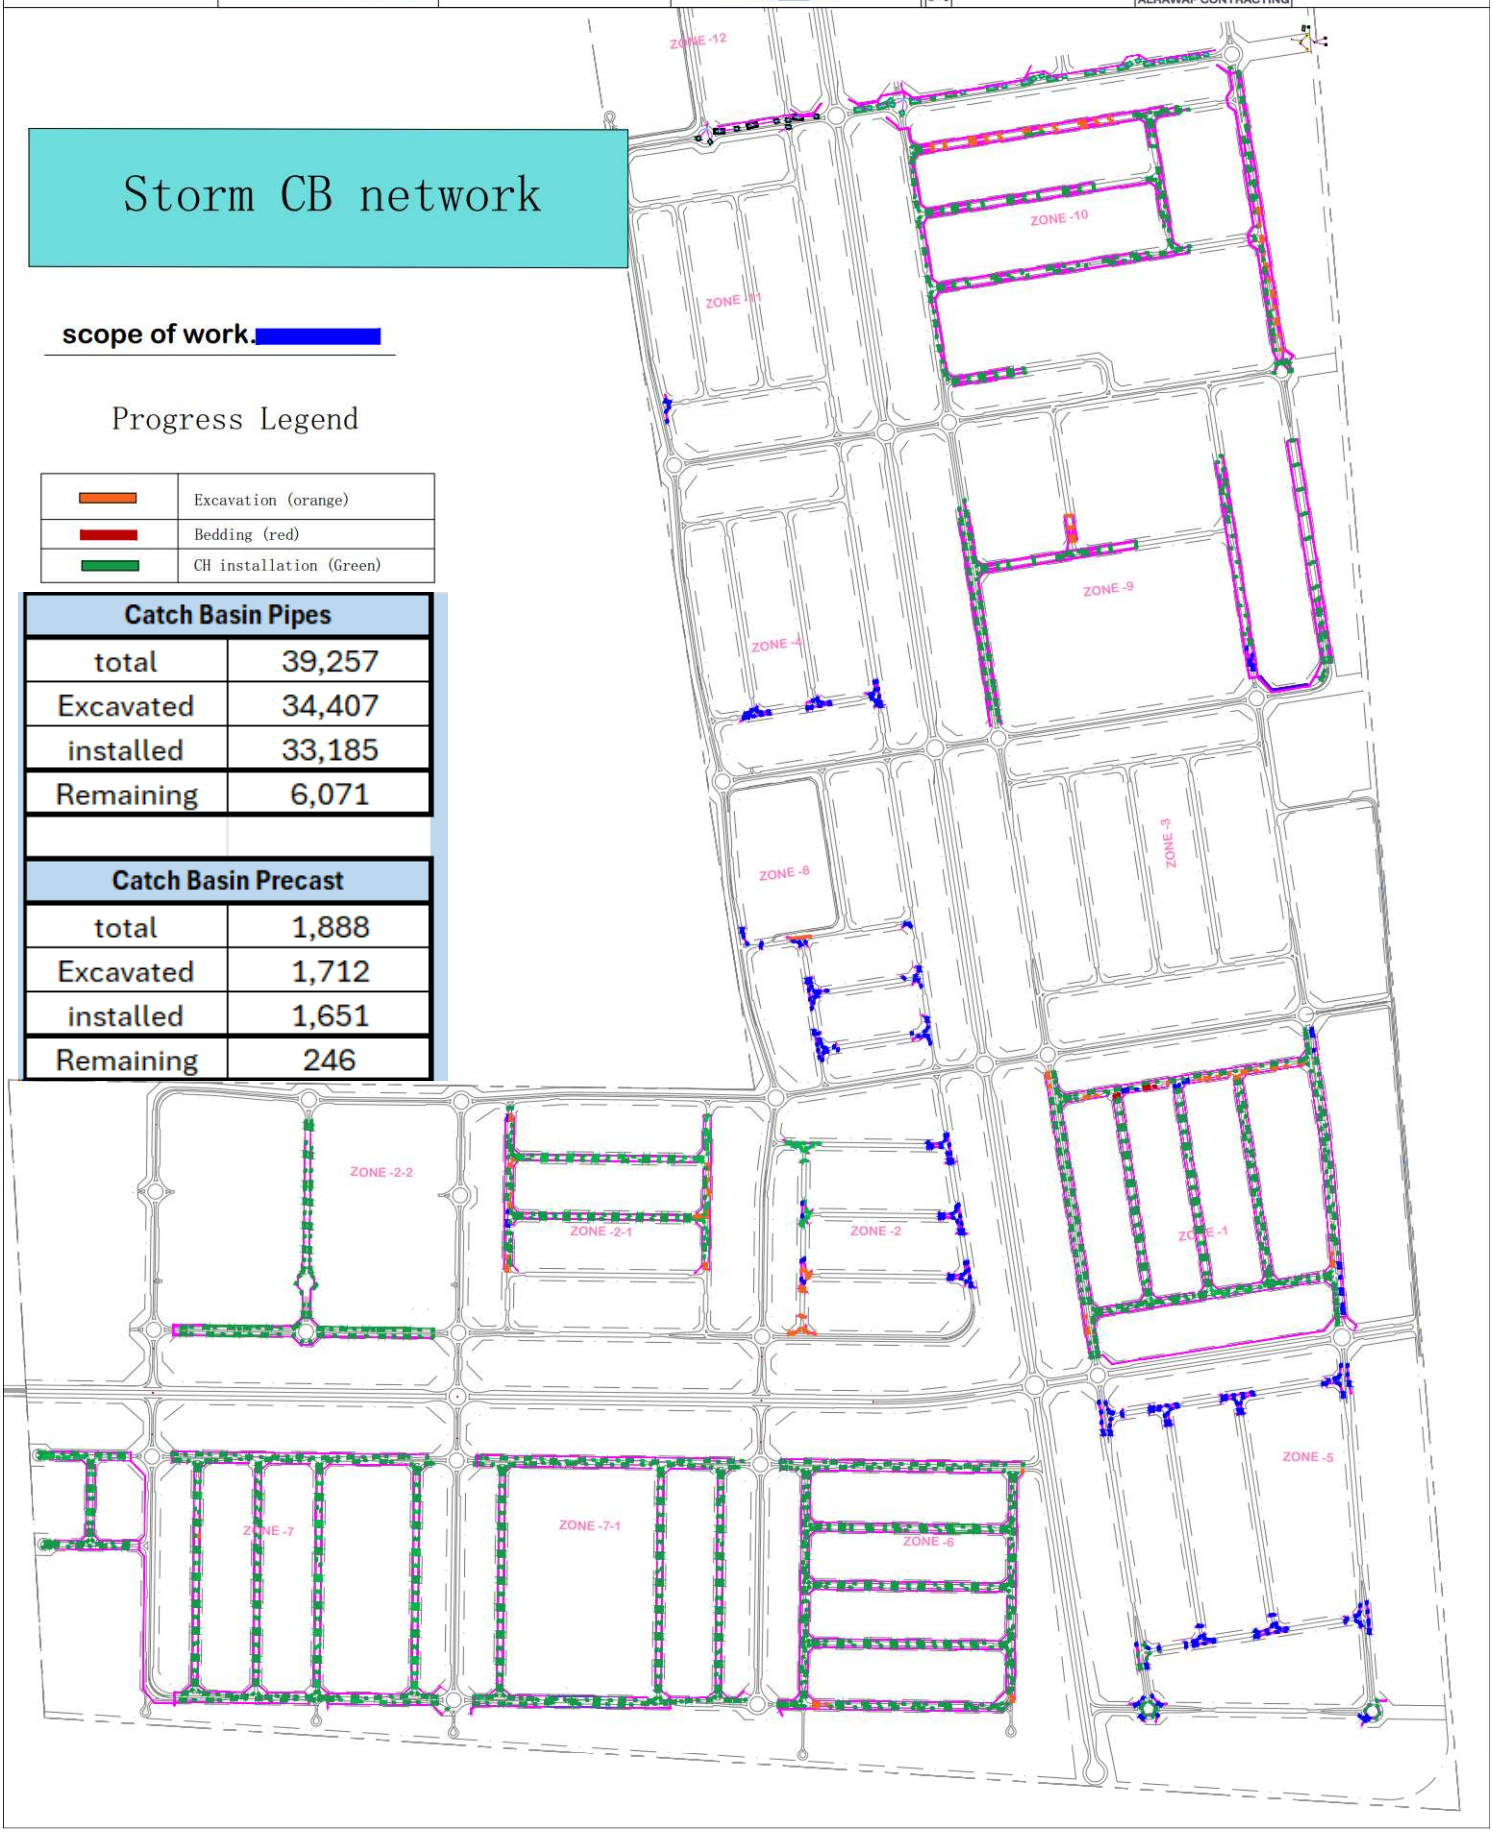

PROGRESS PLAN

MODON مدن	egis	Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City	Current Date : 09/08/2026

الرواف للمقاولات ALRAWAF CONTRACTING

open Channel for Storm network

scope of work

Progress Legend

	Excavation (orange)
	Compaction (black)
	Riprap (Green)

COMPLETED



PROGRESS PLAN

MODON مدن — egis — Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City — Current Date : 09/08/2026 — 5 — الرواف للمقاولات ALRAWAF CONTRACTING


Sewer network

scope of work

Progress Legend

	Excavation (orange)
	Bedding (red)
	Pipe Installation (blue)
	Testing (Grey)
	Backfilling (black)
	Manhole (Green)

COMPLETED

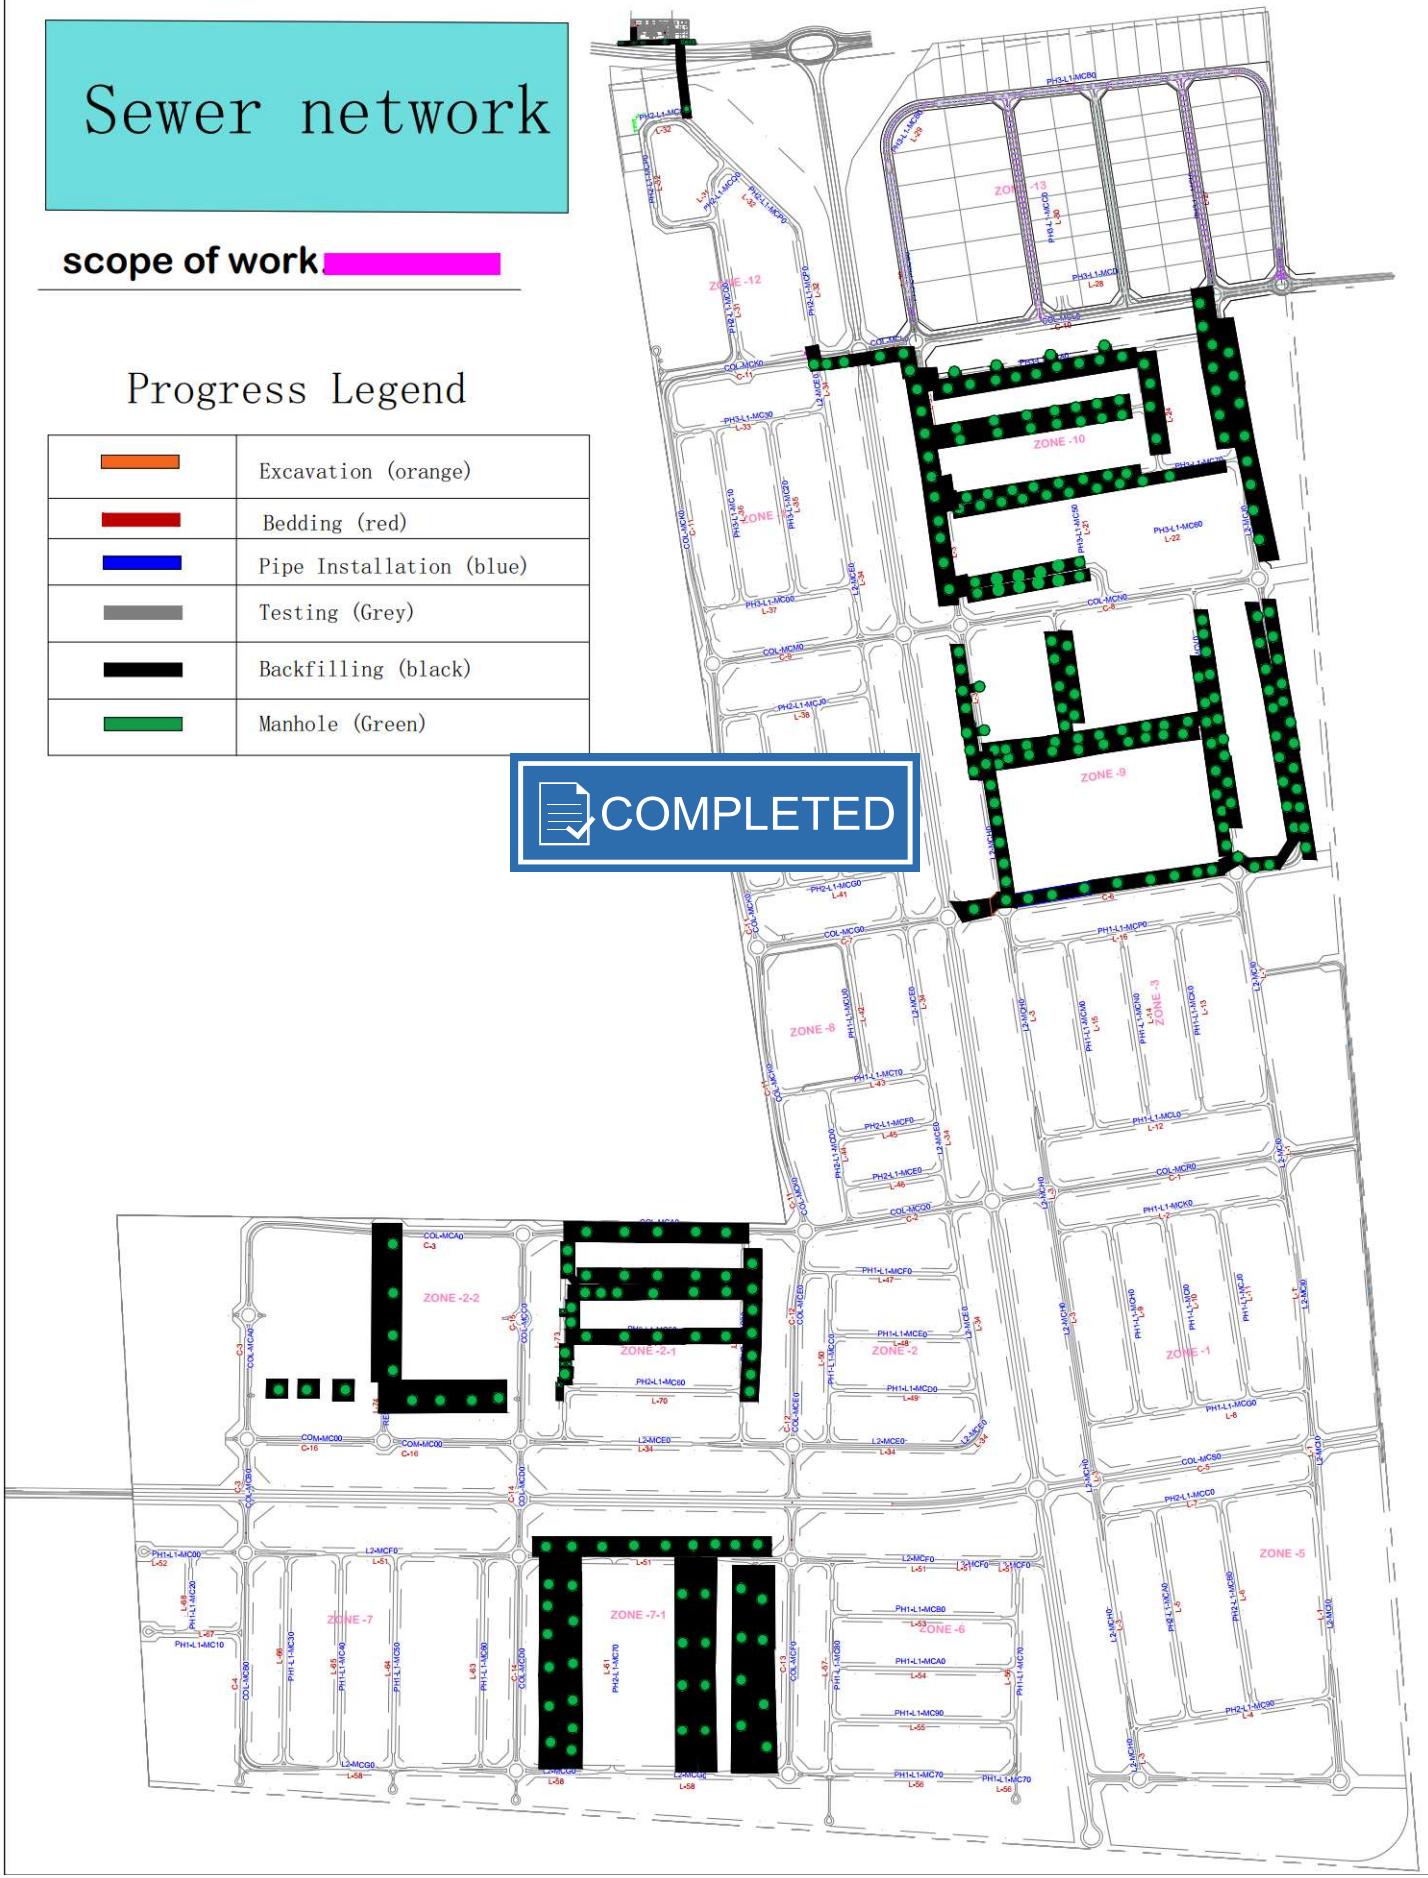

PROGRESS PLAN

MODON مدن — egis — Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City — Current Date : 09/08/2026 — 9 — الرواف للمقاولات ALRAWAF CONTRACTING

Water network

scope of work.

Progress Legend

	Excavation (orange)
	Bedding (red)
	Pipe Installation (blue)
	Testing (Grey)
	Backfilling (black)

COMPLETED



PROGRESS PLAN

Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City

Current Date : 09/08/2026

9-1

Water Valve Chambers


scope of work.

Progress Legend

	Excavation (orange)
	lean concrete (red)
	Reinforcement Steel (blue)
	Concrete Pouring foundation (Purple)
	Mechanical Installation (Green)
	Concrete Pouring Wall & slap (Grey)
	Backfilling (Black)

	Air Valve
	Gate Valve
	Washout

COMPLETED

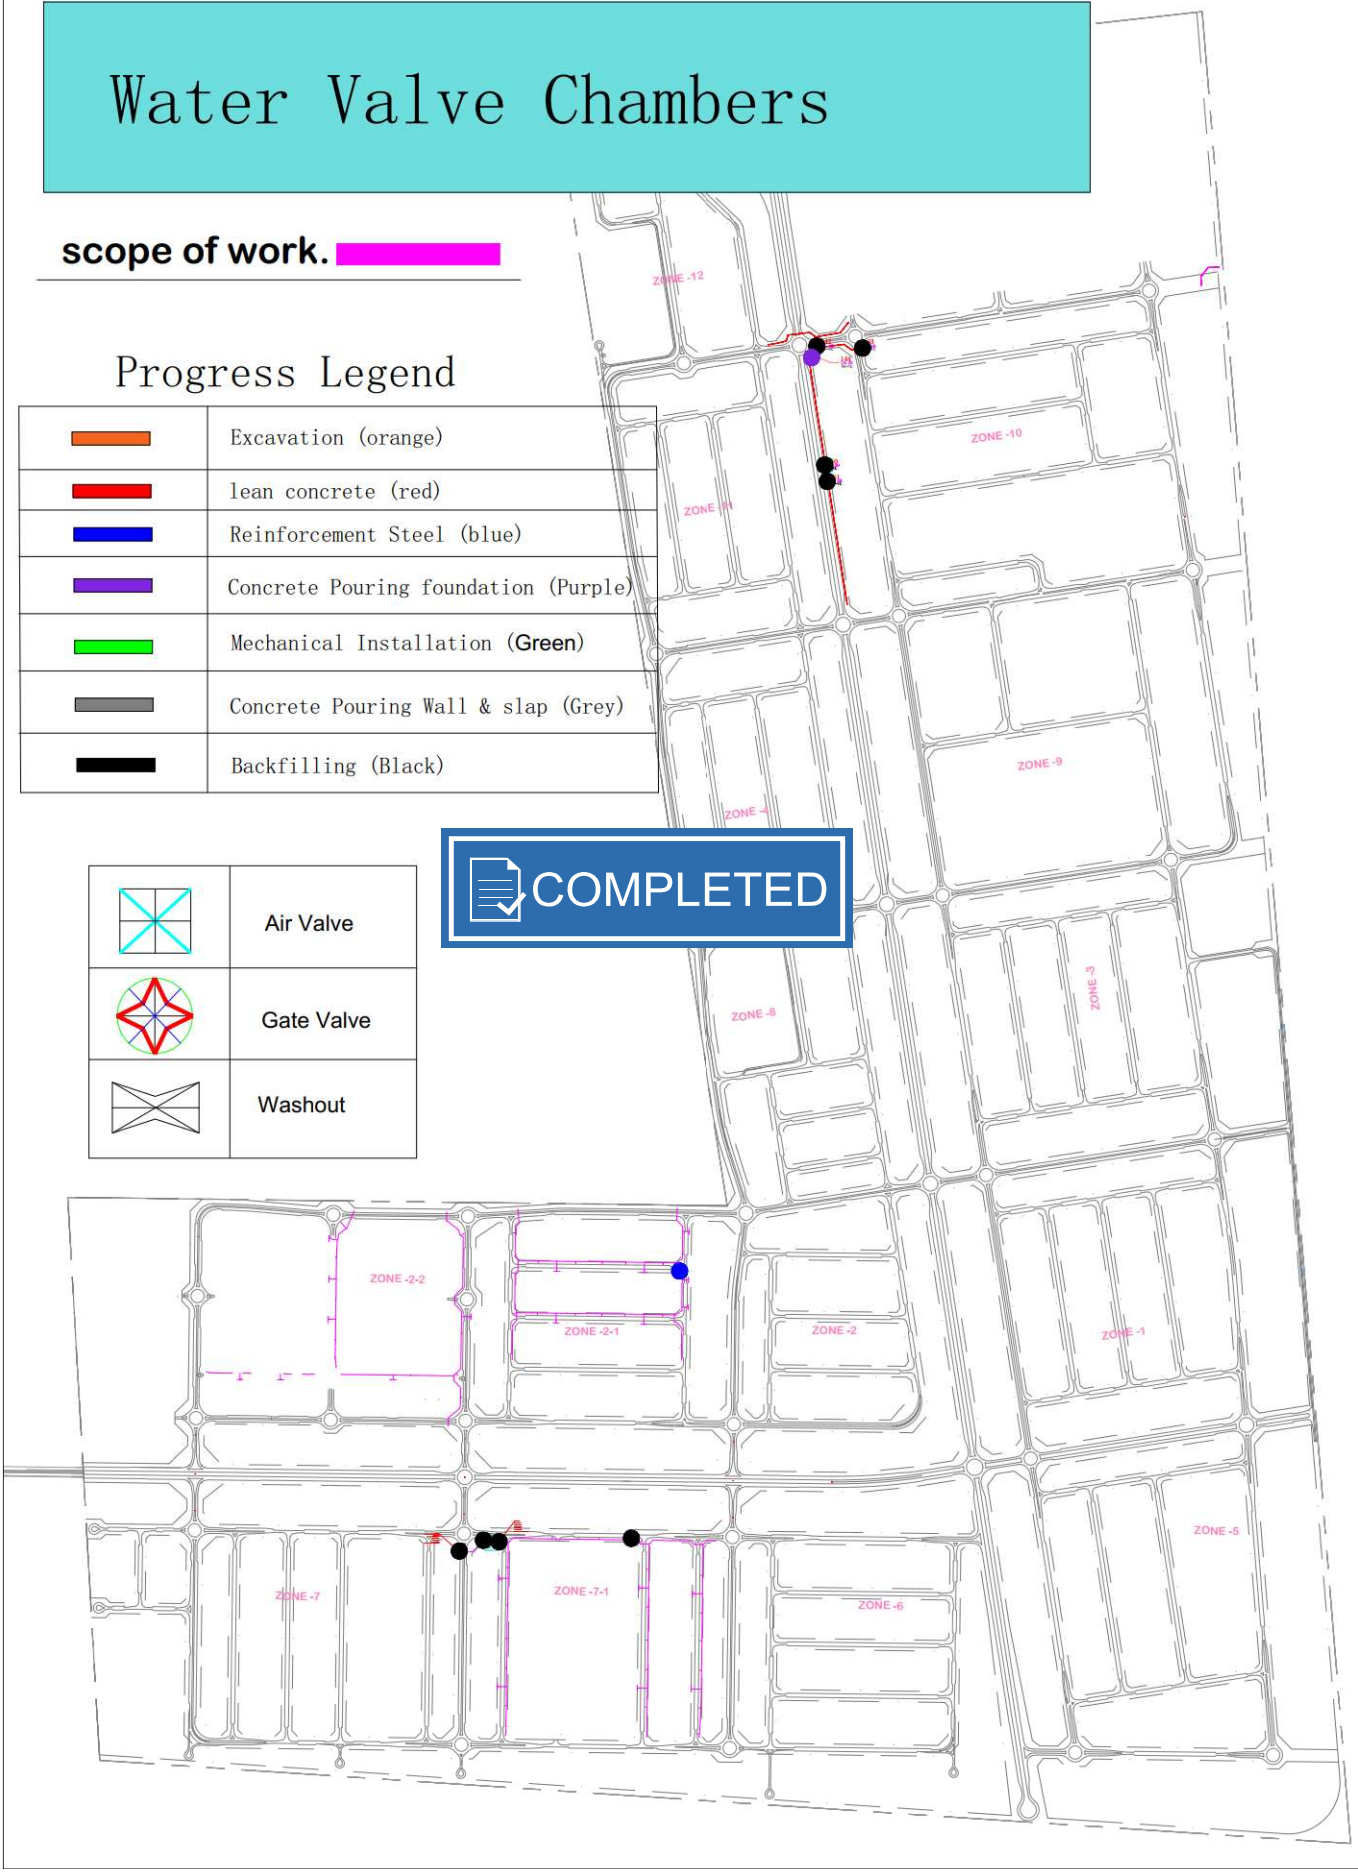

PROGRESS PLAN

MODON مدن
الهيئة السعودية للمدن الصناعية ومناطق التقنية
Saudi Authority for Industrial Cities and Technology Zones

egis

Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City

Current Date : 09/08/2026

الرواف للمقاولات
ALRAWAF CONTRACTING

Potable wAter Road crossing

COMPLETED



PROGRESS PLAN

MODON مدن — Saudi Authority for Industrial Cities and Technology Zones | egis | Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City | Current Date : 09/08/2026 | 12 | الرواف للمقاولات ALRAWAF CONTRACTING

Fire Hydrant

scope of work.

Progress Legend

	Excavation (orange)
	Bedding (red)
	Fire Hydrant installation (blue)
	Testing (Grey)
	Backfilling (black)

COMPLETED




Irrigation network

scope of work

Progress Legend

	Excavation (orange)
	Bedding (red)
	Pipe Installation (blue)
	Testing (Grey)
	Backfilling (black)

TSE Pipes	
total	68,627
Excavated	68,045
installed	67,994
Remaining	633

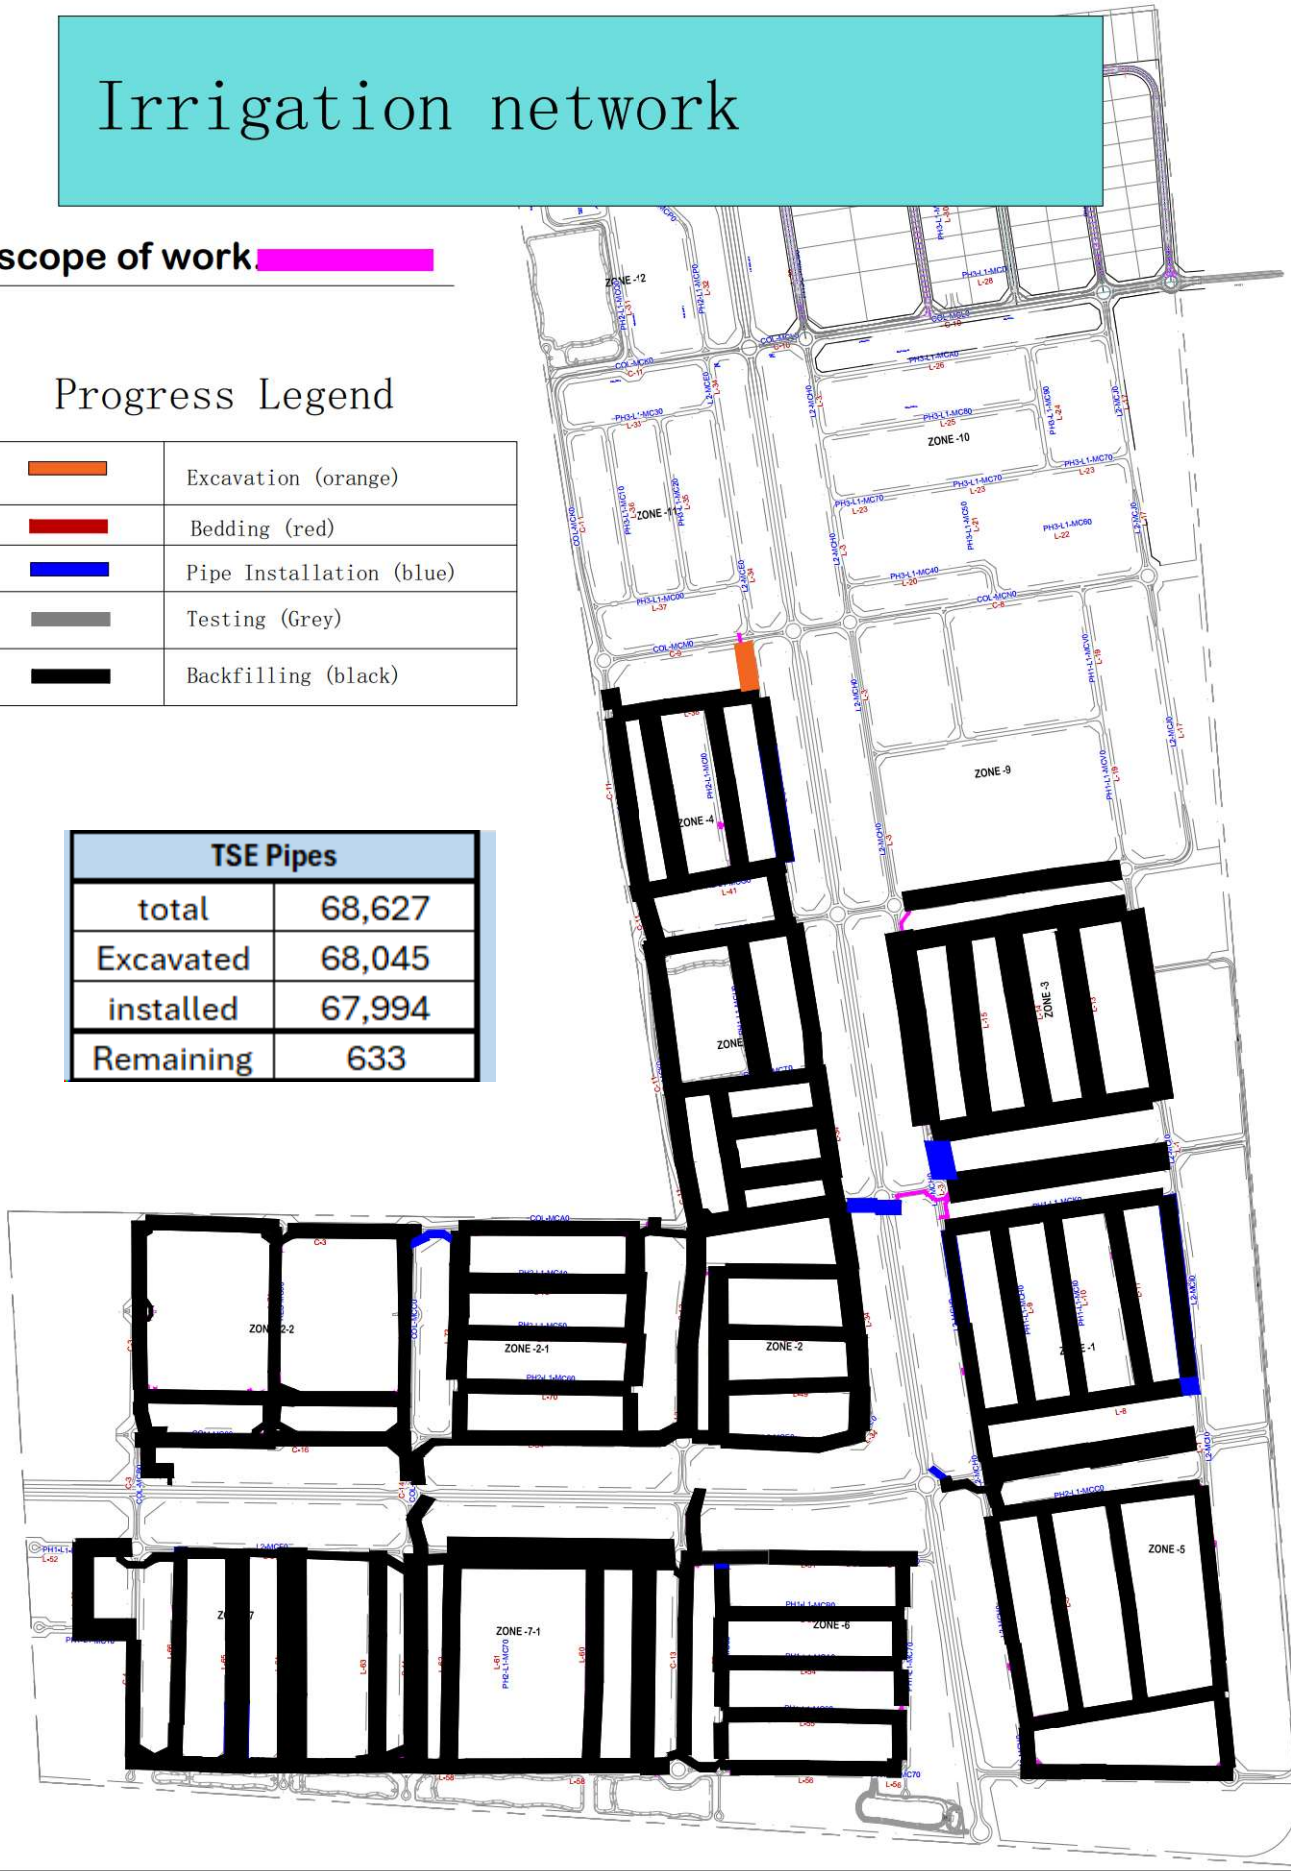

Irrigation Valve Chambers

scope of work

Progress Legend

	Excavation (orange)
	lean concrete (red)
	Reinforcement Steel (blue)
	Concrete Pouring foundation (Purple)
	Mechanical Installation (Green)
	Concrete Pouring Wall & slap (Grey)
	Backfilling (Black)

	Air Valve
	Gate Valve
	Washout



PROGRESS PLAN

MODON مدن	egis	Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City	Current Date : 09/08/2026


الرواف للمقاولات ALRAWAF CONTRACTING

TSE Road crossing

Total = 73

Excuted = 57

Remaining = 16

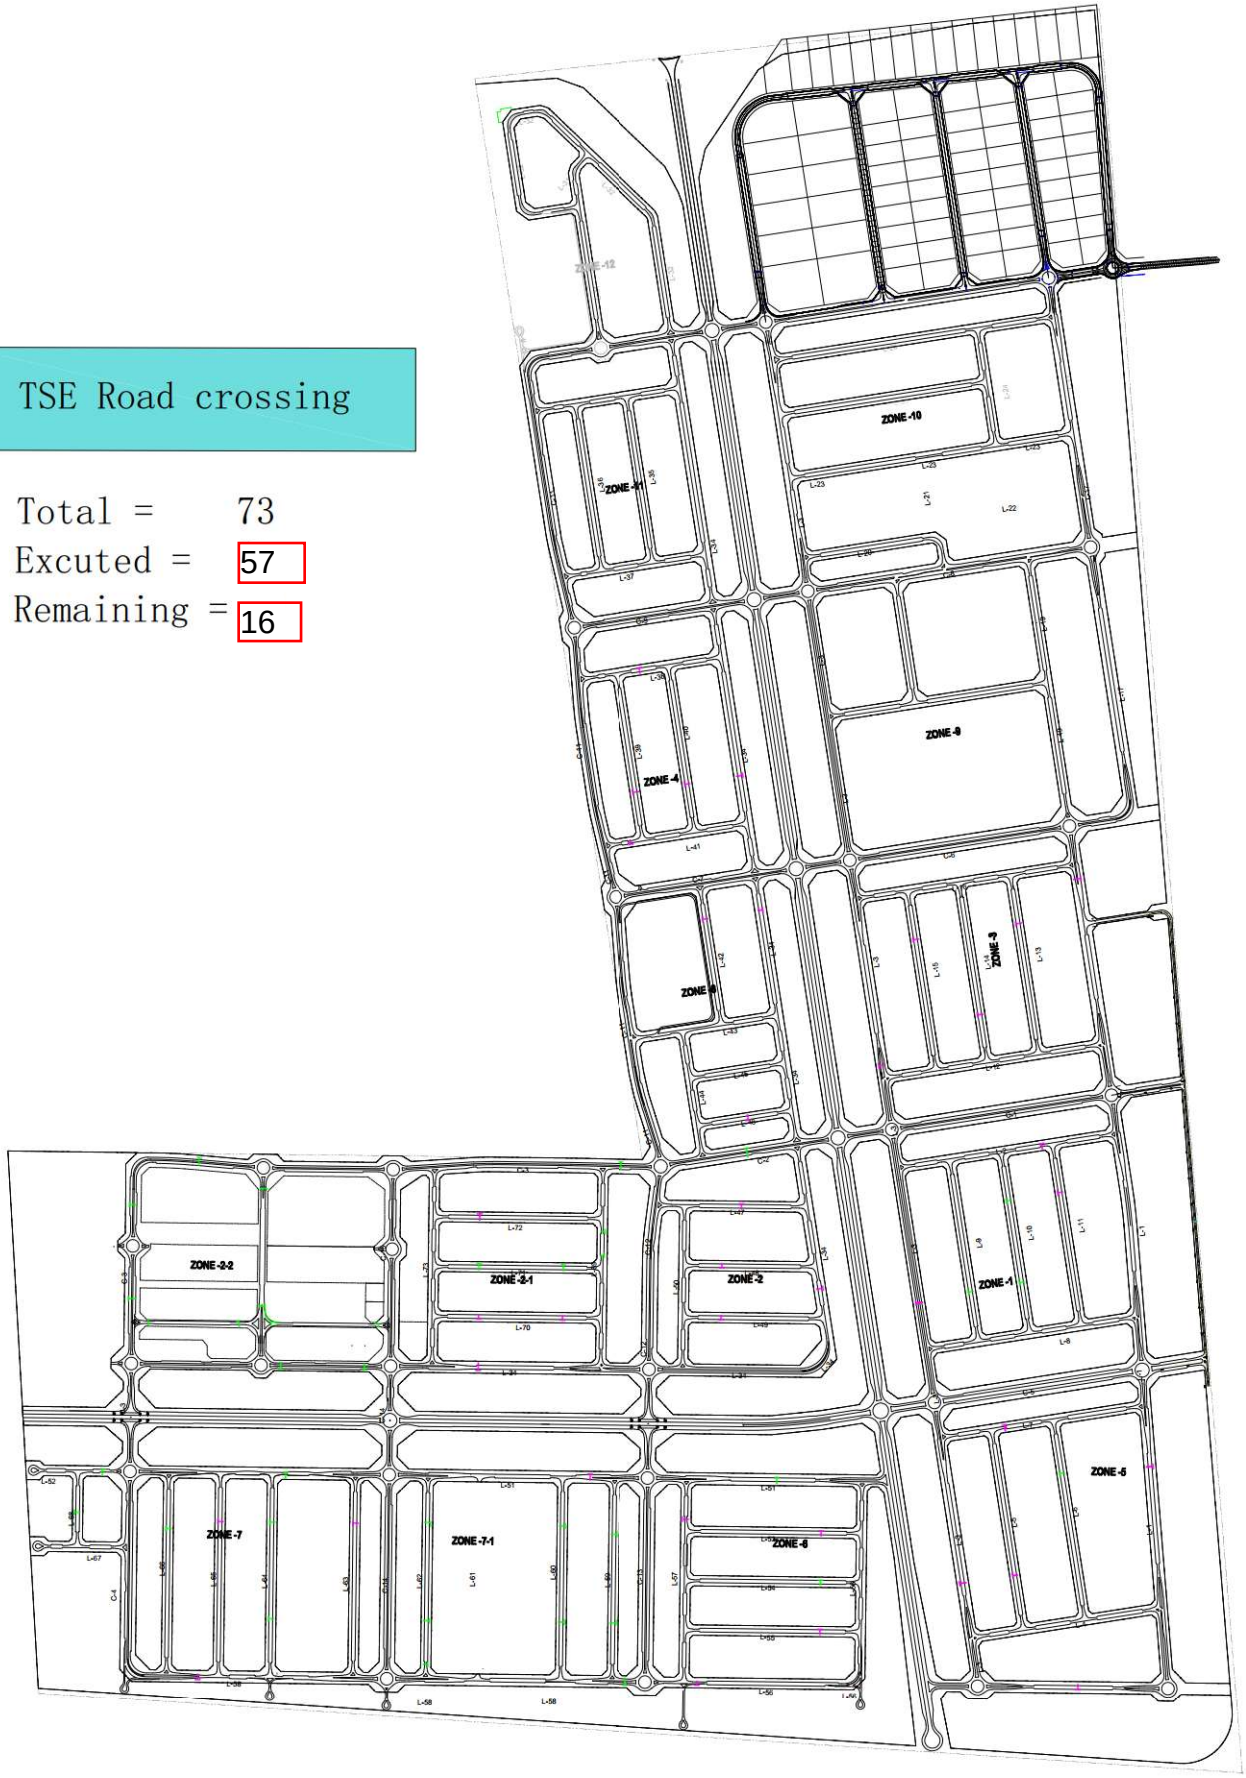

PROGRESS PLAN

MODON مدن	egis	Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City	Current Date : 09/08/2026 8	الرواف للمقاولات ALRAWAF CONTRACTING


Street Light network

scope of work

Progress Legend

	Excavation (orange)
	Bedding (red)
	Cables Installation (blue)
	Testing (Grey)
	Backfilling (black)
	Lightening Poles installation (Green)

COMPLETED

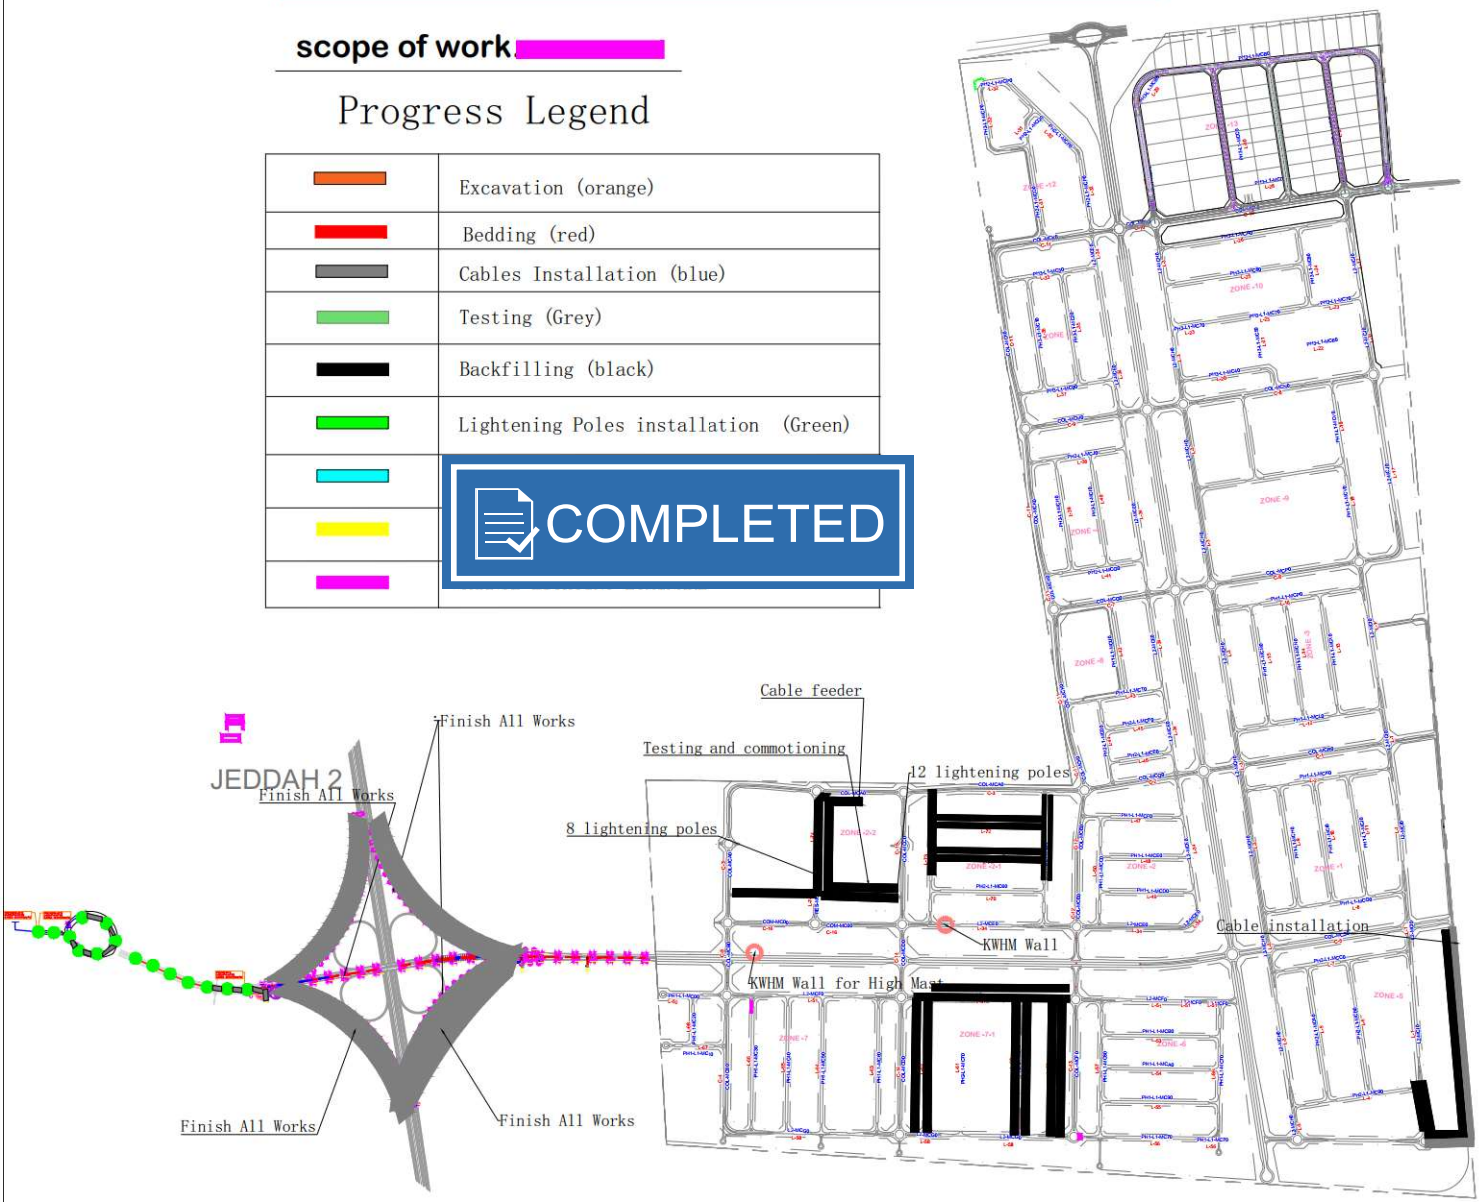

Telecom network

scope of work

Progress Legend

	Excavation (Orange)
	Bedding (Red)
	Duct Installation (Blue)
	Manhole (Green)
	BBC (Gray)
	BWC (Black)

COMPLETED



PROGRESS PLAN

MODON مدن — egis — Infrastructure Complete of Phase (1) For 3rd Industrial Jeddah City — Current Date : 09/08/2026 — 2 — الرواف للمقاولات ALRAWAF CONTRACTING


Box Culvert for Storm network

scope of work


Progress Legend

	Excavation (orange)
	lean concrete (red)
	Reinforcement (blue)
	Concrete Pouring foundation (Purple)
	Concrete Pouring Wall & slap (Grey)
	Backfilling (black)

COMPLETED

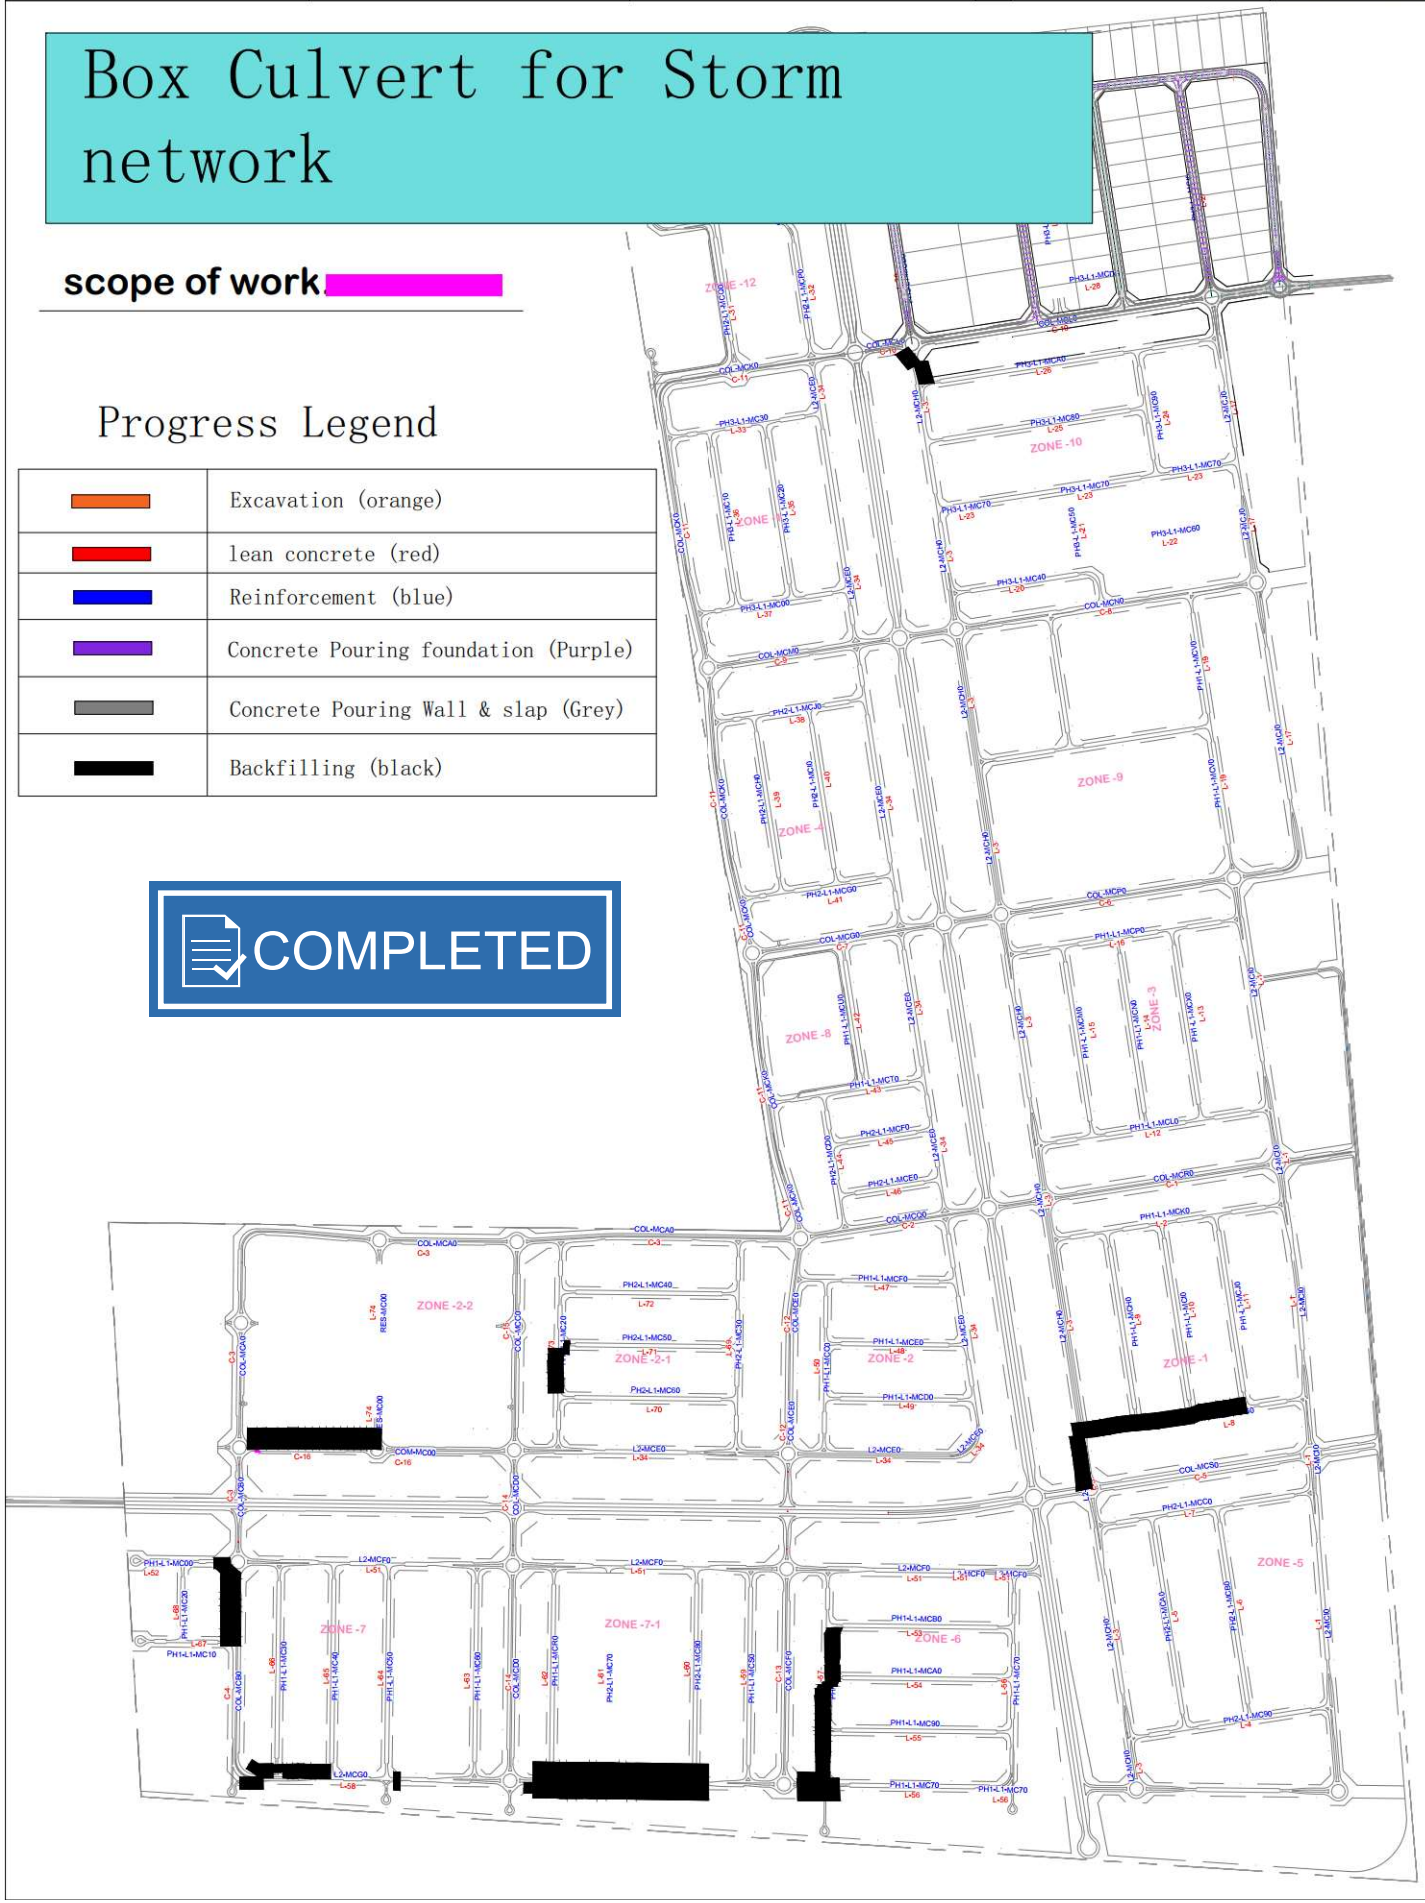

COMPLETED

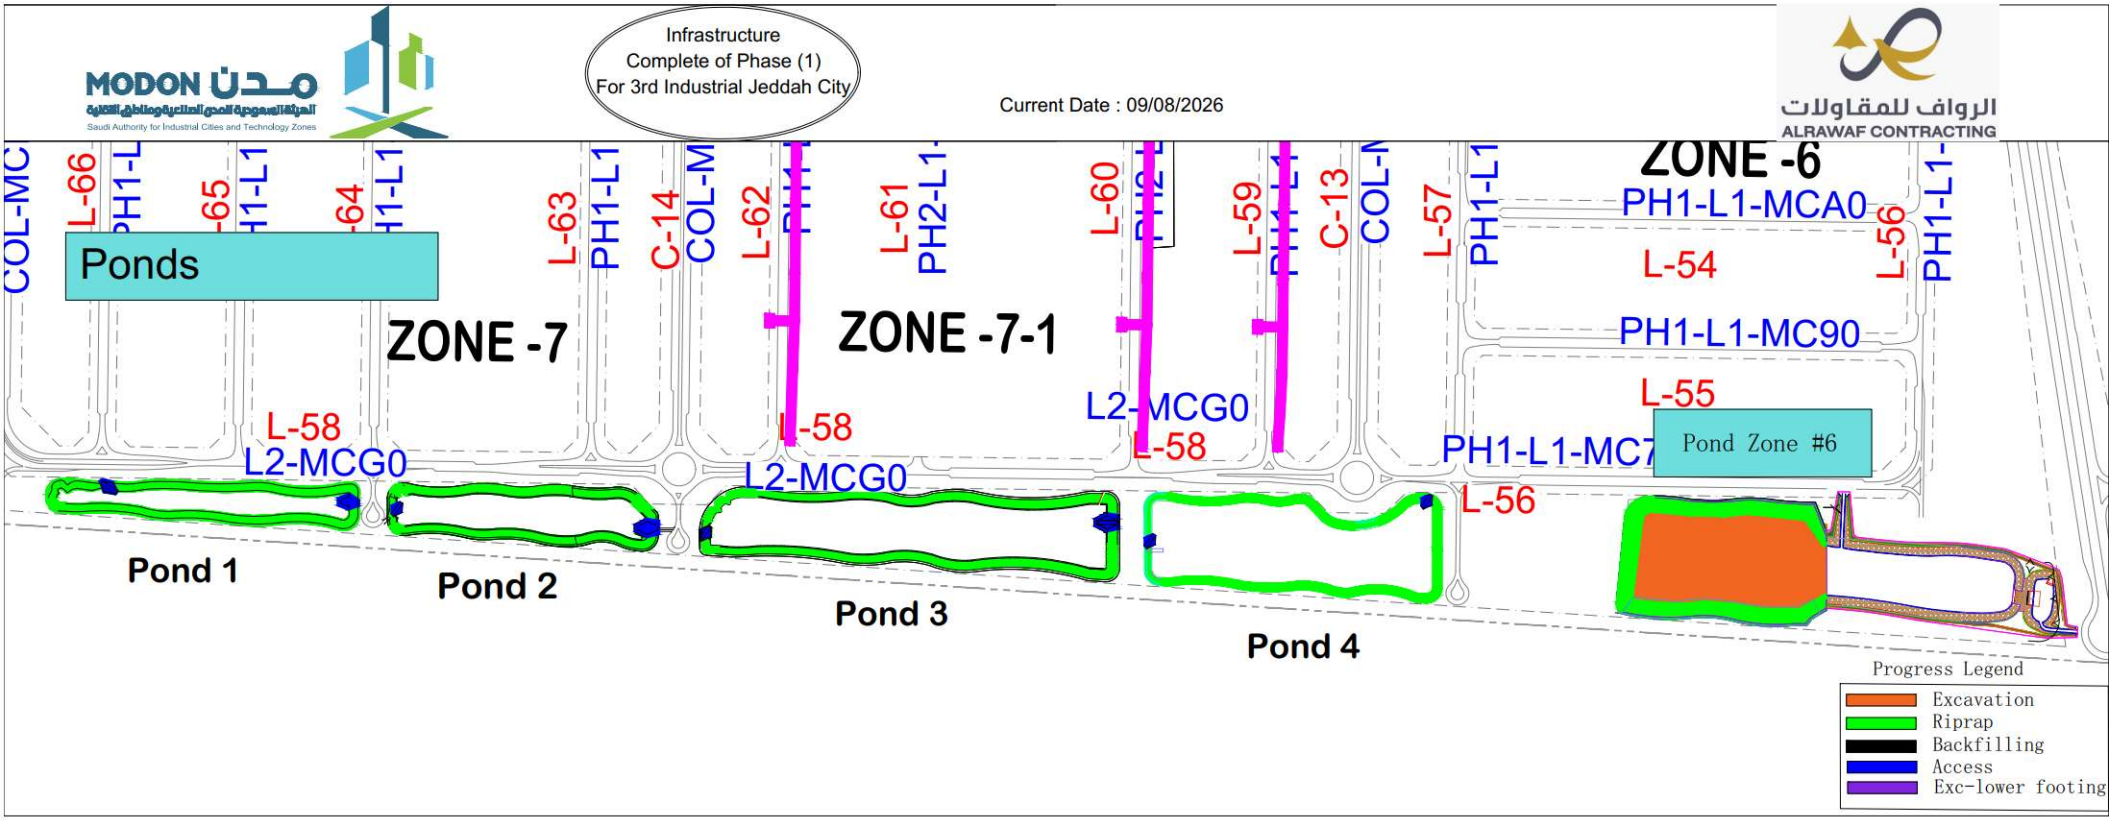
MODON مدن
Saudi Authority for Industrial Cities and Technology Zones
Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City
Current Date : 09/08/2026
الرواف للمقاولات
ALRAWAF CONTRACTING
Ponds
ZONE -7
ZONE -7-1
ZONE -6
L-66
L-65
L-64
L-63
PH1-L1
C-14
COL-M
L-62
L-61
PH2-L1
L-60
L-59
C-13
L-57
L-56
PH1-L1-MCA0
L-54
PH1-L1-MC90
L-55
PH1-L1-MC7
L-58
L2-MCG0
Pond Zone #6
Pond 1
Pond 2
Pond 3
Pond 4
Progress Legend
Excavation
Riprap
Backfilling
Access
Exc-lower footing

PROGRESS PLAN

MODON مدن

egis

Infrastructure
Complete of Phase (1)
For 3rd Industrial Jeddah City

Current Date : 09/08/2026

13


الرواف للمقاولات
ALRAWAF CONTRACTING

Pond Zone #12

Progress Legend

- Excavation
- Riprap
- Backfilling
- Access
- Exc-lower footing

COMPLETED

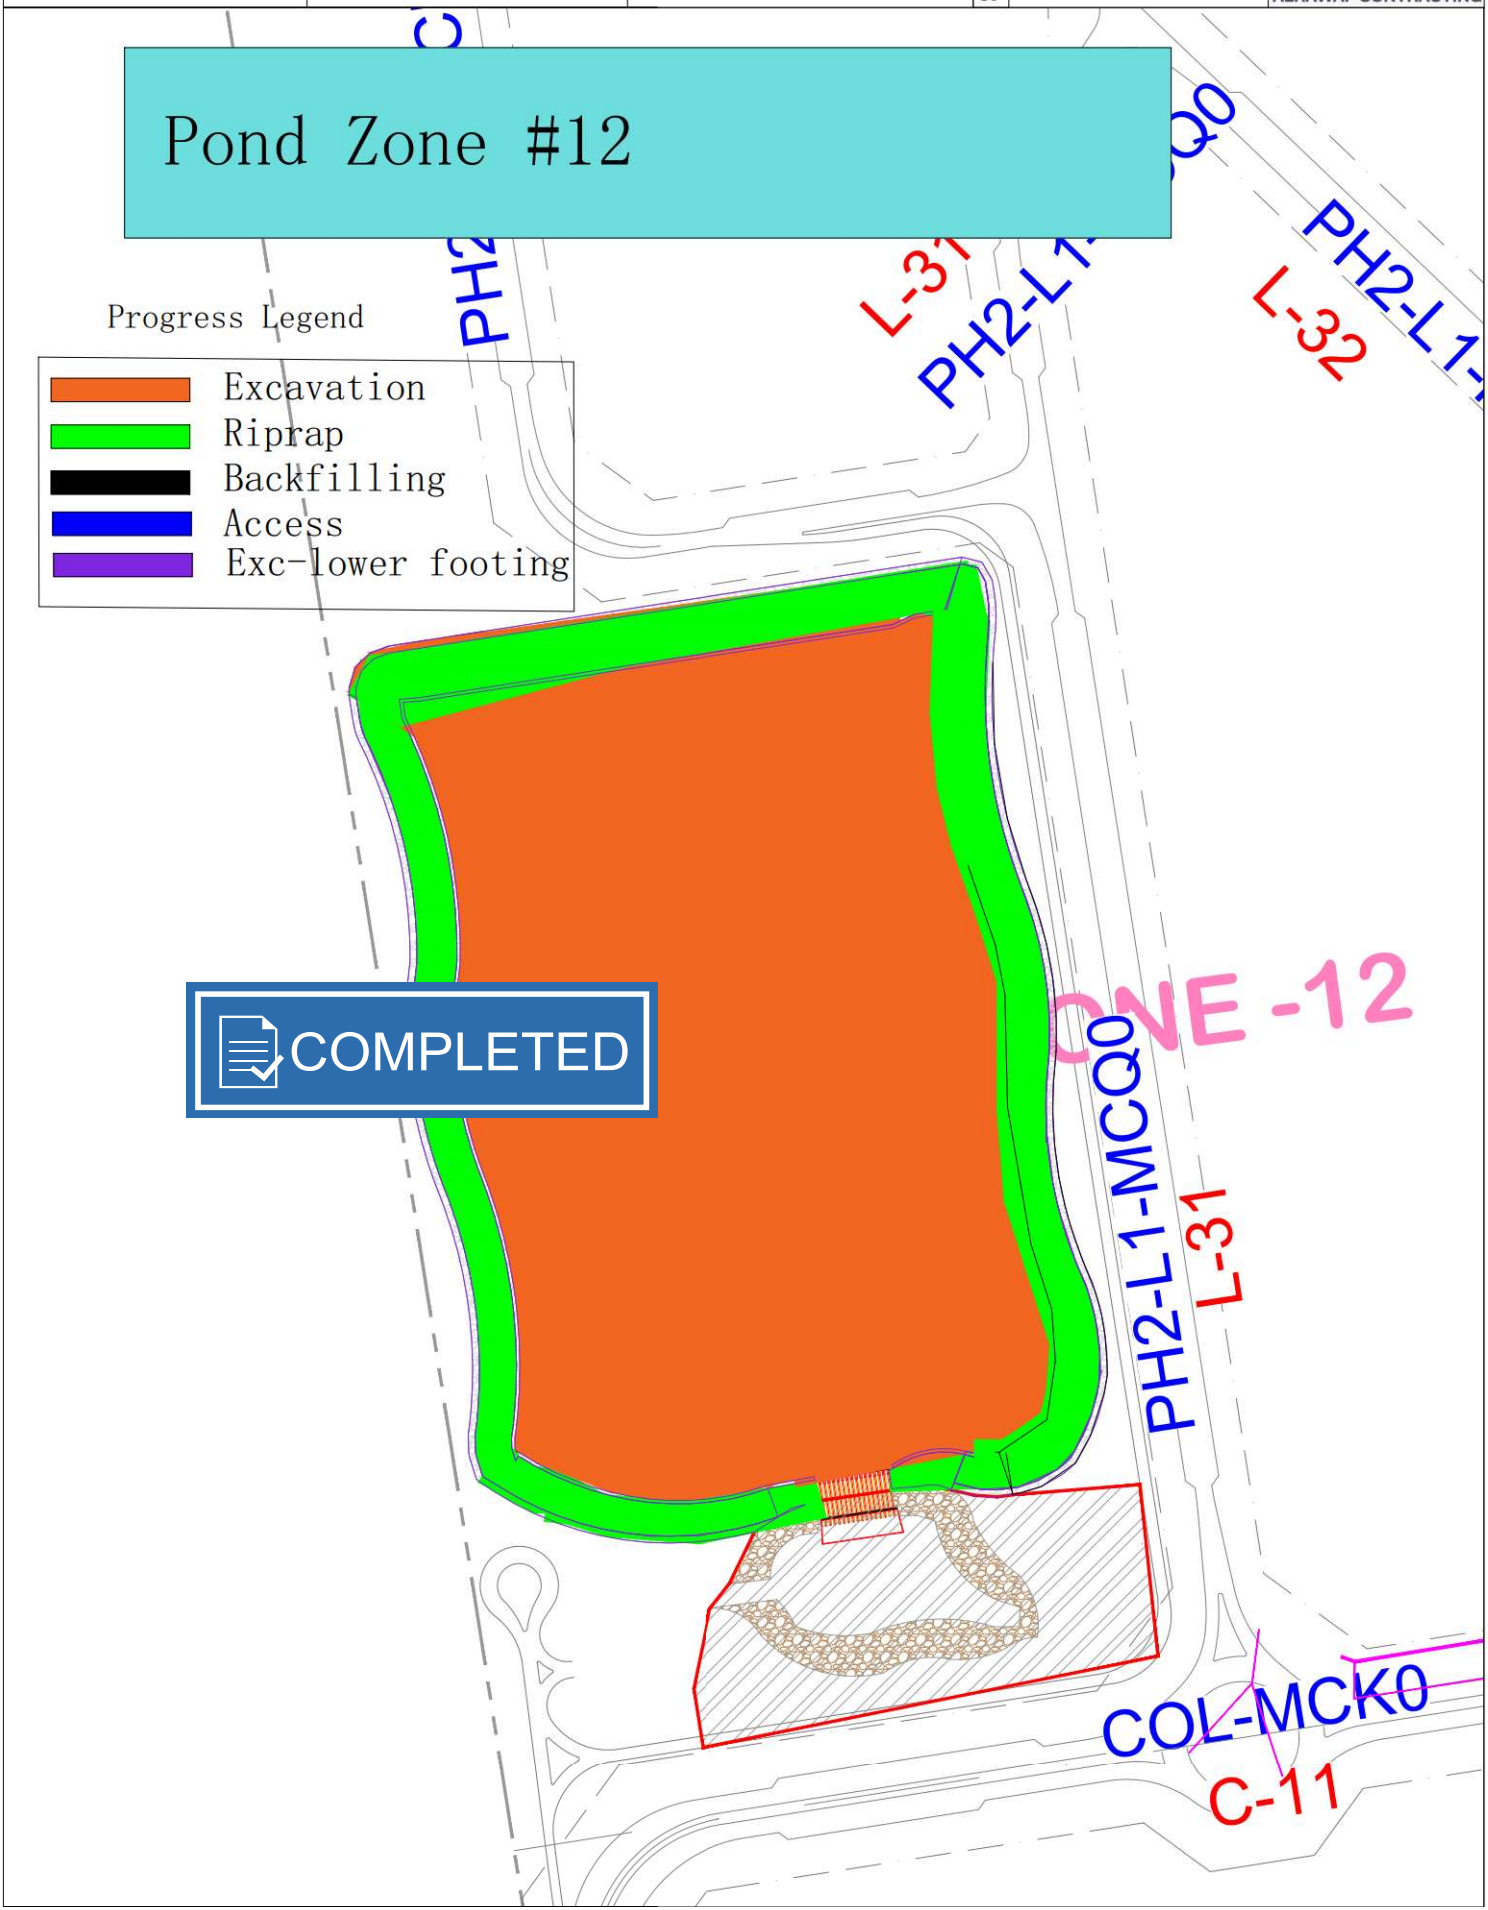

PROGRESS PLAN

Current Date : 09/08/2026

