Construction of Industrial Units for Artisans in Najran

مبادرة الحرفيين (الصناعات منخفضة العمليات التصنيعية بنجران)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Labenat Al Bena	EGIS	Eng. Ahmed Kotbi	03-Mar-2026	02-Jan-2027

Scope: the Low Process RBF unit, an outside mosque, a pump shed and a GRP water tank, with site works, concrete, masonry, finishes, pre-engineered structures, and mechanical and electrical systems including fire fighting, fire alarm and solar power.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The report now shows the project 100% complete against 85.3% planned, 14.7% ahead of the baseline (SPI 1.172). This week's progress was 1.5%, against 2.9% planned for the week, and closed the remaining close-out and electrical works.

PHYSICAL % COMPLETE

100% / 85.3% plan

▲ SPI 1.172 +14.7%

PROGRESS THIS WEEK

+1.5% / +2.9% plan

● Remaining 1.5% completed this week

CONTRACT TIME ELAPSED

78.0% · day 238 of 305

● Reported complete 27-Oct-2026

INVOICED TO DATE (GROSS)

83.1% · 7.94M SAR

6 invoices, all paid; last period ends 30-Sep-2026

The project is reported complete, 67 days before the contract date, but this needs to be verified.

The weekly report marks all works, including testing, commissioning and close-out, as complete on 27-Oct-2026, and all 1,462 schedule activities as finished. However, the Testing sheet still plans testing and commissioning for 09-Dec-2026 to 19-Dec-2026 with no actual dates, the Procurement sheet still lists 22 of 108 items as not delivered, and the site layout still marks the asphalt wearing course as not started. The consultant should confirm completion before initial handover.

Site photos this week

Two of the three photos in the "Weekly Photos" sheet of the 27-Oct-2026 weekly report (pump room works), stamped 27-Oct-2026, Najran Region. Select a photo to view it larger, then use the arrows to move between photos.



Fire pump shed

Fire-fighting pipework and fenced pump shed beside the GRP tank. Stamped 27-Oct-2026, 08:39.




Pump shed and GRP water tank

Pump shed with its chain-link fence, interlock paving around it. Stamped 27-Oct-2026, 08:40.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly; the October value is to 27-Oct-2026. Source: Physical-Chart Data sheet.

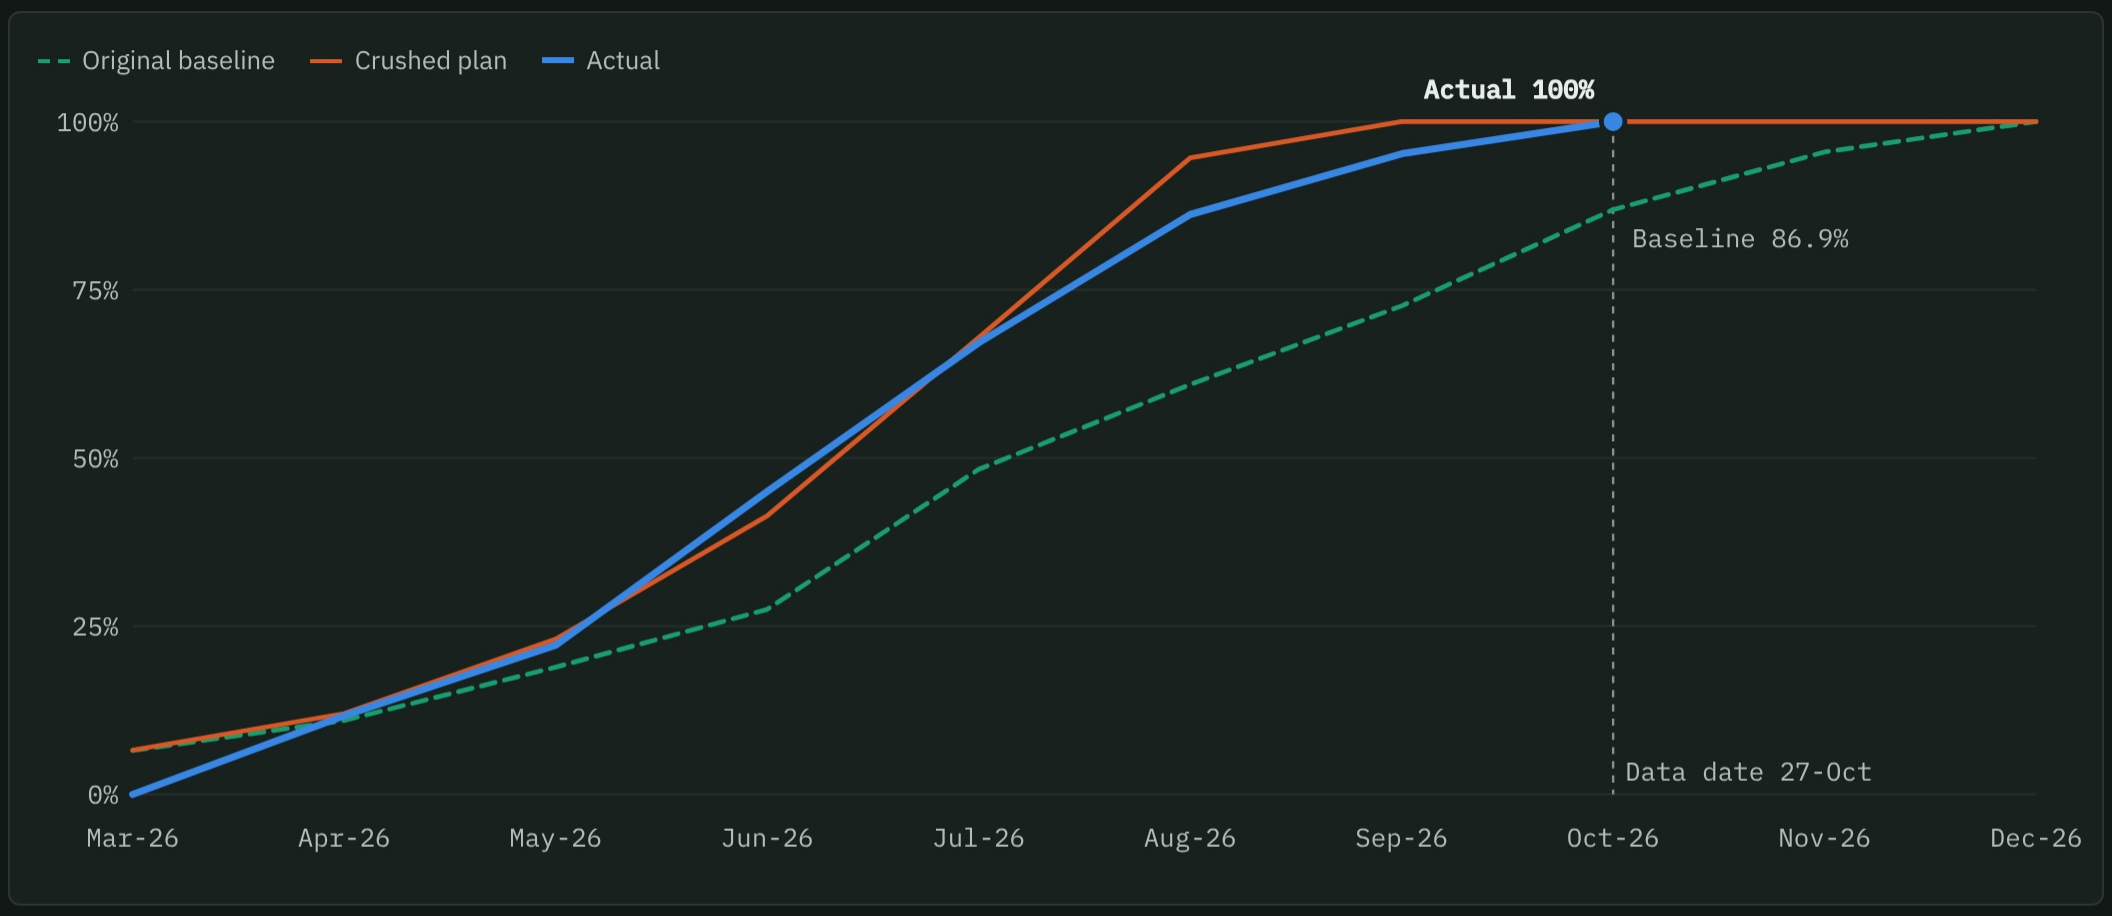

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
21-Oct-2026	82.4	98.5	+16.1	+2.0	1.195
27-Oct-2026	**85.3**	**100.0**	**+14.7**	**+1.5**	**1.172**

Physical % complete from the weekly reports of 21-Oct-2026 and 27-Oct-2026; earlier weeks were not uploaded. The gain this week (+1.5%, against +2.9% planned) matches the change from 98.5% to 100%.

Progress by phase

Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report and Progress sheets.


PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	4.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.0%	100.0%	100.0%	0.0%	1.00	✓ Complete
Procurement	12.0%	99.9%	100.0%	+0.1%	1.00	✓ Complete
Construction	**76.3%**	**85.6%**	**100.0%**	**+14.4%**	**1.17**	✓ Complete
· Site works	4.7%	71.5%	100.0%	+28.5%	1.40	✓ Complete
· Concrete	17.4%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Masonry	2.2%	100.0%	100.0%	0.0%	1.00	✓ Complete
· Metal works	0.6%	47.8%	100.0%	+52.2%	2.09	✓ Complete
· Thermal and moisture protection	2.7%	95.6%	100.0%	+4.4%	1.05	✓ Complete
· Doors and windows	3.6%	78.7%	100.0%	+21.3%	1.27	✓ Complete
· Finishes	5.0%	36.3%	100.0%	+63.7%	2.76	✓ Complete
· Specialties	0.6%	0.0%	100.0%	+100.0%	–	✓ Complete
· Pre-engineered structure	8.1%	100.0%	100.0%	0.0%	1.00	✓ Complete

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
· Mechanical works	13.1%	89.5%	100.0%	+10.5%	1.12	✓ Complete
· Electrical works	18.3%	82.3%	100.0%	+17.7%	1.22	✓ Complete
Close-out	3.7%	0.0%	100.0%	+100.0%	–	✓ Complete
Total	100%	**85.3%**	**100.0%**	**+14.7%**	**1.172**	✓ Complete

The P6 schedule status in the report lists all 1,462 activities as completed (last week: 1,430 completed, 17 in progress, 15 not started).

Scope of work: quantities

Total and installed quantity for each major item, from the Major Quantities sheet of the 27-Oct-2026 weekly report. "This week" is the change since the 21-Oct-2026 report; no installed quantity changed this week.

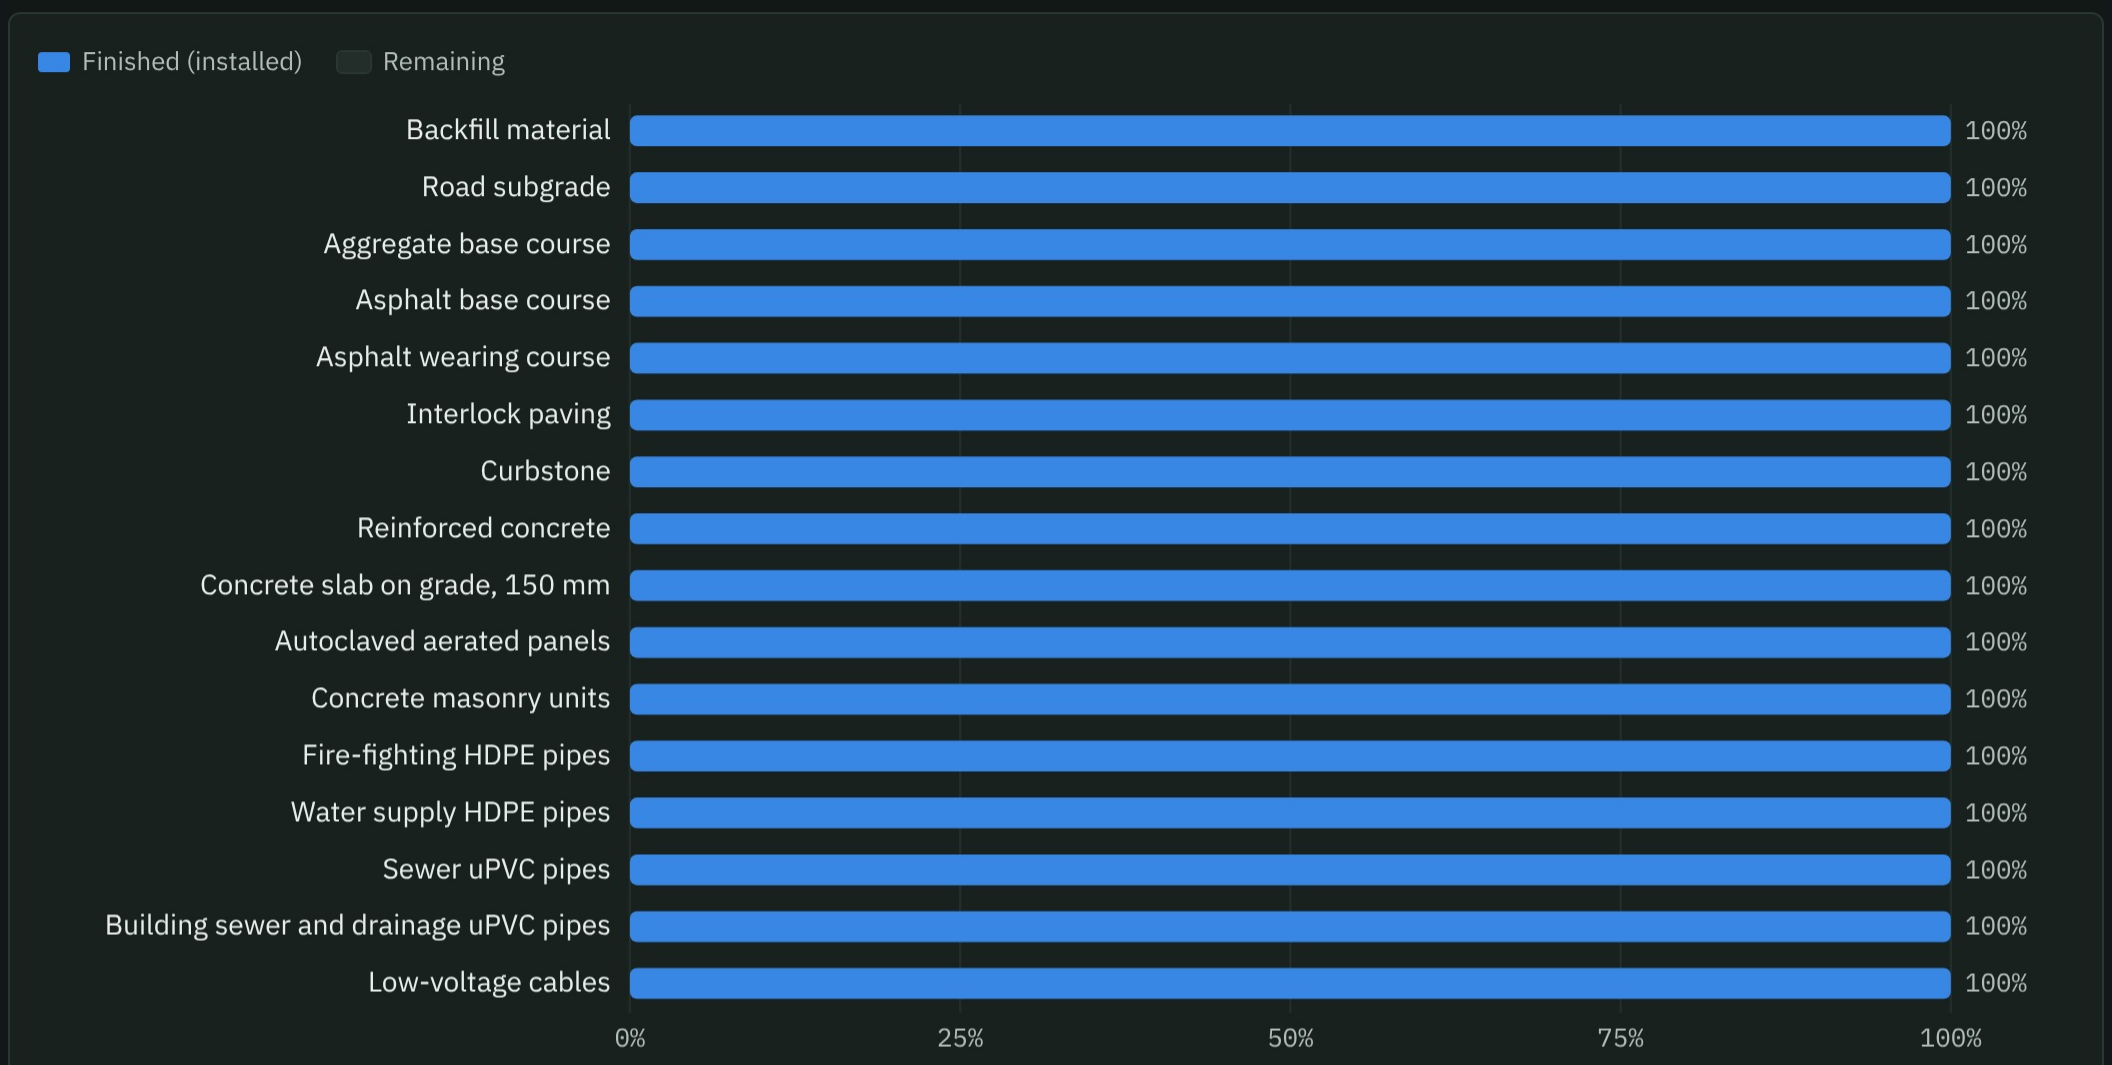

SCOPE ITEM	BOQ ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Backfill material	2.1.6	m³	2,615	2,615	0	0	100.0%
Road subgrade	2.2.4	m³	1,300	1,300	0	0	100.0%
Aggregate base course	2.2.3	m³	867	867	0	0	100.0%
Asphalt base course	2.2.2	m³	304	304	0	0	100.0%
Asphalt wearing course	2.2.1	m³	217	217	0	0	100.0%
Interlock paving	2.2.7.1	m²	1,326	1,326	0	0	100.0%
Curbstone	2.3.8	LM	1,294	1,294	0	0	100.0%
Reinforced concrete	3.2	m³	449	449	0	0	100.0%
Concrete slab on grade, 150 mm	3.3	m³	307	307	0	0	100.0%
Autoclaved aerated panels	3.4	m²	55	55	0	0	100.0%
Concrete masonry units	4.1	m²	444	444	0	0	100.0%

SCOPE ITEM	BOQ ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Fire-fighting HDPE pipes	15.1.2.1 · 200 mm	LM	48	48	0	0	100.0%
	15.1.2.2 · 150 mm	LM	200	200	0	0	100.0%
	15.4.1.1 · 8 in	LM	15	15	0	0	100.0%
	Total	LM	**263**	**263**	**0**	**0**	**100.0%**
Water supply HDPE pipes	15.2.2.1 · 100 mm	LM	20	20	0	0	100.0%
	15.2.2.2 · 90 mm	LM	235	235	0	0	100.0%
	15.2.2.3 · 63 mm	LM	8	8	0	0	100.0%
	15.2.2.4 · 50 mm	LM	40	40	0	0	100.0%
	15.5.1.1 · 63 mm	LM	40	40	0	0	100.0%
	Total	LM	**343**	**343**	**0**	**0**	**100.0%**
Sewer uPVC pipes	15.3.2.1 · 110 mm	LM	105	105	0	0	100.0%
	15.3.2.2 · 160 mm	LM	75	75	0	0	100.0%
	Total	LM	**180**	**180**	**0**	**0**	**100.0%**
Building sewer and drainage uPVC pipes	15.6.1.1 · 4 in	LM	168	168	0	0	100.0%
	15.6.1.2 · 3 in	LM	30	30	0	0	100.0%
	15.6.1.3 · 2 in	LM	132	132	0	0	100.0%
	15.6.1.4 · 1 in	LM	180	180	0	0	100.0%
	Total	LM	**510**	**510**	**0**	**0**	**100.0%**
Low-voltage cables	16.6.1 · 4C×185 mm²	LM	120	120	0	0	100.0%
	16.6.2 · 4C×120 mm²	LM	75	75	0	0	100.0%
	Total	LM	**195**	**195**	**0**	**0**	**100.0%**

Asphalt status disagrees between sheets

The Major Quantities sheet reports both asphalt layers and the interlock paving as fully installed, but the Procurement sheet lists both asphalt layers as "Ready for delivery" and the site layout on the Project Summary sheet marks the wearing course as "Not Started".

Milestones

Baseline, latest plan and forecast or actual dates from the Milestones sheet. Change is the number of days stated in the sheet.

MILESTONE	BASELINE	LATEST PLAN	FORECAST / ACTUAL	CHANGE (DAYS)	STATUS
Contract award	25-Jan-2026	25-Jan-2026	25-Jan-2026	0	✓ Done
Contract signature	12-Feb-2026	12-Feb-2026	12-Feb-2026	0	✓ Done
Site handover	03-Mar-2026	03-Mar-2026	03-Mar-2026	0	✓ Done
Complete mobilisation	31-Mar-2025	31-Mar-2025	31-Mar-2025	0	✓ Done
Existing condition survey and final reports	31-Mar-2025	31-Mar-2025	31-Mar-2025	0	✓ Done

MILESTONE	BASELINE	LATEST PLAN	FORECAST / ACTUAL	CHANGE (DAYS)	STATUS
Long-lead procurement and delivery	27-Oct-2026	27-Oct-2026	27-Oct-2026	0	✓ Done
Short-lead procurement and delivery	29-Oct-2026	05-Sep-2026	05-Sep-2026	0	✓ Done
All warehouse works	29-Nov-2026	03-Oct-2026	03-Oct-2026	0	✓ Done
Outside mosque (prayer room)	05-Dec-2026	30-Sep-2026	30-Sep-2026	0	✓ Done
GRP water tank and pump shed	24-Aug-2026	19-Oct-2026	19-Oct-2026	0	✓ Done, 56 days after baseline
All external works	25-Nov-2026	19-Oct-2026	19-Oct-2026	0	✓ Done
All works incl. testing, commissioning and close-out (initial handover)	02-Jan-2027	27-Oct-2026	27-Oct-2026	0	? Done, to be verified
Demobilisation	02-Jan-2027	27-Oct-2026	27-Oct-2026	0	✓ Done

All milestones are now marked as achieved.

This week the GRP water tank and pump shed and the external works were recorded as achieved on 19-Oct-2026, and completion of all works and demobilisation on 27-Oct-2026. The GRP tank and pump shed finished 56 days after its baseline, although the change column shows 0. Completion of all works includes testing and commissioning, which the Testing sheet still shows as planned for December 2026 without actual dates.

Procurement of key materials

Share of material items delivered to site, by discipline. Source: Procurement sheet, weekly report 27-Oct-2026 (86 of 108 items delivered, unchanged from last week).



Finishes: 5 of 11 items delivered


Granite tiles, marble strip and wood skirting are "Ready for delivery"; marble chips and phenolic partitions are "Contractor ready"; carpet is "Locally available".

Other items not yet delivered

Both asphalt layers and road paint (ready for delivery), HVAC fans, ductwork, diffusers and grilles (contractor ready), roof deck waterproofing (delivery ongoing), aluminium cladding, galvanized steel fence and fence gate, water sprinklers, a Corian countertop, and toilet and mosque signage and MODON logos.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

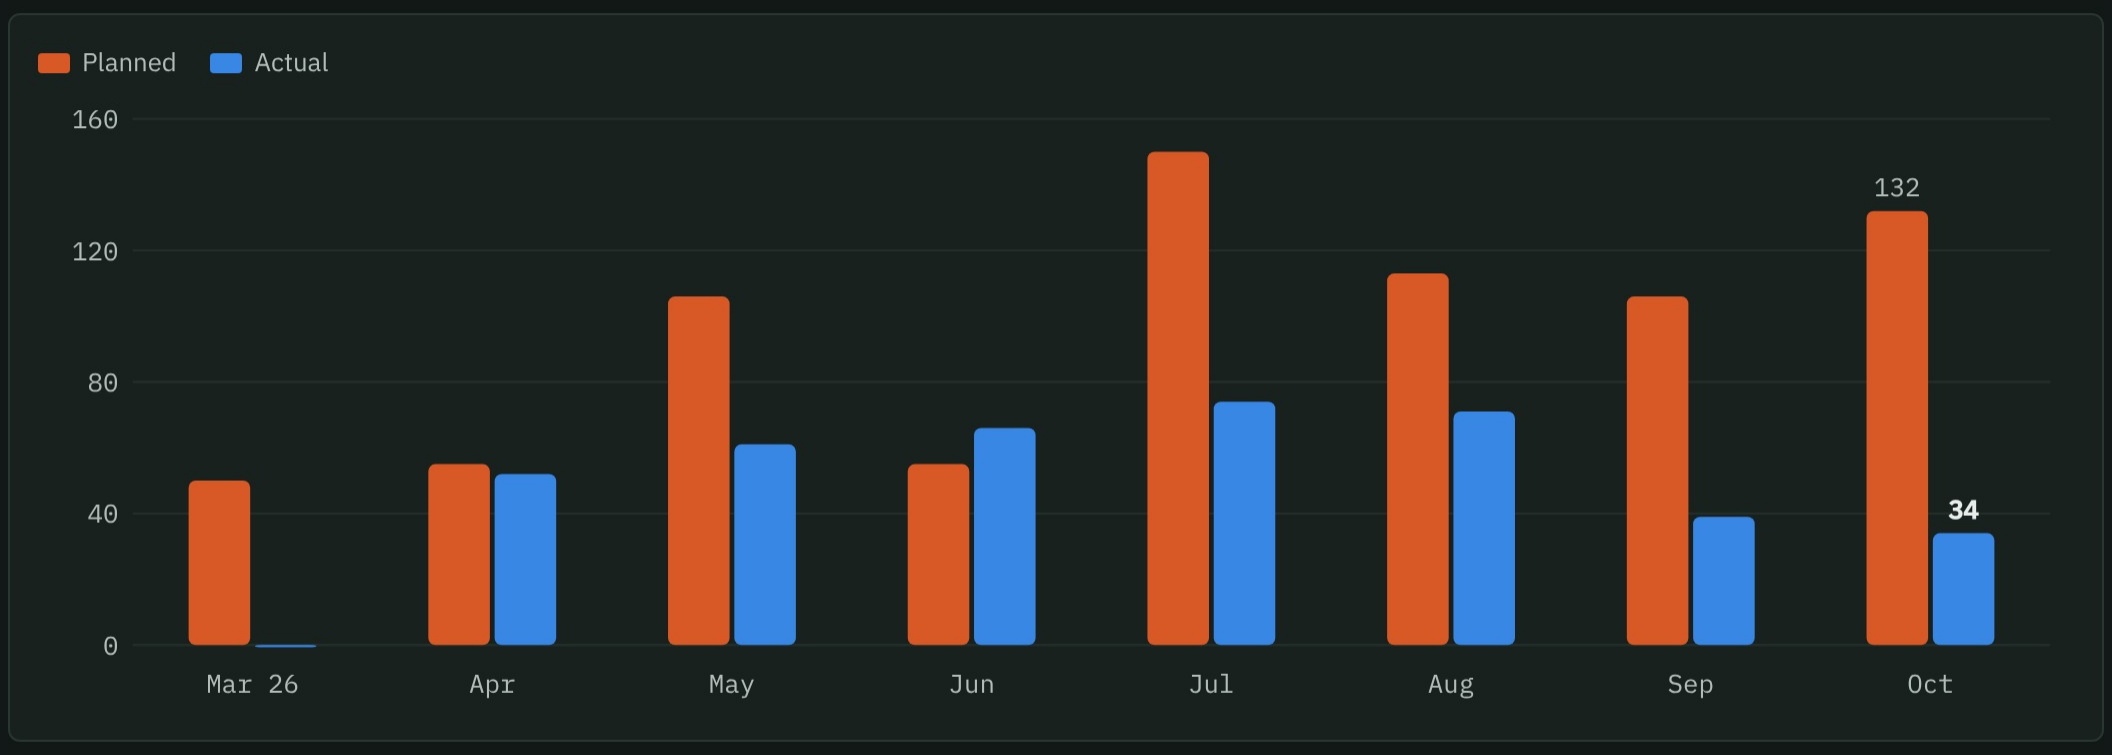

October head count is 34 (13 non-manual, 21 manual) against 132 planned (−74%). Equipment on site is 8 against 34 planned. The manpower figures are the same as last week.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	9,554,134
Revised contract value	9,554,134
Contract value incl. 15% VAT	10,987,254
Change orders	0

All values in SAR. The change order log is empty.

Invoices

Invoices submitted / PM approved	6 / 6
Gross value	7,935,744
Invoices paid	6
Paid value	7,935,744
Retention	0
Deductions and penalties	−20,000
Net incl. VAT	9,106,107
FIR value to date	9,623,075

Invoicing is 83.1% of the contract value against 100% physical progress; 1,618,390 SAR of the contract value is not yet invoiced. Invoices 5 and 6 were paid on 20-Oct-2026 and 27-Oct-2026.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	85,094
Man-hours this week	1,104
Lost-time injuries	0
Fatalities	0
First-aid cases	2
Near misses (year to date)	9
Fire incidents	0
Inductions / toolbox talks	41 / 29

From the HSE-Stat sheet; the summary panel differs, see Data notes.

Quality Score 0.89

FIRs issued / closed	407 / 407
MIRs issued / closed	64 / 64
NCRs issued / closed	17 / 17
Site instructions issued / closed	18 / 18
Approved shop drawings	93 / 93
Approved material submittals	95 / 95
FIR value this period (SAR)	290,865

FIR period: 19-Oct-2026 to 25-Oct-2026.

Data notes

- The report marks all works complete on 27-Oct-2026, but the Testing sheet still plans testing and commissioning for 09-Dec-2026 to 19-Dec-2026 and shows no actual dates.
- Milestones: mobilisation and the existing condition survey have baseline dates of 31-Mar-2025, before the contract award of 25-Jan-2026. For long-lead procurement the summary panel gives a latest plan of 03-Oct-2026 while the Milestones sheet gives 27-Oct-2026. The change column shows 0 days for every milestone, although actual dates range from 66 days before to 56 days after baseline.
- S-curve: the Physical-Chart Data sheet divides earned man-hours by 241,519.85 (the crushed plan total) for April to September but by 224,320 for October. This report uses 224,320, the budget in the Progress sheet, for every month; with the sheet's own percentages September would be 88.4% instead of 95.2%.
- This-week values come from comparing this report with the 21-Oct-2026 report (Weekly Report #29). Earlier weekly reports were not uploaded.
- Asphalt: the Major Quantities sheet and the Lookahead sheet report the base and wearing courses as 100% installed, but the Procurement sheet lists both as "Ready for delivery" and the Project Summary layout marks the wearing course as "Not Started". Their Plan to Date cells are blank and the variance column shows the full quantity.
- Procurement: the Procurement sheet shows 86 of 108 items delivered, but the summary panel shows 95 of 95 materials on site. The sheet header still reads "as of 26-Jul-2026". Finishes and Specialties are reported 100% physically complete although 6 of 11 finishes items and 2 of 3 specialties items are not delivered.
- Manpower: October non-manual actual is 13 in the monthly table, 16 in the Manpower sheet summary and 14 in the weekly report panel. The Manpower sheet, the Procurement sheet and the HSE incident counts are unchanged from last week.
- FIR summary for 19-Oct-2026 to 25-Oct-2026 (290,865 SAR) claims installed carpet (51.6), wood skirting (38.2), galvanized steel fence (36) and a fence swing gate (1), which the Procurement sheet still lists as not delivered.
- HSE: the weekly report panel shows 1 first-aid case, 2 near misses and 1 fire incident; the HSE-Stat sheet shows 2 first-aid cases, 9 near misses year to date (0 cumulative) and no fire incidents.
- The hidden PV-PH and PV sheets hold planned-value data for another project (HAL1-05-1, Civil Defense Fire Station in Hail Industrial City, 2024–2025). They were not used.
- The Invoice Log shows a revised contract value of 21,100,000, an estimate at completion of 20,900,000 and potential changes of 200,000 next to the 9,554,134 contract value. Invoice 1 and the Lookahead sheet use project ID NJR1-01-007, and the Lookahead names Mohammed Alharbi as project manager.
- The Project Summary sheet splits the contract value by component differently from the Progress sheet (for example Site Works 1,067,430 against 682,299), though both total 9,554,134. It also labels a cost-based progress figure as planned progress; this report uses physical (man-hour) progress only.
- The Issues log and the Risk Register are empty, so the issues and risks section is left out. The weekly quality score is 0.8878 in every week since April. Several summary cells show #REF!.
- Contract duration: the Milestones sheet now reads "Current Contract Weeks: 34 of 34" (last week "33 of 44"), and the revised, committed and forecast completion dates are all 27-Oct-2026, while the original completion date is still 02-Jan-2027. This report uses the contract week 34 stated in the sheet (the file is "Weekly Report #30") and keeps 02-Jan-2027 as the contract completion date.

Compiled 01-Nov-2026 from the weekly report for 27-Oct-2026 (Weekly Report #30), with the 21-Oct-2026 report for this-week values.
