Playgrounds Initiative: Qassim Oasis, Hail and Tabuk Industrial City

مبادرة الملاعب بالمنطقة الوسطى (حائل, واحة القصيم, تبوك)

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Advanced Construction & Contracting Co.	Egis	Bader Alrowaidan	17-Feb-2026	16-Dec-2026

Scope: playgrounds at three locations (Qassim Oasis, Hail and Tabuk Industrial City), with civil, architectural, electrical, mechanical and landscape works and general site works, including air domes at Qassim and Tabuk and a toilet building at each site.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours (weekly report, Physical Progress sheet). At 01-Nov-2026 the project is 80.06% complete against 85.46% planned, behind by 5.40% (SPI 0.94). It gained 2.42% this week against 2.20% planned, so the gap narrowed slightly.

PHYSICAL % COMPLETE
80.06% / 85.46%
plan
▼ SPI 0.94 5.40% behind plan

PROGRESS THIS WEEK
+2.42% / +2.20%
plan
▲ 0.22% above the weekly plan

CONTRACT TIME ELAPSED
85.1% · day 257 of 302
▼ P6 finish 23-Feb-2027

INVOICED TO DATE (GROSS)
9.4% · 3.36M SAR
2 invoices, last period ends 30-Sep-2026

The schedule now finishes the project 69 days after the contract date.

The P6 update (data date 30-Oct-2026) and the weekly report both forecast handover on 23-Feb-2027 against the contract completion date of 16-Dec-2026, with −58.8 days of float; last week the forecast was 14-Feb-2027. 169 of the 301 open activities have negative float and 37 activities have failed to start. The air domes are furthest behind: Qassim 39.96% against 83.02% planned and Tabuk 35.13% against 78.32%, with no progress this week.

Site photos this week

Six photos from the weekly report of 01-Nov-2026, stamped 28 and 29 Oct 2026 where the stamp is visible. Curbstone, irrigation, fencing, tartan, cladding and toilet fit-out works continue. Select a photo to view it larger, then use the arrows to move between photos.



Curbstone installation

Curbs set around a landscaped area. No date stamp.



Irrigation main line, Tabuk

Main line laid in the trench. Stamped 29-Oct-2026, 08:06, Tabuk Industrial City.



Chain-link fence posts, football area

Posts set for the chain-link fence. No date stamp.



Tartan layer, Hail

Tartan layer laid. GPS-stamped 29-Oct-2026, 09:58, Hail.



Stone wall cladding, Qassim

Cladding on the toilet building. GPS-stamped 29-Oct-2026, 14:31, Buraydah.




Corian countertop

Countertop with wash basins installed. No date stamp.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet of the weekly report.

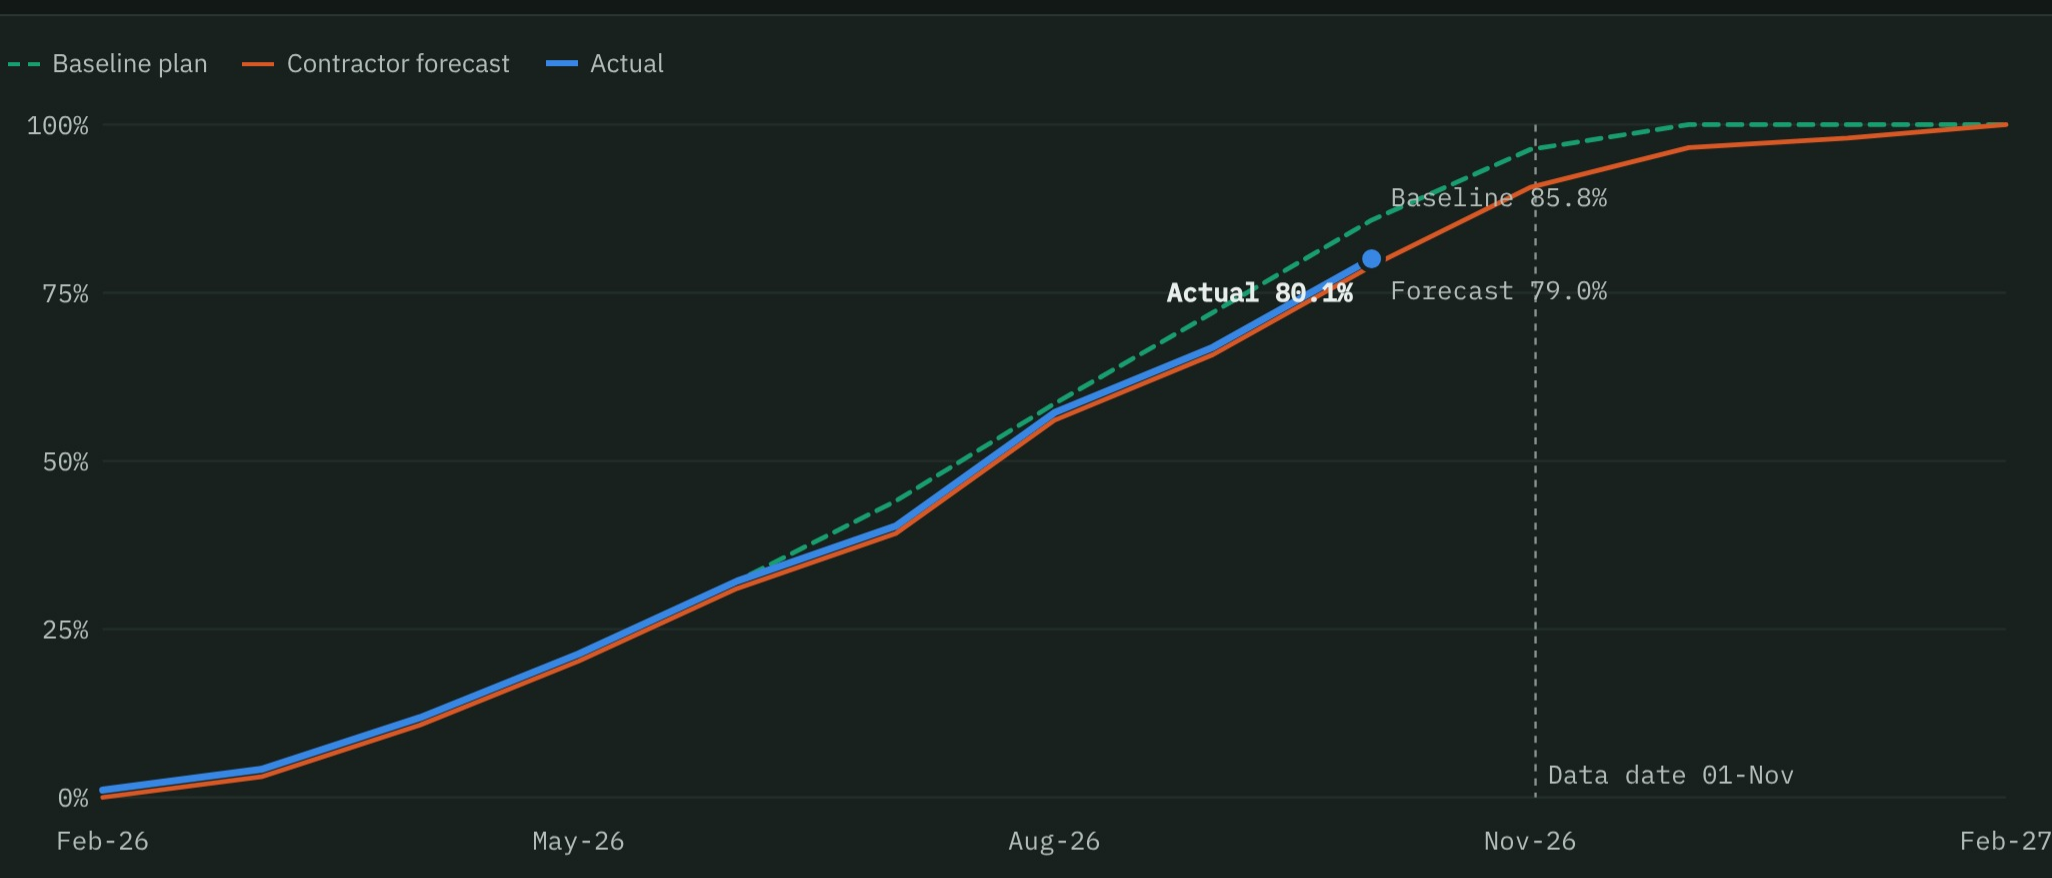

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
18-Oct-2026	80.25	74.79	−5.46	–	0.93
25-Oct-2026	83.26	77.64	−5.62	+2.85	0.93
01-Nov-2026	**85.46**	**80.06**	**−5.40**	**+2.42**	**0.94**

Physical % complete from the weekly reports of 18 Oct, 25 Oct and 01 Nov 2026, the only three weekly reports uploaded so far. The monthly baseline in the chart reaches 85.82% at the end of October and 96.29% at the end of November.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours (weekly report, Progress sheet). Engineering and procurement carry no man-hours in the report, so they are not shown.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Project milestone (management time)	**30.0%**	**84.05%**	**84.07%**	**+0.02%**	**1.00**	▲ Ahead
Construction	**66.6%**	**90.38%**	**81.45%**	**−8.93%**	**0.90**	▼ Behind
Qassim Oasis	24.3%	88.77%	81.14%	−7.63%	0.91	▼ Behind
Hail	17.9%	94.78%	83.41%	−11.36%	0.88	▼ Behind
Tabuk	24.3%	88.75%	80.30%	−8.45%	0.90	▼ Behind
Closeout	**3.5%**	**2.92%**	**18.67%**	**+15.75%**	**6.40**	▲ Ahead
Total	100%	**85.46%**	**80.06%**	**−5.40%**	**0.94**	▼ Behind

Within construction, the air domes are furthest behind: Qassim 446 of 1,116 man-hours earned against 926.5 planned, and Tabuk 392 against 874; neither earned any man-hours this week. The P6 update (data date 30-Oct-2026) has 1,929 activities: 1,628 completed, 234 in progress and 67 not started.

Scope of work: quantities

Total, finished and remaining quantity of the major items, all three sites together, from the Major Quantities sheet of the 01-Nov-2026 weekly report. The last column is the quantity planned to date. “This week” compares with the 25-Oct-2026 report.

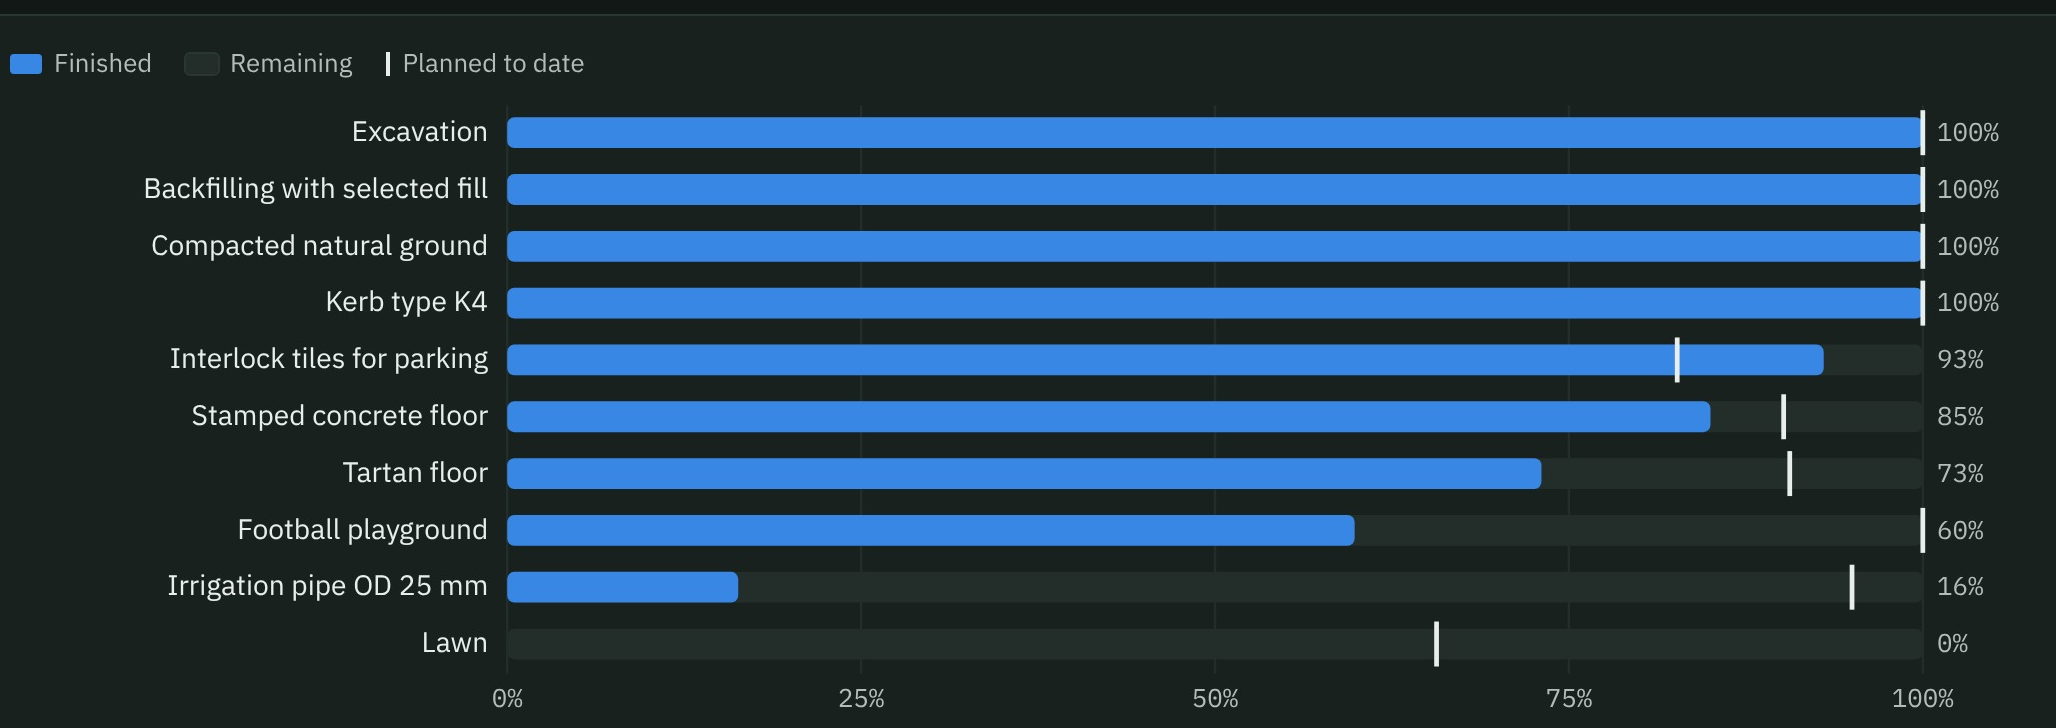

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Excavation	All	m³	29,400	29,400	0	0	100.0%	100.0%
Backfilling with selected fill	All	m³	29,400	29,400	0	0	100.0%	100.0%
Compacted natural ground	All	m²	33,300	33,300	0	0	100.0%	100.0%
Kerb type K4	All	LM	27,100	27,100	0	0	100.0%	100.0%
Interlock tiles for parking	All	m²	7,140	6,640	0	499.8	93.0%	82.7%
Stamped concrete floor	All	m²	7,800	6,630	0	1,170	85.0%	90.2%
Tartan floor	All	m²	10,950	8,000	0	2,950	73.1%	90.6%
Football playground	All	m²	7,350	4,400	0	2,950	59.9%	100.0%

SCOPE ITEM	SITES	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED	PLANNED %
Irrigation pipe OD 25 mm	All	m	11,100	1,812	0	9,288	16.3%	95.0%
Lawn	All	m²	19,100	0	0	19,100	0.0%	65.6%

Reported this week

Tartan layer, stone wall cladding, Corian countertops, irrigation work, curbstone and chain-link fence posts for the football area (weekly executive summary). Next week: tartan, cable pulling for the toilet area, irrigation, curbstone, fencing and light pole foundations.

Lawn, irrigation pipe and playgrounds lag

Lawn is at 0 of 12,539 m² planned to date, the 25 mm irrigation pipe at 1,812 of 10,545 m, the football playground at 4,400 of 7,350 m² and the tartan floor at 8,000 of 9,921 m². All major quantities are unchanged for the second week running, although tartan, irrigation and curbstone work was reported.

Milestones

The weekly report's milestone sheet and the P6 update disagree on some dates. Both are shown so the difference can be resolved with the contractor. P6 float is from the update with data date 30-Oct-2026.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	17-Feb-2026	17-Feb-2026	17-Feb-2026 (actual)	–	✓ Done
Complete mobilisation	18-Mar-2026	14-Apr-2026	–	–	✓ Done late
Complete engineering	16-Aug-2026	03-Nov-2026 (+79 d)	–	–	▼ Late
Complete procurement	27-Aug-2026	05-Nov-2026 (+70 d)	–	–	▼ Late
Completion of toilet building	28-Oct-2026	–	12-Nov-2026	+8.2	▼ At risk
Completion of playground works	07-Dec-2026	–	10-Dec-2026	+5.7	▼ At risk
Complete construction	14-Dec-2026	06-Feb-2026 (0 d as stated)	06-Feb-2027	–	? Conflicts with P6
Completion of landscape works	16-Dec-2026	–	10-Jan-2027	−20.2	▼ Late
Complete all works, ready for initial handover	16-Dec-2026	18-Feb-2027 (+64 d)	23-Feb-2027	−58.8	▼ Late
Complete demobilisation	16-Dec-2026	22-Feb-2027 (+68 d)	–	–	▼ Late
Project handover	16-Dec-2026	23-Feb-2027 (+69 d)	23-Feb-2027	−58.8	▼ Late

The weekly report gives “Complete construction” as 06-Feb-2026, a date already past.

P6 finishes the construction stage on 03-Feb-2027 at Qassim, 20-Dec-2026 at Hail and 06-Feb-2027 at Tabuk, so the intended date is probably 06-Feb-2027. The handover forecast moved from 14-Feb-2027 to 23-Feb-2027 this week. Of the contractual milestones, only the toilet building (+8.2 days) and the playground works (+5.7 days) keep positive float.

Procurement of key materials

Physical % complete of the open “delivery to site” activities with the lowest progress (P6 update, data date 30-Oct-2026). All other open delivery activities are at 90–95%.



Air dome materials: 80% delivered


At both Qassim and Tabuk, with −58.8 and −55.0 days of float; Qassim's equals the float of project completion. The procurement log still shows the air dome purchase order as “under process” with a 150-day lead time.

Purchase orders and materials on site

The weekly report's procurement summary lists 57 materials: 33 purchase orders issued, 25 remaining and 8 materials on site. The curtain wall remainder is at 70% at Qassim and Tabuk and 80% at Hail.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet of the weekly report.

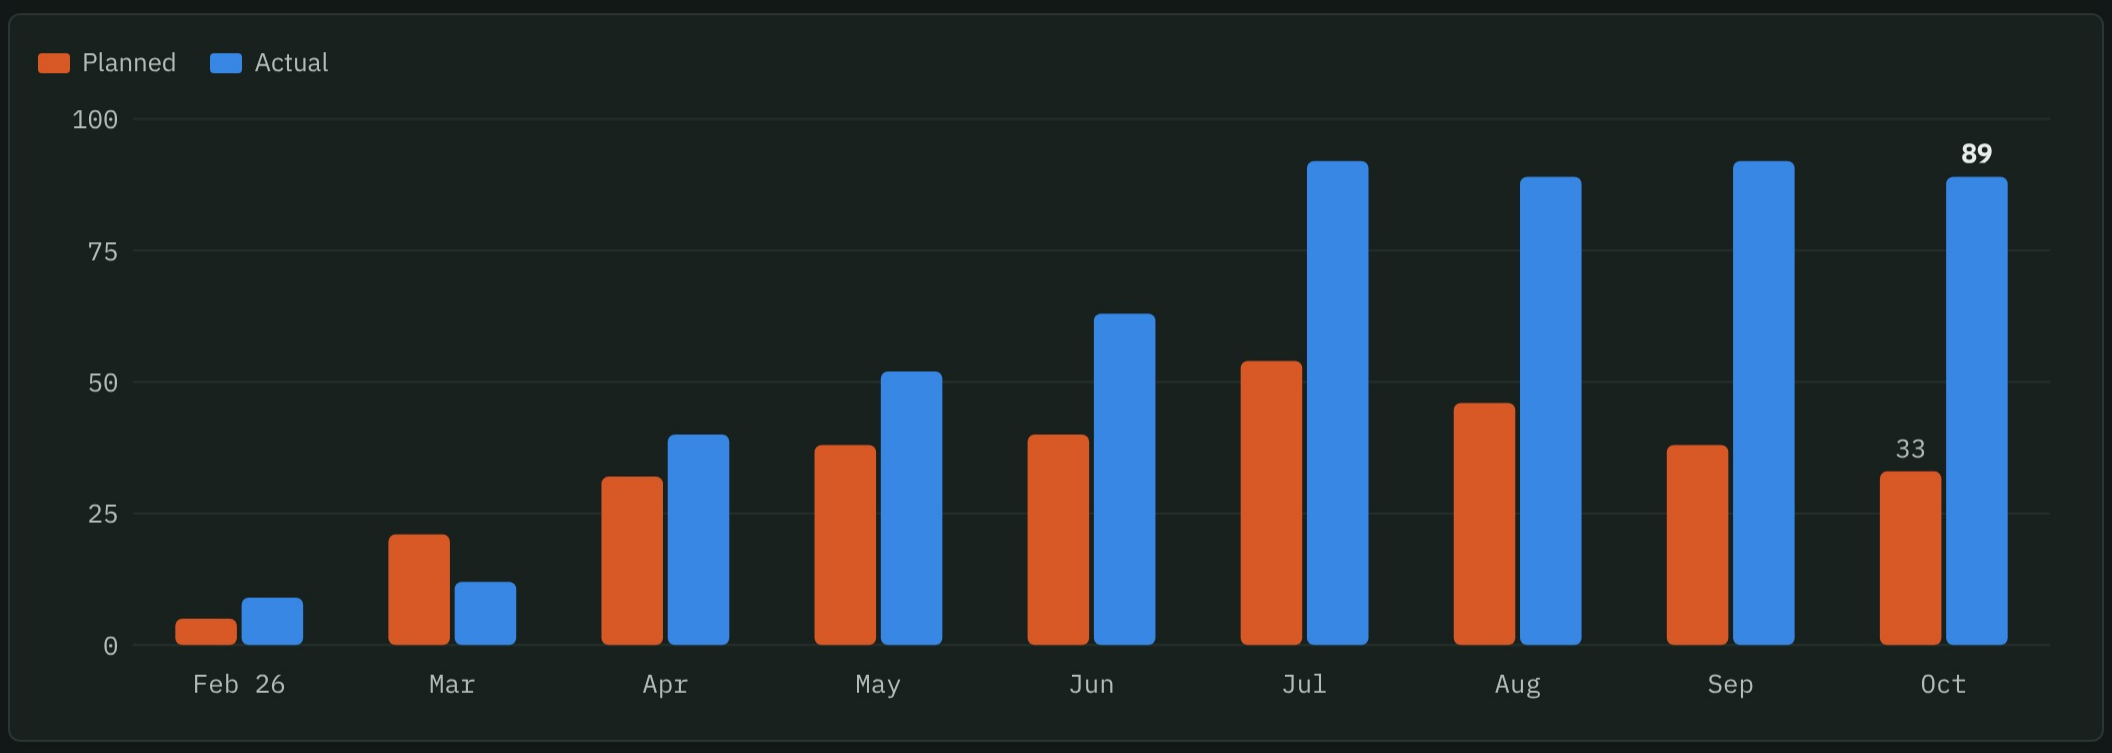

October head count is 89 against 33 planned (16 non-manual and 73 manual). The dashboard of the 01-Nov-2026 report shows 77 manual against 32 planned and no non-manual staff, and the November columns are still empty. Equipment on site in October: 30 against 8 planned.

Cost and invoicing

Contract value

Original contract value (excl. VAT)	35,709,993
Revised contract value	35,709,993
Change orders	0
Potential changes	0

All values in SAR. No contract change orders are registered.

Invoices

Invoices in the log	2
Gross value	3,357,105
Advance payment recovery	−335,711
Deductions and penalties	−38,000
Approved by MODON PM	0
FIR value to date	3,688,354

Invoicing is 9.4% of the contract value against 80.06% physical progress. IPC-01 (2,317,493) and IPC-02 (1,039,612) are approved by the consultant; neither is approved by the MODON PM.

Health, safety and quality

Safety Score 0.95

Safe man-hours (cumulative)	117,530
Man-hours this week	10,000
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Inductions / toolbox talks	248 / 650

MODON HSE inspection no. 30 (29-Oct-2026): 18 items good practice, 5 need improvement, 0 fail.

Quality Score 0.91

FIRs issued / closed / pending	776 / 656 / 120
MIRs issued / closed / pending	99 / 77 / 22
NCRs issued / closed / pending	22 / 10 / 12
Site instructions issued / closed	7 / 6
Shop drawings approved (A+B) / total	333 / 445
Material approvals (A+B) / total	138 / 156

25 shop drawings and 6 material submittals are pending.

Open issues and risks

The issue log of the weekly report has one issue, now closed (Hail work permit, closed 19-Apr-2026). The items below come from the progress, quantity, schedule and risk sheets.

ISSUE	SITE	DETAIL
Air dome works	Qassim, Tabuk	Physical progress 39.96% (Qassim) and 35.13% (Tabuk) against 83.02% and 78.32% planned; no air dome man-hours were earned for the third week running. Air dome materials are 80% delivered.
Schedule slippage	All sites	Forecast handover moved from 07-Feb-2027 (18-Oct report) to 14-Feb-2027 and now 23-Feb-2027. 169 of 301 open activities have negative float, 169 activities are on the critical path and 37 have failed to start (Qassim 13, Hail 8, Tabuk 16).
Landscaping and irrigation	All sites	Lawn not started against 12,539 m² planned to date; 25 mm irrigation pipe at 1,812 of 10,545 m planned. Landscape completion is forecast for 10-Jan-2027 (−20.2 days of float).
Playground surfaces	All sites	Football playground at 4,400 of 7,350 m² and tartan floor at 8,000 of 9,921 m² planned to date.
Procurement	All sites	25 of 57 purchase orders remain to be issued and 8 materials are on site; the curtain wall remainder is at 70–80%.
Soil investigation (risk register)	Tabuk	Open risk: borehole test results take 7–10 days from the laboratory, which may delay the start of excavation.

Data notes

- Progress figures are the weekly report's physical progress (effort), weighted by 33,340 budgeted man-hours, of which 10,000 belong to the “Project milestone” management line. The report's dashboard and the Weekly Progress Report presentation show cost-based progress labelled as actual; this report uses physical progress only.
- The report states “Current Contract Weeks: 0 of 0”, so the week number is counted from site handover (17-Feb-2026): 257 days, week 36.
- The “Weekly Physical Progress” columns hold 77.20% planned and 70.12% earned, which match neither week's to-date figures. Progress this week is taken as the change in to-date progress since the 25-Oct-2026 report.
- All major quantities are identical to the 18-Oct and 25-Oct-2026 reports, although tartan, irrigation and curbstone work was reported; the sheet appears not to have been updated.
- Man-hours by site: Tabuk toilet building still shows 0 of 1,708 man-hours earned with only 40 planned, and Tabuk closeout has no budget but 71.68 man-hours earned.
- The milestone sheet gives complete construction as 06-Feb-2026 with 0 days change, and complete mobilisation as 14-Apr-2026 against 18-Mar-2026 with 0 days change.
- Procurement: the summary has 8 of 57 materials on site, unchanged for two weeks, while the P6 delivery activities are 70–95% complete. The procurement log has no delivered quantities or dates.
- Invoices: the summary shows 0 submitted invoices while the log lists IPC-01 and IPC-02. Paid invoices (3,436,604 SAR) exceed the gross submitted value although none is PM-approved. The dashboard's penalties of −373,711 combine advance payment recovery and deductions.
- Manpower: the dashboard shows 0 non-manual staff against 16 a week earlier, and the November columns of the Manpower sheet are empty. The DB sheet still holds another project's data (HAL1-02-005).
- The P6 update has a data date of 30-Oct-2026, against 01-Nov-2026 for the weekly report; 131 in-progress activities have a finish date before the data date. Three PDFs are named MLTX-05-047 although they belong to MLTX-02-003.
- The contractor forecast in the Physical-Chart Data sheet starts at 0 in February, 365 man-hours below the actual, so it stays slightly below actual until October.

Compiled 03-Nov-2026 from the weekly reports of 18 Oct, 25 Oct and 01 Nov 2026 and the P6 update with data date 30-Oct-2026.
