Land Development of Jeddah Oasis

مشروع تطوير اراضي بواحة جدة

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Al-Enjaz Trading and Contracting Co.	EGIS	Mohammed Alshunaifi	24-Nov-2025	23-May-2027

Scope: roads, storm water piping with catch basins, manholes, box culvert and channels, sewerage network with a sewage lift station, potable water and TSE networks with fire hydrants, 36 kV medium-voltage cables with ring main units, and street lighting. Contract duration 18 months.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. At 96.5% against 77.8% planned under the revised plan, the project is 18.7% ahead. This week it gained only 0.36% against 1.35% planned, and the earthworks-for-plots and road-works milestones, both forecast for 13-Oct-2026, are still open.

PHYSICAL % COMPLETE

96.5% / 77.8% plan

▲ SPI 1.24 +18.7%

PROGRESS THIS WEEK

+0.36% / +1.35% plan

▼ 0.99% below the weekly plan

CONTRACT TIME ELAPSED

60.6% · day 330 of 545

● Forecast finish 19-Jan-2027

INVOICED TO DATE (GROSS)

80.3% · 46.0M SAR

10 invoices, last period ends 18-Oct-2026

Well ahead overall, but this week fell short of plan and two milestones are past their forecast.

The weekly report forecast both the earthworks for plots and the road works to finish on 13-Oct-2026. The P6 update (data date 20-Oct-2026) still shows both as not started, scheduled for the data date, and lists them as failed starts. Project completion is forecast for 19-Jan-2027 in the weekly report and 14-Jan-2027 in P6, both well before the contract date of 23-May-2027.

Site photos this week

Six photos from the progress presentation (Tracking Sheet) of the 20-Oct-2026 weekly report, time-stamped 14 to 19 Oct 2026 where the stamp is visible. Select a photo to view it larger, then use the arrows to move between photos.



Plot backfilling

Rollers compacting fill on a plot. GPS-stamped 19-Oct-2026, 07:06.



Wearing course, Tent Road

Fresh asphalt on Tent Road behind cones and barriers. Stamped 14-Oct-2026, 10:01.



Manhole finishing

Crew finishing a manhole on a marked asphalt road. Stamped 19-Oct-2026, 08:47.



MV cable backfilling, existing area

Backfilled cable route along the boundary wall. Stamped 19-Oct-2026, 11:15.



Sign board installation

New traffic signs at a junction with fresh road markings. Stamped 19-Oct-2026, 11:49.




Pump installation, lift station

Pump pipework inside the wet well. No date stamp.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

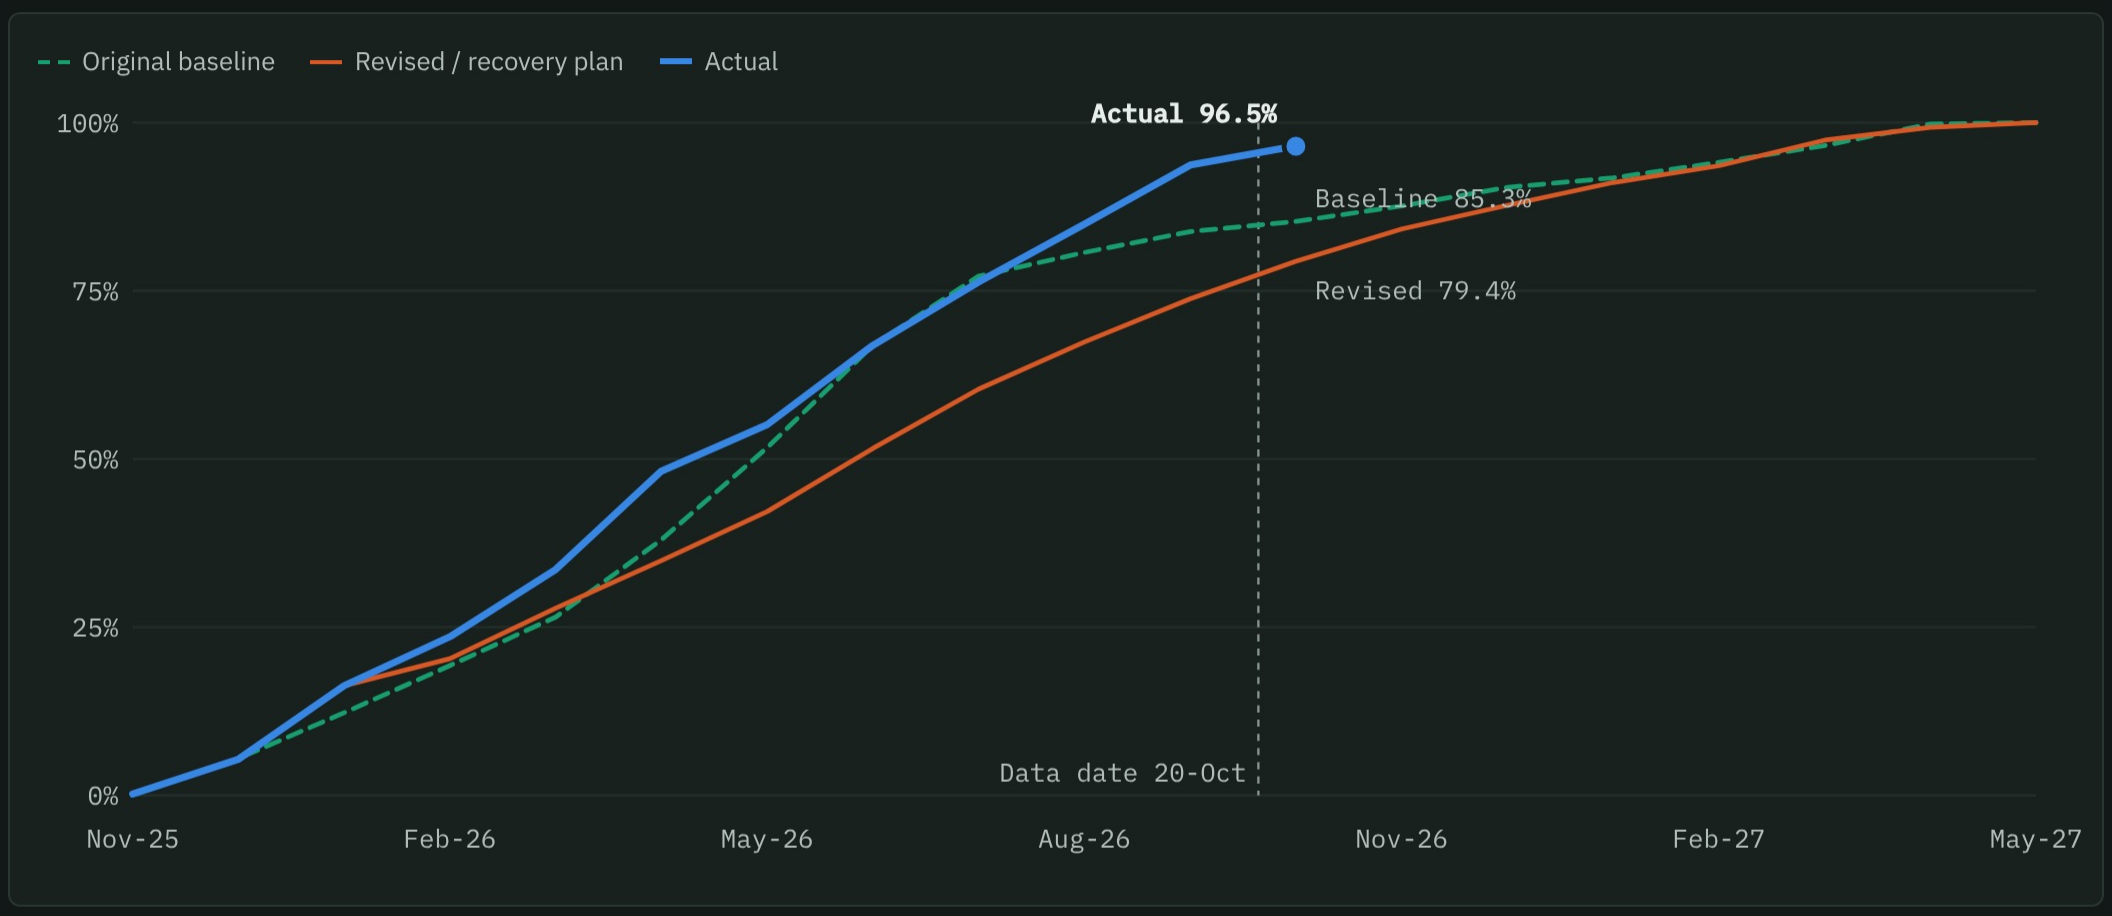

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
13-Oct-2026	76.4	96.1	+19.7%	–	1.26
20-Oct-2026	**77.8**	**96.5**	**+18.7%**	**+0.36%**	**1.24**

Only this week and the previous week's cumulative man-hours are given in the latest report (Progress (2) sheet), so the table has two rows. Planned values follow the revised / recovery plan; the original baseline called for 85.3% by the end of October.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Weekly Progress Report sheet.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Preliminaries	2.1%	100.0%	100.0%	0.0%	1.00	✓ Complete
Engineering	4.5%	99.7%	100.0%	+0.3%	1.00	▲ Ahead
Procurement	20.2%	97.9%	102.2%	+4.3%	1.04	▲ Ahead
Road works	13.1%	75.8%	106.1%	+30.3%	1.40	▲ Ahead
Electrical works	14.4%	41.0%	84.0%	+43.0%	2.05	▲ Ahead
Demolition works	3.6%	109.5%	109.5%	0.0%	1.00	✓ Complete
Storm water network	7.2%	92.7%	102.8%	+10.1%	1.11	▲ Ahead
Plots	3.1%	82.5%	111.7%	+29.2%	1.35	▲ Ahead
Sewer network	6.0%	84.2%	84.2%	0.0%	1.00	● On plan
TSE network	9.7%	84.6%	94.1%	+9.5%	1.11	▲ Ahead
Potable water network	7.7%	74.3%	86.8%	+12.5%	1.17	▲ Ahead
Sewage lift station	3.8%	12.9%	87.8%	+74.9%	6.80	▲ Ahead
Box culvert	0.5%	114.3%	114.3%	0.0%	1.00	✓ Complete
Open drain channel	1.2%	128.1%	128.1%	0.0%	1.00	✓ Complete
Underpass	0.3%	100.0%	100.0%	0.0%	1.00	✓ Complete
Testing & commissioning	2.4%	13.1%	68.6%	+55.5%	5.24	▲ Ahead
Total	100%	**77.8%**	**96.5%**	**+18.7%**	**1.24**	▲ Ahead

Seven phases report more earned man-hours than budgeted (above 100%). The P6 update (data date 20-Oct-2026) has 1,218 activities: 1,176 completed, 24 in progress and 18 not started. Its scheduled finish is 14-Jan-2027, 129 days before the contract date.

Scope of work: quantities

Total quantity, quantity finished to date and quantity remaining for the main BOQ items, from the Major Quantities sheet of the 20-Oct-2026 weekly report. The report gives no previous-week quantities, so the "This week" column is blank.

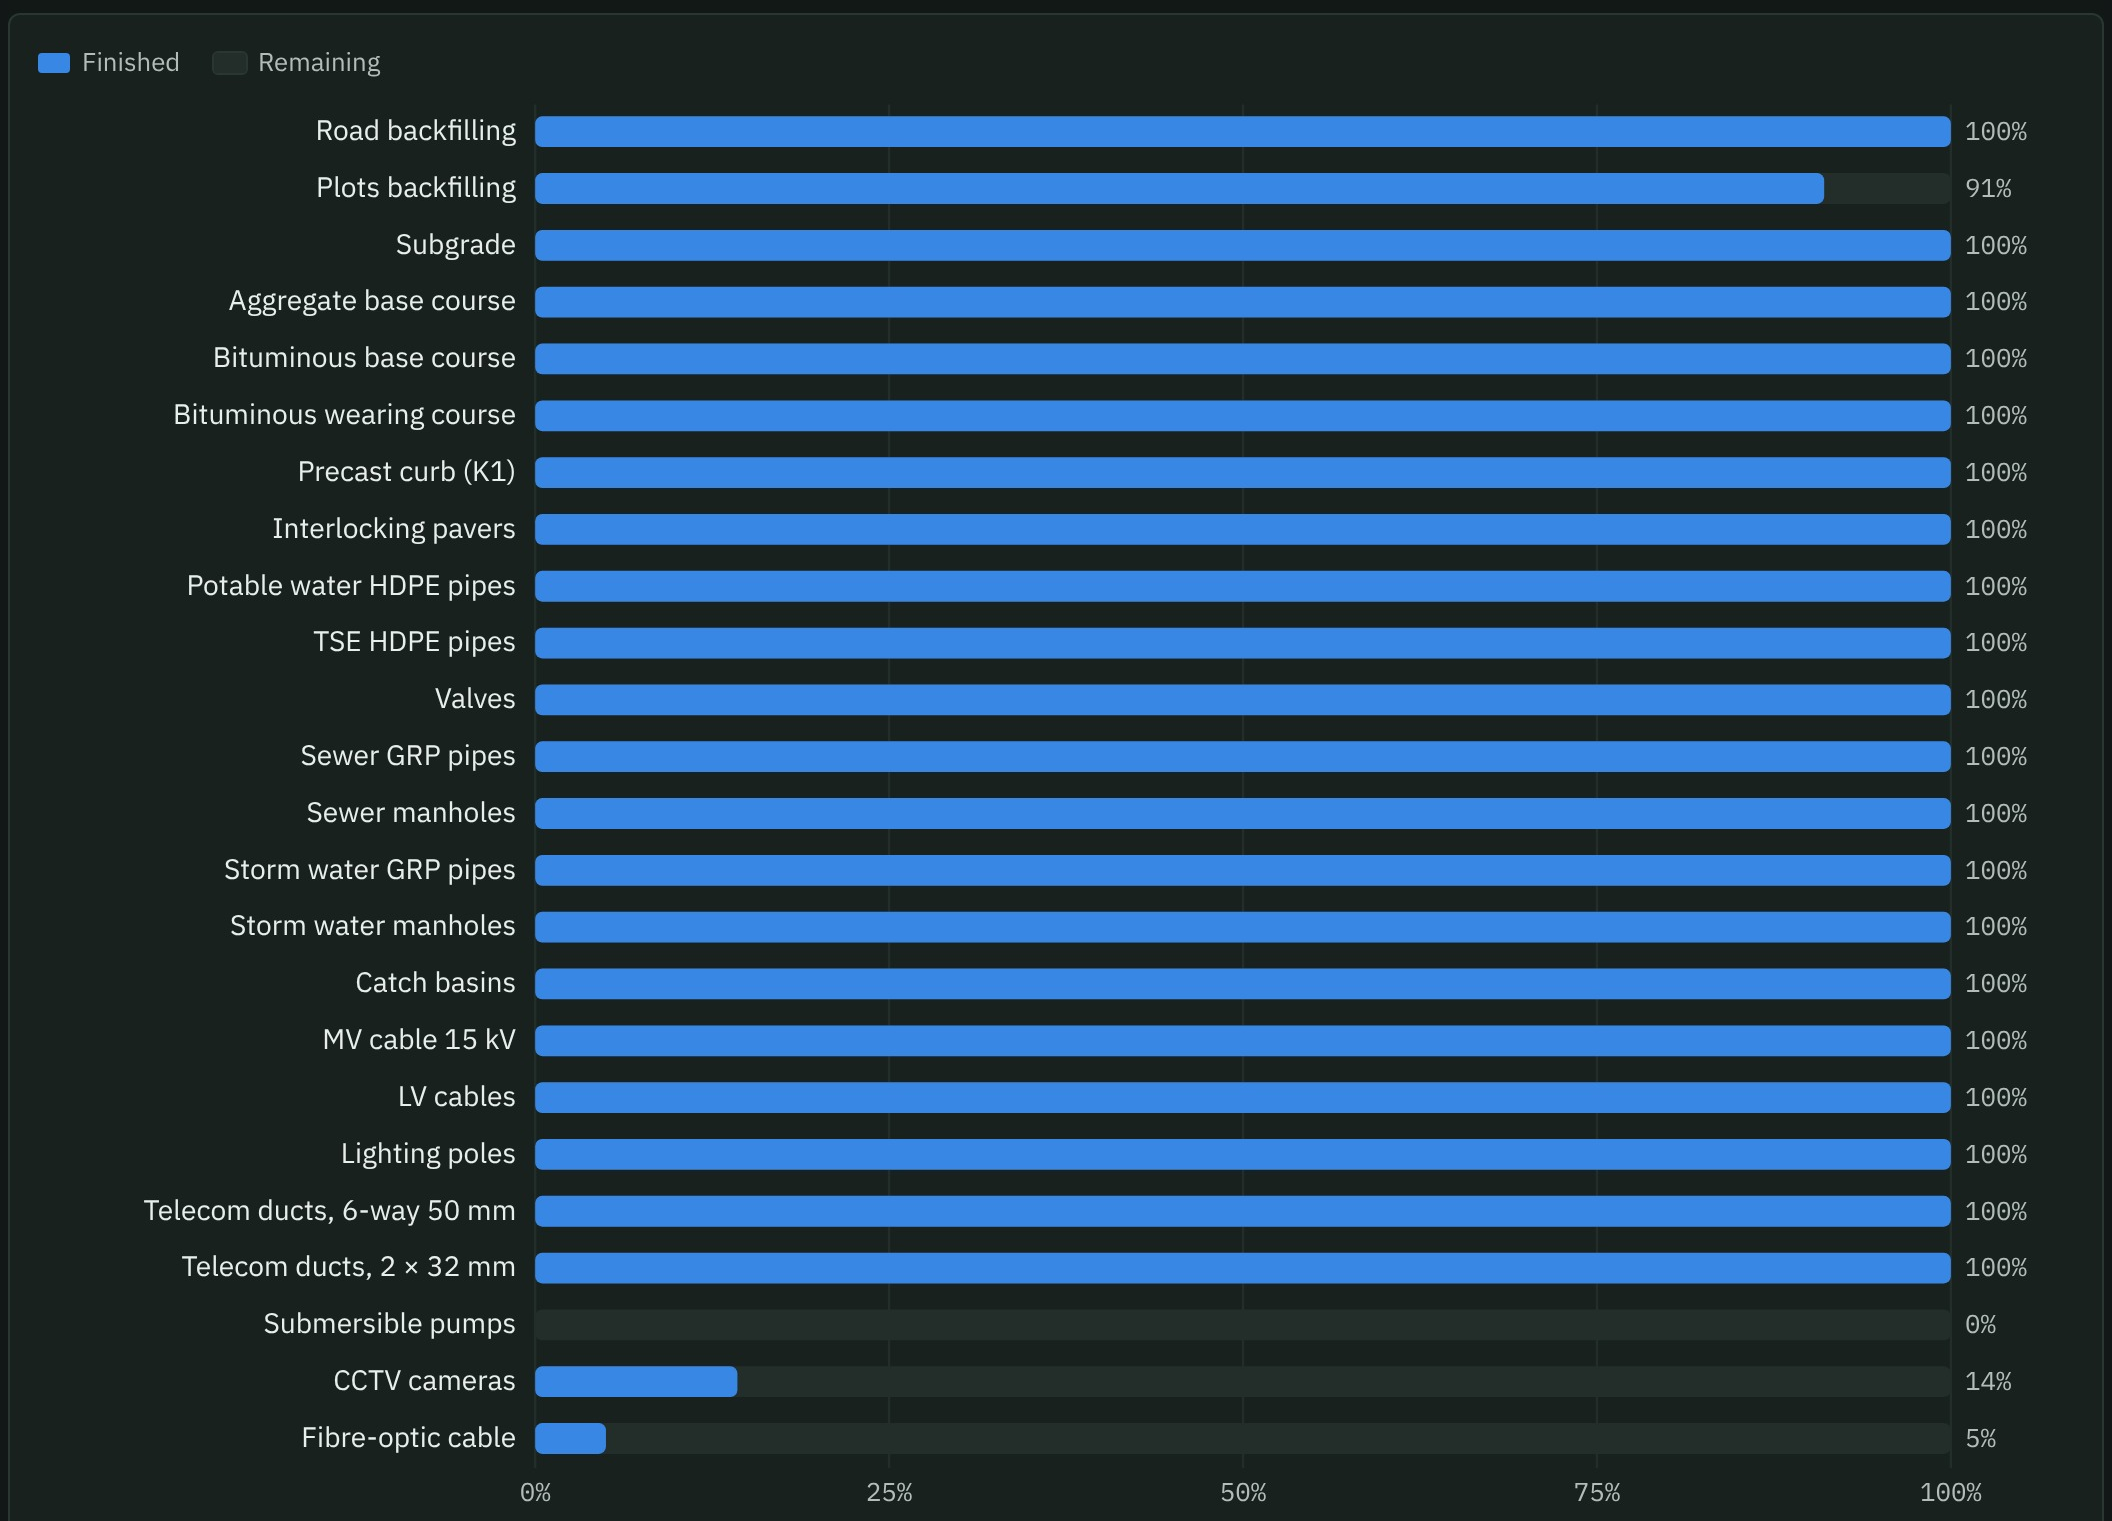

SCOPE ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Road backfilling	m³	329,707	329,707	–	0	100.0%
Plots backfilling	m³	718,628	654,314	–	64,314	91.1%
Subgrade	m³	30,812	30,812	–	0	100.0%
Aggregate base course	m³	19,162	19,162	–	0	100.0%
Bituminous base course	m³	7,129	7,129	–	0	100.0%
Bituminous wearing course	m³	4,052	4,052	–	0	100.0%
Precast curb (K1)	m³	22,496	22,496	–	0	100.0%
Interlocking pavers	m²	12,677	12,677	–	0	100.0%
Potable water HDPE pipes	m	4,025	4,025	–	0	100.0%
TSE HDPE pipes	m	4,209	4,209	–	0	100.0%
Valves	nr	77	77	–	0	100.0%
Sewer GRP pipes	m	2,735	2,735	–	0	100.0%
Sewer manholes	nr	45	45	–	0	100.0%
Storm water GRP pipes	m	3,971	3,971	–	0	100.0%

SCOPE ITEM	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Storm water manholes	nr	42	42	–	0	100.0%
Catch basins	nr	77	77	–	0	100.0%
MV cable 15 kV	m²	5,632	5,632	–	0	100.0%
LV cables	m	6,457	6,457	–	0	100.0%
Lighting poles	nr	258	258	–	0	100.0%
Telecom ducts, 6-way 50 mm	m	6,424	6,424	–	0	100.0%
Telecom ducts, 2 × 32 mm	m	4,604	4,604	–	0	100.0%
Submersible pumps	nr	2	0	–	2	0.0%
CCTV cameras	nr	7	1	–	6	14.3%
Fibre-optic cable	m	20	1	–	19	5.0%

Networks: all lengths installed

The Progress Summary sheet shows every network fully installed: roads 5,657 m, MV 13,171 m, street lighting 9,910 m, telecom 11,025 m, potable water 4,025 m, TSE 4,209 m, sewer 2,735 m and storm water 3,791 m.

Still open

Plot backfilling is at 91% (64,314 m³ remaining). At the lift station, the 2 submersible pumps are reported as not installed, 1 of 7 CCTV cameras is in place and 1 of 20 m of fibre-optic cable.

Milestones

The weekly report and the P6 schedule update give different forecasts for the open milestones. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Site handover	24-Nov-2025	24-Nov-2025	24-Nov-2025 (actual)	–	✓ Done
Complete mobilisation	23-Dec-2025	23-Dec-2025	23-Dec-2025 (actual)	–	✓ Done
Long-lead items ordered	21-Nov-2026	14-Jul-2026	–	–	✓ Done
Sewerage network	22-Jul-2026	–	26-Aug-2026 (actual)	–	✓ Done
TSE network	23-Nov-2026	–	30-Aug-2026 (actual)	–	✓ Done
Potable water network	23-Nov-2026	05-Sep-2026	05-Sep-2026 (actual)	–	✓ Done
Delivery of all equipment and materials	31-Dec-2026	06-Oct-2026	–	–	? Conflicts with procurement log
Earthworks and site grading for plots	23-Mar-2026	13-Oct-2026	20-Oct-2026	102	▼ Late
Road works	22-Sep-2026	13-Oct-2026	20-Oct-2026	155	▼ Late
Electrical (MV) networks	06-May-2027	13-Oct-2026	19-Nov-2026	140	? Forecasts disagree
All works complete, ready for initial handover	23-May-2027	06-Jan-2027	30-Dec-2026	115	● On time

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project completion / demobilisation	23-May-2027	19-Jan-2027	14-Jan-2027	102	On time

Three weekly-report forecasts of 13-Oct-2026 have passed without completion.

Earthworks for plots and road works were forecast for 13-Oct-2026; P6 still shows both as not started and on the failed start list, moved to the data date of 20-Oct-2026. The electrical networks were also forecast for 13-Oct-2026 in the weekly report, but P6 plans them for 19-Nov-2026. Baseline dates are from the weekly report's Milestones sheet; the sewerage and TSE baselines are the P6 baseline finishes.

Procurement of key materials

Long-lead materials on site by discipline. Source: Procurement Summary, weekly report 20-Oct-2026.



Lift station equipment: 9 items still "under manufacturing"


Pumps, MCCB (VFD), local control panels, generator, capacitor bank, PLC, process instrumentation, flow meter and ATS. Most were due on site by 15-Sep-2026. This week's work list reports MCC panel, PLC and pump installation at the lift station, so the log may not be up to date.

Enclosed switches and circuit breakers: 4 of 7

The only item below 100% in the procurement log; it is marked as in progress. The other 26 items are completed.

Manpower

Monthly head count on site (manual and non-manual), planned vs actual. Source: Manpower sheet.

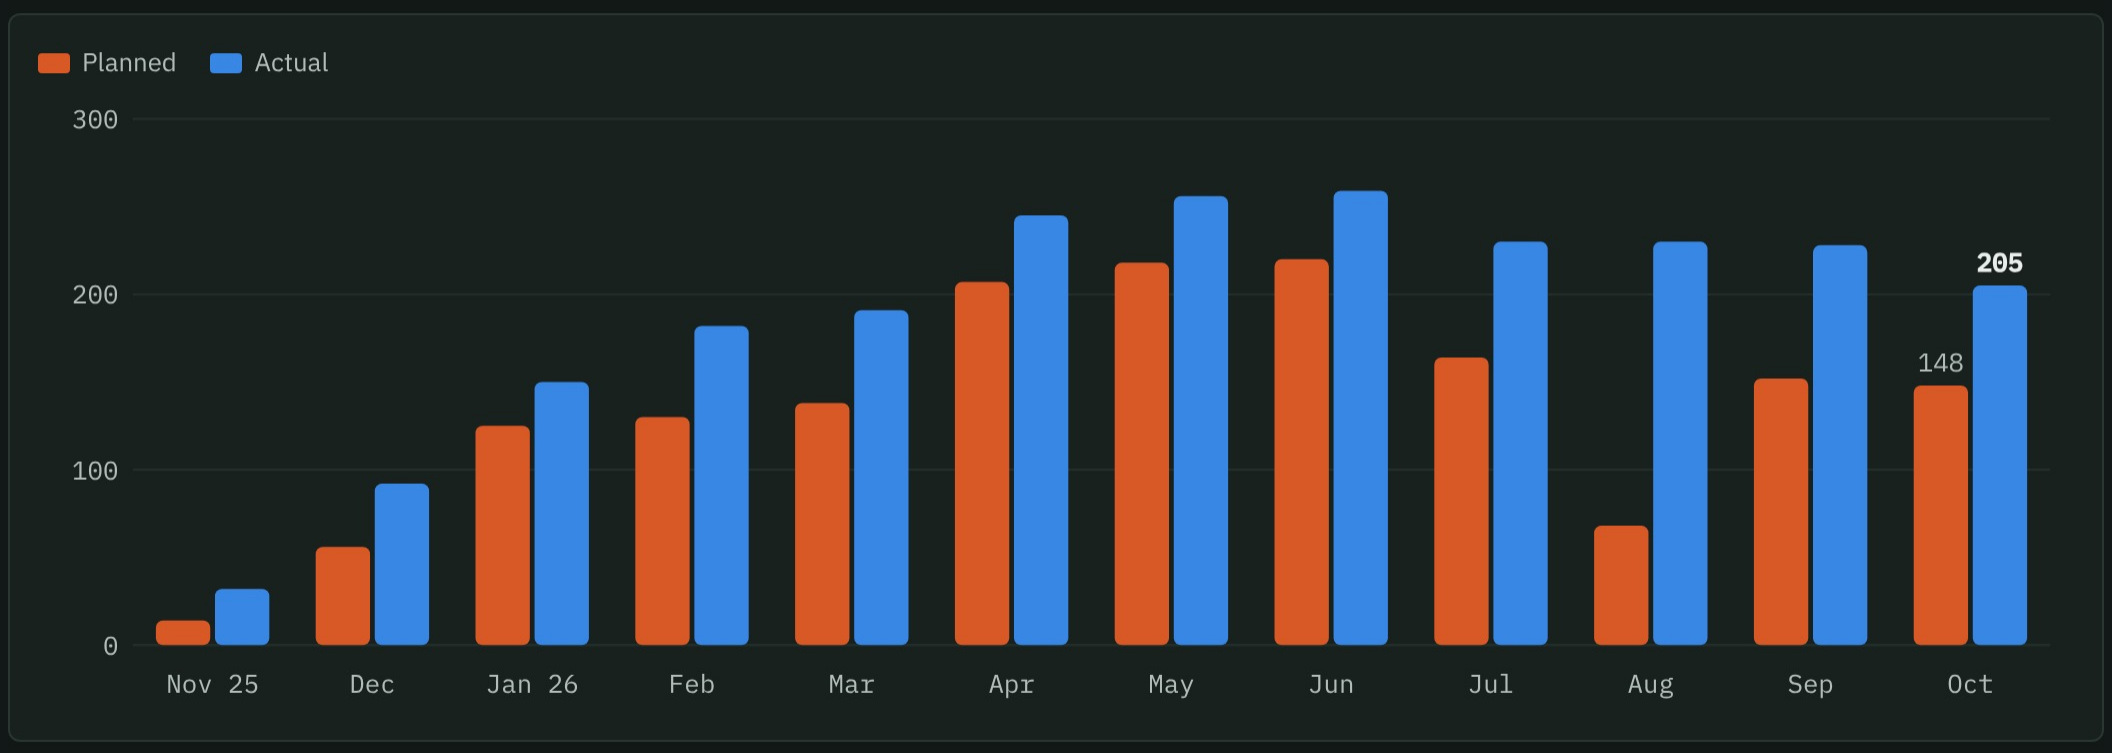

October head count is 205 (49 non-manual, 156 manual) against 148 planned. Equipment on site in October: 76 against 75 planned.

Cost and invoicing

Contract value

Road works	31,180,897
Electrical and telecom network	8,774,396
Storm water network	5,894,425
Lift station	3,284,426
TSE network	2,885,131
Sewage network	2,756,313
Potable water network	2,528,760
BOQ total (excl. VAT)	**57,304,348**
Contract value incl. 15% VAT	65,900,000
Change orders	0

All values in SAR. Breakdown from the Progress Summary sheet. No change orders or potential changes are registered.

Invoices

Invoices submitted	10
Gross value	45,992,129
Net incl. VAT	52,890,948
Approved by MODON PM (7)	33,617,268
Paid to date	27,469,389
Retention / deductions	0 / 0
FIR value to date	54,882,530

Gross invoicing is 80.3% of the contract value against 96.5% physical progress. All 10 invoices are approved by the consultant; invoices 8 to 10 are not yet approved by MODON. The amount paid equals invoices 1 to 6.

Health, safety and quality

Safety Score 0.88

Safe man-hours (cumulative)	515,278
Man-hours this week	10,512
Lost-time injuries	0
Fatalities	0
First-aid cases	0
Near misses	0
Property damage	0
Inductions / toolbox talks	81 / 44

Quality Score 0.85

FIRs issued / closed (cumulative)	1,571 / 1,551
FIRs pending	20
NCRs issued / closed	43 / 43
Site instructions issued / closed	10 / 10
MIRs issued / closed	116 / 116
Shop drawings processed	394
Materials approved	146

Network tests are complete for sewerage, potable water, storm water and TSE. Road testing is at 10%; the lift station and electrical network tests have not started.

Open issues and risks

ISSUE	STATUS	DETAIL
Scope reduction, Road No. 6	Closed 25-Jan-2026	Road No. 6 and its utility networks were removed from the scope; a new scope of work covering all ongoing activities was issued.
Rock protection, wadi channel and box culvert	Closed 25-Jan-2026	The scope had no rock protection at the culvert inlet and outlet or along the wadi; a decision on grouted riprap was needed.
Wadi channel vs culvert width	Closed 30-Dec-2025	The 15 m wadi bed is much wider than the 6.7 m culvert CU-02; the IFC drawings are followed.
Existing underpasses	Closed 25-Jan-2026	To avoid leakage and odour, the underpass concrete is removed completely and backfilled.
MV network materials and quantities	Closed 30-Apr-2026	Approval of MV materials and quantities by SEC and MODON.
Safety: deep openings, heat stress, traffic	Closed	Hard barriers, summer work break, flagmen and signboards in place.

Every item in the issue log (8 issues) and the risk register (7 risks) is closed, and the challenges box in the Tracking Sheet is empty. What remains open, from the other sheets: the earthworks-for-plots and road-works milestones, the lift station equipment, 20 pending FIRs, and the road, lift station and electrical tests.

Data notes

- The weekly report's headline, the Tracking Sheet and the summary sheets use cost-based earned value: 95.17% actual against 61.39% planned. This report uses physical progress (man-hours): 96.5% against 77.75%. The Look Ahead file gives 78.06% achieved at the end of Q3 2026 against a 77% target, on a basis that is not stated.
- The report states its own week number (Report No. 48, Week-48), which is used here. Counting whole weeks from site handover (24-Nov-2025 to 20-Oct-2026, 330 days) gives week 47.
- This-week values: the latest report gives only this week's and last week's cumulative man-hours, so the S-curve table has two rows, and it gives no previous-week quantities, so "This week" in the scope table is blank.
- Earned man-hours exceed the budget in seven phases (up to 128% for the open drain channel), and planned man-hours also exceed the budget in three of them. The baseline and revised plans use different totals (406,229 and 406,774 man-hours). The forecast column of the Physical-Chart Data sheet shows 93.7% for October, below the 96.5% actual.
- The milestone "Complete delivery of all equipment and materials" is marked achieved on 06-Oct-2026, but the procurement log has 9 items "under manufacturing" and one at 4 of 7, and the Procurement Summary has 27 of 34 materials on site. The log lists 36 items, the summary 34.
- Completion dates differ between files: 19-Jan-2027 (weekly report forecast), 14-Jan-2027 (P6), 23-Nov-2026 (Tracking Sheet target and Look Ahead), and 23-May-2026 as the contract end in the "work done this week" file (the contract end is 23-May-2027).
- Milestone baselines differ between the Milestones sheet and P6: electrical networks 06-May-2027 vs 04-Jan-2027, project completion 23-May-2027 vs 14-Jun-2027.
- Scope quantities disagree between sheets: storm water 3,791 m (Progress Summary) vs 3,971 m of GRP pipe (Major Quantities); MV network 13,171 m vs 5,632 of 15 kV cable. The Major Quantities sheet gives curbs in m³ and MV cable in m². Telecom supply shows 6,395 m delivered against 11,025 m installed.
- Shop drawing totals differ: 394 (dashboard), 703 (Quality-Stat sheet) and 621 (Tracking Sheet).
- Manpower for October: the dashboard shows 61 planned and 181 actual manual workers (by trade), the Manpower sheet 136 and 156.
- Other files name the consultant EGIS as contractor (Look Ahead), give the PM as Abdullah Alshunaifi, and place the project in the central sector instead of the western sector. The invoice summary counts 3 paid invoices, but the paid amount equals invoices 1 to 6. Several cells show #REF ! (issue owners, EAC). The FIR summary has dates such as 25-Aug-2062.

Compiled 28-Oct-2026 from the weekly report for the week ending 20-Oct-2026 (W3 upload).
