


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
02-11-2026		440	20-May-26 A	17-Nov-27	98	33,781,495	22,186,673	84,583,109
JDH3-02-009-Al-Khorayef Factory Road		75	03-Nov-26	28-Jan-27	340	54,099	0	381,418
Construction		75	03-Nov-26	28-Jan-27	340	54,099	0	381,418
JDH3-02-009-KF-Sewage Network- SW		24	02-Jan-27	28-Jan-27	272	0	0	33,630
JDH3-02-009-R151-(SW)-GRP Pipes-150 mm diameter depth from 1.5		18	09-Jan-27	28-Jan-27	169	0	0	23,980
JDI	Bedding Works for GRP Pipe Line 200 mm - depth from 0 to 1.:	6	09-Jan-27	14-Jan-27	169	0	0	1,713
JDI	Installing for GRP Pipe Line 200 mm - depth from 0 to 1.5 m- (E	6	16-Jan-27	21-Jan-27	169	0	0	18,841
JDI	Primary Test for GRP Pipe Line 200 mm - depth from 0 to 1.5 m	6	23-Jan-27	28-Jan-27	169	0	0	3,426
JDH3-02-009-R151-(SW)-MH Works depth from 0 to 1.50 Diam 1200 m		11	02-Jan-27	13-Jan-27	285	0	0	9,650
JDI	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	9	02-Jan-27	11-Jan-27	285	0	0	7,506
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	12-Jan-27	13-Jan-27	285	0	0	2,144
JDH3-02-009-KF-Storm Network - ST		18	03-Nov-26	23-Nov-26	397	54,099	0	54,099
JDH3-02-009-KF-(ST)-MH Works (1200) mm diameter depth from 1.50		4	15-Nov-26	18-Nov-26	169	1,052	0	1,052
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	15-Nov-26	16-Nov-26	169	701	0	701
JDI	Steel Coverfor MH 1200 mm - depth from 1.50 to 2.0 m- (B6.33	2	17-Nov-26	18-Nov-26	169	351	0	351
JDH3-02-009-KF-(ST)-MH Works (1200) mm diameter depth from 2.01		4	17-Nov-26	21-Nov-26	169	3,217	0	3,217
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	17-Nov-26	18-Nov-26	169	2,144	0	2,144
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.5 m- (B6.33	2	19-Nov-26	21-Nov-26	169	1,072	0	1,072
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 2.01		4	03-Nov-26	07-Nov-26	403	4,513	0	4,513
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	169	3,009	0	3,009
JDI	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	403	1,504	0	1,504
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 2.51		4	05-Nov-26	09-Nov-26	403	13,509	0	13,509
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	05-Nov-26	07-Nov-26	169	9,006	0	9,006
JDI	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2	08-Nov-26	09-Nov-26	403	4,503	0	4,503
JDH3-02-009-KF-(ST)-MH Works (1500) mm diameter depth from 3.01		4	19-Nov-26	23-Nov-26	169	1,819	0	1,819
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	19-Nov-26	21-Nov-26	169	1,213	0	1,213
JDI	Steel Coverfor MH 1500 mm - depth from 3.01 to 3.5 m- (B6.33	2	22-Nov-26	23-Nov-26	169	606	0	606
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 2.01		2	22-Nov-26	23-Nov-26	169	1,367	0	1,367
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	22-Nov-26	23-Nov-26	169	1,367	0	1,367
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 2.51		4	08-Nov-26	11-Nov-26	403	15,605	0	15,605
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	08-Nov-26	09-Nov-26	169	10,403	0	10,403
JDI	Steel Coverfor MH 2000 mm - depth from 2.51 to 3.00 m- (B6.3	2	10-Nov-26	11-Nov-26	403	5,202	0	5,202
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 3.01		4	12-Nov-26	16-Nov-26	403	2,400	0	2,400
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	12-Nov-26	14-Nov-26	169	1,600	0	1,600
JDI	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2	15-Nov-26	16-Nov-26	403	800	0	800
JDH3-02-009-KF-(ST)-MH Works (2000) mm diameter depth from 4.01		4	10-Nov-26	14-Nov-26	403	10,617	0	10,617
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	10-Nov-26	11-Nov-26	169	7,078	0	7,078
JDI	Steel Coverfor MH 2000 mm - depth from 4.01 to 4.50 m- (B6.3	2	12-Nov-26	14-Nov-26	403	3,539	0	3,539
JDH3-02-009-KF-Potable Water Network - WT		14	17-Dec-26	02-Jan-27	363	0	0	156,791
JDH3-02-009-R16-(WT)-HDPE Pipes-160 mm diameter depth from 0 to		12	17-Dec-26	30-Dec-26	363	0	0	31,953
JDI	Primary Test for HDPE Pipe Line 160 mm - depth from 0 to 1.5	6	17-Dec-26	23-Dec-26	363	0	0	15,976
JDI	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	6	24-Dec-26	30-Dec-26	363	0	0	15,976
JDH3-02-009-R16-(WT)-Gate Valve-150 mm on pipe dia (160) mm		4	17-Dec-26	21-Dec-26	363	0	0	17,265
JDI	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B3.33	2	17-Dec-26	19-Dec-26	363	0	0	15,539
JDI	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 mi	2	20-Dec-26	21-Dec-26	363	0	0	1,727
JDH3-02-009-R08-(WT)-Wash-Out Valve-100 mm on pipe dia (160) mm		2	22-Dec-26	23-Dec-26	363	0	0	752
JDI	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2	22-Dec-26	23-Dec-26	363	0	0	752
JDH3-02-009-R08-(WT)-Wash-Out Valve-100 mm on pipe dia (225) mm		2	24-Dec-26	26-Dec-26	363	0	0	767
JDI	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2	24-Dec-26	26-Dec-26	363	0	0	767
JDH3-02-009-R08-(WT)-Wash-Out Chamber on 160 mm dia pipeline d		2	27-Dec-26	28-Dec-26	363	0	0	4,173
JDI	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - c	2	27-Dec-26	28-Dec-26	363	0	0	4,173
JDH3-02-009-R08-(WT)-Wash-Out Chamber on 225 mm dia pipeline d		2	29-Dec-26	30-Dec-26	363	0	0	4,173

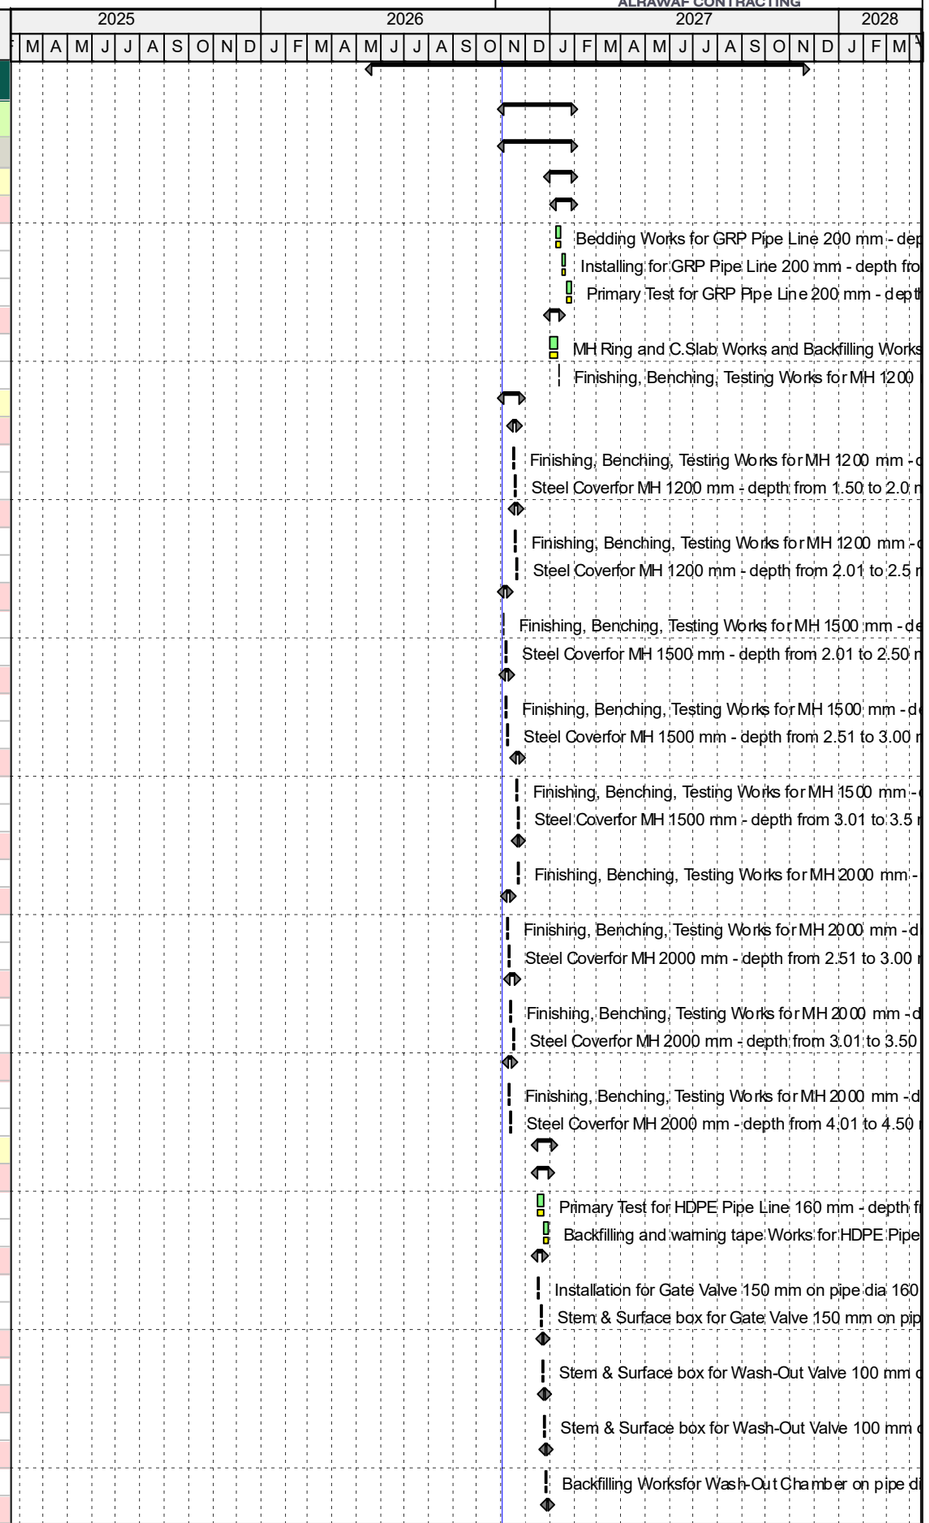


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - (	2	29-Dec-26	30-Dec-26	363	0	0	4,173
JDH3-02-009-R08-(WT)-Fire Hydrant		12	20-Dec-26	02-Jan-27	363	0	0	97,708
JDH	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	20-Dec-26	21-Dec-26	365	0	0	9,771
JDH	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-WT	2	22-Dec-26	23-Dec-26	365	0	0	19,542
JDH	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-WT	2	24-Dec-26	26-Dec-26	365	0	0	29,312
JDH	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-WT	2	27-Dec-26	28-Dec-26	365	0	0	34,198
JDH	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-W	2	31-Dec-26	02-Jan-27	363	0	0	4,885
JDH3-02-009-KF-TSE Network - TSE		13	03-Dec-26	17-Dec-26	358	0	0	136,898
JDH3-02-009-R151-(TSE)-HDPE Pipes-160 mm diameter depth from 1		13	03-Dec-26	17-Dec-26	358	0	0	133,862
JDH	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51	3	03-Dec-26	06-Dec-26	358	0	0	11,155
JDH	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5	10	07-Dec-26	17-Dec-26	358	0	0	122,707
JDH3-02-009-R152-(TSE)-HDPE Pipes-110 mm diameter depth from 0		8	03-Dec-26	12-Dec-26	349	0	0	3,037
JDH	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 to	4	03-Dec-26	07-Dec-26	349	0	0	2,429
JDH	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4	08-Dec-26	12-Dec-26	349	0	0	607
JDH3-02-009-New Roads - NR		152	03-Sep-26 A	01-Mar-27	314	1,799,781	441,257	2,468,934
A-MCG		101	20-Oct-26 A	01-Mar-27	310	266,457	107,652	931,780
JDH3-02-009-AMCG-Storm Network- ST		12	03-Nov-26	16-Nov-26	359	27,232	0	32,515
JDH3-02-009-AMCG-(ST)-MH Works (1500) mm diameter depth from 2		4	03-Nov-26	07-Nov-26	359	1,560	0	1,560
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	359	1,003	0	1,003
JDH	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	359	557	0	557
JDH3-02-009-AMCG-(ST)-MH Works (1200) mm diameter depth from 2		4	05-Nov-26	09-Nov-26	359	1,112	0	1,112
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	05-Nov-26	07-Nov-26	359	715	0	715
JDH	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2	08-Nov-26	09-Nov-26	359	397	0	397
JDH3-02-009-AMCG-(ST)-MH Works (1500) mm diameter depth from 2		4	08-Nov-26	11-Nov-26	359	1,751	0	1,751
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	08-Nov-26	09-Nov-26	359	1,126	0	1,126
JDH	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2	10-Nov-26	11-Nov-26	359	625	0	625
JDH3-02-009-AMCG-(ST)-MH Works (2000) mm diameter depth from 3		4	10-Nov-26	14-Nov-26	359	2,489	0	2,489
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	10-Nov-26	11-Nov-26	359	1,600	0	1,600
JDH	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2	12-Nov-26	14-Nov-26	359	889	0	889
JDH3-02-009-AMCG-(ST)-MH Works (2000) mm diameter depth from 3		4	12-Nov-26	16-Nov-26	359	20,320	0	25,603
JDH	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	12-Nov-26	14-Nov-26	359	17,068	0	17,068
JDH	Steel Coverfor MH 2000 mm - depth from 3.51 to 4.0- (B6.33 05	2	15-Nov-26	16-Nov-26	359	3,251	0	8,534
JDH3-02-009-AMCG-Road Works - RD		69	20-Oct-26 A	01-Mar-27	310	239,226	107,652	899,265
JDH3(	Supply and installation Traffic signs 1 Sheet with Single post - (E	7	16-Feb-27	24-Feb-27	310	0	0	6,540
JDH3-02-009-AMCG-(RD)-Aggregate Base Course		2	20-Oct-26 A	23-Dec-26	287	239,226	107,652	239,226
JDH	Supply, lay and compaction Aggregate base course compacted	2	20-Oct-26 A	23-Dec-26	287	239,226	107,652	239,226
JDH3-02-009-AMCG-(RD)-Bituminous concrete wearing course 50 mn		6	09-Feb-27	15-Feb-27	310	0	0	415,000
JDH	Supply, lay and compaction Asphaltic wearing course 50 mm in	6	09-Feb-27	15-Feb-27	310	0	0	415,000
JDH3-02-009-AMCG-(RD)-Precast Concrete Curb		4	25-Feb-27	01-Mar-27	310	0	0	1,131
JDH	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	25-Feb-27	01-Mar-27	310	0	0	1,131
JDH3-02-009-AMCG-(RD)-Precast Interlocking Block Pavers		12	09-Feb-27	23-Feb-27	287	0	0	237,368
JDH	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12	09-Feb-27	23-Feb-27	287	0	0	237,368
A-MCH		6	03-Nov-26	09-Nov-26	409	3,742	0	3,742
JDH3-02-009-AMCH-Earthworks - EW		2	03-Nov-26	04-Nov-26	370	38	0	38
JDH3(	Backfill Layers with Imported Material Side Walk for Road - (B1.3	2	03-Nov-26	04-Nov-26	370	38	0	38
JDH3-02-009-AMCH-Storm Network - ST		6	03-Nov-26	09-Nov-26	409	3,704	0	3,704
JDH3-02-009-AMCH-(ST)-MH Works (1500) mm diameter depth from 2		4	03-Nov-26	07-Nov-26	409	1,560	0	1,560
JDH	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	409	1,003	0	1,003
JDH	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	409	557	0	557
JDH3-02-009-AMCH-(ST)-MH Works (1200) mm diameter depth from 2		4	05-Nov-26	09-Nov-26	409	2,144	0	2,144
JDH	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	05-Nov-26	07-Nov-26	409	1,430	0	1,430
JDH	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2	08-Nov-26	09-Nov-26	409	715	0	715

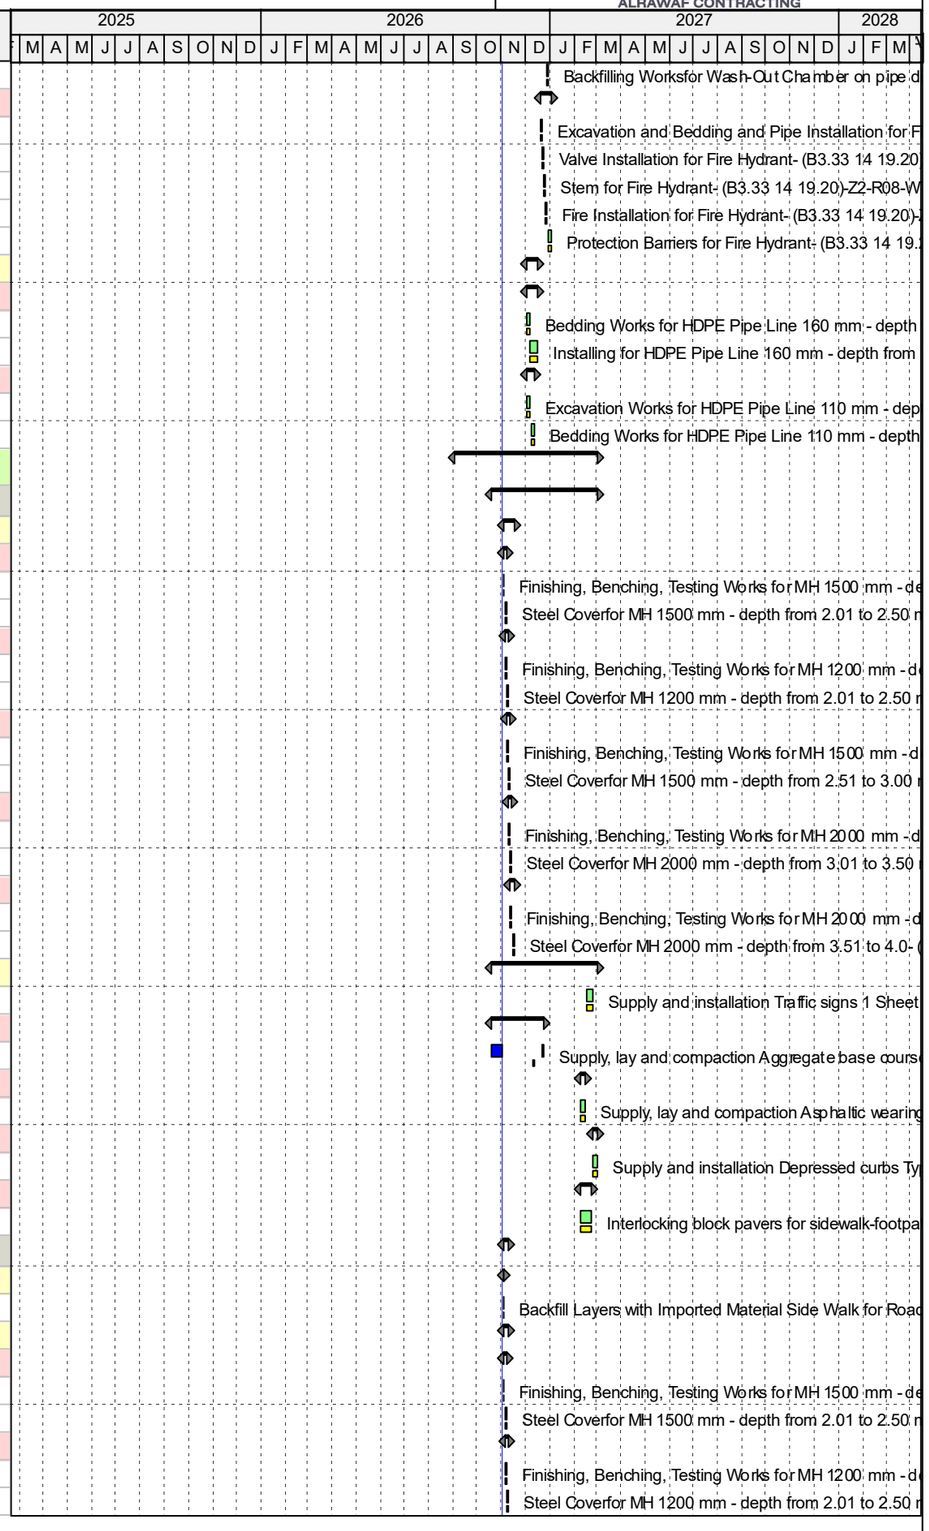

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
A-MCA		139	03-Sep-26 A	13-Feb-27	327	1,323,094	333,606	1,326,924
JDH3-02-009-AMCA-Sewage Network - SW		71	03-Sep-26 A	25-Nov-26	395	236,115	75,694	236,115
JDH3-02-009-AMCA-(SW)-GRP Pipes-150 mm diameter depth from 1.5		20	03-Nov-26	25-Nov-26	371	25,222	0	25,222
JDI	Excavation Works for GRP Pipe Line 150 mm - depth from 1.51	2	03-Nov-26	04-Nov-26	363	5,044	0	5,044
JDI	Bedding Works for GRP Pipe Line 150 mm - depth from 1.51 to	3	05-Nov-26	08-Nov-26	363	1,261	0	1,261
JDI	Installing for GRP Pipe Line 150 mm - depth from 1.51 to 2.5 m	3	09-Nov-26	11-Nov-26	363	13,872	0	13,872
JDI	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	6	12-Nov-26	18-Nov-26	363	2,522	0	2,522
JDI	Backfilling and warning tape Works for GRP Pipe Line 150 mm	6	19-Nov-26	25-Nov-26	371	2,522	0	2,522
JDH3-02-009-AMCA-(SW)-GRP Pipes-150 mm diameter depth from 2.5		5	19-Nov-26	24-Nov-26	363	5,308	0	5,308
JDI	Excavation Works for GRP Pipe Line 150 mm - depth from 2.51	2	19-Nov-26	21-Nov-26	363	4,246	0	4,246
JDI	Bedding Works for GRP Pipe Line 150 mm - depth from 2.51 to	3	22-Nov-26	24-Nov-26	363	1,062	0	1,062
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 1.5		6	03-Nov-26	09-Nov-26	391	8,738	0	8,738
JDI	Primary Test for GRP Pipe Line 200 mm - depth from 1.51 to 2.	6	03-Nov-26	09-Nov-26	391	8,738	0	8,738
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 2.5		6	03-Nov-26	09-Nov-26	391	11,329	0	11,329
JDI	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	6	03-Nov-26	09-Nov-26	391	11,329	0	11,329
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 3.5		6	03-Nov-26	09-Nov-26	391	8,831	0	8,831
JDI	Primary Test for GRP Pipe Line 200 mm - depth from 3.51 to 4.	6	03-Nov-26	09-Nov-26	391	8,831	0	8,831
JDH3-02-009-AMCA-(SW)-GRP Pipes-200 mm diameter depth from 4.5		6	03-Nov-26	09-Nov-26	391	3,647	0	3,647
JDI	Primary Test for GRP Pipe Line 200 mm - depth from 4.51 to 5.	6	03-Nov-26	09-Nov-26	391	3,647	0	3,647
JDH3-02-009-AMCA-(SW)-MH Works depth from 1.51 to 2.5 Diam 120		52	08-Sep-26 A	08-Nov-26	404	113,723	48,332	113,723
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	04-Nov-26	05-Nov-26	404	11,372	0	11,372
JDI	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	2	07-Nov-26	08-Nov-26	404	5,686	0	5,686
JDI	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	2	16-Sep-26 A	03-Nov-26	404	39,803	19,902	39,803
JDI	Excavation and PC Blinding Works for MH 1200 mm - depth fro	2	08-Sep-26 A	03-Nov-26	404	28,431	14,215	28,431
JDI	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	2	10-Sep-26 A	03-Nov-26	404	28,431	14,215	28,431
JDH3-02-009-AMCA-(SW)-MH Works depth from 2.51 to 3.5 Diam 120		58	03-Sep-26 A	10-Nov-26	404	48,773	27,362	48,773
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	07-Nov-26	08-Nov-26	404	4,877	0	4,877
JDI	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3	2	09-Nov-26	10-Nov-26	404	2,439	0	2,439
JDI	Excavation and PC Blinding Works for MH 1200 mm - depth fro	2	03-Sep-26 A	03-Nov-26	406	12,193	8,048	12,193
JDI	Installation of Basefor MH 1200 mm - depth from 2.51 to 3.5 m	2	06-Sep-26 A	03-Nov-26	406	12,193	8,048	12,193
JDI	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	2	16-Sep-26 A	03-Nov-26	406	17,071	11,267	17,071
JDH3-02-009-AMCA-(SW)-MH Works depth from 3.51 to 4.5 Diam 120		4	09-Nov-26	12-Nov-26	404	5,027	0	5,027
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	09-Nov-26	10-Nov-26	404	3,351	0	3,351
JDI	Steel Coverfor MH 1200 mm - depth from 3.51 to 4.5 m- (B5.33	2	11-Nov-26	12-Nov-26	404	1,676	0	1,676
JDH3-02-009-AMCA-(SW)-MH Works depth from 4.51 to 5.5 Diam 120		4	11-Nov-26	15-Nov-26	404	5,518	0	5,518
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	11-Nov-26	12-Nov-26	404	3,679	0	3,679
JDI	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	2	14-Nov-26	15-Nov-26	404	1,839	0	1,839
JDH3-02-009-AMCA-Storm Network- ST		12	03-Nov-26	16-Nov-26	375	59,914	0	59,914
JDH3-02-009-AMCA-(ST)-MH Works (1200) mm diameter depth from 3		4	03-Nov-26	07-Nov-26	375	1,358	0	1,358
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	375	873	0	873
JDI	Steel Coverfor MH 1200 mm - depth from 3.01 to 3.50 m- (B6.3	2	05-Nov-26	07-Nov-26	375	485	0	485
JDH3-02-009-AMCA-(ST)-MH Works (1500) mm diameter depth from 2		4	05-Nov-26	09-Nov-26	375	5,129	0	5,129
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	05-Nov-26	07-Nov-26	375	3,377	0	3,377
JDI	Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3	2	08-Nov-26	09-Nov-26	375	1,751	0	1,751
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 3		4	08-Nov-26	11-Nov-26	375	12,088	0	12,088
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	08-Nov-26	09-Nov-26	375	8,000	0	8,000
JDI	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2	10-Nov-26	11-Nov-26	375	4,089	0	4,089
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 3		4	10-Nov-26	14-Nov-26	375	30,723	0	30,723
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	10-Nov-26	11-Nov-26	375	20,482	0	20,482
JDI	Steel Coverfor MH 2000 mm - depth from 3.51 to 4.0- (B6.33 05	2	12-Nov-26	14-Nov-26	375	10,241	0	10,241
JDH3-02-009-AMCA-(ST)-MH Works (2000) mm diameter depth from 4		4	12-Nov-26	16-Nov-26	375	10,617	0	10,617
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	12-Nov-26	14-Nov-26	375	7,078	0	7,078
JDI	Steel Coverfor MH 2000 mm - depth from 4.01 to 4.5- (B6.33 05	2	15-Nov-26	16-Nov-26	375	3,539	0	3,539

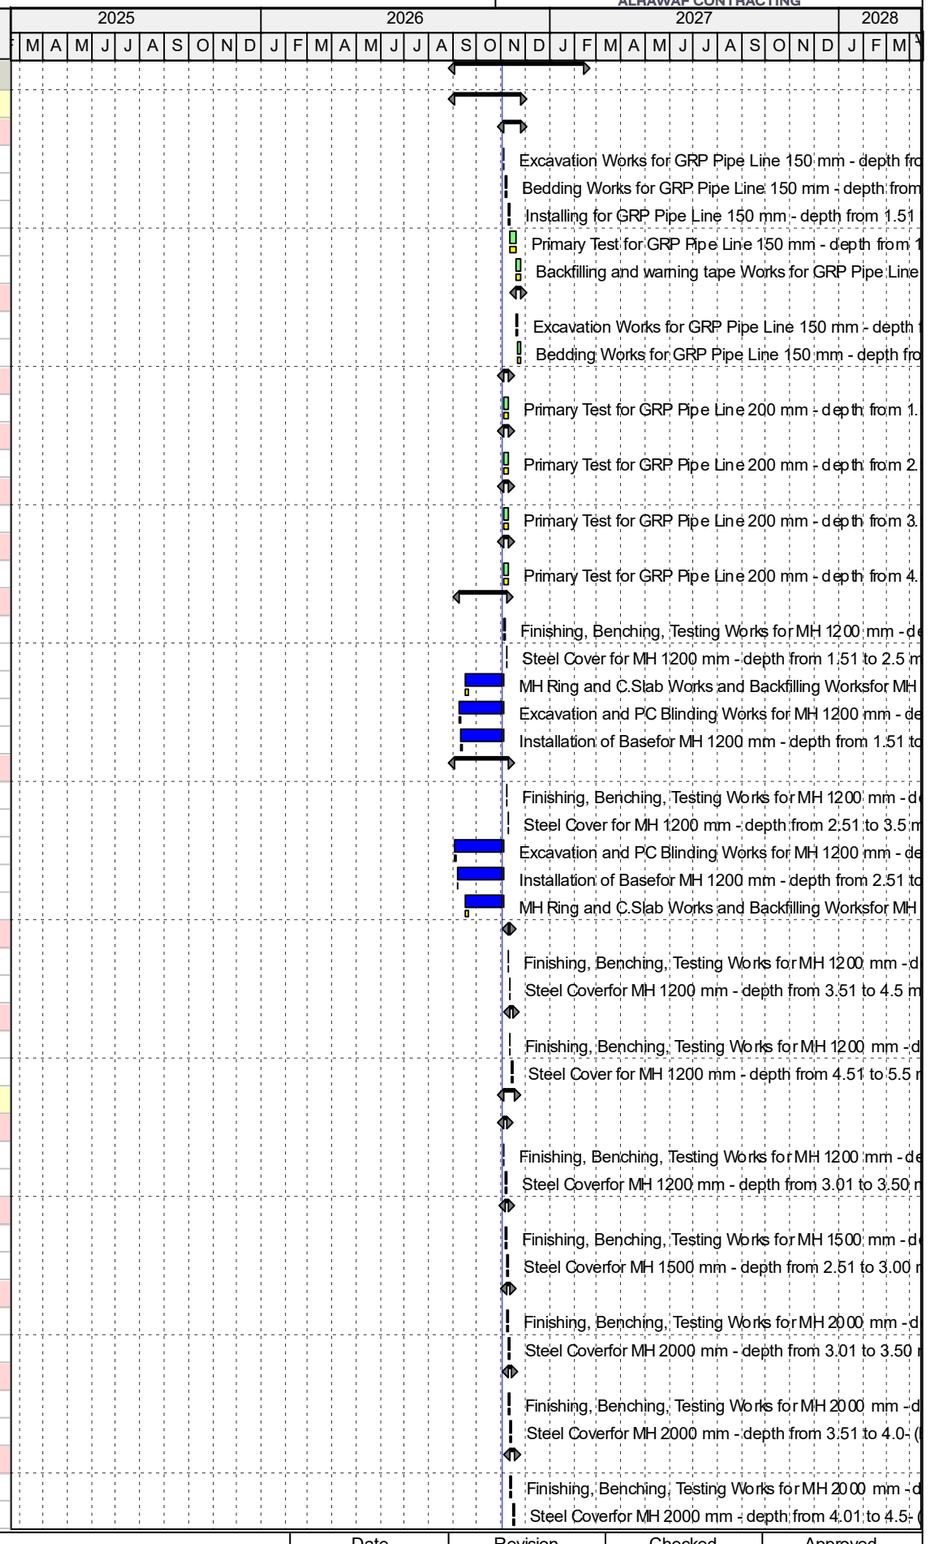

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-AMCA-Road Works - RD	54	20-Oct-26 A	13-Feb-27	299	573,138	257,912	576,967
	JDH3-02-009-AMCA-(RD)-Bituminous base course 70 mm, including F	2	20-Oct-26 A	23-Dec-26	299	573,138	257,912	573,138
JDI	Supply, lay and compaction Asphaltic base course 70 mm - (B1	2	20-Oct-26 A	23-Dec-26	299	573,138	257,912	573,138
	JDH3-02-009-AMCA-(RD)-Precast Concrete Curb	3	10-Feb-27	13-Feb-27	299	0	0	3,830
JDI	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3	10-Feb-27	13-Feb-27	299	0	0	3,830
	JDH3-02-009-AMCA-Potable Water Network- WT	19	03-Nov-26	24-Nov-26	396	246,797	0	246,797
	(WT)-HDPE Pipes-160 mm diameter depth from 0 to 1.5 m	12	03-Nov-26	16-Nov-26	403	5,004	0	5,004
JDI	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	2	03-Nov-26	04-Nov-26	390	1,001	0	1,001
JDI	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	2	05-Nov-26	07-Nov-26	390	250	0	250
JDI	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m- (	4	08-Nov-26	11-Nov-26	390	2,752	0	2,752
JDI	Primary Test for HDPE Pipe Line 160 mm - depth from 0 to 1.5	2	12-Nov-26	14-Nov-26	390	500	0	500
JDI	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	2	15-Nov-26	16-Nov-26	403	500	0	500
	(WT)-HDPE Pipes-225 mm diameter depth from 0 to 1.5 m	8	15-Nov-26	23-Nov-26	393	189,595	0	189,595
JDI	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 t	2	15-Nov-26	16-Nov-26	393	47,399	0	47,399
JDI	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	2	17-Nov-26	18-Nov-26	393	11,850	0	11,850
JDI	Installing for HDPE Pipe Line 225 mm - depth from 0 to 1.5 m- (	4	19-Nov-26	23-Nov-26	393	130,347	0	130,347
	(WT)-Gate Valve-150 mm on pipe dia (160) mm	4	15-Nov-26	18-Nov-26	390	3,453	0	3,453
JDI	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B3.33	2	15-Nov-26	16-Nov-26	390	3,108	0	3,108
JDI	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 mi	2	17-Nov-26	18-Nov-26	390	345	0	345
	(WT)-Gate Valve-200 mm on pipe dia (225) mm	4	03-Nov-26	07-Nov-26	411	10,638	0	10,638
JDI	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B3.33	2	03-Nov-26	04-Nov-26	411	9,574	0	9,574
JDI	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 mi	2	05-Nov-26	07-Nov-26	411	1,064	0	1,064
	(WT)-Fire Hydrant	5	19-Nov-26	24-Nov-26	390	38,106	0	38,106
JDI	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	19-Nov-26	21-Nov-26	390	12,702	0	12,702
JDI	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-NR-AMCA-V	3	22-Nov-26	24-Nov-26	390	25,404	0	25,404
	JDH3-02-009-AMCA-TSE Network - TSE	18	03-Nov-26	23-Nov-26	397	207,130	0	207,130
	JDH3-02-009-AMCA-(TSE)-HDPE Pipes-110 mm diameter depth from (	18	03-Nov-26	23-Nov-26	393	9,808	0	9,808
JDI	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	3	03-Nov-26	05-Nov-26	393	2,180	0	2,180
JDI	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	3	07-Nov-26	09-Nov-26	393	545	0	545
JDI	Installing for HDPE Pipe Line 110 mm - depth from 0 to 1.5 m- (	8	10-Nov-26	18-Nov-26	393	5,994	0	5,994
JDI	Primary Test for HDPE Pipe Line 110 mm - depth from 0 to 1.5	4	19-Nov-26	23-Nov-26	393	1,090	0	1,090
	JDH3-02-009-AMCA-(TSE)-HDPE Pipes-160 mm diameter depth from	10	03-Nov-26	14-Nov-26	405	174,460	0	174,460
JDI	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	2	03-Nov-26	04-Nov-26	405	34,892	0	34,892
JDI	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51	2	05-Nov-26	07-Nov-26	405	8,723	0	8,723
JDI	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5	2	08-Nov-26	09-Nov-26	405	95,953	0	95,953
JDI	Primary Test for HDPE Pipe Line 160 mm - depth from 1.51 to 2	2	10-Nov-26	11-Nov-26	405	17,446	0	17,446
JDI	Backfilling and warning tape Works for HDPE Pipe Line 160 mm	2	12-Nov-26	14-Nov-26	405	17,446	0	17,446
	JDH3-02-009-AMCA-(TSE)-Gate Valve-100 mm on pipe dia (110) mm	4	19-Nov-26	23-Nov-26	395	10,147	0	10,147
JDI	Installation for Gate Valve 100 mm on pipe dia 110 mm- (B4.33	2	19-Nov-26	21-Nov-26	395	9,132	0	9,132
JDI	Stem & Surface box for Gate Valve 100 mm on pipe dia 110 mi	2	22-Nov-26	23-Nov-26	395	1,015	0	1,015
	JDH3-02-009-AMCA-(TSE)-Gate Valve-150 mm on pipe dia (160) mm	2	22-Nov-26	23-Nov-26	395	12,715	0	12,715
JDI	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B4.33	2	22-Nov-26	23-Nov-26	395	12,715	0	12,715
	D-MCA	4	03-Nov-26	07-Nov-26	411	1,112	0	1,112
	JDH3-02-009-DMCA-Storm Network- ST	4	03-Nov-26	07-Nov-26	411	1,112	0	1,112
	JDH3-02-009-DMCA-(ST)-MH Works (1200) mm diameter depth from 2	4	03-Nov-26	07-Nov-26	411	1,112	0	1,112
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	411	715	0	715
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	411	397	0	397
	D-MCE	20	03-Nov-26	25-Nov-26	395	109,340	0	109,340
	JDH3-02-009-DMCE-Storm Network - ST	6	03-Nov-26	09-Nov-26	409	19,366	0	19,366
	JDH3-02-009-DMCE-(ST)-MH Works (2000) mm diameter depth from 3	4	03-Nov-26	07-Nov-26	409	12,088	0	12,088
JDI	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	03-Nov-26	04-Nov-26	409	8,000	0	8,000
JDI	Steel Coverfor MH 2000 mm - depth from 3.01 to 3.50 m- (B6.3	2	05-Nov-26	07-Nov-26	409	4,089	0	4,089

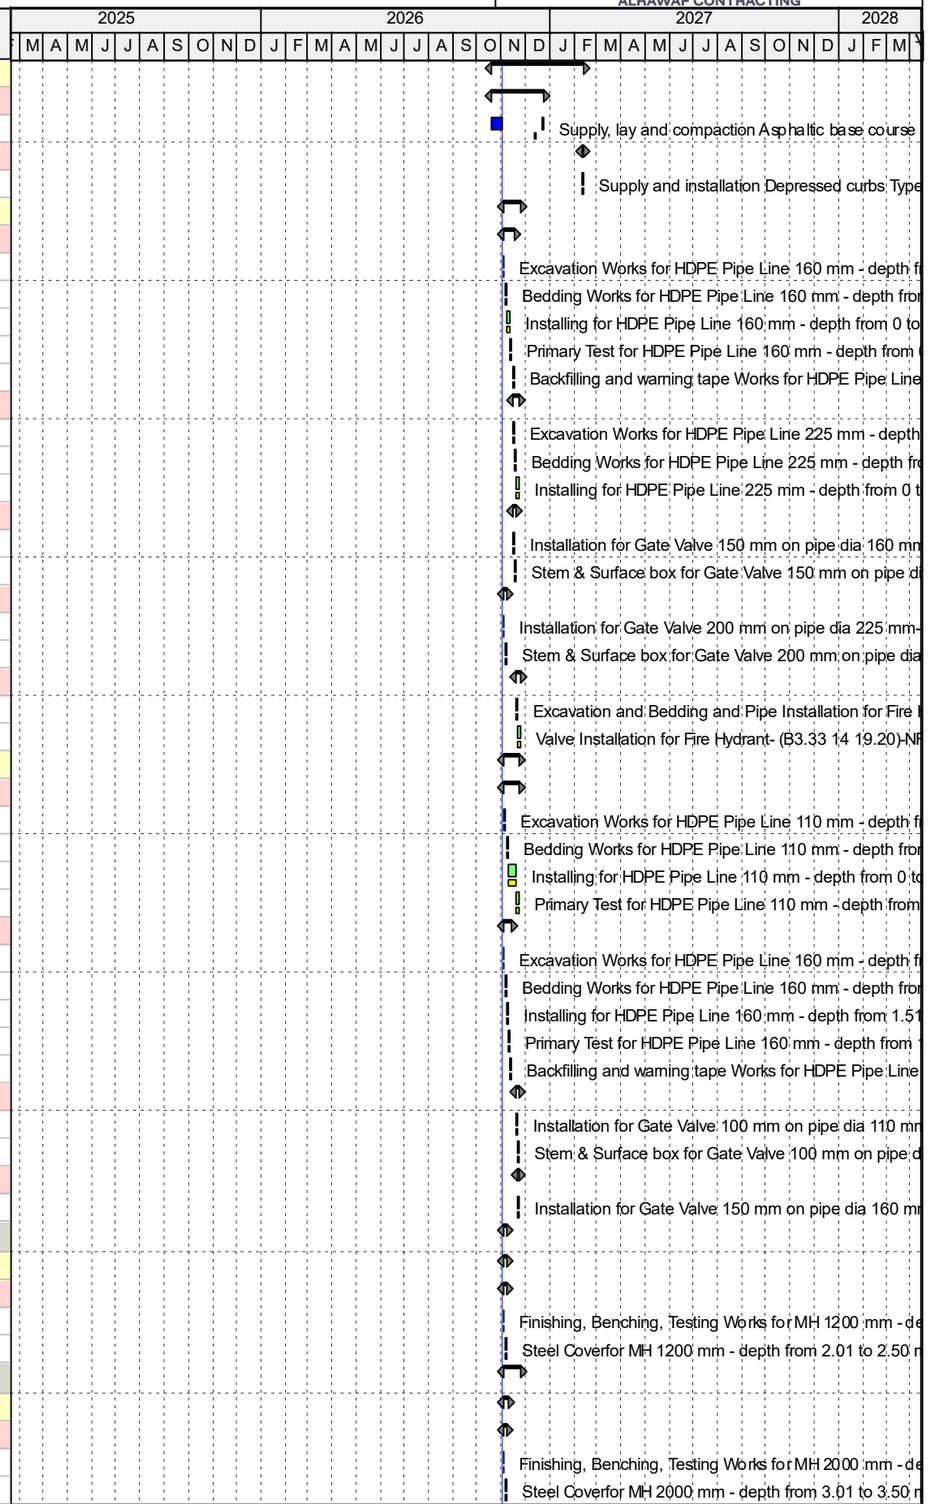


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-DMCE-(ST)-MH Works (1500) mm diameter depth from 3	4	05-Nov-26	09-Nov-26	409	7,278	0	7,278
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	05-Nov-26	07-Nov-26	409	4,852	0	4,852
JDI	Steel Coverfor MH 1500 mm - depth from 3.01 to 3.50 m- (B6.3	2	08-Nov-26	09-Nov-26	409	2,426	0	2,426
	JDH3-02-009-DMCE-Road Works - RD	20	03-Nov-26	25-Nov-26	287	89,974	0	89,974
	JDH3-02-009-DMCE-(RD)-Precast Concrete Curb	20	03-Nov-26	25-Nov-26	287	89,974	0	89,974
JDI	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8	03-Nov-26	11-Nov-26	287	68,785	0	68,785
JDI	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	12	12-Nov-26	25-Nov-26	287	21,189	0	21,189
	C-MCA	8	03-Nov-26	11-Nov-26	407	9,418	0	9,418
	JDH3-02-009-CMCA-Storm Network- ST	8	03-Nov-26	11-Nov-26	407	9,418	0	9,418
	JDH3-02-009-CMCA-(ST)-MH Works (1200) mm diameter depth from 1	4	03-Nov-26	07-Nov-26	407	5,298	0	5,298
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	407	3,506	0	3,506
JDI	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2	05-Nov-26	07-Nov-26	407	1,792	0	1,792
	JDH3-02-009-CMCA-(ST)-MH Works (1200) mm diameter depth from 2	6	03-Nov-26	09-Nov-26	407	1,112	0	1,112
JDI	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	409	715	0	715
JDI	Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3	2	08-Nov-26	09-Nov-26	407	397	0	397
	JDH3-02-009-CMCA-(ST)-MH Works (1500) mm diameter depth from 2	8	03-Nov-26	11-Nov-26	407	3,009	0	3,009
JDI	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	411	2,006	0	2,006
JDI	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	10-Nov-26	11-Nov-26	407	1,003	0	1,003
	C-MCB	18	03-Nov-26	23-Nov-26	385	86,617	0	86,617
	JDH3-02-009-CMCB-Storm Network - ST	18	03-Nov-26	23-Nov-26	385	86,617	0	86,617
	JDH3-02-009-CMCB-(ST)-GRP Pipes-400 mm diameter depth from 1.5	15	03-Nov-26	19-Nov-26	385	82,666	0	82,666
JDI	Excavation Works for GRP Pipe Line 400 mm - depth from 1.51	3	03-Nov-26	05-Nov-26	385	16,533	0	16,533
JDI	Bedding Works for GRP Pipe Line 400 mm - depth from 1.51 to	3	07-Nov-26	09-Nov-26	385	4,133	0	4,133
JDI	Installing for GRP Pipe Line 400 mm - depth from 1.51 to 2.00	3	10-Nov-26	12-Nov-26	385	45,466	0	45,466
JDI	Primary Test for GRP Pipe Line 400 mm - depth from 1.51 to 2.	3	14-Nov-26	16-Nov-26	385	8,267	0	8,267
JDI	Backfilling and warning tape Works for GRP Pipe Line 400 mm	3	17-Nov-26	19-Nov-26	385	8,267	0	8,267
	JDH3-02-009-CMCB-(ST)-GRP Pipes-500 mm diameter depth from 2.5	3	21-Nov-26	23-Nov-26	385	3,952	0	3,952
JDI	Excavation Works for GRP Pipe Line 500 mm - depth from 2.51	3	21-Nov-26	23-Nov-26	385	3,952	0	3,952
	JDH3-02-009-Infrastructure Networks	440	20-May-26 A	09-Oct-27	132	28,987,342	12,890,153	48,724,151
	JDH3-02-009-Milestone	27	15-Nov-26	16-Dec-26	377	0	0	0
	Network Milestones	5	15-Nov-26	21-Nov-26	399	0	0	0
JDH3S	Finish of Sewage Network - SS - .FMI-SS	0		21-Nov-26	399	0	0	0
JDH3S	Finish of Storm Network - ST - .FMI-ST	0		15-Nov-26	404	0	0	0
	Zones Millestones	24	18-Nov-26	16-Dec-26	377	0	0	0
JDH3(	Finish Z3	0		16-Dec-26	377	0	0	0
JDH3(	Finish EX	0		18-Nov-26	401	0	0	0
	JDH3-02-009-Engineering - EN	2	03-Nov-26	04-Nov-26	413	0	0	0
	JDH3-02-009-Prequalification and Material	2	03-Nov-26	04-Nov-26	413	0	0	0
	JDH3-02-009-Submittals of Material and Prequalifications - SUB	2	03-Nov-26	04-Nov-26	413	0	0	0
	JDH3-02-009-Submittals of Material and Prequalifications - SUB-La	2	03-Nov-26	04-Nov-26	413	0	0	0
	Prepare Material Submittal for Landscape and Irrigation - PR-LS	2	03-Nov-26	04-Nov-26	413	0	0	0
	JDH3-02-009-Procurement- PR	50	15-Sep-26 A	26-Nov-26	392	369,797	0	369,797
	Long Lead Items	10	03-Nov-26	12-Nov-26	488	369,797	0	369,797
	JDH3-02-009-Material Delivery and staging on Site - DOS	10	03-Nov-26	12-Nov-26	488	369,797	0	369,797
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z03	10	03-Nov-26	12-Nov-26	310	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10	03-Nov-26	12-Nov-26	310	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z03-DOS	10	03-Nov-26	12-Nov-26	310	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z01	10	03-Nov-26	12-Nov-26	389	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10	03-Nov-26	12-Nov-26	389	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z01-DOS	10	03-Nov-26	12-Nov-26	389	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z02	10	03-Nov-26	12-Nov-26	431	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10	03-Nov-26	12-Nov-26	431	92,449	0	92,449

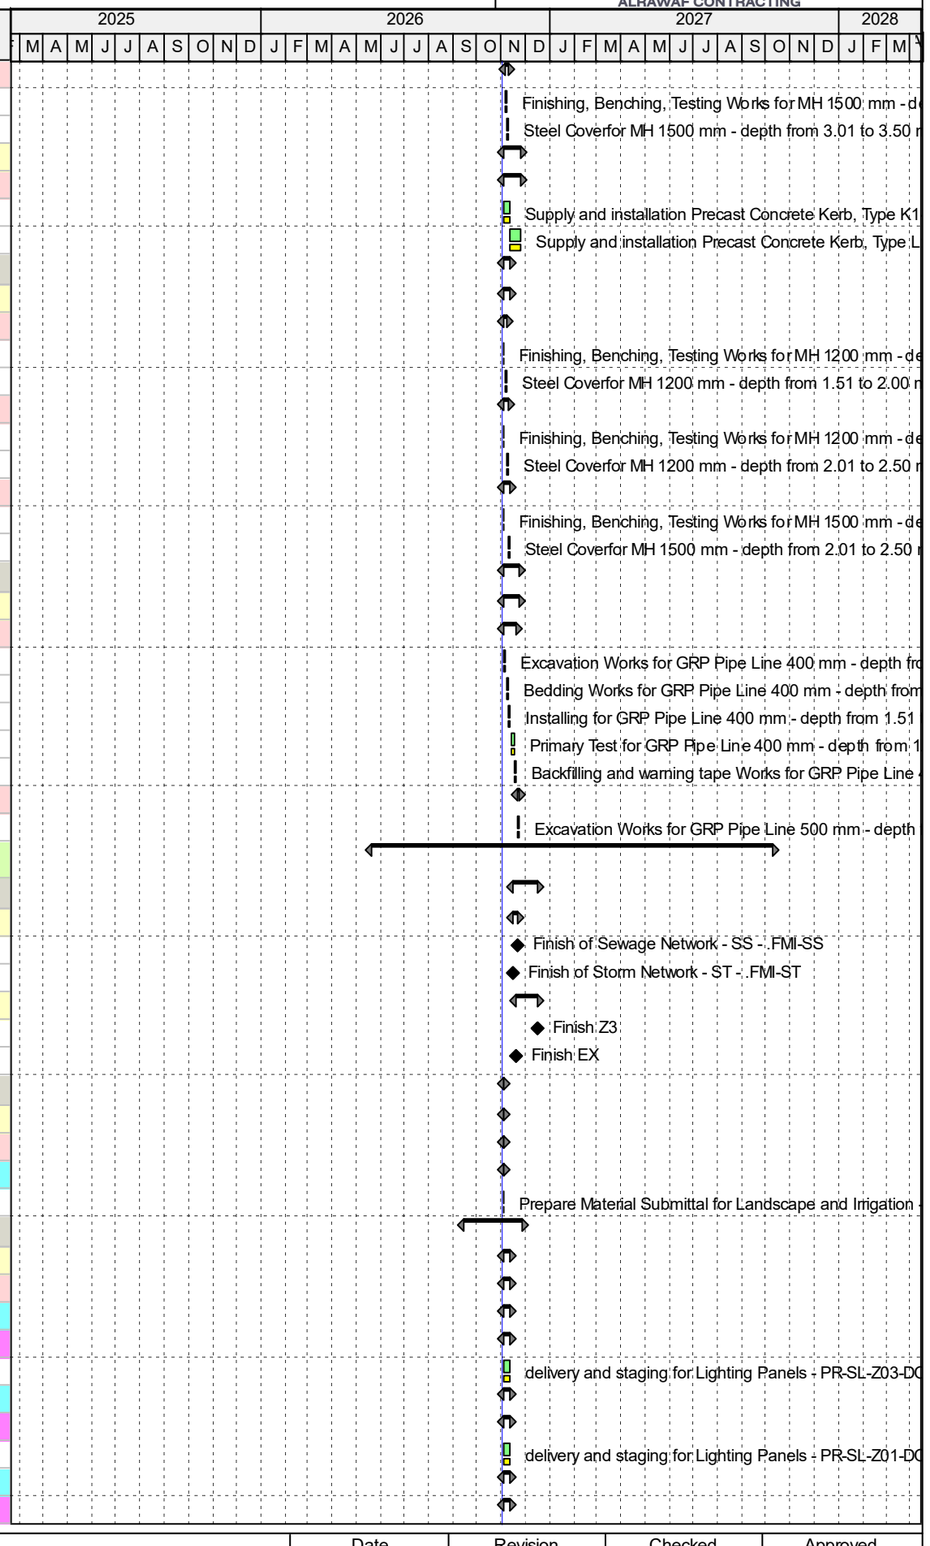


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	delivery and staging for Lighting Panels - PR-SL-Z02-DOS	10	03-Nov-26	12-Nov-26	431	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z04	10	03-Nov-26	12-Nov-26	488	92,449	0	92,449
	JDH3-02-009-Material Delivery and staging on Site - DOS-Street	10	03-Nov-26	12-Nov-26	488	92,449	0	92,449
	delivery and staging for Lighting Panels - PR-SL-Z04-DOS	10	03-Nov-26	12-Nov-26	488	92,449	0	92,449
	Short Lead items	21	15-Sep-26 A	26-Nov-26	118	0	0	0
	JDH3-02-009-Material Purchase Order - PO	21	15-Sep-26 A	26-Nov-26	118	0	0	0
	JDH3-Material Purchase Order - PO-Landscape and Irrigation- LS	21	15-Sep-26 A	26-Nov-26	118	0	0	0
	Material Purchase Order for Landscape and Irrigation - PR-LS-P	21	15-Sep-26 A	26-Nov-26	118	0	0	0
	JDH3-02-009-Execution	440	20-May-26 A	26-Jul-27	195	28,617,545	9,885,822	42,465,471
	JDH3-02-009-XX-Execution	3	03-Nov-26	05-Nov-26	412	11,854	0	11,854
	Z2	3	03-Nov-26	05-Nov-26	412	8,413	0	8,413
	R102	3	03-Nov-26	05-Nov-26	412	8,413	0	8,413
	JDH3-02-009-XX-R102-Potable Water Network - WT	3	03-Nov-26	05-Nov-26	412	8,413	0	8,413
	JDH3-02-009-XX-R102-(WT)-HDPE Pipes-800 mm diameter d	3	03-Nov-26	05-Nov-26	412	8,413	0	8,413
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	3	03-Nov-26	05-Nov-26	412	8,413	0	8,413
	Z3	2	03-Nov-26	04-Nov-26	413	3,442	0	3,442
	R103	2	03-Nov-26	04-Nov-26	413	3,442	0	3,442
	JDH3-02-009-XX-R103-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	3,442	0	3,442
	JDH3-02-009-XX-R103-(WT)-HDPE Pipes-800 mm diameter d	2	03-Nov-26	04-Nov-26	413	3,442	0	3,442
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	2	03-Nov-26	04-Nov-26	413	3,442	0	3,442
	Pond - PS	123	03-Nov-26	30-Mar-27	292	405,364	0	2,899,943
	JDH3-02-009-ST1-Pond 1 - ST	17	03-Nov-26	22-Nov-26	371	0	0	627,213
	JDH3-02-009-ST3-Stage (3) - Pond 1	5	03-Nov-26	08-Nov-26	371	0	0	313,607
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5	03-Nov-26	08-Nov-26	371	0	0	313,607
	JDH3-02-009-ST4-Stage (4) - Pond 1	12	09-Nov-26	22-Nov-26	371	0	0	313,607
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	09-Nov-26	22-Nov-26	371	0	0	313,607
	JDH3-02-009-ST1-Pond 2 - ST	24	03-Nov-26	30-Nov-26	391	0	0	326,099
	JDH3-02-009-ST3-Stage (3) - Pond 2	12	03-Nov-26	16-Nov-26	391	0	0	163,050
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	03-Nov-26	16-Nov-26	391	0	0	163,050
	JDH3-02-009-ST4-Stage (4) - Pond 2	12	17-Nov-26	30-Nov-26	391	0	0	163,050
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	17-Nov-26	30-Nov-26	391	0	0	163,050
	JDH3-02-009-ST1-Pond 3 - ST	24	03-Nov-26	30-Nov-26	391	0	0	812,429
	JDH3-02-009-ST2-Stage (2) - Pond 3	15	03-Nov-26	19-Nov-26	400	0	0	282,543
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	03-Nov-26	16-Nov-26	400	0	0	264,943
	Access Ramp for Pond 3- (B6.31 22 00.05)-PS-PN3-ST2	3	17-Nov-26	19-Nov-26	400	0	0	17,600
	JDH3-02-009-ST3-Stage (3) - Pond 3	12	03-Nov-26	16-Nov-26	391	0	0	264,943
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	03-Nov-26	16-Nov-26	391	0	0	264,943
	JDH3-02-009-ST4-Stage (4) - Pond 3	12	17-Nov-26	30-Nov-26	391	0	0	264,943
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	12	17-Nov-26	30-Nov-26	391	0	0	264,943
	JDH3-02-009-ST1-Pond 6 - ST	19	03-Nov-26	24-Nov-26	396	121,471	0	247,820
	JDH3-02-009-ST1-Stage (1) - Pond 6	8	03-Nov-26	11-Nov-26	407	0	0	126,349
	Chain Link Fence for Pond 6- (B6.31 22 00.04)-PS-PN6-ST1	8	03-Nov-26	11-Nov-26	407	0	0	126,349
	JDH3-02-009-PN6-Landscape Works - LS	19	03-Nov-26	24-Nov-26	256	121,471	0	121,471
	JDH3-02-009-PN6-(LS)-Trees	19	03-Nov-26	24-Nov-26	256	121,471	0	121,471
	Ref. ACA AMP (Acacia Ampliceps) - (B7.32 93 00.01)-PS-PN6-LS	4	03-Nov-26	07-Nov-26	256	20,683	0	20,683
	Ref. AZA INC (Azadirachta Indica) - (B7.32 93 00.03)-PS-PN6-LS	2	08-Nov-26	09-Nov-26	264	9,192	0	9,192
	Ref. COR SEB (Cordia Sebestena) - (B7.32 93 00.05)-PS-PN6-LS	5	19-Nov-26	24-Nov-26	256	32,502	0	32,502
	Ref. DEL REG (Delonix Regia) - (B7.32 93 00.07)-PS-PN6-LS	6	12-Nov-26	18-Nov-26	256	30,204	0	30,204
	Ref. FIC REL (Ficus Religiosa) - (B7.32 93 00.08)-PS-PN6-LS	4	08-Nov-26	11-Nov-26	256	28,890	0	28,890
	JDH3-02-009-ST1-Pond 9 - ST	123	03-Nov-26	30-Mar-27	256	0	0	595,531
	JDH3-02-009-ST1-Stage (1) - Pond 9	18	03-Nov-26	23-Nov-26	337	0	0	594,951
	Coarse Sand for bottom of Pond with 600mm thickness for Pon	18	03-Nov-26	23-Nov-26	337	0	0	594,951
	JDH3-02-009-PN9-Landscape Works - LS	4	27-Mar-27	30-Mar-27	256	0	0	580

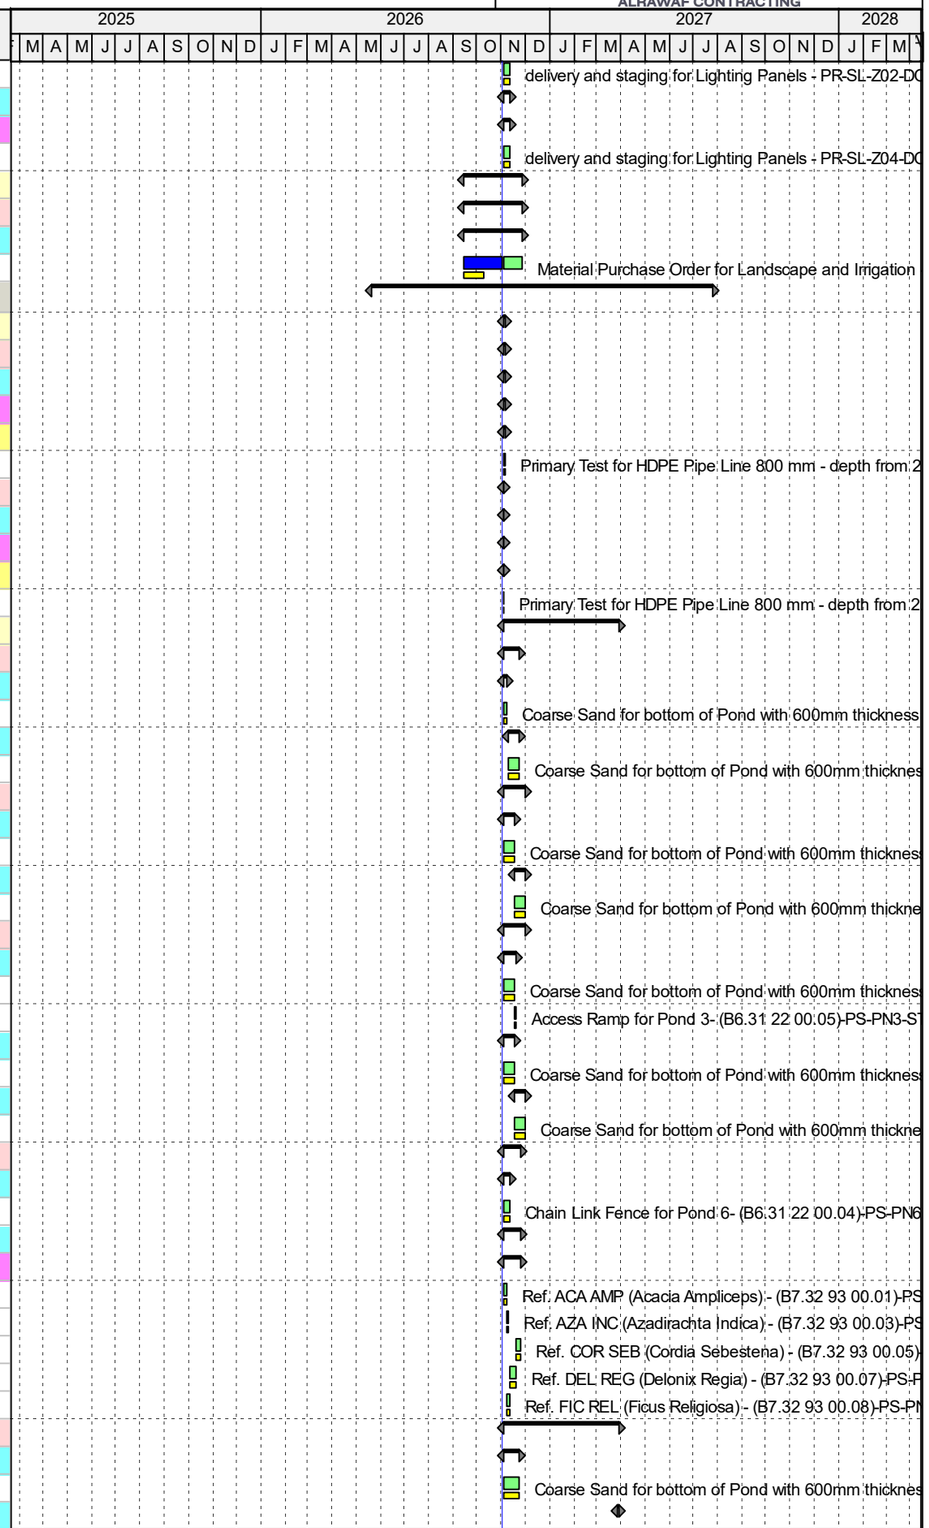


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-PN9-(LS)-Design, Delive, install, wiring, control, pı	4	27-Mar-27	30-Mar-27	256	0	0	580
	Online pressure compensating emitters with - - (B7.32.80.00.0	4	27-Mar-27	30-Mar-27	256	0	0	580
	JDH3-02-009-ST1-Pond 4 - ST	3	03-Nov-26	05-Nov-26	412	283,893	0	290,850
	JDH3-02-009-BW-Backfilling Works	3	03-Nov-26	05-Nov-26	412	283,893	0	290,850
	Backfill Layers Works Imported Material for Pond 4 - (B1.31 22 (	3	03-Nov-26	05-Nov-26	412	283,893	0	290,850
	Earthworks - EW	335	25-May-26 A	26-Jul-27	195	714,729	1,605,924	3,146,786
	JDH3-02-009-Block 01-Block Works - BW	20	25-May-26 A	26-Jul-27	195	0	131,875	146,528
	Z1	20	25-May-26 A	26-Jul-27	195	0	131,875	146,528
	JDH3-02-009-Block Works - BWZ1-Block 01	20	25-May-26 A	26-Jul-27	195	0	131,875	146,528
	Excavation Works for Block 01 - (B1.31 22 00.05)-Z1-B01-BW	20	25-May-26 A	26-Jul-27	195	0	131,875	146,528
	JDH3-02-009-R01-Road Works - RW	57	21-Jul-26 A	07-Jan-27	307	714,729	1,474,049	3,000,258
	Z1	17	21-Jul-26 A	26-Nov-26	344	0	621,753	690,837
	JDH3-02-009-Road Works - RWZ1-R101	8	21-Jul-26 A	26-Nov-26	310	0	241,236	268,040
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	8	21-Jul-26 A	26-Nov-26	310	0	241,236	268,040
	JDH3-02-009-Road Works - RWZ1-R06	12	01-Sep-26 A	04-Nov-26	363	0	380,517	422,797
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	12	01-Sep-26 A	04-Nov-26	363	0	380,517	422,797
	Z2	43	17-Sep-26 A	07-Jan-27	294	714,729	852,296	2,309,421
	JDH3-02-009-Road Works - RWZ2-R102	19	17-Sep-26 A	10-Dec-26	319	0	637,877	1,594,692
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	19	17-Sep-26 A	10-Dec-26	319	0	637,877	1,594,692
	JDH3-02-009-Road Works - RWZ2-R14	15	24-Sep-26 A	07-Jan-27	281	714,729	214,419	714,729
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	15	24-Sep-26 A	07-Jan-27	281	714,729	214,419	714,729
	Z3	197	20-May-26 A	25-Jan-27	343	4,368,765	942,603	4,454,542
	R152	146	22-Jul-26 A	17-Jan-27	350	658,357	143,222	683,461
	JDH3-02-009-R152-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	5,862	0	5,862
	JDH3-02-009-R152-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	5,862	0	5,862
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R152-W	2	03-Nov-26	04-Nov-26	413	5,862	0	5,862
	JDH3-02-009-R152-Electrical Network - EL	16	22-Jul-26 A	11-Nov-26	389	186,075	93,037	186,075
	JDH3-02-009-R152-(EL)-MV cable trench size 1.5m wide and 80	16	22-Jul-26 A	11-Nov-26	389	8,712	4,356	8,712
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	5	22-Jul-26 A	11-Nov-26	362	5,227	2,614	5,227
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5	26-Jul-26 A	11-Nov-26	389	3,485	1,742	3,485
	JDH3-02-009-R152-(EL)-MV cables AL/XLPE/LLDPE Unarmored	6	23-Jul-26 A	11-Nov-26	389	177,363	88,681	177,363
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4	23-Jul-26 A	11-Nov-26	389	168,662	84,331	168,662
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	25-Jul-26 A	11-Nov-26	389	8,701	4,351	8,701
	JDH3-02-009-R152-Street Lighting Network -SL	20	03-Nov-26	25-Nov-26	389	50,625	0	50,625
	JDH3-02-009-R152-(SL)- LV Cables - Copper, 4 Cx 16 mm²,Cu/XLP	12	12-Nov-26	25-Nov-26	389	46,686	0	46,686
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	12-Nov-26	16-Nov-26	389	5,187	0	5,187
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4	17-Nov-26	21-Nov-26	389	38,905	0	38,905
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	22-Nov-26	25-Nov-26	389	2,594	0	2,594
	JDH3-02-009-R152-(SL)-Lighting Pole with single arm 12 m heig	5	03-Nov-26	08-Nov-26	404	3,940	0	3,940
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	5	03-Nov-26	08-Nov-26	404	3,940	0	3,940
	JDH3-02-009-R152-Road Works - RD	117	01-Sep-26 A	16-Jan-27	351	415,795	50,185	418,942
	JDH3-02-009-R152-(RD)-Precast Concrete Curb	70	01-Sep-26 A	22-Nov-26	334	161,910	50,185	161,910
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5	03-Nov-26	09-Nov-26	334	37,429	0	37,429
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	11	09-Nov-26	22-Nov-26	334	69,333	0	69,333
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8	01-Sep-26 A	03-Nov-26	334	55,148	50,185	55,148
	JDH3-02-009-R152-(RD)-Precast Interlocking Block Pavers	13	22-Nov-26	07-Dec-26	334	253,884	0	253,884
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	13	22-Nov-26	07-Dec-26	334	253,884	0	253,884
	JDH3-02-009-R152-(RD)-Pavement Marking	6	09-Jan-27	16-Jan-27	351	0	0	3,147
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z3-R152-RD	2	09-Jan-27	11-Jan-27	351	0	0	2,289
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2	11-Jan-27	13-Jan-27	351	0	0	572
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.0	2	13-Jan-27	16-Jan-27	351	0	0	286
	JDH3-02-009-R152-Landscape Works - LS	7	10-Jan-27	17-Jan-27	103	0	0	21,957
	JDH3-02-009-R152-(LS)-HDPE for Secondary Network	7	10-Jan-27	17-Jan-27	103	0	0	21,957

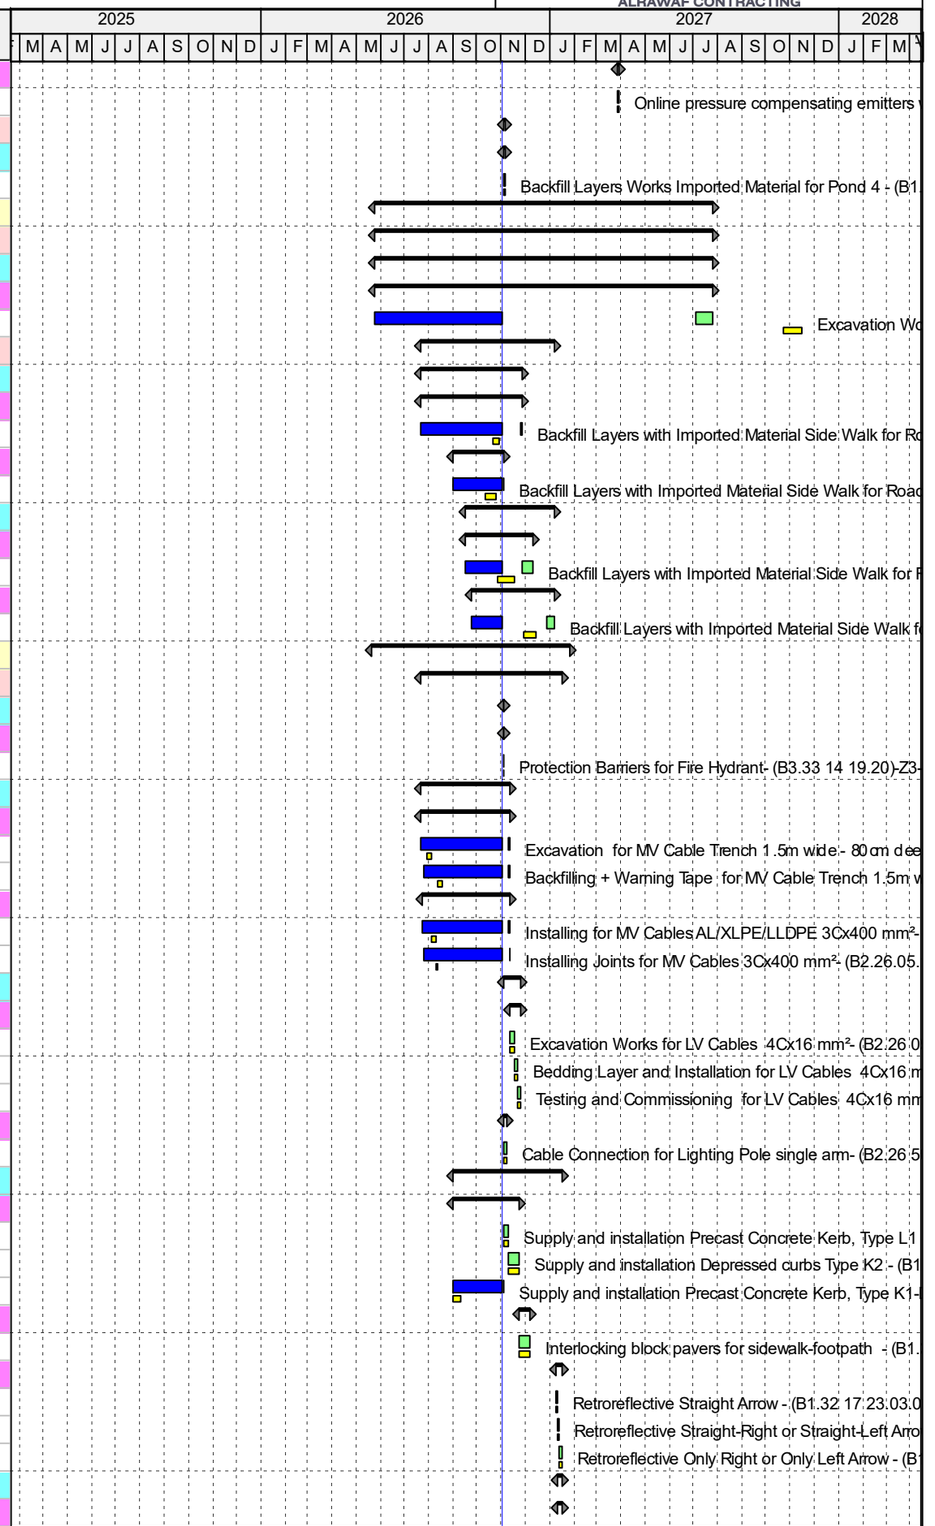


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	7	10-Jan-27	17-Jan-27	103	0	0	21,957
R16		147	20-May-26 A	28-Nov-26	393	342,099	157,895	342,099
JDH3-02-009-R16-Potable Water Network - WT		2	19-Nov-26	21-Nov-26	397	2,931	0	2,931
JDH3-02-009-R16-(WT)-Fire Hydrant		2	19-Nov-26	21-Nov-26	397	2,931	0	2,931
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R16-W	2	19-Nov-26	21-Nov-26	397	2,931	0	2,931
JDH3-02-009-R16-Electrical Network - EL		78	20-May-26 A	03-Nov-26	411	166,206	157,895	166,206
JDH3-02-009-R16-(EL)-MV cable trench size 1.5m wide and 80c		5	09-Jun-26 A	03-Nov-26	411	3,347	3,180	3,347
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5	09-Jun-26 A	03-Nov-26	411	3,347	3,180	3,347
JDH3-02-009-R16-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(		64	20-May-26 A	03-Nov-26	411	162,859	154,716	162,859
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	25-Jun-26 A	03-Nov-26	411	5,801	5,511	5,801
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4	20-May-26 A	03-Nov-26	411	157,058	149,205	157,058
JDH3-02-009-R16-Street Lighting Network -SL		4	03-Nov-26	08-Nov-26	411	3,534	0	3,534
JDH3-02-009-R16-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE		4	03-Nov-26	08-Nov-26	411	2,682	0	2,682
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	03-Nov-26	08-Nov-26	411	2,682	0	2,682
JDH3-02-009-R16-(SL)-Earthing System for Streetlighting feede		2	03-Nov-26	04-Nov-26	413	852	0	852
	Supply, construct, connect and test earthing pits for Street Light	2	03-Nov-26	04-Nov-26	413	852	0	852
JDH3-02-009-R16-Road Works - RD		22	03-Nov-26	28-Nov-26	103	169,428	0	169,428
JDH3-02-009-R16-(RD)-Precast Concrete Curb		10	03-Nov-26	14-Nov-26	103	55,210	0	55,210
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	103	4,724	0	4,724
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8	05-Nov-26	14-Nov-26	103	50,487	0	50,487
JDH3-02-009-R16-(RD)-Precast Interlocking Block Pavers		12	15-Nov-26	28-Nov-26	103	114,218	0	114,218
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12	15-Nov-26	28-Nov-26	103	114,218	0	114,218
R17		22	03-Nov-26	28-Nov-26	393	267,207	0	267,207
JDH3-02-009-R17-Potable Water Network - WT		2	03-Nov-26	04-Nov-26	409	3,908	0	3,908
JDH3-02-009-R17-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	409	3,908	0	3,908
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R17-W	2	03-Nov-26	04-Nov-26	409	3,908	0	3,908
JDH3-02-009-R17-Electrical Network - EL		6	03-Nov-26	09-Nov-26	409	68,946	0	68,946
JDH3-02-009-R17-(EL)-RMU 33 KV		6	03-Nov-26	09-Nov-26	409	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z3-R17-EL	2	03-Nov-26	04-Nov-26	409	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z3-R17-El	2	05-Nov-26	07-Nov-26	409	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z3-R1	2	08-Nov-26	09-Nov-26	409	4,925	0	4,925
JDH3-02-009-R17-Street Lighting Network -SL		11	03-Nov-26	15-Nov-26	404	20,231	0	20,231
JDH3-02-009-R17-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE		4	03-Nov-26	07-Nov-26	411	4,828	0	4,828
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	03-Nov-26	04-Nov-26	411	1,609	0	1,609
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	05-Nov-26	07-Nov-26	411	3,219	0	3,219
JDH3-02-009-R17-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE		5	03-Nov-26	08-Nov-26	410	3,946	0	3,946
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	03-Nov-26	08-Nov-26	410	3,946	0	3,946
JDH3-02-009-R17-(SL)-Earthing System for Distribution panels,S		2	03-Nov-26	04-Nov-26	413	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	03-Nov-26	04-Nov-26	413	1,126	0	1,126
JDH3-02-009-R17-(SL)- Street Lighting Panels		11	03-Nov-26	15-Nov-26	404	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R17-S	2	03-Nov-26	04-Nov-26	409	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2	05-Nov-26	07-Nov-26	409	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R17-S	2	14-Nov-26	15-Nov-26	404	7,232	0	7,232
JDH3-02-009-R17-Road Works - RD		22	03-Nov-26	28-Nov-26	369	174,121	0	174,121
JDH3-02-009-R17-(RD)-Precast Concrete Curb		10	03-Nov-26	14-Nov-26	369	59,977	0	59,977
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	369	9,490	0	9,490
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8	05-Nov-26	14-Nov-26	369	50,487	0	50,487
JDH3-02-009-R17-(RD)-Precast Interlocking Block Pavers		12	15-Nov-26	28-Nov-26	369	114,145	0	114,145
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12	15-Nov-26	28-Nov-26	369	114,145	0	114,145
R18		143	23-Jul-26 A	06-Jan-27	359	525,112	122,550	557,515
JDH3-02-009-R18-Potable Water Network - WT		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
JDH3-02-009-R18-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R18-W	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885

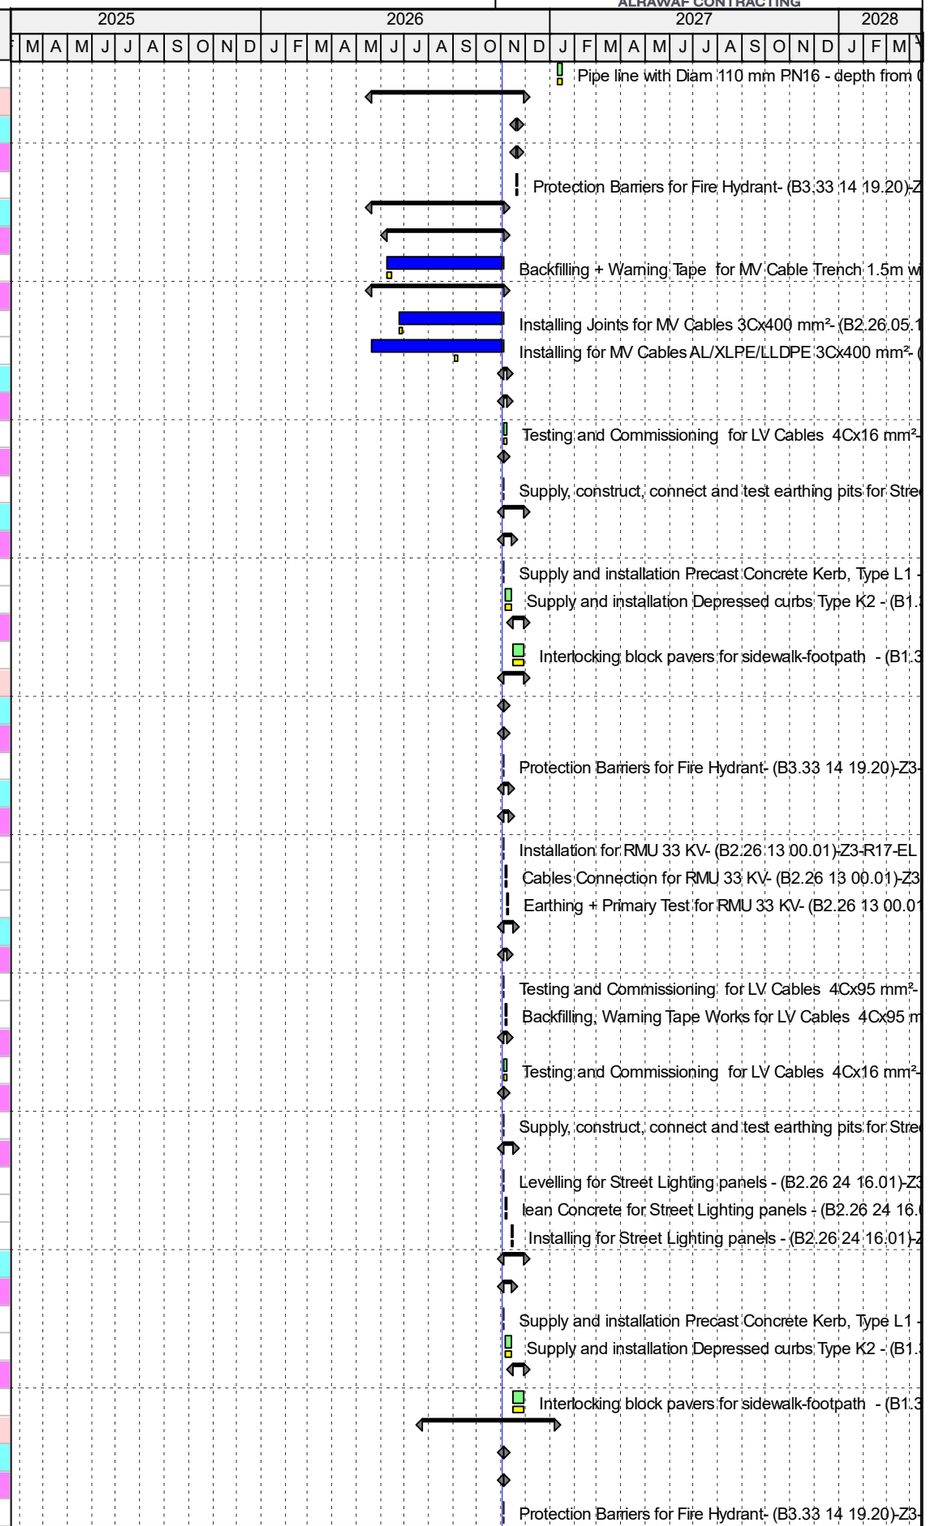


Actual Level of Effort
Actual Work
Primary Baseline
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R18-Street Lighting Network -SL	101	23-Jul-26 A	18-Nov-26	401	192,403	68,163	192,403
	JDH3-02-009-R18-(SL)- LV Cables - Copper, 4Cx95mm², Cu/XLPE	8	03-Nov-26	11-Nov-26	407	96,924	0	96,924
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	03-Nov-26	04-Nov-26	332	9,692	0	9,692
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	05-Nov-26	07-Nov-26	407	72,693	0	72,693
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	08-Nov-26	09-Nov-26	407	4,846	0	4,846
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	10-Nov-26	11-Nov-26	407	9,692	0	9,692
	JDH3-02-009-R18-(SL)- LV Cables - Copper, 4Cx16mm², Cu/XLPE	94	23-Jul-26 A	10-Nov-26	332	75,672	64,699	75,672
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	05-Nov-26	10-Nov-26	332	3,784	0	3,784
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	23-Jul-26 A	04-Nov-26	332	7,567	6,810	7,567
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5	23-Jul-26 A	04-Nov-26	332	56,754	51,078	56,754
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	06-Aug-26 A	10-Nov-26	332	7,567	6,810	7,567
	JDH3-02-009-R18-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2	28-Jul-26 A	03-Nov-26	415	3,849	3,464	3,849
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2	28-Jul-26 A	03-Nov-26	415	3,849	3,464	3,849
	JDH3-02-009-R18-(SL)-Earthing System for Distribution panels,S	3	16-Nov-26	18-Nov-26	328	5,628	0	5,628
	Supply, construct, connect and test earthing pits for Street Light	3	16-Nov-26	18-Nov-26	328	5,628	0	5,628
	JDH3-02-009-R18-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	328	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R18-S	2	03-Nov-26	04-Nov-26	333	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2	05-Nov-26	07-Nov-26	333	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R18-S	2	14-Nov-26	15-Nov-26	328	7,232	0	7,232
	JDH3-02-009-R18-Road Works - RD	101	25-Aug-26 A	06-Jan-27	357	327,824	54,386	360,227
	JDH3-02-009-R18-(RD)-Precast Concrete Curb	59	25-Aug-26 A	18-Nov-26	357	146,698	54,386	146,698
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3	03-Nov-26	07-Nov-26	357	21,085	0	21,085
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10	07-Nov-26	18-Nov-26	357	65,183	0	65,183
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9	25-Aug-26 A	03-Nov-26	357	60,429	54,386	60,429
	JDH3-02-009-R18-(RD)-Precast Interlocking Block Pavers	18	18-Nov-26	09-Dec-26	357	181,126	0	181,126
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18	18-Nov-26	09-Dec-26	357	181,126	0	181,126
	JDH3-02-009-R18-(RD)-Pavement Marking	18	16-Dec-26	06-Jan-27	357	0	0	12,269
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	16-Dec-26	19-Dec-26	357	0	0	3,579
	Thermoplastic continuous 100 mm wide (parking separator line)	2	19-Dec-26	21-Dec-26	357	0	0	1,323
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	21-Dec-26	23-Dec-26	357	0	0	1,901
	Thermoplastic continuous Chevron hatching - white (round abou	2	23-Dec-26	26-Dec-26	357	0	0	309
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2	26-Dec-26	28-Dec-26	357	0	0	1,579
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2	28-Dec-26	30-Dec-26	357	0	0	1,349
	Thermoplastic intermittent 500 mm wide White yield line - (B1.3	2	30-Dec-26	02-Jan-27	357	0	0	512
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z3-R18-RD	2	02-Jan-27	04-Jan-27	357	0	0	1,430
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2	04-Jan-27	06-Jan-27	357	0	0	286
	JDH3-02-009-R18-(RD)-Traffic Signage	6	16-Dec-26	23-Dec-26	369	0	0	20,134
	Supply and installation Traffic signs 2 Sheet with Single post - (B	4	16-Dec-26	21-Dec-26	369	0	0	16,769
	Supply and installation Traffic signs with Double post - (B1.10 14	2	21-Dec-26	23-Dec-26	369	0	0	3,365
R19		83	01-Sep-26 A	07-Dec-26	385	453,555	47,667	459,434
	JDH3-02-009-R19-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R19-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R19-W	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R19-Street Lighting Network -SL	21	03-Nov-26	26-Nov-26	394	140,739	0	146,618
	JDH3-02-009-R19-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	12	03-Nov-26	16-Nov-26	401	47,612	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2	03-Nov-26	04-Nov-26	407	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2	05-Nov-26	07-Nov-26	407	3,401	0	3,401
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2	15-Nov-26	16-Nov-26	401	3,401	0	3,401
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 4Cx95mm², Cu/XLPE	10	03-Nov-26	14-Nov-26	401	2,224	0	2,224
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	03-Nov-26	04-Nov-26	407	741	0	741
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	12-Nov-26	14-Nov-26	401	1,483	0	1,483
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 3x1Cx50mm², Cu/XL	2	05-Nov-26	07-Nov-26	409	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z3-F	2	05-Nov-26	07-Nov-26	409	1,520	0	1,520

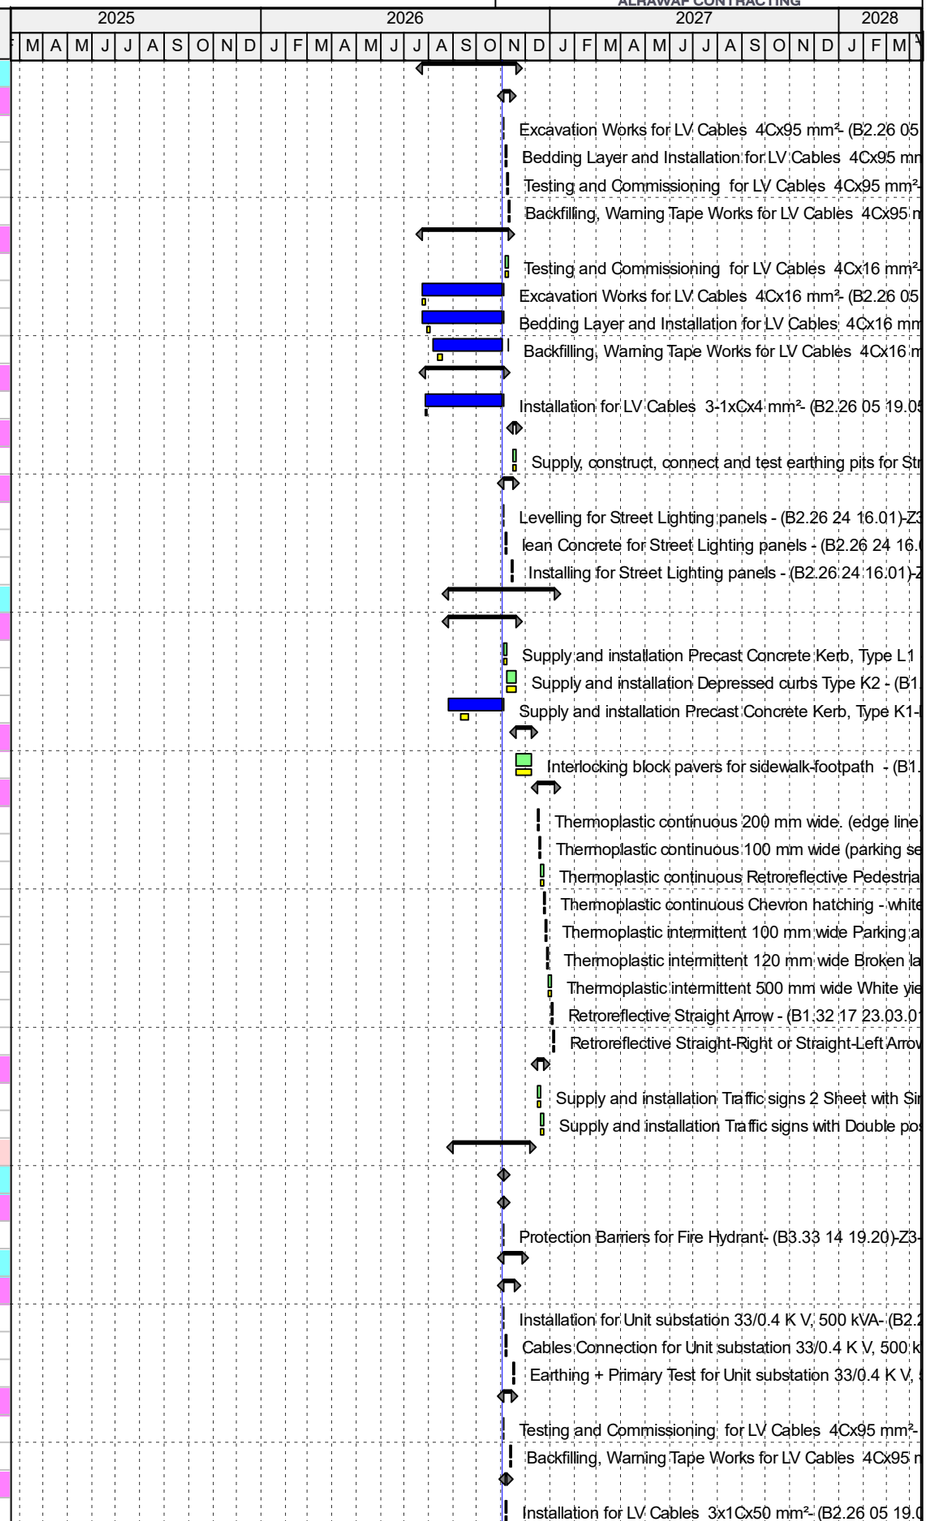


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R19-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	4	03-Nov-26	07-Nov-26	411	2,477	0	2,477
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	03-Nov-26	07-Nov-26	411	2,477	0	2,477
	JDH3-02-009-R19-(SL)-Earthing System for Distribution panels,S	2	21-Nov-26	22-Nov-26	394	300	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	21-Nov-26	22-Nov-26	394	300	0	1,126
	JDH3-02-009-R19-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	394	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R19-S	2	03-Nov-26	04-Nov-26	399	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2	05-Nov-26	07-Nov-26	399	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R19-S	2	14-Nov-26	15-Nov-26	394	7,232	0	7,232
	JDH3-02-009-R19-(SL)- LV Distribution Panel Main: 100A, MCCB	11	05-Nov-26	17-Nov-26	394	18,369	0	18,369
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z3-R19-S	2	05-Nov-26	07-Nov-26	399	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z3-F	2	08-Nov-26	09-Nov-26	399	3,674	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z3-R19-S	2	16-Nov-26	17-Nov-26	394	12,858	0	12,858
	JDH3-02-009-R19-(SL)-KWH meter mounting frame	2	18-Nov-26	19-Nov-26	394	2,072	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z3-R19-SL	2	18-Nov-26	19-Nov-26	394	2,072	0	2,072
	JDH3-02-009-R19-(SL)-Earthing System for Streetlighting feede	2	23-Nov-26	24-Nov-26	394	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2	23-Nov-26	24-Nov-26	394	0	0	852
	JDH3-02-009-R19-(SL)- LV Cables - Aluminium, 4Cx185mm²,ALI	8	03-Nov-26	11-Nov-26	401	1,212	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2	03-Nov-26	04-Nov-26	399	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2	05-Nov-26	07-Nov-26	401	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2	2	08-Nov-26	09-Nov-26	401	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2	10-Nov-26	11-Nov-26	401	121	0	121
	JDH3-02-009-R19-(SL)-RMU 33 KV	21	03-Nov-26	26-Nov-26	394	54,621	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z3-R19-SL	2	03-Nov-26	04-Nov-26	409	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z3-R19-SL	2	05-Nov-26	07-Nov-26	409	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z3-R1	2	25-Nov-26	26-Nov-26	394	0	0	4,202
	JDH3-02-009-R19-Road Works - RD	83	01-Sep-26 A	07-Dec-26	354	308,419	47,667	308,419
	JDH3-02-009-R19-(RD)-Precast Concrete Curb	65	01-Sep-26 A	16-Nov-26	354	122,546	47,667	122,546
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	05-Nov-26	354	15,078	0	15,078
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9	05-Nov-26	16-Nov-26	354	55,656	0	55,656
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	7	01-Sep-26 A	03-Nov-26	354	51,811	47,667	51,811
	JDH3-02-009-R19-(RD)-Precast Interlocking Block Pavers	18	16-Nov-26	07-Dec-26	354	185,873	0	185,873
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18	16-Nov-26	07-Dec-26	354	185,873	0	185,873
	R20	132	28-Jul-26 A	25-Jan-27	343	1,615,623	347,928	1,627,089
	JDH3-02-009-R20-TSE Network - TSE	54	03-Sep-26 A	07-Nov-26	412	84,994	25,206	84,994
	JDH3-02-009-R20-(TSE)-Butterfly Valve-300 mm on pipe dia (315	9	15-Sep-26 A	04-Nov-26	414	48,390	15,969	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2	15-Sep-26 A	04-Nov-26	414	43,551	14,372	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	24-Sep-26 A	04-Nov-26	414	4,839	1,597	4,839
	JDH3-02-009-R20-(TSE)-Valve Chamber on 315 mm dia pipeline	54	03-Sep-26 A	07-Nov-26	412	36,604	9,237	36,604
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	04-Nov-26	07-Nov-26	412	8,613	0	8,613
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	16-Sep-26 A	04-Nov-26	412	23,685	7,816	23,685
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	03-Sep-26 A	04-Nov-26	412	4,306	1,421	4,306
	JDH3-02-009-R20-Potable Water Network - WT	56	01-Sep-26 A	17-Nov-26	402	399,301	138,505	399,301
	JDH3-02-009-R20-(WT)-Wash-Out Valve-150 mm on pipe dia (63	4	03-Nov-26	07-Nov-26	406	19,542	0	19,542
	Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E	2	03-Nov-26	04-Nov-26	402	17,588	0	17,588
	Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6	2	05-Nov-26	07-Nov-26	406	1,954	0	1,954
	JDH3-02-009-R20-(WT)-Wash-Out Chamber on 630 mm dia pipe	8	05-Nov-26	14-Nov-26	402	27,211	0	27,211
	Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m	2	05-Nov-26	07-Nov-26	402	4,082	0	4,082
	PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fr	2	08-Nov-26	09-Nov-26	402	2,721	0	2,721
	Installationfor Wash-Out Chamber on pipe dia 630 mm - depth	2	10-Nov-26	11-Nov-26	402	14,966	0	14,966
	Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm - c	2	12-Nov-26	14-Nov-26	402	5,442	0	5,442
	JDH3-02-009-R20-(WT)-Butterfly Valve-600 mm on pipe dia (630)	6	16-Sep-26 A	14-Nov-26	405	246,581	98,633	246,581
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2	16-Sep-26 A	14-Nov-26	405	221,923	88,769	221,923
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 630	2	22-Sep-26 A	14-Nov-26	405	24,658	9,863	24,658

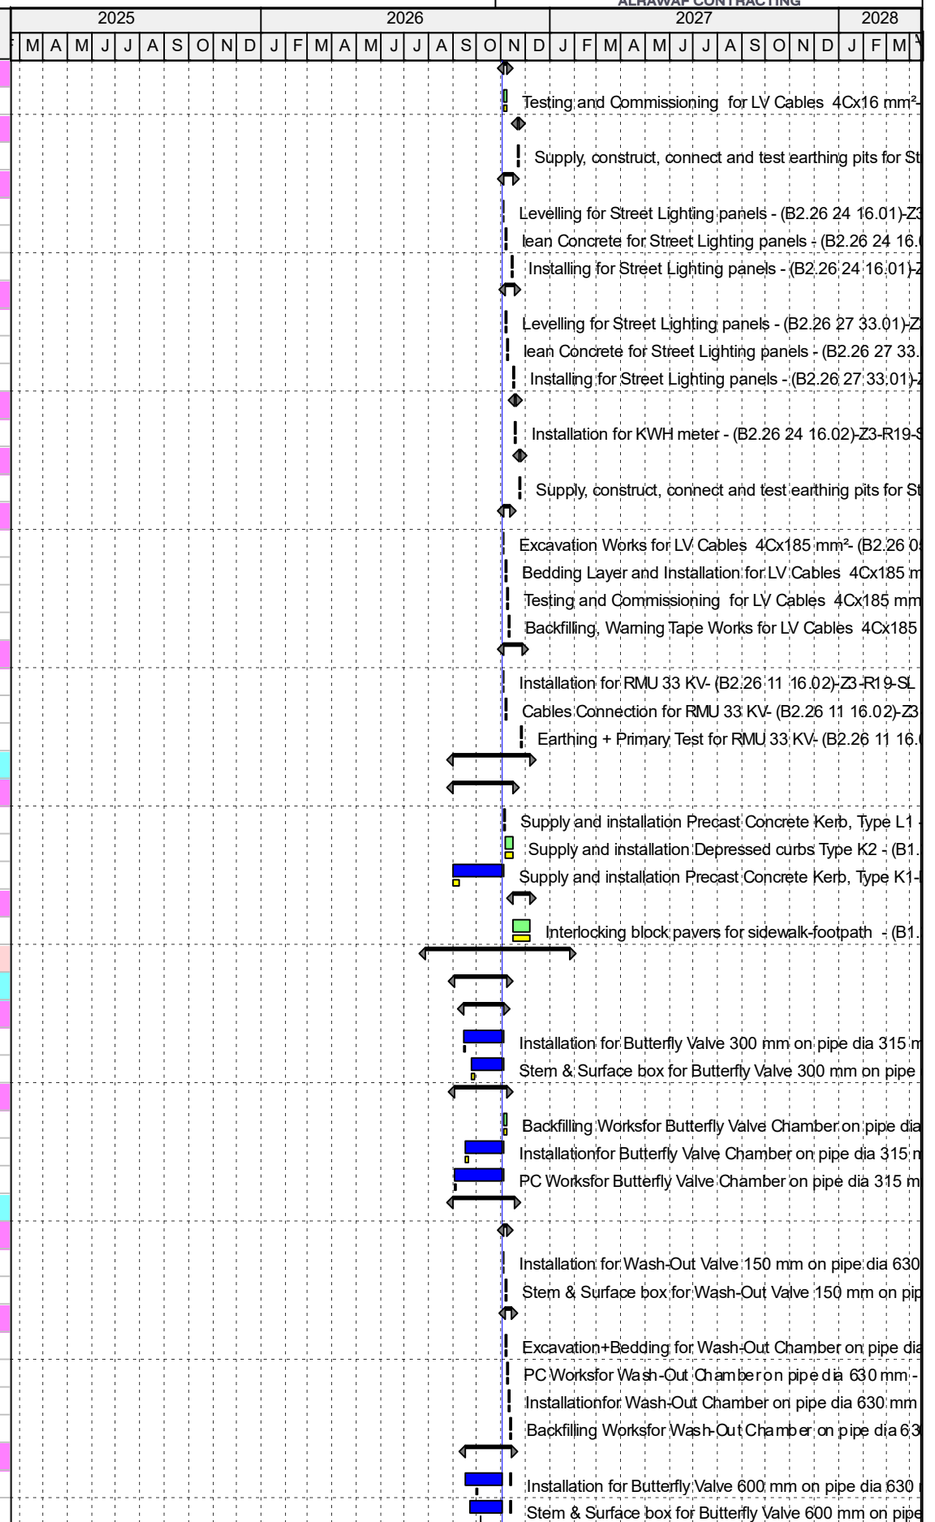

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R20-(WT)-Valve Chamber on 630 mm dia pipeline	55	01-Sep-26 A	16-Nov-26	403	91,796	36,718	91,796
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2	15-Nov-26	16-Nov-26	403	18,359	0	18,359
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2	16-Sep-26 A	14-Nov-26	403	50,488	20,195	50,488
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2	03-Sep-26 A	14-Nov-26	403	9,180	5,508	9,180
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2	01-Sep-26 A	14-Nov-26	402	13,769	11,015	13,769
	JDH3-02-009-R20-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	3,420	0	3,420
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R20-W	2	03-Nov-26	04-Nov-26	413	3,420	0	3,420
	JDH3-02-009-R20-(WT)-Valve Chamber on 400 mm dia pipeline	52	12-Sep-26 A	17-Nov-26	402	10,752	3,154	10,752
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	15-Nov-26	17-Nov-26	402	2,867	0	2,867
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	12-Sep-26 A	15-Nov-26	402	7,885	3,154	7,885
	JDH3-02-009-R20-Electrical Network - EL	10	12-Nov-26	23-Nov-26	362	216,274	0	216,274
	JDH3-02-009-R20-(EL)-MV cable trench size 1.5m wide and 80c	5	12-Nov-26	17-Nov-26	362	3,356	0	3,356
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	5	12-Nov-26	17-Nov-26	362	3,356	0	3,356
	JDH3-02-009-R20-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	5	18-Nov-26	23-Nov-26	362	212,919	0	212,919
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	18-Nov-26	23-Nov-26	362	212,919	0	212,919
	JDH3-02-009-R20-Street Lighting Network -SL	44	28-Jul-26 A	08-Dec-26	381	167,540	149,001	167,540
	JDH3-02-009-R20-(SL)-Lighting Pole with double arms 16 m hei	10	28-Jul-26 A	29-Nov-26	389	79,730	75,146	79,730
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	4	05-Aug-26 A	29-Nov-26	389	3,987	3,189	3,987
	Excavation for RC foundation for Lighting Pole double arms- (B2	2	28-Jul-26 A	29-Nov-26	362	7,973	7,574	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2	29-Jul-26 A	29-Nov-26	385	7,973	7,574	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2.:	2	30-Jul-26 A	29-Nov-26	385	7,973	7,574	7,973
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	4	01-Aug-26 A	29-Nov-26	385	51,825	49,233	51,825
	JDH3-02-009-R20-(SL)-Street Lighting(LED) Luminaire complet	6	01-Aug-26 A	29-Nov-26	389	20,198	19,188	20,198
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.'	3	01-Aug-26 A	29-Nov-26	389	16,159	15,351	16,159
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3	01-Aug-26 A	29-Nov-26	389	4,040	3,838	4,040
	JDH3-02-009-R20-(SL)- LV Cables - Single Core Copper, 3-1 xC 4	2	16-Sep-26 A	29-Nov-26	385	3,849	3,656	3,849
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2	16-Sep-26 A	29-Nov-26	385	3,849	3,656	3,849
	JDH3-02-009-R20-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	23	04-Aug-26 A	08-Dec-26	362	63,763	51,010	63,763
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	5	05-Aug-26 A	01-Dec-26	363	50,339	40,271	50,339
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	19-Aug-26 A	08-Dec-26	362	6,712	5,370	6,712
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	04-Aug-26 A	01-Dec-26	363	6,712	5,370	6,712
	JDH3-02-009-R20-Road Works - RD	50	05-Sep-26 A	13-Dec-26	380	747,513	35,217	748,736
	JDH3-02-009-R20-(RD)-Bituminous concrete wearing course 50	5	03-Nov-26	08-Nov-26	387	494,057	0	494,057
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	03-Nov-26	08-Nov-26	387	494,057	0	494,057
	JDH3-02-009-R20-(RD)-Precast Concrete Curb	6	05-Sep-26 A	13-Dec-26	362	176,083	35,217	176,083
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	6	05-Sep-26 A	13-Dec-26	362	176,083	35,217	176,083
	JDH3-02-009-R20-(RD)-Pavement Marking	23	09-Nov-26	05-Dec-26	387	33,227	0	34,450
	Thermoplastic continuous 120 mm wide centre lane- single line	2	09-Nov-26	10-Nov-26	387	857	0	857
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	5	11-Nov-26	16-Nov-26	387	26,832	0	26,832
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2	17-Nov-26	18-Nov-26	387	1,034	0	1,034
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	19-Nov-26	21-Nov-26	387	3,802	0	3,802
	Thermoplastic continuous Painted rumble strips marking (300m	2	22-Nov-26	23-Nov-26	387	702	0	702
	Retroreflective Straight-Right or Straight-Left Arrow - (B1.32 17 2	2	29-Nov-26	30-Nov-26	387	0	0	429
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.(	2	01-Dec-26	02-Dec-26	387	0	0	715
	Thermoplastic continuous Chevron hatching - white (round abou	2	03-Dec-26	05-Dec-26	387	0	0	78
	JDH3-02-009-R20-(RD)-Traffic Signage	14	09-Nov-26	24-Nov-26	392	44,146	0	44,146
	Supply and installation Traffic signs 1 Sheet with Single post - (E	14	09-Nov-26	24-Nov-26	392	44,146	0	44,146
	JDH3-02-009-R20-Landscape Works - LS	7	18-Jan-27	25-Jan-27	103	0	0	10,243
	JDH3-02-009-R20-(LS)-HDPE for Secondary Network	7	18-Jan-27	25-Jan-27	103	0	0	10,243
	Pipe line with Diam 90 mm PN10 - depth from 0 to 1.5 m- (B7.3	7	18-Jan-27	25-Jan-27	103	0	0	10,243
R151		131	04-Aug-26 A	06-Jan-27	359	506,812	123,341	517,738
	JDH3-02-009-R151-Potable Water Network - WT	2	22-Nov-26	23-Nov-26	397	4,885	0	4,885
	JDH3-02-009-R151-(WT)-Fire Hydrant	2	22-Nov-26	23-Nov-26	397	4,885	0	4,885

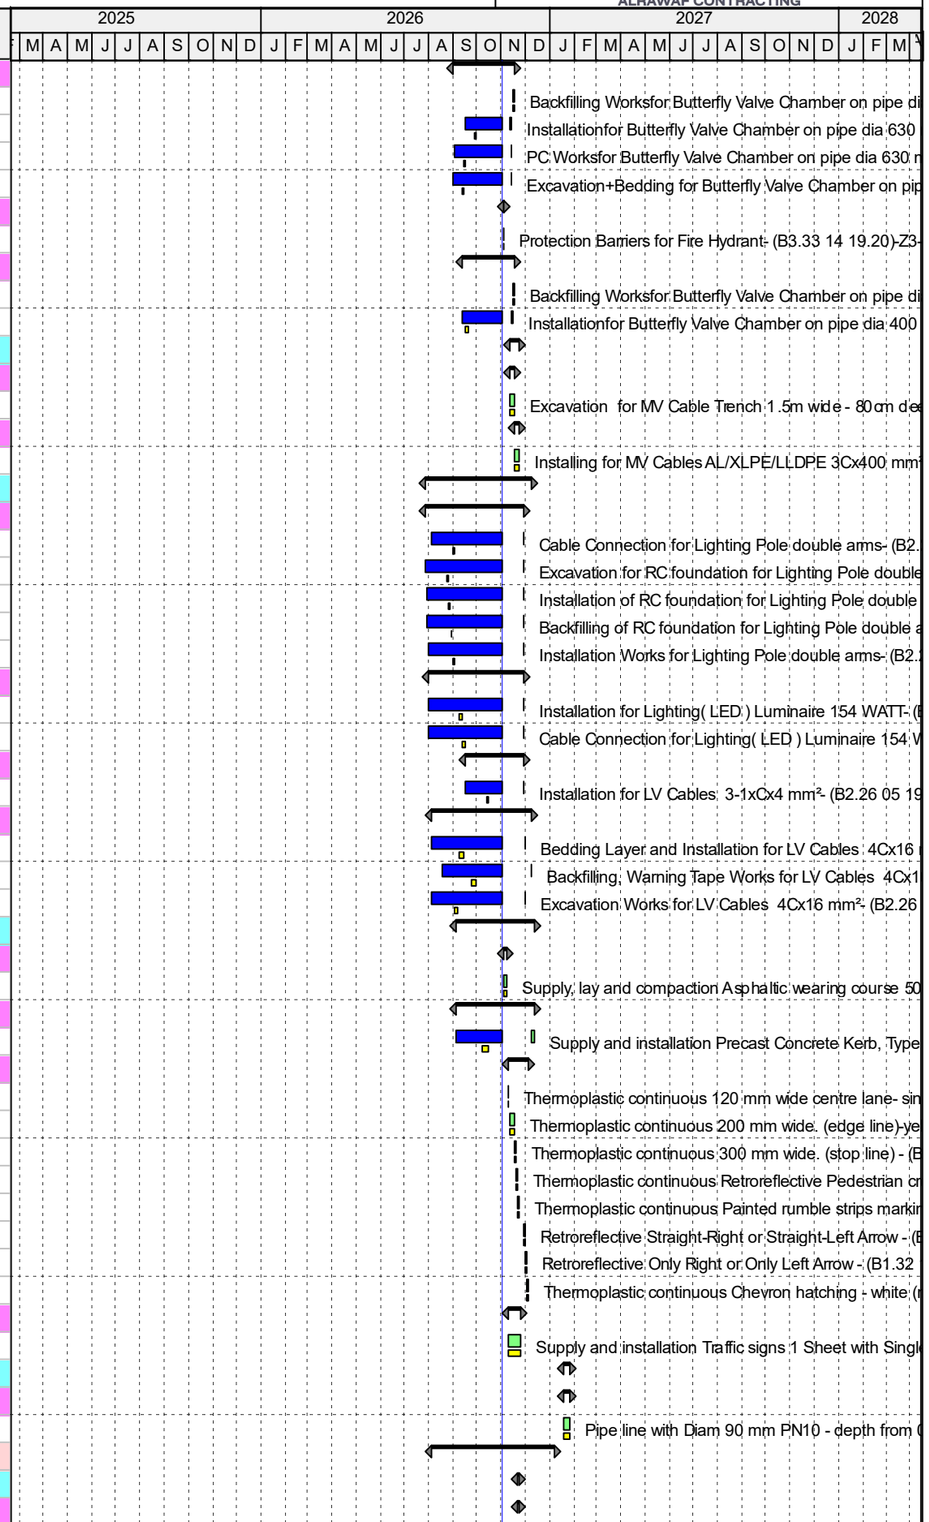

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R151-W	2	22-Nov-26	23-Nov-26	397	4,885	0	4,885
	JDH3-02-009-R151-Street Lighting Network -SL	88	04-Aug-26 A	17-Nov-26	402	180,735	63,744	180,735
	JDH3-02-009-R151-(SL)- LV Cables - Copper, 4 Cx 95 mm²,Cu/XLP	8	03-Nov-26	11-Nov-26	403	80,468	0	80,468
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	03-Nov-26	04-Nov-26	403	8,047	0	8,047
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	05-Nov-26	07-Nov-26	403	60,351	0	60,351
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	08-Nov-26	09-Nov-26	403	4,023	0	4,023
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	10-Nov-26	11-Nov-26	403	8,047	0	8,047
	JDH3-02-009-R151-(SL)- LV Cables - Copper, 4 Cx 16 mm²,Cu/XLP	82	06-Aug-26 A	11-Nov-26	403	77,159	58,641	77,159
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	05-Nov-26	10-Nov-26	404	3,858	0	3,858
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	06-Aug-26 A	04-Nov-26	404	7,716	6,173	7,716
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5	08-Aug-26 A	04-Nov-26	404	57,869	46,295	57,869
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	11-Aug-26 A	11-Nov-26	403	7,716	6,173	7,716
	JDH3-02-009-R151-(SL)-Earthing System for Streetlighting feed	2	12-Nov-26	14-Nov-26	403	426	0	426
	Supply, construct, connect and test earthing pits for Street Light	2	12-Nov-26	14-Nov-26	403	426	0	426
	JDH3-02-009-R151-(SL)-Earthing System for Distribution panels	2	16-Nov-26	17-Nov-26	402	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	16-Nov-26	17-Nov-26	402	1,126	0	1,126
	JDH3-02-009-R151-(SL)- Street Lighting Panels	10	04-Nov-26	15-Nov-26	402	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z3-R151-	2	04-Nov-26	05-Nov-26	406	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z3-F	2	07-Nov-26	08-Nov-26	406	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z3-R151-	2	14-Nov-26	15-Nov-26	402	7,232	0	7,232
	JDH3-02-009-R151-(SL)-Lighting Pole with single arm 12 m heig	7	04-Aug-26 A	11-Nov-26	403	6,378	5,103	6,378
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	7	04-Aug-26 A	11-Nov-26	403	6,378	5,103	6,378
	JDH3-02-009-R151-(SL)- LV Cables - Single Core Copper, 3 -1x C	2	03-Nov-26	04-Nov-26	409	4,847	0	4,847
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2	03-Nov-26	04-Nov-26	409	4,847	0	4,847
	JDH3-02-009-R151-Road Works - RD	89	25-Aug-26 A	08-Dec-26	352	321,192	59,597	321,192
	JDH3-02-009-R151-(RD)-Precast Concrete Curb	71	25-Aug-26 A	17-Nov-26	352	144,497	59,597	144,497
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	05-Nov-26	352	16,813	0	16,813
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10	05-Nov-26	17-Nov-26	352	64,950	0	64,950
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9	25-Aug-26 A	03-Nov-26	352	62,734	59,597	62,734
	JDH3-02-009-R151-(RD)-Precast Interlocking Block Pavers	18	17-Nov-26	08-Dec-26	352	176,695	0	176,695
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	18	17-Nov-26	08-Dec-26	352	176,695	0	176,695
	JDH3-02-009-R151-Landscape Works - LS	4	03-Jan-27	06-Jan-27	103	0	0	10,926
	JDH3-02-009-R151-(LS)-HDPE for Secondary Network	4	03-Jan-27	06-Jan-27	103	0	0	10,926
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	4	03-Jan-27	06-Jan-27	103	0	0	10,926
Z2		239	02-Jun-26 A	05-Apr-27	287	8,013,454	1,664,055	8,929,282
R07		57	08-Sep-26 A	15-Dec-26	378	235,753	47,846	1,009,133
	JDH3-02-009-R07-TSE Network - TSE	4	03-Nov-26	07-Nov-26	411	31,010	0	31,010
	JDH3-02-009-R07-(TSE)-Wash-Out Valve-100 mm on pipe dia (22	4	03-Nov-26	07-Nov-26	411	15,346	0	15,346
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (B	2	03-Nov-26	04-Nov-26	411	13,811	0	13,811
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 22	2	05-Nov-26	07-Nov-26	411	1,535	0	1,535
	JDH3-02-009-R07-(TSE)-Wash-Out Chamber on 225 mm dia pipe	4	03-Nov-26	07-Nov-26	411	15,665	0	15,665
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2	03-Nov-26	04-Nov-26	411	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - d	2	05-Nov-26	07-Nov-26	411	4,177	0	4,177
	JDH3-02-009-R07-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	JDH3-02-009-R07-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R07-W	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	JDH3-02-009-R07-Electrical Network - EL	13	10-Nov-26	24-Nov-26	376	196,152	0	196,152
	JDH3-02-009-R07-(EL)-MV cable trench size 1.5m wide and 80c	6	10-Nov-26	16-Nov-26	376	5,903	0	5,903
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6	10-Nov-26	16-Nov-26	376	5,903	0	5,903
	JDH3-02-009-R07-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7	17-Nov-26	24-Nov-26	376	190,249	0	190,249
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	17-Nov-26	22-Nov-26	376	184,448	0	184,448
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	23-Nov-26	24-Nov-26	376	5,801	0	5,801
	JDH3-02-009-R07-Street Lighting Network -SL	57	08-Sep-26 A	15-Dec-26	378	3,217	47,846	105,415

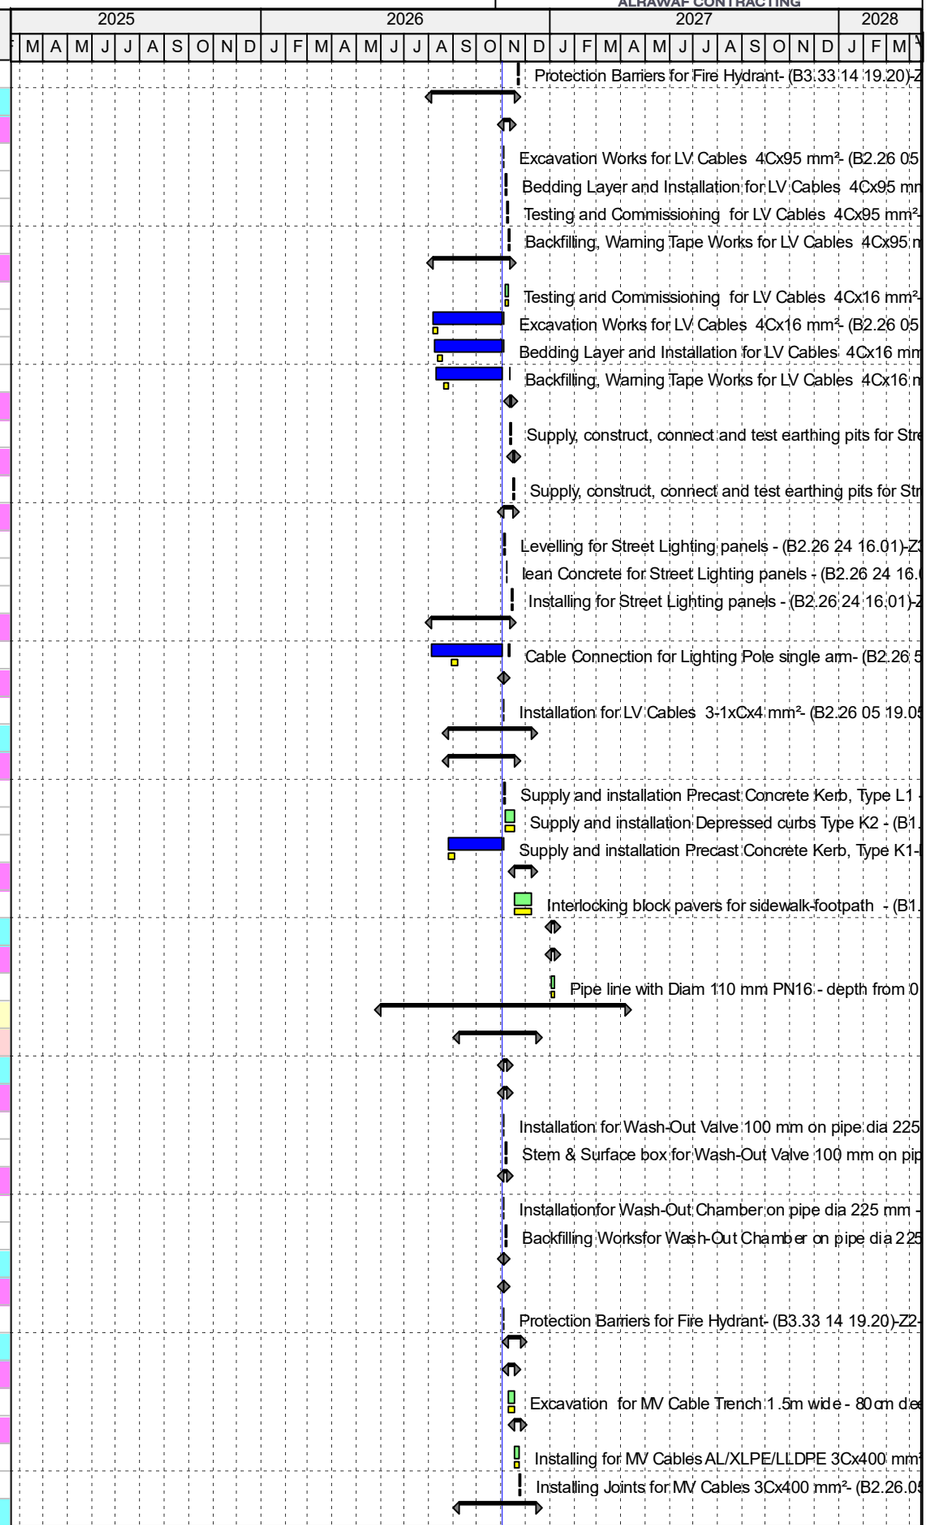


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R07-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	4	07-Dec-26	10-Dec-26	382	0	0	7,730
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	07-Dec-26	08-Dec-26	382	0	0	2,577
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	09-Dec-26	10-Dec-26	382	0	0	5,154
	JDH3-02-009-R07-(SL)-Lighting Pole with single arm 12 m heigh	7	03-Nov-26	10-Nov-26	406	0	0	5,816
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	7	03-Nov-26	10-Nov-26	406	0	0	5,816
	JDH3-02-009-R07-(SL)-Earthing System for Distribution panels,S	2	03-Nov-26	04-Nov-26	411	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	03-Nov-26	04-Nov-26	411	0	0	1,126
	JDH3-02-009-R07-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	404	0	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R07-S	2	03-Nov-26	04-Nov-26	409	0	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2	05-Nov-26	07-Nov-26	409	0	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R07-S	2	14-Nov-26	15-Nov-26	404	0	0	7,232
	JDH3-02-009-R07-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	57	08-Sep-26 A	15-Dec-26	376	3,217	47,846	80,413
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	05-Dec-26	09-Dec-26	376	0	0	4,021
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	10-Dec-26	15-Dec-26	376	0	0	8,041
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	08-Sep-26 A	03-Dec-26	376	3,217	5,629	8,041
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5	10-Sep-26 A	03-Dec-26	376	0	42,217	60,309
	JDH3-02-009-R07-Telecommunications Network - TEL	9	03-Nov-26	12-Nov-26	406	0	0	25,728
	JDH3-02-009-R07-(TEL)-Ducts	9	03-Nov-26	12-Nov-26	406	0	0	25,728
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2	03-Nov-26	04-Nov-26	406	0	0	3,859
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	5	05-Nov-26	10-Nov-26	406	0	0	19,296
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2	11-Nov-26	12-Nov-26	406	0	0	2,573
	JDH3-02-009-R07-Road Works - RD	20	03-Nov-26	25-Nov-26	367	0	0	645,453
	JDH3-02-009-R07-(RD)-Bituminous concrete wearing course 50	6	15-Nov-26	21-Nov-26	367	0	0	369,411
	Supply, lay and compaction Asphaltic wearing course 50 mm in	6	15-Nov-26	21-Nov-26	367	0	0	369,411
	JDH3-02-009-R07-(RD)-Precast Concrete Curb	5	03-Nov-26	08-Nov-26	367	0	0	80,561
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	367	0	0	12,577
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3	05-Nov-26	08-Nov-26	367	0	0	67,984
	JDH3-02-009-R07-(RD)-Precast Interlocking Block Pavers	5	09-Nov-26	14-Nov-26	367	0	0	178,985
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	5	09-Nov-26	14-Nov-26	367	0	0	178,985
	JDH3-02-009-R07-(RD)-Pavement Marking	2	22-Nov-26	23-Nov-26	367	0	0	5,051
	Thermoplastic continuous 120 mm wide centre lane- double lin	2	22-Nov-26	23-Nov-26	367	0	0	5,051
	JDH3-02-009-R07-(RD)-Traffic Signage	4	22-Nov-26	25-Nov-26	367	0	0	11,445
	Supply and installation Traffic signs 1 Sheet with Single post - (E	4	22-Nov-26	25-Nov-26	367	0	0	11,445
	R08	23	03-Nov-26	29-Nov-26	392	748,338	0	748,338
	JDH3-02-009-R08-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	388	4,397	0	4,397
	JDH3-02-009-R08-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	388	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R08-W	2	03-Nov-26	04-Nov-26	388	4,397	0	4,397
	JDH3-02-009-R08-Electrical Network - EL	17	05-Nov-26	24-Nov-26	388	164,372	0	164,372
	JDH3-02-009-R08-(EL)-MV cable trench size 1.5m wide and 80c	17	05-Nov-26	24-Nov-26	388	8,260	0	8,260
	Excavation for MV Cable Trench 1.5m wide - 80 cm deep- (B2.3	6	05-Nov-26	11-Nov-26	388	4,956	0	4,956
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5	19-Nov-26	24-Nov-26	388	3,304	0	3,304
	JDH3-02-009-R08-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	6	12-Nov-26	18-Nov-26	388	156,112	0	156,112
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4	12-Nov-26	16-Nov-26	388	150,311	0	150,311
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	17-Nov-26	18-Nov-26	388	5,801	0	5,801
	JDH3-02-009-R08-Street Lighting Network -SL	13	03-Nov-26	17-Nov-26	402	21,511	0	21,511
	JDH3-02-009-R08-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	10	03-Nov-26	14-Nov-26	405	10,054	0	10,054
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	03-Nov-26	08-Nov-26	405	3,351	0	3,351
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	09-Nov-26	14-Nov-26	405	6,703	0	6,703
	JDH3-02-009-R08-(SL)-Earthing System for Distribution panels,S	2	16-Nov-26	17-Nov-26	382	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	16-Nov-26	17-Nov-26	382	1,126	0	1,126
	JDH3-02-009-R08-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	404	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R08-S	2	03-Nov-26	04-Nov-26	413	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2	03-Nov-26	04-Nov-26	389	2,066	0	2,066

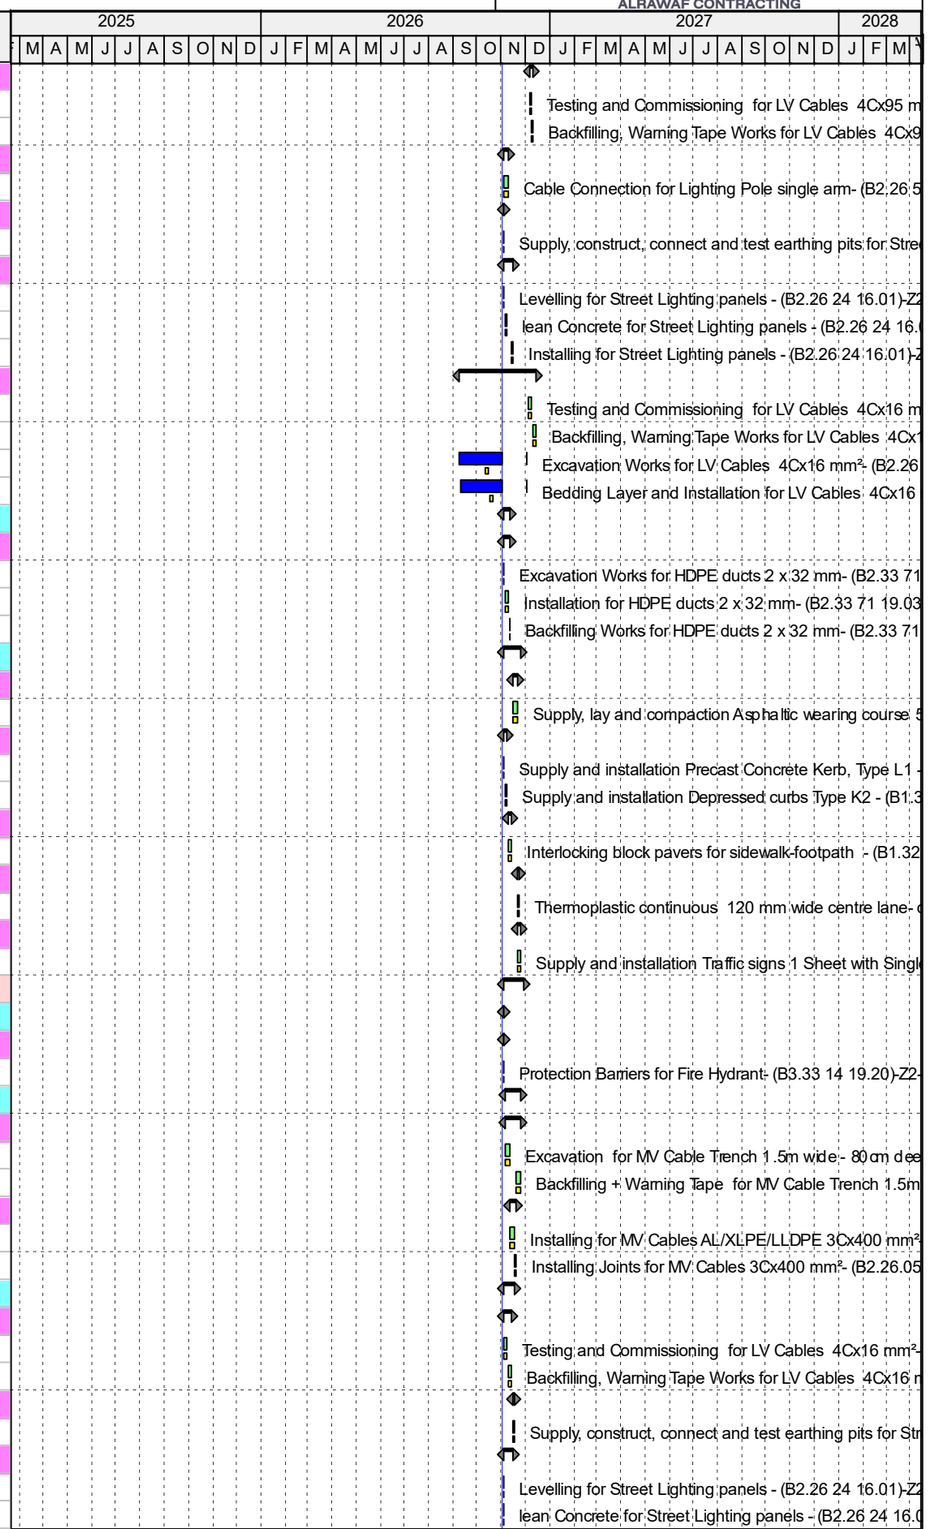


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R08-S	2	14-Nov-26	15-Nov-26	382	7,232	0	7,232
	JDH3-02-009-R08-Telecommunications Network - TEL	23	03-Nov-26	29-Nov-26	382	88,414	0	88,414
	JDH3-02-009-R08-(TEL)-Reinforced Concrete Duct 6-ways ducts	8	03-Nov-26	11-Nov-26	385	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2	03-Nov-26	04-Nov-26	385	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2	05-Nov-26	07-Nov-26	385	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2	08-Nov-26	09-Nov-26	385	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2	10-Nov-26	11-Nov-26	385	191	0	191
	JDH3-02-009-R08-(TEL)-Unreinforced Concrete Duct 6-ways duc	10	18-Nov-26	29-Nov-26	382	86,508	0	86,508
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3	18-Nov-26	21-Nov-26	382	18,537	0	18,537
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	7	22-Nov-26	29-Nov-26	382	67,970	0	67,970
	JDH3-02-009-R08-Road Works - RD	18	03-Nov-26	23-Nov-26	370	469,644	0	469,644
	JDH3-02-009-R08-(RD)-Bituminous concrete wearing course 50	5	18-Nov-26	23-Nov-26	370	285,288	0	285,288
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	18-Nov-26	23-Nov-26	370	285,288	0	285,288
	JDH3-02-009-R08-(RD)-Precast Concrete Curb	11	03-Nov-26	15-Nov-26	370	62,795	0	62,795
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	370	9,001	0	9,001
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9	05-Nov-26	15-Nov-26	370	53,795	0	53,795
	JDH3-02-009-R08-(RD)-Precast Interlocking Block Pavers	2	16-Nov-26	17-Nov-26	370	121,560	0	121,560
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	2	16-Nov-26	17-Nov-26	370	121,560	0	121,560
R09		157	11-Aug-26 A	10-Feb-27	329	400,196	117,626	447,731
	JDH3-02-009-R09-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	JDH3-02-009-R09-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R09-W	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	JDH3-02-009-R09-Electrical Network - EL	82	11-Aug-26 A	15-Nov-26	248	200,109	49,062	200,109
	JDH3-02-009-R09-(EL)-MV cable trench size 1.5m wide and 80c	82	11-Aug-26 A	15-Nov-26	248	9,658	1,449	9,658
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6	08-Nov-26	15-Nov-26	248	3,863	0	3,863
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6	11-Aug-26 A	08-Nov-26	248	5,795	1,449	5,795
	JDH3-02-009-R09-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7	12-Aug-26 A	08-Nov-26	248	190,451	47,613	190,451
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	13-Aug-26 A	08-Nov-26	248	8,701	2,175	8,701
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	12-Aug-26 A	08-Nov-26	248	181,750	45,437	181,750
	JDH3-02-009-R09-Street Lighting Network -SL	46	22-Sep-26 A	24-Nov-26	397	63,630	32,890	63,630
	JDH3-02-009-R09-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	43	22-Sep-26 A	24-Nov-26	324	58,752	29,964	58,752
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	15-Nov-26	19-Nov-26	324	2,938	0	2,938
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4	19-Nov-26	24-Nov-26	324	5,875	0	5,875
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4	23-Sep-26 A	15-Nov-26	248	44,064	26,439	44,064
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	22-Sep-26 A	15-Nov-26	248	5,875	3,525	5,875
	JDH3-02-009-R09-(SL)-Lighting Pole with single arm 12 m heigh	8	27-Sep-26 A	07-Nov-26	412	4,878	2,927	4,878
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	8	27-Sep-26 A	07-Nov-26	412	4,878	2,927	4,878
	JDH3-02-009-R09-Telecommunications Network - TEL	11	12-Nov-26	25-Nov-26	395	91,933	0	91,933
	JDH3-02-009-R09-(TEL)-Unreinforced Concrete Duct 6-ways duc	10	12-Nov-26	24-Nov-26	248	66,205	0	66,205
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	2	12-Nov-26	15-Nov-26	248	11,034	0	11,034
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	4	15-Nov-26	19-Nov-26	248	40,458	0	40,458
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	4	19-Nov-26	24-Nov-26	248	14,712	0	14,712
	JDH3-02-009-R09-(TEL)-Ducts	9	15-Nov-26	25-Nov-26	395	25,728	0	25,728
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2	15-Nov-26	17-Nov-26	395	3,859	0	3,859
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	5	17-Nov-26	23-Nov-26	395	19,296	0	19,296
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2	23-Nov-26	25-Nov-26	395	2,573	0	2,573
	JDH3-02-009-R09-Road Works - RD	95	03-Sep-26 A	10-Feb-27	248	39,638	35,674	87,173
	JDH3-02-009-R09-(RD)-Precast Concrete Curb	6	03-Sep-26 A	26-Nov-26	248	39,638	35,674	39,638
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	6	03-Sep-26 A	26-Nov-26	248	39,638	35,674	39,638
	JDH3-02-009-R09-(RD)-Pavement Marking	19	19-Jan-27	10-Feb-27	248	0	0	13,484
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	19-Jan-27	21-Jan-27	255	0	0	6,596
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2	21-Jan-27	24-Jan-27	255	0	0	609
	Thermoplastic continuous 100 mm wide (parking separator line)	2	24-Jan-27	26-Jan-27	255	0	0	369

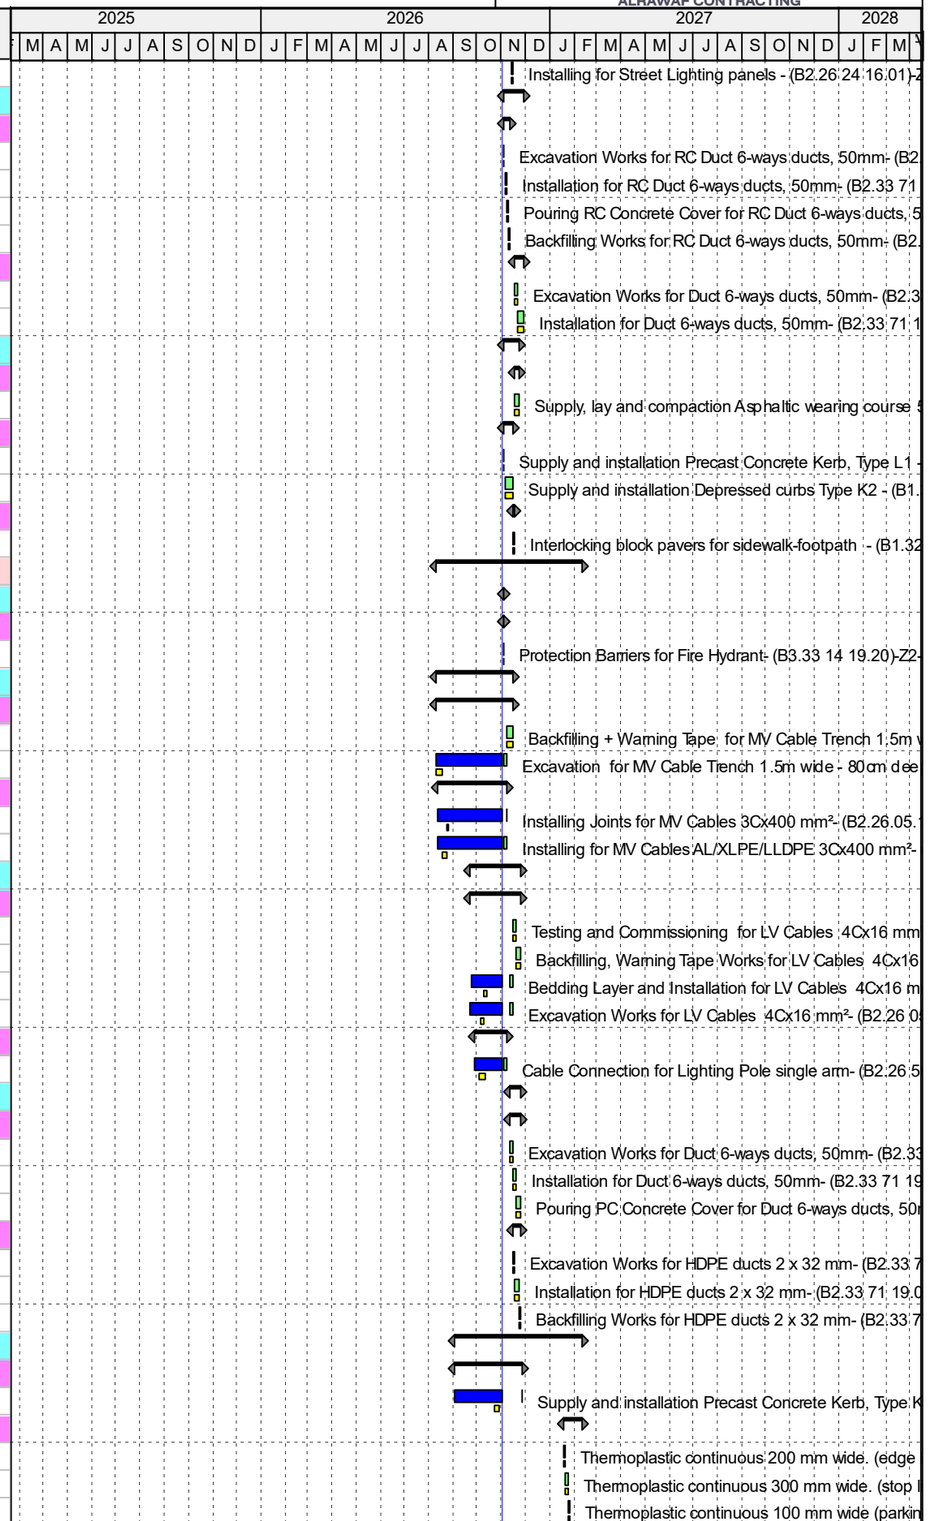


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	26-Jan-27	28-Jan-27	255	0	0	4,753
	Thermoplastic continuous Chevron hatching - white (round abou	2	06-Feb-27	08-Feb-27	248	0	0	726
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2	08-Feb-27	10-Feb-27	248	0	0	430
	JDH3-02-009-R09-(RD)-Traffic Signage	8	27-Jan-27	06-Feb-27	248	0	0	34,050
	Supply and installation Traffic signs 2 Sheet with Single post - (E	5	27-Jan-27	02-Feb-27	248	0	0	23,955
	Supply and installation Traffic signs with Double post - (B1.10 14	3	02-Feb-27	06-Feb-27	248	0	0	10,095
R11		134	13-Jun-26 A	29-Nov-26	392	621,455	128,351	647,881
	JDH3-02-009-R11-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R11-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R11-W	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R11-Electrical Network - EL	118	13-Jun-26 A	10-Nov-26	409	238,478	123,279	238,478
	JDH3-02-009-R11-(EL)-MV cable trench size 1.5m wide and 80c	17	13-Jun-26 A	04-Nov-26	412	8,260	6,195	8,260
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	6	13-Jun-26 A	04-Nov-26	409	4,956	3,717	4,956
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3	04-Jul-26 A	04-Nov-26	412	3,304	2,478	3,304
	JDH3-02-009-R11-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	103	27-Jun-26 A	07-Nov-26	410	161,272	117,084	161,272
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	04-Nov-26	07-Nov-26	410	5,160	0	5,160
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	4	27-Jun-26 A	04-Nov-26	409	150,311	112,733	150,311
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	02-Jul-26 A	04-Nov-26	410	5,801	4,351	5,801
	JDH3-02-009-R11-(EL)-RMU 33 KV	6	03-Nov-26	10-Nov-26	409	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z2-R11-EL	2	03-Nov-26	05-Nov-26	409	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z2-R11-EL	2	05-Nov-26	08-Nov-26	409	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z2-R1	2	08-Nov-26	10-Nov-26	409	4,925	0	4,925
	JDH3-02-009-R11-Street Lighting Network -SL	67	25-Aug-26 A	22-Nov-26	398	190,336	5,072	198,224
	JDH3-02-009-R11-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	10	03-Nov-26	14-Nov-26	401	47,612	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2	03-Nov-26	04-Nov-26	405	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2	05-Nov-26	07-Nov-26	405	3,401	0	3,401
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2	12-Nov-26	14-Nov-26	401	3,401	0	3,401
	JDH3-02-009-R11-(SL)-RMU 33 KV	14	03-Nov-26	18-Nov-26	401	58,823	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z2-R11-SL	2	03-Nov-26	04-Nov-26	409	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z2-R11-SL	2	05-Nov-26	07-Nov-26	409	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z2-R1	2	17-Nov-26	18-Nov-26	401	4,202	0	4,202
	JDH3-02-009-R11-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL/	8	03-Nov-26	11-Nov-26	401	1,212	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2	03-Nov-26	04-Nov-26	401	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2	05-Nov-26	07-Nov-26	401	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2(	2	08-Nov-26	09-Nov-26	401	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2	10-Nov-26	11-Nov-26	401	121	0	121
	JDH3-02-009-R11-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	10	05-Nov-26	16-Nov-26	401	47,015	0	47,015
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	05-Nov-26	07-Nov-26	403	4,702	0	4,702
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	08-Nov-26	09-Nov-26	403	35,261	0	35,261
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	10-Nov-26	11-Nov-26	403	2,351	0	2,351
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	15-Nov-26	16-Nov-26	401	4,702	0	4,702
	JDH3-02-009-R11-(SL)- LV Cables - Copper, 3x1Cx50mm²,Cu/XL	2	08-Nov-26	09-Nov-26	407	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z2-F	2	08-Nov-26	09-Nov-26	407	1,520	0	1,520
	JDH3-02-009-R11-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	55	25-Aug-26 A	08-Nov-26	388	3,382	5,072	10,145
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	03-Nov-26	08-Nov-26	388	3,382	0	3,382
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	25-Aug-26 A	08-Nov-26	388	0	5,072	6,763
	JDH3-02-009-R11-(SL)-Earthing System for Distribution panels,S	2	21-Nov-26	22-Nov-26	378	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	21-Nov-26	22-Nov-26	378	0	0	1,126
	JDH3-02-009-R11-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	378	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R11-S	2	03-Nov-26	04-Nov-26	383	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2	05-Nov-26	07-Nov-26	383	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R11-S	2	14-Nov-26	15-Nov-26	378	7,232	0	7,232
	JDH3-02-009-R11-(SL)- LV Distribution Panel Main: 100A, MCCB	11	05-Nov-26	17-Nov-26	378	18,369	0	18,369

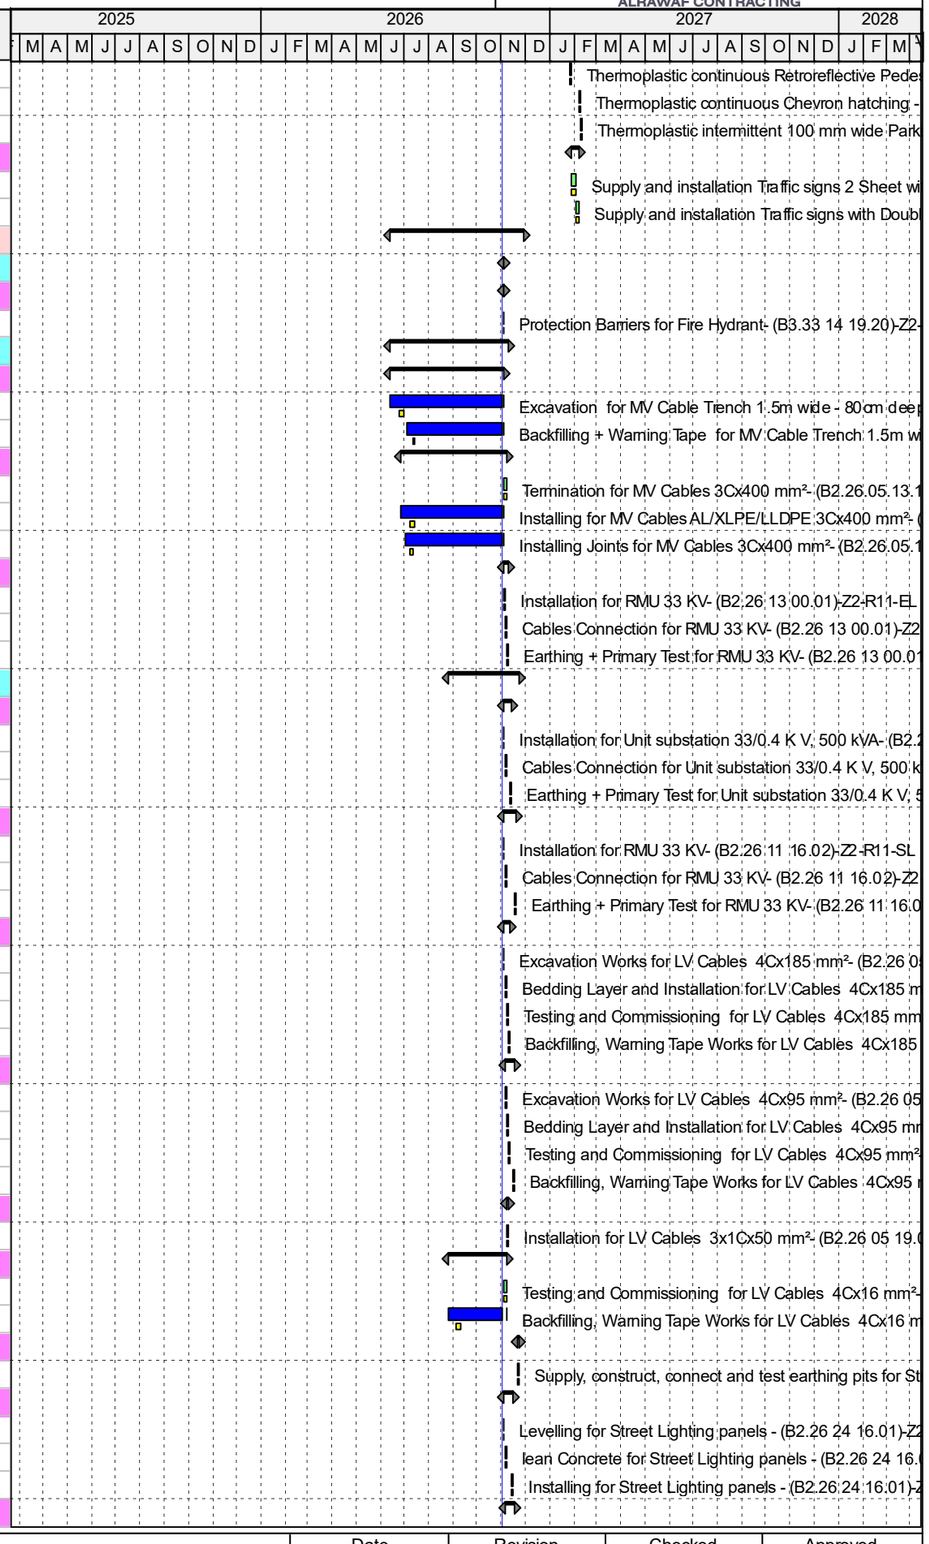

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z2-R11-S	2	05-Nov-26	07-Nov-26	383	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z2-F	2	08-Nov-26	09-Nov-26	383	3,674	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z2-R11-S	2	16-Nov-26	17-Nov-26	378	12,858	0	12,858
	JDH3-02-009-R11-(SL)-KWH meter mounting frame	2	18-Nov-26	19-Nov-26	378	2,072	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z2-R11-SL	2	18-Nov-26	19-Nov-26	378	2,072	0	2,072
	JDH3-02-009-R11-Telecommunications Network -TEL	12	12-Nov-26	25-Nov-26	392	1,907	0	20,444
	JDH3-02-009-R11-(TEL)-Reinforced Concrete Duct 6-ways ducts	8	12-Nov-26	21-Nov-26	396	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2	12-Nov-26	14-Nov-26	385	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2	15-Nov-26	16-Nov-26	396	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2	17-Nov-26	18-Nov-26	396	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2	19-Nov-26	21-Nov-26	396	191	0	191
	JDH3-02-009-R11-(TEL)-Unreinforced Concrete Duct 6-ways duc	3	23-Nov-26	25-Nov-26	378	0	0	18,537
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3	23-Nov-26	25-Nov-26	378	0	0	18,537
	JDH3-02-009-R11-Road Works - RD	23	03-Nov-26	29-Nov-26	355	186,337	0	186,337
	JDH3-02-009-R11-(RD)-Precast Concrete Curb	11	03-Nov-26	15-Nov-26	355	63,413	0	63,413
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	355	9,604	0	9,604
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9	05-Nov-26	15-Nov-26	355	53,809	0	53,809
	JDH3-02-009-R11-(RD)-Precast Interlocking Block Pavers	12	16-Nov-26	29-Nov-26	355	122,925	0	122,925
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	12	16-Nov-26	29-Nov-26	355	122,925	0	122,925
R12		19	03-Nov-26	24-Nov-26	396	614,585	0	614,585
	JDH3-02-009-R12-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R12-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R12-W	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R12-Street Lighting Network -SL	5	03-Nov-26	08-Nov-26	410	6,141	0	6,141
	JDH3-02-009-R12-(SL)-Earthing System for Streetlighting feede	3	03-Nov-26	05-Nov-26	412	2,555	0	2,555
	Supply, construct, connect and test earthing pits for Street Light	3	03-Nov-26	05-Nov-26	412	2,555	0	2,555
	JDH3-02-009-R12-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	5	03-Nov-26	08-Nov-26	410	3,586	0	3,586
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	03-Nov-26	08-Nov-26	410	3,586	0	3,586
	JDH3-02-009-R12-Telecommunications Network - TEL	9	15-Nov-26	24-Nov-26	394	113,131	0	113,131
	JDH3-02-009-R12-(TEL)-Reinforced Concrete Duct 6-ways ducts	8	15-Nov-26	23-Nov-26	395	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2	15-Nov-26	16-Nov-26	394	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2	17-Nov-26	18-Nov-26	395	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2	19-Nov-26	21-Nov-26	395	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2	22-Nov-26	23-Nov-26	395	191	0	191
	JDH3-02-009-R12-(TEL)-Unreinforced Concrete Duct 6-ways duc	7	17-Nov-26	24-Nov-26	394	111,224	0	111,224
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	3	17-Nov-26	19-Nov-26	394	18,537	0	18,537
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	2	21-Nov-26	22-Nov-26	394	67,970	0	67,970
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	2	23-Nov-26	24-Nov-26	394	24,716	0	24,716
	JDH3-02-009-R12-Road Works - RD	19	03-Nov-26	24-Nov-26	375	490,916	0	490,916
	JDH3-02-009-R12-(RD)-Bituminous concrete wearing course 50	5	12-Nov-26	17-Nov-26	375	285,326	0	285,326
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	12-Nov-26	17-Nov-26	375	285,326	0	285,326
	JDH3-02-009-R12-(RD)-Precast Concrete Curb	5	03-Nov-26	08-Nov-26	375	63,766	0	63,766
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	03-Nov-26	04-Nov-26	375	9,920	0	9,920
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	3	05-Nov-26	08-Nov-26	375	53,846	0	53,846
	JDH3-02-009-R12-(RD)-Precast Interlocking Block Pavers	3	09-Nov-26	11-Nov-26	375	122,836	0	122,836
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	3	09-Nov-26	11-Nov-26	375	122,836	0	122,836
	JDH3-02-009-R12-(RD)-Pavement Marking	6	18-Nov-26	24-Nov-26	375	6,136	0	6,136
	Thermoplastic continuous 120 mm wide centre lane- double lin	2	18-Nov-26	19-Nov-26	375	4,338	0	4,338
	Thermoplastic continuous 120 mm wide centre lane- single line	2	21-Nov-26	22-Nov-26	375	364	0	364
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	23-Nov-26	24-Nov-26	375	1,435	0	1,435
	JDH3-02-009-R12-(RD)-Traffic Signage	4	18-Nov-26	22-Nov-26	375	12,852	0	12,852
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2	18-Nov-26	19-Nov-26	375	3,270	0	3,270
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2	21-Nov-26	22-Nov-26	375	9,582	0	9,582




Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
R131		131	04-Aug-26 A	06-Jan-27	359	598,107	153,949	601,095
JDH3-02-009-R131-Potable Water Network - WT		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
JDH3-02-009-R131-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R131-V	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
JDH3-02-009-R131-Electrical Network - EL		20	03-Nov-26	25-Nov-26	258	265,111	0	265,111
JDH3-02-009-R131-(EL)-MV cable trench size 1.5m wide and 80		20	03-Nov-26	25-Nov-26	258	11,379	0	11,379
	Excavation for MV Cable Trench 1.5m wide - 80 cm deep- (B2.3	6	03-Nov-26	09-Nov-26	258	6,828	0	6,828
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6	19-Nov-26	25-Nov-26	258	4,552	0	4,552
JDH3-02-009-R131-(EL)-MV cables AL/XLPE/LLDPE Unarmored		8	10-Nov-26	18-Nov-26	258	253,732	0	253,732
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	6	10-Nov-26	16-Nov-26	258	239,230	0	239,230
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	17-Nov-26	18-Nov-26	258	14,502	0	14,502
JDH3-02-009-R131-Street Lighting Network -SL		10	17-Sep-26 A	25-Nov-26	258	65,230	45,661	65,230
JDH3-02-009-R131-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP		10	17-Sep-26 A	25-Nov-26	258	65,230	45,661	65,230
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	5	19-Sep-26 A	25-Nov-26	258	57,555	40,289	57,555
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	17-Sep-26 A	25-Nov-26	258	7,674	5,372	7,674
JDH3-02-009-R131-Telecommunications Network - TEL		83	04-Aug-26 A	11-Nov-26	407	95,189	56,403	95,189
JDH3-02-009-R131-(TEL)-Ducts		8	03-Nov-26	11-Nov-26	407	19,984	0	19,984
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2	03-Nov-26	04-Nov-26	407	2,998	0	2,998
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	4	05-Nov-26	09-Nov-26	407	14,988	0	14,988
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2	10-Nov-26	11-Nov-26	407	1,998	0	1,998
JDH3-02-009-R131-(TEL)-Manhole Type 1		8	04-Aug-26 A	11-Nov-26	407	41,021	30,765	41,021
	Backfilling Works for MH Type 1 Dim 2000*1000*1000 mm- (B2.	2	06-Aug-26 A	11-Nov-26	407	4,102	3,077	4,102
	Excavation and Bedding Works for MH Type 1 Dim 2000*1000*	2	04-Aug-26 A	04-Nov-26	413	6,153	4,615	6,153
	Installation for MH Type 1 Dim 2000*1000*1000 mm- (B2.33.71	2	05-Aug-26 A	04-Nov-26	413	30,765	23,074	30,765
JDH3-02-009-R131-(TEL)-Manhole Type 2		8	04-Aug-26 A	11-Nov-26	407	34,184	25,638	34,184
	Installation for MH Type 2 Dim 2000*1000*1000 mm- (B2.33.71	2	05-Aug-26 A	04-Nov-26	413	25,638	19,228	25,638
	Backfilling Works for MH Type 2 Dim 2000*1000*1000 mm- (B2.	2	06-Aug-26 A	11-Nov-26	407	3,418	2,564	3,418
	Excavation and Bedding Works for MH Type 2 Dim 2000*1000*	2	04-Aug-26 A	04-Nov-26	413	5,128	3,846	5,128
JDH3-02-009-R131-Road Works - RD		109	01-Sep-26 A	06-Jan-27	345	167,693	51,885	170,681
JDH3-02-009-R131-(RD)-Precast Concrete Curb		74	01-Sep-26 A	26-Nov-26	302	167,693	51,885	167,693
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5	03-Nov-26	09-Nov-26	302	37,285	0	37,285
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	11	14-Nov-26	26-Nov-26	302	69,521	0	69,521
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	09-Nov-26	14-Nov-26	302	3,238	0	3,238
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8	01-Sep-26 A	03-Nov-26	302	57,650	51,885	57,650
JDH3-02-009-R131-(RD)-Pavement Marking		6	30-Dec-26	06-Jan-27	345	0	0	2,988
	Thermoplastic continuous 100 mm wide (parking separator line)	2	30-Dec-26	02-Jan-27	345	0	0	681
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	02-Jan-27	04-Jan-27	345	0	0	1,782
	Thermoplastic continuous Chevron hatching - white (round abou	2	04-Jan-27	06-Jan-27	345	0	0	525
R132		211	02-Jun-26 A	07-Mar-27	309	328,379	178,126	352,274
JDH3-02-009-R132-Potable Water Network - WT		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
JDH3-02-009-R132-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R132-V	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
JDH3-02-009-R132-Electrical Network - EL		71	02-Jun-26 A	01-Dec-26	309	184,680	58,894	190,191
JDH3-02-009-R132-(EL)-MV cable trench size 1.5m wide and 80		71	02-Jun-26 A	01-Dec-26	309	3,674	4,593	9,185
	Excavation for MV Cable Trench 1.5m wide - 80 cm deep- (B2.3	6	02-Jun-26 A	01-Dec-26	309	0	2,756	5,511
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3	18-Aug-26 A	01-Dec-26	309	3,674	1,837	3,674
JDH3-02-009-R132-(EL)-MV cables AL/XLPE/LLDPE Unarmored		7	13-Aug-26 A	01-Dec-26	309	181,006	54,302	181,006
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	13-Aug-26 A	01-Dec-26	309	172,305	51,691	172,305
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	15-Aug-26 A	01-Dec-26	309	8,701	2,610	8,701
JDH3-02-009-R132-Street Lighting Network -SL		46	16-Sep-26 A	15-Dec-26	376	75,616	59,194	75,616
JDH3-02-009-R132-(SL)- LV Cables - Copper, 4 Cx 16 mm², Cu/XLP		19	16-Sep-26 A	15-Dec-26	374	59,656	53,848	59,656
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4	23-Sep-26 A	15-Dec-26	374	6,280	3,140	6,280
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	4	17-Sep-26 A	05-Dec-26	379	47,097	44,742	47,097

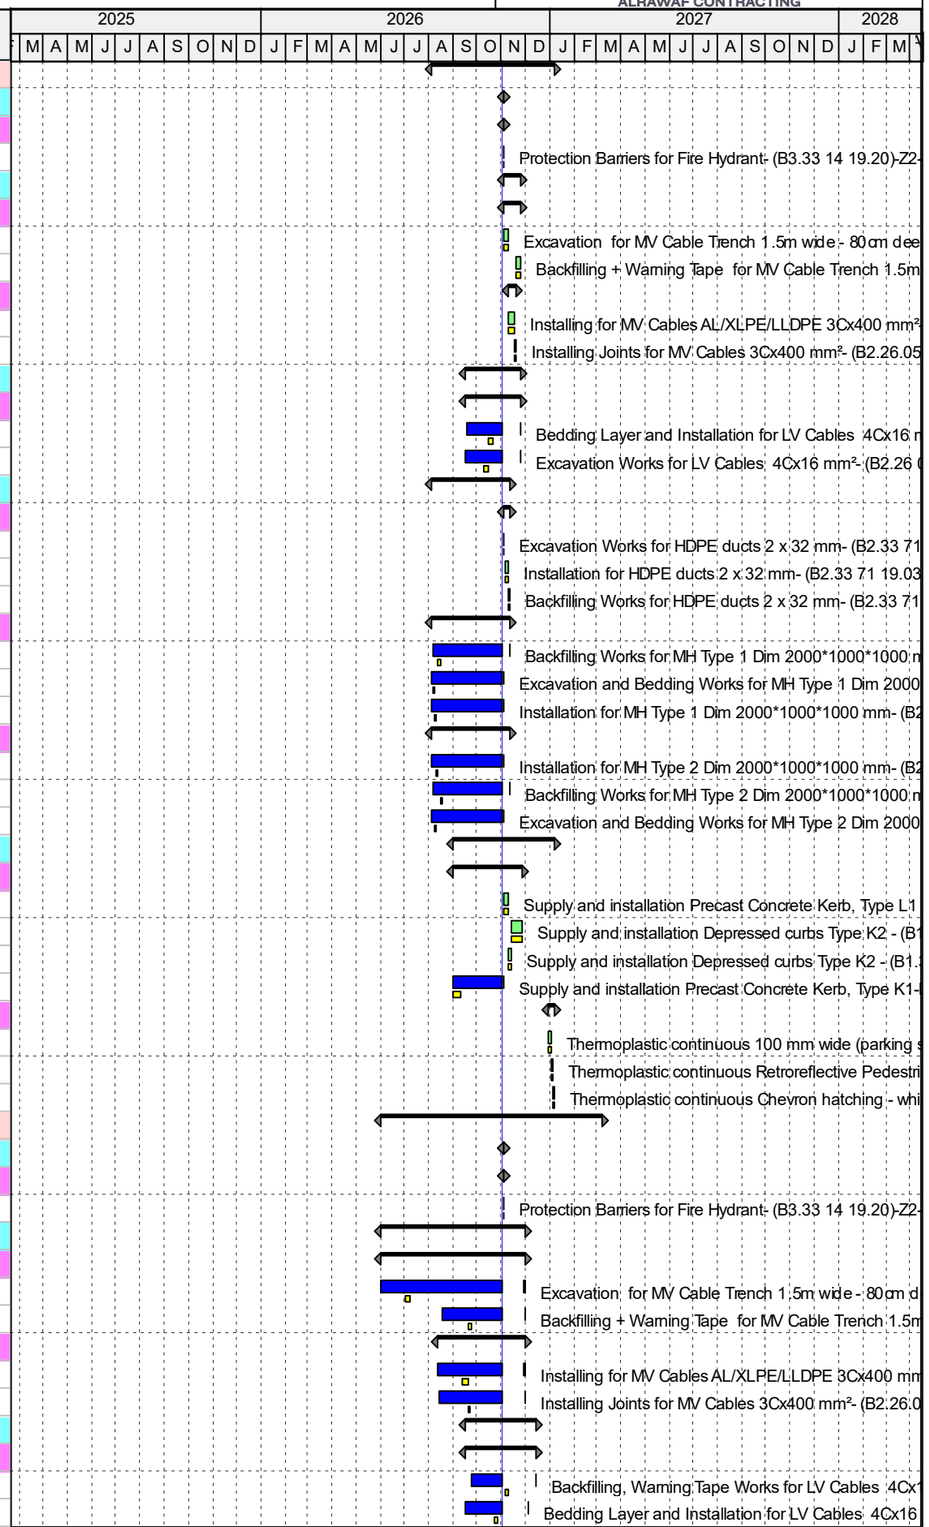


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	16-Sep-26 A	05-Dec-26	379	6,280	5,966	6,280
	JDH3-02-009-R132-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	402	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z2-R132-	2	03-Nov-26	04-Nov-26	407	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z2-F	2	05-Nov-26	07-Nov-26	407	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z2-R132-	2	14-Nov-26	15-Nov-26	402	7,232	0	7,232
	JDH3-02-009-R132-(SL)-Lighting Pole with single arm 12 m heig	6	22-Sep-26 A	03-Nov-26	413	5,628	5,347	5,628
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6	22-Sep-26 A	03-Nov-26	413	5,628	5,347	5,628
	JDH3-02-009-R132-Road Works - RD	9	25-Aug-26 A	30-Nov-26	309	63,197	60,038	63,197
	JDH3-02-009-R132-(RD)-Precast Concrete Curb	9	25-Aug-26 A	30-Nov-26	309	63,197	60,038	63,197
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9	25-Aug-26 A	30-Nov-26	309	63,197	60,038	63,197
	JDH3-02-009-R132-Landscape Works - LS	2	04-Mar-27	07-Mar-27	309	0	0	18,385
	JDH3-02-009-R132-(LS)-HDPE for Secondary Network	2	04-Mar-27	07-Mar-27	309	0	0	18,385
	Pipe line with Diam 110 mm PN16 - depth from 0 to 1.5 m- (B7.	2	04-Mar-27	07-Mar-27	309	0	0	18,385
R14		187	25-Aug-26 A	05-Apr-27	287	4,466,642	1,038,156	4,508,245
	JDH3-02-009-R14-Catch Basins (Storm Network) - ST	10	03-Nov-26	14-Nov-26	405	39,262	0	39,262
	JDH3-02-009-R14-(ST)-Single Catch Basin Works	10	03-Nov-26	14-Nov-26	405	16,848	0	16,848
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5	03-Nov-26	08-Nov-26	405	11,232	0	11,232
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z2-R14-ST	5	09-Nov-26	14-Nov-26	405	5,616	0	5,616
	JDH3-02-009-R14-(ST)-Double Catch Basin Works	4	03-Nov-26	07-Nov-26	406	22,414	0	22,414
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	406	14,942	0	14,942
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z2-R14-ST	2	05-Nov-26	07-Nov-26	406	7,471	0	7,471
	JDH3-02-009-R14-TSE Network - TSE	8	03-Nov-26	11-Nov-26	292	91,453	0	91,453
	JDH3-02-009-R14-(TSE)-Butterfly Valve-300 mm on pipe dia (315	4	05-Nov-26	09-Nov-26	292	48,390	0	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2	05-Nov-26	07-Nov-26	292	43,551	0	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	08-Nov-26	09-Nov-26	292	4,839	0	4,839
	JDH3-02-009-R14-(TSE)-Valve Chamber on 315 mm dia pipeline	8	03-Nov-26	11-Nov-26	292	43,064	0	43,064
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2	03-Nov-26	04-Nov-26	292	6,460	0	6,460
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	05-Nov-26	07-Nov-26	292	4,306	0	4,306
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	08-Nov-26	09-Nov-26	292	23,685	0	23,685
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	10-Nov-26	11-Nov-26	292	8,613	0	8,613
	JDH3-02-009-R14-Potable Water Network - WT	63	01-Sep-26 A	14-Nov-26	405	228,708	32,436	228,708
	JDH3-02-009-R14-(WT)-Butterfly Valve-400 mm on pipe dia (400)	8	16-Sep-26 A	04-Nov-26	391	78,222	25,813	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2	16-Sep-26 A	04-Nov-26	391	70,400	23,232	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2	24-Sep-26 A	04-Nov-26	391	7,822	2,581	7,822
	JDH3-02-009-R14-(WT)-Valve Chamber on 400 mm dia pipeline	57	01-Sep-26 A	07-Nov-26	391	43,007	6,623	43,007
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	05-Nov-26	07-Nov-26	391	8,601	0	8,601
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	16-Sep-26 A	04-Nov-26	391	23,654	3,075	23,654
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	03-Sep-26 A	04-Nov-26	391	4,301	1,419	4,301
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	01-Sep-26 A	04-Nov-26	391	6,451	2,129	6,451
	JDH3-02-009-R14-(WT)-Fire Hydrant	10	03-Nov-26	14-Nov-26	405	107,479	0	107,479
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	03-Nov-26	04-Nov-26	405	10,748	0	10,748
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2	05-Nov-26	07-Nov-26	405	21,496	0	21,496
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2	08-Nov-26	09-Nov-26	405	32,244	0	32,244
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-WT	2	10-Nov-26	11-Nov-26	405	37,618	0	37,618
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R14-W	2	12-Nov-26	14-Nov-26	405	5,374	0	5,374
	JDH3-02-009-R14-Street Lighting Network -SL	8	03-Nov-26	11-Nov-26	407	2,161	0	2,161
	JDH3-02-009-R14-(SL)-Road Crossing Ducts 2 way PVC 2 × 100	8	03-Nov-26	11-Nov-26	407	2,161	0	2,161
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	2	03-Nov-26	04-Nov-26	310	432	0	432
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z2-R	2	05-Nov-26	07-Nov-26	318	1,297	0	1,297
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	2	08-Nov-26	09-Nov-26	318	324	0	324
	Testing and Backfilling Works for PVC Pipes 2×100mm- (B2.33	2	10-Nov-26	11-Nov-26	407	108	0	108
	JDH3-02-009-R14-Road Works - RD	181	25-Aug-26 A	29-Mar-27	293	4,105,058	1,005,720	4,139,078
	JDH3-02-009-R14-(RD)-Aggregate Base Course	2	25-Aug-26 A	03-Nov-26	281	307,847	246,278	307,847

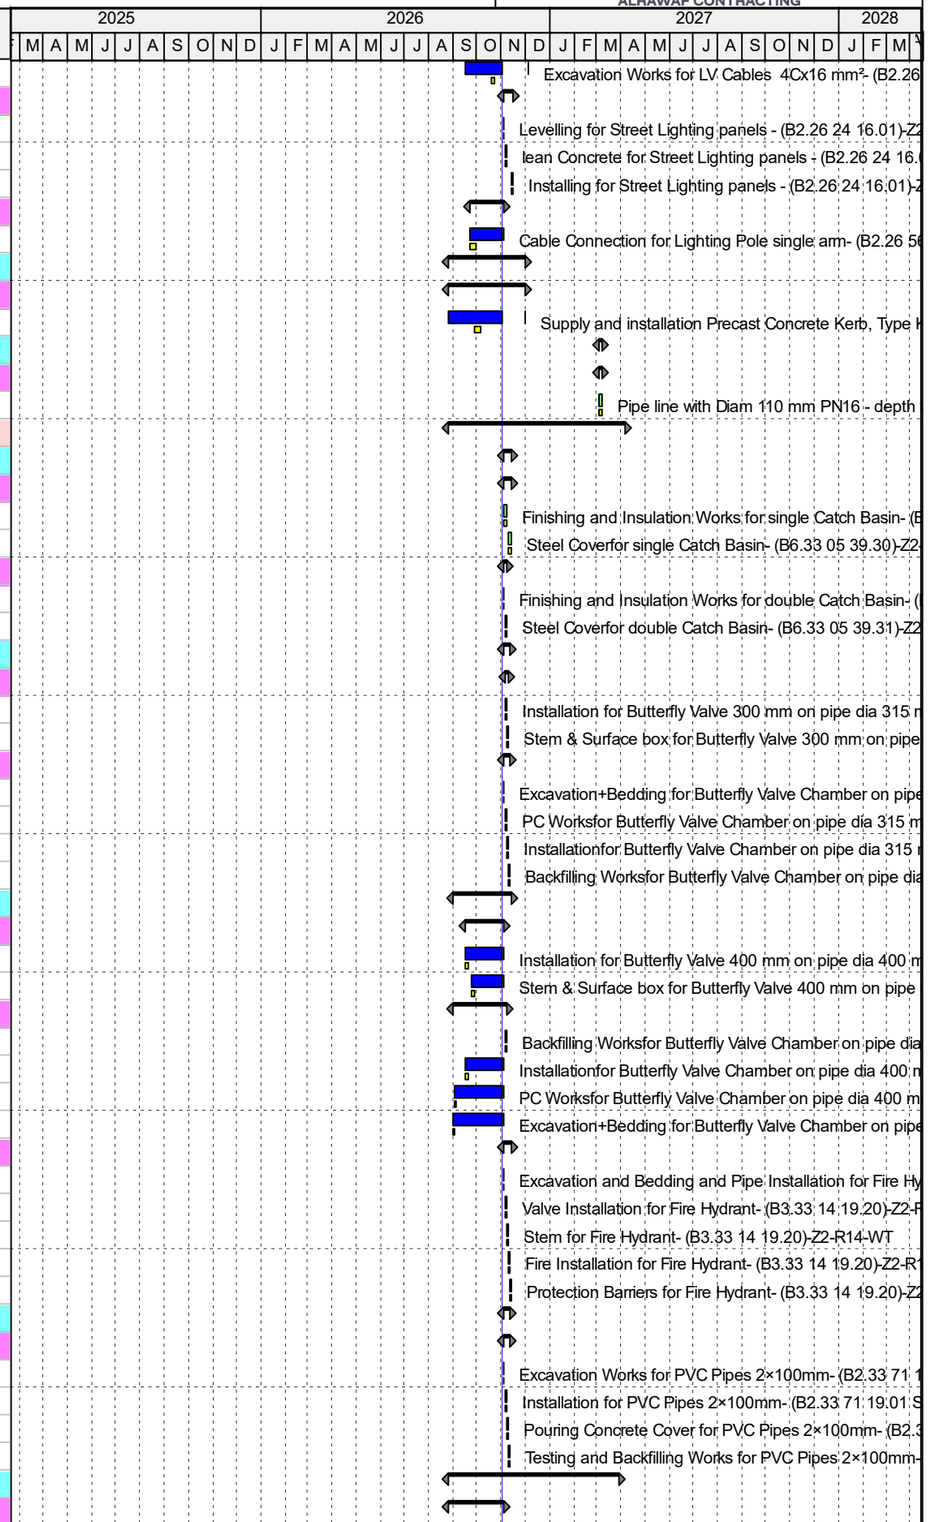


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply, lay and compaction Aggregate base course compacted	2	25-Aug-26 A	03-Nov-26	281	307,847	246,278	307,847
	JDH3-02-009-R14-(RD)-Bituminous base course 200 mm Two La	51	09-Sep-26 A	10-Nov-26	344	3,797,211	759,442	3,797,211
	Supply, lay and Asphaltic base course including tack Coat (RC2)	5	04-Nov-26	10-Nov-26	344	1,898,605	0	1,898,605
	Supply, lay and Asphaltic base course including Prime Coat (MC	2	09-Sep-26 A	04-Nov-26	281	1,898,605	759,442	1,898,605
	JDH3-02-009-R14-(RD)-Pavement Marking	8	16-Mar-27	24-Mar-27	293	0	0	28,355
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	4	16-Mar-27	20-Mar-27	293	0	0	21,403
	Thermoplastic continuous Painted rumble strips marking (300m	2	21-Mar-27	22-Mar-27	293	0	0	3,158
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2	23-Mar-27	24-Mar-27	293	0	0	3,794
	JDH3-02-009-R14-(RD)-Traffic Signage	4	25-Mar-27	29-Mar-27	293	0	0	5,666
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2	25-Mar-27	27-Mar-27	293	0	0	3,270
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2	28-Mar-27	29-Mar-27	293	0	0	2,396
	JDH3-02-009-R14-Landscape Works - LS	14	21-Mar-27	05-Apr-27	281	0	0	7,583
	JDH3-02-009-R14-(LS)-Design, Delive, install, wiring, control, pr	14	21-Mar-27	05-Apr-27	281	0	0	7,583
	Installation of 1" quick coupler valve - (B7.33.14.19.03)-Z2-R14	3	21-Mar-27	23-Mar-27	281	0	0	3,152
	Online pressure compensating emitters - (B7.32.80.00.02)-Z2-R	8	28-Mar-27	05-Apr-27	281	0	0	2,628
	Decoder cables 12 AWG between valves and controllers - (B7.3	6	21-Mar-27	27-Mar-27	281	0	0	1,803
Z1		178	14-Jul-26 A	04-Mar-27	312	2,135,462	1,207,449	4,988,879
R01		77	25-Aug-26 A	23-Nov-26	397	258,389	91,978	517,452
JDH3-02-009-R01-Storm Network - ST		8	03-Nov-26	11-Nov-26	401	3,913	0	3,913
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2	03-Nov-26	04-Nov-26	401	1,402	0	1,402
Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3		2	03-Nov-26	04-Nov-26	401	1,402	0	1,402
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2	05-Nov-26	07-Nov-26	401	485	0	485
Steel Coverfor MH 1200 mm - depth from 3.01 to 3.50 m- (B6.3		2	05-Nov-26	07-Nov-26	401	485	0	485
JDH3-02-009-R01-(ST)-MH Works (1500) mm diameter depth fro		2	08-Nov-26	09-Nov-26	401	1,003	0	1,003
Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3		2	08-Nov-26	09-Nov-26	401	1,003	0	1,003
JDH3-02-009-R01-(ST)-MH Works (1500) mm diameter depth fro		2	03-Nov-26	04-Nov-26	405	625	0	625
Steel Coverfor MH 1500 mm - depth from 2.51 to 3.00 m- (B6.3		2	03-Nov-26	04-Nov-26	405	625	0	625
JDH3-02-009-R01-(ST)-MH Works (1200) mm diameter depth fro		2	10-Nov-26	11-Nov-26	401	397	0	397
Steel Coverfor MH 1200 mm - depth from 2.01 to 2.50 m- (B6.3		2	10-Nov-26	11-Nov-26	401	397	0	397
JDH3-02-009-R01-TSE Network - TSE		56	01-Sep-26 A	07-Nov-26	410	21,532	6,316	21,532
JDH3-02-009-R01-(TSE)-Valve Chamber on 315 mm dia pipeline		56	01-Sep-26 A	07-Nov-26	410	21,532	6,316	21,532
Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m		2	04-Nov-26	07-Nov-26	410	5,742	0	5,742
Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de		2	01-Sep-26 A	04-Nov-26	410	15,790	6,316	15,790
JDH3-02-009-R01-Potable Water Network - WT		63	01-Sep-26 A	14-Nov-26	405	215,011	26,493	215,011
JDH3-02-009-R01-(WT)-Wash-Out Valve-150 mm on pipe dia (63		4	03-Nov-26	07-Nov-26	335	39,083	0	39,083
Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E		2	03-Nov-26	04-Nov-26	335	35,175	0	35,175
Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6		2	05-Nov-26	07-Nov-26	335	3,908	0	3,908
JDH3-02-009-R01-(WT)-Valve Chamber on 630 mm dia pipeline		54	03-Sep-26 A	07-Nov-26	408	27,539	8,078	27,539
Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m		2	04-Nov-26	07-Nov-26	408	7,344	0	7,344
Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de		2	03-Sep-26 A	04-Nov-26	335	20,195	8,078	20,195
JDH3-02-009-R01-(WT)-Wash-Out Chamber on 630 mm dia pipe		8	03-Nov-26	11-Nov-26	405	54,422	0	54,422
Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m		2	03-Nov-26	04-Nov-26	405	8,163	0	8,163
PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fr		2	05-Nov-26	07-Nov-26	405	5,442	0	5,442
Installationfor Wash-Out Chamber on pipe dia 630 mm - depth		2	08-Nov-26	09-Nov-26	405	29,932	0	29,932
Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm - c		2	10-Nov-26	11-Nov-26	405	10,884	0	10,884
JDH3-02-009-R01-(WT)-Air Valve Chamber on 630 mm dia pipeli		2	12-Nov-26	14-Nov-26	405	1,428	0	1,428
Backfilling Worksfor Air Valve Chamber on pipe dia 630 mm - de		2	12-Nov-26	14-Nov-26	405	1,428	0	1,428
JDH3-02-009-R01-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	411	2,443	0	2,443
Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R01-W		2	03-Nov-26	04-Nov-26	411	2,443	0	2,443
JDH3-02-009-R01-(WT)-Valve Chamber on 315 mm dia pipeline		56	01-Sep-26 A	07-Nov-26	410	10,752	3,154	10,752
Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m		2	04-Nov-26	07-Nov-26	410	2,867	0	2,867
Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de		2	01-Sep-26 A	04-Nov-26	410	7,885	3,154	7,885
JDH3-02-009-R01-(WT)-Valve Chamber on 800 mm dia pipeline		58	01-Sep-26 A	09-Nov-26	410	47,994	14,078	47,994

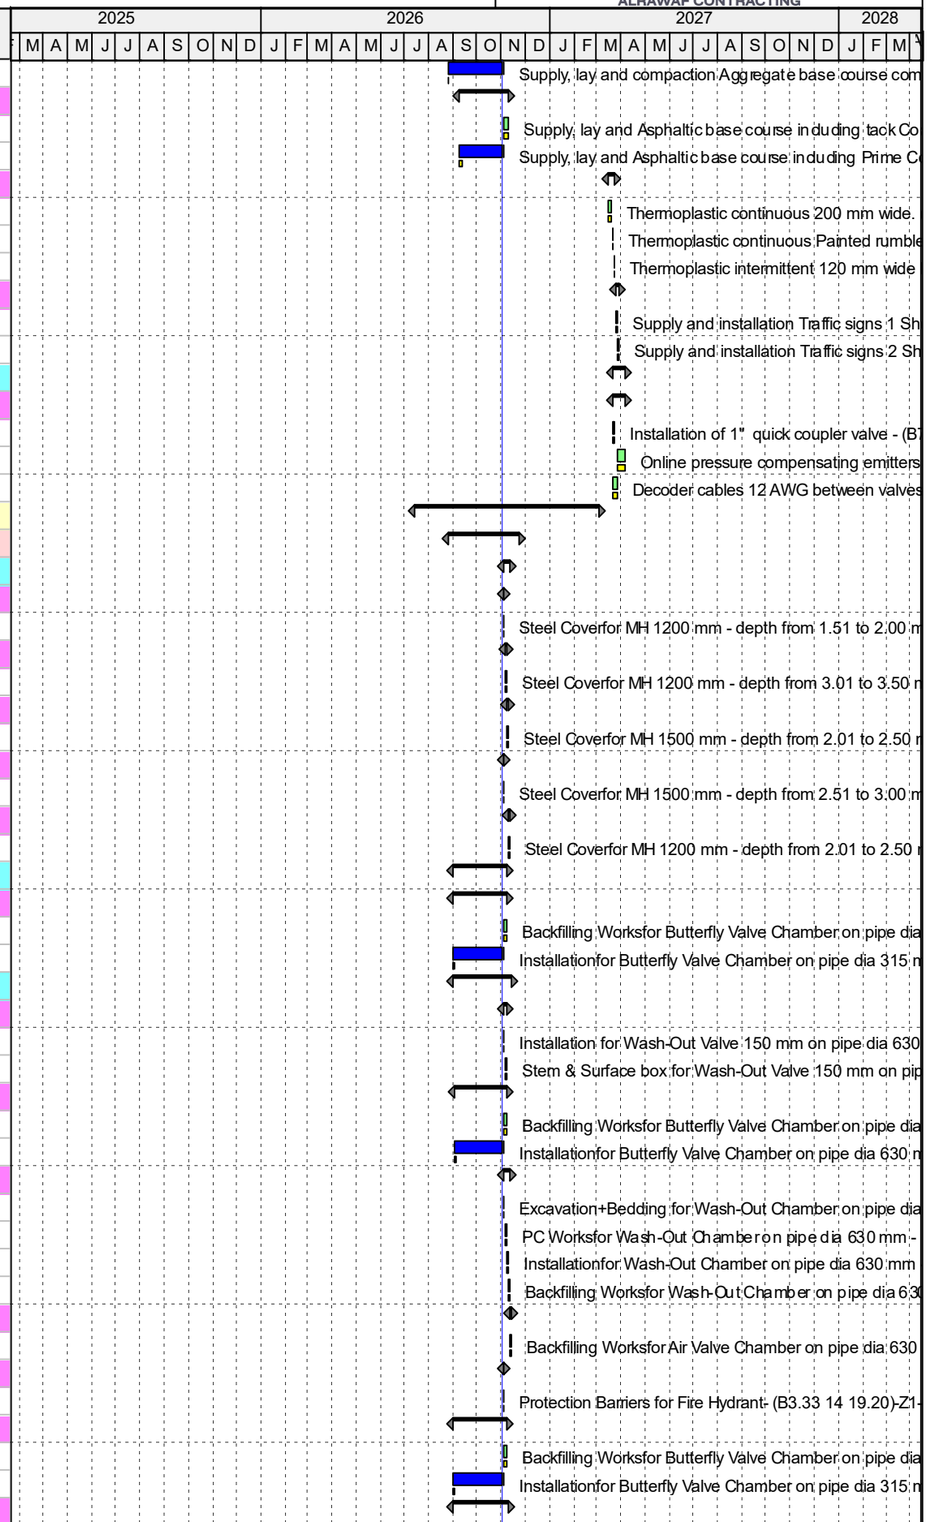


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	07-Nov-26	09-Nov-26	410	12,798	0	12,798
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	01-Sep-26 A	04-Nov-26	412	35,195	14,078	35,195
	JDH3-02-009-R01-(WT)-Butterfly Valve-400 mm on pipe dia (400)	2	04-Nov-26	07-Nov-26	404	23,467	0	23,467
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2	04-Nov-26	07-Nov-26	404	23,467	0	23,467
	JDH3-02-009-R01-(WT)-Valve Chamber on 400 mm dia pipeline	2	01-Sep-26 A	04-Nov-26	404	7,885	1,183	7,885
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	01-Sep-26 A	04-Nov-26	404	7,885	1,183	7,885
	JDH3-02-009-R01-Street Lighting Network -SL	71	25-Aug-26 A	17-Nov-26	403	17,934	59,169	88,943
	JDH3-02-009-R01-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8	03-Nov-26	12-Nov-26	403	0	0	4,702
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	03-Nov-26	05-Nov-26	403	0	0	470
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	05-Nov-26	08-Nov-26	403	0	0	3,526
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	08-Nov-26	10-Nov-26	403	0	0	235
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	10-Nov-26	12-Nov-26	403	0	0	470
	JDH3-02-009-R01-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	71	25-Aug-26 A	17-Nov-26	403	0	51,947	64,330
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	03-Nov-26	08-Nov-26	407	0	0	3,217
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4	12-Nov-26	17-Nov-26	403	0	0	6,433
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4	29-Aug-26 A	03-Nov-26	407	0	45,835	48,248
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	25-Aug-26 A	03-Nov-26	403	0	6,111	6,433
	JDH3-02-009-R01-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2	15-Sep-26 A	03-Nov-26	415	7,603	7,222	7,603
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z1-R	2	15-Sep-26 A	03-Nov-26	415	7,603	7,222	7,603
	JDH3-02-009-R01-(SL)-Earthing System for Distribution panels,	2	03-Nov-26	04-Nov-26	411	0	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	03-Nov-26	04-Nov-26	411	0	0	1,126
	JDH3-02-009-R01-(SL)-Earthing System for Streetlighting feede	2	05-Nov-26	07-Nov-26	411	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2	05-Nov-26	07-Nov-26	411	0	0	852
	JDH3-02-009-R01-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	404	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R01-S	2	03-Nov-26	04-Nov-26	409	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2	05-Nov-26	07-Nov-26	409	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R01-S	2	14-Nov-26	15-Nov-26	404	7,232	0	7,232
	JDH3-02-009-R01-Road Works - RD	18	03-Nov-26	23-Nov-26	351	0	0	188,054
	JDH3-02-009-R01-(RD)-Precast Concrete Curb	18	03-Nov-26	23-Nov-26	351	0	0	188,054
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	12	03-Nov-26	16-Nov-26	351	0	0	174,752
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	17-Nov-26	18-Nov-26	351	0	0	9,457
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	19-Nov-26	23-Nov-26	351	0	0	3,845
	R02	98	22-Aug-26 A	20-Dec-26	375	545,603	69,583	972,326
	JDH3-02-009-R02-Potable Water Network - WT	12	03-Nov-26	16-Nov-26	403	116,265	0	116,265
	JDH3-02-009-R02-(WT)-Air Valve-50 mm on pipe dia (225) mm	4	10-Nov-26	14-Nov-26	403	6,490	0	6,490
	Installation for Air Valve 50 mm on pipe dia 225 mm- (B3.33 14	2	10-Nov-26	11-Nov-26	403	5,841	0	5,841
	Stem & Surface box for Air Valve 50 mm on pipe dia 225 mm- (B	2	12-Nov-26	14-Nov-26	403	649	0	649
	JDH3-02-009-R02-(WT)-Air Valve Chamber on 225 mm dia pipeli	8	03-Nov-26	11-Nov-26	407	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 225 mm	2	03-Nov-26	04-Nov-26	403	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 225 mm - depth fro	2	05-Nov-26	07-Nov-26	403	714	0	714
	Installationfor Air Valve Chamber on pipe dia 225 mm - depth fr	2	08-Nov-26	09-Nov-26	403	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 225 mm - de	2	10-Nov-26	11-Nov-26	407	1,428	0	1,428
	JDH3-02-009-R02-(WT)-Fire Hydrant	2	15-Nov-26	16-Nov-26	403	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R02-W	2	15-Nov-26	16-Nov-26	403	4,885	0	4,885
	JDH3-02-009-R02-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4	03-Nov-26	07-Nov-26	409	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	03-Nov-26	04-Nov-26	409	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 800	2	05-Nov-26	07-Nov-26	409	6,575	0	6,575
	JDH3-02-009-R02-(WT)-Valve Chamber on 800 mm dia pipeline	8	03-Nov-26	11-Nov-26	407	31,996	0	31,996
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2	03-Nov-26	04-Nov-26	407	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	05-Nov-26	07-Nov-26	407	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	08-Nov-26	09-Nov-26	407	17,598	0	17,598
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	10-Nov-26	11-Nov-26	407	6,399	0	6,399
	JDH3-02-009-R02-Electrical Network - EL	64	22-Aug-26 A	09-Nov-26	359	80,227	9,766	80,227

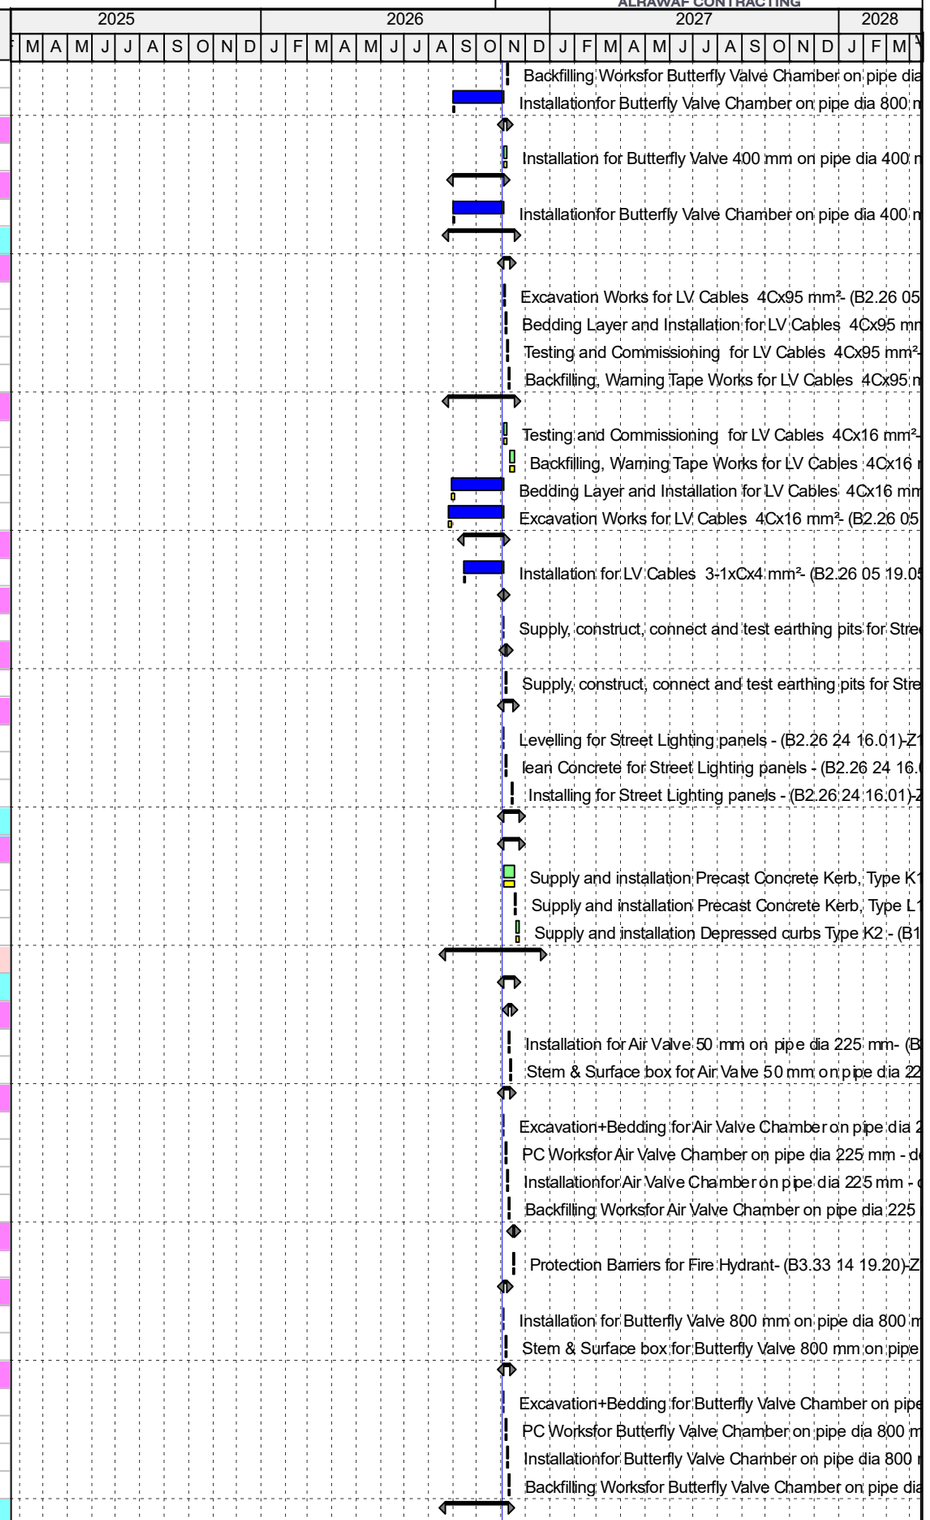

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R02-(EL)-RMU 33 KV	6	03-Nov-26	09-Nov-26	359	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R02-EL	2	03-Nov-26	04-Nov-26	359	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R02-El	2	05-Nov-26	07-Nov-26	359	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2	08-Nov-26	09-Nov-26	359	4,925	0	4,925
	JDH3-02-009-R02-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	4	22-Aug-26 A	03-Nov-26	363	11,281	9,766	11,281
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	23-Aug-26 A	03-Nov-26	363	2,580	1,935	2,580
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	22-Aug-26 A	03-Nov-26	363	8,701	7,831	8,701
	JDH3-02-009-R02-Street Lighting Network -SL	20	03-Nov-26	25-Nov-26	373	126,007	0	126,007
	JDH3-02-009-R02-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8	03-Nov-26	11-Nov-26	377	37,974	0	37,974
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	10-Nov-26	11-Nov-26	359	3,797	0	3,797
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	03-Nov-26	04-Nov-26	379	28,480	0	28,480
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	05-Nov-26	07-Nov-26	379	1,899	0	1,899
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	08-Nov-26	09-Nov-26	379	3,797	0	3,797
	JDH3-02-009-R02-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	12	12-Nov-26	25-Nov-26	359	72,262	0	72,262
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6	12-Nov-26	18-Nov-26	359	8,501	0	8,501
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	6	19-Nov-26	25-Nov-26	359	63,761	0	63,761
	JDH3-02-009-R02-(SL)-Lighting Pole with single arm 12 m heigh	6	03-Nov-26	09-Nov-26	385	5,440	0	5,440
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6	03-Nov-26	09-Nov-26	385	5,440	0	5,440
	JDH3-02-009-R02-(SL)- Street Lighting Panels	11	03-Nov-26	15-Nov-26	382	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R02-S	2	03-Nov-26	04-Nov-26	387	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2	05-Nov-26	07-Nov-26	387	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R02-S	2	14-Nov-26	15-Nov-26	382	7,232	0	7,232
	JDH3-02-009-R02-Road Works - RD	94	01-Sep-26 A	20-Dec-26	373	223,103	59,817	649,827
	JDH3-02-009-R02-(RD)-Bituminous concrete wearing course 50	5	05-Dec-26	10-Dec-26	361	0	0	345,894
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	05-Dec-26	10-Dec-26	361	0	0	345,894
	JDH3-02-009-R02-(RD)-Precast Concrete Curb	67	01-Sep-26 A	18-Nov-26	361	142,002	59,817	142,002
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	04-Nov-26	07-Nov-26	361	6,679	0	6,679
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10	07-Nov-26	18-Nov-26	361	64,950	0	64,950
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10	01-Sep-26 A	04-Nov-26	361	70,373	59,817	70,373
	JDH3-02-009-R02-(RD)-Precast Interlocking Block Pavers	14	18-Nov-26	05-Dec-26	361	81,101	0	141,927
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	14	18-Nov-26	05-Dec-26	361	81,101	0	141,927
	JDH3-02-009-R02-(RD)-Pavement Marking	8	10-Dec-26	20-Dec-26	361	0	0	7,151
	Thermoplastic continuous 120 mm wide centre lane- double lin	2	10-Dec-26	13-Dec-26	361	0	0	5,264
	Thermoplastic continuous 120 mm wide centre lane- single line	2	13-Dec-26	15-Dec-26	361	0	0	332
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	15-Dec-26	17-Dec-26	361	0	0	1,463
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2	17-Dec-26	20-Dec-26	361	0	0	92
	JDH3-02-009-R02-(RD)-Traffic Signage	4	10-Dec-26	15-Dec-26	377	0	0	12,852
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2	10-Dec-26	13-Dec-26	377	0	0	3,270
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2	13-Dec-26	15-Dec-26	377	0	0	9,582
R03		144	02-Sep-26 A	04-Mar-27	312	498,898	232,021	986,154
	JDH3-02-009-R03-Potable Water Network - WT	14	03-Nov-26	18-Nov-26	401	131,172	0	131,172
	JDH3-02-009-R03-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R03-W	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	JDH3-02-009-R03-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4	10-Nov-26	14-Nov-26	401	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	10-Nov-26	11-Nov-26	401	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2	12-Nov-26	14-Nov-26	401	6,575	0	6,575
	JDH3-02-009-R03-(WT)-Wash-Out Valve-100 mm on pipe dia (22	6	12-Nov-26	18-Nov-26	401	7,673	0	7,673
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2	12-Nov-26	14-Nov-26	403	6,906	0	6,906
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2	17-Nov-26	18-Nov-26	401	767	0	767
	JDH3-02-009-R03-(WT)-Valve Chamber on 800 mm dia pipeline	8	03-Nov-26	11-Nov-26	403	31,996	0	31,996
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2	03-Nov-26	04-Nov-26	401	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	05-Nov-26	07-Nov-26	401	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	08-Nov-26	09-Nov-26	401	17,598	0	17,598

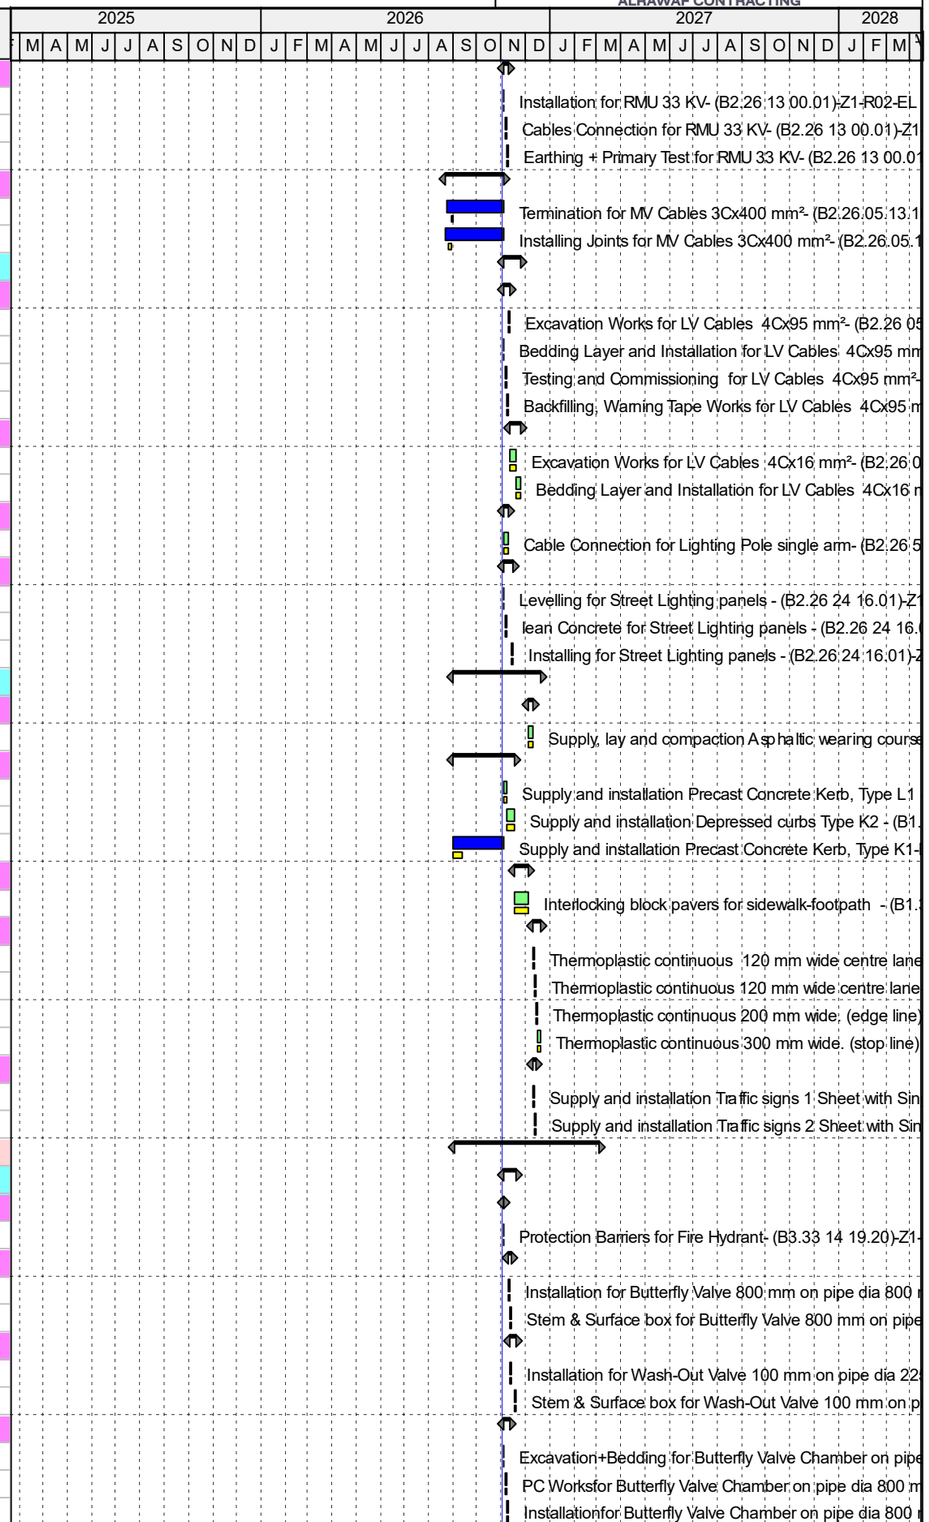


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	10-Nov-26	11-Nov-26	403	6,399	0	6,399
	JDH3-02-009-R03-(WT)-Wash-Out Chamber on 225 mm dia pipe	10	05-Nov-26	16-Nov-26	401	20,864	0	20,864
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2	05-Nov-26	07-Nov-26	403	3,130	0	3,130
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2	08-Nov-26	09-Nov-26	403	2,086	0	2,086
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2	10-Nov-26	11-Nov-26	403	11,475	0	11,475
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - c	2	15-Nov-26	16-Nov-26	401	4,173	0	4,173
	JDH3-02-009-R03-Electrical Network - EL	53	15-Sep-26 A	17-Nov-26	290	275,701	173,789	275,701
	JDH3-02-009-R03-(EL)-MV cable trench size 1.5m wide and 80c	6	05-Nov-26	12-Nov-26	290	3,992	0	3,992
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6	05-Nov-26	12-Nov-26	290	3,992	0	3,992
	JDH3-02-009-R03-(EL)-RMU 33 KV	12	03-Nov-26	17-Nov-26	290	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R03-EL	2	03-Nov-26	04-Nov-26	296	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R03-El	2	05-Nov-26	07-Nov-26	296	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2	15-Nov-26	17-Nov-26	290	4,925	0	4,925
	JDH3-02-009-R03-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	51	15-Sep-26 A	15-Nov-26	290	202,763	173,789	202,763
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	03-Nov-26	05-Nov-26	290	8,701	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	12-Nov-26	15-Nov-26	290	5,160	0	5,160
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	15-Sep-26 A	03-Nov-26	290	188,901	173,789	188,901
	JDH3-02-009-R03-Street Lighting Network -SL	19	03-Nov-26	25-Nov-26	316	23,518	0	23,518
	JDH3-02-009-R03-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	2	03-Nov-26	04-Nov-26	325	3,401	0	3,401
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2	03-Nov-26	04-Nov-26	325	3,401	0	3,401
	JDH3-02-009-R03-(SL)-RMU 33 KV	2	03-Nov-26	04-Nov-26	329	4,202	0	4,202
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z1-R03-SL	2	03-Nov-26	04-Nov-26	329	4,202	0	4,202
	JDH3-02-009-R03-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL/	2	17-Nov-26	19-Nov-26	290	121	0	121
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2	17-Nov-26	19-Nov-26	290	121	0	121
	JDH3-02-009-R03-(SL)- LV Cables - Copper, 3x1Cx50mm²,Cu/XL	2	05-Nov-26	07-Nov-26	327	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z1-F	2	05-Nov-26	07-Nov-26	327	1,520	0	1,520
	JDH3-02-009-R03-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	5	19-Nov-26	25-Nov-26	290	7,730	0	7,730
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	19-Nov-26	25-Nov-26	290	7,730	0	7,730
	JDH3-02-009-R03-(SL)- Street Lighting Panels	2	03-Nov-26	04-Nov-26	329	1,033	0	1,033
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R03-S	2	03-Nov-26	04-Nov-26	329	1,033	0	1,033
	JDH3-02-009-R03-(SL)- LV Distribution Panel Main: 100A, MCCE	4	05-Nov-26	09-Nov-26	329	5,511	0	5,511
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z1-R03-S	2	05-Nov-26	07-Nov-26	329	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z1-F	2	08-Nov-26	09-Nov-26	329	3,674	0	3,674
	JDH3-02-009-R03-Road Works - RD	73	02-Sep-26 A	04-Mar-27	290	68,508	58,232	555,764
	JDH3-02-009-R03-(RD)-Bituminous concrete wearing course 50	5	27-Feb-27	04-Mar-27	290	0	0	345,900
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	27-Feb-27	04-Mar-27	290	0	0	345,900
	JDH3-02-009-R03-(RD)-Precast Concrete Curb	10	02-Sep-26 A	26-Jan-27	290	68,508	58,232	68,508
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10	02-Sep-26 A	26-Jan-27	290	68,508	58,232	68,508
	JDH3-02-009-R03-(RD)-Precast Interlocking Block Pavers	14	09-Feb-27	27-Feb-27	290	0	0	141,356
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	14	09-Feb-27	27-Feb-27	290	0	0	141,356
	R04	80	01-Sep-26 A	03-Dec-26	388	276,448	309,408	1,283,869
	JDH3-02-009-R04-Potable Water Network - WT	63	01-Sep-26 A	14-Nov-26	405	239,434	9,462	239,434
	JDH3-02-009-R04-(WT)-Butterfly Valve-800 mm on pipe dia (800)	4	10-Nov-26	14-Nov-26	405	131,509	0	131,509
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	10-Nov-26	11-Nov-26	405	118,358	0	118,358
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2	12-Nov-26	14-Nov-26	405	13,151	0	13,151
	JDH3-02-009-R04-(WT)-Butterfly Valve-300 mm on pipe dia (315)	2	03-Nov-26	04-Nov-26	411	4,839	0	4,839
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	03-Nov-26	04-Nov-26	411	4,839	0	4,839
	JDH3-02-009-R04-(WT)-Valve Chamber on 315 mm dia pipeline	57	01-Sep-26 A	07-Nov-26	411	32,255	9,462	32,255
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	05-Nov-26	07-Nov-26	411	8,601	0	8,601
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	01-Sep-26 A	04-Nov-26	414	23,654	9,462	23,654
	JDH3-02-009-R04-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	411	6,840	0	6,840
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R04-W	2	03-Nov-26	04-Nov-26	411	6,840	0	6,840
	JDH3-02-009-R04-(WT)-Valve Chamber on 800 mm dia pipeline	8	03-Nov-26	11-Nov-26	407	63,992	0	63,992

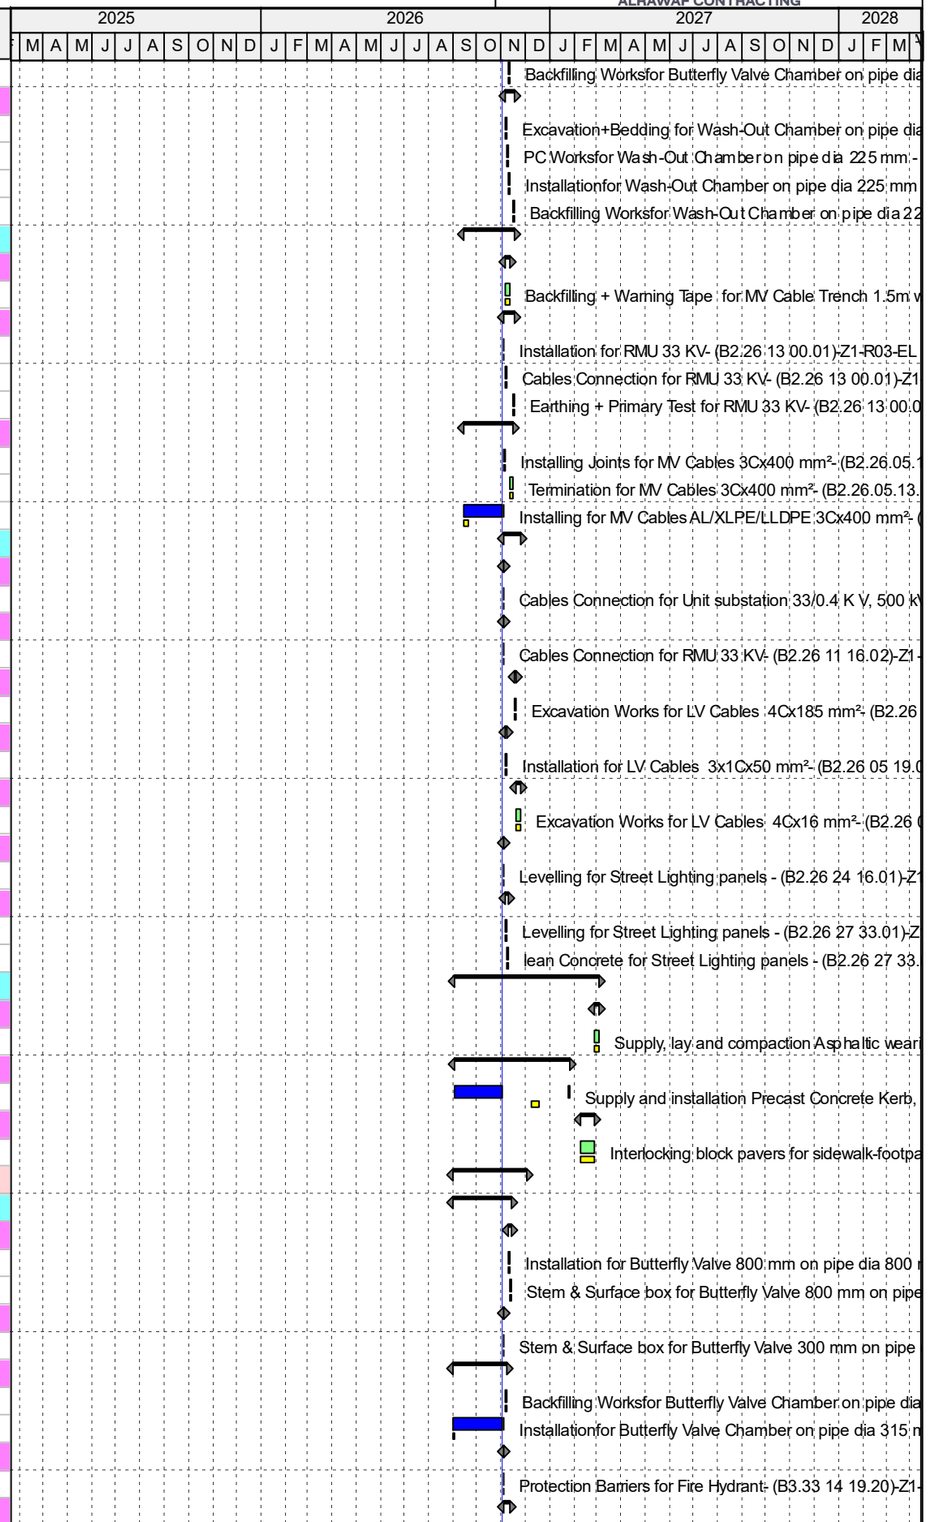


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2	03-Nov-26	04-Nov-26	405	9,599	0	9,599
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	05-Nov-26	07-Nov-26	405	6,399	0	6,399
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	08-Nov-26	09-Nov-26	405	35,195	0	35,195
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	10-Nov-26	11-Nov-26	407	12,798	0	12,798
JDH3-02-009-R04-TSE Network - TSE		8	03-Nov-26	11-Nov-26	407	37,013	0	37,013
JDH3-02-009-R04-(TSE)-Wash-Out Valve-100 mm on pipe dia (3		4	03-Nov-26	07-Nov-26	411	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2	03-Nov-26	04-Nov-26	411	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2	05-Nov-26	07-Nov-26	411	1,613	0	1,613
JDH3-02-009-R04-(TSE)-Wash-Out Chamber on 315 mm dia pipe		8	03-Nov-26	11-Nov-26	407	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2	03-Nov-26	04-Nov-26	407	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2	05-Nov-26	07-Nov-26	407	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2	08-Nov-26	09-Nov-26	407	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - d	2	10-Nov-26	11-Nov-26	407	4,177	0	4,177
JDH3-02-009-R04-Electrical Network - EL		62	08-Sep-26 A	19-Nov-26	321	0	299,947	752,147
JDH3-02-009-R04-(EL)-MV cable trench size 1.5m wide and 80c		26	08-Sep-26 A	15-Nov-26	321	0	606	918
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	2	23-Sep-26 A	15-Nov-26	321	0	110	367
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	2	08-Sep-26 A	03-Nov-26	330	0	496	551
JDH3-02-009-R04-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(		53	16-Sep-26 A	17-Nov-26	321	0	299,341	682,284
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	12-Nov-26	15-Nov-26	321	0	0	14,502
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	15-Nov-26	17-Nov-26	321	0	0	2,580
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	16	16-Sep-26 A	12-Nov-26	321	0	299,341	665,202
JDH3-02-009-R04-(EL)-RMU 33 KV		15	03-Nov-26	19-Nov-26	321	0	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R04-EL	2	03-Nov-26	04-Nov-26	330	0	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R04-El	2	15-Nov-26	17-Nov-26	321	0	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2	17-Nov-26	19-Nov-26	321	0	0	4,925
JDH3-02-009-R04-Street Lighting Network -SL		8	19-Nov-26	29-Nov-26	339	0	0	73,307
JDH3-02-009-R04-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE		4	19-Nov-26	24-Nov-26	343	0	0	63,941
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	19-Nov-26	22-Nov-26	321	0	0	7,522
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	22-Nov-26	24-Nov-26	343	0	0	56,418
JDH3-02-009-R04-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE		6	22-Nov-26	29-Nov-26	321	0	0	9,366
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6	22-Nov-26	29-Nov-26	321	0	0	9,366
JDH3-02-009-R04-Road Works - RD		27	03-Nov-26	03-Dec-26	342	0	0	181,967
JDH3-02-009-R04-(RD)-Precast Concrete Curb		27	03-Nov-26	03-Dec-26	342	0	0	181,967
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10	03-Nov-26	14-Nov-26	342	0	0	71,130
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	4	15-Nov-26	18-Nov-26	342	0	0	27,910
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	13	19-Nov-26	03-Dec-26	342	0	0	82,926
R05		63	15-Sep-26 A	28-Nov-26	393	35,329	206,906	490,261
JDH3-02-009-R05-Potable Water Network - WT		8	03-Nov-26	11-Nov-26	407	33,422	0	33,422
JDH3-02-009-R05-(WT)-Wash-Out Valve-100 mm on pipe dia (22		4	03-Nov-26	07-Nov-26	342	7,673	0	7,673
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2	03-Nov-26	04-Nov-26	342	6,906	0	6,906
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2	2	05-Nov-26	07-Nov-26	342	767	0	767
JDH3-02-009-R05-(WT)-Fire Hydrant		2	03-Nov-26	04-Nov-26	335	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R05-W	2	03-Nov-26	04-Nov-26	335	4,885	0	4,885
JDH3-02-009-R05-(WT)-Wash-Out Chamber on 225 mm dia pipe		8	03-Nov-26	11-Nov-26	407	20,864	0	20,864
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2	03-Nov-26	04-Nov-26	407	3,130	0	3,130
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2	05-Nov-26	07-Nov-26	407	2,086	0	2,086
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2	08-Nov-26	09-Nov-26	407	11,475	0	11,475
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - d	2	10-Nov-26	11-Nov-26	407	4,173	0	4,173
JDH3-02-009-R05-Electrical Network - EL		52	19-Sep-26 A	18-Nov-26	342	0	179,456	273,029
JDH3-02-009-R05-(EL)-MV cable trench size 1.5m wide and 80c		6	08-Nov-26	14-Nov-26	342	0	0	3,901
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	6	08-Nov-26	14-Nov-26	342	0	0	3,901
JDH3-02-009-R05-(EL)-RMU 33 KV		14	03-Nov-26	18-Nov-26	342	0	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z1-R05-EL	2	03-Nov-26	04-Nov-26	350	0	0	59,096

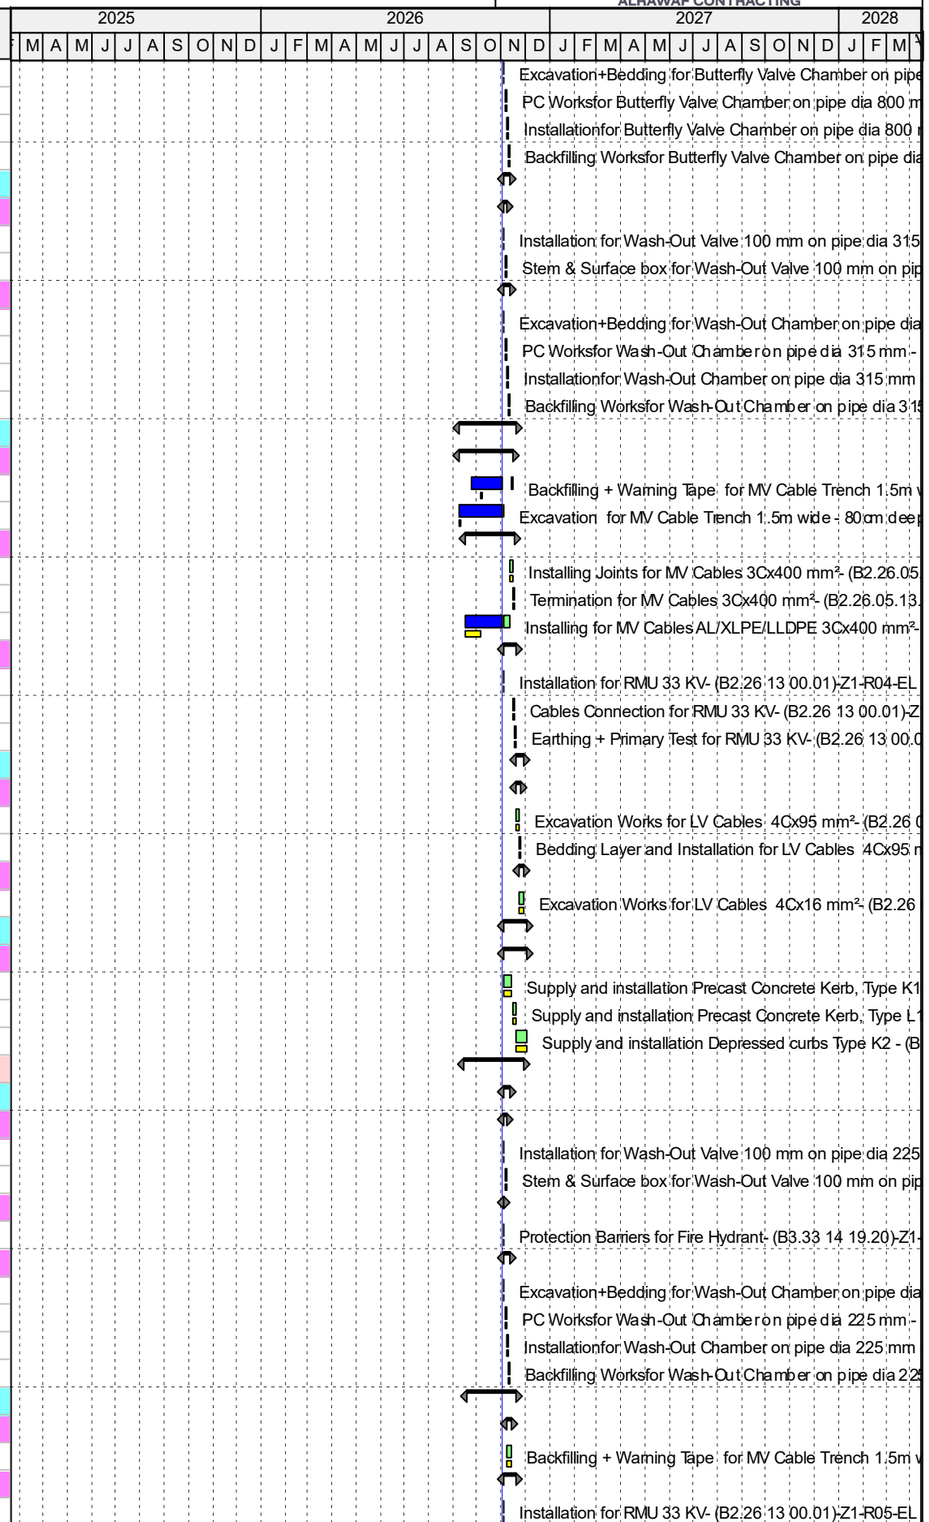


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z1-R05-El	2	05-Nov-26	07-Nov-26	350	0	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z1-R0	2	17-Nov-26	18-Nov-26	342	0	0	4,925
	JDH3-02-009-R05-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	50	19-Sep-26 A	16-Nov-26	342	0	179,456	200,183
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	03-Nov-26	05-Nov-26	344	0	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	15-Nov-26	16-Nov-26	342	0	0	2,580
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	5	19-Sep-26 A	03-Nov-26	344	0	179,456	188,901
	JDH3-02-009-R05-Street Lighting Network -SL	8	19-Nov-26	28-Nov-26	353	0	0	41,901
	JDH3-02-009-R05-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	4	19-Nov-26	23-Nov-26	357	0	0	33,200
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	19-Nov-26	21-Nov-26	342	0	0	3,906
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	22-Nov-26	23-Nov-26	357	0	0	29,294
	JDH3-02-009-R05-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	6	22-Nov-26	28-Nov-26	342	0	0	8,701
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	6	22-Nov-26	28-Nov-26	342	0	0	8,701
	JDH3-02-009-R05-Telecommunications Network - TEL	8	03-Nov-26	11-Nov-26	407	1,907	0	1,907
	JDH3-02-009-R05-(TEL)-Reinforced Concrete Duct 6-ways ducts	8	03-Nov-26	11-Nov-26	407	1,907	0	1,907
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2	03-Nov-26	04-Nov-26	393	286	0	286
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2	05-Nov-26	07-Nov-26	407	858	0	858
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2	08-Nov-26	09-Nov-26	407	572	0	572
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2	10-Nov-26	11-Nov-26	407	191	0	191
	JDH3-02-009-R05-Road Works - RD	59	15-Sep-26 A	23-Nov-26	356	0	27,450	140,003
	JDH3-02-009-R05-(RD)-Precast Concrete Curb	59	15-Sep-26 A	23-Nov-26	356	0	27,450	140,003
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	10-Nov-26	11-Nov-26	356	0	0	6,371
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	10	12-Nov-26	23-Nov-26	356	0	0	65,006
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	10	15-Sep-26 A	09-Nov-26	356	0	27,450	68,626
R06		93	14-Jul-26 A	24-Nov-26	397	520,796	297,553	738,816
	JDH3-02-009-R06-Catch Basins (Storm Network) - ST	5	03-Nov-26	08-Nov-26	404	23,966	0	23,966
	JDH3-02-009-R06-(ST)-Single Catch Basin Works	5	03-Nov-26	08-Nov-26	404	10,684	0	10,684
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5	03-Nov-26	08-Nov-26	404	10,684	0	10,684
	JDH3-02-009-R06-(ST)-Double Catch Basin Works	2	03-Nov-26	04-Nov-26	407	13,282	0	13,282
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	407	13,282	0	13,282
	JDH3-02-009-R06-TSE Network - TSE	58	01-Sep-26 A	08-Nov-26	410	95,630	54,675	95,630
	JDH3-02-009-R06-(TSE)-Butterfly Valve-300 mm on pipe dia (315	9	15-Sep-26 A	03-Nov-26	414	48,390	31,937	48,390
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	22-Sep-26 A	03-Nov-26	414	4,839	3,194	4,839
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2	15-Sep-26 A	03-Nov-26	414	43,551	28,743	43,551
	JDH3-02-009-R06-(TSE)-Valve Chamber on 315 mm dia pipeline	56	01-Sep-26 A	05-Nov-26	410	43,064	22,738	43,064
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	03-Nov-26	05-Nov-26	410	8,613	0	8,613
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	15-Sep-26 A	03-Nov-26	410	23,685	15,632	23,685
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2	01-Sep-26 A	03-Nov-26	410	6,460	4,263	6,460
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	03-Sep-26 A	03-Nov-26	410	4,306	2,842	4,306
	JDH3-02-009-R06-(TSE)-Wash-Out Chamber on 315 mm dia pipe	2	05-Nov-26	08-Nov-26	410	4,177	0	4,177
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2	05-Nov-26	08-Nov-26	410	4,177	0	4,177
	JDH3-02-009-R06-Potable Water Network - WT	55	03-Sep-26 A	07-Nov-26	411	226,043	102,547	226,043
	JDH3-02-009-R06-(WT)-Butterfly Valve-600 mm on pipe dia (630)	44	15-Sep-26 A	05-Nov-26	412	147,949	87,882	147,949
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 630	2	03-Nov-26	05-Nov-26	412	14,795	0	14,795
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2	15-Sep-26 A	03-Nov-26	412	133,154	87,882	133,154
	JDH3-02-009-R06-(WT)-Valve Chamber on 630 mm dia pipeline	54	03-Sep-26 A	07-Nov-26	412	46,816	11,511	46,816
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2	04-Nov-26	07-Nov-26	412	11,015	0	11,015
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2	17-Sep-26 A	04-Nov-26	412	30,293	7,876	30,293
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2	03-Sep-26 A	03-Nov-26	412	5,508	3,635	5,508
	JDH3-02-009-R06-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R06-W	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R06-(WT)-Butterfly Valve-300 mm on pipe dia (315)	4	03-Nov-26	07-Nov-26	405	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2	03-Nov-26	04-Nov-26	405	14,517	0	14,517
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	05-Nov-26	07-Nov-26	405	1,613	0	1,613

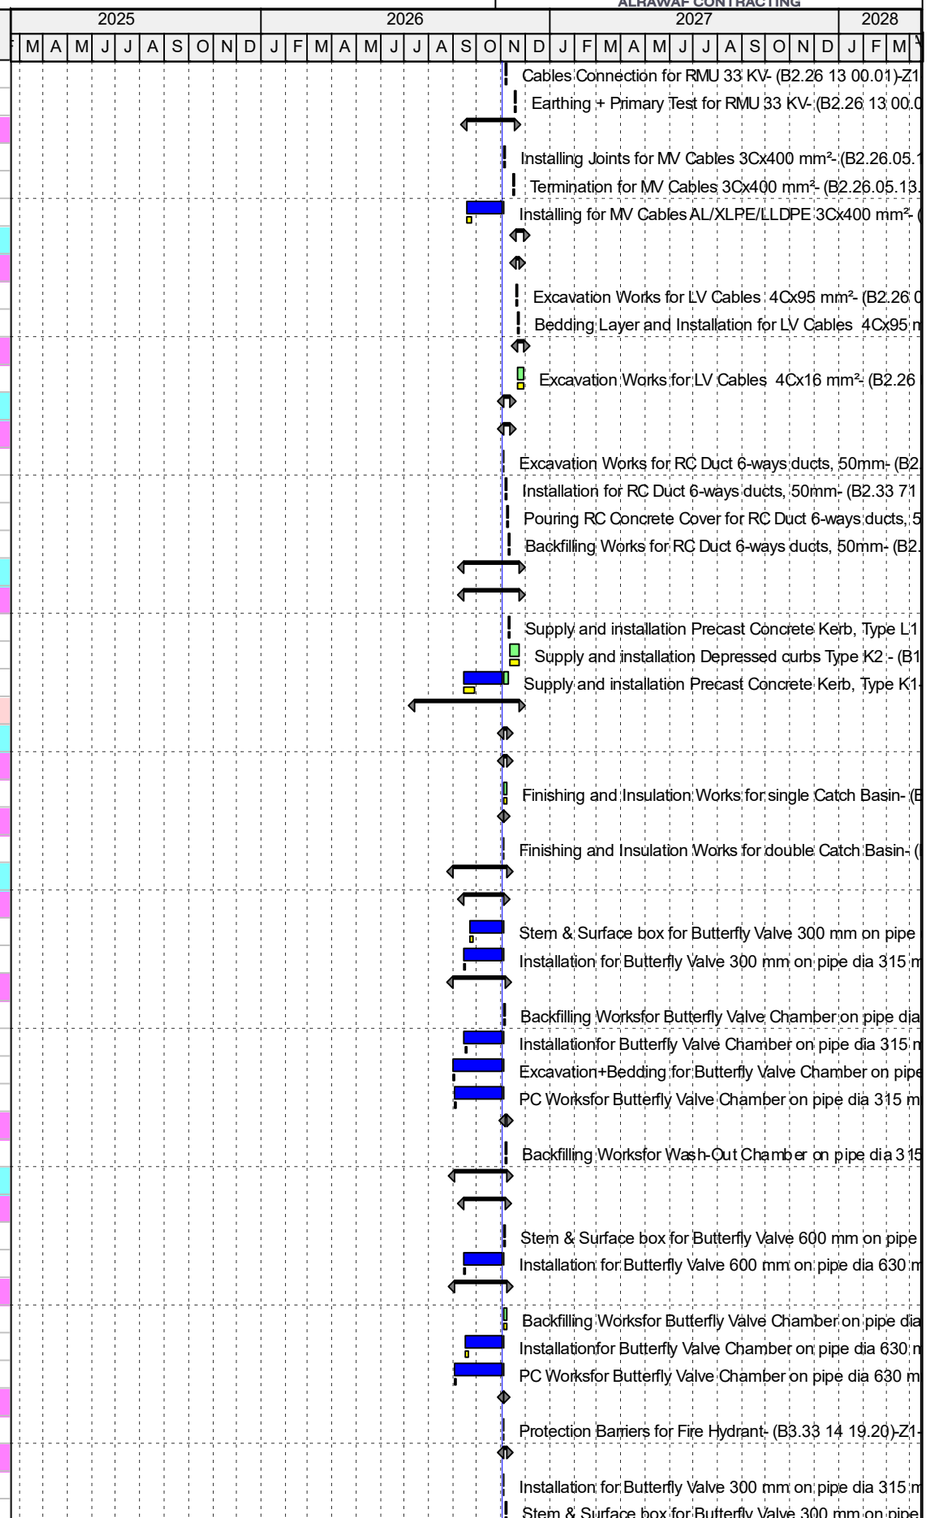


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R06-(WT)-Valve Chamber on 315 mm dia pipeline (	50	08-Sep-26 A	07-Nov-26	412	10,752	3,154	10,752
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	04-Nov-26	07-Nov-26	412	2,867	0	2,867
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	08-Sep-26 A	04-Nov-26	412	7,885	3,154	7,885
	JDH3-02-009-R06-Street Lighting Network -SL	91	14-Jul-26 A	21-Nov-26	390	171,297	140,331	171,297
	JDH3-02-009-R06-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	8	03-Nov-26	11-Nov-26	390	3,978	0	3,978
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	2	03-Nov-26	04-Nov-26	390	398	0	398
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	2	05-Nov-26	07-Nov-26	390	2,984	0	2,984
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	2	08-Nov-26	09-Nov-26	390	199	0	199
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	2	10-Nov-26	11-Nov-26	390	398	0	398
	JDH3-02-009-R06-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	63	03-Sep-26 A	16-Nov-26	390	48,619	39,260	48,619
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	05-Nov-26	09-Nov-26	392	2,431	0	2,431
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4	12-Nov-26	16-Nov-26	390	4,862	0	4,862
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4	05-Sep-26 A	04-Nov-26	392	36,465	34,641	36,465
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	03-Sep-26 A	04-Nov-26	392	4,862	4,619	4,862
	JDH3-02-009-R06-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2	17-Sep-26 A	05-Nov-26	398	6,462	6,139	6,462
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z1-R	2	17-Sep-26 A	05-Nov-26	398	6,462	6,139	6,462
	JDH3-02-009-R06-(SL)-Lighting Pole with double arms 16 m hei	31	14-Jul-26 A	05-Nov-26	400	79,730	75,744	79,730
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	3	18-Jul-26 A	05-Nov-26	398	51,825	49,233	51,825
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3	05-Sep-26 A	05-Nov-26	400	3,987	3,787	3,987
	Excavation for RC foundation for Lighting Pole double arms- (B2	2	14-Jul-26 A	04-Nov-26	396	7,973	7,574	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2	15-Jul-26 A	04-Nov-26	398	7,973	7,574	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2.2	2	16-Jul-26 A	04-Nov-26	398	7,973	7,574	7,973
	JDH3-02-009-R06-(SL)-Street Lighting(LED) Luminaire complet	18	19-Jul-26 A	18-Nov-26	390	20,198	19,188	20,198
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.'	3	19-Jul-26 A	05-Nov-26	398	16,159	15,351	16,159
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3	28-Jul-26 A	18-Nov-26	390	4,040	3,838	4,040
	JDH3-02-009-R06-(SL)-Earthing System for Distribution panels,S	2	19-Nov-26	21-Nov-26	390	1,126	0	1,126
	Supply, construct, connect and test earthing pits for Street Light	2	19-Nov-26	21-Nov-26	390	1,126	0	1,126
	JDH3-02-009-R06-(SL)-Earthing System for Streetlighting feede	2	17-Nov-26	18-Nov-26	390	852	0	852
	Supply, construct, connect and test earthing pits for Street Light	2	17-Nov-26	18-Nov-26	390	852	0	852
	JDH3-02-009-R06-(SL)- Street Lighting Panels	9	05-Nov-26	15-Nov-26	393	10,331	0	10,331
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z1-R06-S	2	05-Nov-26	07-Nov-26	396	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z1-F	2	08-Nov-26	09-Nov-26	396	2,066	0	2,066
	Installing for Street Lighting panels - (B2.26 24 16.01)-Z1-R06-S	2	14-Nov-26	15-Nov-26	393	7,232	0	7,232
	JDH3-02-009-R06-Telecommunications Network - TEL	2	22-Nov-26	23-Nov-26	390	3,859	0	3,859
	JDH3-02-009-R06-(TEL)-Ducts	2	22-Nov-26	23-Nov-26	390	3,859	0	3,859
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2	22-Nov-26	23-Nov-26	390	3,859	0	3,859
	JDH3-02-009-R06-Road Works - RD	17	04-Nov-26	24-Nov-26	363	0	0	218,020
	JDH3-02-009-R06-(RD)-Precast Concrete Curb	17	04-Nov-26	24-Nov-26	363	0	0	218,020
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	12	04-Nov-26	18-Nov-26	363	0	0	178,517
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	5	18-Nov-26	24-Nov-26	363	0	0	39,503
Z4		161	18-Aug-26 A	23-Feb-27	319	2,150,351	156,922	2,567,089
R21		112	18-Aug-26 A	27-Dec-26	368	829,535	56,723	1,178,942
	JDH3-02-009-R21-Sewage Network - SW	75	18-Aug-26 A	14-Nov-26	405	17,420	5,563	17,420
	JDH3-02-009-R21-(SW)-MH Works depth from 1.51 to 2.5 Diam '	68	18-Aug-26 A	05-Nov-26	410	1,334	424	1,334
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3:	2	04-Nov-26	05-Nov-26	410	485	0	485
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	18-Aug-26 A	03-Nov-26	400	849	424	849
	JDH3-02-009-R21-(SW)-MH Works depth from 2.51 to 3.5 Diam '	68	20-Aug-26 A	08-Nov-26	410	2,912	946	2,912
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3:	2	07-Nov-26	08-Nov-26	410	1,019	0	1,019
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	20-Aug-26 A	03-Nov-26	400	1,893	946	1,893
	JDH3-02-009-R21-(SW)-MH Works depth from 3.51 to 4.5 Diam '	65	23-Aug-26 A	07-Nov-26	399	1,834	584	1,834
	Steel Coverfor MH 1200 mm - depth from 3.51 to 4.5 m- (B5.33	2	05-Nov-26	07-Nov-26	399	667	0	667
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	23-Aug-26 A	04-Nov-26	399	1,167	584	1,167
	JDH3-02-009-R21-(SW)-MH Works depth from 3.51 to 4.5 Diam '	65	23-Aug-26 A	09-Nov-26	399	2,154	685	2,154

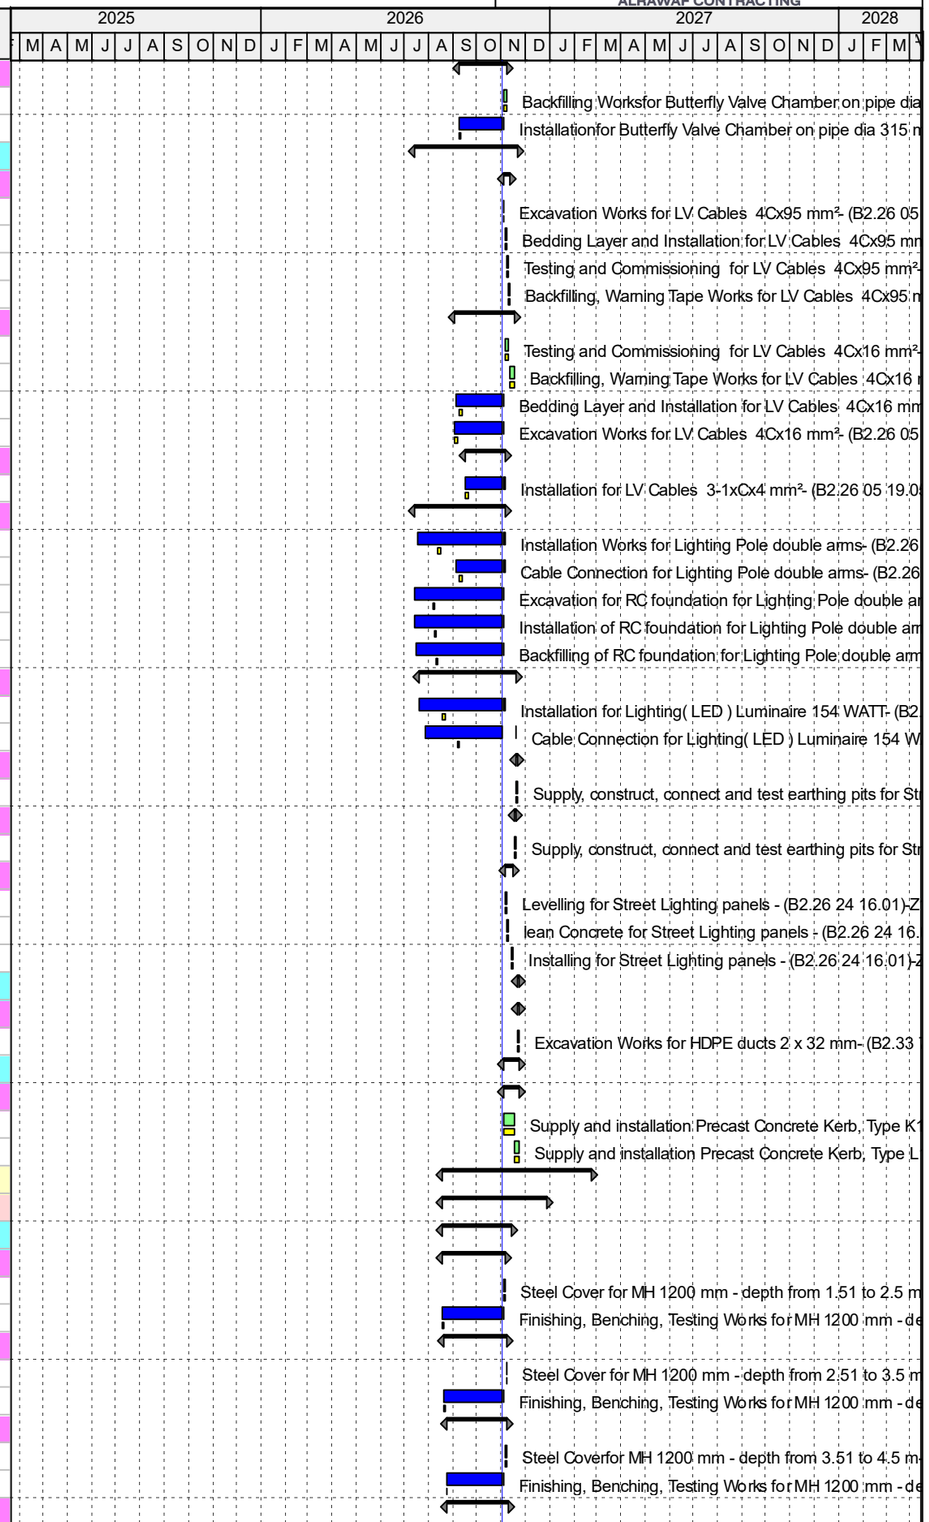


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Steel Cover for MH 1200 mm - depth from 3.51 to 4.5 m- (B5.33	2	08-Nov-26	09-Nov-26	399	783	0	783
	Finishing, Benching Works for MH 1200 mm - depth from 3.51 t	2	23-Aug-26 A	04-Nov-26	401	1,371	685	1,371
	JDH3-02-009-R21-(SW)-MH Works depth from 4.51 to 5.5 Diam	61	23-Aug-26 A	07-Nov-26	411	2,013	641	2,013
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.33	2	05-Nov-26	07-Nov-26	411	732	0	732
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	23-Aug-26 A	04-Nov-26	403	1,281	641	1,281
	JDH3-02-009-R21-(SW)-MH Works depth from 4.51 to 5.5 Diam	59	23-Aug-26 A	07-Nov-26	411	2,343	746	2,343
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.33	2	05-Nov-26	07-Nov-26	411	852	0	852
	Finishing, Benching Works for MH 1200 mm - depth from 4.51 t	2	23-Aug-26 A	04-Nov-26	403	1,491	746	1,491
	JDH3-02-009-R21-(SW)-MH Works depth from 5.51 to 6.5 Diam	61	23-Aug-26 A	11-Nov-26	399	2,250	716	2,250
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.33	2	10-Nov-26	11-Nov-26	399	818	0	818
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	23-Aug-26 A	04-Nov-26	403	1,432	716	1,432
	JDH3-02-009-R21-(SW)-MH Works depth from 5.51 to 6.5 Diam	61	23-Aug-26 A	14-Nov-26	399	2,580	821	2,580
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.33	2	12-Nov-26	14-Nov-26	399	938	0	938
	Finishing, Benching Works for MH 1200 mm - depth from 5.51 t	2	23-Aug-26 A	04-Nov-26	405	1,642	821	1,642
	JDH3-02-009-R21-Storm Network - ST	6	03-Nov-26	09-Nov-26	409	11,086	0	11,086
	JDH3-02-009-R21-(ST)-MH Works (1200) mm diameter depth fro	4	03-Nov-26	07-Nov-26	411	2,104	0	2,104
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	411	1,402	0	1,402
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2	05-Nov-26	07-Nov-26	411	701	0	701
	JDH3-02-009-R21-(ST)-MH Works (2000) mm diameter depth fro	4	03-Nov-26	07-Nov-26	407	6,228	0	6,228
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	03-Nov-26	04-Nov-26	407	4,101	0	4,101
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	407	2,127	0	2,127
	JDH3-02-009-R21-(ST)-MH Works (1500) mm diameter depth fro	4	05-Nov-26	09-Nov-26	407	2,754	0	2,754
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	05-Nov-26	07-Nov-26	407	1,836	0	1,836
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2	08-Nov-26	09-Nov-26	407	918	0	918
	JDH3-02-009-R21-TSE Network - TSE	8	03-Nov-26	11-Nov-26	362	35,502	0	35,502
	JDH3-02-009-R152-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4	03-Nov-26	07-Nov-26	364	14,564	0	14,564
	Installation for Wash-Out Valve 100 mm on pipe dia 110 mm- (E	2	03-Nov-26	04-Nov-26	364	13,108	0	13,108
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 1	2	05-Nov-26	07-Nov-26	364	1,456	0	1,456
	JDH3-02-009-R152-(TSE)-Wash-Out Chamber on 110 mm dia pip	8	03-Nov-26	11-Nov-26	362	20,938	0	20,938
	Excavation+Bedding for Wash-Out Chamber on pipe dia 110 m	2	03-Nov-26	04-Nov-26	362	3,141	0	3,141
	PC Worksfor Wash-Out Chamber on pipe dia 110 mm - depth fr	2	05-Nov-26	07-Nov-26	362	2,094	0	2,094
	Installationfor Wash-Out Chamber on pipe dia 110 mm - depth	2	08-Nov-26	09-Nov-26	362	11,516	0	11,516
	Backfilling Worksfor Wash-Out Chamber on pipe dia 110 mm - c	2	10-Nov-26	11-Nov-26	362	4,188	0	4,188
	JDH3-02-009-R21-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R21-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R21-W	2	03-Nov-26	04-Nov-26	413	4,397	0	4,397
	JDH3-02-009-R21-Electrical Network - EL	72	18-Aug-26 A	11-Nov-26	379	196,180	38,170	196,180
	JDH3-02-009-R21-(EL)-MV cable trench size 1.5m wide and 80c	10	18-Aug-26 A	07-Nov-26	381	7,859	2,358	7,859
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	5	18-Aug-26 A	07-Nov-26	379	4,715	1,415	4,715
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	5	23-Aug-26 A	07-Nov-26	381	3,143	943	3,143
	JDH3-02-009-R21-(EL)-RMU 33 KV	6	04-Nov-26	11-Nov-26	379	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R21-EL	2	04-Nov-26	07-Nov-26	379	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R21-EL	2	07-Nov-26	09-Nov-26	379	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2	09-Nov-26	11-Nov-26	379	4,925	0	4,925
	JDH3-02-009-R21-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7	19-Aug-26 A	07-Nov-26	381	119,376	35,813	119,376
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.0	3	19-Aug-26 A	07-Nov-26	379	105,515	31,654	105,515
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	20-Aug-26 A	07-Nov-26	381	8,701	2,610	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	22-Aug-26 A	07-Nov-26	381	5,160	1,548	5,160
	JDH3-02-009-R21-Street Lighting Network -SL	21	03-Nov-26	28-Nov-26	389	310,515	0	310,515
	JDH3-02-009-R21-(SL)-Lighting Unit Substation 33/0.4 KV, 500 k	4	03-Nov-26	07-Nov-26	395	44,211	0	44,211
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2	03-Nov-26	04-Nov-26	395	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2	05-Nov-26	07-Nov-26	395	3,401	0	3,401
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 4Cx95mm²,Cu/XLPE	9	16-Nov-26	26-Nov-26	390	101,716	0	101,716

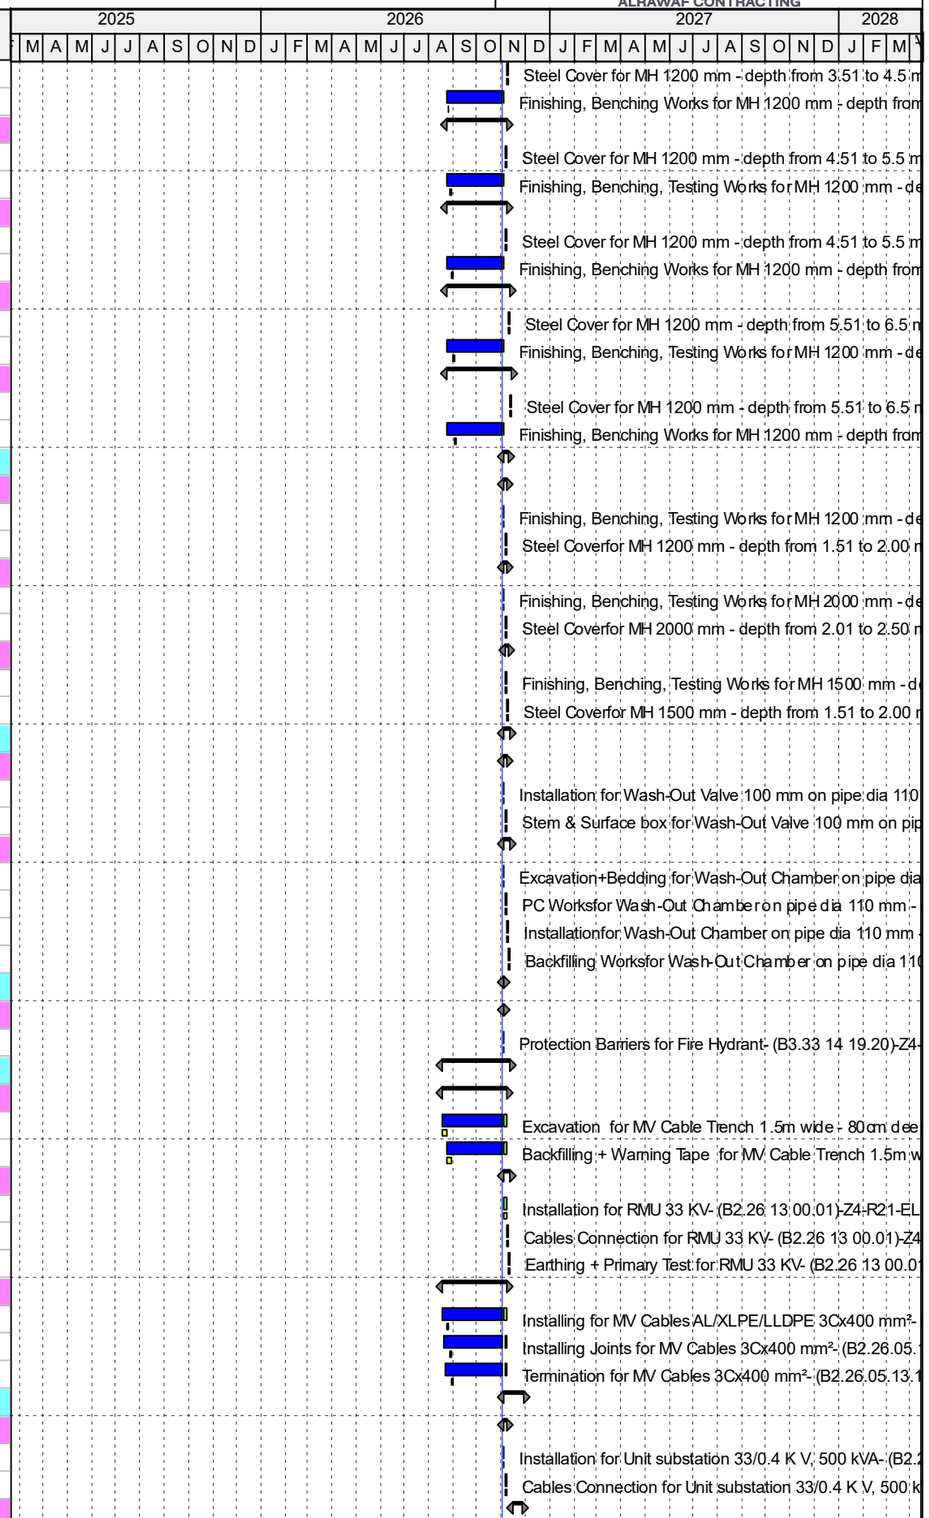


Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	3	16-Nov-26	19-Nov-26	380	11,302	0	11,302
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	3	19-Nov-26	23-Nov-26	390	84,763	0	84,763
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	3	23-Nov-26	26-Nov-26	390	5,651	0	5,651
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 3x1Cx50mm²,Cu/XL	2	08-Nov-26	09-Nov-26	395	1,431	0	1,431
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z4-F	2	08-Nov-26	09-Nov-26	395	1,431	0	1,431
	JDH3-02-009-R21-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	6	19-Nov-26	26-Nov-26	380	35,321	0	35,321
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	3	19-Nov-26	23-Nov-26	380	4,155	0	4,155
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	3	23-Nov-26	26-Nov-26	380	31,166	0	31,166
	JDH3-02-009-R21-(SL)- LV Cables - Single Core Copper, 3-1xC 4	2	23-Nov-26	25-Nov-26	379	2,423	0	2,423
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z4-R	2	23-Nov-26	25-Nov-26	379	2,423	0	2,423
	JDH3-02-009-R21-(SL)-Lighting Pole with single arm 12 m heigh	14	11-Nov-26	28-Nov-26	385	63,784	0	63,784
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	2	11-Nov-26	14-Nov-26	379	6,378	0	6,378
	Installation of RC foundation for Lighting Pole single arm- (B2.2	2	14-Nov-26	16-Nov-26	379	6,378	0	6,378
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	2	16-Nov-26	18-Nov-26	379	6,378	0	6,378
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	4	18-Nov-26	23-Nov-26	379	41,460	0	41,460
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	4	23-Nov-26	28-Nov-26	385	3,189	0	3,189
	JDH3-02-009-R21-(SL)- LV Distribution Panel Main: 100A, MCCB	2	03-Nov-26	04-Nov-26	398	1,837	0	1,837
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z4-R21-S	2	03-Nov-26	04-Nov-26	398	1,837	0	1,837
	JDH3-02-009-R21-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL/	4	14-Nov-26	18-Nov-26	393	970	0	970
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2	14-Nov-26	16-Nov-26	380	114	0	114
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2	16-Nov-26	18-Nov-26	393	855	0	855
	JDH3-02-009-R21-(SL)-RMU 33 KV	8	03-Nov-26	11-Nov-26	395	58,823	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z4-R21-SL	2	03-Nov-26	04-Nov-26	397	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z4-R21-SL	2	05-Nov-26	07-Nov-26	397	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z4-R2	2	10-Nov-26	11-Nov-26	395	4,202	0	4,202
	JDH3-02-009-R21-Telecommunications Network - TEL	8	03-Nov-26	11-Nov-26	407	129,372	0	129,372
	JDH3-02-009-R21-(TEL)-Ducts	8	03-Nov-26	11-Nov-26	407	19,984	0	19,984
	Excavation Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03	2	03-Nov-26	04-Nov-26	348	2,998	0	2,998
	Installation for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 TEL)-Z	4	05-Nov-26	09-Nov-26	407	14,988	0	14,988
	Backfilling Works for HDPE ducts 2 x 32 mm- (B2.33 71 19.03 T	2	10-Nov-26	11-Nov-26	407	1,998	0	1,998
	JDH3-02-009-R21-(TEL)-Manhole Type 1	6	05-Nov-26	11-Nov-26	403	54,694	0	54,694
	Excavation and Bedding Works for MH Type 1 Dim 2000*1000*	2	05-Nov-26	07-Nov-26	403	8,204	0	8,204
	Installation for MH Type 1 Dim 2000*1000*1000 mm- (B2.33.71	2	08-Nov-26	09-Nov-26	403	41,021	0	41,021
	Backfilling Works for MH Type 1 Dim 2000*1000*1000 mm- (B2.	2	10-Nov-26	11-Nov-26	403	5,469	0	5,469
	JDH3-02-009-R21-(TEL)-Manhole Type 2	6	05-Nov-26	11-Nov-26	348	54,694	0	54,694
	Excavation and Bedding Works for MH Type 2 Dim 2000*1000*	2	05-Nov-26	07-Nov-26	348	8,204	0	8,204
	Installation for MH Type 2 Dim 2000*1000*1000 mm- (B2.33.71	2	08-Nov-26	09-Nov-26	348	41,021	0	41,021
	Backfilling Works for MH Type 2 Dim 2000*1000*1000 mm- (B2.	2	10-Nov-26	11-Nov-26	348	5,469	0	5,469
	JDH3-02-009-R21-Road Works - RD	74	26-Sep-26 A	27-Dec-26	368	125,062	12,990	474,469
	JDH3-02-009-R21-(RD)-Bituminous concrete wearing course 50	5	13-Dec-26	17-Dec-26	348	0	0	307,786
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	13-Dec-26	17-Dec-26	348	0	0	307,786
	JDH3-02-009-R21-(RD)-Precast Concrete Curb	46	26-Sep-26 A	24-Nov-26	348	125,062	12,990	125,062
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	2	12-Nov-26	14-Nov-26	348	15,872	0	15,872
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	9	15-Nov-26	24-Nov-26	348	57,229	0	57,229
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	7	26-Sep-26 A	11-Nov-26	348	51,960	12,990	51,960
	JDH3-02-009-R21-(RD)-Pavement Marking	11	13-Dec-26	24-Dec-26	370	0	0	11,011
	Thermoplastic continuous 120 mm wide centre lane- double lin	2	19-Dec-26	20-Dec-26	348	0	0	4,148
	Thermoplastic continuous 120 mm wide centre lane- single line	2	21-Dec-26	22-Dec-26	348	0	0	554
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	23-Dec-26	24-Dec-26	348	0	0	3,113
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	13-Dec-26	16-Dec-26	377	0	0	3,197
	JDH3-02-009-R21-(RD)-Traffic Signage	8	19-Dec-26	27-Dec-26	362	0	0	30,609
	Supply and installation Traffic signs 1 Sheet with Single post - (E	4	19-Dec-26	22-Dec-26	362	0	0	11,445
	Supply and installation Traffic signs 2 Sheet with Single post - (E	4	23-Dec-26	27-Dec-26	362	0	0	19,164

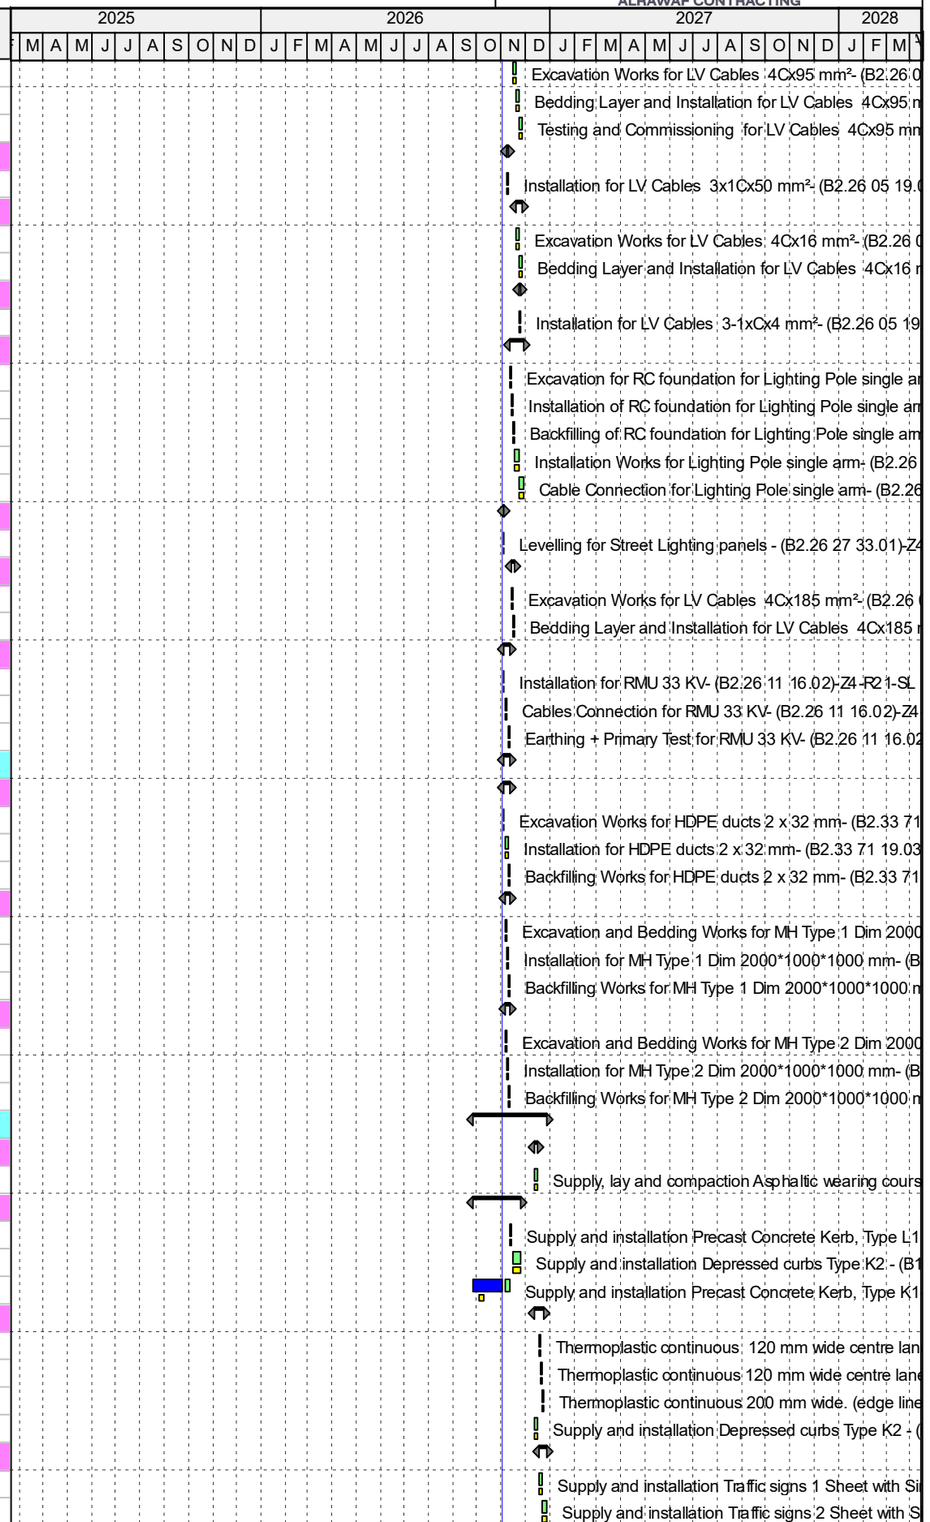


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
R22		161	18-Aug-26 A	23-Feb-27	319	293,744	2,899	299,807
	JDH3-02-009-R22-Sewage Network - SW	79	18-Aug-26 A	18-Nov-26	399	8,759	2,899	8,759
	JDH3-02-009-R22-(SW)-MH Works depth from 1.51 to 2.5 Diam '	77	18-Aug-26 A	16-Nov-26	399	1,334	424	1,334
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3:	2	15-Nov-26	16-Nov-26	399	485	0	485
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	18-Aug-26 A	04-Nov-26	407	849	424	849
	JDH3-02-009-R22-(SW)-MH Works depth from 2.51 to 3.5 Diam '	77	20-Aug-26 A	18-Nov-26	399	7,425	2,475	7,425
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3:	2	17-Nov-26	18-Nov-26	399	2,475	0	2,475
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	20-Aug-26 A	04-Nov-26	409	4,950	2,475	4,950
	JDH3-02-009-R22-Storm Network - ST	8	03-Nov-26	11-Nov-26	407	6,206	0	6,206
	JDH3-02-009-R22-(ST)-MH Works (1200) mm diameter depth fro	4	03-Nov-26	07-Nov-26	411	1,091	0	1,091
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	411	701	0	701
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2	05-Nov-26	07-Nov-26	411	390	0	390
	JDH3-02-009-R22-(ST)-MH Works (2000) mm diameter depth fro	4	03-Nov-26	07-Nov-26	407	2,127	0	2,127
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	03-Nov-26	04-Nov-26	407	1,367	0	1,367
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2	05-Nov-26	07-Nov-26	407	760	0	760
	JDH3-02-009-R22-(ST)-MH Works (1500) mm diameter depth fro	4	05-Nov-26	09-Nov-26	407	1,428	0	1,428
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	05-Nov-26	07-Nov-26	407	918	0	918
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2	08-Nov-26	09-Nov-26	407	510	0	510
	JDH3-02-009-R22-(ST)-MH Works (1500) mm diameter depth fro	4	08-Nov-26	11-Nov-26	407	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	08-Nov-26	09-Nov-26	407	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	10-Nov-26	11-Nov-26	407	557	0	557
	JDH3-02-009-R22-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	2,931	0	2,931
	JDH3-02-009-R22-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	2,931	0	2,931
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R22-W	2	03-Nov-26	04-Nov-26	413	2,931	0	2,931
	JDH3-02-009-R22-Electrical Network - EL	12	03-Nov-26	16-Nov-26	316	205,764	0	205,764
	JDH3-02-009-R22-(EL)-MV cable trench size 1.5m wide and 80c	11	03-Nov-26	15-Nov-26	317	5,449	0	5,449
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	3	03-Nov-26	05-Nov-26	316	3,270	0	3,270
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	3	12-Nov-26	15-Nov-26	317	2,180	0	2,180
	JDH3-02-009-R22-(EL)-MV cables AL/XLPE/LLDPE Unarmored-(	7	07-Nov-26	14-Nov-26	316	131,369	0	131,369
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	3	07-Nov-26	09-Nov-26	316	120,087	0	120,087
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	10-Nov-26	11-Nov-26	316	8,701	0	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	12-Nov-26	14-Nov-26	316	2,580	0	2,580
	JDH3-02-009-R22-(EL)-RMU 33 KV	12	03-Nov-26	16-Nov-26	316	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R22-EL	2	03-Nov-26	04-Nov-26	322	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R22-EL	2	05-Nov-26	07-Nov-26	322	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2	15-Nov-26	16-Nov-26	316	4,925	0	4,925
	JDH3-02-009-R22-Street Lighting Network -SL	10	17-Nov-26	28-Nov-26	325	70,085	0	70,085
	JDH3-02-009-R22-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE	10	17-Nov-26	28-Nov-26	325	59,580	0	59,580
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	17-Nov-26	22-Nov-26	316	7,009	0	7,009
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	5	23-Nov-26	28-Nov-26	325	52,570	0	52,570
	JDH3-02-009-R22-(SL)-Lighting Pole with single arm 12 m heigh	3	23-Nov-26	25-Nov-26	316	10,506	0	10,506
	Excavation for RC foundation for Lighting Pole single arm- (B2.:	3	23-Nov-26	25-Nov-26	316	10,506	0	10,506
	JDH3-02-009-R22-Road Works - RD	14	07-Feb-27	23-Feb-27	316	0	0	6,062
	JDH3-02-009-R22-(RD)-Pavement Marking	14	07-Feb-27	23-Feb-27	316	0	0	6,062
	Thermoplastic continuous 120 mm wide centre lane- single line	2	07-Feb-27	08-Feb-27	316	0	0	356
	Thermoplastic continuous 100 mm wide (parking separator line)	2	09-Feb-27	10-Feb-27	316	0	0	846
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	11-Feb-27	13-Feb-27	316	0	0	1,901
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2	14-Feb-27	15-Feb-27	316	0	0	1,013
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.:	2	16-Feb-27	17-Feb-27	316	0	0	802
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-Z4-R22-RD	2	18-Feb-27	20-Feb-27	316	0	0	572
	Retroreflective Only Right or Only Left Arrow - (B1.32 17 23.03.(	2	21-Feb-27	23-Feb-27	316	0	0	572
R231		106	18-Aug-26 A	20-Dec-26	374	913,568	97,300	974,836
	JDH3-02-009-R231-Sewage Network - SW	81	18-Aug-26 A	21-Nov-26	399	12,077	4,001	12,077

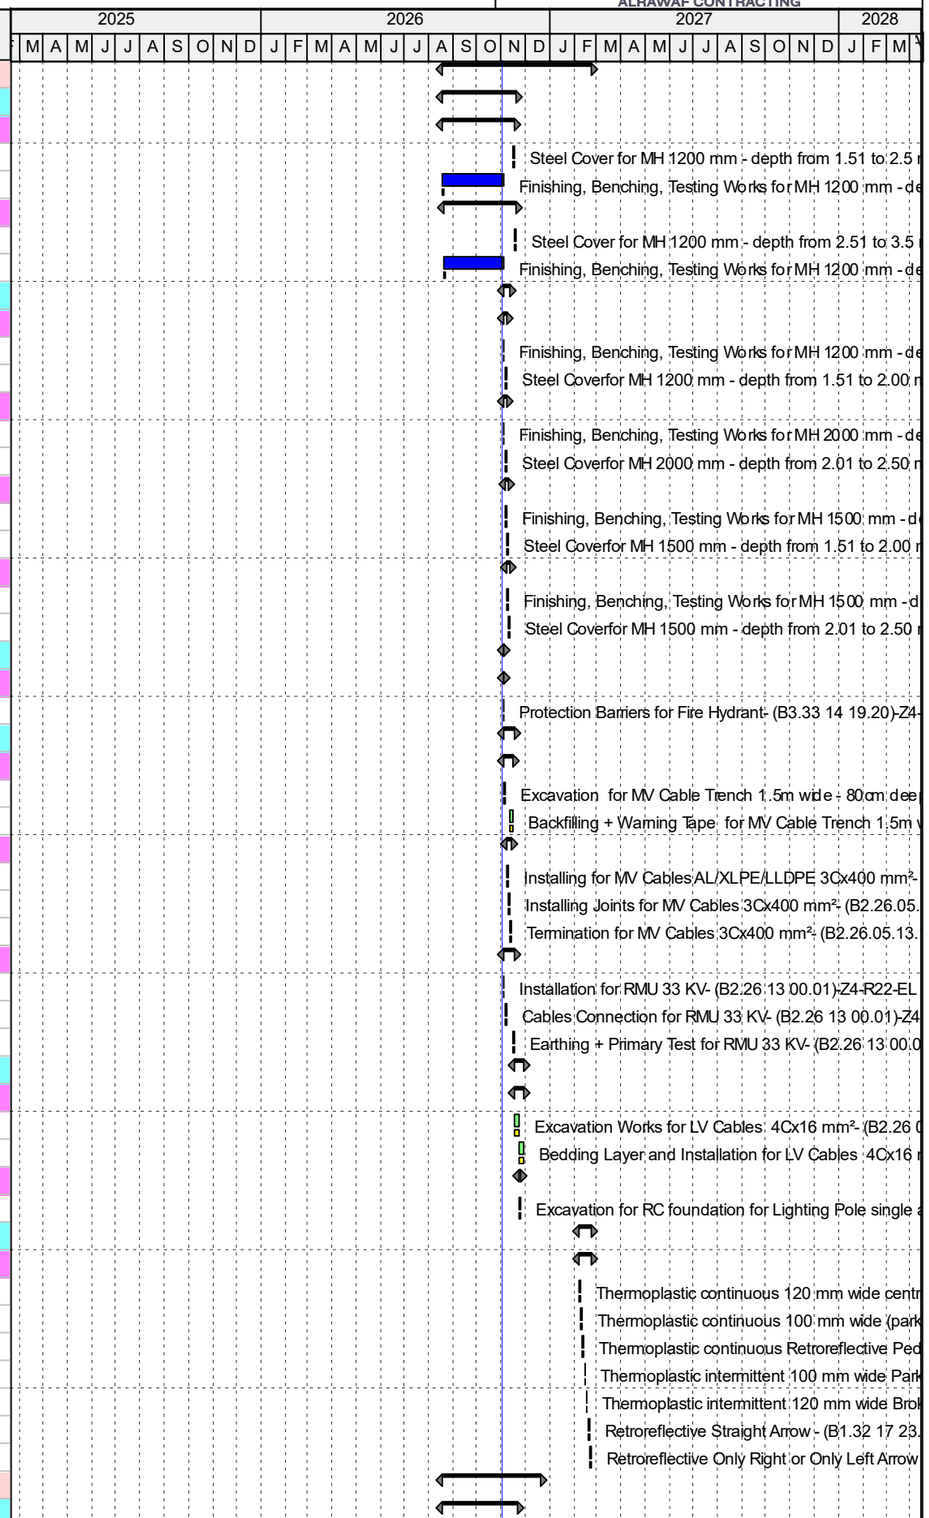

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R231-(SW)-MH Works depth from 0 to 1.50 Diam 1	68	18-Aug-26 A	05-Nov-26	410	3,201	1,067	3,201
	Steel Cover for MH 1200 mm - depth from 0 to 1.5 m- (B5.33 0	2	04-Nov-26	05-Nov-26	410	1,067	0	1,067
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	18-Aug-26 A	03-Nov-26	410	2,134	1,067	2,134
	JDH3-02-009-R231-(SW)-MH Works depth from 1.51 to 2.5 Diam	68	20-Aug-26 A	08-Nov-26	410	7,274	2,425	7,274
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	2	07-Nov-26	08-Nov-26	410	2,425	0	2,425
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	20-Aug-26 A	03-Nov-26	412	4,850	2,425	4,850
	JDH3-02-009-R231-(SW)-MH Works depth from 2.51 to 3.5 Diam	77	23-Aug-26 A	21-Nov-26	399	1,601	510	1,601
	Steel Cover for MH 1200 mm - depth from 2.51 to 3.5 m- (B5.3	2	19-Nov-26	21-Nov-26	399	582	0	582
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	23-Aug-26 A	04-Nov-26	411	1,019	510	1,019
	JDH3-02-009-R231-Storm Network - ST	10	03-Nov-26	14-Nov-26	405	10,457	0	10,457
	JDH3-02-009-R231-(ST)-MH Works (1500) mm diameter depth fr	6	03-Nov-26	09-Nov-26	405	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	407	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	08-Nov-26	09-Nov-26	405	557	0	557
	JDH3-02-009-R231-(ST)-MH Works (2000) mm diameter depth fr	6	05-Nov-26	11-Nov-26	405	2,127	0	2,127
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	05-Nov-26	07-Nov-26	407	1,367	0	1,367
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2	10-Nov-26	11-Nov-26	405	760	0	760
	JDH3-02-009-R231-(ST)-MH Works (2000) mm diameter depth fr	6	08-Nov-26	14-Nov-26	405	6,770	0	6,770
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	08-Nov-26	09-Nov-26	407	4,459	0	4,459
	Steel Coverfor MH 2000 mm - depth from 2.51 to 3.00 m- (B6.3	2	12-Nov-26	14-Nov-26	405	2,312	0	2,312
	JDH3-02-009-R231-TSE Network - TSE	6	03-Nov-26	09-Nov-26	409	35,502	0	35,502
	JDH3-02-009-R231-(TSE)-Wash-Out Chamber on 110 mm dia pip	6	03-Nov-26	09-Nov-26	409	20,938	0	20,938
	Excavation+Bedding for Wash-Out Chamber on pipe dia 110 m	2	03-Nov-26	04-Nov-26	409	3,141	0	3,141
	PC Worksfor Wash-Out Chamber on pipe dia 110 mm - depth fr	2	05-Nov-26	07-Nov-26	409	2,094	0	2,094
	Installationfor Wash-Out Chamber on pipe dia 110 mm - depth	2	08-Nov-26	09-Nov-26	409	11,516	0	11,516
	Backfilling Worksfor Wash-Out Chamber on pipe dia 110 mm - c	2	08-Nov-26	09-Nov-26	366	4,188	0	4,188
	JDH3-02-009-R231-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4	03-Nov-26	07-Nov-26	366	14,564	0	14,564
	Installation for Wash-Out Valve 100 mm on pipe dia 110 mm- (E	2	03-Nov-26	04-Nov-26	366	13,108	0	13,108
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 1	2	05-Nov-26	07-Nov-26	366	1,456	0	1,456
	JDH3-02-009-R231-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	JDH3-02-009-R231-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R231-W	2	03-Nov-26	04-Nov-26	413	4,885	0	4,885
	JDH3-02-009-R231-Electrical Network - EL	70	18-Aug-26 A	15-Nov-26	365	442,139	93,298	442,139
	JDH3-02-009-R231-(EL)-MV cable trench size 1.5m wide and 80	15	18-Aug-26 A	10-Nov-26	365	301	75	301
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	2	18-Aug-26 A	09-Nov-26	366	181	45	181
	Backfilling + Warning Tape for MV Cable Trench 1.5m wide - 80	2	23-Aug-26 A	10-Nov-26	365	120	30	120
	JDH3-02-009-R231-(EL)-MV cables AL/XLPE/LLDPE Unarmored	13	19-Aug-26 A	10-Nov-26	367	372,892	93,223	372,892
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.0	9	19-Aug-26 A	10-Nov-26	365	361,611	90,403	361,611
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0	2	20-Aug-26 A	10-Nov-26	365	8,701	2,175	8,701
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	22-Aug-26 A	10-Nov-26	367	2,580	645	2,580
	JDH3-02-009-R231-(EL)-RMU 33 KV	11	03-Nov-26	15-Nov-26	365	68,946	0	68,946
	Installation for RMU 33 KV- (B2.26 13 00.01)-Z4-R231-EL	2	03-Nov-26	04-Nov-26	370	59,096	0	59,096
	Cables Connection for RMU 33 KV- (B2.26 13 00.01)-Z4-R231-E	2	10-Nov-26	12-Nov-26	365	4,925	0	4,925
	Earthing + Primary Test for RMU 33 KV- (B2.26 13 00.01)-Z4-R2	2	12-Nov-26	15-Nov-26	365	4,925	0	4,925
	JDH3-02-009-R231-Street Lighting Network -SL	10	15-Nov-26	26-Nov-26	376	77,768	0	77,768
	JDH3-02-009-R231-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	10	15-Nov-26	26-Nov-26	369	64,163	0	64,163
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	15-Nov-26	21-Nov-26	365	7,549	0	7,549
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5	21-Nov-26	26-Nov-26	369	56,614	0	56,614
	JDH3-02-009-R231-(SL)- Street Lighting Panels	4	21-Nov-26	25-Nov-26	377	3,099	0	3,099
	Levelling for Street Lighting panels - (B2.26 24 16.01)-Z4-R231-	2	21-Nov-26	23-Nov-26	377	1,033	0	1,033
	lean Concrete for Street Lighting panels - (B2.26 24 16.01)-Z4-F	2	23-Nov-26	25-Nov-26	377	2,066	0	2,066
	JDH3-02-009-R231-(SL)-Lighting Pole with single arm 12 m heig	3	21-Nov-26	24-Nov-26	365	10,506	0	10,506
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3	21-Nov-26	24-Nov-26	365	10,506	0	10,506
	JDH3-02-009-R231-Road Works - RD	41	03-Nov-26	20-Dec-26	372	330,741	0	392,008

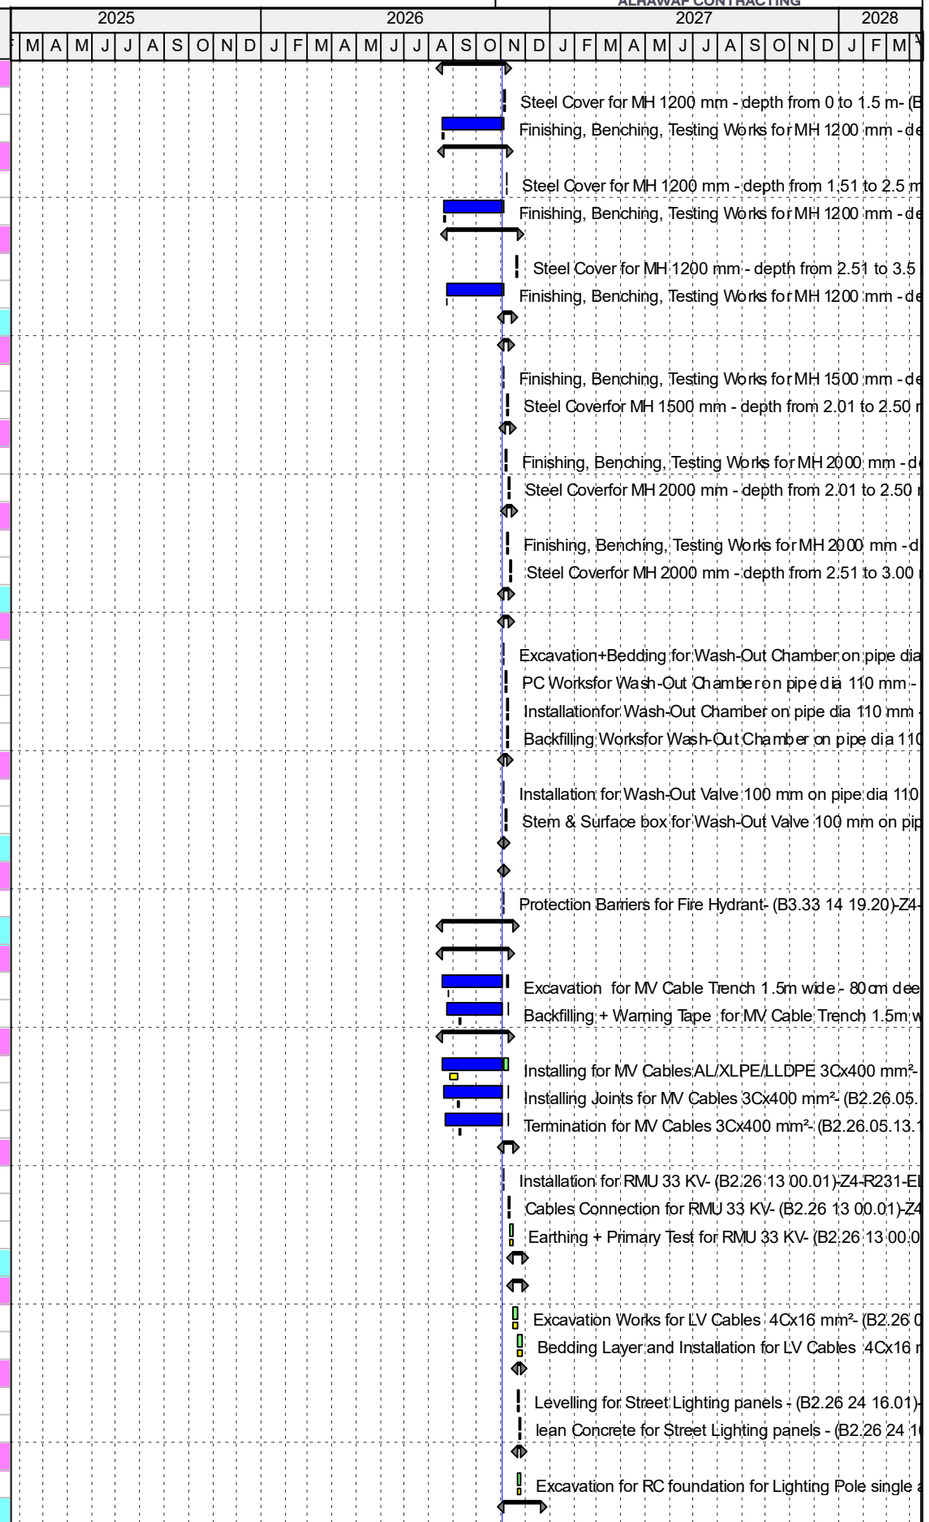


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R231-(RD)-Precast Concrete Curb	19	03-Nov-26	24-Nov-26	368	142,495	0	142,495
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	8	03-Nov-26	11-Nov-26	368	53,533	0	53,533
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3	12-Nov-26	15-Nov-26	368	24,444	0	24,444
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	8	16-Nov-26	24-Nov-26	368	64,518	0	64,518
	JDH3-02-009-R231-(RD)-Precast Interlocking Block Pavers	7	16-Nov-26	23-Nov-26	368	188,245	0	188,245
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	7	16-Nov-26	23-Nov-26	368	188,245	0	188,245
	JDH3-02-009-R231-(RD)-Pavement Marking	18	30-Nov-26	20-Dec-26	368	0	0	13,339
	Thermoplastic continuous 120 mm wide centre lane- double lin	2	30-Nov-26	01-Dec-26	368	0	0	4,325
	Thermoplastic continuous 120 mm wide centre lane- single line	2	02-Dec-26	03-Dec-26	368	0	0	960
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	05-Dec-26	06-Dec-26	368	0	0	2,793
	Thermoplastic continuous 100 mm wide (parking separator line)	2	07-Dec-26	08-Dec-26	368	0	0	1,200
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	09-Dec-26	10-Dec-26	368	0	0	951
	Thermoplastic continuous Chevron hatching - white (round abou	2	12-Dec-26	13-Dec-26	368	0	0	128
	Thermoplastic continuous Painted rumble strips marking (300m	2	14-Dec-26	15-Dec-26	368	0	0	358
	Thermoplastic intermittent 100 mm wide Parking area dotted lin	2	16-Dec-26	17-Dec-26	368	0	0	1,434
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2	19-Dec-26	20-Dec-26	368	0	0	1,189
	JDH3-02-009-R231-(RD)-Traffic Signage	15	30-Nov-26	16-Dec-26	375	0	0	47,929
	Supply and installation Traffic signs 1 Sheet with Single post - (E	9	30-Nov-26	09-Dec-26	375	0	0	27,796
	Supply and installation Traffic signs 2 Sheet with Single post - (E	4	10-Dec-26	14-Dec-26	375	0	0	16,769
	Supply and installation Traffic signs with Double post - (B1.10 14	2	15-Dec-26	16-Dec-26	375	0	0	3,365
R232		21	03-Nov-26	26-Nov-26	394	113,504	0	113,504
	JDH3-02-009-R232-Storm Network - ST	4	03-Nov-26	07-Nov-26	411	8,703	0	8,703
	JDH3-02-009-R232-(ST)-MH Works (1500) mm diameter depth fr	4	03-Nov-26	07-Nov-26	411	5,508	0	5,508
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	03-Nov-26	04-Nov-26	411	3,672	0	3,672
	Steel Coverfor MH 1500 mm - depth from 1.51 to 2.00 m- (B6.3	2	05-Nov-26	07-Nov-26	411	1,836	0	1,836
	JDH3-02-009-R232-(ST)-MH Works (1200) mm diameter depth fr	4	03-Nov-26	07-Nov-26	405	3,194	0	3,194
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	03-Nov-26	04-Nov-26	405	2,104	0	2,104
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	2	05-Nov-26	07-Nov-26	405	1,091	0	1,091
	JDH3-02-009-R232-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	JDH3-02-009-R232-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R232-W	2	03-Nov-26	04-Nov-26	413	5,374	0	5,374
	JDH3-02-009-R232-Street Lighting Network -SL	21	03-Nov-26	26-Nov-26	394	99,427	0	99,427
	JDH3-02-009-R232-(SL)-Lighting Pole with single arm 12 m heig	21	03-Nov-26	26-Nov-26	332	86,296	0	86,296
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3	03-Nov-26	05-Nov-26	332	8,630	0	8,630
	Installation of RC foundation for Lighting Pole single arm- (B2.2	3	07-Nov-26	09-Nov-26	332	8,630	0	8,630
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	3	10-Nov-26	12-Nov-26	332	8,630	0	8,630
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	6	14-Nov-26	19-Nov-26	332	56,092	0	56,092
	Cable Connection for Lighting Pole single arm- (B2.26 56 19.02	6	21-Nov-26	26-Nov-26	332	4,315	0	4,315
	JDH3-02-009-R232-(SL)-Street Lighting(LED) Luminaire comple	4	21-Nov-26	24-Nov-26	396	13,131	0	13,131
	Installation for Lighting(LED) Luminaire 114 WATT- (B2.26.56.1	2	21-Nov-26	22-Nov-26	396	10,505	0	10,505
	Cable Connection for Lighting(LED) Luminaire 114 WATT- (B2.	2	23-Nov-26	24-Nov-26	396	2,626	0	2,626
R45		104	07-Jul-26 A	24-Nov-26	396	74,608	607,073	1,810,102
R450		19	03-Nov-26	24-Nov-26	0	0	0	403,253
	JDH3-02-009-R450-Road Works - RD	19	03-Nov-26	24-Nov-26	0	0	0	403,253
	JDH3-02-009-R450-(RD)-Bituminous base course 200 mm Two L	4	08-Nov-26	11-Nov-26	0	0	0	223,035
	Supply, lay and Asphaltic base course including tack Coat (RC2)	2	10-Nov-26	11-Nov-26	0	0	0	111,517
	Supply, lay and Asphaltic base course including Prime Coat (MC	2	08-Nov-26	09-Nov-26	0	0	0	111,517
	JDH3-02-009-R450-(RD)-Subgrade	2	03-Nov-26	04-Nov-26	0	0	0	27,243
	Supply, lay and compaction subgrade compacted thickness 300	2	03-Nov-26	04-Nov-26	0	0	0	27,243
	JDH3-02-009-R450-(RD)-Bituminous concrete wearing course 5	2	23-Nov-26	24-Nov-26	0	0	0	54,713
	Supply, lay and compaction Asphaltic wearing course 50 mm in	2	23-Nov-26	24-Nov-26	0	0	0	54,713
	JDH3-02-009-R450-(RD)-Precast Concrete Curb	5	12-Nov-26	17-Nov-26	0	0	0	27,935
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	2	12-Nov-26	14-Nov-26	0	0	0	6,376

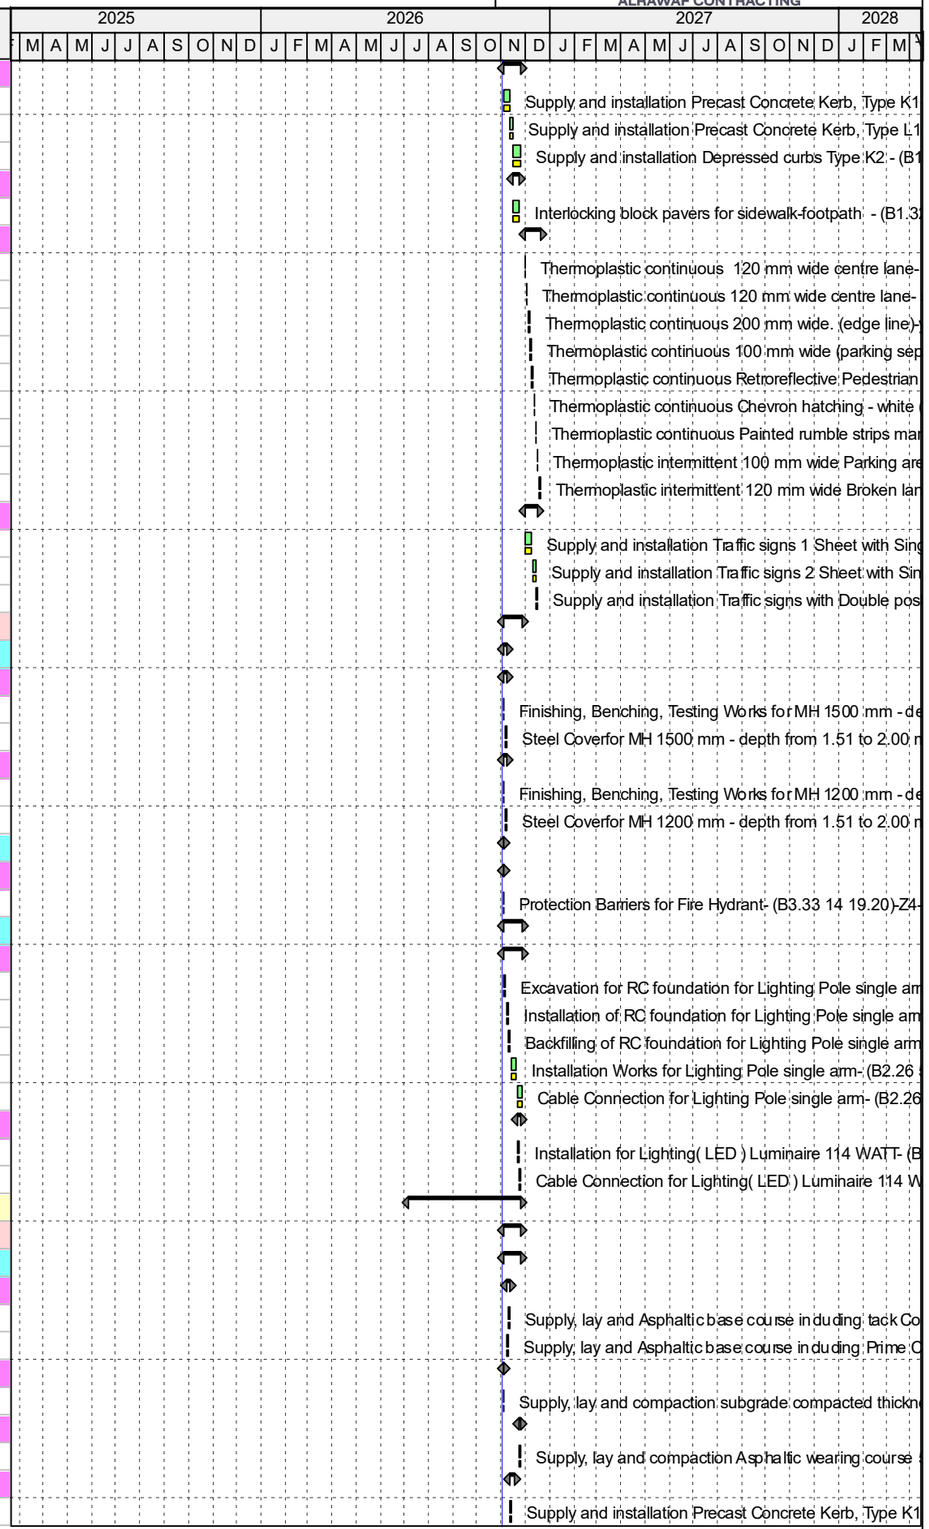


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	3	15-Nov-26	17-Nov-26	0	0	0	21,559
	JDH3-02-009-R450-(RD)-Precast Interlocking Block Pavers	4	18-Nov-26	22-Nov-26	0	0	0	37,971
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	4	18-Nov-26	22-Nov-26	0	0	0	37,971
	JDH3-02-009-R450-(RD)-Aggregate Base Course	2	05-Nov-26	07-Nov-26	0	0	0	32,356
	Supply, lay and compaction Aggregate base course compacted	2	05-Nov-26	07-Nov-26	0	0	0	32,356
R451		65	08-Sep-26 A	24-Nov-26	391	0	124,795	578,594
JDH3-02-009-R451-Road Works - RD		65	08-Sep-26 A	24-Nov-26	389	0	124,795	568,364
	JDH3-02-009-R451-(RD)-Bituminous base course 200 mm Two L	4	12-Sep-26 A	04-Nov-26	376	0	96,688	297,502
	Supply, lay and Asphaltic base course including Prime Coat (MC	2	12-Sep-26 A	04-Nov-26	361	0	44,625	148,751
	Supply, lay and Asphaltic base course including tack Coat (RC2)	2	13-Sep-26 A	04-Nov-26	376	0	52,063	148,751
	JDH3-02-009-R451-(RD)-Subgrade	2	08-Sep-26 A	04-Nov-26	361	0	12,829	36,655
	Supply, lay and compaction subgrade compacted thickness 30(	2	08-Sep-26 A	04-Nov-26	361	0	12,829	36,655
	JDH3-02-009-R451-(RD)-Bituminous concrete wearing course 5(	2	22-Nov-26	24-Nov-26	361	0	0	72,981
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	2	22-Nov-26	24-Nov-26	361	0	0	72,981
	JDH3-02-009-R451-(RD)-Precast Concrete Curb	9	04-Nov-26	15-Nov-26	397	0	0	63,065
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	5	04-Nov-26	10-Nov-26	361	0	0	35,191
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	10-Nov-26	15-Nov-26	361	0	0	21,323
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	10-Nov-26	15-Nov-26	397	0	0	6,550
	JDH3-02-009-R451-(RD)-Precast Interlocking Block Pavers	6	15-Nov-26	22-Nov-26	361	0	0	54,510
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	6	15-Nov-26	22-Nov-26	361	0	0	54,510
	JDH3-02-009-R451-(RD)-Aggregate Base Course	2	10-Sep-26 A	04-Nov-26	361	0	15,278	43,651
	Supply, lay and compaction Aggregate base course compacted	2	10-Sep-26 A	04-Nov-26	361	0	15,278	43,651
JDH3-02-009-R451-Landscape Works - LS		2	15-Nov-26	17-Nov-26	397	0	0	10,230
	JDH3-02-009-R451-(LS)-Miscellaneous Landscaping Items	2	15-Nov-26	17-Nov-26	397	0	0	10,230
	Sand hill in the roundabout with with natural height made from (	2	15-Nov-26	17-Nov-26	397	0	0	10,230
R452		17	03-Nov-26	22-Nov-26	392	0	0	146,987
JDH3-02-009-R452-Road Works - RD		17	03-Nov-26	22-Nov-26	392	0	0	146,987
	JDH3-02-009-R452-(RD)-Bituminous concrete wearing course 5(	2	03-Nov-26	04-Nov-26	379	0	0	46,611
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	2	03-Nov-26	04-Nov-26	379	0	0	46,611
	JDH3-02-009-R452-(RD)-Precast Concrete Curb	13	03-Nov-26	17-Nov-26	392	0	0	61,428
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	4	03-Nov-26	07-Nov-26	392	0	0	22,842
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	5	12-Nov-26	17-Nov-26	392	0	0	30,737
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	08-Nov-26	11-Nov-26	392	0	0	7,850
	JDH3-02-009-R452-(RD)-Precast Interlocking Block Pavers	4	18-Nov-26	22-Nov-26	392	0	0	34,731
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	4	18-Nov-26	22-Nov-26	392	0	0	34,731
	JDH3-02-009-R452-(RD)-Pavement Marking	4	05-Nov-26	09-Nov-26	379	0	0	4,217
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	05-Nov-26	07-Nov-26	379	0	0	2,782
	Thermoplastic intermittent 200 mm wide Broken edge line - (B1.	2	08-Nov-26	09-Nov-26	379	0	0	1,434
R453		101	07-Jul-26 A	21-Nov-26	301	0	482,278	606,661
JDH3-02-009-R453-Road Works - RD		16	03-Nov-26	21-Nov-26	301	0	0	70,797
	JDH3-02-009-R453-(RD)-Bituminous concrete wearing course 5(	2	12-Nov-26	14-Nov-26	301	0	0	21,057
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	2	12-Nov-26	14-Nov-26	301	0	0	21,057
	JDH3-02-009-R453-(RD)-Precast Concrete Curb	6	03-Nov-26	09-Nov-26	301	0	0	31,098
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	2	03-Nov-26	04-Nov-26	301	0	0	11,044
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	05-Nov-26	09-Nov-26	301	0	0	20,054
	JDH3-02-009-R453-(RD)-Precast Interlocking Block Pavers	2	10-Nov-26	11-Nov-26	301	0	0	16,255
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	2	10-Nov-26	11-Nov-26	301	0	0	16,255
	JDH3-02-009-R453-(RD)-Pavement Marking	6	15-Nov-26	21-Nov-26	301	0	0	2,387
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	15-Nov-26	16-Nov-26	301	0	0	1,305
	Thermoplastic intermittent 200 mm wide Broken edge line - (B1.	2	17-Nov-26	18-Nov-26	301	0	0	652
	Retroreflective Straight Arrow - (B1.32 17 23.03.01)-EX-R453-RI	2	19-Nov-26	21-Nov-26	301	0	0	429
JDH3-02-009-R453-Electrical Network - EL		19	07-Jul-26 A	21-Nov-26	301	0	482,278	535,865
	JDH3-02-009-R453-(EL)-MV cable trench size 2.0m wide and 80	10	07-Jul-26 A	21-Nov-26	301	0	8,131	9,035

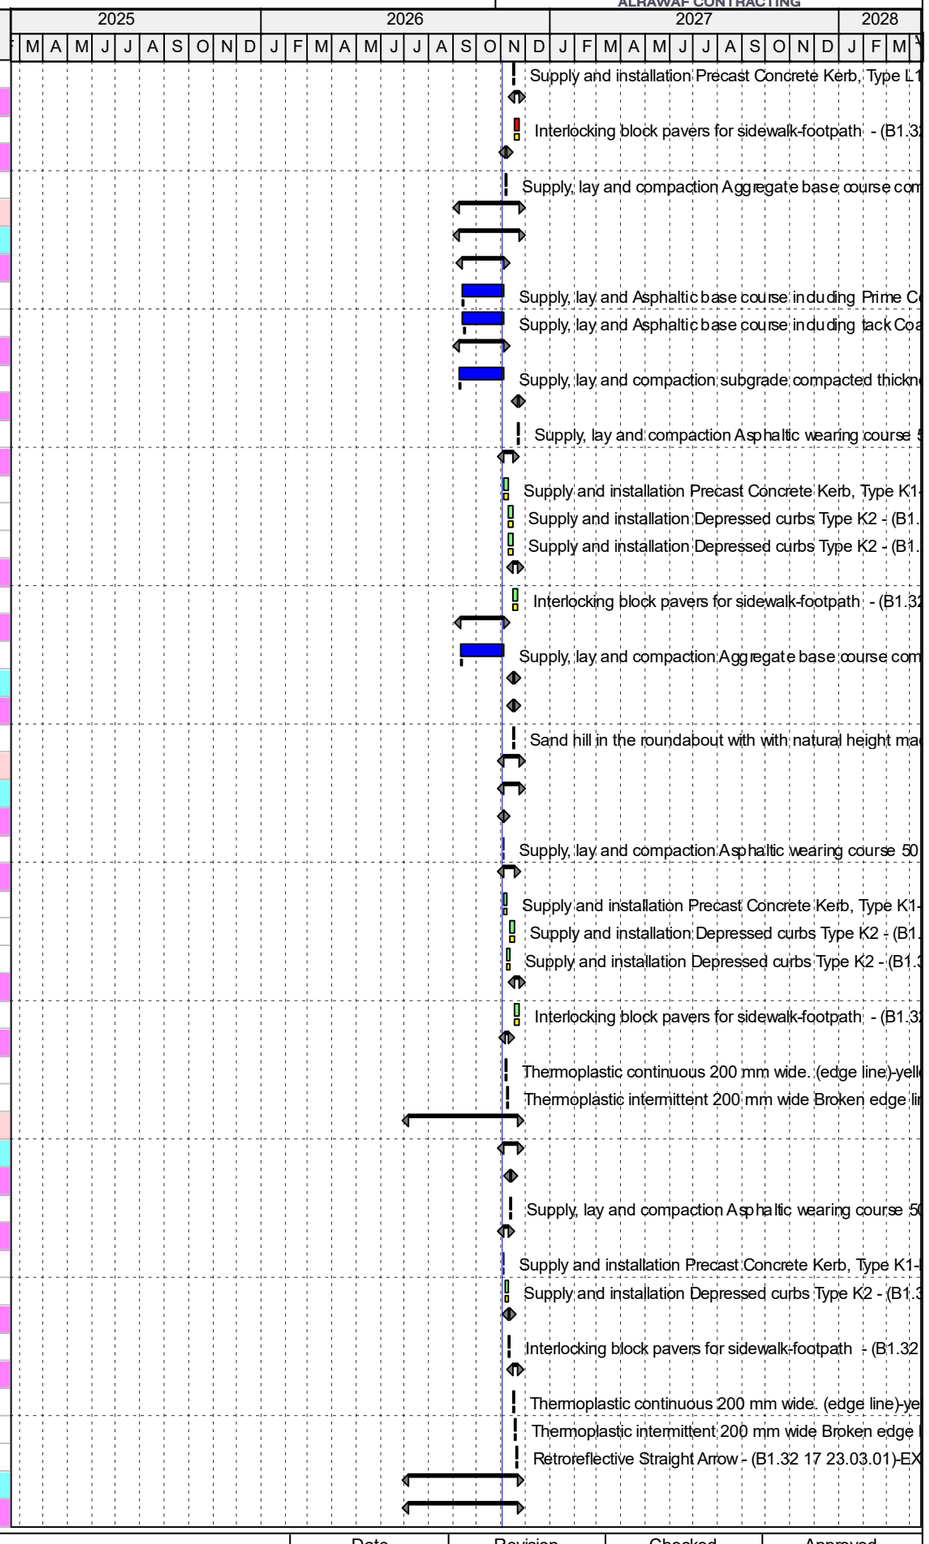


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Backfilling + Warning Tape for MV Cable Trench 2.0m wide - 80	5	09-Jul-26 A	21-Nov-26	301	0	3,252	3,614
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5	07-Jul-26 A	21-Nov-26	301	0	4,879	5,421
	JDH3-02-009-R453-(EL)-MV cables AL/XLPE/LLDPE Unarmored	9	11-Jul-26 A	21-Nov-26	301	0	474,147	526,830
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	7	11-Jul-26 A	21-Nov-26	301	0	466,316	518,129
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	12-Jul-26 A	21-Nov-26	301	0	7,831	8,701
R454		12	03-Nov-26	16-Nov-26	403	74,608	0	74,608
JDH3-02-009-R454-Potable Water Network - WT		12	03-Nov-26	16-Nov-26	403	74,608	0	74,608
JDH3-02-009-R454-(WT)-Valve Chamber on 400 mm dia pipeline		12	03-Nov-26	16-Nov-26	403	14,336	0	14,336
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	03-Nov-26	04-Nov-26	403	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	05-Nov-26	07-Nov-26	403	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	08-Nov-26	09-Nov-26	403	7,885	0	7,885
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	15-Nov-26	16-Nov-26	403	2,867	0	2,867
JDH3-02-009-R454-(WT)-Fire Hydrant		6	03-Nov-26	09-Nov-26	405	34,198	0	34,198
	Stem for Fire Hydrant- (B3.33 14 19.20)-EX-R454-WT	2	03-Nov-26	04-Nov-26	405	14,656	0	14,656
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-EX-R454-WT	2	05-Nov-26	07-Nov-26	405	17,099	0	17,099
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-EX-R454-\	2	08-Nov-26	09-Nov-26	405	2,443	0	2,443
JDH3-02-009-R454-(WT)-Butterfly Valve-400 mm on pipe dia (40		4	10-Nov-26	14-Nov-26	403	26,074	0	26,074
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2	10-Nov-26	11-Nov-26	403	23,467	0	23,467
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2	12-Nov-26	14-Nov-26	403	2,607	0	2,607
R10		165	07-Jul-26 A	02-Feb-27	336	7,350,697	3,669,941	9,274,775
R103		134	28-Jul-26 A	02-Feb-27	336	919,780	121,700	1,832,277
JDH3-02-009-R103-Storm Network - ST		7	03-Nov-26	10-Nov-26	400	11,377	0	11,377
JDH3-02-009-R103-(ST)-MH Works (1200) mm diameter depth fr		3	03-Nov-26	05-Nov-26	400	9,817	0	9,817
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	3	03-Nov-26	05-Nov-26	400	9,817	0	9,817
JDH3-02-009-R103-(ST)-MH Works (1500) mm diameter depth fr		4	07-Nov-26	10-Nov-26	400	1,560	0	1,560
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	07-Nov-26	08-Nov-26	400	1,003	0	1,003
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	09-Nov-26	10-Nov-26	400	557	0	557
JDH3-02-009-R103-Catch Basins (Storm Network) - ST		43	17-Sep-26 A	07-Nov-26	411	36,772	6,129	36,772
JDH3-02-009-R103-(ST)-Single Catch Basin Works		41	19-Sep-26 A	07-Nov-26	411	16,848	2,808	16,848
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4	03-Nov-26	07-Nov-26	411	11,232	0	11,232
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z3-R103-S	4	19-Sep-26 A	07-Nov-26	411	5,616	2,808	5,616
JDH3-02-009-R103-(ST)-Double Catch Basin Works		41	17-Sep-26 A	04-Nov-26	413	19,923	3,321	19,923
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	413	13,282	0	13,282
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z3-R103-S	2	17-Sep-26 A	04-Nov-26	413	6,641	3,321	6,641
JDH3-02-009-R103-TSE Network - TSE		10	03-Nov-26	14-Nov-26	405	135,563	0	135,563
JDH3-02-009-R103-(TSE)-Butterfly Valve-300 mm on pipe dia (31		8	03-Nov-26	11-Nov-26	407	48,390	0	48,390
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2	03-Nov-26	04-Nov-26	411	43,551	0	43,551
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	10-Nov-26	11-Nov-26	407	4,839	0	4,839
JDH3-02-009-R103-(TSE)-Wash-Out Valve-100 mm on pipe dia (3		4	03-Nov-26	07-Nov-26	228	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2	03-Nov-26	04-Nov-26	228	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2	05-Nov-26	07-Nov-26	228	1,613	0	1,613
JDH3-02-009-R103-(TSE)-Air Valve-50 mm on pipe dia (315) mm		4	05-Nov-26	09-Nov-26	228	6,338	0	6,338
	Installation for Air Valve 50 mm on pipe dia 315 mm- (B4.33 14	2	05-Nov-26	07-Nov-26	228	5,704	0	5,704
	Stem & Surface box for Air Valve 50 mm on pipe dia 315 mm- (I	2	08-Nov-26	09-Nov-26	228	634	0	634
JDH3-02-009-R103-(TSE)-Valve Chamber on 315 mm dia pipelin		6	03-Nov-26	09-Nov-26	407	36,604	0	36,604
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	03-Nov-26	04-Nov-26	407	4,306	0	4,306
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	05-Nov-26	07-Nov-26	407	23,685	0	23,685
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	08-Nov-26	09-Nov-26	407	8,613	0	8,613
JDH3-02-009-R103-(TSE)-Wash-Out Chamber on 315 mm dia pi		8	03-Nov-26	11-Nov-26	228	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2	03-Nov-26	04-Nov-26	228	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2	05-Nov-26	07-Nov-26	228	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2	08-Nov-26	09-Nov-26	228	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2	10-Nov-26	11-Nov-26	228	4,177	0	4,177

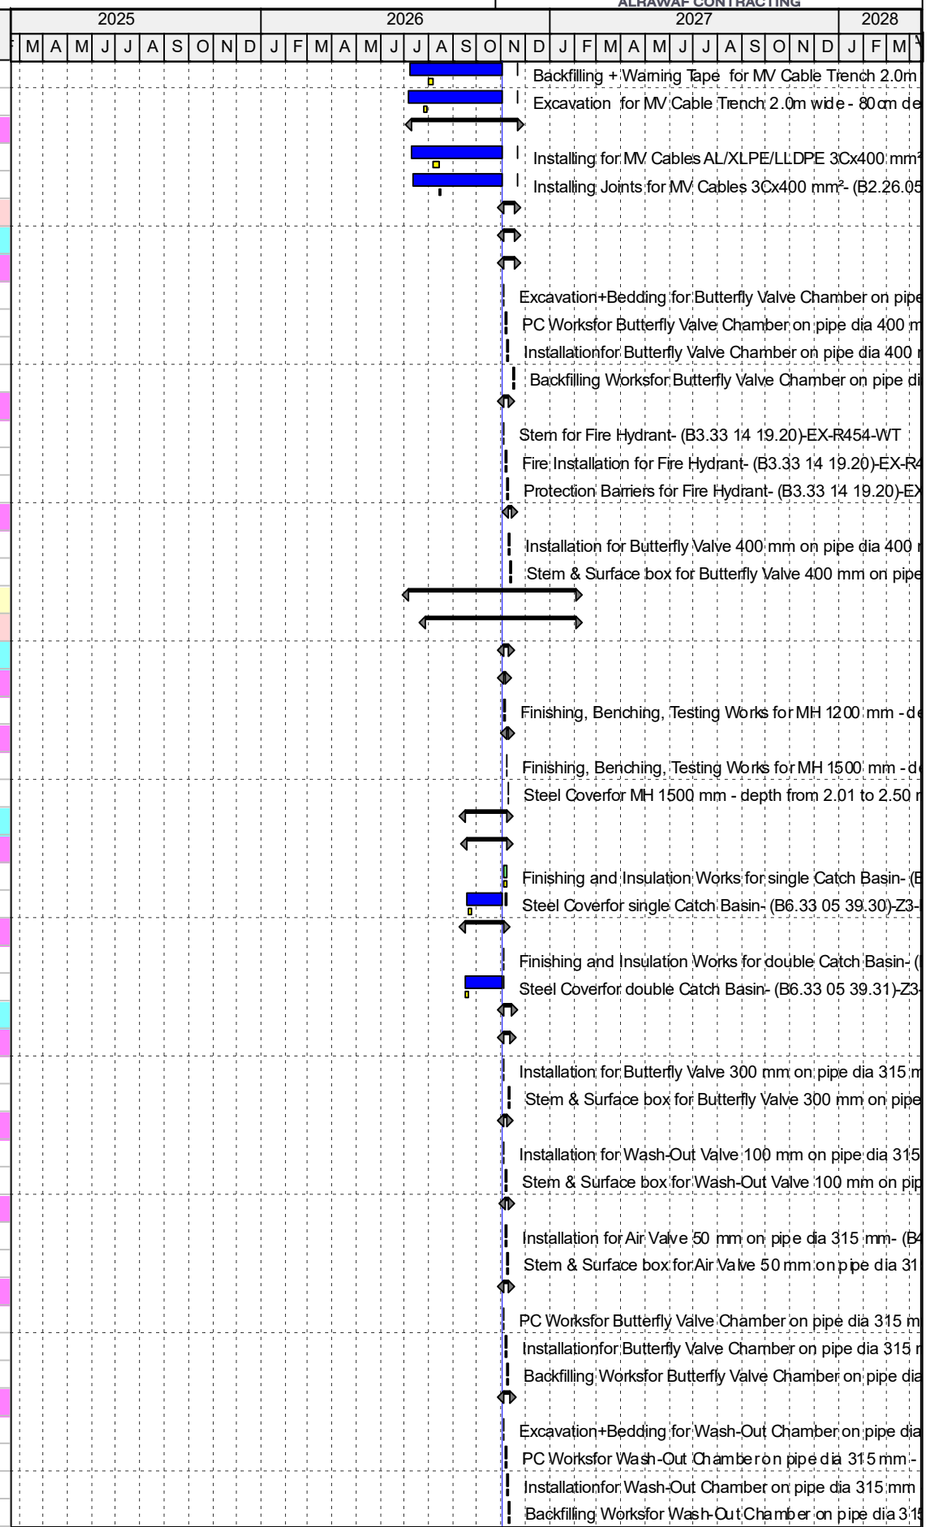


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R103-(TSE)-Air Valve Chamber on 315 mm dia pip	8	05-Nov-26	14-Nov-26	405	7,218	0	7,218
	Excavation+Bedding for Air Valve Chamber on pipe dia 315 mm	2	05-Nov-26	07-Nov-26	407	1,083	0	1,083
	PC Worksfor Air Valve Chamber on pipe dia 315 mm - depth fro	2	08-Nov-26	09-Nov-26	407	722	0	722
	Installationfor Air Valve Chamber on pipe dia 315 mm - depth fr	2	10-Nov-26	11-Nov-26	407	3,970	0	3,970
	Backfilling Worksfor Air Valve Chamber on pipe dia 315 mm - de	2	12-Nov-26	14-Nov-26	228	1,444	0	1,444
	JDH3-02-009-R103-Potable Water Network - WT	43	22-Sep-26 A	11-Nov-26	407	179,197	23,408	179,197
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	6	22-Sep-26 A	08-Nov-26	411	20,256	6,077	20,256
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	6	22-Sep-26 A	08-Nov-26	411	20,256	6,077	20,256
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	4	23-Sep-26 A	08-Nov-26	411	52,791	15,837	52,791
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	4	23-Sep-26 A	08-Nov-26	411	52,791	15,837	52,791
	JDH3-02-009-R103-(WT)-HDPE Pipes-800 mm diameter depth fr	4	24-Sep-26 A	08-Nov-26	411	4,981	1,494	4,981
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	4	24-Sep-26 A	08-Nov-26	411	4,981	1,494	4,981
	JDH3-02-009-R103-(WT)-Butterfly Valve-800 mm on pipe dia (80	4	05-Nov-26	09-Nov-26	407	65,754	0	65,754
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	05-Nov-26	07-Nov-26	407	59,179	0	59,179
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 80(	2	08-Nov-26	09-Nov-26	407	6,575	0	6,575
	JDH3-02-009-R103-(WT)-Valve Chamber on 800 mm dia pipeline	8	03-Nov-26	11-Nov-26	407	31,996	0	31,996
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 8(	2	03-Nov-26	04-Nov-26	407	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	05-Nov-26	07-Nov-26	407	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	08-Nov-26	09-Nov-26	407	17,598	0	17,598
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	10-Nov-26	11-Nov-26	407	6,399	0	6,399
	JDH3-02-009-R103-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	236	3,420	0	3,420
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z3-R103-V	2	03-Nov-26	04-Nov-26	236	3,420	0	3,420
	JDH3-02-009-R103-Electrical Network - EL	15	15-Nov-26	01-Dec-26	386	454,467	0	454,467
	JDH3-02-009-R103-(EL)-MV cable trench size 2.0m wide and 80	10	15-Nov-26	25-Nov-26	228	8,795	0	8,795
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5	15-Nov-26	19-Nov-26	228	5,277	0	5,277
	Backfilling + Warning Tape for MV Cable Trench 2.0m wide - 80	5	21-Nov-26	25-Nov-26	228	3,518	0	3,518
	JDH3-02-009-R103-(EL)-MV cables AL/XLPE/LLDPE Unarmored	10	21-Nov-26	01-Dec-26	386	445,672	0	445,672
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	10	21-Nov-26	01-Dec-26	386	445,672	0	445,672
	JDH3-02-009-R103-Street Lighting Network -SL	49	28-Jul-26 A	09-Dec-26	238	102,404	92,164	102,404
	JDH3-02-009-R103-(SL)- LV Cables - Single Core Copper, 3-1x C	2	17-Sep-26 A	25-Nov-26	244	6,462	5,816	6,462
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z3-R	2	17-Sep-26 A	25-Nov-26	244	6,462	5,816	6,462
	JDH3-02-009-R103-(SL)-Lighting Pole with double arms 16 m he	25	28-Jul-26 A	25-Nov-26	244	75,744	68,169	75,744
	Excavation for RC foundation for Lighting Pole double arms- (B2	2	28-Jul-26 A	25-Nov-26	228	7,973	7,176	7,973
	Installation of RC foundation for Lighting Pole double arms- (B2	2	29-Jul-26 A	25-Nov-26	242	7,973	7,176	7,973
	Backfilling of RC foundation for Lighting Pole double arms- (B2..	2	30-Jul-26 A	25-Nov-26	244	7,973	7,176	7,973
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	3	02-Sep-26 A	25-Nov-26	244	51,825	46,642	51,825
	JDH3-02-009-R103-(SL)-Street Lighting(LED) Luminaire comple	13	16-Sep-26 A	09-Dec-26	238	20,198	18,179	20,198
	Cable Connection for Lighting(LED) Luminaire 154 WATT- (B2.	3	17-Sep-26 A	09-Dec-26	238	4,040	3,636	4,040
	Installation for Lighting(LED) Luminaire 154 WATT- (B2.26.56.1	3	16-Sep-26 A	25-Nov-26	244	16,159	14,543	16,159
	JDH3-02-009-R103-Road Works - RD	79	03-Nov-26	02-Feb-27	228	0	0	894,179
	JDH3-02-009-R103-(RD)-Bituminous concrete wearing course 5(	6	03-Nov-26	09-Nov-26	240	0	0	535,514
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	6	03-Nov-26	09-Nov-26	240	0	0	535,514
	JDH3-02-009-R103-(RD)-Precast Concrete Curb	12	14-Jan-27	27-Jan-27	228	0	0	95,145
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	12	14-Jan-27	27-Jan-27	228	0	0	95,145
	JDH3-02-009-R103-(RD)-Precast Interlocking Block Pavers	17	14-Jan-27	02-Feb-27	228	0	0	253,740
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	17	14-Jan-27	02-Feb-27	228	0	0	253,740
	JDH3-02-009-R103-(RD)-Pavement Marking	12	10-Nov-26	23-Nov-26	240	0	0	9,781
	Thermoplastic continuous 120 mm wide centre lane- single line	2	10-Nov-26	11-Nov-26	240	0	0	1,261
	Thermoplastic continuous 300 mm wide. (stop line) - (B1.32 17	2	12-Nov-26	14-Nov-26	240	0	0	351
	Thermoplastic continuous Retroreflective Pedestrian crossing lin	2	15-Nov-26	16-Nov-26	240	0	0	4,753
	Thermoplastic continuous Chevron hatching - white (round abou	2	17-Nov-26	18-Nov-26	240	0	0	32
	Thermoplastic continuous Painted rumble strips marking (300m	2	19-Nov-26	21-Nov-26	240	0	0	1,403
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2	22-Nov-26	23-Nov-26	240	0	0	1,980

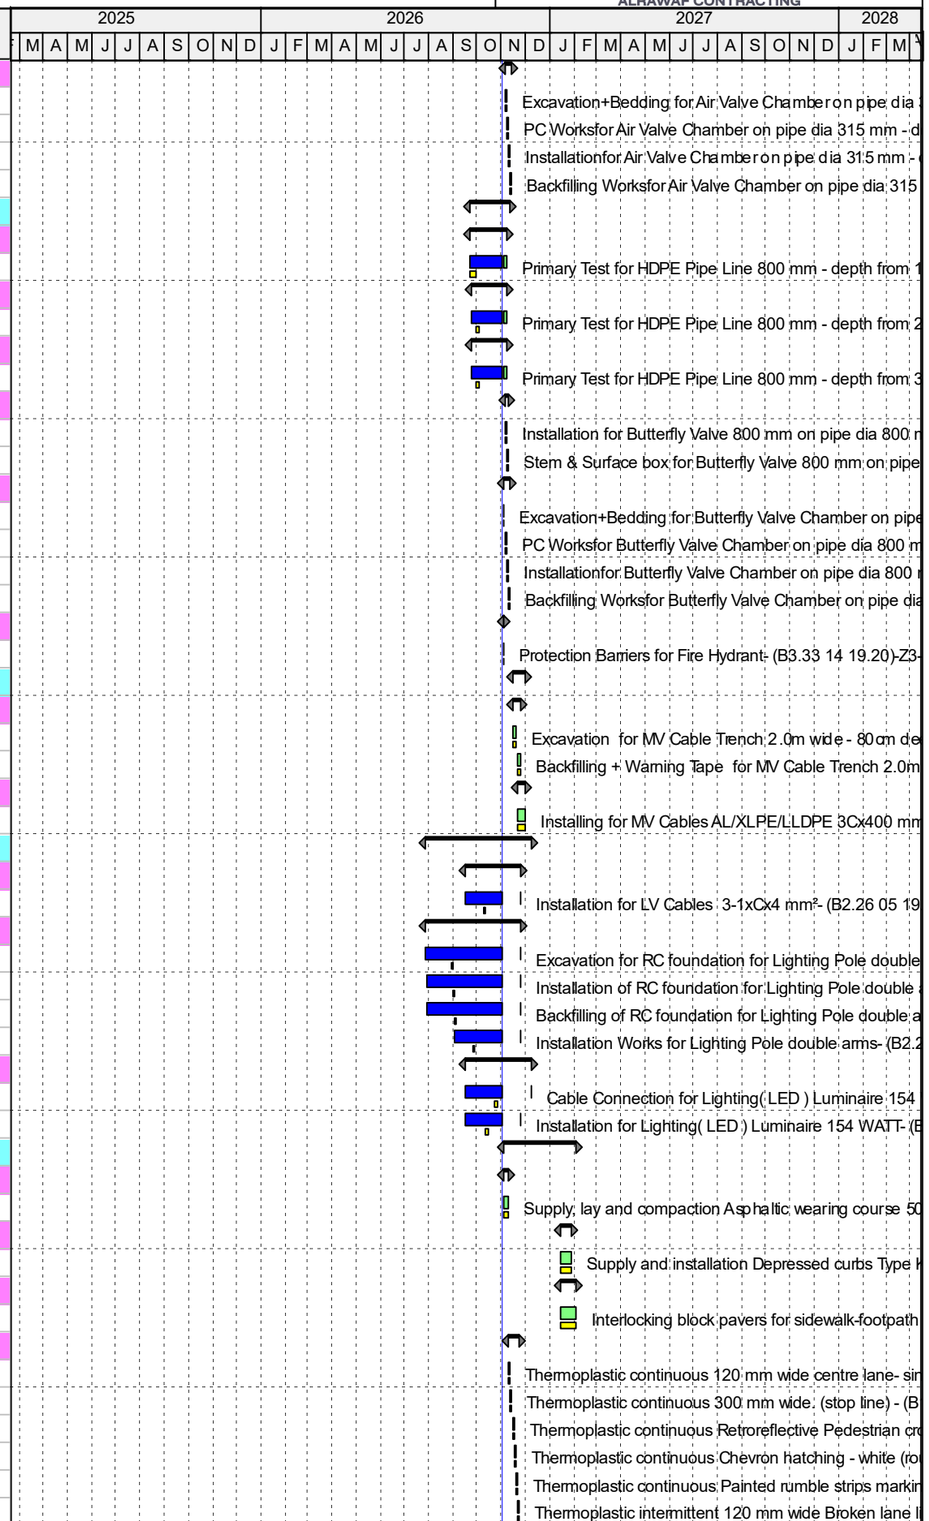


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R103-Landscape Works - LS	13	07-Jan-27	21-Jan-27	134	0	0	18,318
	JDH3-02-009-R103-(LS)-HDPE for Secondary Network	13	07-Jan-27	21-Jan-27	134	0	0	18,318
	Pipe line with Diam 90 mm PN10 - depth from 0 to 1.5 m- (B7.3	2	07-Jan-27	09-Jan-27	103	0	0	2,364
	Pipe linefor Diam 75 mm PN10 - depth from 0 to 1.5 m- (B7.33.	4	10-Jan-27	13-Jan-27	134	0	0	4,940
	Pipe linefor Diam 63 mm PN10 - depth from 0 to 1.5 m- (B7.33.	7	14-Jan-27	21-Jan-27	134	0	0	11,014
R104		109	18-Aug-26 A	23-Jan-27	346	2,052,168	1,765,692	2,845,002
	JDH3-02-009-R104-Storm Network - ST	15	03-Nov-26	19-Nov-26	400	27,156	0	27,156
	JDH3-02-009-R104-(ST)-MH Works (1200) mm diameter depth fr	11	03-Nov-26	15-Nov-26	400	17,919	0	17,919
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4	03-Nov-26	07-Nov-26	403	11,920	0	11,920
	Steel Coverfor MH 1200 mm - depth from 1.51 to 2.00 m- (B6.3	4	11-Nov-26	15-Nov-26	400	5,999	0	5,999
	JDH3-02-009-R104-(ST)-MH Works (2000) mm diameter depth fr	9	08-Nov-26	17-Nov-26	400	6,228	0	6,228
	Finishing, Benching, Testing Works for MH 2000 mm - depth fro	2	08-Nov-26	09-Nov-26	405	4,101	0	4,101
	Steel Coverfor MH 2000 mm - depth from 2.01 to 2.50 m- (B6.3	2	16-Nov-26	17-Nov-26	400	2,127	0	2,127
	JDH3-02-009-R104-(ST)-MH Works (1500) mm diameter depth fr	9	10-Nov-26	19-Nov-26	400	3,009	0	3,009
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	10-Nov-26	11-Nov-26	405	2,006	0	2,006
	Steel Coverfor MH 1500 mm - depth from 2.01 to 2.50 m- (B6.3	2	18-Nov-26	19-Nov-26	400	1,003	0	1,003
	JDH3-02-009-R104-Catch Basins (Storm Network) - ST	74	18-Aug-26 A	14-Nov-26	406	243,657	193,401	243,657
	JDH3-02-009-R104-(ST)-For Catch Basins (GRP) Pipes-300 mm	72	18-Aug-26 A	11-Nov-26	406	213,040	187,901	213,040
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	7	03-Nov-26	11-Nov-26	406	21,304	0	21,304
	Backfilling and warning tape Works for CB GRP Pipe Line 300 r	8	08-Sep-26 A	11-Nov-26	406	21,304	20,878	21,304
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 to	5	22-Aug-26 A	03-Nov-26	406	10,652	10,439	10,652
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	8	23-Aug-26 A	03-Nov-26	406	117,172	114,828	117,172
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	5	18-Aug-26 A	03-Nov-26	406	42,608	41,756	42,608
	JDH3-02-009-R104-(ST)-For Catch Basins (GRP) Pipes-400 mm	40	18-Aug-26 A	14-Nov-26	406	6,236	5,500	6,236
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	2	11-Nov-26	14-Nov-26	406	624	0	624
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 to	2	22-Aug-26 A	11-Nov-26	406	312	306	312
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	2	18-Aug-26 A	11-Nov-26	406	1,247	1,222	1,247
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 n	2	23-Aug-26 A	11-Nov-26	406	3,430	3,361	3,430
	Backfilling and warning tape Works for CB GRP Pipe Line 400 r	2	08-Sep-26 A	14-Nov-26	406	624	611	624
	JDH3-02-009-R104-(ST)-Single Catch Basin Works	8	03-Nov-26	11-Nov-26	407	10,684	0	10,684
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4	03-Nov-26	07-Nov-26	407	7,123	0	7,123
	Steel Coverfor single Catch Basin- (B6.33 05 39.30)-Z4-R104-S	4	08-Nov-26	11-Nov-26	407	3,561	0	3,561
	JDH3-02-009-R104-(ST)-Double Catch Basin Works	4	03-Nov-26	07-Nov-26	161	13,697	0	13,697
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	161	9,131	0	9,131
	Steel Coverfor double Catch Basin- (B6.33 05 39.31)-Z4-R104-S	2	05-Nov-26	07-Nov-26	161	4,566	0	4,566
	JDH3-02-009-R104-TSE Network - TSE	51	15-Sep-26 A	14-Nov-26	405	111,217	2,153	111,217
	JDH3-02-009-R104-(TSE)-Butterfly Valve-300 mm on pipe dia (31	4	03-Nov-26	07-Nov-26	411	32,260	0	32,260
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B4	2	03-Nov-26	04-Nov-26	411	29,034	0	29,034
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	05-Nov-26	07-Nov-26	411	3,226	0	3,226
	JDH3-02-009-R104-(TSE)-Wash-Out Valve-100 mm on pipe dia (3	4	03-Nov-26	07-Nov-26	335	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2	03-Nov-26	04-Nov-26	335	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2	05-Nov-26	07-Nov-26	335	1,613	0	1,613
	JDH3-02-009-R104-(TSE)-Valve Chamber on 315 mm dia pipelin	49	15-Sep-26 A	11-Nov-26	405	28,709	2,153	28,709
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	05-Nov-26	07-Nov-26	405	2,871	0	2,871
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	08-Nov-26	09-Nov-26	405	15,790	0	15,790
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	10-Nov-26	11-Nov-26	405	5,742	0	5,742
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2	15-Sep-26 A	04-Nov-26	405	4,306	2,153	4,306
	JDH3-02-009-R104-(TSE)-Wash-Out Chamber on 315 mm dia pi	8	03-Nov-26	11-Nov-26	333	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2	03-Nov-26	04-Nov-26	333	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2	05-Nov-26	07-Nov-26	333	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2	08-Nov-26	09-Nov-26	333	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - c	2	10-Nov-26	11-Nov-26	333	4,177	0	4,177
	JDH3-02-009-R104-(TSE)-Air Valve-50 mm on pipe dia (110) mm	4	05-Nov-26	09-Nov-26	409	6,016	0	6,016

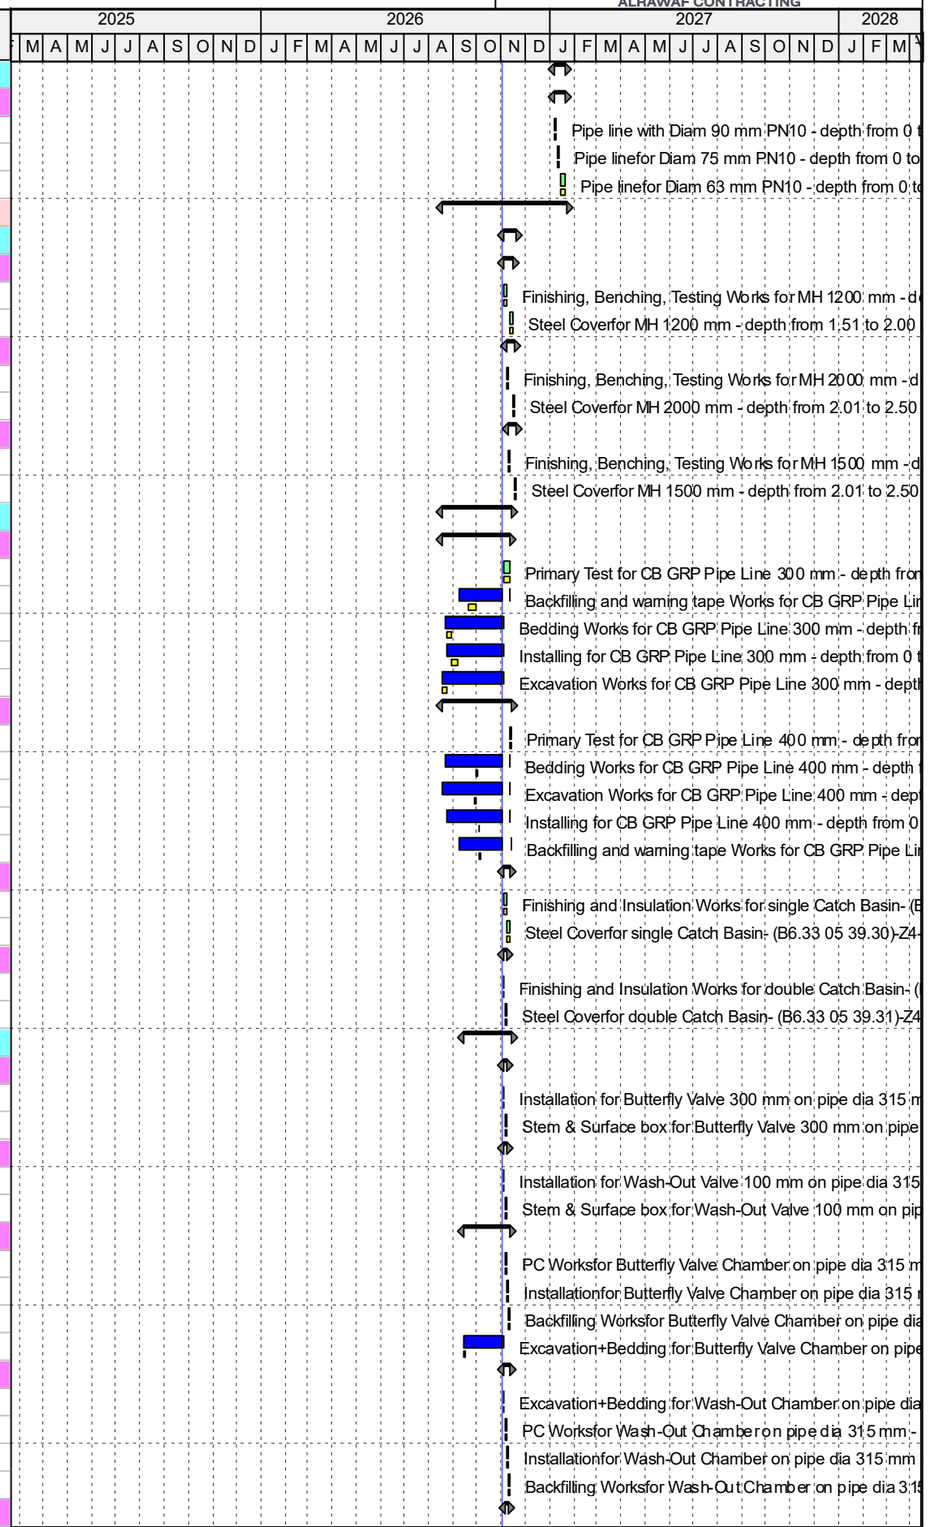


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation for Air Valve 50 mm on pipe dia 110 mm- (B4.33 14	2	05-Nov-26	07-Nov-26	409	5,415	0	5,415
	Stem & Surface box for Air Valve 50 mm on pipe dia 110 mm- (I	2	08-Nov-26	09-Nov-26	409	602	0	602
	JDH3-02-009-R104-(TSE)-Air Valve Chamber on 110 mm dia pip	10	03-Nov-26	14-Nov-26	405	7,218	0	7,218
	Excavation+Bedding for Air Valve Chamber on pipe dia 110 mm	2	03-Nov-26	04-Nov-26	407	1,083	0	1,083
	PC Worksfor Air Valve Chamber on pipe dia 110 mm - depth fro	2	05-Nov-26	07-Nov-26	407	722	0	722
	Installationfor Air Valve Chamber on pipe dia 110 mm - depth fr	2	08-Nov-26	09-Nov-26	407	3,970	0	3,970
	Backfilling Worksfor Air Valve Chamber on pipe dia 110 mm - de	2	12-Nov-26	14-Nov-26	405	1,444	0	1,444
	JDH3-02-009-R104-Potable Water Network - WT	52	22-Sep-26 A	23-Nov-26	398	256,469	2,129	256,469
	JDH3-02-009-R104-(WT)-Butterfly Valve-400 mm on pipe dia (40	4	03-Nov-26	07-Nov-26	407	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2	03-Nov-26	04-Nov-26	407	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2	05-Nov-26	07-Nov-26	407	7,822	0	7,822
	JDH3-02-009-R104-(WT)-Valve Chamber on 400 mm dia pipeline	50	22-Sep-26 A	21-Nov-26	398	43,007	2,129	43,007
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	04-Nov-26	07-Nov-26	398	4,301	0	4,301
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	07-Nov-26	09-Nov-26	398	23,654	0	23,654
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	18-Nov-26	21-Nov-26	398	8,601	0	8,601
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	22-Sep-26 A	04-Nov-26	398	6,451	2,129	6,451
	JDH3-02-009-R104-(WT)-Fire Hydrant	12	04-Nov-26	18-Nov-26	398	78,167	0	78,167
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	04-Nov-26	07-Nov-26	400	7,817	0	7,817
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-W	2	09-Nov-26	11-Nov-26	398	15,633	0	15,633
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-WT	2	11-Nov-26	14-Nov-26	398	23,450	0	23,450
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-WT	2	14-Nov-26	16-Nov-26	398	27,358	0	27,358
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z4-R104-V	2	16-Nov-26	18-Nov-26	398	3,908	0	3,908
	JDH3-02-009-R104-(WT)-Wash-Out Valve-100 mm on pipe dia (2	4	04-Nov-26	09-Nov-26	410	15,346	0	15,346
	Installation for Wash-Out Valve 100 mm on pipe dia 225 mm- (E	2	04-Nov-26	07-Nov-26	410	13,811	0	13,811
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 2:	2	07-Nov-26	09-Nov-26	410	1,535	0	1,535
	JDH3-02-009-R104-(WT)-Wash-Out Chamber on 225 mm dia pip	17	03-Nov-26	23-Nov-26	398	41,727	0	41,727
	Excavation+Bedding for Wash-Out Chamber on pipe dia 225 m	2	03-Nov-26	04-Nov-26	407	6,259	0	6,259
	PC Worksfor Wash-Out Chamber on pipe dia 225 mm - depth fr	2	05-Nov-26	07-Nov-26	407	4,173	0	4,173
	Installationfor Wash-Out Chamber on pipe dia 225 mm - depth	2	08-Nov-26	09-Nov-26	407	22,950	0	22,950
	Backfilling Worksfor Wash-Out Chamber on pipe dia 225 mm - (	2	21-Nov-26	23-Nov-26	398	8,345	0	8,345
	JDH3-02-009-R104-Electrical Network - EL	4	12-Nov-26	16-Nov-26	333	77,785	0	77,785
	JDH3-02-009-R104-(EL)-MV cables AL/XLPE/LLDPE Unarmored	4	12-Nov-26	16-Nov-26	333	77,785	0	77,785
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	2	12-Nov-26	14-Nov-26	333	69,084	0	69,084
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	15-Nov-26	16-Nov-26	333	8,701	0	8,701
	JDH3-02-009-R104-Street Lighting Network -SL	24	17-Oct-26 A	26-Nov-26	340	229,999	17,728	229,999
	JDH3-02-009-R104-(SL)- LV Cables - Copper, 4Cx95 mm²,Cu/XLP	6	17-Nov-26	23-Nov-26	337	129,726	0	129,726
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	3	17-Nov-26	19-Nov-26	333	15,262	0	15,262
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.:	3	21-Nov-26	23-Nov-26	337	114,464	0	114,464
	JDH3-02-009-R104-(SL)-Lighting Pole with double arms 16 m he	24	17-Oct-26 A	26-Nov-26	340	93,566	17,728	93,566
	Backfilling of RC foundation for Lighting Pole double arms- (B2.:	2	21-Nov-26	22-Nov-26	340	9,849	0	9,849
	Installation Works for Lighting Pole double arms- (B2.26 56 19.(	4	23-Nov-26	26-Nov-26	340	64,019	0	64,019
	Excavation for RC foundation for Lighting Pole double arms- (B:	2	17-Oct-26 A	19-Nov-26	340	9,849	8,864	9,849
	Installation of RC foundation for Lighting Pole double arms- (B2	2	20-Oct-26 A	19-Nov-26	340	9,849	8,864	9,849
	JDH3-02-009-R104-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	5	21-Nov-26	25-Nov-26	333	6,707	0	6,707
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	21-Nov-26	25-Nov-26	333	6,707	0	6,707
	JDH3-02-009-R104-Road Works - RD	91	08-Sep-26 A	23-Jan-27	310	1,105,886	1,550,281	1,898,720
	JDH3-02-009-R104-(RD)-Aggregate Base Course	2	08-Sep-26 A	03-Nov-26	342	313,052	281,747	313,052
	Supply, lay and compaction Aggregate base course compacted	2	08-Sep-26 A	03-Nov-26	342	313,052	281,747	313,052
	JDH3-02-009-R104-(RD)-Bituminous base course 150 mm Two L	89	10-Sep-26 A	23-Jan-27	310	792,834	1,268,534	1,585,668
	Supply, lay and Asphaltic base course including tack Coat (RC2)	7	24-Sep-26 A	23-Jan-27	310	0	554,984	792,834
	Supply, lay and Asphaltic base course including Prime Coat (MC	2	10-Sep-26 A	03-Nov-26	342	792,834	713,550	792,834
R101		106	07-Jul-26 A	26-Nov-26	395	2,692,062	1,584,408	2,721,133
	JDH3-02-009-R101-TSE Network - TSE	105	07-Jul-26 A	25-Nov-26	396	344,679	63,009	344,679

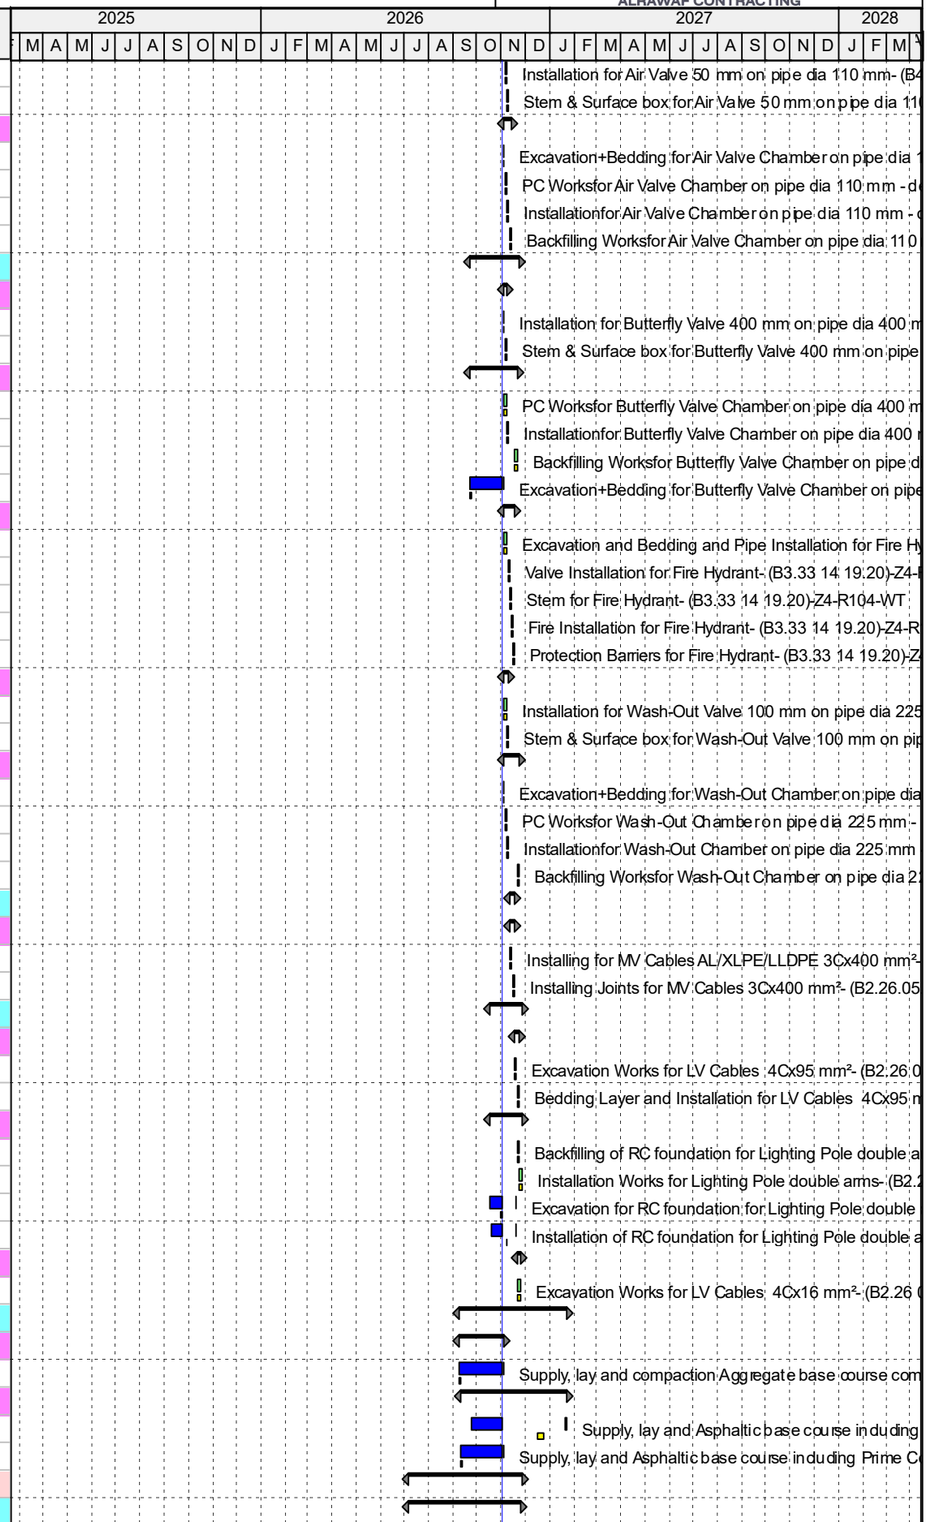


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R101-(TSE)-HDPE Pipes-400 mm diameter depth f	2	03-Nov-26	04-Nov-26	413	42,219	0	42,219
	Primary Test for HDPE Pipe Line 400 mm - depth from 1.51 to 2	2	03-Nov-26	04-Nov-26	413	42,219	0	42,219
	JDH3-02-009-R101-(TSE)-HDPE Pipes-400 mm diameter depth f	90	07-Jul-26 A	07-Nov-26	411	9,426	2,545	9,426
	Primary Test for HDPE Pipe Line 400 mm - depth from 2.51 to 3	2	05-Nov-26	07-Nov-26	411	943	0	943
	Bedding Works for HDPE Pipe Line 400 mm - depth from 2.51 t	2	09-Jul-26 A	04-Nov-26	411	471	141	471
	Excavation Works for HDPE Pipe Line 400 mm - depth from 2.5	2	07-Jul-26 A	04-Nov-26	411	1,885	566	1,885
	Installing for HDPE Pipe Line 400 mm - depth from 2.51 to 3.5	2	11-Jul-26 A	04-Nov-26	411	5,184	1,555	5,184
	Backfilling and warning tape Works for HDPE Pipe Line 400 mm	2	25-Jul-26 A	07-Nov-26	411	943	283	943
	JDH3-02-009-R101-(TSE)-Butterfly Valve-400 mm on pipe dia (31	50	15-Sep-26 A	14-Nov-26	396	130,370	46,933	130,370
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2	11-Nov-26	14-Nov-26	396	13,037	0	13,037
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2	15-Sep-26 A	04-Nov-26	402	117,333	46,933	117,333
	JDH3-02-009-R101-(TSE)-Wash-Out Valve-100 mm on pipe dia (4	10	04-Nov-26	16-Nov-26	396	33,818	0	33,818
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2	04-Nov-26	07-Nov-26	402	30,436	0	30,436
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 4	2	14-Nov-26	16-Nov-26	396	3,382	0	3,382
	JDH3-02-009-R101-(TSE)-Air Valve-65 mm on pipe dia (400) mm	10	07-Nov-26	18-Nov-26	396	7,790	0	7,790
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33 14	2	07-Nov-26	09-Nov-26	402	7,011	0	7,011
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (I	2	16-Nov-26	18-Nov-26	396	779	0	779
	JDH3-02-009-R101-(TSE)-Valve Chamber on 400 mm dia pipelin	74	25-Aug-26 A	21-Nov-26	396	71,973	13,531	71,973
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	18-Nov-26	21-Nov-26	396	14,395	0	14,395
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	16-Sep-26 A	04-Nov-26	407	39,585	6,334	39,585
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	01-Sep-26 A	04-Nov-26	408	7,197	2,879	7,197
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	25-Aug-26 A	04-Nov-26	396	10,796	4,318	10,796
	JDH3-02-009-R101-(TSE)-Wash-Out Chamber on 400 mm dia pi	16	04-Nov-26	23-Nov-26	396	41,949	0	41,949
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2	04-Nov-26	07-Nov-26	396	6,292	0	6,292
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2	07-Nov-26	09-Nov-26	396	4,195	0	4,195
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2	09-Nov-26	11-Nov-26	396	23,072	0	23,072
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm - c	2	21-Nov-26	23-Nov-26	396	8,390	0	8,390
	JDH3-02-009-R101-(TSE)-Air Valve Chamber on 400 mm dia pip	16	07-Nov-26	25-Nov-26	396	7,134	0	7,134
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2	07-Nov-26	09-Nov-26	404	1,070	0	1,070
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2	09-Nov-26	11-Nov-26	404	713	0	713
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2	11-Nov-26	14-Nov-26	404	3,924	0	3,924
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2	23-Nov-26	25-Nov-26	396	1,427	0	1,427
	JDH3-02-009-R101-Potable Water Network - WT	50	22-Sep-26 A	23-Nov-26	397	652,517	39,280	652,517
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	4	03-Nov-26	07-Nov-26	411	27,753	0	27,753
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	4	03-Nov-26	07-Nov-26	411	27,753	0	27,753
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	3	03-Nov-26	05-Nov-26	412	36,144	0	36,144
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	3	03-Nov-26	05-Nov-26	412	36,144	0	36,144
	JDH3-02-009-R101-(WT)-HDPE Pipes-800 mm diameter depth fr	3	03-Nov-26	05-Nov-26	400	59,286	0	59,286
	Primary Test for HDPE Pipe Line 800 mm - depth from 4.51 to 5	3	03-Nov-26	05-Nov-26	400	59,286	0	59,286
	JDH3-02-009-R101-(WT)-Butterfly Valve-400 mm on pipe dia (40	4	03-Nov-26	07-Nov-26	397	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B3	2	03-Nov-26	04-Nov-26	397	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2	05-Nov-26	07-Nov-26	397	7,822	0	7,822
	JDH3-02-009-R101-(WT)-Butterfly Valve-800 mm on pipe dia (80	4	05-Nov-26	09-Nov-26	397	197,263	0	197,263
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	05-Nov-26	07-Nov-26	397	177,537	0	177,537
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 800	2	08-Nov-26	09-Nov-26	397	19,726	0	19,726
	JDH3-02-009-R101-(WT)-Wash-Out Valve-200 mm on pipe dia (8	2	10-Nov-26	11-Nov-26	397	2,736	0	2,736
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 8	2	10-Nov-26	11-Nov-26	397	2,736	0	2,736
	JDH3-02-009-R101-(WT)-Air Valve-110 mm on pipe dia (800) mm	10	03-Nov-26	14-Nov-26	397	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 14	2	03-Nov-26	04-Nov-26	403	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2	12-Nov-26	14-Nov-26	397	2,501	0	2,501
	JDH3-02-009-R101-(WT)-Valve Chamber on 400 mm dia pipeline	44	27-Sep-26 A	16-Nov-26	397	43,007	3,226	43,007
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	07-Nov-26	08-Nov-26	400	4,301	0	4,301
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	09-Nov-26	10-Nov-26	400	23,654	0	23,654

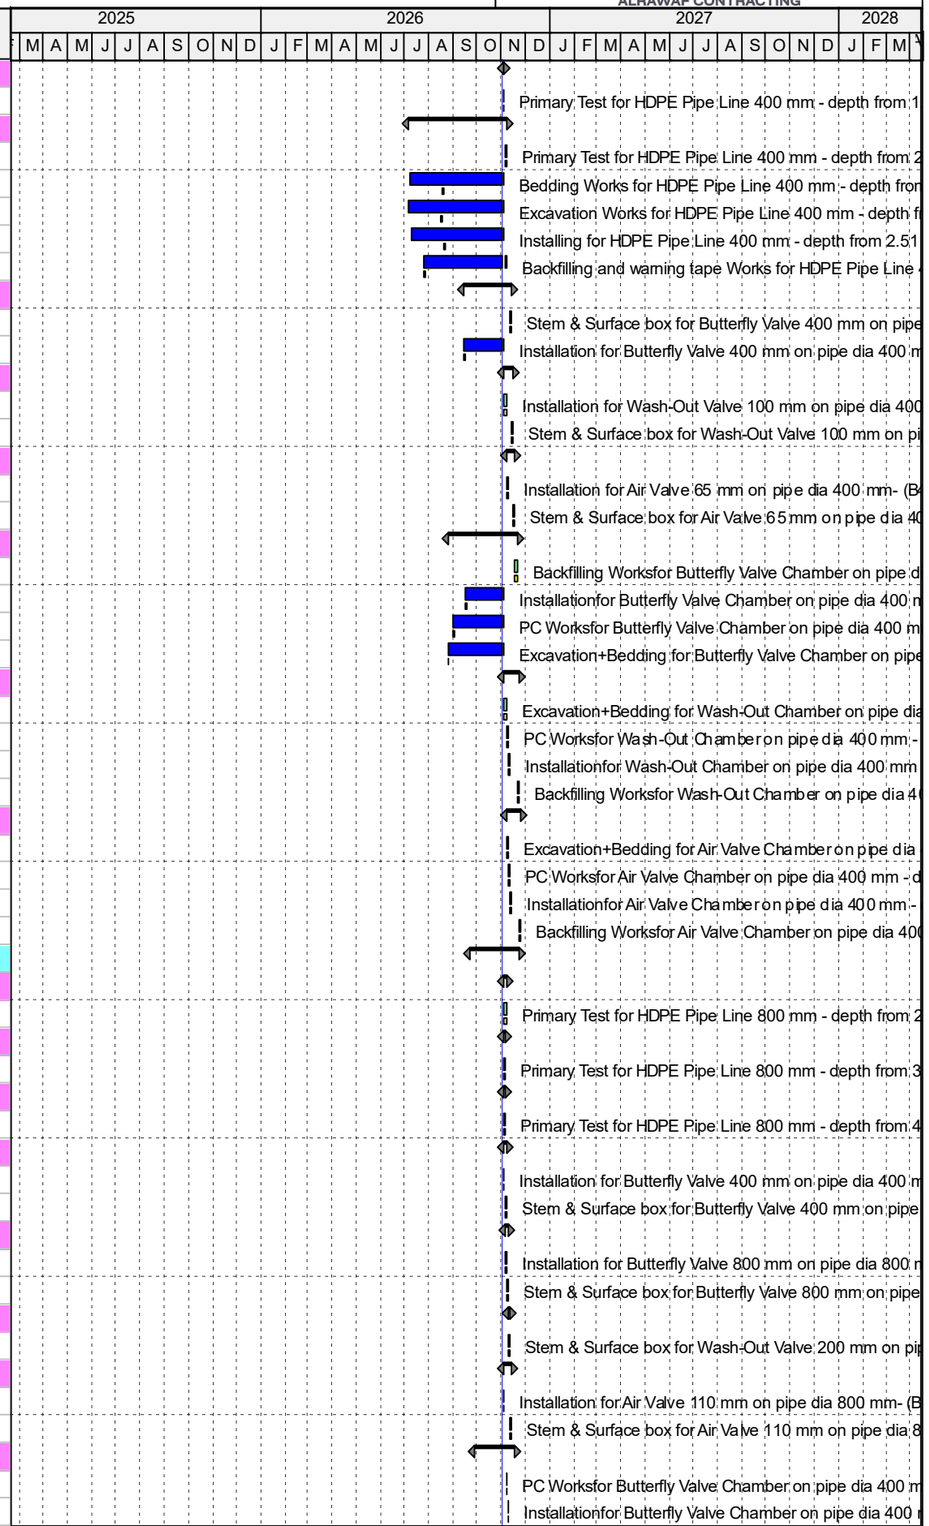


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 m	2	15-Nov-26	16-Nov-26	397	8,601	0	8,601
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	27-Sep-26 A	05-Nov-26	400	6,451	3,226	6,451
	JDH3-02-009-R101-(WT)-Valve Chamber on 800 mm dia pipeline	12	05-Nov-26	18-Nov-26	397	81,589	0	81,589
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	05-Nov-26	07-Nov-26	403	9,599	0	9,599
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	08-Nov-26	09-Nov-26	403	52,793	0	52,793
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	17-Nov-26	18-Nov-26	397	19,197	0	19,197
	JDH3-02-009-R101-(WT)-Wash-Out Chamber on 800 mm dia pip	2	19-Nov-26	21-Nov-26	397	6,427	0	6,427
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm - c	2	19-Nov-26	21-Nov-26	397	6,427	0	6,427
	JDH3-02-009-R101-(WT)-Air Valve Chamber on 800 mm dia pipe	16	05-Nov-26	23-Nov-26	397	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2	05-Nov-26	07-Nov-26	401	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2	08-Nov-26	09-Nov-26	405	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2	10-Nov-26	11-Nov-26	405	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2	22-Nov-26	23-Nov-26	397	1,428	0	1,428
	JDH3-02-009-R101-(WT)-Fire Hydrant	30	22-Sep-26 A	09-Nov-26	401	87,937	36,054	87,937
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-W	2	08-Nov-26	09-Nov-26	401	4,397	0	4,397
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-WT	2	27-Sep-26 A	07-Nov-26	401	30,778	12,311	30,778
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-WT	2	26-Sep-26 A	07-Nov-26	401	26,381	10,552	26,381
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	22-Sep-26 A	07-Nov-26	401	8,794	4,397	8,794
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z1-R101-W	2	24-Sep-26 A	07-Nov-26	401	17,587	8,794	17,587
	JDH3-02-009-R101-Electrical Network - EL	26	11-Aug-26 A	03-Nov-26	310	1,507,917	1,432,521	1,507,917
	JDH3-02-009-R101-(EL)-MV cable trench size 3.0m wide and 80	8	15-Aug-26 A	03-Nov-26	310	7,566	7,188	7,566
	Backfilling + Warning Tape for MV Cable Trench 3.0m wide - 80	8	15-Aug-26 A	03-Nov-26	310	7,566	7,188	7,566
	JDH3-02-009-R101-(EL)-MV cables AL/XLPE/LLDPE Unarmored	16	11-Aug-26 A	03-Nov-26	310	1,500,351	1,425,333	1,500,351
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	14	11-Aug-26 A	03-Nov-26	310	1,431,061	1,359,508	1,431,061
	Installing Joints for MV Cables 3Cx400 mm²- (B2.26.05.13.16.0:	2	13-Aug-26 A	03-Nov-26	310	66,710	63,374	66,710
	Termination for MV Cables 3Cx400 mm²- (B2.26.05.13.16.03)-Z	2	22-Aug-26 A	03-Nov-26	310	2,580	2,451	2,580
	JDH3-02-009-R101-Street Lighting Network -SL	53	22-Sep-26 A	26-Nov-26	310	169,334	49,598	198,404
	JDH3-02-009-R101-(SL)-Lighting Unit Substation 33/0.4 KV, 500	10	03-Nov-26	15-Nov-26	310	47,612	0	47,612
	Installation for Unit substation 33/0.4 K V, 500 kVA- (B2.26 11 1	2	03-Nov-26	05-Nov-26	314	40,810	0	40,810
	Cables Connection for Unit substation 33/0.4 K V, 500 kVA- (B2	2	05-Nov-26	08-Nov-26	314	3,401	0	3,401
	Earthing + Primary Test for Unit substation 33/0.4 K V, 500 kVA-	2	12-Nov-26	15-Nov-26	310	3,401	0	3,401
	JDH3-02-009-R101-(SL)- LV Cables - Copper, 3x1Cx50 mm²,Cu/X	2	08-Nov-26	10-Nov-26	314	1,520	0	1,520
	Installation for LV Cables 3x1Cx50 mm²- (B2.26 05 19.03)-Z1-F	2	08-Nov-26	10-Nov-26	314	1,520	0	1,520
	JDH3-02-009-R101-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	49	26-Sep-26 A	22-Nov-26	310	55,164	46,210	63,958
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	4	05-Nov-26	10-Nov-26	316	799	0	3,198
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	4	17-Nov-26	22-Nov-26	310	0	0	6,396
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.:	4	27-Sep-26 A	05-Nov-26	316	47,969	40,773	47,969
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	26-Sep-26 A	05-Nov-26	316	6,396	5,436	6,396
	JDH3-02-009-R101-(SL)-Lighting Pole with double arms 16 m he	3	22-Sep-26 A	17-Nov-26	310	1,329	3,389	3,987
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3	22-Sep-26 A	17-Nov-26	310	1,329	3,389	3,987
	JDH3-02-009-R101-(SL)-Earthing System for Streetlighting feed	2	22-Nov-26	24-Nov-26	310	0	0	852
	Supply, construct, connect and test earthing pits for Street Light	2	22-Nov-26	24-Nov-26	310	0	0	852
	JDH3-02-009-R101-(SL)- LV Distribution Panel Main: 100A, MCC	6	03-Nov-26	10-Nov-26	322	3,674	0	18,369
	Levelling for Street Lighting panels - (B2.26 27 33.01)-Z1-R101-	2	03-Nov-26	05-Nov-26	322	1,837	0	1,837
	lean Concrete for Street Lighting panels - (B2.26 27 33.01)-Z1-F	2	05-Nov-26	08-Nov-26	322	1,837	0	3,674
	Installing for Street Lighting panels - (B2.26 27 33.01)-Z1-R101-	2	08-Nov-26	10-Nov-26	322	0	0	12,858
	JDH3-02-009-R101-(SL)-KWH meter mounting frame	2	24-Nov-26	26-Nov-26	310	0	0	2,072
	Installation for KWH meter - (B2.26 24 16.02)-Z1-R101-SL	2	24-Nov-26	26-Nov-26	310	0	0	2,072
	JDH3-02-009-R101-(SL)- LV Cables - Aluminium, 4Cx185mm²,AL	8	03-Nov-26	12-Nov-26	310	1,212	0	1,212
	Excavation Works for LV Cables 4Cx185 mm²- (B2.26 05 19.01	2	03-Nov-26	05-Nov-26	310	121	0	121
	Bedding Layer and Installation for LV Cables 4Cx185 mm²- (B2	2	05-Nov-26	08-Nov-26	310	909	0	909
	Testing and Commissioning for LV Cables 4Cx185 mm²- (B2.2(	2	08-Nov-26	10-Nov-26	310	61	0	61
	Backfilling, Warning Tape Works for LV Cables 4Cx185 mm²- (B	2	10-Nov-26	12-Nov-26	310	121	0	121

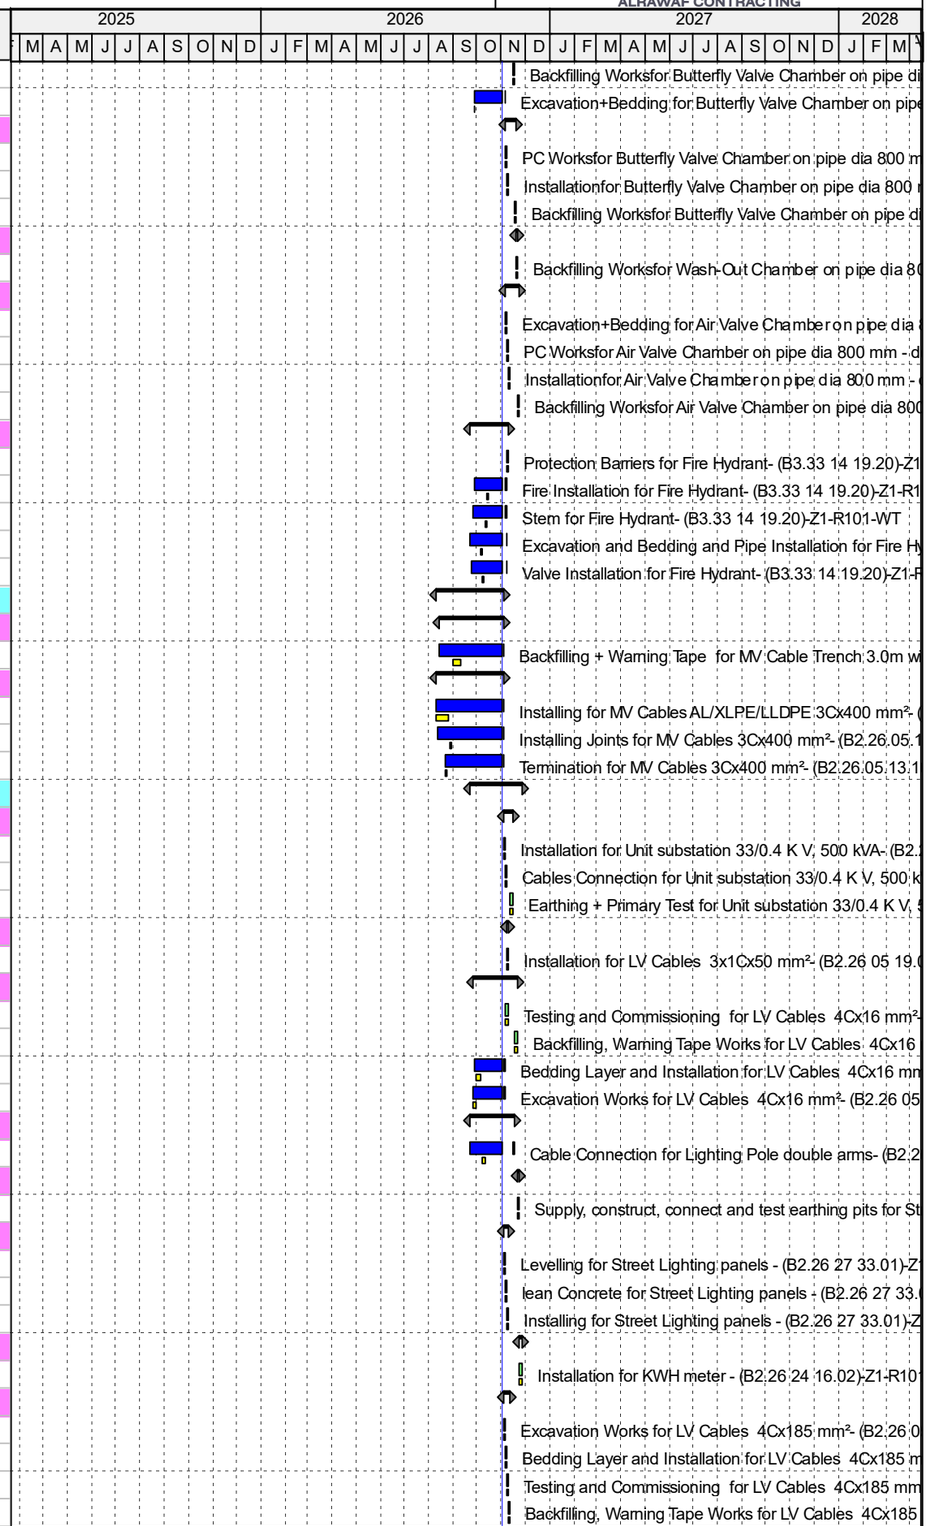


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R101-(SL)-RMU 33 KV	12	03-Nov-26	17-Nov-26	310	58,823	0	58,823
	Installation for RMU 33 KV- (B2.26 11 16.02)-Z1-R101-SL	2	03-Nov-26	05-Nov-26	316	50,420	0	50,420
	Cables Connection for RMU 33 KV- (B2.26 11 16.02)-Z1-R101-S	2	05-Nov-26	08-Nov-26	316	4,202	0	4,202
	Earthing + Primary Test for RMU 33 KV- (B2.26 11 16.02)-Z1-R1	2	15-Nov-26	17-Nov-26	310	4,202	0	4,202
	JDH3-02-009-R101-Catch Basins (Storm Network) - ST	5	03-Nov-26	08-Nov-26	381	17,616	0	17,616
	JDH3-02-009-R101-(ST)-Single Catch Basin Works	5	03-Nov-26	08-Nov-26	381	9,315	0	9,315
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5	03-Nov-26	08-Nov-26	381	9,315	0	9,315
	JDH3-02-009-R101-(ST)-Double Catch Basin Works	2	03-Nov-26	04-Nov-26	384	8,301	0	8,301
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	384	8,301	0	8,301
R102		60	01-Sep-26 A	08-Dec-26	384	1,445,169	194,982	1,445,169
	JDH3-02-009-R102-Catch Basins (Storm Network) - ST	5	03-Nov-26	08-Nov-26	376	21,758	0	21,758
	JDH3-02-009-R102-(ST)-Single Catch Basin Works	5	03-Nov-26	08-Nov-26	376	10,136	0	10,136
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	5	03-Nov-26	08-Nov-26	376	10,136	0	10,136
	JDH3-02-009-R102-(ST)-Double Catch Basin Works	2	03-Nov-26	04-Nov-26	379	11,622	0	11,622
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	2	03-Nov-26	04-Nov-26	379	11,622	0	11,622
	JDH3-02-009-R102-TSE Network - TSE	10	03-Nov-26	14-Nov-26	405	226,152	0	226,152
	JDH3-02-009-R102-(TSE)-Butterfly Valve-400 mm on pipe dia (31	4	05-Nov-26	09-Nov-26	407	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2	05-Nov-26	07-Nov-26	407	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 400	2	08-Nov-26	09-Nov-26	407	7,822	0	7,822
	JDH3-02-009-R102-(TSE)-Wash-Out Valve-100 mm on pipe dia (3	4	03-Nov-26	07-Nov-26	411	16,127	0	16,127
	Installation for Wash-Out Valve 100 mm on pipe dia 315 mm- (E	2	03-Nov-26	04-Nov-26	411	14,515	0	14,515
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 3	2	05-Nov-26	07-Nov-26	411	1,613	0	1,613
	JDH3-02-009-R102-(TSE)-Wash-Out Chamber on 315 mm dia pi	8	03-Nov-26	11-Nov-26	407	20,886	0	20,886
	Excavation+Bedding for Wash-Out Chamber on pipe dia 315 m	2	03-Nov-26	04-Nov-26	407	3,133	0	3,133
	PC Worksfor Wash-Out Chamber on pipe dia 315 mm - depth fr	2	05-Nov-26	07-Nov-26	407	2,089	0	2,089
	Installationfor Wash-Out Chamber on pipe dia 315 mm - depth	2	08-Nov-26	09-Nov-26	407	11,487	0	11,487
	Backfilling Worksfor Wash-Out Chamber on pipe dia 315 mm - (	2	10-Nov-26	11-Nov-26	407	4,177	0	4,177
	JDH3-02-009-R102-(TSE)-Wash-Out Valve-100 mm on pipe dia (4	4	03-Nov-26	07-Nov-26	407	16,909	0	16,909
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2	03-Nov-26	04-Nov-26	407	15,218	0	15,218
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 40	2	05-Nov-26	07-Nov-26	407	1,691	0	1,691
	JDH3-02-009-R102-(TSE)-Air Valve-65 mm on pipe dia (400) mm	4	05-Nov-26	09-Nov-26	407	15,581	0	15,581
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33 14	2	05-Nov-26	07-Nov-26	407	14,023	0	14,023
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (I	2	08-Nov-26	09-Nov-26	407	1,558	0	1,558
	JDH3-02-009-R102-(TSE)-Valve Chamber on 400 mm dia pipelin	8	03-Nov-26	11-Nov-26	407	43,184	0	43,184
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	03-Nov-26	04-Nov-26	407	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	05-Nov-26	07-Nov-26	407	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	08-Nov-26	09-Nov-26	407	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 mi	2	10-Nov-26	11-Nov-26	407	8,637	0	8,637
	JDH3-02-009-R102-(TSE)-Wash-Out Chamber on 400 mm dia pi	8	03-Nov-26	11-Nov-26	407	20,974	0	20,974
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2	03-Nov-26	04-Nov-26	360	3,146	0	3,146
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2	05-Nov-26	07-Nov-26	407	2,097	0	2,097
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2	08-Nov-26	09-Nov-26	407	11,536	0	11,536
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm - (	2	10-Nov-26	11-Nov-26	407	4,195	0	4,195
	JDH3-02-009-R102-(TSE)-Air Valve Chamber on 400 mm dia pip	8	05-Nov-26	14-Nov-26	405	14,269	0	14,269
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2	05-Nov-26	07-Nov-26	360	2,140	0	2,140
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2	08-Nov-26	09-Nov-26	405	1,427	0	1,427
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2	10-Nov-26	11-Nov-26	405	7,848	0	7,848
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2	12-Nov-26	14-Nov-26	405	2,854	0	2,854
	JDH3-02-009-R102-Potable Water Network - WT	24	03-Nov-26	30-Nov-26	391	371,159	0	371,159
	JDH3-02-009-R102-(WT)-Wash-Out Valve-200 mm on pipe dia (8	4	05-Nov-26	09-Nov-26	407	27,358	0	27,358
	Installation for Wash-Out Valve 200 mm on pipe dia 800 mm- (E	2	05-Nov-26	07-Nov-26	407	24,622	0	24,622
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 80	2	08-Nov-26	09-Nov-26	407	2,736	0	2,736
	JDH3-02-009-R102-(WT)-Wash-Out Chamber on 800 mm dia pip	8	03-Nov-26	11-Nov-26	405	32,136	0	32,136

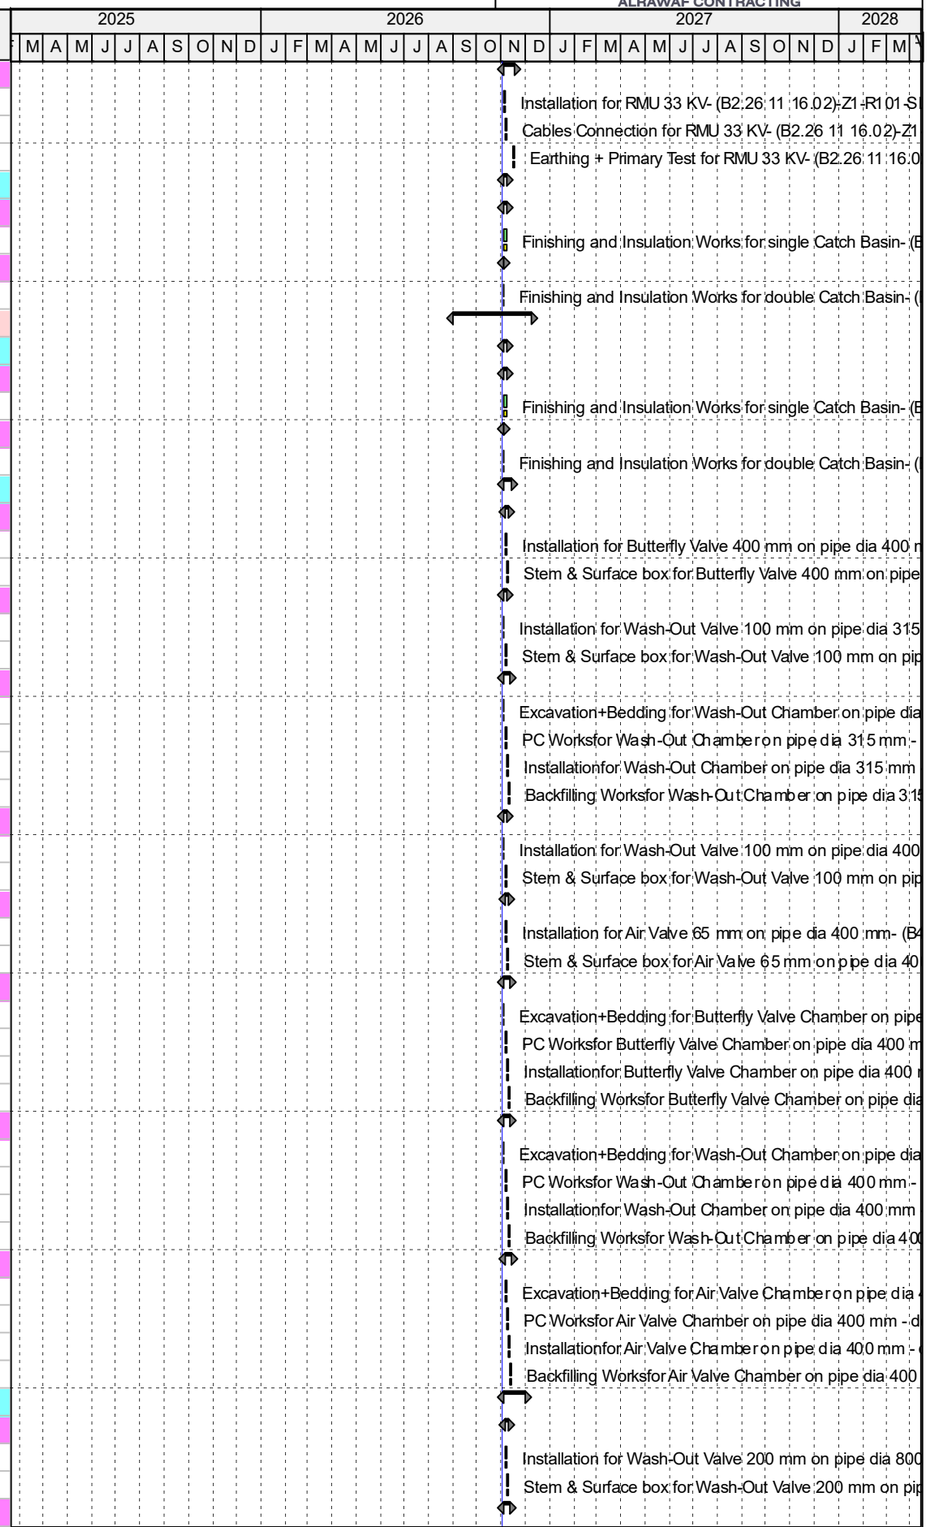


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Wash-Out Chamber on pipe dia 800 m	2	03-Nov-26	04-Nov-26	405	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 800 mm - depth fr	2	05-Nov-26	07-Nov-26	405	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 800 mm - depth	2	08-Nov-26	09-Nov-26	405	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm - c	2	10-Nov-26	11-Nov-26	405	6,427	0	6,427
	JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr	2	03-Nov-26	04-Nov-26	340	1,257	0	1,257
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	2	03-Nov-26	04-Nov-26	340	1,257	0	1,257
	JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr	9	21-Nov-26	30-Nov-26	391	3,141	0	3,141
	Primary Test for HDPE Pipe Line 800 mm - depth from 4.51 to 5	9	21-Nov-26	30-Nov-26	391	3,141	0	3,141
	JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr	9	10-Nov-26	19-Nov-26	391	23,070	0	23,070
	Primary Test for HDPE Pipe Line 800 mm - depth from 2.51 to 3	9	10-Nov-26	19-Nov-26	391	23,070	0	23,070
	JDH3-02-009-R102-(WT)-HDPE Pipes-800 mm diameter depth fr	2	08-Nov-26	09-Nov-26	391	71,275	0	71,275
	Primary Test for HDPE Pipe Line 800 mm - depth from 3.51 to 4	2	08-Nov-26	09-Nov-26	391	71,275	0	71,275
	JDH3-02-009-R102-(WT)-Butterfly Valve-300 mm on pipe dia (315	14	08-Nov-26	23-Nov-26	340	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2	08-Nov-26	09-Nov-26	350	14,517	0	14,517
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 315	2	22-Nov-26	23-Nov-26	340	1,613	0	1,613
	JDH3-02-009-R102-(WT)-Butterfly Valve-800 mm on pipe dia (80	2	10-Nov-26	11-Nov-26	350	59,179	0	59,179
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	10-Nov-26	11-Nov-26	350	59,179	0	59,179
	JDH3-02-009-R102-(WT)-Air Valve-110 mm on pipe dia (800) mm	4	08-Nov-26	11-Nov-26	407	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 14	2	08-Nov-26	09-Nov-26	407	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2	10-Nov-26	11-Nov-26	407	2,501	0	2,501
	JDH3-02-009-R102-(WT)-Valve Chamber on 315 mm dia pipeline	6	05-Nov-26	11-Nov-26	352	11,469	0	11,469
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2	05-Nov-26	07-Nov-26	340	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	08-Nov-26	09-Nov-26	352	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	10-Nov-26	11-Nov-26	352	7,885	0	7,885
	JDH3-02-009-R102-(WT)-Valve Chamber on 800 mm dia pipeline	6	08-Nov-26	14-Nov-26	352	25,597	0	25,597
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2	08-Nov-26	09-Nov-26	340	4,799	0	4,799
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	10-Nov-26	11-Nov-26	352	3,200	0	3,200
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	12-Nov-26	14-Nov-26	352	17,598	0	17,598
	JDH3-02-009-R102-(WT)-Air Valve Chamber on 800 mm dia pipe	8	05-Nov-26	14-Nov-26	405	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2	05-Nov-26	07-Nov-26	405	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2	08-Nov-26	09-Nov-26	405	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2	10-Nov-26	11-Nov-26	405	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2	12-Nov-26	14-Nov-26	405	1,428	0	1,428
	JDH3-02-009-R102-(WT)-Fire Hydrant	10	10-Nov-26	21-Nov-26	340	68,396	0	68,396
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	2	10-Nov-26	11-Nov-26	340	6,840	0	6,840
	Valve Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-W	2	12-Nov-26	14-Nov-26	340	13,679	0	13,679
	Stem for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-WT	2	15-Nov-26	16-Nov-26	340	20,519	0	20,519
	Fire Installation for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-WT	2	17-Nov-26	18-Nov-26	340	23,939	0	23,939
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z2-R102-W	2	19-Nov-26	21-Nov-26	340	3,420	0	3,420
	JDH3-02-009-R102-Electrical Network - EL	44	22-Sep-26 A	02-Dec-26	389	706,544	146,119	706,544
	JDH3-02-009-R102-(EL)-MV cable trench size 3.0m wide and 80	20	22-Sep-26 A	30-Nov-26	391	1,807	1,066	1,807
	Backfilling + Warning Tape for MV Cable Trench 3.0m wide - 80	2	24-Oct-26 A	30-Nov-26	391	723	145	723
	Excavation for MV Cable Trench 3.0m wide - 80cm deep- (B2.3	2	22-Sep-26 A	30-Nov-26	391	1,084	922	1,084
	JDH3-02-009-R102-(EL)-MV cable trench size 2.0m wide and 80	44	23-Sep-26 A	02-Dec-26	389	10,526	6,210	10,526
	Backfilling + Warning Tape for MV Cable Trench 2.0m wide - 80	5	24-Oct-26 A	02-Dec-26	389	4,210	842	4,210
	Excavation for MV Cable Trench 2.0m wide - 80cm deep- (B2.3	5	23-Sep-26 A	30-Nov-26	340	6,316	5,368	6,316
	JDH3-02-009-R102-(EL)-MV cables AL/XLPE/LLDPE Unarmored	14	20-Oct-26 A	30-Nov-26	389	694,212	138,842	694,212
	Installing for MV Cables AL/XLPE/LLDPE 3Cx400 mm²- (B2.26.(	14	20-Oct-26 A	30-Nov-26	389	694,212	138,842	694,212
	JDH3-02-009-R102-Street Lighting Network -SL	14	01-Sep-26 A	08-Dec-26	351	57,487	48,864	57,487
	JDH3-02-009-R102-(SL)- LV Cables - Copper, 4Cx16 mm², Cu/XLP	8	01-Sep-26 A	02-Dec-26	342	46,423	39,460	46,423
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	4	01-Sep-26 A	02-Dec-26	340	5,462	4,642	5,462
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	4	03-Sep-26 A	02-Dec-26	342	40,962	34,817	40,962
	JDH3-02-009-R102-(SL)-Lighting Pole with double arms 16 m he	3	03-Sep-26 A	08-Dec-26	340	4,221	3,588	4,221

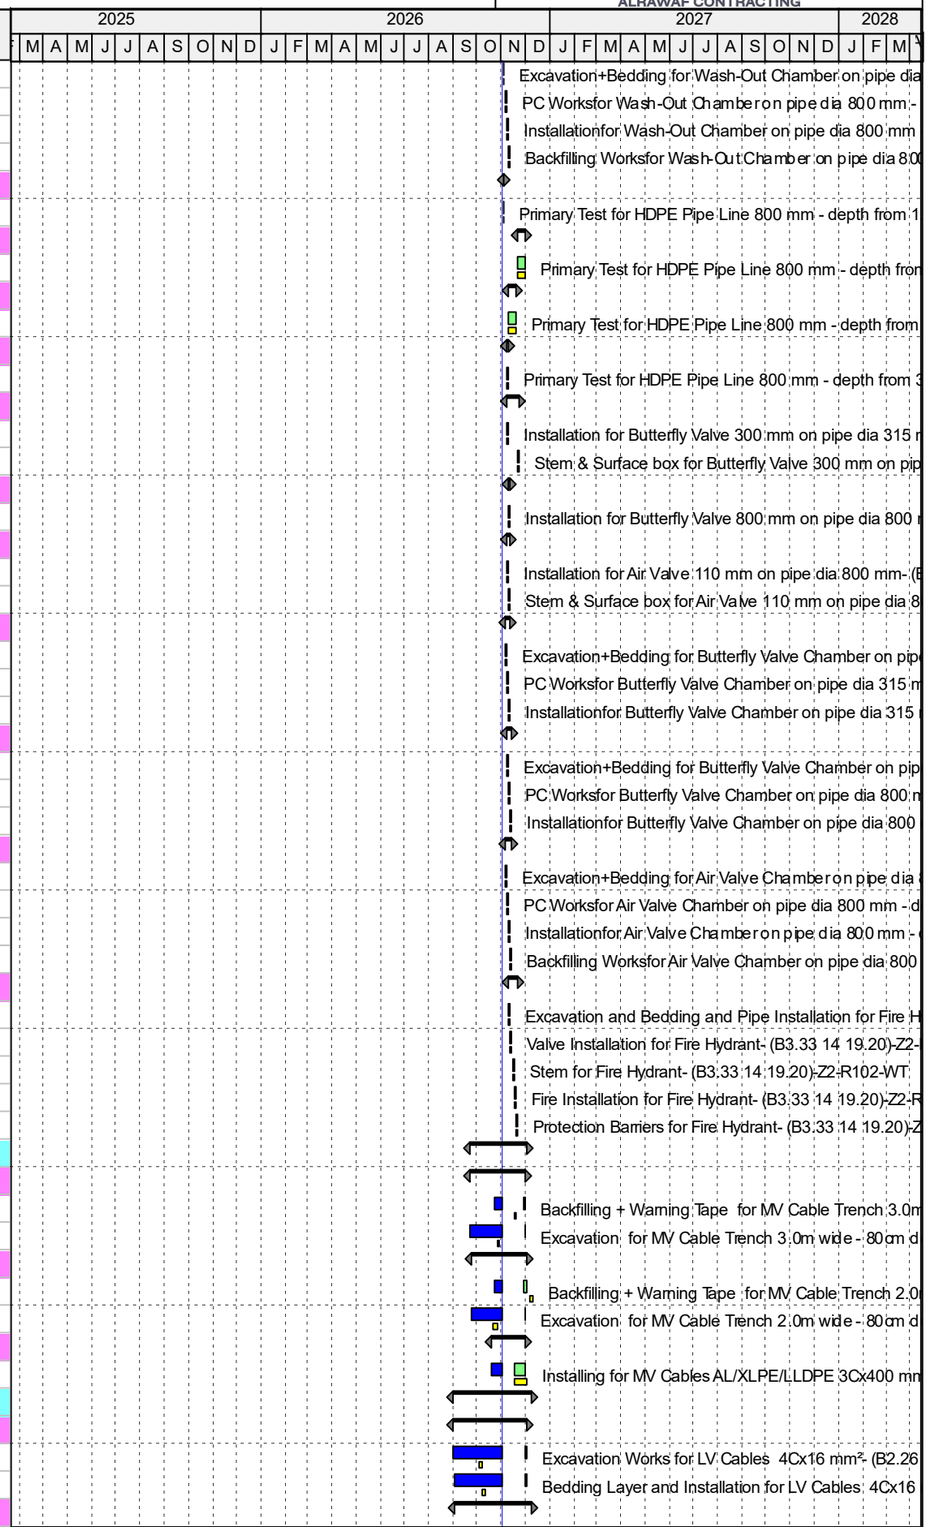


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Cable Connection for Lighting Pole double arms- (B2.26 56 19.(	3	03-Sep-26 A	08-Dec-26	340	4,221	3,588	4,221
	JDH3-02-009-R102-(SL)- LV Cables - Single Core Copper, 3-1x C	2	17-Sep-26 A	01-Dec-26	357	6,842	5,816	6,842
	Installation for LV Cables 3-1xCx4 mm²- (B2.26 05 19.05)-Z2-R	2	17-Sep-26 A	01-Dec-26	357	6,842	5,816	6,842
	JDH3-02-009-R102-Telecommunications Network - TEL	18	03-Nov-26	23-Nov-26	395	62,069	0	62,069
	JDH3-02-009-R102-(TEL)-Reinforced Concrete Duct 6-ways duct	8	03-Nov-26	11-Nov-26	395	3,766	0	3,766
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	2	03-Nov-26	04-Nov-26	395	565	0	565
	Installation for RC Duct 6-ways ducts, 50mm- (B2.33 71 19.01 T	2	05-Nov-26	07-Nov-26	395	1,695	0	1,695
	Pouring RC Concrete Cover for RC Duct 6-ways ducts, 50mm- (I	2	08-Nov-26	09-Nov-26	395	1,130	0	1,130
	Backfilling Works for RC Duct 6-ways ducts, 50mm- (B2.33 71 1	2	10-Nov-26	11-Nov-26	395	377	0	377
	JDH3-02-009-R102-(TEL)-Unreinforced Concrete Duct 6-ways du	10	12-Nov-26	23-Nov-26	395	58,303	0	58,303
	Excavation Works for Duct 6-ways ducts, 50mm- (B2.33 71 19.(	2	12-Nov-26	14-Nov-26	395	9,717	0	9,717
	Installation for Duct 6-ways ducts, 50mm- (B2.33 71 19.02 TEL)	4	15-Nov-26	18-Nov-26	395	35,629	0	35,629
	Pouring PC Concrete Cover for Duct 6-ways ducts, 50mm- (B2.3	4	19-Nov-26	23-Nov-26	395	12,956	0	12,956
R100		84	01-Sep-26 A	08-Dec-26	384	241,519	3,158	431,195
	JDH3-02-009-R100-TSE Network - TSE	56	01-Sep-26 A	07-Nov-26	396	10,766	3,158	10,766
	JDH3-02-009-R100-(TSE)-Valve Chamber on 315 mm dia pipelin	56	01-Sep-26 A	07-Nov-26	396	10,766	3,158	10,766
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	04-Nov-26	07-Nov-26	396	2,871	0	2,871
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	01-Sep-26 A	04-Nov-26	396	7,895	3,158	7,895
	JDH3-02-009-R100-Potable Water Network - WT	2	03-Nov-26	04-Nov-26	413	1,466	0	1,466
	JDH3-02-009-R100-(WT)-Fire Hydrant	2	03-Nov-26	04-Nov-26	413	1,466	0	1,466
	Protection Barriers for Fire Hydrant- (B3.33 14 19.20)-Z1-R100-W	2	03-Nov-26	04-Nov-26	413	1,466	0	1,466
	JDH3-02-009-R100-Street Lighting Network -SL	19	03-Nov-26	25-Nov-26	396	229,287	0	229,287
	JDH3-02-009-R100-(SL)- LV Cables - Copper, 4Cx95 mm²,Cu/XLP	16	07-Nov-26	25-Nov-26	396	207,771	0	207,771
	Excavation Works for LV Cables 4Cx95 mm²- (B2.26 05 19.02)	4	07-Nov-26	11-Nov-26	396	20,777	0	20,777
	Bedding Layer and Installation for LV Cables 4Cx95 mm²- (B2.2	4	11-Nov-26	16-Nov-26	396	155,828	0	155,828
	Testing and Commissioning for LV Cables 4Cx95 mm²- (B2.26	4	16-Nov-26	21-Nov-26	396	10,389	0	10,389
	Backfilling, Warning Tape Works for LV Cables 4Cx95 mm²- (B2	4	21-Nov-26	25-Nov-26	396	20,777	0	20,777
	JDH3-02-009-R100-(SL)- LV Cables - Copper, 4Cx16 mm²,Cu/XLP	14	03-Nov-26	18-Nov-26	384	15,736	0	15,736
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	7	03-Nov-26	10-Nov-26	384	5,245	0	5,245
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	7	11-Nov-26	18-Nov-26	384	10,491	0	10,491
	JDH3-02-009-R100-(SL)-Earthing System for Distribution panels	2	22-Nov-26	23-Nov-26	384	4,502	0	4,502
	Supply, construct, connect and test earthing pits for Street Light	2	22-Nov-26	23-Nov-26	384	4,502	0	4,502
	JDH3-02-009-R100-(SL)-Earthing System for Streetlighting feed	2	19-Nov-26	21-Nov-26	384	1,278	0	1,278
	Supply, construct, connect and test earthing pits for Street Light	2	19-Nov-26	21-Nov-26	384	1,278	0	1,278
	JDH3-02-009-R100-Road Works - RD	31	03-Nov-26	08-Dec-26	384	0	0	189,676
	JDH3-02-009-R100-(RD)-Bituminous concrete wearing course 5(	2	03-Nov-26	04-Nov-26	399	0	0	125,069
	Supply, lay and compaction Asphaltic wearing course 50 mm in(	2	03-Nov-26	04-Nov-26	399	0	0	125,069
	JDH3-02-009-R100-(RD)-Precast Interlocking Block Pavers	3	06-Dec-26	08-Dec-26	384	0	0	51,566
	Interlocking block pavers for sidewalk-footpath - (B1.32 14 13.1	3	06-Dec-26	08-Dec-26	384	0	0	51,566
	JDH3-02-009-R100-(RD)-Pavement Marking	10	05-Nov-26	16-Nov-26	399	0	0	9,010
	Thermoplastic continuous 120 mm wide centre lane- single line	2	05-Nov-26	07-Nov-26	399	0	0	32
	Thermoplastic continuous 200 mm wide. (edge line)-yellow - (B1	2	08-Nov-26	09-Nov-26	399	0	0	7,461
	Thermoplastic continuous Chevron hatching - white (round abou	2	10-Nov-26	11-Nov-26	399	0	0	162
	Thermoplastic continuous Painted rumble strips marking (300m	2	12-Nov-26	14-Nov-26	399	0	0	702
	Thermoplastic intermittent 120 mm wide Broken lane line - (B1.3	2	15-Nov-26	16-Nov-26	399	0	0	654
	JDH3-02-009-R100-(RD)-Traffic Signage	4	17-Nov-26	21-Nov-26	399	0	0	4,031
	Supply and installation Traffic signs 1 Sheet with Single post - (E	2	17-Nov-26	18-Nov-26	399	0	0	1,635
	Supply and installation Traffic signs 2 Sheet with Single post - (E	2	19-Nov-26	21-Nov-26	399	0	0	2,396
Roundabout - Road 450 - RA		20	03-Nov-26	25-Nov-26	342	0	0	989,960
RA5		20	03-Nov-26	25-Nov-26	301	0	0	714,089
	JDH3-02-009-RA5-Earthworks - EW	8	03-Nov-26	11-Nov-26	312	0	0	141,956
	Excavation Works for Roundabout - (B1.31 22 00.01)-Z1-RA5-R	4	03-Nov-26	07-Nov-26	281	0	0	57,908
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	4	08-Nov-26	11-Nov-26	312	0	0	84,048

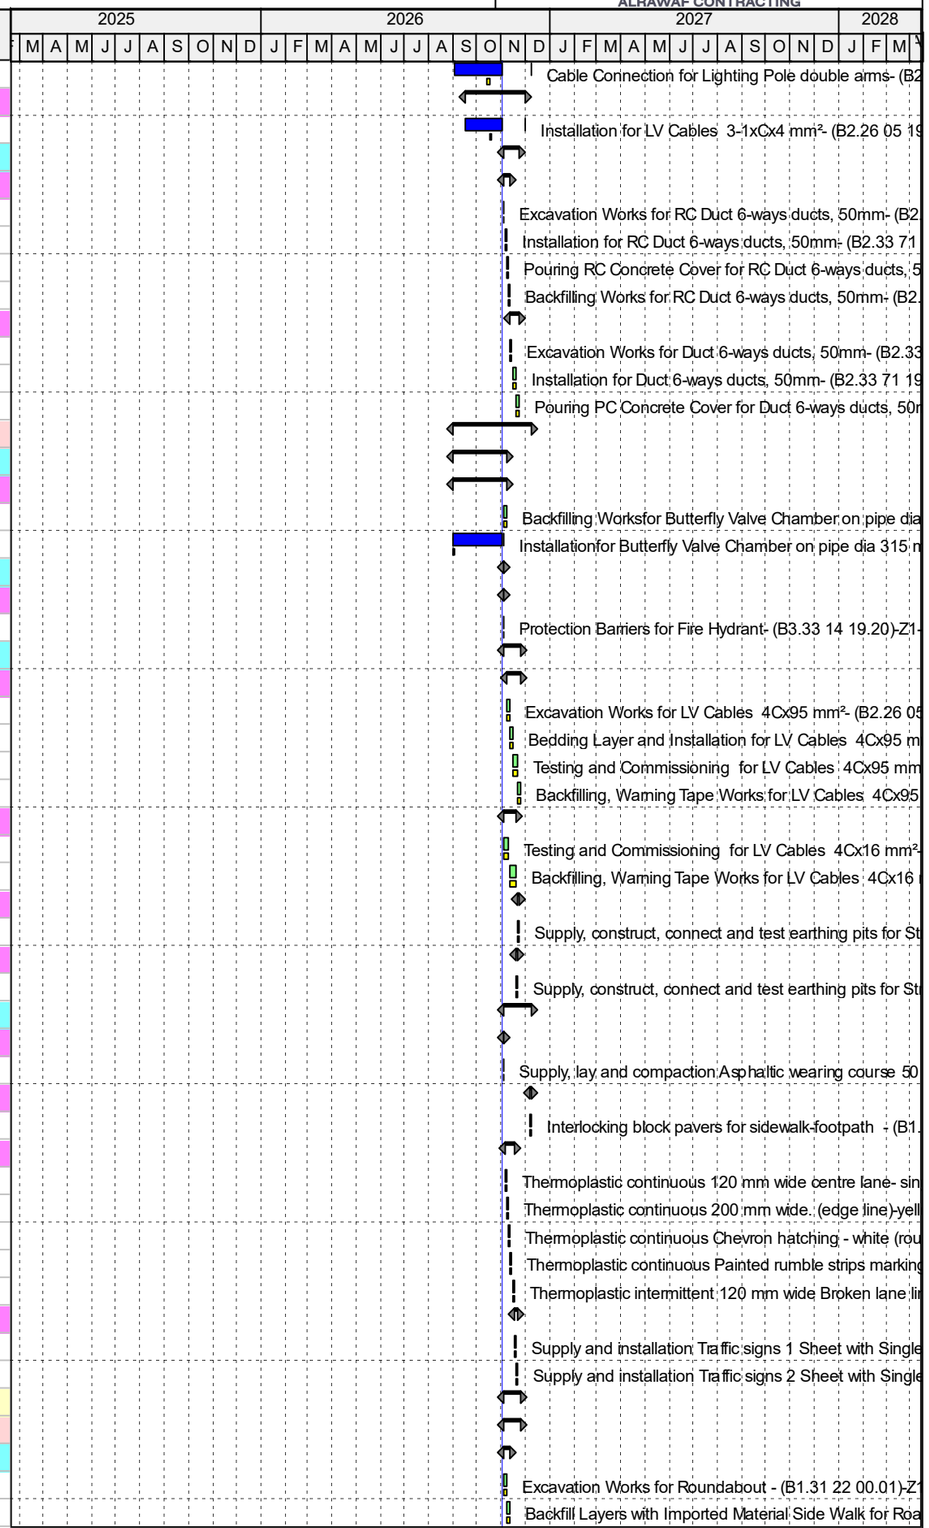

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-RA5-Road Works - RD	16	08-Nov-26	25-Nov-26	301	0	0	572,134
	JDH3-02-009-RA5-(RD)-Subgrade	8	08-Nov-26	16-Nov-26	298	0	0	133,981
	Supply, lay and compaction subgrade compacted thickness 300	8	08-Nov-26	16-Nov-26	298	0	0	133,981
	JDH3-02-009-RA5-(RD)-Bituminous concrete wearing course 50	4	21-Nov-26	25-Nov-26	301	0	0	281,253
	Supply, lay and compaction Asphaltic wearing course 50 mm in	4	21-Nov-26	25-Nov-26	301	0	0	281,253
	JDH3-02-009-RA5-(RD)-Aggregate Base Course	6	17-Nov-26	23-Nov-26	298	0	0	156,900
	Supply, lay and compaction Aggregate base course compacted	6	17-Nov-26	23-Nov-26	298	0	0	156,900
	RA6	15	08-Nov-26	24-Nov-26	342	0	0	275,870
	JDH3-02-009-RA6-Earthworks - EW	10	08-Nov-26	18-Nov-26	347	0	0	151,926
	Excavation Works for Roundabout - (B1.31 22 00.01)-Z2-RA6-R	8	08-Nov-26	16-Nov-26	281	0	0	114,317
	Backfill Layers with Imported Material Side Walk for Road - (B1.3	2	17-Nov-26	18-Nov-26	347	0	0	37,609
	JDH3-02-009-RA6-Road Works - RD	7	17-Nov-26	24-Nov-26	281	0	0	123,944
	JDH3-02-009-RA6-(RD)-Subgrade	7	17-Nov-26	24-Nov-26	281	0	0	123,944
	Supply, lay and compaction subgrade compacted thickness 300	7	17-Nov-26	24-Nov-26	281	0	0	123,944
	External Roads - EX	59	15-Sep-26 A	23-Nov-26	397	3,392,261	31,856	3,392,261
	R241 - Access Road PW Storage Tanks	18	03-Nov-26	23-Nov-26	397	555,912	0	555,912
	JDH3-02-009-R241-Potable Water Network - WT	18	03-Nov-26	23-Nov-26	397	555,912	0	555,912
	JDH3-02-009-R241-(WT)-HDPE Pipes-800 mm diameter depth fr	12	03-Nov-26	16-Nov-26	403	71,871	0	71,871
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	12	03-Nov-26	16-Nov-26	403	71,871	0	71,871
	JDH3-02-009-R241-(WT)-HDPE Pipes-800 mm diameter depth fr	12	03-Nov-26	16-Nov-26	403	1,394	0	1,394
	Primary Test for HDPE Pipe Line 800 mm - depth from 1.51 to 2	12	03-Nov-26	16-Nov-26	403	1,394	0	1,394
	JDH3-02-009-R241-(WT)-Valve Chamber on 800 mm dia pipeline	8	08-Nov-26	16-Nov-26	403	127,983	0	127,983
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 80	2	08-Nov-26	09-Nov-26	397	19,197	0	19,197
	PC Worksfor Butterfly Valve Chamber on pipe dia 800 mm - dep	2	10-Nov-26	11-Nov-26	403	12,798	0	12,798
	Installationfor Butterfly Valve Chamber on pipe dia 800 mm - de	2	12-Nov-26	14-Nov-26	403	70,391	0	70,391
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 800 m	2	15-Nov-26	16-Nov-26	403	25,597	0	25,597
	JDH3-02-009-R241-(WT)-Butterfly Valve-800 mm on pipe dia (80	4	05-Nov-26	09-Nov-26	407	263,018	0	263,018
	Installation for Butterfly Valve 800 mm on pipe dia 800 mm- (B3	2	05-Nov-26	07-Nov-26	407	236,716	0	236,716
	Stem & Surface box for Butterfly Valve 800 mm on pipe dia 800	2	08-Nov-26	09-Nov-26	407	26,302	0	26,302
	JDH3-02-009-R241-(WT)-Air Valve Chamber on 800 mm dia pipe	8	10-Nov-26	18-Nov-26	401	7,139	0	7,139
	Excavation+Bedding for Air Valve Chamber on pipe dia 800 mm	2	10-Nov-26	11-Nov-26	397	1,071	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 800 mm - depth fro	2	12-Nov-26	14-Nov-26	401	714	0	714
	Installationfor Air Valve Chamber on pipe dia 800 mm - depth fr	2	15-Nov-26	16-Nov-26	401	3,926	0	3,926
	Backfilling Worksfor Air Valve Chamber on pipe dia 800 mm - de	2	17-Nov-26	18-Nov-26	401	1,428	0	1,428
	JDH3-02-009-R241-(WT)-Air Valve-110 mm on pipe dia (800) mm	4	03-Nov-26	07-Nov-26	409	25,013	0	25,013
	Installation for Air Valve 110 mm on pipe dia 800 mm- (B3.33 14	2	03-Nov-26	04-Nov-26	409	22,512	0	22,512
	Stem & Surface box for Air Valve 110 mm on pipe dia 800 mm-	2	05-Nov-26	07-Nov-26	409	2,501	0	2,501
	JDH3-02-009-R241-(WT)-Wash-Out Valve-200 mm on pipe dia (8	4	19-Nov-26	23-Nov-26	397	27,358	0	27,358
	Installation for Wash-Out Valve 200 mm on pipe dia 800 mm- (E	2	19-Nov-26	21-Nov-26	397	24,622	0	24,622
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 80	2	22-Nov-26	23-Nov-26	397	2,736	0	2,736
	JDH3-02-009-R241-(WT)-Wash-Out Chamber on 800 mm dia pip	8	12-Nov-26	21-Nov-26	399	32,136	0	32,136
	Excavation+Bedding for Wash-Out Chamber on pipe dia 800 m	2	12-Nov-26	14-Nov-26	397	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 800 mm - depth fr	2	15-Nov-26	16-Nov-26	397	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 800 mm - depth	2	17-Nov-26	18-Nov-26	397	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 800 mm - c	2	19-Nov-26	21-Nov-26	399	6,427	0	6,427
	R242 - Access Road PW Storage Tanks	14	03-Nov-26	18-Nov-26	401	1,130,081	0	1,130,081
JDI	Surveying Works for Road - R242-EX	0	03-Nov-26	03-Nov-26	415	0	0	0
	JDH3-02-009-R242-Potable Water Network - WT	14	03-Nov-26	18-Nov-26	401	1,130,081	0	1,130,081
	JDH3-02-009-R242-(WT)-HDPE Pipes-1000 mm diameter depth f	8	03-Nov-26	11-Nov-26	407	65,924	0	65,924
	Primary Test for HDPE Pipe Line 1000 mm - depth from 1.51 to	8	03-Nov-26	11-Nov-26	407	65,924	0	65,924
	JDH3-02-009-R242-(WT)-HDPE Pipes-1000 mm diameter depth f	8	03-Nov-26	11-Nov-26	407	141,987	0	141,987
	Primary Test for HDPE Pipe Line 1000 mm - depth from 1.51 to	8	03-Nov-26	11-Nov-26	407	141,987	0	141,987
	JDH3-02-009-R242-(WT)-Wash-Out Valve-200 mm on pipe dia (1	4	08-Nov-26	11-Nov-26	403	39,083	0	39,083

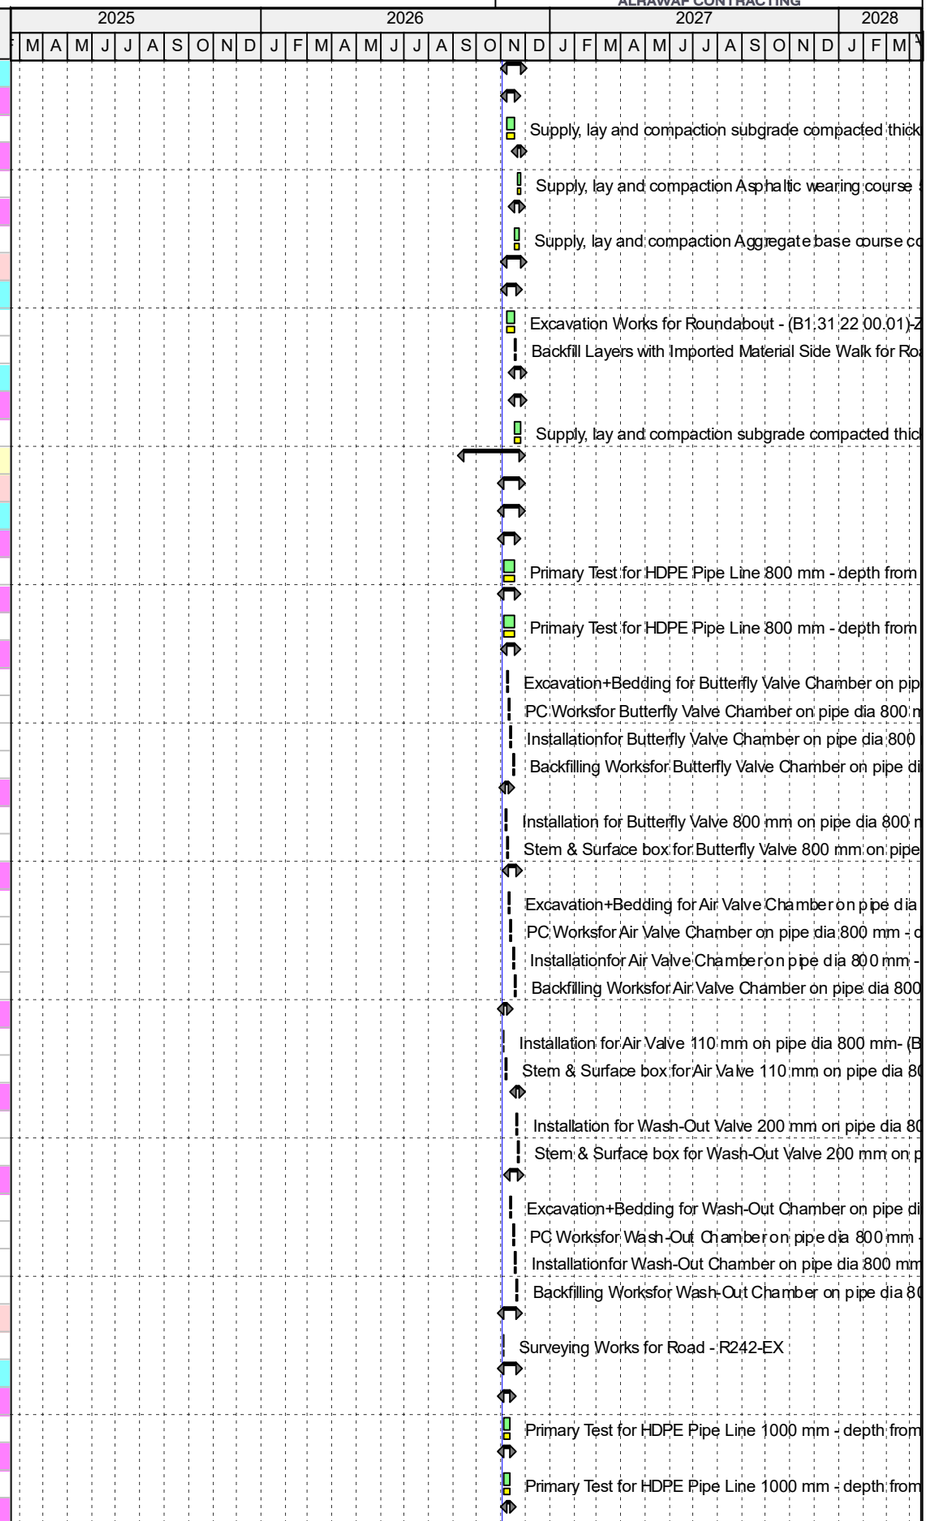


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation for Wash-Out Valve 200 mm on pipe dia 1000 mm-	2	08-Nov-26	09-Nov-26	403	35,175	0	35,175
	Stem & Surface box for Wash-Out Valve 200 mm on pipe dia 1	2	10-Nov-26	11-Nov-26	403	3,908	0	3,908
	JDH3-02-009-R242-(WT)-Valve Chamber on 1000 mm dia pipelir	10	03-Nov-26	14-Nov-26	403	191,975	0	191,975
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 1(	2	03-Nov-26	04-Nov-26	397	28,796	0	28,796
	PC Worksfor Butterfly Valve Chamber on pipe dia 1000 mm - de	2	05-Nov-26	07-Nov-26	405	19,197	0	19,197
	Installationfor Butterfly Valve Chamber on pipe dia 1000 mm - d	2	08-Nov-26	09-Nov-26	405	105,586	0	105,586
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 1000 r	2	12-Nov-26	14-Nov-26	403	38,395	0	38,395
	JDH3-02-009-R242-(WT)-Butterfly Valve-1000 mm on pipe dia (1(	4	05-Nov-26	09-Nov-26	403	493,159	0	493,159
	Installation for Butterfly Valve 1000 mm on pipe dia 1000 mm- (	2	05-Nov-26	07-Nov-26	403	443,843	0	443,843
	Stem & Surface box for Butterfly Valve 1000 mm on pipe dia 1(	2	08-Nov-26	09-Nov-26	403	49,316	0	49,316
	JDH3-02-009-R242-(WT)-Wash-Out Chamber on 1000 mm dia pi	10	05-Nov-26	16-Nov-26	403	32,136	0	32,136
	Excavation+Bedding for Wash-Out Chamber on pipe dia 1000 r	2	05-Nov-26	07-Nov-26	401	4,820	0	4,820
	PC Worksfor Wash-Out Chamber on pipe dia 1000 mm - depth	2	08-Nov-26	09-Nov-26	405	3,214	0	3,214
	Installationfor Wash-Out Chamber on pipe dia 1000 mm - deptl	2	10-Nov-26	11-Nov-26	405	17,675	0	17,675
	Backfilling Worksfor Wash-Out Chamber on pipe dia 1000 mm -	2	15-Nov-26	16-Nov-26	403	6,427	0	6,427
	JDH3-02-009-R242-(WT)-Valve Chamber on 315 mm dia pipeline	8	08-Nov-26	16-Nov-26	403	14,336	0	14,336
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 31	2	08-Nov-26	09-Nov-26	401	2,150	0	2,150
	PC Worksfor Butterfly Valve Chamber on pipe dia 315 mm - dep	2	10-Nov-26	11-Nov-26	401	1,434	0	1,434
	Installationfor Butterfly Valve Chamber on pipe dia 315 mm - de	2	12-Nov-26	14-Nov-26	401	7,885	0	7,885
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 315 m	2	15-Nov-26	16-Nov-26	403	2,867	0	2,867
	JDH3-02-009-R242-(WT)-Butterfly Valve-300 mm on pipe dia (31!	4	15-Nov-26	18-Nov-26	401	16,130	0	16,130
	Installation for Butterfly Valve 300 mm on pipe dia 315 mm- (B3	2	15-Nov-26	16-Nov-26	401	14,517	0	14,517
	Stem & Surface box for Butterfly Valve 300 mm on pipe dia 31!	2	17-Nov-26	18-Nov-26	401	1,613	0	1,613
	JDH3-02-009-R242-(WT)-Butterfly Valve-600 mm on pipe dia (63(	4	03-Nov-26	07-Nov-26	407	98,633	0	98,633
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B3	2	03-Nov-26	04-Nov-26	403	88,769	0	88,769
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 63(	2	05-Nov-26	07-Nov-26	407	9,863	0	9,863
	JDH3-02-009-R242-(WT)-Valve Chamber on 630 mm dia pipeline	8	05-Nov-26	14-Nov-26	403	36,718	0	36,718
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2	05-Nov-26	07-Nov-26	397	5,508	0	5,508
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2	08-Nov-26	09-Nov-26	403	3,672	0	3,672
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2	10-Nov-26	11-Nov-26	403	20,195	0	20,195
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 m	2	12-Nov-26	14-Nov-26	403	7,344	0	7,344
R251 - Access Road TSE Storage Tanks		45	22-Sep-26 A	16-Nov-26	403	227,022	13,498	227,022
JDH3-02-009-R251-TSE Network - TSE		45	22-Sep-26 A	16-Nov-26	403	227,022	13,498	227,022
JDH3-02-009-R251-(TSE)-Air Valve Chamber on 400 mm dia pip		45	22-Sep-26 A	16-Nov-26	403	14,269	5,708	14,269
	Backfilling Worksfor Air Valve Chamber on pipe dia 400 mm - de	2	15-Nov-26	16-Nov-26	403	2,854	0	2,854
	Excavation+Bedding for Air Valve Chamber on pipe dia 400 mm	2	22-Sep-26 A	04-Nov-26	411	2,140	1,070	2,140
	PC Worksfor Air Valve Chamber on pipe dia 400 mm - depth fro	2	23-Sep-26 A	04-Nov-26	411	1,427	713	1,427
	Installationfor Air Valve Chamber on pipe dia 400 mm - depth fr	2	24-Sep-26 A	09-Nov-26	407	7,848	3,924	7,848
	JDH3-02-009-R251-(TSE)-Wash-Out Chamber on 400 mm dia pi	10	03-Nov-26	14-Nov-26	403	41,949	0	41,949
	Excavation+Bedding for Wash-Out Chamber on pipe dia 400 m	2	03-Nov-26	04-Nov-26	405	6,292	0	6,292
	PC Worksfor Wash-Out Chamber on pipe dia 400 mm - depth fr	2	05-Nov-26	07-Nov-26	405	4,195	0	4,195
	Installationfor Wash-Out Chamber on pipe dia 400 mm - depth	2	08-Nov-26	09-Nov-26	405	23,072	0	23,072
	Backfilling Worksfor Wash-Out Chamber on pipe dia 400 mm - c	2	12-Nov-26	14-Nov-26	403	8,390	0	8,390
	JDH3-02-009-R251-(TSE)-Air Valve-65 mm on pipe dia (400) mm	4	26-Sep-26 A	16-Nov-26	403	15,581	7,790	15,581
	Stem & Surface box for Air Valve 65 mm on pipe dia 400 mm- (I	2	27-Sep-26 A	16-Nov-26	403	1,558	779	1,558
	Installation for Air Valve 65 mm on pipe dia 400 mm- (B4.33.14	2	26-Sep-26 A	14-Nov-26	405	14,023	7,011	14,023
	JDH3-02-009-R251-(TSE)-Wash-Out Valve-100 mm on pipe dia (	4	12-Nov-26	16-Nov-26	403	33,818	0	33,818
	Installation for Wash-Out Valve 100 mm on pipe dia 400 mm- (E	2	12-Nov-26	14-Nov-26	403	30,436	0	30,436
	Stem & Surface box for Wash-Out Valve 100 mm on pipe dia 4(	2	15-Nov-26	16-Nov-26	403	3,382	0	3,382
	JDH3-02-009-R251-(TSE)-Butterfly Valve-400 mm on pipe dia (31	4	10-Nov-26	14-Nov-26	405	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2	10-Nov-26	11-Nov-26	405	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40(	2	12-Nov-26	14-Nov-26	405	7,822	0	7,822
	JDH3-02-009-R251-(TSE)-Valve Chamber on 400 mm dia pipelin	8	03-Nov-26	11-Nov-26	407	43,184	0	43,184

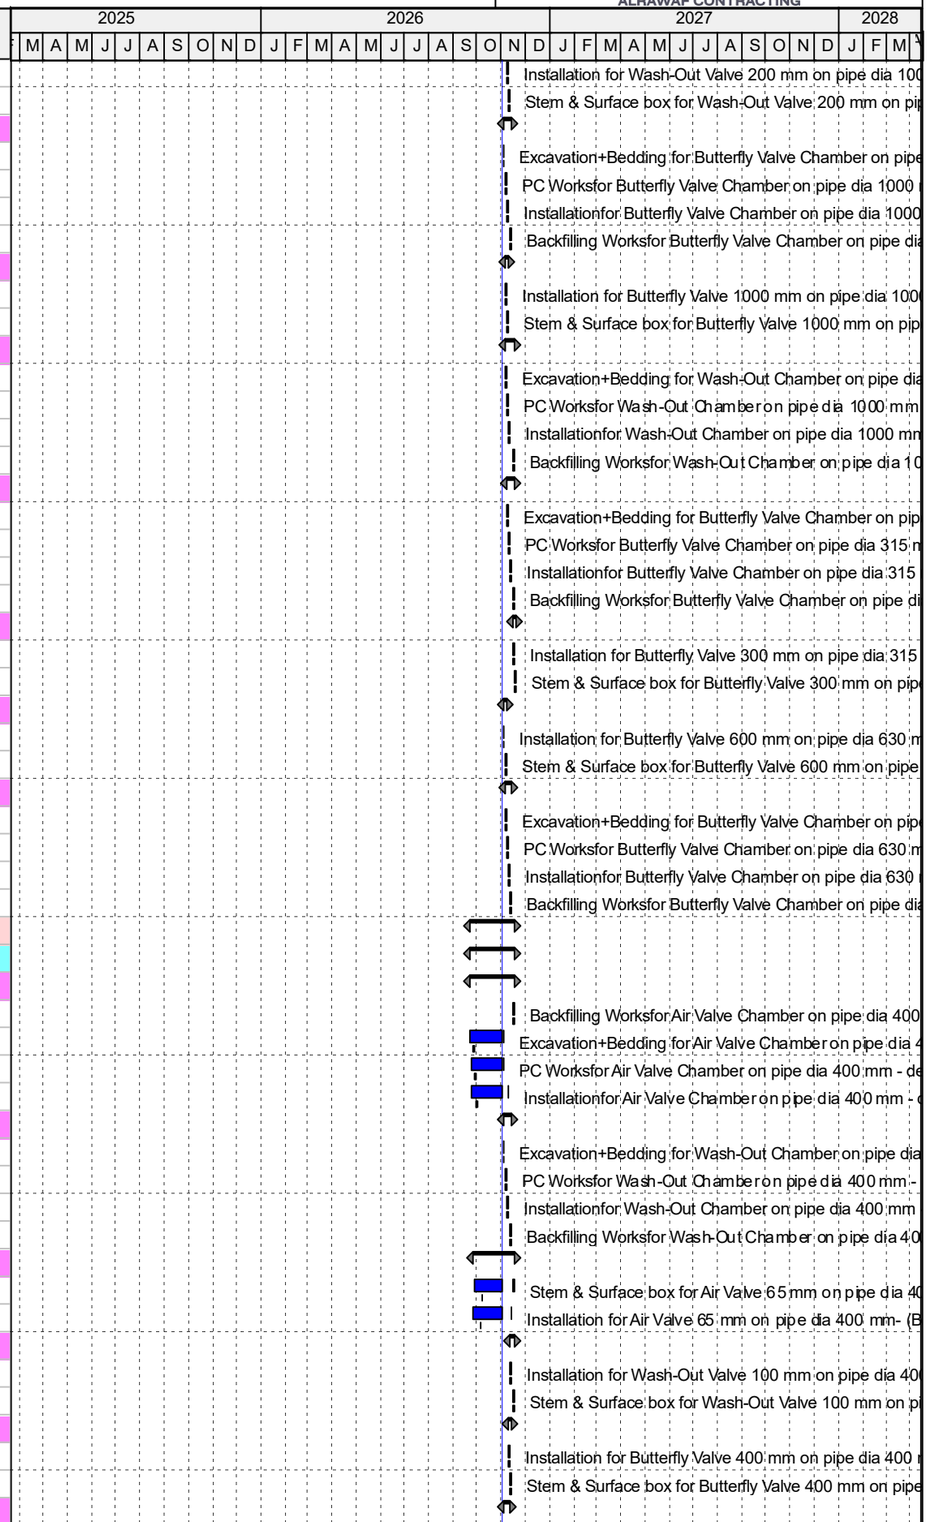


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	03-Nov-26	04-Nov-26	407	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	05-Nov-26	07-Nov-26	407	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	08-Nov-26	09-Nov-26	407	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 mi	2	10-Nov-26	11-Nov-26	407	8,637	0	8,637
R252 - Access Road TSE Storage Tanks		18	03-Nov-26	23-Nov-26	397	1,302,210	0	1,302,210
JDH3-02-009-R252-TSE Network - TSE		18	03-Nov-26	23-Nov-26	397	1,302,210	0	1,302,210
JDH3-02-009-R252-(TSE)-Butterfly Valve-600 mm on pipe dia (63		4	15-Nov-26	18-Nov-26	397	542,479	0	542,479
	Installation for Butterfly Valve 600 mm on pipe dia 630 mm- (B4	2	15-Nov-26	16-Nov-26	397	488,231	0	488,231
	Stem & Surface box for Butterfly Valve 600 mm on pipe dia 630	2	17-Nov-26	18-Nov-26	397	54,248	0	54,248
JDH3-02-009-R252-(TSE)-Wash-Out Valve-150 mm on pipe dia (		4	17-Nov-26	21-Nov-26	397	195,417	0	195,417
	Installation for Wash-Out Valve 150 mm on pipe dia 630 mm- (E	2	17-Nov-26	18-Nov-26	397	175,875	0	175,875
	Stem & Surface box for Wash-Out Valve 150 mm on pipe dia 6:	2	19-Nov-26	21-Nov-26	397	19,542	0	19,542
JDH3-02-009-R252-(TSE)-Air Valve-65 mm on pipe dia (630) mm		4	19-Nov-26	23-Nov-26	397	187,600	0	187,600
	Installation for Air Valve 65 mm on pipe dia 630 mm- (B4.33 14	2	19-Nov-26	21-Nov-26	397	168,840	0	168,840
	Stem & Surface box for Air Valve 65 mm on pipe dia 630 mm- (I	2	22-Nov-26	23-Nov-26	397	18,760	0	18,760
JDH3-02-009-R252-(TSE)-Valve Chamber on 630 mm dia pipelin		8	03-Nov-26	11-Nov-26	403	202,721	0	202,721
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 63	2	03-Nov-26	04-Nov-26	397	30,408	0	30,408
	PC Worksfor Butterfly Valve Chamber on pipe dia 630 mm - dep	2	05-Nov-26	07-Nov-26	397	20,272	0	20,272
	Installationfor Butterfly Valve Chamber on pipe dia 630 mm - de	2	08-Nov-26	09-Nov-26	397	111,497	0	111,497
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 630 mi	2	10-Nov-26	11-Nov-26	403	40,544	0	40,544
JDH3-02-009-R252-(TSE)-Wash-Out Chamber on 630 mm dia pi		8	05-Nov-26	14-Nov-26	403	137,902	0	137,902
	Excavation+Bedding for Wash-Out Chamber on pipe dia 630 m	2	05-Nov-26	07-Nov-26	397	20,685	0	20,685
	PC Worksfor Wash-Out Chamber on pipe dia 630 mm - depth fi	2	08-Nov-26	09-Nov-26	397	13,790	0	13,790
	Installationfor Wash-Out Chamber on pipe dia 630 mm - depth	2	10-Nov-26	11-Nov-26	397	75,846	0	75,846
	Backfilling Worksfor Wash-Out Chamber on pipe dia 630 mm - c	2	12-Nov-26	14-Nov-26	403	27,580	0	27,580
JDH3-02-009-R252-(TSE)-Air Valve Chamber on 630 mm dia pip		8	08-Nov-26	16-Nov-26	403	36,091	0	36,091
	Excavation+Bedding for Air Valve Chamber on pipe dia 630 mm	2	08-Nov-26	09-Nov-26	397	5,414	0	5,414
	PC Worksfor Air Valve Chamber on pipe dia 630 mm - depth fro	2	10-Nov-26	11-Nov-26	397	3,609	0	3,609
	Installationfor Air Valve Chamber on pipe dia 630 mm - depth fr	2	12-Nov-26	14-Nov-26	397	19,850	0	19,850
	Backfilling Worksfor Air Valve Chamber on pipe dia 630 mm - de	2	15-Nov-26	16-Nov-26	403	7,218	0	7,218
R253 - Access Road TSE Storage Tanks		10	03-Nov-26	14-Nov-26	403	121,405	0	121,405
JDH3-02-009-R253-TSE Network - TSE		10	03-Nov-26	14-Nov-26	403	121,405	0	121,405
JDH3-02-009-R253-(TSE)-Valve Chamber on 400 mm dia pipelin		8	03-Nov-26	11-Nov-26	403	43,184	0	43,184
	Excavation+Bedding for Butterfly Valve Chamber on pipe dia 40	2	03-Nov-26	04-Nov-26	403	6,478	0	6,478
	PC Worksfor Butterfly Valve Chamber on pipe dia 400 mm - dep	2	05-Nov-26	07-Nov-26	403	4,318	0	4,318
	Installationfor Butterfly Valve Chamber on pipe dia 400 mm - de	2	08-Nov-26	09-Nov-26	403	23,751	0	23,751
	Backfilling Worksfor Butterfly Valve Chamber on pipe dia 400 mi	2	10-Nov-26	11-Nov-26	403	8,637	0	8,637
JDH3-02-009-R253-(TSE)-Butterfly Valve-400 mm on pipe dia (31		4	10-Nov-26	14-Nov-26	403	78,222	0	78,222
	Installation for Butterfly Valve 400 mm on pipe dia 400 mm- (B4	2	10-Nov-26	11-Nov-26	403	70,400	0	70,400
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 40	2	12-Nov-26	14-Nov-26	403	7,822	0	7,822
R26		48	15-Sep-26 A	10-Nov-26	408	55,631	18,358	55,631
JDH3-02-009-R26-Sewage Network - SW		48	15-Sep-26 A	10-Nov-26	408	55,631	18,358	55,631
JDH3-02-009-R26-(SW)-MH Works depth from 4.5 to 5.5 Diam 1		46	15-Sep-26 A	08-Nov-26	411	29,913	9,971	29,913
	Steel Cover for MH 1500 mm - depth from 4.51 to 5.5 m- (B5.3	3	04-Nov-26	08-Nov-26	411	9,971	0	9,971
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	3	15-Sep-26 A	04-Nov-26	411	19,942	9,971	19,942
JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Dim 1		44	15-Sep-26 A	05-Nov-26	408	4,710	1,475	4,710
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	2	04-Nov-26	05-Nov-26	408	1,761	0	1,761
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	2	15-Sep-26 A	03-Nov-26	408	2,949	1,475	2,949
JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Diam		42	20-Sep-26 A	08-Nov-26	408	16,531	5,510	16,531
	Steel Cover for MH 1500 mm - depth from 5.51 to 6.5 m- (B5.3	2	07-Nov-26	08-Nov-26	408	5,510	0	5,510
	Finishing, Benching, Testing Works for MH 1500 mm - depth fro	2	20-Sep-26 A	05-Nov-26	408	11,021	5,510	11,021
JDH3-02-009-R26-(SW)-MH Works depth from 5.51 to 6.5 Diam 2		48	15-Sep-26 A	10-Nov-26	408	4,477	1,402	4,477
	Steel Cover for MH 2000 mm - depth from 5.51 to 6.5 m- (B5.3	2	09-Nov-26	10-Nov-26	408	1,674	0	1,674

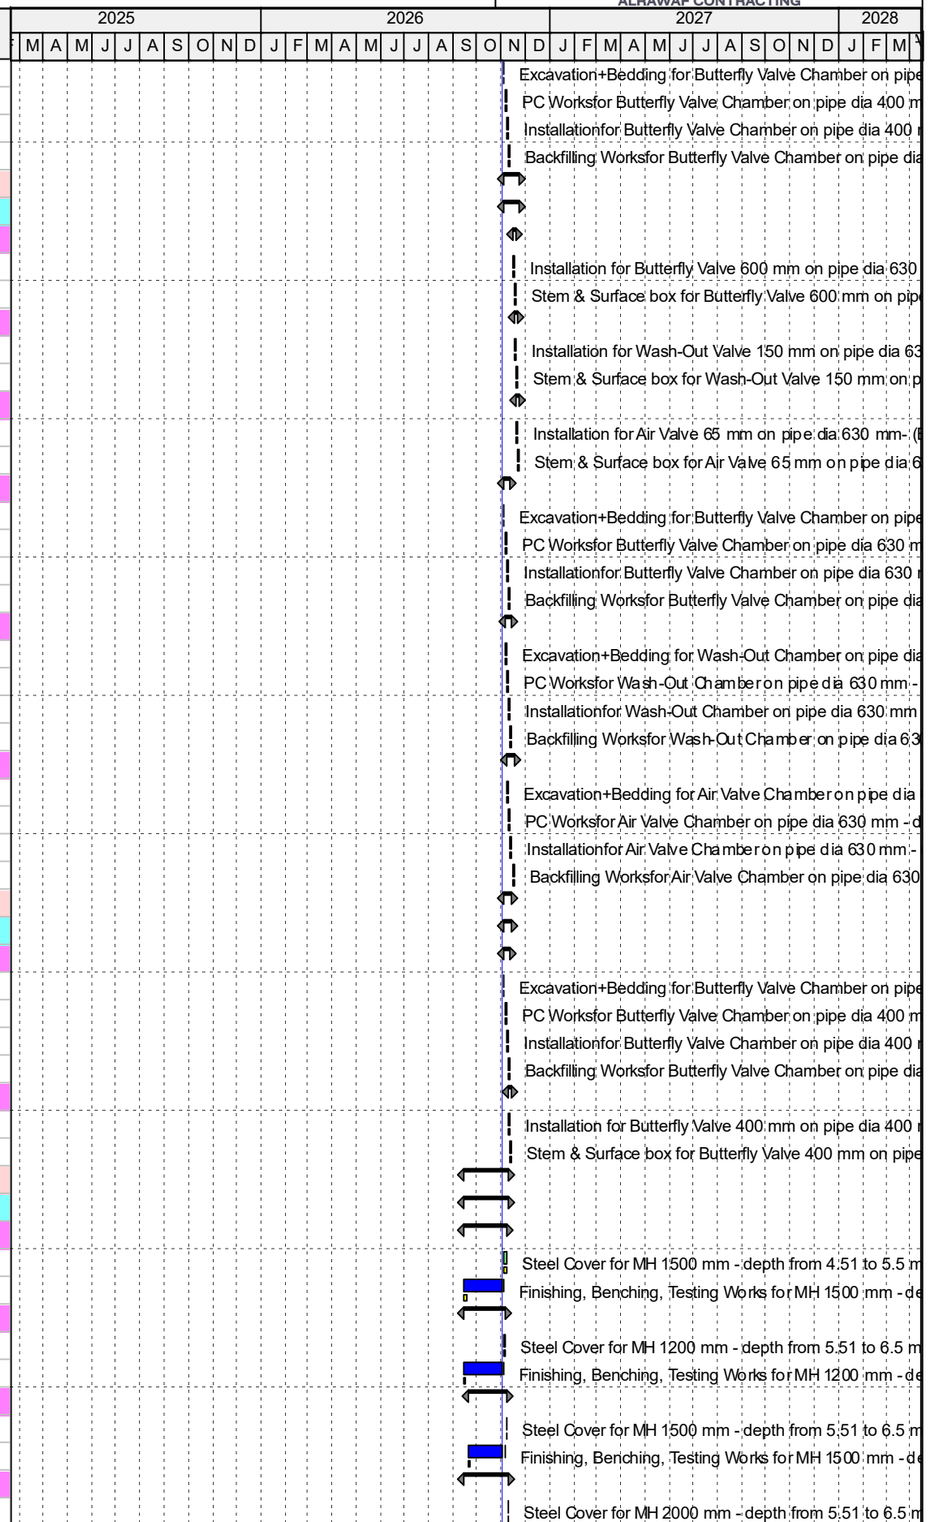

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Finishing, Benching Works for MH 2000 mm - depth from 5.51 t	2	15-Sep-26 A	03-Nov-26	412	2,803	1,402	2,803
	JDH3-02-009-Close Out	344	21-Jul-26 A	09-Oct-27	120	0	3,004,331	5,888,883
	JDH3-02-009-Engineering - EN	141	03-Nov-26	20-Apr-27	262	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB	137	03-Nov-26	15-Apr-27	261	0	0	0
JDI	Prepare and Submit Drawing for Ponds - AS	7	31-Mar-27	07-Apr-27	256	0	0	0
JDI	Prepare and Submit Drawing for Box Culverts - AS	7	08-Apr-27	15-Apr-27	256	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z01	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z01-AS-S'	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z01-A	7	03-Nov-26	10-Nov-26	386	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z02	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z02-AS-S'	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z02-A	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Telecommunication Network fo	7	03-Nov-26	10-Nov-26	386	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z03	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z03-AS-S'	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z03-A	7	03-Nov-26	10-Nov-26	386	0	0	0
	Prepare and Submit Drawing for Telecommunication Network fo	7	03-Nov-26	10-Nov-26	386	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Z04	9	03-Nov-26	12-Nov-26	389	0	0	0
	Prepare and Submit Drawing for Sewage Network for Z04-AS-S'	5	03-Nov-26	08-Nov-26	393	0	0	0
	Prepare and Submit Drawing for Storm Water Network for Z04-A	5	03-Nov-26	08-Nov-26	393	0	0	0
	Prepare and Submit Drawing for TSE Network for Z04-AS-TSE-S	5	08-Nov-26	12-Nov-26	389	0	0	0
	Prepare and Submit Drawing for Potable Water Network for Z04	5	08-Nov-26	12-Nov-26	389	0	0	0
	Prepare and Submit Drawing for Electrical Network for Z04-AS-E	5	08-Nov-26	12-Nov-26	389	0	0	0
	Prepare and Submit Drawing for Street Lighting Network for Z04	5	08-Nov-26	12-Nov-26	389	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-EX	5	03-Nov-26	08-Nov-26	393	0	0	0
	Prepare and Submit Drawing for Electrical Network for EX-AS-EI	5	03-Nov-26	08-Nov-26	393	0	0	0
	Prepare and Submit Drawing for Landscape and Irrigation for E	5	03-Nov-26	08-Nov-26	393	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP	113	09-Nov-26	20-Apr-27	218	0	0	0
JDI	Review and Approval for Ponds for -AS-ST-APP	9	08-Apr-27	20-Apr-27	218	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z01	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Sewage Network for Z01-AS-SW-APP	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Storm Water Network for Z01-AS-ST-AI	9	11-Nov-26	23-Nov-26	320	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z02	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Sewage Network for Z02-AS-SW-APP	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Storm Water Network for Z02-AS-ST-AI	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Telecommunication Network for Z02-AS	9	11-Nov-26	23-Nov-26	320	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z03	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Sewage Network for Z03-AS-SW-APP	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Storm Water Network for Z03-AS-ST-AI	9	11-Nov-26	23-Nov-26	320	0	0	0
	Review and Approval for Telecommunication Network for Z03-AS	9	11-Nov-26	23-Nov-26	320	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Z04	9	09-Nov-26	19-Nov-26	322	0	0	0
	Review and Approval for Sewage Network for Z04-AS-SW-APP	5	09-Nov-26	15-Nov-26	326	0	0	0
	Review and Approval for Storm Water Network for Z04-AS-ST-AI	5	09-Nov-26	15-Nov-26	326	0	0	0
	Review and Approval for TSE Network for Z04-AS-TSE-APP	5	15-Nov-26	19-Nov-26	322	0	0	0
	Review and Approval for Potable Water Network for Z04-AS-WT	5	15-Nov-26	19-Nov-26	322	0	0	0
	Review and Approval for Electrical Network for Z04-AS-EL-APP	5	15-Nov-26	19-Nov-26	322	0	0	0
	Review and Approval for Street Lighting Network for Z04-AS-SL-	5	15-Nov-26	19-Nov-26	322	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-EX	5	09-Nov-26	15-Nov-26	326	0	0	0
	Review and Approval for Electrical Network for EX-AS-EL-APP	5	09-Nov-26	15-Nov-26	326	0	0	0
	Review and Approval for Landscape and Irrigation for EX-AS-LS	5	09-Nov-26	15-Nov-26	326	0	0	0
	JDH3-02-009-Final Testing and Commissioning - FT	344	21-Jul-26 A	09-Oct-27	110	0	3,004,331	5,888,883
	JDH3-02-009-Final Testing and Commissioning - FT-Z01	12	21-Jul-26 A	14-Sep-27	103	0	661,973	1,103,288
JDI	Final Testing and Commissioning for Potable Water - FT-Z01-WT	5	21-Jul-26 A	14-Sep-27	103	0	430,073	716,788




Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Final Testing and Commissioning for TSE Network - FT-Z01-TSE	7	21-Jul-26 A	14-Sep-27	103	0	231,900	386,501
JDH3-02-009-Final Testing and Commissioning - FT-Z02		305	21-Jul-26 A	14-Sep-27	103	0	661,973	1,103,288
JDH	Final Testing and Commissioning for Potable Water - FT-Z02-WT	10	21-Jul-26 A	14-Sep-27	103	0	430,073	716,788
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	10	21-Jul-26 A	25-Nov-26	346	0	231,900	386,501
JDH3-02-009-Final Testing and Commissioning - FT-Z03		305	21-Jul-26 A	14-Sep-27	103	0	551,644	1,103,288
JDH	Final Testing and Commissioning for Potable Water - FT-Z03-WT	10	21-Jul-26 A	14-Sep-27	103	0	358,394	716,788
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	20	21-Jul-26 A	25-Nov-26	346	0	193,250	386,501
JDH3-02-009-Final Testing and Commissioning - FT-Z04		93	21-Jul-26 A	07-Nov-26	389	0	661,973	1,722,782
JDH	Final Testing and Commissioning for Electrical Network - FT-Z04	4	03-Nov-26	07-Nov-26	389	0	0	360,628
JDH	Final Testing and Commissioning for Street Lighting Network - F	4	03-Nov-26	07-Nov-26	389	0	0	258,865
JDH	Final Testing and Commissioning for Potable Water - FT-Z04-WT	4	21-Jul-26 A	07-Nov-26	389	0	430,073	716,788
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	4	21-Jul-26 A	07-Nov-26	389	0	231,900	386,501
JDH3-02-009-Final Testing and Commissioning - FT-EX		11	21-Jul-26 A	09-Oct-27	110	0	466,768	856,236
JDH	Final Testing and Commissioning for Sewage Network - FT-EX-S	5	11-Aug-26 A	09-Oct-27	110	0	234,867	469,735
JDH	Final Testing and Commissioning for TSE (IRRIGATION) Networ	4	21-Jul-26 A	09-Oct-27	110	0	231,900	386,501
JDH3-02-009-New Scope - R.BOQ. NO03		134	14-Jul-26 A	01-Jan-27	364	0	3,179,481	15,760,349
JDH3-02-009-Infrastructure Networks Zone 5		134	14-Jul-26 A	01-Jan-27	364	0	2,006,243	7,281,596
JDH3-02-009-Milestone		0	03-Nov-26	03-Nov-26	346	0	0	0
Network Milestones		0	03-Nov-26	03-Nov-26	346	0	0	0
JDH	Start of Potable Water Network - WT - .SMI-WT	0	03-Nov-26		207	0	0	0
JDH	Start of TSE Network - TSE - .SMI-TSE	0	03-Nov-26		236	0	0	0
JDH	Start of Road Works - RD - .SMI-RD	0	03-Nov-26		346	0	0	0
JDH3-02-009-Engineering - EN		15	03-Nov-26	19-Nov-26	278	0	0	0
JDH3-02-009-Shop Drawings - SD		15	03-Nov-26	19-Nov-26	278	0	0	0
JDH3-02-009-Shop Drawing Submittals - SUB		5	03-Nov-26	08-Nov-26	278	0	0	0
JDH3-02-009-Shop Drawing Submittals - SUB-Z05		5	03-Nov-26	08-Nov-26	278	0	0	0
Prepare and Submit Drawing for Street Lighting Network for Z05		5	03-Nov-26	08-Nov-26	82	0	0	0
Prepare and Submit Drawing for Electrical Network for Z05-SD-E		5	03-Nov-26	08-Nov-26	136	0	0	0
Prepare and Submit Drawing for Telecommunication Network fo		5	03-Nov-26	08-Nov-26	278	0	0	0
JDH3-02-009-Shop Drawing Approvals - APP		10	09-Nov-26	19-Nov-26	278	0	0	0
JDH3-02-009-Shop Drawing Approvals - APP-Z05		10	09-Nov-26	19-Nov-26	278	0	0	0
Review and Approval for Street Lighting Network for Z05-SD-SL-		10	09-Nov-26	19-Nov-26	82	0	0	0
Review and Approval for Electrical Network for Z05-SD-EL-APP		10	09-Nov-26	19-Nov-26	136	0	0	0
Review and Approval for Telecommunication Network for Z05-SI		10	09-Nov-26	19-Nov-26	278	0	0	0
JDH3-02-009-Procurement -PR		134	14-Jul-26 A	01-Jan-27	364	0	1,491,219	1,669,629
Long Lead Items		51	03-Nov-26	01-Jan-27	184	0	0	0
JDH3-02-009-Material Purchase Order - PO		10	21-Nov-26	01-Dec-26	182	0	0	0
JDH3-Material Purchase Order - PO-Electrical Network - EL		10	21-Nov-26	01-Dec-26	138	0	0	0
Material Purchase Order for MV Cables - PR-EL-PO		10	21-Nov-26	01-Dec-26	138	0	0	0
JDH3-Material Purchase Order - PO-Street Lighting Network -SI		10	21-Nov-26	01-Dec-26	182	0	0	0
Material Purchase Order for Cables&Conductors - PR-SL-PO		10	21-Nov-26	01-Dec-26	182	0	0	0
JDH3-02-009-Material Manufacturing- FAB		60	03-Nov-26	01-Jan-27	223	0	0	0
JDH3-Material Purchase Order - PO-Potable Water Network - W		60	03-Nov-26	01-Jan-27	186	0	0	0
Material Fabrication for Valves - PR-WT-FAB		60	03-Nov-26	01-Jan-27	186	0	0	0
JDH3-Material Purchase Order - PO-TSE Network - TSE		60	03-Nov-26	01-Jan-27	223	0	0	0
Material Fabrication for Valves - PR-TSE-FAB		60	03-Nov-26	01-Jan-27	223	0	0	0
Short Lead items		103	14-Jul-26 A	01-Jan-27	364	0	1,491,219	1,669,629
JDH3-02-009-Material Purchase Order - PO		5	21-Nov-26	25-Nov-26	278	0	0	0
JDH3-Material Purchase Order - PO-Electrical Network - EL		5	21-Nov-26	25-Nov-26	136	0	0	0
Material Purchase Order for Ducts - PR-EL-PO		5	21-Nov-26	25-Nov-26	136	0	0	0
JDH3-Material Purchase Order - PO-Street Lighting Network -SI		5	21-Nov-26	25-Nov-26	82	0	0	0
Material Purchase Order for Lighting Columns - PR-SL-PO		5	21-Nov-26	25-Nov-26	82	0	0	0

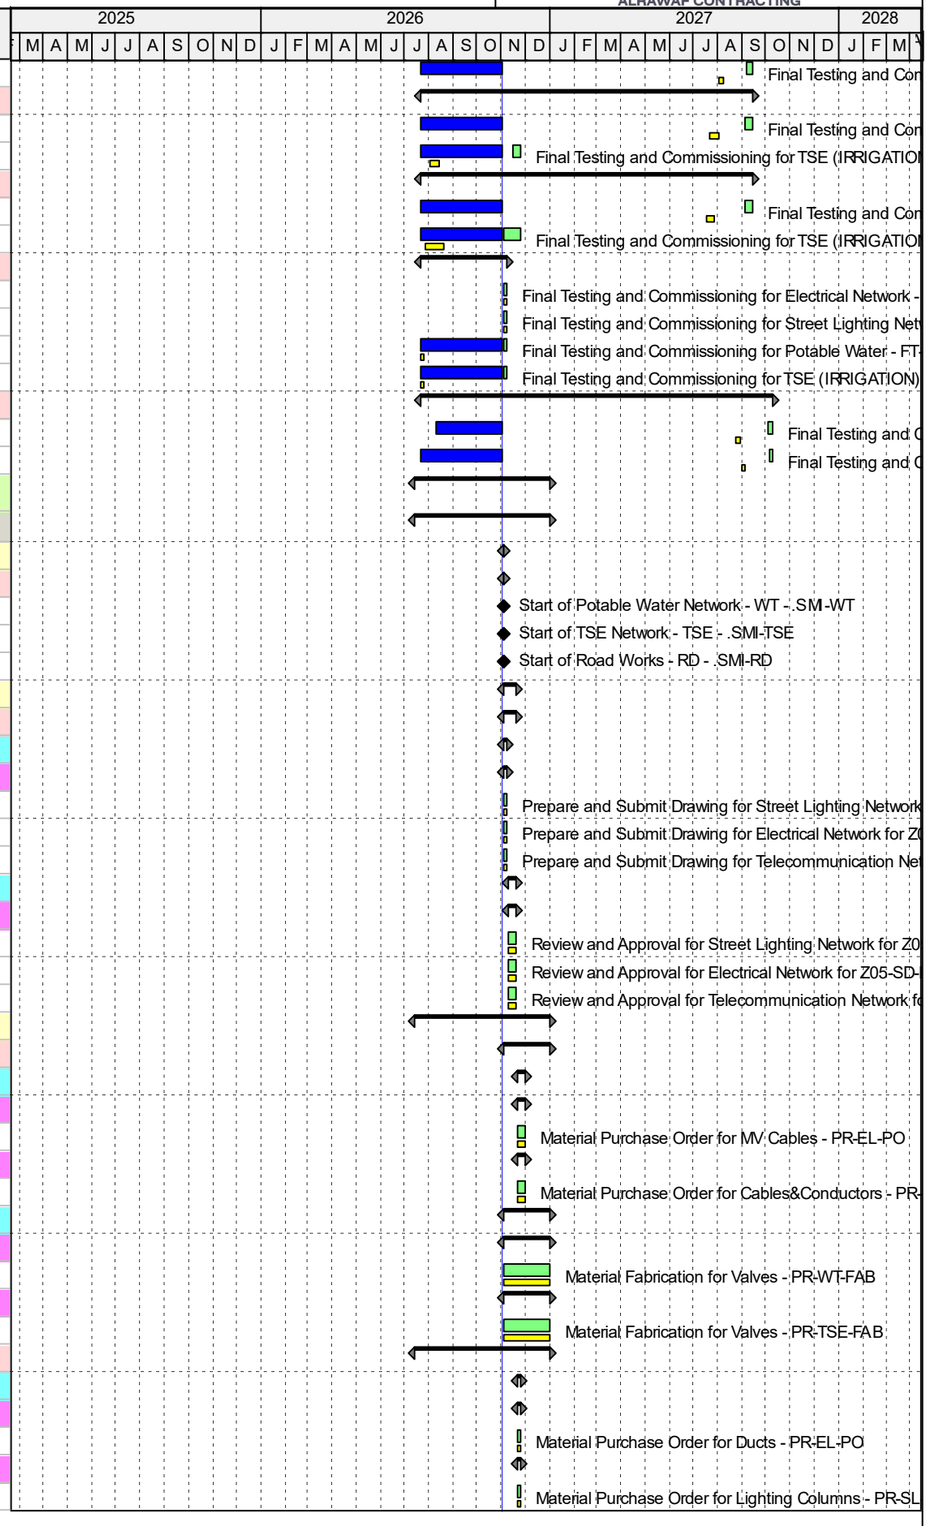

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-Material Purchase Order - PO-Telecommunications Netw	5	21-Nov-26	25-Nov-26	278	0	0	0
	Material Purchase Order for Duct Manhole - PR-TC-PO	5	21-Nov-26	25-Nov-26	278	0	0	0
	JDH3-02-009-Material Delivery and staging on Site - DOS	83	14-Jul-26 A	01-Jan-27	440	0	1,491,219	1,669,629
	JDH3-02-009-Material Delivery and staging on Site - DOS-Z03	83	14-Jul-26 A	01-Jan-27	440	0	1,491,219	1,669,629
	JDH3-02-009-Material Delivery and staging on Site - DOS-Se	73	28-Jul-26 A	01-Jan-27	440	0	655,124	715,983
	delivery and staging for GRP pipes - PR-SS-Z05-DOS	45	28-Jul-26 A	17-Dec-26	455	0	315,032	357,991
	delivery and staging for Metal Works (Stairs - Covers) - PR-SS-Z	60	06-Aug-26 A	01-Jan-27	440	0	340,092	357,991
	JDH3-02-009-Material Delivery and staging on Site - DOS-Stc	60	14-Jul-26 A	01-Jan-27	440	0	825,478	882,864
	delivery and staging for GRP pipes - PR-ST-Z05-DOS	30	14-Jul-26 A	02-Dec-26	470	0	406,117	441,432
	delivery and staging for Metal Works (Stairs - Covers) - PR-ST-Z(	60	06-Aug-26 A	01-Jan-27	133	0	419,360	441,432
	JDH3-02-009-Material Delivery and staging on Site - DOS-Tel	10	17-Sep-26 A	25-Nov-26	335	0	10,617	70,782
	delivery and staging for Duct Manhole - PR-TC-Z05-DOS	10	17-Sep-26 A	25-Nov-26	335	0	10,617	70,782
	JDH3-02-009-Execution	86	18-Aug-26 A	28-Nov-26	394	0	515,024	5,611,967
	Earthworks - EW	55	22-Sep-26 A	25-Nov-26	324	0	197,644	1,782,430
	JDH3-02-009-R01-Road Works - RW	55	22-Sep-26 A	25-Nov-26	324	0	197,644	1,782,430
	Z05	55	22-Sep-26 A	25-Nov-26	324	0	197,644	1,782,430
	JDH3-02-009-Road Works - RWZ3-R6605	41	22-Sep-26 A	10-Nov-26	338	0	105,673	314,206
	Backfill Layers with Imported Material Side Walk for Road - (B1.:	4	05-Nov-26	10-Nov-26	338	0	0	55,741
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R6605-RW	4	22-Sep-26 A	05-Nov-26	338	0	72,892	182,230
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	28-Sep-26 A	05-Nov-26	338	0	32,781	76,235
	JDH3-02-009-Road Works - RWZ3-R4019	18	20-Oct-26 A	10-Nov-26	136	0	21,318	207,529
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	3	07-Nov-26	10-Nov-26	136	0	0	110,628
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	20-Oct-26 A	07-Nov-26	136	0	21,318	96,901
	JDH3-02-009-Road Works - RWZ3-R4017	12	03-Nov-26	16-Nov-26	325	0	0	205,202
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	03-Nov-26	07-Nov-26	187	0	0	84,343
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4	12-Nov-26	16-Nov-26	134	0	0	90,569
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R4017-RW	4	03-Nov-26	07-Nov-26	333	0	0	30,290
	JDH3-02-009-Road Works - RWZ3-R40151	10	15-Oct-26 A	21-Nov-26	134	0	18,477	290,368
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R401511-RW	4	03-Nov-26	07-Nov-26	142	0	0	70,224
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	08-Nov-26	11-Nov-26	142	0	0	111,456
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	3	15-Oct-26 A	21-Nov-26	134	0	18,477	108,688
	JDH3-02-009-Road Works - RWZ3-R40152	20	03-Nov-26	25-Nov-26	145	0	0	290,368
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R401512-RW	4	03-Nov-26	07-Nov-26	134	0	0	70,224
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	08-Nov-26	11-Nov-26	153	0	0	111,456
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4	22-Nov-26	25-Nov-26	145	0	0	108,688
	JDH3-02-009-Road Works - RWZ3-R4016	12	08-Nov-26	21-Nov-26	134	0	0	183,389
	Excavation Works for Road - (B1.31 22 00.01)-Z5-R4016-RW	4	08-Nov-26	11-Nov-26	134	0	0	44,730
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4	17-Nov-26	21-Nov-26	134	0	0	89,863
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	12-Nov-26	16-Nov-26	134	0	0	48,796
	JDH3-02-009-Road Works - RWZ3-R4018	8	22-Sep-26 A	07-Nov-26	135	0	52,176	291,367
	Backfill Layers Works Excavated Material for Road - (B1.31 22 (	4	22-Sep-26 A	07-Nov-26	135	0	25,553	170,356
	Backfill Layers with Imported Material TOE for Road - (B1.31 22	4	27-Sep-26 A	07-Nov-26	135	0	26,622	121,010
	Z05	86	18-Aug-26 A	28-Nov-26	394	0	317,380	3,829,538
	R40151	36	22-Sep-26 A	25-Nov-26	395	0	199,399	1,201,242
	JDH3-02-009-R40151-Sewage Network - SW	36	22-Sep-26 A	25-Nov-26	362	0	199,399	763,072
	JDH3-02-009-R40151-(SW)-GRP Pipes-600 mm diameter dep	36	22-Sep-26 A	25-Nov-26	358	0	199,399	717,835
	Primary Test for (SW)-GRP Pipes-600 mm diameter depth from	4	22-Nov-26	25-Nov-26	358	0	0	79,759
	Bedding Works for (SW)-GRP Pipes-600 mm diameter depth fro	4	23-Sep-26 A	21-Nov-26	358	0	5,982	39,880
	Installing for (SW)-GRP Pipes-600 mm diameter depth from 4.5	4	24-Sep-26 A	21-Nov-26	358	0	65,802	438,677
	Excavation Works for (SW)-GRP Pipes-600 mm diameter depth	4	22-Sep-26 A	21-Nov-26	346	0	127,615	159,519
	JDH3-02-009-R40151-(SW)-GRP Pipes-150 mm diameter dep	4	22-Nov-26	25-Nov-26	346	0	0	14,775
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4	22-Nov-26	25-Nov-26	346	0	0	14,775
	JDH3-02-009-R40151-(SW)-MH Works depth from 1.51 to 2.5	16	03-Nov-26	21-Nov-26	366	0	0	30,462

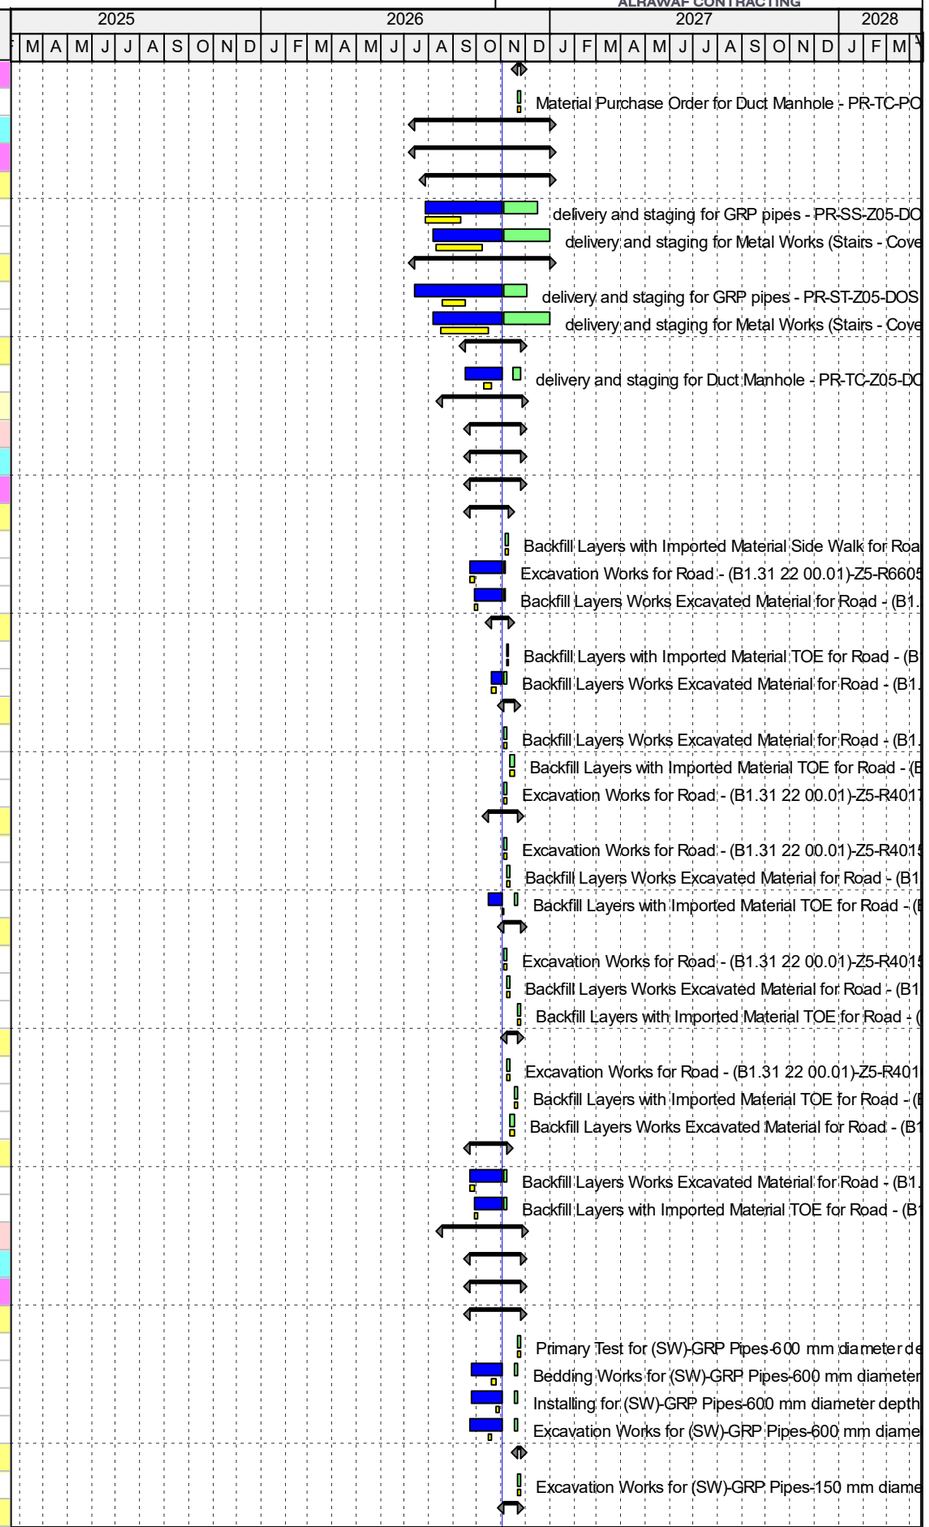


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4	03-Nov-26	07-Nov-26	366	0	0	10,154
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4	08-Nov-26	11-Nov-26	366	0	0	14,215
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4	12-Nov-26	16-Nov-26	366	0	0	4,062
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	4	17-Nov-26	21-Nov-26	366	0	0	2,031
	JDH3-02-009-R40151-Storm Network - ST	20	03-Nov-26	25-Nov-26	395	0	0	126,220
	JDH3-02-009-R40151-(ST)-GRP Pipes-400 mm diameter dept	20	03-Nov-26	25-Nov-26	391	0	0	31,802
	Excavation Works for GRP Pipe Line 400 mm - depth from 1.51	4	03-Nov-26	07-Nov-26	391	0	0	6,360
	Bedding Works for GRP Pipe Line 400 mm - depth from 1.51 to	4	08-Nov-26	11-Nov-26	391	0	0	1,590
	Installing for GRP Pipe Line 400 mm - depth from 1.51 to 2.00	4	12-Nov-26	16-Nov-26	391	0	0	17,491
	Primary Test for GRP Pipe Line 400 mm - depth from 1.51 to 2.	4	17-Nov-26	21-Nov-26	391	0	0	3,180
	Backfilling and warning tape Works for GRP Pipe Line 400 mm	4	22-Nov-26	25-Nov-26	391	0	0	3,180
	JDH3-02-009-R40151-(ST)-GRP Pipes-700 mm diameter dept	16	08-Nov-26	25-Nov-26	391	0	0	75,636
	Excavation Works for (ST)-GRP Pipes-700 mm diameter depth f	4	08-Nov-26	11-Nov-26	391	0	0	16,808
	Bedding Works for (ST)-GRP Pipes-700 mm diameter depth fro	4	12-Nov-26	16-Nov-26	391	0	0	4,202
	Installing for (ST)-GRP Pipes-700 mm diameter depth from 2.01	4	17-Nov-26	21-Nov-26	391	0	0	46,222
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4	22-Nov-26	25-Nov-26	391	0	0	8,404
	JDH3-02-009-R40151-(ST)-GRP Pipes-900 mm diameter dept	4	03-Nov-26	07-Nov-26	411	0	0	18,782
	Primary Test for (ST)-GRP Pipes-900 mm diameter depth from 2	4	03-Nov-26	07-Nov-26	411	0	0	18,782
	JDH3-02-009-R40151-Potable Water Network - WT	20	03-Nov-26	25-Nov-26	322	0	0	157,340
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	20	03-Nov-26	25-Nov-26	322	0	0	976
	Excavation Works for (WT)-HDPE Pipes-225 mm diameter depth	4	03-Nov-26	07-Nov-26	322	0	0	195
	Bedding Works for (WT)-HDPE Pipes-225 mm diameter depth fi	4	08-Nov-26	11-Nov-26	322	0	0	49
	Installing for (WT)-HDPE Pipes-225 mm diameter depth from 3.5	4	12-Nov-26	16-Nov-26	322	0	0	537
	Primary Test for (WT)-HDPE Pipes-225 mm diameter depth from	4	17-Nov-26	21-Nov-26	322	0	0	98
	Backfilling and warning tape Works for (WT)-HDPE Pipes-225 m	4	22-Nov-26	25-Nov-26	322	0	0	98
	JDH3-02-009-R40151-(WT)-Fire Hydrant	4	08-Nov-26	11-Nov-26	322	0	0	9,771
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	4	08-Nov-26	11-Nov-26	322	0	0	9,771
	JDH3-02-009-R40151-(WT)-Air Valve Chamber on 225 mm dia	11	08-Nov-26	19-Nov-26	212	0	0	5,711
	Excavation+Bedding for Air Valve Chamber on pipe dia 225 mm	3	08-Nov-26	10-Nov-26	212	0	0	1,071
	PC Worksfor Air Valve Chamber on pipe dia 225 mm - depth fro	4	11-Nov-26	15-Nov-26	212	0	0	714
	Installationfor Air Valve Chamber on pipe dia 225 mm - depth fr	4	16-Nov-26	19-Nov-26	212	0	0	3,926
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	4	22-Nov-26	25-Nov-26	306	0	0	5,031
	Excavation Works for HDPE Pipe Line 225 mm - depth from 2.5	4	22-Nov-26	25-Nov-26	306	0	0	5,031
	JDH3-02-009-R40151-(WT)-HDPE Pipes-225 mm diameter de	20	03-Nov-26	25-Nov-26	207	0	0	135,850
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	4	03-Nov-26	07-Nov-26	207	0	0	27,170
	Bedding Works for HDPE Pipe Line 225 mm - depth from 1.51 t	4	08-Nov-26	11-Nov-26	207	0	0	6,793
	Installing for HDPE Pipe Line 225 mm - depth from 1.51 to 2.5	4	12-Nov-26	16-Nov-26	207	0	0	74,718
	Primary Test for HDPE Pipe Line 225 mm - depth from 1.51 to 2	4	17-Nov-26	21-Nov-26	207	0	0	13,585
	Backfilling and warning tape Works for HDPE Pipe Line 225 mm	4	22-Nov-26	25-Nov-26	207	0	0	13,585
	JDH3-02-009-R40151-Road Works - RD	20	03-Nov-26	25-Nov-26	318	0	0	154,611
	JDH3-02-009-R40151-(RD)-Subgrade	4	22-Nov-26	25-Nov-26	134	0	0	152,984
	Supply, lay and compaction subgrade compacted thickness 300	4	22-Nov-26	25-Nov-26	134	0	0	152,984
	JDH3-02-009-R40151-(RD)-Precast Concrete Curb	4	03-Nov-26	07-Nov-26	334	0	0	1,627
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	03-Nov-26	07-Nov-26	334	0	0	1,627
	R40152	20	03-Nov-26	25-Nov-26	362	0	0	435,562
	JDH3-02-009-R40152-Sewage Network - SW	20	03-Nov-26	25-Nov-26	362	0	0	276,927
	JDH3-02-009-R40152-(SW)-GRP Pipes-600 mm diameter dep	8	03-Nov-26	11-Nov-26	370	0	0	4,967
	Primary Test for (SW)-GRP Pipes-600 mm diameter depth from	4	03-Nov-26	07-Nov-26	370	0	0	2,484
	Backfilling and warning tape Works for (SW)-GRP Pipes-600 mm	4	08-Nov-26	11-Nov-26	370	0	0	2,484
	JDH3-02-009-R40152-(SW)-GRP Pipes-150 mm diameter dep	20	03-Nov-26	25-Nov-26	362	0	0	33,015
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4	03-Nov-26	07-Nov-26	362	0	0	6,603
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4	08-Nov-26	11-Nov-26	362	0	0	1,651
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0 to	4	12-Nov-26	16-Nov-26	362	0	0	18,158

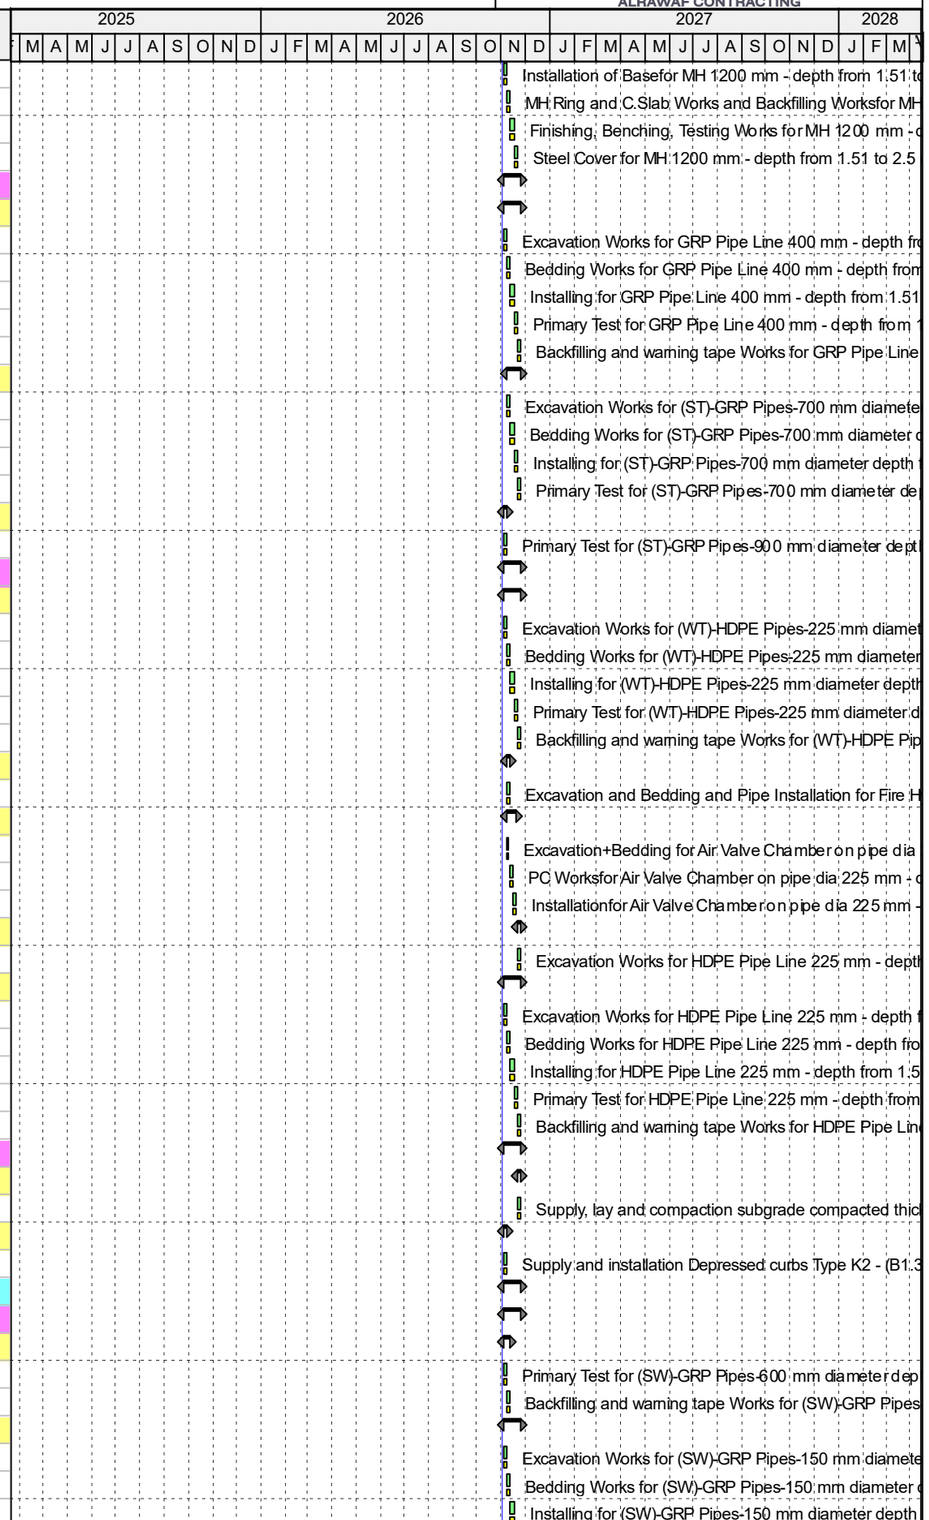


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4	17-Nov-26	21-Nov-26	362	0	0	3,301
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4	22-Nov-26	25-Nov-26	362	0	0	3,301
	JDH3-02-009-R40152-(SW)-MH Works depth from 1.51 to 2.5	13	03-Nov-26	17-Nov-26	369	0	0	109,662
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	3	03-Nov-26	05-Nov-26	369	0	0	36,554
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 r	4	07-Nov-26	10-Nov-26	369	0	0	51,175
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	3	11-Nov-26	14-Nov-26	369	0	0	14,622
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	3	15-Nov-26	17-Nov-26	369	0	0	7,311
	JDH3-02-009-R40152-(SW)-MH Works depth from 4.51 to 5.5	16	03-Nov-26	21-Nov-26	362	0	0	36,788
	Installation of Basefor MH 1200 mm - depth from 4.51 to 5.5 m	4	03-Nov-26	07-Nov-26	362	0	0	12,263
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 r	4	08-Nov-26	11-Nov-26	362	0	0	17,168
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4	12-Nov-26	16-Nov-26	362	0	0	4,905
	Steel Cover for MH 1200 mm - depth from 4.51 to 5.5 m- (B5.3	4	17-Nov-26	21-Nov-26	362	0	0	2,453
	JDH3-02-009-R40152-(SW)-MH Works depth from 5.51 to 6.5	20	03-Nov-26	25-Nov-26	362	0	0	92,495
	Installation of Basefor MH 1200 mm - depth from 5.51 to 6.5 m	4	03-Nov-26	07-Nov-26	366	0	0	30,832
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 r	4	08-Nov-26	11-Nov-26	366	0	0	43,164
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4	17-Nov-26	21-Nov-26	362	0	0	12,333
	Steel Cover for MH 1200 mm - depth from 5.51 to 6.5 m- (B5.3	4	22-Nov-26	25-Nov-26	362	0	0	6,166
	JDH3-02-009-R40152-Storm Network - ST	20	03-Nov-26	25-Nov-26	358	0	0	158,635
	JDH3-02-009-R40152-(ST)-GRP Pipes-1100 mm diameter dep	20	03-Nov-26	25-Nov-26	358	0	0	75,256
	Excavation Works for GRP Pipe Line 1100 mm - depth from 2.0	4	03-Nov-26	07-Nov-26	358	0	0	15,051
	Bedding Works for GRP Pipe Line 1100 mm - depth from 2.01 t	4	08-Nov-26	11-Nov-26	358	0	0	3,763
	Installing for GRP Pipe Line 1100 mm - depth from 2.01 to 2.50	4	12-Nov-26	16-Nov-26	358	0	0	41,391
	Primary Test for GRP Pipe Line 1100 mm - depth from 2.01 to 2	4	17-Nov-26	21-Nov-26	358	0	0	7,526
	Backfilling and warning tape Works for GRP Pipe Line 1100 mm	4	22-Nov-26	25-Nov-26	358	0	0	7,526
	JDH3-02-009-R40152-(ST)-GRP Pipes-1100 mm diameter dep	16	08-Nov-26	25-Nov-26	358	0	0	83,379
	Excavation Works for GRP Pipe Line 1100 mm - depth from 2.5	4	08-Nov-26	11-Nov-26	358	0	0	18,529
	Bedding Works for GRP Pipe Line 1100 mm - depth from 2.51 t	4	12-Nov-26	16-Nov-26	358	0	0	4,632
	Installing for GRP Pipe Line 1100 mm - depth from 2.51 to 3.00	4	17-Nov-26	21-Nov-26	358	0	0	50,954
	Primary Test for GRP Pipe Line 1100 mm - depth from 2.51 to 3	4	22-Nov-26	25-Nov-26	358	0	0	9,264
	R4016	67	08-Sep-26 A	25-Nov-26	395	0	16,683	419,680
	JDH3-02-009-R4016-Sewage Network - SW	55	22-Sep-26 A	25-Nov-26	362	0	12,595	185,524
	JDH3-02-009-R4016-(SW)-GRP Pipes-150 mm diameter deptl	20	03-Nov-26	25-Nov-26	342	0	0	45,076
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4	03-Nov-26	07-Nov-26	342	0	0	9,015
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4	08-Nov-26	11-Nov-26	342	0	0	2,254
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4	12-Nov-26	16-Nov-26	342	0	0	24,792
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4	17-Nov-26	21-Nov-26	342	0	0	4,508
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4	22-Nov-26	25-Nov-26	342	0	0	4,508
	JDH3-02-009-R4016-(SW)-GRP Pipes-250 mm diameter deptl	4	03-Nov-26	07-Nov-26	358	0	0	4,110
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4	03-Nov-26	07-Nov-26	358	0	0	4,110
	JDH3-02-009-R4016-(SW)-GRP Pipes-250 mm diameter deptl	4	03-Nov-26	07-Nov-26	362	0	0	3,364
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4	03-Nov-26	07-Nov-26	362	0	0	3,364
	JDH3-02-009-R4016-(SW)-GRP Pipes-300 mm diameter deptl	4	03-Nov-26	07-Nov-26	366	0	0	5,635
	Primary Test for (SW)-GRP Pipes-300 mm diameter depth from	4	03-Nov-26	07-Nov-26	366	0	0	5,635
	JDH3-02-009-R4016-(SW)-MH Works depth from 1.51 to 2.5 [	42	22-Sep-26 A	10-Nov-26	363	0	7,108	68,234
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 r	4	07-Nov-26	10-Nov-26	363	0	0	39,803
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4	22-Sep-26 A	05-Nov-26	363	0	7,108	28,431
	JDH3-02-009-R4016-(SW)-MH Works depth from 2.51 to 3.5 [	42	22-Sep-26 A	10-Nov-26	367	0	5,487	52,675
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 r	4	07-Nov-26	10-Nov-26	367	0	0	30,727
	Installation of Basefor MH 1200 mm - depth from 2.51 to 3.5 m	4	22-Sep-26 A	05-Nov-26	367	0	5,487	21,948
	JDH3-02-009-R4016-(SW)-GRP Pipes-200 mm diameter deptl	8	03-Nov-26	11-Nov-26	370	0	0	3,386
	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	4	03-Nov-26	07-Nov-26	370	0	0	1,693
	Backfilling and warning tape Works for GRP Pipe Line 200 mm	4	08-Nov-26	11-Nov-26	370	0	0	1,693
	JDH3-02-009-R4016-(SW)-GRP Pipes-150 mm diameter deptl	12	03-Nov-26	16-Nov-26	370	0	0	3,044

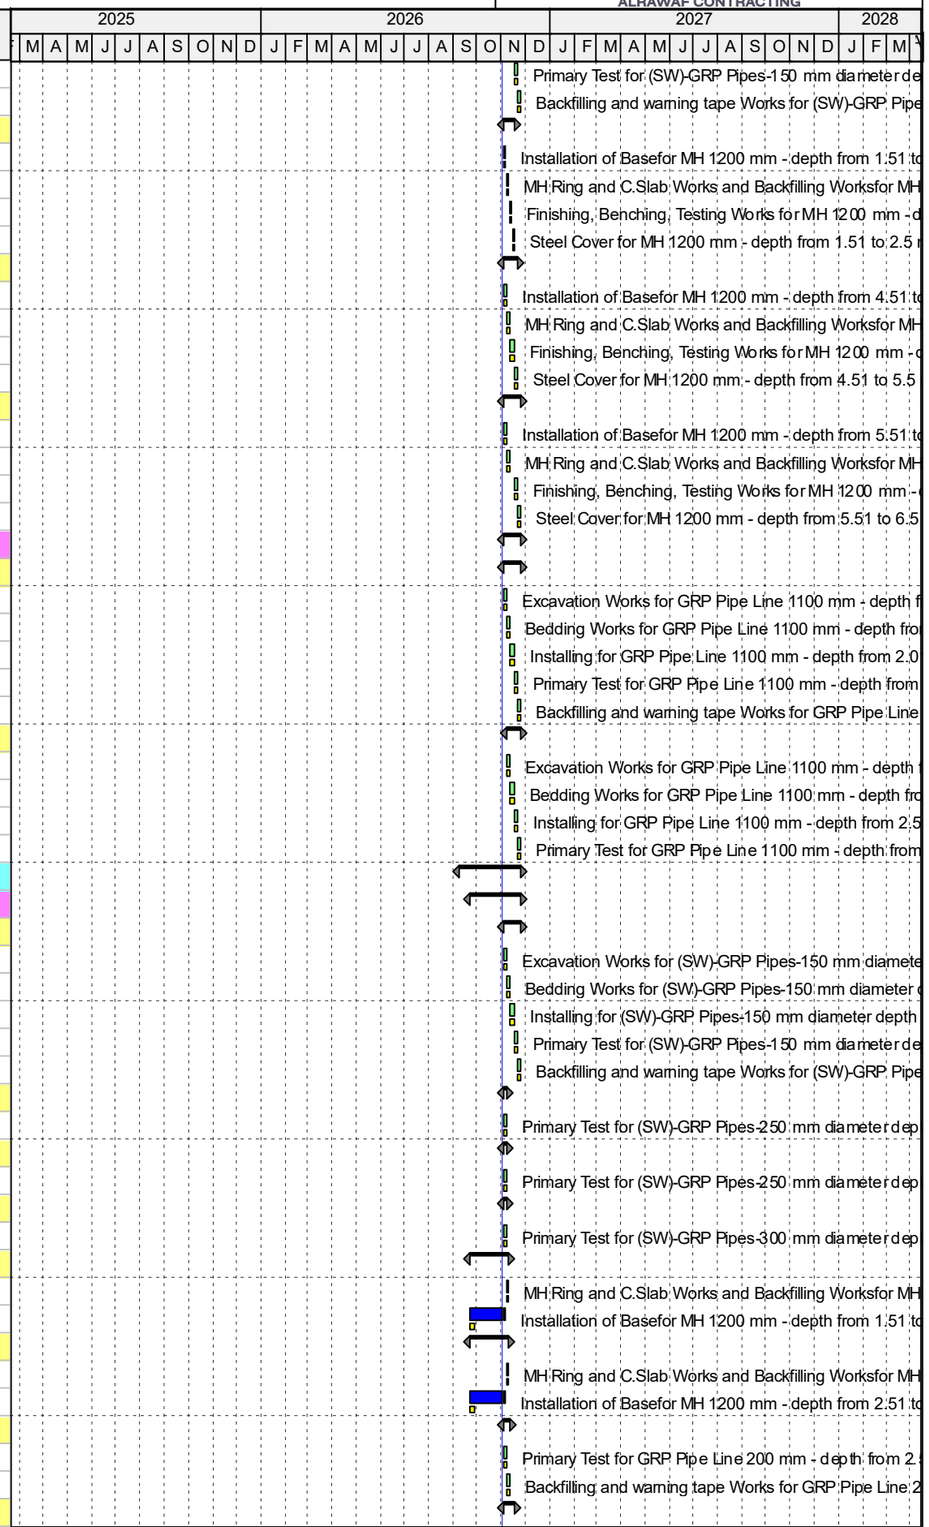


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for GRP Pipe Line 150 mm - depth from 2.51 to 3.	4	03-Nov-26	07-Nov-26	374	0	0	1,522
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4	12-Nov-26	16-Nov-26	370	0	0	1,522
	JDH3-02-009-R4016-Storm Network - ST	65	08-Sep-26 A	23-Nov-26	397	0	4,089	78,161
	JDH3-02-009-R4016-(ST)-GRP Pipes-700 mm diameter depth	12	03-Nov-26	16-Nov-26	403	0	0	24,807
	Installing for (ST)-GRP Pipes-700 mm diameter depth from 2.0	4	03-Nov-26	07-Nov-26	403	0	0	18,192
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4	08-Nov-26	11-Nov-26	403	0	0	3,308
	Backfilling and warning tape Works for (ST)-GRP Pipes-700 mm	4	12-Nov-26	16-Nov-26	403	0	0	3,308
	JDH3-02-009-R4016-(ST)-GRP Pipes-800 mm diameter depth	4	03-Nov-26	07-Nov-26	411	0	0	3,674
	Primary Test for GRP Pipe Line 800 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	411	0	0	3,674
	JDH3-02-009-R4016-(ST)-GRP Pipes-600 mm diameter depth	65	08-Sep-26 A	23-Nov-26	397	0	4,089	34,073
	Bedding Works for GRP Pipe Line 600 mm - depth from 1.51 to	4	04-Nov-26	09-Nov-26	397	0	0	1,704
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4	09-Nov-26	14-Nov-26	397	0	0	18,740
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.	4	14-Nov-26	18-Nov-26	397	0	0	3,407
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	4	18-Nov-26	23-Nov-26	397	0	0	3,407
	Excavation Works for GRP Pipe Line 600 mm - depth from 1.51	4	08-Sep-26 A	04-Nov-26	397	0	4,089	6,815
	JDH3-02-009-R4016-(ST)-GRP Pipes-800 mm diameter depth	3	03-Nov-26	05-Nov-26	412	0	0	15,607
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.	3	03-Nov-26	05-Nov-26	412	0	0	15,607
	JDH3-02-009-R4016-Potable Water Network - WT	20	03-Nov-26	25-Nov-26	223	0	0	29,512
	JDH3-02-009-R4016-(WT)-HDPE Pipes-160 mm diameter dep	8	17-Nov-26	25-Nov-26	179	0	0	13,461
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	4	17-Nov-26	21-Nov-26	179	0	0	10,769
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4	22-Nov-26	25-Nov-26	179	0	0	2,692
	JDH3-02-009-R4016-(WT)-HDPE Pipes-160 mm diameter dep	4	22-Nov-26	25-Nov-26	179	0	0	574
	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	4	22-Nov-26	25-Nov-26	179	0	0	574
	JDH3-02-009-R4016-(WT)-Plot Connection	4	03-Nov-26	07-Nov-26	239	0	0	15,477
	HDPE road crossing with dia 110 mm (Including end cap, isolati	4	03-Nov-26	07-Nov-26	239	0	0	15,477
	JDH3-02-009-R4016-Road Works - RD	4	22-Nov-26	25-Nov-26	134	0	0	126,483
	JDH3-02-009-R4016-(RD)-Subgrade	4	22-Nov-26	25-Nov-26	134	0	0	126,483
	Supply, lay and compaction subgrade compacted thickness 300	4	22-Nov-26	25-Nov-26	134	0	0	126,483
	R4017	61	15-Sep-26 A	26-Nov-26	395	0	59,893	454,182
	JDH3-02-009-R4017-Sewage Network - SW	61	15-Sep-26 A	26-Nov-26	362	0	59,893	193,617
	JDH3-02-009-R4017-(SW)-GRP Pipes-150 mm diameter deptl	49	15-Sep-26 A	12-Nov-26	358	0	38,773	51,017
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4	03-Nov-26	08-Nov-26	358	0	0	5,102
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4	08-Nov-26	12-Nov-26	358	0	0	5,102
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4	15-Sep-26 A	03-Nov-26	358	0	9,693	10,203
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4	21-Sep-26 A	03-Nov-26	358	0	26,656	28,059
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4	20-Sep-26 A	03-Nov-26	358	0	2,423	2,551
	JDH3-02-009-R4017-(SW)-GRP Pipes-250 mm diameter deptl	12	03-Nov-26	17-Nov-26	358	0	0	12,084
	Primary Test for (SW)-GRP Pipes-250 mm diameter depth from	4	03-Nov-26	07-Nov-26	362	0	0	6,042
	Backfilling and warning tape Works for (SW)-GRP Pipes-250 mr	4	12-Nov-26	17-Nov-26	358	0	0	6,042
	JDH3-02-009-R4017-(SW)-GRP Pipes-300 mm diameter deptl	16	03-Nov-26	22-Nov-26	358	0	0	3,177
	Primary Test for (SW)-GRP Pipes-300 mm diameter depth from	4	03-Nov-26	07-Nov-26	366	0	0	1,588
	Backfilling and warning tape Works for (SW)-GRP Pipes-300 mr	4	17-Nov-26	22-Nov-26	358	0	0	1,588
	JDH3-02-009-R4017-(SW)-GRP Pipes-150 mm diameter deptl	20	03-Nov-26	26-Nov-26	358	0	0	5,679
	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	370	0	0	2,840
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4	22-Nov-26	26-Nov-26	358	0	0	2,840
	JDH3-02-009-R4017-(SW)-MH Works depth from 2.51 to 3.5 I	4	03-Nov-26	07-Nov-26	370	0	0	20,485
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4	03-Nov-26	07-Nov-26	370	0	0	20,485
	JDH3-02-009-R4017-(SW)-MH Works depth from 1.51 to 2.5 I	54	15-Sep-26 A	18-Nov-26	369	0	21,120	97,477
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4	04-Nov-26	09-Nov-26	369	0	0	45,489
	Finishing, Benching, Testing Works for MH 1200 mm - depth fro	4	09-Nov-26	14-Nov-26	369	0	0	12,997
	Steel Cover for MH 1200 mm - depth from 1.51 to 2.5 m- (B5.3	4	14-Nov-26	18-Nov-26	369	0	0	6,498
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4	15-Sep-26 A	04-Nov-26	369	0	21,120	32,492
	JDH3-02-009-R4017-(SW)-GRP Pipes-200 mm diameter deptl	4	03-Nov-26	07-Nov-26	374	0	0	3,699

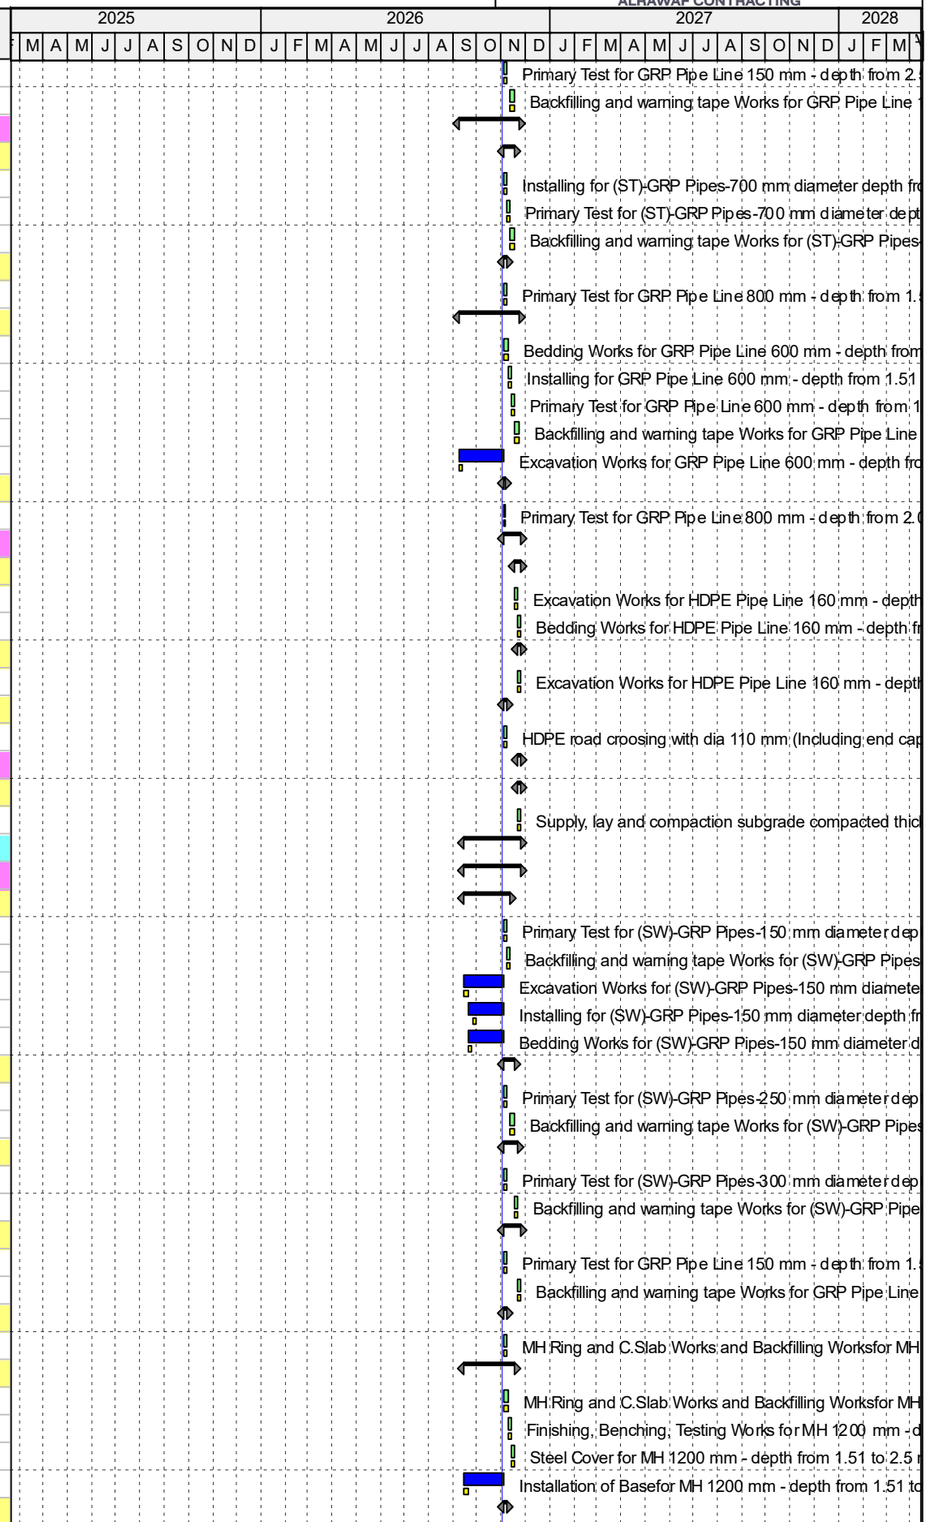


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Primary Test for GRP Pipe Line 200 mm - depth from 2.51 to 3.	4	03-Nov-26	07-Nov-26	374	0	0	3,699
	JDH3-02-009-R4017-Storm Network - ST	8	03-Nov-26	11-Nov-26	407	0	0	53,107
	JDH3-02-009-R4017-(ST)-GRP Pipes-800 mm diameter depth	4	03-Nov-26	07-Nov-26	411	0	0	11,000
	Primary Test for GRP Pipe Line 800 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	411	0	0	11,000
	JDH3-02-009-R4017-(ST)-GRP Pipes-600 mm diameter depth	8	03-Nov-26	11-Nov-26	374	0	0	25,603
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4	03-Nov-26	07-Nov-26	374	0	0	18,965
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.	2	08-Nov-26	09-Nov-26	374	0	0	3,319
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	2	10-Nov-26	11-Nov-26	374	0	0	3,319
	JDH3-02-009-R4017-(ST)-GRP Pipes-700 mm diameter depth	8	03-Nov-26	11-Nov-26	134	0	0	12,494
	Primary Test for GRP Pipe Line 700 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	134	0	0	6,247
	Backfilling and warning tape Works for GRP Pipe Line 700 mm	4	08-Nov-26	11-Nov-26	134	0	0	6,247
	JDH3-02-009-R4017-(ST)-GRP Pipes-800 mm diameter depth	3	03-Nov-26	05-Nov-26	412	0	0	4,011
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.	3	03-Nov-26	05-Nov-26	412	0	0	4,011
	JDH3-02-009-R4017-Catch Basins (Storm Network) - ST	4	22-Nov-26	25-Nov-26	134	0	0	18,865
	JDH3-02-009-R4017-(ST)-For Catch Basins (GRP) Pipes-300	4	22-Nov-26	25-Nov-26	134	0	0	18,865
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4	22-Nov-26	25-Nov-26	134	0	0	18,865
	JDH3-02-009-R4017-TSE Network - TSE	4	22-Nov-26	25-Nov-26	153	0	0	8,270
	JDH3-02-009-R4017-(TSE)-HDPE Pipes-110 mm diameter dep	4	22-Nov-26	25-Nov-26	153	0	0	8,270
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	4	22-Nov-26	25-Nov-26	153	0	0	8,270
	JDH3-02-009-R4017-Potable Water Network - WT	16	03-Nov-26	21-Nov-26	250	0	0	52,572
	JDH3-02-009-R4017-(WT)-HDPE Pipes-160 mm diameter dep	12	08-Nov-26	21-Nov-26	187	0	0	38,815
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	4	08-Nov-26	11-Nov-26	187	0	0	9,704
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4	12-Nov-26	16-Nov-26	187	0	0	2,426
	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m-	4	17-Nov-26	21-Nov-26	187	0	0	26,685
	JDH3-02-009-R4017-(WT)-Plot Connection	4	03-Nov-26	07-Nov-26	262	0	0	13,757
	HDPE road croosing with dia 110 mm (Including end cap, isolati	4	03-Nov-26	07-Nov-26	262	0	0	13,757
	JDH3-02-009-R4017-Telecommunications Network - TEL	3	22-Nov-26	24-Nov-26	142	0	0	286
	JDH3-02-009-R4017-(TEL)-Reinforced Concrete Duct 6-ways	3	22-Nov-26	24-Nov-26	142	0	0	286
	Excavation Works for RC Duct 6-ways ducts, 50mm- (B2.33 71	3	22-Nov-26	24-Nov-26	142	0	0	286
	JDH3-02-009-R4017-Road Works - RD	4	17-Nov-26	21-Nov-26	134	0	0	127,464
	JDH3-02-009-R4017-(RD)-Subgrade	4	17-Nov-26	21-Nov-26	134	0	0	127,464
	Supply, lay and compaction subgrade compacted thickness 300	4	17-Nov-26	21-Nov-26	134	0	0	127,464
	R4018	67	08-Sep-26 A	26-Nov-26	395	0	8,184	700,005
	JDH3-02-009-R4018-Sewage Network - SW	67	08-Sep-26 A	25-Nov-26	359	0	8,184	122,321
	JDH3-02-009-R4018-(SW)-GRP Pipes-150 mm diameter depth	20	03-Nov-26	25-Nov-26	359	0	0	58,961
	Excavation Works for (SW)-GRP Pipes-150 mm diameter depth	4	03-Nov-26	07-Nov-26	359	0	0	11,792
	Bedding Works for (SW)-GRP Pipes-150 mm diameter depth fro	4	08-Nov-26	11-Nov-26	359	0	0	2,948
	Installing for (SW)-GRP Pipes-150 mm diameter depth from 0.0	4	12-Nov-26	16-Nov-26	359	0	0	32,429
	Primary Test for (SW)-GRP Pipes-150 mm diameter depth from	4	17-Nov-26	21-Nov-26	359	0	0	5,896
	Backfilling and warning tape Works for (SW)-GRP Pipes-150 mr	4	22-Nov-26	25-Nov-26	359	0	0	5,896
	JDH3-02-009-R4018-(SW)-MH Works depth from 1.51 to 2.5 [	54	08-Sep-26 A	10-Nov-26	369	0	8,184	63,360
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4	07-Nov-26	10-Nov-26	369	0	0	36,960
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	3	08-Sep-26 A	05-Nov-26	369	0	8,184	26,400
	JDH3-02-009-R4018-Storm Network - ST	16	03-Nov-26	21-Nov-26	399	0	0	66,084
	JDH3-02-009-R4018-(ST)-GRP Pipes-400 mm diameter depth	8	03-Nov-26	11-Nov-26	374	0	0	1,704
	Primary Test for (ST)-GRP Pipes-400 mm diameter depth from 1	4	03-Nov-26	07-Nov-26	374	0	0	852
	Backfilling and warning tape Works for (ST)-GRP Pipes-400 mm	4	08-Nov-26	11-Nov-26	374	0	0	852
	JDH3-02-009-R4018-(ST)-GRP Pipes-700 mm diameter depth	8	03-Nov-26	11-Nov-26	374	0	0	6,597
	Primary Test for (ST)-GRP Pipes-700 mm diameter depth from 2	4	03-Nov-26	07-Nov-26	374	0	0	3,299
	Backfilling and warning tape Works for (ST)-GRP Pipes-700 mm	4	08-Nov-26	11-Nov-26	374	0	0	3,299
	JDH3-02-009-R4018-(ST)-GRP Pipes-600 mm diameter depth	12	03-Nov-26	16-Nov-26	399	0	0	40,426
	Installing for GRP Pipe Line 600 mm - depth from 1.51 to 2.00	4	03-Nov-26	07-Nov-26	399	0	0	29,646
	Primary Test for GRP Pipe Line 600 mm - depth from 1.51 to 2.	4	08-Nov-26	11-Nov-26	399	0	0	5,390

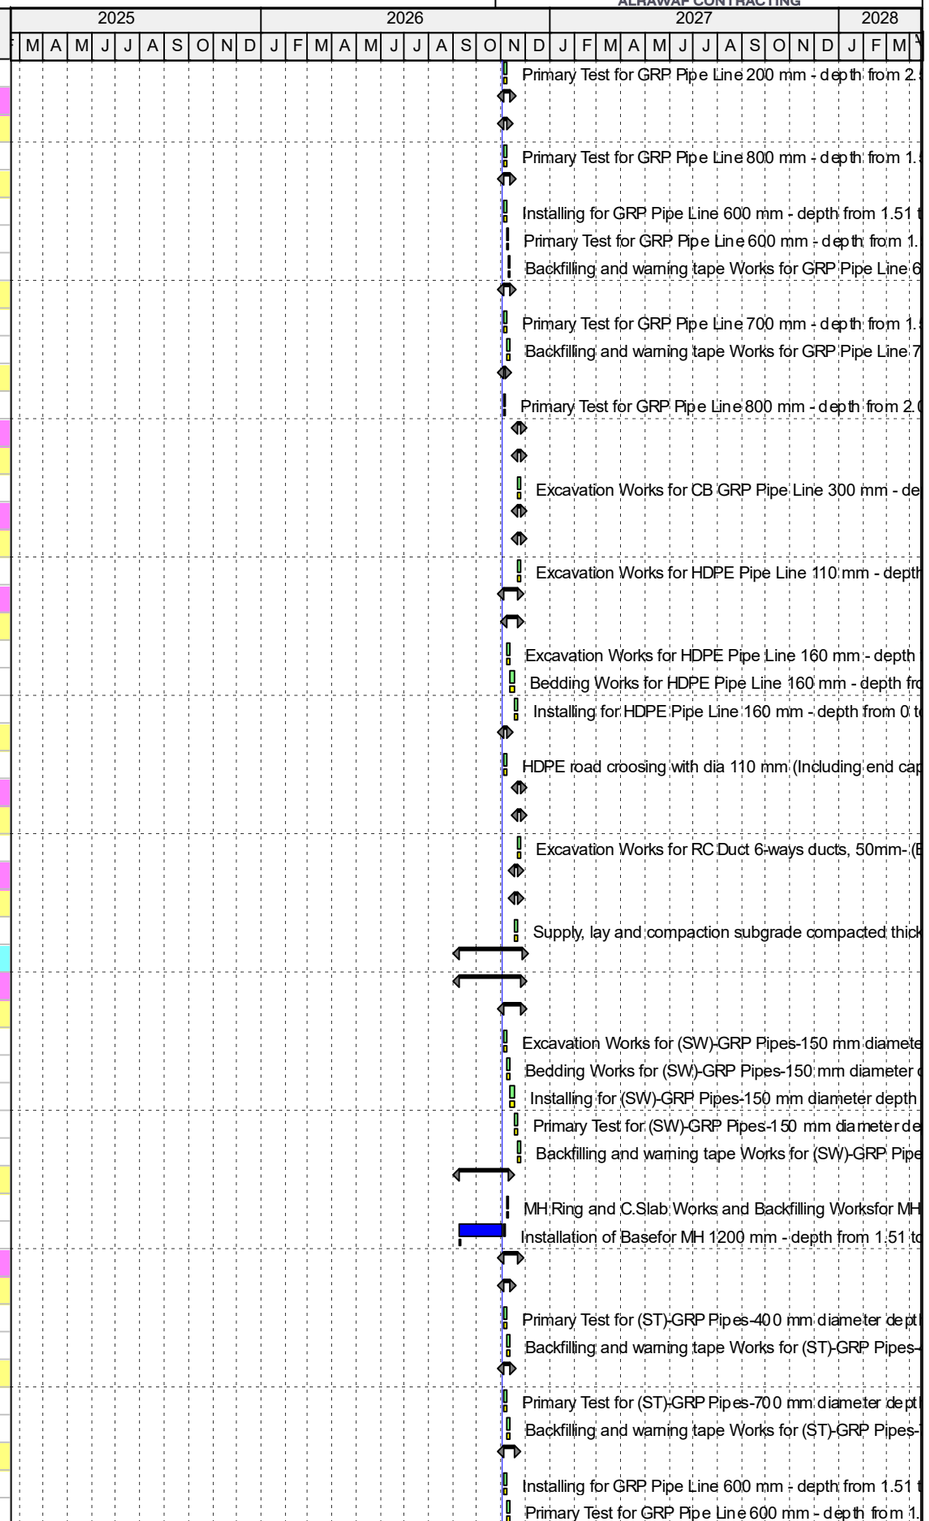


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Backfilling and warning tape Works for GRP Pipe Line 600 mm	4	12-Nov-26	16-Nov-26	399	0	0	5,390
	JDH3-02-009-R4018-(ST)-GRP Pipes-700 mm diameter depth	16	03-Nov-26	21-Nov-26	399	0	0	6,234
	Primary Test for GRP Pipe Line 700 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	407	0	0	3,117
	Backfilling and warning tape Works for GRP Pipe Line 700 mm	4	17-Nov-26	21-Nov-26	399	0	0	3,117
	JDH3-02-009-R4018-(ST)-GRP Pipes-800 mm diameter depth	3	03-Nov-26	05-Nov-26	412	0	0	7,817
	Primary Test for GRP Pipe Line 800 mm - depth from 2.01 to 2.	3	03-Nov-26	05-Nov-26	412	0	0	7,817
	JDH3-02-009-R4018-(ST)-GRP Pipes-500 mm diameter depth	8	03-Nov-26	11-Nov-26	374	0	0	3,305
	Primary Test for GRP Pipe Line 500 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	374	0	0	1,653
	Backfilling and warning tape Works for GRP Pipe Line 500 mm	4	08-Nov-26	11-Nov-26	374	0	0	1,653
	JDH3-02-009-R4018-Catch Basins (Storm Network) - ST	16	08-Nov-26	26-Nov-26	145	0	0	230,113
	JDH3-02-009-R4018-(ST)-For Catch Basins (GRP) Pipes-300	16	08-Nov-26	26-Nov-26	137	0	0	129,156
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4	08-Nov-26	12-Nov-26	135	0	0	28,701
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 to	4	12-Nov-26	17-Nov-26	137	0	0	7,175
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	4	17-Nov-26	22-Nov-26	137	0	0	78,928
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	4	22-Nov-26	26-Nov-26	137	0	0	14,351
	JDH3-02-009-R4018-(ST)-For Catch Basins (GRP) Pipes-400	14	08-Nov-26	24-Nov-26	135	0	0	1,509
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3	08-Nov-26	11-Nov-26	135	0	0	335
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 to	3	11-Nov-26	15-Nov-26	135	0	0	84
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 n	4	15-Nov-26	19-Nov-26	135	0	0	922
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	4	19-Nov-26	24-Nov-26	135	0	0	168
	JDH3-02-009-R4018-(ST)-Single Catch Basin Works	16	08-Nov-26	26-Nov-26	141	0	0	44,244
	Excavation Works for single Catch Basin- (B6.33 05 39.30)-Z3-F	4	08-Nov-26	12-Nov-26	141	0	0	11,643
	PC Blinding and Installationfor single Catch Basin- (B6.33 05 39	4	12-Nov-26	17-Nov-26	141	0	0	11,643
	Rings & C.Slab & Final Backfillfor single Catch Basin- (B6.33 05	4	17-Nov-26	22-Nov-26	141	0	0	16,301
	Finishing and Insulation Works for single Catch Basin- (B6.33 05	4	22-Nov-26	26-Nov-26	141	0	0	4,657
	JDH3-02-009-R4018-(ST)-Double Catch Basin Works	16	08-Nov-26	26-Nov-26	145	0	0	55,204
	Excavation Works for double Catch Basin- (B6.33 05 39.31)-Z3-	4	08-Nov-26	12-Nov-26	145	0	0	14,527
	PC Blinding and Installationfor double Catch Basin- (B6.33 05 3	4	12-Nov-26	17-Nov-26	145	0	0	14,527
	Rings & C.Slab & Final Backfillfor double Catch Basin- (B6.33 05	4	17-Nov-26	22-Nov-26	145	0	0	20,338
	Finishing and Insulation Works for double Catch Basin- (B6.33 (	4	22-Nov-26	26-Nov-26	145	0	0	5,811
	JDH3-02-009-R4018-TSE Network - TSE	12	03-Nov-26	16-Nov-26	236	0	0	45,019
	JDH3-02-009-R4018-(TSE)-HDPE Pipes-110 mm diameter dep	12	03-Nov-26	16-Nov-26	236	0	0	45,019
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 to	4	03-Nov-26	07-Nov-26	236	0	0	11,255
	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4	08-Nov-26	11-Nov-26	236	0	0	2,814
	Installing for HDPE Pipe Line 110 mm - depth from 0 to 1.5 m- (	4	12-Nov-26	16-Nov-26	236	0	0	30,951
	JDH3-02-009-R4018-Potable Water Network - WT	20	03-Nov-26	25-Nov-26	322	0	0	62,052
	JDH3-02-009-R4018-(WT)-HDPE Pipes-225 mm diameter dep	12	03-Nov-26	16-Nov-26	224	0	0	1,368
	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 to	4	03-Nov-26	07-Nov-26	220	0	0	342
	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	4	08-Nov-26	11-Nov-26	224	0	0	86
	Installing for HDPE Pipe Line 225 mm - depth from 0 to 1.5 m- (	4	12-Nov-26	16-Nov-26	224	0	0	941
	JDH3-02-009-R4018-(WT)-Gate Valve-200 mm on pipe dia (22	8	17-Nov-26	25-Nov-26	224	0	0	2,660
	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B3.33	4	17-Nov-26	21-Nov-26	224	0	0	2,394
	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 mi	4	22-Nov-26	25-Nov-26	224	0	0	266
	JDH3-02-009-R4018-(WT)-Fire Hydrant	4	12-Nov-26	16-Nov-26	220	0	0	9,771
	Excavation and Bedding and Pipe Installation for Fire Hydrant- (	4	12-Nov-26	16-Nov-26	220	0	0	9,771
	JDH3-02-009-R4018-(WT)-Plot Connection	3	03-Nov-26	05-Nov-26	253	0	0	6,879
	HDPE road crossing with dia 110 mm (Including end cap, isolati	3	03-Nov-26	05-Nov-26	253	0	0	6,879
	JDH3-02-009-R4018-(WT)-HDPE Pipes-225 mm diameter dep	16	08-Nov-26	25-Nov-26	322	0	0	41,375
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	4	08-Nov-26	11-Nov-26	220	0	0	9,194
	Bedding Works for HDPE Pipe Line 225 mm - depth from 1.51 t	4	12-Nov-26	16-Nov-26	228	0	0	2,299
	Installing for HDPE Pipe Line 225 mm - depth from 1.51 to 2.5	4	17-Nov-26	21-Nov-26	228	0	0	25,285
	Primary Test for HDPE Pipe Line 225 mm - depth from 1.51 to 2	4	22-Nov-26	25-Nov-26	322	0	0	4,597
	JDH3-02-009-R4018-Electrical Network - EL	12	08-Nov-26	22-Nov-26	251	0	0	2,054

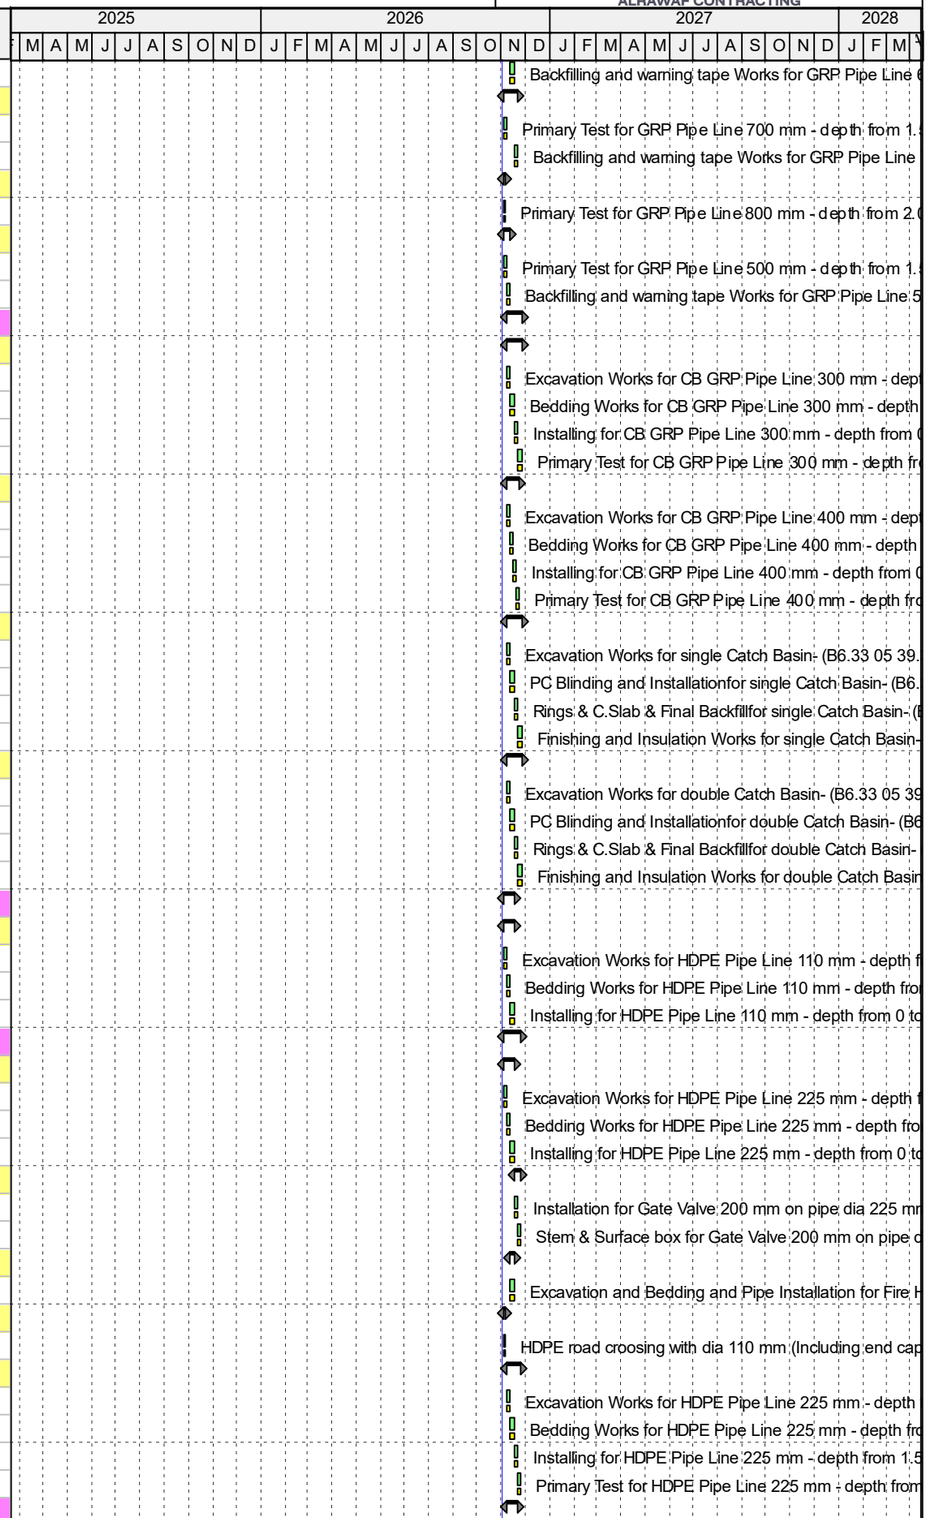


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R4018-(EL)-MV cables duct banks 2-way	12	08-Nov-26	22-Nov-26	251	0	0	2,054
	Excavation for MV cables duct banks 2-way- (B2.33 71 19.07)-Z	3	08-Nov-26	11-Nov-26	249	0	0	205
	Installing upvc pipe for MV cables duct banks 2-way- (B2.33 71	3	11-Nov-26	15-Nov-26	251	0	0	205
	Pouring Concrete Cover for MV cables duct banks 2-way- (B2.3	3	15-Nov-26	18-Nov-26	251	0	0	1,335
	Backfilling Works for MV cables duct banks 2-way- (B2.33 71 19	3	18-Nov-26	22-Nov-26	251	0	0	308
	JDH3-02-009-R4018-Street Lighting Network -SL	12	11-Nov-26	25-Nov-26	279	0	0	2,053
	JDH3-02-009-R4018-(SL)-Road Crossing Ducts 2 way PVC 2	12	11-Nov-26	25-Nov-26	279	0	0	2,053
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	4	11-Nov-26	16-Nov-26	279	0	0	432
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z3-R	4	16-Nov-26	21-Nov-26	279	0	0	1,297
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	4	21-Nov-26	25-Nov-26	279	0	0	324
	JDH3-02-009-R4018-Road Works - RD	4	03-Nov-26	08-Nov-26	135	0	0	170,309
	JDH3-02-009-R4018-(RD)-Subgrade	4	03-Nov-26	08-Nov-26	135	0	0	170,309
	Supply, lay and compaction subgrade compacted thickness 300	4	03-Nov-26	08-Nov-26	135	0	0	170,309
R4019		86	18-Aug-26 A	28-Nov-26	361	0	33,221	513,362
	JDH3-02-009-R4019-Sewage Network - SW	20	03-Nov-26	25-Nov-26	358	0	0	120,010
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter deptl	20	03-Nov-26	25-Nov-26	350	0	0	29,707
	Excavation Works for GRP Pipe Line 150 mm - depth from 1.51	4	03-Nov-26	07-Nov-26	350	0	0	5,941
	Bedding Works for GRP Pipe Line 150 mm - depth from 1.51 to	4	08-Nov-26	11-Nov-26	350	0	0	1,485
	Installing for GRP Pipe Line 150 mm - depth from 1.51 to 2.5 m	4	12-Nov-26	16-Nov-26	350	0	0	16,339
	Primary Test for GRP Pipe Line 150 mm - depth from 1.51 to 2.	4	17-Nov-26	21-Nov-26	350	0	0	2,971
	Backfilling and warning tape Works for GRP Pipe Line 150 mm	4	22-Nov-26	25-Nov-26	350	0	0	2,971
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter deptl	16	07-Nov-26	25-Nov-26	351	0	0	27,061
	Excavation Works for GRP Pipe Line 150 mm - depth from 0 to	4	07-Nov-26	11-Nov-26	351	0	0	6,013
	Bedding Works for GRP Pipe Line 150 mm - depth from 0 to 1.	4	11-Nov-26	16-Nov-26	351	0	0	1,503
	Installing for GRP Pipe Line 150 mm - depth from 0 to 1.5 m- (E	4	16-Nov-26	21-Nov-26	351	0	0	16,537
	Primary Test for GRP Pipe Line 150 mm - depth from 0 to 1.5 m	4	21-Nov-26	25-Nov-26	351	0	0	3,007
	JDH3-02-009-R4019-(SW)-MH Works depth from 1.51 to 2.5 I	8	03-Nov-26	11-Nov-26	362	0	0	43,865
	Installation of Basefor MH 1200 mm - depth from 1.51 to 2.5 m	4	03-Nov-26	07-Nov-26	362	0	0	18,277
	MH Ring and C.Slab Works and Backfilling Worksfor MH 1200 m	4	08-Nov-26	11-Nov-26	362	0	0	25,588
	JDH3-02-009-R4019-(SW)-GRP Pipes-150 mm diameter deptl	16	03-Nov-26	21-Nov-26	362	0	0	19,377
	Excavation Works for GRP Pipe Line 150 mm - depth from 2.51	4	03-Nov-26	07-Nov-26	362	0	0	4,306
	Bedding Works for GRP Pipe Line 150 mm - depth from 2.51 to	4	08-Nov-26	11-Nov-26	362	0	0	1,077
	Installing for GRP Pipe Line 150 mm - depth from 2.51 to 3.5 m	4	12-Nov-26	16-Nov-26	362	0	0	11,842
	Primary Test for GRP Pipe Line 150 mm - depth from 2.51 to 3.	4	17-Nov-26	21-Nov-26	362	0	0	2,153
	JDH3-02-009-R4019-Storm Network - ST	78	18-Aug-26 A	18-Nov-26	369	0	33,221	67,633
	JDH3-02-009-R4019-(ST)-GRP Pipes-400 mm diameter depth	74	18-Aug-26 A	14-Nov-26	369	0	33,221	62,919
	Primary Test for (ST)-GRP Pipes-400 mm diameter depth from 1	4	04-Nov-26	09-Nov-26	369	0	0	6,292
	Backfilling and warning tape Works for (ST)-GRP Pipes-400 mm	4	09-Nov-26	14-Nov-26	369	0	0	6,292
	Installing for (ST)-GRP Pipes-400 mm diameter depth from 1.51	4	23-Aug-26 A	04-Nov-26	369	0	22,839	34,605
	Excavation Works for (ST)-GRP Pipes-400 mm diameter depth	4	18-Aug-26 A	04-Nov-26	369	0	8,305	12,584
	Bedding Works for (ST)-GRP Pipes-400 mm diameter depth fro	4	20-Aug-26 A	04-Nov-26	369	0	2,076	3,146
	JDH3-02-009-R4019-(ST)-GRP Pipes-500 mm diameter depth	13	03-Nov-26	18-Nov-26	369	0	0	4,715
	Primary Test for GRP Pipe Line 500 mm - depth from 1.51 to 2.	4	03-Nov-26	07-Nov-26	374	0	0	2,357
	Backfilling and warning tape Works for GRP Pipe Line 500 mm	4	14-Nov-26	18-Nov-26	369	0	0	2,357
	JDH3-02-009-R4019-Catch Basins (Storm Network) - ST	11	15-Nov-26	28-Nov-26	143	0	0	39,055
	JDH3-02-009-R4019-(ST)-For Catch Basins (GRP) Pipes-300	8	15-Nov-26	24-Nov-26	143	0	0	21,535
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4	15-Nov-26	19-Nov-26	136	0	0	17,228
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 to	4	19-Nov-26	24-Nov-26	143	0	0	4,307
	JDH3-02-009-R4019-(ST)-For Catch Basins (GRP) Pipes-400	6	19-Nov-26	26-Nov-26	144	0	0	1,706
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3	19-Nov-26	23-Nov-26	136	0	0	1,365
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 to	3	23-Nov-26	26-Nov-26	144	0	0	341
	JDH3-02-009-R4019-(ST)-Single Catch Basin Works	4	23-Nov-26	28-Nov-26	136	0	0	9,589
	Excavation Works for single Catch Basin- (B6.33 05 39.30)-Z3-F	4	23-Nov-26	28-Nov-26	136	0	0	9,589

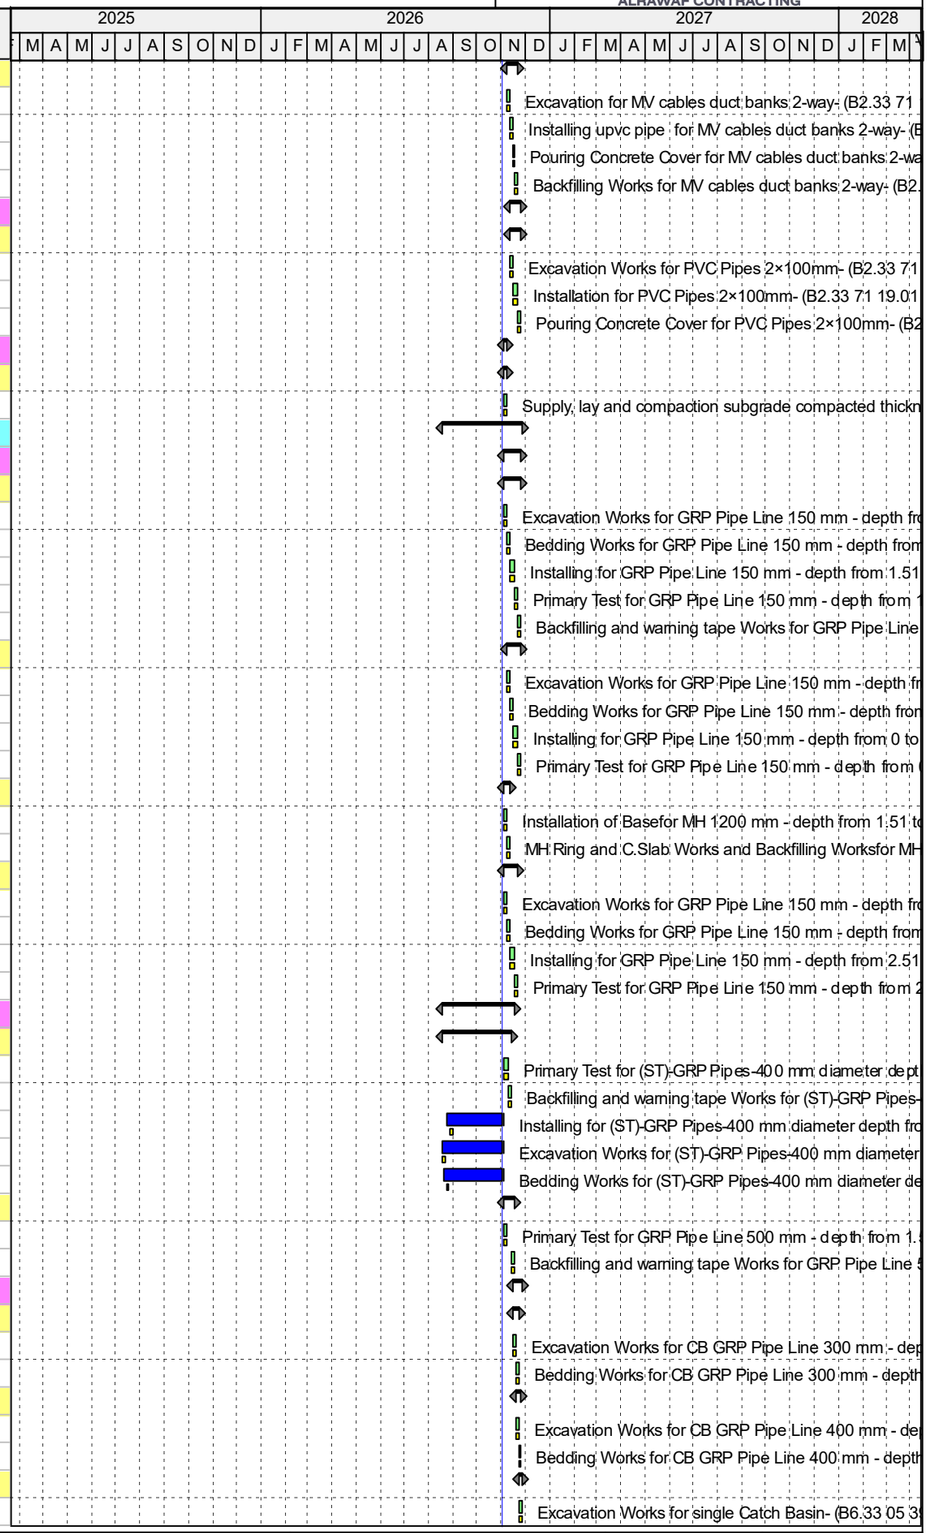

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-R4019-(ST)-Double Catch Basin Works	4	23-Nov-26	28-Nov-26	140	0	0	6,226
	Excavation Works for double Catch Basin- (B6.33 05 39.31)-Z3-	4	23-Nov-26	28-Nov-26	140	0	0	6,226
	JDH3-02-009-R4019-TSE Network - TSE	8	15-Nov-26	24-Nov-26	340	0	0	11,957
	JDH3-02-009-R4019-(TSE)-HDPE Pipes-110 mm diameter dep	8	15-Nov-26	24-Nov-26	340	0	0	9,664
	Excavation Works for HDPE Pipe Line 110 mm - depth from 0 t	4	15-Nov-26	19-Nov-26	340	0	0	7,731
	Bedding Works for HDPE Pipe Line 110 mm - depth from 0 to 1	4	19-Nov-26	24-Nov-26	340	0	0	1,933
	JDH3-02-009-R4019-(TSE)-HDPE Pipes-110 mm diameter dep	4	19-Nov-26	24-Nov-26	340	0	0	2,293
	Excavation Works for HDPE Pipe Line 110 mm - depth from 1.5	4	19-Nov-26	24-Nov-26	340	0	0	2,293
	JDH3-02-009-R4019-Potable Water Network - WT	19	03-Nov-26	25-Nov-26	327	0	0	116,343
	JDH3-02-009-R4019-(WT)-HDPE Pipes-160 mm diameter dep	12	07-Nov-26	21-Nov-26	299	0	0	70,153
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	4	07-Nov-26	11-Nov-26	299	0	0	17,538
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	4	11-Nov-26	16-Nov-26	299	0	0	4,385
	Installing for HDPE Pipe Line 160 mm - depth from 0 to 1.5 m-	4	16-Nov-26	21-Nov-26	299	0	0	48,230
	JDH3-02-009-R4019-(WT)-HDPE Pipes-160 mm diameter dep	12	11-Nov-26	25-Nov-26	299	0	0	41,030
	Excavation Works for HDPE Pipe Line 160 mm - depth from 1.5	4	11-Nov-26	16-Nov-26	299	0	0	10,258
	Bedding Works for HDPE Pipe Line 160 mm - depth from 1.51 t	4	16-Nov-26	21-Nov-26	299	0	0	2,564
	Installing for HDPE Pipe Line 160 mm - depth from 1.51 to 2.5	4	21-Nov-26	25-Nov-26	299	0	0	28,208
	JDH3-02-009-R4019-(WT)-Plot Connection	3	03-Nov-26	05-Nov-26	343	0	0	5,159
	HDPE road croosing with dia 110 mm (Including end cap, isolati	3	03-Nov-26	05-Nov-26	343	0	0	5,159
	JDH3-02-009-R4019-Electrical Network - EL	4	15-Nov-26	19-Nov-26	267	0	0	2,650
	JDH3-02-009-R4019-(EL)-MV cable trench size 1.5m wide an	4	15-Nov-26	19-Nov-26	267	0	0	2,650
	Excavation for MV Cable Trench 1.5m wide - 80cm deep- (B2.3	4	15-Nov-26	19-Nov-26	267	0	0	2,650
	JDH3-02-009-R4019-Road Works - RD	4	10-Nov-26	15-Nov-26	136	0	0	155,714
	JDH3-02-009-R4019-(RD)-Subgrade	4	10-Nov-26	15-Nov-26	136	0	0	155,714
	Supply, lay and compaction subgrade compacted thickness 300	4	10-Nov-26	15-Nov-26	136	0	0	155,714
	R6605	20	03-Nov-26	25-Nov-26	336	0	0	105,505
	JDH3-02-009-R6605-Catch Basins (Storm Network) - ST	20	03-Nov-26	25-Nov-26	336	0	0	64,098
	JDH3-02-009-R6605-(ST)-For Catch Basins (GRP) Pipes-300	20	03-Nov-26	25-Nov-26	336	0	0	38,428
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	4	03-Nov-26	07-Nov-26	321	0	0	7,686
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 t	4	08-Nov-26	11-Nov-26	336	0	0	1,921
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 m	4	12-Nov-26	16-Nov-26	336	0	0	21,135
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	4	17-Nov-26	21-Nov-26	336	0	0	3,843
	Backfilling and warning tape Works for CB GRP Pipe Line 300 m	4	22-Nov-26	25-Nov-26	336	0	0	3,843
	JDH3-02-009-R6605-(ST)-For Catch Basins (GRP) Pipes-400	14	08-Nov-26	23-Nov-26	334	0	0	561
	Excavation Works for CB GRP Pipe Line 400 mm - depth from (	3	08-Nov-26	10-Nov-26	321	0	0	125
	Bedding Works for CB GRP Pipe Line 400 mm - depth from 0 t	3	11-Nov-26	14-Nov-26	334	0	0	31
	Installing for CB GRP Pipe Line 400 mm - depth from 0 to 1.5 m	4	15-Nov-26	18-Nov-26	334	0	0	343
	Primary Test for CB GRP Pipe Line 400 mm - depth from 0 to 1.	4	19-Nov-26	23-Nov-26	334	0	0	62
	JDH3-02-009-R6605-(ST)-Single Catch Basin Works	12	11-Nov-26	24-Nov-26	329	0	0	20,958
	Excavation Works for single Catch Basin- (B6.33 05 39.30)-Z3-F	4	11-Nov-26	15-Nov-26	321	0	0	6,164
	PC Blinding and Installationfor single Catch Basin- (B6.33 05 39	4	16-Nov-26	19-Nov-26	329	0	0	6,164
	Rings & C.Slab & Final Backfillfor single Catch Basin- (B6.33 05	4	21-Nov-26	24-Nov-26	329	0	0	8,630
	JDH3-02-009-R6605-(ST)-Double Catch Basin Works	8	16-Nov-26	24-Nov-26	321	0	0	4,151
	Excavation Works for double Catch Basin- (B6.33 05 39.31)-Z3-	4	16-Nov-26	19-Nov-26	321	0	0	2,075
	PC Blinding and Installationfor double Catch Basin- (B6.33 05 3	4	21-Nov-26	24-Nov-26	321	0	0	2,075
	JDH3-02-009-R6605-Road Works - RD	12	10-Nov-26	24-Nov-26	338	0	0	41,408
	JDH3-02-009-R6605-(RD)-Precast Concrete Curb	12	10-Nov-26	24-Nov-26	338	0	0	41,408
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	4	10-Nov-26	15-Nov-26	338	0	0	31,361
	Supply and installation Precast Concrete Kerb, Type L1 - (B1.32	4	15-Nov-26	19-Nov-26	338	0	0	9,748
	Supply and installation Depressed curbs Type K2 - (B1.32 14 13	4	19-Nov-26	24-Nov-26	338	0	0	298
CMZ Linking Road		94	11-Aug-26 A	30-Nov-26	392	0	1,173,238	6,496,893
JDH3-02-009-Execution		94	11-Aug-26 A	30-Nov-26	392	0	1,173,238	6,496,893
JDH3-02-009-Road Works - CMZ Linking Road		58	03-Sep-26 A	10-Nov-26	408	0	301,368	505,344

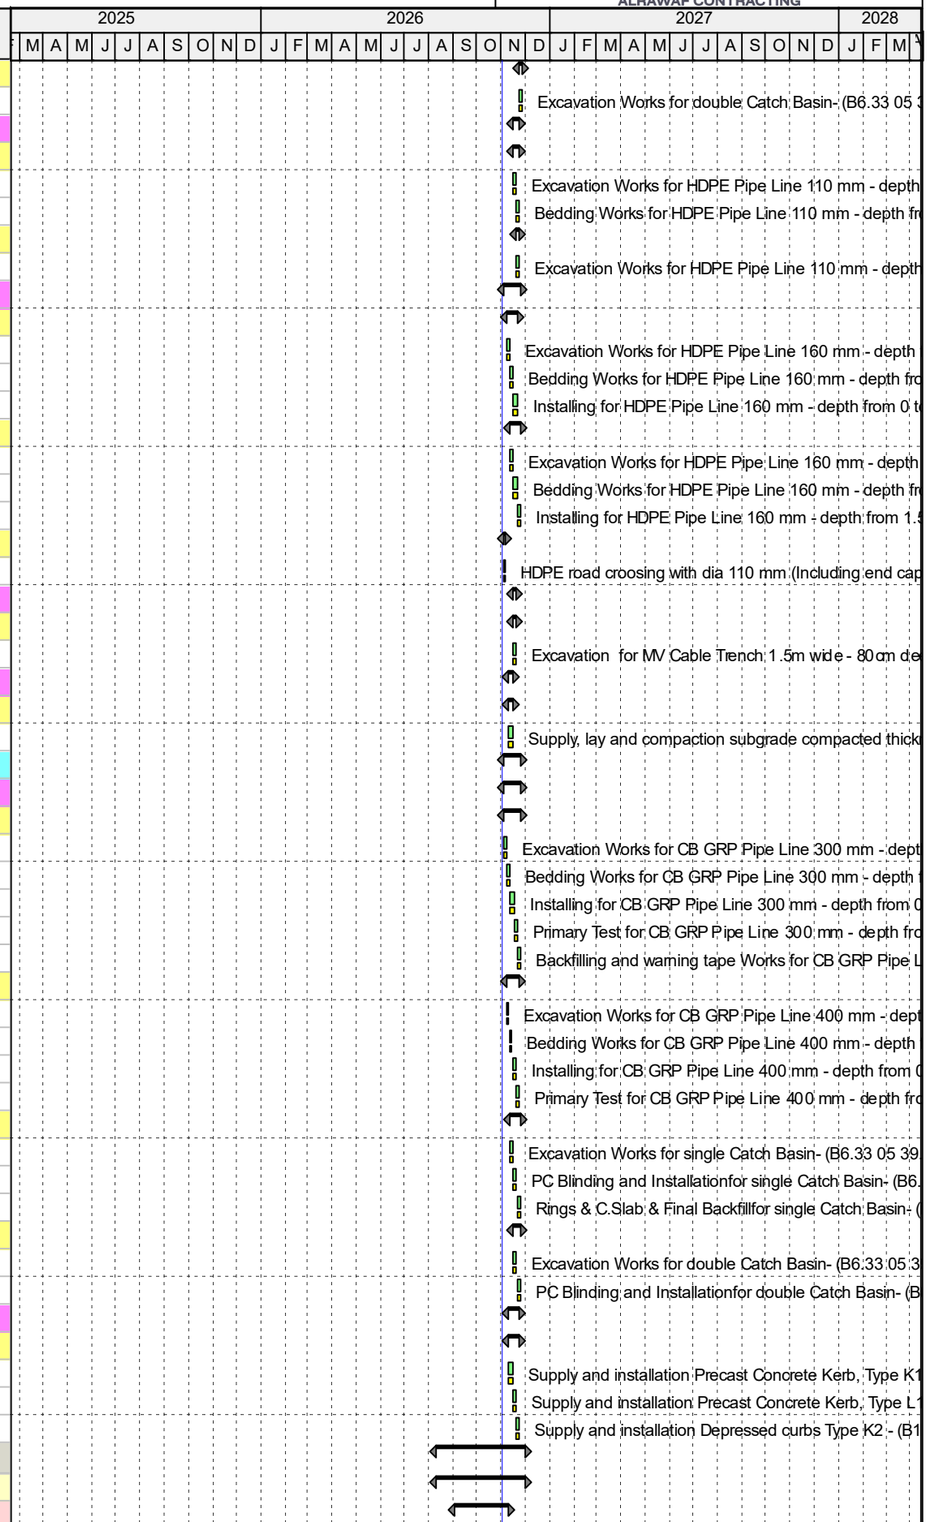


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Riprap with thickness 300mm for Logistic Area- (B6.31 22 00.02	7	03-Nov-26	10-Nov-26	408	0	0	3,064
JDI	Backfill Layers Works Excavated Material for Road - (B1.31 22 0	3	03-Sep-26 A	04-Nov-26	253	0	301,368	502,281
JDH3-02-009-CMZ-Catch Basins (Storm Network) - ST		10	03-Nov-26	14-Nov-26	368	0	0	432,421
JDH3-02-009-R151-(ST)-For Catch Basins (GRP) Pipes-300 mm dia		10	03-Nov-26	14-Nov-26	368	0	0	432,421
	Excavation Works for CB GRP Pipe Line 300 mm - depth from (	2	03-Nov-26	04-Nov-26	368	0	0	86,484
	Bedding Works for CB GRP Pipe Line 300 mm - depth from 0 t	2	05-Nov-26	07-Nov-26	368	0	0	21,621
	Installing for CB GRP Pipe Line 300 mm - depth from 0 to 1.5 n	2	08-Nov-26	09-Nov-26	368	0	0	237,832
	Primary Test for CB GRP Pipe Line 300 mm - depth from 0 to 1.	2	10-Nov-26	11-Nov-26	368	0	0	43,242
	Backfilling and warning tape Works for CB GRP Pipe Line 300 n	2	12-Nov-26	14-Nov-26	368	0	0	43,242
JDH3-02-009-CMZ-TSE Network - TSE		10	15-Nov-26	25-Nov-26	395	0	0	296,010
JDH3-02-009-R07-(TSE)-Gate Valve-200 mm on pipe dia (225) mm		4	15-Nov-26	18-Nov-26	399	0	0	5,319
	Installation for Gate Valve 200 mm on pipe dia 225 mm- (B4.33	2	15-Nov-26	16-Nov-26	399	0	0	4,787
	Stem & Surface box for Gate Valve 200 mm on pipe dia 225 m	2	17-Nov-26	18-Nov-26	399	0	0	532
JDH3-02-009-R151-(TSE)-Gate Valve-150 mm on pipe dia (160) mm		4	15-Nov-26	18-Nov-26	399	0	0	1,766
	Installation for Gate Valve 150 mm on pipe dia 160 mm- (B4.33	2	15-Nov-26	16-Nov-26	399	0	0	1,589
	Stem & Surface box for Gate Valve 150 mm on pipe dia 160 m	2	17-Nov-26	18-Nov-26	399	0	0	177
JDH3-02-009-R151-(TSE)-Gate Valve-100 mm on pipe dia (110) mm		6	15-Nov-26	21-Nov-26	399	0	0	20,293
	Installation for Gate Valve 100 mm on pipe dia 110 mm- (B4.33	2	15-Nov-26	16-Nov-26	401	0	0	18,264
	Stem & Surface box for Gate Valve 100 mm on pipe dia 110 m	2	19-Nov-26	21-Nov-26	399	0	0	2,029
JDH3-02-009-CMZ-Potable Water Network - WT		10	15-Nov-26	25-Nov-26	373	0	0	268,632
JDH3-02-009-R16-(WT)-HDPE Pipes-160 mm diameter depth fro		8	15-Nov-26	23-Nov-26	369	0	0	20,065
	Excavation Works for HDPE Pipe Line 160 mm - depth from 0 t	3	15-Nov-26	17-Nov-26	368	0	0	16,052
	Bedding Works for HDPE Pipe Line 160 mm - depth from 0 to 1	5	18-Nov-26	23-Nov-26	369	0	0	4,013
JDH3-02-009-R151-(WT)-HDPE Pipes-225 mm diameter depth fr		7	18-Nov-26	25-Nov-26	373	0	0	822
	Excavation Works for HDPE Pipe Line 225 mm - depth from 0 t	3	18-Nov-26	21-Nov-26	368	0	0	658
	Bedding Works for HDPE Pipe Line 225 mm - depth from 0 to 1	4	22-Nov-26	25-Nov-26	373	0	0	164
JDH3-02-009-R151-(WT)-HDPE Pipes-225 mm diameter depth fr		3	22-Nov-26	24-Nov-26	368	0	0	247,745
	Excavation Works for HDPE Pipe Line 225 mm - depth from 1.5	3	22-Nov-26	24-Nov-26	368	0	0	247,745
JDH3-02-009-CMZ-Street Lighting Network -SL		22	03-Nov-26	28-Nov-26	383	0	0	219,171
JDH3-02-009-R151-(SL)- LV Cables - Copper, 4Cx16mm²,Cu/XLPE/S		20	03-Nov-26	25-Nov-26	385	0	0	99,495
	Excavation Works for LV Cables 4Cx16 mm²- (B2.26 05 19.04)	5	03-Nov-26	08-Nov-26	383	0	0	9,950
	Bedding Layer and Installation for LV Cables 4Cx16 mm²- (B2.2	5	09-Nov-26	14-Nov-26	385	0	0	74,622
	Testing and Commissioning for LV Cables 4Cx16 mm²- (B2.26	5	15-Nov-26	19-Nov-26	385	0	0	4,975
	Backfilling, Warning Tape Works for LV Cables 4Cx16 mm²- (B2	5	21-Nov-26	25-Nov-26	385	0	0	9,950
JDH3-02-009-R151-(SL)-Road Crossing Ducts 2 way PVC 2 × 100 n		8	03-Nov-26	11-Nov-26	358	0	0	7,879
	Excavation Works for PVC Pipes 2×100mm- (B2.33 71 19.01 S	2	03-Nov-26	04-Nov-26	358	0	0	1,576
	Installation for PVC Pipes 2×100mm- (B2.33 71 19.01 SL)-Z3-R	2	05-Nov-26	07-Nov-26	358	0	0	4,728
	Pouring Concrete Cover for PVC Pipes 2×100mm- (B2.33 71 19	2	08-Nov-26	09-Nov-26	358	0	0	1,182
	Testing and Backfilling Works for PVC Pipes 2×100mm- (B2.33	2	10-Nov-26	11-Nov-26	358	0	0	394
JDH3-02-009-R151-(SL)-Lighting Pole with single arm 12 m height		17	09-Nov-26	28-Nov-26	383	0	0	111,796
	Excavation for RC foundation for Lighting Pole single arm- (B2.2	3	09-Nov-26	11-Nov-26	383	0	0	11,768
	Installation of RC foundation for Lighting Pole single arm- (B2.2	4	12-Nov-26	16-Nov-26	383	0	0	11,768
	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	3	17-Nov-26	19-Nov-26	383	0	0	11,768
	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	7	21-Nov-26	28-Nov-26	383	0	0	76,492
JDH3-02-009-CMZ-Road Works - RD		60	10-Sep-26 A	30-Nov-26	264	0	539,121	3,496,526
JDH3-02-009-R151-(RD)-Aggregate Base Course		3	10-Sep-26 A	03-Nov-26	253	0	308,013	334,797
	Supply, lay and compaction Aggregate base course compacted	3	10-Sep-26 A	03-Nov-26	253	0	308,013	334,797
JDH3-02-009-R151-(RD)-Bituminous base course 150 mm Two Lay		32	15-Oct-26 A	19-Nov-26	250	0	231,107	1,491,016
	Supply, lay and Asphaltic base course including tack Coat (RC2)	11	07-Nov-26	19-Nov-26	250	0	0	745,508
	Supply, lay and Asphaltic base course including Prime Coat (MC	5	15-Oct-26 A	07-Nov-26	250	0	231,107	745,508
JDH3-02-009-R151-(RD)-Bituminous concrete wearing course 50 m		5	07-Nov-26	12-Nov-26	279	0	0	379,592
	Supply, lay and compaction Asphaltic wearing course 50 mm in	5	07-Nov-26	12-Nov-26	279	0	0	379,592
JDH3-02-009-R151-(RD)-Precast Concrete Curb		9	19-Nov-26	30-Nov-26	250	0	0	1,291,121

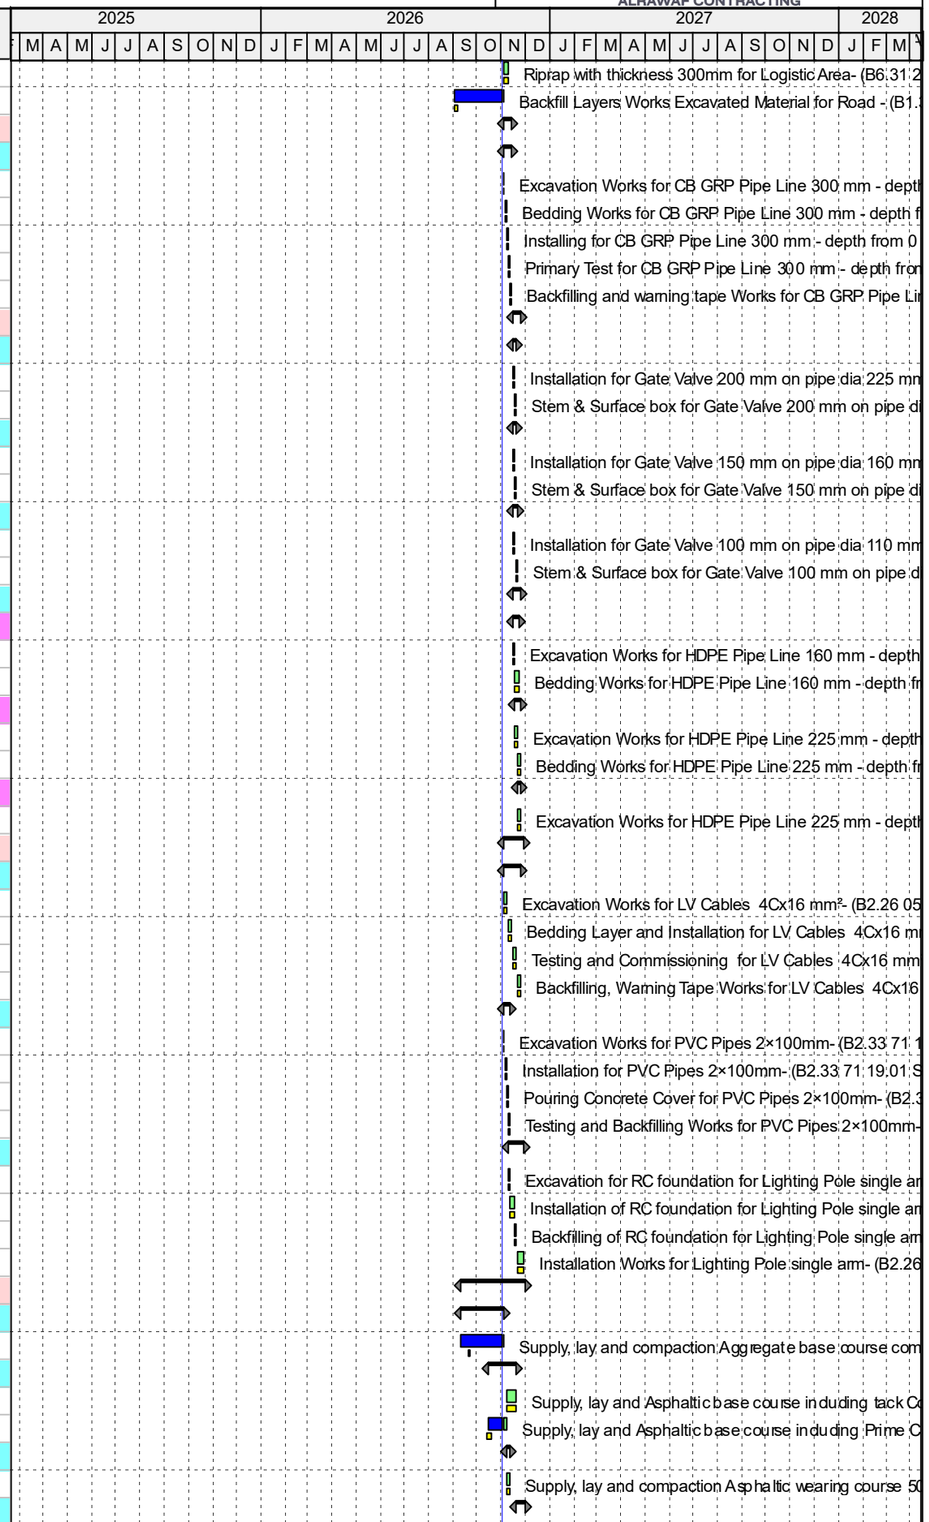

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Supply and installation Precast Concrete Kerb, Type K1-D - (B1.	9	19-Nov-26	30-Nov-26	250	0	0	1,291,121
	Concrete & Guard rail	90	11-Aug-26 A	24-Nov-26	396	0	332,749	1,547,421
	Concrete Works	19	03-Nov-26	24-Nov-26	396	0	0	881,923
	50 mm thickness lean concrete under the foundation and grade	2	03-Nov-26	04-Nov-26	396	0	0	2,825
	Concrete floor slab on grade Including Mastic sealant as per dra	17	05-Nov-26	24-Nov-26	396	0	0	879,099
	Guard Rail	9	11-Aug-26 A	07-Nov-26	411	0	332,749	665,498
	Guard Rail For Roads Station 05 - Left side - Vertical Column	4	11-Aug-26 A	07-Nov-26	411	0	83,187	166,374
	Guard Rail For Roads Station 05 - Left side - Horizontal Guard	4	12-Aug-26 A	07-Nov-26	411	0	83,187	166,374
	Guard Rail For Roads Station 05 - Right side - Vertical Column	4	12-Aug-26 A	07-Nov-26	411	0	83,187	166,374
	Guard Rail For Roads Station 05 - Right side - Horizontal Guard	4	13-Aug-26 A	07-Nov-26	411	0	83,187	166,374
Pond 5		28	03-Nov-26	05-Dec-26	375	0	0	1,981,860
JDH3-02-009-ST1-Stage (1) - Pond 5		11	03-Nov-26	15-Nov-26	386	0	0	693,413
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5	03-Nov-26	08-Nov-26	363	0	0	595,034
JDH3(	Chain Link Fence for Pond 5- (B6.31 22 00.09)-PS-PN5-ST1	6	09-Nov-26	15-Nov-26	386	0	0	98,378
JDH3-02-009-ST2-Stage (2) - Pond 5		12	09-Nov-26	22-Nov-26	386	0	0	693,413
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	5	09-Nov-26	14-Nov-26	363	0	0	595,034
JDH3(	Chain Link Fence for Pond 5- (B6.31 22 00.09)-PS-PN5-ST2	6	16-Nov-26	22-Nov-26	386	0	0	98,378
JDH3-02-009-ST3-Stage (3) - Pond 5		18	15-Nov-26	05-Dec-26	363	0	0	595,034
JDH3(	Coarse Sand for bottom of Pond with 600mm thickness for Pon	18	15-Nov-26	05-Dec-26	363	0	0	595,034
JDH3-02-009-Linking Road between CMZ and Jeddah-Jazan R		118	04-Aug-26 A	15-Feb-27	325	781,836	211,829	781,836
Linking Road Milestones		0	15-Feb-27	15-Feb-27	325	0	0	0
JDH3CCM	Finish of CMZ Road	0		15-Feb-27	325	0	0	0
Construction		26	03-Nov-26	02-Dec-26	389	358,179	0	358,179
JDH3-02-009-CZ-Street Lighting Network -SL		26	03-Nov-26	02-Dec-26	389	358,179	0	358,179
JDH3-02-009-CZ-(SL)-Lighting Pole with double arms 16 m height		16	15-Nov-26	02-Dec-26	354	106,138	0	106,138
JDI	Earthing + Primary Test for Lighting Pole double arms- (B2.26 5	16	15-Nov-26	02-Dec-26	354	106,138	0	106,138
JDH3-02-009-CZ-(SL)-Lighting Pole with single arm 12 m height		10	03-Nov-26	14-Nov-26	354	149,775	0	149,775
JDI	Installation of RC foundation for Lighting Pole single arm- (B2.2	2	03-Nov-26	04-Nov-26	354	37,444	0	37,444
JDI	Backfilling of RC foundation for Lighting Pole single arm- (B2.26	2	05-Nov-26	07-Nov-26	354	28,083	0	28,083
JDI	Installation Works for Lighting Pole single arm- (B2.26 56 19.02	3	08-Nov-26	10-Nov-26	354	65,526	0	65,526
JDI	Earthing + Primary Test for Lighting Pole single arm- (B2.26 56	3	11-Nov-26	14-Nov-26	354	18,722	0	18,722
JDH3-02-009-CZ-(SL)-Road Crossing Ducts 2 way PVC 2 × 150 mm		20	03-Nov-26	25-Nov-26	335	15,355	0	15,355
JDI	Excavation Works for PVC Pipes 2×150mm- (B2.33 71 19.01)-L	20	03-Nov-26	25-Nov-26	335	15,355	0	15,355
JDH3-02-009-CZ-(SL)- LV Cables - Copper, 4 xC 50 mm² XLPE /PVC/S		12	03-Nov-26	16-Nov-26	403	9,255	0	9,255
JDI	Excavation Works for LV Cables 4Cx50 mm²- (B2.26 05 19.02)	2	03-Nov-26	04-Nov-26	403	2,776	0	2,776
JDI	Bedding Layer and Installation for LV Cables 4Cx50 mm²- (B2.2	2	05-Nov-26	07-Nov-26	407	2,776	0	2,776
JDI	Testing and Commissioning for LV Cables 4Cx50 mm²- (B2.26	2	08-Nov-26	09-Nov-26	407	2,776	0	2,776
JDI	Backfilling, Warning Tape Works for LV Cables 4Cx50 mm²- (B2	2	15-Nov-26	16-Nov-26	403	925	0	925
JDH3-02-009-CZ-(SL)- LV Cables - Single Core Copper, 1 xC 25mm² X		8	05-Nov-26	14-Nov-26	403	1,376	0	1,376
JDI	Excavation Works for LV Cables 1Cx25 mm²- (B2.26 05 19.05)	2	05-Nov-26	07-Nov-26	403	413	0	413
JDI	Bedding Layer and Installation for LV Cables 1Cx25 mm²- (B2.2	2	08-Nov-26	09-Nov-26	403	413	0	413
JDI	Testing and Commissioning for LV Cables 1Cx25 mm²- (B2.26	2	10-Nov-26	11-Nov-26	403	413	0	413
JDI	Backfilling, Warning Tape Works for LV Cables 1Cx25 mm²- (B2	2	12-Nov-26	14-Nov-26	403	138	0	138
JDH3-02-009-CZ-(SL)-Street Lighting (LED) Luminaire complete with c		19	03-Nov-26	24-Nov-26	361	76,281	0	76,281
JDI	Earthing & Primary Test for Lighting(LED) Luminaire - (B2.26.5	19	03-Nov-26	24-Nov-26	361	76,281	0	76,281
Close Out		10	04-Aug-26 A	29-Dec-26	354	423,657	211,829	423,657
Final Testing and Commissioning - FT-Jeddah Jazan- CZ		10	04-Aug-26 A	29-Dec-26	354	423,657	211,829	423,657
JDH3F	Testing Street Lighting Work - FT-CZ	10	04-Aug-26 A	29-Dec-26	354	423,657	211,829	423,657
JDH3-02-009-Lift Station 01		184	21-Jul-26 A	19-Apr-27	275	0	900,406	1,854,824
Engineering		18	03-Nov-26	23-Nov-26	318	0	0	0
JDH3-02-009-Method of Statement for Lift Stations		18	03-Nov-26	23-Nov-26	318	0	0	0

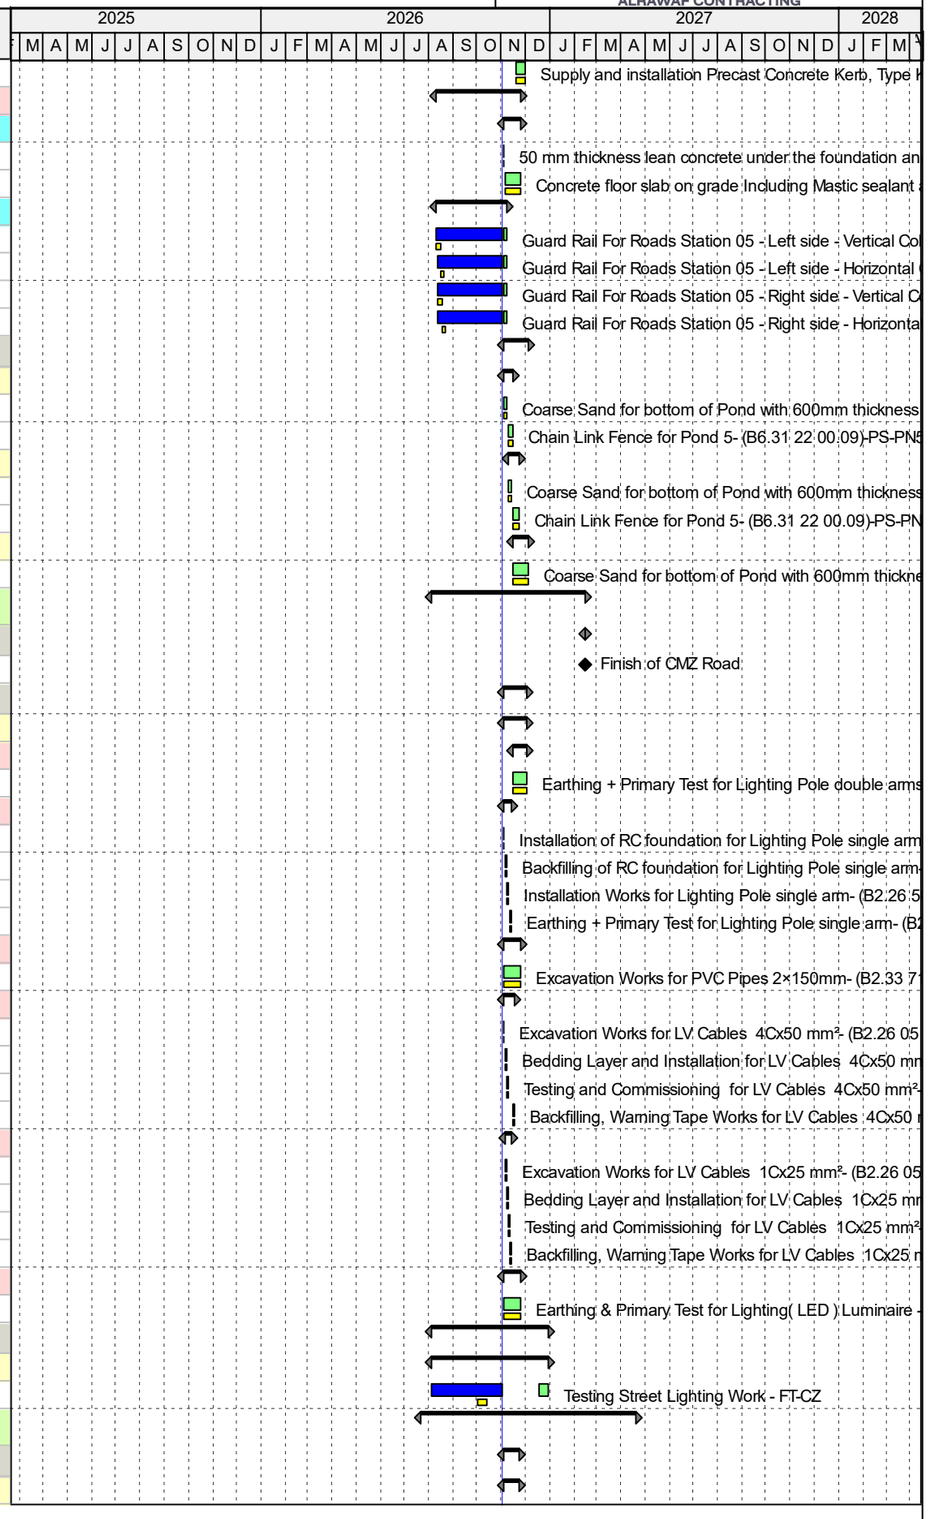


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-Pumps	18	03-Nov-26	23-Nov-26	315	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7	03-Nov-26	10-Nov-26	315	0	0	0
JDI	Review & approval MS for Pumps- MS	9	11-Nov-26	23-Nov-26	261	0	0	0
	JDH3-02-009-Duct Works	18	03-Nov-26	23-Nov-26	229	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7	03-Nov-26	10-Nov-26	230	0	0	0
JDI	Review & approval MS for Duct Works- MS	9	11-Nov-26	23-Nov-26	190	0	0	0
	JDH3-02-009-Drainage System	18	03-Nov-26	23-Nov-26	287	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7	03-Nov-26	10-Nov-26	288	0	0	0
JDI	Review & approval MS for Drainage System- MS	9	11-Nov-26	23-Nov-26	238	0	0	0
	JDH3-02-009-Data Communication	18	03-Nov-26	23-Nov-26	274	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7	03-Nov-26	10-Nov-26	274	0	0	0
JDI	Review & approval MS for Data Communication- MS	9	11-Nov-26	23-Nov-26	227	0	0	0
	JDH3-02-009-Programing Logical Control System	18	03-Nov-26	23-Nov-26	318	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7	03-Nov-26	10-Nov-26	319	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9	11-Nov-26	23-Nov-26	264	0	0	0
Procurement		140	04-Aug-26 A	19-Apr-27	275	0	116,640	324,001
Long Lead Items		140	03-Nov-26	19-Apr-27	275	0	0	64,800
Purchase Order - PO - Lift Station		21	03-Nov-26	26-Nov-26	339	0	0	0
JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR		21	03-Nov-26	26-Nov-26	339	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	21	03-Nov-26	26-Nov-26	339	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	21	03-Nov-26	26-Nov-26	339	0	0	0
JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC		21	03-Nov-26	26-Nov-26	316	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	21	03-Nov-26	26-Nov-26	316	0	0	0
	Material Purchase Order for Data Communication System - LL-T	21	03-Nov-26	26-Nov-26	316	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	21	03-Nov-26	26-Nov-26	292	0	0	0
Fabrication - FAB - Lift Station		168	03-Nov-26	19-Apr-27	332	0	0	0
JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC		168	03-Nov-26	19-Apr-27	332	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	168	03-Nov-26	19-Apr-27	279	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	112	03-Nov-26	22-Feb-27	345	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	168	03-Nov-26	19-Apr-27	279	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	112	03-Nov-26	22-Feb-27	314	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	140	03-Nov-26	22-Mar-27	289	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	112	03-Nov-26	22-Feb-27	388	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	84	03-Nov-26	25-Jan-27	338	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	84	03-Nov-26	25-Jan-27	353	0	0	0
JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL		140	03-Nov-26	22-Mar-27	360	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	84	03-Nov-26	25-Jan-27	370	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	112	03-Nov-26	22-Feb-27	352	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	140	03-Nov-26	22-Mar-27	360	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL-	84	03-Nov-26	25-Jan-27	352	0	0	0
Delivery and staging on Site - DOS- Lift Station		10	03-Nov-26	12-Nov-26	477	0	0	64,800
JDH3-02-009-LOL-DOS-LFT-AR-Architechture -AR		10	03-Nov-26	12-Nov-26	477	0	0	64,800
	Delivery for Steel Gates - LL-AR-DOS	10	03-Nov-26	12-Nov-26	477	0	0	64,800
Short Lead Items		62	04-Aug-26 A	24-Nov-26	396	0	116,640	259,201
Purchase Order - PO - Lift Station		10	03-Nov-26	14-Nov-26	405	0	0	0
JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR		10	03-Nov-26	14-Nov-26	394	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	10	03-Nov-26	14-Nov-26	338	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	10	03-Nov-26	14-Nov-26	228	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	10	03-Nov-26	14-Nov-26	394	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	10	03-Nov-26	14-Nov-26	225	0	0	0
	Material Purchase Order for Interlocking concrete paving - SH-A	10	03-Nov-26	14-Nov-26	230	0	0	0
JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC		10	03-Nov-26	14-Nov-26	377	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	10	03-Nov-26	14-Nov-26	247	0	0	0

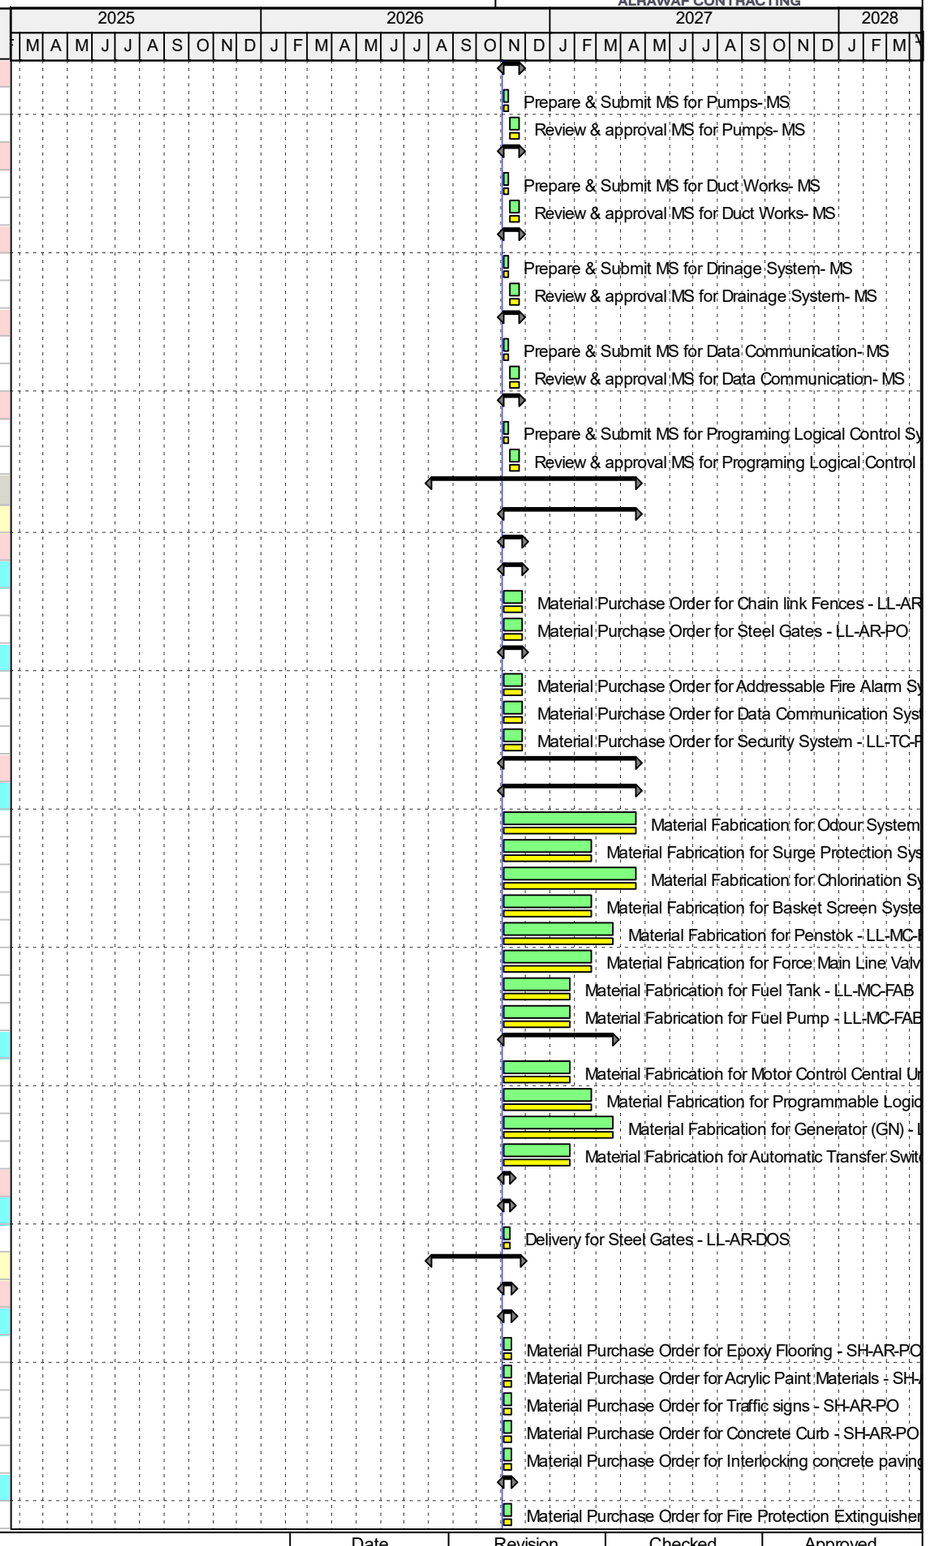


Actual Level of Effort
Actual Work
Remaining Work
Primary Baseline
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	10	03-Nov-26	14-Nov-26	377	0	0	0
	Material Purchase Order for Exhaust Fans - SH-MC-PO	10	03-Nov-26	14-Nov-26	377	0	0	0
	JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL	10	03-Nov-26	14-Nov-26	405	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	10	03-Nov-26	14-Nov-26	405	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	10	03-Nov-26	14-Nov-26	405	0	0	0
	Delivery and staging on Site - DOS- Lift Station	60	04-Aug-26 A	24-Nov-26	476	0	116,640	259,201
	JDH3-02-009-SHL-DOS-LFT-AR-Architechture -AR	10	15-Nov-26	24-Nov-26	476	0	0	64,800
	Delivery for Traffic signs - SH-AR-DOS	10	15-Nov-26	24-Nov-26	476	0	0	64,800
	JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC	10	04-Aug-26 A	14-Nov-26	450	0	116,640	194,401
	Delivery for Wall mounted Split Units - SH-MC-DOS	10	04-Aug-26 A	14-Nov-26	450	0	32,400	64,800
	Delivery for Exhaust Fans - SH-MC-DOS	10	04-Aug-26 A	14-Nov-26	450	0	32,400	64,800
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	10	04-Aug-26 A	12-Nov-26	366	0	51,840	64,800
Construction		71	21-Jul-26 A	24-Nov-26	379	0	783,766	1,530,823
FORCE MAIN		71	21-Jul-26 A	10-Nov-26	392	0	774,397	1,061,371
JDH3-02-009-BQ4-Pipes and Valves		71	21-Jul-26 A	10-Nov-26	392	0	774,397	1,061,371
JDH3-02-009-BQ4-HDPE Pipes-450 mm diameter depth from 2.5 to		71	21-Jul-26 A	03-Nov-26	368	0	774,397	790,201
	Installing for HDPE Pipe Line 450 mm - depth from 2.5 to 3.5 m	17	23-Jul-26 A	03-Nov-26	368	0	425,918	434,611
	Excavation Works for HDPE Pipe Line 450 mm - depth from 2.5	9	21-Jul-26 A	03-Nov-26	368	0	154,879	158,040
	Soil Replacement and Bedding Works for HDPE Pipe Line 450	11	22-Jul-26 A	03-Nov-26	368	0	38,720	39,510
	Primary Test for HDPE Pipe Line 450 mm - depth from 2.5 to 3.	17	28-Jul-26 A	03-Nov-26	368	0	77,440	79,020
	Backfilling and warning tape Works for HDPE Pipe Line 450 mm	17	25-Jul-26 A	03-Nov-26	368	0	77,440	79,020
	JDH3-02-009-BQ4-Butterfly Valve-400 mm	6	03-Nov-26	10-Nov-26	392	0	0	271,170
	Installation for Butterfly Valve 400 mm on pipe dia 450 mm- (J8	3	03-Nov-26	07-Nov-26	392	0	0	244,053
	Stem & Surface box for Butterfly Valve 400 mm on pipe dia 450	3	07-Nov-26	10-Nov-26	392	0	0	27,117
SEWERAGE PUMP STATION		31	18-Oct-26 A	19-Nov-26	376	0	9,369	467,613
JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber		22	18-Oct-26 A	09-Nov-26	307	0	9,369	29,981
JDH3-02-009-BQ4-Valve chamber		22	18-Oct-26 A	09-Nov-26	307	0	9,369	29,981
	RC Casting for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2	05-Nov-26	07-Nov-26	307	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2	08-Nov-26	09-Nov-26	307	0	0	3,748
	Steel Fixing for Valve chamber - (Z900.2)-LFTS1-BQ4-D03	2	18-Oct-26 A	04-Nov-26	307	0	9,369	18,738
JDH3-02-009-BQ4-Sewerage Pumps & MCC		15	03-Nov-26	19-Nov-26	304	0	0	396,985
JDH3-02-009-BQ4-Plinth for Odour Control System		8	03-Nov-26	11-Nov-26	305	0	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS1-BQ4-D03	2	03-Nov-26	04-Nov-26	305	0	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS1-BQ4-D03	2	05-Nov-26	07-Nov-26	305	0	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS1-BQ4-D03	2	08-Nov-26	09-Nov-26	305	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS1-BQ4-D03	2	10-Nov-26	11-Nov-26	305	0	0	2,710
JDH3-02-009-BQ4-Valves and Fittings for Submersible Pumps		6	14-Nov-26	19-Nov-26	304	0	0	369,885
	Gate valves for Pump station - (J899.1)-LFTS1-BQ4-D15	3	14-Nov-26	16-Nov-26	304	0	0	199,169
	Non return valves for Pump station - (J899.2)-LFTS1-BQ4-D15	3	17-Nov-26	19-Nov-26	304	0	0	170,716
JDH3-02-009-BQ4-Pump Lifting System		14	03-Nov-26	19-Nov-26	377	0	0	40,647
JDH3-02-009-BQ4-Surge protection system		14	03-Nov-26	19-Nov-26	377	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS1-BQ4-D15	14	03-Nov-26	19-Nov-26	377	0	0	40,647
MOTOR CONTROL CENTRE BUILDING		4	21-Nov-26	24-Nov-26	304	0	0	1,840
JDH3-02-009-BQ4-Sub Structure		4	21-Nov-26	24-Nov-26	304	0	0	1,840
JDH3-02-009-BQ4-Foundation		4	21-Nov-26	24-Nov-26	304	0	0	1,840
	RC Casting Foundation - (F623)-LFTS1-BQ4-D03	2	21-Nov-26	22-Nov-26	304	0	0	1,226
	Deshuttering Foundation - (F623)-LFTS1-BQ4-D03	2	23-Nov-26	24-Nov-26	304	0	0	613
Close Out		24	03-Nov-26	01-Dec-26	391	0	0	0
As Built Drawing Submittals - SUB-Lift Station - LFTS		24	03-Nov-26	30-Nov-26	381	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR		7	08-Nov-26	15-Nov-26	394	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	08-Nov-26	15-Nov-26	394	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	08-Nov-26	15-Nov-26	394	0	0	0

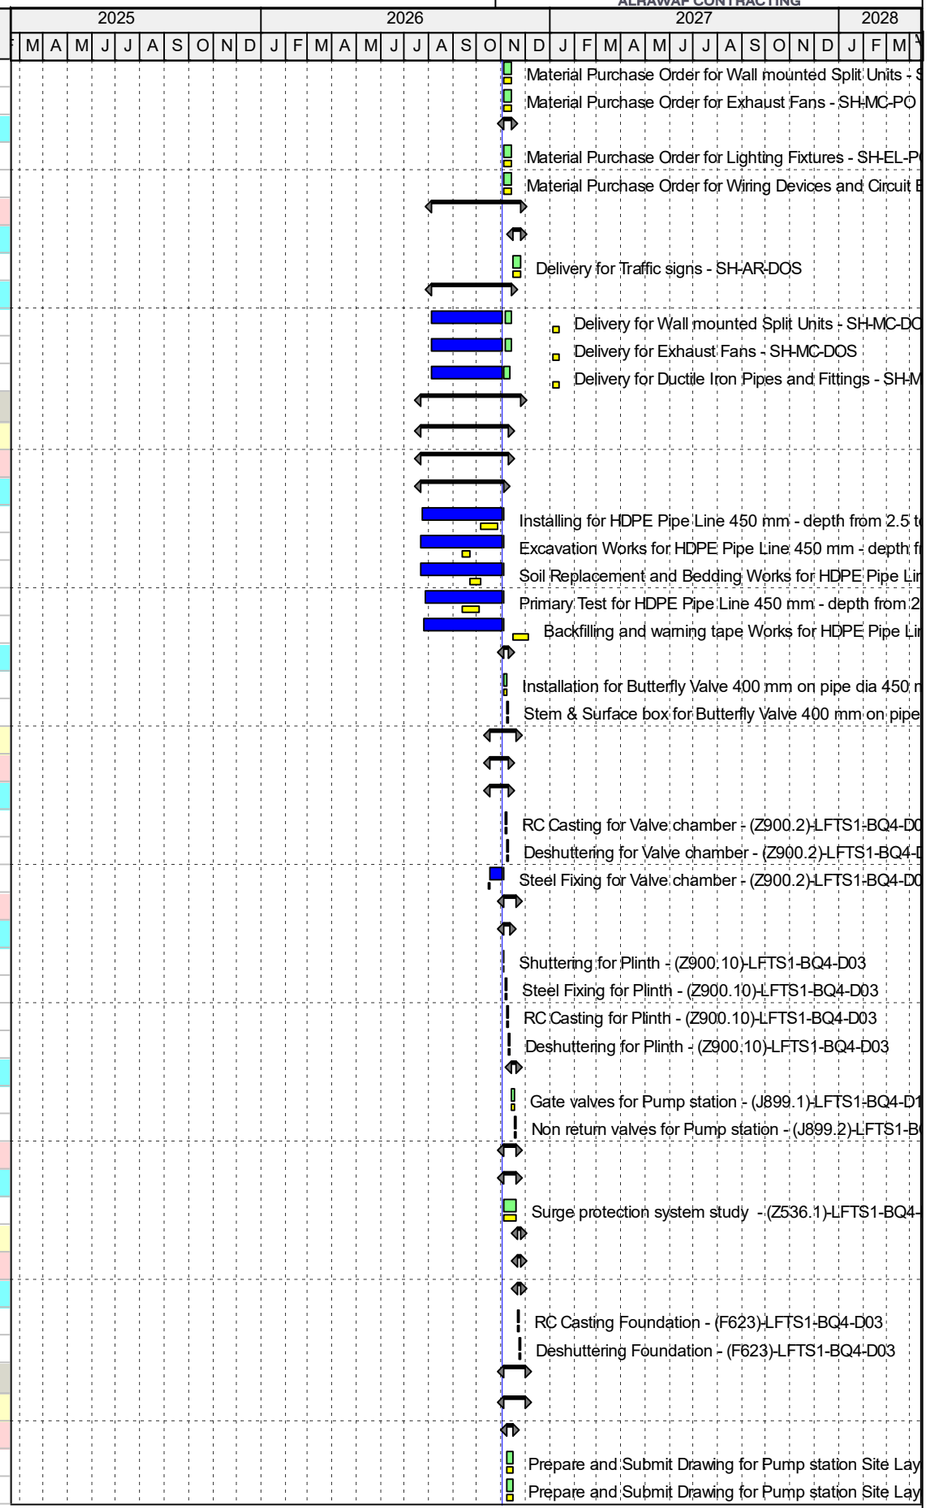


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST	20	08-Nov-26	30-Nov-26	381	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 1	7	08-Nov-26	15-Nov-26	394	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	08-Nov-26	15-Nov-26	394	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 3	7	08-Nov-26	15-Nov-26	394	0	0	0
JDI	Prepare and Submit Drawing for Trench Shopdrawingsfor SUB-A	7	23-Nov-26	30-Nov-26	381	0	0	0
JDI	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -Foundation Shop D	7	23-Nov-26	30-Nov-26	381	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Infra - IN	13	03-Nov-26	18-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Force Main Master Layout (forc	7	03-Nov-26	11-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsIsolation Val	7	10-Nov-26	18-Nov-26	392	0	0	0
	As Built Drawing Approvals - APP-Lift Station -LFTS	14	11-Nov-26	01-Dec-26	325	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR	9	16-Nov-26	26-Nov-26	327	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9	16-Nov-26	26-Nov-26	327	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9	16-Nov-26	26-Nov-26	327	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST	11	16-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Foun	9	16-Nov-26	26-Nov-26	327	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Walls	9	16-Nov-26	26-Nov-26	327	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9	16-Nov-26	26-Nov-26	327	0	0	0
JDI	Review and Approval for Odhour Pads-Foundation Shop Drawin	9	18-Nov-26	30-Nov-26	325	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Infra - IN	14	11-Nov-26	01-Dec-26	325	0	0	0
JDI	Review and Approval for Force Main Master Layout (force Main-	9	11-Nov-26	24-Nov-26	330	0	0	0
JDI	Review and Approval for Mechanical DetailsIsolation Valve Char	9	18-Nov-26	01-Dec-26	325	0	0	0
	JDH3-02-009-Lift Station 02	229	14-Jul-26 A	19-Apr-27	275	0	229,990	641,649
	Procurement	140	04-Aug-26 A	19-Apr-27	275	0	119,790	352,322
	Long Lead Items	140	03-Nov-26	19-Apr-27	275	0	0	0
	Purchase Order - PO - Lift Station	10	03-Nov-26	14-Nov-26	263	0	0	0
	JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR	10	03-Nov-26	14-Nov-26	263	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	10	03-Nov-26	14-Nov-26	256	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	10	03-Nov-26	14-Nov-26	263	0	0	0
	JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC	10	03-Nov-26	14-Nov-26	261	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	10	03-Nov-26	14-Nov-26	261	0	0	0
	Material Purchase Order for Data Communication System - LL-T	10	03-Nov-26	14-Nov-26	261	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	10	03-Nov-26	14-Nov-26	238	0	0	0
	Fabrication - FAB - Lift Station	168	03-Nov-26	19-Apr-27	332	0	0	0
	JDH3-02-009-LOL-MAN-LFT-AR-Architechture -AR	70	15-Nov-26	23-Jan-27	317	0	0	0
	Material Fabrication for Chain link Fences - LL-AR-FAB	70	15-Nov-26	23-Jan-27	308	0	0	0
	Material Fabrication for Steel Gates - LL-AR-FAB	70	15-Nov-26	23-Jan-27	317	0	0	0
	JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC	168	03-Nov-26	19-Apr-27	332	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	168	03-Nov-26	19-Apr-27	182	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	112	03-Nov-26	22-Feb-27	247	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	168	03-Nov-26	19-Apr-27	182	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	112	03-Nov-26	22-Feb-27	217	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	140	03-Nov-26	22-Mar-27	196	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	112	03-Nov-26	22-Feb-27	388	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	84	03-Nov-26	25-Jan-27	288	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	84	03-Nov-26	25-Jan-27	301	0	0	0
	JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL	140	03-Nov-26	22-Mar-27	360	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	84	03-Nov-26	25-Jan-27	296	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	112	03-Nov-26	22-Feb-27	278	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	140	03-Nov-26	22-Mar-27	360	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL	84	03-Nov-26	25-Jan-27	300	0	0	0
	JDH3-02-009-LOL-MAN-LFT-TC-Telecommunications Network - TC	112	15-Nov-26	06-Mar-27	287	0	0	0

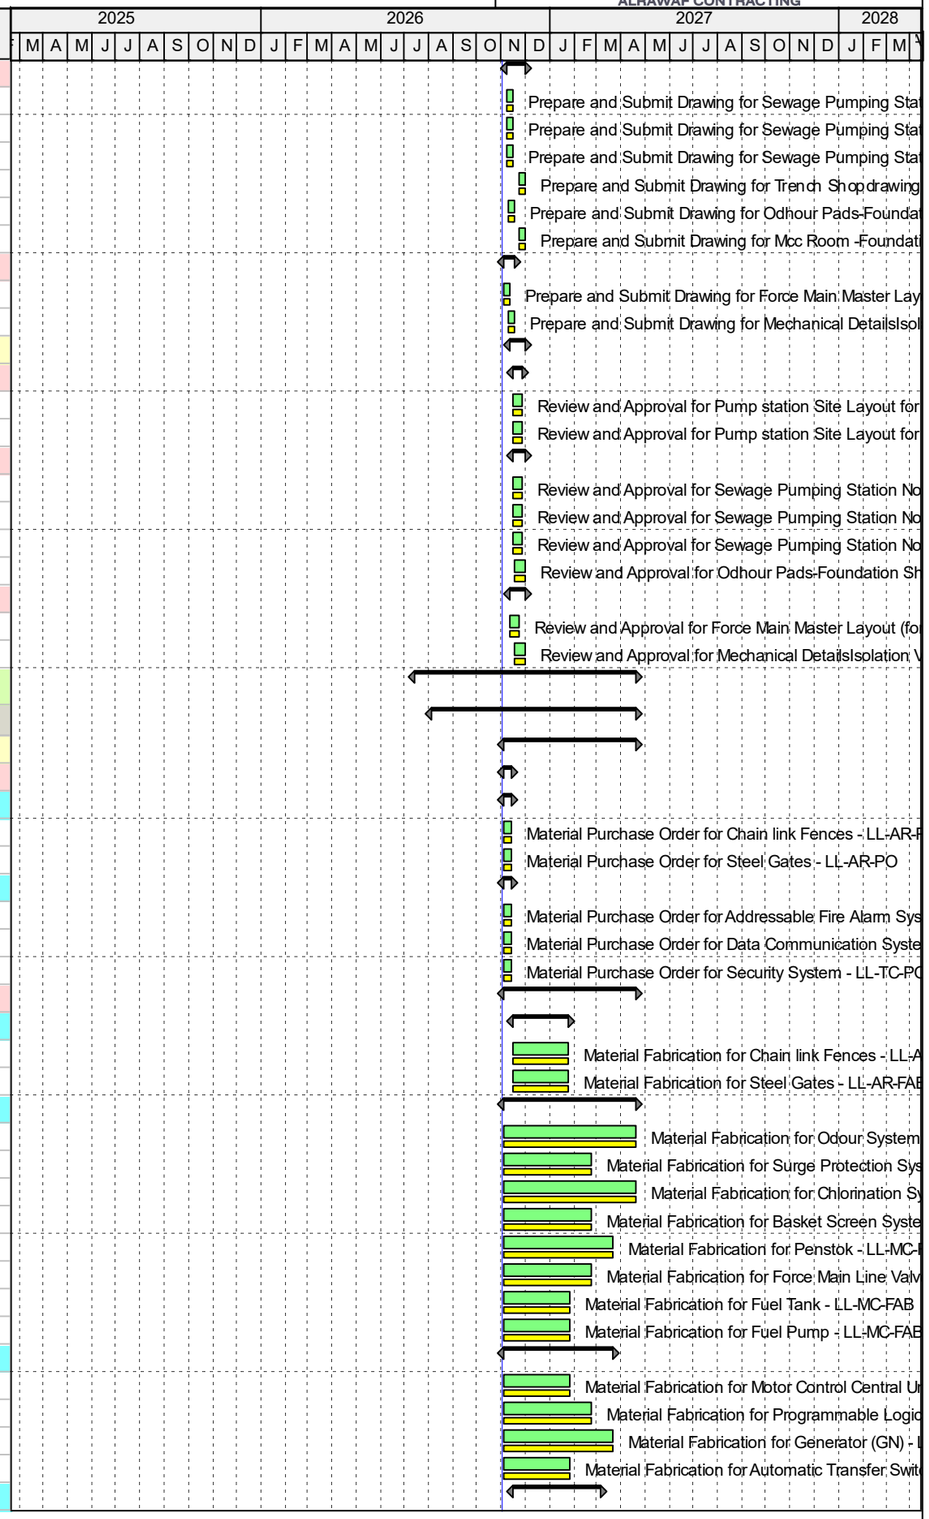


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Material Fabrication for Addressable Fire Alarm System - LL-TC-I	84	15-Nov-26	06-Feb-27	315	0	0	0
	Material Fabrication for Data Communication System - LL-TC-FA	84	15-Nov-26	06-Feb-27	315	0	0	0
	Material Fabrication for Security System - LL-TC-FAB	112	15-Nov-26	06-Mar-27	287	0	0	0
Short Lead Items		38	04-Aug-26 A	27-Jan-27	341	0	119,790	352,322
Purchase Order - PO - Lift Station		14	03-Nov-26	18-Nov-26	401	0	0	0
JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR		14	03-Nov-26	18-Nov-26	389	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	14	03-Nov-26	18-Nov-26	389	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	14	03-Nov-26	18-Nov-26	149	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	14	03-Nov-26	18-Nov-26	158	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	14	03-Nov-26	18-Nov-26	170	0	0	0
	Material Purchase Order for Interlocking concrete paving - SH-A	14	03-Nov-26	18-Nov-26	182	0	0	0
JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC		14	03-Nov-26	18-Nov-26	206	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	14	03-Nov-26	18-Nov-26	194	0	0	0
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	14	03-Nov-26	18-Nov-26	206	0	0	0
	Material Purchase Order for Exhaust Fans - SH-MC-PO	14	03-Nov-26	18-Nov-26	206	0	0	0
JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL		14	03-Nov-26	18-Nov-26	401	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	14	03-Nov-26	18-Nov-26	401	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	14	03-Nov-26	18-Nov-26	401	0	0	0
Delivery and staging on Site - DOS- Lift Station		44	04-Aug-26 A	27-Jan-27	414	0	119,790	352,322
JDH3-02-009-SHL-DOS-LFT-AR-Architechture -AR		14	19-Nov-26	02-Dec-26	180	0	0	70,464
	Delivery for Acrylic Paint Materials - SH-AR-DOS	14	19-Nov-26	02-Dec-26	180	0	0	70,464
JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC		42	04-Aug-26 A	27-Jan-27	180	0	119,790	211,393
	Delivery for Wall mounted Split Units - SH-MC-DOS	14	04-Aug-26 A	27-Jan-27	180	0	35,232	70,464
	Delivery for Exhaust Fans - SH-MC-DOS	14	04-Aug-26 A	27-Jan-27	180	0	35,232	70,464
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	14	04-Aug-26 A	27-Jan-27	180	0	49,325	70,464
JDH3-02-009-SHL-DOS-LFT-EL-Electrical Network - EL		14	03-Nov-26	16-Nov-26	486	0	0	70,464
	Delivery for Panel Boards - SH-EL-DOS	14	03-Nov-26	16-Nov-26	486	0	0	70,464
Construction		102	14-Jul-26 A	17-Nov-26	402	0	110,200	289,327
FORCE MAIN		13	14-Jul-26 A	07-Nov-26	398	0	110,200	157,429
JDH3-02-009-BQ4-Pipes and Valves		13	14-Jul-26 A	07-Nov-26	398	0	110,200	157,429
JDH3-02-009-BQ4-HDPE Pipes-450 mm diameter depth from 1.5 to		13	14-Jul-26 A	07-Nov-26	398	0	110,200	157,429
	Primary Test for HDPE Pipe Line 450 mm - depth from 1.5 to 2.	13	14-Jul-26 A	07-Nov-26	398	0	110,200	157,429
SEWERAGE PUMP STATION		13	03-Nov-26	17-Nov-26	400	0	0	105,224
JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber		8	03-Nov-26	11-Nov-26	212	0	0	37,476
JDH3-02-009-BQ4-Valve chamber		8	03-Nov-26	11-Nov-26	212	0	0	37,476
	Shuttering for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2	03-Nov-26	04-Nov-26	212	0	0	7,495
	Steel Fixing for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2	05-Nov-26	07-Nov-26	212	0	0	18,738
	RC Casting for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2	08-Nov-26	09-Nov-26	212	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS2-BQ4-D03	2	10-Nov-26	11-Nov-26	212	0	0	3,748
JDH3-02-009-BQ4-Sewerage Pumps & MCC		13	03-Nov-26	17-Nov-26	207	0	0	27,101
JDH3-02-009-BQ4-Plinth for Odour Control System		13	03-Nov-26	17-Nov-26	207	0	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS2-BQ4-D03	3	03-Nov-26	05-Nov-26	207	0	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS2-BQ4-D03	6	07-Nov-26	12-Nov-26	207	0	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS2-BQ4-D03	2	14-Nov-26	15-Nov-26	207	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS2-BQ4-D03	2	16-Nov-26	17-Nov-26	207	0	0	2,710
JDH3-02-009-BQ4-Pump Lifting System		2	03-Nov-26	04-Nov-26	411	0	0	40,647
JDH3-02-009-BQ4-Surge protection system		2	03-Nov-26	04-Nov-26	411	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS2-BQ4-D15	2	03-Nov-26	04-Nov-26	411	0	0	40,647
MOTOR CONTROL CENTRE BUILDING		4	03-Nov-26	07-Nov-26	236	0	0	4,292
JDH3-02-009-BQ4-Sub Structure		4	03-Nov-26	07-Nov-26	236	0	0	4,292
JDH3-02-009-BQ4-Foundation		4	03-Nov-26	07-Nov-26	236	0	0	4,292
	Shuttering Foundation - (F623)-LFTS2-BQ4-D03	2	03-Nov-26	04-Nov-26	236	0	0	1,226
	Steel Fixing Foundation - (F623)-LFTS2-BQ4-D03	2	05-Nov-26	07-Nov-26	236	0	0	3,066

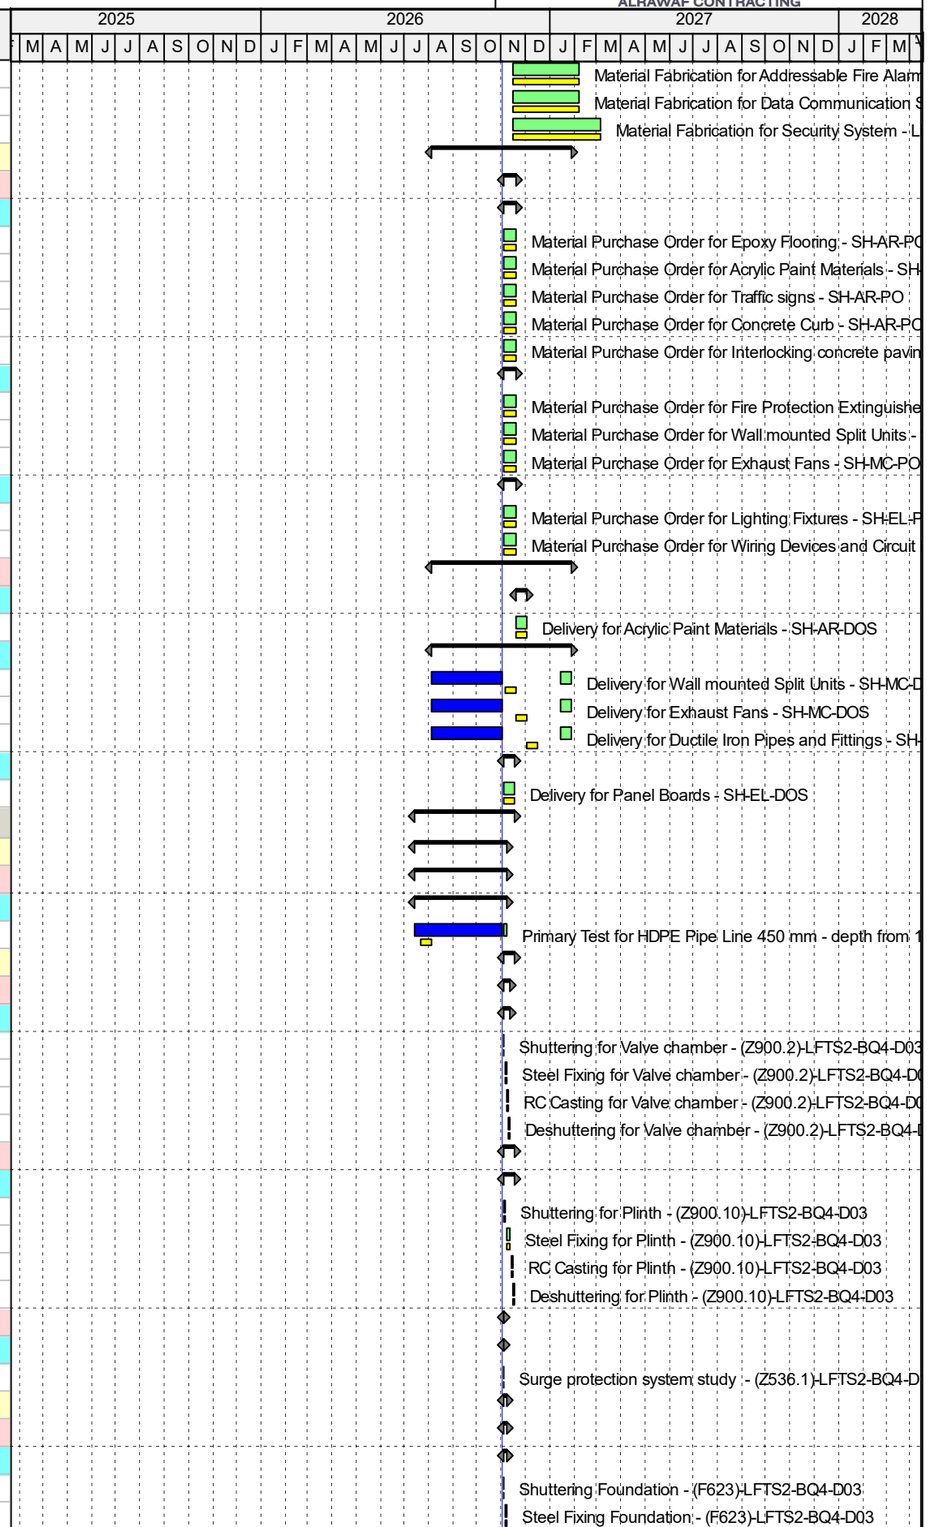


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Site Works	2	05-Nov-26	07-Nov-26	411	0	0	22,383
	JDH3-02-009-BQ4-Site Works	2	05-Nov-26	07-Nov-26	411	0	0	22,383
	JDH3-02-009-BQ4-Earth work	2	05-Nov-26	07-Nov-26	411	0	0	22,383
	Excavation Works - (20301-1)-LFTS2-BQ4-D02	2	05-Nov-26	07-Nov-26	411	0	0	22,383
	Close Out	18	10-Nov-26	30-Nov-26	391	0	0	0
	As Built Drawing Submittals - SUB-Lift Station - LFTS	12	10-Nov-26	23-Nov-26	387	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	10-Nov-26	17-Nov-26	392	0	0	0
	JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST	12	10-Nov-26	23-Nov-26	387	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7	16-Nov-26	23-Nov-26	387	0	0	0
	As Built Drawing Approvals - APP-Lift Station - LFTS	9	18-Nov-26	30-Nov-26	325	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-I	9	18-Nov-26	30-Nov-26	325	0	0	0
	JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Found	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Walls	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9	18-Nov-26	30-Nov-26	325	0	0	0
	JDH3-02-009-Lift Station 03	69	04-Aug-26 A	26-Feb-27	317	18,970	80,439	541,099
	Procurement	57	04-Aug-26 A	26-Feb-27	317	0	70,570	249,072
	Long Lead Items	51	03-Nov-26	01-Jan-27	364	0	0	41,512
	Purchase Order - PO - Lift Station	14	03-Nov-26	18-Nov-26	317	0	0	0
	JDH3-02-009-LOL-PO-LFT-AR-Architechture -AR	14	03-Nov-26	18-Nov-26	307	0	0	0
	Material Purchase Order for Chain link Fences - LL-AR-PO	14	03-Nov-26	18-Nov-26	299	0	0	0
	Material Purchase Order for Steel Gates - LL-AR-PO	14	03-Nov-26	18-Nov-26	307	0	0	0
	JDH3-02-009-LOL-PO-LFT-TC-Telecommunications Network - TC	14	03-Nov-26	18-Nov-26	317	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - LL	14	03-Nov-26	18-Nov-26	293	0	0	0
	Material Purchase Order for Data Communication System - LL-T	14	03-Nov-26	18-Nov-26	305	0	0	0
	Material Purchase Order for Security System - LL-TC-PO	14	03-Nov-26	18-Nov-26	317	0	0	0
	Fabrication - FAB - Lift Station	60	03-Nov-26	01-Jan-27	440	0	0	0
	JDH3-02-009-LOL-MAN-LFT-AR-Architechture -AR	14	19-Nov-26	02-Dec-26	369	0	0	0
	Material Fabrication for Chain link Fences - LL-AR-FAB	14	19-Nov-26	02-Dec-26	360	0	0	0
	Material Fabrication for Steel Gates - LL-AR-FAB	14	19-Nov-26	02-Dec-26	369	0	0	0
	JDH3-02-009-LOL-MAN-LFT-MC-Mechanical Systems -MC	60	03-Nov-26	01-Jan-27	440	0	0	0
	Material Fabrication for Odour System - LL-MC-FAB	60	03-Nov-26	01-Jan-27	324	0	0	0
	Material Fabrication for Surge Protection System - LL-MC-FAB	60	03-Nov-26	01-Jan-27	318	0	0	0
	Material Fabrication for Chlorination System - LL-MC-FAB	60	03-Nov-26	01-Jan-27	332	0	0	0
	Material Fabrication for Basket Screen System - LL-MC-FAB	14	03-Nov-26	16-Nov-26	392	0	0	0
	Material Fabrication for Penstok - LL-MC-FAB	14	03-Nov-26	16-Nov-26	406	0	0	0
	Material Fabrication for Force Main Line Valves - LL-MC-FAB	60	03-Nov-26	01-Jan-27	440	0	0	0
	Material Fabrication for Fuel Tank - LL-MC-FAB	60	03-Nov-26	01-Jan-27	288	0	0	0
	Material Fabrication for Fuel Pump - LL-MC-FAB	14	03-Nov-26	16-Nov-26	348	0	0	0
	JDH3-02-009-LOL-MAN-LFT-EL-Electrical Network - EL	14	03-Nov-26	16-Nov-26	486	0	0	0
	Material Fabrication for Motor Control Central Unit (MCC) - LL-EL	14	03-Nov-26	16-Nov-26	362	0	0	0
	Material Fabrication for Programmable Logic Controllers - LL-EL	14	03-Nov-26	16-Nov-26	376	0	0	0
	Material Fabrication for Generator (GN) - LL-EL-FAB	14	03-Nov-26	16-Nov-26	486	0	0	0
	Material Fabrication for Automatic Transfer Switch (ATS) - LL-EL	14	03-Nov-26	16-Nov-26	355	0	0	0
	JDH3-02-009-LOL-MAN-LFT-TC-Telecommunications Network - TC	14	19-Nov-26	02-Dec-26	381	0	0	0

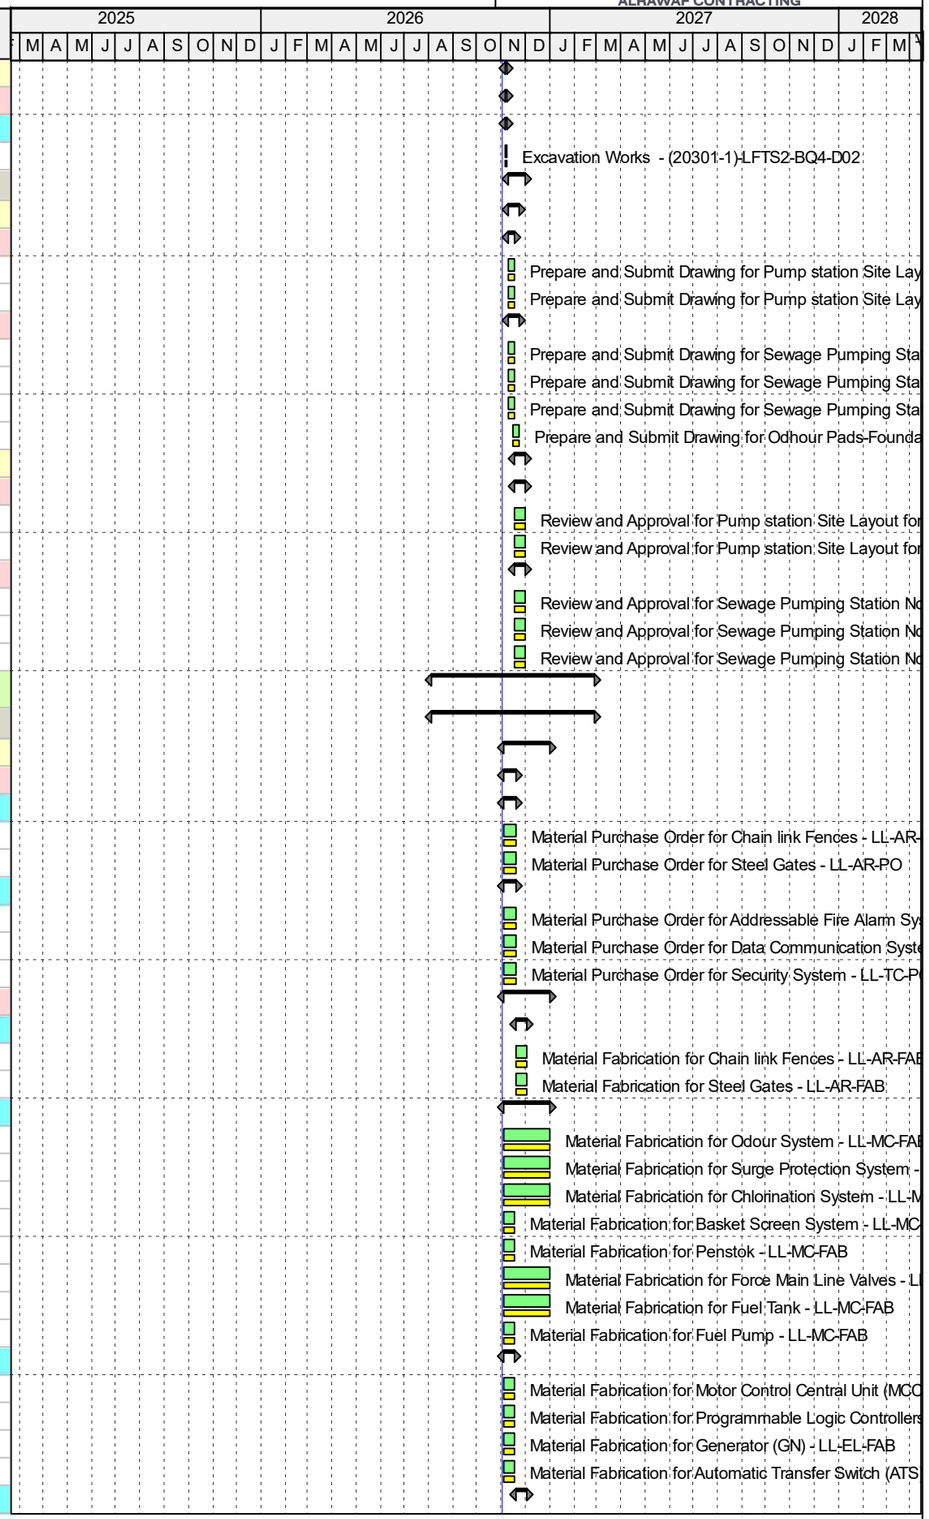

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Material Fabrication for Addressable Fire Alarm System - LL-TC-I	14	19-Nov-26	02-Dec-26	353	0	0	0
	Material Fabrication for Data Communication System - LL-TC-FA	14	19-Nov-26	02-Dec-26	367	0	0	0
	Material Fabrication for Security System - LL-TC-FAB	14	19-Nov-26	02-Dec-26	381	0	0	0
	Delivery and staging on Site - DOS- Lift Station	14	17-Nov-26	30-Nov-26	355	0	0	41,512
	JDH3-02-009-LOL-DOS-LFT-EL-Electrical Network - EL	14	17-Nov-26	30-Nov-26	355	0	0	41,512
	Delivery for Automatic Transfer Switch (ATS) - LL-EL-DOS	14	17-Nov-26	30-Nov-26	355	0	0	41,512
	Short Lead Items	57	04-Aug-26 A	26-Feb-27	317	0	70,570	207,560
	Purchase Order - PO - Lift Station	14	03-Nov-26	18-Nov-26	401	0	0	0
	JDH3-02-009-SHL-PO-LFT-AR-Architechture -AR	14	03-Nov-26	18-Nov-26	366	0	0	0
	Material Purchase Order for Epoxy Flooring - SH-AR-PO	14	03-Nov-26	18-Nov-26	318	0	0	0
	Material Purchase Order for Acrylic Paint Materials - SH-AR-PO	14	03-Nov-26	18-Nov-26	330	0	0	0
	Material Purchase Order for Traffic signs - SH-AR-PO	14	03-Nov-26	18-Nov-26	342	0	0	0
	Material Purchase Order for Concrete Curb - SH-AR-PO	14	03-Nov-26	18-Nov-26	354	0	0	0
	Material Purchase Order for Interlocking concrete paving - SH-AI	14	03-Nov-26	18-Nov-26	366	0	0	0
	JDH3-02-009-SHL-PO-LFT-MC-Mechanical Systems -MC	14	03-Nov-26	18-Nov-26	364	0	0	0
	Material Purchase Order for Fire Protection Extinguisher - SH-MC	14	03-Nov-26	18-Nov-26	352	0	0	0
	Material Purchase Order for Wall mounted Split Units - SH-MC-P	14	03-Nov-26	18-Nov-26	364	0	0	0
	Material Purchase Order for Exhaust Fans - SH-MC-PO	14	03-Nov-26	18-Nov-26	364	0	0	0
	JDH3-02-009-SHL-PO-LFT-EL-Electrical Network - EL	14	03-Nov-26	18-Nov-26	401	0	0	0
	Material Purchase Order for Lighting Fixtures - SH-EL-PO	14	03-Nov-26	18-Nov-26	401	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	14	03-Nov-26	18-Nov-26	401	0	0	0
	Delivery and staging on Site - DOS- Lift Station	67	04-Aug-26 A	26-Feb-27	384	0	70,570	207,560
	JDH3-02-009-SHL-DOS-LFT-MC-Mechanical Systems -MC	67	04-Aug-26 A	26-Feb-27	336	0	70,570	166,048
	Delivery for Pump Lifting Mechanism - SH-MC-DOS	14	03-Nov-26	16-Nov-26	420	0	0	41,512
	Delivery for Wall mounted Split Units - SH-MC-DOS	14	04-Aug-26 A	26-Feb-27	336	0	20,756	41,512
	Delivery for Exhaust Fans - SH-MC-DOS	14	04-Aug-26 A	26-Feb-27	336	0	20,756	41,512
	Delivery for Ductile Iron Pipes and Fittings - SH-MC-DOS	14	04-Aug-26 A	26-Feb-27	336	0	29,058	41,512
	JDH3-02-009-SHL-DOS-LFT-EL-Electrical Network - EL	14	03-Nov-26	16-Nov-26	486	0	0	41,512
	Delivery for Panel Boards - SH-EL-DOS	14	03-Nov-26	16-Nov-26	486	0	0	41,512
	Construction	40	20-Oct-26 A	05-Dec-26	361	18,970	9,868	292,027
	Site Work and Service Road	4	19-Nov-26	23-Nov-26	371	0	0	10,063
	JDH3-02-009-BQ4-Roads Work	4	19-Nov-26	23-Nov-26	371	0	0	10,063
	JDH3-02-009-BQ4-Roads	4	19-Nov-26	23-Nov-26	371	0	0	10,063
	300mm thick Subgrade - (R116)-LFTS3-BQ4-D02	2	19-Nov-26	21-Nov-26	371	0	0	5,063
	200mm thick Aggregate base course - (R343)-LFTS3-BQ4-D02	2	22-Nov-26	23-Nov-26	371	0	0	5,000
	SEWERAGE PUMP STATION	30	20-Oct-26 A	23-Nov-26	365	18,970	7,870	126,766
	JDH3-02-009-BQ4-Wet Well Structure And Valve Chamber	17	20-Oct-26 A	09-Nov-26	373	0	7,870	37,476
	JDH3-02-009-BQ4-Valve chamber	17	20-Oct-26 A	09-Nov-26	373	0	7,870	37,476
	RC Casting for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2	04-Nov-26	07-Nov-26	373	0	0	7,495
	Deshuttering for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2	07-Nov-26	09-Nov-26	373	0	0	3,748
	Shuttering for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2	20-Oct-26 A	04-Nov-26	362	0	2,249	7,495
	Steel Fixing for Valve chamber - (Z900.2)-LFTS3-BQ4-D03	2	22-Oct-26 A	04-Nov-26	362	0	5,621	18,738
	JDH3-02-009-BQ4-Sewerage Pumps & MCC	13	03-Nov-26	17-Nov-26	362	18,970	0	27,101
	JDH3-02-009-BQ4-Plinth for Odour Control System	13	03-Nov-26	17-Nov-26	362	18,970	0	27,101
	Shuttering for Plinth - (Z900.10)-LFTS3-BQ4-D03	3	03-Nov-26	05-Nov-26	362	5,420	0	5,420
	Steel Fixing for Plinth - (Z900.10)-LFTS3-BQ4-D03	6	07-Nov-26	12-Nov-26	362	13,550	0	13,550
	RC Casting for Plinth - (Z900.10)-LFTS3-BQ4-D03	2	14-Nov-26	15-Nov-26	362	0	0	5,420
	Deshuttering for Plinth - (Z900.10)-LFTS3-BQ4-D03	2	16-Nov-26	17-Nov-26	362	0	0	2,710
	JDH3-02-009-BQ4-Pump Lifting System	18	03-Nov-26	23-Nov-26	365	0	0	62,189
	JDH3-02-009-BQ4-Surge protection system	2	03-Nov-26	04-Nov-26	381	0	0	40,647
	Surge protection system study - (Z536.1)-LFTS3-BQ4-D15	2	03-Nov-26	04-Nov-26	381	0	0	40,647
	JDH3-02-009-BQ4-Underground Ducts and Raceways for Electrica	4	19-Nov-26	23-Nov-26	272	0	0	21,543
	Electrical Hand Hole 600 x 600 mm - (K151.1)-LFTS3-BQ4-D16	4	19-Nov-26	23-Nov-26	272	0	0	21,543

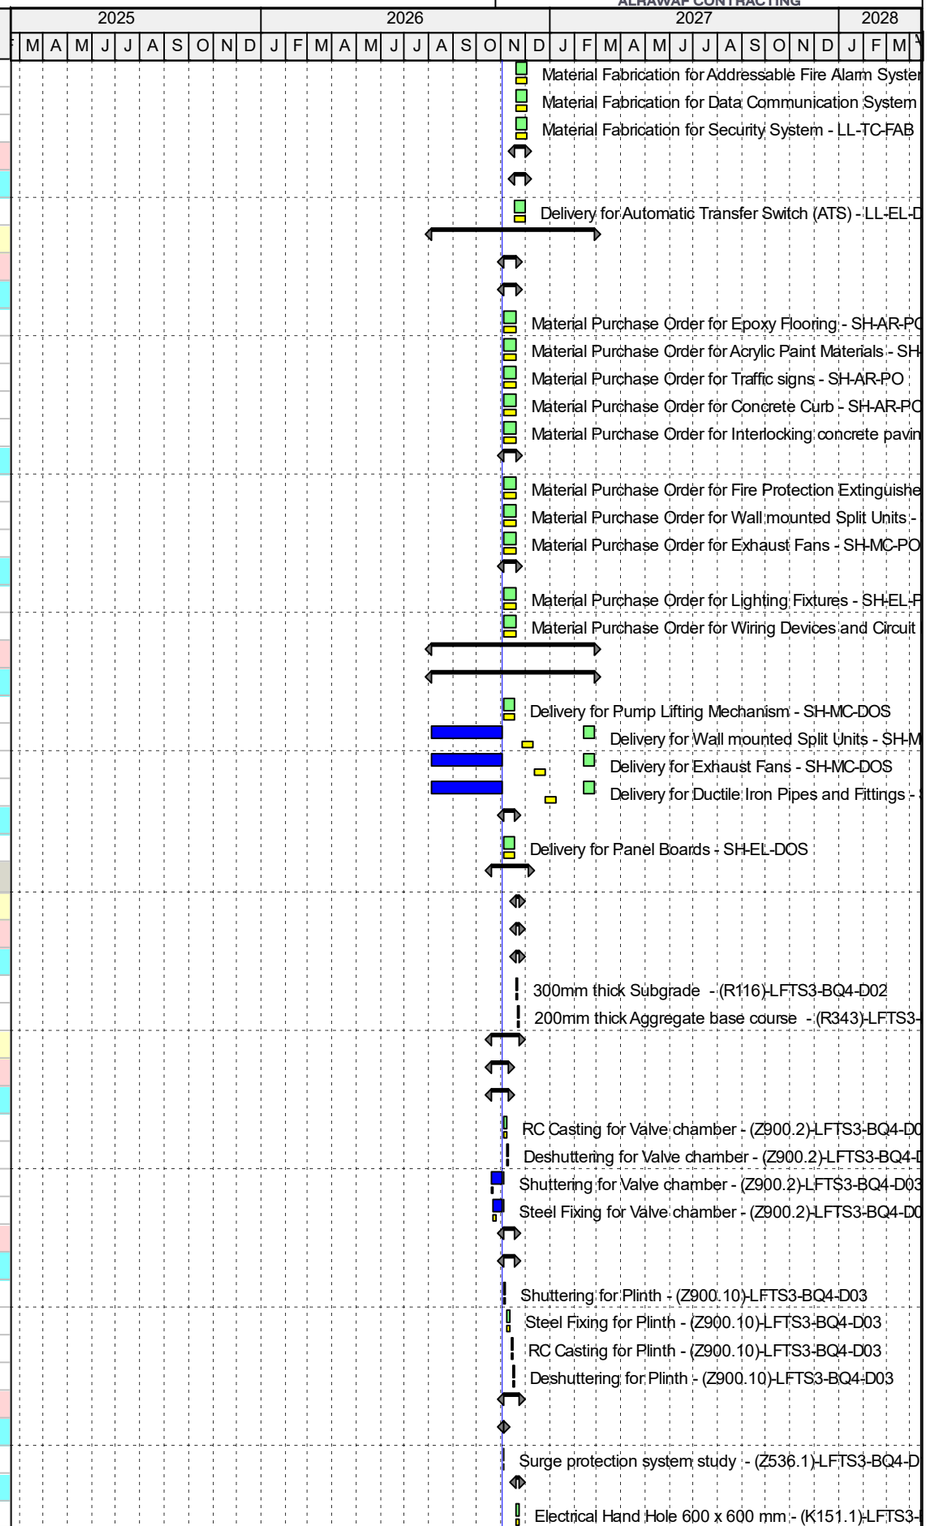

Actual Level of Effort
Remaining Work
Primary Baseline
Critical Remaining Work
Actual Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		


Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	MOTOR CONTROL CENTRE BUILDING	38	22-Oct-26 A	05-Dec-26	269	0	1,998	150,096
	JDH3-02-009-BQ4-Super Structure	18	22-Oct-26 A	11-Nov-26	263	0	1,998	15,988
	JDH3-02-009-BQ4-Roof Slab	18	22-Oct-26 A	11-Nov-26	263	0	1,998	15,988
	RC Casting Roof Slab - (F622)-LFTS3-BQ4-D03	2	08-Nov-26	09-Nov-26	263	0	0	3,997
	Deshuttering Roof Slab - (F622)-LFTS3-BQ4-D03	2	10-Nov-26	11-Nov-26	263	0	0	1,998
	Steel Fixing Roof Slab - (F622)-LFTS3-BQ4-D03	5	22-Oct-26 A	07-Nov-26	263	0	1,998	9,992
	JDH3-02-009-BQ4-Finishes	4	12-Nov-26	16-Nov-26	263	0	0	17,623
	JDH3-02-009-BQ4-Masonary	2	15-Nov-26	16-Nov-26	263	0	0	5,971
	Masonary Block work (CMU walls) Insulated Block Work - (F644)	2	15-Nov-26	16-Nov-26	263	0	0	5,971
	JDH3-02-009-BQ4-Thermal & Moisture Protection	2	12-Nov-26	14-Nov-26	263	0	0	11,652
	Install Roof Isulation - (W149)-LFTS3-BQ4-D07	2	12-Nov-26	14-Nov-26	263	0	0	11,652
	JDH3-02-009-BQ4-Electrical Works	16	17-Nov-26	05-Dec-26	269	0	0	116,486
	JDH3-02-009-BQ4-LV Cables - 4Cx 185mm2 Cu/XLPE//PVC	13	17-Nov-26	01-Dec-26	272	0	0	81,043
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	5	17-Nov-26	22-Nov-26	272	0	0	32,417
	Cable Tray Installation for LV Cables 4Cx185 mm²- (Z711.1)-LF	8	23-Nov-26	01-Dec-26	272	0	0	48,626
	JDH3-02-009-BQ4-LV Cables - 4Cx 95mm2 Cu/XLPE//PVC	16	17-Nov-26	05-Dec-26	264	0	0	12,607
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx9	16	17-Nov-26	05-Dec-26	264	0	0	12,607
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 Cu/XLPE/SWA/PVC	10	17-Nov-26	28-Nov-26	272	0	0	400
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	10	17-Nov-26	28-Nov-26	272	0	0	400
	JDH3-02-009-BQ4-LV Cables - 4Cx 150mm2 + 1Cx25mm2	9	17-Nov-26	26-Nov-26	263	0	0	11,162
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	9	17-Nov-26	26-Nov-26	263	0	0	11,162
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	2	17-Nov-26	18-Nov-26	280	0	0	400
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	2	17-Nov-26	18-Nov-26	280	0	0	400
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	10	17-Nov-26	28-Nov-26	275	0	0	2,001
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	4	17-Nov-26	21-Nov-26	275	0	0	800
	Cable Tray Installation for LV Cables 4Cx10 mm2+1Cx10 mm2	6	22-Nov-26	28-Nov-26	275	0	0	1,201
	JDH3-02-009-BQ4-LV Cables - 4Cx 10mm2 + 1Cx10mm2 Cu/XLPE/	10	17-Nov-26	28-Nov-26	275	0	0	2,001
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	4	17-Nov-26	21-Nov-26	275	0	0	800
	Cable Tray Installation for LV Cables 4Cx10 mm2+1Cx10 mm2	6	22-Nov-26	28-Nov-26	275	0	0	1,201
	JDH3-02-009-BQ4-LV Cables - 4Cx 6mm2 + 1Cx6mm2 Cu/XLPE/P	9	17-Nov-26	26-Nov-26	276	0	0	1,226
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx6	4	17-Nov-26	21-Nov-26	276	0	0	490
	Cable Tray Installation for LV Cables 4Cx6 mm2+1Cx6 mm2- (Z	5	22-Nov-26	26-Nov-26	276	0	0	735
	JDH3-02-009-BQ4-LV Cables - 3Cx 6mm2 Cu/XLPE/PVC FROM MC	10	17-Nov-26	28-Nov-26	275	0	0	1,313
	Electrical Conduits and Pull Box Installation for LV Cables 3Cx6	4	17-Nov-26	21-Nov-26	275	0	0	525
	Cable Tray Installation for LV Cables 3Cx6 mm²- (Z711.9)-LFTS	6	22-Nov-26	28-Nov-26	275	0	0	788
	JDH3-02-009-BQ4-LV Cables - 3Cx 4mm2 Cu/XLPE/PVC to the AC.	9	17-Nov-26	26-Nov-26	276	0	0	900
	Electrical Conduits and Pull Box Installation for LV Cables 3Cx4	4	17-Nov-26	21-Nov-26	276	0	0	360
	Cable Tray Installation for LV Cables 3Cx4 mm²- (Z711.10)-LFT	5	22-Nov-26	26-Nov-26	276	0	0	540
	JDH3-02-009-BQ4-LED Interior Lighting	2	17-Nov-26	18-Nov-26	280	0	0	380
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	17-Nov-26	18-Nov-26	280	0	0	380
	JDH3-02-009-BQ4-Addressable Fire-Alarm System	2	17-Nov-26	18-Nov-26	280	0	0	3,052
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (Z900.	2	17-Nov-26	18-Nov-26	280	0	0	3,052
	Site Works	10	12-Nov-26	23-Nov-26	301	0	0	5,101
	JDH3-02-009-BQ4-Electrical Works	10	12-Nov-26	23-Nov-26	301	0	0	5,101
	JDH3-02-009-BQ4-(LV)-Ducts Bank (1 x 50 mm UPVC)	2	12-Nov-26	14-Nov-26	272	0	0	163
	Duct Bank Installationfor UPVC Duct Bank 1x50 mm - - (K591)-L	2	12-Nov-26	14-Nov-26	272	0	0	163
	JDH3-02-009-BQ4-(LV)-Ducts Bank (2 x 50 mm UPVC)	2	15-Nov-26	16-Nov-26	272	0	0	231
	Duct Bank Installationfor UPVC Duct Bank 2x50 mm - - (K592)-L	2	15-Nov-26	16-Nov-26	272	0	0	231
	JDH3-02-009-BQ4-(LV)-Ducts Bank (8 x 50 mm UPVC)	2	17-Nov-26	18-Nov-26	272	0	0	887
	Duct Bank Installationfor UPVC Duct Bank 8x50 mm - - (K593)-L	2	17-Nov-26	18-Nov-26	272	0	0	887
	JDH3-02-009-BQ4-Earthing	4	19-Nov-26	23-Nov-26	301	0	0	3,821
	Supply, construct, connect and test earthing pitsfor Earthing Sys	2	19-Nov-26	21-Nov-26	301	0	0	813
	Cable draw pit, 600x600mm for Earthing System - - (X900.8)-L	2	22-Nov-26	23-Nov-26	301	0	0	3,008



Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
Close Out		24	03-Nov-26	30-Nov-26	391	0	0	0
As Built Drawing Submittals - SUB-Lift Station - LFTS		19	03-Nov-26	24-Nov-26	386	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Architectural - AR		16	07-Nov-26	24-Nov-26	386	0	0	0
JDI	Prepare and Submit Drawing for Flooring Roof Floor Plan for SU	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Over All Plan Ceiling for SUB-A	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Walls Ground Floor plan for SU	7	17-Nov-26	24-Nov-26	386	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for Motor Control CenterBuilding fo	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Pump station Site Layout for S	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for Motor Control CenterBuilding fo	7	10-Nov-26	17-Nov-26	392	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		18	03-Nov-26	23-Nov-26	387	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for Sewage Pumping Station No. 2	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for Trench Shopdrawings for SUB-A	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Odhour Pads-Foundation Shop	7	16-Nov-26	23-Nov-26	387	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -Foundation Shop D	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -ColumnsShop Draw	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mcc Room -RoofShop Drawing	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Air Release Valve Chamber Str	7	09-Nov-26	17-Nov-26	393	0	0	0
JDI	Prepare and Submit Drawing for Wash-out Valve Chamber Struc	7	09-Nov-26	17-Nov-26	393	0	0	0
JDI	Prepare and Submit Drawing for Single Valve Chamber Structur	7	03-Nov-26	10-Nov-26	398	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Infra - IN		7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Force Main Master Layout (forc	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsIsolation Val	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsAir Chamber	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Mechanical DetailsWashout Ch	7	03-Nov-26	10-Nov-26	398	0	0	0
As Built Drawing Approvals - APP-Lift Station - LFTS		14	11-Nov-26	30-Nov-26	325	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Architectural - AR		12	15-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Flooring Roof Floor Plan for APP-AS-LI	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Over All Plan Ceiling for APP-AS-LFTS	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-L	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for Motor Control CenterBuilding for APP-A	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Pump station Site Layout for APP-AS-L	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for Motor Control CenterBuilding for APP-A	9	18-Nov-26	30-Nov-26	325	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		14	11-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Found	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Walls	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for Sewage Pumping Station No. 2 -Roofs	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for Trench Shopdrawings for APP-AS-LFTS	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mcc Room -Foundation Shop Drawing	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mcc Room -ColumnsShop Drawing for	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mcc Room -RoofShop Drawing for APF	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Air Release Valve Chamber Structure T	9	17-Nov-26	30-Nov-26	326	0	0	0
JDI	Review and Approval for Wash-out Valve Chamber Structure Typ	9	17-Nov-26	30-Nov-26	326	0	0	0
JDI	Review and Approval for Single Valve Chamber Structure Typica	9	11-Nov-26	23-Nov-26	330	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Infra - IN		9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Force Main Master Layout (force Main-A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mechanical DetailsIsolation Valve Char	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mechanical DetailsAir Chambers for AF	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Mechanical DetailsWashout Chambers	9	11-Nov-26	23-Nov-26	330	0	0	0
JDH3-02-009-Mosque		123	28-Jul-26 A	30-Jan-27	339	278,276	149,356	796,344

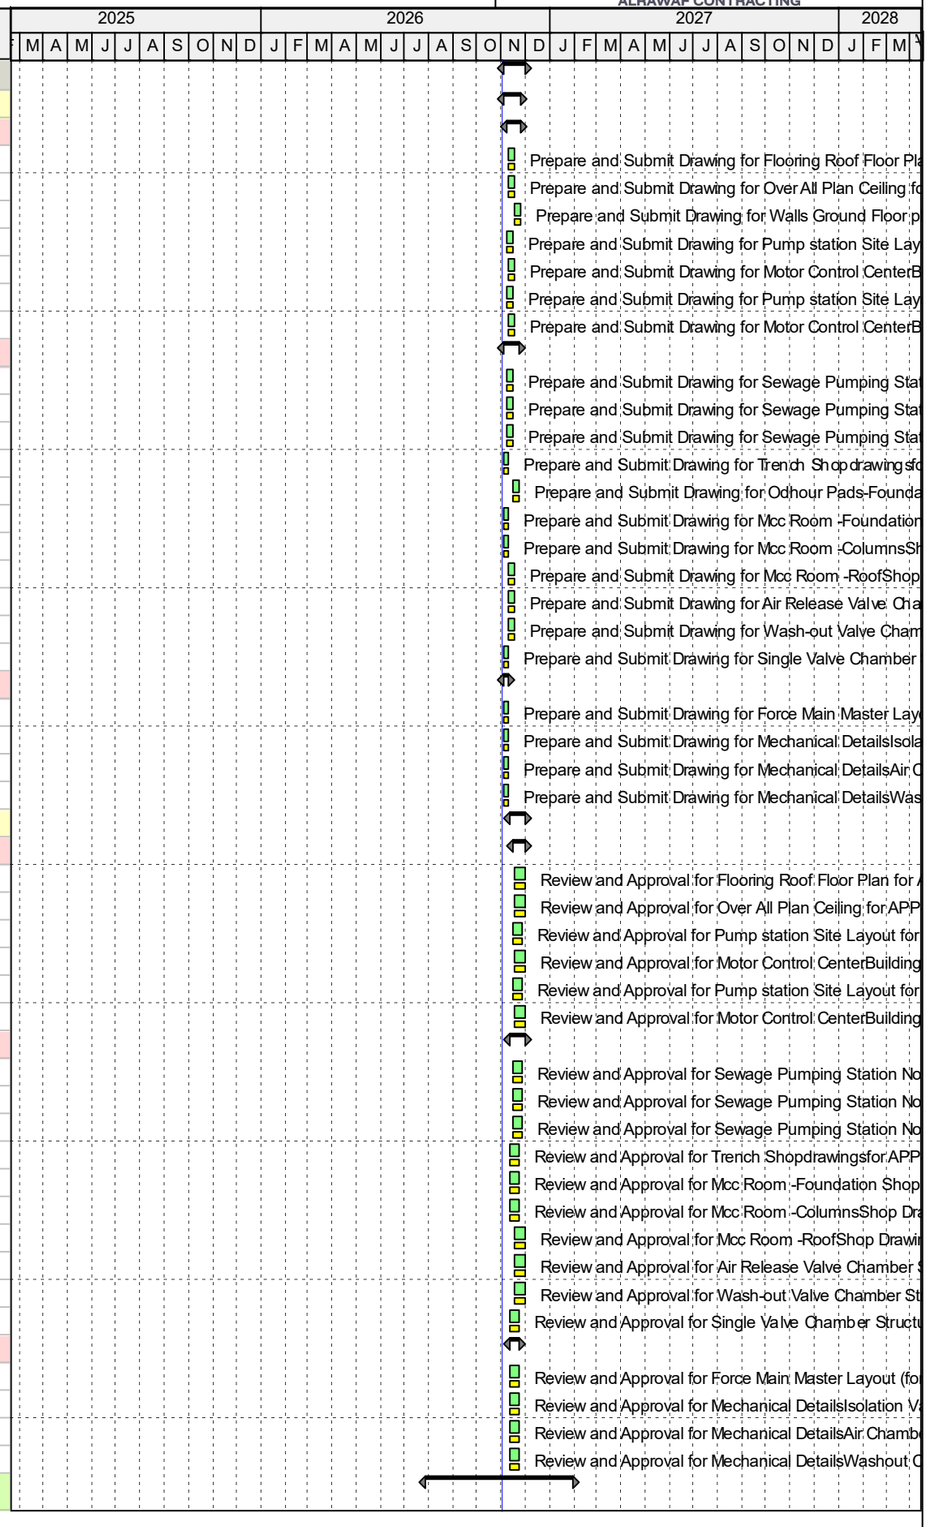

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
Engineering		66	01-Sep-26 A	24-Nov-26	396	26,382	3,693	26,382
JDH3-02-009-Prequalification and Material Submittals - SUB-MQ		54	08-Sep-26 A	10-Nov-26	408	0	0	0
Architectural		7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . doors &	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . eboxy m	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . paint an	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . CEMENT	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . PORCEL	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . anti slip	7	03-Nov-26	10-Nov-26	312	0	0	0
JDI	Submission of P.Q issuance for supplier and material . wall pap	7	03-Nov-26	10-Nov-26	265	0	0	0
JDI	Submission of P.Q issuance for supplier and material . speciel it	7	03-Nov-26	10-Nov-26	288	0	0	0
Steel Material		7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . STAINLE	7	03-Nov-26	10-Nov-26	408	0	0	0
JDI	Submission of P.Q issuance for supplier and material . Steel La	7	03-Nov-26	10-Nov-26	408	0	0	0
Mechanical		7	08-Sep-26 A	10-Nov-26	127	0	0	0
JDI	Submission of P.Q issuance for supplier and material . PLUMBII	7	08-Sep-26 A	10-Nov-26	127	0	0	0
Landscape		7	08-Sep-26 A	10-Nov-26	269	0	0	0
JDI	Submission of P.Q issuance for roads,pavements,trees-PR-MQ-	7	08-Sep-26 A	10-Nov-26	269	0	0	0
JDH3-02-009-Prequalification and Material Approvals - APP-MQ		54	01-Sep-26 A	24-Nov-26	258	26,382	3,693	26,382
Architectural		10	11-Nov-26	24-Nov-26	258	15,829	0	15,829
JDI	Approval of Material Submittal for anti slip matt-PR-MQ-AR-App-	10	11-Nov-26	24-Nov-26	258	5,276	0	5,276
JDI	Approval of Material Submittal for wall paper-PR-MQ-AR-App-13	10	11-Nov-26	24-Nov-26	219	5,276	0	5,276
JDI	Approval of Material Submittal for speciel items for bathrooms ,	10	11-Nov-26	24-Nov-26	238	5,276	0	5,276
Mechanical		10	01-Sep-26 A	16-Nov-26	101	5,276	1,055	5,276
JDI	Approval of Material Submittal for PLUMBING Material-PR-MQ-M	10	01-Sep-26 A	16-Nov-26	101	5,276	1,055	5,276
Landscape		10	01-Sep-26 A	16-Nov-26	219	5,276	2,638	5,276
JDI	Approval of Material Submittal for roads,pavements,trees-PR-MC	10	01-Sep-26 A	16-Nov-26	219	5,276	2,638	5,276
Procurement		47	08-Sep-26 A	10-Dec-26	319	25,229	2,523	50,458
Short Lead Items		47	08-Sep-26 A	10-Dec-26	319	25,229	2,523	50,458
Purchase Order - PO-Mosque		33	03-Nov-26	10-Dec-26	319	0	0	0
Architectural		21	03-Nov-26	26-Nov-26	331	0	0	0
	P.O Issue For Material . CARPET FLOOR ADHERED-PQ-MQ-A	21	03-Nov-26	26-Nov-26	331	0	0	0
	P.O Issue For Material for doors & windows materials-PQ-MQ-A	21	03-Nov-26	26-Nov-26	292	0	0	0
	P.O Issue For Material for eboxy materials-PQ-MQ-AR-PO-1520	21	03-Nov-26	26-Nov-26	327	0	0	0
	P.O Issue For Material for gypsom materials-PQ-MQ-AR-PO-15	21	03-Nov-26	26-Nov-26	323	0	0	0
	P.O Issue For Material for paint and ecrylic materials-PQ-MQ-AF	21	03-Nov-26	26-Nov-26	325	0	0	0
	P.O Issue For Material for CEMENT TILES 300x300 MM-PQ-MC	21	03-Nov-26	26-Nov-26	148	0	0	0
	P.O Issue For Material for PORCELAIN TILE 600X600MM-PQ-M	21	03-Nov-26	26-Nov-26	148	0	0	0
	P.O Issue For Material for Marbles-PQ-MQ-AR-PO-1640	21	03-Nov-26	26-Nov-26	164	0	0	0
Steel Material		21	03-Nov-26	26-Nov-26	290	0	0	0
	P.O Issue For Material . STAINLESS STEEL RAILING WITH WC	21	03-Nov-26	26-Nov-26	287	0	0	0
	P.O Issue For Material . Steel Ladder-PQ-MQ-SM-PO-1200	21	03-Nov-26	26-Nov-26	290	0	0	0
Electrical		21	03-Nov-26	26-Nov-26	320	0	0	0
	P.O Issue For Material . Telecommunication-PQ-MQ-EL-PO-133	21	03-Nov-26	26-Nov-26	320	0	0	0
	P.O Issue For Material . DISTRIBUTION BOARDS-PQ-MQ-EL-P	21	03-Nov-26	26-Nov-26	163	0	0	0
	P.O Issue For Material . FIRE ALARM SYSTEM-PQ-MQ-EL-PO-	21	03-Nov-26	26-Nov-26	111	0	0	0
	P.O Issue For Material . SOUND SYSTEM-PQ-MQ-EL-PO-1360	21	03-Nov-26	26-Nov-26	113	0	0	0
Mechanical		33	03-Nov-26	10-Dec-26	122	0	0	0
	P.O Issue For Material . PLUMBING Material-PQ-MQ-MC-PO-13	21	17-Nov-26	10-Dec-26	122	0	0	0
	P.O Issue For Material . HVAC-PQ-MQ-MC-PO-1390	21	03-Nov-26	26-Nov-26	112	0	0	0
Landscape		21	17-Nov-26	10-Dec-26	264	0	0	0
	P.O Issue For Material for roads,pavements,trees-PQ-MQ-LC-PC	21	17-Nov-26	10-Dec-26	264	0	0	0

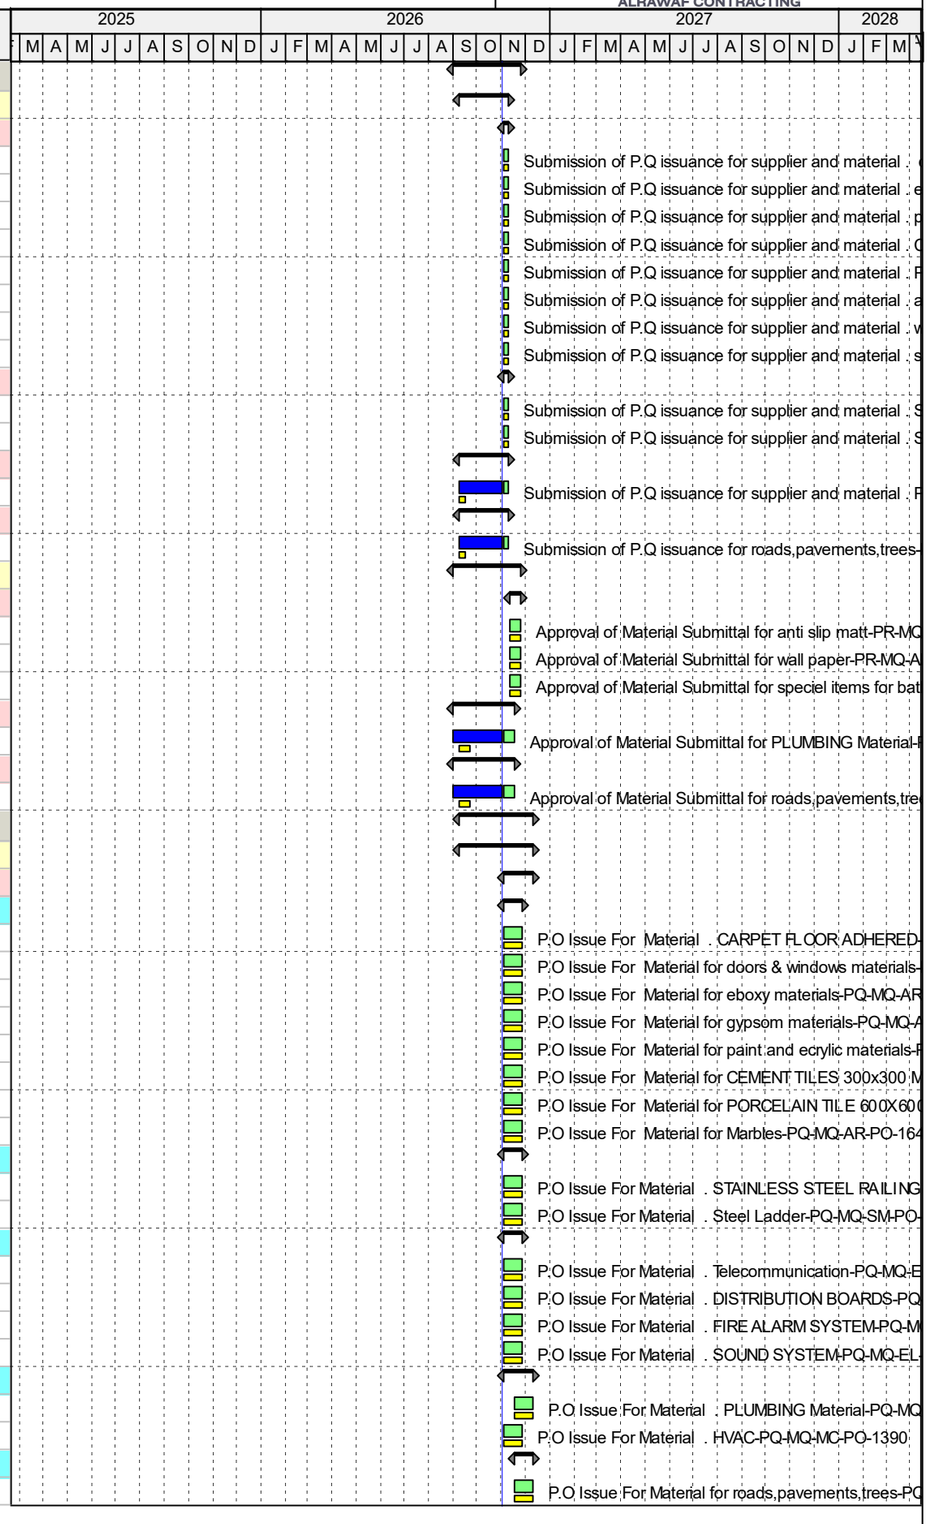


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Delivery and staging on Site - DOS-Mosque	37	08-Sep-26 A	10-Dec-26	207	25,229	2,523	50,458
	Electrical	21	03-Nov-26	23-Nov-26	224	0	0	25,229
	INS&delivery and staging Material . change to wires & caples-P	21	03-Nov-26	23-Nov-26	224	0	0	25,229
	Mechanical	21	08-Sep-26 A	10-Dec-26	147	25,229	2,523	25,229
	INS&delivery and staging Material . PLUMBING Material-PQ-MC	21	08-Sep-26 A	10-Dec-26	147	25,229	2,523	25,229
Construction		117	28-Jul-26 A	30-Jan-27	339	226,665	143,140	719,503
Mosque Main Building		108	01-Sep-26 A	30-Jan-27	339	144,213	33,434	181,803
	SuperStructure for Building	4	03-Nov-26	07-Nov-26	411	4,295	0	4,295
	Slab For Main Building	4	03-Nov-26	07-Nov-26	411	4,295	0	4,295
	Pouring for RC Steps And Ramps - (B3.1.3.4.3)-MQ-MB-SI-D03	1	03-Nov-26	03-Nov-26	411	3,754	0	3,754
	De Shuttering for RC Steps And Ramps - (B3.1.3.4.3)-MQ-MB-S	3	04-Nov-26	07-Nov-26	411	541	0	541
	Finishing of Mosque Building	108	01-Sep-26 A	30-Jan-27	111	139,918	30,462	143,849
	Masonary Work - MSW	37	01-Sep-26 A	08-Nov-26	144	47,259	26,849	47,259
	Installation for External Insulated CMU (Parpet) - 200mm - (B3.1	4	03-Nov-26	08-Nov-26	144	13,697	0	13,697
	Installation for Internal Insulated CMU - 100mm - (B3.1.4.2.1)-M	4	03-Sep-26 A	08-Nov-26	144	987	789	987
	Installation for External Insulated CMU - 200mm - (B3.1.4.1.1)-M	4	01-Sep-26 A	03-Nov-26	144	16,189	12,951	16,189
	Installation for External Insulated CMU - 300mm - (B3.1.4.1.3)-M	4	02-Sep-26 A	08-Nov-26	144	10,718	8,574	10,718
	Installation for Internal Insulated CMU - 200mm - (B3.1.4.2.2)-M	4	01-Sep-26 A	08-Nov-26	144	5,668	4,535	5,668
	Thermal & Moisture Protection - INS	14	08-Nov-26	24-Nov-26	157	56,537	0	56,537
	Provide and Apply 4mm Thick Membrane To Roof - (B3.1.7.4.1	3	08-Nov-26	11-Nov-26	157	21,108	0	21,108
	Provide and Apply 50 Mm Thk Rigid Insulation To Roof - (B3.1.	3	11-Nov-26	15-Nov-26	157	14,734	0	14,734
	Provide and Apply 150 Micron Polyethylene Sheet To Roof - (B3	3	15-Nov-26	18-Nov-26	157	2,742	0	2,742
	Supplying and Fixing 3 Mm Thk Extruded Aluminum Flashing To	2	18-Nov-26	21-Nov-26	157	5,486	0	5,486
	Supplying and Apply Lightweight Concrete Screed To Roof - (B3	3	21-Nov-26	24-Nov-26	157	12,468	0	12,468
	Floor Finishes - FLR	16	12-Jan-27	30-Jan-27	111	0	0	3,930
	Installation of ceramic tiles To Living/Kitchen, women entrance,	8	12-Jan-27	20-Jan-27	111	0	0	2,374
	Installation of ceramic tiles To Steps (Threads & Risers) - (B3.1	4	21-Jan-27	25-Jan-27	111	0	0	61
	Installation ceramic tiles (To toilet-2) - (B3.1.9.1.3)-MQ-MB-FLR-I	4	26-Jan-27	30-Jan-27	111	0	0	1,496
	Walls Finishes - Wal	10	16-Sep-26 A	23-Dec-26	111	36,122	3,612	36,122
	Plastering to internal walls and columns - (B3.1.9.2.4)-MQ-MB-W	10	16-Sep-26 A	23-Dec-26	111	36,122	3,612	36,122
	Electrical Works of Mosque Building	12	15-Sep-26 A	17-Dec-26	321	0	2,972	33,659
	Grounding System - ER	6	15-Sep-26 A	17-Dec-26	320	0	2,972	13,518
	Installation of grounding system Ground rod with inspection pit	2	03-Nov-26	04-Nov-26	350	0	0	1,528
	Installation of grounding system Ground rod without inspection	2	05-Nov-26	07-Nov-26	353	0	0	2,081
	Installation of grounding system PVC insulated copper wire 70 r	2	17-Sep-26 A	17-Dec-26	320	0	619	2,064
	Installation of grounding system Bare copper ground wire 120 n	3	15-Sep-26 A	17-Dec-26	320	0	2,353	7,844
	Lightning system - LIG	10	03-Nov-26	14-Nov-26	350	0	0	20,141
	Installation of lightning protection system Bare tape copper con	5	05-Nov-26	10-Nov-26	350	0	0	12,756
	Installation of lightning protection system Air teminal rod 60 cm	3	11-Nov-26	14-Nov-26	350	0	0	2,845
	Installation of lightning protection system Bare copper down cor	3	03-Nov-26	05-Nov-26	357	0	0	4,540
Mosque Wash Room		58	15-Sep-26 A	22-Nov-26	392	12,837	1,043	24,491
	Finishing of Mosque Wash Room	17	03-Nov-26	22-Nov-26	179	1,403	0	13,056
	Masonary Work - MSW	2	03-Nov-26	04-Nov-26	147	1,403	0	1,403
	Installation for External Insulated CMU (Parpet) - 200 mm - (B3.:	2	03-Nov-26	04-Nov-26	147	1,403	0	1,403
	Thermal & Moisture Protection - INS	17	03-Nov-26	22-Nov-26	174	0	0	7,589
	Installation of 4mm thick membrane to Toilet - (B3.2.7.4.1.1)-M	4	05-Nov-26	09-Nov-26	185	0	0	2,294
	Installation of 4mm thick membrane to roof - (B3.2.7.4.1.2)-MQ	4	03-Nov-26	07-Nov-26	173	0	0	2,399
	Installation of 50 mm thk rigid insulation to Roof - (B3.2.7.4.2.1	4	08-Nov-26	11-Nov-26	173	0	0	1,597
	Installation of 150 micron polyethylene sheet to roof - (B3.2.7.4	4	12-Nov-26	16-Nov-26	173	0	0	286
	Installation of 3 mm thk extruded aluminum flashing to roof - (E	5	17-Nov-26	22-Nov-26	173	0	0	1,012
	Floor Finishes - FLR	2	10-Nov-26	11-Nov-26	188	0	0	4,065
	Installation of Anti -slip Rubber Hollow Mat - (B3.2.9.1.4)-MQ-WI	2	10-Nov-26	11-Nov-26	188	0	0	4,065
	Electrical Works of Wash Room	47	15-Sep-26 A	09-Nov-26	403	11,434	1,043	11,434

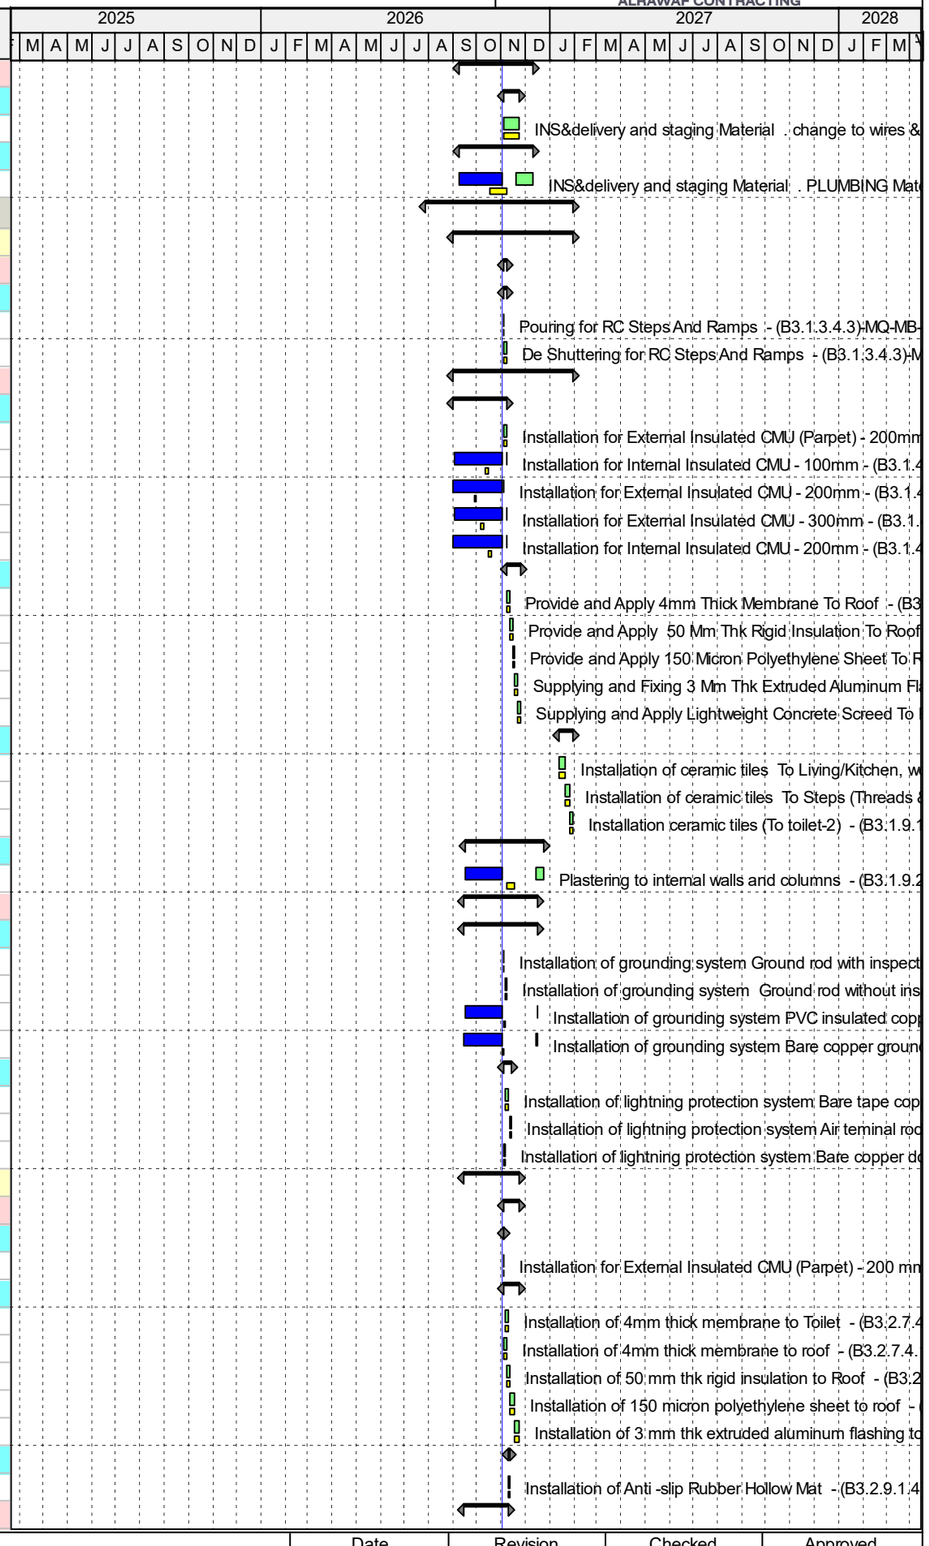


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Grounding System - GR	45	15-Sep-26 A	07-Nov-26	405	4,119	1,043	4,119
	Installation of grounding system Ground rod with inspection pit	2	03-Nov-26	04-Nov-26	372	382	0	382
	Installation of grounding system Ground rod without inspection	2	05-Nov-26	07-Nov-26	372	260	0	260
	Installation of grounding system PVC insulated copper wire 70 r	4	15-Sep-26 A	05-Nov-26	406	413	124	413
	Installation of grounding system Bare copper ground wire 120 n	4	15-Sep-26 A	05-Nov-26	406	3,064	919	3,064
	Lightning system - LIG	4	03-Nov-26	07-Nov-26	405	3,686	0	3,686
	Installation of lightning protection system Bare tape copper con	2	03-Nov-26	04-Nov-26	372	2,658	0	2,658
	Installation of lightning protection system Air teminal rod 60 cm l	2	05-Nov-26	07-Nov-26	372	203	0	203
	Installation of lightning protection system Bare copper down cor	2	03-Nov-26	04-Nov-26	407	825	0	825
	Low Voltage - LV	4	05-Nov-26	09-Nov-26	175	3,629	0	3,629
	Installation of Conduits and wiring outlets - (B5.2.16.4)-MQ-WR	4	05-Nov-26	09-Nov-26	175	3,629	0	3,629
	Mechanical Works For (Mosque Bldg+ Wash Area)	35	13-Aug-26 A	05-Jan-27	142	69,614	27,559	80,182
	Water Supply System - PW	6	08-Nov-26	15-Nov-26	144	18,722	0	18,722
JDI	Installation of for cold and hot water supply pipes 90 mm - (B4.1	6	08-Nov-26	15-Nov-26	144	18,722	0	18,722
	Sewer And Drainage System - SW	35	13-Aug-26 A	05-Jan-27	142	48,453	27,559	59,021
JDI	Installation of Galvanized iron vent - (B4.15.3.5)-MQ-MEP-SW-I	4	08-Nov-26	12-Nov-26	146	3,902	0	3,902
JDI	Installation of UPVC Pipes for Drainage 6" ? - (B4.15.3.1)-MQ-M	6	13-Aug-26 A	10-Dec-26	122	44,551	22,275	44,551
JDI	Installation of Roof Drain - (B4.15.3.4)-MQ-MEP-SW-D15-2nd F	4	09-Sep-26 A	05-Jan-27	142	0	5,284	10,568
	HVAC System - AC	4	08-Nov-26	12-Nov-26	146	2,439	0	2,439
JDI	Installation of Ducted Split Air Conditioning (For women prayer a	4	08-Nov-26	12-Nov-26	146	2,439	0	2,439
	Manarit	23	03-Nov-26	29-Nov-26	355	0	0	62,027
	Finishing For Minarat	23	03-Nov-26	29-Nov-26	351	0	0	58,231
	Masonary Work For Minaret	2	03-Nov-26	04-Nov-26	351	0	0	15,039
	Installation of Insulated CMU (EXTERNAL) 200mm thk - (B3.3.	2	03-Nov-26	04-Nov-26	351	0	0	15,039
	Floor Finishes For Minaret	2	10-Nov-26	11-Nov-26	351	0	0	204
	Installation of 600*600 mm granite tiles - (B3.3.9.1.1)-MQ-MNI	2	10-Nov-26	11-Nov-26	351	0	0	204
	Wall Finishes For Minaret	15	12-Nov-26	29-Nov-26	351	0	0	18,600
	Installation of Marble chips (Exposed Aggregate) at External wal	15	12-Nov-26	29-Nov-26	351	0	0	18,600
	Metal Work -MTW	2	08-Nov-26	09-Nov-26	351	0	0	24,388
	External Cement Plaster For Walls - (B3.3.5.1)-MQ-MNR-MTW-I	2	08-Nov-26	09-Nov-26	351	0	0	24,388
	Electrical Works of Minaret	8	03-Nov-26	11-Nov-26	370	0	0	3,796
	GROUNDING SYSTEM For Minaret	6	03-Nov-26	09-Nov-26	365	0	0	995
	Installation of Bare Copper Ground Wire 120 mm2 - (B5.3.16.1	4	05-Nov-26	09-Nov-26	351	0	0	613
	Installation of Ground Rod With Inspection Pit - (B5.3.16.1.2)-M	2	03-Nov-26	04-Nov-26	369	0	0	382
	LIGHTNING SYSTEM For Minaret	6	05-Nov-26	11-Nov-26	370	0	0	2,151
	Installation of Bare Tape Copper Conductor 3*25 mm - (B5.3.1	3	05-Nov-26	08-Nov-26	369	0	0	1,329
	Installation of Air Teminal Rod 60 Cm Hieght - (B5.3.16.2.2)-MC	2	05-Nov-26	07-Nov-26	370	0	0	203
	Installation of Bare Copper Down Conductor 70 mm2 - (B5.3.1	2	10-Nov-26	11-Nov-26	370	0	0	619
	LIGHTING FIXTURES For Minaret	2	05-Nov-26	07-Nov-26	351	0	0	650
	Installation of Light outlet including wiring ,conduit ,light switch -	2	05-Nov-26	07-Nov-26	351	0	0	650
	Service Building	19	03-Nov-26	24-Nov-26	359	0	0	28,564
	Sub Structure	15	03-Nov-26	19-Nov-26	359	0	0	21,548
	Foundation For pump Room	15	03-Nov-26	19-Nov-26	359	0	0	21,548
	shuttering for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	2	03-Nov-26	04-Nov-26	359	0	0	92
	pouring for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	1	08-Nov-26	08-Nov-26	359	0	0	709
	De shuttering for Plain Concrete - (B6.3.1.1)-MQ-SB-Fou-D03	2	09-Nov-26	10-Nov-26	359	0	0	92
	Shuttering of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2	11-Nov-26	12-Nov-26	359	0	0	2,064
	Steel Fixing of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2	14-Nov-26	15-Nov-26	359	0	0	10,336
	RC Casting of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2	16-Nov-26	17-Nov-26	359	0	0	7,224
	Deshuttering of Foundation - (B6.3.2.1)-MQ-SB-Fou-D03	2	18-Nov-26	19-Nov-26	359	0	0	1,032
	Finishing Service Building	15	05-Nov-26	22-Nov-26	359	0	0	2,951
	Insulation For Service Building	15	05-Nov-26	22-Nov-26	359	0	0	2,951
	Installation of two coats of bitumen waterproofing paint - (B6.7.	2	21-Nov-26	22-Nov-26	359	0	0	975

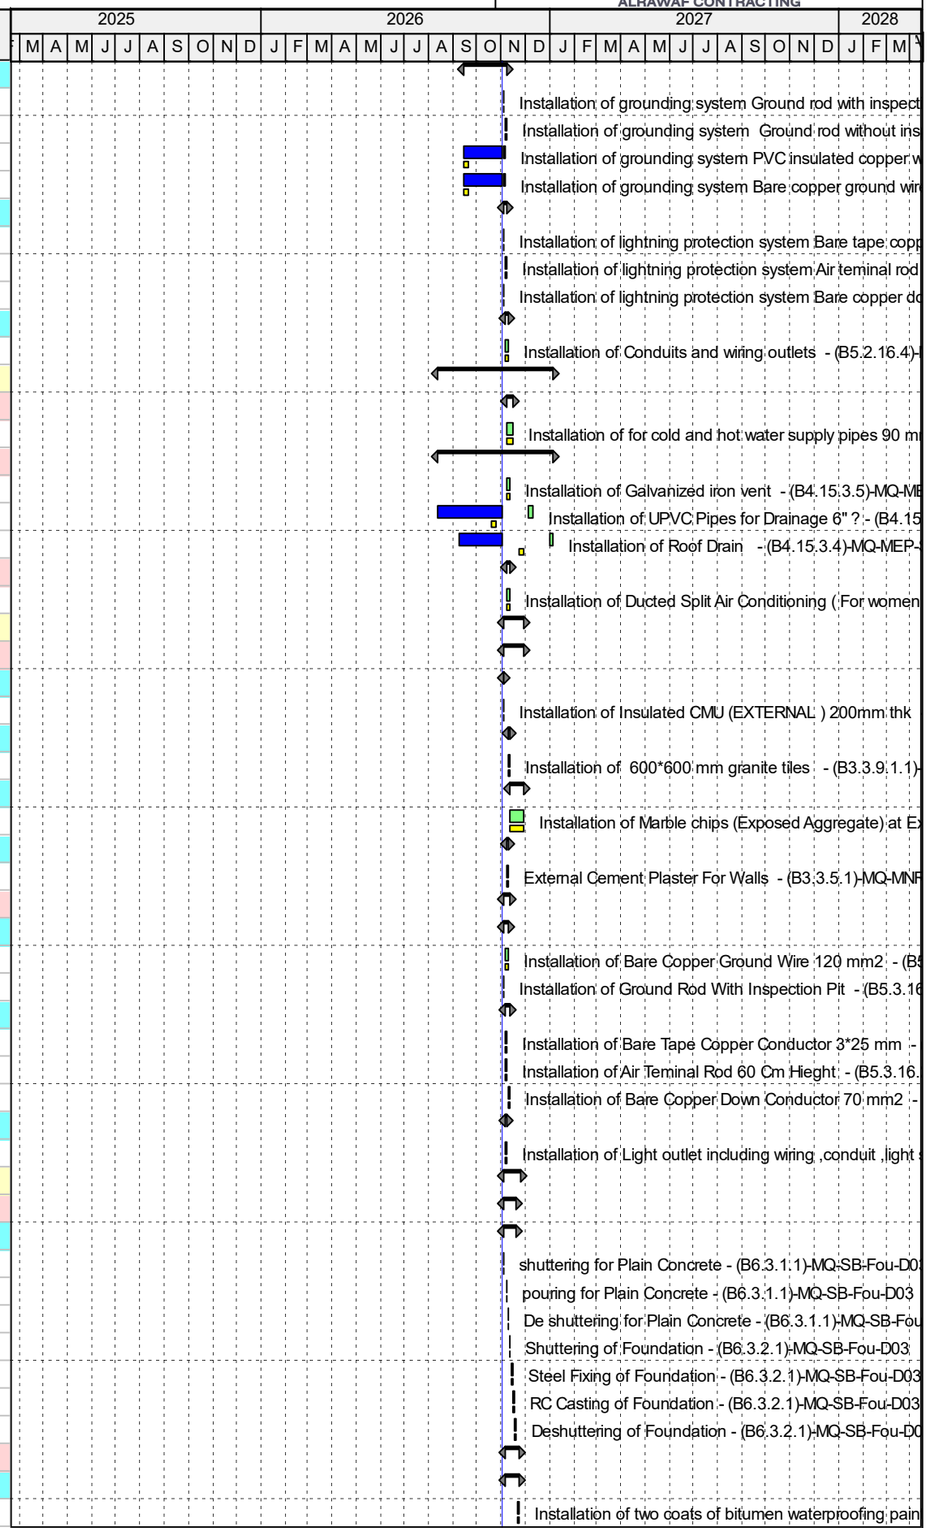


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Installation of two coats of Epoxy for inner surfaces(Slab on gra	2	21-Nov-26	22-Nov-26	359	0	0	1,626
	Installation of 250 micron thick polythelene sheet under blinding	2	05-Nov-26	07-Nov-26	359	0	0	175
	Applying of anti termite under all concrete in touch with earth fo	2	05-Nov-26	07-Nov-26	359	0	0	175
Mechanical Work Service Building		2	23-Nov-26	24-Nov-26	359	0	0	4,065
Water Storage Tank - GRP		2	23-Nov-26	24-Nov-26	359	0	0	4,065
	Supply and install water storage tanks - (B6.15.1.1)-MQ-SB-GR	2	23-Nov-26	24-Nov-26	359	0	0	4,065
External Works		60	28-Jul-26 A	24-Nov-26	307	0	81,103	342,437
Water Supply System		5	19-Nov-26	24-Nov-26	307	0	0	13,208
JDI	Installation of water supply piping system 110 mm - (B2.1.3.1)-M	5	19-Nov-26	24-Nov-26	307	0	0	13,208
Sewer and Drainage		11	03-Nov-26	15-Nov-26	307	0	0	149,368
JDI	Installation of Sewer piping system 150 mm - (B2.1.4.1.1)-MQ-E	4	03-Nov-26	07-Nov-26	307	0	0	29,512
JDI	Installation of Inspection chambe - (B2.1.4.2)-MQ-EW-SW-D15-	2	08-Nov-26	09-Nov-26	307	0	0	36,582
JDI	installation of manhole - (B2.1.4.3)-MQ-EW-SW-D15-2nd Fix	3	10-Nov-26	12-Nov-26	307	0	0	22,304
JDI	Connecting the proposed sewerage network to the exisiting sew	2	14-Nov-26	15-Nov-26	307	0	0	60,970
Storm Water Drainage		49	28-Jul-26 A	18-Nov-26	307	0	81,103	179,861
JDI	Installation of catch basins - (B2.1.5.3)-MQ-EW-SN-D15-2nd Fix	3	16-Nov-26	18-Nov-26	307	0	0	78,482
JDI	Installation of manhole - (B2.1.5.4)-MQ-EW-SN-D15-2nd Fix	3	28-Jul-26 A	03-Nov-26	317	0	81,103	101,379
JDH3-02-009-TSE Pump Station		324	25-Jul-26 A	21-Sep-27	146	458,002	1,280,704	2,464,837
Engineering		18	03-Nov-26	23-Nov-26	397	0	0	0
JDH3-02-009-Prequalification and Material Submittals -SUB-PW Station Station -		10	03-Nov-26	14-Nov-26	405	0	0	0
JDH3-02-009-Prequalifications and Material prepare and Submit - SU		10	03-Nov-26	14-Nov-26	405	0	0	0
JDI	Prepare Material Submittal for Acrylic Paint Materials - EN-AR-SU	10	03-Nov-26	14-Nov-26	405	0	0	0
JDH3-02-009-Method of Statement for TSE Pump Station		18	03-Nov-26	23-Nov-26	362	0	0	0
JDH3-02-009-Pumps		18	03-Nov-26	23-Nov-26	314	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7	03-Nov-26	10-Nov-26	314	0	0	0
JDI	Review & approval MS for Pumps- MS	9	11-Nov-26	23-Nov-26	260	0	0	0
JDH3-02-009-Duct Works		18	03-Nov-26	23-Nov-26	270	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7	03-Nov-26	10-Nov-26	271	0	0	0
JDI	Review & approval MS for Duct Works- MS	9	11-Nov-26	23-Nov-26	224	0	0	0
JDH3-02-009-Drainage System		18	03-Nov-26	23-Nov-26	240	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7	03-Nov-26	10-Nov-26	241	0	0	0
JDI	Review & approval MS for Drainage System- MS	9	11-Nov-26	23-Nov-26	199	0	0	0
JDH3-02-009-Water Supply System		18	03-Nov-26	23-Nov-26	264	0	0	0
JDI	Prepare & Submit MS for Water Supply System- MS	7	03-Nov-26	10-Nov-26	265	0	0	0
JDI	Review & approval MS for Water Supply System- MS	9	11-Nov-26	23-Nov-26	219	0	0	0
JDH3-02-009-Chlorination System		18	03-Nov-26	23-Nov-26	323	0	0	0
JDI	Prepare & Submit MS for Chlorination System- MS	7	03-Nov-26	10-Nov-26	324	0	0	0
JDI	Review & approval MS for Chlorination System- MS	9	11-Nov-26	23-Nov-26	268	0	0	0
JDH3-02-009-Over head Crane		18	03-Nov-26	23-Nov-26	195	0	0	0
JDI	Prepare & Submit MS for Over head Crane- MS	7	03-Nov-26	10-Nov-26	195	0	0	0
JDI	Review & approval MS for Over head Crane- MS	9	11-Nov-26	23-Nov-26	161	0	0	0
JDH3-02-009-GLS Tank		18	03-Nov-26	23-Nov-26	345	0	0	0
JDI	Prepare & Submit MS for GLS Tank- MS	7	03-Nov-26	10-Nov-26	345	0	0	0
JDI	Review & approval MS for GLS Tank- MS	9	11-Nov-26	23-Nov-26	286	0	0	0
JDH3-02-009-Access Control		18	03-Nov-26	23-Nov-26	166	0	0	0
JDI	Prepare & Submit MS for Access Control- MS	7	03-Nov-26	10-Nov-26	166	0	0	0
JDI	Review & approval MS for Access Control- MS	9	11-Nov-26	23-Nov-26	137	0	0	0
JDH3-02-009-Data Communication		18	03-Nov-26	23-Nov-26	165	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7	03-Nov-26	10-Nov-26	165	0	0	0
JDI	Review & approval MS for Data Communication- MS	9	11-Nov-26	23-Nov-26	136	0	0	0
JDH3-02-009-Security System		18	03-Nov-26	23-Nov-26	167	0	0	0
JDI	Prepare & Submit MS for Security System- MS	7	03-Nov-26	10-Nov-26	167	0	0	0

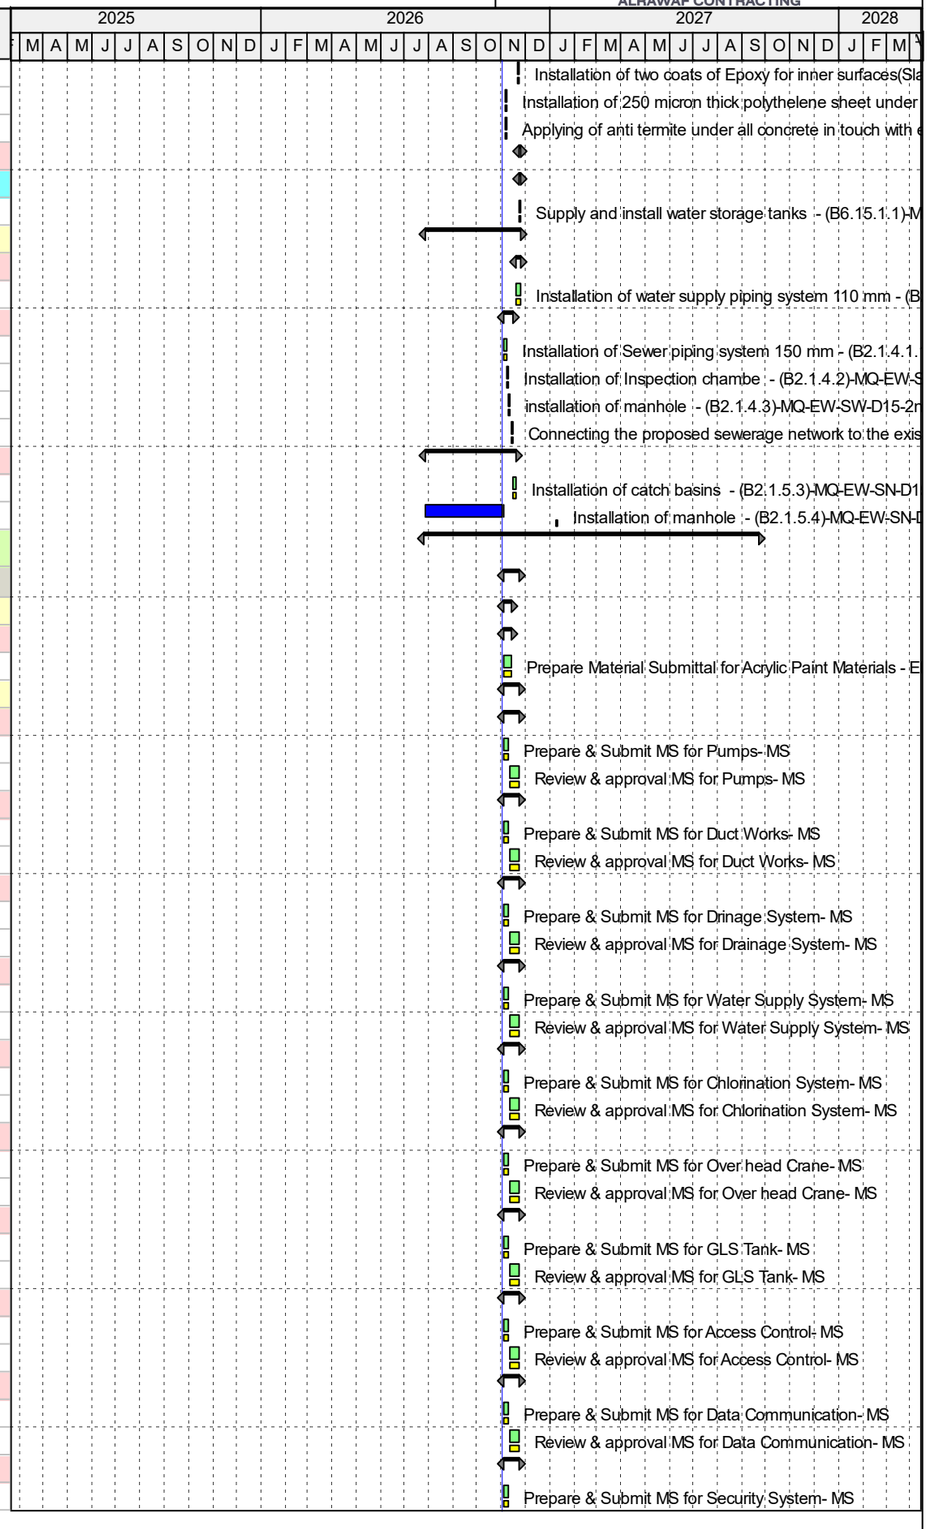

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Review & approval MS for Security System- MS	9	11-Nov-26	23-Nov-26	138	0	0	0
JDH3-02-009-Programing Logical Control System		18	03-Nov-26	23-Nov-26	362	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7	03-Nov-26	10-Nov-26	362	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9	11-Nov-26	23-Nov-26	300	0	0	0
Procurement		143	04-Aug-26 A	12-Feb-27	328	458,002	171,751	801,503
Long Lead Items		87	03-Nov-26	12-Feb-27	278	458,002	0	458,002
Purchase Order - PO - TSE Pump Station		10	03-Nov-26	14-Nov-26	278	0	0	0
JDH3-02-009-Long Lead Items - LOL-Material Purchase Order - PO		10	03-Nov-26	14-Nov-26	278	0	0	0
	Material Purchase Order for Addressable Fire Alarm System - PR	10	03-Nov-26	14-Nov-26	78	0	0	0
	Material Purchase Order for Access Control System - PR-TC-PO	10	03-Nov-26	14-Nov-26	86	0	0	0
	Material Purchase Order for Data Communication System - PR-T	10	03-Nov-26	14-Nov-26	94	0	0	0
	Material Purchase Order for Security System - PR-TC-PO	10	03-Nov-26	14-Nov-26	278	0	0	0
Fabrication - FAB - TSE Pump Station		90	15-Nov-26	12-Feb-27	334	0	0	0
JDH3-02-009-Long Lead Items - LOL-Manufacturing and Custom Ci		90	15-Nov-26	12-Feb-27	334	0	0	0
	Material Fabrication for Addressable Fire Alarm System - PR-TC-	90	15-Nov-26	12-Feb-27	91	0	0	0
	Material Fabrication for Access Control System - PR-TC-FAB	90	15-Nov-26	12-Feb-27	101	0	0	0
	Material Fabrication for Data Communication System - PR-TC-FA	90	15-Nov-26	12-Feb-27	111	0	0	0
	Material Fabrication for Security System - PR-TC-FAB	90	15-Nov-26	12-Feb-27	334	0	0	0
Delivery and staging on Site - DOS -TSE Pump Station		10	03-Nov-26	12-Nov-26	394	458,002	0	458,002
JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging		10	03-Nov-26	12-Nov-26	248	229,001	0	229,001
	delivery and staging for Surge Protection System - PR-MC-DOS	10	03-Nov-26	12-Nov-26	248	114,500	0	114,500
	delivery and staging for Overhead Crane - PR-MC-DOS	10	03-Nov-26	12-Nov-26	248	114,500	0	114,500
JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging		10	03-Nov-26	12-Nov-26	394	229,001	0	229,001
	delivery and staging for Transformer (TR) - PR-EL-DOS	10	03-Nov-26	12-Nov-26	379	114,500	0	114,500
	delivery and staging for Main Distribution Boards (MDB) - PR-EL-	10	03-Nov-26	12-Nov-26	394	114,500	0	114,500
Short Lead Items		77	04-Aug-26 A	26-Nov-26	394	0	171,751	343,501
Purchase Order - PO - TSE Pump Station		21	03-Nov-26	26-Nov-26	394	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - PO		21	03-Nov-26	26-Nov-26	295	0	0	0
	Material Purchase Order for Epoxy Flooring - PR-AR-PO	21	03-Nov-26	26-Nov-26	295	0	0	0
	Material Purchase Order for Acrylic Paint Materials - PR-AR-PO	21	03-Nov-26	26-Nov-26	246	0	0	0
	Material Purchase Order for Chain link Fences - PR-AR-PO	21	03-Nov-26	26-Nov-26	68	0	0	0
	Material Purchase Order for Steel Gates - PR-AR-PO	21	03-Nov-26	26-Nov-26	96	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - PO		21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Fuel Oil System - PR-MC-PO	21	03-Nov-26	26-Nov-26	192	0	0	0
	Material Purchase Order for GRP Tank - PR-MC-PO	21	03-Nov-26	26-Nov-26	250	0	0	0
	Material Purchase Order for Fire Protection System - PR-MC-PO	21	03-Nov-26	26-Nov-26	346	0	0	0
	Material Purchase Order for Wall mounted Split Units - PR-MC-P	21	03-Nov-26	26-Nov-26	339	0	0	0
	Material Purchase Order for Exhaust Fans - PR-MC-PO	21	03-Nov-26	26-Nov-26	358	0	0	0
	Material Purchase Order for Galvanized Iron Sheets for Duct Wo	21	03-Nov-26	26-Nov-26	192	0	0	0
	Material Purchase Order for Air Outlets - PR-MC-PO	21	03-Nov-26	26-Nov-26	262	0	0	0
	Material Purchase Order for GLS Tank - PR-MC-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - PO		21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Low Voltage Cables - PR-EL-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Panel Boards - PR-EL-PO	21	03-Nov-26	26-Nov-26	347	0	0	0
	Material Purchase Order for Earthing Sytem - PR-EL-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Lighting Fixtures - PR-EL-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Wiring Devices and Circuit Breakers	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for KWH Meter - PR-EL-PO	21	03-Nov-26	26-Nov-26	347	0	0	0
Delivery and staging on Site - DOS - TSE Pump Station		14	04-Aug-26 A	26-Nov-26	429	0	171,751	343,501
JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging		14	04-Aug-26 A	26-Nov-26	429	0	171,751	343,501
	delivery and staging for Wall mounted Split Units - PR-MC-DOS	14	04-Aug-26 A	26-Nov-26	407	0	57,250	114,500
	delivery and staging for Exhaust Fans - PR-MC-DOS	14	04-Aug-26 A	26-Nov-26	429	0	57,250	114,500
	delivery and staging for Galvanized Iron Sheets for Duct Works	14	04-Aug-26 A	26-Nov-26	234	0	57,250	114,500

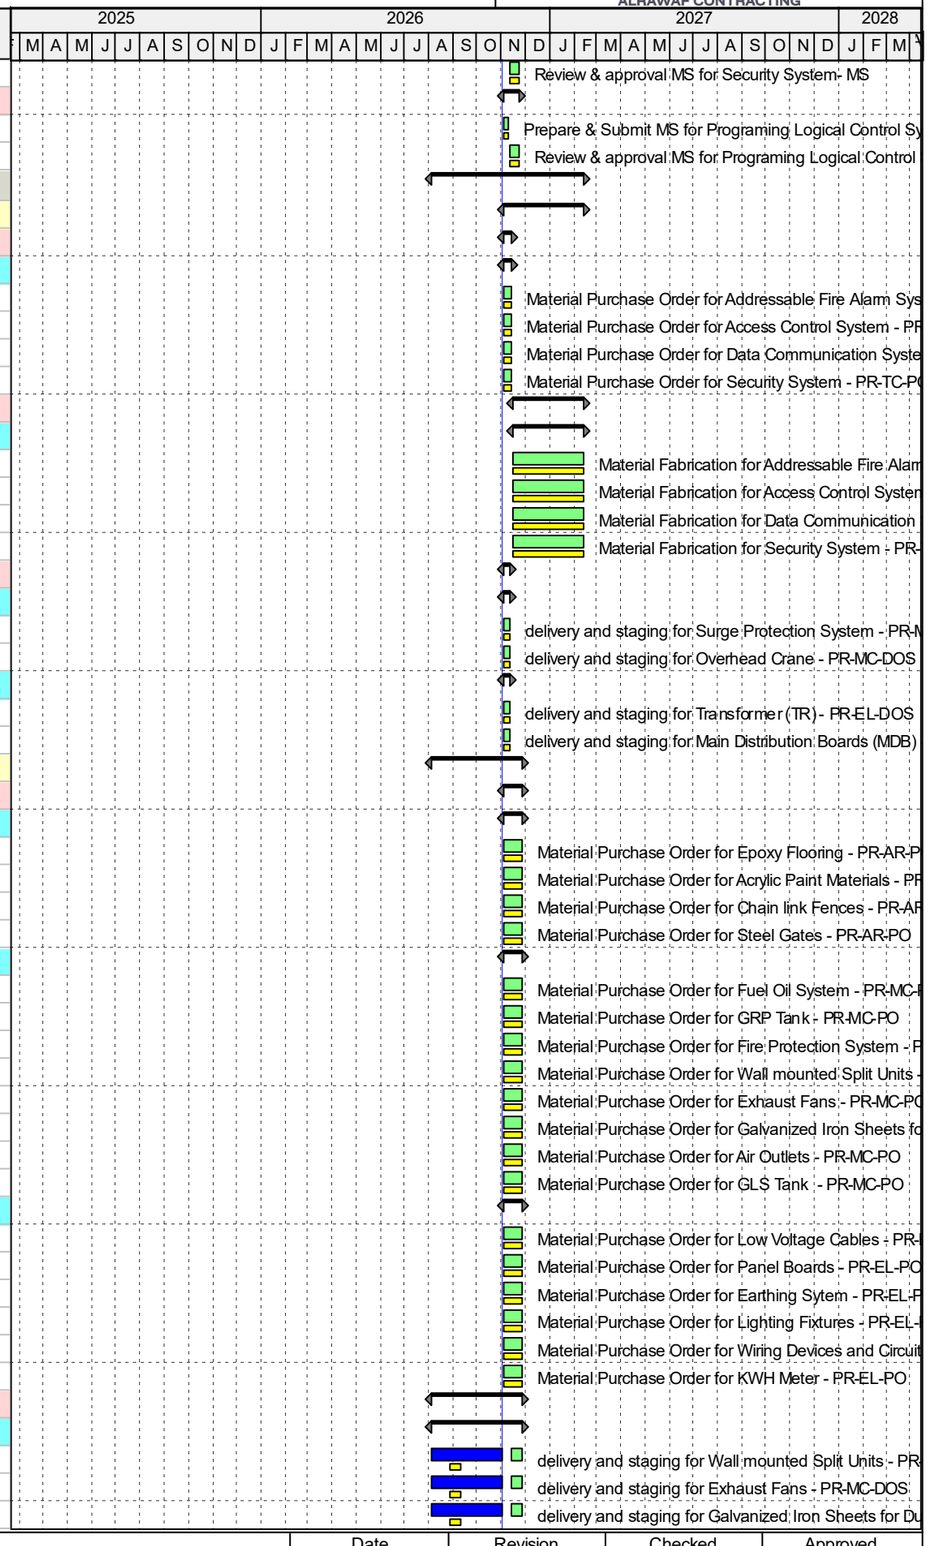


Actual Level of Effort · Remaining Work
Primary Baseline · Critical Remaining Work
Actual Work · Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Construction	324	25-Jul-26 A	21-Sep-27	112	0	1,108,953	1,663,334
	JDH3-02-009 -SITE WORK	12	15-Sep-26 A	21-Sep-27	45	0	77,551	110,787
	JDH3-02-009-B15-Mechanical Works-phase 1	12	15-Sep-26 A	21-Sep-27	45	0	77,551	110,787
	JDH3-02-009-B15-Site Interconnecting Pipes 200mm	12	15-Sep-26 A	21-Sep-27	45	0	20,463	29,233
	Soil Replacement and Bedding for Ductile Iron Pipe 200 mm -	2	16-Sep-26 A	21-Sep-27	45	0	1,279	1,827
	Pipe.Installation for Ductile Iron Pipe 200 mm - Depth from 2.5	8	17-Sep-26 A	21-Sep-27	45	0	14,068	20,098
	Excavation Works for Ductile Iron Pipe 200 mm - Depth from 2.	2	15-Sep-26 A	21-Sep-27	27	0	5,116	7,308
	JDH3-02-009-B15-Site Interconnecting Pipes 400 mm	8	15-Sep-26 A	21-Sep-27	34	0	57,087	81,553
	Excavation Works for Ductile Iron Pipe 400 mm - Depth from 2.5	2	15-Sep-26 A	21-Sep-27	27	0	14,272	20,388
	Soil Replacement and Bedding Works for Ductile Iron Pipe 400	2	16-Sep-26 A	21-Sep-27	34	0	3,568	5,097
	Pipe.Installation for Ductile Iron Pipe 400 mm - Depth from 2.51	4	17-Sep-26 A	21-Sep-27	34	0	39,248	56,068
	JDH3-02-009 -PUMP STATION	164	28-Jul-26 A	22-May-27	0	0	112,809	197,230
	JDH3-02-009-B16-Site Works	2	28-Jul-26 A	22-May-27	0	0	10,107	14,439
	JDH3-02-009-B16-Earth work	2	28-Jul-26 A	22-May-27	0	0	10,107	14,439
	Backfill Layers Works Excavated Material - (B16. 2.2)-TSEP-B1	2	28-Jul-26 A	22-May-27	0	0	10,107	14,439
	JDH3-02-009-B16-Sub Structure	124	15-Sep-26 A	06-Apr-27	0	0	62,694	98,566
	JDH3-02-009-B16-Grade Beams	10	03-Nov-26	14-Nov-26	119	0	0	17,144
	Shuttering Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2	03-Nov-26	04-Nov-26	119	0	0	3,429
	Steel Fixing Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	4	05-Nov-26	09-Nov-26	119	0	0	8,572
	RC Casting Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2	10-Nov-26	11-Nov-26	119	0	0	3,429
	Deshuttering Grade Beams - (B16. 3.2.3)-TSEP-B16-D03	2	12-Nov-26	14-Nov-26	119	0	0	1,714
	JDH3-02-009-B16-Concrete trench (Walls and Slabs)	124	15-Sep-26 A	06-Apr-27	0	0	62,694	81,421
	Deshuttering Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2	19-Sep-26 A	06-Apr-27	0	0	5,699	8,142
	RC Casting Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2	17-Sep-26 A	06-Apr-27	0	0	11,399	16,284
	Shuttering Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	2	15-Sep-26 A	14-Nov-26	119	0	13,027	16,284
	Steel Fixing Concrete trench - (B16. 3.2.7)-TSEP-B16-D03	4	16-Sep-26 A	14-Nov-26	119	0	32,569	40,711
	JDH3-02-009-B16-Super Structure	14	15-Sep-26 A	18-Apr-27	0	0	40,007	84,225
	JDH3-02-009-B16-Columns	14	15-Sep-26 A	18-Apr-27	0	0	40,007	84,225
	Deshuttering Columns - (B16. 3.2.2)-TSEP-B16-D03	2	19-Sep-26 A	18-Apr-27	0	0	1,263	8,422
	Shuttering Columns - (B16. 3.2.2)-TSEP-B16-D03	2	15-Sep-26 A	13-Apr-27	0	0	2,527	16,845
	RC Casting Columns - (B16. 3.2.2)-TSEP-B16-D03	2	17-Sep-26 A	18-Apr-27	0	0	2,527	16,845
	Steel Fixing Columns - (B16. 3.2.2)-TSEP-B16-D03	4	16-Sep-26 A	13-Apr-27	0	0	33,690	42,112
	JDH3-02-009 -GUARD HOUSE	19	03-Nov-26	24-Nov-26	346	0	0	16,607
	JDH3-02-009-B17-Sub Structure	16	03-Nov-26	21-Nov-26	319	0	0	8,072
	JDH3-02-009-B17-Foundation	8	03-Nov-26	11-Nov-26	237	0	0	1,560
	Shuttering Foundation - (B17. 3.2.1)-TSEP-B17-D03	2	03-Nov-26	04-Nov-26	237	0	0	312
	Steel Fixing Foundation - (B17. 3.2.1)-TSEP-B17-D03	2	05-Nov-26	07-Nov-26	237	0	0	780
	RC Casting Foundation - (B17. 3.2.1)-TSEP-B17-D03	2	08-Nov-26	09-Nov-26	237	0	0	312
	Deshuttering Foundation - (B17. 3.2.1)-TSEP-B17-D03	2	10-Nov-26	11-Nov-26	237	0	0	156
	JDH3-02-009-B17-Columns neck	8	12-Nov-26	21-Nov-26	237	0	0	3,147
	Shuttering Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2	12-Nov-26	14-Nov-26	237	0	0	629
	Steel Fixing Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2	15-Nov-26	16-Nov-26	237	0	0	1,573
	RC Casting Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2	17-Nov-26	18-Nov-26	237	0	0	629
	Deshuttering Columns neck - (B17. 3.2.2)-TSEP-B17-D03	2	19-Nov-26	21-Nov-26	237	0	0	315
	JDH3-02-009-B17-Grade Beams	8	12-Nov-26	21-Nov-26	237	0	0	1,532
	Shuttering Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2	12-Nov-26	14-Nov-26	237	0	0	306
	Steel Fixing Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2	15-Nov-26	16-Nov-26	237	0	0	766
	RC Casting Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2	17-Nov-26	18-Nov-26	237	0	0	306
	Deshuttering Grade Beams - (B17. 3.2.3)-TSEP-B17-D03	2	19-Nov-26	21-Nov-26	237	0	0	153
	JDH3-02-009-B17-Slab on Grade	8	05-Nov-26	14-Nov-26	325	0	0	1,832
	Shuttering Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2	05-Nov-26	07-Nov-26	325	0	0	366
	Steel Fixing Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2	08-Nov-26	09-Nov-26	325	0	0	916
	RC Casting Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2	10-Nov-26	11-Nov-26	325	0	0	366

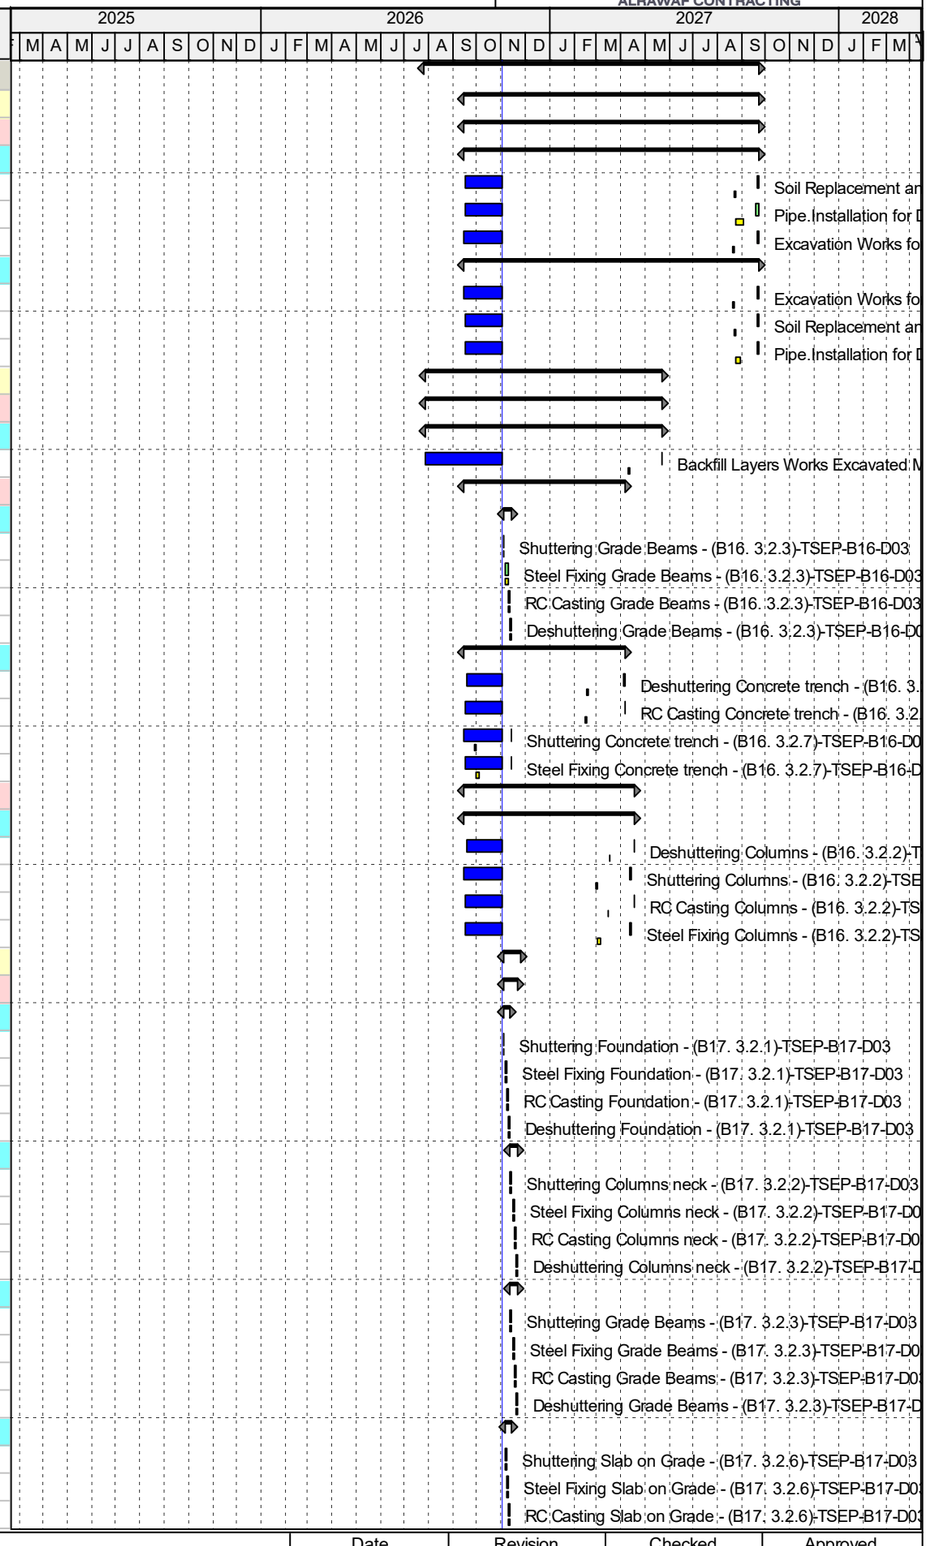

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Deshuttering Slab on Grade - (B17. 3.2.6)-TSEP-B17-D03	2	12-Nov-26	14-Nov-26	325	0	0	183
	JDH3-02-009-B17-Electrical Works for Potable Water Pump Station	5	19-Nov-26	24-Nov-26	344	0	0	1,706
	JDH3-02-009-B17-LED Interior Lighting	2	19-Nov-26	21-Nov-26	329	0	0	303
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	19-Nov-26	21-Nov-26	329	0	0	303
	JDH3-02-009-B17-Addressable Fire-Alarm System	4	19-Nov-26	23-Nov-26	329	0	0	349
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B17.	4	19-Nov-26	23-Nov-26	329	0	0	349
	JDH3-02-009-B17-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+	5	19-Nov-26	24-Nov-26	328	0	0	908
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	5	19-Nov-26	24-Nov-26	328	0	0	908
	JDH3-02-009-B17-Data Communications	2	19-Nov-26	21-Nov-26	347	0	0	146
	1st Fix, Conduits and Pull Box Installation for Data Communicat	2	19-Nov-26	21-Nov-26	347	0	0	146
	JDH3-02-009-B17-Finishes	18	03-Nov-26	23-Nov-26	347	0	0	4,493
	JDH3-02-009-B17-Thermal & Moisture Protection	18	03-Nov-26	23-Nov-26	347	0	0	1,873
	Applying Bitumen waterproofing Paint Insulation Bitumen water	2	22-Nov-26	23-Nov-26	237	0	0	494
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	2	03-Nov-26	04-Nov-26	325	0	0	96
	Applying Foam concrete screed Insulation Foam concrete - (B1	2	19-Nov-26	21-Nov-26	347	0	0	536
	Applying PVC Waterproofing Membrane PVC Membrane - (B17	2	22-Nov-26	23-Nov-26	347	0	0	747
	JDH3-02-009-B17-Masonary	4	15-Nov-26	18-Nov-26	325	0	0	2,620
	Masonary Block work ACC Block - (B17. 4.1.1)-TSEP-B17-D04	2	15-Nov-26	16-Nov-26	325	0	0	2,251
	Masonary Block work Block Work - (B17. 4.1.2)-TSEP-B17-D04	2	17-Nov-26	18-Nov-26	325	0	0	369
	JDH3-02-009-B17-Mechanical Works-phase 1	4	19-Nov-26	23-Nov-26	325	0	0	2,336
	JDH3-02-009-B17-PPR For Cold Water Supply Piping System	4	19-Nov-26	23-Nov-26	325	0	0	2,336
	PPR Pipes Installation 32 mm - (B17. 15.3.1.1)-TSEP-B17-D15	2	19-Nov-26	21-Nov-26	325	0	0	1,005
	PPR Pipes Installation 25 mm - (B17. 15.3.1.2)-TSEP-B17-D15	2	22-Nov-26	23-Nov-26	325	0	0	1,331
	JDH3-02-009 -ADMIN BUILDING	47	28-Jul-26 A	25-Nov-26	243	0	1,605	48,797
	JDH3-02-009-B18-Site Works	2	28-Jul-26 A	25-Nov-26	208	0	1,605	1,783
	JDH3-02-009-B18-Earth work	2	28-Jul-26 A	25-Nov-26	208	0	1,605	1,783
	Backfill Layers Works Excavated Material - (B18. 2.2)-TSEP-B1	2	28-Jul-26 A	25-Nov-26	208	0	1,605	1,783
	JDH3-02-009-B18-Super Structure	20	03-Nov-26	25-Nov-26	208	0	0	24,233
	JDH3-02-009-B18-Roof Beam	4	03-Nov-26	07-Nov-26	224	0	0	546
	RC Casting Roof Beam - (B18. 3.2.6)-TSEP-B18-D03	2	03-Nov-26	04-Nov-26	224	0	0	364
	Deshuttering Roof Beam - (B18. 3.2.6)-TSEP-B18-D03	2	05-Nov-26	07-Nov-26	224	0	0	182
	JDH3-02-009-B18-Roof Slab	20	03-Nov-26	25-Nov-26	208	0	0	23,688
	Shuttering Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2	03-Nov-26	04-Nov-26	208	0	0	4,738
	Steel Fixing Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2	05-Nov-26	07-Nov-26	208	0	0	11,844
	RC Casting Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	2	08-Nov-26	09-Nov-26	208	0	0	4,738
	Deshuttering Roof Slab - (B18. 3.2.4)-TSEP-B18-D03	14	10-Nov-26	25-Nov-26	208	0	0	2,369
	JDH3-02-009-B18-Finishes	2	03-Nov-26	04-Nov-26	242	0	0	2,259
	JDH3-02-009-B18-Thermal & Moisture Protection	2	03-Nov-26	04-Nov-26	242	0	0	2,259
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2	03-Nov-26	04-Nov-26	242	0	0	2,259
	JDH3-02-009-B18-Electrical Works for Potable Water Pump Station	4	03-Nov-26	07-Nov-26	259	0	0	20,522
	JDH3-02-009-B18-Grounding and Bonding	4	03-Nov-26	07-Nov-26	259	0	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	259	0	0	20,522
	JDH3-02-009 -TSE STO RAGE TANK	47	25-Jul-26 A	14-Dec-26	345	0	916,989	1,248,666
	JDH3-02-009-B19-Mechanical Works-phase 1	47	25-Jul-26 A	14-Dec-26	345	0	916,989	1,248,666
	JDH3-02-009-B19-Storage Tank	47	25-Jul-26 A	14-Dec-26	345	0	916,989	1,248,666
	Laying and Welding of First Ring for Base of shell - (B19. 15.1)	16	25-Jul-26 A	23-Nov-26	345	0	299,159	598,319
	Roof Aluminum Cover Installation - (B19. 15.1)-TSEP-B19-D15	13	29-Jul-26 A	14-Dec-26	345	0	247,132	260,139
	Roof Steel Structure Installation - (B19. 15.1)-TSEP-B19-D15	10	28-Jul-26 A	14-Dec-26	345	0	370,698	390,208
	JDH3-02-009 -CHLORINATION BUILDING	22	03-Nov-26	28-Nov-26	310	0	0	41,248
	JDH3-02-009-B20-Sub Structure	8	12-Nov-26	21-Nov-26	289	0	0	7,009
	JDH3-02-009-B20-Slab on Grade	8	12-Nov-26	21-Nov-26	289	0	0	7,009
	Shuttering Slab on Grade - (B20. 3.2.6)-TSEP-B20-D03	2	12-Nov-26	14-Nov-26	289	0	0	1,402
	Steel Fixing Slab on Grade - (B20. 3.2.6)-TSEP-B20-D03	2	15-Nov-26	16-Nov-26	289	0	0	3,505

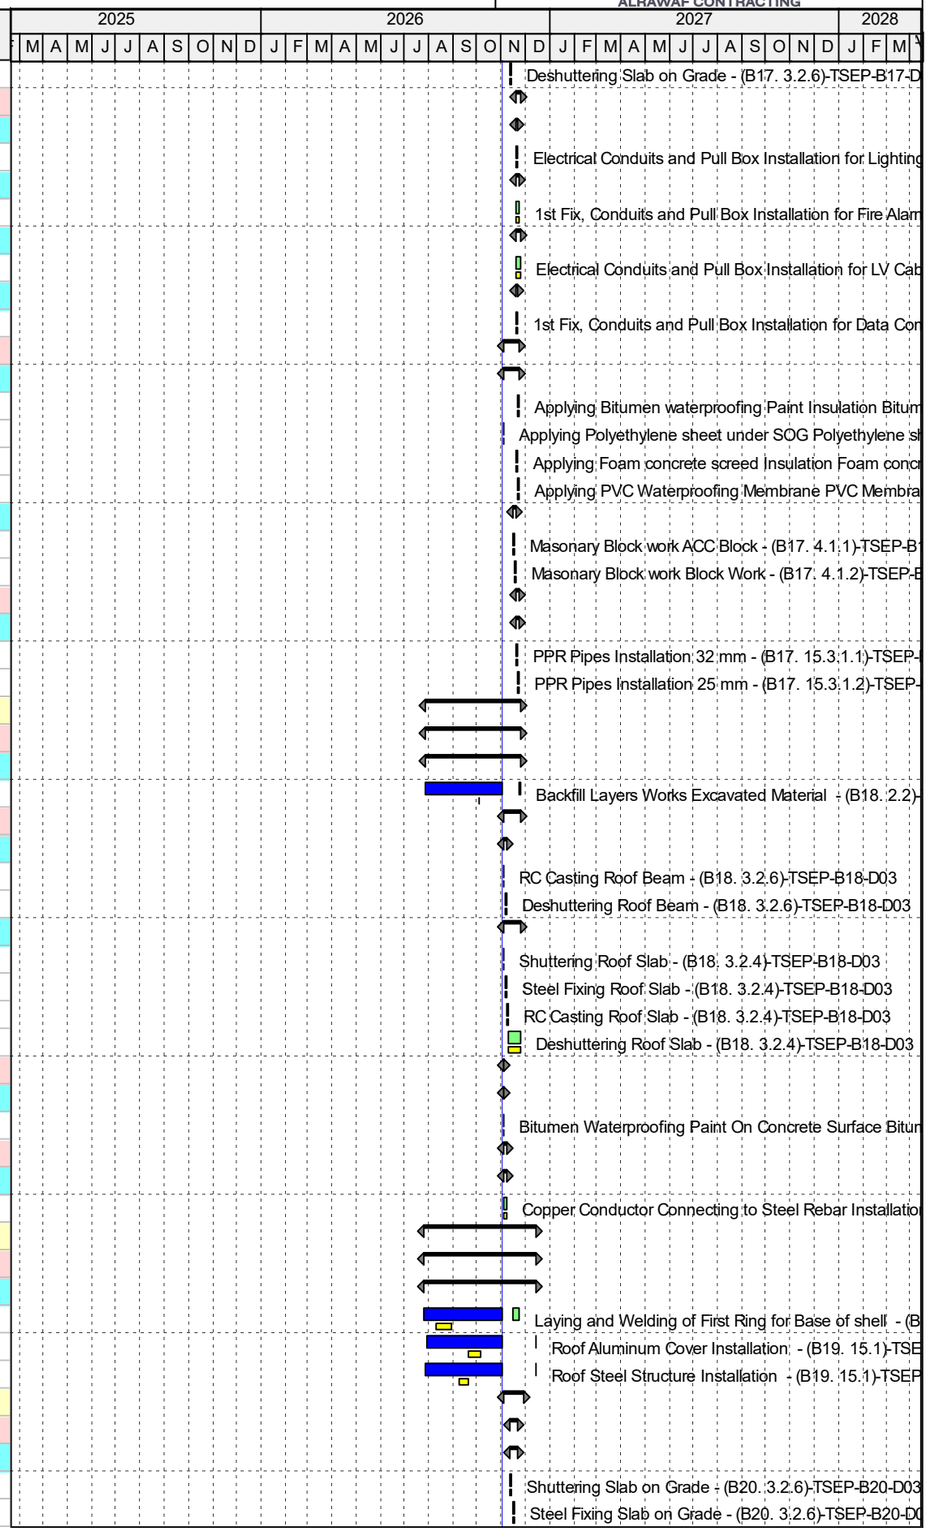


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	RC Casting Slab on Grade - (B20. 3.2.6)-TSEP-B20-D03	2	17-Nov-26	18-Nov-26	289	0	0	1,402
	Deshuttering Slab on Grade - (B20. 3.2.6)-TSEP-B20-D03	2	19-Nov-26	21-Nov-26	289	0	0	701
JDH3-02-009-B20-Super Structure		22	03-Nov-26	28-Nov-26	296	0	0	21,511
JDH3-02-009-B20-Roof Beam		8	03-Nov-26	11-Nov-26	296	0	0	2,214
	Shuttering Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2	03-Nov-26	04-Nov-26	296	0	0	443
	Steel Fixing Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2	05-Nov-26	07-Nov-26	296	0	0	1,107
	RC Casting Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2	08-Nov-26	09-Nov-26	296	0	0	443
	Deshuttering Roof Beam - (B20. 3.2.4)-TSEP-B20-D03	2	10-Nov-26	11-Nov-26	296	0	0	221
JDH3-02-009-B20-Roof Slab		22	03-Nov-26	28-Nov-26	296	0	0	18,745
	Shuttering Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2	03-Nov-26	04-Nov-26	298	0	0	3,749
	Steel Fixing Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2	05-Nov-26	07-Nov-26	298	0	0	9,372
	RC Casting Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	2	08-Nov-26	09-Nov-26	298	0	0	3,749
	Deshuttering Roof Slab - (B20. 3.2.5)-TSEP-B20-D03	14	12-Nov-26	28-Nov-26	296	0	0	1,874
JDH3-02-009-B20-Mechanical Equipment Pads		2	22-Nov-26	23-Nov-26	289	0	0	552
	Shuttering Mechanical Pads - (B20. 3.2.8)-TSEP-B20-D03	2	22-Nov-26	23-Nov-26	289	0	0	552
JDH3-02-009-B20-Finishes		4	03-Nov-26	07-Nov-26	289	0	0	1,772
JDH3-02-009-B20-Thermal & Moisture Protection		4	03-Nov-26	07-Nov-26	289	0	0	1,772
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2	03-Nov-26	04-Nov-26	289	0	0	1,429
	Polyethylene Sheet Under SOG Polyethylene sheet - (B20. 7.2)	2	05-Nov-26	07-Nov-26	289	0	0	343
JDH3-02-009-B20-Electrical Works for Potable Water Pump Station		4	03-Nov-26	07-Nov-26	328	0	0	6,529
JDH3-02-009-B20-Grounding and Bonding		4	03-Nov-26	07-Nov-26	328	0	0	6,529
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	328	0	0	6,529
JDH3-02-009-B20-Mechanical Works-phase 1		4	08-Nov-26	11-Nov-26	289	0	0	4,427
JDH3-02-009-B20-Water Supply System		4	08-Nov-26	11-Nov-26	289	0	0	2,395
	Cold Water Pipes Installation PPR 32 mm - (B20. 15.4.1.1)-TSE	2	08-Nov-26	09-Nov-26	289	0	0	1,507
	Cold Water Pipes Installation PPR 25 mm - (B20. 15.4.1.2)-TSE	2	10-Nov-26	11-Nov-26	289	0	0	887
JDH3-02-009-B20-Sewer And Drainage System		2	08-Nov-26	09-Nov-26	291	0	0	2,032
	Drainage Pipe Installation UPVC 75 mm - (B20. 15.5.3.1)-TSEP	2	08-Nov-26	09-Nov-26	291	0	0	2,032
Close Out		26	03-Nov-26	02-Dec-26	389	0	0	0
As Built Drawing Submittals - SUB-TSE Pump Station - TSEP		21	03-Nov-26	26-Nov-26	384	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		21	03-Nov-26	26-Nov-26	384	0	0	0
JDI	Prepare and Submit Drawing for Irrigation Pump Building - Four	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Irrigation Pump Building - Grou	7	12-Nov-26	19-Nov-26	390	0	0	0
JDI	Prepare and Submit Drawing for GLS Tank - Shopdrawings Plar	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Founc	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Colum	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Grade	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof S	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof E	7	05-Nov-26	12-Nov-26	396	0	0	0
JDI	Prepare and Submit Drawing for SEC Building - Foundation for	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for SEC Building - Grade Beam fo	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Foundat	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Columns	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Slab On	7	19-Nov-26	26-Nov-26	384	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Grade B	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof for	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof Be	7	10-Nov-26	17-Nov-26	392	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Plans & Sectior	7	12-Nov-26	19-Nov-26	390	0	0	0
As Built Drawing Approvals - APP-TSE Pump Station - TSEP		16	11-Nov-26	02-Dec-26	323	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		16	11-Nov-26	02-Dec-26	323	0	0	0
JDI	Review and Approval for Irrigation Pump Building - Foundation f	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Irrigation Pump Building - Ground Beal	9	22-Nov-26	02-Dec-26	323	0	0	0
JDI	Review and Approval for GLS Tank - Shopdrawings Plan & Sect	9	11-Nov-26	23-Nov-26	330	0	0	0

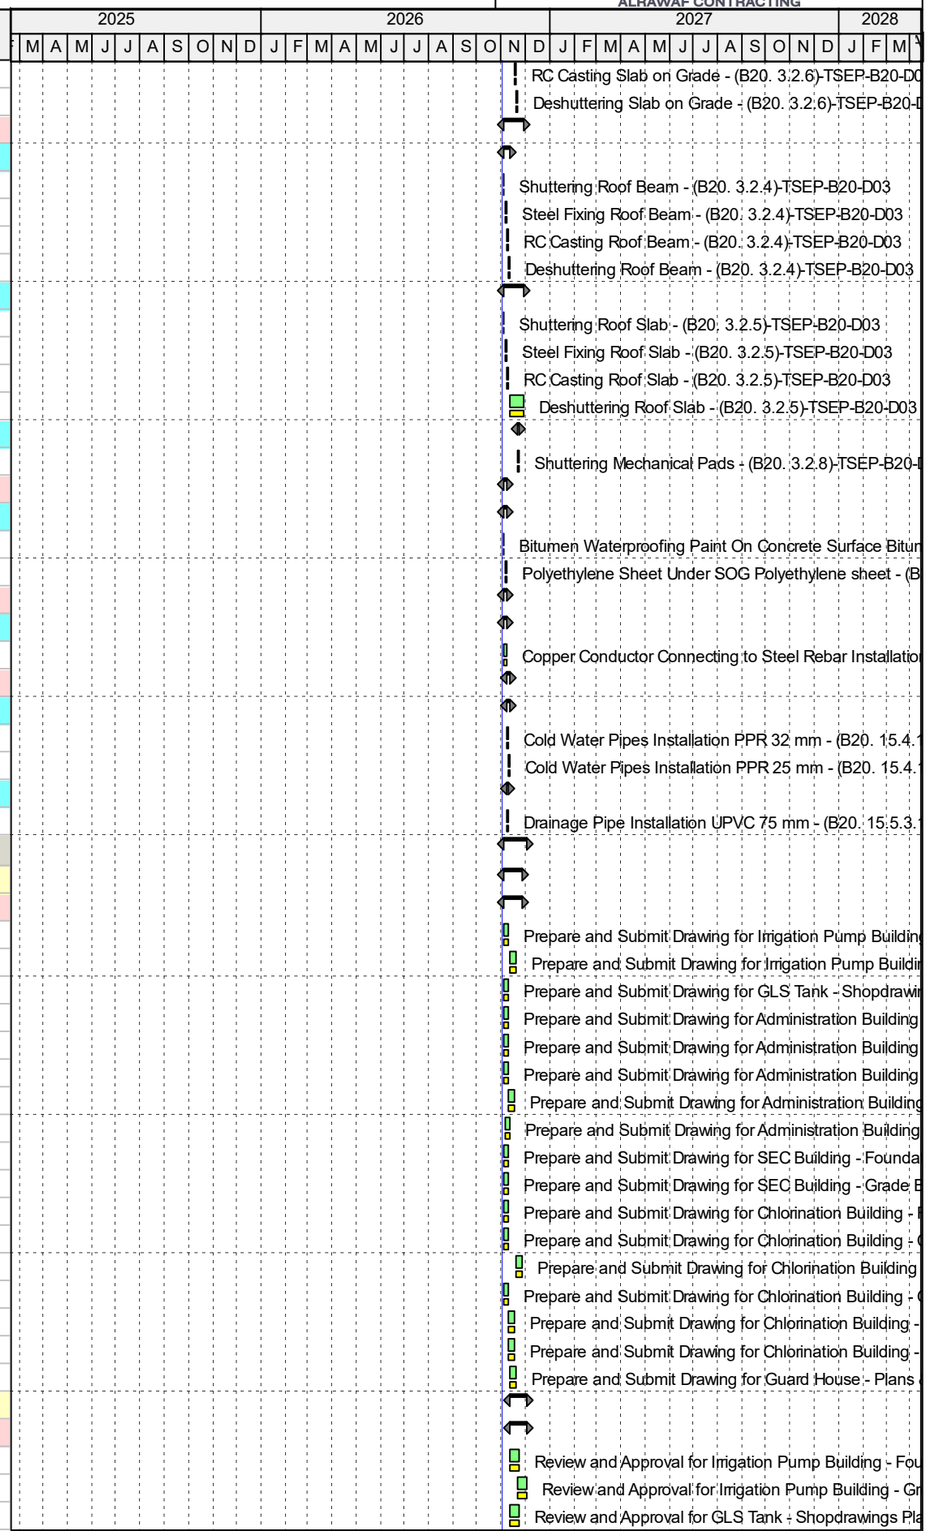


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Review and Approval for Administration Building - Foundation Sl	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Columns & Ax	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Grade Beam	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Roof Shop Dr	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Administration Building - Roof Beam Sl	9	15-Nov-26	25-Nov-26	328	0	0	0
JDI	Review and Approval for SEC Building - Foundation for APP-AS	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for SEC Building - Grade Beam for APP-A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Foundation for A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Columns & Axis	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Grade Beam for	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Roof for APP-AS	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Chlorination Building - Roof Beam for A	9	18-Nov-26	30-Nov-26	325	0	0	0
JDI	Review and Approval for Guard House - Plans & Sections for AF	9	22-Nov-26	02-Dec-26	323	0	0	0
JDH3-02-009-PW Pump Station		358	16-Jun-26 A	17-Nov-27	98	1,403,190	2,823,058	10,167,669
Engineering		18	03-Nov-26	23-Nov-26	397	0	0	0
JDH3-02-009-Prequalification and Material Submittals -SUB-PW Station Station -		11	03-Nov-26	15-Nov-26	404	0	0	0
JDH3-02-009-Prequalifications and Material prepare and Submit - SU		11	03-Nov-26	15-Nov-26	404	0	0	0
JDI	Prepare Material Submittal for Acrylic Paint Materials - EN-AR-SU	11	03-Nov-26	15-Nov-26	404	0	0	0
JDH3-02-009-Method of Statement for PW Pump Stations		18	03-Nov-26	23-Nov-26	377	0	0	0
JDH3-02-009-Pumps		18	03-Nov-26	23-Nov-26	336	0	0	0
JDI	Prepare & Submit MS for Pumps- MS	7	03-Nov-26	10-Nov-26	337	0	0	0
JDI	Review & approval MS for Pumps- MS	9	11-Nov-26	23-Nov-26	279	0	0	0
JDH3-02-009-Duct Works		18	03-Nov-26	23-Nov-26	357	0	0	0
JDI	Prepare & Submit MS for Duct Works- MS	7	03-Nov-26	10-Nov-26	357	0	0	0
JDI	Review & approval MS for Duct Works- MS	9	11-Nov-26	23-Nov-26	296	0	0	0
JDH3-02-009-Drainage System		18	03-Nov-26	23-Nov-26	240	0	0	0
JDI	Prepare & Submit MS for Drinage System- MS	7	03-Nov-26	10-Nov-26	241	0	0	0
JDI	Review & approval MS for Drainage System- MS	9	11-Nov-26	23-Nov-26	199	0	0	0
JDH3-02-009-Water Supply System		18	03-Nov-26	23-Nov-26	330	0	0	0
JDI	Prepare & Submit MS for Water Supply System- MS	7	03-Nov-26	10-Nov-26	331	0	0	0
JDI	Review & approval MS for Water Supply System- MS	9	11-Nov-26	23-Nov-26	274	0	0	0
JDH3-02-009-Chlorination System		18	03-Nov-26	23-Nov-26	353	0	0	0
JDI	Prepare & Submit MS for Chlorination System- MS	7	03-Nov-26	10-Nov-26	354	0	0	0
JDI	Review & approval MS for Chlorination System- MS	9	11-Nov-26	23-Nov-26	293	0	0	0
JDH3-02-009-Over head Crane		18	03-Nov-26	23-Nov-26	137	0	0	0
JDI	Prepare & Submit MS for Over head Crane- MS	7	03-Nov-26	10-Nov-26	138	0	0	0
JDI	Review & approval MS for Over head Crane- MS	9	11-Nov-26	23-Nov-26	114	0	0	0
JDH3-02-009-Access Control		18	03-Nov-26	23-Nov-26	247	0	0	0
JDI	Prepare & Submit MS for Access Control- MS	7	03-Nov-26	10-Nov-26	248	0	0	0
JDI	Review & approval MS for Access Control- MS	9	11-Nov-26	23-Nov-26	205	0	0	0
JDH3-02-009-Data Communication		18	03-Nov-26	23-Nov-26	199	0	0	0
JDI	Prepare & Submit MS for Data Communication- MS	7	03-Nov-26	10-Nov-26	200	0	0	0
JDI	Review & approval MS for Data Communication- MS	9	11-Nov-26	23-Nov-26	165	0	0	0
JDH3-02-009-Security System		18	03-Nov-26	23-Nov-26	377	0	0	0
JDI	Prepare & Submit MS for Security System- MS	7	03-Nov-26	10-Nov-26	378	0	0	0
JDI	Review & approval MS for Security System- MS	9	11-Nov-26	23-Nov-26	313	0	0	0
JDH3-02-009-Programing Logical Control System		18	03-Nov-26	23-Nov-26	302	0	0	0
JDI	Prepare & Submit MS for Programing Logical Control System- M	7	03-Nov-26	10-Nov-26	302	0	0	0
JDI	Review & approval MS for Programing Logical Control System- I	9	11-Nov-26	23-Nov-26	250	0	0	0
Procurement		151	04-Aug-26 A	22-Feb-27	320	0	492,877	2,957,261
Long Lead Items		112	03-Nov-26	22-Feb-27	378	0	0	985,754
Fabrication - FAB - PW Pump Station		112	03-Nov-26	22-Feb-27	342	0	0	0

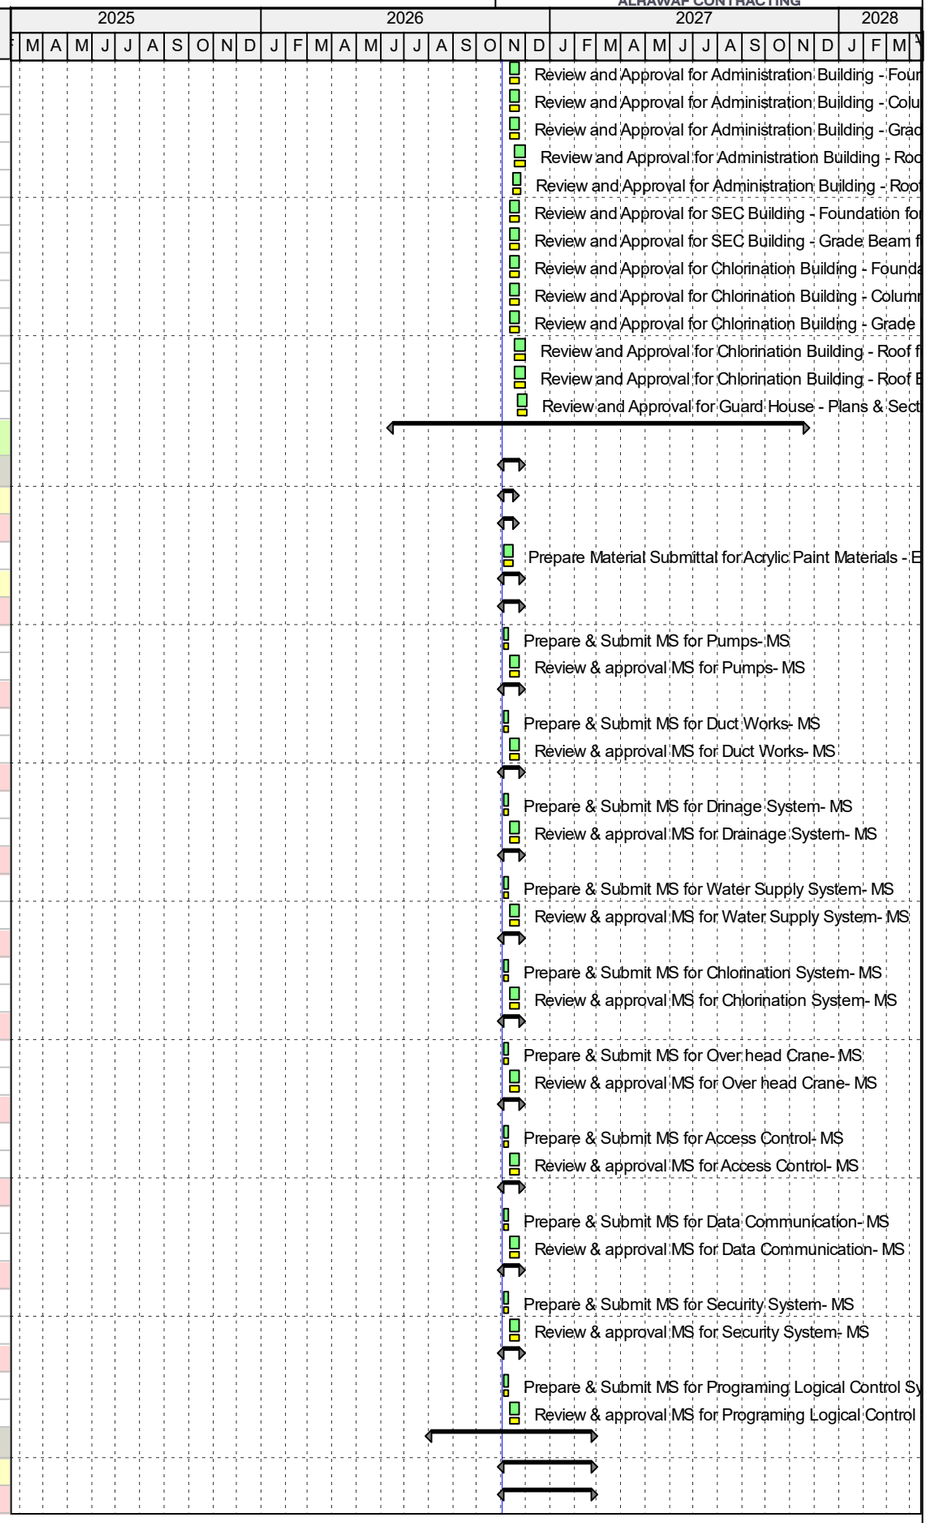

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	JDH3-02-009-Long Lead Items - LOL-Manufacturing and Custom C	112	03-Nov-26	22-Feb-27	342	0	0	0
	Material Fabrication for Addressable Fire Alarm System - PR-TC-	84	03-Nov-26	25-Jan-27	10	0	0	0
	Material Fabrication for Access Control System - PR-TC-FAB	84	03-Nov-26	25-Jan-27	35	0	0	0
	Material Fabrication for Data Communication System - PR-TC-F/	84	03-Nov-26	25-Jan-27	357	0	0	0
	Material Fabrication for Security System - PR-TC-FAB	112	03-Nov-26	22-Feb-27	342	0	0	0
	Delivery and staging on Site - DOS - PW Pump Station	21	03-Nov-26	23-Nov-26	469	0	0	985,754
	JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging	21	03-Nov-26	23-Nov-26	144	0	0	328,585
	delivery and staging for Surge Protection System - PR-MC-DOS	21	03-Nov-26	23-Nov-26	144	0	0	328,585
	JDH3-02-009-Long Lead Items - LOL-Material Delivery and staging	10	03-Nov-26	12-Nov-26	480	0	0	657,169
	delivery and staging for Transformer (TR) - PR-EL-DOS	10	03-Nov-26	12-Nov-26	480	0	0	328,585
	delivery and staging for Main Distribution Boards (MDB) - PR-EL-	10	03-Nov-26	12-Nov-26	318	0	0	328,585
	Short Lead Items	77	04-Aug-26 A	06-Dec-26	386	0	492,877	1,971,507
	Purchase Order - PO - PW Pump Station	21	03-Nov-26	26-Nov-26	394	0	0	0
	JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Epoxy Flooring - PR-AR-PO	21	03-Nov-26	26-Nov-26	356	0	0	0
	Material Purchase Order for Acrylic Paint Materials - PR-AR-PO	21	03-Nov-26	26-Nov-26	377	0	0	0
	Material Purchase Order for Chain link Fences - PR-AR-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Steel Gates - PR-AR-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	JDH3-02-009-Short Lead Items - SHL-Material Purchase Order - P(	21	03-Nov-26	26-Nov-26	394	0	0	0
	Material Purchase Order for Fuel Oil System - PR-MC-PO	21	03-Nov-26	26-Nov-26	262	0	0	0
	Material Purchase Order for Fire Protection System - PR-MC-PO	21	03-Nov-26	26-Nov-26	232	0	0	0
	Material Purchase Order for Wall mounted Split Units - PR-MC-P	21	03-Nov-26	26-Nov-26	240	0	0	0
	Material Purchase Order for Exhaust Fans - PR-MC-PO	21	03-Nov-26	26-Nov-26	240	0	0	0
	Material Purchase Order for Galvanized Iron Sheets for Duct Wc	21	03-Nov-26	26-Nov-26	240	0	0	0
	Material Purchase Order for Air Outlets - PR-MC-PO	21	03-Nov-26	26-Nov-26	394	0	0	0
	Delivery and staging on Site - DOS - PW Pump Station	77	04-Aug-26 A	06-Dec-26	440	0	492,877	1,971,507
	JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging	77	04-Aug-26 A	06-Dec-26	280	0	492,877	1,314,338
	delivery and staging for GRP Tank - PR-MC-DOS	10	03-Nov-26	12-Nov-26	304	0	0	328,585
	delivery and staging for Wall mounted Split Units - PR-MC-DOS	10	04-Aug-26 A	06-Dec-26	280	0	164,292	328,585
	delivery and staging for Exhaust Fans - PR-MC-DOS	10	04-Aug-26 A	06-Dec-26	280	0	164,292	328,585
	delivery and staging for Galvanized Iron Sheets for Duct Works	10	04-Aug-26 A	06-Dec-26	280	0	164,292	328,585
	JDH3-02-009-Short Lead Items - SHL-Material Delivery and staging	10	03-Nov-26	12-Nov-26	464	0	0	657,169
	delivery and staging for Panel Boards - PR-EL-DOS	10	03-Nov-26	12-Nov-26	318	0	0	328,585
	delivery and staging for KWH Meter - PR-EL-DOS	10	03-Nov-26	12-Nov-26	464	0	0	328,585
	Construction	358	16-Jun-26 A	17-Nov-27	98	1,403,190	2,330,182	7,210,408
	JDH3-02-009-B8-SITE WORK	358	24-Jun-26 A	17-Nov-27	81	0	600,511	3,096,849
	JDH3-02-009-B8-Site Works	23	03-Nov-26	29-Nov-26	326	0	0	855,764
	JDH3-02-009-B8-Roads	7	03-Nov-26	10-Nov-26	130	0	0	763,520
	Bituminrus base course, Including Prime Coat (MC1) - (B8 2.2.1	4	03-Nov-26	07-Nov-26	130	0	0	436,444
	Bituminrus concrete wearing course, Including Tack coat (RC2).	3	08-Nov-26	10-Nov-26	130	0	0	327,076
	JDH3-02-009-B8-Pavement Markings	16	11-Nov-26	29-Nov-26	326	0	0	26,527
	120mm wide centre lane- double line (solid) - M4 - (B8 2.2.3)-P'	5	11-Nov-26	16-Nov-26	326	0	0	2,390
	200mm wide. (edge line)-yellow - M1 - (B8 2.2.4)-PWPS-B8-D0:	11	17-Nov-26	29-Nov-26	326	0	0	24,137
	JDH3-02-009-B8-Traffic Signage	12	11-Nov-26	24-Nov-26	130	0	0	65,717
	Traffic signs, ground mounted, 1 Sheet Alumenium, (breakawa	12	11-Nov-26	24-Nov-26	130	0	0	65,717
	JDH3-02-009-B8-Mechanical Works-phase 1	358	24-Jun-26 A	17-Nov-27	81	0	600,511	2,241,084
	JDH3-02-009-B8-Site Interconnecting Pipes 400 mm	8	10-Nov-26	18-Nov-26	354	0	0	1,155,666
	Excavation Works for Ductile Iron Pipe 400 mm - Depth from 2.5	2	10-Nov-26	11-Nov-26	343	0	0	231,036
	Soil Replacement and Bedding Works for Ductile Iron Pipe 400	2	12-Nov-26	14-Nov-26	343	0	0	57,759
	Pipe.Installationfor Ductile Iron Pipe 400 mm - Depth from 2.51	4	15-Nov-26	18-Nov-26	343	0	0	635,348
	Fitting.Installationfor Ductile Iron Pipe 400 mm - Depth from 2.5	4	15-Nov-26	18-Nov-26	354	0	0	231,523
	JDH3-02-009-B8-Site Interconnecting Pipes 500 mm	344	24-Jun-26 A	17-Nov-27	81	0	146,058	243,430
	Pipe.Installationfor Ductile Iron Pipe 500 mm - Depth from 2.51	6	27-Jun-26 A	13-Feb-27	280	0	114,760	191,266

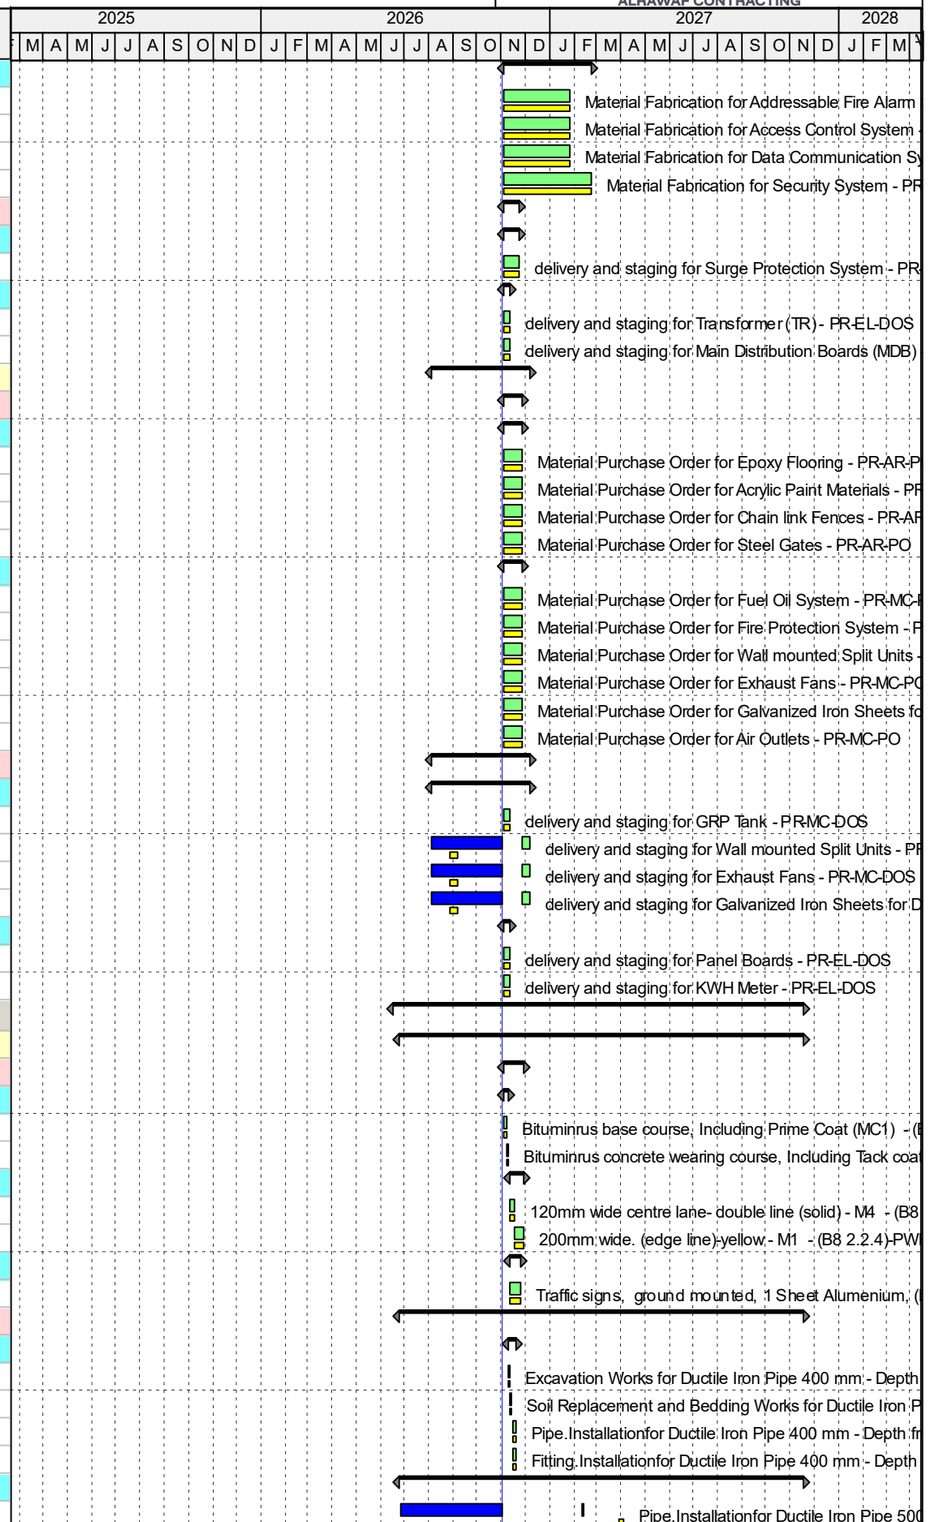


Actual Level of Effort | Remaining Work
Primary Baseline | Critical Remaining Work
Actual Work | Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Soil Replacement and Bedding Works for Ductile Iron Pipe 500	2	24-Jun-26 A	03-Nov-26	359	0	10,433	17,388
	Backfilling and warning tape Works for Ductile Iron Pipe 500 mn	4	22-Jul-26 A	17-Nov-27	81	0	20,865	34,776
	JDH3-02-009-B8-Site Interconnecting Pipes 600 mm	2	03-Nov-26	04-Nov-26	358	0	0	175
	Soil Replacement and Bedding Works for Ductile Iron Pipe 600	2	03-Nov-26	04-Nov-26	358	0	0	175
	JDH3-02-009-B8-Site Interconnecting Pipes 800 mm	218	08-Jul-26 A	06-Mar-27	279	0	108,234	216,468
	Soil Replacement and Bedding Works for Ductile Iron Pipe 800	2	09-Jul-26 A	03-Nov-26	356	0	7,731	15,462
	Backfilling and warning tape Works for Ductile Iron Pipe 800 mn	2	22-Jul-26 A	06-Mar-27	279	0	15,462	30,924
	Pipe.Installationfor Ductile Iron Pipe 800 mm - Depth from 2.51	4	08-Jul-26 A	03-Feb-27	277	0	85,041	170,082
	JDH3-02-009-B8-Site Interconnecting Pipes 1000 mm	322	11-Aug-26 A	17-Nov-27	79	0	346,219	494,598
	Pipe.Installationfor Ductile Iron Pipe 1000 mm - Depth from 2.5	4	13-Aug-26 A	16-Feb-27	282	0	272,029	388,613
	Soil Replacement and Bedding Works for Ductile Iron Pipe 100(	2	11-Aug-26 A	03-Nov-26	373	0	24,730	35,328
	Backfilling and warning tape Works for Ductile Iron Pipe 1000 m	2	13-Aug-26 A	17-Nov-27	79	0	49,460	70,657
	JDH3-02-009-B8-Connection of main inlet pipe 800 mm with exterr	6	03-Nov-26	09-Nov-26	343	0	0	32,586
	Excavation Works for Flow Meter Chamber - - (B8 15.3.1)-PWP	2	03-Nov-26	04-Nov-26	343	0	0	7,241
	PC Casting for Flow Meter Chamber - - (B8 15.3.1)-PWPS-B8-[	2	05-Nov-26	07-Nov-26	343	0	0	7,241
	Base RC Casting Flow Meter Chamber - (B8 15.3.1)-PWPS-B8-I	2	08-Nov-26	09-Nov-26	343	0	0	18,103
	JDH3-02-009-B8-Connection of main inlet pipe 1000 mm with exte	6	03-Nov-26	09-Nov-26	392	0	0	45,727
	Excavation Works for Flow Meter Chamber - - (B8 15.3.2)-PWP	2	03-Nov-26	04-Nov-26	392	0	0	10,162
	PC Casting for Flow Meter Chamber - - (B8 15.3.2)-PWPS-B8-[	2	05-Nov-26	07-Nov-26	392	0	0	10,162
	Base RC Casting Flow Meter Chamber - (B8 15.3.2)-PWPS-B8-I	2	08-Nov-26	09-Nov-26	392	0	0	25,404
	JDH3-02-009-B8-Connection of main overflow pipe 500 mm with ex	4	03-Nov-26	07-Nov-26	356	0	0	12,194
	Excavation Works for Ductile Iron Pipe 1200 mm - Depth from 2	2	03-Nov-26	04-Nov-26	356	0	0	8,129
	Soil Replacement and Bedding Works for Ductile Iron Pipe 120(	2	05-Nov-26	07-Nov-26	356	0	0	4,065
	JDH3-02-009-B8-Connection with existing CMZ site and feeding PS	6	03-Nov-26	09-Nov-26	343	0	0	3,658
	Excavation Works for Flow Meter Chamber - - (B8 15.3.4)-PWP	2	03-Nov-26	04-Nov-26	343	0	0	813
	PC Casting for Flow Meter Chamber - - (B8 15.3.4)-PWPS-B8-[	2	05-Nov-26	07-Nov-26	343	0	0	813
	Base RC Casting Flow Meter Chamber - (B8 15.3.4)-PWPS-B8-I	2	08-Nov-26	09-Nov-26	343	0	0	2,032
	JDH3-02-009-B8-Fuel Tank	4	03-Nov-26	07-Nov-26	301	0	0	36,582
	Excavation Works for FRP Fuel Tank - Depth from 1.51 to 2.50-	2	03-Nov-26	04-Nov-26	301	0	0	12,194
	Concrete Base Castingfor FRP Fuel Tank - Depth from 1.51 to 2	2	05-Nov-26	07-Nov-26	301	0	0	24,388
	JDH3-02-009-B9-PUMP STATION	39	27-Sep-26 A	24-Nov-26	396	275,288	6,572	315,371
	JDH3-02-009-B9-Sub Structure	9	03-Nov-26	12-Nov-26	276	33,790	0	33,790
	JDH3-02-009-B9-Slab on Grade	9	03-Nov-26	12-Nov-26	276	33,790	0	33,790
	Shuttering Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2	03-Nov-26	04-Nov-26	276	6,758	0	6,758
	Steel Fixing Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	3	05-Nov-26	08-Nov-26	276	16,895	0	16,895
	RC Casting Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2	09-Nov-26	10-Nov-26	276	6,758	0	6,758
	Deshuttering Slab on Grade - (B9. 3.2.6)-PWPS-B9-D03	2	11-Nov-26	12-Nov-26	276	3,379	0	3,379
	JDH3-02-009-B9-Super Structure	38	27-Sep-26 A	24-Nov-26	217	166,907	6,572	166,907
	JDH3-02-009-B9-Roof Beam	19	27-Sep-26 A	09-Nov-26	220	18,617	4,654	18,617
	RC Casting Roof Beam - (B9. 3.2.4)-PWPS-B9-D03	2	04-Nov-26	07-Nov-26	220	4,654	0	4,654
	Deshuttering Roof Beam - (B9. 3.2.4)-PWPS-B9-D03	2	07-Nov-26	09-Nov-26	220	2,327	0	2,327
	Steel Fixing Roof Beam - (B9. 3.2.4)-PWPS-B9-D03	2	27-Sep-26 A	04-Nov-26	220	11,636	4,654	11,636
	JDH3-02-009-B9-Roof Slab	25	27-Sep-26 A	09-Nov-26	103	7,672	1,918	7,672
	RC Casting Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2	04-Nov-26	07-Nov-26	103	1,918	0	1,918
	Deshuttering Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2	07-Nov-26	09-Nov-26	103	959	0	959
	Steel Fixing Roof Slab - (B9. 3.2.5)-PWPS-B9-D03	2	27-Sep-26 A	04-Nov-26	103	4,795	1,918	4,795
	JDH3-02-009-B9-Hollow Core slab	10	09-Nov-26	21-Nov-26	220	137,001	0	137,001
	Hollow Core Slab Installation Hollow Core slab - (B9. 3.3.1)-PWI	2	09-Nov-26	11-Nov-26	220	27,400	0	27,400
	Hollow Core Slab Screed Hollow Core slab - (B9. 3.3.1)-PWPS-I	8	11-Nov-26	21-Nov-26	220	109,601	0	109,601
	JDH3-02-009-B9-pump pads	2	22-Nov-26	24-Nov-26	211	3,617	0	3,617
	Shuttering Pump Pads - (B9. 3.2.9)-PWPS-B9-D03	2	22-Nov-26	24-Nov-26	211	3,617	0	3,617
	JDH3-02-009-B9-Finishes	18	03-Nov-26	24-Nov-26	397	46,860	0	49,285
	JDH3-02-009-B9-Masonary	13	09-Nov-26	24-Nov-26	108	34,746	0	34,746

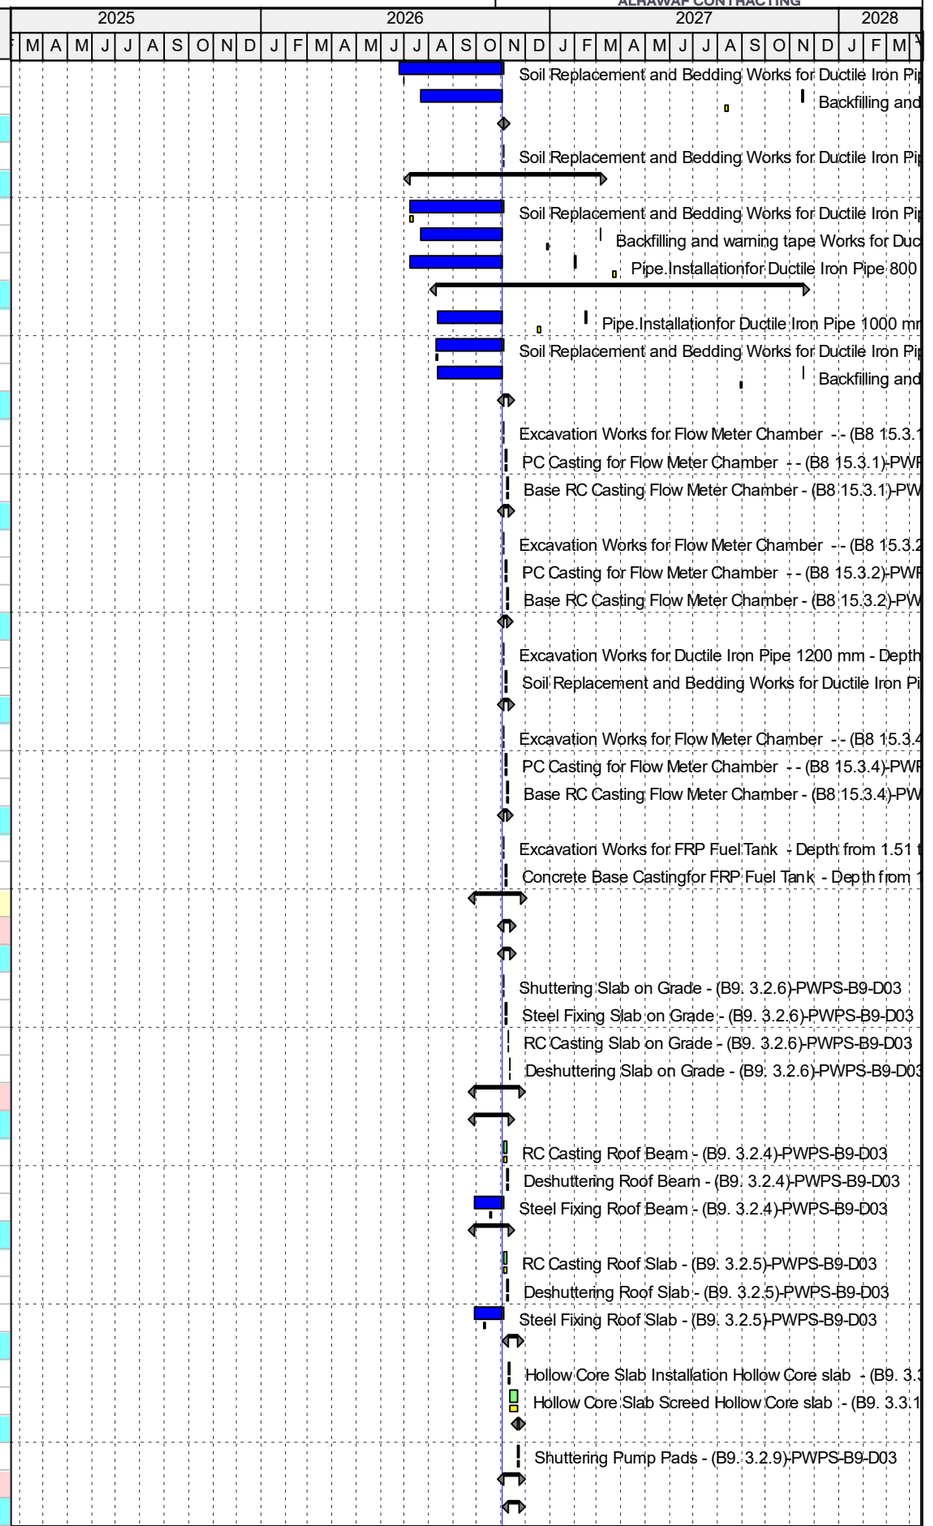


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Masonary Block work Insulated Block Work - (B9. 4.1.1)-PWPS-I	11	09-Nov-26	22-Nov-26	103	33,109	0	33,109
	Masonary Block work Block Work - (B9. 4.1.2)-PWPS-B9-D04	2	22-Nov-26	24-Nov-26	108	1,637	0	1,637
JDH3-02-009-B9-Thermal & Moisture Protection		11	03-Nov-26	15-Nov-26	404	12,114	0	14,538
	Applying Bitumen waterproofing Paint Insulation Bitumen water	7	03-Nov-26	10-Nov-26	404	12,114	0	12,114
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	4	11-Nov-26	15-Nov-26	404	0	0	2,424
JDH3-02-009-B9-Mechanical Works-phase 1		19	03-Nov-26	24-Nov-26	363	2,845	0	40,504
JDH3-02-009-B9-Soakage Pits (For AC Condensated Water)		10	14-Nov-26	24-Nov-26	276	2,845	0	2,845
	Soakage Pits Installation 600*600 mm - (B9. 15.8.3.1)-PWPS-E	10	14-Nov-26	24-Nov-26	276	2,845	0	2,845
JDH3-02-009-B9-Manhole Works depth 1.50 Diam 600 mm		16	07-Nov-26	24-Nov-26	363	0	0	25,912
	Excavation and PC Blinding Works for Manhole 600 mm - - (B9.	3	07-Nov-26	09-Nov-26	369	0	0	4,573
	Installation of Basefor Manhole 600 mm - - (B9. 15.8.5.1)-PWP	4	17-Nov-26	21-Nov-26	363	0	0	15,243
	MH Ring and C.Slab Works and Backfilling Worksfor Manhole 6(	3	22-Nov-26	24-Nov-26	363	0	0	6,097
JDH3-02-009-B9-Manhole Works depth 2.00 Diam 600 mm		12	03-Nov-26	16-Nov-26	363	0	0	11,747
	Excavation and PC Blinding Works for Manhole 600 mm - - (B9.	3	03-Nov-26	05-Nov-26	363	0	0	2,073
	Installation of Basefor Manhole 600 mm - - (B9. 15.8.5.2)-PWP	5	07-Nov-26	11-Nov-26	363	0	0	6,910
	MH Ring and C.Slab Works and Backfilling Worksfor Manhole 6(	4	12-Nov-26	16-Nov-26	363	0	0	2,764
JDH3-02-009-B9-Electrical Works for Potable Water Pump Station		18	03-Nov-26	24-Nov-26	337	24,885	0	24,885
JDH3-02-009-B9-LED Interior Lighting		2	22-Nov-26	24-Nov-26	105	4,363	0	4,363
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	22-Nov-26	24-Nov-26	105	4,363	0	4,363
JDH3-02-009-B9-Grounding and Bonding		4	03-Nov-26	07-Nov-26	351	20,522	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	351	20,522	0	20,522
JDH3-02-009-B10-GUARD HOUSE		22	03-Nov-26	28-Nov-26	393	6,054	0	14,950
JDH3-02-009-B10-Sub Structure		8	05-Nov-26	14-Nov-26	194	1,852	0	1,852
JDH3-02-009-B10-Slab on Grade		8	05-Nov-26	14-Nov-26	194	1,852	0	1,852
	Shuttering Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2	05-Nov-26	07-Nov-26	194	370	0	370
	Steel Fixing Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2	08-Nov-26	09-Nov-26	194	926	0	926
	RC Casting Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2	10-Nov-26	11-Nov-26	194	370	0	370
	Deshuttering Slab on Grade - (B10. 3.2.6)-PWPS-B10-D03	2	12-Nov-26	14-Nov-26	194	185	0	185
JDH3-02-009-B10-Finishes		16	03-Nov-26	21-Nov-26	399	2,716	0	3,728
JDH3-02-009-B10-Masonary		4	15-Nov-26	18-Nov-26	194	2,616	0	2,616
	Masonary Block work ACC Block - (B10. 4.1.1)-PWPS-B10-D04	2	15-Nov-26	16-Nov-26	194	2,263	0	2,263
	Masonary Block work Block Work - (B10. 4.1.2)-PWPS-B10-D04	2	17-Nov-26	18-Nov-26	194	353	0	353
JDH3-02-009-B10-Thermal & Moisture Protection		16	03-Nov-26	21-Nov-26	399	101	0	1,112
	Applying Bitumen waterproofing Paint Insulation Bitumen water	2	03-Nov-26	04-Nov-26	413	0	0	501
	Applying Polyethylene sheet under SOG Polyethylene sheet - (I	2	03-Nov-26	04-Nov-26	194	101	0	101
	Applying Foam concrete screed Insulation Foam concrete - (B1	2	19-Nov-26	21-Nov-26	203	0	0	511
JDH3-02-009-B10-Mechanical Works-phase 1		4	19-Nov-26	23-Nov-26	201	0	0	2,336
JDH3-02-009-B10-PPR For Cold Water Supply Piping System		4	19-Nov-26	23-Nov-26	201	0	0	2,336
	PPR Pipes Installation 32 mm - (B10. 15.3.1.1)-PWPS-B10-D15	2	19-Nov-26	21-Nov-26	201	0	0	1,005
	PPR Pipes Installation 25 mm - (B10. 15.3.1.2)-PWPS-B10-D15	2	22-Nov-26	23-Nov-26	201	0	0	1,331
JDH3-02-009-B10-Electrical Works for Potable Water Pump Station		22	03-Nov-26	28-Nov-26	212	1,486	0	7,035
JDH3-02-009-B10-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+		8	19-Nov-26	28-Nov-26	194	1,486	0	1,486
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	8	19-Nov-26	28-Nov-26	194	1,486	0	1,486
JDH3-02-009-B10-LED Interior Lighting		2	19-Nov-26	21-Nov-26	203	0	0	303
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	19-Nov-26	21-Nov-26	203	0	0	303
JDH3-02-009-B10-Grounding and Bonding		4	03-Nov-26	07-Nov-26	230	0	0	4,897
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	230	0	0	4,897
JDH3-02-009-B10-Addressable Fire-Alarm System		4	19-Nov-26	23-Nov-26	203	0	0	349
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B10.	4	19-Nov-26	23-Nov-26	203	0	0	349
JDH3-02-009-B11-ADMIN BUILDING		81	13-Aug-26 A	25-Nov-26	395	0	1,564	106,377
JDH3-02-009-B11-Sub Structure		8	05-Nov-26	14-Nov-26	405	0	0	13,752
JDH3-02-009-B11-Slab on Grade		8	05-Nov-26	14-Nov-26	405	0	0	13,752
	Shuttering Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2	05-Nov-26	07-Nov-26	390	0	0	2,750

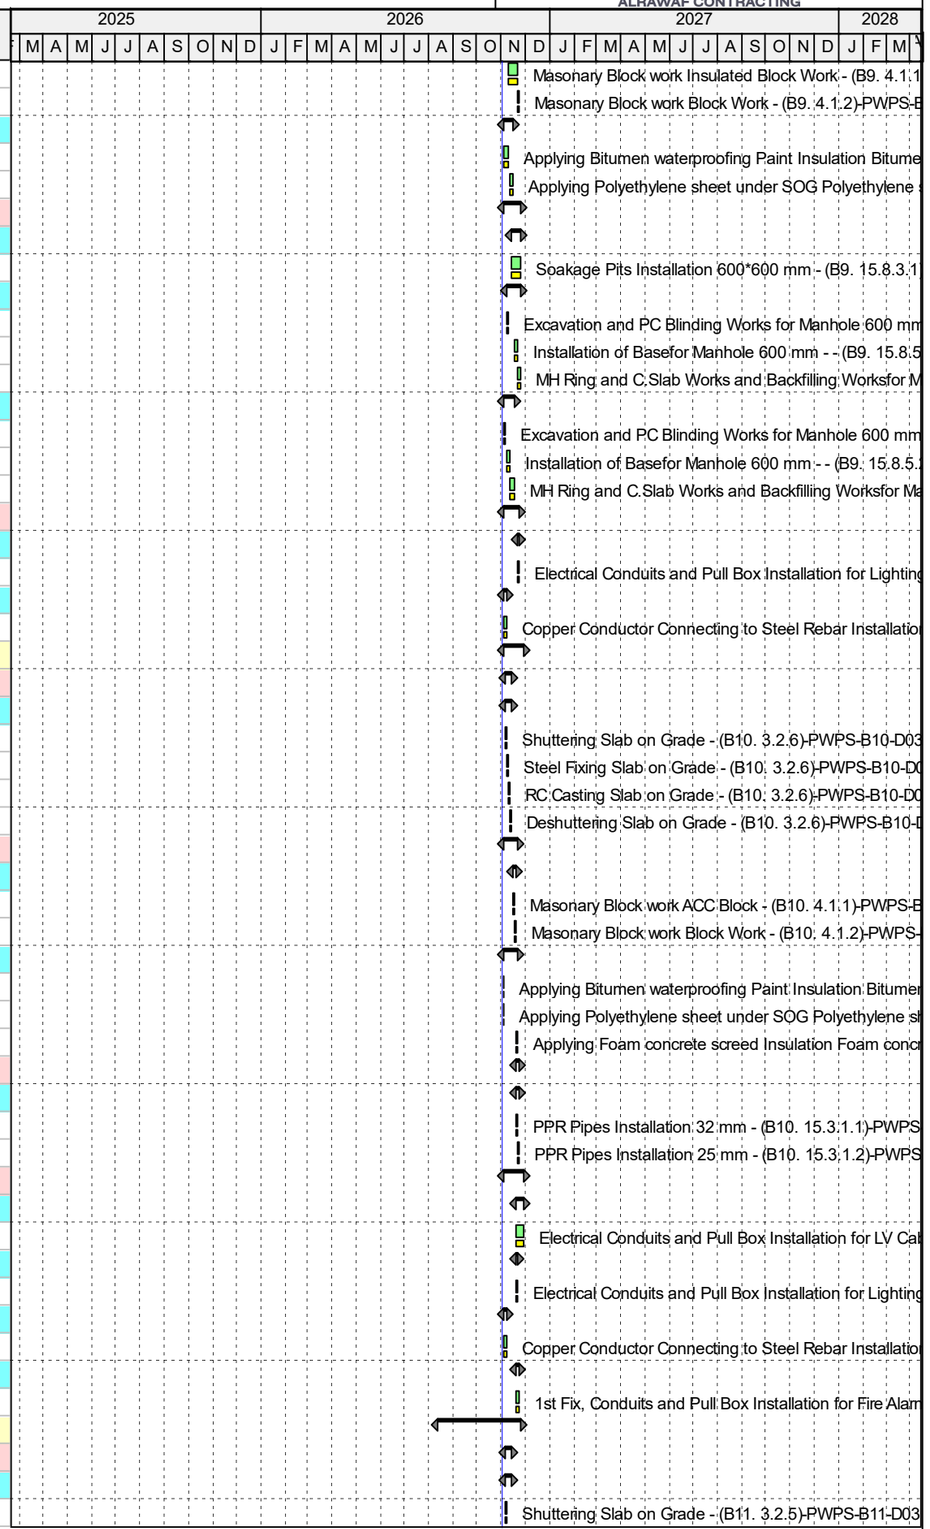


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Steel Fixing Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2	08-Nov-26	09-Nov-26	390	0	0	6,876
	RC Casting Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2	10-Nov-26	11-Nov-26	390	0	0	2,750
	Deshuttering Slab on Grade - (B11. 3.2.5)-PWPS-B11-D03	2	12-Nov-26	14-Nov-26	405	0	0	1,375
JDH3-02-009-B11-Super Structure		5	21-Nov-26	25-Nov-26	251	0	0	2,629
JDH3-02-009-B11-Entrance and Ramps		5	21-Nov-26	25-Nov-26	251	0	0	2,629
	Shuttering Landing & Steel Ladder Pad - (B11. 3.2.7)-PWPS-B1	2	21-Nov-26	22-Nov-26	251	0	0	751
	Steel Fixing Landing & Steel Ladder Pad - (B11. 3.2.7)-PWPS-E	3	23-Nov-26	25-Nov-26	251	0	0	1,878
JDH3-02-009-B11-Finishes		19	03-Nov-26	24-Nov-26	373	0	0	59,041
JDH3-02-009-B11-Masonary		6	03-Nov-26	09-Nov-26	250	0	0	13,121
	Masonary Block work Insulated Masonary Unit - (B11. 4.1.1)-PW	2	03-Nov-26	04-Nov-26	248	0	0	5,918
	Masonary Block work Block Work - (B11. 4.1.2)-PWPS-B11-D04	2	05-Nov-26	07-Nov-26	250	0	0	1,919
	Masonary Block work Block Work - (B11. 4.1.3)-PWPS-B11-D04	4	05-Nov-26	09-Nov-26	248	0	0	3,333
	Precast Concrete Scupper Scrupper - (B11. 4.2)-PWPS-B11-D0	2	08-Nov-26	09-Nov-26	250	0	0	1,951
JDH3-02-009-B11-Metals		2	23-Nov-26	24-Nov-26	252	0	0	17,654
	Steel Ladder Installation Aluminum Canopy Shade - (B11. 5.2)-I	2	23-Nov-26	24-Nov-26	252	0	0	17,654
JDH3-02-009-B11-Thermal & Moisture Protection		8	03-Nov-26	11-Nov-26	384	0	0	4,939
	Polyethylene Sheet Under SOG Polyethylene sheet - (B11. 7.1)	2	03-Nov-26	04-Nov-26	390	0	0	520
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2	03-Nov-26	04-Nov-26	252	0	0	2,238
	Liquid Applied Waterproofing Membrane For Toilets Liquid Wate	2	10-Nov-26	11-Nov-26	248	0	0	2,181
JDH3-02-009-B11-Architecture Finishes		6	16-Nov-26	22-Nov-26	252	0	0	23,326
	Internal Cement Plaster For Walls 15 mm - (B11. 9.2.1)-PWPS-I	2	16-Nov-26	17-Nov-26	248	0	0	6,903
	External Cement Plaster For Walls Cement Plaster - (B11. 9.3.1	2	18-Nov-26	19-Nov-26	248	0	0	9,040
	External Acrylic Paint For Walls - (B11. 9.3.2)-PWPS-B11-D09	2	21-Nov-26	22-Nov-26	248	0	0	5,056
	Plaster On Internal Ceiling Cement Plaster - (B11. 9.4.3)-PWPS	2	18-Nov-26	19-Nov-26	252	0	0	604
	Acrylic Paint Applied On Plaster Acrylic Paint - (B11. 9.4.4)-PWF	2	21-Nov-26	22-Nov-26	252	0	0	1,724
JDH3-02-009-B11-Electrical Works for Potable Water Pump Station		72	13-Aug-26 A	23-Nov-26	397	0	1,564	30,955
JDH3-02-009-B11-LV Cables - Copper, 4Cx10mm2 CU/XLPE/SWA/I		3	12-Nov-26	15-Nov-26	248	0	0	495
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	3	12-Nov-26	15-Nov-26	248	0	0	495
JDH3-02-009-B11-LED Interior Lighting		2	12-Nov-26	14-Nov-26	249	0	0	2,116
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	12-Nov-26	14-Nov-26	249	0	0	2,116
JDH3-02-009-B11-Grounding and Bonding		4	03-Nov-26	07-Nov-26	411	0	0	20,522
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	411	0	0	20,522
JDH3-02-009-B11-Data Communications		4	13-Aug-26 A	11-Nov-26	251	0	289	1,445
	1st Fix, Conduits and Pull Box Installation for Data Communicat	4	13-Aug-26 A	11-Nov-26	251	0	289	1,445
JDH3-02-009-B11-Addressable Fire-Alarm System		4	13-Aug-26 A	23-Nov-26	247	0	622	3,111
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B11.	4	13-Aug-26 A	23-Nov-26	247	0	622	3,111
JDH3-02-009-B11-Access control system		4	13-Aug-26 A	23-Nov-26	247	0	412	2,060
	1st Fix, Conduits and Pull Box Installation for Access control - (B	4	13-Aug-26 A	23-Nov-26	247	0	412	2,060
JDH3-02-009-B11-CCTV system		2	13-Aug-26 A	09-Nov-26	253	0	241	1,207
	1st Fix, Conduits and Pull Box Installation for CCTV Camera - (E	2	13-Aug-26 A	09-Nov-26	253	0	241	1,207
JDH3-02-009-B12-POTABLE WATER TANK		145	16-Jun-26 A	22-Dec-26	232	1,121,848	1,719,354	3,560,648
JDH3-02-009-B12-Mechanical Works-phase 1		145	16-Jun-26 A	22-Dec-26	232	1,121,848	1,719,354	3,560,648
JDH3-02-009-B12-Storage Tank 2		145	16-Jun-26 A	22-Dec-26	232	1,121,848	1,719,354	3,560,648
	Laying and Welding of second Ring - (B12. 15.1.2)-PWPS-B12	17	12-Nov-26	02-Dec-26	232	0	0	1,219,400
	Laying and Welding of First Ring for Base of shell - (B12. 15.1.:	17	16-Jun-26 A	12-Nov-26	232	1,121,848	560,924	1,121,848
	Roof Aluminum Cover Installation - (B12. 15.1.2)-PWPS-B12-D	17	21-Jul-26 A	22-Dec-26	232	0	463,372	487,760
	Roof Steel Structure Installation - (B12. 15.1.2)-PWPS-B12-D1	17	24-Jun-26 A	22-Dec-26	232	0	695,058	731,640
JDH3-02-009-B13-CHLORINATION BUILDING		82	15-Aug-26 A	23-Nov-26	397	0	2,180	116,214
JDH3-02-009-B13-Super Structure		13	09-Nov-26	23-Nov-26	351	0	0	6,968
JDH3-02-009-B13-Entrance and Ramps		4	19-Nov-26	23-Nov-26	351	0	0	1,397
	Shuttering Landing & Steel Ladder Pad - (B13. 3.2.7)-PWPS-B1	2	19-Nov-26	21-Nov-26	351	0	0	399
	Steel Fixing Landing & Steel Ladder Pad - (B13. 3.2.7)-PWPS-E	2	22-Nov-26	23-Nov-26	351	0	0	998
JDH3-02-009-B13-Mechanical Equipment Pads		9	09-Nov-26	18-Nov-26	351	0	0	5,571

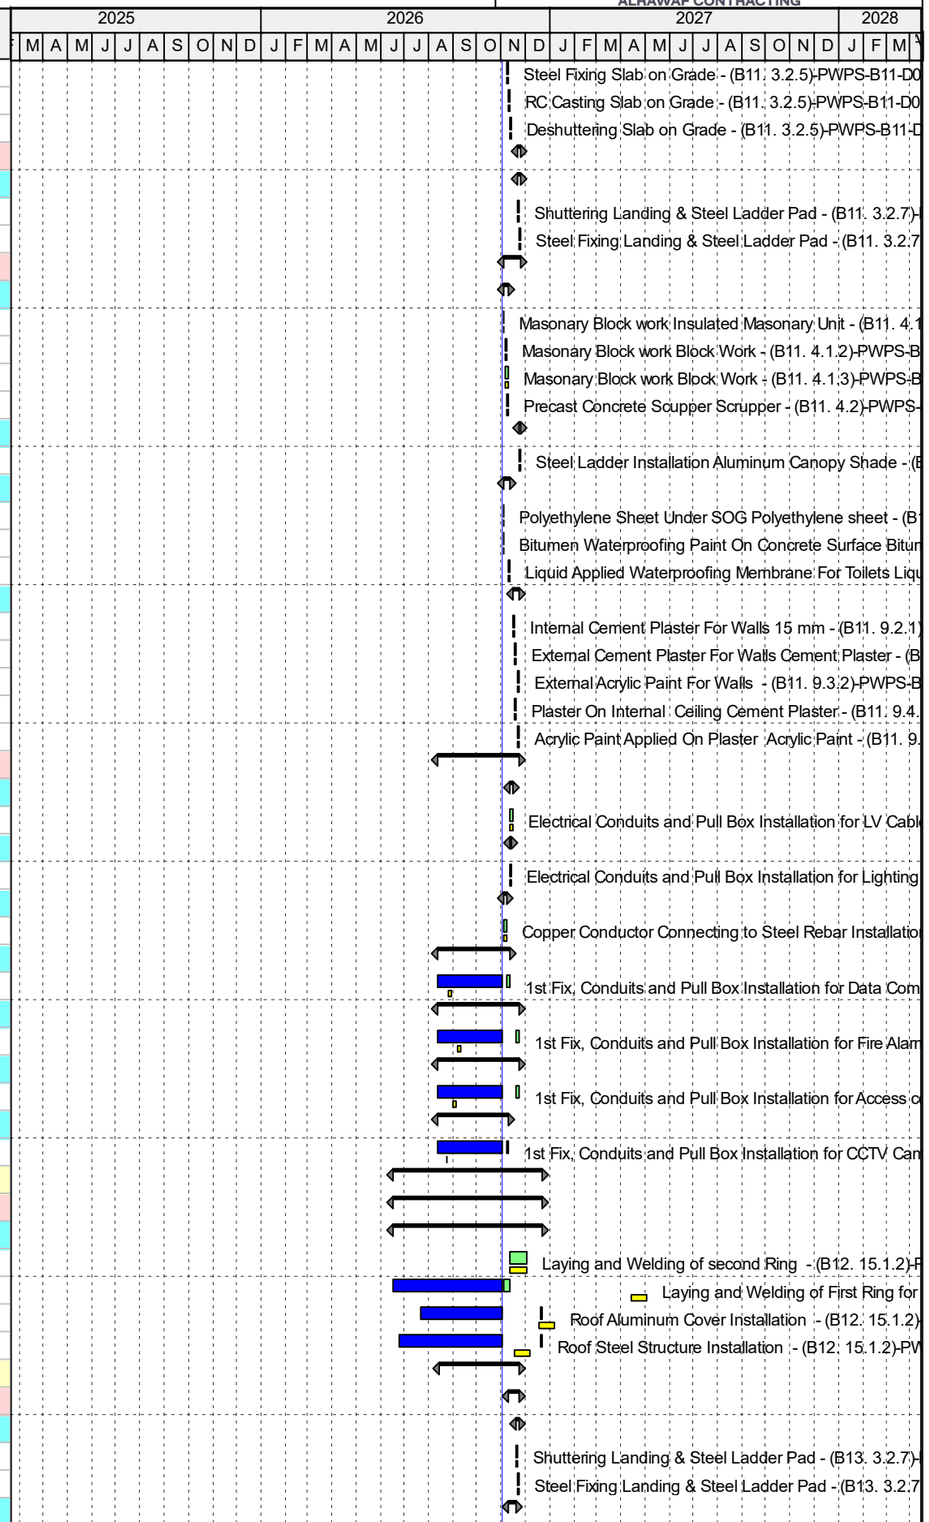


Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
	Shuttering Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2	09-Nov-26	10-Nov-26	351	0	0	1,114
	Steel Fixing Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	3	11-Nov-26	14-Nov-26	351	0	0	2,786
	RC Casting Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2	15-Nov-26	16-Nov-26	351	0	0	1,114
	Deshuttering Mechanical Pads - (B13. 3.2.8)-PWPS-B13-D03	2	17-Nov-26	18-Nov-26	351	0	0	557
JDH3-02-009-B13-Finishes		18	03-Nov-26	23-Nov-26	397	0	0	76,235
JDH3-02-009-B13-Masonary		3	03-Nov-26	05-Nov-26	324	0	0	8,929
	Masonary Block work Insulated Masonary Unit - (B13. 4.1.1)-PW	3	03-Nov-26	05-Nov-26	324	0	0	8,929
JDH3-02-009-B13-Metals		2	15-Nov-26	16-Nov-26	324	0	0	31,777
	Steel Ladder Installation Steel Ladder - (B13. 5.1.1)-PWPS-B13	2	15-Nov-26	16-Nov-26	324	0	0	31,777
JDH3-02-009-B13-Thermal & Moisture Protection		13	03-Nov-26	17-Nov-26	402	0	0	13,489
	Bitumen Waterproofing Paint On Concrete Surface Bitumen Co	2	03-Nov-26	04-Nov-26	413	0	0	1,487
	Polyethylene Sheet Under SOG Polyethylene sheet - (B13. 7.2)	2	03-Nov-26	04-Nov-26	361	0	0	369
	Concrete Screed Foam - (B13. 7.3.1)-PWPS-B13-D07	2	07-Nov-26	08-Nov-26	325	0	0	2,169
	Waterproofing Membrane PVC - (B13. 7.3.2)-PWPS-B13-D07	2	09-Nov-26	10-Nov-26	325	0	0	3,023
	Installation Of Rigid Insulation Extruded Polystyrene - (B13. 7.3.	2	14-Nov-26	15-Nov-26	332	0	0	5,981
	Geotextile Sheet Geotextile Sheet - (B13. 7.3.4)-PWPS-B13-D0	2	16-Nov-26	17-Nov-26	332	0	0	460
JDH3-02-009-B13-Architecture Finishes		15	07-Nov-26	23-Nov-26	324	0	0	22,040
	Internal Cement Plaster For Walls 25 mm - (B13. 9.2.1)-PWPS-I	2	15-Nov-26	16-Nov-26	324	0	0	2,876
	External Cement Plaster For Walls Cement Plaster - (B13. 9.2.2	2	07-Nov-26	08-Nov-26	324	0	0	9,556
	External Acrylic Paint For Walls - (B13. 9.2.3)-PWPS-B13-D09	5	09-Nov-26	14-Nov-26	324	0	0	4,212
	Alkyd Enamel Paint For Internal Walls - (B13. 9.2.4)-PWPS-B1	2	22-Nov-26	23-Nov-26	324	0	0	2,064
	Plaster On Internal Ceiling Cement Plaster - (B13. 9.3.1)-PWPS	2	17-Nov-26	18-Nov-26	324	0	0	2,128
	Acrylic Paint Applied for Internal Ceiling Acrylic Paint - (B13. 9.3.	2	19-Nov-26	21-Nov-26	324	0	0	1,203
JDH3-02-009-B13-Mechanical Works-phase 1		37	19-Sep-26 A	23-Nov-26	349	0	1,016	15,551
JDH3-02-009-B13-HVAC System		4	15-Nov-26	18-Nov-26	324	0	0	4,065
	Sand Trap Louvers Installation -(B13. 15.3.2)-PWPS-B13-D15	4	15-Nov-26	18-Nov-26	324	0	0	4,065
JDH3-02-009-B13-Water Supply System		4	05-Nov-26	09-Nov-26	361	0	0	2,626
	Cold Water Pipes Installation PPR 32 mm - (B13. 15.4.1.1)-PW	2	05-Nov-26	07-Nov-26	361	0	0	1,331
	Cold Water Pipes Installation PPR 25 mm - (B13. 15.4.1.2)-PW	2	08-Nov-26	09-Nov-26	361	0	0	1,295
JDH3-02-009-B13-Sewer And Drainage System		32	19-Sep-26 A	23-Nov-26	349	0	1,016	8,861
	Roof Drain Installation - (B13. 15.5.1)-PWPS-B13-D15	2	11-Nov-26	12-Nov-26	325	0	0	6,829
	Drainage Pipe Installation UPVC 75 mm - (B13. 15.5.3.1)-PWPS	2	19-Sep-26 A	23-Nov-26	349	0	1,016	2,032
JDH3-02-009-B13-Electrical Works for Potable Water Pump Station		79	15-Aug-26 A	19-Nov-26	400	0	1,164	17,459
JDH3-02-009-B13-LV Cables - Copper, 4Cx10mm² (CU/XLPE/PVC)+		7	07-Nov-26	14-Nov-26	324	0	0	1,238
	Electrical Conduits and Pull Box Installation for LV Cables 4Cx1	3	07-Nov-26	09-Nov-26	324	0	0	495
	Cable Tray Installation for LV Cables 4Cx10 mm²- (B13. 16.1.1)	4	10-Nov-26	14-Nov-26	324	0	0	743
JDH3-02-009-B13-LED Interior Lighting		2	07-Nov-26	08-Nov-26	329	0	0	606
	Electrical Conduits and Pull Box Installation for Lighting Fixtures	2	07-Nov-26	08-Nov-26	329	0	0	606
JDH3-02-009-B13-Grounding and Bonding		15	03-Nov-26	19-Nov-26	400	0	0	9,794
	Copper Conductor Connecting to Steel Rebar Installation for Co	4	03-Nov-26	07-Nov-26	411	0	0	6,529
	Earth pits Installation for Copper Rods - (B13. 16.5.1)-PWPS-B1	4	09-Nov-26	12-Nov-26	336	0	0	1,632
	Earth Bars Installation for Copper Rods - (B13. 16.5.1)-PWPS-B	6	14-Nov-26	19-Nov-26	336	0	0	1,632
JDH3-02-009-B13-Addressable Fire-Alarm System		4	15-Aug-26 A	07-Nov-26	331	0	65	324
	1st Fix, Conduits and Pull Box Installation for Fire Alarm - (B13.	4	15-Aug-26 A	07-Nov-26	331	0	65	324
JDH3-02-009-B13-Data Communications		2	15-Aug-26 A	05-Nov-26	329	0	15	73
	1st Fix, Conduits and Pull Box Installation for Data Communicat	2	15-Aug-26 A	05-Nov-26	329	0	15	73
JDH3-02-009-B13-Access control system		4	15-Aug-26 A	08-Nov-26	329	0	967	4,837
	1st Fix, Conduits and Pull Box Installation for Access control - (B	4	15-Aug-26 A	08-Nov-26	329	0	967	4,837
JDH3-02-009-B13-CCTV system		2	15-Aug-26 A	05-Nov-26	331	0	117	585
	1st Fix, Conduits and Pull Box Installation for CCTV Camera - (E	2	15-Aug-26 A	05-Nov-26	331	0	117	585
Close Out		26	03-Nov-26	02-Dec-26	389	0	0	0
As Built Drawing Submittals - SUB-PW Pump Station - PWPS		15	03-Nov-26	19-Nov-26	390	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Structural - ST		15	03-Nov-26	19-Nov-26	390	0	0	0

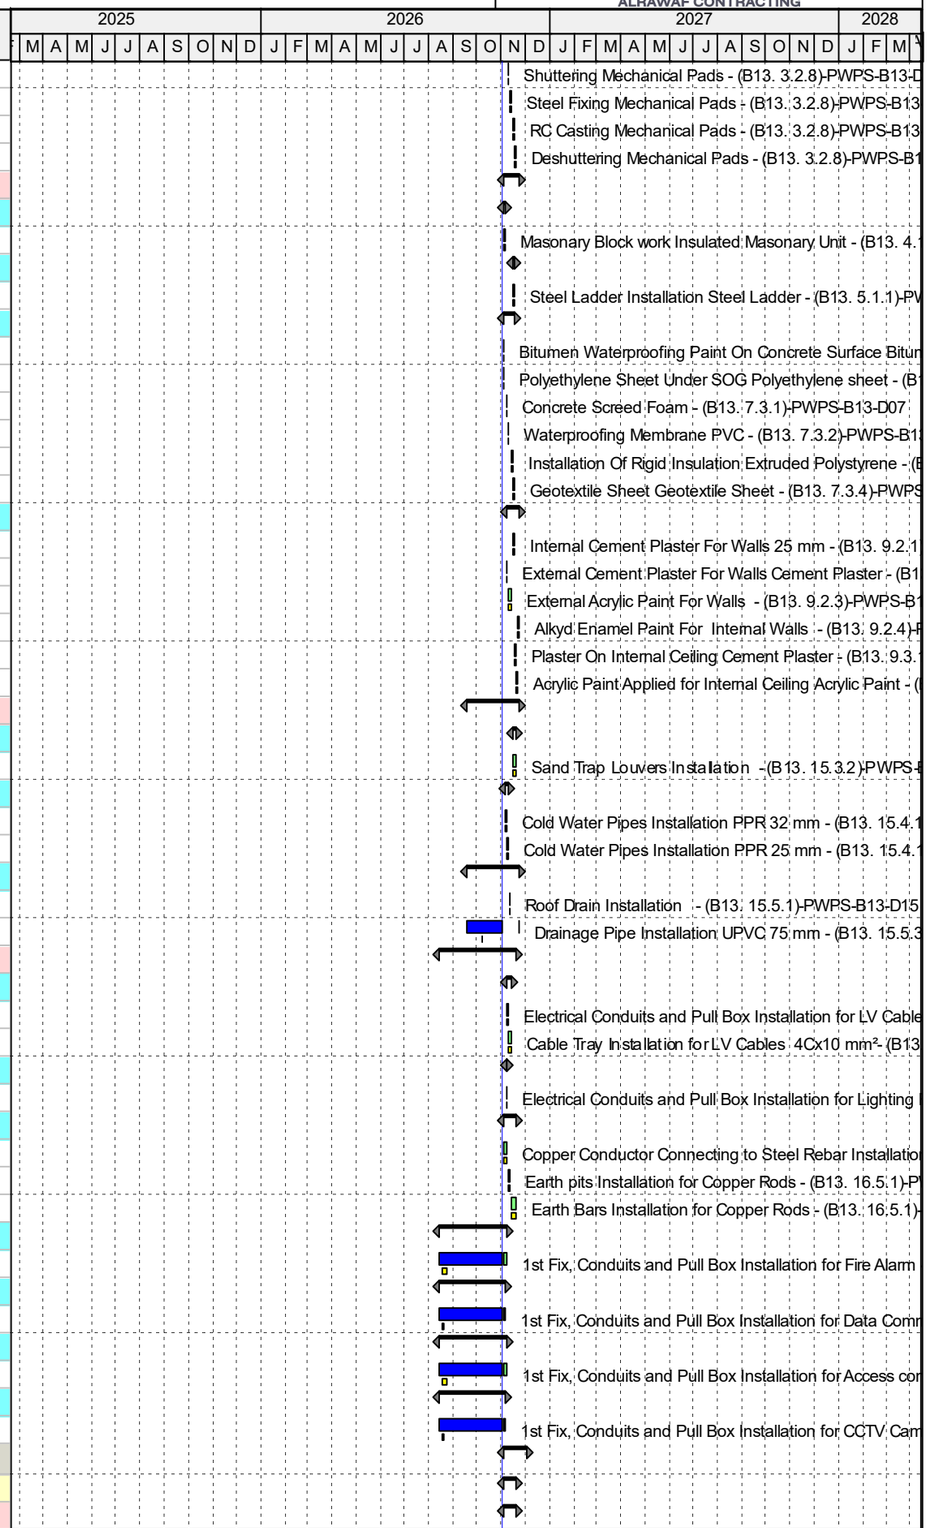

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDI	Prepare and Submit Drawing for PW Pump Building - Columns	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Foundatic	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Slab On (	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Ground B	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Roof Bea	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for PW Pump Building - Roof for S	7	07-Nov-26	15-Nov-26	395	0	0	0
JDI	Prepare and Submit Drawing for GLS1 Tank - Shopdrawings Pla	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for GLS2 Tank - Shopdrawings Pla	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Founc	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Colum	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Slab (	7	12-Nov-26	19-Nov-26	390	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Grade	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof S	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Administration Building - Roof B	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Foundat	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Columns	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Grade B	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof for	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Chlorination Building - Roof Be	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Foundation & C	7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Guard House - Plans & Sectior	7	12-Nov-26	19-Nov-26	390	0	0	0
JDI	Prepare and Submit Drawing for Valve Chamber - Raft for SUB-	7	10-Nov-26	17-Nov-26	392	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Mechanical - MC		7	03-Nov-26	10-Nov-26	398	0	0	0
JDI	Prepare and Submit Drawing for Water Tank 1 Piping System fo	7	03-Nov-26	10-Nov-26	398	0	0	0
JDH3-02-009-As Built Drawing Submittals - SUB-Roads - RD		7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Overall Road Layout Plan for S	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Road Layout Plan - Sheet 01 (	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Roads Profiles for SUB-AS-PW	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Roads Finish Grading Overall F	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Typical Road Details for SUB-A	7	11-Nov-26	18-Nov-26	391	0	0	0
JDI	Prepare and Submit Drawing for Swept Path Analysis for SUB-A	7	11-Nov-26	18-Nov-26	391	0	0	0
As Built Drawing Approvals - APP-PW Pump Station - PWPS		16	11-Nov-26	02-Dec-26	323	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Structural - ST		16	11-Nov-26	02-Dec-26	323	0	0	0
JDI	Review and Approval for PW Pump Building - Columns for APP-	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for PW Pump Building - Foundation for AF	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for PW Pump Building - Slab On Grade fo	9	19-Nov-26	01-Dec-26	324	0	0	0
JDI	Review and Approval for PW Pump Building - Ground Beam for	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for PW Pump Building - Roof Beam for A	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for PW Pump Building - Roof for APP-AS-	9	15-Nov-26	26-Nov-26	328	0	0	0
JDI	Review and Approval for GLS1 Tank - Shopdrawings Plan & Sec	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for GLS2 Tank - Shopdrawings Plan & Sec	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Foundation Sl	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Columns & Ax	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Slab On Grad	9	22-Nov-26	02-Dec-26	323	0	0	0
JDI	Review and Approval for Administration Building - Grade Beam	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Roof Shop Dr	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Administration Building - Roof Beam Sl	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Foundation for A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Columns & Axis	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Grade Beam for	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Roof for APP-AS	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Chlorination Building - Roof Beam for A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDI	Review and Approval for Guard House - Foundation & Columns	9	11-Nov-26	23-Nov-26	330	0	0	0

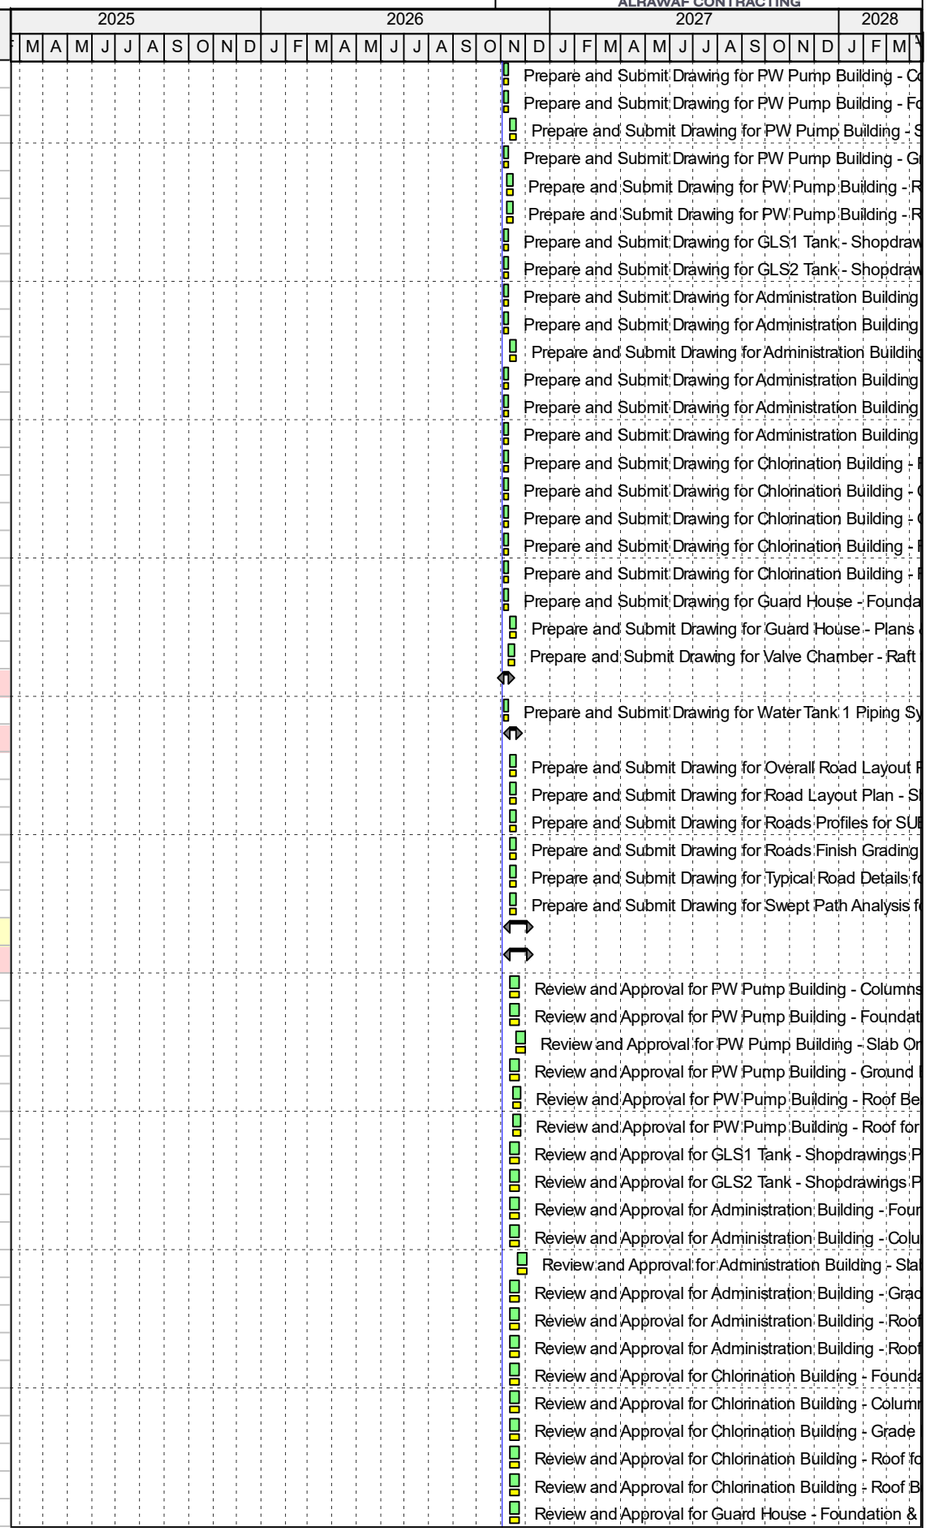

Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template -Three Weeks Lookahead

Date	Revision	Checked	Approved
02-Nov-26	Weekly Report		

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	Planned Value Cost	Earned Value Cost	Budgeted Total Cost
JDH	Review and Approval for Guard House - Plans & Sections for AF	9	22-Nov-26	02-Dec-26	323	0	0	0
JDH	Review and Approval for Valve Chamber - Raft for APP-AS-PWF	9	18-Nov-26	30-Nov-26	325	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Mechanical - MC		9	11-Nov-26	23-Nov-26	330	0	0	0
JDH	Review and Approval for Water Tank 1 Piping System for APP-A	9	11-Nov-26	23-Nov-26	330	0	0	0
JDH3-02-009-As Built Drawing Approvals - APP-Roads - RD		9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Overall Road Layout Plan for APP-AS-I	9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Road Layout Plan - Sheet 01 Of 01 for	9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Roads Profiles for APP-AS-PWPS-RD	9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Roads Finish Grading Overall Plan for /	9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Typical Road Details for APP-AS-PWPS	9	19-Nov-26	01-Dec-26	324	0	0	0
JDH	Review and Approval for Swept Path Analysis for APP-AS-PWPS	9	19-Nov-26	01-Dec-26	324	0	0	0

