Construction of a SAR Train Passenger Drop-Off Station in Sudair

محطة ركاب لسار في سدير

CLIENT	CONTRACTOR	CONSULTANT	MODON PM	SITE HANDOVER	CONTRACT COMPLETION
MODON	Technical Development Co. (TDC)	EGIS	Zyad Al Shabat	07-Apr-2026	06-Aug-2027

Scope: a passenger station for the SAR railway at Sudair Industrial City (platform, canopy, finishes and station electrical, CCTV and voice evacuation systems) with its access roads RD-01 and RD-02 and their storm water, sewer, potable water, street lighting, telecom and MV/LV networks.

Status at a glance

Progress is measured as physical % complete, weighted by budgeted man-hours. The 09-Nov-2026 report puts the project at 29.9% against 42.3% planned (SPI 0.71), behind by 12.4%. Its own previous-week column restates 02-Nov-2026 at 28.4%, so the 40.4% shown in last week's report no longer stands. The P6 update now forecasts completion on 12-Aug-2027, 6 days after the contract date.

PHYSICAL % COMPLETE
29.9% / 42.3% plan
▼ SPI 0.71 −12.4%

PROGRESS THIS WEEK
+1.46% / +2.11% plan
▼ 1.85% a week now needed

CONTRACT TIME ELAPSED
44.4% · day 216 of 486
▼ P6 finish 12-Aug-2027, 6 days late

INVOICED TO DATE (GROSS)
13.0% · 4.29M SAR
3 invoices, none approved or paid

P6 now finishes the project 6 days after the contract date.

The 09-Nov-2026 P6 update moves the project finish from 06-Aug-2027 to 12-Aug-2027 (total float −6 days). Kerbstone and asphalt deliveries, the telecom and LV cable trenches, street-lighting poles and the road finishing works (curbstone, interlock, markings) are on the negative-float path. This week earned 1.46% against 2.11% planned, below the 1.85% a week now needed to finish on 06-Aug-2027. Procurement is at 25.3% against 83.3% planned and the station package has not started.


Site photos this week

The six photos from the Weekly Photos sheet of the 09-Nov-2026 weekly report, with the report's own titles. They carry no date or GPS stamp. Select a photo to view it larger, then use the arrows to move between photos.



Base course laying, Road 1

Paver laying the base course layer on Road 1.

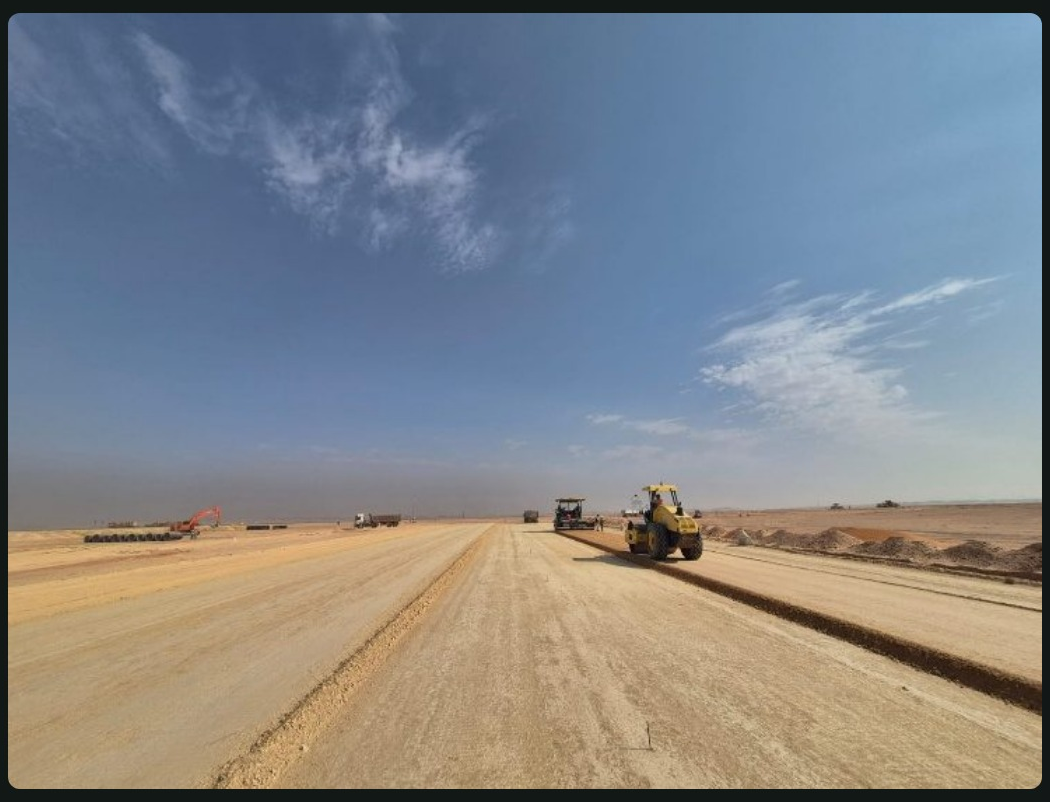

Base course compaction, Road 1

Roller compacting the base course layer on Road 1.



Base course grading, Road 1

Grader levelling the surface for the base course on Road 1.



Aggregate base course, Road 1

Laying and compacting the aggregate base course on Road 1.



Subgrade second layer, Road 1

Grading the second subgrade layer on Road 1.




Subgrade second layer, Road 2

Grading the second subgrade layer on Road 2.

Progress S-curve

Cumulative physical progress (man-hour weighted), monthly. Source: Physical-Chart Data sheet.

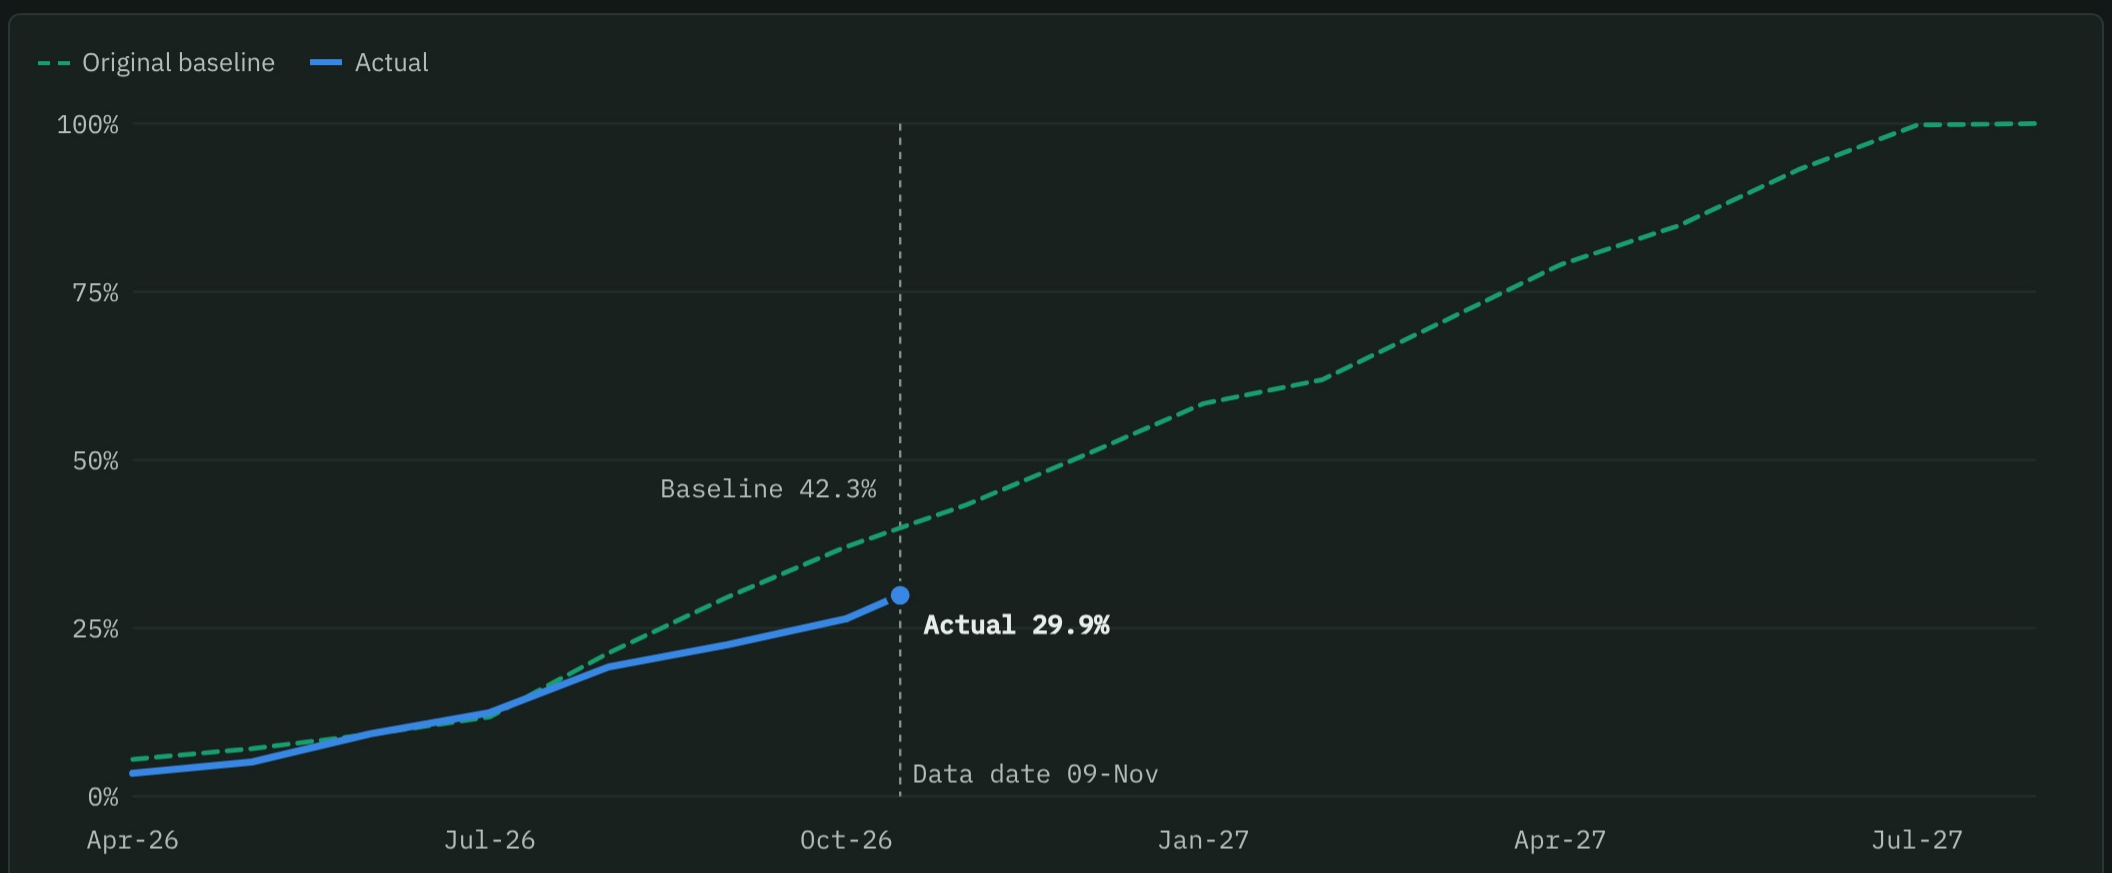

WEEK ENDING	PLANNED %	ACTUAL %	VARIANCE	GAINED THIS WEEK	SPI
05-Oct-2026	33.9	24.4	−9.5	+1.1	0.72
12-Oct-2026	36.2	24.8	−11.4	+0.4	0.69
19-Oct-2026	38.1	26.1	−12.0	+1.3	0.69
26-Oct-2026	40.0	27.3	−12.7	+1.2	0.68
02-Nov-2026	40.1*	28.4*	−11.7	+2.0	0.71
09-Nov-2026	**42.3***	**29.9***	**−12.4**	**+1.5**	**0.71**

05-Oct to 26-Oct come from those weeks' reports (budget 638,468 man-hours). * 02-Nov is the previous-week column of this week's report and 09-Nov this week's figure (budget 659,762 man-hours). Gained this week is the man-hours earned that week divided by that week's budget. The S-curve uses this week's chart sheet, on the 659,762 budget, with monthly points on the 26th.

Progress by phase


Physical progress to date by WBS, weighted by budgeted man-hours. Source: Progress sheet, 09-Nov-2026.

PHASE	WEIGHT	PLANNED	ACTUAL	VARIANCE	SPI	STATUS
Mobilisation	3%	100.0%	100.0%	0.0	1.00	✓ Complete
Engineering	5%	100.0%	95.0%	−5.0	0.95	▼ Behind
Procurement	14%	83.3%	25.3%	−57.9	0.30	▼ Far behind
Construction	75%	30.1%	24.8%	−5.4	0.82	▼ Behind
· Package 1: roads and utilities	53.9%	38.3%	34.5%	−3.8	0.90	▼ Behind
· · Street lighting network	7.7%	37.3%	15.6%	−21.7	0.42	▼ Far behind
· · Telecommunications	2.2%	45.5%	29.1%	−16.4	0.64	▼ Far behind
· Package 3: station (platform, canopy, systems)	21.1%	9.3%	0.0%	−9.3	0.00	▼ Not started
Testing & commissioning	2%	0.0%	0.0%	0.0	–	● Not yet due
Close-out	1%	0.0%	0.0%	0.0	–	● Not yet due
Total	100%	**42.3%**	**29.9%**	**−12.4**	**0.71**	▼ Behind

Road Works 1 is at 44.6% against 44.9% planned (SPI 0.99). The P6 update (data date 09-Nov-2026) has 855 activities: 268 completed, 95 in progress and 492 not started. Its scheduled finish is 12-Aug-2027, 6 days after the contract date.

Scope of work: quantities

Major BOQ quantities from the Major Quantities sheet of the 09-Nov-2026 weekly report: total, finished to date and remaining. "This week" is the change since the 26-Oct-2026 report, the last earlier weekly report on file.

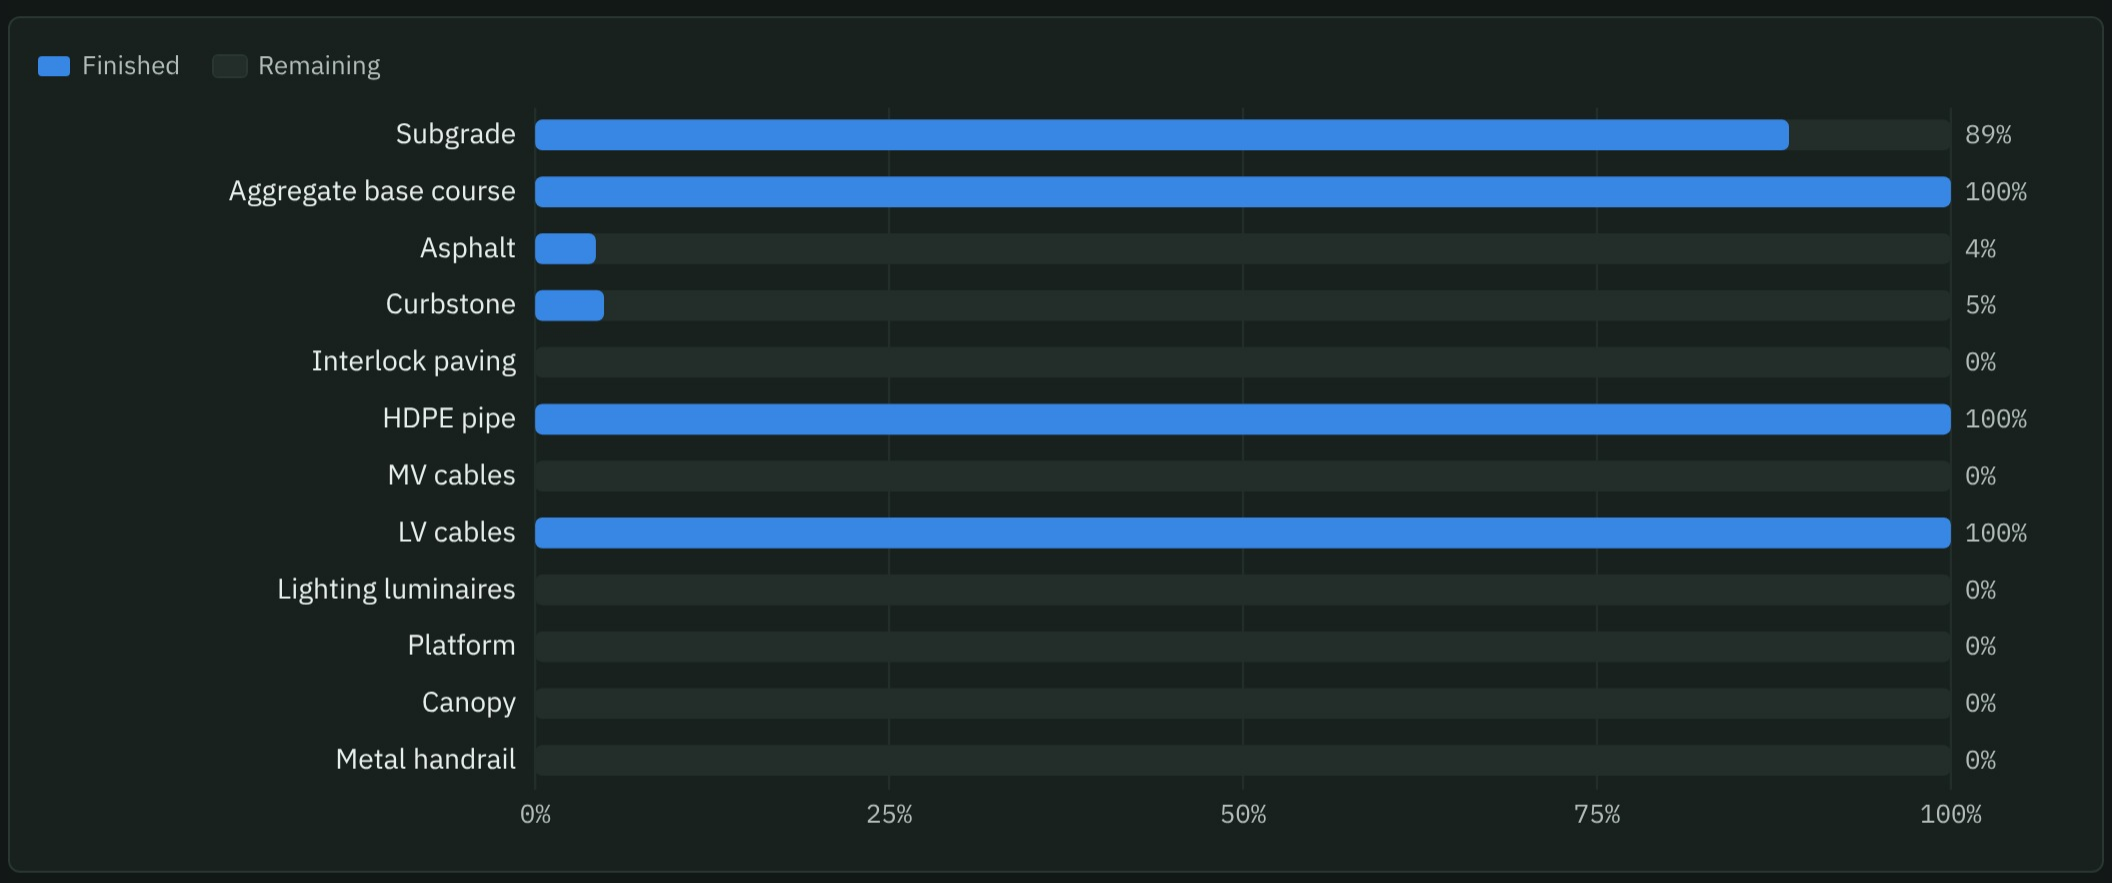

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Subgrade	B1.32 11 13.01	m³	20,530	18,182	0	2,348	88.6%
Aggregate base course	B1.32 11 23.01	m³	13,485	13,485	−7,974	0	100.0%
Asphalt	B1.32 12 16.01	m³	13,360	573	0	12,787	4.3%
Curbstone	B1.32 16 13.23.01	m²	20,555	1,000	+718	19,555	4.9%

SCOPE ITEM	BOQ NO.	UNIT	TOTAL	FINISHED	THIS WEEK	REMAINING	% FINISHED
Interlock paving	B1.32 14 13.13.01	m²	27,900	0	0	27,900	0.0%
HDPE pipe	B4.33 31 23.01	LM	5,808	5,808	0	0	100.0%
MV cables	B2.31 23 00.01	LM	7,120	0	0	7,120	0.0%
LV cables	B2.33 71 00 02.01	LM	7,500	7,500	0	0	100.0%
Lighting luminaires	B2.26 56 19.01	EA	116	0	0	116	0.0%
Platform	03 00 00	m²	4,000	0	0	4,000	0.0%
Canopy	31 00 00	LM	4,000	0	0	4,000	0.0%
Metal handrail	B4.05 52 00.01	LM	440	0	0	440	0.0%

Station works not started

Platform (4,000 m²), canopy (4,000 m), metal handrail (440 m) and lighting luminaires (116) are all at 0%. The platform and canopy wait for the SAR fence permission and the client's design.

Figures to check

Curbstone rose by 718 m² to 1,000 m², although no kerbstone installation activity has started in P6. Aggregate base course was corrected from 21,459 m³ (of 16,376 m³) to 13,485 m³ of 13,485 m³, so it now reads 100% finished, while P6 started another base course activity on 08-Nov-2026. Subgrade, asphalt, HDPE pipe and LV cables are unchanged.

Milestones

The weekly report and the P6 schedule update give different forecasts for several milestones. Both are shown so the difference can be resolved with the contractor.

MILESTONE	BASELINE	WEEKLY REPORT FORECAST	P6 UPDATE FORECAST	P6 FLOAT (DAYS)	STATUS
Project start	07-Apr-2026	07-Apr-2026	07-Apr-2026 (actual)	–	✓ Done
Mobilisation finish	06-May-2026	06-May-2026	06-May-2026 (actual)	–	✓ Done
Work plan and baseline submission	06-May-2026	16-Aug-2026 (+102 d)	15-Aug-2026 (actual)	–	✓ Done late
Engineering phase finish	06-May-2026	21-Sep-2026 (+138 d)	10-Nov-2026	52	▼ Late
Road and paving works	06-Dec-2026	31-Dec-2026 (+25 d)	10-Feb-2027	−1	▼ Late
Procurement phase finish	15-Apr-2027	09-Jun-2027 (+55 d)	30-Mar-2027	46	? Forecasts differ
MV works	12-May-2027	05-May-2027	09-Jun-2027	0	▼ Late in P6
Site and platform works	20-Jul-2027	05-Aug-2027 (+16 d)	01-May-2027	78	? Forecasts differ
Finishing and general site works	20-Jul-2027	06-Aug-2027 (+17 d)	12-Aug-2027	−6	▼ Late
Project finish	06-Aug-2027	06-Aug-2027	12-Aug-2027	−6	▼ 6 days late in P6

P6 misses the contract finish by 6 days, while the weekly report still forecasts 06-Aug-2027.

A week ago P6 finished on the contract date with no float. It now has the project finish on 12-Aug-2027, road and paving works on 10-Feb-2027 (against 31-Dec-2026 in the weekly report) and MV works on 09-Jun-2027 with no float (against 05-May-2027). P6 still completes site and platform works on 01-May-2027 with 78 days of float, although platform work has not started and is waiting for the SAR fence permission. The engineering phase, forecast for 21-Sep-2026 in the weekly report, is still open in P6.

Procurement of key materials

Share of the required quantity delivered, from the Completion Rate column. Source: Procurement sheet, weekly report 09-Nov-2026, unchanged from 26-Oct-2026.



Eight long-lead items not yet submitted


Metal railing, canopy, MV duct banks, MV cables, substations, lighting poles, street-lighting luminaires and outdoor lighting fixtures are all marked "Not submitted". The required PO dates for the railing (25-Aug-2026), the MV duct banks and cables (12-Oct-2026) and the substations (19-Oct-2026) have passed; those for the street-lighting luminaires (10-Nov-2026), canopy (19-Nov-2026) and outdoor fixtures (23-Nov-2026) fall within two weeks.

Deliveries on the critical path

P6 puts the kerbstone delivery (−6 days of float) and the asphalt delivery (−5 days) on the path that now delays the finish. Interlock, waterproofing, the LV distribution panel, street-lighting feeder panels, CCTV, voice evacuation, manhole covers and valves have no delivery figure yet. The summary counts 22 of 27 purchase orders issued.

Manpower

Monthly head count on site, planned vs actual. Source: Manpower sheet.

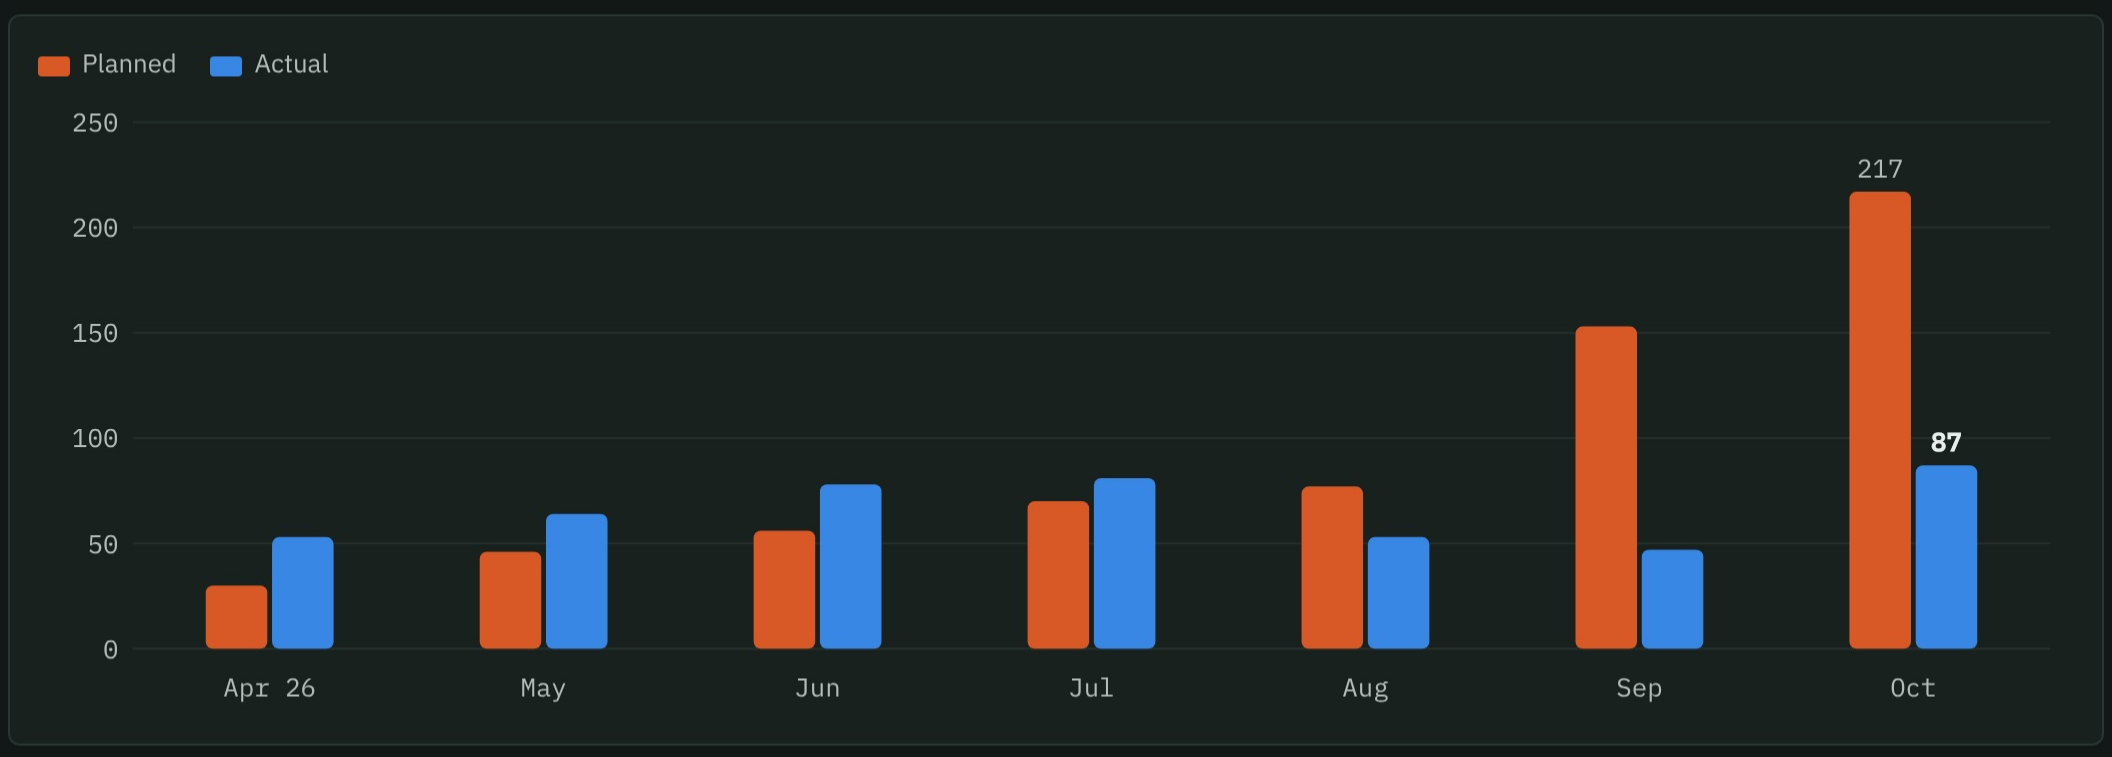

Manual and non-manual head count combined. October is 87 against 217 planned (−60%). The November column repeats October's 87 (65 manual, 22 non-manual) against 232 planned, so November is not shown. The plan peaks at 263 in December 2026.

Cost and invoicing

Contract value

Original contract value	33,090,825
Change orders	0
Estimate at completion	33,090,825

All values in SAR. The change order log has no entries. The BOQ total on the Progress sheet is 33,090,852, 27 SAR more than the contract value.

Invoices

Invoices submitted	3
Gross value	4,289,046
VAT	643,357
Deductions and penalties	8,000
Net incl. VAT	4,924,402
PM-approved / paid	0 / 0

Invoicing is 13.0% of the contract value against 29.9% physical progress. Invoice 3 (1,240,646 SAR gross, 31-Aug-2026 to 28-Oct-2026) is new since the 26-Oct-2026 report. None of the three invoices is yet approved by the PM or paid.

Health, safety and quality

Safety Score 0.83

Safe man-hours (cumulative)	92,590
Man-hours this week	5,220
Internal trainings (cumulative)	25
Toolbox talks (cumulative)	23
HSE observations logged / open	21 / 0

Quality Score 0.89

FIRs issued / closed / pending	194 / 183 / 11
MIRs issued / closed	17 / 16
NCRs issued / closed	4 / 4
Site instructions	0
Shop drawings submitted (of 229)	229
Material submittals (of 46)	46

Since the 26-Oct-2026 report, 37 FIRs and 2 MIRs were added. Shop drawings: 174 approved (A), 42 approved as noted (B) and 13 C. Material submittals: 1 A, 42 B and 3 C.

Open issues and risks

ISSUE	OWNER	DETAIL
Finish date slipping	Contractor	P6 forecasts completion on 12-Aug-2027, 6 days late. The telecom and LV cable trenches, street-lighting poles, kerbstone and asphalt deliveries and the road finishing works carry negative float.
SAR fence permission	MODON / SAR	Permission to work inside the platform area is still pending, so the platform and canopy works cannot start. Rated very high (5 × 5) in the risk register, open since 16-Sep-2026.
Canopy and platform design	MODON (client)	The client has not yet issued the canopy and platform design, so the related shop drawings, procurement and construction cannot be finalised. Rated very high (5 × 5); value 9,867,379 SAR.
MV duct crossings	MODON (client)	Client approval of the proposed MV duct crossings is pending, and MV cable installation depends on it. Rated high (4 × 4). The MV works milestone now has no float in P6.
Long-lead procurement	Contractor	Eight long-lead items are not yet submitted for approval, several past their required PO dates. Procurement is at 25.3% against 83.3% planned.
Progress reporting	Contractor / Consultant	The 40.4% reported for 02-Nov-2026 has been replaced by 28.4% without explanation. The consultant should confirm the progress basis and approve the 659,762 man-hour budget.

The issue log lists 21 HSE observations from 02-Sep-2026 to 06-Nov-2026, all closed; two were added this week. Two older risks, the SAR permit for the geotechnical report and the platform tender drawing, are marked closed.

Data notes

- The previous week folder (05-Nov-2026) holds only a P6 update and a look-ahead plan, no weekly report. Weekly-report values are therefore compared with the 26-Oct-2026 report (29-Oct-2026 folder) and with this report's own previous-week columns; P6 values are compared with the 01-Nov-2026 update.
- Last week's report showed 40.4% for 02-Nov-2026, from a weekly report that is not in the previous week folder. This week's file gives 02-Nov-2026 as 28.4% (187,466 of 659,762 man-hours), and Road Works 1 earned man-hours are 80,414 instead of the 161,207 quoted last week. The change is not explained.
- The man-hour budget is 659,762, against 638,468 in the 26-Oct-2026 report. The Physical-Chart Data sheet now uses it too, and its October actual is back to 174,265 man-hours.
- The chart sheet's Achieved % for April and May (4.24% and 8.17%) does not match its own man-hours (3.42% and 5.09%). The S-curve uses the man-hours.
- Procurement earned man-hours rose from 17,130 (26-Oct-2026) to 23,398, all of it in the week to 02-Nov-2026; none was earned this week.
- Major Quantities: the aggregate base course total changed from 16,375.94 to 13,485 m³ and the finished quantity from 21,459.19 to 13,485 m³, while two helper columns still show 9,875.94 and 21,459.19. Curbstone is in m² there but in m on the Procurement sheet, and the Procurement sheet gives kerbstone a completion rate of 1.4 (140%). The asphalt total is 13,360 m³ there but 3,420 m³ on the Procurement sheet.
- The cover sheet's headline "Earn Value" and its SPI are cost-based (BOQ value), not physical progress, and are not used in this report.
- The weekly report gives forecast completion 06-Aug-2027 with zero variance, while the P6 update of the same date finishes on 12-Aug-2027. The cover sheet still gives "Revised Completion" as 07-Apr-2026, the site handover date.
- MV works baseline: 12-May-2027 on the Milestones sheet but 22-May-2027 on the cover sheet.
- The FIR summary lists FIRs only up to 02-Nov-2026 (FIR-0176), although the FIR count rose to 194.
- P6 gives activity SDR-ST-CON-P1-3300 (200 mm GRP pipe laying) an actual finish of 14-Nov-2026, after its 09-Nov-2026 data date.
- Manpower: the October plan is 217 in the monthly histogram but 60 in the weekly summary panel, and the November actual repeats October.
- The HSE inspection sheet and the FIR summary still carry project ID SUD1-02-011, and the Conclusion sheet describes a different project. The risk register still describes the project as ahead of schedule, and risks 3120-4 and 3120-5 are marked Open in one column and Close in another.

Compiled 10-Nov-2026 from the weekly report and the P6 update (both data date 09-Nov-2026) uploaded for week 31, compared with the 26-Oct-2026 report and the 01-Nov-2026 P6 update.
