
Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Total Float	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
28-09-2026		914d	16-Mar-25	15-Mar-28	16-Mar-25 A	15-Mar-28	55.04%	58.28%	0d	560,000,000	308,200,422	326,367,462
JDH3-02-009-Contractual Milestones		914d	16-Mar-25	15-Mar-28	16-Mar-25 A	15-Mar-28	0%	0%	0d	0	0	0
JDH3-02-009-Mobilization - Mob		71d	16-Mar-25	05-Jun-25	16-Mar-25 A	08-Jun-25 A	0%	0%		0	0	0
JDH3-02-009-Authorities Permits & Approval - AT		243d	15-Oct-25	16-Jul-26	15-Oct-25 A	20-Sep-26 A	0%	0%		0	0	0
JDH3-02-009-Al-Khorayef Factory Road		683d	05-Apr-25	06-May-27	05-Apr-25 A	03-Jul-27	59.83%	59.05%	214d	6,788,542	4,053,987	4,001,270
JDH3-02-009-New Roads - NR		510d	02-Jul-25	16-Mar-27	02-Jul-25 A	28-Feb-27	74.55%	65.01%	314d	16,300,167	12,152,417	10,597,408
JDH3-02-009-Infrastructure Networks		815d	16-Mar-25	14-Feb-28	16-Mar-25 A	13-Oct-27	76.35%	73.58%	127d	348,958,591	266,454,196	256,785,773
JDH3-02-009-New Scope - R.BOQ. NO03		457d	21-Apr-26	13-Mar-28	21-Apr-26 A	20-Oct-27	2.6%	27.4%	121d	56,640,099	1,471,317	15,516,564
JDH3-02-009-Linking Road between CMZ and Jeddah-		520d	04-May-25	14-Nov-26	04-May-25 A	13-Jan-27	100%	81.21%	352d	4,118,894	4,118,893	3,345,143
JDH3-02-009-Lift Station 01		900d	16-Mar-25	02-Mar-28	16-Mar-25 A	23-Feb-28	8.08%	29.77%	14d	11,664,038	942,103	3,472,719
JDH3-02-009-Lift Station 02		782d	03-May-25	01-Dec-27	03-May-25 A	24-Nov-27	15.46%	33.38%	91d	13,017,026	2,013,083	4,344,597
JDH3-02-009-Lift Station 03		614d	03-May-25	13-Mar-28	03-May-25 A	06-May-27	8.64%	14.05%	259d	7,778,233	672,024	1,092,577
JDH3-02-009-Mosque		733d	04-May-25	05-Dec-27	04-May-25 A	29-Sep-27	24.99%	30.75%	139d	5,867,246	1,466,040	1,804,056
JDH3-02-009-TSE Pump Station		864d	04-May-25	15-Mar-28	04-May-25 A	06-Mar-28	6.16%	20.87%	8d	21,924,870	1,351,437	4,576,037
Milestone		864d	04-May-25	15-Mar-28	04-May-25 A	06-Mar-28	0%	0%	8d	0	0	0
Engineering		644d	04-May-25	29-Jun-27	04-May-25 A	19-Oct-26	97.83%	100%	426d	657,746	643,464	657,746
Procurement		345d	03-Jan-26	07-Aug-27	03-Jan-26 A	17-Feb-27	13.89%	43.06%	322d	4,122,017	572,502	1,774,757
Authorities Permits & Approval		9d	23-Jun-26	09-Jul-26	29-Sep-26	11-Oct-26	0%	0%	245d	0	0	0
Construction		586d	31-Mar-26	04-Mar-28	31-Mar-26 A	04-Mar-28	0.91%	14.34%	10d	14,952,627	135,471	2,143,533
JDH3-02-009 -SITE WORK		579d	31-Mar-26	07-Feb-28	31-Mar-26 A	19-Feb-28	3.96%	6.54%	8d	3,004,460	118,947	196,497
JDH3-02-009-B15-Site Works		579d	31-Mar-26	07-Feb-28	31-Mar-26 A	19-Feb-28	11.8%	11.8%	8d	1,007,722	118,947	118,947
JDH3-02-009-B15-Mechanical Works-phase 1		276d	13-Jul-27	17-Jan-28	15-Sep-26 A	04-Oct-27	0%	4.96%	124d	1,564,873	0	77,551
JDH3-02-009-B15-Fuel Tank		19d	04-Oct-27	25-Oct-27	07-Nov-26	28-Nov-26	0%	0%	314d	93,487	0	0
JDH3-02-009-B15-Chlorination Piping Network		18d	28-Dec-27	17-Jan-28	10-Aug-27	30-Aug-27	0%	0%	153d	40,647	0	0
JDH3-02-009-B15-Drainage Holder Tank		11d	13-Jul-27	25-Jul-27	12-Jul-27	24-Jul-27	0%	0%	8d	7,650	0	0
JDH3-02-009-B15-Water Tank (GRP Tank)		6d	11-Aug-27	17-Aug-27	10-Aug-27	16-Aug-27	0%	0%	8d	5,284	0	0
JDH3-02-009-B15-Potable water System		12d	14-Aug-27	26-Aug-27	12-Aug-27	25-Aug-27	0%	0%	17d	12,194	0	0
JDH3-02-009-B15-Site Interconnecting Pipes 200mm		16d	18-Aug-27	09-Sep-27	15-Sep-26 A	04-Sep-27	0%	26.86%	31d	76,172	0	20,463
JDH3CTSEPE	Excavation Works for Ductile Iron Pipe 2(	2d	18-Aug-27	19-Aug-27	15-Sep-26 A	18-Aug-27	0%	70%	31d	7,308	0	5,116
JDH3CTSEPE	Soil Replacement and Bedding for Ductil	2d	21-Aug-27	22-Aug-27	16-Sep-26 A	18-Aug-27	0%	70%	31d	1,827	0	1,279
JDH3CTSEPE	Pipe.Installation for Ductile Iron Pipe 20(	8d	23-Aug-27	31-Aug-27	17-Sep-26 A	18-Aug-27	0%	70%	31d	20,098	0	14,068
JDH3CTSEPE	Fitting.Installation for Ductile Iron Pipe 2(	8d	23-Aug-27	31-Aug-27	16-Aug-27	25-Aug-27	0%	0%	31d	33,777	0	0
JDH3CTSEPE	Valves.Installation for Ductile Iron Pipe 2(	4d	01-Sep-27	05-Sep-27	25-Aug-27	30-Aug-27	0%	0%	31d	5,853	0	0
JDH3CTSEPE	Primary Test for Ductile Iron Pipe 200 mr	2d	06-Sep-27	07-Sep-27	30-Aug-27	01-Sep-27	0%	0%	31d	3,654	0	0
JDH3CTSEPE	Backfilling and warning tapefor Ductile Ir(	2d	08-Sep-27	09-Sep-27	01-Sep-27	04-Sep-27	0%	0%	31d	3,654	0	0
JDH3-02-009-B15-Site Interconnecting Pipes 400 mm		29d	18-Aug-27	21-Sep-27	15-Sep-26 A	20-Sep-27	0%	30.22%	17d	188,926	0	57,087
JDH3-02-009-B15-Site Interconnecting Pipes 500 mm		41d	18-Aug-27	05-Oct-27	17-Aug-27	04-Oct-27	0%	0%	8d	253,456	0	0
JDH3-02-009-B15-Site Interconnecting Pipes 600 mm		41d	18-Aug-27	05-Oct-27	17-Aug-27	04-Oct-27	0%	0%	8d	224,516	0	0
JDH3-02-009-B15-Interface and Connection Works		25d	28-Aug-27	26-Sep-27	26-Aug-27	25-Sep-27	0%	0%	8d	662,541	0	0
JDH3-02-009-B15-Electrical Works for TSE Water Pump Sta		121d	22-Sep-27	29-Jan-28	21-Sep-27	09-Feb-28	0%	0%	8d	431,866	0	0
JDH3-02-009 -PUMP STATION		511d	10-Dec-26	04-Mar-28	30-Jun-26 A	04-Mar-28	0%	2%	10d	6,410,316	0	128,208
JDH3-02-009 -GUARD HOUSE		121d	29-Apr-27	21-Sep-27	27-Apr-27	19-Sep-27	0%	0%	130d	102,908	0	0
JDH3-02-009 -ADMIN BUILDING		195d	02-May-27	22-Nov-27	30-Jun-26 A	07-Mar-27	0%	5.39%	233d	546,419	0	29,447
JDH3-02-009 -TSE STO RAGE TANK		287d	05-May-26	11-May-27	05-May-26 A	17-Nov-26	0.48%	51.24%	384d	3,454,374	16,524	1,769,976
JDH3-02-009 -CHLORINATION BUILDING		265d	27-Jul-27	24-Jan-28	30-Jun-26 A	04-May-27	0%	3.84%	233d	505,030	0	19,404
JDH3-02-009 -SEC ROOM		47d	29-Jul-27	09-Nov-27	20-Oct-26	13-Dec-26	0%	0%	344d	929,120	0	0
Close Out		436d	17-Jan-27	15-Mar-28	29-Sep-26	06-Mar-28	0%	0%	8d	2,192,481	0	0

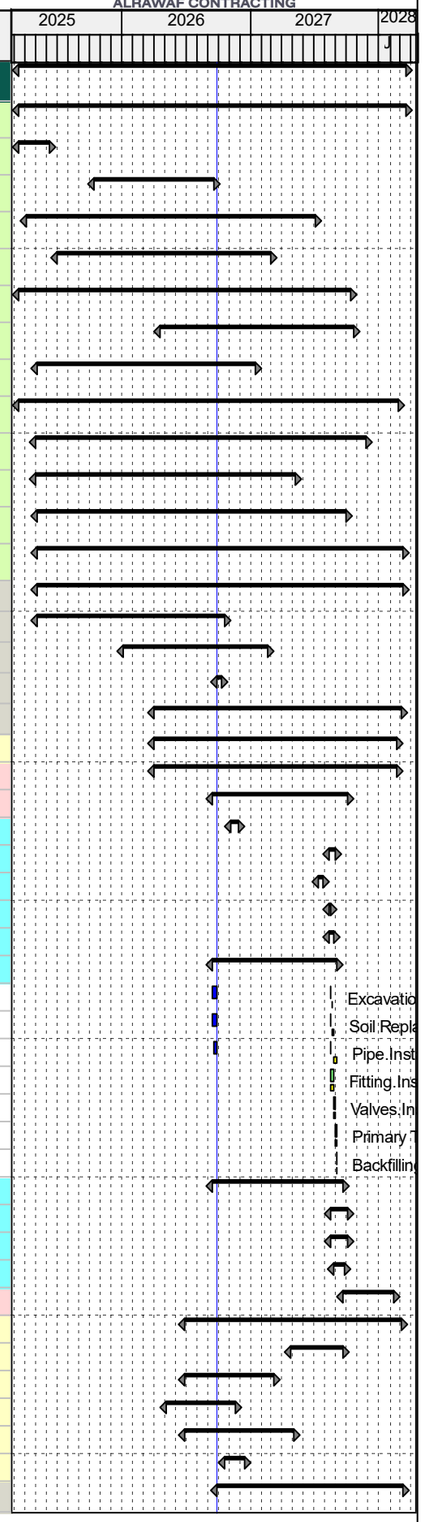


Actual Level of Effort
Actual Work
Remaining Work
Primary Baseline
Critical Remaining Work
Milestone

EGIS Template-Progress Certificate Mod_1

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		

28-09-2026

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete	Total Float	Budgeted Total Cost	Planned Value Cost	Earned Value Cost
JDH3-02-009-PW Pump Station		899d	16-Mar-25	08-Mar-28	16-Mar-25 A	21-Feb-28	21.84%	32.76%	15d	61,830,929	13,504,925	20,258,733
Provisional Sum		1d	15-Mar-28	15-Mar-28	25-Aug-26 A	15-Mar-28	0%	11.2%	0d	5,111,365	0	572,584
JDH3-02-009-Close Out		12d	07-Feb-28	13-Feb-28	21-Oct-27	03-Nov-27	0%	0%	109d	0	0	0



Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

EGIS Template-Progress Certificate Mod_1

Date	Revision	Checked	Approved
28-Sep-26	Weekly Report		
