
Development of the Technology City in Dammam -Upda
10-11-2026

WBS Summary Schedule

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Performance % Complete
Development of the Technology City in Dammam -Update 10-11-2		438	23-Dec-25	24-Feb-27	23-Dec-25 A	21-Jun-27	39.21%
Key Milestones		438	23-Dec-25	24-Feb-27	23-Dec-25 A	21-Jun-27	0%
Preliminaries and Mobilization Works		30	23-Dec-25	27-Jan-26	23-Dec-25 A	26-Jan-26 A	0%
Engineering Works		239	06-Jan-26	14-Jul-26	06-Jan-26 A	20-Aug-26 A	0%
Procurement Cycle		377	28-Jan-26	28-Jan-27	28-Jan-26 A	11-May-27	0%
Construction Works		366	07-Mar-26	23-Feb-27	07-Mar-26 A	05-Jun-27	39.21%
Testing and Comissioning		171	04-Jan-27	21-Feb-27	08-Nov-26	12-Jun-27	0%
Handing over and close out		179	04-Jan-27	24-Feb-27	08-Nov-26	21-Jun-27	0%

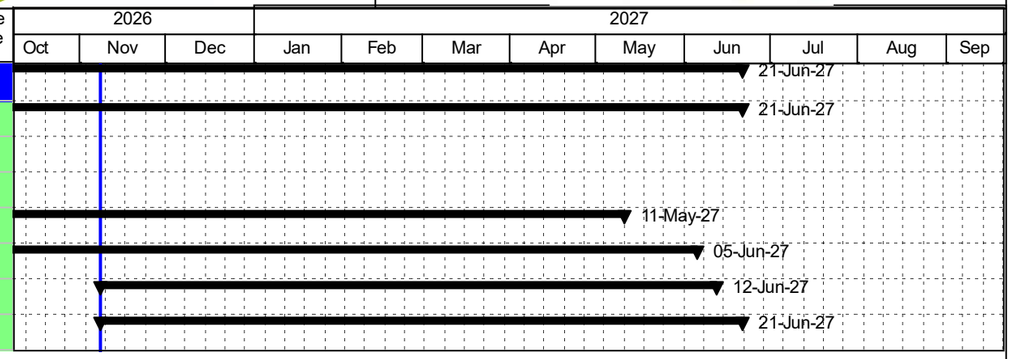

Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
10-Nov-26	Third Industrial City		
