
Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Project:PASSENGER STATION FOR SAR RAILWAY - PACKAGE 1 SUDAIR- Update 12/10/2026.....		205	07-Jul-26	09-Feb-27	03-Aug-26 A	16-Nov-26	8.52%	26.72%
Construction		205	07-Jul-26	09-Feb-27	03-Aug-26	16-Nov-26	8.52%	26.72%
Package-1		205	03-Aug-26	09-Feb-27	03-Aug-26	16-Nov-26	6.54%	27.3%
ROAD WORKS 1		167	13-Oct-26	01-Dec-26	07-Sep-26	16-Nov-26	0%	24.21%
ROAD - 01		161	13-Oct-26	01-Dec-26	10-Sep-26	15-Nov-26	0%	23.18%
ROAD-01 From 0 to 470 m (3)		21	05-Nov-26	29-Nov-26	11-Oct-26 A	04-Nov-26	0%	39.13%
Asphalt Works		6	21-Nov-26	29-Nov-26	11-Oct-26 A	18-Oct-26	0%	50%
Bituminous base course		6	21-Nov-26	29-Nov-26	11-Oct-26 A	18-Oct-26	0%	50%
SDR-ST-CON-P1-4410	Bituminous base course (Grading I - Class A 1st Layer with MC-01	6	21-Nov-26	29-Nov-26	11-Oct-26 A	18-Oct-26	0%	50%
Kerbstone Installation		21	05-Nov-26	29-Nov-26	12-Oct-26	04-Nov-26	0%	0%
SDR-ST-CON-P1-3860	Precast Concrete Curbstone, Type A2	21	05-Nov-26	29-Nov-26	12-Oct-26	04-Nov-26	0%	0%
ROAD-01 From 470 to 1125 m (6)		20	09-Nov-26	01-Dec-26	08-Oct-26 A	03-Nov-26	0%	10.41%
Base Course		10	09-Nov-26	21-Nov-26	08-Oct-26 A	22-Oct-26	0%	50%
SDR-ST-CON-P1-3720	Aggregate base course layer	10	09-Nov-26	21-Nov-26	08-Oct-26 A	22-Oct-26	0%	50%
Asphalt Works		6	22-Nov-26	28-Nov-26	24-Oct-26	29-Oct-26	0%	0%
Bituminous base course		6	22-Nov-26	28-Nov-26	24-Oct-26	29-Oct-26	0%	0%
SDR-ST-CON-P1-4430	Bituminous base course (Grading I - Class A 1st Layer with MC-01	6	22-Nov-26	28-Nov-26	24-Oct-26	29-Oct-26	0%	0%
Kerbstone Installation		20	09-Nov-26	01-Dec-26	12-Oct-26	03-Nov-26	0%	0%
SDR-ST-CON-P1-3730	Precast Concrete Curbstone, Type A2	20	09-Nov-26	01-Dec-26	12-Oct-26	03-Nov-26	0%	0%
ROAD-01 From 1125 to 1765 m (7)		151	13-Oct-26	22-Nov-26	10-Sep-26	15-Nov-26	0%	23.44%
Subgrade		10	13-Oct-26	29-Oct-26	10-Sep-26	22-Oct-26	0%	75%
SDR-ST-CON-P1-3600	Subgrade layer works	10	13-Oct-26	29-Oct-26	10-Sep-26	22-Oct-26	0%	75%
Base Course		9	31-Oct-26	16-Nov-26	24-Oct-26	02-Nov-26	0%	0%
SDR-ST-CON-P1-4220	Aggregate base course layer	9	31-Oct-26	16-Nov-26	24-Oct-26	02-Nov-26	0%	0%
Kerbstone Installation		20	31-Oct-26	22-Nov-26	24-Oct-26	15-Nov-26	0%	0%
SDR-ST-CON-P1-4230	Precast Concrete Curbstone, Type A2	20	31-Oct-26	22-Nov-26	24-Oct-26	15-Nov-26	0%	0%
ROAD - 02		159	15-Oct-26	26-Nov-26	07-Sep-26	16-Nov-26	0%	27.33%
ROAD-01 From 0 to 400 m (9)		13	15-Oct-26	29-Oct-26	07-Sep-26	26-Oct-26	0%	75%
Subgrade		13	15-Oct-26	29-Oct-26	07-Sep-26	26-Oct-26	0%	75%
SDR-ST-CON-P1-3390	Subgrade layer works	13	15-Oct-26	29-Oct-26	07-Sep-26	26-Oct-26	0%	75%
ROAD-01 From 400 to 900 m (10)		156	19-Oct-26	26-Nov-26	07-Sep-26	16-Nov-26	0%	15.62%
Subgrade		11	19-Oct-26	03-Nov-26	07-Sep-26	24-Oct-26	0%	50%
SDR-ST-CON-P1-3540	Subgrade layer works	11	19-Oct-26	03-Nov-26	07-Sep-26	24-Oct-26	0%	50%
Base Course		10	04-Nov-26	19-Nov-26	25-Oct-26	04-Nov-26	0%	0%
SDR-ST-CON-P1-4130	Aggregate base course layer	10	04-Nov-26	19-Nov-26	25-Oct-26	04-Nov-26	0%	0%
Kerbstone Installation		20	04-Nov-26	26-Nov-26	25-Oct-26	16-Nov-26	0%	0%
SDR-ST-CON-P1-4140	Precast Concrete Curbstone, Type A2	20	04-Nov-26	26-Nov-26	25-Oct-26	16-Nov-26	0%	0%
ROAD-01 From 900 to 1239 m (11)		155	18-Oct-26	09-Nov-26	07-Sep-26	28-Oct-26	0%	22.68%
Subgrade		8	18-Oct-26	29-Oct-26	07-Sep-26	20-Oct-26	0%	50%
SDR-ST-CON-P1-3740	Subgrade layer works	8	18-Oct-26	29-Oct-26	07-Sep-26	20-Oct-26	0%	50%
Base Course		7	31-Oct-26	09-Nov-26	21-Oct-26	28-Oct-26	0%	0%
SDR-ST-CON-P1-4290	Aggregate base course layer	7	31-Oct-26	09-Nov-26	21-Oct-26	28-Oct-26	0%	0%
ELECTRICAL WORKS		133	03-Aug-26	11-Nov-26	03-Aug-26	12-Nov-26	72.8%	4.06%
MV Network		28	28-Sep-26	29-Oct-26	12-Oct-26	12-Nov-26	40.53%	0%
ROAD - 01		28	28-Sep-26	29-Oct-26	12-Oct-26	12-Nov-26	40.53%	0%
ROAD-01 From 1125 to 1765 m (7)		21	28-Sep-26	21-Oct-26	12-Oct-26	04-Nov-26	57.14%	0%

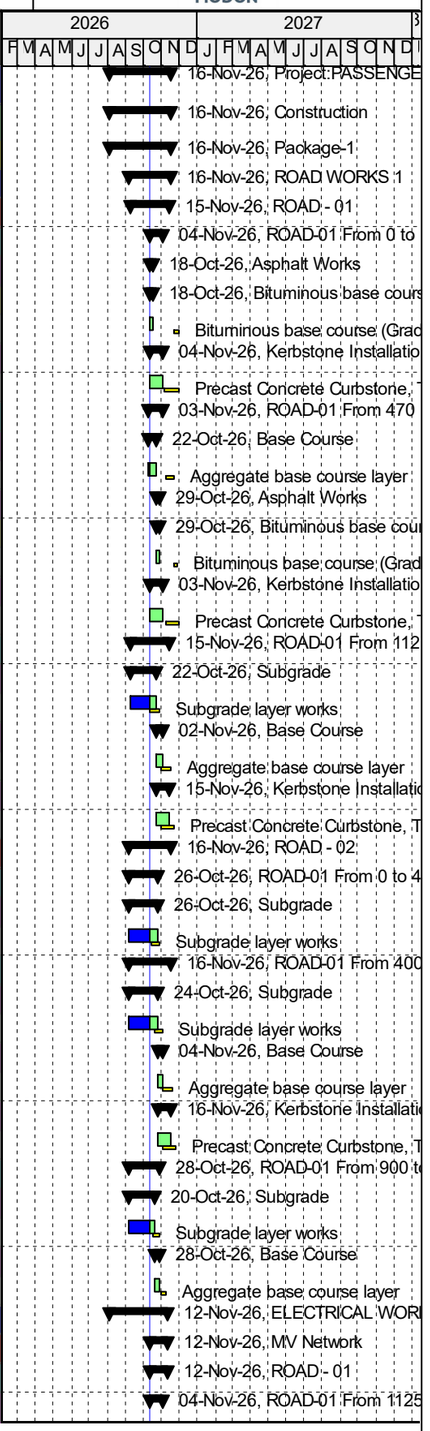

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	28-Sep-26	21-Oct-26	12-Oct-26	04-Nov-26	57.14%	0%
SDR-ST-CON-P1-1570	Excavation Works Part 1	21	28-Sep-26	21-Oct-26	12-Oct-26	04-Nov-26	57.14%	0%
ROAD-01 From 470 to 1125 m (6)		21	06-Oct-26	29-Oct-26	20-Oct-26	12-Nov-26	23.92%	0%
Excavation		21	06-Oct-26	29-Oct-26	20-Oct-26	12-Nov-26	23.92%	0%
SDR-ST-CON-P1-1720	Excavation Works Part 1	21	06-Oct-26	29-Oct-26	20-Oct-26	12-Nov-26	23.81%	0%
Street Lighting Network		133	03-Aug-26	11-Nov-26	03-Aug-26	07-Nov-26	84.79%	7%
ROAD - 01		133	03-Aug-26	11-Nov-26	03-Aug-26	07-Nov-26	76.56%	10.78%
ROAD-01 From 470 to 1125 m (6)		112	03-Aug-26	18-Oct-26	03-Aug-26	04-Nov-26	90.59%	16.67%
Excavation		112	03-Aug-26	18-Oct-26	03-Aug-26	04-Nov-26	90.59%	16.67%
SDR-ST-CON-P1-1180	Excavation for LV Cable trench Section 1	21	03-Aug-26	26-Aug-26	03-Aug-26	03-Nov-26	100%	50%
SDR-ST-CON-P1-1560	Excavation for LV Cable trench Section 2	21	30-Aug-26	22-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2250	Excavation for LV Cable trench Section 3	21	24-Sep-26	18-Oct-26	12-Oct-26	04-Nov-26	71.43%	0%
ROAD-01 From 1125 to 1765 m (7)		21	27-Aug-26	20-Sep-26	03-Aug-26	03-Nov-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	03-Aug-26	03-Nov-26	100%	50%
SDR-ST-CON-P1-1590	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	03-Aug-26	03-Nov-26	100%	50%
ROAD-01 From 0 to 470 m (3)		133	27-Aug-26	09-Nov-26	05-Sep-26	04-Nov-26	60.32%	8.33%
Excavation		133	27-Aug-26	09-Nov-26	05-Sep-26	04-Nov-26	60.32%	8.33%
SDR-ST-CON-P1-1500	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	05-Sep-26	04-Nov-26	100%	25%
SDR-ST-CON-P1-2320	Excavation for LV Cable trench Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
SDR-ST-CON-P1-3040	Excavation for LV Cable trench Section 3	21	17-Oct-26	09-Nov-26	12-Oct-26	04-Nov-26	0%	0%
ROAD-01 N (1)		23	27-Aug-26	11-Nov-26	12-Oct-26	07-Nov-26	57.14%	0%
Excavation		23	27-Aug-26	11-Nov-26	12-Oct-26	07-Nov-26	57.14%	0%
SDR-ST-CON-P1-1700	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2410	Excavation for LV Cable trench Section 2	21	24-Sep-26	18-Oct-26	14-Oct-26	07-Nov-26	71.43%	0%
SDR-ST-CON-P1-3190	Excavation for LV Cable trench Section 3	21	19-Oct-26	11-Nov-26	14-Oct-26	07-Nov-26	0%	0%
Road Crossing & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD - 01		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 470 to 1125 m (6)		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 1125 to 1765 m (7)		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 0 to 470 m (3)		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 N (1)		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD - 02		21	13-Aug-26	07-Oct-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 0 to 400 m (9) 2 Way 110 mm		15	15-Aug-26	31-Aug-26	12-Oct-26	28-Oct-26	100%	0%
Excavation		15	15-Aug-26	31-Aug-26	12-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-P1-1310	Excavation for LV Cable trench Section 1	15	15-Aug-26	31-Aug-26	12-Oct-26	28-Oct-26	100%	0%

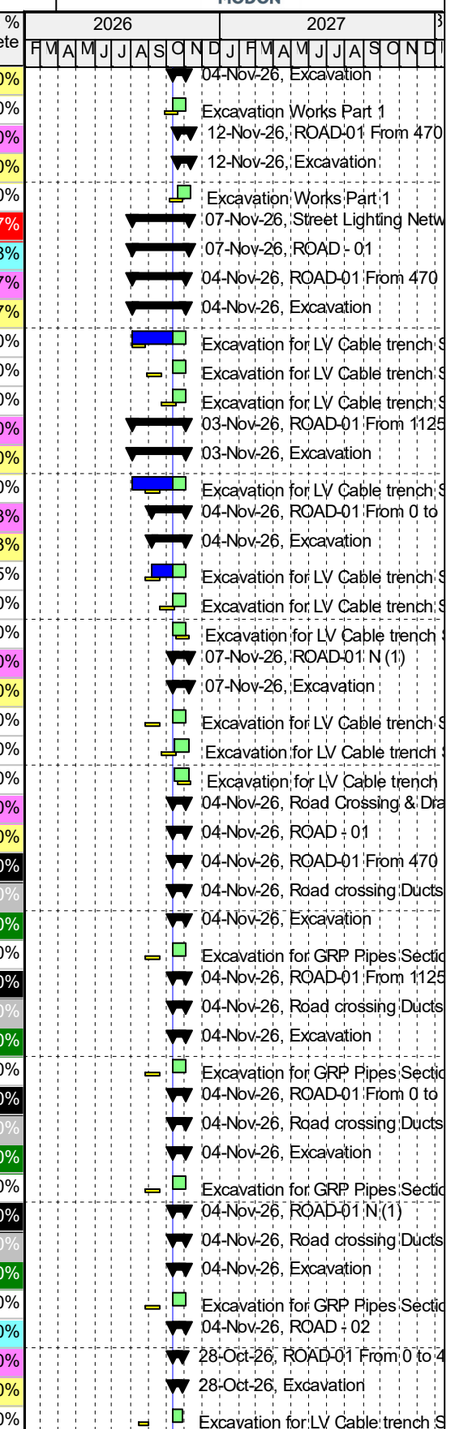

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
ROAD-01 From 400 to 900 m (10) 4 Way 110 mm		15	13-Aug-26	07-Oct-26	12-Oct-26	28-Oct-26	100%	0%
Excavation		15	13-Aug-26	07-Oct-26	12-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-P1-1260	Excavation for LV Cable trench Section 1	15	13-Aug-26	30-Aug-26	12-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-P1-1760	Excavation for LV Cable trench Section 2	15	02-Sep-26	19-Sep-26	12-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-P1-2260	Excavation for LV Cable trench Section 3	15	20-Sep-26	07-Oct-26	12-Oct-26	28-Oct-26	100%	0%
ROAD-01 From 900 to 1239 m (11) 2 Way 110 mm		14	27-Aug-26	12-Sep-26	12-Oct-26	27-Oct-26	100%	0%
Excavation		14	27-Aug-26	12-Sep-26	12-Oct-26	27-Oct-26	100%	0%
SDR-ST-CON-P1-1360	Excavation for LV Cable trench Section 1	14	27-Aug-26	12-Sep-26	12-Oct-26	27-Oct-26	100%	0%
Road Crossing & Drawpits		21	13-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD - 02		21	13-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 0 to 400 m (9) 2 Way 110 mm		21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 400 to 900 m (10) 4 Way 110 mm		21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 900 to 1239 m (11) 2 Way 110 mm		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
TELECOMMUNICATIONS WORKS		133	13-Aug-26	27-Oct-26	21-Sep-26	05-Nov-26	81.92%	1.92%
ROAD - 01		133	15-Aug-26	15-Oct-26	21-Sep-26	05-Nov-26	89.84%	5%
ROAD-01 N 1 (2X3)X50 mm MH-15 to MH-16		133	27-Aug-26	15-Oct-26	21-Sep-26	04-Nov-26	87.29%	16.65%
Ducts		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Excavation		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
SDR-ST-CON-P1-23	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Manholes		21	27-Aug-26	20-Sep-26	21-Sep-26	04-Nov-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	21-Sep-26	04-Nov-26	100%	50%
SDR-ST-CON-P1-16	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	21-Sep-26	04-Nov-26	100%	50%
ROAD-01 From 0 to 470 m (3) (2X3)X50 mm MH-12 to MH-14		133	27-Aug-26	15-Oct-26	30-Sep-26	04-Nov-26	85.71%	6.24%
Ducts		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Excavation		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
SDR-ST-CON-P1-21	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Manholes		133	27-Aug-26	15-Oct-26	30-Sep-26	04-Nov-26	90.48%	12.5%
Excavation		133	27-Aug-26	15-Oct-26	30-Sep-26	04-Nov-26	90.48%	12.5%
SDR-ST-CON-P1-15	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	30-Sep-26	04-Nov-26	100%	25%
SDR-ST-CON-P1-22	Excavation for Telecom Manhole Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
ROAD-01 From 470 to 1125 m (6) (2X3)X50 mm MH-10 to MH-11		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Ducts		21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-17	Excavation for telecom trench Section 2	21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Manholes		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-12	Excavation for Telecom Manhole Section 1	21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-18	Excavation for Telecom Manhole Section 2	21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%

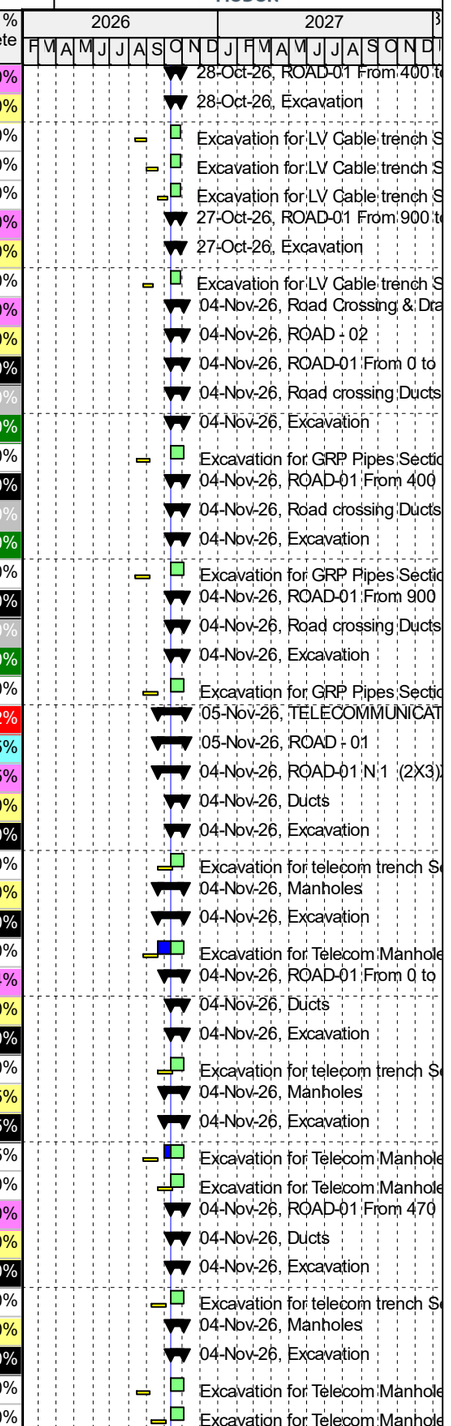

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
ROAD-01 From 1125 to 1765 m (7) (2X3)X50 mm MH-8 to MH-9		22	27-Aug-26	15-Oct-26	12-Oct-26	05-Nov-26	85.71%	0%
Ducts		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Excavation		21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
SDR-ST-CON-P1-229	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
Manholes		22	27-Aug-26	15-Oct-26	12-Oct-26	05-Nov-26	90.48%	0%
Excavation		22	27-Aug-26	15-Oct-26	12-Oct-26	05-Nov-26	90.48%	0%
SDR-ST-CON-P1-161	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-230	Excavation for Telecom Manhole Section 2	21	21-Sep-26	15-Oct-26	13-Oct-26	05-Nov-26	80.95%	0%
ROAD - 02		21	13-Aug-26	27-Oct-26	12-Oct-26	04-Nov-26	76.98%	0%
ROAD-01 From 0 to 400 m (9) (2X3)X50 mm MH-5 to MH-7		21	15-Aug-26	27-Oct-26	12-Oct-26	04-Nov-26	61.9%	0%
Ducts		21	15-Aug-26	27-Oct-26	12-Oct-26	04-Nov-26	55.56%	0%
Excavation		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-134	Excavation for telecom trench Section 1	21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-196	Excavation for telecom trench Section 2	21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Pipe laying		21	04-Oct-26	27-Oct-26	12-Oct-26	04-Nov-26	33.33%	0%
SDR-ST-CON-P1-267	HDPE Pipes for Telecom Installation	21	04-Oct-26	27-Oct-26	12-Oct-26	04-Nov-26	33.33%	0%
Manholes		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	15-Aug-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-133	Excavation for Telecom Manhole Section 1	21	15-Aug-26	07-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-197	Excavation for Telecom Manhole Section 2	21	08-Sep-26	03-Oct-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 400 to 900 m (10) (2X3)X50 mm MH-1 to MH-4		21	13-Aug-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Ducts		21	13-Aug-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	13-Aug-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-129	Excavation for telecom trench Section 1	21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-188	Excavation for telecom trench Section 2	21	07-Sep-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Manholes		21	13-Aug-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	13-Aug-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-128	Excavation for Telecom Manhole Section 1	21	13-Aug-26	06-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-189	Excavation for Telecom Manhole Section 2	21	07-Sep-26	01-Oct-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 900 to 1239 m (11) (2)X32 mm MH-1		21	27-Aug-26	15-Oct-26	12-Oct-26	04-Nov-26	95.24%	0%
Ducts		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-139	Excavation for telecom trench Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Manholes		21	27-Aug-26	15-Oct-26	12-Oct-26	04-Nov-26	90.48%	0%
Excavation		21	27-Aug-26	15-Oct-26	12-Oct-26	04-Nov-26	90.48%	0%
SDR-ST-CON-P1-138	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-208	Excavation for Telecom Manhole Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
LOW VOLTAGE		35	22-Oct-26	01-Dec-26	20-Aug-26	04-Nov-26	0%	56.67%
ROAD - 01		21	22-Oct-26	15-Nov-26	20-Aug-26	04-Nov-26	0%	70%
ROAD-01 From 470 to 1125 m (6)		21	22-Oct-26	15-Nov-26	20-Aug-26	04-Nov-26	0%	70%
Excavation		21	22-Oct-26	15-Nov-26	20-Aug-26	04-Nov-26	0%	70%
SDR-ST-CON-P1-1670	Excavation Works Part 1	21	22-Oct-26	15-Nov-26	20-Aug-26	04-Nov-26	0%	70%
ROAD - 02		28	31-Oct-26	01-Dec-26	24-Aug-26	04-Nov-26	0%	50%
ROAD-01 From 400 to 900 m (10)		21	31-Oct-26	23-Nov-26	24-Aug-26	04-Nov-26	0%	50%
Excavation		21	31-Oct-26	23-Nov-26	24-Aug-26	04-Nov-26	0%	50%
SDR-ST-CON-P1-1740	Excavation Works Part 1	21	31-Oct-26	23-Nov-26	24-Aug-26	04-Nov-26	0%	50%
ROAD-01 From 900 to 1239 m (11)		21	08-Nov-26	01-Dec-26	24-Aug-26	04-Nov-26	0%	50%

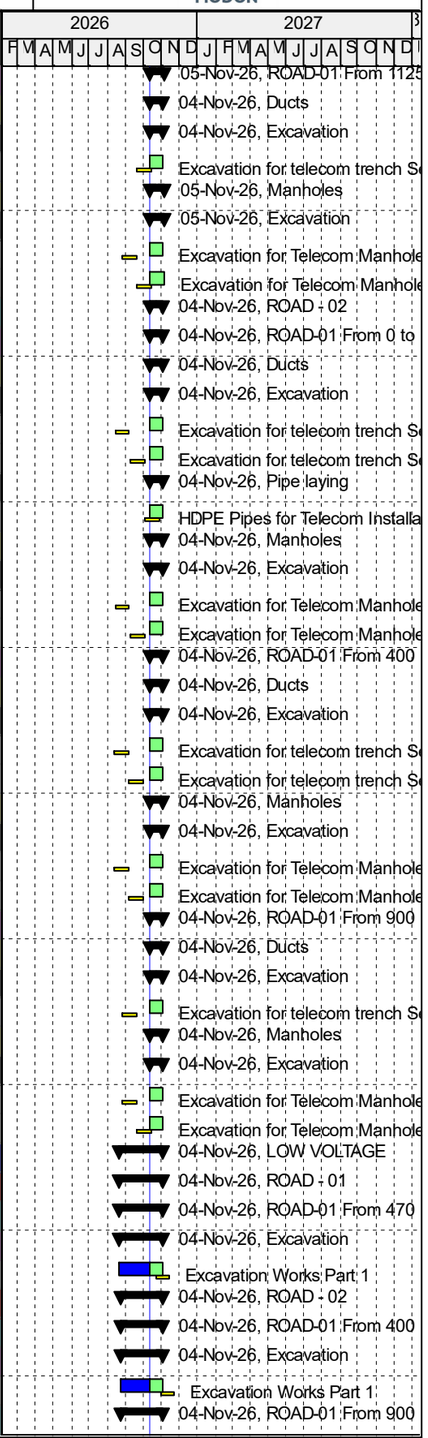

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		21	08-Nov-26	01-Dec-26	24-Aug-26	04-Nov-26	0%	50%
SDR-ST-CON-P1-1750	Excavation Works Part 1	21	08-Nov-26	01-Dec-26	24-Aug-26	04-Nov-26	0%	50%
PORTABLE WATER		205	07-Sep-26	09-Feb-27	22-Sep-26	09-Nov-26	6.31%	50.05%
ROAD - 01		25	12-Sep-26	09-Feb-27	12-Oct-26	09-Nov-26	14.34%	0%
ROAD-01 From 0 to 470 m (3)		25	22-Sep-26	09-Feb-27	12-Oct-26	09-Nov-26	8.34%	0%
Pipes Work		21	17-Jan-27	09-Feb-27	17-Oct-26	09-Nov-26	0%	0%
Backfilling		21	17-Jan-27	09-Feb-27	17-Oct-26	09-Nov-26	0%	0%
SDR-ST-CON-P1-4800	Backfilling of PW HDPE Pipe 315 mm.	21	17-Jan-27	09-Feb-27	17-Oct-26	09-Nov-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	22-Sep-26	17-Oct-26	12-Oct-26	04-Nov-26	76.19%	0%
Excavation		21	22-Sep-26	17-Oct-26	12-Oct-26	04-Nov-26	76.19%	0%
SDR-ST-CON-P1-1490	Excavation for Valve Chambers Section 1	21	22-Sep-26	17-Oct-26	12-Oct-26	04-Nov-26	76.19%	0%
ROAD-01 From 470 to 1125 m (6)		25	12-Sep-26	28-Jan-27	12-Oct-26	09-Nov-26	10.95%	0%
Pipes Work		21	05-Jan-27	28-Jan-27	17-Oct-26	09-Nov-26	0%	0%
Backfilling		21	05-Jan-27	28-Jan-27	17-Oct-26	09-Nov-26	0%	0%
SDR-ST-CON-P1-4700	Backfilling of PW HDPE Pipe 315 mm.	21	05-Jan-27	28-Jan-27	17-Oct-26	09-Nov-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		21	12-Sep-26	06-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	12-Sep-26	06-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-1420	Excavation for Valve Chambers Section 1	21	12-Sep-26	06-Oct-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 1125 to 1765 m (7)		21	13-Sep-26	07-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Valve Chambers & Valves & Fire Hydrant		21	13-Sep-26	07-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	13-Sep-26	07-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-1640	Excavation for Valve Chambers Section 1	21	13-Sep-26	07-Oct-26	12-Oct-26	04-Nov-26	100%	0%
ROAD - 02		205	07-Sep-26	14-Dec-26	22-Sep-26	09-Nov-26	4.16%	63.42%
ROAD-01 From 0 to 400 m (9)		205	07-Sep-26	14-Dec-26	22-Sep-26	04-Nov-26	4.69%	71.48%
Pipes Work		42	27-Oct-26	14-Dec-26	22-Sep-26	04-Nov-26	0%	75%
bedding Works		21	27-Oct-26	19-Nov-26	22-Sep-26	04-Nov-26	0%	75%
SDR-ST-CON-P1-3130	Sand bedding for PW HDPE Pipes 315 mm	21	27-Oct-26	19-Nov-26	22-Sep-26	04-Nov-26	0%	75%
Pipes Laying		21	21-Nov-26	14-Dec-26	24-Sep-26	04-Nov-26	0%	75%
SDR-ST-CON-P1-3650	Install PW 315 mm HDPE Pipe	21	21-Nov-26	14-Dec-26	24-Sep-26	04-Nov-26	0%	75%
Valve Chambers & Valves & Fire Hydrant		20	07-Sep-26	30-Sep-26	12-Oct-26	03-Nov-26	100%	0%
Excavation		20	07-Sep-26	30-Sep-26	12-Oct-26	03-Nov-26	100%	0%
SDR-ST-CON-P1-1940	Excavation for Valve Chambers Section 1	20	07-Sep-26	30-Sep-26	12-Oct-26	03-Nov-26	100%	0%
ROAD-01 From 400 to 900 m (10)		179	08-Sep-26	30-Nov-26	22-Sep-26	09-Nov-26	3.94%	60.04%
Pipes Work		168	19-Oct-26	30-Nov-26	22-Sep-26	09-Nov-26	0%	62.5%
bedding Works		12	19-Oct-26	01-Nov-26	22-Sep-26	25-Oct-26	0%	75%
SDR-ST-CON-P1-3060	Sand bedding for PW HDPE Pipes 315 mm	12	19-Oct-26	01-Nov-26	22-Sep-26	25-Oct-26	0%	75%
Pipes Laying		11	02-Nov-26	14-Nov-26	24-Sep-26	24-Oct-26	0%	75%
SDR-ST-CON-P1-3570	Install PW 315 mm HDPE Pipe	11	02-Nov-26	14-Nov-26	24-Sep-26	24-Oct-26	0%	75%
Testing		14	15-Nov-26	30-Nov-26	25-Oct-26	09-Nov-26	0%	0%
SDR-ST-CON-P1-4060	Testing of PW HDPE Pipe 315 mm.	14	15-Nov-26	30-Nov-26	25-Oct-26	09-Nov-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		20	08-Sep-26	01-Oct-26	12-Oct-26	03-Nov-26	100%	0%
Excavation		20	08-Sep-26	01-Oct-26	12-Oct-26	03-Nov-26	100%	0%
SDR-ST-CON-P1-1860	Excavation for Valve Chambers Section 1	20	08-Sep-26	01-Oct-26	12-Oct-26	03-Nov-26	100%	0%
ROAD-01 From 900 to 1239 m (11)		175	09-Sep-26	25-Nov-26	22-Sep-26	08-Nov-26	3.94%	60.04%
Pipes Work		165	18-Oct-26	25-Nov-26	22-Sep-26	08-Nov-26	0%	62.5%
bedding Works		10	18-Oct-26	28-Oct-26	22-Sep-26	22-Oct-26	0%	75%
SDR-ST-CON-P1-3220	Sand bedding for PW HDPE Pipes 315 mm	10	18-Oct-26	28-Oct-26	22-Sep-26	22-Oct-26	0%	75%

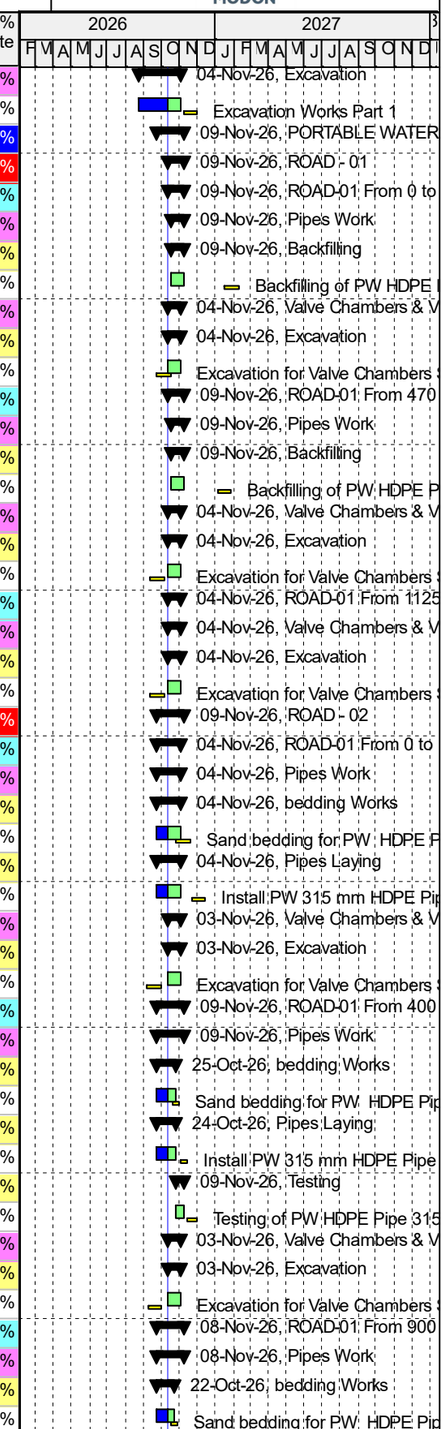

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Pipes Laying		10	29-Oct-26	09-Nov-26	24-Sep-26	22-Oct-26	0%	75%
SDR-ST-CON-P1-3610	Install PW 315 mm HDPE Pipe	10	29-Oct-26	09-Nov-26	24-Sep-26	22-Oct-26	0%	75%
Testing		14	10-Nov-26	25-Nov-26	24-Oct-26	08-Nov-26	0%	0%
SDR-ST-CON-P1-4090	Testing of PW HDPE Pipe 315 mm.	14	10-Nov-26	25-Nov-26	24-Oct-26	08-Nov-26	0%	0%
Valve Chambers & Valves & Fire Hydrant		20	09-Sep-26	03-Oct-26	12-Oct-26	03-Nov-26	100%	0%
Excavation		20	09-Sep-26	03-Oct-26	12-Oct-26	03-Nov-26	100%	0%
SDR-ST-CON-P1-2020	Excavation for Valve Chambers Section 1	20	09-Sep-26	03-Oct-26	12-Oct-26	03-Nov-26	100%	0%
SEWARAGE NETWORK		188	26-Aug-26	16-Dec-26	07-Sep-26	16-Nov-26	47.93%	45.1%
ROAD - 01		188	26-Aug-26	16-Dec-26	07-Sep-26	16-Nov-26	35.66%	40.77%
ROAD-01 From 0 to 470 m (3) 110 mm HDPE		188	27-Aug-26	16-Dec-26	07-Sep-26	16-Nov-26	14.42%	42.09%
Pipes Work		178	20-Sep-26	16-Dec-26	07-Sep-26	16-Nov-26	12.86%	42.86%
Excavation		20	20-Sep-26	13-Oct-26	07-Sep-26	03-Nov-26	90%	50%
SDR-ST-CON-P1-2380	Excavation for GRP Pipe 200mm Diameter Section 2	20	20-Sep-26	13-Oct-26	07-Sep-26	03-Nov-26	90%	50%
bedding Works		15	14-Oct-26	31-Oct-26	22-Sep-26	28-Oct-26	0%	50%
SDR-ST-CON-P1-3050	Sand bedding for GRP Pipe 200mm Diameter	15	14-Oct-26	31-Oct-26	22-Sep-26	28-Oct-26	0%	50%
Pipes Laying		21	01-Nov-26	23-Nov-26	24-Sep-26	22-Oct-26	0%	50%
SDR-ST-CON-P1-3710	200 mm GRP Pipe Laying	21	01-Nov-26	23-Nov-26	24-Sep-26	22-Oct-26	0%	50%
Testing		21	24-Nov-26	16-Dec-26	24-Oct-26	16-Nov-26	0%	0%
SDR-ST-CON-P1-4590	Testing of 200 mm GRP Pipe.	21	24-Nov-26	16-Dec-26	24-Oct-26	16-Nov-26	0%	0%
Manholes		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-1550	Excavation for manhole. Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
ROAD-01 From 470 to 1125 m (6) 110 mm HDPE		148	26-Aug-26	08-Nov-26	07-Sep-26	04-Nov-26	86.79%	35.04%
Pipes Work		17	19-Sep-26	08-Oct-26	07-Sep-26	31-Oct-26	100%	50%
Excavation		17	19-Sep-26	08-Oct-26	07-Sep-26	31-Oct-26	100%	50%
SDR-ST-CON-P1-2110	Excavation for GRP Pipe 200mm Diameter Section 2	17	19-Sep-26	08-Oct-26	07-Sep-26	31-Oct-26	100%	50%
Manholes		21	26-Aug-26	08-Nov-26	12-Oct-26	04-Nov-26	55.84%	0%
Excavation		21	26-Aug-26	14-Oct-26	12-Oct-26	04-Nov-26	93.06%	0%
SDR-ST-CON-P1-1440	Excavation for manhole. Section 1	21	26-Aug-26	19-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2120	Excavation for manhole. Section 2	21	20-Sep-26	14-Oct-26	12-Oct-26	04-Nov-26	85.71%	0%
bedding Works		21	15-Oct-26	08-Nov-26	12-Oct-26	04-Nov-26	0%	0%
SDR-ST-CON-P1-2870	Sand bedding for manhole.	21	15-Oct-26	08-Nov-26	12-Oct-26	04-Nov-26	0%	0%
ROAD-01 From 1125 to 1765 m (7) 110 mm HDPE		149	27-Aug-26	15-Oct-26	07-Sep-26	04-Nov-26	98.06%	39.81%
Pipes Work		17	20-Sep-26	10-Oct-26	07-Sep-26	31-Oct-26	100%	50%
Excavation		17	20-Sep-26	10-Oct-26	07-Sep-26	31-Oct-26	100%	50%
SDR-ST-CON-P1-2240	Excavation for GRP Pipe 200mm Diameter Section 2	17	20-Sep-26	10-Oct-26	07-Sep-26	31-Oct-26	100%	50%
Manholes		21	27-Aug-26	15-Oct-26	12-Oct-26	04-Nov-26	90.48%	0%
Excavation		21	27-Aug-26	15-Oct-26	12-Oct-26	04-Nov-26	90.48%	0%
SDR-ST-CON-P1-1660	Excavation for manhole. Section 1	21	27-Aug-26	20-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2310	Excavation for manhole. Section 2	21	21-Sep-26	15-Oct-26	12-Oct-26	04-Nov-26	80.95%	0%
ROAD - 02		139	30-Aug-26	18-Oct-26	07-Sep-26	04-Nov-26	98.47%	62.91%
ROAD-01 From 400 to 900 m (10) 110 mm HDPE		131	30-Aug-26	18-Oct-26	07-Sep-26	04-Nov-26	97.09%	59.71%
Pipes Work		17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Excavation		17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
SDR-ST-CON-P1-1810	Excavation for GRP Pipe 200mm Diameter Section 1	17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Manholes		21	30-Aug-26	18-Oct-26	12-Oct-26	04-Nov-26	85.71%	0%
Excavation		21	30-Aug-26	18-Oct-26	12-Oct-26	04-Nov-26	85.71%	0%

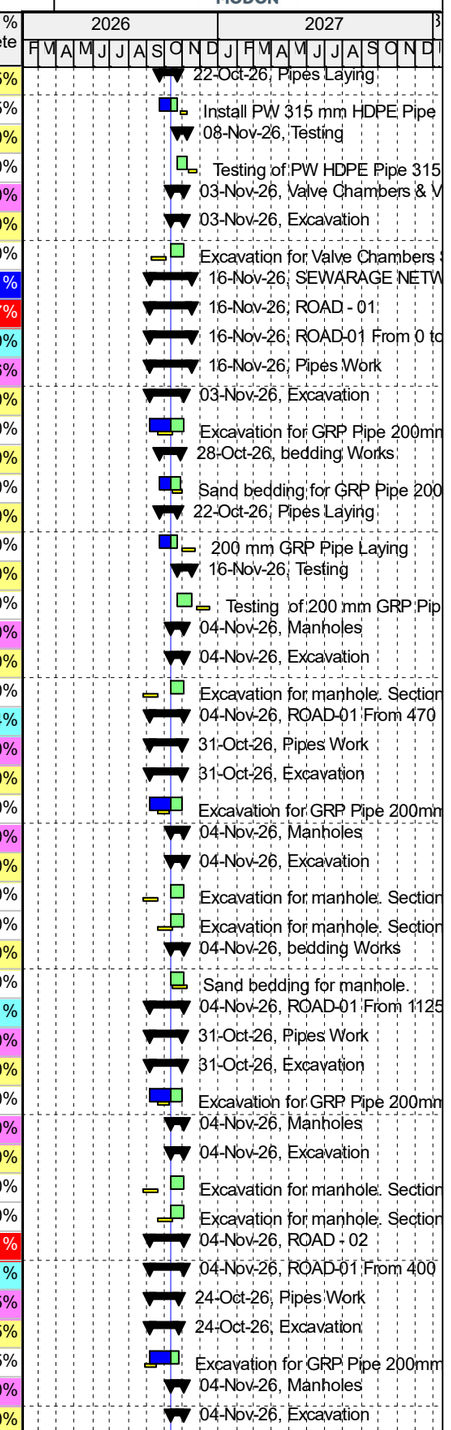

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-ST-CON-P1-1820	Excavation for manhole. Section 1	21	30-Aug-26	22-Sep-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2580	Excavation for manhole. Section 2	21	24-Sep-26	18-Oct-26	12-Oct-26	04-Nov-26	71.43%	0%
ROAD-01 From 900 to 1239 m (11) 110 mm HDPE		139	09-Sep-26	04-Oct-26	07-Sep-26	04-Nov-26	100%	66.49%
Pipes Work		16	09-Sep-26	28-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Excavation		16	09-Sep-26	28-Sep-26	07-Sep-26	24-Oct-26	100%	75%
SDR-ST-CON-P1-2030	Excavation for GRP Pipe 200mm Diameter Section 1	16	09-Sep-26	28-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Manholes		21	09-Sep-26	04-Oct-26	12-Oct-26	04-Nov-26	100%	0%
Excavation		21	09-Sep-26	04-Oct-26	12-Oct-26	04-Nov-26	100%	0%
SDR-ST-CON-P1-2040	Excavation for manhole. Section 1	21	09-Sep-26	04-Oct-26	12-Oct-26	04-Nov-26	100%	0%
STORM WATER		42	22-Sep-26	10-Nov-26	15-Sep-26	10-Nov-26	7.62%	75%
ROAD N...		42	22-Sep-26	10-Nov-26	15-Sep-26	10-Nov-26	7.62%	75%
Pipes Works		42	22-Sep-26	10-Nov-26	15-Sep-26	10-Nov-26	7.62%	75%
bedding Works		21	22-Sep-26	17-Oct-26	22-Sep-26	04-Nov-26	76.19%	75%
SDR-ST-CON-P1-2170	Sand bedding for GRP Pipes	21	22-Sep-26	17-Oct-26	22-Sep-26	04-Nov-26	76.19%	75%
Pipes Laying		21	18-Oct-26	10-Nov-26	15-Sep-26	10-Nov-26	0%	75%
SDR-ST-CON-P1-2910	Install ST GRP Pipes	21	18-Oct-26	10-Nov-26	15-Sep-26	10-Nov-26	0%	75%
Package-3		20	07-Jul-26	03-Sep-26	12-Oct-26	03-Nov-26	100%	0%
Site Works		20	07-Jul-26	16-Aug-26	12-Oct-26	03-Nov-26	100%	0%
Earthworks		20	07-Jul-26	16-Aug-26	12-Oct-26	03-Nov-26	100%	0%
Excavation		20	07-Jul-26	29-Jul-26	12-Oct-26	03-Nov-26	100%	0%
SDR-ST-CON-P3-1000	Excavation in all types of soil to the required depth includes removal of waste material	20	07-Jul-26	29-Jul-26	12-Oct-26	03-Nov-26	100%	0%
Fill		15	30-Jul-26	16-Aug-26	12-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-P3-1010	Backfilling with improved and select fill material from the site or imported	15	30-Jul-26	16-Aug-26	12-Oct-26	28-Oct-26	100%	0%
Platform Works		16	17-Aug-26	03-Sep-26	12-Oct-26	29-Oct-26	100%	0%
Platform		16	17-Aug-26	03-Sep-26	12-Oct-26	29-Oct-26	100%	0%
Earthworks		16	17-Aug-26	03-Sep-26	12-Oct-26	29-Oct-26	100%	0%
Excavation		16	17-Aug-26	03-Sep-26	12-Oct-26	29-Oct-26	100%	0%
SDR-ST-CON-P3-1020	Excavation in all types of soil to the required depth includes removal of waste material	16	17-Aug-26	03-Sep-26	12-Oct-26	29-Oct-26	100%	0%

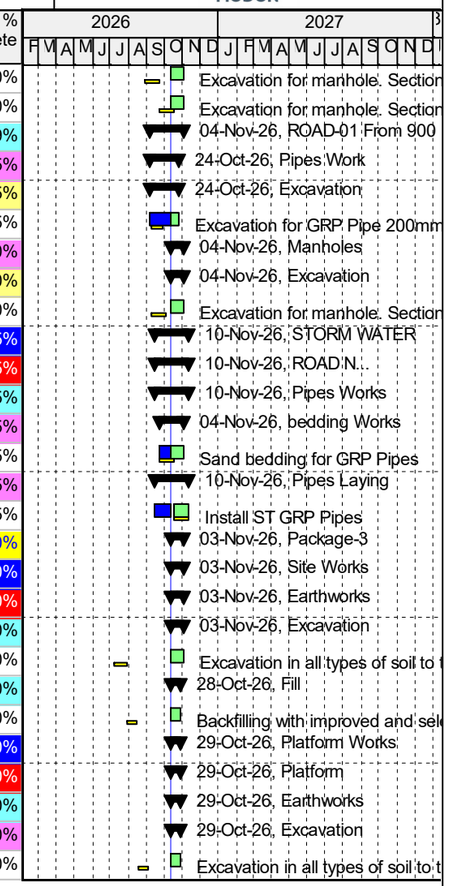

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone

TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation
