
Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Project:PASSENGER STATION FOR SAR RAILWAY - PACKAGE 1 SUDA		69	07-Jul-26	01-Dec-26	03-Aug-26 A	09-Nov-26	10.57%	17.25%
Construction		69	07-Jul-26	01-Dec-26	03-Aug-26	09-Nov-26	10.57%	17.25%
Package-1		69	03-Aug-26	01-Dec-26	03-Aug-26	09-Nov-26	7.29%	17.89%
ROAD WORKS		48	13-Oct-26	01-Dec-26	07-Sep-26	09-Nov-26	0%	16.83%
ROAD - 01		48	13-Oct-26	01-Dec-26	10-Sep-26	09-Nov-26	0%	19.53%
ROAD-01 From 470 to 1125 m (6)		48	17-Oct-26	01-Dec-26	10-Sep-26	09-Nov-26	0%	23.44%
Subgrade		11	17-Oct-26	08-Nov-26	10-Sep-26	17-Oct-26	0%	75%
SDR-ST-CON-P1-	Subgrade layer works	11	17-Oct-26	08-Nov-26	10-Sep-26	17-Oct-26	0%	75%
Base Course		10	09-Nov-26	21-Nov-26	18-Oct-26	28-Oct-26	0%	0%
SDR-ST-CON-P1-	Aggregate base course layer	10	09-Nov-26	21-Nov-26	18-Oct-26	28-Oct-26	0%	0%
Kerbstone Installation		20	09-Nov-26	01-Dec-26	18-Oct-26	09-Nov-26	0%	0%
SDR-ST-CON-P1-	Precast Concrete Curbstone, Type A2	20	09-Nov-26	01-Dec-26	18-Oct-26	09-Nov-26	0%	0%
ROAD-01 From 1125 to 1765 m (7)		47	13-Oct-26	22-Nov-26	10-Sep-26	08-Nov-26	0%	15.62%
Subgrade		10	13-Oct-26	29-Oct-26	10-Sep-26	15-Oct-26	0%	50%
SDR-ST-CON-P1-	Subgrade layer works	10	13-Oct-26	29-Oct-26	10-Sep-26	15-Oct-26	0%	50%
Base Course		9	31-Oct-26	16-Nov-26	17-Oct-26	26-Oct-26	0%	0%
SDR-ST-CON-P1-	Aggregate base course layer	9	31-Oct-26	16-Nov-26	17-Oct-26	26-Oct-26	0%	0%
Kerbstone Installation		20	31-Oct-26	22-Nov-26	17-Oct-26	08-Nov-26	0%	0%
SDR-ST-CON-P1-	Precast Concrete Curbstone, Type A2	20	31-Oct-26	22-Nov-26	17-Oct-26	08-Nov-26	0%	0%
ROAD - 02		48	15-Oct-26	26-Nov-26	07-Sep-26	09-Nov-26	0%	13.51%
ROAD-02 From 0 to 400 m (9)		13	15-Oct-26	29-Oct-26	07-Sep-26	19-Oct-26	0%	50%
Subgrade		13	15-Oct-26	29-Oct-26	07-Sep-26	19-Oct-26	0%	50%
SDR-ST-CON-P1-	Subgrade layer works	13	15-Oct-26	29-Oct-26	07-Sep-26	19-Oct-26	0%	50%
ROAD-02 From 400 to 900 m (10)		48	19-Oct-26	26-Nov-26	07-Sep-26	09-Nov-26	0%	7.81%
Subgrade		11	19-Oct-26	03-Nov-26	07-Sep-26	17-Oct-26	0%	25%
SDR-ST-CON-P1-	Subgrade layer works	11	19-Oct-26	03-Nov-26	07-Sep-26	17-Oct-26	0%	25%
Base Course		10	04-Nov-26	19-Nov-26	18-Oct-26	28-Oct-26	0%	0%
SDR-ST-CON-P1-	Aggregate base course layer	10	04-Nov-26	19-Nov-26	18-Oct-26	28-Oct-26	0%	0%
Kerbstone Installation		20	04-Nov-26	26-Nov-26	18-Oct-26	09-Nov-26	0%	0%
SDR-ST-CON-P1-	Precast Concrete Curbstone, Type A2	20	04-Nov-26	26-Nov-26	18-Oct-26	09-Nov-26	0%	0%
ROAD-02 From 900 to 1239 m (11)		45	18-Oct-26	22-Nov-26	07-Sep-26	05-Nov-26	0%	7.81%
Subgrade		8	18-Oct-26	29-Oct-26	07-Sep-26	13-Oct-26	0%	25%
SDR-ST-CON-P1-	Subgrade layer works	8	18-Oct-26	29-Oct-26	07-Sep-26	13-Oct-26	0%	25%
Base Course		7	31-Oct-26	09-Nov-26	14-Oct-26	21-Oct-26	0%	0%
SDR-ST-CON-P1-	Aggregate base course layer	7	31-Oct-26	09-Nov-26	14-Oct-26	21-Oct-26	0%	0%
Kerbstone Installation		20	31-Oct-26	22-Nov-26	14-Oct-26	05-Nov-26	0%	0%
SDR-ST-CON-P1-	Precast Concrete Curbstone, Type A2	20	31-Oct-26	22-Nov-26	14-Oct-26	05-Nov-26	0%	0%
ELECTRICAL WORKS		61	03-Aug-26	29-Oct-26	03-Aug-26	05-Nov-26	63.85%	6.21%
MV Network		28	28-Sep-26	29-Oct-26	05-Oct-26	05-Nov-26	14.29%	0%
ROAD - 01		28	28-Sep-26	29-Oct-26	05-Oct-26	05-Nov-26	14.29%	0%
ROAD-01 From 1125 to 1765 m (7)		21	28-Sep-26	21-Oct-26	05-Oct-26	28-Oct-26	28.57%	0%
Excavation		21	28-Sep-26	21-Oct-26	05-Oct-26	28-Oct-26	28.57%	0%
SDR-ST-CON-I	Excavation Works Part 1	21	28-Sep-26	21-Oct-26	05-Oct-26	28-Oct-26	28.57%	0%
ROAD-01 From 470 to 1125 m (6)		21	06-Oct-26	29-Oct-26	13-Oct-26	05-Nov-26	0%	0%
Excavation		21	06-Oct-26	29-Oct-26	13-Oct-26	05-Nov-26	0%	0%
SDR-ST-CON-I	Excavation Works Part 1	21	06-Oct-26	29-Oct-26	13-Oct-26	05-Nov-26	0%	0%

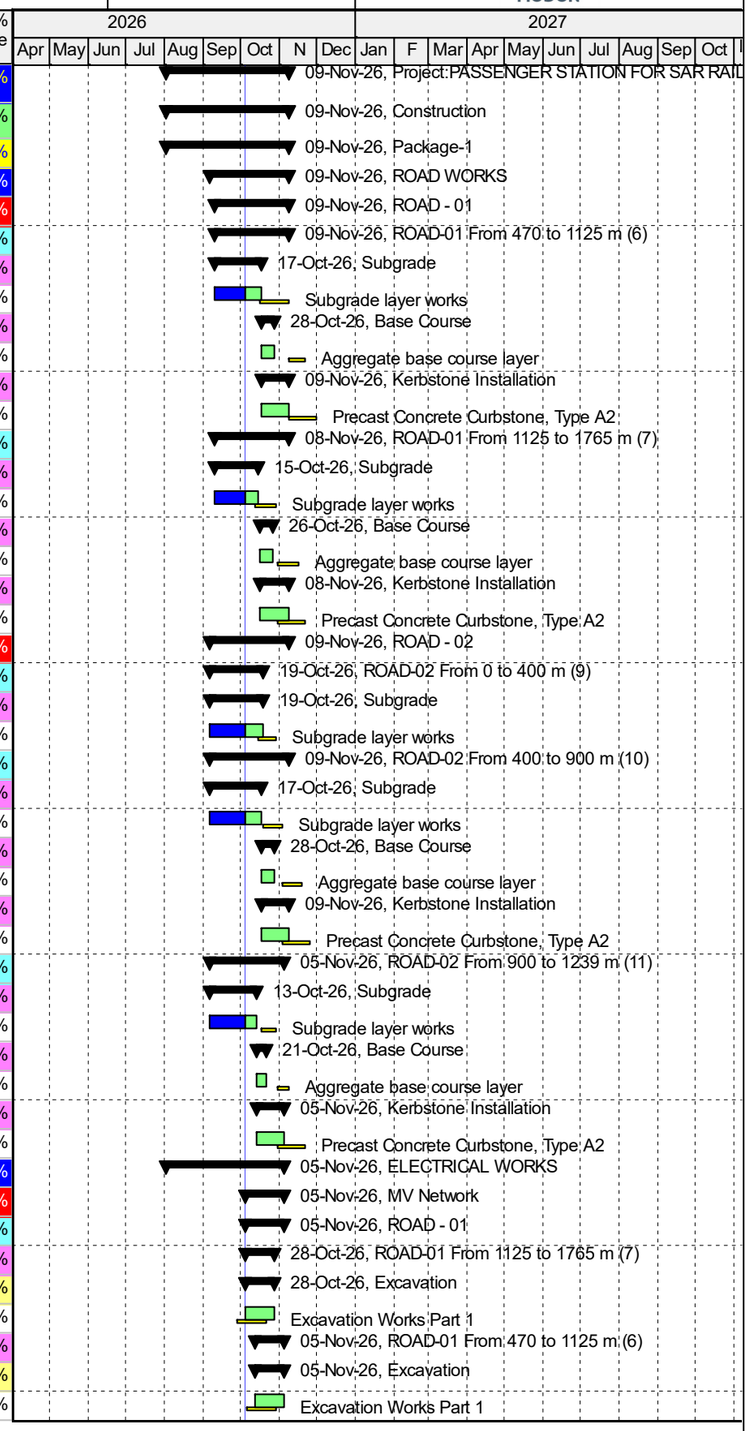

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Street Lighting Network		54	03-Aug-26	20-Sep-26	03-Aug-26	03-Nov-26	100%	13.15%
ROAD - 01		54	03-Aug-26	20-Sep-26	03-Aug-26	03-Nov-26	100%	23.86%
ROAD-01 From 470 to 1125 m (6)		21	03-Aug-26	26-Aug-26	03-Aug-26	03-Nov-26	100%	50%
Excavation		21	03-Aug-26	26-Aug-26	03-Aug-26	03-Nov-26	100%	50%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	21	03-Aug-26	26-Aug-26	03-Aug-26	03-Nov-26	100%	50%
ROAD-01 From 1125 to 1765 m (7)		21	27-Aug-26	20-Sep-26	03-Aug-26	27-Oct-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	03-Aug-26	27-Oct-26	100%	50%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	03-Aug-26	27-Oct-26	100%	50%
ROAD-01 From 0 to 470 m (3)		21	27-Aug-26	20-Sep-26	05-Sep-26	28-Oct-26	100%	25%
Excavation		21	27-Aug-26	20-Sep-26	05-Sep-26	28-Oct-26	100%	25%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	05-Sep-26	28-Oct-26	100%	25%
ROAD-01 N (1)		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road Crossing & Drawpits		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD - 01		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-01 From 1125 to 1765 m (7)		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-01 From 0 to 470 m (3)		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-01 N (1)		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD - 02		21	13-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 0 to 400 m (9) 2 Way 110 mm		15	15-Aug-26	31-Aug-26	05-Oct-26	21-Oct-26	100%	0%
Excavation		15	15-Aug-26	31-Aug-26	05-Oct-26	21-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	15	15-Aug-26	31-Aug-26	05-Oct-26	21-Oct-26	100%	0%
ROAD-02 From 400 to 900 m (10) 4 Way 110 mm		15	13-Aug-26	30-Aug-26	05-Oct-26	21-Oct-26	100%	0%
Excavation		15	13-Aug-26	30-Aug-26	05-Oct-26	21-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	15	13-Aug-26	30-Aug-26	05-Oct-26	21-Oct-26	100%	0%
ROAD-02 From 900 to 1239 m (11) 2 Way 110 mm		14	27-Aug-26	12-Sep-26	05-Oct-26	20-Oct-26	100%	0%
Excavation		14	27-Aug-26	12-Sep-26	05-Oct-26	20-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for LV Cable trench Section 1	14	27-Aug-26	12-Sep-26	05-Oct-26	20-Oct-26	100%	0%
Road Crossing & Drawpits		21	13-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD - 02		21	13-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 0 to 400 m (9) 2 Way 110 mm		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 400 to 900 m (10) 4 Way 110 mm		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%

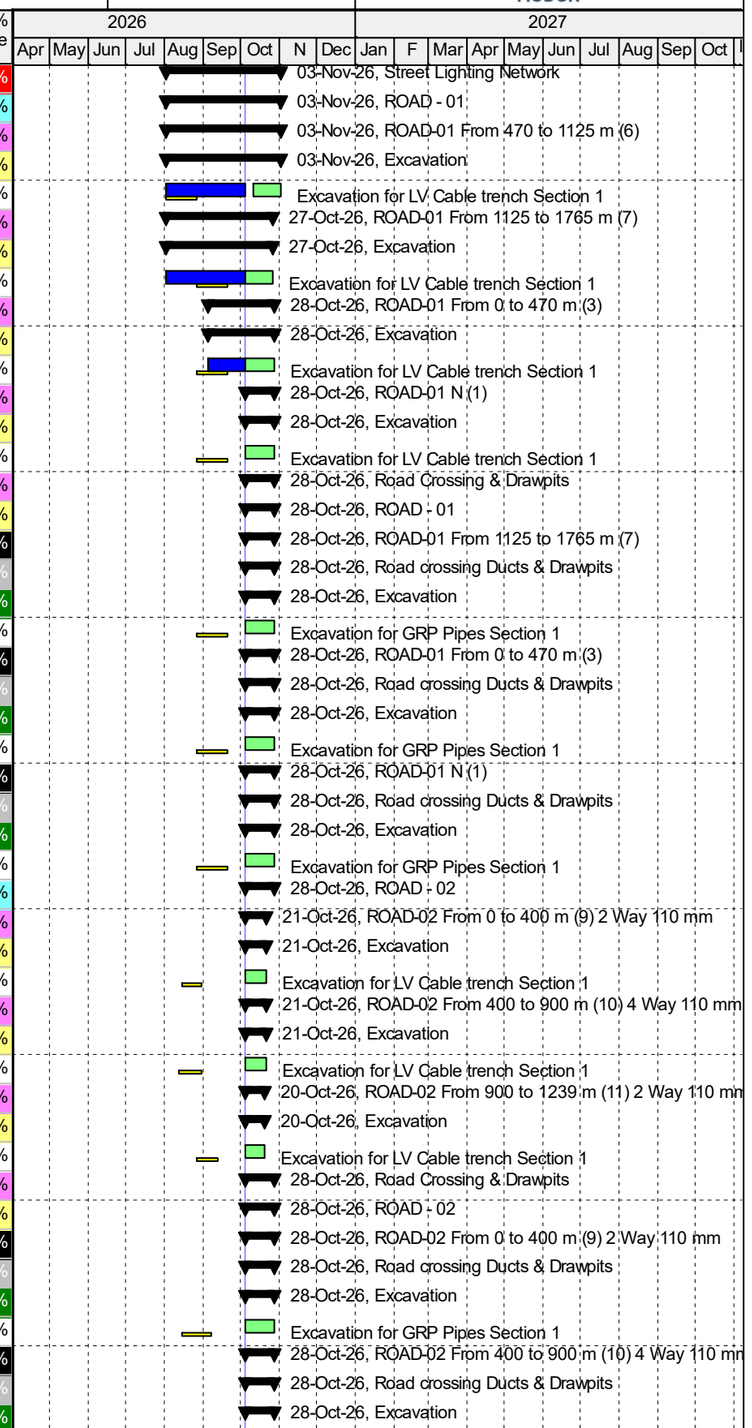

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
SDR-	Excavation for GRP Pipes Section 1	21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 900 to 1239 m (11) 2 Way 110 mm		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Road crossing Ducts & Drawpits		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-	Excavation for GRP Pipes Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
TELECOMMUNICATIONS WORKS		26	13-Aug-26	15-Oct-26	21-Sep-26	03-Nov-26	86.39%	3.57%
ROAD - 01		26	15-Aug-26	15-Oct-26	21-Sep-26	03-Nov-26	76.18%	6.24%
ROAD-01 N 1 (2X3)X50 mm MH-15 to MH-16		21	27-Aug-26	15-Oct-26	21-Sep-26	28-Oct-26	68.24%	16.65%
Ducts		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Excavation		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
SDR-ST-CC	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Manholes		21	27-Aug-26	20-Sep-26	21-Sep-26	28-Oct-26	100%	50%
Excavation		21	27-Aug-26	20-Sep-26	21-Sep-26	28-Oct-26	100%	50%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	21-Sep-26	28-Oct-26	100%	50%
ROAD-01 From 0 to 470 m (3) (2X3)X50 mm MH-12 to MH-14		21	27-Aug-26	15-Oct-26	30-Sep-26	28-Oct-26	68.24%	8.32%
Ducts		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Excavation		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
SDR-ST-CC	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Manholes		21	27-Aug-26	20-Sep-26	30-Sep-26	28-Oct-26	100%	25%
Excavation		21	27-Aug-26	20-Sep-26	30-Sep-26	28-Oct-26	100%	25%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	30-Sep-26	28-Oct-26	100%	25%
ROAD-01 From 470 to 1125 m (6) (2X3)X50 mm MH-10 to MH-11		21	15-Aug-26	03-Oct-26	11-Oct-26	03-Nov-26	100%	0%
Ducts		21	08-Sep-26	03-Oct-26	11-Oct-26	03-Nov-26	100%	0%
Excavation		21	08-Sep-26	03-Oct-26	11-Oct-26	03-Nov-26	100%	0%
SDR-ST-CC	Excavation for telecom trench Section 2	21	08-Sep-26	03-Oct-26	11-Oct-26	03-Nov-26	100%	0%
Manholes		21	15-Aug-26	07-Sep-26	11-Oct-26	03-Nov-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	11-Oct-26	03-Nov-26	100%	0%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	15-Aug-26	07-Sep-26	11-Oct-26	03-Nov-26	100%	0%
ROAD-01 From 1125 to 1765 m (7) (2X3)X50 mm MH-8 to MH-9		21	27-Aug-26	15-Oct-26	05-Oct-26	28-Oct-26	68.24%	0%
Ducts		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Excavation		21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
SDR-ST-CC	Excavation for telecom trench Section 2	21	21-Sep-26	15-Oct-26	05-Oct-26	28-Oct-26	52.38%	0%
Manholes		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD - 02		21	13-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 0 to 400 m (9) (2X3)X50 mm MH-5 to MH-7		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Ducts		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for telecom trench Section 1	21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Manholes		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	15-Aug-26	07-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 400 to 900 m (10) (2X3)X50 mm MH-1 to MH-4		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Ducts		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for telecom trench Section 1	21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%

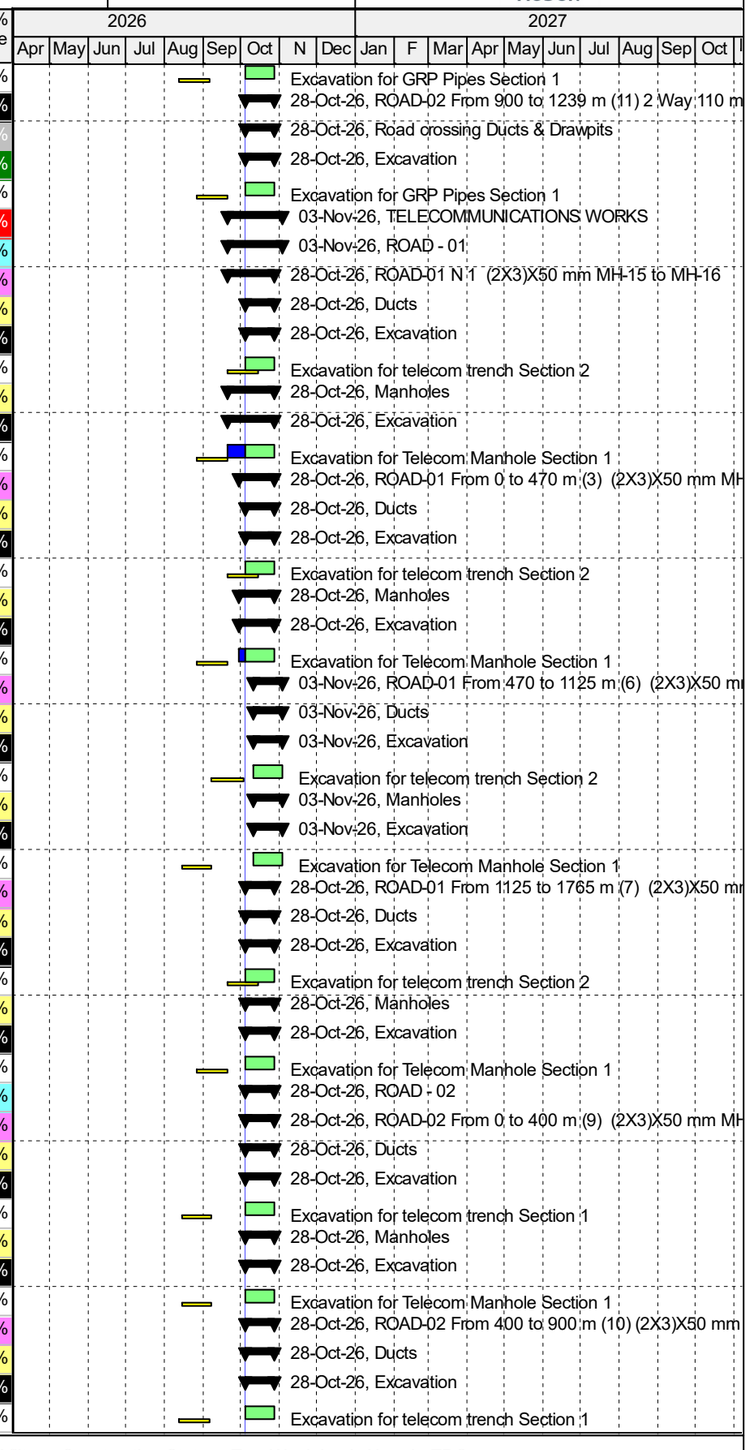

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
	Manholes	21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	Excavation	21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	13-Aug-26	06-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	ROAD-02 From 900 to 1239 m (11) (2)X32 mm MH-1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	Ducts	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	Excavation	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for telecom trench Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	Manholes	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	Excavation	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CC	Excavation for Telecom Manhole Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
	PORTABLE WATER	36	07-Sep-26	19-Nov-26	22-Sep-26	28-Oct-26	52.54%	30.29%
	ROAD - 01	21	12-Sep-26	17-Oct-26	05-Oct-26	28-Oct-26	76.27%	0%
	ROAD-01 From 0 to 470 m (3)	21	22-Sep-26	17-Oct-26	05-Oct-26	28-Oct-26	47.62%	0%
	Valve Chambers & Valves & Fire Hydrant	21	22-Sep-26	17-Oct-26	05-Oct-26	28-Oct-26	47.62%	0%
	Excavation	21	22-Sep-26	17-Oct-26	05-Oct-26	28-Oct-26	47.62%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	21	22-Sep-26	17-Oct-26	05-Oct-26	28-Oct-26	47.62%	0%
	ROAD-01 From 470 to 1125 m (6)	21	12-Sep-26	06-Oct-26	05-Oct-26	28-Oct-26	95.48%	0%
	Valve Chambers & Valves & Fire Hydrant	21	12-Sep-26	06-Oct-26	05-Oct-26	28-Oct-26	95.48%	0%
	Excavation	21	12-Sep-26	06-Oct-26	05-Oct-26	28-Oct-26	95.48%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	21	12-Sep-26	06-Oct-26	05-Oct-26	28-Oct-26	90.48%	0%
	ROAD-01 From 1125 to 1765 m (7)	21	13-Sep-26	07-Oct-26	05-Oct-26	28-Oct-26	85.71%	0%
	Valve Chambers & Valves & Fire Hydrant	21	13-Sep-26	07-Oct-26	05-Oct-26	28-Oct-26	85.71%	0%
	Excavation	21	13-Sep-26	07-Oct-26	05-Oct-26	28-Oct-26	85.71%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	21	13-Sep-26	07-Oct-26	05-Oct-26	28-Oct-26	85.71%	0%
	ROAD - 02	36	07-Sep-26	19-Nov-26	22-Sep-26	28-Oct-26	42.46%	43.15%
	ROAD-02 From 0 to 400 m (9)	36	07-Sep-26	19-Nov-26	22-Sep-26	28-Oct-26	32.97%	50.27%
	Pipes Work	21	27-Oct-26	19-Nov-26	22-Sep-26	28-Oct-26	0%	75%
	bedding Works	21	27-Oct-26	19-Nov-26	22-Sep-26	28-Oct-26	0%	75%
SDR-ST-CON-I	Sand bedding for PW HDPE Pipes 315 mm	21	27-Oct-26	19-Nov-26	22-Sep-26	28-Oct-26	0%	75%
	Valve Chambers & Valves & Fire Hydrant	20	07-Sep-26	30-Sep-26	05-Oct-26	27-Oct-26	100%	0%
	Excavation	20	07-Sep-26	30-Sep-26	05-Oct-26	27-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	20	07-Sep-26	30-Sep-26	05-Oct-26	27-Oct-26	100%	0%
	ROAD-02 From 400 to 900 m (10)	23	08-Sep-26	01-Nov-26	22-Sep-26	27-Oct-26	32.97%	50.27%
	Pipes Work	12	19-Oct-26	01-Nov-26	22-Sep-26	18-Oct-26	0%	75%
	bedding Works	12	19-Oct-26	01-Nov-26	22-Sep-26	18-Oct-26	0%	75%
SDR-ST-CON-I	Sand bedding for PW HDPE Pipes 315 mm	12	19-Oct-26	01-Nov-26	22-Sep-26	18-Oct-26	0%	75%
	Valve Chambers & Valves & Fire Hydrant	20	08-Sep-26	01-Oct-26	05-Oct-26	27-Oct-26	100%	0%
	Excavation	20	08-Sep-26	01-Oct-26	05-Oct-26	27-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	20	08-Sep-26	01-Oct-26	05-Oct-26	27-Oct-26	100%	0%
	ROAD-02 From 900 to 1239 m (11)	20	09-Sep-26	03-Oct-26	05-Oct-26	27-Oct-26	100%	0%
	Valve Chambers & Valves & Fire Hydrant	20	09-Sep-26	03-Oct-26	05-Oct-26	27-Oct-26	100%	0%
	Excavation	20	09-Sep-26	03-Oct-26	05-Oct-26	27-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for Valve Chambers Section 1	20	09-Sep-26	03-Oct-26	05-Oct-26	27-Oct-26	100%	0%
	SEWARAGE NETWORK	38	26-Aug-26	13-Oct-26	07-Sep-26	28-Oct-26	83.6%	53.19%
	ROAD - 01	38	26-Aug-26	13-Oct-26	07-Sep-26	28-Oct-26	72.67%	44.32%
	ROAD-01 From 0 to 470 m (3) 110 mm HDPE	38	27-Aug-26	13-Oct-26	07-Sep-26	28-Oct-26	64.54%	44.32%
	Pipes Work	20	20-Sep-26	13-Oct-26	07-Sep-26	27-Oct-26	60%	50%

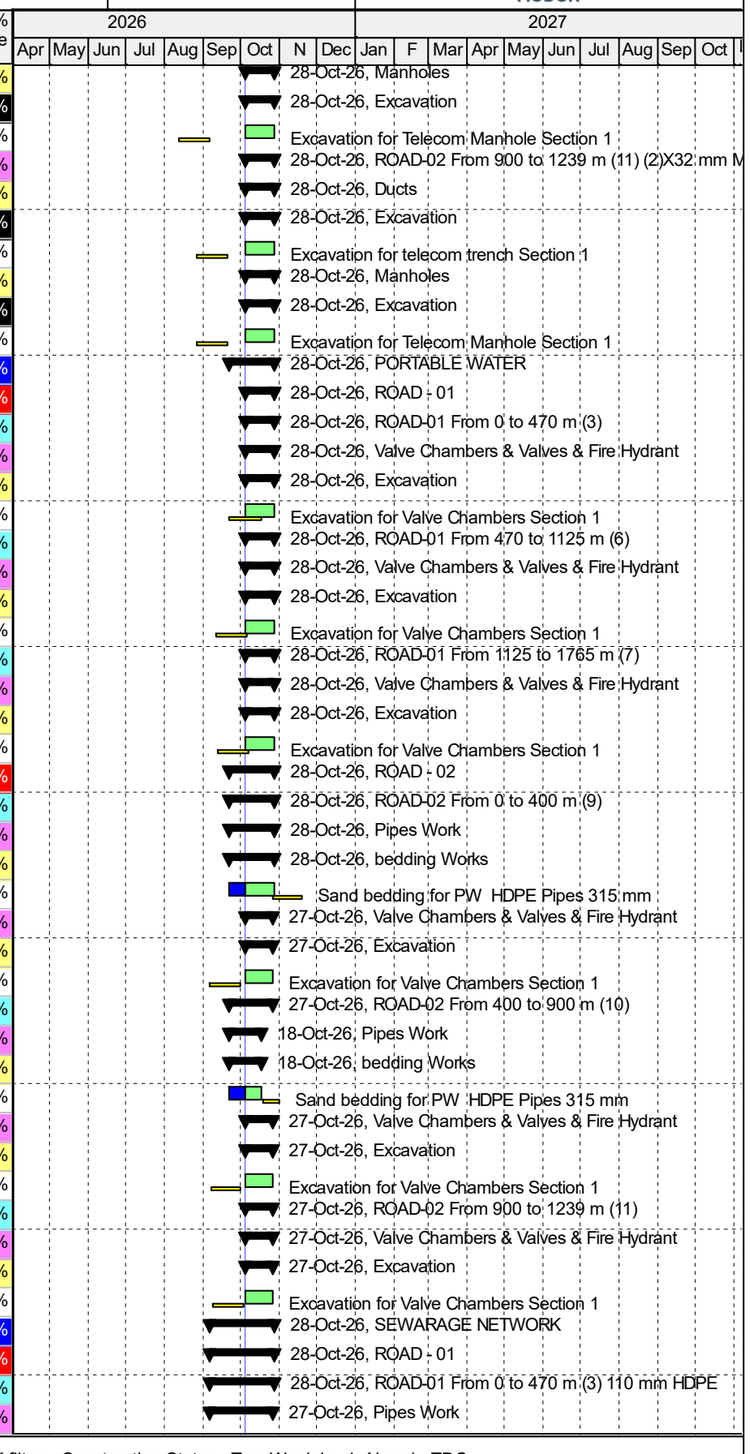

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Excavation		20	20-Sep-26	13-Oct-26	07-Sep-26	27-Oct-26	60%	50%
SDR-ST-CON-I	Excavation for GRP Pipe 200mm Diameter Section 2	20	20-Sep-26	13-Oct-26	07-Sep-26	27-Oct-26	60%	50%
Manholes		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for manhole. Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-01 From 470 to 1125 m (6) 110 mm HDPE		38	26-Aug-26	08-Oct-26	07-Sep-26	28-Oct-26	79.54%	44.32%
Pipes Work		17	19-Sep-26	08-Oct-26	07-Sep-26	24-Oct-26	76.92%	50%
Excavation		17	19-Sep-26	08-Oct-26	07-Sep-26	24-Oct-26	76.92%	50%
SDR-ST-CON-I	Excavation for GRP Pipe 200mm Diameter Section 2	17	19-Sep-26	08-Oct-26	07-Sep-26	24-Oct-26	76.47%	50%
Manholes		21	26-Aug-26	19-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	26-Aug-26	19-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for manhole. Section 1	21	26-Aug-26	19-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-01 From 1125 to 1765 m (7) 110 mm HDPE		38	27-Aug-26	10-Oct-26	07-Sep-26	28-Oct-26	73.93%	44.32%
Pipes Work		17	20-Sep-26	10-Oct-26	07-Sep-26	24-Oct-26	70.59%	50%
Excavation		17	20-Sep-26	10-Oct-26	07-Sep-26	24-Oct-26	70.59%	50%
SDR-ST-CON-I	Excavation for GRP Pipe 200mm Diameter Section 2	17	20-Sep-26	10-Oct-26	07-Sep-26	24-Oct-26	70.59%	50%
Manholes		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for manhole. Section 1	21	27-Aug-26	20-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD - 02		38	30-Aug-26	04-Oct-26	07-Sep-26	28-Oct-26	100%	66.49%
ROAD-02 From 400 to 900 m (10) 110 mm HDPE		38	30-Aug-26	22-Sep-26	07-Sep-26	28-Oct-26	100%	66.49%
Pipes Work		17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Excavation		17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
SDR-ST-CON-I	Excavation for GRP Pipe 200mm Diameter Section 1	17	30-Aug-26	17-Sep-26	07-Sep-26	24-Oct-26	100%	75%
Manholes		21	30-Aug-26	22-Sep-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	30-Aug-26	22-Sep-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for manhole. Section 1	21	30-Aug-26	22-Sep-26	05-Oct-26	28-Oct-26	100%	0%
ROAD-02 From 900 to 1239 m (11) 110 mm HDPE		38	09-Sep-26	04-Oct-26	07-Sep-26	28-Oct-26	100%	66.49%
Pipes Work		16	09-Sep-26	28-Sep-26	07-Sep-26	22-Oct-26	100%	75%
Excavation		16	09-Sep-26	28-Sep-26	07-Sep-26	22-Oct-26	100%	75%
SDR-ST-CON-I	Excavation for GRP Pipe 200mm Diameter Section 1	16	09-Sep-26	28-Sep-26	07-Sep-26	22-Oct-26	100%	75%
Manholes		21	09-Sep-26	04-Oct-26	05-Oct-26	28-Oct-26	100%	0%
Excavation		21	09-Sep-26	04-Oct-26	05-Oct-26	28-Oct-26	100%	0%
SDR-ST-CON-I	Excavation for manhole. Section 1	21	09-Sep-26	04-Oct-26	05-Oct-26	28-Oct-26	100%	0%
STORM WATER		21	22-Sep-26	17-Oct-26	22-Sep-26	28-Oct-26	47.62%	75%
ROAD N...		21	22-Sep-26	17-Oct-26	22-Sep-26	28-Oct-26	47.62%	75%
Pipes Works		21	22-Sep-26	17-Oct-26	22-Sep-26	28-Oct-26	47.62%	75%
bedding Works		21	22-Sep-26	17-Oct-26	22-Sep-26	28-Oct-26	47.62%	75%
SDR-ST-CON-P1-	Sand bedding for GRP Pipes	21	22-Sep-26	17-Oct-26	22-Sep-26	28-Oct-26	47.62%	75%
Package-3		24	07-Jul-26	03-Sep-26	05-Oct-26	01-Nov-26	100%	0%
Site Works		20	07-Jul-26	16-Aug-26	05-Oct-26	27-Oct-26	100%	0%
Earthworks		20	07-Jul-26	16-Aug-26	05-Oct-26	27-Oct-26	100%	0%
Excavation		20	07-Jul-26	29-Jul-26	05-Oct-26	27-Oct-26	100%	0%
SDR-ST-CON-P3-10(	Excavation in all types of soil to the required depth includes removal	20	07-Jul-26	29-Jul-26	05-Oct-26	27-Oct-26	100%	0%
Fill		15	30-Jul-26	16-Aug-26	05-Oct-26	21-Oct-26	100%	0%
SDR-ST-CON-P3-10'	Backfilling with improved and select fill material from the site or impo	15	30-Jul-26	16-Aug-26	05-Oct-26	21-Oct-26	100%	0%
Platform Works		16	17-Aug-26	03-Sep-26	14-Oct-26	01-Nov-26	100%	0%

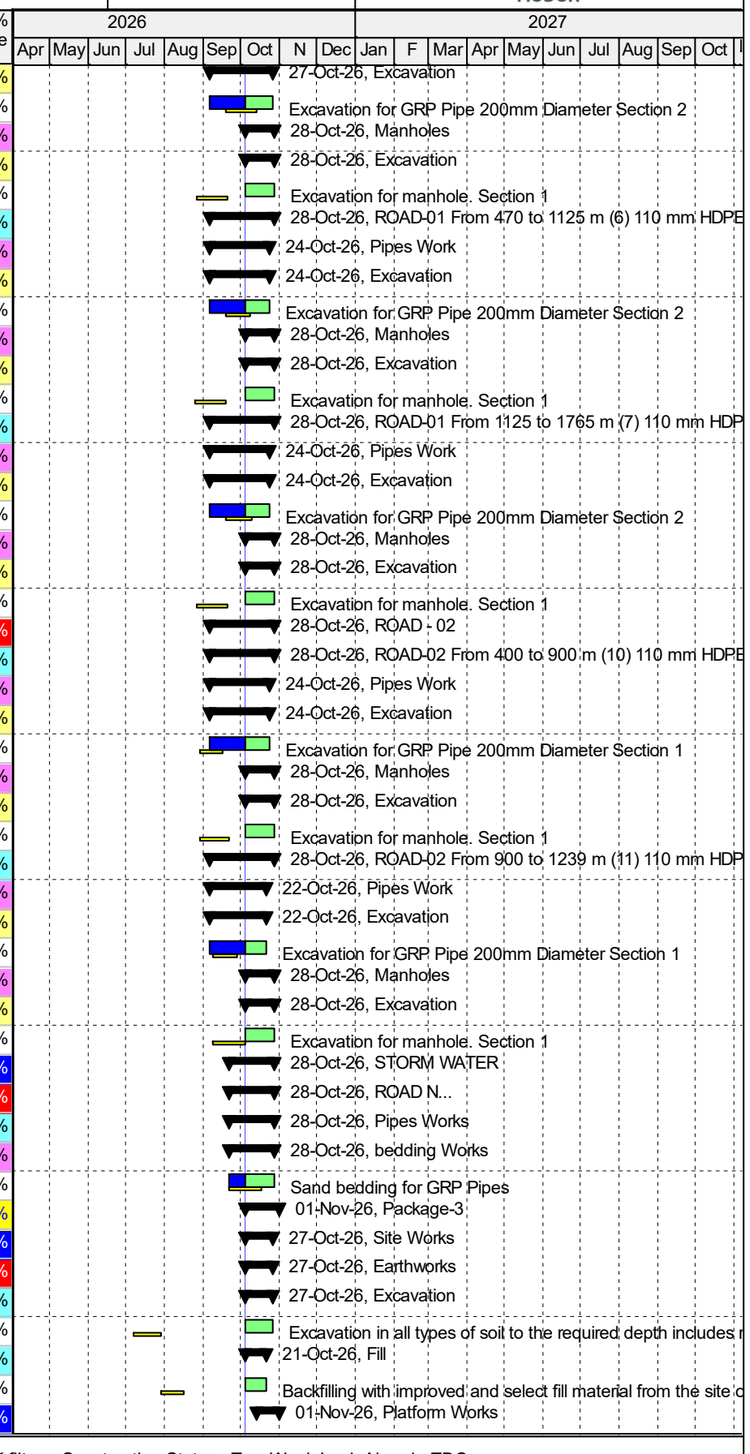

Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Baseline Milestone


TASK filters: Construction Status , Two Week Look Ahead - TDC.

© Oracle Corporation

Construction of Passenger Station for SAR Railway Sudair Industrial City

Two Week Look Ahead Plan

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish	Start	Finish	Schedule % Complete	Performance % Complete
Platform		16	17-Aug-26	03-Sep-26	14-Oct-26	01-Nov-26	100%	0%
Earthworks		16	17-Aug-26	03-Sep-26	14-Oct-26	01-Nov-26	100%	0%
Excavation		16	17-Aug-26	03-Sep-26	14-Oct-26	01-Nov-26	100%	0%
SDR-ST-CON-P3-	Excavation in all types of soil to the required depth includes removal	16	17-Aug-26	03-Sep-26	14-Oct-26	01-Nov-26	100%	0%



© Oracle Corporation
