
Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Development of the Technology City in Dammam-RECOVERY SCHEDULE		219	22-Jul-26 A	26-Feb-27	23-Jun-26	28-Jan-27	16,392,627
Engineering Works		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Material Submittals and Approvals		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Short Lead Time Items		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Superstructure Works		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Storage Tank (TSE)		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Submission of Material		7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
ENG-MT-TSE-CV-S	Material Submittal for Civil Works for Storage Tank (TSE)	7	20-Oct-26	27-Oct-26	23-Jun-26	30-Jun-26	0
Procurement Cycle		183	22-Jul-26 A	26-Feb-27	23-Jun-26	28-Jan-27	0
Short Lead Time Items		183	22-Jul-26 A	26-Feb-27	23-Jun-26	28-Jan-27	0
Infrastructure Networks		183	22-Jul-26 A	26-Feb-27	23-Jun-26	28-Jan-27	0
Road Works		11	02-Aug-26 A	20-Oct-26	02-Nov-26	05-Dec-26	0
Material Delivery & Site Inspection		11	02-Aug-26 A	20-Oct-26	02-Nov-26	05-Dec-26	0
Pre-Bituminous Construction		11	02-Aug-26 A	20-Oct-26	02-Nov-26	12-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	20-Oct-26	02-Nov-26	02-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0
Bituminous Construction		0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Prime Coat of Road Works	0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	0	20-Oct-26	20-Oct-26	05-Dec-26	05-Dec-26	0
Pavement Works		0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Curbstones for Landscaping	0	20-Oct-26	20-Oct-26	12-Nov-26	12-Nov-26	0
Traffic Signs Boards and Roads Marking		0	20-Oct-26	20-Oct-26	08-Nov-26	25-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	20-Oct-26	20-Oct-26	08-Nov-26	08-Nov-26	0
PRO-R25-RD-DL-	Material Delivery & Site Inspection of Road Markings For Road Works	0	20-Oct-26	20-Oct-26	25-Nov-26	25-Nov-26	0
Softscape and Planting Works		83	20-Oct-26	24-Jan-27	11-Jul-26	17-Oct-26	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	11-Jul-26	19-Jul-26	0
Main Line Pipes		6	20-Oct-26	26-Oct-26	11-Jul-26	19-Jul-26	0
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	20-Oct-26	26-Oct-26	12-Jul-26	19-Jul-26	0
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and	6	20-Oct-26	26-Oct-26	11-Jul-26	18-Jul-26	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	18-Jul-26	17-Oct-26	0
Main Line Pipes		90	27-Oct-26	24-Jan-27	18-Jul-26	17-Oct-26	0
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	27-Oct-26	24-Jan-27	19-Jul-26	17-Oct-26	0
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gra	90	27-Oct-26	24-Jan-27	18-Jul-26	16-Oct-26	0
Sewage Network		113	13-Sep-26 A	26-Feb-27	15-Jul-26	21-Nov-26	0
Manufacturing of Material		130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0
Testing and Finishes		130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	20-Oct-26	26-Feb-27	15-Jul-26	21-Nov-26	0
Material Delivery & Site Inspection		0	13-Sep-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0
Main Line Sections		0	13-Sep-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0
PRO-R25-SW-DL-	Material Delivery & Site Inspection of Manholes for Sewage Network	0	13-Sep-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0
Storm Drainage Network		158	02-Aug-26 A	27-Jan-27	15-Jul-26	22-Oct-26	0
Manufacturing of Material		100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0
Testing and Finishes		100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	20-Oct-26	27-Jan-27	15-Jul-26	22-Oct-26	0
1st Material Delivery & Site Inspection		6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	0
Catch Basin Sections		6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	0
PRO-SD-1DL-120	1ST Material Delivery for Catch Basin Pipes of Storm Drainage Network	6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	0
PRO-SD-1DL-130	1ST Material Delivery for Catch Basins of Storm Drainage Network	6	13-Sep-26 A	26-Oct-26	20-Jul-26	26-Jul-26	0
Material Delivery & Site Inspection		11	02-Aug-26 A	27-Oct-26	27-Jul-26	09-Aug-26	0
Main Line Sections		0	02-Aug-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0

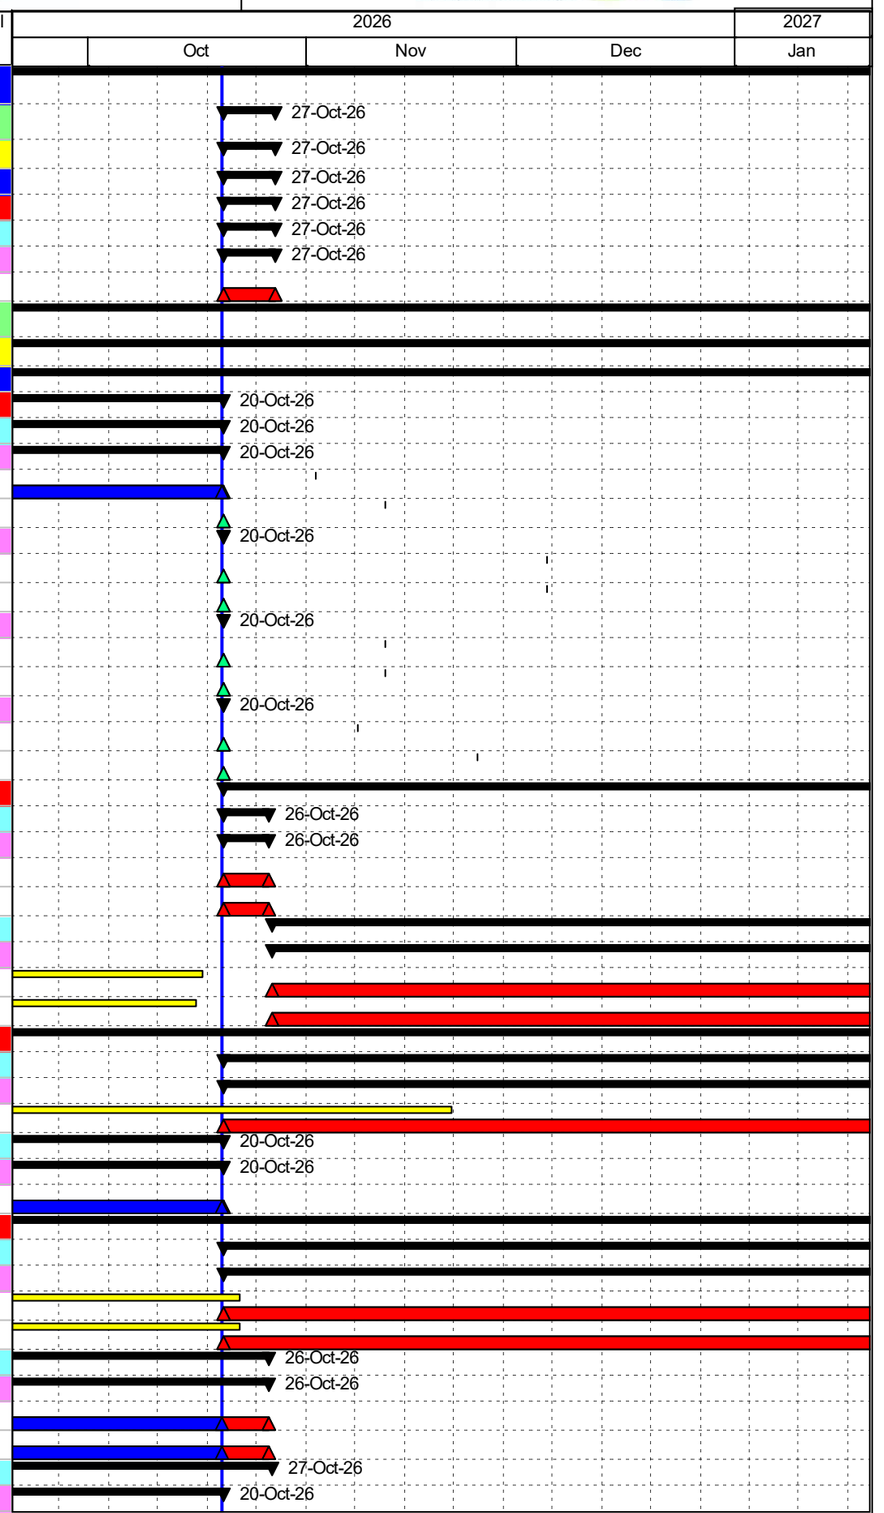


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	20-Oct-26	09-Aug-26	09-Aug-26	0
Catch Basin Sections		0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	0
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	27-Oct-26	27-Jul-26	27-Jul-26	0
Potable Water Network		121	30-Jul-26 A	18-Feb-27	07-Jul-26	06-Nov-26	0
Issuance of Purchase Orders		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0
Main Line Sections		6	20-Oct-26	26-Oct-26	08-Jul-26	14-Jul-26	0
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	20-Oct-26	26-Oct-26	08-Jul-26	14-Jul-26	0
Fire Hydrant		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0
Testing and Finishes		10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	20-Oct-26	31-Oct-26	08-Jul-26	19-Jul-26	0
Manufacturing of Material		115	27-Oct-26	18-Feb-27	15-Jul-26	06-Nov-26	0
Main Line Sections		90	27-Oct-26	24-Jan-27	15-Jul-26	12-Oct-26	0
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	27-Oct-26	24-Jan-27	15-Jul-26	12-Oct-26	0
Fire Hydrant		60	01-Nov-26	30-Dec-26	20-Jul-26	17-Sep-26	0
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	01-Nov-26	30-Dec-26	20-Jul-26	17-Sep-26	0
Testing and Finishes		110	01-Nov-26	18-Feb-27	20-Jul-26	06-Nov-26	0
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	01-Nov-26	18-Feb-27	20-Jul-26	06-Nov-26	0
1st Material Delivery & Site Inspection		71	30-Jul-26 A	10-Jan-27	07-Jul-26	28-Sep-26	0
Main Line Sections		71	30-Jul-26 A	10-Jan-27	07-Jul-26	28-Sep-26	0
PRO-PW-1DL-100	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	30-Jul-26 A	10-Jan-27	07-Jul-26	28-Sep-26	0
Material Delivery & Site Inspection		0	02-Aug-26 A	10-Jan-27	29-Sep-26	29-Sep-26	0
Main Line Sections		0	02-Aug-26 A	10-Jan-27	29-Sep-26	29-Sep-26	0
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Re	0	02-Aug-26 A	10-Jan-27	29-Sep-26	29-Sep-26	0
Irrigation Network		164	22-Jul-26 A	31-Jan-27	15-Jul-26	19-Oct-26	0
Issuance of Purchase Orders		6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0
Main Line Pipes		6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	27-Oct-26	02-Nov-26	15-Jul-26	21-Jul-26	0
Manufacturing of Material		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0
Main Line Pipes		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0
1st Material Delivery & Site Inspection		5	22-Jul-26 A	25-Oct-26	05-Oct-26	11-Oct-26	0
Main Line Pipes		5	22-Jul-26 A	25-Oct-26	05-Oct-26	11-Oct-26	0
PRO-IR-1DL-100	1ST Material Delivery for Main Line Pipes of Irrigation Network	5	22-Jul-26 A	25-Oct-26	05-Oct-26	11-Oct-26	0
Material Delivery & Site Inspection		0	26-Oct-26	26-Oct-26	11-Oct-26	11-Oct-26	0
Main Line Pipes		0	26-Oct-26	26-Oct-26	11-Oct-26	11-Oct-26	0
PRO-R25-IR-DL-1	Material Delivery & Site Inspection of Main Line Pipes for Irrigation Network	0	26-Oct-26	26-Oct-26	11-Oct-26	11-Oct-26	0
Treated Sewage Effluent (Tse)		92	02-Aug-26 A	24-Jan-27	27-Jun-26	10-Oct-26	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0
Main Line Pipes		6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	20-Oct-26	26-Oct-26	27-Jun-26	04-Jul-26	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0
Main Line Pipes		90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	27-Oct-26	24-Jan-27	04-Jul-26	02-Oct-26	0
Material Delivery & Site Inspection		0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0
Main Line Pipes		0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0
PRO-R25-TSE-DL-	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (T	0	02-Aug-26 A	20-Oct-26	10-Oct-26	10-Oct-26	0
Medium Voltage Network		89	20-Oct-26	31-Jan-27	23-Jun-26	19-Oct-26	0
Issuance of Purchase Orders		12	20-Oct-26	02-Nov-26	23-Jun-26	21-Jul-26	0
Cabling Works		12	20-Oct-26	02-Nov-26	23-Jun-26	06-Jul-26	0
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	20-Oct-26	02-Nov-26	23-Jun-26	06-Jul-26	0
Termination and Testing Works		12	20-Oct-26	02-Nov-26	08-Jul-26	21-Jul-26	0
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Netw	12	20-Oct-26	02-Nov-26	08-Jul-26	21-Jul-26	0

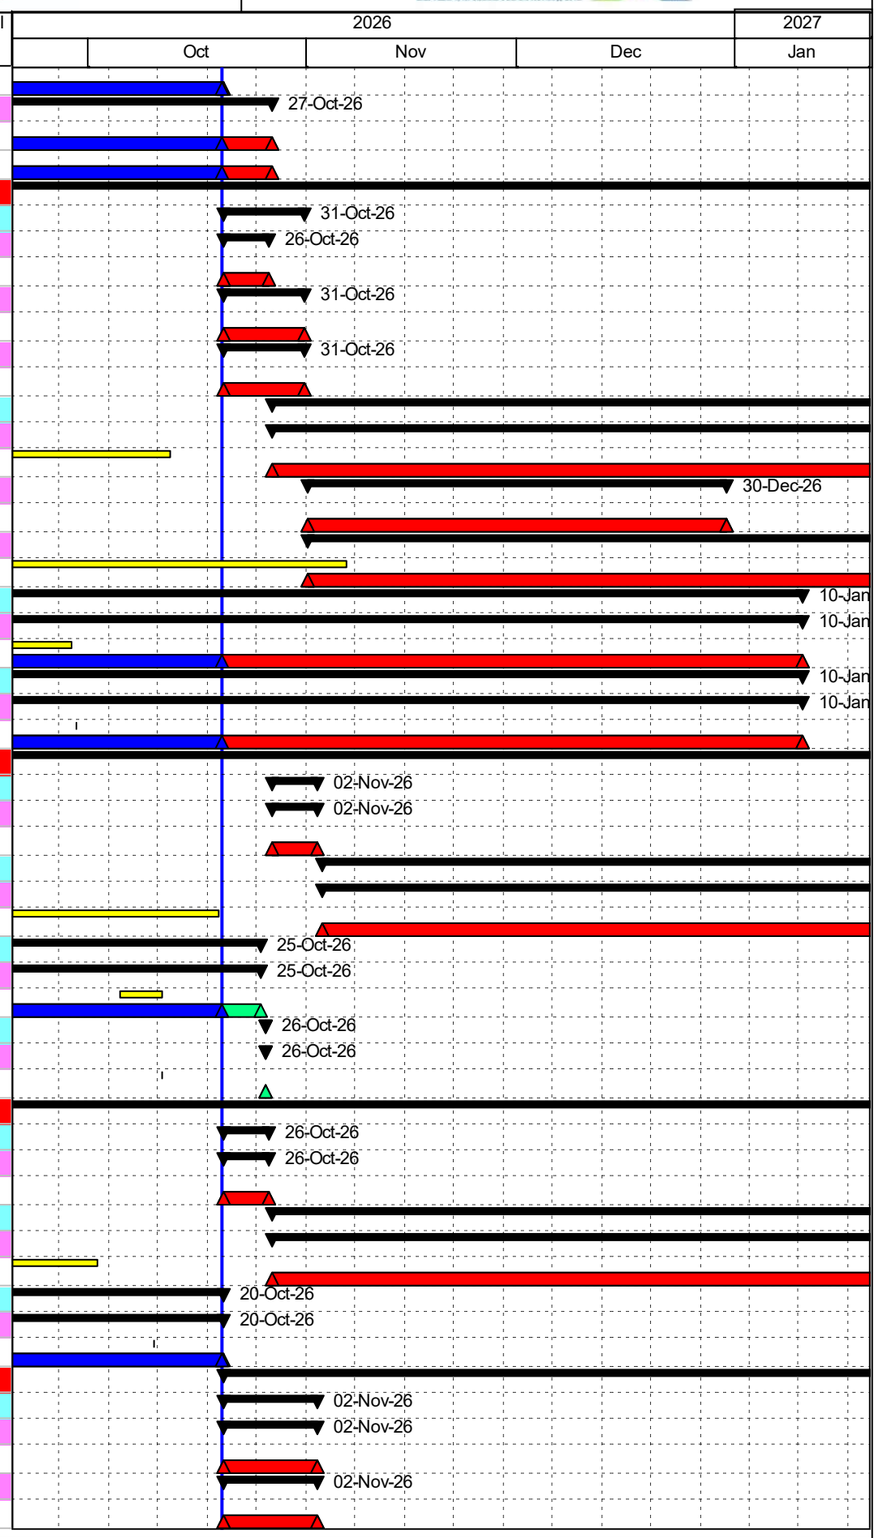


Primary Baseline · Actual Work · Summary
Remaining Work · Baseline Milestone
Critical Remaining Work · Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Manufacturing of Material		90	03-Nov-26	31-Jan-27	07-Jul-26	19-Oct-26	0
Cabling Works		60	03-Nov-26	01-Jan-27	07-Jul-26	04-Sep-26	0
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	03-Nov-26	01-Jan-27	07-Jul-26	04-Sep-26	0
Termination and Testing Works		90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	03-Nov-26	31-Jan-27	22-Jul-26	19-Oct-26	0
Low Voltage and Street Lighting Network		41	20-Oct-26	06-Dec-26	28-Sep-26	28-Jan-27	0
1st Material Delivery & Site Inspection		15	20-Oct-26	05-Nov-26	28-Sep-26	29-Dec-26	0
Cabling Works		6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-100	1ST Material Delivery for Lighting Cables of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0
Lighting Poles Works		6	20-Oct-26	26-Oct-26	28-Sep-26	19-Dec-26	0
PRO-SL-1DL-110	1ST Material Delivery for Lighting Poles Foundations of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-120	1ST Material Delivery for Lighting Poles of Street Lighting Network	6	20-Oct-26	26-Oct-26	28-Sep-26	04-Oct-26	0
PRO-SL-1DL-140	1ST Material Delivery for Lighting Fixtures of Street Lighting Network	6	20-Oct-26	26-Oct-26	13-Dec-26	19-Dec-26	0
Distribution Panel Board		6	20-Oct-26	26-Oct-26	24-Oct-26	29-Oct-26	0
PRO-SL-1DL-160	1ST Material Delivery for Distrubution Panel Boards of Street Lighting Network	6	20-Oct-26	26-Oct-26	24-Oct-26	29-Oct-26	0
Termination and Testing Works		15	20-Oct-26	05-Nov-26	03-Nov-26	29-Dec-26	0
PRO-SL-1DL-130	1ST Material Delivery for Fuse Boxes of Street Lighting Network	15	20-Oct-26	05-Nov-26	13-Dec-26	29-Dec-26	0
PRO-SL-1DL-170	1ST Material Delivery for Cable Lugs of Street Lighting Network	15	20-Oct-26	05-Nov-26	03-Nov-26	21-Nov-26	0
Earthing System Works		6	20-Oct-26	26-Oct-26	03-Dec-26	09-Dec-26	0
PRO-SL-1DL-150	1ST Material Delivery for Lighting Earthing of Street Lighting Network	6	20-Oct-26	26-Oct-26	03-Dec-26	09-Dec-26	0
Material Delivery & Site Inspection		35	27-Oct-26	06-Dec-26	05-Oct-26	28-Jan-27	0
Cabling Works		0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Cables for Street Lighting Network	0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0
Lighting Poles Works		18	27-Oct-26	16-Nov-26	05-Oct-26	20-Dec-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles Foundations for Street Lighting I	18	27-Oct-26	16-Nov-26	05-Oct-26	25-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Poles for Street Lighting Network	0	27-Oct-26	27-Oct-26	05-Oct-26	05-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Fixtures for Street Lighting Network	0	27-Oct-26	27-Oct-26	20-Dec-26	20-Dec-26	0
Distribution Panel Board		0	27-Oct-26	27-Oct-26	31-Oct-26	31-Oct-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Distrubution Panel Boards for Street Lighting N	0	27-Oct-26	27-Oct-26	31-Oct-26	31-Oct-26	0
Termination and Testing Works		26	07-Nov-26	06-Dec-26	21-Nov-26	28-Jan-27	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Fuse Boxes for Street Lighting Network	26	07-Nov-26	06-Dec-26	30-Dec-26	28-Jan-27	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Cable Lugs for Street Lighting Network	26	07-Nov-26	06-Dec-26	21-Nov-26	21-Dec-26	0
Earthing System Works		0	27-Oct-26	27-Oct-26	10-Dec-26	10-Dec-26	0
PRO-R25-SL-DL-1	Material Delivery & Site Inspection of Lighting Earthing for Street Lighting Network	0	27-Oct-26	27-Oct-26	10-Dec-26	10-Dec-26	0
Telecom Network		83	20-Oct-26	24-Jan-27	07-Jul-26	11-Oct-26	0
Issuance of Purchase Orders		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
Ducts Works		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
Manholes Works		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
CCTV System Wroks		6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	20-Oct-26	26-Oct-26	07-Jul-26	13-Jul-26	0
Manufacturing of Material		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0
Ducts Works		60	27-Oct-26	25-Dec-26	14-Jul-26	11-Sep-26	0
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	27-Oct-26	25-Dec-26	14-Jul-26	11-Sep-26	0
Manholes Works		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0
CCTV System Wroks		90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	27-Oct-26	24-Jan-27	14-Jul-26	11-Oct-26	0
Superstructure Works		151	02-Aug-26 A	17-Jan-27	23-Jun-26	11-Oct-26	0
Issuance of Purchase Orders		18	20-Oct-26	09-Nov-26	23-Jun-26	13-Jul-26	0
Storage Tank (TSE)		11	28-Oct-26	09-Nov-26	01-Jul-26	13-Jul-26	0
PRO-TSE-CV-PO-3(	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	28-Oct-26	09-Nov-26	01-Jul-26	13-Jul-26	0

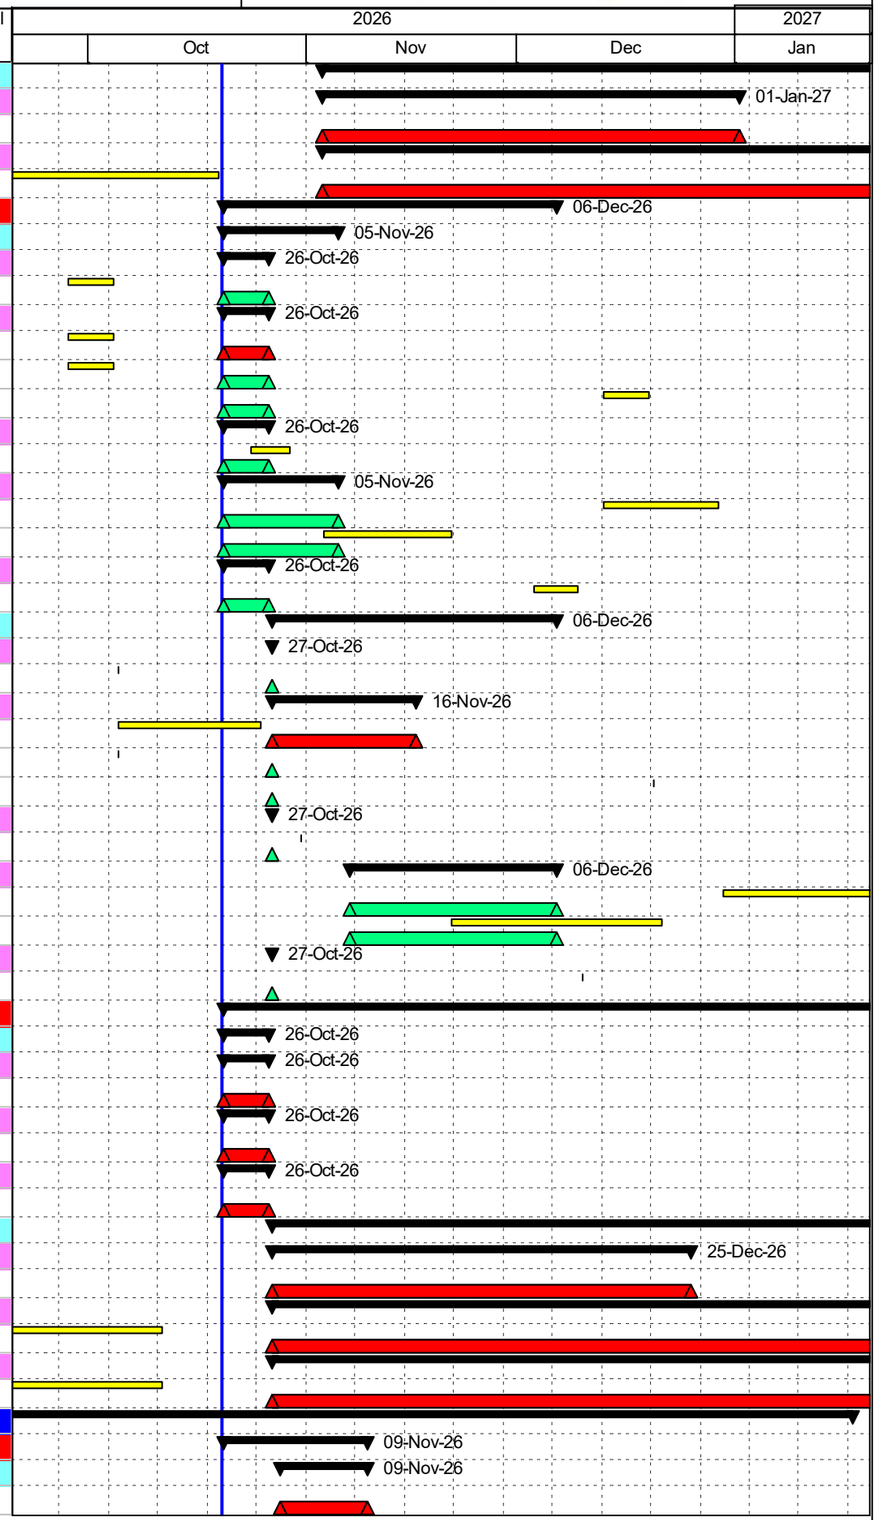


Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Gaurd Room		11	20-Oct-26	01-Nov-26	23-Jun-26	05-Jul-26	0
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	20-Oct-26	01-Nov-26	23-Jun-26	05-Jul-26	0
Manufacturing of Material		90	20-Oct-26	17-Jan-27	05-Jul-26	11-Oct-26	0
Gaurd Room		40	01-Nov-26	11-Dec-26	05-Jul-26	14-Aug-26	0
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	01-Nov-26	11-Dec-26	05-Jul-26	14-Aug-26	0
Softscape and Planting Works		90	20-Oct-26	17-Jan-27	13-Jul-26	11-Oct-26	0
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	20-Oct-26	17-Jan-27	13-Jul-26	11-Oct-26	0
Material Delivery & Site Inspection		109	02-Aug-26 A	20-Oct-26	25-Jul-26	03-Aug-26	0
Lift Station		0	17-Sep-26 A	20-Oct-26	03-Aug-26	03-Aug-26	0
PRO-LS-CV-DL-50	Material Delivery & Site Inspection for Civil Works for Lift Stations	0	17-Sep-26 A	20-Oct-26	03-Aug-26	03-Aug-26	0
Fence		0	02-Aug-26 A	20-Oct-26	25-Jul-26	25-Jul-26	0
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	20-Oct-26	25-Jul-26	25-Jul-26	0
Long Lead Time Items		83	26-Aug-26 A	18-Dec-26	23-Jun-26	05-Oct-26	0
Infrastructure Networks		20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0
CCTV System Wroks of Telecom Network		20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0
Issuance of Purchase Orders		20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0
PRO-CTV-LL-PO-1(	Issuance of Purchase Order for Low Current Works of CCTV Complete System with	20	20-Oct-26	11-Nov-26	23-Jun-26	15-Jul-26	0
Superstructure Works		83	26-Aug-26 A	18-Dec-26	04-Jul-26	05-Oct-26	0
Pump Stations		60	26-Aug-26 A	18-Dec-26	07-Aug-26	05-Oct-26	0
Manufacturing of Material		60	26-Aug-26 A	18-Dec-26	07-Aug-26	05-Oct-26	0
PRO-SPS-LL-MF-10	Manufacturing of Electromechanical Works for Pump Stations	60	26-Aug-26 A	18-Dec-26	07-Aug-26	05-Oct-26	0
Lift Stations		60	20-Oct-26	18-Dec-26	07-Aug-26	05-Oct-26	0
Manufacturing of Material		60	20-Oct-26	18-Dec-26	07-Aug-26	05-Oct-26	0
PRO-LS-LL-MF-20	Manufacturing of Electromechanical Works for Lift Stations	60	20-Oct-26	18-Dec-26	07-Aug-26	05-Oct-26	0
Storage Tank (TSE)		30	20-Oct-26	23-Nov-26	04-Jul-26	06-Aug-26	0
Issuance of Purchase Orders		30	20-Oct-26	23-Nov-26	04-Jul-26	06-Aug-26	0
PRO-TSE-LL-PO-30	Issuance of Purchase Order for Electromechanical Works for Storage Tank (TSE)	30	20-Oct-26	23-Nov-26	04-Jul-26	06-Aug-26	0
Construction Works		219	02-Aug-26 A	23-Nov-26	04-Jul-26	26-Dec-26	16,392,627
Infrastructure Networks		124	02-Aug-26 A	23-Nov-26	04-Jul-26	27-Aug-26	6,314,977
Earthworks		26	02-Aug-26 A	07-Nov-26	04-Jul-26	02-Aug-26	3,797,029
Earthworks		26	02-Aug-26 A	07-Nov-26	04-Jul-26	02-Aug-26	3,797,029
CO-EW-200_R	Excavation Works Upto Design Level for Earthworks-P1(Remaining)	10	02-Aug-26 A	31-Oct-26	04-Jul-26	14-Jul-26	522,497
CO-EW-110_R	Embankments Works Upto Design Level for Earthworks(Remaining)	16	02-Aug-26 A	07-Nov-26	15-Jul-26	02-Aug-26	2,419,920
CO-EW-210_R	Excavation Works Upto Design Level for Earthworks-P2(Remaining)	10	02-Aug-26 A	31-Oct-26	04-Jul-26	14-Jul-26	275,827
CO-EW-220_R	Excavation Works Upto Design Level for Earthworks-P3(Remaining)	12	02-Aug-26 A	02-Nov-26	04-Jul-26	16-Jul-26	578,784
Storm Drainage Network		113	02-Aug-26 A	23-Nov-26	15-Jul-26	27-Aug-26	2,455,841
FROM MH-25:MH-12		109	02-Aug-26 A	18-Nov-26	15-Jul-26	27-Aug-26	2,049,483
Main Line Sections		18	02-Aug-26 A	08-Nov-26	15-Jul-26	04-Aug-26	1,787,973
CO-SD-ML-100	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	3	02-Aug-26 A	31-Oct-26	15-Jul-26	18-Jul-26	496,659
CO-SD-ML-120	Pipes Laying Works for Main Lines of Storm Drainage Network	5	02-Aug-26 A	02-Nov-26	19-Jul-26	23-Jul-26	893,986
CO-SD-ML-130	Trench Backfilling and Compaction Works for Main Lines of Storm Drainage Network	10	02-Aug-26 A	08-Nov-26	25-Jul-26	04-Aug-26	397,327
Manholes		9	17-Oct-26 A	15-Nov-26	09-Aug-26	24-Aug-26	132,091
CO-SD-MH-180	Trench Excavation and Bedding Works for Manholes of Storm Drainage Network	7	17-Oct-26 A	07-Nov-26	09-Aug-26	16-Aug-26	49,534
CO-SD-MH-190	Install RC Footing Works for Manholes of Storm Drainage Network	7	08-Nov-26	15-Nov-26	17-Aug-26	24-Aug-26	82,557
Catch Basin Sections		10	08-Nov-26	18-Nov-26	17-Aug-26	27-Aug-26	129,420
CO-SD-CB-140	Trench Excavation and Bedding Works for Catch Basins of Storm Drainage Network	10	08-Nov-26	18-Nov-26	17-Aug-26	27-Aug-26	129,420
FROM MH-12:MH-01		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
Main Line Sections		14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
CO-SD-ML-140	Trench Excavation and Bedding Works for Main Lines of Storm Drainage Network	14	08-Nov-26	23-Nov-26	03-Aug-26	18-Aug-26	406,357
Sewage Network		12	08-Nov-26	21-Nov-26	03-Aug-26	16-Aug-26	62,108
FROM MH-18:MH-10		12	08-Nov-26	21-Nov-26	03-Aug-26	16-Aug-26	62,108
Main Line Sections		12	08-Nov-26	21-Nov-26	03-Aug-26	16-Aug-26	62,108
CO-SW-ML-100	Trench Excavation and Bedding Works for Main Lines of Sewage Network	12	08-Nov-26	21-Nov-26	03-Aug-26	16-Aug-26	62,108

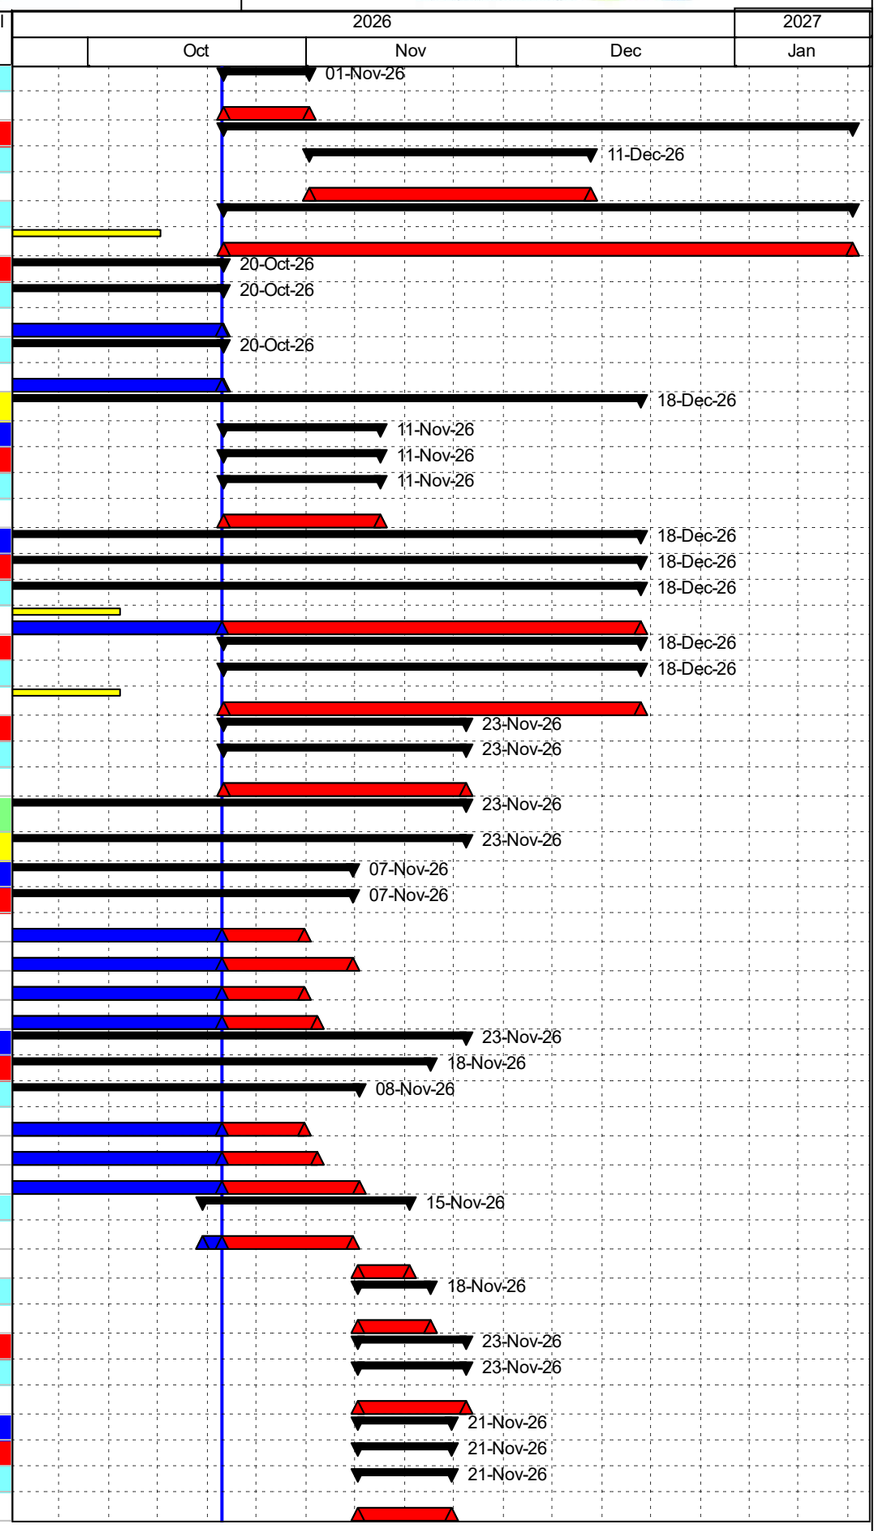


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Superstructure Work		186	02-Aug-26 A	17-Nov-26	11-Aug-26	26-Dec-26	10,077,650
Utility Buildings		125	23-Sep-26 A	17-Nov-26	15-Oct-26	26-Dec-26	1,809,742
Pump Station		22	20-Oct-26	14-Nov-26	30-Nov-26	26-Dec-26	847,916
Civil work		2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	72,069
Super structure		2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	72,069
CO-UB-PS-250	curing and deshuttering formwork for pump roof	2	20-Oct-26	21-Oct-26	30-Nov-26	02-Dec-26	72,069
Architectural work		15	22-Oct-26	08-Nov-26	02-Dec-26	20-Dec-26	640,717
CO-UB-PS-260	Executing Masonry Works for Pump station building	5	22-Oct-26	27-Oct-26	02-Dec-26	08-Dec-26	183,776
CO-UB-PS-270	Executing Plastering Works for Pump station building	5	28-Oct-26	02-Nov-26	08-Dec-26	14-Dec-26	229,720
CO-UB-PS-280	Executing Painting Works for Pump station building	5	03-Nov-26	08-Nov-26	14-Dec-26	20-Dec-26	227,221
Electrical work		5	09-Nov-26	14-Nov-26	20-Dec-26	26-Dec-26	135,130
CO-UB-PS-290	Lighting system for pump house	5	09-Nov-26	14-Nov-26	20-Dec-26	26-Dec-26	135,130
Lift Station		51	23-Sep-26 A	11-Nov-26	15-Oct-26	16-Nov-26	395,179
Civil work		51	23-Sep-26 A	11-Nov-26	15-Oct-26	16-Nov-26	395,179
Super structure		51	23-Sep-26 A	11-Nov-26	15-Oct-26	16-Nov-26	395,179
CO-UB-LS-290	Formwork for Wall and columns for Lift Station	7	23-Sep-26 A	27-Oct-26	15-Oct-26	22-Oct-26	84,081
CO-UB-LS-300	Steel fixing for Wall columns	9	23-Sep-26 A	29-Oct-26	24-Oct-26	02-Nov-26	84,081
CO-UB-LS-310	pouring for Wall columns	1	30-Sep-26 A	29-Oct-26	03-Nov-26	03-Nov-26	50,448
CO-UB-LS-320	curing and deshuttering formwork for Wall columns	2	31-Oct-26	01-Nov-26	04-Nov-26	05-Nov-26	8,408
CO-UB-LS-330	Waterproofing for Walls columns	4	02-Nov-26	05-Nov-26	07-Nov-26	10-Nov-26	84,081
CO-UB-LS-340	Formwork for pump roof	5	07-Nov-26	11-Nov-26	11-Nov-26	16-Nov-26	84,081
IrrigationTank		119	14-Oct-26 A	11-Nov-26	10-Nov-26	02-Dec-26	73,453
Eearth Work		119	14-Oct-26 A	01-Nov-26	10-Nov-26	22-Nov-26	7,354
CO-UB-IRT-140	Excavation work for tank foundation tank formation level	6	14-Oct-26 A	26-Oct-26	10-Nov-26	16-Nov-26	0
CO-UB-IRT-150	Soil replacement Up to tank formation level	5	27-Oct-26	01-Nov-26	17-Nov-26	22-Nov-26	7,354
Structural Work		9	02-Nov-26	11-Nov-26	23-Nov-26	02-Dec-26	66,100
CO-UB-IRT-160	Plain Concrete works	3	02-Nov-26	04-Nov-26	23-Nov-26	25-Nov-26	24,787
CO-UB-IRT-170	Form work for Tank Foundation	6	05-Nov-26	11-Nov-26	26-Nov-26	02-Dec-26	41,312
Control Room		25	20-Oct-26	17-Nov-26	19-Oct-26	16-Nov-26	493,193
Civil Work		16	20-Oct-26	07-Nov-26	19-Oct-26	05-Nov-26	397,101
CO-UB-CR-130	Pouring R.C Columns For Control Room	8	20-Oct-26	28-Oct-26	19-Oct-26	27-Oct-26	144,859
CO-UB-CR-140	Pouring Beams and Slab For Control Room	8	29-Oct-26	07-Nov-26	28-Oct-26	05-Nov-26	252,242
Finishing Work		9	08-Nov-26	17-Nov-26	07-Nov-26	16-Nov-26	96,092
Architictural work		9	08-Nov-26	17-Nov-26	07-Nov-26	16-Nov-26	96,092
CO-UB-CR-150	Brick Work For Control Room	9	08-Nov-26	17-Nov-26	07-Nov-26	16-Nov-26	96,092
Fence and Gaurd Room		108	02-Aug-26 A	17-Nov-26	11-Aug-26	02-Dec-26	8,267,908
Fence Work		108	02-Aug-26 A	17-Nov-26	11-Aug-26	02-Dec-26	8,267,908
Northern Fence N01:N03		25	20-Oct-26	17-Nov-26	29-Aug-26	27-Sep-26	43,078
Finishing Work		25	20-Oct-26	17-Nov-26	29-Aug-26	27-Sep-26	43,078
Electrical Work		25	20-Oct-26	17-Nov-26	29-Aug-26	27-Sep-26	43,078
CO-SU-FE-N-EL-	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	8	20-Oct-26	28-Oct-26	29-Aug-26	06-Sep-26	17,844
CO-SU-FE-N-EL-	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	8	20-Oct-26	28-Oct-26	29-Aug-26	06-Sep-26	8,182
CO-SU-FE-N-EL-	Fixing of Control cable,CAT6A cable	9	29-Oct-26	08-Nov-26	07-Sep-26	16-Sep-26	4,241
CO-SU-FE-N-EL-	Install 800mm x 800mm x 800mm height concrete handhole	9	29-Oct-26	08-Nov-26	07-Sep-26	16-Sep-26	4,436
CO-SU-FE-N-EL-	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	8	29-Oct-26	07-Nov-26	07-Sep-26	15-Sep-26	5,767
CO-SU-FE-N-EL-	Fixing Earthing Work (Earth Pit,Grounding rod,Tinned Copper wire)	8	09-Nov-26	17-Nov-26	17-Sep-26	27-Sep-26	2,609
Western Fence P1 (W01:W06)		30	17-Sep-26 A	14-Nov-26	12-Sep-26	01-Nov-26	1,126,313
Civil Work		28	17-Sep-26 A	25-Oct-26	12-Sep-26	01-Nov-26	757,244
CO-SU-FE-WP1-C	Pouring R.C Columns For Northern Fence	16	17-Sep-26 A	24-Oct-26	12-Sep-26	01-Oct-26	675,382
CO-SU-FE-WP1-C	Pouring Beams For Northern Fence	17	05-Oct-26 A	25-Oct-26	12-Oct-26	01-Nov-26	81,862
Finishing Work		23	29-Sep-26 A	14-Nov-26	01-Oct-26	28-Oct-26	369,069
Electrical Work		14	29-Oct-26	14-Nov-26	12-Oct-26	28-Oct-26	52,051
CO-SU-FE-WP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	14	29-Oct-26	14-Nov-26	12-Oct-26	28-Oct-26	35,687

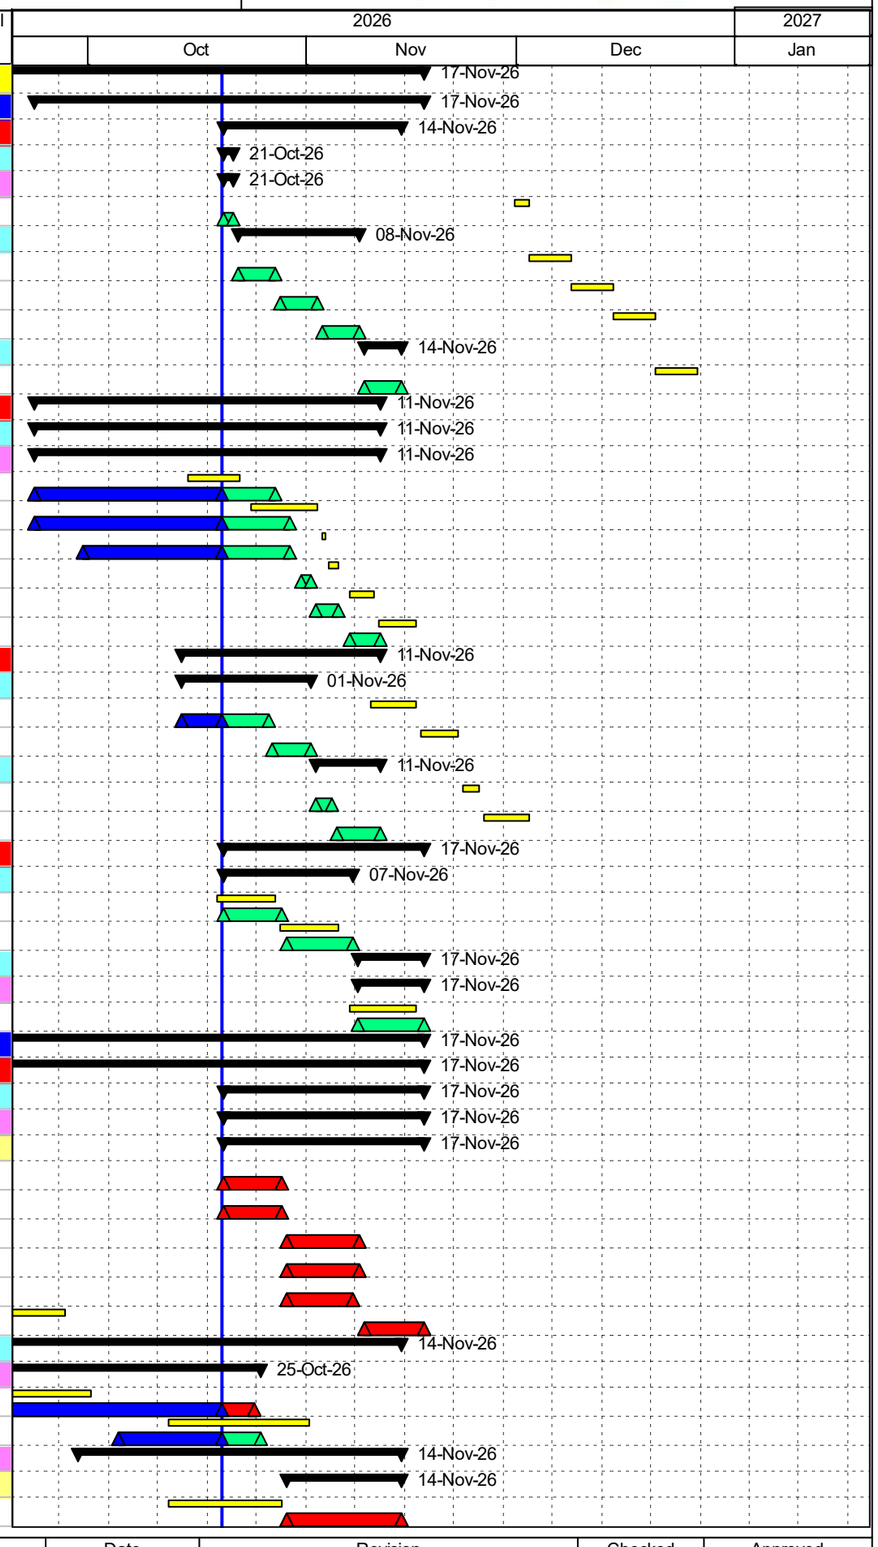


Primary Baseline | Actual Work | Summary
Remaining Work | Baseline Milestone
Critical Remaining Work | Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
CO-SU-FE-WP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	14	29-Oct-26	14-Nov-26	12-Oct-26	28-Oct-26	16,364
Architictural work		9	29-Sep-26 A	24-Oct-26	01-Oct-26	12-Oct-26	317,018
CO-SU-FE-WP1-A	Install Brick Work For Northern Fence	9	29-Sep-26 A	24-Oct-26	01-Oct-26	12-Oct-26	317,018
Western Fence P2 (W07:W12)		36	19-Sep-26 A	14-Nov-26	07-Oct-26	11-Nov-26	1,046,994
Civil Work		36	19-Sep-26 A	29-Oct-26	07-Oct-26	09-Nov-26	649,037
CO-SU-FE-WP2-C	Pouring R.C Columns For Northern Fence	9	19-Sep-26 A	29-Oct-26	07-Oct-26	18-Oct-26	567,175
CO-SU-FE-WP2-C	Pouring Beams For Northern Fence	7	11-Oct-26 A	29-Oct-26	01-Nov-26	09-Nov-26	81,862
Finishing Work		13	29-Sep-26 A	14-Nov-26	18-Oct-26	11-Nov-26	397,957
Electrical Work		13	31-Oct-26	14-Nov-26	27-Oct-26	11-Nov-26	80,939
CO-SU-FE-WP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	31-Oct-26	03-Nov-26	27-Oct-26	01-Nov-26	35,687
CO-SU-FE-WP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	6	31-Oct-26	05-Nov-26	27-Oct-26	03-Nov-26	16,364
CO-SU-FE-WP2-E	Fixing of Control cable,CAT6A cable	7	07-Nov-26	14-Nov-26	03-Nov-26	11-Nov-26	8,482
CO-SU-FE-WP2-E	Install 800mm x 800mm x 800mm height concrete handhole	7	07-Nov-26	14-Nov-26	03-Nov-26	10-Nov-26	8,871
CO-SU-FE-WP2-E	Hot dipped galvanized cable conduits for CAT6A cable and Control Cables embedde	6	07-Nov-26	12-Nov-26	03-Nov-26	10-Nov-26	11,535
Architictural work		8	29-Sep-26 A	29-Oct-26	18-Oct-26	27-Oct-26	317,018
CO-SU-FE-WP2-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	29-Oct-26	18-Oct-26	27-Oct-26	317,018
Southern Fence S01:S05		80	02-Aug-26 A	10-Nov-26	11-Aug-26	21-Sep-26	2,173,732
Civil Work		76	02-Aug-26 A	03-Nov-26	11-Aug-26	14-Sep-26	1,866,175
CO-SU-FE-S-CI-26	Pouring for Plain Concrete Northern Fence	3	02-Aug-26 A	22-Oct-26	11-Aug-26	13-Aug-26	89,091
CO-SU-FE-S-CI-27	Pouring R.C Footing For Northern Fence	8	02-Aug-26 A	28-Oct-26	15-Aug-26	23-Aug-26	990,000
CO-SU-FE-S-CI-28	Pouring R.C Columns For Northern Fence	10	05-Oct-26 A	31-Oct-26	24-Aug-26	03-Sep-26	718,865
CO-SU-FE-S-CI-29	Pouring Beams For Northern Fence	9	08-Oct-26 A	03-Nov-26	05-Sep-26	14-Sep-26	68,218
Finishing Work		19	29-Sep-26 A	10-Nov-26	05-Sep-26	21-Sep-26	307,558
Electrical Work		15	25-Oct-26	10-Nov-26	05-Sep-26	21-Sep-26	43,376
CO-SU-FE-S-EL-5	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	15	25-Oct-26	10-Nov-26	05-Sep-26	21-Sep-26	29,739
CO-SU-FE-S-EL-6	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	15	25-Oct-26	10-Nov-26	05-Sep-26	21-Sep-26	13,636
Architictural work		6	29-Sep-26 A	31-Oct-26	05-Sep-26	10-Sep-26	264,182
CO-SU-FE-S-AR-3	Install Brick Work For Northern Fence	6	29-Sep-26 A	31-Oct-26	05-Sep-26	10-Sep-26	264,182
Eastern Fence P1 (E01:E06)		68	02-Aug-26 A	10-Nov-26	29-Aug-26	26-Oct-26	2,264,655
Civil Work		68	02-Aug-26 A	05-Nov-26	29-Aug-26	26-Oct-26	1,895,585
CO-SU-FE-EP1-CI	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	28-Oct-26	29-Aug-26	06-Sep-26	106,909
CO-SU-FE-EP1-CI	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	02-Nov-26	07-Sep-26	20-Sep-26	1,188,000
CO-SU-FE-EP1-CI	Pouring R.C Columns For Northern Fence	15	06-Oct-26 A	05-Nov-26	21-Sep-26	08-Oct-26	518,815
CO-SU-FE-EP1-CI	Pouring Beams For Northern Fence	7	08-Oct-26 A	05-Nov-26	19-Oct-26	26-Oct-26	81,862
Finishing Work		10	29-Sep-26 A	10-Nov-26	10-Oct-26	22-Oct-26	369,069
Electrical Work		4	07-Nov-26	10-Nov-26	19-Oct-26	22-Oct-26	52,051
CO-SU-FE-EP1-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	19-Oct-26	22-Oct-26	35,687
CO-SU-FE-EP1-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	07-Nov-26	10-Nov-26	19-Oct-26	22-Oct-26	16,364
Architictural work		8	29-Sep-26 A	05-Nov-26	10-Oct-26	18-Oct-26	317,018
CO-SU-FE-EP1-A	Install Brick Work For Northern Fence	8	29-Sep-26 A	05-Nov-26	10-Oct-26	18-Oct-26	317,018
Eastern Fence P2 (E07:E13)		61	02-Aug-26 A	11-Nov-26	06-Oct-26	02-Dec-26	1,613,137
Civil Work		61	02-Aug-26 A	11-Nov-26	06-Oct-26	02-Dec-26	1,182,556
CO-SU-FE-EP2-CI	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	07-Nov-26	06-Oct-26	19-Oct-26	124,727
CO-SU-FE-EP2-CI	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	07-Nov-26	20-Oct-26	02-Nov-26	486,000
CO-SU-FE-EP2-CI	Pouring R.C Columns For Northern Fence	10	15-Sep-26 A	07-Nov-26	03-Nov-26	14-Nov-26	476,324
CO-SU-FE-EP2-CI	Pouring Beams For Northern Fence	10	01-Oct-26 A	11-Nov-26	22-Nov-26	02-Dec-26	95,505
Finishing Work		29	29-Sep-26 A	11-Nov-26	15-Nov-26	25-Nov-26	430,581
Electrical Work		4	08-Nov-26	11-Nov-26	22-Nov-26	25-Nov-26	60,726
CO-SU-FE-EP2-E	Trench excavation to receive 2 nos 50mm diameter PVC Conduit	4	08-Nov-26	11-Nov-26	22-Nov-26	25-Nov-26	41,635
CO-SU-FE-EP2-E	Trench excavation to receive 3 nos 50mm diameter PVC Conduit	4	08-Nov-26	11-Nov-26	22-Nov-26	25-Nov-26	19,091
Architictural work		6	29-Sep-26 A	07-Nov-26	15-Nov-26	21-Nov-26	369,855
CO-SU-FE-EP2-A	Install Brick Work For Northern Fence	6	29-Sep-26 A	07-Nov-26	15-Nov-26	21-Nov-26	369,855

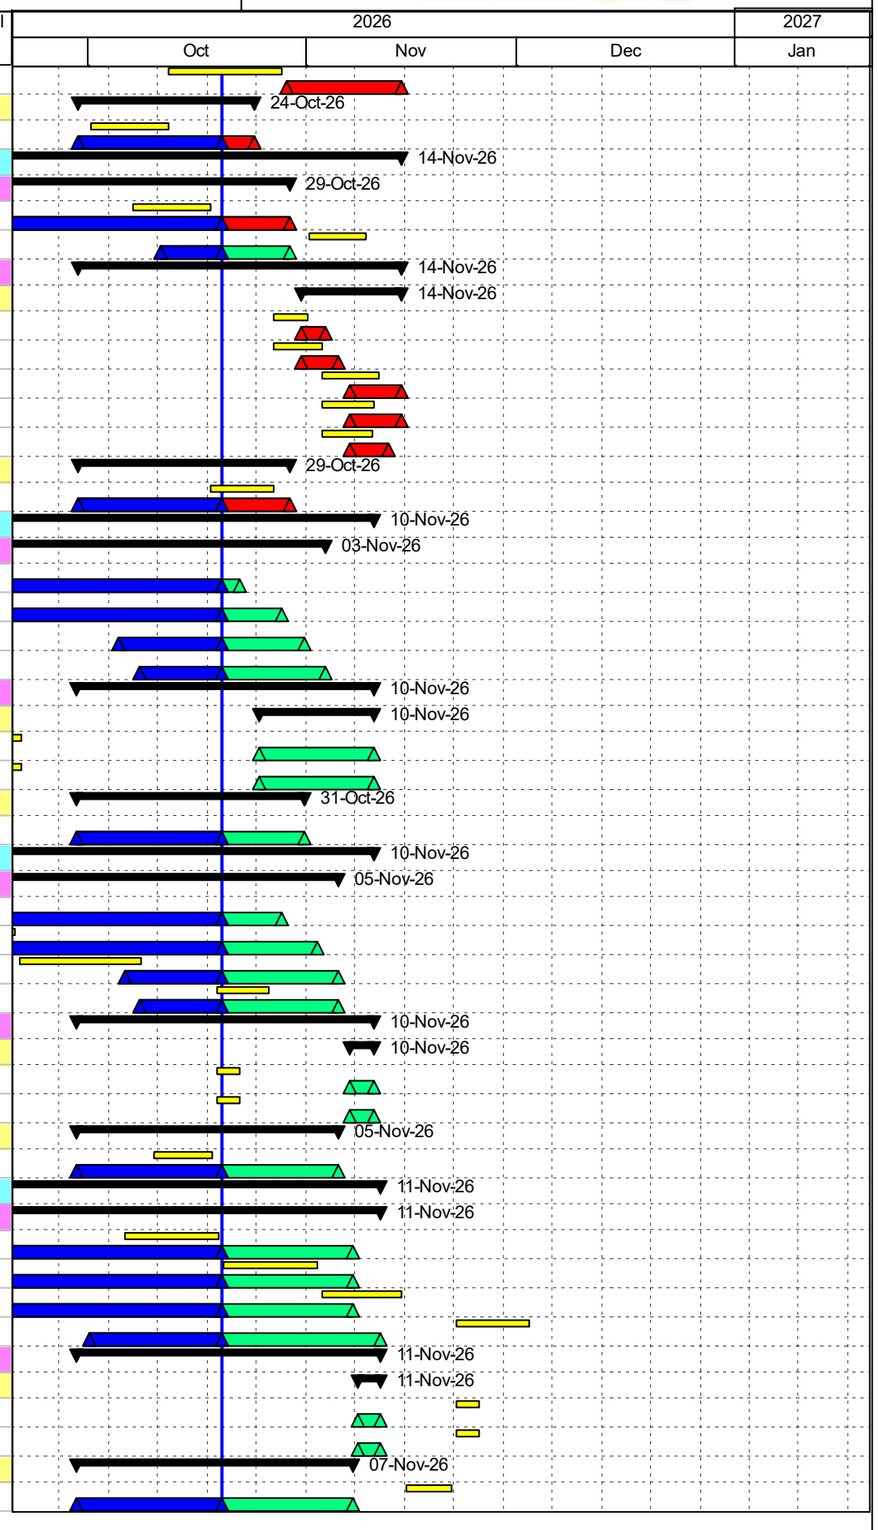


Primary Baseline
Actual Work
Summary
Remaining Work
Baseline Milestone
Critical Remaining Work
Milestone

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		

Development of the Technology City in Dammam-
RECOVERY SCHEDULE -Update20-10-2026
3Week Lookahead Schedule

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost
Testing and Comissioning		0	20-Oct-26	20-Oct-26	04-Jan-27	04-Jan-27	0
Utility Buildings		0	20-Oct-26	20-Oct-26	04-Jan-27	04-Jan-27	0
T/C-DPO	Testing and Commissioning of Storm Drainage Ponds	0	20-Oct-26	20-Oct-26	04-Jan-27	04-Jan-27	0
Handing over and close out		14	20-Oct-26	04-Nov-26	04-Jan-27	19-Jan-27	0
As-Built		14	20-Oct-26	04-Nov-26	04-Jan-27	19-Jan-27	0
HO-130	Submission As-Built Drawing For Pond	14	20-Oct-26	04-Nov-26	04-Jan-27	19-Jan-27	0

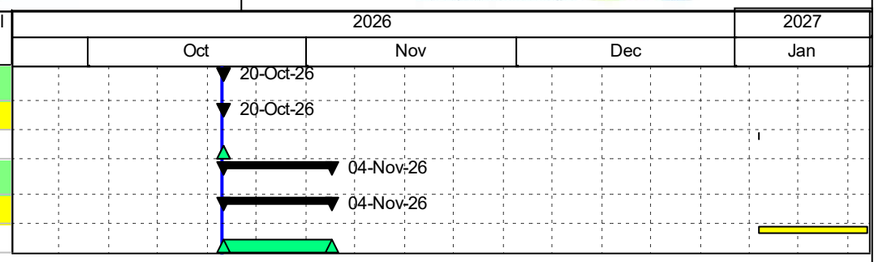

Primary Baseline
Remaining Work
Critical Remaining Work
Actual Work
Baseline Milestone
Milestone
Summary

Date	Revision	Checked	Approved
20-Oct-26	Third Industrial City		
